PUNJAB RURAL MUNICIPAL SERVICES COMPANY

5th Floor, KD Plaza, MM Alam Road, Gulberg-III, Lahore, Pakistan
Telephone: +92-42-99333613

Request for Bids

Punjab Rural Sustainable Water Supply & Sanitation Project (PRSWSSP)

(One-Envelope Bidding Process)

RFB Reference No: PK-LG& CD-559576-CW-RFB

Project: PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT

Contract Title: **Civil Works under PRSWSSP, Tehsil Bahawalnagar, Cluster South-III (Bahawalnagar-29) (CW-25)**
Villages: AKKANWALI KHURD, SHER MOHD, KARTAR SINGH, KHOBER, DHARAM PURA, HIRA BASHNOAI, ALLAHABAD, AMIN ABAD, BARASAJWAR KHAN, CHAK ABDUL HAQ, DADOO MAMMUNKA, DARA SANATTEKA, DHANRAJ PURA, HASAN RAIKA, JAGGA SANATTEKA, JALWALA, JANOOWALA, KHAWAJA BUX BODLA, MAHNI BEGKA, MALAK PURA, MINA SANATTEKA, MUHAMMAD ASAD KHAN, MUHSAN PURA, NOOR JAHANIAN, PARAN WALA, RAMNAGAR, SANDAR BASHNOI, SHER SINGH WALA, TOBI QAMAR-UD-DIN

Employer: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

Country: PAKISTAN

Loan No.: IBRD-92670

Issued On: 15-07-2026

PRSWSSP

PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

A COMPANY SET UP UNDER SECTION 42 OF THE COMPANIES ACT, 2017

SPECIFIC PROCUREMENT NOTICE
REQUEST FOR BIDS

Procurement of Civil Works of Priority Villages Pilot Phase-II (Part-a)

Country:	PAKISTAN
Name of Project:	PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT
Employer:	PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)
Loan No.:	IBRD-92670

1. Government of the Islamic Republic of Pakistan (who has extended the financing to Punjab Rural Municipal Services Company) has received a loan from the **World Bank** (IBRD) towards the cost of the Punjab Rural Sustainable Water Supply & Sanitation Project (PRSWSSP) and intends to apply part of the proceeds toward payments under the Procurement of Civil Works of Priority Villages.

2. Punjab Rural Municipal Services Company - PRMSC (the Employer) now invites sealed Bids from eligible Bidders for the following Contract Packages;

Sr. No.	Description / STEP Activity No.	Bid Security (Pak. Rs.)
1	PK-LG& CD-559542-CW-RFB - Civil Works under PRSWSSP, Tehsil Liaqatpur, Cluster South-I (Liaqatpur-13) (CW-11) Villages: Chak No 08 Abbasia, Chak No 6A Channa, Chak No 08 Abbasia Jinnah Colony, Chak No 9 Abbasia, Chak No 09 Abbasia Colony, Chak No 09 Abbasia Shiekhan, Chak 11 Abbsia, Chak No 12 Abbasia, Chak No 16 Abbasia Colony, Chak No 19 Abbasia, Chak No 20 Abbasia Colony, Chak No 20 Abbasia, Chak No 22 Abbasia Jinnah Colony, Chak No 22 Abbasia, Chak No 23 Abbasia, Chak No 23 Abbasia Colony_1, Chak No 23 Abbasia Colony_2, Chak No 28 Abbasia, Chak No 31 Abbasia, Chak No 31 Abbasia Colony_1, Chak No 31 Abbasia Colony_2, Chak No 46 Abbasia, Chak No 47 Abbasia, Chak No 48 Abbasia	65,500,000
2	PK-LG& CD-559549-CW-RFB - Civil Works under PRSWSSP, Tehsil Liaqatpur, Cluster South-I (Liaqatpur-24) (CW-12) Villages: Chak No 42 Abbasia, Chak No 43 Abbasia, Chak No 43 Abbasia Colony, Chak No 143 Abbasia, Chak No 144 5R, Chak No 145 5R, Chak No 147 5R, Chak No 148 5R, Chak No 32 Abbasia, Chak No 33 Abbasia, Chak No 40 Abbasia, Chak No 41 Abbasia, Chak No 38 Abbasia (Zia Colony), Chak No 37 Abbasia, Murad Colony Chak 38 Abbasia, Chak No 39 Abbasia, Chak No 63 Abbasia, Chak No 89 Abbasia, Chak No 88 Abbasia Chota, Chak 85-A Colony, Chak No 86 Abbasia, Chak No 313/6R, Chak No 88 Abbasia Bara,	71,000,000

	Chak No 87 Abbasia, Basti Abdul Ghafooor, CHAK 315/6R, Chak 316/6R, CHAK 317/6R	
3	PK-LG& CD-559552-CW-RFB - Civil Works under PRSWSSP, Tehsil Liaqatpur, Cluster South-I (Liaqatpur-20) (CW-13) Villages: Chak No 150 Abbasia, Chak NO 179 7R, Adda Gulshan Farid, Chak No 180 7R, Chak No 194 1L, Chak No 195 1L, Chak No 182 1L, Chak 152 7R, Chak 153 7R, Chak 154 7R, Chak 155 7R, Chak 156 7R, Chak 177 7R, Chak 178 7R, Chak 183 7R, Chak 191-1L, Chak No 36 Abbasia, Basti Tok, Basti Saleh Muhammad, Chak 70 Firoza, Basti Khokhran	39,000,000
4	PK-LG& CD-559554-CW-RFB - Civil Works under PRSWSSP, Tehsil Liaqatpur, Cluster South-I (Liaqatpur-15) (CW-14) Villages: Basti Malik Parvez Akhtar, Basti Kukara, Basti Ghalo, Basti Imam Bux, Basti Waryam Solangi, Basti Allah Bux/M. Murad, Basti Sadat, Jindu Pir Kamal, Chak No 3 Abbasia, Chak No 3A Colony, Chak No 140 NP, Basti Malik Allah Ditta Solangi, Basti Elahi Bux Toor, Chak No 139 NP, Basti Azmat Lar, Basti Jam kareem Bahakas, Basti Marri, Basti Lal Maha, Basti Bhattian, Basti Buraha, Basti Haji Abdur Rehman Khosa, Basti Hussain Abad, Basti Noor Muhammad, Basti Haji Kamal, Basti Ameer Bux, Basti Chak 04A, Chak No 4 Abbasia, Basti Ishaq, Khangah, Basti Sanaullah Khan, Basti Pannua, Basti Nabi, Chak No 134 NP, Chak No 135 NP, Chak No 136 NP, Basti Manzoor Ahmed Lar, Basti Malik Lal Machi, Basti Haji Mehar Ali Drig, Basti Marral, Basti Abdul Rasheed Lar, Basti Noor Din	44,500,000
5	PK-LG& CD-559558-CW-RFB - Civil Works under PRSWSSP, Tehsil Rojhan, Cluster South-I (Rojhan-08) (CW-16) Villages: Dera Dildar (Catchment-1, Catchment-2, Catchment-3, Catchment-4, Catchment-5, Catchment-6, Catchment-7, Catchment-8), Chak Karia (Catchment-1, Catchment-2, Basti Silachi), Dera Jiwan Khas (Catchment-1), Miranpur (Catchment-1, Catchment-2, Catchment-3, Catchment-4, Catchment-5), Badli (Catchment-1), KotlaGulsher (Catchment-1, Catchment-2, Catchment-3), Badli Chak Ladh (Catchment-1, Catchment-2), Kaheeri(Catchment-1, Catchment-2)	22,500,000
6	PK-LG& CD-559561-CW-RFB - Civil Works under PRSWSSP, Tehsil Rojhan, Cluster South-I (Rojhan-12) (CW-17) Villages: Rakh Sabzani,Bhagsar, Rakh Qadra (Basti Panjwani, Basti Lajwani, Basti Juma, Basti Gola), C1, C2, Dhohra (Basti Dhora), Pera Ditta, Qadir Ganadi, Basti Duriwala, Basti Chakar, Basti Gianmal, Kotla Hassan Shah, Chak Safdar Abad (C1 to C3), Chak Dilbar (C1 to C6), Chak Tariq abad (C1-C3), Chak Saleem Abad (C1-C5), Chak Mutrfriq Marzari(C1 to C2)	42,000,000
7	PK-LG& CD-559568-CW-RFB - Civil Works under PRSWSSP, Tehsil Pakpattan , Cluster South-I (Pakpattan-36) (CW-21) Villages: AMIRA AHLUKA, BABLANA, BAHDAR KHARA, BAHMANI, BAHWAN SHAH, BONGA AMAM DIN, CHAK NO.12.K.B., CHAK NO.5.K.B., CHHINAH, DADA AHLUKA & NURA AHLUKA (MVS), GHAR TAJ, JAGGA BALUCH, JAND WALA, JATTU WAL, JAWAYA MAL, KALA CHISHTI, KHAMBA DOGAR, KIRPARAM, KOT HAKIM, LAKH WIRA, MALIK RAHMUN, MANAWAR, MUSTEQIM MAMUNKA, NABI BAKISH, PIR GHULAM QADIR, WARA PERAN KHURD, WARA PIRAN KALAN, BARHAN DIN, BUNGA BALUCH, CHAK ELAHYA WALA, CHAK HAKIMAN, CHAK NO.4KB, JAHANA MAHMUNKA, KALANCHI, KHALITA.	26,500,000
8	PK-LG& CD-559572-CW-RFB - Civil Works under PRSWSSP, Tehsil Khairpur Tamewali, Cluster South-III (Khairpur tamewali-47) (CW-22) Villages: FAZLU KUKARA, MAMDU MANGERO, KHAIRI BHABI,	34,500,000

	LADAR, KOTLA MAHI, BUNGA YARANI, DARUD GARAN, GOTH ALI, GOTH KAMAL, KAMALIA, AHMED MILKHI, AMIN FATANI, BAGHBAN, BINDA CHADHRAN, KHARAL NAU BARAMAD,CHAK NO.26,DHARALA RANDU, HALEEM, KHANAN ARAIN, DEDA, KHUDA BUX SEYAL, KOTLA QAIM KHAN, KUKARA NAGANA, LAL SOHANRA, LUTHRAN, MEHTI, MOHAMMAD SHARIF, MUHAMMAD KHAN, MUNGRANI, MURADPUR, MURADPUR DHRALA, NURREY, PIR KORA, QAZI KALRA, RAJA, RAMELI, RUKRANI, SARDAR PUR, AZIMPURA, NOOR MOHD KHAN, KHAIR PUR, GAWAINS, GOTH JHUMAR, GAMUN WAGI, DHARALA NAU BARAMDA, DILDAR WAINS, DHARALA OTTAM CHAND	
9	PK-LG& CD-559574-CW-RFB- Civil Works under PRSWSSP, Tehsil Bahawalnagar, Cluster South-III (Bahawalnagar-33) (CW-24) Villages: ABRERAH HITTHAR, ABRERAH UTTAR, ALI GOHER NO. 326, BEG KANOOR PUR, BHANGRAN, BHOREKA, BILARA NABI BUX, BILLU KA HITHAR, BONGA IHSAN BIBI, BONGA RANUKA, BOOLE SHAH HITTHAR, PIR SIKANDAR OTAR, GAMAN DONGI, GAUSPUR, GHANIPUR, HUSSIAN ABAD HITHAR, HUSSIAN ABAD UTTAR, JHULAN CHISHTIAN, KAKKU BODLA, KHILOWALA, MADARSA, MAMUNKA HATAR, MAMUNKA UTTAR, MARI MIAN SAHAB HITHAR, MEHMUD LANGAH, MOSLA, MUQIM SHAH, PIR SHAH, RAMZAN LANGAH, SHARAF DIN, TUGHERA SHARIF, WARA PIRAN, WILAYAT PUR	24,000,000
10	PK-LG& CD-559576-CW-RFB - Civil Works under PRSWSSP, Bahawalnagar, Cluster South-III (Bahawalnagar-29) (CW-25) Villages: AKKANWALI KHURD, SHER MOHD, KARTAR SINGH, KHOBER, DHARAM PURA, HIRA BASHNOAI, ALLAHABAD, AMIN ABAD, BARASAJWAR KHAN, CHAK ABDUL HAQ, DADOO MAMMUNKA, DARA SANATTEKA, DHANRAJ PURA, HASAN RAIKA, JAGGA SANATTEKA, JALWALA, JANOOWALA, KHAWAJA BUX BODLA, MAHNI BEGKA, MALAK PURA, MINA SANATTEKA, MUHAMMAD ASAD KHAN, MUHSAN PURA, NOOR JAHANIAN, PARAN WALA, RAMNAGAR, SANDAR BASHNOI, SHER SINGH WALA, TOBI QAMAR-UD-DIN	36,000,000
11	PK-LG& CD-559581-CW-RFB - Civil Works under PRSWSSP, Shujabad, Cluster South-II (Shujabad-09) (CW-29) Villages: CHAHAN MIRAN KHAN, MOHAN PUR SHARQI, SARAI, NASEER PUR, NAWAN CHAK, BASTI DAAD, SANGRAI, SHAH PURABHA SHUMALI, WAHI RAKI	23,000,000
12	PK-LG& CD-559582-CW-RFB - Civil Works under PRSWSSP, Taunsa, Cluster South-II (Taunsa-29) (CW-30) Villages: Chak Soharna Bacha, Aqupur, Berand, Boda Mana, Ghali, Jalal Khan, Jhok Rahul, Jin Pur, Wani, Rakh Sanjar, Rakh Zor, Jhok Chapri, Khitaran Wala, Mirkhar, Pukhan, Rakh Mari Pachaudi, Rindwala, Dumra Janubi, Bet Obai, Jhok Yaran, Baghon Wala, Langha, Kotla Marrani, Basti Habib, Rakhana, Bakhri, Arakhar Dao, Ghadi Sandila, Basti Nasir	27,900,000
13	PK-LG& CD-559587-CW-RFB - Civil Works under PRSWSSP, Alipur, Cluster South-II Alipur-21/23) (CW-34) Villages: SHEIKHANI, DAHAK, NUSRAT PUR, BET DEWAN SAHB, GHARI, KHACHI LAL, DAMAR WALA JANUBI 1, BET CHANNA, FATEH PUR JANUBI 1, MOZIZDIN, MADD SOHANARSHAH, BASTI HAJI, BET PANOHAN, CHAK DAUD WALA, DAULAT PUR, WALWAT,	33,500,000

	MOHIB SHAH, KHAIR PUR PARA, KHAN PUR NAHRKA, PAKKA NAICH, KHANGARH DOMA	

3. Bidding will be conducted through national competitive procurement using Request for Bids (RFB) as specified in the World Bank's Procurement Regulations for IPF Borrowers dated July 2016 (Revised November 2017 & August 2018)("Procurement Regulations"), and is open to all eligible Bidders as defined in the Procurement Regulations &Bidding Document.

4. Interested eligible Bidders may obtain further information from the Office of the Employer and inspect the Bidding Document during office hours [Monday to Friday] at the address given below.

5. The Bidders may download the Bidding Document at no cost from the website: www.prmsc.punjab.gov.pk/tenders. Soft copy of Bidding Document can also be obtained from PRMSC Head Office, Lahore free of cost. Bidders opting to download the Bidding Documents from any of the aforesaid website, shall inform the Punjab Rural Municipal Services Company, in writing at the address given below failing which Company shall not be responsible if they do not receive clarifications and amendments, if any from the Company.

6. A Pre-bid Meeting shall take place on July 16, 2026 on 01:00 pm at Conference Room, PRMSC, 5th floor KD Plaza MM Alam Road, Lahore. Bidders have the option to attend online pre-bid meeting through zoom link, Meeting ID: 811 2002 3773, Passcode: 095698
https://us06web.zoom.us/j/81120023773?pwd=eXBDC4GhHawydaM8pwJLRmeugaM5wA.1

7. Bids must be delivered to the address below on or before **August 04, 2026 at 1500 hours** for all the above-mentioned packages. Electronic Bidding will not be permitted. Late Bids will be rejected. Bids will be publicly opened in the presence of the Bidders' designated representatives and anyone who chooses to attend at the address below on **August 04, 2026 at 1530 hours**.

8. The Bids must be accompanied by a Bid Security as mentioned above, for each contract package in the shape of unconditional Bank Guarantee or Call Deposit Receipt (CDR) in the name of **"Punjab Rural Municipal Services Company"**.

9. Attention is drawn to the Procurement Regulations for IPF Borrowers dated November 2020 requiring the Borrower to disclose information on the successful Bidder's beneficial ownership, as part of the Contract Award Notice, using the Beneficial Ownership Disclosure Form as included in the Bidding Document.

10. The address referred to above is:

Chief Executive Officer
Punjab Rural Municipal Services Company (PRMSC)
5th Floor, KD Plaza, MM Alam Road, Gulberg-III, Lahore, Pakistan
Telephone: +92-42-99333613
Email address: proc.prmsc@punjab.gov.pk

PRMSC

Table of Contents

PART 1 – Bidding Procedures 3

Section I - Instructions to Bidders 5
Section II - Bid Data Sheet (BDS) 33
Section III - Evaluation and Qualification Criteria 39
Section IV - Bidding Forms 51
Section V - Eligible Countries 89
Section VI - Fraud and Corruption 91

PART 2 – Works' Requirements 95

Section VII-Works' Requirements 96

PART 3 – Conditions of Contract and Contract Forms 97

Section VIII - General Conditions of Contract 98
Section IX -Particular Conditions of Contract 131
Section X - Contract Forms 141

PRSWSSP

PART 1 – Bidding Procedures

PRSWSSP

Section I - Instructions to Bidders

Contents

A. General 7

1. Scope of Bid 7
2. Source of Funds 7
3. Fraud and Corruption 8
4. Eligible Bidders 8
5. Eligible Materials, Equipment and Services 11

B. Contents of Bidding Document 11

6. Sections of Bidding Document 11
7. Clarification of Bidding Document, Site Visit, Pre-Bid Meeting 12
8. Amendment of Bidding Document 13

C. Preparation of Bids 13

9. Cost of Bidding 13
10. Language of Bid 13
11. Documents Comprising the Bid 14
12. Letter of Bid and Schedules 14
13. Alternative Bids 14
14. Bid Prices and Discounts 15
15. Currencies of Bid and Payment 16
16. Documents Comprising the Technical Proposal 16
17. Documents Establishing the Eligibility and Qualifications of the Bidder 16
18. Period of Validity of Bids 17
19. Bid Security 17
20. Format and Signing of Bid 19

D. Submission and Opening of Bids 20

21. Sealing and Marking of Bids 20
22. Deadline for Submission of Bids 21
23. Late Bids 21
24. Withdrawal, Substitution, and Modification of Bids 21
25. Bid Opening 22

E. Evaluation and Comparison of Bids 23

26. Confidentiality 23
27. Clarification of Bids 23

PBWSP

28. Deviations, Reservations, and Omissions 24
29. Determination of Responsiveness 24
30. Nonmaterial Nonconformities 24
31. Correction of Arithmetical Errors 25
32. Conversion to Single Currency 25
33. Margin of Preference 26
34. Subcontractors 26
35. Evaluation of Bids 26
36. Comparison of Bids 27
37. Unbalanced or Front Loaded Bids 27
38. Qualification of the Bidder 28
39. Most Advantageous Bid 28
40. Employer'sRight to Accept Any Bid, and to Reject Any or All Bids 28
41. Notification of Intention to Award 29

F. Award of Contract 29

42. Award Criteria 29
43. Notification of Award 29
44. Debriefing by the Employer 30
45. Signing of Contract 30
46. Performance Security 31
47. Adjudicator 31
48. Procurement Related Complaint 31

PRSWSP

Section I - Instructions to Bidders

A. General

1. Scope of Bid

1.1 In connection with the Specific Procurement Notice - Request for Bids (RFB), specified in the Bid Data Sheet (BDS)**,** the Employer, as specified **in the BDS,** issues this bidding document for the provision of Works as specified in Section VII, Works' Requirements. The name, identification and number of lots (contracts) of this RFB are specified **in the BDS.**

1.2 Throughout this bidding document:

(a) the term "in writing" means communicated in written form (e.g. by mail, e-mail, and fax, including if specified **in the BDS**, distributed or received through the electronic-procurement system used by the Employer) with proof of receipt;

(b) if the context so requires, "singular" means "plural" and vice versa;

(c) "Day" means calendar day, unless otherwise specified as "Business Day". A Business Day is any day that is an official working day of the Borrower. It excludes the Borrower's official public holidays; and

(d) "ESHS" means environmental, social (including sexual exploitation and abuse (SEA) and gender based violence (GBV)), health and safety.

2. -Source of Funds

2.1 The Borrower or Recipient (hereinafter called "Borrower") specified **in the BDS** has received or has applied for financing (hereinafter called "funds") from the International Bank for Reconstruction and Development or the International Development Association (hereinafter called "the Bank") in an amount specified **in the BDS**, toward the project named **in the BDS**. The Borrower intends to apply a portion of the funds to eligible payments under the contract(s) for which this bidding document is issued.

2.2 Payment by the Bank will be made only at the request of the Borrower and upon approval by the Bank, and will be subject, in all respects, to the terms and conditions of the Loan (or other financing) Agreement. The Loan (or other financing) Agreement prohibits a withdrawal from the loan account for the purpose of any payment to persons or entities, or for any import of goods, equipment, plant, or

PRSWSP

materials, if such payment or import is prohibited by a decision of the United Nations Security Council taken under Chapter VII of the Charter of the United Nations. No party other than the Borrower shall derive any rights from the Loan (or other financing) Agreement or have any claim to the proceeds of the Loan (or other financing).

3. Fraud and Corruption

3.1 The Bank requires compliance with the Bank's Anti-Corruption Guidelines and its prevailing sanctions policies and procedures as set forth in the WBG's Sanctions Framework, as set forth in Section VI.

3.2 In further pursuance of this policy, bidders shall permit and shall cause their agents (where declared or not), subcontractors, subconsultants, service providers, suppliers, and their personnel, to permit the Bank to inspect all accounts, records and other documents relating to any initial selection process, prequalification process, bid submission, proposal submission, and contract performance (in the case of award), and to have them audited by auditors appointed by the Bank.

4. Eligible Bidders

4.1 A Bidder may be a firm that is a private entity, or a state-owned enterprise or institution, subject to ITB 4.6, or any combination of them in the form of a joint venture (JV), under an existing agreement, or with the intent to enter into such an agreement supported by a letter of intent. In the case of a joint venture, all members shall be jointly and severally liable for the execution of the entire Contract in accordance with the Contract terms. The JV shall nominate a Representative who shall have the authority to conduct all business for and on behalf of any and all the members of the JV during the Bidding process and, in the event the JV is awarded the Contract, during contract execution. Unless specified **in the BDS**, there is no limit on the number of members in a JV.

4.2 A Bidder shall not have a conflict of interest. All Bidders found to have a conflict of interest shall be disqualified. A Bidder may be considered to have a conflict of interest for the purpose of this Bidding process, if the Bidder:

(a) directly or indirectly controls, is controlled by or is under common control with another Bidder; or

(b) receives or has received any direct or indirect subsidy from another Bidder; or

(c) has the same legal representative as another Bidder; or

(d) has a relationship with another Bidder, directly or through common third parties, that puts it in a position to influence

PRSNSD

the Bid of another Bidder, or influence the decisions of the Employer regarding this bidding process; or

(e) or any of its affiliates participated as a consultant in the preparation of the design or technical specifications of the works that are the subject of the Bid; or

(f) or any of its affiliates has been hired (or is proposed to be hired) by the Employer or Borrower as Project Manager for the Contract implementation;

(g) would be providing goods, works, or non-consulting services resulting from or directly related to consulting services for the preparation or implementation of the project specified in the BDS ITB 2.1 that it provided or were provided by any affiliate that directly or indirectly controls, is controlled by, or is under common control with that firm;

(h) has a close business or family relationship with a professional staff of the Borrower (or of the project implementing agency, or of a recipient of a part of the loan) who: (i) are directly or indirectly involved in the preparation of the bidding document or specifications of the contract, and/or the Bid evaluation process of such contract; or (ii) would be involved in the implementation or supervision of such contract unless the conflict stemming from such relationship has been resolved in a manner acceptable to the Bank throughout the procurement process and execution of the contract.

4.3 A firm that is a Bidder (either individually or as a JV member) shall not participate in more than one Bid, except for permitted alternative Bids. This includes participation as a Subcontractor in other Bids. Such participation shall result in the disqualification of all Bids in which the firm is involved. A firm that is not a Bidder or a JV member may participate as a subcontractor in more than one Bid.

4.4 A Bidder may have the nationality of any country, subject to the restrictions pursuant to ITB 4.8. A Bidder shall be deemed to have the nationality of a country if the Bidder is constituted, incorporated or registered in and operates in conformity with the provisions of the laws of that country, as evidenced by its articles of incorporation (or equivalent documents of constitution or association) and its registration documents, as the case may be. This criterion also shall apply to the determination of the nationality of proposed subcontractors or subconsultants for any part of the Contract including related Services.

PRSWSP

4.5 A Bidder that has been sanctioned by the Bank, pursuant to the Bank's Anti-Corruption Guidelines, in accordance with its prevailing sanctions policies and procedures as set forth in the WBG's Sanctions Framework as described in Section VI paragraph 2.2 d., shall be ineligible to be prequalified for, initially selected for, bid for, propose for, or be awarded a Bank-financed contract or benefit from a Bank-financed contract, financially or otherwise, during such period of time as the Bank shall have determined. The list of debarred firms and individuals is available at the electronic address specified in the BDS.

4.6 Bidders that are state-owned enterprises or institutions in the Employer's Country may be eligible to compete and be awarded a Contract(s) only if they can establish, in a manner acceptable to the Bank, that they (i) are legally and financially autonomous (ii) operate under commercial law, and (iii) are not under supervision of the Employer.

4.7 A Bidder shall not be under suspension from Bidding by the Employer as the result of the operation of a Bid–Securing or Proposal-Securing Declaration.

4.8 Firms and individuals may be ineligible if so indicated in Section V and (a) as a matter of law or official regulations, the Borrower's country prohibits commercial relations with that country, provided that the Bank is satisfied that such exclusion does not preclude effective competition for the supply of goods or the contracting of works or services required; or (b) by an act of compliance with a decision of the United Nations Security Council taken under Chapter VII of the Charter of the United Nations, the Borrower's country prohibits any import of goods or contracting of works or services from that country, or any payments to any country, person, or entity in that country. When the Works are implemented across jurisdictional boundaries (and more than one country is a Borrower, and is involved in the procurement), then exclusion of a firm or individual on the basis of ITB 4.8 (a) above by any country may be applied to that procurement across other countries involved, if the Bank and the Borrowers involved in the procurement agree.

4.9 A Bidder shall provide such documentary evidence of eligibility satisfactory to the Employer, as the Employer shall reasonably request.

4.10 A firm that is under a sanction of debarment by the Borrower from being awarded a contract is eligible to participate in this

PRSMSP

procurement, unless the Bank, at the Borrower's request, is satisfied that the debarment;

(a) relates to fraud or corruption, and

(b) followed a judicial or administrative proceeding that afforded the firm adequate due process.

5. Eligible Materials, Equipment and Services

5.1 The materials, equipment and services to be supplied under the Contract and financed by the Bank may have their origin in any country subject to the restrictions specified in Section V, Eligible Countries, and all expenditures under the Contract will not contravene such restrictions. At the Employer's request, Bidders may be required to provide evidence of the origin of materials, equipment and services.

B. Contents of Bidding Document

6. Sections of Bidding Document

6.1 The bidding document consists of Parts 1, 2, and3, which include all the sections specified below, and which should be read in conjunction with any Addenda issued in accordance with ITB 8.

PART 1 Bidding Procedures

- Section I - Instructions to Bidders (ITB)
- Section II - Bid Data Sheet (BDS)
- Section III - Evaluation and Qualification Criteria
- Section IV - Bidding Forms
- Section V - Eligible Countries
- Section VI - Fraud and Corruption

PART 2 Works' Requirements

- Section VII- Works' Requirements

PART 3 Conditions of Contract and Contract Forms

- Section VIII - General Conditions of Contract (GCC)
- Section IX - Particular Conditions of Contract (PCC)
- Section X - Contract Forms

6.2 The Specific Procurement Notice - Request for Bids (RFB) issued by the Employer is not part of this bidding document.

6.3 Unless obtained directly from the Employer, the Employer is not responsible for the completeness of the bidding document,

PRSWSP

responses to requests for clarification, the minutes of the pre-Bid meeting (if any), or Addenda to the bidding document in accordance with ITB 8. In case of any contradiction, documents obtained directly from the Employer shall prevail.

6.4 The Bidder is expected to examine all instructions, forms, terms, and specifications in the bidding document and to furnish with its Bid all information and documentation as is required by the bidding document.

7. Clarification of Bidding Document, Site Visit, Pre-Bid Meeting

7.1 A Bidder requiring any clarification of the bidding document shall contact the Employer in writing at the Employer's address specified **in the BDS** or raise its inquiries during the pre-Bid meeting if provided for in accordance with ITB 7.4. The Employer will respond in writing to any request for clarification, provided that such request is received prior to the deadline for submission of Bids within a period specified **in the BDS**. The Employer shall forward copies of its response to all Bidders who have acquired the bidding document in accordance with ITB 6.3, including a description of the inquiry but without identifying its source. If so specified **in the BDS**, the Employer shall also promptly publish its response at the web page identified in the BDS. Should the clarification result in changes to the essential elements of the bidding document, the Employer shall amend the bidding document following the procedure under ITB 8 and ITB 22.2.

7.2 The Bidder is advised to visit and examine the Site of Works and its surroundings and obtain for itself on its own responsibility all information that may be necessary for preparing the bid and entering into a contract for construction of the Works. The costs of visiting the Site shall be at the Bidder's own expense.

7.3 The Bidder and any of its personnel or agents will be granted permission by the Employer to enter upon its premises and lands for the purpose of such visit, but only upon the express condition that the Bidder, its personnel, and agents will release and indemnify the Employer and its personnel and agents from and against all liability in respect thereof, and will be responsible for death or personal injury, loss of or damage to property, and any other loss, damage, costs, and expenses incurred as a result of the inspection.

7.4 If so specified **in the BDS**, the Bidder's designated representative is invited to attend a pre-Bid meeting and/or a Site of Works visit. The purpose of the meeting will be to clarify issues and to answer questions on any matter that may be raised at that stage.

PRSWCSP

7.5 The Bidder is requested, to submit any questions in writing, to reach the Employer not later than one week before the meeting.

7.6 Minutes of the pre-Bid meeting, if applicable, including the text of the questions asked by Bidders, without identifying the source, and the responses given, together with any responses prepared after the meeting, will be transmitted promptly to all Bidders who have acquired the bidding document in accordance with ITB 6.3 Any modification to the bidding document that may become necessary as a result of the pre-Bid meeting shall be made by the Employer exclusively through the issue of an addendum pursuant to ITB 8 and not through the minutes of the pre-Bid meeting. Nonattendance at the pre-Bid meeting will not be a cause for disqualification of a Bidder.

8. Amendment of Bidding Document

8.1 At any time prior to the deadline for submission of bids, the Employer may amend the bidding document by issuing addenda.

8.2 Any addendum issued shall be part of the bidding document and shall be communicated in writing to all who have obtained the bidding document from the Employer in accordance with ITB 6. The Employer shall also promptly publish the addendum on the Employer's web page in accordance with ITB 7.1.

8.3 To give prospective Bidders reasonable time in which to take an addendum into account in preparing their Bids, the Employer may, at its discretion, extend the deadline for the submission of Bids, pursuant to ITB 22.2.

C. Preparation of Bids

9. Cost of Bidding

9.1 The Bidder shall bear all costs associated with the preparation and submission of its Bid, and the Employer shall in no case be responsible or liable for those costs, regardless of the conduct or outcome of the Bidding process.

10. Language of Bid

10.1 The Bid, as well as all correspondence and documents relating to the Bid exchanged by the Bidder and the Employer, shall be written in the language specified **in the BDS**. Supporting documents and printed literature that are part of the Bid may be in another language provided they are accompanied by an accurate translation of the relevant passages in the language specified **in the BDS**, in which case, for purposes of interpretation of the Bid, such translation shall govern.

PRSWCSP

11. Documents Comprising the Bid

11.1 The Bid shall comprise the following:

(a) **Letter of Bid** prepared in accordance with ITB 12;

(b) **Bill of Quantities or Activity Schedule**: completed in accordance with ITB 12 and ITB 14, as specified **in the BDS**;

(c) **Bid Security or Bid-Securing Declaration**, in accordance with ITB 19.1;

(d) **Alternative Bid**, if permissible, in accordance with ITB 13;

(e) **Authorization:** written confirmation authorizing the signatory of the Bid to commit the Bidder, in accordance with ITB 20.3;

(f) **Bidder's Eligibility:** documentary evidence in accordance with ITB 17 establishing the Bidder's eligibility to Bid;

(g) **Qualifications**: documentary evidence in accordance with ITB 17 establishing the Bidder's qualifications to perform the contract if its Bid is accepted;

(h) **Conformity**: a technical proposal in accordance with ITB 16;

(i) any other document required **in the BDS**.

11.2 In addition to the requirements under ITB 11.1, Bids submitted by a JV shall include a copy of the Joint Venture Agreement entered into by all members. Alternatively, a letter of intent to execute a Joint Venture Agreement in the event of a successful bid shall be signed by all members and submitted with the Bid, together with a copy of the proposed Agreement.

11.3 The Bidder shall furnish in the Letter of Bid information on commissions and gratuities, if any, paid or to be paid to agents or any other party relating to this Bid.

12. Letter of Bid and Schedules

12.1 The Letter of Bid and Schedules shall be prepared using the relevant forms furnished in Section IV, Bidding Forms. The forms must be completed without any alterations to the text, and no substitutes shall be accepted except as provided under ITB 20.3. All blank spaces shall be filled in with the information requested.

13. Alternative Bids

13.1 Unless otherwise specified **in the BDS**, alternative Bids shall not be considered.

13.2 When alternative times for completion are explicitly invited, a statement to that effect will be included **in the BDS** and the method of evaluating different alternative times for completion will be described in Section III, Evaluation and Qualification Criteria.

PROVISO

13.3 Except as provided under ITB 13.4 below, Bidders wishing to offer technical alternatives to the requirements of the bidding document must first price the Employer's design as described in the bidding document and shall further provide all information necessary for a complete evaluation of the alternative by the Employer, including drawings, design calculations, technical specifications, breakdown of prices, and proposed construction methodology and other relevant details. Only the technical alternatives, if any, of the Bidder with the Most Advantageous Bid conforming to the basic technical requirements shall be considered by the Employer.

13.4 When specified **in the BDS**, Bidders are permitted to submit alternative technical solutions for specified parts of the Works. Such parts will be identified **in the BDS** and described in Section VII, Works 'Requirements. The method for their evaluation will be stipulated in Section III, Evaluation and Qualification Criteria.

14. Bid Prices and Discounts

14.1 The prices and discounts quoted by the Bidder in the Letter of Bid and in the Activity Schedule or Bill of Quantities shall conform to the requirements specified below.

14.2 The Bidder shall submit a Bid for the whole of the Works described in ITB 1.1 by filling in prices for all items of the Works, as identified in Section IV. Bidding Forms. In case of admeasurement contracts, the Bidder shall fill in rates and prices for all items of the Works described in the Bill of Quantities. Items against which no rate or price is entered by the Bidder will not be paid for by the Employer when executed and shall be deemed covered by the rates for other items and prices in the Bill of Quantities.

14.3 The price to be quoted in the Letter of Bid,in accordance with ITB 12.1, shall be the total price of the Bid, excluding any discounts offered.

14.4 The Bidder shall quote any discounts and indicate the methodology for their application in the Letter of Bidin accordance with ITB 12.1.

14.5 Unless otherwise specified **in the BD S**and the Conditions of Contract, the prices quoted by the Bidder shall be fixed. If the prices quoted by the Bidder are subject to adjustment during the performance of the Contract in accordance with the provisions of the Conditions of Contract, the Bidder shall furnish the indices and weightings for the price adjustment formulae in the Schedule of Adjustment Data in Section IV- Bidding Forms and the Employer may require the Bidder to justify its proposed indices and weightings.

PRIVATE

14.6 If so specified in ITB 1.1, Bids are invited for individual lots (contracts)or for any combination of lots (packages). Bidders wishing to offer discounts for the award of more than one Contract shall specify in their Bid the price reductions applicable to each package, or alternatively, to individual Contracts within the package. Discounts shall be submitted in accordance with ITB 14.4, provided the Bids for all lots (contracts) are opened at the same time.

14.7 All duties, taxes, and other levies payable by the Contractor under the Contract, or for any other cause, as of the date 28 days prior to the deadline for submission of Bids, shall be included in the rates and prices[1] and the total Bid price submitted by the Bidder.

15. Currencies of Bid and Payment

15.1 The currency(ies) of the Bid and the currency(ies) of payments shall be in Pak Rupees.

15.2 However with prior agreement of Bank the bids can be invited in up to three freely convertible currencies.

15.3 Subject to 15.1 bidders may be required by the Employer to justify, to the Employer's satisfaction, their local and foreign currency requirements, and to substantiate that the amounts included in the unit rates and prices and shown in the Schedule of Adjustment Data are reasonable[2],in which case a detailed breakdown of the foreign currency requirements shall be provided by Bidders.

16. Documents Comprising the Technical Proposal

16.1 The Bidder shall furnish a technical proposal including a statement of work methods, equipment, personnel, schedule and any other information as stipulated in Section IV, Bidding Forms, in sufficient detail to demonstrate the adequacy of the Bidders' proposal to meet the work's requirements and the completion time.

17. Documents Establishing the Eligibility and Qualifications of the Bidder

17.1 To establish Bidder's eligibility in accordance with ITB 4, Bidders shall complete the Letter of Bid, included in Section IV, Bidding Forms.

17.2 In accordance with Section III, Evaluation and Qualification Criteria, to establish its qualifications to perform the Contract, the Bidder shall provide the information requested in the corresponding information sheets included in Section IV, Bidding Forms.

17.3 If a margin of preference applies as specified in accordance with ITB 33.1, domestic Bidders, individually or in joint ventures,

[1] In lump sum contracts, delete "rates and prices and the."

[2] For lump sum contracts, delete "unit rates and prices and shown in the Schedule of Adjustment Data are reasonable" and replace with "Lump Sum."

PROVISIONAL

applying for eligibility for domestic preference shall supply all information required to satisfy the criteria for eligibility specified in accordance with ITB 33.1.

18. Period of Validity of Bids

18.1 Bids shall remain valid for the Bid Validity period specified **in the BDS**. The Bid Validity period starts from the date fixed for the Bid submission deadline (as prescribed by the Employer in accordance with ITB 22.1). A Bid valid for a shorter period shall be rejected by the Employer as nonresponsive.

18.2 In exceptional circumstances, prior to the expiration of the Bid validity period, the Employer may request Bidders to extend the period of validity of their Bids. The request and the responses shall be made in writing. If a Bid Security is requested in accordance with ITB 19, it shall also be extended for twenty-eight (28) days beyond the deadline of the extended validity period. A Bidder may refuse the request without forfeiting its Bid Security. A Bidder granting the request shall not be required or permitted to modify its Bid, except as provided in ITB 18.3.

18.3 If the award is delayed by a period exceeding fifty-six (56) days beyond the expiry of the initial Bid validity period, the Contract price shall be determined as follows:

(a) in the case of **fixed price** contracts, the Contract price shall be the Bid price adjusted by the factor specified **in the BDS;**

(b) in the case of **adjustable** price contracts, no adjustment shall be made; or

(c) in any case, Bid evaluation shall be based on the Bid price without taking into consideration the applicable correction from those indicated above.

19. Bid Security

19.1 The Bidder shall furnish as part of its Bid, either a Bid-Securing Declaration or a Bid Security as specified **in the BDS**, in original form and, in the case of a Bid Security, in the amount and currency specified **in the BDS**.

19.2 A Bid Securing Declaration shall use the form included in Section IV, Bidding Forms.

19.3 If a Bid Security is specified pursuant to ITB 19.1, the Bid Security shall be a demand guarantee in any of the following forms at the Bidder's option:

PRSWSD

(a) an unconditional guarantee issued by a bank or non-bank financial institution (such as an insurance, bonding or surety company);

(b) an irrevocable letter of credit;

(c) a cashier's or certified check; or

(d) another security specified **in the BDS**,

from a reputable source from an eligible country. If an unconditional guarantee is issued by a non-bank financial institution located outside the Employer's Country, the issuing non-bank financial institution shall have a correspondent financial institution located in the Employer's Country to make it enforceable, unless the Employer has agreed in writing, prior to Bid submission, that a correspondent financial institution is not required. In the case of a bank guarantee, the Bid Security shall be submitted either using the Bid Security Form included in Section IV, Bidding Forms, or in another substantially similar format approved by the Employer prior to Bid submission. The Bid Security shall be valid for twenty-eight (28) days beyond the original validity period of the Bid, or beyond any period of extension if requested under ITB 18.2.

19.4 If a Bid Security or Bid Securing Declaration is specified pursuant to ITB 19.1, any Bid not accompanied by a substantially responsive Bid Security or Bid-Securing Declaration shall be rejected by the Employer as non-responsive.

19.5 If a Bid Security is specified pursuant to ITB 19.1, the Bid Security of unsuccessful Bidders shall be returned as promptly as possible upon the successful Bidder's signing the Contract and furnishing the Performance Security and if required in the BDS, the Environmental, Social, Health and Safety (ESHS) Performance Security pursuant to ITB 48.

19.6 The Bid Security of the successful Bidder shall be returned as promptly as possible once the successful Bidder has signed the Contract and furnished the required Performance Security and if required in the BDS, the Environmental, Social, Health and Safety (ESHS) Performance Security.

19.7 The Bid Security may be forfeited or the Bid-Securing Declaration executed:

PROVIDED

(a) if a Bidder withdraws its Bid during the period of Bid validity specified by the Bidder on the Letter of Bid, or any extension thereto provided by the Bidder; or

(b) if the successful Bidder fails to:

(i) sign the Contract in accordance with ITB 47; or

(ii) furnish a Performance Security and if required in the BDS, the Environmental, Social, Health and Safety (ESHS) Performance Security in accordance with ITB 48.

19.8 The Bid Security or the Bid-Securing Declaration of a JV shall be in the name of the JV that submits the Bid. If the JV has not been constituted into a legally enforceable JV, at the time of Bidding, the Bid Security or the Bid-Securing Declaration shall be in the names of all future members as named in the letter of intent mentioned in ITB 4.1 and ITB 11.2.

19.9 If a Bid Security is not required **in the BDS**, pursuant to ITB 19.1, and;

(a) if a Bidder withdraws its Bid during the period of Bid validity specified by the Bidder on the Letter of Bid; or

(b) if the successful Bidder fails to: sign the Contract in accordance with ITB 45, or furnish a Performance Security and if required in the BDS, the Environmental, Social, Health and Safety (ESHS) Performance Security in accordance with ITB 46;

the Borrower may**,** if provided for **in the BDS,** declare the Bidder ineligible to be awarded a contract by the Employer for a period of time stated **in the BDS**.

20. Format and Signing of Bid

20.1 The Bidder shall prepare one original of the documents comprising the Bid as described in ITB 11 and clearly mark it "ORIGINAL". Alternative Bids, if permitted in accordance with ITB 13, shall be clearly marked "ALTERNATIVE". In addition, the Bidder shall submit copies of the Bid in the number specified **in the BDS,** and clearly mark each of them "COPY." In the event of any discrepancy between the original and the copies, the original shall prevail.

20.2 Bidders shall mark as "CONFIDENTIAL" information in their Bids which is confidential to their business. This may include proprietary information, trade secrets, or commercial or financially sensitive information.

PRSNSD

20.3 The original and all copies of the Bid shall be typed or written in indelible ink and shall be signed by a person duly authorized to sign on behalf of the Bidder. This authorization shall consist of a written confirmation as specified **in the BDS** and shall be attached to the Bid. The name and position held by each person signing the authorization must be typed or printed below the signature. All pages of the Bid where entries or amendments have been made shall be signed or initialed by the person signing the Bid.

20.4 In case the Bidder is a JV, the Bid shall be signed by an authorized representative of the JV on behalf of the JV, and so as to be legally binding on all the members as evidenced by a power of attorney signed by their legally authorized representatives.

20.5 Any interlineations, erasures, or overwriting shall be valid only if they are signed or initialed by the person signing the Bid.

D. Submission and Opening of Bids

21. Sealing and Marking of Bids

21.1 The Bidder shall deliver the Bid in a single, sealed envelope (one-envelope Bidding process). Within the single envelope the Bidder shall place the following separate, sealed envelopes:

(a) in an envelope marked "ORIGINAL", all documents comprising the Bid, as described in ITB 11; and

(b) in an envelope marked "COPIES", all required copies of the Bid; and

(c) if alternative Bids are permitted in accordance with ITB 13, and if relevant:

(i) in an envelope marked "ORIGINAL- ALTERNATIVE BID", the alternative Bid; and

(ii) in the enveloped marked "COPIES – ALTERNATIVE BID" all required copies of the alternative Bid.

21.2 The inner and outer envelopes shall:

(a) bear the name and address of the Bidder;

(b) be addressed to the Employer in accordance with ITB 22.1;

(c) bear the specific identification of this Bidding process specified in accordance with BDS 1.1; and

PRSWSD

(d) bear a warning not to open before the time and date for Bid opening.

21.3 If all envelopes are not sealed and marked as required, the Employer will assume no responsibility for the misplacement or premature opening of the Bid.

22. Deadline for Submission of Bids

22.1 Bids must be received by the Employer at the address and no later than the date and time specified **in the BDS**. When so specified **in the BDS**, Bidders shall have the option of submitting their Bids electronically. Bidders submitting Bids electronically shall follow the electronic bid submission procedures specified **in the BDS.**

22.2 The Employer may, at its discretion, extend the deadline for the submission of Bids by amending the bidding document in accordance with ITB 8, in which case all rights and obligations of the Employer and Bidders previously subject to the deadline shall thereafter be subject to the deadline as extended.

23. Late Bids

23.1 The Employer shall not consider any Bid that arrives after the deadline for submission of Bids, in accordance with ITB 22. Any Bid received by the Employer after the deadline for submission of Bids shall be declared late, rejected, and returned unopened to the Bidder.

24. Withdrawal, Substitution, and Modification of Bids

24.1 A Bidder may withdraw, substitute, or modify its Bid after it has been submitted by sending a written notice, duly signed by an authorized representative, and shall include a copy of the authorization in accordance with ITB 20.3, (except that withdrawal notices do not require copies). The corresponding substitution or modification of the Bid must accompany the respective written notice. All notices must be:

(a) prepared and submitted in accordance with ITB 20 and ITB 21 (except that withdrawal notices do not require copies), and in addition, the respective envelopes shall be clearly marked "WITHDRAWAL," "SUBSTITUTION," "MODIFICATION"; and

(b) received by the Employer prior to the deadline prescribed for submission of Bids, in accordance with ITB 22.

24.2 Bids requested to be withdrawn in accordance with ITB 24.1 shall be returned unopened to the Bidders.

24.3 No Bid may be withdrawn, substituted, or modified in the interval between the deadline for submission of Bids and the expiration of the period of Bid validity specified by the Bidder on the Letter of Bid or any extension thereof.

PRVCSD

25. Bid Opening

25.1 Except in the cases specified in ITB 23 and ITB 24.2, the Employer shall publicly open and read out in accordance with this ITB, all Bids received by the deadline, at the date, time and place specified **in the BDS**, in the presence of Bidders' designated representatives and anyone who chooses to attend. All Bidders, or their representatives and any interested party may attend a public opening. Any specific electronic Bid opening procedures required if electronic bidding is permitted in accordance with ITB 22.1, shall be as specified **in the BDS**.

25.2 First, envelopes marked "WITHDRAWAL" shall be opened and read out and the envelope with the corresponding Bid shall not be opened, but returned to the Bidder. No Bid withdrawal shall be permitted unless the corresponding withdrawal notice contains a valid authorization to request the withdrawal and is read out at Bid opening.

25.3 Next, envelopes marked "SUBSTITUTION" shall be opened and read out and exchanged with the corresponding Bid being substituted, and the substituted Bid shall not be opened, but returned to the Bidder. No Bid substitution shall be permitted unless the corresponding substitution notice contains a valid authorization to request the substitution and is read out at Bid opening.

25.4 Next, envelopes marked "MODIFICATION" shall be opened and read out with the corresponding Bid. No Bid modification shall be permitted unless the corresponding modification notice contains a valid authorization to request the modification and is read out at bid opening.

25.5 Next, all remaining envelopes shall be opened one at a time, reading out: the name of the Bidder and whether there is a modification; the total Bid Price, per lot (contract) if applicable, including any discounts and alternative Bids; the presence or absence of a Bid Security, or Bid Securing Declaration, if required; and any other details as the Employer may consider appropriate.

25.6 Only Bids, alternative Bids and discounts that are opened and read out at Bid opening shall be considered further for evaluation. The Letter of Bid underpriced Schedules are to be initialed by representatives of the Employer attending Bid opening in the manner specified **in the BDS**.

25.7 The Employer shall neither discuss the merits of any Bid nor reject any Bid (except for late Bids, in accordance with ITB 23.1).

25.8 The Employer shall prepare a record of the Bid opening that shall include, as a minimum:

PRSWSD

(a) the name of the Bidder and whether there is a withdrawal, substitution, or modification;

(b) the Bid Price, per lot (contract) if applicable, including any discounts;

(c) the presence or absence of a Bid Security or Bid-Securing Declaration, if one was required; and

(d) any alternative Bids.

25.9 The Bidders' representatives who are present shall be requested to sign the record. The omission of a Bidder's signature on the record shall not invalidate the contents and effect of the record. A copy of the record shall be distributed to all Bidders.

E. Evaluation and Comparison of Bids

26. Confidentiality

26.1 Information relating to the evaluation of Bids and recommendation of contract award, shall not be disclosed to Bidders or any other persons not officially concerned with the Bidding process until information on Intention to Award the Contract is transmitted to all Bidders in accordance with ITB 43.

26.2 Any effort by a Bidder to influence the Employer in the evaluation of the Bids or Contract award decisions may result in the rejection of its Bid.

26.3 Notwithstanding ITB 26.2, from the time of Bid opening to the time of Contract award, if a Bidder wishes to contact the Employer on any matter related to the Bidding process, it shall do so in writing.

27. Clarification of Bids

27.1 To assist in the examination, evaluation, and comparison of the Bids, and qualification of the Bidders, the Employer may, at its discretion, ask any Bidder for a clarification of its Bid given a reasonable time for a response. Any clarification submitted by a Bidder that is not in response to a request by the Employer shall not be considered. The Employer's request for clarification and the response shall be in writing. No change, including any voluntary increase or decrease in the prices or substance of the Bid shall be sought, offered, or permitted, except to confirm the correction of arithmetic errors discovered by the Employer in the evaluation of the Bids, in accordance with ITB 31.

PRSWSP

27.2 If a Bidder does not provide clarifications of its Bid by the date and time set in the Employer's request for clarification, its Bid may be rejected.

28. Deviations, Reservations, and Omissions

28.1 During the evaluation of Bids, the following definitions apply:

(a) "Deviation" is a departure from the requirements specified in the bidding document;

(b) "Reservation" is the setting of limiting conditions or withholding from complete acceptance of the requirements specified in the bidding document; and

(c) "Omission" is the failure to submit part or all of the information or documentation required in the bidding document.

29. Determination of Responsiveness

29.1 The Employer's determination of a Bid's responsiveness is to be based on the contents of the Bid itself, as defined in ITB11.

29.2 A substantially responsive Bid is one that meets the requirements of the bidding document without material deviation, reservation, or omission. A material deviation, reservation, or omission is one that:

(a) if accepted, would:

(i) affect in any substantial way the scope, quality, or performance of the Works specified in the Contract; or

(ii) limit in any substantial way, inconsistent with the bidding document, the Employer's rights or the Bidder's obligations under the proposed Contract; or

(b) if rectified, would unfairly affect the competitive position of other Bidders presenting substantially responsive Bids.

29.3 The Employer shall examine the technical aspects of the Bid submitted in accordance with ITB 16, in particular, to confirm that all requirements of Section VII, Works' Requirements have been met without any material deviation, reservation or omission.

29.4 If a Bid is not substantially responsive to the requirements of the bidding document, it shall be rejected by the Employer and may not subsequently be made responsive by correction of the material deviation, reservation, or omission.

30. Nonmaterial Nonconformities

30.1 Provided that a Bid is substantially responsive, the Employer may waive any nonconformities in the Bid.

PRSWSP

30.2 Provided that a Bid is substantially responsive, the Employer may request that the Bidder submit the necessary information or documentation, within a reasonable period of time, to rectify nonmaterial nonconformities in the Bid related to documentation requirements. Requesting information or documentation on such nonconformities shall not be related to any aspect of the price of the Bid. Failure of the Bidder to comply with the request may result in the rejection of its Bid.

30.3 Provided that a Bid is substantially responsive, the Employer shall rectify quantifiable nonmaterial nonconformities related to the Bid Price. To this effect, the Bid Price shall be adjusted, for comparison purposes only, to reflect the price of a missing or nonconforming item or component in the manner specified **in the BDS**.

31. Correction of Arithmetical Errors

31.1 Provided that the Bid is substantially responsive, the Employer shall correct arithmetical errors on the following basis:

(a) only for admeasurement contracts, if there is a discrepancy between the unit price and the total price that is obtained by multiplying the unit price and quantity, the unit price shall prevail and the total price shall be corrected, unless in the opinion of the Employer there is an obvious misplacement of the decimal point in the unit price, in which case the total price as quoted shall govern and the unit price shall be corrected;

(b) if there is an error in a total corresponding to the addition or subtraction of subtotals, the subtotals shall prevail and the total shall be corrected; and

(c) if there is a discrepancy between words and figures, the amount in words shall prevail, unless the amount expressed in words is related to an arithmetic error, in which case the amount in figures shall prevail subject to (a) and (b) above.

31.2 Bidders shall be requested to accept correction of arithmetical errors. Failure to accept the correction in accordance with ITB 31.1, shall result in the rejection of the Bid.

32. Conversion to Single Currency

32.1 For evaluation and comparison purposes, the currency(ies) of the Bid shall be converted into a single currency as specified **in the BDS**.

PRSWSP

33. Margin of Preference

33.1 Unless otherwise specified **in the BDS,** a margin of preference for domestic Bidders[3] shall not apply.

34. Subcontractors

34.1 Unless otherwise stated **in the BDS**, the Employer does not intend to execute any specific elements of the Works by subcontractors selected in advance by the Employer, Financial Parts

34.2 The subcontractor's qualifications shall not be used by the Bidder to qualify for the Works unless their specialized parts of the Works were previously designated by the Employer **in the BDS** as can be met by subcontractors referred to hereafter as 'Specialized Subcontractors', in which case, the qualifications of the Specialized Subcontractors proposed by the Bidder may be added to the qualifications.

34.3 Bidders may propose subcontracting up to the percentage of total value of contracts or the volume of works as specified **in the BDS**. Subcontractors proposed by the Bidder shall be fully qualified for their parts of the Works.

35. Evaluation of Bids

35.1 The Employer shall use the criteria and methodologies listed in this ITB and Section III, Evaluation and Qualification criteria. No other evaluation criteria or methodologies shall be permitted. By applying the criteria and methodologies the Employer shall determine the Most Advantageous Bid. This is the Bid of the Bidder that meets the Qualification Criteria and whose Bid has been determined to be:

(a) substantially responsive to the bidding document; and

(b) the lowest evaluated cost.

35.2 To evaluate a Bid, the Employershall consider the following:

(a) the Bid price, excluding Provisional Sums and the provision, if any, for contingencies in the Summary Bill of Quantities[4]

[3] An individual firm is considered a domestic Bidder for purposes of the margin of preference if it is registered in the country of the Employer, has more than 50 percent ownership by nationals of the country of the Employer, and if it does not subcontract more than 10 percent of the contract price, excluding provisional sums, to foreign contractors. JVs are considered as domestic Bidders and eligible for domestic preference only if the individual member firms are registered in the country of the Employer or have more than 50 percent ownership by nationals of the country of the Employer, and the JV shall be registered in the country of the Borrower. The JV shall not subcontract more than 10 percent of the contract price, excluding provisional sums, to foreign firms. JVs between foreign and national firms will not be eligible for domestic preference.

[4] In lump sum contracts, delete "Bill of Quantities" and replace with "Activity Schedule."

PROVISIONAL

for admeasurement contracts, but including Daywork[5] items, where priced competitively;

(b) price adjustment for correction of arithmetic errors in accordance with ITB 31.1;

(c) price adjustment due to discounts offered in accordance with ITB 14.4;

(d) converting the amount resulting from applying (a) to (c) above, if relevant, to a single currency in accordance with ITB 32;

(e) price adjustment for nonconformities in accordance with ITB 30.3; and

(f) the additional evaluation factors are specified in Section III, Evaluation and Qualification Criteria.

35.3 The estimated effect of the price adjustment provisions of the Conditions of Contract, applied over the period of execution of the Contract, shall not be taken into account in Bid evaluation.

35.4 If this bidding document allows Bidders to quote separate prices for different lots (contracts), the methodology to determine the lowest evaluated cost of the contract combinations, including any discounts offered in the Letter of Bid, is specified in Section III, Evaluation and Qualification Criteria.

36. Comparison of Bids

36.1 The Employer shall compare the evaluated costs of all substantially responsive Bids established in accordance with ITB 35.2 to determine the Bid that has the lowest evaluated cost.

37. Unbalanced or Front-Loaded Bids

37.1 If the Bid for an admeasurement contract, which results in the lowest evaluated costis, in the Employer's opinion, seriously unbalanced or, front loaded, the Employer may require the Bidder to provide written clarifications. Clarifications may include detailed price analyses to demonstrate the consistency of the Bid priceas with the scope of works, proposed methodology, schedule and any other requirements of the bidding document.

[5] Daywork is work carried out following instructions of the Project Manager and paid for on the basis of time spent by workers, and the use of materials and the Contractor's equipment, at the rates quoted in the Bid. For Daywork to be priced competitively for Bid evaluation purposes, the Employer must list tentative quantities for individual items to be costed against Daywork (e.g., a specific number of tractor driver staff-days, or a specific tonnage of Portland cement), to be multiplied by the Bidders' quoted rates and included in the total Bid price.

PRSWCSP

37.2 After the evaluation of the information and detailed price analyses presented by the Bidder, the Employer may as appropriate:

(a) accept the Bid; or

(b) require that the amount of the Performance Security be increased at the expense of the Bidder to a level not exceeding 20% of the Contract Price; or

(c) reject the Bid.

38. Qualification of the Bidder

38.1 The Employer shall determine to its satisfaction whether the eligible Bidder that is selected as having submitted the lowest evaluated cost and substantially responsive Bid meets the qualifying criteria specified in Section III, Evaluation and Qualification Criteria.

38.2 The determination shall be based upon an examination of the documentary evidence of the Bidder's qualifications submitted by the Bidder, pursuant to ITB 17. The determination shall not take into consideration the qualifications of other firms such as the Bidder's subsidiaries, parent entities, affiliates, subcontractors (other than Specialized Subcontractors if permitted in the bidding document), or any other firm(s) different from the Bidder.

38.3 An affirmative determination of qualification shall be a prerequisite for award of the Contract to the Bidder. A negative determination shall result in disqualification of the Bid, in which event the Employer shall proceed to the substantially responsive Bid which offers the next lowest evaluated cost to make a similar determination of that Bidder's qualifications to perform satisfactorily.

39. Most Advantageous Bid

39.1 Having compared the evaluated costs of Bids, the Employer shall determine the Most Advantageous Bid. The Most Advantageous Bid is the Bid of the Bidder that meets the Qualification Criteria and whose Bid has been determined to be:

(a) substantially responsive to the bidding document; and

(b) the lowest evaluated cost.

40. Employer's Right to Accept Any Bid, and to Reject Any or All Bids

40.1 The Employer reserves the right to accept or reject any Bid, and to annul the Bidding process and reject all Bids at any time prior to Contract Award, without thereby incurring any liability to Bidders. In case of annulment, all Bids submitted and specifically, Bid securities, shall be promptly returned to the Bidders.

PRVISD

41. Notification of Intention to Award

41.1 The Employer shall send to each Bidder the Notification of Intention to Award the Contract to the successful Bidder. The Notification of Intention to Award shall contain, at a minimum, the following information:

(a) the name and address of the Bidder submitting the successful Bid;

(b) the Contract price of the successful Bid;

(c) the names of all Bidders who submitted Bids, and their Bid prices as readout, and as evaluated;

(d) a statement of the reason(s) the Bid (of the unsuccessful Bidder to whom the notification is addressed) was unsuccessful, unless the price information in c) above already reveals the reason;

(e) instructions on how to request a debriefing and/or submit a complaint.

F. Award of Contract

42. Award Criteria

42.1 Subject to ITB 41, the Employer shall award the Contract to the successful Bidder. This is the Bidder whose Bid has been determined to be the Most Advantageous Bid as specified in ITB 40.

43. Notification of Award

43.1 Prior to the expiration of the Bid Validity Period or any extension thereof, and, upon satisfactorily addressing any complaint that has been filed, the Employer shall notify the successful Bidder, in writing, that its Bid has been accepted. The notification of award (hereinafter and in the Conditions of Contract and Contract Forms called the "Letter of Acceptance") shall specify the sum that the Employer will pay the Contractor in consideration of the execution of the contract (hereinafter and in the Conditions of Contract and Contract Forms called "the Contract Price").

43.2 Within ten (10) Business Days after the date of transmission of the Letter of Acceptance, the Employer shall publish the Contract Award Notice which shall contain, at a minimum, the following information:

(a) name and address of the Employer;

(b) name and reference number of the contract being awarded, and the selection method used;

(c) names of all Bidders that submitted Bids, and their Bid prices as read out at Bid opening, and as evaluated;

PRSWSD

(d) names of all Bidders whose Bids were rejected either as nonresponsive or as not meeting qualification criteria, or were not evaluated, with the reasons therefor;

(e) the name of the successful Bidder, the final total contract price, the contract duration and a summary of its scope; and

(f) successful Bidder's Beneficial Ownership Disclosure Form, if specified in BDS ITB 47.1.

43.3 The Contract Award Notice shall be published on the Employer's website with free access if available, or in at least one newspaper of national circulation in the Employer's Country, or in the official gazette. The Employer shall also publish the contract award notice in UNDB online.

43.4 Until a formal contract is prepared and executed, the Letter of Acceptance shall constitute a binding Contract.

44. Debriefing by the Employer

44.1 On receipt of the Employer's Notification of Intention to Award referred to in ITB 43.1, an unsuccessful Bidder has three (3) Business Days to make a written request to the Employer for a debriefing. The Employer shall provide a debriefing to all unsuccessful Bidders whose request is received within this deadline.

44.2 Where a request for debriefing is received within the deadline, the Employer shall provide a debriefing within five (5) Business Days, unless the Employer decides, for justifiable reasons, to provide the debriefing outside this timeframe.

44.3 Where a request for debriefing is received by the Employer later than the three (3)-Business Day deadline, the Employer should provide the debriefing as soon as practicable, and normally no later than fifteen (15) Business Days from the date of publication of Public Notice of Award of contract.

44.4 Debriefings of unsuccessful Bidders may be done in writing or verbally. The Bidder shall bear their own costs of attending such a debriefing meeting.

45. Signing of Contract

45.1 The Employer shall send to the successful Bidder the Letter of Acceptance including the Contract Agreement, and, if specified in the BDS, a request to submit the Beneficial Ownership Disclosure Form providing additional information on its beneficial ownership. The Beneficial Ownership Disclosure Form, if so requested, shall be submitted within eight (8) Business Days of receiving this request.

PROVISP

45.2 The successful Bidder shall sign, date and return to the Employer, the Contract Agreement within twenty-eight (28) days of its receipt.

46. Performance Security

46.1 Within twenty-eight (28) days of the receipt of the Letter of Acceptance from the Employer, the successful Bidder shall furnish the Performance Security and, if required in the BDS, the Environmental, Social, Health and Safety (ESHS) Performance Security in accordance with the General Conditions of Contract, subject to ITB 38.2 (b), using for that purpose the Performance Security and ESHS Performance Security Forms included in Section X, Contract Forms, or another form acceptable to the Employer. If the Performance Security furnished by the successful Bidder is in the form of a bond, it shall be issued by a bonding or insurance company that has been determined by the successful Bidder to be acceptable to the Employer. A foreign institution providing a bond shall have a correspondent financial institution located in the Employer's Country, unless the Employer has agreed in writing that a correspondent financial institution is not required.

46.2 Failure of the successful Bidder to submit the above-mentioned Performance Security and, if required in the BDS, the Environmental, Social, Health and Safety (ESHS) Performance Security, or to sign the Contract Agreement shall constitute sufficient grounds for the annulment of the award and forfeiture of the Bid Security. In that event the Employer may award the Contract to the Bidder offering the next Most Advantageous Bid.

47. Adjudicator

47.1 The Employer proposes the person named **in the BDS** to be appointed as Adjudicator under the Contract, at the hourly fee specified **in the BDS**, plus reimbursable expenses. If the Bidder disagrees with this proposal, the Bidder should so state in his Bid. If, in the Letter of Acceptance, the Employer does not agree on the appointment of the Adjudicator, the Employer will request the Appointing Authority designated in the Particular Conditions of Contract (PCC) pursuant to Clause 23.1 of the General Conditions of Contract (GCC), to appoint the Adjudicator.

48. Procurement Related Complaint

48.1 The procedures for making a Procurement-related Complaint are as specified in the BDS.

PROVISIONAL

Section II - Bid Data Sheet (BDS)

The following specific data for the Works to be procured shall complement, supplement, or amend the provisions in the Instructions to Bidders (ITB). Whenever there is a conflict, the provisions herein shall prevail over those in ITB.

ITB Reference	A. General
ITB 1.1	The Employer is: **Punjab Rural Municipal Services Company (PRMSC)** The reference number of the Request for Bids (RFB) is: **PK-LG& CD-559576-CW-RFB** The name of the RFB is: **Civil Works under PRSWSSP, Tehsil Bahawalnagar, Cluster South-III (Bahawalnagar-29) (CW-25)**
ITB 1.2(a)	**Electronic –Procurement System** Not Used
ITB 2.1	The Borrower is: Government of Islamic Republic of Pakistan (who has extended the financing to Punjab Rural Municipal Services Company) Loan Agreement amount: US$ 442.40Million The name of the Project is: **Punjab Rural Sustainable Water Supply and Sanitation Project**
ITB 4.1	Maximum number of members in the Joint Venture (JV) shall be: Three (03)
ITB 4.5	A list of debarred firms and individuals is available on the Bank's external website: http://www.worldbank.org/debarr.
	The following new Sub-Clauses are added at the end of ITB 4: "The Bidder shall also meet the following eligibility requirements: ITB 4.11 If Bidder is not registered at the time of submission of its Bid, s/he shall be required to register its firm with the respective Tax Entity(s) and Pakistan Engineering Council in the appropriate category and specialization code CE-09, CE-10 prior to the signing of Contract.
B. Contents of Bidding Document	

PRWSSP

<table>
<tr><td>ITB 7.1</td><td>For <u>Clarification of Bid purposes</u> only, the Employer’s address is:
Attention: Chief Executive Officer, PRMSC
Address: Punjab Rural Municipal Services Company (PRMSC)
5th Floor, KD Plaza, MM Alam Road, Gulberg-III, Lahore, Pakistan
Telephone: +92-42-99333613
Electronic mail address: proc.prmsc@punjab.gov.pk</td></tr>
<tr><td>ITB 7.1</td><td>Requests for clarification should be received by the Employer no later than: 07 days</td></tr>
<tr><td>ITB 7.1</td><td>Web page: https://prmsc.punjab.gov.pk</td></tr>
<tr><td>ITB 7.4</td><td>A Pre-Bid meeting shall take place, if so required, at the following date, time and place:

Conference Room: Punjab Rural Municipal Services Company (PRMSC)
5th Floor, KD Plaza, MM Alam Road, Gulberg-III, Lahore, Pakistan
Telephone: +92-42-99333613
Electronic mail address: Proc.prmsc@punjab.gov.pk

Maximum two (02) representatives of a bidder, will be allowed. Further, for ease of bidder, the bidder can attend the pre-bid meeting online at the following zoom link;
<table>
<tr><td>Topic:</td><td>Pre-Bid Civil Works Meeting</td></tr>
<tr><td>Date:</td><td>July 16, 2026</td></tr>
<tr><td>Time:</td><td>01:00 pm</td></tr>
<tr><td>Zoom Link:</td><td>https://us06web.zoom.us/j/86422148825?pwd=LMRbMKY1LS6gOcGccfCiiNxC4WIAOh.1</td></tr>
<tr><td>Meeting ID:</td><td>811 2002 3773</td></tr>
<tr><td>Passcode:</td><td>095698</td></tr>
</table>
A site visit conducted by the Employer shall not be organized.</td></tr>
<tr><td colspan="2">C. Preparation of Bids</td></tr>
<tr><td>ITB 10.1</td><td>Language of the Bid: English
All correspondence exchange shall be in English language.
Language for translation of supporting documents and printed literature is English.</td></tr>
<tr><td>ITB 11.1 (b)</td><td>The following schedules shall be submitted with the Bid:</td></tr>
</table>

PRMSD

	Bill of Quantities as required in accordance with the Bidding Document
ITB 11.1 (i)	The Bidder shall submit the following additional documents in its Bid: • Registration of the firm with concerned authority for doing business • **Code of Conduct (ESHS)** The Bidder shall submit its Code of Conduct that will apply to its employees and subcontractors, to ensure compliance with its Environmental, Social, Health and Safety (ESHS) obligations under the contract that will include the following requirements, e.g. risks associated with: labor influx, spread of communicable diseases, sexual harassment, gender based violence, sexual exploitation and abuse, illicit behavior and crime, and maintaining a safe environment etc. In addition, the Bidder shall detail how this Code of Conduct will be implemented. This will include: how it will be introduced into conditions of employment/engagement, what training will be provided, how it will be monitored and how the Contractor proposes to deal with any breaches. The Contractor shall be required to implement the agreed Code of Conduct. • **Management Strategies and Implementation Plans (MSIP) to Manage the (ESHS) Risks** The Bidder shall submit Management Strategies and Implementation Plans (MSIP) to manage the following key Environmental, Social, Health and Safety (ESHS) risks. ▪ Traffic Management Plan to ensure safety of local communities from construction traffic; ▪ Water Resource Protection Plan to prevent contamination of drinking water; ▪ Boundary Marking and Protection Strategy for mobilization and construction to prevent offsite adverse impacts; ▪ Strategy for obtaining Consents/Permits prior to the start of relevant works such as opening a quarry or borrow pit, if so required; ▪ Gender based violence and sexual exploitation and abuse (GBV/SEA) prevention and response action plan. The Contractor shall be required to submit for approval, and subsequently implement, the Contractor's Environment and Social Management Plans (C-ESMP), in accordance with the Particular Conditions of Contract Sub-Clause 16.2, that includes the agreed Management Strategies and Implementation Plans described here. The Bidder shall also submit the additional documents as per specified requirements of the Bidding Document.
ITB 13.1	Alternative Bids shall not be considered.
ITB 13.2	Alternative times for completion shall not be permitted.

PPWSP

ITB 13.4	Alternative technical solutions shall not be permitted for the Works.
ITB 14.5	The prices quoted by the Bidder shall be subject to adjustment during the performance of the Contract.
ITB 15.1	The price shall be quoted by the Bidder in: Pak Rupees only. All payments under the Contract shall be made in Pak Rupees only. A Bidder expecting to incur expenditures in other currencies for inputs to the Works supplied from outside the Employer's Country shall bear all costs and risks for arranging such currencies including currency exchange rate parity.
ITB 15.2	Not Applicable
ITB 15.3	Not Applicable
ITB 18.1	The Bid validity period shall be 120 days.
ITB 18.3 (a)	The Bid price shall be adjusted by the following factor(s): Not Applicable
ITB 19.1	A Bid Security shall be required, in the shape of unconditional Bank Guarantee or Call Deposit Receipt (CDR) duly supported by undertaking provided in the Bidding Document. A Bid-Securing Declaration shall not be required. The amount and currency of the Bid Security shall be **PKR 36,000,000/- (Pak Rupees Thirty-six Million Only)**
ITB 19.3	The text of ITB 19.3 is substituted with the following: "The Bid Security shall be in the form of unconditional Bank Guarantee or Call Deposit Receipt (CDR) issued by a Scheduled Bank in Pakistan using the Bid Security Form included in Section IV, Bidding Forms, in favour of the **Punjab Rural Municipal Services Company** valid for a period of 28 days beyond the original validity period of the Bid, or beyond any period of extension if requested under ITB 18.2."
ITB 19.8	In case of Joint Venture, the Bid Security shall be in the name of the Joint Venture or in the name of any JV member.
ITB 19.9	Not Applicable
ITB 20.1	In addition to the original of the Bid, the number of copies is**:** One (01) The Bidders shall also submit the PDF copy of the entire Bid and **Word/Excel** copy of the technical and financial parts of Bid on a USB device, which is mandatory. ***In case of non-compliance, the bid may be declared as non-Responsive.***
ITB 20.3	***In case the bid is not typed or written in indelible ink, the bid may be declared as non-Responsive.***

PPRA SBD

	The written confirmation of authorization to sign on behalf of the Bidder shall consist of**:** An Authority Letter in original issued by the Bidder duly signed and stamped.
D. Submission and Opening of Bids	
ITB 22.1	For **Bid submission purposes** only, the Purchaser's address is: Attention: Chief Executive Officer Address: Punjab Rural Municipal Services Company (PRMSC) 5th Floor, KD Plaza, MM Alam Road, Gulberg-III, Lahore, Pakistan The deadline for Bid submission is: **Date: August 04, 2026 Time: 1500 hours** **Bidders shall not have the option of submitting their Bids electronically.**
ITB 25.1	The Bid opening shall take place at: Conference Room Punjab Rural Municipal Services Company (PRMSC) 5th Floor, KD Plaza, MM Alam Road, Gulberg-III, Lahore, Pakistan **Date: August 04, 2026 Time: 1530 hours**
ITB 25.1	Bidders shall not have the option of submitting their Bids electronically.
ITB 25.6	The Letter of Bid and priced Summary of Bill of Quantities shall be initialed by all representatives of the Employer conducting Bid opening.
E. Evaluation and Comparison of Bids	
ITB 30.3	The adjustment shall be based on the average price of the item or component as quoted in other substantially responsive Bids. If the price of the item or component cannot be derived from the price of other substantially responsive Bids, the Employer shall use its best estimate.
ITB 32.1	Not Applicable
ITB 33.1	A margin of domestic preference shall not apply.
ITB 34.1	At this time the Employer does not intend to execute certain specific parts of the Works by subcontractors selected in advance.
ITB 34.2	Not Applicable

PRMSP

ITB 34.3	Contractor's proposed subcontracting: Maximum percentage of subcontracting permitted is 10% of the Accepted Contract Amount excluding the Provisional Sums.
F. Award of Contract	
ITB 45.1	The successful Bidder shall submit the Beneficial Ownership Disclosure Form.
ITB 46.1 and 46.2	The successful Bidder shall be required to submit the Performance Security only in accordance with the Conditions of Contract.
ITB 47.1	The Adjudicator and its hourly fee shall be mutually agreed at the time of finalization of the Adjudicator in accordance with GCC 23.1.
ITB 48.1	The procedures for making a Procurement-related Complaint are detailed in the "Procurement Regulations for IPF Borrowers (Annex III)." If a Bidder wishes to make a Procurement-related Complaint, the Bidder should submit its complaint following these procedures, in writing (by the quickest means available, that is either by email or fax), to: Attention: **PRMSC GRIEVANCES REDRESSAL MECHANISM COMMITTEE** 5th Floor, KD Plaza, MM Alam Road, Gulberg-III, Lahore, Pakistan (Off): +92(42)99333610 In summary, a Procurement-related Complaint may challenge any of the following: **1.** the terms of the Bidding Documents; and **2.** the Employer's decision to award the Contract.

PRSMSP

Section III - Evaluation and Qualification Criteria

This section contains all the criteria that the Employer shall use to evaluate Bids and qualify Bidders through post-qualification. No other factors, methods or criteria shall be used other than specified in this bidding document. The Bidder shall provide all the information requested in the forms included in Section IV, Bidding Forms.

PRSWSSP

Table of Criteria

1. Margin of Preference 41

2. Evaluation 41

3. Qualification 42

4. Key Personnel 48

5. Equipment 50

PRSWSSP

1. Margin of Preference

Not Applicable

2. Evaluation

In addition to the criteria listed in ITB 35.2 (a) – (e) the following criteria shall apply:

2.1 Adequacy of Technical Proposal

Evaluation of the Bidder's Technical Proposal will include an assessment of the Bidder's technical capacity to mobilize key equipment and personnel for the contract consistent with its proposal regarding work methods, scheduling, and material sourcing in sufficient detail and fully in accordance with the requirements stipulated in Section VII, Works'Requirements.

Assessment of adequacy of Technical Proposal shall be carried out in accordance with the Bidding Document especially the Requirements as described in Section VII, Scope of Works.

2.2 Multiple Contracts

Not Applicable

2.3 Alternative Completion Times

Not Applicable

2.4 Sustainable procurement

Not Applicable

2.5 Alternative Technical Solutions for Specified Parts of Works

Not Applicable

2.6 Specialized Subcontractors

Not Applicable

PRSWSP

3. Qualification

Eligibility and Qualification Criteria			Compliance Requirements				Documentation
No.	Subject	Requirement	Single Entity	Joint Venture (existing or intended)			Submission Requirements
				All members Combined	Each Member	At least one Member	
1. Eligibility							
1.1	**Nationality**	Nationality in accordance with ITB 4.4	Must meet requirement	N/A	Must meet requirement	N/A	Forms ELI – 1.1 and 1.2, with attachments
1.2	**Conflict of Interest**	No conflicts of interest in accordance with ITB 4.2	Must meet requirement	N/A	Must meet requirement	N/A	Letter of Bid
1.3	**Bank Eligibility**	Not having been declared ineligible by the Bank, as described in ITB 4.5.	Must meet requirement	N/A	Must meet requirement	N/A	Letter of Bid
1.4	**State-owned enterprise or institution of the Borrower country**	Meets conditions of ITB 4.6	Must meet requirement	N/A	Must meet requirement	N/A	Forms ELI – 1.1 and 1.2, with attachments
1.5	**United Nations resolution or Borrower's country law**	Not having been excluded as a result of prohibition in the Borrower's country laws or official regulations against commercial relations with the Bidder's country, or by an act of compliance with UN Security Council resolution, both in accordance with ITB 4.8 and Section V.	Must meet requirement	N/A	Must meet requirement	N/A	Letter of Bid

Eligibility and Qualification Criteria			Compliance Requirements				Documentation
No.	Subject	Requirement	Single Entity	Joint Venture (existing or intended)			Submission Requirements
				All members Combined	Each Member	At least one Member	
2. Historical Contract Non-Performance							
2.1	**History of Non-Performing Contracts**	Non-performance of a contract[1] did not occur as a result of contractor default since 1st July 2016, based on all information on fully settled disputes or litigation.	Must meet requirement[1] & 2	N/A	Must meet requirement[2]	N/A	Form CON-2
2.2	**Suspension Based on Execution of Bid /Proposal Securing Declaration by the Employer or withdrawal of the Bid within Bid validity period**	Not under suspension based on execution of a Bid/Proposal Securing Declaration pursuant to ITB 4.7 or withdrawal of the Bid pursuant ITB 19.9	Must meet requirement	N/A	Must meet requirement	N/A	Letter of Bid
2.3	**Pending Litigation**	Bidder's financial position and prospective long term profitability sound according to criteria established in 3.1	Must meet requirement	N/A	Must meet requirement	N/A	Form CON – 2

[1] Nonperformance, as decided by the Employer, shall include all contracts where (a) nonperformance was not challenged by the contractor, including through referral to the dispute resolution mechanism under the respective contract, and (b) contracts that were so challenged but fully settled against the contractor. Nonperformance shall not include contracts where Employers decision was overruled by the dispute resolution mechanism. Nonperformance must be based on all information on fully settled disputes or litigation, i.e. dispute or litigation that has been resolved in accordance with the dispute resolution mechanism under the respective contract and where all appeal instances available to the Bidder have been exhausted.

[2] This requirement also applies to contracts executed by the Bidder as JV member.

PROVISO

Eligibility and Qualification Criteria			Compliance Requirements				Documentation
No.	Subject	Requirement	Single Entity	Joint Venture (existing or intended)			Submission Requirements
				All members Combined	Each Member	At least one Member	
		below and assuming that all pending litigation will be resolved against the Bidder					
2.4	**Litigation History**	No consistent history of court/arbitral award decisions against the Bidder[3] since 1st July 2016	Must meet requirement	N/A	Must meet requirement	N/A	Form CON – 2
2.5	**Declaration: Environmental, Social, Health, and Safety (ESHS) past performance**	Declare any civil work contracts that have been suspended or terminated and/or performance security called by an employer for reasons related to the non-compliance of any environmental, or social (including sexual exploitation and abuse (SEA) and gender-based violence (GBV)), or health or safety requirements or safeguard in the **past five years (05).**	Must make the declaration. Where there are Specialized Sub-contractor/s, the Specialized Sub-contractor/s must also make the declaration.	N/A	Each must make the declaration. Where there are Specialized Sub-contractor/s, the Specialized Sub-contractor/s must also make the declaration.	N/A	Form CON-3 ESHS Performance Declaration

[3]The Bidder shall provide accurate information on the Letter of Bid about any litigation or arbitration resulting from contracts completed or ongoing under its execution over the last five years. A consistent history of court/arbitral awards against the Bidder or any member of a joint venture may result in disqualifying the Bidder.

PBWSP

Eligibility and Qualification Criteria			Compliance Requirements				Documentation
No.	Subject	Requirement	Single Entity	Joint Venture (existing or intended)			Submission Requirements
				All members Combined	Each Member	At least one Member	
3. Financial Situation and Performance							
3.1	**Financial Capabilities**	(i) The Bidder shall demonstrate that it has access to, or has available, liquid assets, unencumbered real assets, lines of credit, and other financial means (independent of any contractual advance payment) sufficient to meet the construction cash flow requirements of Eq. **PKR 435 million** for the subject contract(s) net of the Bidder's other commitments	Must meet requirement	Must meet Requirement	N/A	N/A	Form FIN – 3.1, with attachments
		(ii) The Bidders shall also demonstrate, to the satisfaction of the Employer, that it has adequate sources of finance to meet the cash flow requirements on works currently in progress and for future contract commitments.	Must meet requirement	Must meet requirement	N/A	N/A	
		(iii) The audited balance sheets or, if not required by the laws of the Bidder's country, other	Must meet requirement	N/A	Must meet requirement	N/A	

PPWSP

Eligibility and Qualification Criteria			Compliance Requirements				Documentation
No.	Subject	Requirement	Single Entity	Joint Venture (existing or intended)			Submission Requirements
				All members Combined	Each Member	At least one Member	
		financial statements acceptable to the Employer, for the last three (03) years shall be submitted and must demonstrate the current soundness of the Bidder's financial position and indicate its prospective long-term profitability.					
3.2	**Average Annual Construction Turnover**	Minimum average annual construction turnover of Eq. **PKR 1450 million**, calculated as total certified payments received for contracts in progress and/or completed within the last three (03) years, divided by three (03) years.	Must meet requirement	Must meet requirement	N/A	Must meet 50% of the requirement	Form FIN – 3.2
4. Experience							
4.1 (a)	**General Construction Experience**	Experience under construction contracts in the role of prime contractor, JV member, subcontractor, or management contractor for at least the last ten (10) years, starting 1st July 2016	Must meet requirement	N/A	Must meet requirement	N/A	Form EXP – 4.1

PSWSP

Eligibility and Qualification Criteria			Compliance Requirements				Documentation
No.	Subject	Requirement	Single Entity	Joint Venture (existing or intended)			Submission Requirements
				All members Combined	Each Member	At least one Member	
4.2	**Specific Construction & Contract Management Experience**	A minimum number of two (02) similar contracts, each with a value of at least Eq. **PKR 1450 million** that have been satisfactorily and substantially[4] completed as a prime contractor, joint venture member[5], management contractor or sub-contractor between 1st July 2016 and bid submission deadline. The similarity shall be based on the physical size, complexity, methods/technology and/or other characteristics described in Section VII, Works' Requirements.	Must meet requirement	Must meet requirement[6]	N/A	N/A	Form EXP 4.2

[4] Substantial completion shall be based on **70%** or more works completed under the contract.

[5] For contracts under which the Bidder participated as a joint venture member or sub-contractor, only the Bidder's share, by value, shall be considered to meet this requirement.

[6] In the case of JV, the value of contracts completed by its members shall not be aggregated to determine whether the requirement of the minimum value of a single contract has been met. Instead, each contract performed by each member shall satisfy the minimum value of a single contract as required for single entity. In determining whether the JV meets the requirement of total number of contracts, only the number of contracts completed by all members each of value equal or more than the minimum value required shall be aggregated.

4. Key Personnel

The Bidder must demonstrate that it will have a suitably qualified (and in adequate numbers) minimum Key Personnel, as described in the table below, that are required to perform the Contract.

The Bidder shall provide details of the Key Personnel and such other Key Personnel that the Bidder considers appropriate, together with their academic qualifications and work experience. The Bidder shall complete the relevant Forms in Section IV, Bidding Forms. Failure to provide the required information will result in the bidder being declared non-responsive.

The Contractor shall require the Employer's consent to substitute or replace the Key Personnel (reference the Particular Conditions of Contract 9.1).

No.	PERSONNEL	Relevant Academic Qualifications	Minimum Years of Relevant Work Experience	Nos. Required
1	Project Engineer	B.Sc. Civil Engineering	8	01
2	Site Engineer	B.Sc. Civil Engineering	5	02
3	Sub Engineers	DAE in Civil	5	03
4	Sub Engineers	DAE in Electrical	5	01
5	Quantity Surveyor	DAE in Civil	5	01

PPWSP

Item No.	Position/ specialization	Relevant academic qualifications	Minimum years of relevant work experience
Suitable experts in the following specializations			
1	Health, Safety and Environment (HSE) Expert	Graduate (16 years education) in Environmental Engineer/Sciences	Five (05) years' experience in similar work related to HSE.
2	Social Safeguards Specialist	Graduate (16 years education) in Sociology	Five (05) years' experience in similar work related to social safeguards
3	Gender Specialist	Graduate (16 years education) in Sociology/Gender Sciences	Five (05) years' experience in similar work related to gender action plan implementation

PRSWSP

5. Equipment

The Bidder must demonstrate that it will have access to the key Contractor's equipment listed hereafter:

No.	Equipment	Minimum Number required
1	Excavator	01 No
2	Concrete mixing machine capacity one bag	06 No
3	Concrete mixing machine capacity half bag	06 No
4	Scaffoldings and shattering	20,000 Sft
5	Water Bowsers	06 No
6	Total Station Machine	02 No
7	Level Machine	02 No
8	Concrete Vibrators	04 No

The Bidder shall provide further details of proposed items of equipment using the relevant Form in Section IV. Failure to provide the required information will result in the bidder being declared non-responsive.

PRSWSP

Section IV - Bidding Forms

Table of Forms

Letter of Bid..... 52

Schedules..... 55

1. Bill of Quantities.....55
2. Schedule of Payment Currencies 56
3. Schedule of Adjustment Data 57

Form of Bid Security 58

Form of Bid Security - Bank Guarantee 58

Technical Proposal..... 62

Technical Proposal Forms.....62
Equipment.....67
Site Organization 68
Method Statement 69
Mobilization Schedule 70
Construction Schedule 71
ESHS Management Strategies and Implementation Plans 72
Code of Conduct: Environmental, Social, Health and Safety (ESHS) 73
Others.....74

Bidder's Qualification 75

Form ELI -1.1: Bidder Information Form.....76
Form ELI -1.2: Information Form for JV Bidders.....77
Form CON – 2: Historical Contract Non-Performance, Pending Litigation and Litigation History.....78
Form CON – 3: Environmental, Social, Health, and Safety.....80
Form FIN – 3.1: Financial Situation and Performance.....82
Form FIN - 3.2: Average Annual Construction Turnover 85
Form EXP - 4.1: General Construction Experience.....86
Form EXP - 4.2: Specific Construction and Contract Management Experience.....87

PRSWSP

Letter of Bid

INSTRUCTIONS TO BIDDERS: DELETE THIS BOX ONCE YOU HAVE COMPLETED THE DOCUMENT

The Bidder must prepare this Letter of Bid on stationery with its letterhead clearly showing the Bidder's complete name and business address.

Note: All italicized text is to help Bidders in preparing this form.

Date of this Bid submission: [*insert date (as day, month and year) of Bid submission*]
RFB No.: [*insert number of RFB process*]
Alternative No.:[*insert identification No. if this is a Bid for an alternative*]

To: **[*insert complete name of Employer*]**

(a) **No reservations:** We have examined and have no reservations to the bidding document, including Addenda issued in accordance with ITB 8;

(b) **Eligibility**: We meet the eligibility requirements and have no conflict of interest in accordance with ITB 4;

(c) **Bid-Securing Declaration:** We have not been suspended nor declared ineligible by the Employer based on execution of a Bid-Securing Declaration or Proposal-Securing Declaration in the Employer's Country in accordance with ITB 4.7;

(d) **Conformity:** We offer to execute in conformity with the bidding document the following Works: **[***insert a brief description of the Works]*

(e) **Bid Price**: The total price of our Bid, excluding any discounts offered in item (f) below is:

Total price is: PKR _____ [*insert the total price of the Bid in words and figures*];

(f) **Discounts:** The discounts offered and the methodology for their application are:

(i) The discounts offered are: [*Specify in detail each discount offered.*]

(ii) The exact method of calculations to determine the net price after application of discounts is shown below: [*Specify in detail the method that shall be used to apply the discounts*];

(g) **Bid Validity Period:** Our Bid shall be valid for a period specified in BDS ITB 18.1 of days from the date fixed for the Bid submission deadline in accordance with the bidding document, and it shall remain binding upon us and may be accepted at any time before the expiration of that period;

PRWSP

(h) **Performance Security:** If our Bid is accepted, we commit to obtain a performance security in accordance with the Bidding Document;

(i) **One Bid Per Bidder:** We are not submitting any other Bid(s) as an individual Bidder or as a subcontractor, and we are not participating in any other Bid(s) as a Joint Venture member, and meet the requirements of ITB 4.3, other than alternative Bids submitted in accordance with ITB 13;

(j) **Suspension and Debarment**: We, along with any of our subcontractors, suppliers, consultants, manufacturers, or service providers for any part of the contract, are not subject to, and not controlled by any entity or individual that is subject to, a temporary suspension or a debarment imposed by the World Bank Group or a debarment imposed by the World Bank Group in accordance with the Agreement for Mutual Enforcement of Debarment Decisions between the World Bank and other development banks. Further, we are not ineligible under the Employer's Country laws or official regulations or pursuant to a decision of the United Nations Security Council;

(k) **State-owned enterprise or institution:** [*select the appropriate option and delete the other*] [*We are not a state-owned enterprise or institution*] / [*We are a state-owned enterprise or institution but meet the requirements of ITB 4.6*];

(l) **Commissions, gratuities and fees:** We have paid, or will pay the following commissions, gratuities, or fees with respect to the Bidding process or execution of the Contract: [*insert complete name of each Recipient, its full address, the reason for which each commission or gratuity was paid and the amount and currency of each such commission or gratuity*]

Name of Recipient	Address	Reason	Amount

(If none has been paid or is to be paid, indicate "none.")

(m) **Binding Contract**: We understand that this Bid, together with your written acceptance thereof included in your Letter of Acceptance, shall constitute a binding contract between us, until a formal contract is prepared and executed;

(n) **Not Bound to Accept:** We understand that you are not bound to accept the lowest evaluated cost Bid, the Most Advantageous Bid or any other Bid that you may receive; and

(o) **Fraud and Corruption:** We hereby certify that we have taken steps to ensure that no person acting for us or on our behalf engages in any type of Fraud and Corruption; and

(p) **Adjudicator:** We accept the appointment of *[insert name proposed in Bid Data Sheet]* as the Adjudicator.

PRSWSD

[or]

We do not accept the appointment of *[insert name proposed in Bid Data Sheet]* as the Adjudicator, and propose instead that *[insert name]* be appointed as Adjudicator, whose daily fees and biographical data are attached.

Name of the Bidder: *[*insert complete name of person signing the Bid*]

Name of the person duly authorized to sign the Bid on behalf of the Bidder:**[*insert complete name of person duly authorized to sign the Bid*]

Title of the person signing the Bid: [*insert complete title of the person signing the Bid*]

Signature of the person named above: [*insert signature of person whose name and capacity are shown above*]

Date signed [*insert date of signing*] **day of** [*insert month*], [*insert year*]

*: In the case of the Bid submitted by joint venture specify the name of the Joint Venture as Bidder
**: Person signing the Bid shall have the power of attorney given by the Bidder to be attached with the Bid

PRSWSP

Schedules

1. Bill of Quantities

[Available at Part-II]

PRSWSSP

2. Schedule of Payment Currencies

NOT APPLICABLE

PRSWSSP

3. Schedule of Adjustment Data

Element Number	Element Description	Bidder's Amount [PKR]	Bidder's Proposed Weighting for Coefficients*
i.	Non-adjustable		a: (0.2)
ii.	Cement (OPC)		b: ( )
iii.	Steel (M.S. bars [deformed, 40/60 grade]		c: ( )
iv.	High Speed Diesel		d: ( )
v.	Labour (Un-skilled/skilled)		e: ( )
vi.	HDPE/PVC Pipe		f: ( )
vii	RCC Pipe		g: ( )
viii	Bricks		h: ( )
ix	Crush		i: ( )
		Total	**1.00**

* The Bidder shall enter a value within the range such that the total weighting shall be equal to 1.00.

The base and current rates of each cost element shall be taken from the notification(s) by Finance Department of Government of the Punjab for Price Variation Adjustment for the district prescribed in the list, nearest to the location of the Works.

Note:

1. Cement (OPC) [Bags] shall represent all kinds of Cement.
2. Steel (M.S. bars deformed, 40/60 grade) shall represent all kinds of steel reinforcing bars and structural steel and all kind of MS angle/sheet and sections.
3. High Speed Diesel [Litre] shall represent all kinds of fuels and lubricants.
4. Labour (Un-skilled/skilled) shall represent all kinds of labour.
5. HDPE/PVC pipe shall represent all kind of pressure (PN)/class and size of pipes
6. RCC pipes shall represent all kinds/class and size of pipes
7. Bricks shall represent all kind of bricks, bricks ballast and bricks tiles
8. Crush shall represent all size and grade of crush

CWSP

Form of Bid Security

Form of Bid Security - Bank Guarantee

[Guarantor letterhead or SWIFT identifier code]

Beneficiary:

[Insert name and address of the Employer*]*

Request for Bids No: *_[Insert reference number for the Request for Bids]*

Date: [*Insert date of issue]*

BID GUARANTEE No.:*[Insert guarantee reference number]*

Guarantor: *_[Insert name and address of place of issue, unless indicated in the letterhead]*

We have been informed that *[insert name of the Bidder, which in the case of a joint venture shall be the name of the joint venture (whether legally constituted or prospective) or the names of all members thereof]* (hereinafter called "the Applicant") has submitted or will submit to the Beneficiary its Bid (hereinafter called "the Bid") for the execution of *[insert description of contract]* under Request for Bids No. [*insert number*] ("the RFB").

Furthermore, we understand that, according to the Beneficiary's conditions, Bids must be supported by a Bid guarantee.

At the request of the Applicant, we, as Guarantor, hereby irrevocably undertake to pay the Beneficiary any sum or sums not exceeding in total an amount of *[insert amount in letters]* (*insert amount in numbers*) upon receipt by us of the Beneficiary's complying supported by the Beneficiary's statement, whether in the demand itself or a separate signed document accompanying or identifying the demand, stating either that the Applicant:

(a) has withdrawn its Bid during the period of Bid validity specified by the Applicant in the Letter of Bid ("the Bid Validity Period"), or any extension thereto provided by the Applicant; or

(b) having been notified of the acceptance of its Bid by the Beneficiary during the period of Bid validity, (i) fails to execute the contract agreement or (ii) fails to furnish the performance security and, if required, the Environmental, Social, Health and Safety (ESHS) Performance Security, in accordance with the Instructions to Bidders ("ITB") of the Beneficiary's bidding document.

PRWSP

This guarantee will expire: (a) if the Applicant is the successful Bidder, upon our receipt of copies of the contract agreement signed by the Applicant and the performance security and, if required, the Environmental, Social, Health and Safety (ESHS) Performance Security, issued to the Beneficiary in relation to such contract agreement; and (b) if the Applicant is not the successful Bidder, upon the earlier of (i) our receipt of a copy of the Beneficiary's notification to the Applicant of the results of the Bidding process; or (ii) twenty-eight days after the end of the Bid Validity Period.

Consequently, any demand for payment under this guarantee must be received by us at the office indicated above on or before that date.

This guarantee is subject to the Uniform Rules for Demand Guarantees (URDG) 2010 Revision, ICC Publication No. 758.

_____

[signature(s)]

Note: All italicized text is for use in preparing this form and shall be deleted from the final product.

PRSWSSP

Form of Call Deposit Receipt (CDR) Undertaking

[Guarantor letterhead or SWIFT identifier code]

Beneficiary:

[Insert name and address of the Employer*]*

Request for Bids No: *_[Insert reference number for the Request for Bids]*

Date: [*Insert date of issue]*

CDR No.:*[Insert guarantee reference number]*

Guarantor: *_[Insert name and address of place of issue, unless indicated in the letterhead]*

We have been informed that *[insert name of the Bidder, which in the case of a joint venture shall be the name of the joint venture (whether legally constituted or prospective) or the names of all members thereof]* (hereinafter called "the Applicant") has submitted or will submit to the Beneficiary its Bid (hereinafter called "the Bid") for the execution of *[insert description of contract]* under Request for Bids No. [*insert number*] ("the RFB").

Furthermore, we understand that, according to the Beneficiary's conditions, Bids must be supported by a CDR.

At the request of the Applicant, we, as Guarantor, hereby irrevocably undertake to pay the Beneficiary any sum or sums not exceeding in total an amount of *[insert amount in letters]* (*insert amount in numbers*) upon receipt by us of the Beneficiary's complying supported by the Beneficiary's statement, whether in the demand itself or a separate signed document accompanying or identifying the demand, stating either that the Applicant:

(a) has withdrawn its Bid during the period of Bid validity specified by the Applicant in the Letter of Bid ("the Bid Validity Period"), or any extension thereto provided by the Applicant; or

(b) having been notified of the acceptance of its Bid by the Beneficiary during the period of Bid validity, (i) fails to execute the contract agreement or (ii) fails to furnish the performance security and, if required, the Environmental, Social, Health and Safety (ESHS) Performance Security, in accordance with the Instructions to Bidders ("ITB") of the Beneficiary's bidding document.

This guarantee will expire: (a) if the Applicant is the successful Bidder, upon our receipt of copies of the contract agreement signed by the Applicant and the performance security and, if required, the Environmental, Social, Health and Safety (ESHS) Performance Security, issued

PPSMSP

to the Beneficiary in relation to such contract agreement; and (b) if the Applicant is not the successful Bidder, upon the earlier of (i) our receipt of a copy of the Beneficiary's notification to the Applicant of the results of the Bidding process; or (ii) twenty-eight days after the end of the Bid Validity Period.

Consequently, any demand for payment under this guarantee must be received by us at the office indicated above on or before that date.

_____

[signature(s)]

Note: All italicized text is for use in preparing this form and shall be deleted from the final product.

PRSWSP

Technical Proposal

Technical Proposal Forms

- **Key Personnel Schedule**
- **Equipment**
- **Site Organization**
- **Method Statement**
- **Mobilization Schedule**
- **Construction Schedule**
- **ESHS Management Strategies and Implementation Plans**
- **Code of Conduct (ESHS)**
- **Others**

PRSWSP

FORM PER -1

Key Personnel Schedule

Bidders should provide the names and details of the suitably qualified Key Personnel to perform the Contract. The data on their experience should be supplied using the Form PER-2 below for each candidate.

Key Personnel

1.	**Title of position:**	
	Name of candidate:	
	Duration of appointment:	[*insert the whole period (start and end dates) for which this position will be engaged*]
	Time commitment: for this position:	[*insert the number of days/week/months/ that has been scheduled for this position*]
	Expected time schedule for this position:	[*insert the expected time schedule for this position (e.g. attach high level Gantt chart*]
2.	**Title of position:** *[Environmental Specialist]*	
	Name of candidate:	
	Duration of appointment:	[*insert the whole period (start and end dates) for which this position will be engaged*]
	Time commitment: for this position:	[*insert the number of days/week/months/ that has been scheduled for this position*]
	Expected time schedule for this position:	[*insert the expected time schedule for this position (e.g. attach high level Gantt chart*]
3.	**Title of position:** *[Health and Safety Specialist]*	
	Name of candidate:	
	Duration of appointment:	[*insert the whole period (start and end dates) for which this position will be engaged*]
	Time commitment: for this position:	[*insert the number of days/week/months/ that has been scheduled for this position*]
	Expected time schedule for this position:	[*insert the expected time schedule for this position (e.g. attach high level Gantt chart*]
4.	**Title of position:** *[Social Specialist]*	
	Name of candidate:	

PRSWSP

	Duration of appointment:	[*insert the whole period (start and end dates) for which this position will be engaged*]
	Time commitment: for this position:	[*insert the number of days/week/months/ that has been scheduled for this position*]
	Expected time schedule for this position:	[*insert the expected time schedule for this position (e.g. attach high level Gantt chart*]
5.	**Title of position:** *[insert title]*	
	Name of candidate	
	Duration of appointment:	[*insert the whole period (start and end dates) for which this position will be engaged*]
	Time commitment: for this position:	[*insert the number of days/week/months/ that has been scheduled for this position*]
	Expected time schedule for this position:	[*insert the expected time schedule for this position (e.g. attach high level Gantt chart*]

PRSWSP

Form PER-2:

Resume and Declaration

Key Personnel

Name of Bidder

Position [*#1*]: [*title of position from Form PER-1*]		
Personnel information	**Name:**	**Date of birth:**
	Address:	**E-mail:**
	Professional qualifications:	
	Academic qualifications:	
	Language proficiency: *[language and levels of speaking, reading and writing skills]*	
details		
	Address of employer:	
	Telephone:	**Contact (manager / personnel officer):**
	Fax:	
	Job title:	**Years with present employer:**

Summarize professional experience in reverse chronological order. Indicate particular technical and managerial experience relevant to the project.

Project	**Role**	**Duration of involvement**	**Relevant experience**
[main project details]	*[role and responsibilities on the project]*	*[time in role]*	*[describe the experience relevant to this position]*

PRSWSP

Declaration

I, the undersigned Key Personnel, certify that to the best of my knowledge and belief, the information contained in this Form PER-2 correctly describes myself, my qualifications and my experience.

I confirm that I am available as certified in the following table and throughout the expected time schedule for this position as provided in the Bid:

Commitment	**Details**
Commitment to duration of contract:	*[insert period (start and end dates) for which this Key Personnel is available to work on this contract]*
Time commitment:	*[insert the number of days/week/months/ that this Key Personnel will be engaged]*

I understand that any misrepresentation or omission in this Form may:

(a) be taken into consideration during Bid evaluation;

(b) my disqualification from participating in the Bid;

(c) my dismissal from the contract.

Name of Key Personnel: [*insert name*]

Signature: _____

Date: (day month year): _____

Countersignature of authorized representative of the Bidder:

Signature: _____

Date: (day month year): _____

PRSWSP

Equipment

The Bidder shall provide adequate information to demonstrate clearly that it has the capability to meet the requirements for the key equipment listed in Section III (Evaluation and Qualification Criteria). A separate Form shall be prepared for each item of equipment listed, or for alternative equipment proposed by the Bidder. The Bidder shall provide all the information requested below, to the extent possible. Fields with asterisk (*) shall be used for evaluation.

Type of Equipment*		
Equipment Information	**Name of manufacturer,**	**Model and power rating**
	Capacity*	**Year of manufacture***
Current Status	**Current location**	
	Details of current commitments	
Source	**Indicate source of the equipment** **☐ Owned ☐ Rented ☐ Leased ☐ Specially manufactured**	

The following information shall be provided only for equipment not owned by the Bidder.

Owner	**Name of owner**	
	Address of owner	
	Telephone	**Contact name and title**
	Fax	**Telex**
Agreements	**Details of rental / lease / manufacture agreements specific to the project**	

PRSWSP

Site Organization

[insert Site Organization information]

PRSWSSP

Method Statement

[insert Method Statement]

PRSWSSP

Mobilization Schedule

[insert Mobilization Schedule]

PRSWSSP

Construction Schedule

[insert Construction Schedule]

PRSWSSP

ESHS Management Strategies and Implementation Plans

(ESHS-MSIP)

The Bidder shall submit comprehensive and concise Environmental, Social, Health and Safety Management Strategies and Implementation Plans (ESHS-MSIP) as required by ITB 11.1 (i) of the Bid Data Sheet. These strategies and plans shall describe in detail the actions, materials, equipment, management processes etc. that will be implemented by the Contractor, and its subcontractors.

In developing these strategies and plans, the Bidder shall have regard to the ESHS provisions of the contract including those as may be more fully described in the Works Requirements in Section VII.

PRSWSP

Code of Conduct: Environmental, Social, Health and Safety (ESHS)

The Bidder shall submit the Code of Conduct that will apply to the Contractor's employees and subcontractors as required by ITB 11.1 (i) of the Bid Data Sheet. The Code of Conduct shall ensure compliance with the ESHS provisions of the contract, including those as may be more fully described in the Works Requirements in Section VII.

In addition, the Bidder shall submit an outline of how this Code of Conduct will be implemented. This will include: how it will be introduced into conditions of employment/engagement, what training will be provided, how it will be monitored and how the Contractor proposes to deal with any breaches.

PRSWSSP

Others

PRSWSSP

-

Bidder's Qualification

To establish its qualifications to perform the contract in accordance with Section III (Evaluation and Qualification Criteria) the Bidder shall provide the information requested in the corresponding Information Sheets/Forms included hereunder

The information provided in the Forms shall be substantiated with valid documentary evidences otherwise the requirement will not be considered as complied.

PRSWSSP

Form ELI -1.1: Bidder Information Form

Date: _____
RFB No. and title: _____
Page_____of _____pages

Bidder's name
In case of Joint Venture (JV), name of each member:
Bidder's actual or intended country of registration: *[indicate country of Constitution]*
Bidder's actual or intended year of incorporation:
Bidder's legal address [in country of registration]:
Bidder's authorized representative information Name: _____ Address: _____ Telephone/Fax numbers: _____ E-mail address: _____
1. Attached are copies of original documents of ☐ Articles of Incorporation (or equivalent documents of constitution or association), and/or documents of registration of the legal entity named above, in accordance with ITB 4.4. ☐ In case of JV, letter of intent to form JV or JV agreement, in accordance with ITB 4.1. ☐ In case of state-owned enterprise or institution, in accordance with ITB 4.6 documents establishing: • Legal and financial autonomy • Operation under commercial law • Establishing that the Bidder is not under the supervision of the Employer 2. Included are the organizational chart, a list of Board of Directors, and the beneficial ownership.*[If required under BDS ITB 45.1, the successful Bidder shall provide additional information on beneficial ownership, using the Beneficial Ownership Disclosure Form.]*

PBSWSP

Form ELI -1.2: Information Form for JV Bidders

(tobe completed for each member of Joint Venture)

Date: _____
RFB No. and title: _____
Page _____ of _____ pages

Bidder's Joint Venture name:
JV member's name:
JV member's country of registration:
JV member's year of constitution:
JV member's legal address in country of constitution:
JV member's authorized representative information Name: _____ Address: _____ Telephone/Fax numbers: _____ E-mail address: _____
1. Attached are copies of original documents of ☐ Articles of Incorporation (or equivalent documents of constitution or association), and/or registration documents of the legal entity named above, in accordance with ITB 4.4. ☐ In case of a state-owned enterprise or institution, documents establishing legal and financial autonomy, operation in accordance with commercial law, and is not under the supervision of the Employer, in accordance with ITB 4.6. 2. Included are the organizational chart, a list of Board of Directors, and the beneficial ownership. *[If required under BDS ITB 45.1, the successful Bidder shall provide additional information on beneficial ownership for each JV member using the Beneficial Ownership Disclosure Form.]*

PBSWSSP

Form CON – 2: Historical Contract Non-Performance, Pending Litigation and Litigation History

Bidder's Name: _____
Date: _____
Joint Venture Member's Name_____
RFB No. and title: _____
Page _____of _____pages

Non-Performed Contracts in accordance with Section III, Evaluation and Qualification Criteria			
☐ Contract non-performance did not occur since 1st January *[insert year]*specified in Section III, Evaluation and Qualification Criteria, Sub-Factor 2.1. ☐ Contract(s) not performed since 1st January *[insert year]* specified in Section III, Evaluation and Qualification Criteria, requirement 2.1			
Year	**Non-performed portion of contract**	**Contract Identification**	**Total Contract Amount (Equivalent PKR)**
[insert year]	*[insert amount and percentage]*	Contract Identification: *[indicate complete contract name/ number, and any other identification]* Name of Employer: *[insert full name]* Address of Employer: *[insert street/city/country]* Reason(s) for nonperformance: *[indicate main reason(s)]*	*[insert amount]*
Pending Litigation, in accordance with Section III, Evaluation and Qualification Criteria			
☐ No pending litigation in accordance with Section III, Evaluation and Qualification Criteria, Sub-Factor 2.3. ☐ Pending litigation in accordance with Section III, Evaluation and Qualification Criteria, Sub-Factor 2.3 as indicated below.			

PPRA/SP

Year of dispute	Amount in dispute (currency)	Contract Identification	Total Contract Amount (Equivalent PKR)
		Contract Identification: _____ Name of Employer: _____ Address of Employer: _____ Matter in dispute: _____ Party who initiated the dispute: ____ Status of dispute: _____	
		Contract Identification: Name of Employer: Address of Employer: Matter in dispute: Party who initiated the dispute: Status of dispute:	

Litigation History in accordance with Section III, Evaluation and Qualification Criteria

☐ No Litigation History in accordance with Section III, Evaluation and Qualification Criteria, Sub-Factor 2.4.

☐ Litigation Historyin accordance with Section III, Evaluation and Qualification Criteria, Sub-Factor 2.4 as indicated below.

Year of award	Outcome as percentage of Net Worth	Contract Identification	Total Contract Amount (Equivalent PKR)
[insert year]	*[insert percentage]*	Contract Identification: [indicate complete contract name, number, and any other identification] Name of Employer: *[insert full name]* Address of Employer: *[insert street/city/country]* Matter in dispute: *[indicate main issues in dispute]* Party who initiated the dispute: *[indicate "Employer" or "Contractor"]* Reason(s) for Litigation and award decision *[indicate main reason(s)]*	*[insert amount]*

PROVISO

Form CON – 3: Environmental, Social, Health, and Safety Performance Declaration

[The following table shall be filled in for the Bidder/ each member of a Joint Venture]

Bidder's Name: *[insert full name]*
Date: *[insert day, month, year]*
Joint Venture Member's Name: *[insert full name]*
RFB No. and title: *[insert RFB number and title]*
Page *[insert page number]* of *[insert total number]* pages

Environmental, Social, Health, and Safety Performance Declaration

in accordance with Section III, Qualification Criteria, and Requirements

☐ **No suspension or termination of contract**: An employer has not suspended or terminated a contract and/or called the performance security for a contract for reasons related to Environmental, Social, Health, or Safety (ESHS) performance since the date specified in Section III, Qualification Criteria, and Requirements, Sub-Factor 2.5.

☐ **Declaration of suspension or termination of contract**: The following contract(s) has/have been suspended or terminated and/or Performance Security called by an employer(s) for reasons related to Environmental, Social, Health, or Safety (ESHS) performance since the date specified in Section III, Qualification Criteria, and Requirements, Sub-Factor 2.5. Details are described below:

Year	Suspended or terminated portion of contract	Contract Identification	Total Contract Amount (Equivalent PKR)
[insert year]	*[insert amount and percentage]*	Contract Identification: *[indicate complete contract name/ number, and any other identification]* Name of Employer: *[insert full name]* Address of Employer: *[insert street/city/country]* Reason(s) for suspension or termination: *[indicate main reason(s) e.g. for GBV/ SEA breaches]*	*[insert amount]*
[insert year]	*[insert amount and percentage]*	Contract Identification: *[indicate complete contract name/ number, and any other identification]* Name of Employer: *[insert full name]* Address of Employer: *[insert street/city/country]* Reason(s) for suspension or termination: *[indicate main reason(s)]*	*[insert amount]*

PPSW SCP

…	…	*[list all applicable contracts]*	…
Performance Security called by an employer(s) for reasons related to ESHS performance			
Year	**Contract Identification**		**Total Contract Amount (Equivalent PKR)**
[insert year]	Contract Identification: *[indicate complete contract name/ number, and any other identification]* Name of Employer: *[insert full name]* Address of Employer: *[insert street/city/country]* Reason(s) for calling of performance security: *[indicate main reason(s) e.g. for GBV/ SEA breaches]*		*[insert amount]*

PRSWSSP

Form FIN – 3.1: Financial Situation and Performance

Bidder's Name: _____
Date: _____
Joint Venture Member's Name_____
RFB No. and title: _____
Page _____of _____pages

1. Financial Data

Type of Financial Information in (PKR)	**Historic information for previous three (03) *years*, (Equivalent PKR, exchange rate)**		
	Year 1	**Year 2**	**Year 3**
Statement of Financial Position (Information from Balance Sheet)			
Total Assets (TA)			
Total Liabilities (TL)			
Total Equity/Net Worth (NW)			
Current Assets (CA)			
Current Liabilities (CL)			
Working Capital (WC)			
Information from Income Statement			
Total Revenue (TR)			
Profits Before Taxes (PBT)			
Cash Flow Information			
Cash Flow from Operating Activities			

PRSWSP

2. Sources of Finance

Specify sources of finance to meet the cash flow requirements on works currently in progress and for future contract commitments.

No.	Source of finance	Amount (Equivalent PKR)
1		
2		
3		

3. Financial documents

The Bidder and its parties shall provide copies of financial statements for three (03) years pursuant Section III, Evaluation and Qualifications Criteria, Sub-factor 3.2. The financial statements shall:

(a) reflect the financial situation of the Bidder or in case of JV member, and not an affiliated entity (such as parent company or group member).

(b) be independently audited or certified in accordance with local legislation.

(c) be complete, including all notes to the financial statements.

(d) correspond to accounting periods already completed and audited.

☐ Attached are copies of financial statements[12] for the three (03) years required above; and complying with the requirements

[12] If the most recent set of financial statements is for a period earlier than 12 months from the date of bid, the reason for this should be justified.

PRSWSP

Current Contract Commitments / Works in Progress

Bidders and each member to a JV should provide information on their current commitments on all contracts that have been awarded, or for which a letter of intent or acceptance has been received, or for contracts approaching completion, but for which an unqualified, full completion certificate has yet to be issued.

Current Contract Commitments					
No.	**Name of Contract**	**Employer's Contact Address, Tel, Fax**	**Value of Outstanding Work [Current PKR Equivalent]**	**Estimated Completion Date**	**Average Monthly Invoicing Over Last Six Months [Eq. PKR/month)]**
1					
2					
3					
4					
5					

PRSWSP

Form FIN - 3.2: Average Annual Construction Turnover

Bidder's Name: _____
Date: _____
Joint Venture Member's Name_____
RFB No. and title: _____
Page _____of _____pages

	Annual turnover data (construction only)		
Year	**Amount** **Currency**	**Exchange rate**	**PKR equivalent**
[indicate year]	*[insert amount and indicate currency]*		
Average Annual Construction Turnover *			

* See Section III, Evaluation and Qualification Criteria, Sub-Factor 3.2.

PRSWSP

Form EXP - 4.1: General Construction Experience

Bidder's Name: _____
Date: _____
Joint Venture Member's Name_____
RFB No. and title: _____
Page _____of _____pages

Starting Year	Ending Year	Contract Identification	Role of Bidder
		Contract name: _____ Brief Description of the Works performed by the Bidder: _____ Amount of contract: _____ Name of Employer: _____ Address: _____	
		Contract name: _____ Brief Description of the Works performed by the Bidder: _____ Amount of contract: _____ Name of Employer: _____ Address: _____	
		Contract name: _____ Brief Description of the Works performed by the Bidder: _____ Amount of contract: _____ Name of Employer: _____ Address: _____	

PDWSP

Form EXP - 4.2: Specific Construction and Contract Management Experience

Bidder's Name: _____
Date: _____
Joint Venture Member's Name_____
RFB No. and title: _____
Page _____of _____pages

Similar Contract No.	**Information**			
Contract Identification				
Award date				
Completion date				
Role in Contract	Prime Contractor ☐	Member in JV ☐	Management Contractor ☐	Sub-contractor ☐
Total Contract Amount			Eq. PKR*	
If member in a JV or subcontractor, specify participation in total Contract amount			*	
Employer's Name:				
Address: Telephone/fax number E-mail:				

PRSWSP

Form EXP - 4.2 (cont.)
Specific Construction and Contract Management Experience (cont.)

Similar Contract No.	Information
Description of the similarity in accordance with Sub-Factor 4.2of Section III:	
1. Amount	
2. Physical size of required works items	
3. Complexity	
4. Methods/Technology	
5. Construction rate for key activities	
6. Other Characteristics	

PRSWSP

Section V - Eligible Countries

Eligibility for the Provision of Goods, Works and Services in Bank-Financed Procurement

In reference to ITB 4.8, and 5.1, for the information of the Bidders, at the present time firms, goods and services from the following countries are excluded from this Bidding process:

Under ITB 4.8(a) and 5.1: Israel

Under ITB 4.8(b) and 5.1: Israel

PRSWSSP

Section VI - Fraud and Corruption

(Section VI shall not be modified)

1. Purpose

1.1 The Bank's Anti-Corruption Guidelines and this annex apply with respect to procurement under Bank Investment Project Financing operations.

2. Requirements

2.1 The Bank requires that Borrowers (including beneficiaries of Bank financing); bidders (applicants/proposers), consultants, contractors and suppliers; any sub-contractors, sub-consultants, service providers or suppliers; any agents (whether declared or not); and any of their personnel, observe the highest standard of ethics during the procurement process, selection and contract execution of Bank-financed contracts, and refrain from Fraud and Corruption.

2.2 To this end, the Bank:

a. Defines, for the purposes of this provision, the terms set forth below as follows:

i. "corrupt practice" is the offering, giving, receiving, or soliciting, directly or indirectly, of anything of value to influence improperly the actions of another party;

ii. "fraudulent practice" is any act or omission, including misrepresentation, that knowingly or recklessly misleads, or attempts to mislead, a party to obtain financial or other benefit or to avoid an obligation;

iii. "collusive practice" is an arrangement between two or more parties designed to achieve an improper purpose, including to influence improperly the actions of another party;

iv. "coercive practice" is impairing or harming, or threatening to impair or harm, directly or indirectly, any party or the property of the party to influence improperly the actions of a party;

v. "obstructive practice" is:

(a) deliberately destroying, falsifying, altering, or concealing of evidence material to the investigation or making false statements to investigators in order to materially impede a Bank investigation into allegations of a corrupt, fraudulent, coercive, or collusive practice; and/or threatening, harassing, or intimidating any party to prevent it from disclosing its knowledge of matters relevant to the investigation or from pursuing the investigation; or

PDWSSP

(b) acts intended to materially impede the exercise of the Bank's inspection and audit rights provided for under paragraph 2.2 e. below.

b. Rejects a proposal for award if the Bank determines that the firm or individual recommended for award, any of its personnel, or its agents, or its sub-consultants, sub-contractors, service providers, suppliers and/ or their employees, has, directly or indirectly, engaged in corrupt, fraudulent, collusive, coercive, or obstructive practices in competing for the contract in question;

c. In addition to the legal remedies set out in the relevant Legal Agreement, may take other appropriate actions, including declaring mis-procurement, if the Bank determines at any time that representatives of the Borrower or of a recipient of any part of the proceeds of the loan engaged in corrupt, fraudulent, collusive, coercive, or obstructive practices during the procurement process, selection and/or execution of the contract in question, without the Borrower having taken timely and appropriate action satisfactory to the Bank to address such practices when they occur, including by failing to inform the Bank in a timely manner at the time they knew of the practices;

d. Pursuant to the Bank's Anti- Corruption Guidelines and in accordance with the Bank's prevailing sanctions policies and procedures, may sanction a firm or individual, either indefinitely or for a stated period of time, including by publicly declaring such firm or individual ineligible (i) to be awarded or otherwise benefit from a Bank-financed contract, financially or in any other manner;1 (ii) to be a nominated2 sub-contractor, consultant, manufacturer or supplier, or service provider of an otherwise eligible firm being awarded a Bank-financed contract; and (iii) to receive the proceeds of any loan made by the Bank or otherwise to participate further in the preparation or implementation of any Bank-financed project;

e. Requires that a clause be included in bidding/request for proposals documents and in contracts financed by a Bank loan, requiring (i) bidders (applicants/proposers), consultants, contractors, and suppliers, and their sub-contractors, sub-consultants, service providers, suppliers, agents personnel, permit the Bank to inspect3 all accounts, records and other documents relating to the procurement process, selection

[1] For the avoidance of doubt, a sanctioned party's ineligibility to be awarded a contract shall include, without limitation, (i) applying for pre-qualification, expressing interest in a consultancy, and bidding, either directly or as a nominated sub-contractor, nominated consultant, nominated manufacturer or supplier, or nominated service provider, in respect of such contract, and (ii) entering into an addendum or amendment introducing a material modification to any existing contract.

[2] A nominated sub-contractor, nominated consultant, nominated manufacturer or supplier, or nominated service provider (different names are used depending on the particular bidding document) is one which has been: (i) included by the bidder in its pre-qualification application or bid because it brings specific and critical experience and know-how that allow the bidder to meet the qualification requirements for the particular bid; or (ii) appointed by the Borrower.

[3] Inspections in this context usually are investigative (i.e., forensic) in nature. They involve fact-finding activities undertaken by the Bank or persons appointed by the Bank to address specific matters related to investigations/audits, such as evaluating the veracity of an allegation of possible Fraud and Corruption, through the appropriate mechanisms. Such activity includes but is not limited to: accessing and examining a firm's or individual's financial records and information, and making copies thereof as relevant; accessing and examining any other documents, data and information (whether in hard copy or electronic format) deemed relevant for the investigation/audit, and making copies thereof as relevant; interviewing staff and other relevant individuals; performing physical inspections and site visits; and obtaining third party verification of information.

PSWGP

and/or contract execution, and to have them audited by auditors appointed by the Bank.

PRSWSSP

PART 2 – Works' Requirements

PRSWSSP

Section VII-Works' Requirements

PRSWSSP

PREAMBLES

1. The Bill of Quantities shall be read in conjunction with the Conditions of Contract, Technical Provisions and Drawings.
2. In case of any variation or item not available in the priced bill of quantities, the same will be analyzed as per prevalent market rate adopting standard procedure for the purpose.
3. The rates entered against the various Items in the following Bill of Quantities are those referred to in the Contract as the Contract Rates and shall cover the execution, completion and maintenance in every respect as shown on and described in the Contract, with or without such modifications, either by way of additions or deductions or such alterations as may be ordered in writing during the progress of the works and include but not by way of limitation all matters and things particularly referred to in the Contract.
4. The quantities in the Bill of Quantities are estimated amounts and the Employer does not expressly nor by implication agree that the actual amount of work to be performed will correspond therewith. No payments will be made on account of anticipated profits for work covered by the Contract which is not performed.
5. The rates shall be quoted in figures as well as in words and shall cover all costs of every kind whatsoever, including but not limited to all office charges, supervision, transport, materials, and labour, the provision, maintenance, use and efficient repair of all plant equipment, and appliances of every kind the construction and maintenance of all Temporary Works of every description and the performance of all services that may be required for the proper execution completion and maintenance of the Works in full and complete accordance with the provisions of the Contract and the undertaking and discharge of all obligations and responsibilities therein defined.
6. The Contractor shall be deemed to have fully considered all the conditions obligations and requirements of Contract before entering the respective rates against the various Items in the following Bill of Quantities.
7. Where a discrepancy exists between the unit rate and extended total amount the unit rate shall be taken as correct and the total amount adjusted accordingly. Similarly, where a discrepancy exists between the rates quoted in the figures and the words the rates quoted in words shall be taken as correct and the total amount adjusted accordingly.
8. A rate or price shall be entered against each item in the priced Bill of Quantities, whether quantities are stated or not. The cost of items against which the Contractor will have failed to enter a rate or price shall be deemed to be covered by other rates and prices entered in the Bill of Quantities.
9. The whole cost of complying with the provisions of the Contract shall be included in the items provided in the priced Bill of Quantities, and where no items are provided, the cost shall be deemed to be distributed among the rates and prices entered for the related items of the Works.
10. All measurements shall be taken net except when otherwise specified and shall be applicable to finished work only as completed notwithstanding any trade custom to the contrary.

11. Except as may otherwise be provided under the terms of the Contract of the unit rates, prices, and lump sum amount entered in the Bill of Quantities, will be the rates at which the Contractor with be paid and shall be deemed to have included all costs of whatsoever nature for performing the works including but not limited to income tax, super tax, profits, rentals of equipment, etc. and the costs of accepting the general risks, liabilities and obligations set forth or implied in the Contract.
12. The unit rate in the bill of quantities for any item of work shall apply to completed work in all respects conforming to the Contract covering the total cost of material, labour, plant, shuttering and equipment required for the execution of that item of work, as well as covering the share of any from the other general expenses to be incurred by the Contractor during the execution of the Works. These general expenses shall include, but are not restricted to, the following, unless otherwise stated in the Contract.

    i. Preparation and submission of bids including the Site inspection;
    ii. Employment, mobilization and accommodation of the Contractor's staff including official holidays, annual leaves, sick leaves, compensation, bonuses insurance etc.;
    iii. Mobilization and demobilization of construction plant and equipment, transportation within the Site, operation, maintenance, repair, depreciation and all related costs;
    iv. Costs related to the Contractor's Site Camps, office for the Engineer including the provisions of all utility facilities;
    v. Costs shall also include providing, testing and commissioning of the complete installation;
    vi. Costs of laboratory testing, survey work and all assistance to the Engineer as required by the Contract;
    vii. Cost of bank / insurance guarantees / bonds;
    viii. Costs of all temporary works;
    ix. Costs of all work items for which there is no direct payment, and which are considered in the Contract as subsidiary to other items in the bill of quantities; Overheads and profit;
    x. All other expenses the Contractor may encounter in the proper execution of the Contract.

ENGINEERING DESIGN AND CONSTRUCTION SUPERVISION SERVICES (EDCS)
PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT (PRSWSSP), CLUSTER SOUTH-III

TEHSIL BAHAWALNAGAR (CW-25) (PHASE-I)

BILL OF QUANTITIES

ABSTRACT OF COST

Bill No.	Description	AMOUNT (Rs.)
1	WATER SUPPLY SYSTEM	
2	SEWERGE SYSTEM	
3	STREET PAVEMENT	
4	ESMP COST	
5	EMPLOYER FACILITY	
	TOTAL COST	
	ADD 5% (PRA charges)	
	TOTAL COST	
	TOTAL COST (Million)	

ENGINEERING DESIGN AND CONSTRUCTION SUPERVISION SERVICES (EDCS)
PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT (PRSWSSP), CLUSTER SOUTH-III

TEHSIL BAHAWALNAGAR (CW-25) (PHASE-I)
BILL OF QUANTITIES
ABSTRACT OF COST

Sr.No	Description	Amount (Rs.)
1	**Water Supply Network**	
1.1	TW Installation 0.2 Cusec	
1.2	TW Installation 0.25 Cusec	
1.3	TW Installation 0.1 Cusec	
1.4	TW Installation Ejector Pump	
1.5	TW Installation (RO)	
1.6	Stand Post with Chamber	
1.7	Pump House (Civil)	
1.8	Electrical Works 0.10	
1.9	Electrical Works 0.05	
1.10	Stand Post	
1.11	Pipe Network	
1.12	Valves Chambers	
1.13	Boundary Wall	
1.14	Pump Room Rehabilitation Works	
1.15	Electrical Rehabilitation Works	
1.16	Rehabilitation of Exisitng pipe Network	
1.17	Rehabilitation of exisitng Valves Chambers	
	Sub Total A	
2	**Sewerage System**	
2.1	Drainage Network	
2.2	Septic Tank Type-I(A)	
2.3	Septic Tank Type-I	
2.4	Septic Tank Type-II	
2.5	Septic Tank Type-III	
2.6	Septic Tank Type-IV	
2.7	Septic Tank Type-V	
2.8	Septic Tank Type-VI	
2.9	Communal Septic Tank	
	Sub Total B	
3	**Streets Pavement Works**	
	Sub Total C	
	Total Cost (A+B+C)	
	GRAND TOTAL AMOUNT	

ENGINEERING DESIGN AND CONSTRUCTION SUPERVISION SERVICES (EDCS)
PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT (PRSWSSP), CLUSTER SOUTH-III

TEHSIL BAHAWALNAGAR (CW-25) (PHASE-I)
BILL OF QUANTITIES
ABSTRACT OF COST

Bill No. 1: WATER SUPPLY SYSTEM

Bill No. 1.1.: Tubewell Installation (0.2 Cusec)

Sr. No.	Ref. MRS	Description	Unit	Quantity	Unit Rate (Rs)	Amount (Rs)
1.1.1	23/2a(i)	Direct Rotary/ Reverse Rotary drilling of bore for tubewells, in all types of soil except shingle, gravel and rock:-				
		a) from ground level to 250 ft. (75 m) below ground level:-	Per Rft. of bore			
		i) 15" to 18" (375 to 450 mm) i/d		90.00		
		Housing Pipe				
1.1.2	23/13	Providing and installing P.V.C. blind pipe, B.S.S. in tubewell bore hole, including sockets and solvents and jointing with strainer, (PS-3051=BS-3505), etc. complete. b) Class-D (12 bar) vii) 6" i/d (150 mm)	Per Rft	45.00		
		Blind Pipe				
1.1.3	23/10	Providing and installing Fiber glass Reinforced Polypropelene (FRP) bail plug of specified wall thickness having slot size of 0.9 mm to 1.10 mm in Tubewell bore hole i/c the cost of male / female coupling with Nylone Strip, studs complete in all respect as approved and directed by the Engineer Incharge. v) 8"dia (5mm thickness)	Per Rft	10.00		
		Strainer Pipe				
1.1.4	23/09	Providing and installing Fiberglass Reinforced Polypropelene (FRP) strainer of specifid wall thickness having slot size of 0.9 mm to 1.10 mm in Tubewell borehole i/c the cost of male/female coupling with Nylone Strip,studs complete in all respect as approved and directed by the Engineer Incharge. v) 8" inch dia (5 mm thickness)	Per Rft	25.00		
		Bail Plug				
1.1.5	23/10	Providing and installing Fiber glass Reinforced Polypropelene (FRP) bail plug of specified wall thickness having slot size of 0.9 mm to 1.10 mm in Tubewell bore hole i/c the cost of male / female coupling with Nylone Strip, studs complete in all respect as approved and directed by the Engineer. v) 8"dia (5mm thickness)	Per Rft	10.00		
		Delivery Pipe				
1.1.6	23/13	Providing and installing P.V.C. blind pipe, B.S.S. in tubewell bore hole, including sockets and solvents and jointing with strainer, (PS-3051=BS-3505), etc. complete. b) Class-D (12 bar)				
		iv) 3" i/d (75 mm)	Per Rft	20.00		
1.1.7	23/17	Shrouding with graded pea gravel 3/8 to 1/8 inch (10 to 3 mm) arround tubewell in bore hole.	Per Cft	173.63		
1.1.8	23/5	Furnishing sample of water from borehole.	Per set of 2 bottles	3.00		

ENGINEERING DESIGN AND CONSTRUCTION SUPERVISION SERVICES (EDCS)
PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT (PRSWSSP), CLUSTER SOUTH-III

TEHSIL BAHAWALNAGAR (CW-25) (PHASE-I)
BILL OF QUANTITIES
ABSTRACT OF COST

Bill No. 1: WATER SUPPLY SYSTEM

Bill No. 1.1.: Tubewell Installation (0.2 Cusec)

Sr. No.	Ref. MRS	Description	Unit	Quantity	Unit Rate (Rs)	Amount (Rs)
1.1.9	23/16	Testing and developing of tubewell of size 6" (150 mm) i/d and above continuously.				
		i) upto 1.5 cs. Discharge	P. Hour	72.00		
1.1.10	23/31	Providing & mixing bentonite clay / powder have swelling factor of 1200% for lining /seal and plug earthen bore holes / ponds in the specified ratio conforming to IS:6186 for stabilization of soil as specified by the designer etc complete in all respect.	Per Kg.	15.00		
1.1.11	6/5	Cement concrete plain including placing, compacting, finishing and curing complete (including screening and washing of stone aggregate): (f) Ratio 1: 2: 4	100Cft	0.28		
1.1.12	1/1	Carriage of 100 Cft. (2.83 cu.m) of all materials like stone aggregate, spawl, kankar lime (unslaked), surkhi, etc. or 150 Cft. (4.25 cu.m) of timber, by truck or by any other means owned by the contractor. (crushed stone aggregate and bajri used in concrete items) (Lead 350 Km)	100Cft	0.25		
1.1.13	N/S	Geophysical Logging of Borehole, including Data Collection, Interpretation, and Preparation/ Submission of Detailed Report to the Competent Authority/Incharge, Complete in All Respects.	P/Job	1.00		
1.1.14	N/S	Conducting Chemical, Physical, and Arsenic Analysis of Water through an Approved Water Testing Laboratory, including Collection, Testing, and Submission of Test Report to the Competent Authority/Incharge, Complete in All Respects.	P/Job	1.00		

ENGINEERING DESIGN AND CONSTRUCTION SUPERVISION SERVICES (EDCS)
PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT (PRSWSSP), CLUSTER SOUTH-III

TEHSIL BAHAWALNAGAR (CW-25) (PHASE-I)
BILL OF QUANTITIES
ABSTRACT OF COST

Bill No. 1: WATER SUPPLY SYSTEM

Bill No. 1.1.: Tubewell Installation (0.2 Cusec)

Sr. No.	Ref. MRS	Description	Unit	Quantity	Unit Rate (Rs)	Amount (Rs)
1.1.15	N/S	Supplying, installing, testing and commissioning of submersible water supply pump set of Approved manufacturer of HUD & PHED and should be ISO 9001 Certified, complete in all respects as per specifications and direction of the Engineer Incharge. The pump set shall have the following specifications: Pump Set: Flow: 0.2 Cusec Head: 250 ft Riser pipe up to 120 ft Material: Complete Pump Set in SS304 (EN 1.4301) Maximum Operating Temperature: 40C or higher Maximum Liquid Temperature: 40C or higher Minimum Efficiency Index: 0.40 or more Approved for drinking water ACS,DM174 or equivalent 3×400V, 50 Hz, 2 Pole, Submersible IP68 motor, Insulation class F		-		
		Motor Control Unit (MCU): MCU (Motor Control Unit) with VFD consisting of MCCB, Over/Under voltage relay, Phase reversal relay, volt meter, ampere meter, indicating lights for all above relays, on/off push buttons. ASD Motor Control Unit with Dry running relay, Magnetic Contactor, Circuit Breaker, EOCR, EVR, Volt Selector Switch, Ampere Selector Switch, Current Transformer etc. All contained in lockable cabinet complete in all respect.				
		Accessoires: Cable Termination Kit, MS Flanged Riser Pipes 120 ft Schedule 40, Sluice Valve, Non-return Valve, air release vlve, pressure guage, MS Nipple, MS Bend, bore cover plate, Installation clamp, Gaskets, Nut Bolts, Drop Cable 3x10mm2 140 ft length with cable connector & clamps, Electrode and Electrode wire 90 ft and other necessary fittings.	P/Job	1.00		
1.1.16	N/S	Providing, installing, testing, and commissioning of Hypo Dosing Chlorinator unit of European make, having an injection capacity of 8 liters/second and maximum operating pressure of 10 bar, complete in all respects as per specifications, drawings, and as directed by the Engineer Incharge.	P/Job	1.00		

ENGINEERING DESIGN AND CONSTRUCTION SUPERVISION SERVICES (EDCS)
PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT (PRSWSSP), CLUSTER SOUTH-III

TEHSIL BAHAWALNAGAR (CW-25) (PHASE-I)
BILL OF QUANTITIES
ABSTRACT OF COST

Bill No. 1: WATER SUPPLY SYSTEM

Bill No. 1.1.: Tubewell Installation (0.2 Cusec)

Sr. No.	Ref. MRS	Description	Unit	Quantity	Unit Rate (Rs)	Amount (Rs)
1.1.17	N/S	Providing and fixing Electromagnetic Flow meter of specified dia as per Delivery Size in Pump House complete in all respect. Typically of Following Specificication: Line Size: 6", DN150 Flanged, RF ANSI 150# Flow range: 32 ~ 320 m^3/h Liner Material: PTFE Electrode Material: 316L Stainless Steel Body Material: Carbon Steel Power Supply: 220 VAC Output: 4 ~ 20mA Protection Class: IP68 Accuracy: Class –II (OIML R49/ISO4064) ISO 9001 Certified manufacturer	P/Job	1.00		
1.1.18	N/S	Providing and fixing M.S cap 1/4 "(6mm) thick to cover tubewell casing pipe.	P/Job	1.00		
1.1.19	N/S	Providing / fixing M.S Centralizer of required Size as per drawing and directions of the engineers incharge.	P/Job	5.00		
					Total Amount	

ENGINEERING DESIGN AND CONSTRUCTION SUPERVISION SERVICES (EDCS)
PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT (PRSWSSP), CLUSTER SOUTH-III
TEHSIL BAHAWALNAGAR (CW-25) (PHASE-I)
BILL OF QUANTITIES
ABSTRACT OF COST

Bill No. 1: WATER SUPPLY SYSTEM

Bill No. 1.2: Tubewell Installation

Sr. No.	Ref. MRS	Description	Unit	Quantity	Unit Rate (Rs)	Amount (Rs)
1.2.1	23/2	Direct Rotary/ Reverse Rotary drilling of bore for tubewells, in all types of soil except shingle, gravel and rock:-				
		a) from ground level to 250 ft. (75 m) below ground level:-				
		i) 15" to 18" (375 to 450 mm) i/d	Rft of bore	120.00		
1.2.2	23/13	Providing and installing P.V.C. blind pipe, B.S.S. in tubewell bore hole, including sockets and solvents and jointing with strainer, (PS-3051=BS-3505), etc. complete. b) Class-D (12 bar) vii) 6" i/d (150 mm)	Per Rft	50.00		
		Blind Pipe				
1.2.3		v) 4" i/d (100 mm)	Per Rft	38.00		
		Strainer Pipe				
1.2.4	23/09	Providing and installing Fiberglass Reinforced Polypropelene (FRP) strainer of specifid wall thickness having slot size of 0.9 mm to 1.10 mm in Tubewell borehole i/c the cost of male/female coupling with Nylone Strip,studs complete in all respect as approved and directed by the Engineer Incharge. iii) 4" inch dia (5 mm thickness)	Per Rft	30.00		
		Bail Plug				
1.2.5	23/10	Providing and installing Fiber glass Reinforced Polypropelene (FRP) bail plug of specified wall thickness having slot size of 0.9 mm to 1.10 mm in Tubewell bore hole i/c the cost of male / female coupling with Nylone Strip, studs complete in all respect as approved and directed by the Engineer. iii) 4"dia (5mm thickness)	Per Rft	2.00		
		Delivery Pipe				
1.2.6	23/13	Providing and installing P.V.C. blind pipe, B.S.S. in tubewell bore hole, including sockets and solvents and jointing with strainer, (PS-3051=BS-3505), etc. complete. b) Class-D (12 bar)				
		iv) 3" i/d (75 m	Per Rft	20.00		
1.2.7	23/17	Shrouding with graded pea gravel 3/8 to 1/8 inch (10 to 3 mm) arround tubewell in bore hole.	Per Cft	209.05		
1.2.8	23/5	Furnishing sample of water from borehole.	Per set of 2 bottles	3.00		
1.2.9	23/16	Testing and developing of tubewell of size 6" (150 mm) i/d and above continuously.				
		i) upto 1.5 cs. Discharge	P. Hour	72.00		

ENGINEERING DESIGN AND CONSTRUCTION SUPERVISION SERVICES (EDCS)
PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT (PRSWSSP), CLUSTER SOUTH-III
TEHSIL BAHAWALNAGAR (CW-25) (PHASE-I)
BILL OF QUANTITIES
ABSTRACT OF COST

Bill No. 1: WATER SUPPLY SYSTEM

Bill No. 1.2: Tubewell Installation

Sr. No.	Ref. MRS	Description	Unit	Quantity	Unit Rate (Rs)	Amount (Rs)
1.2.10	23/31	Providing & mixing bentonite clay / powder have swelling factor of 1200% for lining /seal and plug earthen bore holes / ponds in the specified ratio conforming to IS:6186 for stabilization of soil as specified by the designer etc complete in all respect.	Per Kg.	5.00		
1.2.11	6/5	Cement concrete plain including placing, compacting, finishing and curing complete (including screening and washing of stone aggregate): (f) Ratio 1: 2: 4	100Cft	0.29		
1.2.12	1/1	Carriage of 100 Cft. (2.83 cu.m) of all materials like stone aggregate, spawl, kankar lime (unslaked), surkhi, etc. or 150 Cft. (4.25 cu.m) of timber, by truck or by any other means owned by the contractor. (crushed stone aggregate and bajri used in concrete items) (**Form Sargodha Querry)**	100 CFT	0.26		
1.2.13	N/S	Geophysical Logging of Borehole, including Data Collection, Interpretation, and Preparation/ Submission of Detailed Report to the Competent Authority/Incharge, Complete in All Respects.	P/Job	1.00		
1.2.14	N/S	Conducting Chemical, Physical, and Arsenic Analysis of Water through an Approved Water Testing Laboratory, including Collection, Testing, and Submission of Test Report to the Competent Authority/Incharge, Complete in All Respects.	P/Job	1.00		
1.2.15	N/S	Supplying, installing, testing and commissioning of submersible water supply pump set of Approved manufacturer of HUD & PHED and should be ISO 9001 Certified, complete in all respects as per specifications and direction of the Engineer Incharge. The pump set shall have the following specifications: Discharge: 0.25 Cusec Total Head: 250 ft Setting Depth: 100 ft Motor rating: 15 HP Speed: 2900 RPM				
		Submersible Borehole Pump Accessories including Installation: Cable transmission kit, MS Flang Riser pipe 3" Dia 100 Ft, Sluice Valve, NRV, MS Nipple, Bend, Cover Plate, Installation Clamp, Gaskets, Nut Bolts, Cable 3x6 mm2, with Cable Connecter and Clamps.				

ENGINEERING DESIGN AND CONSTRUCTION SUPERVISION SERVICES (EDCS)
PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT (PRSWSSP), CLUSTER SOUTH-III
TEHSIL BAHAWALNAGAR (CW-25) (PHASE-I)
BILL OF QUANTITIES
ABSTRACT OF COST

Bill No. 1: WATER SUPPLY SYSTEM

Bill No. 1.2: Tubewell Installation

Sr. No.	Ref. MRS	Description	Unit	Quantity	Unit Rate (Rs)	Amount (Rs)
		VFD mounted Motor Control Unit (MCU) consisting of MCCB over/under voltage relay, phase reversal relay, volt meter, ampare meter, EVR, Volt selector Switch, ampare selector switch, current transformer, indicating lights for all acove relay, On/Of Push Buttens,MCU with Dry Runnig Relay, Circuit breaker, change over switch etc, all contained in lockable cabinet complete in all Resppect.	P/Job	1.00		
1.2.16	N/S	Providing, installing, testing, and commissioning of Hypo Dosing Chlorinator unit of European make, having an injection capacity of 8 liters/second and maximum operating pressure of 10 bar, complete in all respects as per specifications, drawings, and as directed by the Engineer Incharge.	P/Job	1.00		
1.2.17	N/S	Providing and fixing Electromagnetic Flow meter of specified dia as per Delivery Size in Pump House complete in all respect. Typically of Following Specificication: Line Size: 3", DN80 Flanged, RF ANSI 150# Flow range: 9 ~ 90 m³/h Liner Material: PTFE Electrode Material: 316L Stainless Steel Body Material: Carbon Steel Power Supply: 220 VAC Output: 4 ~ 20mA Protection Class: IP68 Accuracy class-III (OIMLR49/ISO4064) ISO 9001 certified Manufacturer	P/Job	1.00		
1.2.18	N/S	Providing / fixing M.S Centralizer of required Size as per drawing and directions of the engineers incharge.	P/Job	5.00		
					Total Amount	

ENGINEERING DESIGN AND CONSTRUCTION SUPERVISION SERVICES (EDCS)
PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT (PRSWSSP), CLUSTER SOUTH-III

TEHSIL BAHAWALNAGAR (CW-25) (PHASE-I)
BILL OF QUANTITIES
ABSTRACT OF COST

Bill No. 1: WATER SUPPLY SYSTEM

Bill No. 1.3: Tubewell Installation (0.1 cusecs)

Sr. No.	Ref. MRS	Description	Unit	Quantity	Unit Rate (Rs)	Amount (Rs)
1.3.1	23/2a(i)	Direct Rotary/ Reverse Rotary drilling of bore for tubewells, in all types of soil except shingle, gravel and rock:-				
		a) from ground level to 250 ft. (75 m) below ground level:-	Per Rft. of bore			
		i) 15" to 18" (375 to 450 mm) i/d		300.00		
		Housing Pipe				
1.3.2	23/13	Providing and installing P.V.C. blind pipe, B.S.S. in tubewell bore hole, including sockets and solvents and jointing with strainer, (PS-3051=BS-3505), etc. complete. b) Class-D (12 bar) vii) 6" i/d (150 mm)	Per Rft	90.00		
		Blind Pipe				
1.3.3		v) 4" i/d (100 mm)	Per Rft	160.00		
		Strainer Pipe				
1.3.4	23/09	Providing and installing Fiberglass Reinforced Polypropelene (FRP) strainer of specifid wall thickness having slot size of 0.9 mm to 1.10 mm in Tubewell borehole i/c the cost of male/female coupling with Nylone Strip,studs complete in all respect as approved and directed by the Engineer Incharge. iii) 4" inch dia (5 mm thickness)	Per Rft	30.00		
		Bail Plug				
1.3.5	23/10	Providing and installing Fiber glass Reinforced Polypropelene (FRP) bail plug of specified wall thickness having slot size of 0.9 mm to 1.10 mm in Tubewell bore hole i/c the cost of male / female coupling with Nylone Strip, studs complete in all respect as approved and directed by the Engineer. iii) 4"dia (5mm thickness)	Per Rft	20.00		
		Delivery Pipe				
1.3.6	23/13	Providing and installing P.V.C. blind pipe, B.S.S. in tubewell bore hole, including sockets and solvents and jointing with strainer, (PS-3051=BS-3505), etc. complete. b) Class-D (12 bar)				
		iv) 3" i/d (75 m	Per Rft	40.00		
1.3.7	23/17	Shrouding with graded pea gravel 3/8 to 1/8 inch (10 to 3 mm) arround tubewell in bore hole.	Per Cft	220.00		
1.3.8	23/5	Furnishing sample of water from borehole.	Per set of 2 bottles	6.00		
1.3.9	23/16	Testing and developing of tubewell of size 6" (150 mm) i/d and above continuously.				
		i) upto 1.5 cs. Discharge	P. Hour	144.00		

ENGINEERING DESIGN AND CONSTRUCTION SUPERVISION SERVICES (EDCS)
PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT (PRSWSSP), CLUSTER SOUTH-III

TEHSIL BAHAWALNAGAR (CW-25) (PHASE-I)
BILL OF QUANTITIES
ABSTRACT OF COST

Bill No. 1: WATER SUPPLY SYSTEM

Bill No. 1.3: Tubewell Installation (0.1 cusecs)

Sr. No.	Ref. MRS	Description	Unit	Quantity	Unit Rate (Rs)	Amount (Rs)
1.3.10	23/31	Providing & mixing bentonite clay / powder have swelling factor of 1200% for lining /seal and plug earthen bore holes / ponds in the specified ratio conforming to IS:6186 for stabilization of soil as specified by the designer etc complete in all respect.	Per Kg.	20.00		
1.3.11	6/5	Cement concrete plain including placing, compacting, finishing and curing complete (including screening and washing of stone aggregate): (f) Ratio 1: 2: 4	100Cft	0.59		
1.3.12	1/1	Carriage of 100 Cft. (2.83 cu.m) of all materials like stone aggregate, spawl, kankar lime (unslaked), surkhi, etc. or 150 Cft. (4.25 cu.m) of timber, by truck or by any other means owned by the contractor. (crushed stone aggregate and bajri used in concrete items) (**Form Sargodha Querry)**	100 CFT	0.52		
1.3.13	N/S	Geophysical Logging of Borehole, including Data Collection, Interpretation, and Preparation/ Submission of Detailed Report to the Competent Authority/Incharge, Complete in All Respects.	P/Job	2.00		
1.3.14	N/S	Conducting Chemical, Physical, and Arsenic Analysis of Water through an Approved Water Testing Laboratory, including Collection, Testing, and Submission of Test Report to the Competent Authority/Incharge, Complete in All Respects.	P/Job	2.00		
1.3.15	N/S	Supplying, installing, testing and commissioning of submersible water supply pump set of Approved manufacturer of HUD & PHED and should be ISO 9001 Certified, complete in all respects as per specifications and direction of the Engineer Incharge. The pump set shall have the following specifications: Pump Set: Flow: 0.1 Cusec Head: 250 ft Riser Pipe Upto: 120 ft Material: Complete Pump Set in SS304 (EN 1.4301) Maximum Operating Temperature: 40C or higher Maximum Liquid Temperature: 40C or higher Minimum Efficiency Index: 0.40 or more Approved for drinking water ACS,DM174 or equivalent 3×400V, 50 Hz, 2 Pole, Submersible IP68 motor, Insulation class F				

TEHSIL BAHAWALNAGAR (CW-25) (PHASE-I)
BILL OF QUANTITIES
ABSTRACT OF COST

Bill No. 1: WATER SUPPLY SYSTEM

Bill No. 1.3: Tubewell Installation (0.1 cusecs)

Sr. No.	Ref. MRS	Description	Unit	Quantity	Unit Rate (Rs)	Amount (Rs)
		Motor Control Unit (MCU): MCU (Motor Control Unit) with VFD consisting of MCCB, Over/Under voltage relay, Phase reversal relay, volt meter, ampere meter, indicating lights for all above relays, on/off push buttons. ASD Motor Control Unit with Dry running relay, Magnetic Contactor, Circuit Breaker, EOCR, EVR, Volt Selector Switch, Ampere Selector Switch, Current Transformer etc. All contained in lockable cabinet complete in all respect.		-		
		Accessoires: Cable Termination Kit, MS Flanged Riser Pipes 120 ft Schedule 40, Sluice Valve, Non-return Valve, air release vlve, pressure guage, MS Nipple, MS Bend, bore cover plate, Installation clamp, Gaskets, Nut Bolts, Drop Cable 3×4 mm2 140 ft length with cable connector & clamps, Electrode and Electrode wire 90 ft and other necessary fittings.	P/Job	2.00		
1.3.16	N/S	Providing, installing, testing, and commissioning of Hypo Dosing Chlorinator unit of European make, having an injection capacity of 8 liters/second and maximum operating pressure of 10 bar, complete in all respects as per specifications, drawings, and as directed by the Engineer Incharge.	P/Job	2.00		
1.3.17	N/S	Providing and fixing Electromagnetic Flow meter of specified dia as per Delivery Size in Pump House complete in all respect. Typically of Following Specificication: Line Size: 3", DN80 Flanged, RF ANSI 150# Flow range: 9 ~ 90 m^3/h Liner Material: PTFE Electrode Material: 316L Stainless Steel Body Material: Carbon Steel Power Supply: 220 VAC Output: 4 ~ 20mA Protection Class: IP68 Accuracy: Class –II (OIML R49/ISO4064) ISO 9001 Certified manufacturer	P/Job	2.00		
1.3.18	N/S	Providing / fixing M.S Centralizer of required Size as per drawing and directions of the engineers incharge.	P/Job	10.00		
					Total Amount	

ENGINEERING DESIGN AND CONSTRUCTION SUPERVISION SERVICES (EDCS)
PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT (PRSWSSP), CLUSTER SOUTH-III

TEHSIL BAHAWALNAGAR (CW-25) (PHASE-I)
BILL OF QUANTITIES
ABSTRACT OF COST

Bill No. 1: WATER SUPPLY SYSTEM

Bill No. 1.4: Tubewell Installation Ejector Pump

Sr. No.	Ref. MRS	Description	Unit	Quantity	Unit Rate (Rs)	Amount (Rs)
1.4.1	23/2a(i)	Direct Rotary/ Reverse Rotary drilling of bore for tubewells, in all types of soil except shingle, gravel and rock:-				
		a) from ground level to 250 ft. (75 m) below ground level:-	Per Rft. of bore			
		i) 15" to 18" (375 to 450 mm) i/d		1,420.00		
		b) exceeding 250 ft. (75 m) depth below ground level:-	Per Rft. of bore			
		i) 15" to 18" (375 to 450 mm) i/d		75.00		
		Housing Pipe				
1.4.1	23/13	Providing and installing P.V.C. blind pipe, B.S.S. in tubewell bore hole, including sockets and solvents and jointing with strainer, (PS-3051=BS-3505), etc. complete. b) Class-D (12 bar) vii) 6" i/d (150 mm)	Per Rft	407.00		
		Blind Pipe				
1.4.2		v) 4" i/d (100 mm)	Per Rft	873.00		
		Strainer Pipe				
1.4.3	23/09	Providing and installing Fiberglass Reinforced Polypropelene (FRP) strainer of specifid wall thickness having slot size of 0.9 mm to 1.10 mm in Tubewell borehole i/c the cost of male/female coupling with Nylone Strip,studs complete in all respect as approved and directed by the Engineer Incharge. iii) 4" inch dia (5 mm thickness)	Per Rft	145.00		
		Bail Plug				
1.4.4	23/10	Providing and installing Fiber glass Reinforced Polypropelene (FRP) bail plug of specified wall thickness having slot size of 0.9 mm to 1.10 mm in Tubewell bore hole i/c the cost of male / female coupling with Nylone Strip, studs complete in all respect as approved and directed by the Engineer. iii) 4"dia (5mm thickness)	Per Rft	90.00		
		Delivery Pipe				
1.4.5	23/13	Providing and installing P.V.C. blind pipe, B.S.S. in tubewell bore hole, including sockets and solvents and jointing with strainer, (PS-3051=BS-3505), etc. complete. b) Class-D (12 bar)				
		iv) 3" i/d (75 m	Per Rft	180.00		
1.4.6	23/17	Shrouding with graded pea gravel 3/8 to 1/8 inch (10 to 3 mm) arround tubewell in bore hole.	Per Cft	990.00		
1.4.7	23/5	Furnishing sample of water from borehole.	Per set of 2 bottles	27.00		
1.4.8	23/16	Testing and developing of tubewell of size 6" (150 mm) i/d and above continuously.				
		i) upto 1.5 cs. Discharge	P. Hour	648.00		

ENGINEERING DESIGN AND CONSTRUCTION SUPERVISION SERVICES (EDCS)
PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT (PRSWSSP), CLUSTER SOUTH-III

TEHSIL BAHAWALNAGAR (CW-25) (PHASE-I)
BILL OF QUANTITIES
ABSTRACT OF COST

Bill No. 1: WATER SUPPLY SYSTEM

Bill No. 1.4: Tubewell Installation Ejector Pump

Sr. No.	Ref. MRS	Description	Unit	Quantity	Unit Rate (Rs)	Amount (Rs)
1.4.9	23/31	Providing & mixing bentonite clay / powder have swelling factor of 1200% for lining /seal and plug earthen bore holes / ponds in the specified ratio conforming to IS:6186 for stabilization of soil as specified by the designer etc complete in all respect.	Per Kg.	90.00		
1.4.10	6/5	Cement concrete plain including placing, compacting, finishing and curing complete (including screening and washing of stone aggregate): (f) Ratio 1: 2: 4	100Cft	2.65		
1.4.12	23/32	P/F Ejector Pump of specified Suction and Delivery heads,coupled with Single Phase Seimen Electric Motor of required rating for water supply i/c the cost of connection charges, necessary wire, PVC pipes etc complete in all respect as approved and directed by the Engineer Incharge. ii) G-IV (2-1/2"x2") with 2.5 HP Electric Motor, 38-Mtr Suction and 38 M delivery head	Each	9.00		
1.4.12	1/1	Carriage of 100 Cft. (2.83 cu.m) of all materials like stone aggregate, spawl, kankar lime (unslaked), surkhi, etc. or 150 Cft. (4.25 cu.m) of timber, by truck or by any other means owned by the contractor. (crushed stone aggregate and bajri used in concrete items) (**Form Sargodha Querry)**	100 CFT	2.33		
1.4.13	N/S	Geophysical Logging of Borehole, including Data Collection, Interpretation, and Preparation/ Submission of Detailed Report to the Competent Authority/Incharge, Complete in All Respects.	P/Job	9.00		
1.4.14	N/S	Conducting Chemical, Physical, and Arsenic Analysis of Water through an Approved Water Testing Laboratory, including Collection, Testing, and Submission of Test Report to the Competent Authority/Incharge, Complete in All Respects.	P/Job	9.00		
1.4.15	N/S	Providing, installing, testing, and commissioning of Hypo Dosing Chlorinator unit of European make, having an injection capacity of 8 liters/second and maximum operating pressure of 10 bar, complete in all respects as per specifications, drawings, and as directed by the Engineer Incharge.	P/Job	9.00		

TEHSIL BAHAWALNAGAR (CW-25) (PHASE-I)
BILL OF QUANTITIES
ABSTRACT OF COST

Bill No. 1: WATER SUPPLY SYSTEM

Bill No. 1.4: Tubewell Installation Ejector Pump

Sr. No.	Ref. MRS	Description	Unit	Quantity	Unit Rate (Rs)	Amount (Rs)
1.4.16	N/S	Providing and fixing Electromagnetic Flow meter of specified dia as per Delivery Size in Pump House complete in all respect. Typically of Following Specificication: Line Size: 3", DN80 Flanged, RF ANSI 150# Flow range: 9 ~ 90 m^3/h Liner Material: PTFE Electrode Material: 316L Stainless Steel Body Material: Carbon Steel Power Supply: 220 VAC Output: 4 ~ 20mA Protection Class: IP68 Accuracy: Class –II (OIML R49/ISO4064) ISO 9001 Certified manufacturer	P/Job	9.00		

ENGINEERING DESIGN AND CONSTRUCTION SUPERVISION SERVICES (EDCS)
PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT (PRSWSSP), CLUSTER SOUTH-III

TEHSIL BAHAWALNAGAR (CW-25) (PHASE-I)
BILL OF QUANTITIES
ABSTRACT OF COST

Bill No. 1: WATER SUPPLY SYSTEM

Bill No. 1.4: Tubewell Installation Ejector Pump

Sr. No.	Ref. MRS	Description	Unit	Quantity	Unit Rate (Rs)	Amount (Rs)
1.4.17	N/S	Providing and fixing M.S cap 1/4 "(6mm) thick to cover tubewell casing pipe.	P/Job	9.00		
1.4.18	N/S	Providing / fixing M.S Centralizer of required Size as per drawing and directions of the engineers incharge.	P/Job	45.00		
					Total Amount	

TEHSIL BAHAWALNAGAR (CW-25) (PHASE-I)
BILL OF QUANTITIES
ABSTRACT OF COST

Bill No. 1: WATER SUPPLY SYSTEM

Bill No. 1.5: Installation of Pump and RO Plant

Sr. No.	Ref. MRS	Description	Unit	Quantity	Unit Rate (Rs)	Amount (Rs)
1.5.1	23/2 a(i)	Direct Rotary/ Reverse Rotary drilling of bore for tubewells, in all types of soil except shingle, gravel and rock:-				
		a) from ground level to 250 ft. (75 m) below ground level:-	Per Rft. of bore			
		i) 15" to 18" (375 to 450 mm) i/d		505.00		
		Housing Pipe				
1.5.2	23/13	Providing and installing P.V.C. blind pipe, B.S.S. in tubewell bore hole, including sockets and solvents and jointing with strainer, (PS-3051=BS-3505), etc. complete. b) Class-D (12 bar) v) 4" i/d (100 mm)	Per Rft	325.00		
		Strainer Pipe				
1.5.3	23/09	Providing and installing Fiberglass Reinforced Polypropelene (FRP) strainer of specifid wall thickness having slot size of 0.9 mm to 1.10 mm in Tubewell borehole i/c the cost of male/female coupling with Nylone Strip,studs complete in all respect as approved and directed by the Engineer Incharge. iii) 4" inch dia (5 mm thickness)	Per Rft	120.00		
		Bail Plug				
1.5.4	23/10	Providing and installing Fiber glass Reinforced Polypropelene (FRP) bail plug of specified wall thickness having slot size of 0.9 mm to 1.10 mm in Tubewell bore hole i/c the cost of male / female coupling with Nylone Strip, studs complete in all respect as approved and directed by the Engineer. iii) 4"dia (5mm thickness)	Per Rft	60.00		
		Delivery Pipe				
1.5.5	23/13	Providing and installing P.V.C. blind pipe, B.S.S. in tubewell bore hole, including sockets and solvents and jointing with strainer, (PS-3051=BS-3505), etc. complete. b) Class-D (12 bar)				
		iv) 3" i/d (75 m	Per Rft	120.00		
1.5.6	23/17	Shrouding with graded pea gravel 3/8 to 1/8 inch (10 to 3 mm) arround tubewell in bore hole.	Per Cft	660.00		
1.5.7	23/5	Furnishing sample of water from borehole.	Per set of 2 bottles	18.00		
1.5.8	23/16	Testing and developing of tubewell of size 6" (150 mm) i/d and above continuously.				
		i) upto 1.5 cs. Discharge	P. Hour	432.00		
1.5.9	23/31	Providing & mixing bentonite clay / powder have swelling factor of 1200% for lining /seal and plug earthen bore holes / ponds in the specified ratio conforming to IS:6186 for stabilization of soil as specified by the designer etc complete in all respect.	Per Kg.	60.00		

TEHSIL BAHAWALNAGAR (CW-25) (PHASE-I)
BILL OF QUANTITIES
ABSTRACT OF COST

Bill No. 1: WATER SUPPLY SYSTEM

Bill No. 1.5: Installation of Pump and RO Plant

Sr. No.	Ref. MRS	Description	Unit	Quantity	Unit Rate (Rs)	Amount (Rs)
1.5.10	6/5	Cement concrete plain including placing, compacting, finishing and curing complete (including screening and washing of stone aggregate): (f) Ratio 1: 2: 4	100Cft	1.77		
1.5.11	1/1	Carriage of 100 Cft. (2.83 cu.m) of all materials like stone aggregate, spawl, kankar lime (unslaked), surkhi, etc. or 150 Cft. (4.25 cu.m) of timber, by truck or by any other means owned by the contractor. (crushed stone aggregate and bajri used in concrete items) (**Form Sargodha Querry)**	100 CFT	1.56		
1.5.12	23/32	P/F Ejector Pump of specified Suction and Delivery heads,coupled with Single Phase Seimen Electric Motor of required rating for water supply i/c the cost of connection charges, necessary wire, PVC pipes etc complete in all respect as approved and directed by the Engineer Incharge. ii) G-IV (2-1/2"x2") with 2.5 HP Electric Motor, 38-Mtr Suction and 38 M delivery head	Each	6.00		
1.5.13	N/S	Geophysical Logging of Borehole, including Data Collection, Interpretation, and Preparation/ Submission of Detailed Report to the Competent Authority/Incharge, Complete in All Respects.	P/Job	6.00		
1.5.14	N/S	Conducting Chemical, Physical, and Arsenic Analysis of Water through an Approved Water Testing Laboratory, including Collection, Testing, and Submission of Test Report to the Competent Authority/Incharge, Complete in All Respects.	P/Job	6.00		
1.5.15	N/S	Design, Supply, Install, Testing and Commissioning of RO water filtration plant, capable of removing Turbidity, Heavy Metals, Bacteria & Viruses and Dissolved Solids, having capacity of 2000 litres/ hour, blending of UF filtered water (if required) and fully automated (Auto filtration, flush and backwash process) complete in all respects as per drawings, specifications and directions of the Engineer. The major components include;				

TEHSIL BAHAWALNAGAR (CW-25) (PHASE-I)
BILL OF QUANTITIES
ABSTRACT OF COST

Bill No. 1: WATER SUPPLY SYSTEM

Bill No. 1.5: Installation of Pump and RO Plant

Sr. No.	Ref. MRS	Description	Unit	Quantity	Unit Rate (Rs)	Amount (Rs)
		Feed, Backwash and High Pressure Pumps (Stainless Steel, NEMA Insulation Class F and Pump Efficiency ≥ 50%) Silica Sand Media (Suspended Solids Removal upto 100 micron) Activated Carbon Media (Coconut shells, NSF Certified Manufacturer) Arsenic Removal Media (Ferric Hydroxide, NSF Certified) FRP Vessels (OP 150 psi, NSF Certified) Screen Filter (Washable, 70-100 Micron, Stainless Steel) UF Module for Blending water, if required, (Multibore, PES/ PVDF Material, NSF Certified, Pore Size ≤ 0.02µm, Bacteria removal efficiency 99.9999% (log 6), Viruses removal efficiency 99.99% (log 4) RO Membranes (Salt Rejection > 97%, Permeate efficiency ≥ 50%) Raw and Product Water Tanks (500 Gallons, Food Garde Material) Pressure Gauges, Rotameters, Flow Meters, Level Switches/ Sensors,				
		Concentrate Regulating Valve, Multiport valves and Solenoid Valves Stainless Steel 304 Frame Skid Panel Control panel, for complete system including PLC (Compatible with GPRS/ Remote Monitoring), Mimic Panel (10"), Connections, Sensors, Actuators andany other complete in all aspects . Pipe work including feed water pipe line connection and delivery pipeline and necessary gate and flow regulating valves. Origin of Pumps, UF and RO membranes, PLC, FRP Vessels shall be European/ USA/ Japan region or equivalent.	P/Job	6.00		
					Total Amount	

ENGINEERING DESIGN AND CONSTRUCTION SUPERVISION SERVICES (EDCS)
PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT (PRSWSSP), CLUSTER SOUTH-III

TEHSIL BAHAWALNAGAR (CW-25) (PHASE-I)
BILL OF QUANTITIES
ABSTRACT OF COST

Bill No. 1: WATER SUPPLY SYSTEM

Bill No. 1.6: Stand Post with Tubewell Chamber

Sr. No.	Ref. MRS	Description	Unit	Quantity	Unit Rate (Rs)	Amount (Rs)
1.6.1	3/21	Excavation in foundation of building, bridges and other structures, including dagbelling, dressing, refilling in layers around structure with excavated earth, watering and ramming lead upto one chain (30 m)lift upto 5 ft (1.5m)				
		1) By Manual				
		ii) in ordinary soil.	1000 Cft.	9.03		
1.6.2	6/3	Cement concrete brick or stone ballast 1½ " to 2" (40 mm to 50 mm) gauge, in foundation and plinth:-				
		(d) Ratio 1: 6:12 (with Brick ballast)	100 Cft	20.96		
1.6.3	7/4	Pacca brick work in foundation and plinth in: i) Cement, sand mortar Ratio 1:6	100 Cft	49.52		
1.6.4	6/37	Providing and laying damp proof course of cement concrete 1:2:4 (using cement, sand and shingle), including bitumen coating:				
		b) with 2 coats of bitumen:				
		ii) 2" thick	100 Sft	11.44		
1.6.5	6/39	Providing and laying vertical damp proof course with cement sand plaster and bitumen coating:- (b) with 2 coats of bitumen:-				
		ii) Ratio 1:3				
		b) ¾ " thick (20mm)	100 Sft	6.24		
1.6.6	7/5	Pacca brick work in ground floor (super structure) i). Cement, sand mortar Ratio 1:5	100 Cft	52.40		
1.6.7	6/6	Providing and laying reinforced cement concrete (including prestressed concrete), using coarse sand and screened graded and washed aggregate, in required shape and design, including forms, moulds, shuttering, lifting, compacting, curing, rendering and finishing exposed surface, complete (but excluding the cost of steel reinforcement, its fabrication and placing in position, etc.):-				
		(a) (i) Reinforced cement concrete in roof slab, beams, columns lintels, girders and other structural members laid in situ or precast laid in position, or prestressed members cast in situ, complete in all respects:-				
		(3) Type C (nominal mix 1: 2: 4)	Per Cft	2,784.00		
1.6.8	6/12 b	Providing and fabrication of mild steel reinforcement for cement concrete, including cutting, bending, laying in position, making joints and fastenings, including cost of binding wire and labor charges for binding of steel reinforcement (also includes removal of rust from bars), Deformed bars (Grade 60)	100 Kg	82.11		
1.6.9	10/3	Supplying and filling sand under floor; or plugging in wells.	100 Cft	69.20		

TEHSIL BAHAWALNAGAR (CW-25) (PHASE-I)
BILL OF QUANTITIES
ABSTRACT OF COST

Bill No. 1: WATER SUPPLY SYSTEM

Bill No. 1.6: Stand Post with Tubewell Chamber

Sr. No.	Ref. MRS	Description	Unit	Quantity	Unit Rate (Rs)	Amount (Rs)
1.6.10	10/16	Providing and laying topping of cement concrete 1:2:4, including surface finishing and dividing in panels:-				
		(e) 2"(50 mm) thick	100 Sft	41.12		
1.6.11	11/18	Cement pointing struck joints, on walls, upto 20' (6.00 m) hiehgt:- b) ratio 1:3	100 Sft	92.08		
1.6.12	11/9	Cement plaster 1:4 upto 20' (6.00 m) height:- b) ½" (13 mm) thick	100 Sft	94.50		
	.					
1.6.13	11/12	Cement plaster 3/8" (10 mm) thick under soffit of R.C.C. roof slabs only, upto 20' height				
		. b) 1:3	100 Sft	46.15		
1.6.14	9/5	Single layer of tiles 9"x4½"x1½" (225x113x40 mm) laid over 4"(100 mm) earth and 1" (25 mm) mud plaster without Bhoosa, grouted with cement sand 1:3 on top of RCC roof slab, provided with 34 lbs.per %Sft. or 1.72 Kg/Sq.m bitumen coating sand blinded.	100 Sft	48.58		
1.6.15	10/46-17.65 deduction for matt finishes	Providing and laying superb quality Porcelain glazed tiles flooring of Master/ Stile brand or approved equivalent manufacturer of specified size in approved design, Color and Shade with adhesive/ bond over 3/4" thick (1:3) cement plaster i/c the cost of sealer for finishing the joints i/c cutting grinding complete in all respect as approved and directed by the Engineer Incharge. a) Full body Matt tiles				
		(ii) 300mmx 600mm	Sft	960.00		
1.6.16	10/36-18.90 deduction for matt finishes	Providing and laying superb quality Porcelain glazed tiles of Master/ Stile brand or approved equivalent manufacturer, skirting/ dado of specified size, Color and Shade with adhesive/ bond over 1/2" thick (1:2) cement plaster i/c the cost of matching sealer for finishing the joints, cutting grinding complete in all respect as approved and directed by the Engineer Incharge. a) Full body Matt tiles				
		(ii) 300mmx 600mm	Sft	2,688.00		
1.6.17	10/48	Providing and laying 3/4" thick full width Prepolished Marble slab for Vanities/ Shelves/ Treads/ Window Cills, having Uniform texture (Spotless) with adhesive bond over 3/4" thick (1:2) cement sand mortor i/c the cost of matching sealer complete in all respects as approved and directed by the Engineer Incharge.				
		i) China Verona	Sft	962.00		

TEHSIL BAHAWALNAGAR (CW-25) (PHASE-I)
BILL OF QUANTITIES
ABSTRACT OF COST

Bill No. 1: WATER SUPPLY SYSTEM

Bill No. 1.6: Stand Post with Tubewell Chamber

Sr. No.	Ref. MRS	Description	Unit	Quantity	Unit Rate (Rs)	Amount (Rs)
1.6.18	10-35	Mosaic dado or skirting with one part of cement and marble powder in the ratio of 3:1 and two parts of marble chips, laid over ½"(13 mm) thick cement plaster 1:3, including rubbing and polishing, complete with finishing: (b) using white cement : ii) ½"(13 mm) thick	100 Sft	1.84		
1.6.19	10/43	Providing and laying Tuff Pavers, having 7000 PSI, crushing strength of approved manufacturer, over 2" to 3" sand cushion i/c grouting with sand in joints i/c finishing to require slope . complete in all respect. (50% Grey / 50% Coloured)				
		a) 50-mm thick	Sft	1,411.20		
1.6.20	11/26	White washing a) new surface:- iii) three coats	100 Sft	77.45		
1.6.21	25/31	Making and fixing steel grated door with 1/16" thick (1.5mm) sheeting, including angle iron frame 2"x2"x3/8" (50x50x10 mm) and ¾" (20 mm) square bars 4" (100 mm) centre to centre, with locking arrangement.				
			Per Sft	560.00		
1.6.22	12/15	Providing and fixing mild steel chowkat of doors, windows, C.window, etc. including holdfast, making and threading holes for hinges, etc. complete:- a) M.S. angle iron 1½"x 1½"x ¼" (40x40x6 mm) welded with M.S. flat 2"x ¼" (50 mm x 6 mm)	Per Sft	560.00		
1.6.23	25/32	Making and fixing grating in opening, including fixing at site with flat iron 2"x3/8" (50x10 mm) and ¾" (19 mm) square bars, at 4" (100 mm) centre to centre.	Per Sft	1,464.00		
1.6.24	18-23	Providing and fixing M.S Grating comprising of Angle Iron frame size 1.50"x1.50"x3/16" and 1/2" square bars duly welded @ 4" c/c, including painting charges etc complete in all respect.(For Drain)	Per Sft	234.08		
1.6.25	9/15	Khuras on roof 2'x2'x6" (600 x 600 x 150 mm)	Each	8.00		
1.6.26	9/16	Bottom Khuras of brick masonry in cement mortar 1:6, 4' x 2' x 4.5" over 3" cement concrete 1:4:8	Each	8.00		

TEHSIL BAHAWALNAGAR (CW-25) (PHASE-I)
BILL OF QUANTITIES
ABSTRACT OF COST

Bill No. 1: WATER SUPPLY SYSTEM

Bill No. 1.6: Stand Post with Tubewell Chamber

Sr. No.	Ref. MRS	Description	Unit	Quantity	Unit Rate (Rs)	Amount (Rs)
1.6.27	1/1	Carriage of 100 Cft. (2.83 cu.m) of all materials like stone aggregate, spawl, kankar lime (unslaked), surkhi, etc. or 150 Cft. (4.25 cu.m) of timber, by truck or by any other means owned by the contractor. (crushed stone aggregate and bajri used in concrete items) (**Form Sargodha Querry)**	100 Cft.	55.38		
1.6.28	25/61	P/F Iron door comprising of specified leaves made of 1-1/4" x1-1/4" x3/16" MS angle iron for leaf frame, diagonal and horizontal braces duly welded with MS. sheet 18-SWG i/c the cost of sliding bolt, tower bolt and painting 3-coats but excluding the cost of Chowkat complete in all respect as approved and directed by the Engineer incharge.				
		(i) Single Leaf	Per Sft	256.00		
1.6.29	12/15	Providing and fixing mild steel chowkat of doors, windows, C.window, etc. including holdfast, making and threading holes for hinges, etc. complete:- a) M.S. angle iron 1½"x 1½"x ¼" (40x40x6 mm) welded with M.S. flat 2"x ¼" (50 mm x 6 mm)	Per Sft	256.00		
1.6.30	25/45	Providing and fixing steel windows using M.S. sheet (16 SWG) moulded tubular pipe 1½"x1½" (40x40mm) for frameand 1¼"x1¼" (30x30mm) for leaves including M.S. square bars ¼"x¼" (6x6 mm) welded around each panel of frame, 5 mm thick glass panes fixed with double M.S. square tubular pipe 3/8"x3/8" (10x10mm) (22 SWG) beading with U' shaped rubber lining, brass fitting,holdfast, including painting three coats complete in all respects.	Per Sft	96.00		
1.6.31	25/57	Providing and fixing M.S. flat ½"x1/8" (13mm x 3mm) grill including ¾" x 1/8" (20 mmx3 mm) M.S. flat frame, in windows of approved design, including painting three coats, complete in all respects.	Per Sft	96.00		
1.6.32	25/10+ 11	Fabrication & Erection of heavy steel work, with angle, tees, flat iron round iron and sheet iron for making trusses, girders, tanks, etc., including cutting, drilling, revitting, handling, assembling and fixing, including erection in position. (Top Cover, & Girder)	100 Kg	10.24		
1.6.33	23-52	Providing and fixing Chain Pulley Block of 5 ton capacity with 5 meter length of chain, as per required specifications complete in all respect and as approved by the Engineer Incharge.	Each	8.00		
		Plumbing Work				

TEHSIL BAHAWALNAGAR (CW-25) (PHASE-I)
BILL OF QUANTITIES
ABSTRACT OF COST

Bill No. 1: WATER SUPPLY SYSTEM

Bill No. 1.6: Stand Post with Tubewell Chamber

Sr. No.	Ref. MRS	Description	Unit	Quantity	Unit Rate (Rs)	Amount (Rs)
1.6.34	19-16	Providing and fixing, chromium plated soap dish.	Each	8.00		
1.6.35	19-5	Providing and fitting white glazed earthen ware water closet squartter type, with separate foot rest.	Each	8.00		
1.6.36	19-7	Providing and fitting glazed earthen ware wash hand basin /vanity 56x40 cm (22"x16") including bracket set, waste pipe and waste coupling, etc				
		i) white, with pedestal	Each	8.00		
1.6.37	19-45	Providing and fixing brass stop cock/bib cock:- b)20 mm (¾") dia	Each	96.00		
1.6.38	19-28	Providing and fixing chromium plated tee stop cock 15mm (½").	Each	16.00		
1.6.39	19-52	Providing and fixing CP bath Room Set made of Sonex/Master/Faisal or approved equvilent manufacturer, comprising of 3-No Tee stop cocks, lever type Basin Mixer, double Bib Cock, open wall shower, Muslim shower,waste coupling and bottle trap etc. complete in all respect as approved and directed by the Engineer incharge.				
		v) Muslim shower	Each	8.00		
1.6.40	19-47	Providing, fixing, testing and commissioning of µ-PVC (Unplasticized Polyvinyl Chloride) Nikasi/ SWV pipe, Dadex / Popular / Beta or approved equivalent manufacturer, plain / Bell Ended / Z - Joints conforming to BS 4514 / BS 5255 - EN 1329 including the cost of specials and Solvents complete in all respects, as per drawings & specifications and / or as approved and directed by the Engineer Incharge. (v) 110 mm	Per Rft	200.00		
		(iv) 82mm	Per Rft	400.00		
1.6.41	19-49	Providing, fixing, testing and commissioning of µ-PVC (Unplasticized polyvinyl Chloride) Nikasi/ waste pipe Fittings make of Dadex /Popular/Beta or approved equivalent manufacturer, conforming to BS 4514 / BS 5255 including the cost of Solvents complete in all respect as approved and directed by the Engineer Incharge.				
		c) Vent Cowel				
		(ii) 3" dia	Each	8.00		
		d) Clean Out				
		(ii) 3" dia	Each	8.00		
		PIPING & VALVES				

ENGINEERING DESIGN AND CONSTRUCTION SUPERVISION SERVICES (EDCS)
PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT (PRSWSSP), CLUSTER SOUTH-III

TEHSIL BAHAWALNAGAR (CW-25) (PHASE-I)
BILL OF QUANTITIES
ABSTRACT OF COST

Bill No. 1: WATER SUPPLY SYSTEM

Bill No. 1.6: Stand Post with Tubewell Chamber

Sr. No.	Ref. MRS	Description	Unit	Quantity	Unit Rate (Rs)	Amount (Rs)
1.6.42	23-33	Providing, laying, testing and commissioning of POLYPROPYLENE RANDOM COPOLYMER (PPRC) water supply pipe (Dadex /Popular/Beta or approved equivalent manufacturer, with specified pressure rating PN (PRESSURE NOMINAL)and conforming to DIN 8077-8078 code i/c cost of solvent, specials,making jharries complete in all respect as approved and directed by Engineer Incharge.(Internal/External Diameters mentioned).				
		b) PN-20 pipe				
		ii) 25 mm	Rft	1,600.00		
		iv) 40 mm	Rft	400.00		

ENGINEERING DESIGN AND CONSTRUCTION SUPERVISION SERVICES (EDCS)
PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT (PRSWSSP), CLUSTER SOUTH-III

TEHSIL BAHAWALNAGAR (CW-25) (PHASE-I)
BILL OF QUANTITIES
ABSTRACT OF COST

Bill No. 1: WATER SUPPLY SYSTEM

Bill No. 1.6: Stand Post with Tubewell Chamber

Sr. No.	Ref. MRS	Description	Unit	Quantity	Unit Rate (Rs)	Amount (Rs)
1.6.43	19/31	Providing and fixing brass peet/gate valve (screwed):-				
		i) 30 mm (1¼") dia	Each	8.00		
		ii) 40 mm(1½") dia	Each	8.00		
1.6.44	23-45	Supply & installation of heavy duty Brass PN-16 air Vents of specified sizeprovided at thehighest points(PipeRisers) to expel air as approved and directed by the Engineer Incharge				
		(a) Automatic				
		(iii) 1" Dia	Each	16.00		
1.6.45	19-34	Providing and fixing, floor trap of cast iron, including concrete chamber all round, and C.I. grating:-				
		(ii) 10x7.5 cm (4"x3")	Each	16.00		
1.6.46	19-51	Providing and hoisting vertical/ horizontal type storage tank of required capacity made of rotationally molded from (HDPE), double ply polyethelene of approved manufacturer i/c cost of making connection for inlet/outlet pipe, float valve i/c all cost of specials & labour complete in all respect as approved and directed by the Engineer Incharge.	Per Gallon	8,000.00		
					Total Amount	

TEHSIL BAHAWALNAGAR (CW-25) (PHASE-I)
BILL OF QUANTITIES
ABSTRACT OF COST

Bill No. 1: WATER SUPPLY SYSTEM

Bill No. 1.7: Pump Room (Civil Work)

Sr. No.	Ref. MRS	Description	Unit	Quantity	Unit Rate (Rs)	Amount (Rs)
1.7.1	3/21	Excavation in foundation of building, bridges and other structures, including dagbelling, dressing, refilling in layers around structure with excavated earth, watering and ramming lead upto one chain (30 m)lift upto 5 ft (1.5m)				
		1) By Manual				
		ii) in ordinary soil.	1000 Cft.	8.60		
1.7.2	6/3	Cement concrete brick or stone ballast 1½ " to 2" (40 mm to 50 mm) gauge, in foundation and plinth:-				
		(d) Ratio 1: 6:12 (with Brick ballast)	100 Cft	15.36		
1.7.3	7/4	Pacca brick work in foundation and plinth in: i) Cement, sand mortar Ratio 1:6	100 Cft	41.28		
1.7.4	6/37	Providing and laying damp proof course of cement concrete 1:2:4 (using cement, sand and shingle), including bitumen coating:				
		b) with 2 coats of bitumen:				
		i) 1½" thick (40 mm)	100 Sft	9.60		
1.7.5	6/39	Providing and laying vertical damp proof course with cement sand plaster and bitumen coating:- (b) with 2 coats of bitumen:-				
		2) Ratio 1:3				
		b) ¾ " thick (20mm)	100 Sft	8.16		
1.7.6	7/5	Pacca brick work in ground floor (super structure) i). Cement, sand mortar Ratio 1:5	100 Cft	69.48		
1.7.7	6/6	Providing and laying reinforced cement concrete (including prestressed concrete), using coarse sand and screened graded and washed aggregate, in required shape and design, including forms, moulds, shuttering, lifting, compacting, curing, rendering and finishing exposed surface, complete (but excluding the cost of steel reinforcement, its fabrication and placing in position, etc.):-				
		(a) (i) Reinforced cement concrete in roof slab, beams, columns lintels, girders and other structural members laid in situ or precast laid in position, or prestressed members cast in situ, complete in all respects:-				
		(3) Type C (nominal mix 1: 2: 4)	Per Cft	2,321.76		
1.7.8	6/12 b	Providing and fabrication of mild steel reinforcement for cement concrete, including cutting, bending, laying in position, making joints and fastenings, including cost of binding wire and labor charges for binding of steel reinforcement (also includes removal of rust from bars), Deformed bars (Grade 60)	100 Kg	68.47		
1.7.9	10/3	Supplying and filling sand under floor; or plugging in wells.	100 Cft	32.28		

Bill No. 1: WATER SUPPLY SYSTEM

Bill No. 1.7: Pump Room (Civil Work)

Sr. No.	Ref. MRS	Description	Unit	Quantity	Unit Rate (Rs)	Amount (Rs)
1.7.10	10/16	Providing and laying topping of cement concrete 1:2:4, including surface finishing and dividing in panels:-				
		(e) 2"(50 mm) thick	100 Sft	26.28		
1.7.11	11/18	Cement pointing struck joints, on walls, upto 20' (6.00 m) hiehgt:- b) ratio 1:3	100 Sft	88.87		
1.7.12	11/9	Cement plaster 1:4 upto 20' (6.00 m) height:-				
		b) ½" (13 mm) thick	100 Sft	111.63		
	.					
1.7.13	11/12	Cement plaster 3/8" (10 mm) thick under soffit of R.C.C. roof slabs only, upto 20' height				
		. b) 1:3	100 Sft	18.57		
1.7.14	10-35	Mosaic dado or skirting with one part of cement and marble powder in the ratio of 3:1 and two parts of marble chips, laid over ½"(13 mm) thick cement plaster 1:3, including rubbing and polishing, complete with finishing: (b) using white cement : ii) ½"(13 mm) thick	100 Sft	8.88		
1.7.15	10/43	Providing and laying Tuff Pavers, having 7000 PSI, crushing strength of approved manufacturer, over 2" to 3" sand cushion i/c grouting with sand in joints i/c finishing to require slope . complete in all respect. (50% Grey / 50% Coloured)				
		a) 50-mm thick	Sft	1,530.00		
1.7.16	9/5	Single layer of tiles 9"x4½"x1½" (225x113x40 mm) laid over 4"(100 mm) earth and 1" (25 mm) mud plaster without Bhoosa, grouted with cement sand 1:3 on top of RCC roof slab, provided with 34 lbs.per %Sft. or 1.72 Kg/Sq.m bitumen coating sand blinded.	100 Sft	22.99		
1.7.17	11/26	White washing a) new surface:- iii) three coats	100 Sft	82.45		
1.7.18	25/61	P/F Iron door comprising of specified leaves made of 1-1/4" x1-1/4" x3/16" MS angle iron for leaf frame, diagonal and horizontal braces duly welded with MS. sheet 18-SWG i/c the cost of sliding bolt, tower bolt and painting 3-coats but excluding the cost of Chowkat complete in all respect as approved and directed by the Engineer incharge.				
		(ii) Double Leaf	Per Sft	516.00		

TEHSIL BAHAWALNAGAR (CW-25) (PHASE-I)
BILL OF QUANTITIES
ABSTRACT OF COST

Bill No. 1: WATER SUPPLY SYSTEM

Bill No. 1.7: Pump Room (Civil Work)

Sr. No.	Ref. MRS	Description	Unit	Quantity	Unit Rate (Rs)	Amount (Rs)
1.7.19	12/15	Providing and fixing mild steel chowkat of doors, windows, C.window, etc. including holdfast, making and threading holes for hinges, etc. complete:- a) M.S. angle iron 1½"x 1½"x ¼" (40x40x6 mm) welded with M.S. flat 2"x ¼" (50 mm x 6 mm)	Per Sft	516.00		
1.7.20	25/45	Providing and fixing steel windows using M.S. sheet (16 SWG) moulded tubular pipe 1½"x1½" (40x40mm) for frameand 1¼"x1¼" (30x30mm) for leaves including M.S. square bars ¼"x¼" (6x6 mm) welded around each panel of frame, 5 mm thick glass panes fixed with double M.S. square tubular pipe 3/8"x3/8" (10x10mm) (22 SWG) beading with U' shaped rubber lining, brass fitting,holdfast, including painting three coats complete in all respects.	Per Sft.	651.00		
1.7.21	25/10+ 11	Fabrication & Erection of heavy steel work, with angle, tees, flat iron round iron and sheet iron for making trusses, girders, tanks, etc., including cutting, drilling, revitting, handling, assembling and fixing, including erection in position. (Top Cover & Girder)	100 Kg	15.36		
1.7.22	23-52	Providing and fixing Chain Pulley Block of 5 ton capacity with 5 meter length of chain, as per required specifications complete in all respect and as approved by the Engineer Incharge.	Each	12.00		
1.7.23	13/5 c	Painting new surface:- Preparing surface and painting of doors and windows any type (including edges):- (Chowkath Only) a) Priming coat	100 Sft	6.44		
		b) Two Coats	100 Sft	6.44		
1.7.24	1/1	Carriage of 100 Cft. (2.83 cu.m) of all materials like stone aggregate, spawl, kankar lime (unslaked), surkhi, etc. or 150 Cft. (4.25 cu.m) of timber, by truck or by any other means owned by the contractor. (crushed stone aggregate and bajri used in concrete items) (**Form Sargodha Querry)**	100 Cft.	940.07		
1.7.25	9/15	Khuras on roof 2'x2'x6" (600 x 600 x 150 mm)	Each	24.00		
1.7.26	9/16	Bottom Khuras of brick masonry in cement mortar 1:6, 4' x 2' x 4.5" over 3" cement concrete 1:4:8	Each	24.00		
		Plumbing Items				
1.7.27	19-16	Providing and fixing, chromium plated soap dish.	Each	12.00		

TEHSIL BAHAWALNAGAR (CW-25) (PHASE-I)
BILL OF QUANTITIES
ABSTRACT OF COST

Bill No. 1: WATER SUPPLY SYSTEM

Bill No. 1.7: Pump Room (Civil Work)

Sr. No.	Ref. MRS	Description	Unit	Quantity	Unit Rate (Rs)	Amount (Rs)
1.7.28	19-5	Providing and fitting white glazed earthen ware water closet squartter type, with separate foot rest.	Each	12.00		
1.7.29	19-7	Providing and fitting glazed earthen ware wash hand basin /vanity 56x40 cm (22"x16") including bracket set, waste pipe and waste coupling, etc				
		i) white, with pedestal	Each	12.00		
1.7.30	19-30	Providing and fixing, chromium plated mixing valve, for wash hand basin, sink or shower.	Each	12.00		
1.7.31	19-52	Providing and fixing CP bath Room Set made of Sonex/Master/Faisal or approved equvilent manufacturer, comprising of 3-No Tee stop cocks, lever type Basin Mixer, double Bib Cock, open wall shower, Muslim shower,waste coupling and bottle trap etc. complete in all respect as approved and directed by the Engineer incharge.				
		i) 3 No Tee Stop Cock (set)	Each	24.00		
		iii) Double Bib Cock	Each	12.00		
		v) Muslim shower	Each	12.00		
1.7.32	19-47	Providing, fixing, testing and commissioning of µ-PVC (Unplasticized Polyvinyl Chloride) Nikasi/ SWV pipe, Dadex / Popular / Beta or approved equivalent manufacturer, plain / Bell Ended / Z - Joints conforming to BS 4514 / BS 5255 - EN 1329 including the cost of specials and Solvents complete in all respects, as per drawings & specifications and / or as approved and directed by the Engineer Incharge. (v) 110 mm	Per Rft	300.00		
		(iv) 82mm	Per Rft	600.00		
1.7.33	19-49	Providing, fixing, testing and commissioning of µ-PVC (Unplasticized polyvinyl Chloride) Nikasi/ waste pipe Fittings make of Dadex /Popular/Beta or approved equivalent manufacturer, conforming to BS 4514 / BS 5255 including the cost of Solvents complete in all respect as approved and directed by the Engineer Incharge.				
		c) Vent Cowel				
		(ii) 3" dia	Each	12.00		
		d) Clean Out				
		(ii) 3" dia	Each	12.00		
		PIPING & VALVES				

TEHSIL BAHAWALNAGAR (CW-25) (PHASE-I)
BILL OF QUANTITIES
ABSTRACT OF COST

Bill No. 1: WATER SUPPLY SYSTEM

Bill No. 1.7: Pump Room (Civil Work)

Sr. No.	Ref. MRS	Description	Unit	Quantity	Unit Rate (Rs)	Amount (Rs)
1.7.34	23-33	Providing, laying, testing and commissioning of POLYPROPYLENE RANDOM COPOLYMER (PPRC) water supply pipe (Dadex /Popular/Beta or approved equivalent manufacturer, with specified pressure rating PN (PRESSURE NOMINAL)and conforming to DIN 8077-8078 code i/c cost of solvent, specials,making jharries complete in all respect as approved and directed by Engineer Incharge.(Internal/External Diameters mentioned).				
		b) PN-20 pipe				
		ii) 25 mm	Rft	1,200.00		
1.7.35	19/31	Providing and fixing brass peet/gate valve (screwed):-				
		i) 30 mm (1¼") dia	Each	12.00		
		ii) 40 mm(1½") dia	Each	12.00		
1.7.36	19-34	Providing and fixing, floor trap of cast iron, including concrete chamber all round, and C.I. grating:-				
		(ii) 10x7.5 cm (4"x3")	Each	24.00		
1.7.37	19-51	Providing and hoisting vertical/ horizontal type storage tank of required capacity made of rotationally molded from (HDPE), double ply polyethelene of approved manufacturer i/c cost of making connection for inlet/outlet pipe, float valve i/c all cost of specials & labour complete in all respect as approved and directed by the Engineer Incharge.	Per Gallon	1,200.00		
					Total Amount	

TEHSIL BAHAWALNAGAR (CW-25) (PHASE-I)
BILL OF QUANTITIES
ABSTRACT OF COST

Bill No. 1: WATER SUPPLY SYSTEM

Bill No. 1.8 :Pump House (Electrical)

Sr. No.	Ref. MRS	Description	Unit	Quantity	Unit Rate (Rs)	Amount (Rs)
1.8.1	24/3	Supply and erection of PVC pipe for wiring including inspection boxes, pull boxes, hooks, and repairing surface, etc., complete with all specials.				
	a)	Recessed in walls i/c making jharries				
		iii) 25 mm i/d	Rft	1,177.00		
		vi) 50 mm i/d	Rft	1,100.00		
1.8.2	24/09	Supply and erection of single core PVC insulated, PVC sheathed copper conductor, 250/440 volts grade cable (BSS-2004), in prelaid PVC pipes/M.S. conduit/G.I. pipe/wooden strip batten/wooden casing and capping/trenches, etc. (rate for cable only):-				
		i) 3/0.74 mm (3/0.029") (P+N+E) for Point Wiring	Rft	1,584.00		
		iii) 7/0.74 mm (7/0.029") (P+N+E) for Circuit Wiring	Rft	495.00		
		iv) 7/0.91 mm (7/0.036") (P+N+E) for Power Wiring	Rft	561.00		
1.8.3	24/11	Supply and erection of PVC insulated, PVC sheathed copper conductor cables for service connection, in prelaid pipe/G.I. wire/trenches, etc. (rate for cable only):-				
	d)	Four Core, 600/1000 volt armoured cable:-				
		viii) 16 mm sq (7/0.064) for MCC-TW Main Power Cable	Rft	2,200.00		
1.8.4	24/08	Supply and erection of single core PVC insulated copper conductor cables, in prelaid PVC pipe/M.S. conduit/G.I pipe/wooden strip batten/wooden casing an capping/G.I. wire/trenches (rate for cables only):-				
	(c)	450/750 volts, PVC insulated:				
		vi) 10 mm sq (7/0.052")	Rft	165.00		
		vii) 16 mm sq (7/0.064")	Rft	2,200.00		
1.8.5	24/103	Providing and fixing Pakistan Energy Label NEECA approved Copper winded wall bracket Fan i/c the cost of necessary cable and hardware for connection as approved and directed by Engineer Incharge.				
	(i)	18" Sweep dia	Each	22.00		
1.8.6	24/105	P/F PVC double layer Switch kit Face plate with specified switch holes i/c the cost of switches / sockets / dimmer made of Hi-Life / Bush / Schenider, screws complete as approved and directed by the Engineer Incharge				
		a) One Way Gang Switch (Small)				
		(ii) 02 Gang	Each	11.00		
		(iii) 3-Pin power plug 13A	Each	11.00		
		b) One Way Gang Switch (Large)				
		(ii) 05 Gang	Each	11.00		

TEHSIL BAHAWALNAGAR (CW-25) (PHASE-I)
BILL OF QUANTITIES
ABSTRACT OF COST

Bill No. 1: WATER SUPPLY SYSTEM

Bill No. 1.8 :Pump House (Electrical)

Sr. No.	Ref. MRS	Description	Unit	Quantity	Unit Rate (Rs)	Amount (Rs)
1.8.7	24/106	Supply, installation, testing & commissioning of 16 SWG Sheet steel powder coated back boxes with earth terminal, recessed in wall, includingaccessories, complete in all respect as per specifications and as approved by Engineer				
	i)	Small 3"x3"	Each	33.00		
	ii)	Large 6"x3"	Each	11.00		
1.8.8	24/112	Providing, maki ng & testing/commissioning of Bore type earthing point by drilling 3" dia bore hole up to water table/moist soil by laying 2"dia perforated GI.pipe (Medium Quality) fixed with 40mm dia and 250 mm long tinned copper spike at bottom , i/c the cost of Tinned earth test link copper pl ate (300x50x10mm), brass nuts, spacers,bol ts washers lugs etc but excluding the cost of copper strand & manhole. as approved and directed by Engineer Incharge (Bore Type Earthing). (2 No. Earthing Bores)	P.Rft	880.00		
1.8.9	24/113	Supply, installation, testing and commissioning of bare copper conductor for Earthing/ Grounding System (2 No. Earthing Bores)				
		50 mm² CU bare conductor	Per Rft	1,100.00		
1.8.8	N.S	Providing & laying 2 core, of following sizes, PVC insulated & PVC sheathed, 600/1000 volts grade with stranded copper conductor, un armored L.T cable in prelaid pipe/G.I. wire/trenches, etc.				
	(i)	2 Core 10 mm.sq Cu/PVC/PVC for DBLP TW	Rft	165.00		
1.8.9	N.S	Supply, installation, testing & commissioning of following various types of LED lights along with the accessories required for light fitting including light boxes:				
1.8.10	(i)	12 W Surface Mounted Down Light, (SMD) (90~265VAC), System Lumens: 80~90 lm/W, Power Factor: ≥0.9, LED Driver: Isolated (THD≤20) @ 220 VAC, Housing Material: Die Cast Aluminum, Protection Class: IP-20	Each	55.00		
1.8.11	(ii)	Bulkhead 18 W LED Light, (SMD) (100~265VAC), System Lumens: 80~90 lm/W, Power Factor: ≥0.9, LED Driver: Isolated (THD≤20) @ 220 VAC, Housing Material: Aluminum Alloy + PC, Protection Class: IP-65	Each	11.00		

TEHSIL BAHAWALNAGAR (CW-25) (PHASE-I)
BILL OF QUANTITIES
ABSTRACT OF COST

Bill No. 1: WATER SUPPLY SYSTEM

Bill No. 1.8 :Pump House (Electrical)

Sr. No.	Ref. MRS	Description	Unit	Quantity	Unit Rate (Rs)	Amount (Rs)
1.8.12	N.S	Fabrication, supply at site installation and commissioning & connection of wires/cables of distribution boards IP-54 made of 14 SWG M.S sheet degreased , derusted, zinc phosphated, finished with electrostatic powder coating of 100 micron tickness in approved colour with hinged door, flexible earthing strap lockable handle, catcher, earthing bar, neutral strip, internal wiring, designation labels on MCB, earthing bar, numbering beads on control wires, suitable for system 240V, 50HZ, 1 Phase & neutral, bus bars of 99.8% purity electrolytic copper, including cost of cable termination lugs, brass cable glands for incoming & outgoing cables, wiring from breakers, indication lamps, instruments & control all accessories.	Each	11.00		
		Incoming:				
		01 No. 32A DP MCB 10 kA				
		01 No. Digital Volt Meter 0~240V				
		0 No. Control Fuse for Protection				
		01 No. Indication Lamp (R)				
		01 Job. Brass Cable Gland for Incoming cable				
		Outgoing:				
		02 Nos. 10A SP MCB 6 kA				
		01 No. 20A SP MCB 6 kA				
		01 No. 20A SP MCB 6 kA (Spare)				

TEHSIL BAHAWALNAGAR (CW-25) (PHASE-I)
BILL OF QUANTITIES
ABSTRACT OF COST

Bill No. 1: WATER SUPPLY SYSTEM

Bill No. 1.8 :Pump House (Electrical)

Sr. No.	Ref. MRS	Description	Unit	Quantity	Unit Rate (Rs)	Amount (Rs)
1.8.13	N.S	Fabrication, supply at site installation and commissioning of 16 SWG mild steel sheet fabricated distribution board for MCC (Motor Control Centre), free standing/ wall mounting, indoor type, front access, insulation class 600 Volts, incoming and outgoing connections from top or bottom as per site requirement, door to body earth with flexible copper cable suitable for 415VAC, 3 Phase 4 wire, 400/230 50Hz TPN&E system, having rated service short circuit breaking capacity as mentioned in the details. Complete in all respects as per the satisfaction of the engineer and single line diagram.	Each	11.00		
		Incoming:				
		01 No: 40 ATP MCCB, RC:16 kA				
		01 No: Digital Ampere Meter 0~100A With Selector Switch				
		01 No: Digital Volt Meter 0~600VAC With Selector Switch				
		03 Nos: Current Transformer 80/5A				
		03 Nos: Control MCB for protection				
		03 Nos: Indication Lamp (R+Y+B)				
		01 Job: Brass Cable Gland for Incoming Cable				
		01 No: 3 Phase, 4-Wire Energy Meter				
		Outgoing:				
		01 No. 32A DP MCB RC:10 kA for DBLP-TR				
		01 No. 32A TP MCCB RC:16 kA for 10 kW Pump				
		01 No. 32A DP MCB RC:10 kA (Spare)				
		01 No. 32A TP MCCB RC:16 kA (Spare)				
1.8.14	N.S.	Supply and erection of eletric connection from WAPDA including the cost of security deposit and obtaining of 11 kV electrical connection, TRANSMISSION LINE INCLUDING CONDUCTOR, ELECTRIC POLES, transformer 11/0.415 kVA Pole mounted 25 KVA complete with all accessories as per WAPDA specifications and practice as per approved design and specification. with installation, testing and commissioning including all material, labour, tools, accessories, etc. required for proper completion of each item as per specification of WAPDA/DISCO.	Provisional Amount			
					Total Amount	

TEHSIL BAHAWALNAGAR (CW-25) (PHASE-I)
BILL OF QUANTITIES
ABSTRACT OF COST

Bill No. 1: WATER SUPPLY SYSTEM

Bill No. 1.9 :Pump House (Electrical)

Sr. No.	Ref. MRS	Description	Unit	Quantity	Unit Rate (Rs)	Amount (Rs)
1.9.1	24/3	Supply and erection of PVC pipe for wiring including inspection boxes, pull boxes, hooks, and repairing surface, etc., complete with all specials.				
	a)	Recessed in walls i/c making jharries				
		iii) 25 mm i/d	Rft	963.00		
		vi) 50 mm i/d	Rft	900.00		
1.9.2	24/09	Supply and erection of single core PVC insulated, PVC sheathed copper conductor, 250/440 volts grade cable (BSS-2004), in prelaid PVC pipes/M.S. conduit/G.I. pipe/wooden strip batten/wooden casing and capping/trenches, etc. (rate for cable only):-				
		i) 3/0.74 mm (3/0.029") (P+N+E) for Point Wiring	Rft	1,296.00		
		iii) 7/0.74 mm (7/0.029") (P+N+E) for Circuit Wiring	Rft	405.00		
		iv) 7/0.91 mm (7/0.036") (P+N+E) for Power Wiring	Rft	459.00		
1.9.3	24/11	Supply and erection of PVC insulated, PVC sheathed copper conductor cables for service connection, in prelaid pipe/G.I. wire/trenches, etc. (rate for cable only):-				
	d)	Four Core, 600/1000 volt armoured cable:-				
		iii) 10 mm sq (7/0.052) for MCC-TW Main Power Cable	Rft	1,800.00		
1.9.4	24/08	Supply and erection of single core PVC insulated copper conductor cables, in prelaid PVC pipe/M.S. conduit/G.I pipe/wooden strip batten/wooden casing an capping/G.I. wire/trenches (rate for cables only):-				
	(c)	450/750 volts, PVC insulated:				
		vi) 10 mm sq (7/0.052")	Rft	1,935.00		
1.9.5	24/103	Providing and fixing Pakistan Energy Label NEECA approved Copper winded wall bracket Fan i/c the cost of necessary cable and hardware for connection as approved and directed by Engineer Incharge.				
	(i)	18" Sweep dia	Each	18.00		
1.9.6	24/105	P/F PVC double layer Switch kit Face plate with specified switch holes i/c the cost of switches / sockets / dimmer made of Hi-Life / Bush / Schenider, screws complete as approved and directed by the Engineer Incharge				
		a) One Way Gang Switch (Small)				
		(ii) 02 Gang	Each	9.00		
		(iii) 3-Pin power plug 13A	Each	9.00		
		b) One Way Gang Switch (Large)				
		(ii) 05 Gang	Each	9.00		

TEHSIL BAHAWALNAGAR (CW-25) (PHASE-I)
BILL OF QUANTITIES
ABSTRACT OF COST

Bill No. 1: WATER SUPPLY SYSTEM

Bill No. 1.9 :Pump House (Electrical)

Sr. No.	Ref. MRS	Description	Unit	Quantity	Unit Rate (Rs)	Amount (Rs)
1.9.7	24/106	Supply, installation, testing & commissioning of 16 SWG Sheet steel powder coated back boxes with earth terminal, recessed in wall, includingaccessories, complete in all respect as per specifications and as approved by Engineer				
	i)	Small 3"x3"	Each	27.00		
	ii)	Large 6"x3"	Each	9.00		
1.9.8	24/112	Providing, making & testing/commissioning of Bore type earthing point by drilling 3" dia bore hole up to water table/moist soil by laying 2"dia perforated GI.pipe (Medium Quality) fixed with 40mm dia and 250 mm long tinned copper spike at bottom , i/c the cost of Tinned earth test link copper pl ate (300x50x10mm), brass nuts, spacers,bol ts washers lugs etc but excluding the cost of copper strand & manhole. as approved and directed by Engineer Incharge (Bore Type Earthing). (2 No. Earthing Bores)	P.Rft	720.00		
1.9.9	24/113	Supply, installation, testing and commissioning of bare copper conductor for Earthing/ Grounding System (2 No. Earthing Bores)				
		50 mm² CU bare conductor	Per Rft	900.00		
1.9.8	N.S	Providing & laying 2 core, of following sizes, PVC insulated & PVC sheathed, 600/1000 volts grade with stranded copper conductor, un armored L.T cable in prelaid pipe/G.I. wire/trenches, etc.				
	(i)	2 Core 10 mm.sq Cu/PVC/PVC for DBLP TW	Rft	135.00		
1.9.9	N.S	Supply, installation, testing & commissioning of following various types of LED lights along with the accessories required for light fitting including light boxes:				
1.9.10	(i)	12 W Surface Mounted Down Light, (SMD) (90~265VAC), System Lumens: 80~90 lm/W, Power Factor: ≥0.9, LED Driver: Isolated (THD≤20) @ 220 VAC, Housing Material: Die Cast Aluminum, Protection Class: IP-20	Each	45.00		
1.9.11	(ii)	Bulkhead 18 W LED Light, (SMD) (100~265VAC), System Lumens: 80~90 lm/W, Power Factor: ≥0.9, LED Driver: Isolated (THD≤20) @ 220 VAC, Housing Material: Aluminum Alloy + PC, Protection Class: IP-65	Each	9.00		

Bill No. 1: WATER SUPPLY SYSTEM

Bill No. 1.9 :Pump House (Electrical)

Sr. No.	Ref. MRS	Description	Unit	Quantity	Unit Rate (Rs)	Amount (Rs)
1.9.12	N.S	Fabrication, supply at site installation and commissioning & connection of wires/cables of distribution boards IP-54 made of 14 SWG M.S sheet degreased , derusted, zinc phosphated, finished with electrostatic powder coating of 100 micron tickness in approved colour with hinged door, flexible earthing strap lockable handle, catcher, earthing bar, neutral strip, internal wiring, designation labels on MCB, earthing bar, numbering beads on control wires, suitable for system 240V, 50HZ, 1 Phase & neutral, bus bars of 99.8% purity electrolytic copper, including cost of cable termination lugs, brass cable glands for incoming & outgoing cables, wiring from breakers, indication lamps, instruments & control all accessories.	Each	9.00		
		Incoming:				
		01 No. 32A DP MCB 10 kA				
		01 No. Digital Volt Meter 0~240V				
		0 No. Control Fuse for Protection				
		01 No. Indication Lamp (R)				
		01 Job. Brass Cable Gland for Incoming cable				
		Outgoing:				
		02 Nos. 10A SP MCB 6 kA				
		01 No. 20A SP MCB 6 kA				
		01 No. 20A SP MCB 6 kA (Spare)				
1.9.13	N.S	Fabrication, supply at site installation and commissioning of 16 SWG mild steel sheet fabricated distribution board for MCC (Motor Control Centre), free standing/ wall mounting, indoor type, front access, insulation class 600 Volts, incoming and outgoing connections from top or bottom as per site requirement, door to body earth with flexible copper cable suitable for 415VAC, 3 Phase 4 wire, 400/230 50Hz TPN&E system, having rated service short circuit breaking capacity as mentioned in the details. Complete in all respects as per the satisfaction of the engineer and single line diagram.	Each	9.00		
		Incoming:				
		01 No: 40 ATP MCCB, RC:16 kA				
		01 No: Digital Ampere Meter 0~100A With Selector Switch				
		01 No: Digital Volt Meter 0~600VAC With Selector Switch				
		03 Nos: Current Transformer 80/5A				
		03 Nos: Control MCB for protection				
		03 Nos: Indication Lamp (R+Y+B)				
		01 Job: Brass Cable Gland for Incoming Cable				
		01 No: 3 Phase, 4-Wire Energy Meter				
		Outgoing:				
		01 No. 32A DP MCB RC:10 kA for DBLP-TR				
		01 No. 32A DP MCB RC:10 kA for Pump 5HP				
		01 No. 32A DP MCB RC:10 kA (Spare)				

ENGINEERING DESIGN AND CONSTRUCTION SUPERVISION SERVICES (EDCS)
PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT (PRSWSSP), CLUSTER SOUTH-III

TEHSIL BAHAWALNAGAR (CW-25) (PHASE-I)
BILL OF QUANTITIES
ABSTRACT OF COST

Bill No. 1: WATER SUPPLY SYSTEM

Bill No. 1.9 :Pump House (Electrical)

Sr. No.	Ref. MRS	Description	Unit	Quantity	Unit Rate (Rs)	Amount (Rs)
		01 No. 50A TP MCCB RC:16 kA (Spare)				
					Total Amount	

TEHSIL BAHAWALNAGAR (CW-25) (PHASE-I)
BILL OF QUANTITIES
ABSTRACT OF COST

Bill No. 1: WATER SUPPLY SYSTEM

Bill No. 1.10 : Stand Post

Sr. No.	Ref. MRS	Description	Unit	Quantity	Unit Rate (Rs)	Amount (Rs)
1.10.1	3/21	Excavation in foundation of building, bridges and other structures, including dagbelling, dressing, refilling in layers around structure with excavated earth, watering and ramming lead upto one chain (30 m)lift upto 5 ft (1.5m)				
		1) By Manual				
		ii) in ordinary soil.	1000 Cft.	6.71		
1.10.2	6/3	Cement concrete brick or stone ballast 1½ " to 2" (40 mm to 50 mm) gauge, in foundation and plinth:-				
		(d) Ratio 1: 6:12 (with Brick ballast)	100 Cft	21.90		
1.10.3	7/4	Pacca brick work in foundation and plinth in: i) Cement, sand mortar Ratio 1:6	100 Cft	67.65		
1.10.4	6/37	Providing and laying damp proof course of cement concrete 1:2:4 (using cement, sand and shingle), including bitumen coating:				
		b) with 2 coats of bitumen:				
		ii) 2" thick	100 Sft	7.95		
1.10.5	6/39	Providing and laying vertical damp proof course with cement sand plaster and bitumen coating:- (b) with 2 coats of bitumen:-				
		ii) Ratio 1:3				
		b) ¾ " thick (20mm)	100 Sft	6.60		
1.10.6	7/5	Pacca brick work in ground floor (super structure) i). Cement, sand mortar Ratio 1:5	100 Cft	49.50		
1.10.7	6/6	Providing and laying reinforced cement concrete (including prestressed concrete), using coarse sand and screened graded and washed aggregate, in required shape and design, including forms, moulds, shuttering, lifting, compacting, curing, rendering and finishing exposed surface, complete (but excluding the cost of steel reinforcement, its fabrication and placing in position, etc.):-				
		(a) (i) Reinforced cement concrete in roof slab, beams, columns lintels, girders and other structural members laid in situ or precast laid in position, or prestressed members cast in situ, complete in all respects:-				
		(3) Type C (nominal mix 1: 2: 4)	Per Cft	2,649.30		
1.10.8	6/12 b	Providing and fabrication of mild steel reinforcement for cement concrete, including cutting, bending, laying in position, making joints and fastenings, including cost of binding wire and labor charges for binding of steel reinforcement (also includes removal of rust from bars), Deformed bars (Grade 60)	100 Kg	78.13		
1.10.9	10/3	Supplying and filling sand under floor; or plugging in wells.	100 Cft	23.85		

Bill No. 1: WATER SUPPLY SYSTEM

Bill No. 1.10 : Stand Post

Sr. No.	Ref. MRS	Description	Unit	Quantity	Unit Rate (Rs)	Amount (Rs)
1.10.10	10/16	Providing and laying topping of cement concrete 1:2:4, including surface finishing and dividing in panels:-				
		(e) 2"(50 mm) thick	100 Sft	48.45		
1.10.11	11/18	Cement pointing struck joints, on walls, upto 20' (6.00 m) hiehgt:- b) ratio 1:3	100 Sft	88.12		
1.10.12	11/9	Cement plaster 1:4 upto 20' (6.00 m) height:- b) ½" (13 mm) thick	100 Sft	88.83		
	.					
1.10.13	11/12	Cement plaster 3/8" (10 mm) thick under soffit of R.C.C. roof slabs only, upto 20' height				
		. b) 1:3	100 Sft	36.54		
1.10.14	9/5	Single layer of tiles 9"x4½"x1½" (225x113x40 mm) laid over 4"(100 mm) earth and 1" (25 mm) mud plaster without Bhoosa, grouted with cement sand 1:3 on top of RCC roof slab, provided with 34 lbs.per %Sft. or 1.72 Kg/Sq.m bitumen coating sand blinded.	100 Sft	39.76		
1.10.15	10/45-17.65 deduction for matt finishes	Providing and laying superb quality Porcelain glazed tiles flooring of Master/ Stile brand or approved equivalent manufacturer of specified size in approved design, Color and Shade with adhesive/ bond over 3/4" thick (1:3) cement plaster i/c the cost of sealer for finishing the joints i/c cutting grinding complete in all respect as approved and directed by the Engineer Incharge. a) Full body Matt tiles				
		(ii) 300mmx 600mm	Sft	1,585.65		
1.10.16	10/36-18.90 deduction for matt finishes	Providing and laying superb quality Porcelain glazed tiles of Master/ Stile brand or approved equivalent manufacturer, skirting/ dado of specified size, Color and Shade with adhesive/ bond over 1/2" thick (1:2) cement plaster i/c the cost of matching sealer for finishing the joints, cutting grinding complete in all respect as approved and directed by the Engineer Incharge. a) Full body Matt tiles				
		(ii) 300mmx 600mm	Sft	5,181.75		
1.10.17	10/48	Providing and laying 3/4" thick full width Prepolished Marble slab for Vanities/ Shelves/ Treads/ Window Cills, having Uniform texture (Spotless) with adhesive bond over 3/4" thick (1:2) cement sand mortor i/c the cost of matching sealer complete in all respects as approved and directed by the Engineer Incharge.				
		i) China Verona	Sft	1,803.75		

Bill No. 1: WATER SUPPLY SYSTEM

Bill No. 1.10 : Stand Post

Sr. No.	Ref. MRS	Description	Unit	Quantity	Unit Rate (Rs)	Amount (Rs)
1.10.18	10/43	Providing and laying Tuff Pavers, having 7000 PSI, crushing strength of approved manufacturer, over 2" to 3" sand cushion i/c grouting with sand in joints i/c finishing to require slope . complete in all respect. (50% Grey / 50% Coloured)				
		a) 50-mm thick	Sft	1,630.20		
1.10.19	11/26	White washing a) new surface:- iii) three coats	100 Sft	125.37		
1.10.20	25/31	Making and fixing steel grated door with 1/16" thick (1.5mm) sheeting, including angle iron frame 2"x2"x3/8" (50x50x10 mm) and ¾" (20 mm) square bars 4" (100 mm) centre to centre, with locking arrangement.				
			Per Sft	1,050.00		
1.10.21	12/15	Providing and fixing mild steel chowkat of doors, windows, C.window, etc. including holdfast, making and threading holes for hinges, etc. complete:- a) M.S. angle iron 1½"x 1½"x ¼" (40x40x6 mm) welded with M.S. flat 2"x ¼" (50 mm x 6 mm)	Per Sft	1,050.00		
1.10.22	25/32	Making and fixing grating in opening, including fixing at site with flat iron 2"x3/8" (50x10 mm) and ¾" (19 mm) square bars, at 4" (100 mm) centre to centre.	Per Sft	2,745.00		
1.10.23	18-23	Providing and fixing M.S Grating comprising of Angle Iron frame size 1.50"x1.50"x3/16" and 1/2" square bars duly welded @ 4" c/c, including painting charges etc complete in all respect.(For Drain)	Per Sft	438.90		
1.10.24	9/15	Khuras on roof 2'x2'x6" (600 x 600 x 150 mm)	Each	15.00		
1.10.25	9/16	Bottom Khuras of brick masonry in cement mortar 1:6, 4' x 2' x 4.5" over 3" cement concrete 1:4:8	Each	15.00		
1.10.26	1/1	Carriage of 100 Cft. (2.83 cu.m) of all materials like stone aggregate, spawl, kankar lime (unslaked), surkhi, etc. or 150 Cft. (4.25 cu.m) of timber, by truck or by any other means owned by the contractor. (crushed stone aggregate and bajri used in concrete items) (**Form Sargodha Querry)**	100 Cft.	88.16		
		Electrical Works				
1.10.27	24/3	Supply and erection of PVC pipe for wiring including inspection boxes, pull boxes, hooks, and repairing surface, etc., complete with all specials.				
	a)	Recessed in walls i/c making jharries				

Bill No. 1: WATER SUPPLY SYSTEM

Bill No. 1.10 : Stand Post

Sr. No.	Ref. MRS	Description	Unit	Quantity	Unit Rate (Rs)	Amount (Rs)
		iii) 25 mm i/d	Rft	570.00		
1.10.28	24/09	Supply and erection of single core PVC insulated, PVC sheathed copper conductor, 250/440 volts grade cable (BSS-2004), in prelaid PVC pipes/M.S. conduit/G.I. pipe/wooden strip batten/wooden casing and capping/trenches, etc. (rate for cable only):-				
		i) 3/0.74 mm (3/0.029") (P+N+E) for Point Wiring	Rft	1,710.00		
		iii) 7/0.74 mm (7/0.029") (P+N+E) for Circuit Wiring	Rft	1,650.00		
1.10.29	24/104	Providing and fixing Pakistan Energy Label NEECA approved Copper winded Ceiling Fan i/c the cost of necessary cable and hardware for connection as approved and directed by Engineer Incharge.				
		iii) 56" dia	Each	30.00		
1.10.30	24/105	P/F PVC double layer Switch kit Face plate with specified switch holes i/c the cost of switches / sockets / dimmer made of Hi-Life / Bush / Schenider, screws complete as approved and directed by the Engineer Incharge				
		a) One Way Gang Switch (Small)				
		(ii) 02 Gang	Each	30.00		
1.10.31	24/106	Supply, installation, testing & commissioning of 16 SWG Sheet steel powder coated back boxes with earth terminal, recessed in wall, includingaccessories, complete in all respect as per specifications and as approved by Engineer				
	i)	Small 3"x3"	Each	30.00		
1.10.32	N.S	Supply, installation, testing & commissioning of following various types of LED lights along with the accessories required for light fitting including light boxes:				
	(i)	12 W Surface Mounted Down Light, (SMD) (90~265VAC), System Lumens: 80~90 lm/W, Power Factor: ≥0.9, LED Driver: Isolated (THD≤20) @ 220 VAC, Housing Material: Die Cast Aluminum, Protection Class: IP-20	Each	60.00		
		Plumbing Work				
1.10.33	19-16	Providing and fixing, chromium plated soap dish.	Each	15.00		
1.10.34	19-5	Providing and fitting white glazed earthen ware water closet squartter type, with separate foot rest.	Each	15.00		
1.10.35	19-7	Providing and fitting glazed earthen ware wash hand basin /vanity 56x40 cm (22"x16") including bracket set, waste pipe and waste coupling, etc				
		i) white, with pedestal	Each	15.00		
1.10.36	19-45	Providing and fixing brass stop cock/bib cock:- b)20 mm (¾") dia	Each	180.00		

TEHSIL BAHAWALNAGAR (CW-25) (PHASE-I)
BILL OF QUANTITIES
ABSTRACT OF COST

Bill No. 1: WATER SUPPLY SYSTEM

Bill No. 1.10 : Stand Post

Sr. No.	Ref. MRS	Description	Unit	Quantity	Unit Rate (Rs)	Amount (Rs)
1.10.37	19-28	Providing and fixing chromium plated tee stop cock 15mm (½").	Each	30.00		
1.10.38	19-52	Providing and fixing CP bath Room Set made of Sonex/Master/Faisal or approved equvilent manufacturer, comprising of 3-No Tee stop cocks, lever type Basin Mixer, double Bib Cock, open wall shower, Muslim shower,waste coupling and bottle trap etc. complete in all respect as approved and directed by the Engineer incharge.				
		v) Muslim shower	Each	15.00		
1.10.39	19-47	Providing, fixing, testing and commissioning of µ-PVC (Unplasticized Polyvinyl Chloride) Nikasi/ SWV pipe, Dadex / Popular / Beta or approved equivalent manufacturer, plain / Bell Ended / Z - Joints conforming to BS 4514 / BS 5255 - EN 1329 including the cost of specials and Solvents complete in all respects, as per drawings & specifications and / or as approved and directed by the Engineer Incharge. (v) 110 mm	Per Rft	375.00		
		(iv) 82mm	Per Rft	750.00		
1.10.40	19-49	Providing, fixing, testing and commissioning of µ-PVC (Unplasticized polyvinyl Chloride) Nikasi/ waste pipe Fittings make of Dadex /Popular/Beta or approved equivalent manufacturer, conforming to BS 4514 / BS 5255 including the cost of Solvents complete in all respect as approved and directed by the Engineer Incharge.				
		c) Vent Cowel				
		(ii) 3" dia	Each	15.00		
		d) Clean Out				
		(ii) 3" dia	Each	15.00		
		PIPING & VALVES				
1.10.41	23-33	Providing, laying, testing and commissioning of POLYPROPYLENE RANDOM COPOLYMER (PPRC) water supply pipe (Dadex /Popular/Beta or approved equivalent manufacturer, with specified pressure rating PN (PRESSURE NOMINAL)and conforming to DIN 8077-8078 code i/c cost of solvent, specials,making jharries complete in all respect as approved and directed by Engineer Incharge.(Internal/External Diameters mentioned).				
		b) PN-20 pipe				
		ii) 25 mm	Rft	3,000.00		
		iv) 40 mm	Rft	750.00		
1.10.42	19/31	Providing and fixing brass peet/gate valve (screwed):-				

ENGINEERING DESIGN AND CONSTRUCTION SUPERVISION SERVICES (EDCS)
PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT (PRSWSSP), CLUSTER SOUTH-III

TEHSIL BAHAWALNAGAR (CW-25) (PHASE-I)
BILL OF QUANTITIES
ABSTRACT OF COST

Bill No. 1: WATER SUPPLY SYSTEM

Bill No. 1.10 : Stand Post

Sr. No.	Ref. MRS	Description	Unit	Quantity	Unit Rate (Rs)	Amount (Rs)
		i) 30 mm (1¼") dia	Each	15.00		
		ii) 40 mm(1½") dia	Each	15.00		
1.10.43	23-45	Supply & installation of heavy duty Brass PN-16 air Vents of specified sizeprovided at thehighest points(PipeRisers) to expel air as approved and directed by the Engineer Incharge				
		(a) Automatic				
		(iii) 1" Dia	Each	30.00		
1.10.44	19-34	Providing and fixing, floor trap of cast iron, including concrete chamber all round, and C.I. grating:-				
		(ii) 10x7.5 cm (4"x3")	Each	30.00		
1.10.45	19-51	Providing and hoisting vertical/ horizontal type storage tank of required capacity made of rotationally molded from (HDPE), double ply polyethelene of approved manufacturer i/c cost of making connection for inlet/outlet pipe, float valve i/c all cost of specials & labour complete in all respect as approved and directed by the Engineer Incharge.	Per Gallon	15,000.00		
					Total Amount	

ENGINEERING DESIGN AND CONSTRUCTION SUPERVISION SERVICES (EDCS)
PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT (PRSWSSP), CLUSTER SOUTH-III

TEHSIL BAHAWALNAGAR (CW-25) (PHASE-I)
BILL OF QUANTITIES
ABSTRACT OF COST

Bill No. 1: WATER SUPPLY SYSTEM

Bill No. 1.11: Pipe Network

Sr. No.	Ref. MRS	Description	Unit	Quantity	Unit Rate (Rs)	Amount (Rs)
		Earthwork				
1.11.1	3/46	Excavation of trenches in all kinds of soil, except cutting rock, for watersupply pipelines/electric cables upto 5 ft. (1.5 m) depth from ground level, including backfilling, trimming, dressing sides, leveling the beds of trenches to correct grade and cutting pits for joints, etc. complete in all respects.	1000Cft	378.43		
		HDPE Pipe				
1.11.2	23/30	Providing, laying, cutting, jointing, testing and disinfecting High Density Polyethylene Pipe (HDPE-100) working presure pipe, Beta/ Dadex/ Popular/ IIL or equivalent including the cost of specials, in trenches, as approved & directed by the engineer incharge, complete in all respects.				
		Distibution Network				
		a) PN-6 (SDR-26)				
		90 mm Dia	Rft	68,188.00		
1.11.3	6/5	Cement concrete plain including placing, compacting, finishing and curing complete (including screening and washing of stone aggregate): (f) Ratio 1: 2: 4	100Cft	98.69		
1.11.4	1/1	Carriage of 100 Cft. (2.83 cu.m) of all materials like stone aggregate, spawl, kankar lime (unslaked), surkhi, etc. or 150 Cft. (4.25 cu.m) of timber, by truck or by any other means owned by the contractor. (crushed stone aggregate and bajri used in concrete items) (**Form Sargodha Querry)**	100 CFT	86.85		
		Valves				
		Sluice Valce				
1.11.5	23/35	Providing and fixing sluice valve of B.S.S. quality and weight, Class `B', for cast iron pipe line, and Asbestos cement pipe line (including cost of jointing material):-				
		3" i/d (75 mm)	Each	32.00		

ENGINEERING DESIGN AND CONSTRUCTION SUPERVISION SERVICES (EDCS)
PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT (PRSWSSP), CLUSTER SOUTH-III

TEHSIL BAHAWALNAGAR (CW-25) (PHASE-I)
BILL OF QUANTITIES
ABSTRACT OF COST

Bill No. 1: WATER SUPPLY SYSTEM

Bill No. 1.11: Pipe Network

Sr. No.	Ref. MRS	Description	Unit	Quantity	Unit Rate (Rs)	Amount (Rs)
		Air Release				
1.11.6	23/37	Providing and fixing, air valve 2½ (65mm) dia of B.S.S. quality and weight (complete with jointing material).				
		b) double	Each	15.00		
1.11.7	23/22	Providing and fixing cast iron specials of B.S.S. Class 'B' (such as bend, tee, cross collar, reducer, tail piece, flanged socket, flanged spigot, cap, taper, angle branch, plug, etc) for Asbestos cement pipe line, with comet joint and rubber ring, complete. i) 3" to 6" (75 to 150 mm) i/d	Per Kg	225.00		
1.11.8	23/35	Providing and fixing sluice valve of B.S.S. quality and weight, Class `B', for cast iron pipe line, and Asbestos cement pipe line (including cost of jointing material):- a) 3" i/d (75 mm)	Each	15.00		
		Washout Valve				
1.11.9	23/35	Providing and fixing sluice valve of B.S.S. quality and weight, Class `B', for cast iron pipe line, and Asbestos cement pipe line (including cost of jointing material):- 3" i/d (75 mm)	Each	15.00		
					Total Amount	

TEHSIL BAHAWALNAGAR (CW-25) (PHASE-I)
BILL OF QUANTITIES
ABSTRACT OF COST

Bill No. 1: WATER SUPPLY SYSTEM

Bill No. 1.12: Valves and Chambers

Sr. No.	Ref. MRS	Description	Unit	Quantity	Unit Rate (Rs)	Amount (Rs)
1.12.1	3/21	Excavation in foundation of building, bridges and other structures, including dagbelling, dressing, refilling in layers around structure with excavated earth, watering and ramming lead 'upto one chain (30 m) and lift upto 5 ft. (1.5 m). a) By Manual ii) Ordinary soil	1000 Cft.	9.24		
1.12.2	6/5	Cement concrete plain including placing, compacting, finishing and curing complete (including screening and washing of stone aggregate): (i) Ratio 1: 4: 8	100Cft	4.07		
1.12.3	6/5	Cement concrete plain including placing, compacting, finishing and curing complete (including screening and washing of stone aggregate): (f) Ratio 1: 2: 4	100Cft	7.83		
1.12.4	7/7	Pacca brick work other than building upto 10ft. (3 m) height. i) cement, sand mortar:- (1:4)	100 Cft	33.11		
1.12.5	11/8	Cement plaster 1:3 upto 20' (6.00 m) height:- b) ½" (13 mm) thick	100 Sft	63.27		
	6/6	Providing and laying reinforced cement concrete (including prestressed concrete), using Ordinary Portland Cement / Sulphate resisting cement / Slag cement as may be required; coarse sand and screened graded and washed aggregate, in required shape and design, including forms, moulds, shuttering, lifting, compacting, curing, rendering and finishing exposed surface, complete (but excluding the cost of steel reinforcement, its fabrication and placing in position, etc.):-				
1.12.6		(a) Reinforced cement concrete in roof slab, beams, columns lintels, girders and other structural members laid in situ or precast laid in position, or prestressed members cast in situ, complete in all respects:- (3) Type C (nominal mix 1: 2: 4)	Per Cft	573.51		
1.12.7	1/1	Carriage of 100 Cft. (2.83 cu.m) of all materials like stone aggregate, spawl, kankar lime (unslaked), surkhi, etc. or 150 Cft. (4.25 cu.m) of timber, by truck or by any other means owned by the contractor. (crushed stone aggregate and bajri used in concrete items) (**Form Sargodha Querry)**	100 CFT	12.70		
1.12.8	6/12 b	Fabrication of mild steel reinforcement for cement concrete including cutting, bending, laying in position, making joints and fastenings, including cost of binding wire and labour charges for binding of steel reinforcement (also includes removal of rust from bars):- b) Deformed bars (Grade-60)	100 Kg	13.03		

ENGINEERING DESIGN AND CONSTRUCTION SUPERVISION SERVICES (EDCS)
PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT (PRSWSSP), CLUSTER SOUTH-III

TEHSIL BAHAWALNAGAR (CW-25) (PHASE-I)
BILL OF QUANTITIES
ABSTRACT OF COST

Bill No. 1: WATER SUPPLY SYSTEM

Bill No. 1.12: Valves and Chambers

Sr. No.	Ref. MRS	Description	Unit	Quantity	Unit Rate (Rs)	Amount (Rs)
1.12.9	N.S.	Providing and fixing of RPC Manhole Cover Manufactured with 100% Recycled Plastic Composite Material, 650 mm (26"dia) with clear opening size 600 mm (24" dia) and RPC manhole frame having dia meter 790 mm (31.1") with average breaking load capacity of 10 Ton and weight including frame of 50 kg (Minimum).	Each	62.00		
					Total Amount	

ENGINEERING DESIGN AND CONSTRUCTION SUPERVISION SERVICES (EDCS)
PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT (PRSWSSP), CLUSTER SOUTH-III

TEHSIL BAHAWALNAGAR (CW-25) (PHASE-I)
BILL OF QUANTITIES
ABSTRACT OF COST

Bill No. 1: WATER SUPPLY SYSTEM

Bill No. 1.13: Boundary Wall

Sr. No.	Ref. MRS	Description	Unit	Quantity	Unit Rate (Rs)	Amount (Rs)
1.13.1	3/21	Excavation in foundation of building, bridges and other structures, including dagbelling, dressing, refilling in layers around structure with excavated earth, watering and ramming lead upto one chain (30 m)lift upto 5 ft (1.5m)				
		1) By Manual				
		ii) in ordinary soil.	1000 Cft.	8.66		
1.13.2	6/5	Cement concrete plain including placing, compacting, finishing and curing complete (including screening and washing of stone aggregate):				
		(i) Ratio 1: 4: 8	100 Cft	58.84		
1.13.3	18/3	a) Providing and laying sub-base course of stone product of approved quality and grade, including placing, mixing, spreading and compaction of sub-base material to required depth, camber, grade to achieve 100% maximum modified AASHO dry density, including carriage of all material to site of work except gravel and. aggregate.				
		ii) Crushed stone aggregate.	100 Cft	8.16		
1.13.4	7/4	Pacca brick work in foundation and plinth in: i) Cement, sand mortar Ratio 1:5	100 Cft	21.72		
1.13.5	7/7	Pacca brick work other than building upto 10ft. (3 m) height. i) cement, sand mortar:- Ratio 1:4	100 Cft	23.88		

TEHSIL BAHAWALNAGAR (CW-25) (PHASE-I)
BILL OF QUANTITIES
ABSTRACT OF COST

Bill No. 1: WATER SUPPLY SYSTEM

Bill No. 1.13: Boundary Wall

Sr. No.	Ref. MRS	Description	Unit	Quantity	Unit Rate (Rs)	Amount (Rs)
1.13.6	6/6	Providing and laying reinforced cement concrete (including prestressed concrete), using coarse sand and screened graded and washed aggregate, in required shape and design, including forms, moulds, shuttering, lifting, compacting, curing, rendering and finishing exposed surface, complete (but excluding the cost of steel reinforcement, its fabrication and placing in position, etc.):-				
		(a) Reinforced cement concrete in roof slab, beams, columns lintels, girders and other structural members laid in situ or precast laid in position, or prestressed members cast in situ, complete in all respects:-				
		(3) Type C (nominal mix 1: 2: 4)	Per Cft	240.00		
		(c) Reinforced cement concrete in Pile cap, slab of rafts / strip foundation, base slab of column and retaining walls; etc and footing beams, other structural members other than those mentioned in 6(a-d) above not requiring form work (i.e. horizontal shuttering) complete in all respects:-				
		(3) Type C (nominal mix 1: 2: 4)	Per Cft	337.54		
1.13.7	6/12 b	Providing and fabrication of mild steel reinforcement for cement concrete, including cutting, bending, laying in position, making joints and fastenings, including cost of binding wire and labor charges for binding of steel reinforcement (also includes removal of rust from bars), Deformed bars (Grade 60)	100 Kg	17.03		
1.13.8	11/9	Cement plaster 1:4 upto 20' (6.00 m) height:-				
		b) ½" (13 mm) thick	100 Sft	43.36		
1.13.9	25/31	Making and fixing steel grated door with 1/16" thick (1.5mm) sheeting, including angle iron frame 2"x2"x3/8" (50x50x10 mm) and ¾" (20 mm) square bars 4" (100 mm) centre to centre, with locking arrangement.	Per Sft	1,080.00		
1.13.10	13/5 d	Painting new surface:- Preparing surface and painting guard bars, gates of iron bars, gratings, railing (including standards, braces, etc.) and in similar open work:- a) Priming coat	100 Sft	21.60		
		b) Two Coats	100 Sft	21.60		
1.13.11	1/1	Carriage of 100 Cft. (2.83 cu.m) of all materials like stone aggregate, spawl, kankar lime (unslaked), surkhi, etc. or 150 Cft. (4.25 cu.m) of timber, by truck or by any other means owned by the contractor. (crushed stone aggregate and bajri used in concrete items) (**Form Sargodha Querry)**	100 Cft.	64.88		
1.13.12	3/5	Filling, watering and ramming earth under floors:-				
		i) With surplus earth from foundation, etc.	1000 Cft.	10.53		
		ii) With new earth excavated from outside, lead upto one chain (30 m).	1000 Cft.	94.77		

ENGINEERING DESIGN AND CONSTRUCTION SUPERVISION SERVICES (EDCS)
PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT (PRSWSSP), CLUSTER SOUTH-III

TEHSIL BAHAWALNAGAR (CW-25) (PHASE-I)
BILL OF QUANTITIES
ABSTRACT OF COST

Bill No. 1: WATER SUPPLY SYSTEM

Bill No. 1.13: Boundary Wall

Sr. No.	Ref. MRS	Description	Unit	Quantity	Unit Rate (Rs)	Amount (Rs)
1.13.13	3/17	Transportation of earth all types when the total distance, including the lead covered in the item of work, is more than 1000 ft. (300 m)				
		a) Upto ¼ mile (400 m).	1000 Cft.	94.77		
		b) For every 330 ft. (100 m) additional lead or part thereof, beyond ¼ mile (400 m) upto one mile. (1.6 Km.)	1000 Cft.	94.77		
1.13.14	6/2	Dry rammed brick or stone ballast, 1½" to 2"(40 mm to 50 mm) gauge.	100 Cft.	1,071.43		
1.13.15	18/20	Providing and laying dry brick pavement/soling in streets or roads, etc. sand grounted, laid in proper camber, including preparation, watering, compaction of bed to proper camber, and sand cushion.	100 Cft.	128.12		
		Precast Wall				
1.13.16	NS	Providing and Fixing in Position Precast boundary wall up to 6 ft high of standard precast component as per drawing and direction of the engineer incharge. The rate of Boundary wall includes wall Pannels of size (2"x1'x8'), columns (6"x6.5"x8') with Cap,transported to site,loading/unloading and fixing in position finished, complete in all respect.	Rft	2,096.00		
					Total Amount	

ENGINEERING DESIGN AND CONSTRUCTION SUPERVISION SERVICES (EDCS)
PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT (PRSWSSP), CLUSTER SOUTH-III

TEHSIL BAHAWALNAGAR (CW-25) (PHASE-I)
BILL OF QUANTITIES
ABSTRACT OF COST

Bill No. 1: WATER SUPPLY SYSTEM

Bill No. 1.144: Pump Room Rehabilitation Works

Sr. No.	Ref. MRS	Description	Unit	Quantity	Unit Rate (Rs)	Amount (Rs)
		Plinth Protection				
1.14.1	7/5	Pacca brick work in ground floor (super structure) i). Cement, sand mortar Ratio 1:5	100 Cft	31.68		
				-		
1.14.2	10/3	Supplying and filling sand under floor; or plugging in wells.	100Cft.	49.50		
				-		
1.14.3	6/2	Dry rammed brick or stone ballast, 1½" to 2"(40 mm to 50 mm) gauge.	100Cft.	12.38		
				-		
1.14.4	10/16	Providing and laying topping of cement concrete 1:2:4, including surface finishing and dividing in panels:-		-		
		(e) 2"(50 mm) thick	100 Sft	60.50		
		Pump Room and Plinth		-		
1.14.5	11/9	Cement plaster 1:4 upto 20' (6.00 m) height:-		-		
		b) ½" (13 mm) thick	100 Sft	51.70		
	.			-		
1.14.6	11/26	White washing a) new surface:- iii) three coats	100 Sft	40.92		
				-		
1.14.7	23/35	Providing and fixing sluice valve of B.S.S. quality and weight, Class `B', for cast iron pipe line, and Asbestos cement pipe line (including cost of jointing material):- b) 4" i/d (100 mm)	Each	11.00		
1.14.8	23/37	Providing and fixing, air valve 2½ (65mm) dia of B.S.S. quality and weight (complete with jointing material). b) double	Each	22.00		
1.14.9	23/44	Providing and fixing heavy duty Check valve of specified diameter and material for pressure rating PN-16 made of Crane (USA), Hatersly (UK), Scon (Pakistan) or approved equivalent manufacturer i/c the cost of all accessories flanges,nut/bolt and gaskit where required complete in all respect as approved and directed by the Engineer Incharge. (b) Flange Ended Ductile Iron Valve (ix) 4" dia	Each	11.00		
1.14.10	N/S	Providing, installing, testing, and commissioning of Hypo Dosing Chlorinator unit of European make, having an injection capacity of 8 liters/second and maximum operating pressure of 10 bar, complete in all respects as per specifications, drawings, and as directed by the Engineer Incharge.	P/Job	11.00		
					Total Amount	

TEHSIL BAHAWALNAGAR (CW-25) (PHASE-I)
BILL OF QUANTITIES
ABSTRACT OF COST

Bill No. 1: WATER SUPPLY SYSTEM

Bill No. 1.15:Pump House (Electrical) Rehabilitation Work

Sr. No.	Ref. MRS	Description	Unit	Quantity	Unit Rate (Rs)	Amount (Rs)
1.15.1	24/09	Supply and erection of single core PVC insulated, PVC sheathed copper conductor, 250/440 volts grade cable (BSS-2004), in prelaid PVC pipes/M.S. conduit/G.I. pipe/wooden strip batten/wooden casing and capping/trenches, etc. (rate for cable only):-				
		i) 3/0.74 mm (3/0.029") (P+N+E) for Point Wiring	Rft	1,584.00		
		iii) 7/0.74 mm (7/0.029") (P+N+E) for Circuit Wiring	Rft	495.00		
		iv) 7/0.91 mm (7/0.036") (P+N+E) for Power Wiring	Rft	561.00		
				-		
1.15.2	24/11	Supply and erection of PVC insulated, PVC sheathed copper conductor cables for service connection, in prelaid pipe/G.I. wire/trenches, etc. (rate for cable only):-		-		
	(b)	Three core, 600/1000 volt non armoured cable:-		-		
		vi) 7/1.63 mm (7/0.064") for ASDS Starter	Rft	407.00		
	(c)	Four core, 600/1000 volt non armoured cable:-		-		
		vii) 16 mm (7/0.064") for DBLP-TR Main Power Cable	Rft	165.00		
		viii) 25 mm (19/0.052") for MCC-TW Main Power Cable	Rft	1,100.00		
				-		
1.15.3	24/08	Supply and erection of single core PVC insulated copper conductor cables, in prelaid PVC pipe/M.S. conduit/G.I pipe/wooden strip batten/wooden casing an capping/G.I. wire/trenches (rate for cables only):-		-		
	(c)	450/750 volts, PVC insulated:		-		
		vi) 10 mm sq (7/0.052")	Rft	165.00		
		vii) 16 mm sq (7/0.064")	Rft	330.00		
		viii) 25 mm sq (19/0.052")	Rft	1,100.00		
1.15.4	24/103	Providing and fixing Pakistan Energy Label NEECA approved Copper winded wall bracket Fan i/c the cost of necessary cable and hardware for connection as approved and directed by Engineer Incharge.		-		
	(i)	18" Sweep dia	Each	22.00		
				-		
1.15.5	24/105	P/F PVC double layer Switch kit Face plate with specified switch holes i/c the cost of switches / sockets / dimmer made of Hi-Life / Bush / Schenider, screws complete as approved and directed by the Engineer Incharge		-		
		a) One Way Gang Switch (Small)		-		
		(ii) 02 Gang	Each	11.00		
		(iv) 3-Pin power plug 13A	Each	11.00		
		b) One Way Gang Switch (Large)		-		
		(ii) 05 Gang	Each	11.00		
				-		

TEHSIL BAHAWALNAGAR (CW-25) (PHASE-I)
BILL OF QUANTITIES
ABSTRACT OF COST

Bill No. 1: WATER SUPPLY SYSTEM

Bill No. 1.15:Pump House (Electrical) Rehabilitation Work

Sr. No.	Ref. MRS	Description	Unit	Quantity	Unit Rate (Rs)	Amount (Rs)
1.15.6	24/106	Supply, installation, testing & commissioning of 16 SWG Sheet steel powder coated back boxes with earth terminal, recessed in wall, includingaccessories, complete in all respect as per specifications and as approved by Engineer		-		
	i)	Small 3"x3"	Each	33.00		
	ii)	Large 6"x3"	Each	11.00		
				-		
1.15.7	N.S	Supply, installation, testing and commissioning of complete earthing system for MCC-TW. The work shall include 3 meter long copper rod of 20 mm dia size with bare copper conductor 1x50 mm.sq ssc upto earth connecting point, insection chamber, etc to achieve less than 3 ohm specified earthing results. Complete in all respects as per drawing and specification or as directed by the Engineer	Each	22.00		
				-		
1.15.8	N.S	Supply, installation, testing & commissioning of following various types of LED lights along with the accessories required for light fitting including light boxes:		-		
				-		
	(i)	12 W Surface Mounted Down Light, (SMD) (90~265VAC), System Lumens: 80~90 lm/W, Power Factor: ≥0.9, LED Driver: Isolated (THD≤20) @ 220 VAC, Housing Material: Die Cast Aluminum, Protection Class: IP-20	Each	44.00		
				-		
	(ii)	Bulkhead 18 W LED Light, (SMD) (100~265VAC), System Lumens: 80~90 lm/W, Power Factor: ≥0.9, LED Driver: Isolated (THD≤20) @ 220 VAC, Housing Material: Aluminum Alloy + PC, Protection Class: IP-65	Each	11.00		
				-		
1.15.9	N.S	Fabrication, supply at site installation and commissioning & connection of wires/cables of distribution boards IP-54 made of 14 SWG M.S sheet degreased , derusted, zinc phosphated, finished with electrostatic powder coating of 100 micron tickness in approved colour with hinged door, flexible earthing strap lockable handle, catcher, earthing bar, neutral strip, internal wiring, designation labels on MCB, earthing bar, numbering beads on control wires, suitable for system 240V, 50HZ, 1 Phase & neutral, bus bars of 99.8% purity electrolytic copper, including cost of cable termination lugs, brass cable glands for incoming & outgoing cables, wiring from breakers, indication lamps, instruments & control all accessories.	Each	11.00		
		Incoming:		-		
		01 No. 32A DP MCB 10 kA		-		

TEHSIL BAHAWALNAGAR (CW-25) (PHASE-I)
BILL OF QUANTITIES
ABSTRACT OF COST

Bill No. 1: WATER SUPPLY SYSTEM

Bill No. 1.15:Pump House (Electrical) Rehabilitation Work

Sr. No.	Ref. MRS	Description	Unit	Quantity	Unit Rate (Rs)	Amount (Rs)
		01 No. Digital Volt Meter 0~240V		-		
		0 No. Control Fuse for Protection		-		
		01 No. Indication Lamp (R)		-		
		01 Job. Brass Cable Gland for Incoming cable		-		
		Outgoing:		-		
		02 Nos. 10A SP MCB 6 kA		-		
		01 No. 20A SP MCB 6 kA		-		
		01 No. 20A SP MCB 6 kA (Spare)		-		
				-		
1.15.10	N.S	Fabrication, supply at site installation and commissioning of 16 SWG mild steel sheet fabricated distribution board for MCC (Motor Control Centre), free standing/ wall mounting, indoor type, front access, insulation class 600 Volts, incoming and outgoing connections from top or bottom as per site requirement, door to body earth with flexible copper cable suitable for 415VAC, 3 Phase 4 wire, 400/230 50Hz TPN&E system, having rated service short circuit breaking capacity as mentioned in the details. Complete in all respects as per the satisfaction of the engineer and single line diagram.	Each	11.00		
		Incoming:		-		
		01 No: 80 ATP MCCB, RC:16 kA		-		
		01 No: Digital Ampere Meter 0~100A With Selector Switch		-		
		01 No: Digital Volt Meter 0~600VAC With Selector Switch		-		
		03 Nos: Current Transformer 80/5A		-		
		03 Nos: Control MCB for protection		-		
		03 Nos: Indication Lamp (R+Y+B)		-		
		01 Job: Brass Cable Gland for Incoming Cable		-		
		01 No: 3 Phase, 4-Wire Energy Meter		-		
		Outgoing:		-		
		01 No. 32A DP MCB RC:10 kA for DBLP-TR		-		
		01 No. 50A TP MCCB RC:16 kA		-		
		01 No. 32A DP MCB RC:10 kA (Spare)		-		
		01 No. 50A TP MCCB RC:16 kA (Spare)		-		
					Total Amount	

ENGINEERING DESIGN AND CONSTRUCTION SUPERVISION SERVICES (EDCS)
PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT (PRSWSSP), CLUSTER SOUTH-III
TEHSIL BAHAWALNAGAR (CW-25) (PHASE-I)
BILL OF QUANTITIES
ABSTRACT OF COST

Bill No. 1: WATER SUPPLY SYSTEM

Bill No. 1.16: Rehabilitation of Exisitng pipe Network

Sr. No.	Ref. MRS	Description	Unit	Quantity	Unit Rate (Rs)	Amount (Rs)
		Earthwork				
1.11.1	3/46	Excavation of trenches in all kinds of soil, except cutting rock, for watersupply pipelines/electric cables upto 5 ft. (1.5 m) depth from ground level, including backfilling, trimming, dressing sides, leveling the beds of trenches to correct grade and cutting pits for joints, etc. complete in all respects.	1000Cft	231.38		
		HDPE Pipe		-		
1.11.2	23/30	Providing, laying, cutting, jointing, testing and disinfecting High Density Polyethylene Pipe (HDPE-100) working presure pipe, Beta/ Dadex/ Popular/ IIL or equivalent including the cost of specials, in trenches, as approved & directed by the engineer incharge, complete in all respects.		-		
		Distibution Network		-		
		a) PN-6 (SDR-26)		-		
		90 mm Dia	Rft	41,690.00		
				-		
1.11.3	6/5	Cement concrete plain including placing, compacting, finishing and curing complete (including screening and washing of stone aggregate): (f) Ratio 1: 2: 4	100Cft	103.40		
1.11.4	1/1	Carriage of 100 Cft. (2.83 cu.m) of all materials like stone aggregate, spawl, kankar lime (unslaked), surkhi, etc. or 150 Cft. (4.25 cu.m) of timber, by truck or by any other means owned by the contractor. (crushed stone aggregate and bajri used in concrete items) (**Form Sargodha Querry)**	100 CFT	91.00		
		Valves		-		
		Sluice Valce		-		
1.11.5	23/35	Providing and fixing sluice valve of B.S.S. quality and weight, Class `B', for cast iron pipe line, and Asbestos cement pipe line (including cost of jointing material):-		-		
		3" i/d (75 mm)	Each	20.00		
				-		

ENGINEERING DESIGN AND CONSTRUCTION SUPERVISION SERVICES (EDCS)
PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT (PRSWSSP), CLUSTER SOUTH-III
TEHSIL BAHAWALNAGAR (CW-25) (PHASE-I)
BILL OF QUANTITIES
ABSTRACT OF COST

Bill No. 1: WATER SUPPLY SYSTEM

Bill No. 1.16: Rehabilitation of Exisitng pipe Network

Sr. No.	Ref. MRS	Description	Unit	Quantity	Unit Rate (Rs)	Amount (Rs)
		Air Release		-		
1.11.6	23/37	Providing and fixing, air valve 2½ (65mm) dia of B.S.S. quality and weight (complete with jointing material).		-		
		b) double	Each	10.00		
1.11.7	23/22	Providing and fixing cast iron specials of B.S.S. Class 'B' (such as bend, tee, cross collar, reducer, tail piece, flanged socket, flanged spigot, cap, taper, angle branch, plug, etc) for Asbestos cement pipe line, with comet joint and rubber ring, complete. i) 3" to 6" (75 to 150 mm) i/d	Per Kg	150.00		
1.11.8	23/35	Providing and fixing sluice valve of B.S.S. quality and weight, Class `B', for cast iron pipe line, and Asbestos cement pipe line (including cost of jointing material):- a) 3" i/d (75 mm)	Each	10.00		
				-		
		Washout Valve		-		
1.11.9	23/35	Providing and fixing sluice valve of B.S.S. quality and weight, Class `B', for cast iron pipe line, and Asbestos cement pipe line (including cost of jointing material):- 3" i/d (75 mm)	Each	10.00		
					Total Amount	

TEHSIL BAHAWALNAGAR (CW-25) (PHASE-I)
BILL OF QUANTITIES
ABSTRACT OF COST

Bill No. 1: WATER SUPPLY SYSTEM

Bill No. 1.17: Rehabilitation of exisitng Valves Chambers

Sr. No.	Ref. MRS	Description	Unit	Quantity	Unit Rate (Rs)	Amount (Rs)
1.12.1	3/21	Excavation in foundation of building, bridges and other structures, including dagbelling, dressing, refilling in layers around structure with excavated earth, watering and ramming lead 'upto one chain (30 m) and lift upto 5 ft. (1.5 m). a) By Manual ii) Ordinary soil	1000 Cft.	5.96		
1.12.2	6/5	Cement concrete plain including placing, compacting, finishing and curing complete (including screening and washing of stone aggregate): (i) Ratio 1: 4: 8	100Cft	2.62		
1.12.3	6/5	Cement concrete plain including placing, compacting, finishing and curing complete (including screening and washing of stone aggregate): (f) Ratio 1: 2: 4	100Cft	5.05		
1.12.4	7/7	Pacca brick work other than building upto 10ft. (3 m) height. i) cement, sand mortar:- (1:4)	100 Cft	21.36		
1.12.5	11/8	Cement plaster 1:3 upto 20' (6.00 m) height:- b) ½" (13 mm) thick	100 Sft	54.70		
	6/6	Providing and laying reinforced cement concrete (including prestressed concrete), using Ordinary Portland Cement / Sulphate resisting cement / Slag cement as may be required; coarse sand and screened graded and washed aggregate, in required shape and design, including forms, moulds, shuttering, lifting, compacting, curing, rendering and finishing exposed surface, complete (but excluding the cost of steel reinforcement, its fabrication and placing in position, etc.):-		-		
1.12.6		(a) Reinforced cement concrete in roof slab, beams, columns lintels, girders and other structural members laid in situ or precast laid in position, or prestressed members cast in situ, complete in all respects:- (3) Type C (nominal mix 1: 2: 4)	Per Cft	370.02		
1.12.7	1/1	Carriage of 100 Cft. (2.83 cu.m) of all materials like stone aggregate, spawl, kankar lime (unslaked), surkhi, etc. or 150 Cft. (4.25 cu.m) of timber, by truck or by any other means owned by the contractor. (crushed stone aggregate and bajri used in concrete items) (**Form Sargodha Querry)**	100 CFT	8.28		
1.12.8	6/12 b	Fabrication of mild steel reinforcement for cement concrete including cutting, bending, laying in position, making joints and fastenings, including cost of binding wire and labour charges for binding of steel reinforcement (also includes removal of rust from bars):- b) Deformed bars (Grade-60)	100 Kg	8.41		

ENGINEERING DESIGN AND CONSTRUCTION SUPERVISION SERVICES (EDCS)
PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT (PRSWSSP), CLUSTER SOUTH-III

TEHSIL BAHAWALNAGAR (CW-25) (PHASE-I)
BILL OF QUANTITIES
ABSTRACT OF COST

Bill No. 1: WATER SUPPLY SYSTEM

Bill No. 1.17: Rehabilitation of exisitng Valves Chambers

Sr. No.	Ref. MRS	Description	Unit	Quantity	Unit Rate (Rs)	Amount (Rs)
1.12.9	N.S.	Providing and fixing of RPC Manhole Cover Manufactured with 100% Recycled Plastic Composite Material, 650 mm (26"dia) with clear opening size 600 mm (24" dia) and RPC manhole frame having dia meter 790 mm (31.1") with average breaking load capacity of 10 Ton and weight including frame of 50 kg (Minimum).	Each	40.00		
					Total Amount	

ENGINEERING DESIGN AND CONSTRUCTION SUPERVISION SERVICES (EDCS)
PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT (PRSWSSP), CLUSTER SOUTH-III
TEHSIL BAHAWALNAGAR (CW-25) (PHASE-I)
BILL OF QUANTITIES
ABSTRACT OF COST

Bill No.2. SEWERAGE SYSTEM

Bill No. 2.1: DRAIN NETWORK

Sr. No.	Ref	Description	Unit	Quantity	Unit Rate (Rs)	Amount (Rs)
2.1.1	4/29	Dismantling brick or flagged flooring without concrete foundation.	100 Sft	3,197.18		
				-		
2.1.2	21/8	Restoration of brick pavement on edge, over laid service line, with 2" (50 mm) sand cushion under soling.	100 Sft	3,197.18		
				-		
2.1.3	4/19 a	Dismantling cement concrete plain 1:4:8.	100Cft.	50.40		
				-		
2.1.4	4/46	Dismantling and removing road pavement, etc., including screening and stacking of byproducts upto one chain lead (30 metre).	100 Cft	663.42		
				-		
2.1.5	21/10	Restoration of metalled road, on laid service line, including Restoration of metalled road, on laid service line, including compaction:- a) Carpetted road, with 2" (50 mm) carpet and 10" (250 mm) depth of stone metal for sub-base and base.	100 Sft	799.30		
				-		
2.1.6	21/24	Desilting including disposal of sludge upto one Chain (30 Meters). a) Open Drain	100 Cft	159.86		
				-		
2.1.7	3/9	Earthwork excavation in irrigation channels, drains, etc. to designed section, grades and profiles, excavated material disposed off and dressed within 100 ft. (30 m) lead:-		-		
		i) Ordinary	1000 Cft.	1,633.81		
				-		
2.1.8	6/3	Cement concrete brick or stone ballast 1½ " to 2" (40 mm to 50 mm) gauge, in foundation and plinth:- (d) Ratio 1: 6:12	100 Cft.	1,140.69		
				-		
2.1.9	6/5	Cement concrete plain including placing, compacting, finishing and curing complete (including screening and washing of stone aggregate): (f) Ratio 1: 2: 4	100 Cft.	944.43		
				-		
2.1.10	20/6	Constructing Punjab Standard Drains. of cement concrete 1:2 ½ :5, with cement concrete bedding ratio 1:6:12, complete, laid to lines, grades, slopes and shapes, rendering exposed surface of concrete with 1:1 cement, sand mortar, ¼" (6 mm) thick, as per Engineer's drawing (excluding excavation):- a) Type I	Per Rft	159,859.22		
2.1.11	7/4	Pacca brick work in foundation and plinth in:- Ratio 1:5	100 Cft.	3,255.83		
				-		

ENGINEERING DESIGN AND CONSTRUCTION SUPERVISION SERVICES (EDCS)
PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT (PRSWSSP), CLUSTER SOUTH-III
TEHSIL BAHAWALNAGAR (CW-25) (PHASE-I)
BILL OF QUANTITIES
ABSTRACT OF COST

Bill No.2. SEWERAGE SYSTEM

Bill No. 2.1: DRAIN NETWORK

Sr. No.	Ref	Description	Unit	Quantity	Unit Rate (Rs)	Amount (Rs)
2.1.12	20/1	Tega formed of pacca bricks on end, laid in and over cement sand mortar projecting to a height of not more than 6" (150 mm) top of drain along the property side where required, laid to lines, grades, slopes and shape according to the Engineer's drawing:- a) 3" thick (75 mm) ii) ratio 1:5	100Rft	1,598.59		
				-		
2.1.13	20/3	Pacca brick on edge, laid in reimbursement, in cement, sand mortar, on sides of drains and on other works where required. All joints to be completely filled and struck flush:- b) ratio 1:5	100Sft	1,198.94		
				-		
		Top Slab (R.C.C. 1:2:4)		-		
2.1.14	6/6	Providing and laying reinforced cement concrete (including prestressed concrete), using Ordinary Portland Cement / Sulphate resisting cement / Slag cement as may be required; coarse sand and screened graded and washed aggregate, in required shape and design,including forms, moulds, shuttering, lifting, compacting, curing, rendering and finishing exposed surface, complete (but excluding the cost of steel reinforcement, its fabricationand placing in position, etc.):-		-		
		(d) Precast reinforced cement concrete and prestressed reinforced cement concrete in columns, beams, lintels, stair cases, shelves, etc. (3) Type C (nominal mix 1: 2: 4)	Per Cft	77,873.80		
2.1.15	1/1	Carriage of 100 Cft. (2.83 cu.m) of all materials like stone aggregate, spawl, kankar lime (unslaked), surkhi, etc. or 150 Cft. (4.25 cu.m) of timber, by truck or by any other means owned by the contractor. **(From Sargodha Querry)**	100 Cft	1,848.39		
2.1.16	6/12	Fabrication of mild steel reinforcement for cement concrete, including cutting, bending, laying in position, making joints and fastenings, including cost of binding wire and labour charges for binding of steel reinforcement (also includes removal of rust from bars):- (b) Deformed bars (ii) (Grade-60)	100 Kg	2,296.12		
				-		
2.1.17	3/5	Earthowrk in ordinary soil for embankments lead upto 100 ft. (30 m), including ploughing, mixing and compaction by mechanical means at optimum moisture content and dressing to designed section, complete in all respects:- ii) 90% maximum modified AASHTO dry density.	1000 Cft.	1,119.01		

ENGINEERING DESIGN AND CONSTRUCTION SUPERVISION SERVICES (EDCS)
PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT (PRSWSSP), CLUSTER SOUTH-III
TEHSIL BAHAWALNAGAR (CW-25) (PHASE-I)
BILL OF QUANTITIES
ABSTRACT OF COST

Bill No.2. SEWERAGE SYSTEM

Bill No. 2.1: DRAIN NETWORK

Sr. No.	Ref	Description	Unit	Quantity	Unit Rate (Rs)	Amount (Rs)
2.1.18	3/17	Transportation of earth all types when the total distance, including the lead covered in the item of work, is more than 1000 ft. (300 m)		-		
		a) Upto ¼ mile (400 m).	1000 Cft.	1,119.01		
		b) For every 330 ft. (100 m) additional lead or part thereof, beyond ¼ mile (400 m) upto one mile. (1.6 Km.)	1000 Cft.	1,119.01		
		Drain House Connnection		-		
2.1.19	R.A.A.	Construction of house Connection Chamber of specified size, complete in all respects as per drawings, specifications & instructions of the Engineer incharge. The unit rate includes but not limited to excavation, backfilling, compaction, PCC (1:6:12) in bedding, PCC (1:2:4) benching, brick masonry in 1:4, C/S mortar, 1/2" thick 1:4 C/S plaster on both sides, precasted Cover slabs, 4" dia uPVC pipe gor house connection and connection to manhole with 6" dia uPVC pipe (excluding cost of 6" dia pipe) finished etc complete in all respects.		-		
		Type-1	Job	2,574.60		
		Type-2	Job	357.00		
		Type-3	Job	107.10		
2.1.20	19/48	Providing, fixing, testing and commissioning of µ-PVC (Unplasticized Polyvinyl Chloride) sewerage pipe make of Dadex /Popular/Beta or approved equivalent manufacturer, plain /socket ended conforming to code EN-1401 of specified SDR (Standard Dimension Ratio) including the cost of specials and Solvents complete in all respect as approved and directed by the Engineer Incharge. Type (SDR 34/SN-8)		-		
		i) 6" dia 150mm	Per Rft	45,580.50		
		RPC SLAB		-		
2.1.21	N.S.	RPC Slab Perforated 1.5 ft x 3 ft 50mm thickness load bearing (4 Ton axle load/ point load)	Each	13,321.60		
2.1.22	N.S.	RPC Slab Perforated 3 ft x 3 ft 50mm thickness load bearing (4 Ton axle load/ point load)	Each	3,215.78		
					Total Amount	

ENGINEERING DESIGN AND CONSTRUCTION SUPERVISION SERVICES (EDCS)
PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT (PRSWSSP), CLUSTER SOUTH-III
TEHSIL BAHAWALNAGAR (CW-25) (PHASE-I)
BILL OF QUANTITIES
ABSTRACT OF COST

Bill No.2. SEWERAGE SYSTEM

Bill No. 2.2: Septic Tank Type-I (A)

Sr. Nr.	MRS Ref.	Description	Unit	Quantity	Unit Rate	Amount Rs.
2.2.1	3/21	Excavation in foundation of building, bridges and other structures, including dagbelling, dressing, refilling in layers around structure with excavated earth, watering and ramming lead upto one chain (30 m)lift upto 5 ft (1.5m). 2) a) By Excavator ii) Ordinary soil				
		a) Lift up to 5 ft (1.5 m)	1000 Cft	17.04		
		b) Lift from 5ft (1.5m) to 15 ft (4.5 m):-	1000 Cft	7.87		
		Concrete Works				
2.2.2	6/3	Cement concrete brick or stone ballast 1½ " to 2" (40 mm to 50 mm) gauge, in foundation and plinth:-				
		(b) Ratio 1: 4: 8 (with Brick Ballast)	100Cft	2.96		
2.2.3	7/4	Pacca brick work in foundation and plinth in:-				
		Ratio 1:3	100Cft	26.13		
2.2.4	6/6	Providing and laying reinforced cement concrete (including prestressed concrete), using Ordinary Portland Cement / Sulphate resisting cement / Slag cement as may be required; coarse sand and screened graded and washed aggregate, in required shape and design, including forms, moulds, shuttering, lifting, compacting, curing, rendering and finishing exposed surface, complete (but excluding the cost of steel reinforcement, its fabrication and placing in position, etc.):-				
		(a) (i) Reinforced cement concrete in roof slab, beams, columns lintels, girders and other structural members laid in situ or precast laid in position, or prestressed members cast in situ, complete in all respects:-				
		(2) Type B (nominal mix 1: 1½: 3)	Per Cft	262.08		
		(c) Reinforced cement concrete in Pile cap, slab of rafts / strip foundation, base slab of column and retaining walls; etc and footing beams, other structural members other than those mentioned in 6(a-d) above not requiring form work (i.e. horizontal shuttering) complete in all respects:-				
		Type B (nominal mix 1: 1.5: 3)	Per Cft	659.16		
2.2.5	6/12	Fabrication of mild steel reinforcement for cement concrete, including cutting, bending, laying in position, making joints and steel chairs, etc. complete in all respect. and fastenings, including cost of binding wire and labour charges for binding of steel reinforcement (also Includes removal of rust from bars):- (b) Deformed bars (Grade-60)	100 Kg	27.17		

ENGINEERING DESIGN AND CONSTRUCTION SUPERVISION SERVICES (EDCS)
PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT (PRSWSSP), CLUSTER SOUTH-III
TEHSIL BAHAWALNAGAR (CW-25) (PHASE-I)
BILL OF QUANTITIES
ABSTRACT OF COST

Bill No.2. SEWERAGE SYSTEM

Bill No. 2.2: Septic Tank Type-I (A)

Sr. Nr.	MRS Ref.	Description	Unit	Quantity	Unit Rate	Amount Rs.
2.2.6	1/1	Carriage of 100 Cft. (2.83 cu.m) of all materials like stone aggregate, spawl, kankar lime (unslaked), surkhi, etc. or 150 Cft. (4.25 cu.m) of timber, by truck or by any other means owned by the contractor. (crushed stone aggregate and bajri used in concrete items) **(Form Sargodha Querry**)	100Cft	7.74		
2.2.7	6/32	Providing and embedding 10" (250mm) wide PVC water stopper in expansion joints of RCC structures (Retaining walls, water tanks, Slabs) complete in all respect. Charge				
		ii) 10" wide 10 mm thick	Rft	330.84		
2.2.8	13/09	Bitumen coating to plastered or cement concrete surface:- i) 20 lbs. per 100 Sft. (9.07 Kg per Sq.m)	100Sft.	65.98		
				-		
2.2.9	21/11	Providing and fixing 1¼"x1¼"x3/16" (31x31x5 mm) angle iron step, in manhole chambers, including carriage and setting the same in work to correct lines and levels.	Each	110.00		
2.2.10	23/30	Providing, laying, cutting, jointing, testing and disinfecting High Density Polyethylene Pipe (HDPE-100) working presure pipe conforming to standard ISO 4427, DIN 8074 / 8075, PS 3580, Beta/ Dadex / Popular/ IIL or approved equivalent manufacturer, including the cost of specials, intrenches, as approved & directed by the Engineer incharge, complete in all respects. **a) PN-6 (SDR-26)**		-		
		1) 90 mm	Rft	745.00		
				-		
2.2.11	23/18	Providing, laying, cutting, jointing, testing and disinfecting cast iron pipe line (BS-2035/4622) in trenches, including cost of materials, such as lead, yarn, etc.complete in all respects:- b) With Flanged and Flanged Joints 4" Dia (Vent Pipe)	Rft	24.00		
				-		
2.2.12	N.S.	P/F RPC Manhole Cover Manufactured with 100% Recycled Plastic Composite Material, 650 mm (26"dia) with clear opening size 600 mm (24" Dia) and RPC manhole frame having Dia meter 790 mm (31.1") with average breaking load capacity of 10 Ton and weight including frame of 50 kg (Minimum).	Each	11.00		

ENGINEERING DESIGN AND CONSTRUCTION SUPERVISION SERVICES (EDCS)
PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT (PRSWSSP), CLUSTER SOUTH-III
TEHSIL BAHAWALNAGAR (CW-25) (PHASE-I)
BILL OF QUANTITIES
ABSTRACT OF COST

Bill No.2. SEWERAGE SYSTEM

Bill No. 2.2: Septic Tank Type-I (A)

Sr. Nr.	MRS Ref.	Description	Unit	Quantity	Unit Rate	Amount Rs.
2.2.13	26/46	Providing and fixing hot dipped Galvanized Iron chainlink mesh/fence of 2"x2"mesh made of wire of specified guage, with the help of 1"x1/8" GI patti, GI.clamps and screws, i/c the cost of 3 nos 8 SWG GI tie wires penetrated through mesh at top,middle and bottom, fixed on vertical posts of 2" diameter GI pipes (medium quality) erected @ 8 ft C/C duly embeded in PCC(1:2:4) etc. complete in all respect as approved and directed by the Engineer Incharge. (ii) 10 SWG	Each	2,000.00		
	N.S	Supplying, installing, testing and commissioning of submersible waste water pump set of approved make, complete in all respects as per specifications and direction of the Engineer Incharge. The pump set shall have the following specifications: Flow: 0.05 Cusec Head: 25~30 ft Motor Rating: 0.75 HP, 1x220V 50H, 2 Pole, Submersible IP68 motor, Insulation class F Motor: 1.5 KW / 0.75HP / 2Pole Material of Construction Impeller - Stainless Steel AISI 403 Mechanical seal- Silicon Carbide Motor Housing- Stainless Steel AISI 403 Shaft- Stainless Steel AISI 403 Motor Control Unit (MCU): MCU (Motor Control Unit) consisting of MCCB, Over/Under voltage relay, Phase reversal relay, Volt meter, Ampere meter, EVR, Volt Selector Switch, Ampere Selector Switch, Current Transformer, Over load relay, indicating lights for all above relays, on/off push buttons. VFD Motor Control Unit with Dry running Protection relay, Circuit Breaker, DC SPD, AC SPD, DC Change Over Switch, Auto Start Stop with Any input, Self-diagnostic and Self Protection, Dry Run Protection, Digital Controls with Complete Protective Functions, Ground Fault Monitoring, AC Short Circuit Protection, Under/Over Voltage and Over/Current Protection, Reverse	Job	4.00		
					Total Amount	

ENGINEERING DESIGN AND CONSTRUCTION SUPERVISION SERVICES (EDCS)
PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT (PRSWSSP), CLUSTER SOUTH-III
TEHSIL BAHAWALNAGAR (CW-25) (PHASE-I)
BILL OF QUANTITIES
ABSTRACT OF COST

Bill No.2. SEWERAGE SYSTEM

Bill No. 2.3: Septic Tank Type-I

Sr. Nr.	MRS Ref.	Description	Unit	Quantity	Unit Rate	Amount Rs.
2.3.1	3/21	Excavation in foundation of building, bridges and other structures, including dagbelling, dressing, refilling in layers around structure with excavated earth, watering and ramming lead upto one chain (30 m)lift upto 5 ft (1.5m). 2) a) By Excavator ii) Ordinary soil				
		a) Lift up to 5 ft (1.5 m)	1000 Cft	117.65		
		b) Lift from 5ft (1.5m) to 15 ft (4.5 m):-	1000 Cft	23.22		
	Concrete Works					
2.3.2	6/3	Cement concrete brick or stone ballast 1½ " to 2" (40 mm to 50 mm) gauge, in foundation and plinth:-				
		(b) Ratio 1: 4: 8 (with Brick Ballast)	100Cft	15.32		
2.3.3	6/6	Providing and laying reinforced cement concrete (including prestressed concrete), using Ordinary Portland Cement / Sulphate resisting cement / Slag cement as may be required; coarse sand and screened graded and washed aggregate, in required shape and design, including forms, moulds, shuttering, lifting, compacting, curing, rendering and finishing exposed surface, complete (but excluding the cost of steel reinforcement, its fabrication and placing in position, etc.):-				
		(a) (i) Reinforced cement concrete in roof slab, beams, columns lintels, girders and other structural members laid in situ or precast laid in position, or prestressed members cast in situ, complete in all respects:-				
		(2) Type B (nominal mix 1: 1½: 3)	Per Cft	2,128.00		
		(b) Reinforced cement concrete in retaining/ Shear walls laid in situ or precast laid in position, or prestressed members castin situ (Formwork on both sides), complete in all respects: (b) Type B (nominal mix 1:1-1/2:3)				
		(i) Upto 9" thick (Avg)	Per Cft	9,054.24		
		(c) Reinforced cement concrete in Pile cap, slab of rafts / strip foundation, base slab of column and retaining walls; etc and footing beams, other structural members other than those mentioned in 6(a-d) above not requiring form work (i.e. horizontal shuttering) complete in all respects:-				
		Type B (nominal mix 1: 1.5: 3)	Per Cft	3,532.48		

Bill No.2. SEWERAGE SYSTEM

Bill No. 2.3: Septic Tank Type-I

Sr. Nr.	MRS Ref.	Description	Unit	Quantity	Unit Rate	Amount Rs.
2.3.4	6/12	Fabrication of mild steel reinforcement for cement concrete, including cutting, bending, laying in position, making joints and steel chairs, etc. complete in all respect. and fastenings, including cost of binding wire and labour charges for binding of steel reinforcement (also Includes removal of rust from bars):- (b) Deformed bars (Grade-60)	100 Kg	433.96		
2.3.5	1/1	Carriage of 100 Cft. (2.83 cu.m) of all materials like stone aggregate, spawl, kankar lime (unslaked), surkhi, etc. or 150 Cft. (4.25 cu.m) of timber, by truck or by any other means owned by the contractor. (crushed stone aggregate and bajri used in concrete items) **(Form Sargodha Querry**)	100Cft	123.60		
2.3.6	6/32	Providing and embedding 10" (250mm) wide PVC water stopper in expansion joints of RCC structures (Retaining walls, water tanks, Slabs) complete in all respect. Charge				
		ii) 10" wide 10 mm thick	Rft	1,273.44		
2.3.7	13/09	Bitumen coating to plastered or cement concrete surface:- i) 20 lbs. per 100 Sft. (9.07 Kg per Sq.m)	100Sft.	215.35		
2.3.8	21/11	Providing and fixing 1¼"x1¼"x3/16" (31x31x5 mm) angle iron step, in manhole chambers, including carriage and setting the same in work to correct lines and levels.	Each	480.00		
2.3.9	23/30	Providing, laying, cutting, jointing, testing and disinfecting High Density Polyethylene Pipe (HDPE-100) working presure pipe conforming to standard ISO 4427, DIN 8074 / 8075, PS 3580, Beta/ Dadex / Popular/ IIL or approved equivalent manufacturer, including the cost of specials, intrenches, as approved & directed by the Engineer incharge, complete in all respects. **a) PN-6 (SDR-26)**				
		1) 90 mm	Rft	6,295.60		
2.3.10	23/18	Providing, laying, cutting, jointing, testing and disinfecting cast iron pipe line (BS-2035/4622) in trenches, including cost of materials, such as lead, yarn, etc.complete in all respects:- b) With Flanged and Flanged Joints 4" Dia (Vent Pipe)	Rft	96.00		
2.3.11	23/12	Providing and installing M.S. blind pipe socketed/welded joint, M.S. reducer (where necessary), in tubewell bore hole, including jointing/welding with strainer, etc. complete:- (Chamber to ABR Connection Pipe)				
		e) 6" i/d, 3/16" (150 mm i/d 5 mm) thick	Rft	800.00		

ENGINEERING DESIGN AND CONSTRUCTION SUPERVISION SERVICES (EDCS)
PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT (PRSWSSP), CLUSTER SOUTH-III
TEHSIL BAHAWALNAGAR (CW-25) (PHASE-I)
BILL OF QUANTITIES
ABSTRACT OF COST

Bill No.2. SEWERAGE SYSTEM

Bill No. 2.3: Septic Tank Type-I

Sr. Nr.	MRS Ref.	Description	Unit	Quantity	Unit Rate	Amount Rs.
2.3.12	N.S.	P/F RPC Manhole Cover Manufactured with 100% Recycled Plastic Composite Material, 650 mm (26"dia) with clear opening size 600 mm (24" Dia) and RPC manhole frame having Dia meter 790 mm (31.1") with average breaking load capacity of 10 Ton and weight including frame of 50 kg (Minimum).	Each	48.00		
2.3.13	26/46	Providing and fixing hot dipped Galvanized Iron chainlink mesh/fence of 2"x2"mesh made of wire of specified guage, with the help of 1"x1/8" GI patti, GI.clamps and screws, i/c the cost of 3 nos 8 SWG GI tie wires penetrated through mesh at top,middle and bottom, fixed on vertical posts of 2" diameter GI pipes (medium quality) erected @ 8 ft C/C duly embeded in PCC(1:2:4) etc. complete in all respect as approved and directed by the Engineer Incharge. (ii) 10 SWG	Each	8,000.00		
2.3.14	N.S	Supplying, installing, testing and commissioning of submersible waste water pump set of approved make, complete in all respects as per specifications and direction of the Engineer Incharge. The pump set shall have the following specifications: Flow: 0.05 Cusec Head: 25~30 ft Motor Rating: 0.75 HP, 1x220V 50H, 2 Pole, Submersible IP68 motor, Insulation class F Motor: 1.5 KW / 0.75HP / 2Pole Material of Construction Impeller - Stainless Steel AISI 403 Mechanical seal- Silicon Carbide Motor Housing- Stainless Steel AISI 403 Shaft- Stainless Steel AISI 403 Motor Control Unit (MCU): MCU (Motor Control Unit) consisting of MCCB, Over/Under voltage relay, Phase reversal relay, Volt meter, Ampere meter, EVR, Volt Selector Switch, Ampere Selector Switch, Current Transformer, Over load relay, indicating lights for all above relays, on/off push buttons. VFD Motor Control Unit with Dry running Protection relay, Circuit Breaker, DC SPD, AC SPD, DC Change Over Switch, Auto Start Stop with Any input, Self-diagnostic and Self Protection, Dry Run Protection, Digital Controls with Complete Protective Functions, Ground Fault Monitoring, AC Short Circuit Protection, Under/Over Voltage and Over/Current Protection, Reverse	Job	12.00		
					Total Amount	

ENGINEERING DESIGN AND CONSTRUCTION SUPERVISION SERVICES (EDCS)
PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT (PRSWSSP), CLUSTER SOUTH-III
TEHSIL BAHAWALNAGAR (CW-25) (PHASE-I)
BILL OF QUANTITIES
ABSTRACT OF COST

Bill No.2. SEWERAGE SYSTEM

Bill No. 2.4: Septic Tank Type-II

Sr. Nr.	MRS Ref.	Description	Unit	Quantity	Unit Rate	Amount Rs.
2.4.1	3/21	Excavation in foundation of building, bridges and other structures, including dagbelling, dressing, refilling in layers around structure with excavated earth, watering and ramming lead upto one chain (30 m)lift upto 5 ft (1.5m). 2) a) By Excavator ii) Ordinary soil				
		a) Lift up to 5 ft (1.5 m)	1000 Cft	107.17		
		b) Lift from 5ft (1.5m) to 15 ft (4.5 m):-	1000 Cft	31.03		
	Concrete Works					
2.4.2	6/3	Cement concrete brick or stone ballast 1½ " to 2" (40 mm to 50 mm) gauge, in foundation and plinth:-				
		(b) Ratio 1: 4: 8 (with Brick Ballast)	100Cft	11.66		
2.4.3	6/6	Providing and laying reinforced cement concrete (including prestressed concrete), using Ordinary Portland Cement / Sulphate resisting cement / Slag cement as may be required; coarse sand and screened graded and washed aggregate, in required shape and design, including forms, moulds, shuttering, lifting, compacting, curing, rendering and finishing exposed surface, complete (but excluding the cost of steel reinforcement, its fabrication and placing in position, etc.):-				
		(a) (i) Reinforced cement concrete in roof slab, beams, columns lintels, girders and other structural members laid in situ or precast laid in position, or prestressed members cast in situ, complete in all respects:-				
		(2) Type B (nominal mix 1: 1½: 3)	Per Cft	1,634.04		
		(b) Reinforced cement concrete in retaining/ Shear walls laid in situ or precast laid in position, or prestressed members castin situ (Formwork on both sides), complete in all respects: (b) Type B (nominal mix 1:1-1/2:3)				
		(i) Upto 9" thick (Avg)	Per Cft	1,057.50		
		(ii) More Than 9" thick (Avg)	Per Cft	8,102.16		
		(c) Reinforced cement concrete in Pile cap, slab of rafts / strip foundation, base slab of column and retaining walls; etc and footing beams, other structural members other than those mentioned in 6(a-d) above not requiring form work (i.e. horizontal shuttering) complete in all respects:-				
		(2) Type B (nominal mix 1: 1½: 3)	Per Cft	2,712.60		

ENGINEERING DESIGN AND CONSTRUCTION SUPERVISION SERVICES (EDCS)
PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT (PRSWSSP), CLUSTER SOUTH-III
TEHSIL BAHAWALNAGAR (CW-25) (PHASE-I)
BILL OF QUANTITIES
ABSTRACT OF COST

Bill No.2. SEWERAGE SYSTEM

Bill No. 2.4: Septic Tank Type-II

Sr. Nr.	MRS Ref.	Description	Unit	Quantity	Unit Rate	Amount Rs.
2.4.4	6/12	Fabrication of mild steel reinforcement for cement concrete, including cutting, bending, laying in position, making joints and steel chairs, etc. complete in all respect. and fastenings, including cost of binding wire and labour charges for binding of steel reinforcement (also Includes removal of rust from bars):- (b) Deformed bars (Grade-60)	100 Kg	398.32		
2.4.5	1/1	Carriage of 100 Cft. (2.83 cu.m) of all materials like stone aggregate, spawl, kankar lime (unslaked), surkhi, etc. or 150 Cft. (4.25 cu.m) of timber, by truck or by any other means owned by the contractor. (crushed stone aggregate and bajri used in concrete items) **(Form Sargodha Querry**)	100Cft	113.45		
2.4.6	6/32	Providing and embedding 10" (250mm) wide PVC water stopper in expansion joints of RCC structures (Retaining walls, water tanks, Slabs) complete in all respect. Charge				
		ii) 10" wide 10 mm thick	Rft	770.49		
2.4.9	13/09	Bitumen coating to plastered or cement concrete surface:- i) 20 lbs. per 100 Sft. (9.07 Kg per Sq.m)	100Sft.	195.23		
2.4.9	21/11	Providing and fixing 1¼"x1¼"x3/16" (31x31x5 mm) angle iron step, in manhole chambers, including carriage and setting the same in work to correct lines and levels.	Each	270.00		
2.4.9	23/30	Providing, laying, cutting, jointing, testing and disinfecting High Density Polyethylene Pipe (HDPE-100) working presure pipe conforming to standard ISO 4427, DIN 8074 / 8075, PS 3580, Beta/ Dadex / Popular/ IIL or approved equivalent manufacturer, including the cost of specials, intrenches, as approved & directed by the Engineer incharge, complete in all respects. **a) PN-6 (SDR-26)**				
		1) 90 mm	Rft	5,966.60		
2.4.10	23/18	Providing, laying, cutting, jointing, testing and disinfecting cast iron pipe line (BS-2035/4622) in trenches, including cost of materials, such as lead, yarn, etc.complete in all respects:- b) With Flanged and Flanged Joints 4" Dia (Vent Pipe)	Rft	54.00		
2.2.11	23/12	Providing and installing M.S. blind pipe socketed/welded joint, M.S. reducer (where necessary), in tubewell bore hole, including jointing/welding with strainer, etc. complete:- (Chamber to ABR Connection Pipe)				
		e) 6" i/d, 3/16" (150 mm i/d 5 mm) thick	Rft	450.00		

ENGINEERING DESIGN AND CONSTRUCTION SUPERVISION SERVICES (EDCS)
PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT (PRSWSSP), CLUSTER SOUTH-III
TEHSIL BAHAWALNAGAR (CW-25) (PHASE-I)
BILL OF QUANTITIES
ABSTRACT OF COST

Bill No.2. SEWERAGE SYSTEM

Bill No. 2.4: Septic Tank Type-II

Sr. Nr.	MRS Ref.	Description	Unit	Quantity	Unit Rate	Amount Rs.
2.4.12	N.S.	P/F RPC Manhole Cover Manufactured with 100% Recycled Plastic Composite Material, 650 mm (26"dia) with clear opening size 600 mm (24" Dia) and RPC manhole frame having Dia meter 790 mm (31.1") with average breaking load capacity of 10 Ton and weight including frame of 50 kg (Minimum).	Each	27.00		
2.2.13	26/46	Providing and fixing hot dipped Galvanized Iron chainlink mesh/fence of 2"x2"mesh made of wire of specified guage, with the help of 1"x1/8" GI patti, GI.clamps and screws, i/c the cost of 3 nos 8 SWG GI tie wires penetrated through mesh at top,middle and bottom, fixed on vertical posts of 2" diameter GI pipes (medium quality) erected @ 8 ft C/C duly embeded in PCC(1:2:4) etc. complete in all respect as approved and directed by the Engineer Incharge. (ii) 10 SWG	Each	4,500.00		
2.2.14	N.S	Supplying, installing, testing and commissioning of submersible waste water pump set of approved make, complete in all respects as per specifications and direction of the Engineer Incharge. The pump set shall have the following specifications: Flow: 0.05 Cusec Head: 25~30 ft Motor Rating: 0.75 HP, 1x220V 50H, 2 Pole, Submersible IP68 motor, Insulation class F Motor: 1.5 KW / 0.75HP / 2Pole Material of Construction Impeller - Stainless Steel AISI 403 Mechanical seal- Silicon Carbide Motor Housing- Stainless Steel AISI 403 Shaft- Stainless Steel AISI 403 Motor Control Unit (MCU): MCU (Motor Control Unit) consisting of MCCB, Over/Under voltage relay, Phase reversal relay, Volt meter, Ampere meter, EVR, Volt Selector Switch, Ampere Selector Switch, Current Transformer, Over load relay, indicating lights for all above relays, on/off push buttons. VFD Motor Control Unit with Dry running Protection relay, Circuit Breaker, DC SPD, AC SPD, DC Change Over Switch, Auto Start Stop with Any input, Self-diagnostic and Self Protection, Dry Run Protection, Digital Controls with Complete Protective Functions, Ground Fault Monitoring, AC Short Circuit Protection, Under/Over Voltage and Over/Current Protection, Reverse	Job	6.00		
					Total Amount	

ENGINEERING DESIGN AND CONSTRUCTION SUPERVISION SERVICES (EDCS)
PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT (PRSWSSP), CLUSTER SOUTH-III
TEHSIL BAHAWALNAGAR (CW-25) (PHASE-I)
BILL OF QUANTITIES
ABSTRACT OF COST

Bill No.2. SEWERAGE SYSTEM

Bill No. 2.5: Septic Tank Type-III

Sr. Nr.	MRS Ref.	Description	Unit	Quantity	Unit Rate	Amount Rs.
#REF!	3/21	Excavation in foundation of building, bridges and other structures, including dagbelling, dressing, refilling in layers around structure with excavated earth, watering and ramming lead upto one chain (30 m)lift upto 5 ft (1.5m). 2) a) By Excavator ii) Ordinary soil				
		a) Lift up to 5 ft (1.5 m)	1000 Cft	52.51		
		b) Lift from 5ft (1.5m) to 15 ft (4.5 m):-	1000 Cft	33.36		
#REF!						
#REF!	**Concrete Works**					
#REF!	6/3	Cement concrete brick or stone ballast 1½ " to 2" (40 mm to 50 mm) gauge, in foundation and plinth:-				
		(b) Ratio 1: 4: 8 (with Brick Ballast)	100Cft	12.76		
#REF!						
		Providing and laying reinforced cement concrete (including prestressed concrete), using Ordinary Portland Cement / Sulphate resisting cement / Slag cement as may be required; coarse sand and screened graded and washed aggregate, in required shape and design, including forms, moulds, shuttering, lifting, compacting, curing, rendering and finishing exposed surface, complete (but excluding the cost of steel reinforcement, its fabrication and placing in position, etc.):-				
		(a) (i) Reinforced cement concrete in roof slab, beams, columns lintels, girders and other structural members laid in situ or precast laid in position, or prestressed members cast in situ, complete in all respects:-				
#REF!	6/6	Type B (nominal mix 1:1.5: 3)	Per Cft	1,795.28		
		(b) Reinforced cement concrete in retaining/ Shear walls laid in situ or precast laid in position, or prestressed members castin situ (Formwork on both sides), complete in all respects: (b) Type B (nominal mix 1:1-1/2:3)				
		(i) Upto 9" thick (Avg)	Per Cft	940.00		
		(ii) More Than 9" thick (Avg)	Per Cft	8,438.64		
		(c) Reinforced cement concrete in Pile cap, slab of rafts / strip foundation, base slab of column and retaining walls; etc and footing beams, other structural members other than those mentioned in 6(a-d) above not requiring form work (i.e. horizontal shuttering) complete in all respects:-				
		Type B (nominal mix 1: 1.5: 3)	Per Cft	2,980.24		
#REF!						

ENGINEERING DESIGN AND CONSTRUCTION SUPERVISION SERVICES (EDCS)
PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT (PRSWSSP), CLUSTER SOUTH-III
TEHSIL BAHAWALNAGAR (CW-25) (PHASE-I)
BILL OF QUANTITIES
ABSTRACT OF COST

Bill No.2. SEWERAGE SYSTEM

Bill No. 2.5: Septic Tank Type-III

Sr. Nr.	MRS Ref.	Description	Unit	Quantity	Unit Rate	Amount Rs.
#REF!	6/12	Fabrication of mild steel reinforcement for cement concrete, including cutting, bending, laying in position, making joints and steel chairs, etc. complete in all respect. and fastenings, including cost of binding wire and labour charges for binding of steel reinforcement (also Includes removal of rust from bars):- ('b) Deformed bars (Grade-60)	100 Kg	417.43		
#REF!						
#REF!	1/1	Carriage of 100 Cft. (2.83 cu.m) of all materials like stone aggregate, spawl, kankar lime (unslaked), surkhi, etc. or 150 Cft. (4.25 cu.m) of timber, by truck or by any other means owned by the contractor. (crushed stone aggregate and bajri used in concrete items) **(Form Sargodha Querry**)	100Cft	118.90		
#REF!						
#REF!	6/32	Providing and embedding 10" (250mm) wide PVC water stopper in expansion joints of RCC structures (Retaining walls, water tanks, Slabs) complete in all respect. Charge				
		ii) 10" wide 10 mm thick	Rft	802.48		
#REF!						
#REF!	13/09	Bitumen coating to plastered or cement concrete surface:- i) 20 lbs. per 100 Sft. (9.07 Kg per Sq.m)	100Sft.	203.34		
#REF!						
#REF!	21/11	Providing and fixing 1¼"x1¼"x3/16" (31x31x5 mm) angle iron step, in manhole chambers, including carriage and setting the same in work to correct lines and levels.	Each	240.00		
#REF!	23/30	Providing, laying, cutting, jointing, testing and disinfecting High Density Polyethylene Pipe (HDPE-100) working presure pipe conforming to standard ISO 4427, DIN 8074 / 8075, PS 3580, Beta/ Dadex / Popular/ IIL or approved equivalent manufacturer, including the cost of specials, intrenches, as approved & directed by the Engineer incharge, complete in all respects. **a) PN-6 (SDR-26)**				
		1) 90 mm	Rft	2,212.30		
#REF!						
#REF!	23/18	Providing, laying, cutting, jointing, testing and disinfecting cast iron pipe line (BS-2035/4622) in trenches, including cost of materials, such as lead, yarn, etc.complete in all respects:- b) With Flanged and Flanged Joints 4" Dia (Vent Pipe)	Rft	48.00		
#REF!						
#REF!	23/12	Providing and installing M.S. blind pipe socketed/welded joint, M.S. reducer (where necessary), in tubewell bore hole, including jointing/welding with strainer, etc. complete:- (Chamber to ABR Connection Pipe)				
		e) 6" i/d, 3/16" (150 mm i/d 5 mm) thick	Rft	400.00		
#REF!						

ENGINEERING DESIGN AND CONSTRUCTION SUPERVISION SERVICES (EDCS)
PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT (PRSWSSP), CLUSTER SOUTH-III
TEHSIL BAHAWALNAGAR (CW-25) (PHASE-I)
BILL OF QUANTITIES
ABSTRACT OF COST

Bill No.2. SEWERAGE SYSTEM

Bill No. 2.5: Septic Tank Type-III

Sr. Nr.	MRS Ref.	Description	Unit	Quantity	Unit Rate	Amount Rs.
#REF!	N.S.	P/F RPC Manhole Cover Manufactured with 100% Recycled Plastic Composite Material, 650 mm (26"dia) with clear opening size 600 mm (24" Dia) and RPC manhole frame having Dia meter 790 mm (31.1") with average breaking load capacity of 10 Ton and weight including frame of 50 kg (Minimum).	Each	24.00		
#REF!	26/46	Providing and fixing hot dipped Galvanized Iron chainlink mesh/fence of 2"x2"mesh made of wire of specified guage, with the help of 1"x1/8" GI patti, GI.clamps and screws, i/c the cost of 3 nos 8 SWG GI tie wires penetrated through mesh at top,middle and bottom, fixed on vertical posts of 2" diameter GI pipes (medium quality) erected @ 8 ft C/C duly embeded in PCC(1:2:4) etc. complete in all respect as approved and directed by the Engineer Incharge. (ii) 10 SWG	Each	4,000.00		
#REF!	N.S	Supplying, installing, testing and commissioning of submersible waste water pump set of approved make, complete in all respects as per specifications and direction of the Engineer Incharge. The pump set shall have the following specifications: Flow: 0.05 Cusec Head: 25~30 ft Motor Rating: 0.75 HP, 1x220V 50H, 2 Pole, Submersible IP68 motor, Insulation class F Motor: 1.5 KW / 0.75HP / 2Pole Material of Construction Impeller - Stainless Steel AISI 403 Mechanical seal- Silicon Carbide Motor Housing- Stainless Steel AISI 403 Shaft- Stainless Steel AISI 403 Motor Control Unit (MCU): MCU (Motor Control Unit) consisting of MCCB, Over/Under voltage relay, Phase reversal relay, Volt meter, Ampere meter, EVR, Volt Selector Switch, Ampere Selector Switch, Current Transformer, Over load relay, indicating lights for all above relays, on/off push buttons. VFD Motor Control Unit with Dry running Protection relay, Circuit Breaker, DC SPD, AC SPD, DC Change Over Switch, Auto Start Stop with Any input, Self-diagnostic and Self Protection, Dry Run Protection, Digital Controls with Complete Protective Functions, Ground Fault Monitoring, AC Short Circuit Protection, Under/Over Voltage and Over/Current Protection, Reverse current	Job	8.00		
					Total Amount	

ENGINEERING DESIGN AND CONSTRUCTION SUPERVISION SERVICES (EDCS)
PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT (PRSWSSP), CLUSTER SOUTH-III
TEHSIL BAHAWALNAGAR (CW-25) (PHASE-I)
BILL OF QUANTITIES
ABSTRACT OF COST

Bill No.2. SEWERAGE SYSTEM

Bill No. 2.2: Septic Tank Type-IV

Sr. Nr.	MRS Ref.	Description	Unit	Quantity	Unit Rate	Amount Rs.
2.2.1	3/21	Excavation in foundation of building, bridges and other structures, including dagbelling, dressing, refilling in layers around structure with excavated earth, watering and ramming lead upto one chain (30 m)lift upto 5 ft (1.5m). 2) a) By Excavator ii) Ordinary soil				
		a) Lift up to 5 ft (1.5 m)	1000 Cft	18.48		
		b) Lift from 5ft (1.5m) to 15 ft (4.5 m):-	1000 Cft	14.78		
	Concrete Works					
2.2.2	6/3	Cement concrete brick or stone ballast 1½ " to 2" (40 mm to 50 mm) gauge, in foundation and plinth:-				
		(b) Ratio 1: 4: 8 (with Brick Ballast)	100Cft	5.73		
2.2.3	6/6	Providing and laying reinforced cement concrete (including prestressed concrete), using Ordinary Portland Cement / Sulphate resisting cement / Slag cement as may be required; coarse sand and screened graded and washed aggregate, in required shape and design, including forms, moulds, shuttering, lifting, compacting, curing, rendering and finishing exposed surface, complete (but excluding the cost of steel reinforcement, its fabrication and placing in position, etc.):-				
		(a) (i) Reinforced cement concrete in roof slab, beams, columns lintels, girders and other structural members laid in situ or precast laid in position, or prestressed members cast in situ, complete in all respects:-				
		Type B (nominal mix 1:1.5: 3)	Per Cft	810.75		
		(b) Reinforced cement concrete in retaining/ Shear walls laid in situ or precast laid in position, or prestressed members castin situ (Formwork on both sides), complete in all respects: (b) Type B (nominal mix 1:1-1/2:3)				
		(i) Upto 9" thick (Avg)	Per Cft	387.75		
		(ii) More Than 9" thick (Avg)	Per Cft	3,492.60		
		(c) Reinforced cement concrete in Pile cap, slab of rafts / strip foundation, base slab of column and retaining walls; etc and footing beams, other structural members other than those mentioned in 6(a-d) above not requiring form work (i.e. horizontal shuttering) complete in all respects:-				
		Type B (nominal mix 1: 1.5: 3)	Per Cft	1,345.83		

Bill No.2. SEWERAGE SYSTEM

Bill No. 2.2: Septic Tank Type-IV

Sr. Nr.	MRS Ref.	Description	Unit	Quantity	Unit Rate	Amount Rs.
2.2.4	6/12	Fabrication of mild steel reinforcement for cement concrete, including cutting, bending, laying in position, making joints and steel chairs, etc. complete in all respect. and fastenings, including cost of binding wire and labour charges for binding of steel reinforcement (also Includes removal of rust from bars):- (b) Deformed bars (Grade-60)	100 Kg	178.04		
2.2.5	1/1	Carriage of 100 Cft. (2.83 cu.m) of all materials like stone aggregate, spawl, kankar lime (unslaked), surkhi, etc. or 150 Cft. (4.25 cu.m) of timber, by truck or by any other means owned by the contractor. (crushed stone aggregate and bajri used in concrete items) **(Form Sargodha Querry**)	100Cft	50.71		
2.2.6	6/32	Providing and embedding 10" (250mm) wide PVC water stopper in expansion joints of RCC structures (Retaining walls, water tanks, Slabs) complete in all respect. Charge				
		ii) 10" wide 10 mm thick	Rft	332.13		
2.2.7	13/09	Bitumen coating to plastered or cement concrete surface:- i) 20 lbs. per 100 Sft. (9.07 Kg per Sq.m)	100Sft.	84.16		
2.2.8	21/11	Providing and fixing 1¼"x1¼"x3/16" (31x31x5 mm) angle iron step, in manhole chambers, including carriage and setting the same in work to correct lines and levels.	Each	90.00		
2.2.9	23/30	Providing, laying, cutting, jointing, testing and disinfecting High Density Polyethylene Pipe (HDPE-100) working presure pipe conforming to standard ISO 4427, DIN 8074 / 8075, PS 3580, Beta/ Dadex / Popular/ IIL or approved equivalent manufacturer, including the cost of specials, intrenches, as approved & directed by the Engineer incharge, complete in all respects. **a) PN-6 (SDR-26)**				
		1) 90 mm	Rft	653.80		
2.2.10	23/18	Providing, laying, cutting, jointing, testing and disinfecting cast iron pipe line (BS-2035/4622) in trenches, including cost of materials, such as lead, yarn, etc.complete in all respects:- b) With Flanged and Flanged Joints 4" Dia (Vent Pipe)	Rft	18.00		
2.2.11	23/12	Providing and installing M.S. blind pipe socketed/welded joint, M.S. reducer (where necessary), in tubewell bore hole, including jointing/welding with strainer, etc. complete:- (Chamber to ABR Connection Pipe)				
		e) 6" i/d, 3/16" (150 mm i/d 5 mm) thick	Rft	150.00		

ENGINEERING DESIGN AND CONSTRUCTION SUPERVISION SERVICES (EDCS)
PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT (PRSWSSP), CLUSTER SOUTH-III
TEHSIL BAHAWALNAGAR (CW-25) (PHASE-I)
BILL OF QUANTITIES
ABSTRACT OF COST

Bill No.2. SEWERAGE SYSTEM

Bill No. 2.2: Septic Tank Type-IV

Sr. Nr.	MRS Ref.	Description	Unit	Quantity	Unit Rate	Amount Rs.
2.2.12	N.S.	P/F RPC Manhole Cover Manufactured with 100% Recycled Plastic Composite Material, 650 mm (26"dia) with clear opening size 600 mm (24" Dia) and RPC manhole frame having Dia meter 790 mm (31.1") with average breaking load capacity of 10 Ton and weight including frame of 50 kg (Minimum).	Each	9.00		
2.2.13	26/46	Providing and fixing hot dipped Galvanized Iron chainlink mesh/fence of 2"x2"mesh made of wire of specified guage, with the help of 1"x1/8" GI patti, GI.clamps and screws, i/c the cost of 3 nos 8 SWG GI tie wires penetrated through mesh at top,middle and bottom, fixed on vertical posts of 2" diameter GI pipes (medium quality) erected @ 8 ft C/C duly embeded in PCC(1:2:4) etc. complete in all respect as approved and directed by the Engineer Incharge. (ii) 10 SWG	Each	1,500.00		
2.2.14	N.S	**Supplying, installing, testing and commissioning of submersible waste water pump set of approved make, complete in all respects as per specifications and direction of the Engineer Incharge. The pump set shall have the following specifications:** **Flow: 0.15 Cusec** Head: 25~30 ft Motor Rating: 2 HP, 3x400V 50H, 2 Pole, Submersible IP68 motor, Insulation class F Motor: 1.5 KW / 2HP / 2Pole Material of Construction Impeller - Stainless Steel AISI 403 Mechanical seal- Silicon Carbide Motor Housing- Stainless Steel AISI 403 Shaft- Stainless Steel AISI 403 **Motor Control Unit (MCU):** MCU (Motor Control Unit) consisting of MCCB, Over/Under voltage relay, Phase reversal relay, Volt meter, Ampere meter, EVR, Volt Selector Switch, Ampere Selector Switch, Current Transformer, Over load relay, indicating lights for all above relays, on/off push buttons. VFD Motor Control Unit with Dry running Protection relay, Circuit Breaker, DC SPD, AC SPD, DC Change Over Switch, Auto Start Stop with Any input, Self-diagnostic and Self Protection, Dry Run Protection, Digital Controls with Complete Protective Functions, Ground Fault Monitoring, AC Short Circuit Protection, Under/Over Voltage and Over/Current Protection, Reverse current Blocking, to , Remote Monitoring and	Job	3.00		
					Total Amount	

ENGINEERING DESIGN AND CONSTRUCTION SUPERVISION SERVICES (EDCS)
PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT (PRSWSSP), CLUSTER SOUTH-III
TEHSIL BAHAWALNAGAR (CW-25) (PHASE-I)
BILL OF QUANTITIES
ABSTRACT OF COST

Bill No.2. SEWERAGE SYSTEM

Bill No. 2.7: Septic Tank Type-V

Sr. Nr.	MRS Ref.	Description	Unit	Quantity	Unit Rate	Amount Rs.
2.7.1	3/21	Excavation in foundation of building, bridges and other structures, including dagbelling, dressing, refilling in layers around structure with excavated earth, watering and ramming lead upto one chain (30 m)lift upto 5 ft (1.5m). 2) a) By Excavator ii) Ordinary soil				
		a) Lift up to 5 ft (1.5 m)	1000 Cft	11.62		
		b) Lift from 5ft (1.5m) to 15 ft (4.5 m):-	1000 Cft	112.72		
	Concrete Works					
2.7.2	6/3	Cement concrete brick or stone ballast 1½ " to 2" (40 mm to 50 mm) gauge, in foundation and plinth:-				
		(b) Ratio 1: 4: 8 (with Brick Ballast)	100Cft	4.40		
2.7.3	6/6	Providing and laying reinforced cement concrete (including prestressed concrete), using Ordinary Portland Cement / Sulphate resisting cement / Slag cement as may be required; coarse sand and screened graded and washed aggregate, in required shape and design, including forms, moulds, shuttering, lifting, compacting, curing, rendering and finishing exposed surface, complete (but excluding the cost of steel reinforcement, its fabrication and placing in position, etc.):-				
		(a) (i) Reinforced cement concrete in roof slab, beams, columns lintels, girders and other structural members laid in situ or precast laid in position, or prestressed members cast in situ, complete in all respects:-				
		Type B (nominal mix 1:1.5: 3)	Per Cft	626.22		
		(b) Reinforced cement concrete in retaining/ Shear walls laid in situ or precast laid in position, or prestressed members castin situ (Formwork on both sides), complete in all respects: (b) Type B (nominal mix 1:1-1/2:3)				
		(i) Upto 9" thick (Avg)	Per Cft	282.00		
		(ii) More Than 9" thick (Avg)	Per Cft	2,502.96		
		(c) Reinforced cement concrete in Pile cap, slab of rafts / strip foundation, base slab of column and retaining walls; etc and footing beams, other structural members other than those mentioned in 6(a-d) above not requiring form work (i.e. horizontal shuttering) complete in all respects:-				
		Type B (nominal mix 1: 1.5: 3)	Per Cft	1,039.52		

Bill No.2. SEWERAGE SYSTEM

Bill No. 2.7: Septic Tank Type-V

Sr. Nr.	MRS Ref.	Description	Unit	Quantity	Unit Rate	Amount Rs.
2.7.4	6/12	Fabrication of mild steel reinforcement for cement concrete, including cutting, bending, laying in position, making joints and steel chairs, etc. complete in all respect. and fastenings, including cost of binding wire and labour charges for binding of steel reinforcement (also Includes removal of rust from bars):- (b) Deformed bars (Grade-60)	100 Kg	131.26		
2.7.5	1/1	Carriage of 100 Cft. (2.83 cu.m) of all materials like stone aggregate, spawl, kankar lime (unslaked), surkhi, etc. or 150 Cft. (4.25 cu.m) of timber, by truck or by any other means owned by the contractor. (crushed stone aggregate and bajri used in concrete items) **(Form Sargodha Querry**)	100Cft	37.39		
2.7.6	6/32	Providing and embedding 10" (250mm) wide PVC water stopper in expansion joints of RCC structures (Retaining walls, water tanks, Slabs) complete in all respect. Charge				
		ii) 10" wide 10 mm thick	Rft	238.02		
2.7.7	13/09	Bitumen coating to plastered or cement concrete surface:- i) 20 lbs. per 100 Sft. (9.07 Kg per Sq.m)	100Sft.	60.31		
2.7.8	21/11	Providing and fixing 1¼"x1¼"x3/16" (31x31x5 mm) angle iron step, in manhole chambers, including carriage and setting the same in work to correct lines and levels.	Each	60.00		
2.7.9	23/30	Providing, laying, cutting, jointing, testing and disinfecting High Density Polyethylene Pipe (HDPE-100) working presure pipe conforming to standard ISO 4427, DIN 8074 / 8075, PS 3580, Beta/ Dadex / Popular/ IIL or approved equivalent manufacturer, including the cost of specials, intrenches, as approved & directed by the Engineer incharge, complete in all respects. **a) PN-6 (SDR-26)**				
		1) 90 mm	Rft	329.90		
2.7.10	23/18	Providing, laying, cutting, jointing, testing and disinfecting cast iron pipe line (BS-2035/4622) in trenches, including cost of materials, such as lead, yarn, etc.complete in all respects:- b) With Flanged and Flanged Joints 4" Dia (Vent Pipe)	Rft	12.00		
2.7.11	23/12	Providing and installing M.S. blind pipe socketed/welded joint, M.S. reducer (where necessary), in tubewell bore hole, including jointing/welding with strainer, etc. complete:- (Chamber to ABR Connection Pipe)				
		e) 6" i/d, 3/16" (150 mm i/d 5 mm) thick	Rft	100.00		

ENGINEERING DESIGN AND CONSTRUCTION SUPERVISION SERVICES (EDCS)
PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT (PRSWSSP), CLUSTER SOUTH-III
TEHSIL BAHAWALNAGAR (CW-25) (PHASE-I)
BILL OF QUANTITIES
ABSTRACT OF COST

Bill No.2. SEWERAGE SYSTEM

Bill No. 2.7: Septic Tank Type-V

Sr. Nr.	MRS Ref.	Description	Unit	Quantity	Unit Rate	Amount Rs.
2.7.12	N.S.	P/F RPC Manhole Cover Manufactured with 100% Recycled Plastic Composite Material, 650 mm (26"dia) with clear opening size 600 mm (24" Dia) and RPC manhole frame having Dia meter 790 mm (31.1") with average breaking load capacity of 10 Ton and weight including frame of 50 kg (Minimum).	Each	6.00		
2.7.13	26/46	Providing and fixing hot dipped Galvanized Iron chainlink mesh/fence of 2"x2"mesh made of wire of specified guage, with the help of 1"x1/8" GI patti, GI.clamps and screws, i/c the cost of 3 nos 8 SWG GI tie wires penetrated through mesh at top,middle and bottom, fixed on vertical posts of 2" diameter GI pipes (medium quality) erected @ 8 ft C/C duly embeded in PCC(1:2:4) etc. complete in all respect as approved and directed by the Engineer Incharge. (ii) 10 SWG	Each	1,000.00		
2.7.14	N.S	**Supplying, installing, testing and commissioning of submersible waste water pump set of approved make, complete in all respects as per specifications and direction of the Engineer Incharge. The pump set shall have the following specifications:** **Flow: 0.15 Cusec** Head: 25~30 ft Motor Rating: 2 HP, 3x400V 50H, 2 Pole, Submersible IP68 motor, Insulation class F Motor: 1.5 KW / 2HP / 2Pole Material of Construction Impeller - Stainless Steel AISI 403 Mechanical seal- Silicon Carbide Motor Housing- Stainless Steel AISI 403 Shaft- Stainless Steel AISI 403 **Motor Control Unit (MCU):** MCU (Motor Control Unit) consisting of MCCB, Over/Under voltage relay, Phase reversal relay, Volt meter, Ampere meter, EVR, Volt Selector Switch, Ampere Selector Switch, Current Transformer, Over load relay, indicating lights for all above relays, on/off push buttons. VFD Motor Control Unit with Dry running Protection relay, Circuit Breaker, DC SPD, AC SPD, DC Change Over Switch, Auto Start Stop with Any input, Self-diagnostic and Self Protection, Dry Run Protection, Digital Controls with Complete Protective Functions, Ground Fault Monitoring, AC Short Circuit Protection, Under/Over Voltage and Over/Current Protection, Reverse current Blocking, to , Remote Monitoring and	Job	2.00		
					Total Amount	

ENGINEERING DESIGN AND CONSTRUCTION SUPERVISION SERVICES (EDCS)
PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT (PRSWSSP), CLUSTER SOUTH-III
TEHSIL BAHAWALNAGAR (CW-25) (PHASE-I)
BILL OF QUANTITIES
ABSTRACT OF COST

Bill No.2. SEWERAGE SYSTEM

Bill No. 2.8: Septic Tank Type-VI

Sr. Nr.	MRS Ref.	Description	Unit	Quantity	Unit Rate	Amount Rs.
2.8.1	3/21	Excavation in foundation of building, bridges and other structures, including dagbelling, dressing, refilling in layers around structure with excavated earth, watering and ramming lead upto one chain (30 m)lift upto 5 ft (1.5m). 2) a) By Excavator ii) Ordinary soil				
		a) Lift up to 5 ft (1.5 m)	1000 Cft	4.42		
		b) Lift from 5ft (1.5m) to 15 ft (4.5 m):-	1000 Cft	5.64		
	Concrete Works					
2.8.2	6/3	Cement concrete brick or stone ballast 1½ " to 2" (40 mm to 50 mm) gauge, in foundation and plinth:-				
		(b) Ratio 1: 4: 8 (with Brick Ballast)	100Cft	2.20		
2.8.3	6/6	Providing and laying reinforced cement concrete (including prestressed concrete), using Ordinary Portland Cement / Sulphate resisting cement / Slag cement as may be required; coarse sand and screened graded and washed aggregate, in required shape and design, including forms, moulds, shuttering, lifting, compacting, curing, rendering and finishing exposed surface, complete (but excluding the cost of steel reinforcement, its fabrication and placing in position, etc.):-				
		(a) (i) Reinforced cement concrete in roof slab, beams, columns lintels, girders and other structural members laid in situ or precast laid in position, or prestressed members cast in situ, complete in all respects:-				
		Type B (nominal mix 1:1.5: 3)	Per Cft	313.11		
		(b) Reinforced cement concrete in retaining/ Shear walls laid in situ or precast laid in position, or prestressed members castin situ (Formwork on both sides), complete in all respects: (b) Type B (nominal mix 1:1-1/2:3)				
		(i) Upto 9" thick (Avg)	Per Cft	141.00		
		(ii) More Than 9" thick (Avg)	Per Cft	1,251.48		
		(c) Reinforced cement concrete in Pile cap, slab of rafts / strip foundation, base slab of column and retaining walls; etc and footing beams, other structural members other than those mentioned in 6(a-d) above not requiring form work (i.e. horizontal shuttering) complete in all respects:-				
		Type B (nominal mix 1: 1.5: 3)	Per Cft	519.76		

ENGINEERING DESIGN AND CONSTRUCTION SUPERVISION SERVICES (EDCS)
PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT (PRSWSSP), CLUSTER SOUTH-III
TEHSIL BAHAWALNAGAR (CW-25) (PHASE-I)
BILL OF QUANTITIES
ABSTRACT OF COST

Bill No.2. SEWERAGE SYSTEM

Bill No. 2.8: Septic Tank Type-VI

Sr. Nr.	MRS Ref.	Description	Unit	Quantity	Unit Rate	Amount Rs.
2.8.4	6/12	Fabrication of mild steel reinforcement for cement concrete, including cutting, bending, laying in position, making joints and steel chairs, etc. complete in all respect. and fastenings, including cost of binding wire and labour charges for binding of steel reinforcement (also Includes removal of rust from bars):- (b) Deformed bars (Grade-60)	100 Kg	65.63		
2.8.5	1/1	Carriage of 100 Cft. (2.83 cu.m) of all materials like stone aggregate, spawl, kankar lime (unslaked), surkhi, etc. or 150 Cft. (4.25 cu.m) of timber, by truck or by any other means owned by the contractor. (crushed stone aggregate and bajri used in concrete items) **(Form Sargodha Querry**)	100Cft	18.69		
2.8.6	6/32	Providing and embedding 10" (250mm) wide PVC water stopper in expansion joints of RCC structures (Retaining walls, water tanks, Slabs) complete in all respect. Charge				
		ii) 10" wide 10 mm thick	Rft	119.01		
2.8.9	13/09	Bitumen coating to plastered or cement concrete surface:- i) 20 lbs. per 100 Sft. (9.07 Kg per Sq.m)	100Sft.	30.16		
2.8.9	21/11	Providing and fixing 1¼"x1¼"x3/16" (31x31x5 mm) angle iron step, in manhole chambers, including carriage and setting the same in work to correct lines and levels.	Each	30.00		
2.8.9	23/30	Providing, laying, cutting, jointing, testing and disinfecting High Density Polyethylene Pipe (HDPE-100) working presure pipe conforming to standard ISO 4427, DIN 8074 / 8075, PS 3580, Beta/ Dadex / Popular/ IIL or approved equivalent manufacturer, including the cost of specials, intrenches, as approved & directed by the Engineer incharge, complete in all respects. **a) PN-6 (SDR-26)**				
		1) 90 mm	Rft	72.00		
2.8.10	23/18	Providing, laying, cutting, jointing, testing and disinfecting cast iron pipe line (BS-2035/4622) in trenches, including cost of materials, such as lead, yarn, etc.complete in all respects:- b) With Flanged and Flanged Joints 4" Dia (Vent Pipe)	Rft	6.00		
2.2.11	23/12	Providing and installing M.S. blind pipe socketed/welded joint, M.S. reducer (where necessary), in tubewell bore hole, including jointing/welding with strainer, etc. complete:- (Chamber to ABR Connection Pipe)				
		e) 6" i/d, 3/16" (150 mm i/d 5 mm) thick	Rft	50.00		

ENGINEERING DESIGN AND CONSTRUCTION SUPERVISION SERVICES (EDCS)
PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT (PRSWSSP), CLUSTER SOUTH-III
TEHSIL BAHAWALNAGAR (CW-25) (PHASE-I)
BILL OF QUANTITIES
ABSTRACT OF COST

Bill No.2. SEWERAGE SYSTEM

Bill No. 2.8: Septic Tank Type-VI

Sr. Nr.	MRS Ref.	Description	Unit	Quantity	Unit Rate	Amount Rs.
2.8.12	N.S.	P/F RPC Manhole Cover Manufactured with 100% Recycled Plastic Composite Material, 650 mm (26"dia) with clear opening size 600 mm (24" Dia) and RPC manhole frame having Dia meter 790 mm (31.1") with average breaking load capacity of 10 Ton and weight including frame of 50 kg (Minimum).	Each	3.00		
2.2.13	26/46	Providing and fixing hot dipped Galvanized Iron chainlink mesh/fence of 2"x2"mesh made of wire of specified guage, with the help of 1"x1/8" GI patti, GI.clamps and screws, i/c the cost of 3 nos 8 SWG GI tie wires penetrated through mesh at top,middle and bottom, fixed on vertical posts of 2" diameter GI pipes (medium quality) erected @ 8 ft C/C duly embeded in PCC(1:2:4) etc. complete in all respect as approved and directed by the Engineer Incharge. (ii) 10 SWG	Each	500.00		
2.2.14	N.S	**Supplying, installing, testing and commissioning of submersible waste water pump set of approved make, complete in all respects as per specifications and direction of the Engineer Incharge. The pump set shall have the following specifications:** **Flow: 0.15 Cusec** Head: 25~30 ft Motor Rating: 2 HP, 3x400V 50H, 2 Pole, Submersible IP68 motor, Insulation class F Motor: 1.5 KW / 2HP / 2Pole Material of Construction Impeller - Stainless Steel AISI 403 Mechanical seal- Silicon Carbide Motor Housing- Stainless Steel AISI 403 Shaft- Stainless Steel AISI 403 **Motor Control Unit (MCU):** MCU (Motor Control Unit) consisting of MCCB, Over/Under voltage relay, Phase reversal relay, Volt meter, Ampere meter, EVR, Volt Selector Switch, Ampere Selector Switch, Current Transformer, Over load relay, indicating lights for all above relays, on/off push buttons. VFD Motor Control Unit with Dry running Protection relay, Circuit Breaker, DC SPD, AC SPD, DC Change Over Switch, Auto Start Stop with Any input, Self-diagnostic and Self Protection, Dry Run Protection, Digital Controls with Complete Protective Functions, Ground Fault Monitoring, AC Short Circuit Protection, Under/Over Voltage and Over/Current Protection, Reverse current Blocking, to , Remote Monitoring and	Job	1.00		
					Total Amount	

ENGINEERING DESIGN AND CONSTRUCTION SUPERVISION SERVICES (EDCS)
PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT (PRSWSSP), CLUSTER SOUTH-III
TEHSIL BAHAWALNAGAR (CW-25) (PHASE-I)
BILL OF QUANTITIES
ABSTRACT OF COST

Bill No.2. SEWERAGE SYSTEM

Bill No. 2.9: Communa Tank (2-House hold) RCC work

Sr. Nr.	MRS Ref.	Description	Unit	Quantity	Unit Rate	Amount Rs.
2.9.1	3/21	Excavation in foundation of building, bridges and other structures, including dagbelling, dressing, refilling in layers around structure with excavated earth, watering and ramming lead upto one chain (30 m)lift upto 5 ft (1.5m). 2) a) By Excavator ii) Ordinary soil				
		a) Lift up to 5 ft (1.5 m)	1000 Cft	1.88		
		Concrete Works				
2.9.2	6/3	Cement concrete brick or stone ballast 1½ " to 2" (40 mm to 50 mm) gauge, in foundation and plinth:-				
		(b) Ratio 1: 4: 8 (with Brick Ballast)	100Cft	1.01		
2.9.3	6/6	Providing and laying reinforced cement concrete (including prestressed concrete), using Ordinary Portland Cement / Sulphate resisting cement / Slag cement as may be required; coarse sand and screened graded and washed aggregate, in required shape and design, including forms, moulds, shuttering, lifting, compacting, curing, rendering and finishing exposed surface, complete (but excluding the cost of steel reinforcement, its fabrication and placing in position, etc.):-				
		(a) (i) Reinforced cement concrete in roof slab, beams, columns lintels, girders and other structural members laid in situ or precast laid in position, or prestressed members cast in situ, complete in all respects:-				
		(2) Type B (nominal mix 1: 1½: 3)	Per Cft	66.56		
		(b) Reinforced cement concrete in retaining/ Shear walls laid in situ or precast laid in position, or prestressed members castin situ (Formwork on both sides), complete in all respects: (2) Type B (nominal mix 1:1-1/2:3)				
		(i) Upto 9" thick (Avg)	Per Cft	474.64		
		(c) Reinforced cement concrete in Pile cap, slab of rafts / strip foundation, base slab of column and retaining walls; etc and footing beams, other structural members other than those mentioned in 6(a-d) above not requiring form work (i.e. horizontal shuttering) complete in all respects:-				
		Type B (nominal mix 1: 1.5: 3)	Per Cft	100.80		
2.9.4	6/12	Fabrication of mild steel reinforcement for cement concrete, including cutting, bending, laying in position, making joints and steel chairs, etc. complete in all respect. and fastenings, including cost of binding wire and labour charges for binding of steel reinforcement (also Includes removal of rust from bars):- (b) Deformed bars ii-(Grade-60)	100 Kg	18.93		

ENGINEERING DESIGN AND CONSTRUCTION SUPERVISION SERVICES (EDCS)
PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT (PRSWSSP), CLUSTER SOUTH-III
TEHSIL BAHAWALNAGAR (CW-25) (PHASE-I)
BILL OF QUANTITIES
ABSTRACT OF COST

Bill No.2. SEWERAGE SYSTEM

Bill No. 2.9: Communa Tank (2-House hold) RCC work

Sr. Nr.	MRS Ref.	Description	Unit	Quantity	Unit Rate	Amount Rs.
2.9.5	1/1	Carriage of 100 Cft. (2.83 cu.m) of all materials like stone aggregate, spawl, kankar lime (unslaked), surkhi, etc. or 150 Cft. (4.25 cu.m) of timber, by truck or by any other means owned by the contractor. (crushed stone aggregate and bajri used in concrete items) **(Form Sargodha Querry**)	100Cft	5.39		
2.9.6	6/32	Providing and embedding 10" (250mm) wide PVC water stopper in expansion joints of RCC structures (Retaining walls, water tanks, Slabs) complete in all respect. Charge				
		ii) 10" wide 10 mm thick	Rft	214.40		
2.9.7	13/09	Bitumen coating to plastered or cement concrete surface:- i) 20 lbs. per 100 Sft. (9.07 Kg per Sq.m)	100Sft.	14.59		
2.9.8	21/11	Providing and fixing 1¼"x1¼"x3/16" (31x31x5 mm) angle iron step, in manhole chambers, including carriage and setting the same in work to correct lines and levels.	Each	160.00		
2.9.9	23/30	Providing, laying, cutting, jointing, testing and disinfecting High Density Polyethylene Pipe (HDPE-100) working presure pipe conforming to standard ISO 4427, DIN 8074 / 8075, PS 3580, Beta/ Dadex / Popular/ IIL or approved equivalent manufacturer, including the cost of specials, intrenches, as approved & directed by the Engineer incharge, complete in all respects. **a) PN-6 (SDR-26)**				
		1) 90 mm	Rft	400.00		
2.9.10	23/18	Providing, laying, cutting, jointing, testing and disinfecting cast iron pipe line (BS-2035/4622) in trenches, including cost of materials, such as lead, yarn, etc.complete in all respects:- b) With Flanged and Flanged Joints 4" Dia (Vent Pipe)	Rft	32.00		
				-		

ENGINEERING DESIGN AND CONSTRUCTION SUPERVISION SERVICES (EDCS)
PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT (PRSWSSP), CLUSTER SOUTH-III
TEHSIL BAHAWALNAGAR (CW-25) (PHASE-I)
BILL OF QUANTITIES
ABSTRACT OF COST

Bill No.2. SEWERAGE SYSTEM

Bill No. 2.9: Communa Tank (2-House hold) RCC work

Sr. Nr.	MRS Ref.	Description	Unit	Quantity	Unit Rate	Amount Rs.
2.9.12	N/S	Providing, installation, testing and commissioning of non clogging sewerage submersible pump of Approved manufacturer of HUD & PHED and should be ISO 9001 Certified, complete in all respect having following Specification Pump Set: Flow: 350L/min Head: 30 ft Power :- 1HO/750Watts Including 1x Sluice valve and 1x NRV Motor Control Unit (MCU): VFD Motor Control Unit with Dry running protection relay, Circuit Breaker, DC SPD, AC SPD, DC Change Over Switch, Auto Start Stop with Any input, Self-diagnostic and Self Protection, Ground Fault Monitoring, AC Short Circuit Protection, Under / Over Voltage and Over/ Current Protection, Reverse current Blocking, -10 to 40 Degree Celsius. All contained in lockable cabinet complete in all respect.	Each	9.00		
					Total Amount	

ENGINEERING DESIGN AND CONSTRUCTION SUPERVISION SERVICES (EDCS)
PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT (PRSWSSP), CLUSTER SOUTH-III

TEHSIL BAHAWALNAGAR (CW-25) (PHASE-I)

BILL OF QUANTITIES

ABSTRACT OF COST

Bill No. 3: Street Pavement Works

Sr. No.	Ref	Description	Unit	Quantity	Unit Rate (Rs)	Amount (Rs)
3.1	18/20	Providing and laying dry brick pavement/ soling in streets or roads, etc. sand grounted, laid in proper camber, including preparation, watering, compaction of bed to proper camber, and sand cushion.	100Cft.	6,854.73		
3.2	10/43	Providing and laying Tuff Pavers, having 7000 PSI, crushing strength of approved manufacturer, over 2" to 3" sand cushion i/c grouting with sand in joints i/c finishing to require slope . complete in all respect.				
		b) 60-mm thick	Per Sft	131,678.75		
		c) 80-mm thick	Per Sft	131,678.75		
3.3	18/3	a) Providing and laying sub-base course of stone product of approved quality and grade, including placing, mixing, spreading and compaction of sub-base material to required depth, camber, grade to achieve 100% maximum modified AASHO dry density, including carriage of all material to site of work except gravel and aggregate.				
		ii) Crushed stone aggregate.	100Cft.	1,316.78		
		(b) Subsequent carriage of gravel and crushed stone aggregate	100Cft.	1,580.13		
3.4	18/4	a) Providing and laying base course of crushed stone aggregate of approved quality and grade, and supply and spreading of stone screening, including placing, mixing, spreading and compaction of base course material to required depth, camber and grade to achieve 100% maximum modified AASHO dry density, including carriage of all materials to site of work except gravel and. aggregate.				
		ii) Crushed stone aggregate.	100Cft.	658.36		
		(b) Subsequent carriage of gravel and crushed stone aggregate	100Cft.	790.04		
3.5	3/18	Dressing and levelling of earhtwork to designed section, etc complete:- b) Ordinary or hard soil.	1000Cft	161.90		
3.6	3/5	Earthowrk in ordinary soil for embankments lead upto 100 ft. (30 m), including ploughing, mixing and compaction by mechanical means at optimum moisture content and dressing to designed section, complete in all respects:- ii) 90% maximum modified AASHTO dry density.	1000 Cft.	2,428.46		
3.7	3/17	Transportation of earth all types when the total distance, including the lead covered in the item of work, is more than 1000 ft. (300 m)				
		a) Upto ¼ mile (400 m).x1	1000 Cft.	2,428.46		
		b) For every 330 ft. (100 m) additional lead or part thereof, beyond ¼ mile (400 m) upto one mile. (1.6 Km.)x12	1000 Cft.	2,428.46		

ENGINEERING DESIGN AND CONSTRUCTION SUPERVISION SERVICES (EDCS)
PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT (PRSWSSP), CLUSTER SOUTH-III

TEHSIL BAHAWALNAGAR (CW-25) (PHASE-I)

BILL OF QUANTITIES

ABSTRACT OF COST

Bill No. 3: Street Pavement Works

Sr. No.	Ref	Description	Unit	Quantity	Unit Rate (Rs)	Amount (Rs)
		Sign Board Works				
3.8	18/19	Providing and erection at site of work:- (The rate is for complete item of work according to Standard design including cement concrete foundation block and painting letters etc. b) Warning/Direction/Informatory.	Each	131.25		
					Total Amount	

ENGINEERING DESIGN AND CONSTRUCTION SUPERVISION SERVICES (EDCS)
PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT (PRSWSSP), CLUSTER SOUTH-III

TEHSIL BAHAWALNAGAR (CW-25) (PHASE-I)

BILL OF QUANTITIES

ABSTRACT OF COST

Bill No. 4 : ESMP Cost

Sr. No.	Item Description	ISO / Standard Code / Description	Unit	Quantity	Unit Rate (Rs)	Amount (Rs)
Personal Protective Equipments						
1	Safety Jackets	EN ISO 20471: 360 degree visibility Fluorescent yellow/orange; retro-reflective strips; breathable mesh fabric; secure Velcro or zipper closure, provided in approriate sizes are required by Staff, PRMSC name and logo printed	Each	30.00		
2	Safety Helmets	EN-397 High-density polyethylene (HDPE) or ABS plastic; adjustable screw harness; Adjustable headbands, chin straps, and non-allergic sweatbands. color-coded (white for engineers, yellow for workers) PRMSC Brading and LOGO PRINTED with sr number mentioned on each helmet for ease of record keeping	Each	30.00		
3	Safety Gloves	EN 388 : Nitrile-coated or leather palm; abrasion and cut-resistant; breathable back; conforms to EN388 safety ratings	Each	50.00		
4	Dust Mask (Dust proof mask)	ISO 16975: Disposable N95 or FFP2 class mask; elastic bands; nose clip for sealing; replace after use	Each	100.00		
5	Safety Shoes & Toes	EN ISO 20345, requiring a toe cap to withstand a minimum 200-joule impact and 15 kilonewtons (kN) of compression Steel toe cap; anti-slip, oil-resistant sole; leather upper; ankle support for shoes only	Each	35.00		
6	Safety Harness Belt	ISO 10333: High-tenacity polyester webbing, minimum width 45mm; adjustable shoulder and thigh straps with metal buckles; dorsal D-ring for fall arrest, side D-rings for positioning; and chest strap with quick-connect buckle; Renowned Brand	Each	3.00		
7	Protective Goggles	ISO 16321: Anti-fog, scratch-resistant; side shielding for wrap-around protection; adjustable strap	Each	10.00		
8	Ear Plugs	ISO 4869-1: Soft polyurethane foam; noise reduction rating (NRR) of 30 dB or more	Each	20.00		
Health Safety Environment Materials / Testing						
9	First Aid Kit	ISO 7010-E003: Painkiller, eyewash solution, antibiotic ointment, thermometer, plasters, sterile gauze, dressings, sterile eye dressings, triangular bandages, crepe rolled bandages, safety pins, disposable sterile gloves and tweezers), pain killers, burn creams, pyodine solution (big bottle), other medication as required by tehsil team is adequate size and quantity	Each	1.00		
10	Warning / Safety Signs	ISO 7010: Weatherproof PVC or Plastic or aluminum signs; reflective print; standardized colors and pictograms (danger, caution, mandatory)	Each	25.00		
11	Green Mesh	Green safety netting for site periphery; 50% shading; UV-stabilized HDPE material.	S.ft	200.00		
12	DCP Fire Extinguisher (Dry Chemical Powder)	ISO 7165: 6-kg; ABC type; The extinguishing agent is mono ammonium phosphate and ammonium sulphate powder and the discharge time of the agent is 13 second	No.	1.00		

ENGINEERING DESIGN AND CONSTRUCTION SUPERVISION SERVICES (EDCS)
PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT (PRSWSSP), CLUSTER SOUTH-III

TEHSIL BAHAWALNAGAR (CW-25) (PHASE-I)

BILL OF QUANTITIES

ABSTRACT OF COST

Bill No. 4 : ESMP Cost

Sr. No.	Item Description	ISO / Standard Code / Description	Unit	Quantity	Unit Rate (Rs)	Amount (Rs)
13	CO_2 Fire Extinguisher	ISO 7165: 5 kg; frost-free horn; suitable for electrical and liquid fires; discharge time of the agent in 13 second)	No.	1.00		
14	Fire Alarm	ICS 13.030.10: Proper segregation, PPE for handlers, timely removal, recordkeeping per solid waste rules	No.	2.00		
15	Trapuline	Waterproof tarpaulin sheet made from polyethylene or canva	Sq.ft	30.00		
16	Safety Cones	UV-resistant PVC or rubber material; at least 28 to 36 inches in height; high-visibility orange color with reflective collars (minimum 4-inch reflective band) for day and night visibility		12.00		
17	Tree Plantation	5-6 feet height; Native species plantation; soil preparation and watering included	No.	100.00		
18	Barricading / Fencing (Reflective tape, poles, safety mesh/netting)	ISO 13857: Includes poles, reflective tape, plastic mesh netting; minimum 3 feet height; durable and visible	Rft	300.00		
19	Trainings	HSE Training, Rescue Training, Labour Code of Conduct, Environmental Code of Conduct, Defensive Driver Trainings, Labour Laws and Labour Rights, GAP Training, C-ESMP Training and anyother as required by E&S wing	Quaterly	4.00		
20	Water Sprinkling	Water sprinkling through tank mounted on tractor	Per Trip	30.00		
21	Medical Screening for Workers	CBC, Anti HCV, HBsAG, HIV, RPR, LFTs, RFTs etc.	Persons	30.00		
Environmental Testing and Monitoring						
22	Ambient Air Quality Monitoring	As per the parameters and methodology defined by EPA (Quarterly in every village	Each	3.00		
23	Groundwater Quality Test	As per the parameters and methodology defined by EPA (Quarterly in every village	Each	3.00		
24	Surface Water Quality Test	(As per the parameters and methodology defined by EPA (Quarterly in every village	Each	3.00		
25	waste Water Quality Test	(As per the parameters and methodology defined by EPA (Quarterly in every village	Each	3.00		
26	Noise Level Monitoring	(As per the parameters and methodology defined by EPA (Quarterly in every village)	Each	3.00		
Site Specific / Contractors Environmntal and Social Management Plan						
27	CESMP Formulation	By an individual or firm as approved by PRMSC Environment Wing	per village	1.00		
HSE Staff						
28	HSE Supervisor	Bachelor's degree in Environmental Sciences / Engineering , NEBOSH or IOSH certification will be preffered, with over one year of experience in Occupational Health and Safety, one HSE person for 10-15 village, hiring of HSE staff will be approved by E&S prior to contract signing	Per month per village	12.00		

ENGINEERING DESIGN AND CONSTRUCTION SUPERVISION SERVICES (EDCS)
PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT (PRSWSSP), CLUSTER SOUTH-III

TEHSIL BAHAWALNAGAR (CW-25) (PHASE-I)

BILL OF QUANTITIES

ABSTRACT OF COST

Bill No. 4 : ESMP Cost

Sr. No.	Item Description	ISO / Standard Code / Description	Unit	Quantity	Unit Rate (Rs)	Amount (Rs)
Waste Management and House Keeping						
29	Handling and disposal of Hazardous Material	ICS 13.030.30: Safe storage, labeling, and transportation; spill kits and secondary containment as per MSDS	3 times per village for duration of contract	3.00		
30	Handling and dispodal of Solid Waste Material	ICS 13.030.10: Proper segregation, PPE for handlers, timely removal, recordkeeping per solid waste rules	3 times per village for duration of contract	3.00		
Sub Total ESMP Implementation Cost per year (PKR)						
NUMBERS						**8**
Grand Total ESMP Implementation Cost per year (PKR)						

ENGINEERING DESIGN AND CONSTRUCTION SUPERVISION SERVICES (EDCS)
PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT (PRSWSSP), CLUSTER SOUTH-III
TEHSIL BAHAWALNAGAR (CW-25) (PHASE-I)
BILL OF QUANTITIES
ABSTRACT OF COST

Bill No. 5 : Employer Facilities

Sr. No.	Description	Unit	Quantity	Unit Rate (Rs)	Amount (Rs)
1	Providing and maintaining site offices (portable air condition (1,5 ton AC) cabin containers lined with win board size 20'x8'x8.5' with toilet & kitchen, all-time availability of water and electricity) for the entire duration of the project to the Employer and the Engineer. It includes office tables, chairs, water dispenser, electric heater, steel almirah for document storage, etc complete with all respect. After completion of the project these containers and all accessories will be the property of PRMSC	Nos	1.0		
2	Providing 02 Nos office boy in accordance with the special provisions of the bidding document and up to the satisfaction of the Employer/Engineer.	Per month	20.0		
3	Providing and maintaining the Cost of Utility Services (Electricity, Water, Gas, etc.) for the 01 No. office.	Per month	20.0		
				Total Amount	

PART 3 – Conditions of Contract and Contract Forms

PRSWSSP

Section VIII - General Conditions of Contract

PRSWSSP

Table of Clauses

A. General 101

1. Definitions 101
2. Interpretation 103
3. Language and Law 104
4. Project Manager's Decisions 105
5. Delegation 105
6. Communications 105
7. Subcontracting 105
8. Other Contractors 105
9. Personnel and Equipment 105
10. Employer's and Contractor's Risks 106
11. Employer's Risks 106
12. Contractor's Risks 106
13. Insurance 106
14. Site Data 107
15. Contractor to Construct the Works 107
16. The Works to Be Completed by the Intended Completion Date 107
17. Approval by the Project Manager 108
18. Safety and Protection of the Environment 108
19. Discoveries 108
20. Possession of the Site 108
21. Access to the Site 108
22. Instructions, Inspections and Audits 108
23. Appointment of the Adjudicator 109
24. Procedure for Disputes 109
25. Fraud and Corruption 110

B. Time Control 110

26. Program 110
27. Extension of the Intended Completion Date 111
28. Acceleration 111
29. Delays Ordered by the Project Manager 111
30. Management Meetings 111
31. Early Warning 112

C. Quality Control 112

32. Identifying Defects 112
33. Tests 112
34. Correction of Defects 112
35. Uncorrected Defects 112

D. Cost Control 113

PRSWSDP

36. Contract Price....113
37. Changes in the Contract Price....113
38. Variations....113
39. Cash Flow Forecasts....115
40. Payment Certificates....115
41. Payments....116
42. Compensation Events....116
43. Tax....117
44. Currencies....118
45. Price Adjustment....118
46. Retention....118
47. Liquidated Damages....119
48. Bonus....119
49. Advance Payment....119
50. Securities....120
51. Dayworks....120
52. Cost of Repairs....120

E. Finishing the Contract....120

53. Completion....120
54. Taking Over....121
55. Final Account....121
56. Operating and Maintenance Manuals....121
57. Termination....121
58. Payment upon Termination....122
59. Property....123
60. Release from Performance....123
61. Suspension of Bank Loan or Credit....123

PRSWSP

General Conditions of Contract

A. General

1. Definitions

1.1 Boldface type is used to identify defined terms.

(a) The Accepted Contract Amount means the amount accepted in the Letter of Acceptance for the execution and completion of the Works and the remedying of any defects.

(b) The Activity Schedule is a schedule of the activities comprising the construction, installation, testing, and commissioning of the Works in a lump sum contract. It includes a lump sum price for each activity, which is used for valuations and for assessing the effects of Variations and Compensation Events.

(c) The Adjudicator is the person appointed jointly by the Employer and the Contractor to resolve disputes in the first instance, as provided for in GCC 23.

(d) Bank means the financing institution **named in the PCC**.

(e) Bill of Quantities means the priced and completed Bill of Quantities forming part of the Bid.

(f) Compensation Events are those defined in GCC Clause 42 hereunder.

(g) The Completion Date is the date of completion of the Works as certified by the Project Manager, in accordance with GCC Sub-Clause 53.1.

(h) The Contract is the Contract between the Employer and the Contractor to execute, complete, and maintain the Works. It consists of the documents listed in GCC Sub-Clause 2.3 below.

(i) The Contractor is the party whose Bid to carry out the Works has been accepted by the Employer.

(j) The Contractor's Bid is the completed bidding document submitted by the Contractor to the Employer.

(k) The Contract Price is the Accepted Contract Amount stated in the Letter of Acceptance and thereafter as adjusted in accordance with the Contract.

PRSWSP

(l) Days are calendar days; months are calendar months.

(m) Dayworks are varied work inputs subject to payment on a time basis for the Contractor's employees and Equipment, in addition to payments for associated Materials and Plant.

(n) A Defect is any part of the Works not completed in accordance with the Contract.

(o) The Defects Liability Certificate is the certificate issued by Project Manager upon correction of defects by the Contractor.

(p) The Defects Liability Period is the period **named in the PCC** pursuant to Sub-Clause 34.1 and calculated from the Completion Date.

(q) Drawings means the drawings of the Works, as included in the Contract, and any additional and modified drawings issued by (or on behalf of) the Employer in accordance with the Contract, include calculations and other information provided or approved by the Project Manager for the execution of the Contract.

(r) The Employer is the party who employs the Contractor to carry out the Works, **as specified in the PCC**.

(s) Equipment is the Contractor's machinery and vehicles brought temporarily to the Site to construct the Works.

(t) "In writing" or "written" means hand-written, type-written, printed or electronically made, and resulting in a permanent record;

(u) The Initial Contract Price is the Contract Price listed in the Employer's Letter of Acceptance.

(v) The Intended Completion Date is the date on which it is intended that the Contractor shall complete the Works. The Intended Completion Date is **specified in the PCC**. The Intended Completion Date may be revised only by the Project Manager by issuing an extension of time or an acceleration order.

(w) Materials are all supplies, including consumables, used by the Contractor for incorporation in the Works.

PRSWSP

(x) Plant is any integral part of the Works that shall have a mechanical, electrical, chemical, or biological function.

(y) The Project Manager is the person **named in the PCC** (or any other competent person appointed by the Employer and notified to the Contractor, to act in replacement of the Project Manager) who is responsible for supervising the execution of the Works and administering the Contract.

(z) PCC means Particular Conditions of Contract.

(aa) The Site is the area **defined as such in the PCC**.

(bb) Site Investigation Reports are those that were included in the bidding document and are factual and interpretative reports about the surface and subsurface conditions at the Site.

(cc) Specification means the Specification of the Works included in the Contract and any modification or addition made or approved by the Project Manager.

(dd) The Start Date is **given in the PCC**. It is the latest date when the Contractor shall commence execution of the Works. It does not necessarily coincide with any of the Site Possession Dates.

(ee) A Subcontractor is a person or corporate body who has a Contract with the Contractor to carry out a part of the work in the Contract, which includes work on the Site.

(ff) Temporary Works are works designed, constructed, installed, and removed by the Contractor that are needed for construction or installation of the Works.

(gg) A Variation is an instruction given by the Project Manager which varies the Works.

(hh) The Works are what the Contract requires the Contractor to construct, install, and turn over to the Employer, **as defined in the PCC**.

2. Interpretation 2.1 In interpreting these GCC, words indicating one gender include all genders. Words indicating the singular also include the plural and words indicating the plural also include the singular. Headings have no significance. Words have their normal meaning under the language of the Contract unless specifically defined.

PRSWCSP

The Project Manager shall provide instructions clarifying queries about these GCC.

2.2 If sectional completion is **specified in the PCC**, references in the GCC to the Works, the Completion Date, and the Intended Completion Date apply to any Section of the Works (other than references to the Completion Date and Intended Completion Date for the whole of the Works).

2.3 The documents forming the Contract shall be interpreted in the following order of priority:

(a) Agreement,

(b) Letter of Acceptance,

(c) Contractor's Bid,

(d) Particular Conditions of Contract,

(e) General Conditions of Contract, including Appendices,

(f) Specifications,

(g) Drawings,

(h) Bill of Quantities,[1] and

(i) any other document **listed in the PCC** as forming part of the Contract.

3. Language and Law

3.1 The language of the Contract and the law governing the Contract are **stated in the PCC**.

3.2 Throughout the execution of the Contract, the Contractor shall comply with the import of goods and services prohibitions in the Employer's Country when

(a) as a matter of law or official regulations, the Borrower's country prohibits commercial relations with that country; or

(b) by an act of compliance with a decision of the United Nations Security Council taken under Chapter VII of the Charter of the United Nations, the Borrower's Country prohibits any import of goods from that country or any payments to any country, person, or entity in that country.

[1] In lump sum contracts, delete "Bill of Quantities" and replace with "Activity Schedule."

PCWSP

4. Project Manager's Decisions	4.1	Except where otherwise specifically stated, the Project Manager shall decide contractual matters between the Employer and the Contractor in the role representing the Employer.
5. Delegation	5.1	Otherwise **specified in the PCC,** the Project Manager may delegate any of his duties and responsibilities to other people, except to the Adjudicator, after notifying the Contractor, and may revoke any delegation after notifying the Contractor.
6. Communications	6.1	Communications between parties that are referred to in the Conditions shall be effective only when in writing. A notice shall be effective only when it is delivered.
7. Subcontracting	7.1	The Contractor may subcontract with the approval of the Project Manager, but may not assign the Contract without the approval of the Employer in writing. Subcontracting shall not alter the Contractor's obligations.
8. Other Contractors	8.1	The Contractor shall cooperate and share the Site with other contractors, public authorities, utilities, and the Employer between the dates given in the Schedule of Other Contractors, as **referred to in the PCC.** The Contractor shall also provide facilities and services for them as described in the Schedule. The Employer may modify the Schedule of Other Contractors, and shall notify the Contractor of any such modification.
9. Personnel and Equipment	9.1	The Contractor shall employ the key personnel and use the equipment identified in its Bid, to carry out the Works or other personnel and equipment approved by the Project Manager. The Project Manager shall approve any proposed replacement of key personnel and equipment only if their relevant qualifications or characteristics are substantially equal to or better than those proposed in the Bid.
	9.2	If the Project Manager asks the Contractor to remove a person who is a member of the Contractor's staff or work force, stating the reasons, the Contractor shall ensure that the person leaves the Site within seven days and has no further connection with the work in the Contract.
	9.3	If the Employer, Project Manager or Contractor determines, that any employee of the Contractor be determined to have engaged in Fraud and Corruption during the execution of the Works, then that employee shall be removed in accordance with Clause 9.2 above.

PRSWSP

10. Employer's and Contractor's Risks

10.1 The Employer carries the risks which this Contract states are Employer's risks, and the Contractor carries the risks which this Contract states are Contractor's risks.

11. Employer's Risks

11.1 From the Start Date until the Defects Liability Certificate has been issued, the following are Employer's risks:

(a) The risk of personal injury, death, or loss of or damage to property (excluding the Works, Plant, Materials, and Equipment), which are due to

(i) use or occupation of the Site by the Works or for the purpose of the Works, which is the unavoidable result of the Works or

(ii) negligence, breach of statutory duty, or interference with any legal right by the Employer or by any person employed by or contracted to him except the Contractor.

(b) The risk of damage to the Works, Plant, Materials, and Equipment to the extent that it is due to a fault of the Employer or in the Employer's design, or due to war or radioactive contamination directly affecting the country where the Works are to be executed.

11.2 From the Completion Date until the Defects Liability Certificate has been issued, the risk of loss of or damage to the Works, Plant, and Materials is an Employer's risk except loss or damage due to

(a) a Defect which existed on the Completion Date,

(b) an event occurring before the Completion Date, which was not itself an Employer's risk, or

(c) the activities of the Contractor on the Site after the Completion Date.

12. Contractor's Risks

12.1 From the Starting Date until the Defects Liability Certificate has been issued, the risks of personal injury, death, and loss of or damage to property (including, without limitation, the Works, Plant, Materials, and Equipment) which are not Employer's risks are Contractor's risks.

13. Insurance

13.1 The Contractor shall provide, in the joint names of the Employer and the Contractor, insurance cover from the Start Date to the end of the Defects Liability Period, in the amounts and

PRSWSCP

deductibles **stated in the PCC** for the following events which are due to the Contractor's risks:

(a) loss of or damage to the Works, Plant, and Materials;

(b) loss of or damage to Equipment;

(c) loss of or damage to property (except the Works, Plant, Materials, and Equipment) in connection with the Contract; and

(d) personal injury or death.

13.2 Policies and certificates for insurance shall be delivered by the Contractor to the Project Manager for the Project Manager's approval before the Start Date. All such insurance shall provide for compensation to be payable in the types and proportions of currencies required to rectify the loss or damage incurred.

13.3 If the Contractor does not provide any of the policies and certificates required, the Employer may effect the insurance which the Contractor should have provided and recover the premiums the Employer has paid from payments otherwise due to the Contractor or, if no payment is due, the payment of the premiums shall be a debt due.

13.4 Alterations to the terms of an insurance shall not be made without the approval of the Project Manager.

13.5 Both parties shall comply with any conditions of the insurance policies.

14. Site Data

14.1 The Contractor shall be deemed to have examined any Site Data **referred to in the PCC**, supplemented by any information available to the Contractor.

15. Contractor to Construct the Works

15.1 The Contractor shall construct and install the Works in accordance with the Specifications and Drawings.

16. The Works to Be Completed by the Intended Completion Date

16.1 The Contractor may commence execution of the Works on the Start Date and shall carry out the Works in accordance with the Program submitted by the Contractor, as updated with the approval of the Project Manager, and complete them by the Intended Completion Date.

PRVCSD

17. Approval by the Project Manager

17.1 The Contractor shall submit Specifications and Drawings showing the proposed Temporary Works to the Project Manager, for his approval.

17.2 The Contractor shall be responsible for design of Temporary Works.

17.3 The Project Manager's approval shall not alter the Contractor's responsibility for design of the Temporary Works.

17.4 The Contractor shall obtain approval of third parties to the design of the Temporary Works, where required.

17.5 All Drawings prepared by the Contractor for the execution of the temporary or permanent Works, are subject to prior approval by the Project Manager before this use.

18. Safety and Protection of the Environment

18.1 The Contractor shall be responsible for the safety of all activities on the Site.

18.2 The Contractor shall take all reasonable steps to protect the environment (both on and off the Site) and to limit damage and nuisance to people and property resulting from pollution, noise and other results of his operations.

19. Discoveries

19.1 Anything of historical or other interest or of significant value unexpectedly discovered on the Site shall be the property of the Employer. The Contractor shall notify the Project Manager of such discoveries and carry out the Project Manager's instructions for dealing with them.

20. Possession of the Site

20.1 The Employer shall give possession of all parts of the Site to the Contractor. If possession of a part is not given by the date **stated in the PCC,** the Employer shall be deemed to have delayed the start of the relevant activities, and this shall be a Compensation Event.

21. Access to the Site

21.1 The Contractor shall allow the Project Manager and any person authorized by the Project Manager access to the Site and to any place where work in connection with the Contract is being carried out or is intended to be carried out.

22. Instructions, Inspections and Audits

22.1 The Contractor shall carry out all instructions of the Project Manager which comply with the applicable laws where the Site is located.

22.2 The Contractor shall keep, and shall make all reasonable efforts to cause its Subcontractors and subconsultants to keep, accurate and systematic accounts and records in respect of the Works in

PROVISO

such form and details as will clearly identify relevant time changes and costs.

22.3 Pursuant to paragraph 2.2 e. of Appendix B to the General Conditions, the Contractor shall permit and shall cause its subcontractors and subconsultants to permit, the Bank and/or persons appointed by the Bank to inspect the Site and/or the accounts and records relating to the procurement process, selection and/or contract execution, and to have such accounts and records audited by auditors appointed by the Bank if requested by the Bank. The Contractor's and its Subcontractors' and subconsultants' attention is drawn to Sub-Clause 25.1 (Fraud and Corruption) which provides, inter alia, that acts intended to materially impede the exercise of the Bank's inspection and audit rights constitute a prohibited practice subject to contract termination (as well as to a determination of ineligibility pursuant to the Bank's prevailing sanctions procedures).]

23. Appointment of the Adjudicator

23.1 The Adjudicator shall be appointed jointly by the Employer and the Contractor, at the time of the Employer's issuance of the Letter of Acceptance. If, in the Letter of Acceptance, the Employer does not agree on the appointment of the Adjudicator, the Employer will request the Appointing Authority **designated in the PCC**, to appoint the Adjudicator within 14 days of receipt of such request.

23.2 Should the Adjudicator resign or die, or should the Employer and the Contractor agree that the Adjudicator is not functioning in accordance with the provisions of the Contract, a new Adjudicator shall be jointly appointed by the Employer and the Contractor. In case of disagreement between the Employer and the Contractor, within 30 days, the Adjudicator shall be designated by the Appointing Authority **designated in the PCC** at the request of either party, within 14 days of receipt of such request.

24. Procedure for Disputes

24.1 If the Contractor believes that a decision taken by the Project Manager was either outside the authority given to the Project Manager by the Contract or that the decision was wrongly taken, the decision shall be referred to the Adjudicator within 14 days of the notification of the Project Manager's decision.

24.2 The Adjudicator shall give a decision in writing within 28 days of receipt of a notification of a dispute.

24.3 The Adjudicator shall be paid by the hour at the **rate specified in the PCC,** together with reimbursable expenses of the types

PROVISO

specified in the PCC, and the cost shall be divided equally between the Employer and the Contractor, whatever decision is reached by the Adjudicator. Either party may refer a decision of the Adjudicator to an Arbitrator within 28 days of the Adjudicator's written decision. If neither party refers the dispute to arbitration within the above 28 days, the Adjudicator's decision shall be final and binding.

24.4 The arbitration shall be conducted in accordance with the arbitration procedures published by the institution named and, in the place, **specified in the PCC.**

25. Fraud and Corruption

25.1 The Bank requires compliance with the Bank's Anti-Corruption Guidelines and its prevailing sanctions policies and procedures as set forth in the WBG's Sanctions Framework, as set forth in Appendix A to the GCC.

25.2 The Employer requires the Contractor to disclose any commissions or fees that may have been paid or are to be paid to agents or any other party with respect to the bidding process or execution of the Contract. The information disclosed must include at least the name and address of the agent or other party, the amount and currency, and the purpose of the commission, gratuity or fee.

B. Time Control

26. Program

26.1 Within the time **stated in the PCC**, after the date of the Letter of Acceptance, the Contractor shall submit to the Project Manager for approval a Program showing the general methods, arrangements, order, and timing for all the activities in the Works. In the case of a lump sum contract, the activities in the Program shall be consistent with those in the Activity Schedule.

26.2 An update of the Program shall be a program showing the actual progress achieved on each activity and the effect of the progress achieved on the timing of the remaining work, including any changes to the sequence of the activities.

26.3 The Contractor shall submit to the Project Manager for approval an updated Program at intervals no longer than the period **stated in the PCC.** If the Contractor does not submit an updated Program within this period, the Project Manager may withhold the amount **stated in the PCC** from the next payment certificate and continue to withhold this amount until the next payment after the date on which the overdue Program has been submitted. In the case of a lump sum contract, the Contractor shall provide an

PRSWSP

updated Activity Schedule within 14 days of being instructed to by the Project Manager.

26.4 The Project Manager's approval of the Program shall not alter the Contractor's obligations. The Contractor may revise the Program and submit it to the Project Manager again at any time. A revised Program shall show the effect of Variations and Compensation Events.

27. Extension of the Intended Completion Date

27.1 The Project Manager shall extend the Intended Completion Date if a Compensation Event occurs or a Variation is issued which makes it impossible for Completion to be achieved by the Intended Completion Date without the Contractor taking steps to accelerate the remaining work, which would cause the Contractor to incur additional cost.

27.2 The Project Manager shall decide whether and by how much to extend the Intended Completion Date within 21 days of the Contractor asking the Project Manager for a decision upon the effect of a Compensation Event or Variation and submitting full supporting information. If the Contractor has failed to give early warning of a delay or has failed to cooperate in dealing with a delay, the delay by this failure shall not be considered in assessing the new Intended Completion Date.

28. Acceleration

28.1 When the Employer wants the Contractor to finish before the Intended Completion Date, the Project Manager shall obtain priced proposals for achieving the necessary acceleration from the Contractor. If the Employer accepts these proposals, the Intended Completion Date shall be adjusted accordingly and confirmed by both the Employer and the Contractor.

28.2 If the Contractor's priced proposals for an acceleration are accepted by the Employer, they are incorporated in the Contract Price and treated as a Variation.

29. Delays Ordered by the Project Manager

29.1 The Project Manager may instruct the Contractor to delay the start or progress of any activity within the Works.

30. Management Meetings

30.1 Either the Project Manager or the Contractor may require the other to attend a management meeting. The business of a management meeting shall be to review the plans for remaining work and to deal with matters raised in accordance with the early warning procedure.

30.2 The Project Manager shall record the business of management meetings and provide copies of the record to those attending the

PROVISO

meeting and to the Employer. The responsibility of the parties for actions to be taken shall be decided by the Project Manager either at the management meeting or after the management meeting and stated in writing to all who attended the meeting.

31. Early Warning

31.1 The Contractor shall warn the Project Manager at the earliest opportunity of specific likely future events or circumstances that may adversely affect the quality of the work, increase the Contract Price, or delay the execution of the Works. The Project Manager may require the Contractor to provide an estimate of the expected effect of the future event or circumstance on the Contract Price and Completion Date. The estimate shall be provided by the Contractor as soon as reasonably possible.

31.2 The Contractor shall cooperate with the Project Manager in making and considering proposals for how the effect of such an event or circumstance can be avoided or reduced by anyone involved in the work and in carrying out any resulting instruction of the Project Manager.

C. Quality Control

32. Identifying Defects

32.1 The Project Manager shall check the Contractor's work and notify the Contractor of any Defects that are found. Such checking shall not affect the Contractor's responsibilities. The Project Manager may instruct the Contractor to search for a Defect and to uncover and test any work that the Project Manager considers may have a Defect.

33. Tests

33.1 If the Project Manager instructs the Contractor to carry out a test not specified in the Specification to check whether any work has a Defect and the test shows that it does, the Contractor shall pay for the test and any samples. If there is no Defect, the test shall be a Compensation Event.

34. Correction of Defects

34.1 The Project Manager shall give notice to the Contractor of any Defects before the end of the Defects Liability Period, which begins at Completion, and is **defined in the PCC.** The Defects Liability Period shall be extended for as long as Defects remain to be corrected.

34.2 Every time notice of a Defect is given, the Contractor shall correct the notified Defect within the length of time specified by the Project Manager's notice.

35. Uncorrected Defects

35.1 If the Contractor has not corrected a Defect within the time specified in the Project Manager's notice, the Project Manager

PRSWSP

shall assess the cost of having the Defect corrected, and the Contractor shall pay this amount.

D. Cost Control

36. Contract Price[2]

36.1 The Bill of Quantities shall contain priced items for the Works to be performed by the Contractor. The Bill of Quantities is used to calculate the Contract Price. The Contractor will be paid for the quantity of the work accomplished at the rate in the Bill of Quantities for each item.

37. Changes in the Contract Price[3]

37.1 If the final quantity of the work done differs from the quantity in the Bill of Quantities for the particular item by more than 25 percent, provided the change exceeds 1 percent of the Initial Contract Price, the Project Manager shall adjust the rate to allow for the change. The Project Manager shall not adjust rates from changes in quantities if thereby the Initial Contract Price is exceeded by more than 15 percent, except with the prior approval of the Employer.

37.2 If requested by the Project Manager, the Contractor shall provide the Project Manager with a detailed cost breakdown of any rate in the Bill of Quantities.

38. Variations

38.1 All Variations shall be included in updated Programs[4]produced by the Contractor.

38.2 The Contractor shall provide the Project Manager with a quotation for carrying out the Variation when requested to do so by the Project Manager. The Project Manager shall assess the quotation, which shall be given within seven (7) days of the request or within any longer period stated by the Project Manager and before the Variation is ordered.

38.3 If the Contractor's quotation is unreasonable, the Project Manager may order the Variation and make a change to the Contract Price, which shall be based on the Project Manager's

---

[2] In lump sum contracts, replace GCC Sub-Clauses 36.1 as follows:
36.1The Contractor shall provide updated Activity Schedules within 14 days of being instructed to by the Project Manager. The Activity Schedule shall contain the priced activities for the Works to be performed by the Contractor. The Activity Schedule is used to monitor and control the performance of activities on which basis the Contractor will be paid. If payment for materials on site shall be made separately, the Contractor shall show delivery of Materials to the Site separately on the Activity Schedule.

[3] In lump sum contracts, replace entire GCC Clause 37 with new GCC Sub-Clause 37.1, as follows:
37.1 The Activity Schedule shall be amended by the Contractor to accommodate changes of Program or method of working made at the Contractor's own discretion. Prices in the Activity Schedule shall not be altered when the Contractor makes such changes to the Activity Schedule.

[4] In lump sum contracts, add "and Activity Schedules" after "Programs."

PRSWSD

own forecast of the effects of the Variation on the Contractor's costs.

38.4 If the Project Manager decides that the urgency of varying the work would prevent a quotation being given and considered without delaying the work, no quotation shall be given and the Variation shall be treated as a Compensation Event.

38.5 The Contractor shall not be entitled to additional payment for costs that could have been avoided by giving early warning.

38.6 If the work in the Variation corresponds to an item description in the Bill of Quantities and if, in the opinion of the Project Manager, the quantity of work above the limit stated in Sub-Clause 39.1 or the timing of its execution do not cause the cost per unit of quantity to change, the rate in the Bill of Quantities shall be used to calculate the value of the Variation. If the cost per unit of quantity changes, or if the nature or timing of the work in the Variation does not correspond with items in the Bill of Quantities, the quotation by the Contractor shall be in the form of new rates for the relevant items of work.[5]

38.7 Value Engineering: The Contractor may prepare, at its own cost, a value engineering proposal at any time during the performance of the contract. The value engineering proposal shall, at a minimum, include the following;

(a) the proposed change(s), and a description of the difference to the existing contract requirements;

(b) a full cost/benefit analysis of the proposed change(s) including a description and estimate of costs (including life cycle costs) the Employer may incur in implementing the value engineering proposal; and

(c) a description of any effect(s) of the change on performance/functionality.

The Employer may accept the value engineering proposal if the proposal demonstrates benefits that:

(a) accelerate the contract completion period; or

(b) reduce the Contract Price or the life cycle costs to the Employer; or

[5] In lump sum contracts, delete this paragraph.

PRSNSD

(c) improve the quality, efficiency, safety or sustainability of the Facilities; or

(d) yield any other benefits to the Employer,

without compromising the functionality of the Works.

If the value engineering proposal is approved by the Employer and results in:

(a) a reduction of the Contract Price; the amount to be paid to the Contractor shall be the **percentage specified in the PCC** of the reduction in the Contract Price; or

(b) an increase in the Contract Price; but results in a reduction in life cycle costs due to any benefit described in (a) to (d) above, the amount to be paid to the Contractor shall be the full increase in the Contract Price.

39. Cash Flow Forecasts

39.1 When the Program,[6] is updated, the Contractor shall provide the Project Manager with an updated cash flow forecast. The cash flow forecast shall include different currencies, as defined in the Contract, converted as necessary using the Contract exchange rates.

40. Payment Certificates

40.1 The Contractor shall submit to the Project Manager monthly statements of the estimated value of the work executed less the cumulative amount certified previously.

40.2 The Project Manager shall check the Contractor's monthly statement and certify the amount to be paid to the Contractor.

40.3 The value of work executed shall be determined by the Project Manager.

40.4 The value of work executed shall comprise the value of the quantities of work in the Bill of Quantities that have been completed.[7]

40.5 The value of work executed shall include the valuation of Variations and Compensation Events.

[6] In lump sum contracts, add "or Activity Schedule" after "Program."

[7] In lump sum contracts, replace this paragraph with the following: "The value of work executed shall comprise the value of completed activities in the Activity Schedule."

PRSVSD

40.6 The Project Manager may exclude any item certified in a previous certificate or reduce the proportion of any item previously certified in any certificate in the light of later information.

41. Payments

41.1 Payments shall be adjusted for deductions for advance payments and retention. The Employer shall pay the Contractor the amounts certified by the Project Manager within 28 days of the date of each certificate. If the Employer makes a late payment, the Contractor shall be paid interest on the late payment in the next payment. Interest shall be calculated from the date by which the payment should have been made up to the date when the late payment is made at the prevailing rate of interest for commercial borrowing for each of the currencies in which payments are made.

41.2 If an amount certified is increased in a later certificate or as a result of an award by the Adjudicator or an Arbitrator, the Contractor shall be paid interest upon the delayed payment as set out in this clause. Interest shall be calculated from the date upon which the increased amount would have been certified in the absence of dispute.

41.3 Unless otherwise stated, all payments and deductions shall be paid or charged in the proportions of currencies comprising the Contract Price.

41.4 Items of the Works for which no rate or price has been entered in shall not be paid for by the Employer and shall be deemed covered by other rates and prices in the Contract.

42. Compensation Events

42.1 The following shall be Compensation Events:

(a) The Employer does not give access to a part of the Site by the Site Possession Date pursuant to GCC Sub-Clause 20.1.

(b) The Employer modifies the Schedule of Other Contractors in a way that affects the work of the Contractor under the Contract.

(c) The Project Manager orders a delay or does not issue Drawings, Specifications, or instructions required for execution of the Works on time.

(d) The Project Manager instructs the Contractor to uncover or to carry out additional tests upon work, which is then found to have no Defects.

(e) The Project Manager unreasonably does not approve a subcontract to be let.

PRSM SBD

(f) Ground conditions are substantially more adverse than could reasonably have been assumed before issuance of the Letter of Acceptance from the information issued to bidders (including the Site Investigation Reports), from information available publicly and from a visual inspection of the Site.

(g) The Project Manager gives an instruction for dealing with an unforeseen condition, caused by the Employer, or additional work required for safety or other reasons.

(h) Other contractors, public authorities, utilities, or the Employer does not work within the dates and other constraints stated in the Contract, and they cause delay or extra cost to the Contractor.

(i) The advance payment is delayed.

(j) The effects on the Contractor of any of the Employer's Risks.

(k) The Project Manager unreasonably delays issuing a Certificate of Completion.

42.2 If a Compensation Event would cause additional cost or would prevent the work being completed before the Intended Completion Date, the Contract Price shall be increased and/or the Intended Completion Date shall be extended. The Project Manager shall decide whether and by how much the Contract Price shall be increased and whether and by how much the Intended Completion Date shall be extended.

42.3 As soon as information demonstrating the effect of each Compensation Event upon the Contractor's forecast cost has been provided by the Contractor, it shall be assessed by the Project Manager, and the Contract Price shall be adjusted accordingly. If the Contractor's forecast is deemed unreasonable, the Project Manager shall adjust the Contract Price based on the Project Manager's own forecast. The Project Manager shall assume that the Contractor shall react competently and promptly to the event.

42.4 The Contractor shall not be entitled to compensation to the extent that the Employer's interests are adversely affected by the Contractor's not having given early warning or not having cooperated with the Project Manager.

43. Tax

43.1 The Project Manager shall adjust the Contract Price if taxes, duties, and other levies are changed between the date 28 days before the submission of bids for the Contract and the date of the

PRWSP

last Completion certificate. The adjustment shall be the change in the amount of tax payable by the Contractor, provided such changes are not already reflected in the Contract Price or are a result of GCC Clause 44.

44. Currencies

44.1 Where payments are made in currencies other than the currency of the Employer's Country **specified in the PCC,** the exchange rates used for calculating the amounts to be paid shall be the exchange rates stated in the Contractor's Bid.

45. Price Adjustment

45.1 Prices shall be adjusted for fluctuations in the cost of inputs only if **provided for in the PCC.** If so provided, the amounts certified in each payment certificate, before deducting for Advance Payment, shall be adjusted by applying the respective price adjustment factor to the payment amounts due in each currency. A separate formula of the type specified below applies to each Contract currency:

$$\mathbf{P_c = A_c + B_c\, Imc/Ioc}$$

where:

P_c is the adjustment factor for the portion of the Contract Price payable in a specific currency "c."

A_c and B_c are coefficients[8] **specified in the PCC,** representing the nonadjustable and adjustable portions, respectively, of the Contract Price payable in that specific currency "c;" and

Imc is the index prevailing at the end of the month being invoiced and Ioc is the index prevailing 28 days before Bid opening for inputs payable; both in the specific currency "c."

45.2 If the value of the index is changed after it has been used in a calculation, the calculation shall be corrected and an adjustment made in the next payment certificate. The index value shall be deemed to take account of all changes in cost due to fluctuations in costs.

46. Retention

46.1 The Employer shall retain from each payment due to the Contractor the proportion **stated in the PCC** until Completion of the whole of the Works.

[8] The sum of the two coefficients A_c and B_c should be 1 (one) in the formula for each currency. Normally, both coefficients shall be the same in the formulae for all currencies, since coefficient A, for the nonadjustable portion of the payments, is a very approximate figure (usually 0.15) to take account of fixed cost elements or other nonadjustable components. The sum of the adjustments for each currency are added to the Contract Price.

PRSWSD

46.2 Upon the issue of a Certificate of Completion of the Works by the Project Manager, in accordance with GCC 53.1, half the total amount retained shall be repaid to the Contractor and half when the Defects Liability Period has passed and the Project Manager has certified that all Defects notified by the Project Manager to the Contractor before the end of this period have been corrected. The Contractor may substitute retention money with an "on demand" Bank guarantee.

47. Liquidated Damages

47.1 The Contractor shall pay liquidated damages to the Employer at the rate per day **stated in the PCC** for each day that the Completion Date is later than the Intended Completion Date. The total amount of liquidated damages shall not exceed the amount **defined in the PCC.** The Employer may deduct liquidated damages from payments due to the Contractor. Payment of liquidated damages shall not affect the Contractor's liabilities.

47.2 If the Intended Completion Date is extended after liquidated damages have been paid, the Project Manager shall correct any overpayment of liquidated damages by the Contractor by adjusting the next payment certificate. The Contractor shall be paid interest on the overpayment, calculated from the date of payment to the date of repayment, at the rates specified in GCC Sub-Clause 41.1.

48. Bonus

48.1 The Contractor shall be paid a Bonus calculated at the rate per calendar day **stated in the PCC** for each day (less any days for which the Contractor is paid for acceleration) that the Completion is earlier than the Intended Completion Date. The Project Manager shall certify that the Works are complete, although they may not be due to be complete.

49. Advance Payment

49.1 The Employer shall make advance payment to the Contractor of the amounts **stated in the PCC** by the date **stated in the PCC,** against provision by the Contractor of an Unconditional Bank Guarantee in a form and by a bank acceptable to the Employer in amounts and currencies equal to the advance payment. The Guarantee shall remain effective until the advance payment has been repaid, but the amount of the Guarantee shall be progressively reduced by the amounts repaid by the Contractor. Interest shall not be charged on the advance payment.

49.2 The Contractor is to use the advance payment only to pay for Equipment, Plant, Materials, and mobilization expenses required specifically for execution of the Contract. The Contractor shall demonstrate that advance payment has been used in this way by

PRSWCSP

supplying copies of invoices or other documents to the Project Manager.

49.3 The advance payment shall be repaid by deducting proportionate amounts from payments otherwise due to the Contractor, following the schedule of completed percentages of the Works on a payment basis. No account shall be taken of the advance payment or its repayment in assessing valuations of work done, Variations, price adjustments, Compensation Events, Bonuses, or Liquidated Damages.

50. Securities

50.1 The Performance Security shall be provided to the Employer no later than the date specified in the Letter of Acceptance and shall be issued in an amount **specified in the PCC,** by a bank or surety acceptable to the Employer, and denominated in the types and proportions of the currencies in which the Contract Price is payable. The Performance Security shall be valid until a date 28 days from the date of issue of the Certificate of Completion in the case of a Bank Guarantee, and until one year from the date of issue of the Completion Certificate in the case of a Performance Bond.

51. Dayworks

51.1 If applicable, the Dayworks rates in the Contractor's Bid shall be used only when the Project Manager has given written instructions in advance for additional work to be paid for in that way.

51.2 All work to be paid for as Dayworks shall be recorded by the Contractor on forms approved by the Project Manager. Each completed form shall be verified and signed by the Project Manager within two days of the work being done.

51.3 The Contractor shall be paid for Dayworks subject to obtaining signed Dayworks forms.

52. Cost of Repairs

52.1 Loss or damage to the Works or Materials to be incorporated in the Works between the Start Date and the end of the Defects Correction periods shall be remedied by the Contractor at the Contractor's cost if the loss or damage arises from the Contractor's acts or omissions.

E. Finishing the Contract

53. Completion

53.1 The Contractor shall request the Project Manager to issue a Certificate of Completion of the Works, and the Project Manager shall do so upon deciding that the whole of the Works is completed.

PREVIOUS

54. Taking Over

54.1 The Employer shall take over the Site and the Works within seven days of the Project Manager's issuing a certificate of Completion.

55. Final Account

55.1 The Contractor shall supply the Project Manager with a detailed account of the total amount that the Contractor considers payable under the Contract before the end of the Defects Liability Period. The Project Manager shall issue a Defects Liability Certificate and certify any final payment that is due to the Contractor within 56 days of receiving the Contractor's account if it is correct and complete. If it is not, the Project Manager shall issue within 56 days a schedule that states the scope of the corrections or additions that are necessary. If the Final Account is still unsatisfactory after it has been resubmitted, the Project Manager shall decide on the amount payable to the Contractor and issue a payment certificate.

56. Operating and Maintenance Manuals

56.1 If "as built" Drawings and/or operating and maintenance manuals are required, the Contractor shall supply them by the dates **stated in the PCC.**

56.2 If the Contractor does not supply the Drawings and/or manuals by the dates **stated in the PCC** pursuant to GCC Sub-Clause 56.1**,** or they do not receive the Project Manager's approval, the Project Manager shall withhold the amount **stated in the PCC** from payments due to the Contractor.

57. Termination

57.1 The Employer or the Contractor may terminate the Contract if the other party causes a fundamental breach of the Contract.

57.2 Fundamental breaches of Contract shall include, but shall not be limited to, the following:

(a) the Contractor stops work for 28 days when no stoppage of work is shown on the current Program and the stoppage has not been authorized by the Project Manager;

(b) the Project Manager instructs the Contractor to delay the progress of the Works, and the instruction is not withdrawn within 28 days;

(c) the Employer or the Contractor is made bankrupt or goes into liquidation other than for a reconstruction or amalgamation;

(d) a payment certified by the Project Manager is not paid by the Employer to the Contractor within 84 days of the date of the Project Manager's certificate;

(e) the Project Manager gives Notice that failure to correct a particular Defect is a fundamental breach of Contract and the

PRSWSP

Contractor fails to correct it within a reasonable period of time determined by the Project Manager;

(f) the Contractor does not maintain a Security, which is required;

(g) the Contractor has delayed the completion of the Works by the number of days for which the maximum amount of liquidated damages can be paid, as **defined in the PCC**; or

(h) if the Contractor, in the judgment of the Employer has engaged in Fraud and Corruption, as defined in paragrpah 2.2 a of the Appendix A to the GCC, in competing for or in executing the Contract, then the Employer may, after giving fourteen (14) days written notice to the Contractor, terminate the Contract and expel him from the Site.

57.3 Notwithstanding the above, the Employer may terminate the Contract for convenience.

57.4 If the Contract is terminated, the Contractor shall stop work immediately, make the Site safe and secure, and leave the Site as soon as reasonably possible.

57.5 When either party to the Contract gives notice of a breach of Contract to the Project Manager for a cause other than those listed under GCC Sub-Clause 56.2 above, the Project Manager shall decide whether the breach is fundamental or not.

58. Payment upon Termination

58.1 If the Contract is terminated because of a fundamental breach of Contract by the Contractor, the Project Manager shall issue a certificate for the value of the work done and Materials ordered less advance payments received up to the date of the issue of the certificate and less the percentage to apply to the value of the work not completed, as **specified in the PCC.** Additional Liquidated Damages shall not apply. If the total amount due to the Employer exceeds any payment due to the Contractor, the difference shall be a debt payable to the Employer.

58.2 If the Contract is terminated for the Employer's convenience or because of a fundamental breach of Contract by the Employer, the Project Manager shall issue a certificate for the value of the work done, Materials ordered, the reasonable cost of removal of Equipment, repatriation of the Contractor's personnel employed solely on the Works, and the Contractor's costs of protecting and securing the Works, and less advance payments received up to the date of the certificate.

PROVISO

59. Property

59.1 All Materials on the Site, Plant, Equipment, Temporary Works, and Works shall be deemed to be the property of the Employer if the Contract is terminated because of the Contractor's default.

60. Release from Performance

60.1 If the Contract is frustrated by the outbreak of war or by any other event entirely outside the control of either the Employer or the Contractor, the Project Manager shall certify that the Contract has been frustrated. The Contractor shall make the Site safe and stop work as quickly as possible after receiving this certificate and shall be paid for all work carried out before receiving it and for any work carried out afterwards to which a commitment was made.

61. Suspension of Bank Loan or Credit

61.1 In the event that the Bank suspends the Loan or Credit to the Employer, from which part of the payments to the Contractor are being made:

(a) The Employer is obligated to notify the Contractor of such suspension within 7 days of having received the Bank's suspension notice.

(b) If the Contractor has not received sums due to it within the 28 days for payment provided for in Sub-Clause 40.1, the Contractor may immediately issue a 14-day termination notice.

PRSWSP

APPENDIX A
TO GENERAL CONDITIONS

Fraud and Corruption

(Text in this Appendix shall not be modified)

1. Purpose

1.1 The Bank's Anti-Corruption Guidelines and this annex apply with respect to procurement under Bank Investment Project Financing operations.

2. Requirements

2.1 The Bank requires that Borrowers (including beneficiaries of Bank financing); bidders (applicants/proposers), consultants, contractors and suppliers; any sub-contractors, sub-consultants, service providers or suppliers; any agents (whether declared or not); and any of their personnel, observe the highest standard of ethics during the procurement process, selection and contract execution of Bank-financed contracts, and refrain from Fraud and Corruption.

2.2 To this end, the Bank:

a. Defines, for the purposes of this provision, the terms set forth below as follows:

i. "corrupt practice" is the offering, giving, receiving, or soliciting, directly or indirectly, of anything of value to influence improperly the actions of another party;

ii. "fraudulent practice" is any act or omission, including misrepresentation, that knowingly or recklessly misleads, or attempts to mislead, a party to obtain financial or other benefit or to avoid an obligation;

iii. "collusive practice" is an arrangement between two or more parties designed to achieve an improper purpose, including to influence improperly the actions of another party;

iv. "coercive practice" is impairing or harming, or threatening to impair or harm, directly or indirectly, any party or the property of the party to influence improperly the actions of a party;

v. "obstructive practice" is:

(a) deliberately destroying, falsifying, altering, or concealing of evidence material to the investigation or making false statements to investigators in order to materially impede a Bank investigation into allegations of a corrupt, fraudulent, coercive, or collusive practice; and/or threatening, harassing, or intimidating any party to prevent it from disclosing its knowledge of matters relevant to the investigation or from pursuing the investigation; or

PROVISO

(b) acts intended to materially impede the exercise of the Bank's inspection and audit rights provided for under paragraph 2.2 e. below.

b. Rejects a proposal for award if the Bank determines that the firm or individual recommended for award, any of its personnel, or its agents, or its sub-consultants, sub-contractors, service providers, suppliers and/ or their employees, has, directly or indirectly, engaged in corrupt, fraudulent, collusive, coercive, or obstructive practices in competing for the contract in question;

c. In addition to the legal remedies set out in the relevant Legal Agreement, may take other appropriate actions, including declaring mis-procurement, if the Bank determines at any time that representatives of the Borrower or of a recipient of any part of the proceeds of the loan engaged in corrupt, fraudulent, collusive, coercive, or obstructive practices during the procurement process, selection and/or execution of the contract in question, without the Borrower having taken timely and appropriate action satisfactory to the Bank to address such practices when they occur, including by failing to inform the Bank in a timely manner at the time they knew of the practices;

d. Pursuant to the Bank's Anti- Corruption Guidelines and in accordance with the Bank's prevailing sanctions policies and procedures, may sanction a firm or individual, either indefinitely or for a stated period of time, including by publicly declaring such firm or individual ineligible (i) to be awarded or otherwise benefit from a Bank-financed contract, financially or in any other manner;1 (ii) to be a nominated2 sub-contractor, consultant, manufacturer or supplier, or service provider of an otherwise eligible firm being awarded a Bank-financed contract; and (iii) to receive the proceeds of any loan made by the Bank or otherwise to participate further in the preparation or implementation of any Bank-financed project;

e. Requires that a clause be included in bidding/request for proposals documents and in contracts financed by a Bank loan, requiring (i) bidders(applicants/proposers), consultants, contractors, and suppliers, and their sub-contractors, sub-consultants, service providers, suppliers, agents personnel, permit the Bank to inspect[3] all accounts, records and other documents relating to the procurement process, selection and/or contract execution, and to have them audited by auditors appointed by the Bank.

PROVISIONAL

1 For the avoidance of doubt, a sanctioned party's ineligibility to be awarded a contract shall include, without limitation, (i) applying for pre-qualification, expressing interest in a consultancy, and bidding, either directly or as a nominated sub-contractor, nominated consultant, nominated manufacturer or supplier, or nominated service provider, in respect of such contract, and (ii) entering into an addendum or amendment introducing a material modification to any existing contract.

2 A nominated sub-contractor, nominated consultant, nominated manufacturer or supplier, or nominated service provider (different names are used depending on the particular bidding document) is one which has been: (i) included by the bidder in its pre-qualification application or bid because it brings specific and critical experience and know-how that allow the bidder to meet the qualification requirements for the particular bid; or (ii) appointed by the Borrower.

3 Inspections in this context usually are investigative (i.e., forensic) in nature. They involve fact-finding activities undertaken by the Bank or persons appointed by the Bank to address specific matters related to investigations/audits, such as evaluating the veracity of an allegation of possible Fraud and Corruption, through the appropriate mechanisms. Such activity includes but is not limited to: accessing and examining a firm's or individual's financial records and information, and making copies thereof as relevant; accessing and examining any other documents, data and information (whether in hard copy or electronic format) deemed relevant for the investigation/audit, and making copies thereof as relevant; interviewing staff and other relevant individuals; performing physical inspections and site visits; and obtaining third party verification of information.

APPENDIX B

Environmental, Social, Health and Safety (ESHS) Metrics for Progress Reports

[Note to Employer: the following metrics may be amended to reflect the Employer's environmental, social, health and safety policies and/or the ESHS requirements of the project. The metrics that are required should be determined by the ESHS risks of the Works and not necessarily by the scale of the Works]

Metrics for regular reporting:

a. environmental incidents or non-compliances with contract requirements, including contamination, pollution or damage to ground or water supplies;

b. health and safety incidents, accidents, injuries and all fatalities that require treatment;

c. interactions with regulators: identify agency, dates, subjects, outcomes (report the negative if none);

d. status of all permits and agreements:

i. work permits: number required, number received, actions taken for those not received;

ii. status of permits and consents:

iii. list areas/facilities with permits required (quarries, asphalt & batch plants), dates of application, dates issued (actions to follow up if not issued), dates submitted to resident engineer (or equivalent), status of area (waiting for permits, working, abandoned without reclamation, decommissioning plan being implemented, etc.);

- *list areas with landowner agreements required (borrow and spoil areas, camp sites), dates of agreements, dates submitted to resident engineer (or equivalent);*
- *identify major activities undertaken in each area in the reporting period and highlights of environmental and social protection (land clearing, boundary marking, topsoil salvage, traffic management, decommissioning planning, decommissioning implementation);*
- *for quarries: status of relocation and compensation (completed, or details of activities and current status in the reporting period).*

e. health and safety supervision:

PBWSP

i. safety officer: number days worked, number of full inspections & partial inspections, reports to construction/project management;

ii. number of workers, work hours, metric of PPE use (percentage of workers with full personal protection equipment (PPE), partial, etc.), worker violations observed (by type of violation, PPE or otherwise), warnings given, repeat warnings given, follow-up actions taken (if any);

f. worker accommodations:

i. number of expats housed in accommodations, number of locals;

ii. date of last inspection, and highlights of inspection including status of accommodations' compliance with national and local law and good practice, including sanitation, space, etc.;

iii. actions taken to recommend/require improved conditions, or to improve conditions.

g. HIV/AIDS: provider of health services, information and/or training, location of clinic, number of non-safety disease or illness treatments and diagnoses (no names to be provided);

h. gender (for expats and locals separately): number of female workers, percentage of workforce, gender issues raised and dealt with (cross-reference grievances or other sections as needed);

i. training:

i. number of new workers, number receiving induction training, dates of induction training;

ii. number and dates of toolbox talks, number of workers receiving Occupational Health and Safety (OHS), environmental and social training;

iii. number and dates of HIV/AIDS sensitization and/or training, no. workers receiving training (this reporting period and in the past); same questions for gender sensitization, flag person training.

iv. number and date of GBV /SEA sensitization and/or training, number of workers receiving training on code of conduct (in the reporting period and in the past), etc.

j. environmental and social supervision:

i. environmentalist: days worked, areas inspected and numbers of inspections of each (road section, work camp, accommodations, quarries, borrow areas, spoil areas, swamps, forest crossings, etc.), highlights of activities/findings (including violations of environmental and/or social best practices, actions taken), reports to environmental and/or social specialist/construction/site management;

PRSWSP

ii. sociologist: days worked, number of partial and full site inspections (by area: road section, work camp, accommodations, quarries, borrow areas, spoil areas, clinic, HIV/AIDS center, community centers, etc.), highlights of activities (including violations of environmental and/or social requirements observed, actions taken), reports to environmental and/or social specialist/construction/site management; and

iii. community liaison person(s): days worked (hours community center open), number of people met, highlights of activities (issues raised, etc.), reports to environmental and/or social specialist /construction/site management.

k. *Grievances*: list new grievances (e.g. allegations of GBV / SEA) received in the reporting period and unresolved past grievances by date received, complainant, how received, to whom referred to for action, resolution and date (if completed), data resolution reported to complainant, any required follow-up(Cross-reference other sections as needed):

i. Worker grievances;

ii. Community grievances

l. Traffic and vehicles/equipment:

i. traffic accidents involving project vehicles & equipment: provide date, location, damage, cause, follow-up;

ii. accidents involving non-project vehicles or property (also reported under immediate metrics): provide date, location, damage, cause, follow-up;

iii. overall condition of vehicles/equipment (subjective judgment by environmentalist); non-routine repairs and maintenance needed to improve safety and/or environmental performance (to control smoke, etc.).

m. Environmental mitigations and issues (what has been done):

i. dust: number of working bowsers, number of waterings/day, number of complaints, warnings given by environmentalist, actions taken to resolve; highlights of quarry dust control (covers, sprays, operational status); % of rock/spoil lorries with covers, actions taken for uncovered vehicles;

ii. erosion control: controls implemented by location, status of water crossings, environmentalist inspections and results, actions taken to resolve issues, emergency repairs needed to control erosion/sedimentation;

iii. quarries, borrow areas, spoil areas, asphalt plants, batch plants: identify major activities undertaken in the reporting period at each, and highlights of environmental and social protection: land clearing, boundary marking, topsoil salvage, traffic management, decommissioning planning, decommissioning implementation;

RSVSP

iv. blasting: number of blasts (and locations), status of implementation of blasting plan (including notices, evacuations, etc.), incidents of off-site damage or complaints (cross-reference other sections as needed);

v. spill cleanups, if any: material spilled, location, amount, actions taken, material disposal (report all spills that result in water or soil contamination;

vi. waste management: types and quantities generated and managed, including amount taken offsite (and by whom) or reused/recycled/disposed on-site;

vii. details of tree plantings and other mitigations required undertaken in the reporting period;

viii. details of water and swamp protection mitigations required undertaken in the reporting period.

n. compliance:

i. compliance status for conditions of all relevant consents/permits, for the Work, including quarries, etc.): statement of compliance or listing of issues and actions taken (or to be taken) to reach compliance;

ii. compliance status of C-ESMP/ESIP requirements: statement of compliance or listing of issues and actions taken (or to be taken) to reach compliance

iii. compliance status of GBV/SEA prevention and response action plan: statement of compliance or listing of issues and actions taken (or to be taken) to reach compliance

iv. compliance status of Health and Safety Management Plan re: statement of compliance or listing of issues and actions taken (or to be taken) to reach compliance

v. other unresolved issues from previous reporting periods related to environmental and social: continued violations, continued failure of equipment, continued lack of vehicle covers, spills not dealt with, continued compensation or blasting issues, etc. Cross-referene other sections as needed.

PRSWSP

Section IX -Particular Conditions of Contract

A. General	
GCC 1.1 (d)	The financing institution is: World Bank/IBRD
GCC 1.1 (r)	The Employer is: **Punjab Rural Municipal Services Company (PRMSC)** Address: Punjab Rural Municipal Services Company (PRMSC) 5th Floor, KD Plaza, MM Alam Road, Gulberg-III, Lahore, Pakistan Telephone: +92-42-99333613 Electronic mail address: proc.prmsc@punjab.gov.pk Chief Executive Officer / Project Director
GCC 1.1 (v)	The Intended Completion Date for the whole of the Works shall be 14 months.
GCC 1.1 (y)	The Project Manager is Chief Resident Engineer (CRE) or any other official nominated by the Engineering Design and Construction Supervision (EDCS) Consultant (the Consultant hired by the Employer) and approved by the Employer
GCC 1.1 (aa)	The Site is located at _____ and is defined in drawings No. *[insert numbers]*
GCC 1.1 (dd)	The Start Date shall be_____*[date to be inserted at the time of signing of the Contract, maximum 14 days beyond date of signing of the Contract]*.
GCC 1.1 (hh)	The Works are described in Section VII –"Works' Requirements"
GCC 1.1 (ii)	The following is added as GCC 1.1. (ii) "ESHS" means environmental, social (including sexual exploitation and abuse (SEA) and gender-based violence (GBV)), health and safety.
GCC 2.2	Sectional Completions are: Not Applicable
GCC 2.3(i)	The following documents also form part of the Contract: (i) the ESHS Management Strategies and Implementation Plans; and

PRWSP

	(ii) Code of Conduct (ESHS).
GCC 3.1	The language of the Contract is English. The law that applies to the Contract is the law of Islamic Republic of Pakistan.
GCC 4.1	With reference to Sub-Clause 4.1, the following provisions shall also apply; The Project Manager shall obtain the specific approval of the Employer before carrying out his duties in accordance with the following Clauses/Sub-Clauses: a) Any action regarding sub-letting of any part of the Works under Sub-Clause 7.1 "Subcontracting". b) Approving Key Personnel under Sub-Clause 9.1 "Personnel and Equipment". c) Any action under Clause 27 regarding "Extension of the Intended Completion Date" and "additional cost". d) Issuing a Variation Order under Clause 38 "Variations". e) Release of Retention Money to the Contractor under Sub-Clause 46.2 "Retention". f) Issuance of "Certificate of Completion" under Clause 53 "Completion". g) Issuing "Defect Liability Certificate" and "final payment certificate" under Clause 55 "Final Account". h) The amount to be withheld for late submission of an updated Program
GCC 5.1	The Project manager may delegate any of his duties and responsibilities.
GCC 8.1	Schedule of other contractors: Not Applicable
GCC 9.1	The names of other Key Personnel and equipment shall be mutually agreed prior to signing of the Contract Agreement.
GCC 9.2	**Code of Conduct (ESHS)** The following is inserted at the end of GCC 9.2: "The reasons to remove a person include behavior which breaches the Code of Conduct (ESHS) (e.g. spreading communicable diseases, sexual harassment, gender based violence (GBV), sexual exploitation or abuse, illicit activity or crime)."
GCC 13.1	The minimum insurance amounts and deductibles shall be: (a) for loss or damage to the Works, Plant and Materials: to the full replacement value plus additional amount of fifteen percent (15%) of such

PRSMSP

	replacement value to cover any additional costs incidental to rectification of loss or damage, including professional fees and the cost of demolition and removal of debris. The permitted deductible shall not exceed 10% of loss amount on each & every loss. (b) For loss or damage to Equipment: to the full replacement value including delivery to the Site. (c) for loss or damage to property (except the Works, Plant, Materials, and Equipment) in connection with Contract: to the full value of loss or damage. (d) for personnel injury or death: (at least PKR 0.5 million for bodily injury (any one person) and at least 1 million for fatal case (any one person) (i) of the Contractor's employees: as per statutory requirements of the Islamic Republic of Pakistan. (ii) of other people: as per statutory requirements of the Islamic Republic of Pakistan. The permitted deductible(s) are 'Nil' for para (b), (c) and (d).
GCC 14.1	Site Data are: as per Section VII - Works' Requirements.
GCC 16.1 (add new 16.2)	**ESHS Management Strategies and Implementation Plans** The following is inserted as a new Sub-Clause 16.2: " **16.2** The Contractor shall not carry out any Works, including mobilization and/or pre-construction activities (e.g. limited clearance for haul roads, site accesses and work site establishment, geotechnical investigations or investigations to select ancillary features such as quarries and borrow pits), unless the Project Manager is satisfied that appropriate measures are in place to address environmental, social, health and safety risks and impacts. At a minimum, the Contractor shall apply the Management Strategies and Implementation Plans and Code of Conduct, submitted as part of the Bid and agreed as part of the Contract. The Contractor shall submit, on a continuing basis, for the Project Manager's prior approval, such supplementary Management Strategies and Implementation Plans as are necessary to manage the ESHS risks and impacts of ongoing works. These Management Strategies and Implementation Plans collectively comprise the Contractor's Environmental and Social Management Plan (C-ESMP). The C-ESMP shall be approved prior to the commencement of construction activities (e.g. excavation, earth works, bridge and structure works, stream and road diversions, quarrying or extraction of materials, concrete batching and asphalt manufacture). The approved C-ESMP shall be reviewed, periodically (but not less than every six (6) months), and updated in a timely manner, as required, by the Contractor to

PPWSP

	ensure that it contains measures appropriate to the Works activities to be undertaken. The updated C-ESMP shall be subject to prior approval by the Project Manager."
GCC 20.1	The text of Sub-Clause 20.1 is replaced as under: "The Employer shall give the Contractor possession of those parts of the Site within such times as may be required to enable the Contractor to proceed in accordance with the Program."
GCC 23.1 & GCC 23.2	Appointing Authority for the Adjudicator: Chairman Pakistan Engineering Council
GCC 24.3	Hourly rate and types of reimbursable expenses to be paid to the Adjudicator shall be mutually agreed at the time of finalization of the Adjudicator in accordance with GCC 23.1.
GCC 24.4	Any dispute arising out of or in connection with this Contract, including any question regarding its existence, validity, or termination shall be referred to and finally resolved by arbitration under the Rules and Provisions of the Pakistan Arbitration Act 1940 amended from time to time. The place of arbitration shall be: Lahore
B. Time Control	
GCC 26.1	The Contractor shall submit for approval a Program for the Works within fourteen (14) days from the date of the Letter of Acceptance to the Project Manager showing the general methods, arrangements, order, and timing for all the activities in the Works in the form of using project management tools like MS project, Primavera or equal etc.
GCC 26.2	**ESHS Reporting** Inserted at the end of GCC 26.2: "In addition to the progress report, the Contractor shall also provide a report on the Environmental, Social, Health and Safety (ESHS) metrics set out in Appendix B. In addition to Appendix B reports, the Contractor shall also provide immediate notification to the Project Manager of incidents in the following categories. Full details of such incidents shall be provided to the Project Manager within the timeframe agreed with the Project Manager. (a) confirmed or likely violation of any law or international agreement; (b) any fatality or serious (lost time) injury; (c) significant adverse effects or damage to private property (e.g. vehicle accident, damage from fly rock, working beyond the boundary)

PRSWSP

	(d) major pollution of drinking water aquifer or damage or destruction of rare or endangered habitat (including protected areas) or species; or (e) any allegation of gender-based violence (GBV), sexual exploitation or abuse, sexual harassment or sexual misbehavior, rape, sexual assault, child abuse or defilement, or other violations involving children.
GCC 26.3	The period between Program updates is fourteen (14) days. The amount to be withheld for late submission of an updated Program is PKR 500,000.
C. Quality Control	
GCC 34.1	The Defects Liability Period is: three hundred and sixty-five (365) days after issuance of Certificate of Completion.
D. Cost Control	
GCC 38.2	At the end of 38.2 add after the first sentence: "The Contractor shall also provide information of any ESHS risks and impacts of the Variation."
GCC 38.7	Not Applicable
GCC 40 (Add new GCC 40.7)	The following is inserted as a new Sub-Clause 40.7: "**40.7** If the Contractor was, or is, failing to perform any ESHS obligations "or work under the Contract, the value of this work or obligation, as determined by the Project Manager, may be withheld until the work or obligation has been performed, and/or the cost of rectification or replacement, as determined by the Project Manager, may be withheld until rectification or replacement has been completed. Failure to perform includes, but is not limited to the following: (i) failure to comply with any ESHS obligations or work described in the Works' Requirements which may include: working outside site boundaries, excessive dust, failure to keep public roads in a safe usable condition, damage to offsite vegetation, pollution of water courses from oils or sedimentation, contamination of land e.g. from oils, human waste, damage to archeology or cultural heritage features, air pollution as a result of unauthorized and/or inefficient combustion; (ii) failure to regularly review C-ESMP and/or update it in a timely manner to address emerging ESHS issues, or anticipated risks or impacts;

PPWSP

	(iii) failure to implement the C-ESMP e.g. failure to provide required training or sensitization; (iv) failing to have appropriate consents/permits prior to undertaking Works or related activities; (v) failure to submit ESHS report/s (as described in Appendix C), or failure to submit such reports in a timely manner; (vi) failure to implement remediation as instructed by the Engineer within the specified timeframe (e.g. remediation addressing non-compliance/s).
GCC 41.1	The 3rd and 4th sentences comprising text "If the Employer makes a late payment, …….the currencies in which payments are made." are deleted.
GCC 44.1	The currency of the Employer's Country is: Pak. Rupees (PKR)
GCC 45.1	The text of Sub-Clause GCC 45.1 is replaced as under: Prices of Civil Works shall be adjusted for fluctuations in the cost of labour and material inputs only. The amounts certified in each payment certificate, before deducting for Advance Payment, shall be adjusted by applying the following price adjustment factor to the due payment amounts. To the extent that full compensation for any rise or fall in Costs is not covered by the provisions of this or other Clauses, the Accepted Contract Amount shall be deemed to have included amounts to cover the contingency of other rises and falls in costs. $P_n = a + b\frac{L_n}{L_0} + c\frac{E_n}{E_0} + d\frac{M_n}{M_0} + \ldots\ldots\ldots\ldots\ldots\ldots$ where: "P_n" is the adjustment factor for the portion of the Contract Price for Civil Works carried out in period "n", this period being a month; "a" is a fixed coefficient, stated in the Schedule of Adjustment Data, representing the non-adjustable portion in contractual payments; "b", "c", "d", ... are coefficients representing the estimated proportion of each cost element related to the execution of the Civil Works as stated in the Schedule of Adjustment Data; "L_n", "E_n", "M_n", ... are the current rates for period "n", each of which is applicable to the relevant tabulated cost element; and "L_o", "E_o", "M_o", ... are the base rates, each of which is applicable to the relevant tabulated cost elements for the month falling on the date thirty (30) days prior to the deadline for submission of Bids. The following conditions shall apply to the price adjustment(s):

PPSWSP

	a. No price increase will be allowed beyond the Intended Completion Date unless extended by the Project Manager under the terms of the Contract. No price increase will be allowed for periods of delay for which the Contractor is responsible. The Employer will, however, be entitled to any price decrease occurring during such periods of delay. b. No price adjustment shall be payable on the portion of the Contract price paid to the Contractor as an advance payment. c. No price adjustment shall be payable for any fluctuation in the rates of elements other than those given in Schedule of Adjustment Data.
GCC 46.1	The proportion of payments retained is: 10% of Interim Payment Certificate and ceiling amount shall be 5% of the Accepted Contract Amount.
GCC 47.1	The liquidated damages for the whole of the Works are 0.10% of the final Contract Price per day. The maximum amount of liquidated damages for the whole of the Works is 10% of the Accepted Contract Price.
GCC 48.1	Not Applicable
GCC 49.1	The Advance Payment shall be 15% of the Accepted Contract Amount and shall be paid to the Contractor within 28 days after: a) receipt of an acceptable Performance Security by the Employer in accordance with Sub-Clause COC50.1; b) signing of Contract Agreement by the Parties; c) receipt of an acceptable bank guarantee by the Employer for the same amount and currency of the advance payment from a Scheduled Bank in Pakistan, in the prescribed form; and d) receipt of Contractor's invoice for advance payment by the Employer.
GCC 49.1 (added)	The following shall stand inserted/added in the clause: a) **"Secure Advance Payment"**: The Contractor shall be entitled to receive from the Employer Secure Advance in the case of non-perishable materials required, namely; (i) **Steel, HDPE Pipe, RCC Pipe**, @ **50%** of the total material required with an amount not exceeding seventy five percent (**75%**) of the monetary value of the materials, as per BOQ, and (ii) in case of **pumping unit** @ **75%** of cost as per BOQ, that shall be for bonafide use of Work, when those are delivered at respective site upon assessment, verification and certification by the Engineer/Project Manager. Following shall be the conditions precedent:

PROVISIONAL

	b) For the provision of Secure Advance, the Contractor can bring **maximum 50%** of the total required material mentioned in Bill of Quantities (BOQs) to the site, c) The non-perishable materials delivered to the site must "appear to be in accordance with the Specifications for the Permanent Works defined in the Contract", d) Upon inspection, verification, necessary testing where required, certification and satisfactory acceptance by the Engineer/Project Manager, the non-perishable materials shall become the Employer's property, e) The requirement of plant and materials shall be for near use in the Work, nonperishable, nonfragile, and noncombustible, f) The non-perishable materials shall be hypothecated to the Employer by the Contractor and the Contractor shall submit corresponding invoice for advance payment to the Employer through Engineer/Project Manager, g) The Materials shipped and en-route to the Site shall be insured by the Contractor. The Contractor shall be exclusively responsible for safe delivery of the Material at site covering all the related risks. In case of any damage to the Materials till the delivery at site and before their usage in Permanent Works, the Contractor shall manage the replacement of material at its own cost & expenses without any liability towards the Employer, h) The Contractor shall ensure and guarantee Materials, delivered at site are properly stored on Site, protected against loss, theft, damage or deterioration to the satisfaction of the Engineer/Project Manager, at the risk and cost of the Contractor, until their use in Permanent Works is accepted by the Employer, i) In case the Contractor does not replace or compensate the damaged shipment of Material (including items/quantities) that are damaged during their storage at site before their use in Permanent Works, the Employer shall confiscate/recover the corresponding value of the Material from the next Interim Payment (IPC), appropriately determined by the Employer, without any notice to the Contractor, j) The Contractor shall notify the Employer/Engineer of the Materials shipped and en-route to the Site and mail the following documents to the Employer/Engineer: i. one original plus four copies of the Contractor's invoice showing Materials' description, quantity, unit price, and total amount,

PPWSP

	ii. delivery note, railway receipt, or truck receipt, iii. detailed description of Materials, packing details, weight, dimension and volume of consignment be provided, k) The Contractor's records of the requirements, orders, receipts and use of materials must be kept in a form approved by the Engineer, and such records shall be available for inspection by the Engineer/Project Manager, l) The Contractor shall submit with his monthly statement the estimated value of the materials delivered on Site together with such documents as may be required by the Engineer/Project Manager for the purpose of valuation of materials and providing evidence of ownership and adjustment/payment therefor, m)The Engineer/Project Manager shall assess the value of delivered Materials and accord a certificate for its use at site, n) **The escalation/price adjustment shall not be applied to payments for materials brought onto Site for which a secure advance has been paid.** Only the value of the executed works shall be included in the formula governing Price Adjustment under Clause 45 viz. Price Adjustment which shall be applied to the value of the executed works for the relevant month (which will include the cost of the incorporated plant and materials but not the stockpiled plant and materials); o) The Material so brought on site, shall neither be allowed to be shifted from the site nor disposed of, and the Employer and/or its Engineer/Project Manager shall keep an eye on the delivered Material ensuring that dual advance is not given on same Material. p) The Secure Advance paid to the Contractor under the above provisions shall be adjusted from the monthly payments on actual consumption basis of respective material, duly certified by the Engineer/Project Manager. q) Secure **Advance shall only be grated, at risk and cost of the Contractor, against an indemnity bond** acceptable to the employer, specifying that materials have been delivered at the site and have properly been stored and protected against any loss or damage or deterioration up to the satisfaction of the Engineer.
GCC 49.3	The text of sub-clause 49.3 is replaced as under: "Advance payment shall be recovered in equal installation over the remaining contract period after three months from the date of receipt of mobilization advance."

PPWSP

GCC 50.1	An Environmental, Social, Safety and Health (ESHS) Performance Security shall not be provided to the Employer.
GCC 50.1	The Performance Security shall be in the form of an unconditional and irrevocable Bank Guarantee issued by a Scheduled Bank in Pakistan in the amount of five percent (05%) of the Accepted Contract Amount and in the same currency of the Accepted Contract Amount. However, additional performance security is required, in case of abnormally low bids. In case of Joint Venture, the Performance Security shall be in the name of the Joint Venture.
E. Finishing the Contract	
GCC 56.1	The Contractor shall furnish to the Project Manager "As-Built drawings and Operation & Maintenance manuals" at the completion of whole of the Works under the Contract as per GCC Sub-Clause 53.1.
GCC 56.2	The amount to be withheld for failing to produce "As-Built drawings and Operation & Maintenance manuals" by the time required in GCC 56.1 is PKR 2.00 million.
GCC 57.2 (g)	The maximum number of days is: one hundred (100)
GCC 58.1	The percentage to apply to the value of the work not completed, representing the Employer's additional cost for completing the Works, is 35%.

PRSWSDP

Section X - Contract Forms

Table of Forms

Notification of Intention to Award **142**

Letter of Acceptance **148**

Contract Agreement **149**

Performance Security- Bank Guarantee **151**

Advance Payment Security **153**

PRSWSSP

Notification of Intention to Award

[*This Notification of Intention to Award shall be sent to each Bidder that submitted a Bid.*]

[*Send this Notification to the Bidder's Authorized Representative named in the Bidder Information Form*]
For the attention of Bidder's Authorized Representative
Name: *[insert Authorized Representative's name]*
Address: *[insert Authorized Representative's Address]*
Telephone/Fax numbers: *[insert Authorized Representative's telephone/fax numbers]*
Email Address: *[insert Authorized Representative's email address]*

[IMPORTANT: insert the date that this Notification is transmitted to Bidders. The Notification must be sent to all Bidders simultaneously. This means on the same date and as close to the same time as possible.]
DATE OF TRANSMISSION: This Notification is sent by: [*email/fax*] on [*date*] (local time)

Notification of Intention to Award

Employer: *[insert the name of the Employer]*
Project:*[insert name of project]*
Contract title: *[insert the name of the contract]*
Country: *[insert country where RFB is issued]*
Loan No. /Credit No. / Grant No.: *[insert reference number for loan/credit/grant]*
RFB No: *[insert RFB reference number from Procurement Plan]*

This Notification of Intention to Award (Notification) notifies you of our decision to award the above contract after which, you may:

a) request a debriefing in relation to the evaluation of your Bid, and/or

b) submit a Procurement-related Complaint in relation to the decision to award the contract.

1. The successful Bidder

Name:	[*insert name of successful Bidder*]
Address:	[*insert address of the successful Bidder*]
Contract price:	[*insert contract price of the successful Bid*]

PROVISO

2. Other Bidders ***[INSTRUCTIONS: insert names of all Bidders that submitted a Bid. If the Bid's price was evaluated include the evaluated price as well as the Bid price as read out.]***

Name of Bidder	Bid price	Evaluated Bid price (if applicable)
[*insert name*]	[*insert Bid price*]	[*insert evaluated price*]
[*insert name*]	[*insert Bid price*]	[*insert evaluated price*]
[*insert name*]	[*insert Bid price*]	[*insert evaluated price*]
[*insert name*]	[*insert Bid price*]	[*insert evaluated price*]
[*insert name*]	[*insert Bid price*]	[*insert evaluated price*]

3. Reason/s why your Bid was unsuccessful

[INSTRUCTIONS: State the reason/s why <u>this</u> Bidder's Bid was unsuccessful. Do NOT include: (a) a point-by-point comparison with another Bidder's Bid or (b) information that is marked confidential by the Bidder in its Bid.]

4. How to request a debriefing

DEADLINE: The deadline to request a debriefing expires at midnight on [*insert date*] (local time).

You may request a debriefing in relation to the results of the evaluation of your Bid. If you decide to request a debriefing your written request must be made within three (3) Business Days of receipt of this Notification of Intention to Award.

Provide the contract name, reference number, name of the Bidder, contact details; and address the request for debriefing as follows:

Attention: [*insert full name of person, if applicable*]

Title/position: [*insert title/position*]

Agency: [*insert name of Employer*]

Email address: [*insert email address*]

Fax number: [*insert fax number*] ***delete if not used***

If your request for a debriefing is received within the 3 Business Days deadline, we will provide the debriefing within five (5) Business Days of receipt of your request.

The debriefing may be in writing, by phone, video conference call or in person. We shall promptly advise you in writing how the debriefing will take place and confirm the date and time.

PBWSP

If the deadline to request a debriefing has expired, you may still request a debriefing. In this case, we will provide the debriefing as soon as practicable, and normally no later than fifteen (15) Business Days from the date of publication of the Contract Award Notice.

5. How to make a complaint

Period: Procurement-related Complaint challenging the decision to award shall be submitted by midnight, [*insert date*] (local time).

Provide the contract name, reference number, name of the Bidder, contact details; and address the Procurement-related Complaint as follows:

Attention: [*insert full name of person, if applicable*]

Title/position: [*insert title/position*]

Agency: [*insert name of Employer*]

Email address: [*insert email address*]

Fax number: [*insert fax number*] ***delete if not used***

At this point in the procurement process, you may submit a Procurement-related Complaint challenging the decision to award the contract. You do not need to have requested, or received, a debriefing before making this complaint. Your complaint must be submitted within the seven business days after issuance of NoIA.

Further information:

For more information see the Procurement Regulations for IPF Borrowers (Procurement Regulations)[https://policies.worldbank.org/sites/ppf3/PPFDocuments/Forms/DispPage.aspx?docid=4005] (Annex III). You should read these provisions before preparing and submitting your complaint. In addition, the World Bank's Guidance "How to make a Procurement-related Complaint" [http://www.worldbank.org/en/projects-operations/products-and-services/brief/procurement-new-framework#framework] provides a useful explanation of the process, as well as a sample letter of complaint.

In summary, there are four essential requirements:

1. You must be an 'interested party'. In this case, that means a Bidder who submitted a Bid in this bidding process, and is the recipient of a Notification of Intention to Award.
2. The complaint can only challenge the decision to award the contract.
3. You must submit the complaint within the period stated above.
4. You must include, in your complaint, all of the information required by the Procurement Regulations (as described in Annex III).

If you have any questions regarding this Notification, please do not hesitate to contact us.

On behalf of the Employer:

PPSSP

Signature: _____

Name: _____

Title/position: _____

Telephone: _____

Email: _____

PRSWSSP

Beneficial Ownership Disclosure Form

INSTRUCTIONS TO BIDDERS: DELETE THIS BOX ONCE YOU HAVE COMPLETED THE FORM

This Beneficial Ownership Disclosure Form ("Form") is to be completed by the successful Bidder[1]. In case of joint venture, the Bidder must submit a separate Form for each member. The beneficial ownership information to be submitted in this Form shall be current as of the date of its submission.

For the purposes of this Form, a Beneficial Owner of a Bidder is any natural person who ultimately owns or controls the Bidder by meeting one or more of the following conditions:

- *directly or indirectly holding 25% or more of the shares*
- *directly or indirectly holding 25% or more of the voting rights*
- *directly or indirectly having the right to appoint a majority of the board of directors or equivalent governing body of the Bidder*

RFB No.: [*insert number of RFB process*]
Request for Bid No.: [*insert identification*]

To: **[*insert complete name of Employer*]**

In response to your request in the Letter of Acceptance *dated [insert date of letter of Acceptance]* to furnish additional information on beneficial ownership: *[select one option as applicable and delete the options that are not applicable]*

(i) we hereby provide the following beneficial ownership information.

Details of beneficial ownership

Identity of Beneficial Owner	Directly or indirectly holding 25% or more of the shares (Yes / No)	Directly or indirectly holding 25 % or more of the Voting Rights (Yes / No)	Directly or indirectly having the right to appoint a majority of the board of the directors or an equivalent governing body of the Bidder (Yes / No)
[include full name (last, middle, first),			

nationality, country of residence]			

OR

(ii) *We declare that there is no Beneficial Owner meeting one or more of the following conditions:*

- directly or indirectly holding 25% or more of the shares
- directly or indirectly holding 25% or more of the voting rights
- directly or indirectly having the right to appoint a majority of the board of directors or equivalent governing body of the Bidder

OR

(iii) We declare that we are unable to identify any Beneficial Owner meeting one or more of the following conditions. [If this option is selected, the Bidder shall provide explanation on why it is unable to identify any Beneficial Owner]

- directly or indirectly holding 25% or more of the shares
- directly or indirectly holding 25% or more of the voting rights
- directly or indirectly having the right to appoint a majority of the board of directors or equivalent governing body of the Bidder]"

Name of the Bidder:*[*insert complete name of the Bidder*]_____

Name of the person duly authorized to sign the Bid on behalf of the Bidder:**[*insert complete name of person duly authorized to sign the Bid*]_____

Title of the person signing the Bid: [*insert complete title of the person signing the Bid*]_____

Signature of the person named above: [*insert signature of person whose name and capacity are shown above*]_____

Date signed [*insert date of signing*] **day of** [*insert month*], [*insert year*]____

* In the case of the Bid submitted by a Joint Venture specify the name of the Joint Venture as Bidder. In the event that the Bidder is a joint venture, each reference to "Bidder" in the Beneficial Ownership Disclosure Form (including this Introduction thereto) shall be read to refer to the joint venture member.

** Person signing the Bid shall have the power of attorney given by the Bidder. The power of attorney shall be attached with the Bid Schedules.

PBWSP

Letter of Acceptance

[on letterhead paper of the Employer***]***

. . . . . ***[date]***. . . . . .

To: . . . . . ***.[name and address of the Contractor]*** . . . . . .

Subject: . . . . . ***.[Notification of Award Contract No]***. . . . . .

This is to notify you that your Bid dated . . . ***.[insert date]*** . . . . for execution of the . . . . . ***. . . .[insert name of the contract and identification number, as given in the PCC]***. . . . . for the Accepted Contract Amount of . . . . . ***.[insertamount in numbers and words and name of currency],*** as corrected and modified in accordance with the Instructions to Bidders is hereby accepted by our Agency.

You are requested to furnish (i) the Performance Security and an Environmental, Social, Health and Safety Performance Security ***[Delete ESHS Performance Security if it is not required under the contract]***within 28 days in accordance with the Conditions of Contract, using for that purpose the of the Performance Security Form and the ESHS Performance Security Form, ***[Delete reference to the ESHS Performance Security Form if it is not required under the contract]***and (ii)the additional information on beneficial ownership in accordance with BDSITB 47.1, within eight (8) Business days using the Beneficial Ownership Disclosure Form, included in Section X -Contract Forms, of the bidding document.
[Choose one of the following statements:]

We accept that _____***[insert the name of Adjudicator proposed by the Bidder]*** be appointed as the Adjudicator.

[or]

We do not accept that _____***[insert the name of the Adjudicator proposed by the Bidder]*** be appointed as the Adjudicator, and by sending a copy of this Letter of Acceptance to _____***[insert name of the Appointing Authority],*** the Appointing Authority, we are hereby requesting such Authority to appoint the Adjudicator in accordance with ITB48.1 and GCC23.1.

Authorized Signature: .....

Name and Title of Signatory: .....

Name of Agency: .....

Attachment: Contract Agreement

Contract Agreement

THIS AGREEMENT made the . . . . . .day of . . . . . ., ..., between . . . . . ***[name of the*** Employer***]***. . . . . (hereinafter "the Employer"), of the one part, and . . . . . ***[name of the Contractor]***. . . . .(hereinafter "the Contractor"), of the other part:

WHEREAS the Employer desires that the Works known as . . . . .***[name of the Contract]***. . . . .should be executed by the Contractor, and has accepted a Bid by the Contractor for the execution and completion of these Works and the remedying of any defects therein,

The Employer and the Contractor agree as follows:

1. In this Agreement words and expressions shall have the same meanings as are respectively assigned to them in the Contract documents referred to.

2. The following documents shall be deemed to form and be read and construed as part of this Agreement. This Agreement shall prevail over all other Contract documents.

(a) the Letter of Acceptance

(b) the Letter of Bid

(c) the addenda Nos _____(if any)

(d) the Particular Conditions

(e) the General Conditions of Contract, including appendix;

(f) the Specification

(g) the Drawings

(h) Bill of Quantities;[4]and

(i) any other document **listed in the PCC** as forming part of the Contract;

3. In consideration of the payments to be made by the Employer to the Contractor as specified in this Agreement, the Contractor hereby covenants with the Employer to execute the Works and to remedy defects therein in conformity in all respects with the provisions of the Contract.

4. The Employer hereby covenants to pay the Contractor in consideration of the execution and completion of the Works and the remedying of defects therein, the Contract Price or such other sum as may become payable under the provisions of the Contract at the times and in the manner prescribed by the Contract.

[4] In lump sum contracts, delete "Bill of Quantities" and replace with "Activity Schedule."

PRSWSP

IN WITNESS whereof the parties hereto have caused this Agreement to be executed in accordance with the laws of . . . . . ***[name of the borrowing country]***. . . . .on the day, month and year specified above.

Signed by:	Signed by: .....
for and on behalf of the Employer	for and on behalf the Contractor
in the presence of:	in the presence of: .....
Witness, Name, Signature, Address, Date	Witness, Name, Signature, Address, Date

PRSWSSP

Performance Security- Bank Guarantee

[Guarantor letterhead or SWIFT identifier code]

Beneficiary: *[insert name and Address of* Employer*]*

Date: *_ [Insert date of issue]*

PERFORMANCE GUARANTEE No.: *[Insert guarantee reference number]*

Guarantor: *[Insert name and address of place of issue, unless indicated in the letterhead]*

We have been informed that *_ [insert name of Contractor, which in the case of a joint venture shall be the name of the joint venture]* (hereinafter called "the Applicant") has entered into Contract No. *[insert reference number of the contract]* dated *[insert date]* with the Beneficiary, for the execution of *_ [insert name of contract and brief description of* Works*]* (hereinafter called "the Contract").

Furthermore, we understand that, according to the conditions of the Contract, a performance guarantee is required.

At the request of the Applicant, we as Guarantor, hereby irrevocably undertake to pay the Beneficiary any sum or sums not exceeding in total an amount of *[insert amount in figures]* (_____) *[insert amount in words]*,[1] such sum being payable in the types and proportions of currencies in which the Contract Price is payable, upon receipt by us of the Beneficiary's complying demand supported by the Beneficiary's statement, whether in the demand itself or in a separate signed document accompanying or identifying the demand, stating that the Applicant is in breach of its obligation(s) under the Contract, without the Beneficiary needing to prove or to show grounds for your demand or the sum specified therein.

This guarantee shall expire, no later than the …. Day of ……, 2… [2], and any demand for payment under it must be received by us at this office indicated above on or before that date.

This guarantee is subject to the Uniform Rules for Demand Guarantees (URDG) 2010 Revision, ICC Publication No. 758, except that the supporting statement under Article 15(a)

---

[1] *The Guarantor shall insert an amount representing the percentage of the Accepted Contract Amount specified in the Letter of Acceptance, less provisional sums, if any, and denominated either in the currency(ies) of the Contract or a freely convertible currency acceptable to the Beneficiary.*

[2] *Insert the date twenty-eight days after the expected completion date as described in GC Clause 53.1. The Employer should note that in the event of an extension of this date for completion of the Contract, the Employer would need to request an extension of this guarantee from the Guarantor. Such request must be in writing and must be made prior to the expiration date established in the guarantee. In preparing this guarantee, the Employer might consider adding the following text to the form, at the end of the penultimate paragraph: "The Guarantor agrees to a one-time extension of this guarantee for a period not to exceed [six months] [one year], in response to the Beneficiary's written request for such extension, such request to be presented to the Guarantor before the expiry of the guarantee."*

is hereby excluded.

_____

[signature(s)]

Note: All italicized text (including footnotes) is for use in preparing this form and shall be deleted from the final product.

PRSWSSP

Advance Payment Security

Bank Guarantee

[Guarantor letterhead or SWIFT identifier code]

Beneficiary: *[Insert name and Address of* Employer*]*

Date: *[Insert date of issue]*

ADVANCE PAYMENT GUARANTEE No.: *[Insert guarantee reference number]*

Guarantor: *[Insert name and address of place of issue, unless indicated in the letterhead]*

We have been informed that *[insert name of Contractor, which in the case of a joint venture shall be the name of the joint venture]* (hereinafter called "the Applicant") has entered into Contract No. *[insert reference number of the contract]* dated *[insert date]* with the Beneficiary, for the execution of *[insert name of contract and brief description of* Works*]* (hereinafter called "the Contract").

Furthermore, we understand that, according to the conditions of the Contract, an advance payment in the sum *[insert amount in figures]* () *[insert amount in words]* is to be made against an advance payment guarantee.

At the request of the Applicant, we as Guarantor, hereby irrevocably undertake to pay the Beneficiary any sum or sums not exceeding in total an amount of *[insert amount in figures]* () *[insert amount in words]*[1] upon receipt by us of the Beneficiary's complying demand supported by the Beneficiary's statement, whether in the demand itself or in a separate signed document accompanying or identifying the demand, stating either that the Applicant:

(a) has used the advance payment for purposes other than the costs of mobilization in respect of the Works; or

(b) has failed to repay the advance payment in accordance with the Contract conditions, specifying the amount which the Applicant has failed to repay.

A demand under this guarantee may be presented as from the presentation to the Guarantor of a certificate from the Beneficiary's bank stating that the advance payment referred to above

[1] *The Guarantor shall insert an amount representing the amount of the advance payment and denominated either in the currency(ies) of the advance payment as specified in the Contract, or in a freely convertible currency acceptable to the Employer.*

PBWSP

has been credited to the Applicant on its account number *[insert number]* at *[insert name and address of Applicant's bank]*.

The maximum amount of this guarantee shall be progressively reduced by the amount of the advance payment repaid by the Applicant as specified in copies of interim statements or payment certificates which shall be presented to us. This guarantee shall expire, at the latest, upon our receipt of a copy of the interim payment certificate indicating that ninety (90) percent of the Accepted Contract Amount, less provisional sums, has been certified for payment, or on the *[insert day]* day of *[insert month]*, 2 *[insert year]*,[2] whichever is earlier. Consequently, any demand for payment under this guarantee must be received by us at this office on or before that date.

This guarantee is subject to the Uniform Rules for Demand Guarantees (URDG) 2010 Revision, ICC Publication No. 758, except that the supporting statement under Article 15(a) is hereby excluded.

_____

[signature(s)]

Note: All italicized text (including footnotes) is for use in preparing this form and shall be deleted from the final product.

PRSWSP

[2] *Insert the expected expiration date of the Time for Completion. The Employer should note that in the event of an extension of the time for completion of the Contract, the Employer would need to request an extension of this guarantee from the Guarantor. Such request must be in writing and must be made prior to the expiration date established in the guarantee. In preparing this guarantee, the Employer might consider adding the following text to the form, at the end of the penultimate paragraph: "The Guarantor agrees to a one-time extension of this guarantee for a period not to exceed [six months][one year], in response to the Beneficiary's written request for such extension, such request to be presented to the Guarantor before the expiry of the guarantee."*

PRMSC
Punjab Rural Municipal Services Company

Punjab Rural Municipal Services Company (PRMSC)

"Engineering, Design &

Construction Supervision Consultant (Cluster South - III")

Detailed **Engineering** Design

BAHAWALNAGAR
[WATER SUPPLY SYSTEM]

AKKANWALI KHURD,SHER MOHD,KARTAR SINGH,KHOBER(MVS)DHARAM PURA,HIRA BASHNOAI (MVS) ALLAHABAD,AMIN ABAD,BARASAJWAR KHAN,HASAN RAIKA,JAGGA SANATTEKA,JALWALA,JANOOWALA,KHAWAJA BUX BODLA,MAHNI BEGKA,MALAK PURA,MINA SANATTEKA,MUHAMMAD ASAD KHAN,MUHSAN PURA,NOOR JAHANIAN,PARAN WALA,RAMNAGAR,SANDAR BASHNOI,SHER SINGH WALA,TOBI QAMAR-UD-DIN,

MARCH-2026

ENVIRONMENTAL TECHNOLOGIES

ASIAN CONSULTING ENGINEERS (PVT.) LTD
www.asiancon.com

Head Office:
C-3, Jhelum Block, Green Fort-II, Lahore.
Phone: +92 42 35450914-15
Fax: +92 42 35450916,
Email: arslan@asiancon.com

ACS REGISTRARS Quality Assurance ISO 9001 UKAS 229

LIST OF DRAWING

AKKANWALI KHURD,SHER MOHD,KRTAR SINGH&KHOBER(MVS)

KEY PLAN

Revenue Village: **AKANWALI KHURD & KHOBAR & KARTAR SINGH & SHER MUHAMMAD**

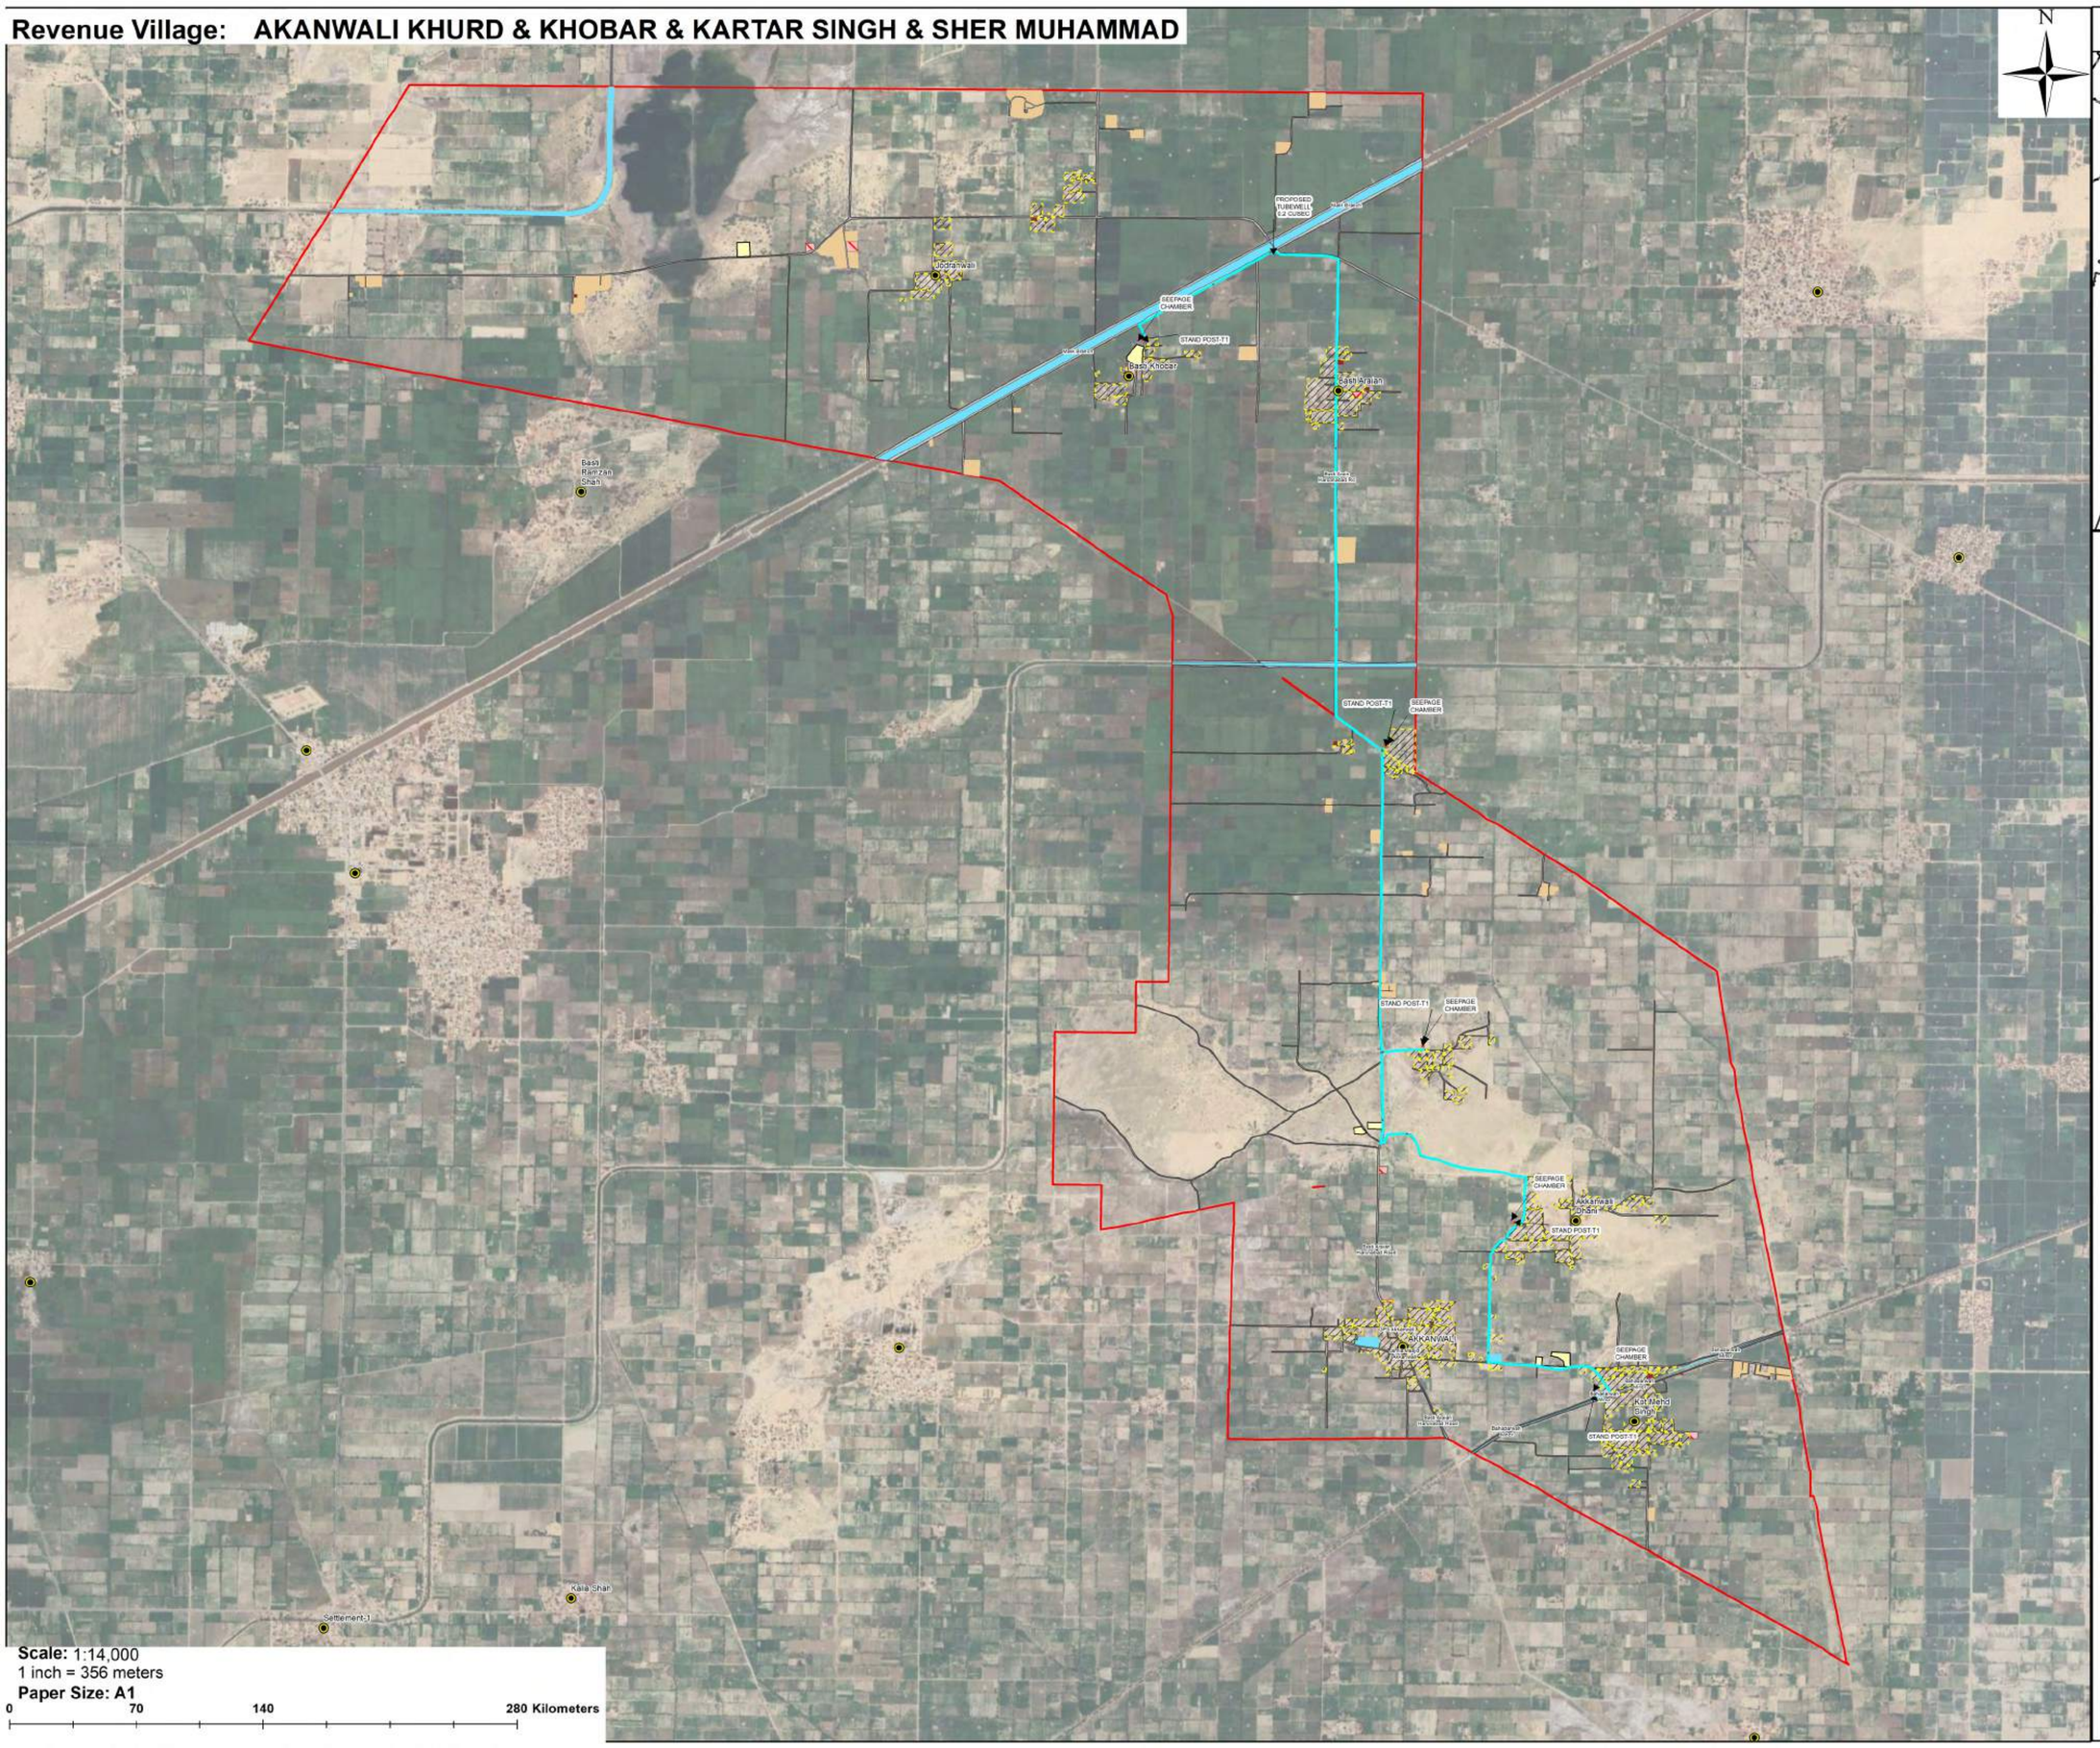

Title:

Proposed Water Supply Map

Legend

DISTRIBUTION NETWORK

- 110 mm Ø
- SETTLEMENT
- STAND POST
- PROPOSED TUBEWELL
- EDUCATIONAL
- GRAVEYARD
- RELIGIOUS
- WATER BODY
- ROAD
- MAJOR SETTLEMENT
- SCATTERED SETTLEMENT
- REVENUE VILLAGE BOUNDARY

Project:

Engineering Design & Construction Supervision, Punjab Rural Sustainable Water Supply & Sanitation Project, Cluster South-III

Scale: 1:14,000
1 inch = 356 meters
Paper Size: A1

0 70 140 280 Kilometers

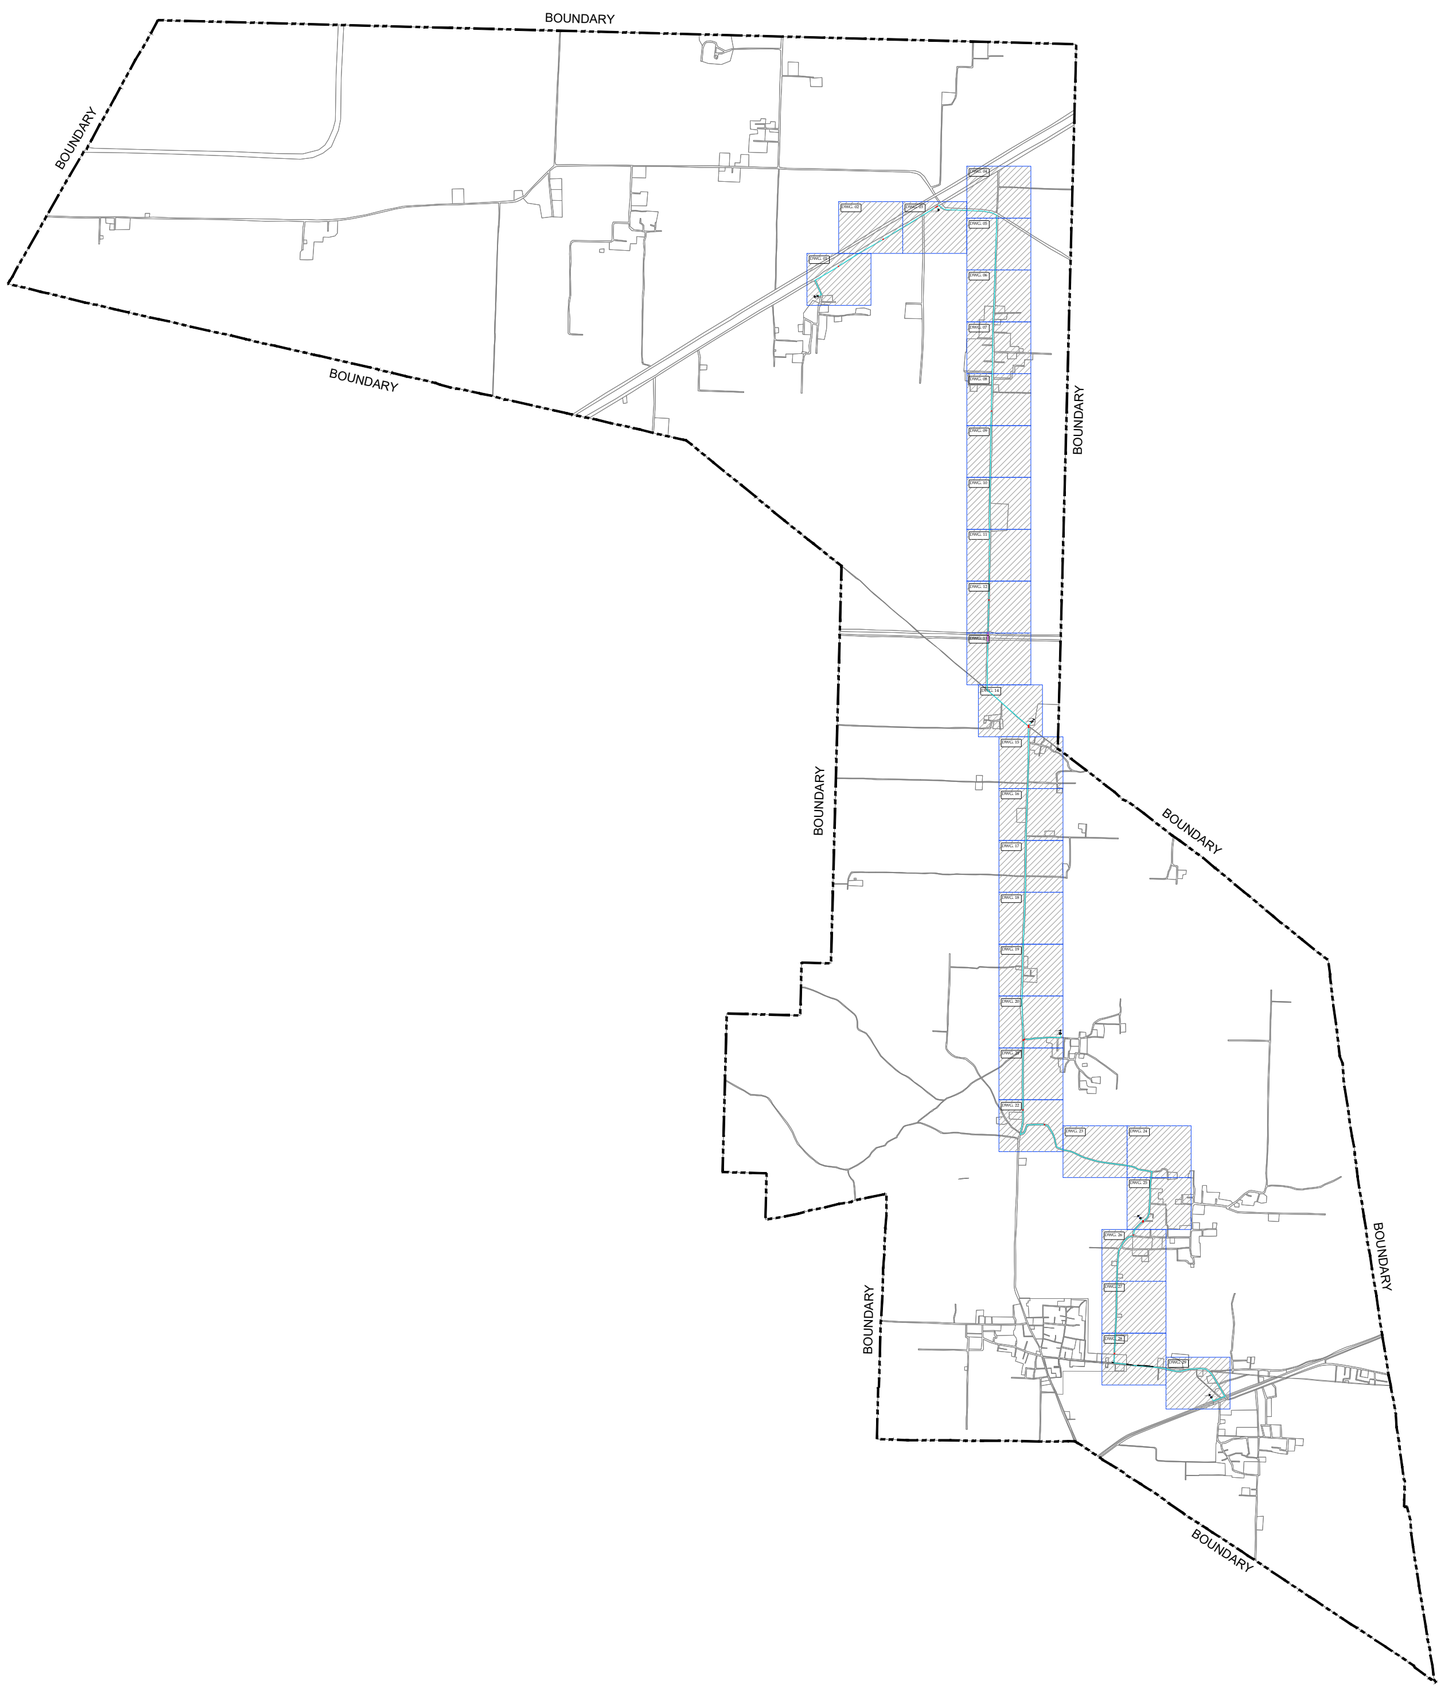

LEGEND:

- 110mm Ø PN - 8 HDPE PIPE
- MS PIPE
- SLUICE VALVE
- WASHOUT VALVE
- AIR RELEASE VALVE
- PROPOSED STAND POST TYPE-I
- PROPOSED TUBE WELL
- BOUNDARY

VILLAGE:

Akanwali Khurd,Sher Mohammad,Khober&Kartar Singh(MVS)(BWN)

TITLE.

WATER SUPPLY SYSTEM KEY PLAN

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 1650'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	12-01-2026	DETAILED DESIGN	ASAD	ENGR. FAEIZ	ENGR. HSAN-UL HAQ
02	19-02-2026	DETAILED DESIGN	ASAD	ENGR. FAEIZ	ENGR. HSAN-UL HAQ
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-AKK-WS-KP-00	00 OF 00	01

PROJECT:

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:

PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT

ASIAN CONSULTING ENGINEERS www.asiancon.com.pk

PRMSC-BWN-AS-WS-KP-00

LAYOUT PLANS

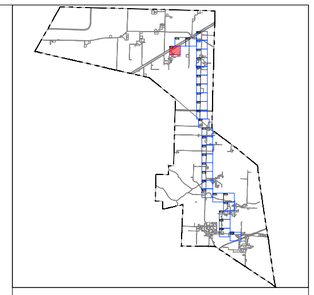

KEY PLAN

LEGEND:

- 110mm Ø PN - 8 HDPE PIPE
- MS PIPE
- SLUICE VALVE
- WASHOUT VALVE
- AIR RELEASE VALVE
- PROPOSED STAND POST TYPE-I
- PROPOSED TUBE WELL
- BOUNDARY

VILLAGE:

Akanwali Khurd&Sher Mohammad&Khober&Kartar Singh(MVS)(BWN)

TITLE.

WATER SUPPLY SYSTEM LAYOUT PLAN-01

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	12-01-2026	DETAILED DESIGN	ASAD	ENGR. FAEIZ	ENGR. HSAN-UL HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-AKK-WS-LP-01	01 OF 29	00

PROJECT:

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:

PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT

ASIAN CONSULTING ENGINEERS
www.asianceh.com

PRMSC-BWN-AKK-WS-LP-01

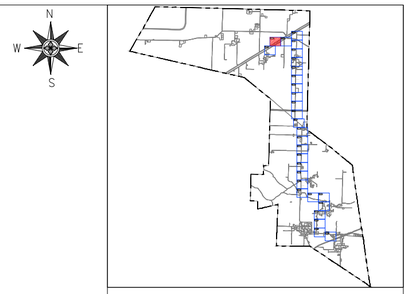

KEY PLAN

LEGEND:

110mm Ø PN - 8 HDPE PIPE

MS PIPE

SLUICE VALVE

WASHOUT VALVE

AIR RELEASE VALVE

PROPOSED STAND POST TYPE-I

PROPOSED TUBE WELL

BOUNDARY

Ø110mm

2124'

PRMSC-BWN-AKK-WS-LP-02

VILLAGE:

Akanwali Khurd&Sher Mohammad&Khober&Kartar Singh(MVS)(BWN)

TITLE.

WATER SUPPLY SYSTEM LAYOUT PLAN-02

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	12-01-2026	DETAILED DESIGN	ASAD	ENGR. FAEIZ	ENGR. IHSAN-UL HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-AKK-WS-LP-02	02 OF 29	00

PROJECT:

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:

PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT

ARD ENVIRONMENTAL TECHNOLOGIES

ASIAN CONSULTING ENGINEERS www.asianconi.com

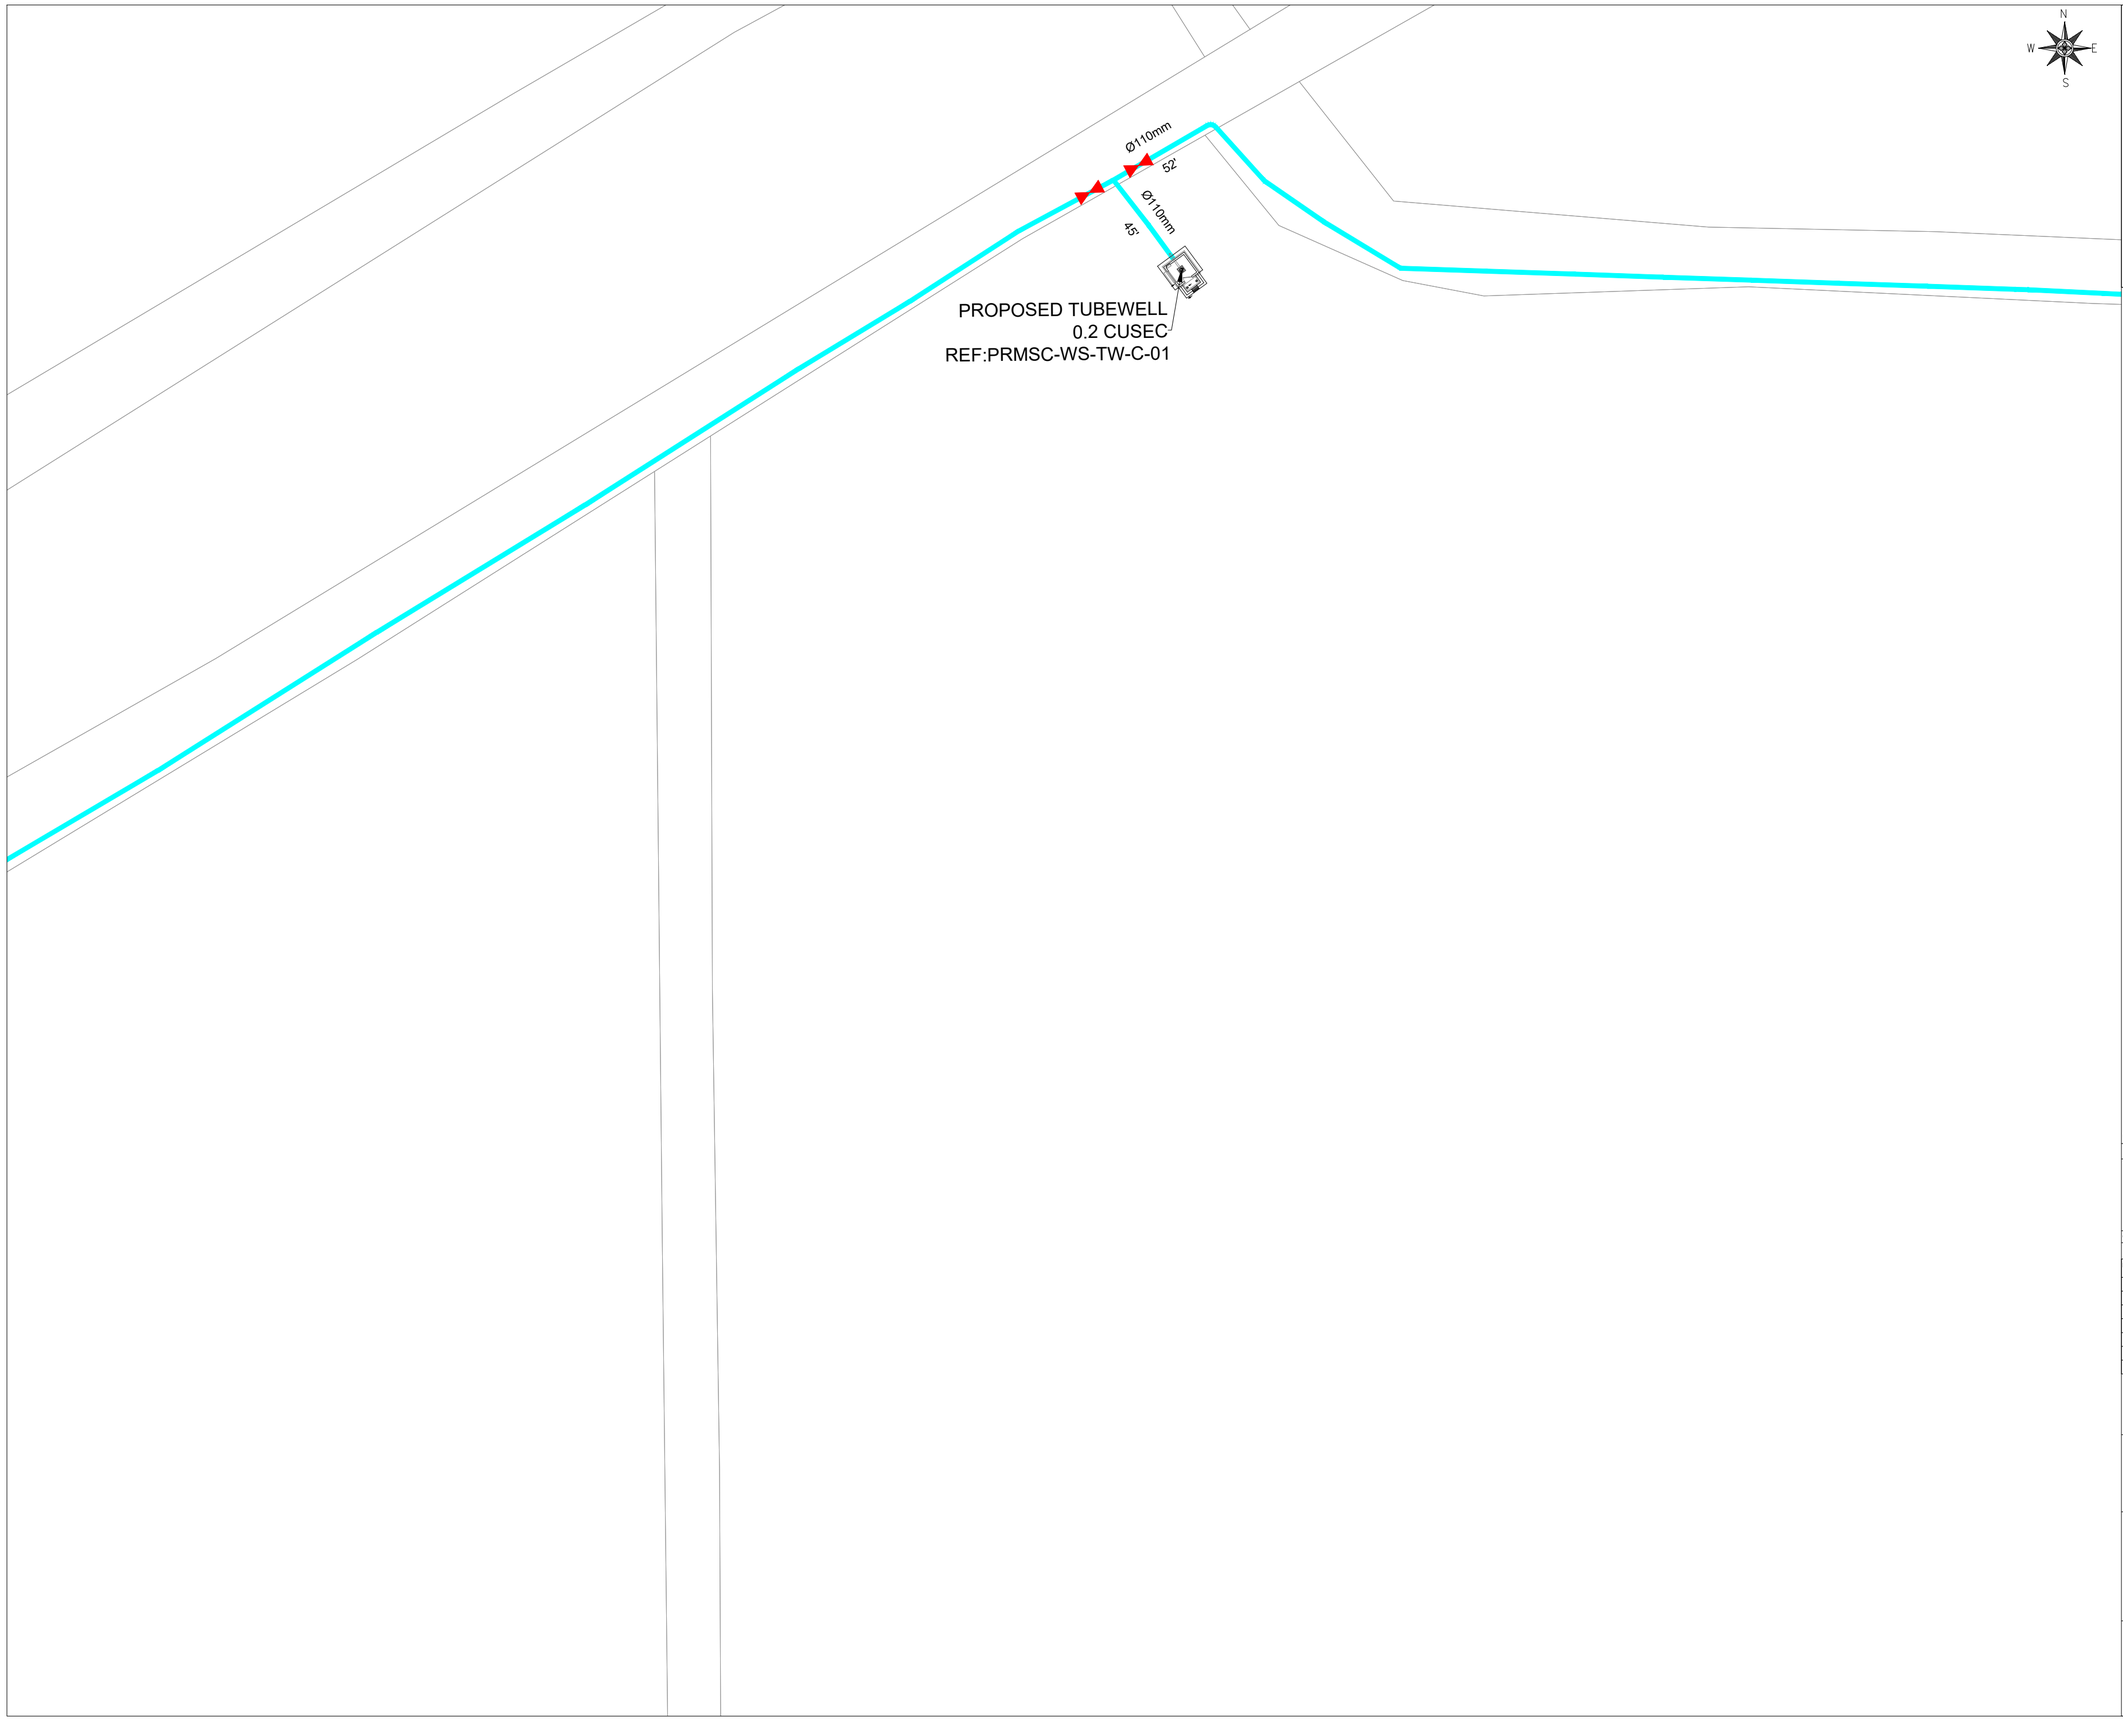

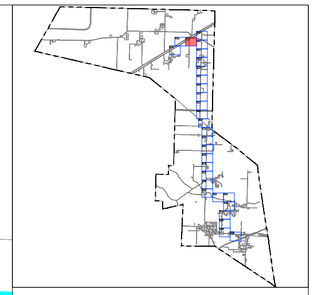

KEY PLAN

LEGEND:

- 110mm Ø PN - 8 HDPE PIPE
- MS PIPE
- SLUICE VALVE
- WASHOUT VALVE
- AIR RELEASE VALVE
- PROPOSED STAND POST TYPE-I
- PROPOSED TUBE WELL
- BOUNDARY

VILLAGE:

Akanwali Khurd&Sher Mohammad&Khober&Kartar Singh(MVS)(BWN)

TITLE.

WATER SUPPLY SYSTEM LAYOUT PLAN-03

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	12-01-2026	DETAILED DESIGN	ASAD	ENGR. FAEIZ	ENGR. IHSAN-UL HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-AKK-WS-LP-03	03 OF 29	00

PROJECT:

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:

PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT

ASIAN CONSULTING ENGINEERS (PVT) LTD. www.asiancon.com

ENVIRONMENTAL TECHNOLOGIES

PRMSC-BWN-AKK-WS-LP-03

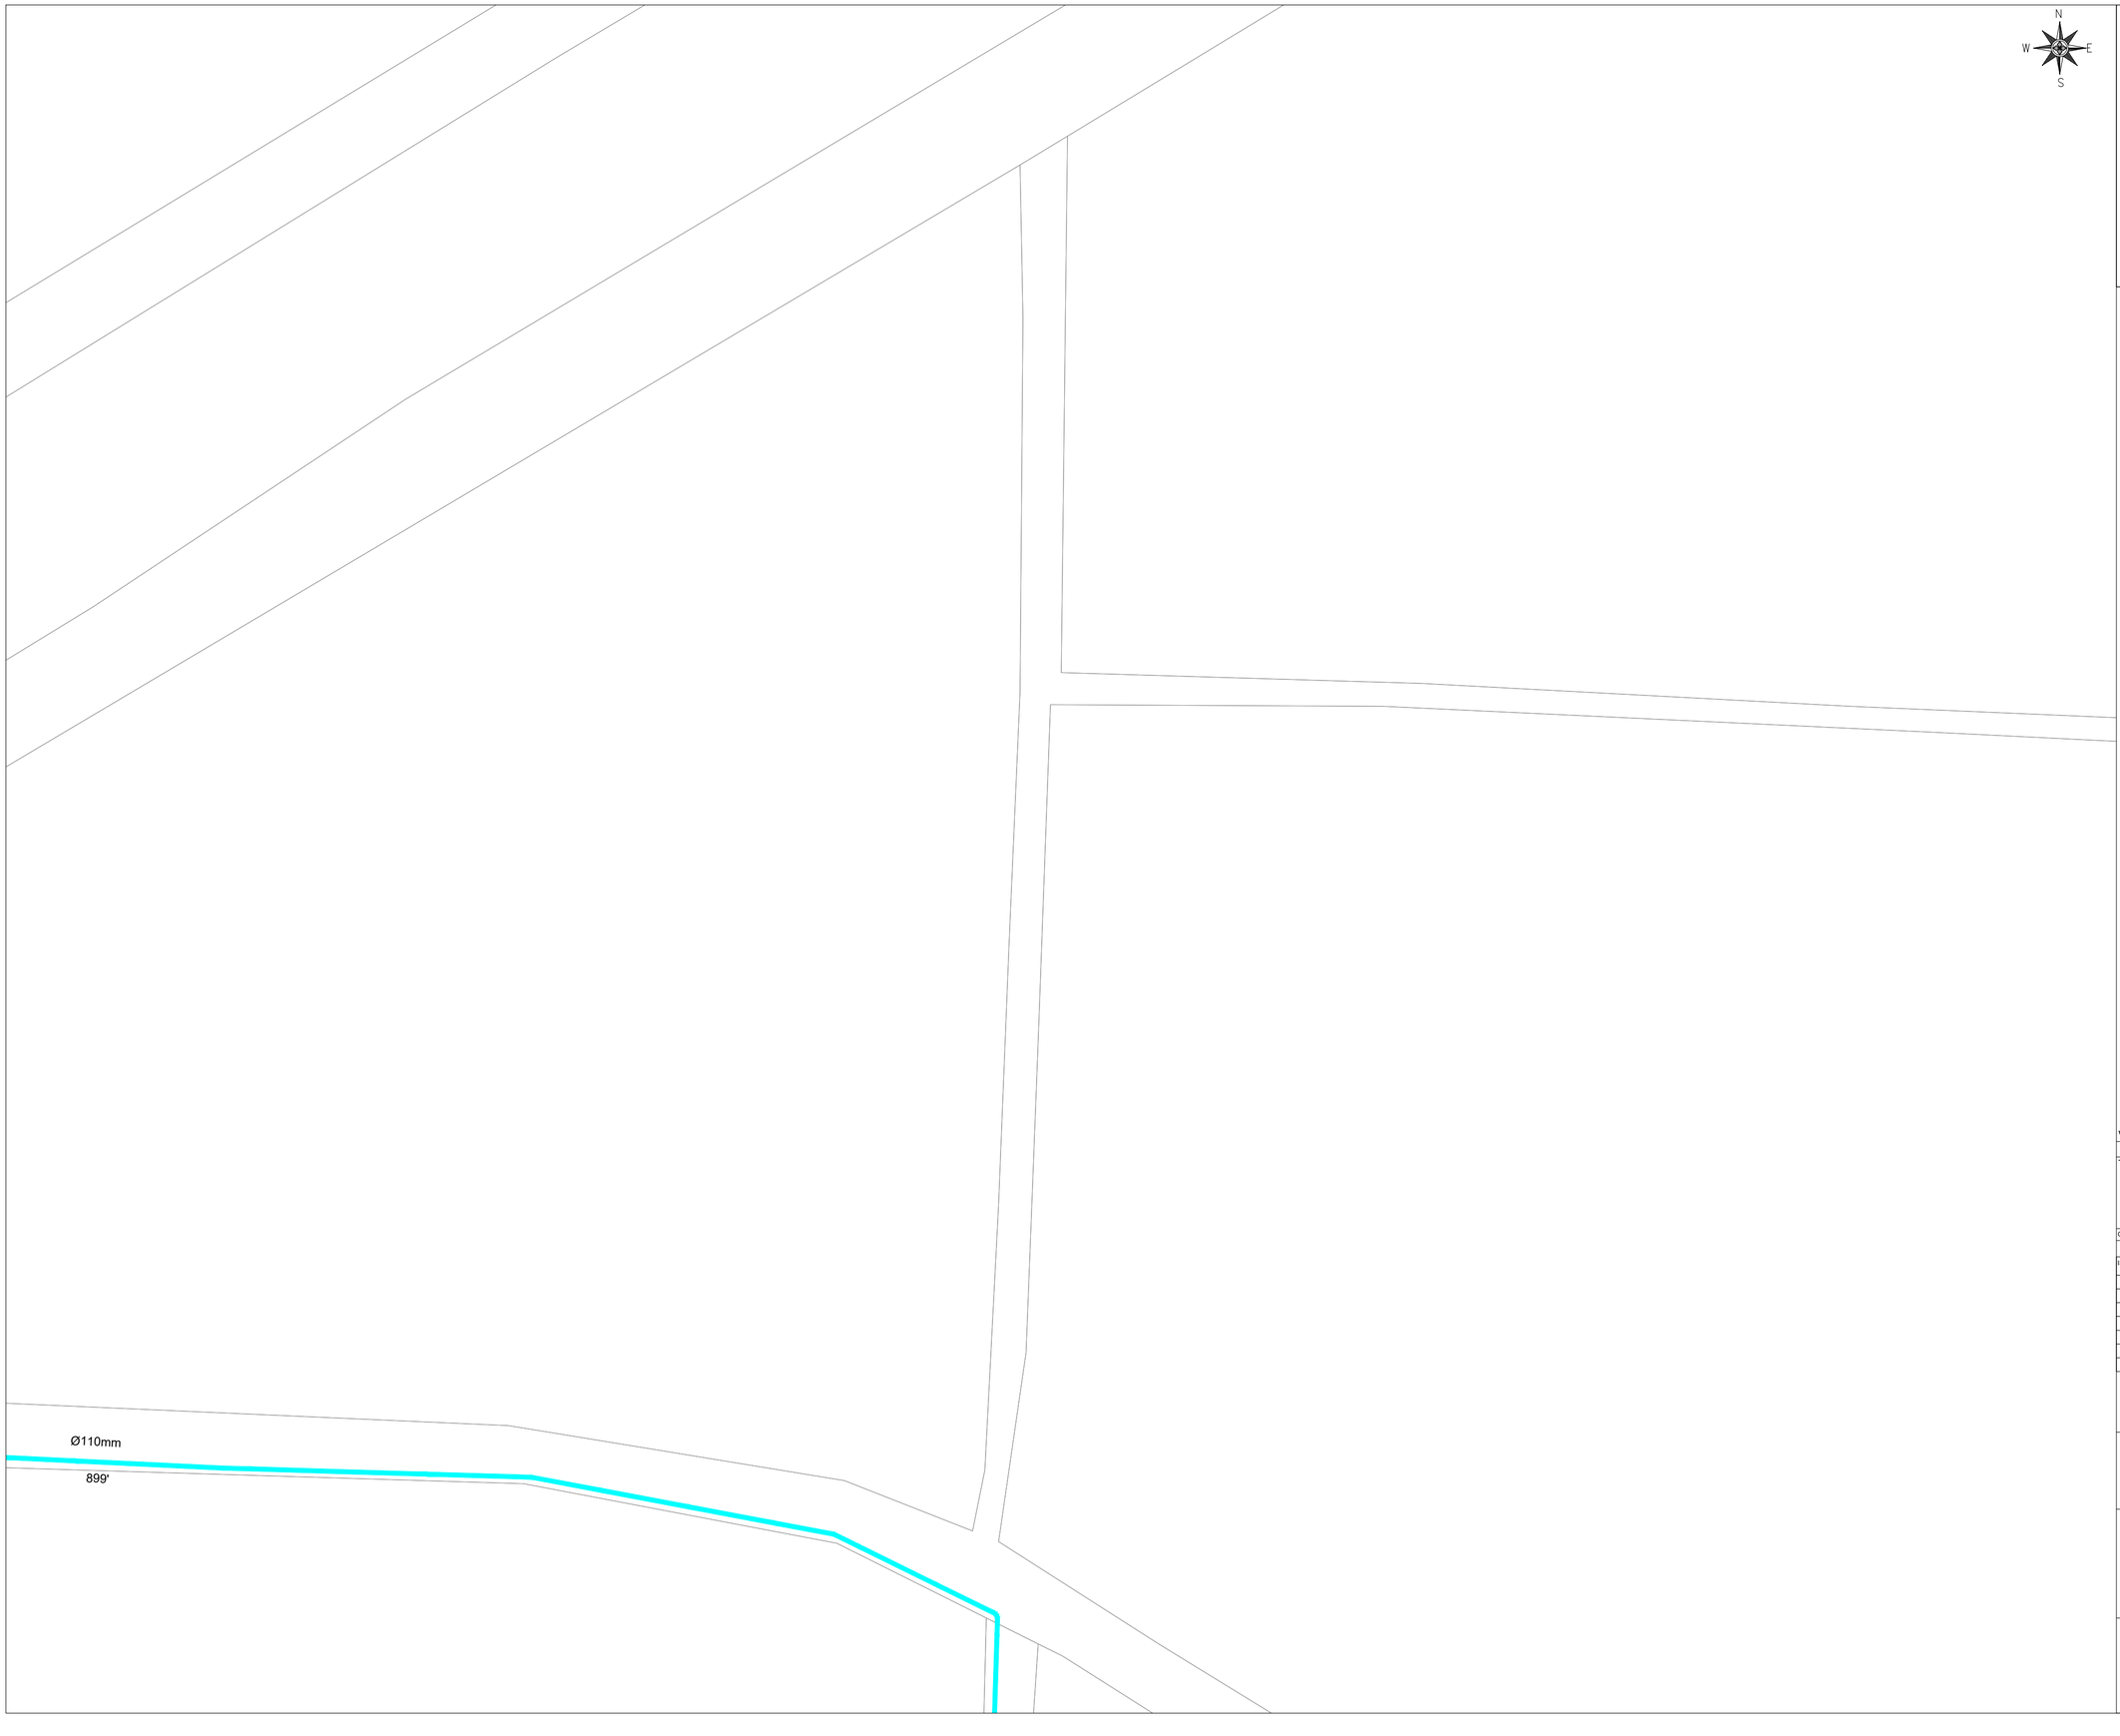

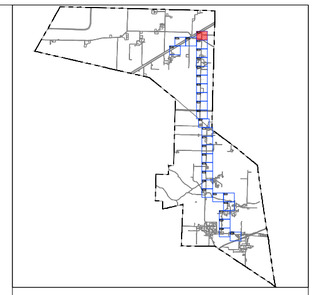

KEY PLAN

LEGEND:

- 110mm Ø PN - 8 HDPE PIPE
- MS PIPE
- SLUICE VALVE
- WASHOUT VALVE
- AIR RELEASE VALVE
- PROPOSED STAND POST TYPE-I
- PROPOSED TUBE WELL
- BOUNDARY

VILLAGE:

Akanwali Khurd&Sher Mohammad&Khober&Kartar Singh(MVS)(BWN)

TITLE.

WATER SUPPLY SYSTEM LAYOUT PLAN-04

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	12-01-2026	DETAILED DESIGN	ASAD	ENGR FAEIZ	ENGR IHSAN-UL HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-AKK-WS-LP-04	04 OF 29	00

PROJECT:

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:

PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT

ENVIRONMENTAL TECHNOLOGIES

ASIAN CONSULTING ENGINEERS www.asianconsultingengineers.com

PRMSC-BWN-AKK-WS-LP-04

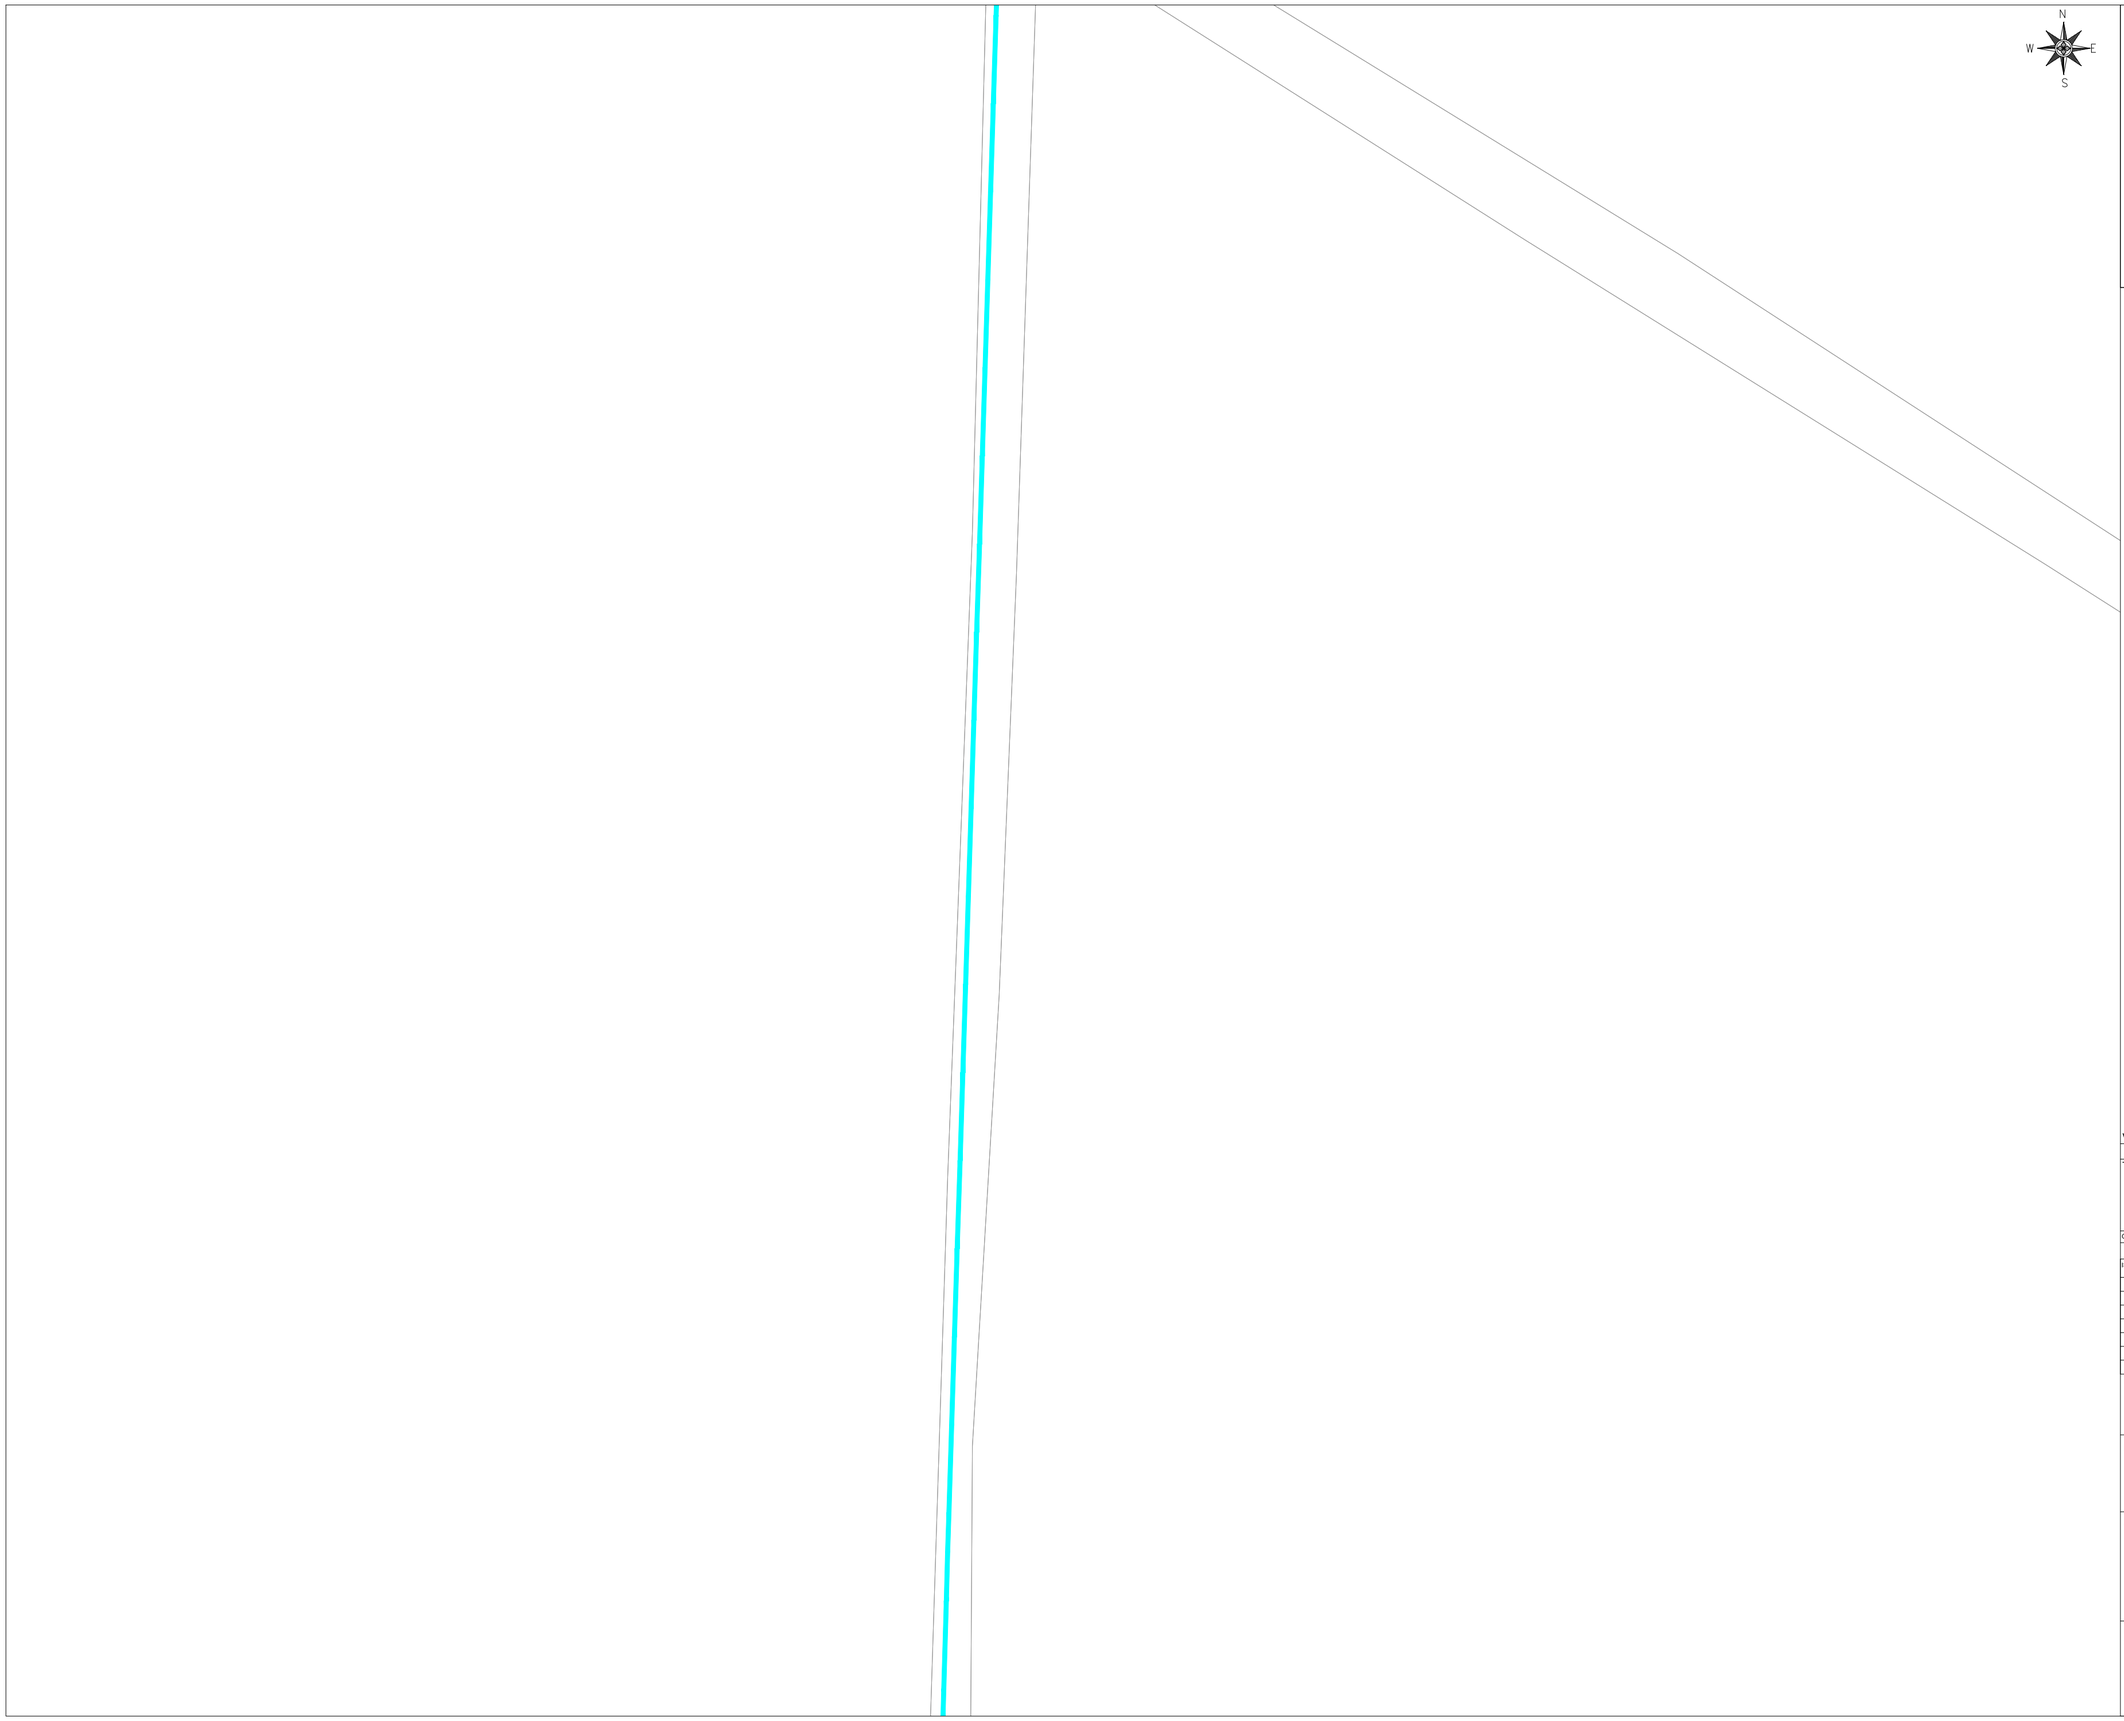

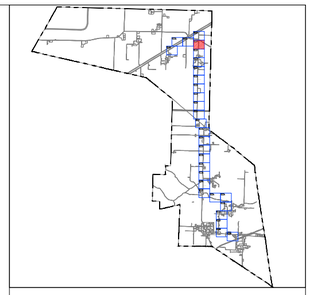

KEY PLAN

LEGEND:

- 110mm Ø PN - 8 HDPE PIPE
- MS PIPE
- SLUICE VALVE
- WASHOUT VALVE
- AIR RELEASE VALVE
- PROPOSED STAND POST TYPE-I
- PROPOSED TUBE WELL
- BOUNDARY

VILLAGE:

Akanwali Khurd&Sher Mohammad&Khober&Kartar Singh(MVS)(BWN)

TITLE.

WATER SUPPLY SYSTEM LAYOUT PLAN-05

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	D E S C R I P T I O N	DRAWN	DESIGNED	APPROVED
01	12-01-2026	DETAILED DESIGN	ASAD	ENGR. FAEIZ	ENGR. IHSAN-UL HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:

PRMSC-BWN-AKK-WS-LP-05

SHEET 05 OF 29

REV 00

PROJECT:

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:

PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT

ASIAN CONSULTING ENGINEERS www.asiancon.com

PRMSC-BWN-AKK-WS-LP-05

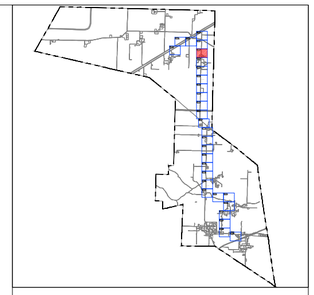

KEY PLAN

LEGEND:

110mm Ø PN - 8 HDPE PIPE

MS PIPE

SLUICE VALVE

WASHOUT VALVE

AIR RELEASE VALVE

PROPOSED STAND POST TYPE-I

PROPOSED TUBE WELL

BOUNDARY

VILLAGE:

Akanwali Khurd&Sher Mohammad&Khober&Kartar Singh(MVS)(BWN)

TITLE.

WATER SUPPLY SYSTEM LAYOUT PLAN-06

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	12-01-2026	DETAILED DESIGN	ASAD	ENGR. FAEIZ	ENGR. IHSAN-UL HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-AKK-WS-LP-06	06 OF 29	00

PROJECT:

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:

PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT

ENVIRONMENTAL TECHNOLOGIES

ASIAN CONSULTING ENGINEERS (PVT) LTD. www.asianconsultingengineers.com

PRMSC-BWN-AKK-WS-LP-06

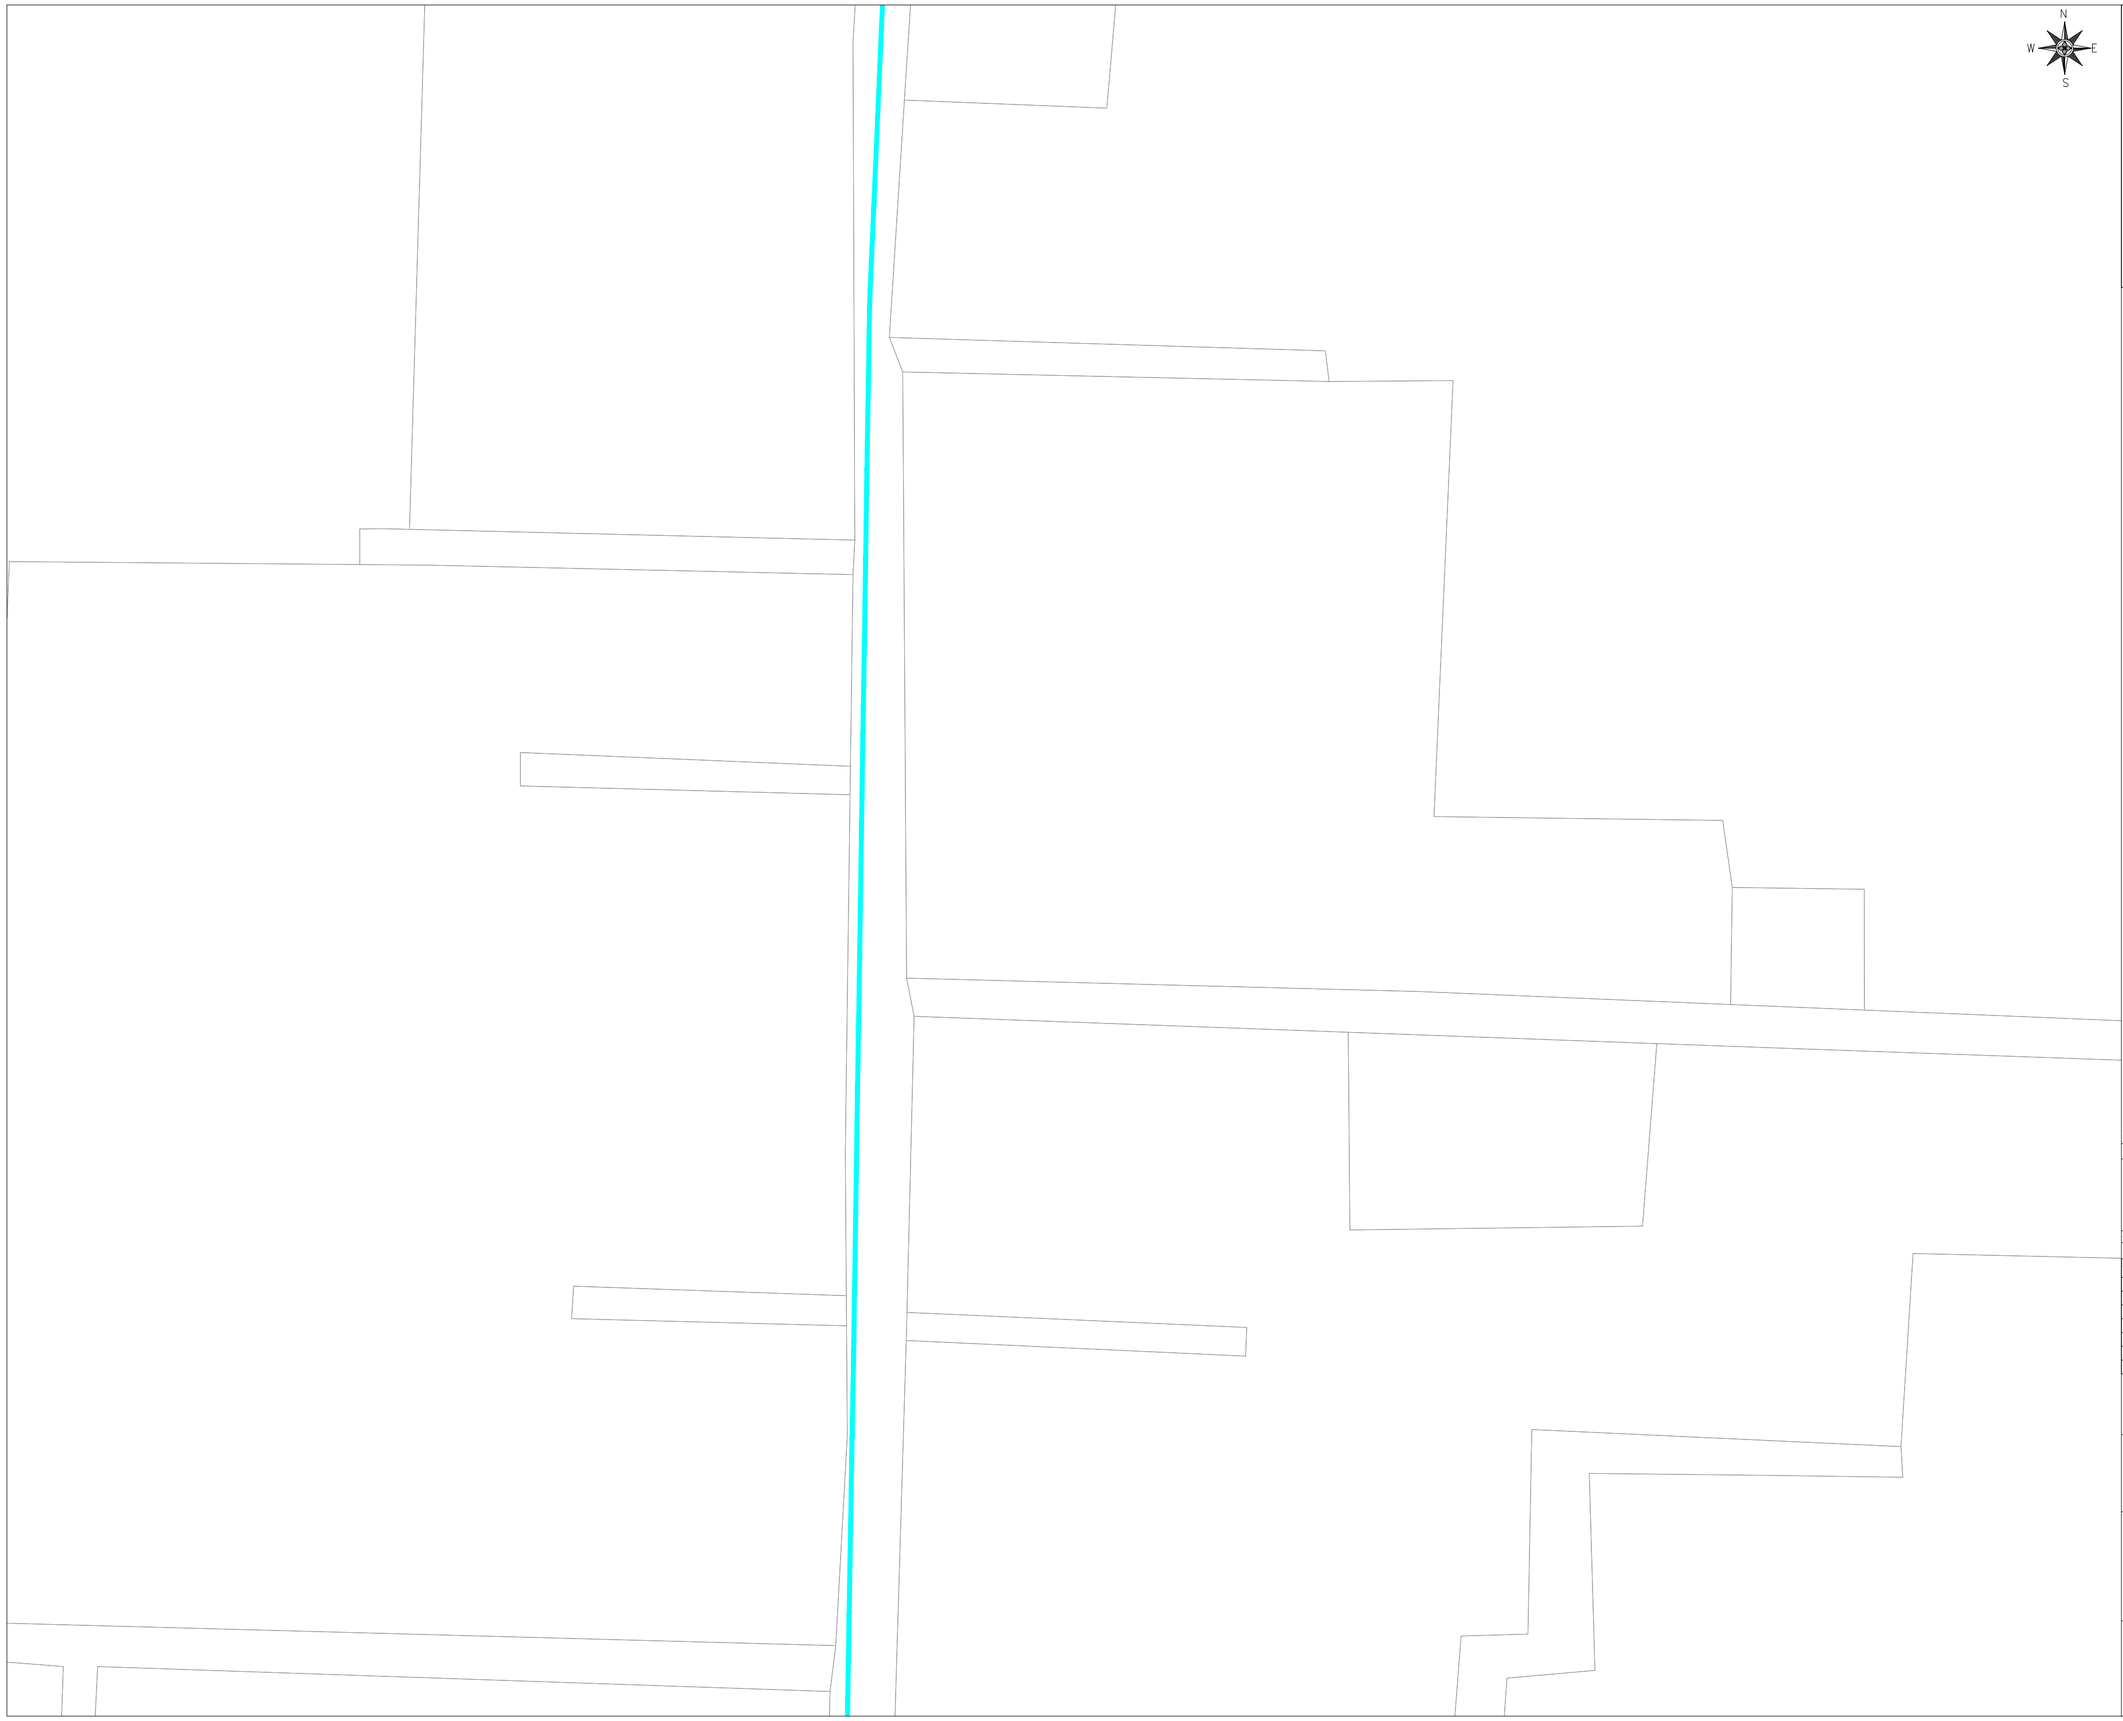

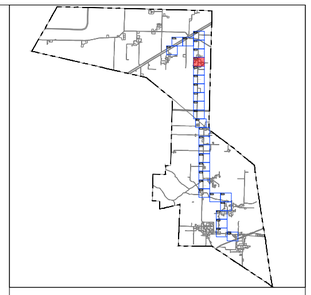

KEY PLAN

LEGEND:

- 110mm Ø PN - 8 HDPE PIPE
- MS PIPE
- SLUICE VALVE
- WASHOUT VALVE
- AIR RELEASE VALVE
- PROPOSED STAND POST TYPE-I
- PROPOSED TUBE WELL
- BOUNDARY

VILLAGE:

Akanwali Khurd&Sher Mohammad&Khober&Kartar Singh(MVS)(BWN)

TITLE.

WATER SUPPLY SYSTEM LAYOUT PLAN-07

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	12-01-2026	DETAILED DESIGN	ASAD	ENGR. FAEIZ	ENGR. IHSAN-UL HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº: PRMSC-BWN-AKK-WS-LP-07

SHEET 07 OF 29

REV 00

PROJECT:

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:

PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT

ASIAN CONSULTING ENGINEERS www.asiancon.com

PRMSC-BWN-AKK-WS-LP-07

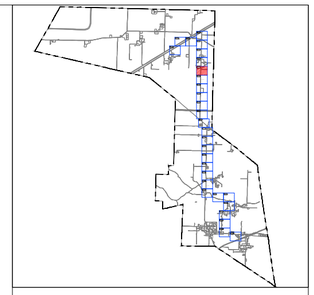

KEY PLAN

LEGEND:

- 110mm Ø PN - 8 HDPE PIPE
- MS PIPE
- SLUICE VALVE
- WASHOUT VALVE
- AIR RELEASE VALVE
- PROPOSED STAND POST TYPE-I
- PROPOSED TUBE WELL
- BOUNDARY

VILLAGE:

Akanwali Khurd&Sher Mohammad&Khober&Kartar Singh(MVS)(BWN)

TITLE.

WATER SUPPLY SYSTEM LAYOUT PLAN-08

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	12-01-2026	DETAILED DESIGN	ASAD	ENGR FAEIZ	ENGR IHSAN-UL HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-AKK-WS-LP-08	08 OF 29	00

PROJECT:

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:

PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT

ASIAN CONSULTING ENGINEERS www.asianceb.com

PRMSC-BWN-AKK-WS-LP-08

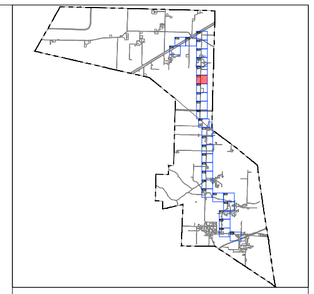

KEY PLAN

LEGEND:

110mm Ø PN - 8 HDPE PIPE

MS PIPE

SLUICE VALVE

WASHOUT VALVE

AIR RELEASE VALVE

PROPOSED STAND POST TYPE-I

PROPOSED TUBE WELL

BOUNDARY

VILLAGE:

Akanwali Khurd&Sher Mohammad&Khober&Kartar Singh(MVS)(BWN)

TITLE.

WATER SUPPLY SYSTEM LAYOUT PLAN-09

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	12-01-2026	DETAILED DESIGN	ASAD	ENGR FAEIZ	ENGR HSAN-UL HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº: PRMSC-BWN-AKK-WS-LP-09

SHEET 09 OF 29

REV 00

PROJECT:

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:

PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT

ENVIRONMENTAL TECHNOLOGIES

ASIAN CONSULTING ENGINEERS (PVT) LTD. www.asiancon.com

PRMSC-BWN-AKK-WS-LP-09

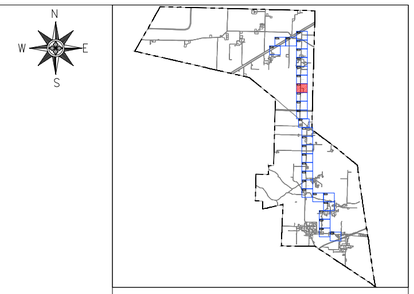

KEY PLAN

LEGEND:

110mm Ø PN - 8 HDPE PIPE

MS PIPE

SLUICE VALVE

WASHOUT VALVE

AIR RELEASE VALVE

PROPOSED STAND POST TYPE-I

PROPOSED TUBE WELL

BOUNDARY

VILLAGE:

Akanwali Khurd&Sher Mohammad&Khober&Kartar Singh(MVS)(BWN)

TITLE.

WATER SUPPLY SYSTEM LAYOUT PLAN-10

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	12-01-2026	DETAILED DESIGN	ASAD	ENGR. FAEIZ	ENGR. IHSAN-UL HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:

PRMSC-BWN-AKK-WS-LP-10

SHEET 10 OF 29

REV 00

PROJECT:

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:

PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT

ASIAN CONSULTING ENGINEERS www.asiancon.com

PRMSC-BWN-AKK-WS-LP-10

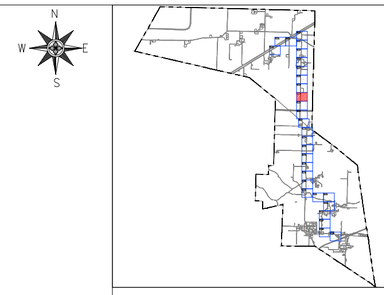

KEY PLAN

LEGEND:

110mm Ø PN - 8 HDPE PIPE

MS PIPE

SLUICE VALVE

WASHOUT VALVE

AIR RELEASE VALVE

PROPOSED STAND POST TYPE-I

PROPOSED TUBE WELL

BOUNDARY

VILLAGE:

Akanwali Khurd&Sher Mohammad&Khober&Kartar Singh(MVS)(BWN)

TITLE:

WATER SUPPLY SYSTEM LAYOUT PLAN-11

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	12-01-2026	DETAILED DESIGN	ASAD	ENGR. FARIZ	ENGR. HSAN-UL HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº: PRMSC-BWN-AKK-WS-LP-11

SHEET 11 OF 29

REV 00

PROJECT:

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:

PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT

ASIAN CONSULTING ENGINEERS www.asiancon.com.pk

PRMSC-BWN-AKK-WS-LP-11

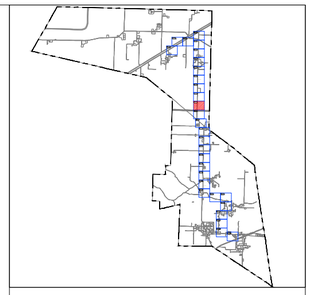

KEY PLAN

LEGEND:

110mm Ø PN - 8 HDPE PIPE

MS PIPE

SLUICE VALVE

WASHOUT VALVE

AIR RELEASE VALVE

PROPOSED STAND POST TYPE-I

PROPOSED TUBE WELL

BOUNDARY

VILLAGE:

Akanwali Khurd&Sher Mohammad&Khober&Kartar Singh(MVS)(BWN)

TITLE.

WATER SUPPLY SYSTEM LAYOUT PLAN-12

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	12-01-2026	DETAILED DESIGN	ASAD	ENGR. FAEIZ	ENGR. IHSAN UL HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-AKK-WS-LP-12	12 OF 29	00

PROJECT:

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:

PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT

ASIAN CONSULTING ENGINEERS www.asiancon.com

PRMSC-BWN-AKK-WS-LP-12

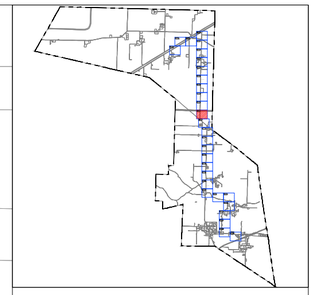

KEY PLAN

LEGEND:

110mm Ø PN - 8 HDPE PIPE
MS PIPE
SLUICE VALVE
WASHOUT VALVE
AIR RELEASE VALVE
PROPOSED STAND POST TYPE-I
PROPOSED TUBE WELL
BOUNDARY

VILLAGE:
Akanwali Khurd&Sher Mohammad&Khober&Kartar Singh(MVS)(BWN)

TITLE.
WATER SUPPLY SYSTEM LAYOUT PLAN-13

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	12-01-2026	DETAILED DESIGN	ASAD	ENGR. FAEIZ	ENGR. IHSAN UL HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº: PRMSC-BWN-AKK-WS-LP-13

SHEET 13 OF 29

REV 00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT
ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

PRMSC-BWN-AKK-WS-LP-13

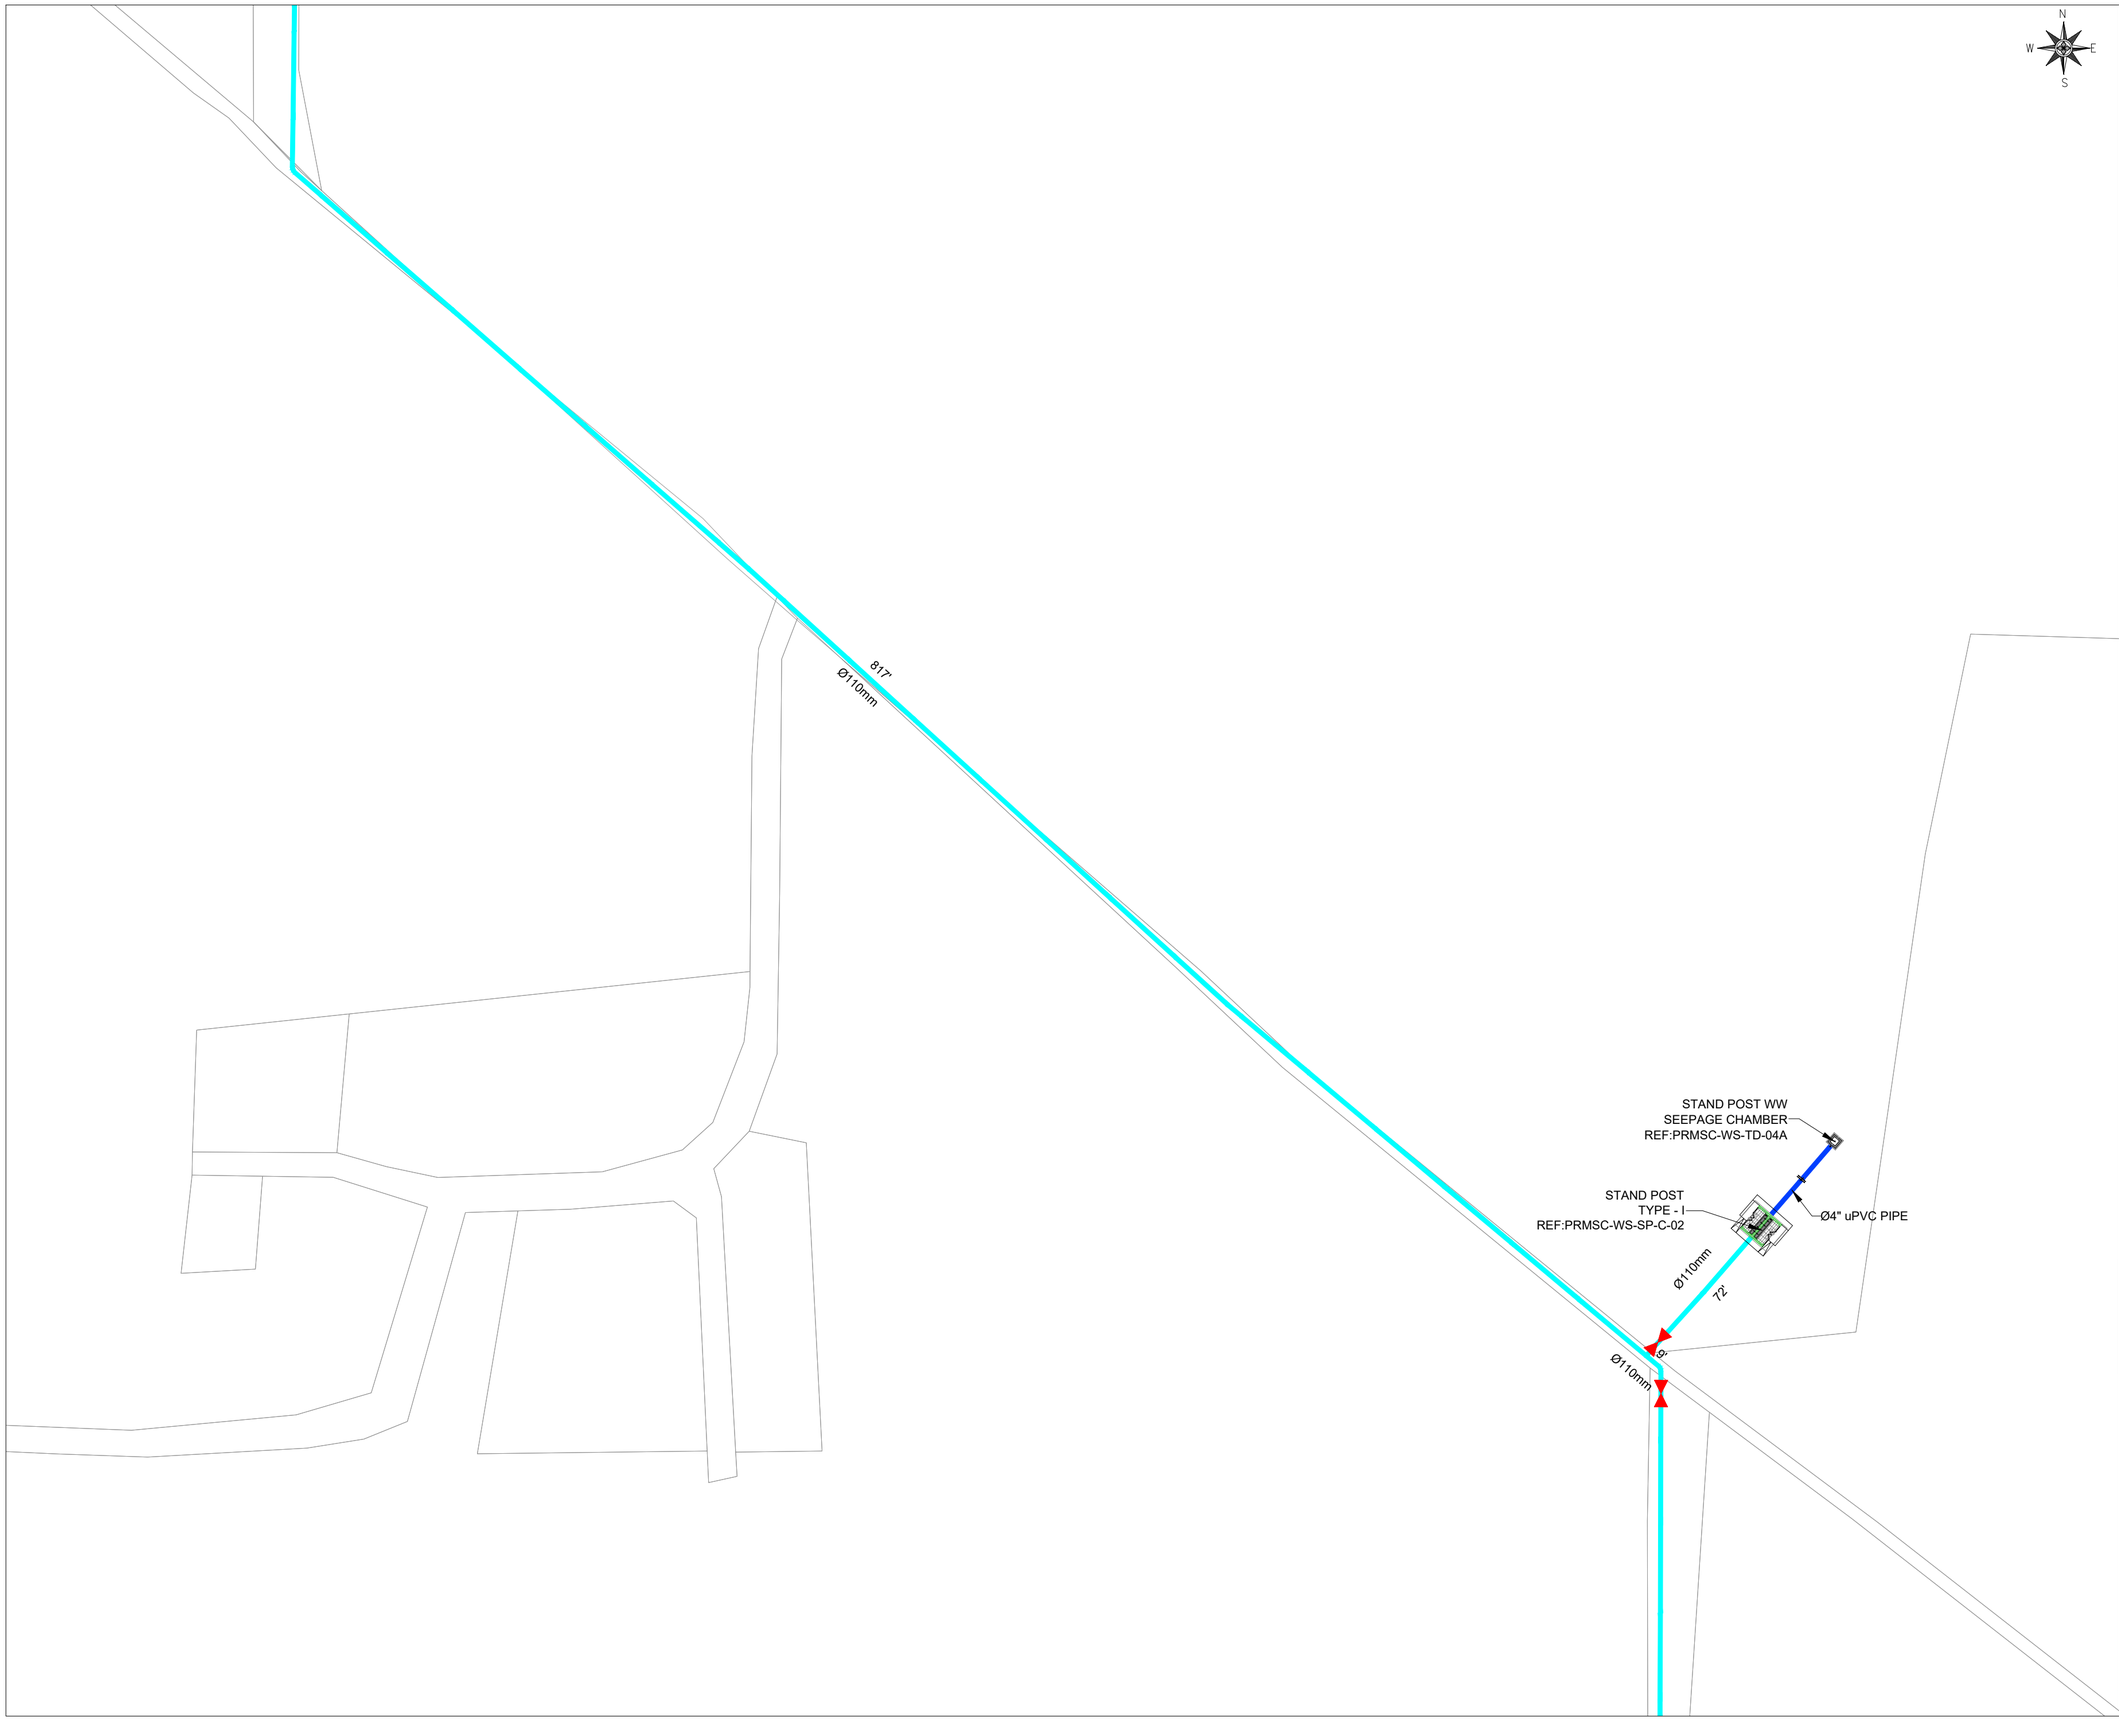

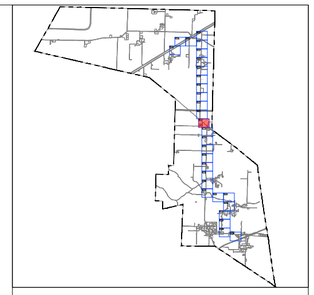

KEY PLAN

LEGEND:

- 110mm Ø PN - 8 HDPE PIPE
- MS PIPE
- SLUICE VALVE
- WASHOUT VALVE
- AIR RELEASE VALVE
- PROPOSED STAND POST TYPE-I
- PROPOSED TUBE WELL
- BOUNDARY

VILLAGE:
Akanwali Khurd&Sher Mohammad&Khober&Kartar Singh(MVS)(BWN)

TITLE.
WATER SUPPLY SYSTEM LAYOUT PLAN-14

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	12-01-2026	DETAILED DESIGN	ASAD	ENGR. FAEIZ	ENGR. HSAN-UL HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-AKK-WS-LP-14	14 OF 29	00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT
ASIAN CONSULTING ENGINEERS
www.asiancon.com

PRMSC-BWN-AKK-WS-LP-14

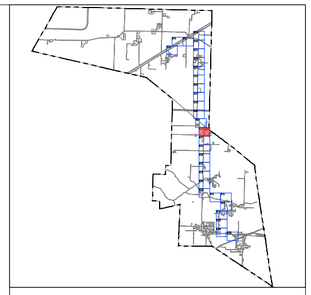

KEY PLAN

LEGEND:

- 110mm Ø PN - 8 HDPE PIPE
- MS PIPE
- SLUICE VALVE
- WASHOUT VALVE
- AIR RELEASE VALVE
- PROPOSED STAND POST TYPE-I
- PROPOSED TUBE WELL
- BOUNDARY

VILLAGE:

Akanwali Khurd&Sher Mohammad&Khober&Kartar Singh(MVS)(BWN)

TITLE.

WATER SUPPLY SYSTEM LAYOUT PLAN-15

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	12-01-2026	DETAILED DESIGN	ASAD	ENGR FAEIZ	ENGR IHSAN-UL HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:

PRMSC-BWN-AKK-WS-LP-15

SHEET 15 OF 29

REV 00

PROJECT:

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:

PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT

ASIAN CONSULTING ENGINEERS www.asianconsultingengineers.com

PRMSC-BWN-AKK-WS-LP-15

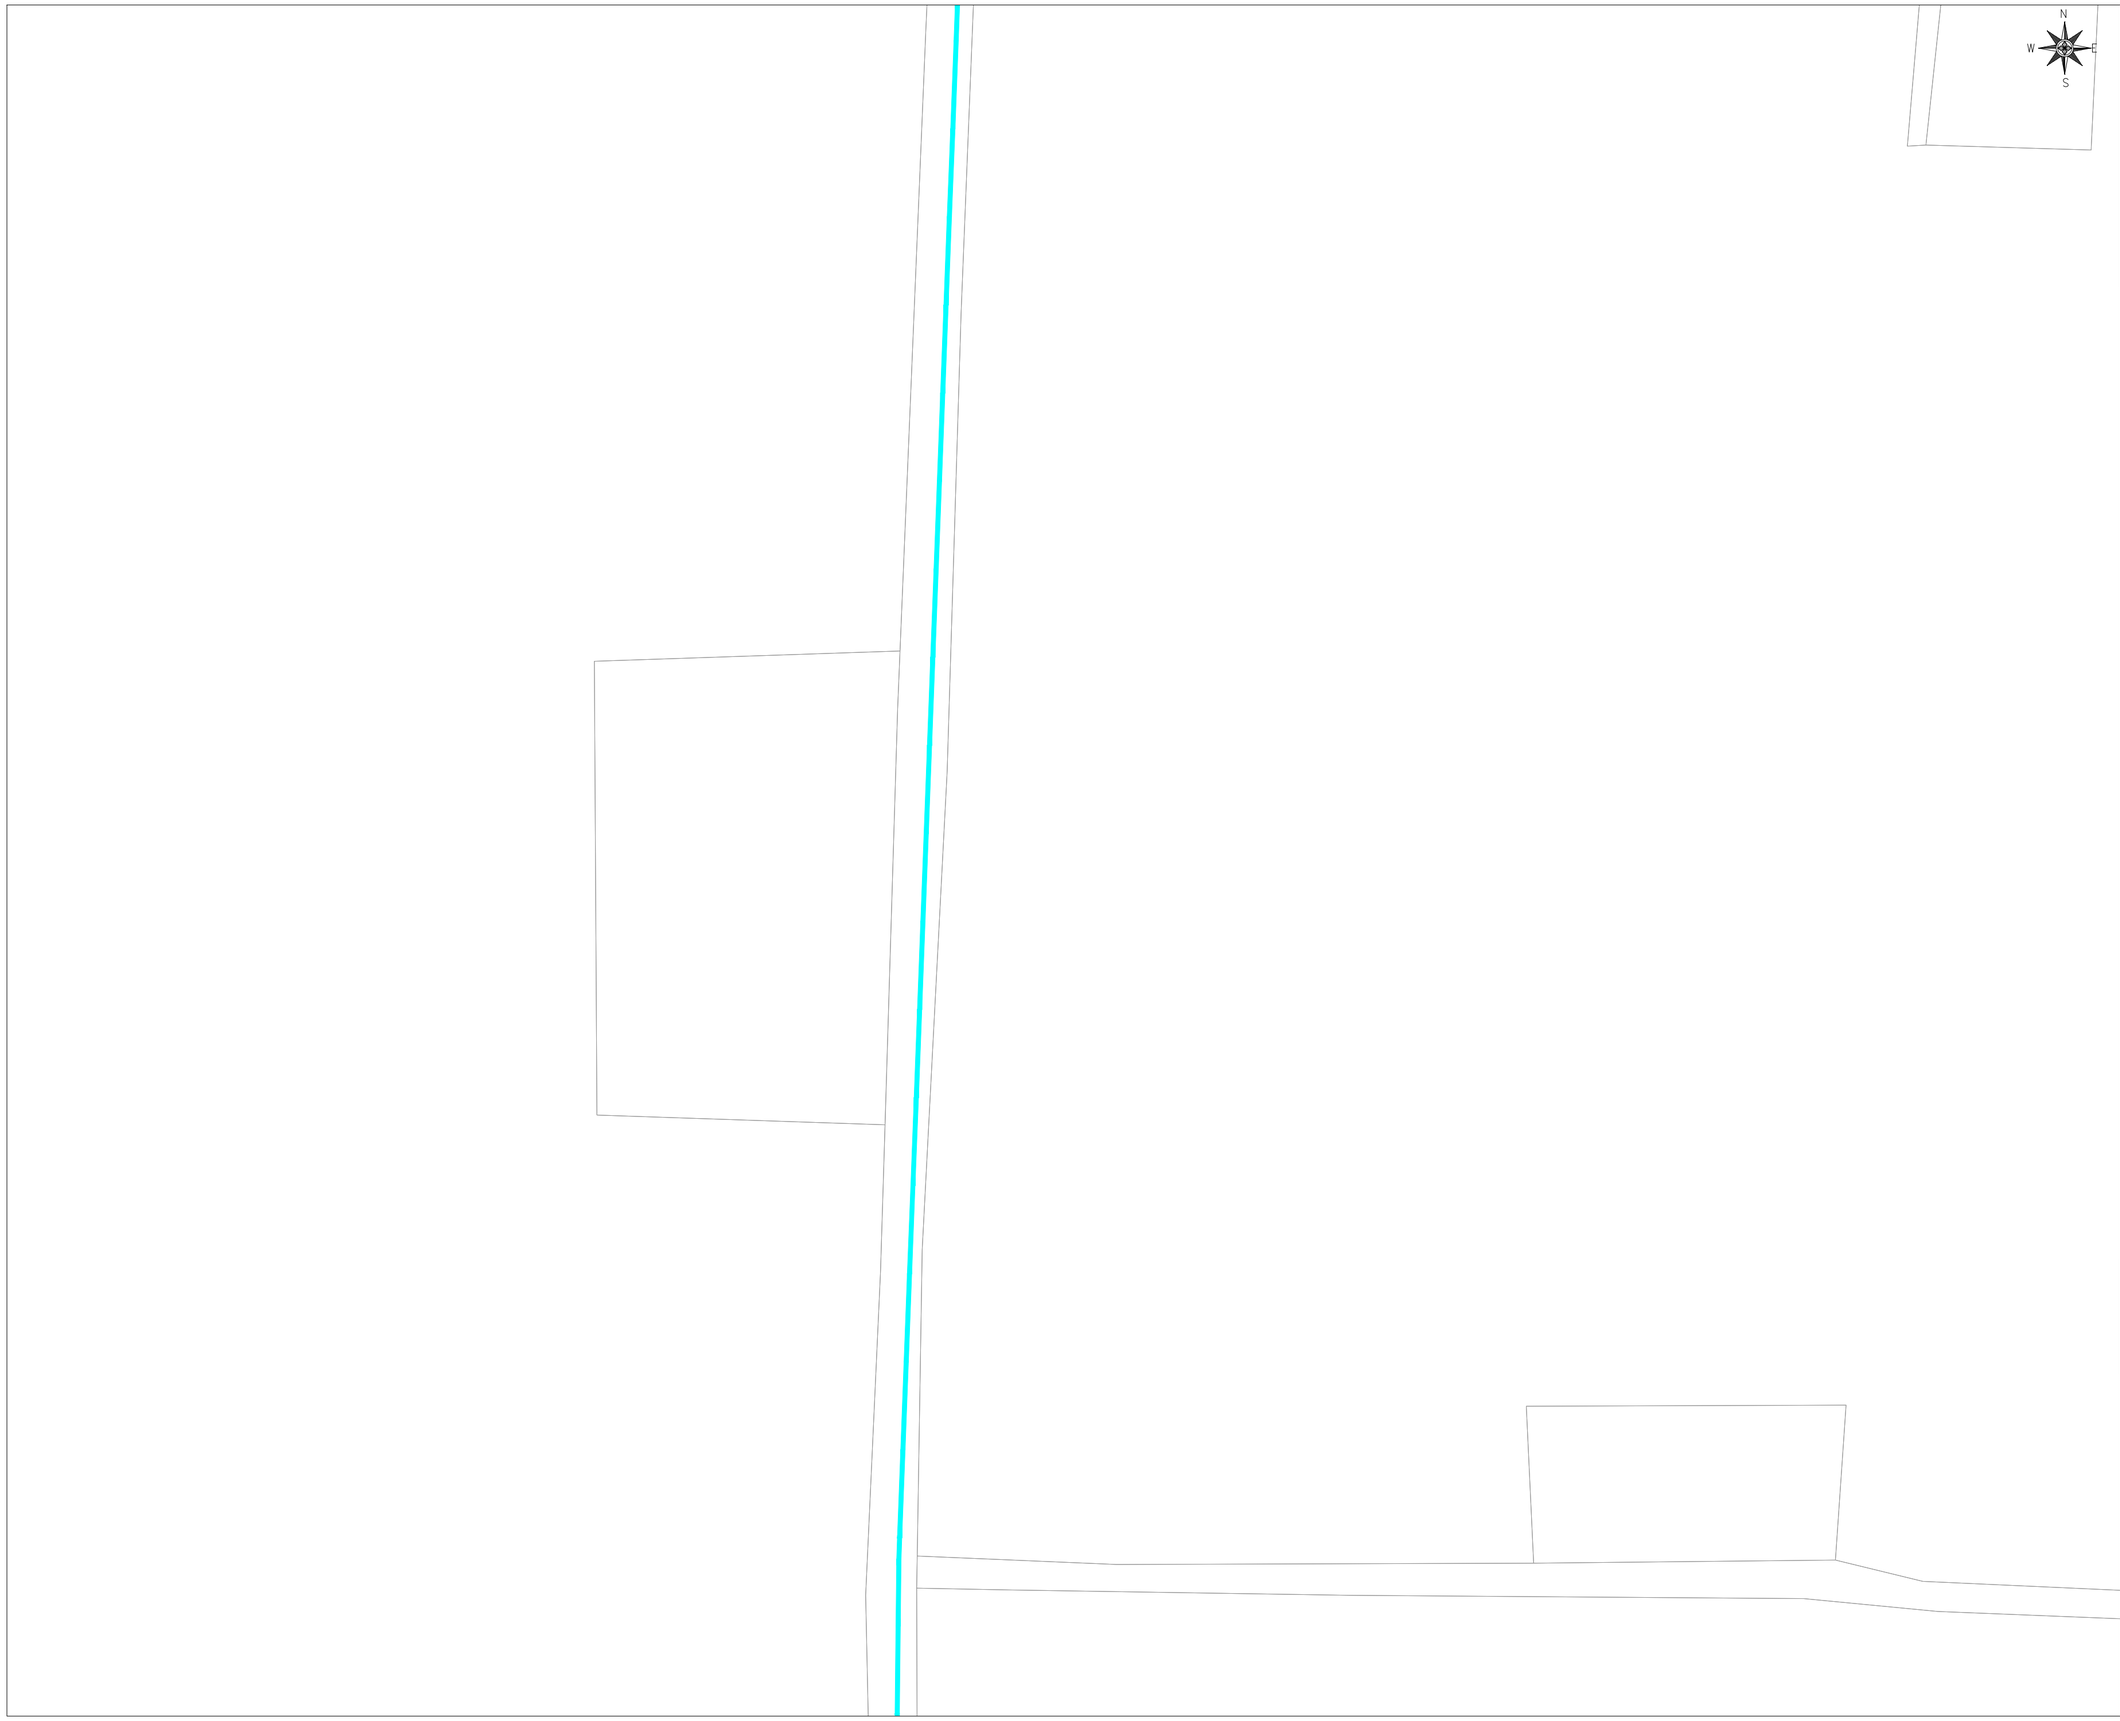

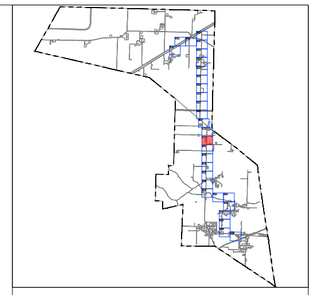

KEY PLAN

LEGEND:

110mm Ø PN - 8 HDPE PIPE

MS PIPE

SLUICE VALVE

WASHOUT VALVE

AIR RELEASE VALVE

PROPOSED STAND POST TYPE-I

PROPOSED TUBE WELL

BOUNDARY

VILLAGE:

Akanwali Khurd&Sher Mohammad&Khober&Kartar Singh(MVS)(BWN)

TITLE.

WATER SUPPLY SYSTEM LAYOUT PLAN-16

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	12-01-2026	DETAILED DESIGN	ASAD	ENGR. FAEIZ	ENGR. IHSAN-UL HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-AKK-WS-LP-16	16 OF 29	00

PROJECT:

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:

PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT

ASIAN CONSULTING ENGINEERS www.asiancon.com

PRMSC-BWN-AKK-WS-LP-16

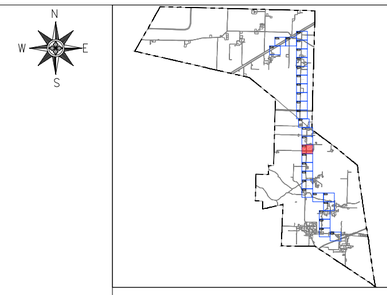

KEY PLAN

LEGEND:

110mm Ø PN - 8 HDPE PIPE

MS PIPE

SLUICE VALVE

WASHOUT VALVE

AIR RELEASE VALVE

PROPOSED STAND POST TYPE-I

PROPOSED TUBE WELL

BOUNDARY

VILLAGE:

Akanwali Khurd&Sher Mohammad&Khober&Kartar Singh(MVS)(BWN)

TITLE.

WATER SUPPLY SYSTEM LAYOUT PLAN-17

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	12-01-2026	DETAILED DESIGN	ASAD	ENGR. FAEIZ	ENGR. IHSAN-UL HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-AKK-WS-LP-17	17 OF 29	00

PROJECT:

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:

PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT

ASIAN CONSULTING ENGINEERS www.asiancon.com

PRMSC-BWN-AKK-WS-LP-17

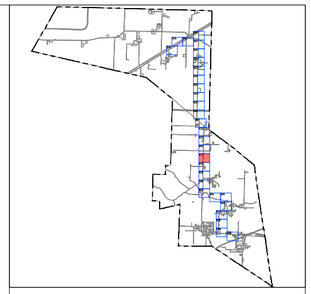

KEY PLAN

LEGEND:

110mm Ø PN - 8 HDPE PIPE

MS PIPE

SLUICE VALVE

WASHOUT VALVE

AIR RELEASE VALVE

PROPOSED STAND POST TYPE-I

PROPOSED TUBE WELL

BOUNDARY

VILLAGE:

Akanwali Khurd&Sher Mohammad&Khober&Kartar Singh(MVS)(BWN)

TITLE.

WATER SUPPLY SYSTEM LAYOUT PLAN-18

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	12-01-2026	DETAILED DESIGN	ASAD	ENGR. FAEIZ	ENGR. IHSAN-UL HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-AKK-WS-LP-18	18 OF 29	00

PROJECT:

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:

PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT

ASIAN CONSULTING ENGINEERS www.asiancon.com

PRMSC-BWN-AKK-WS-LP-18

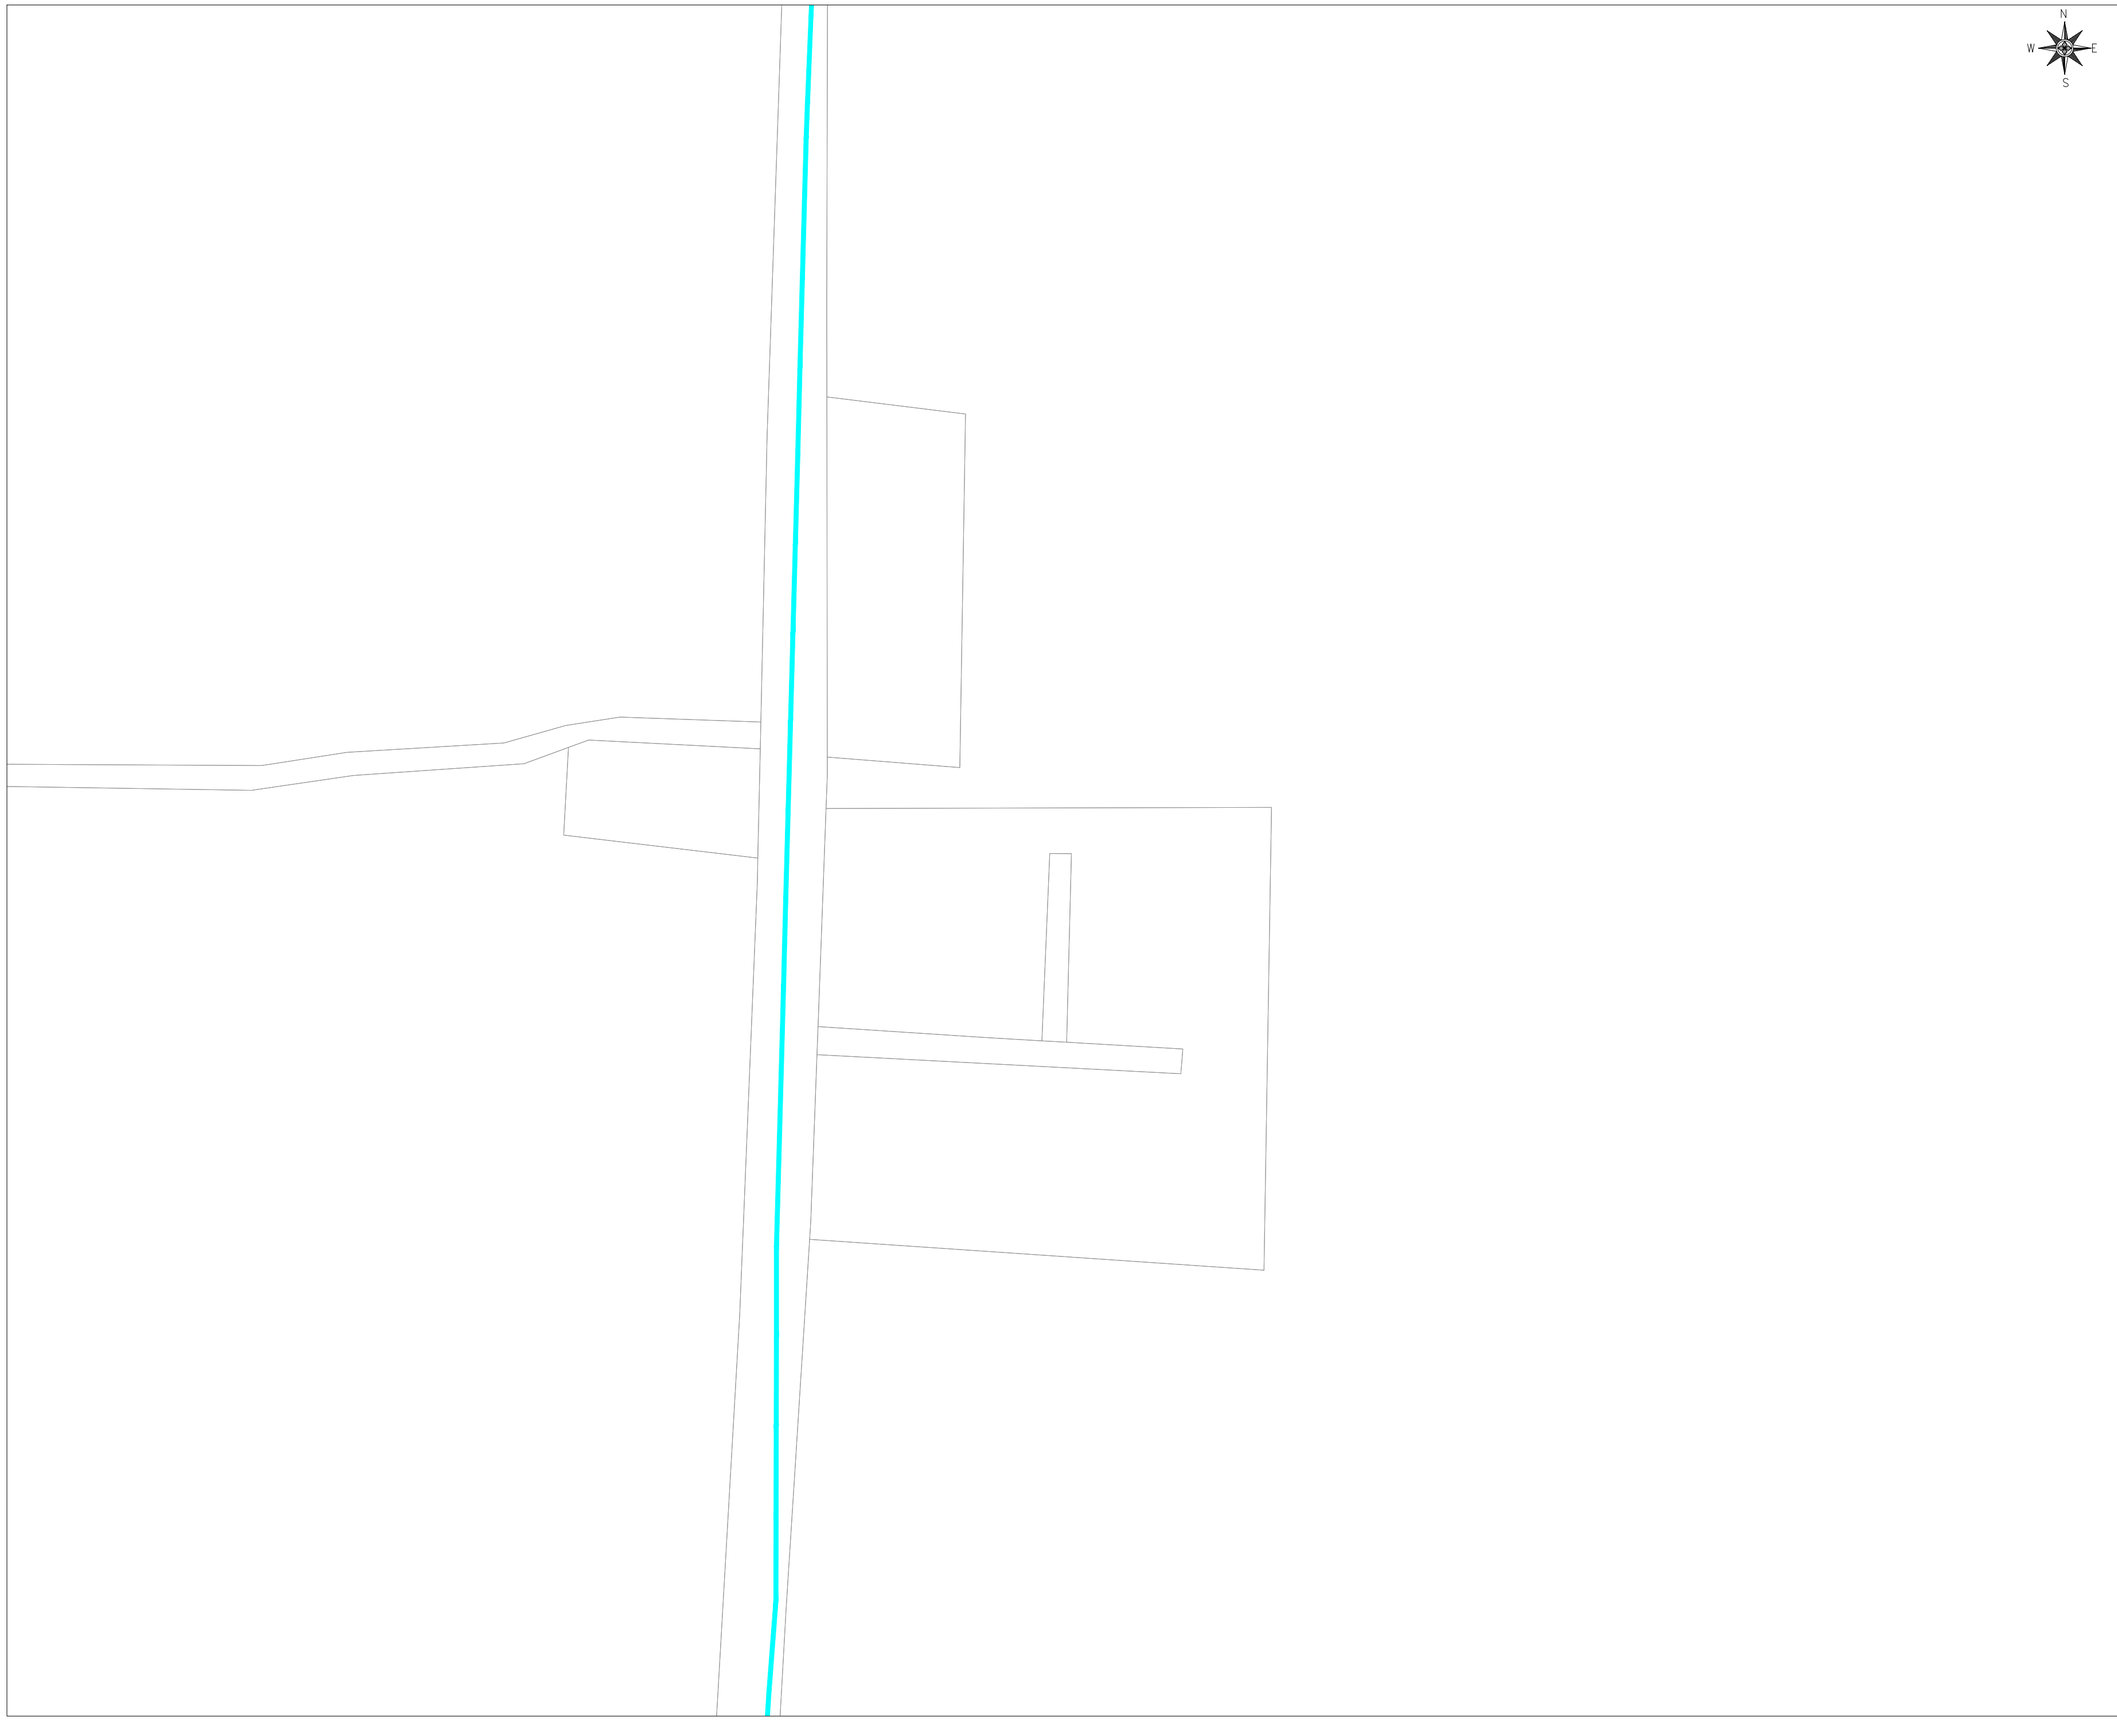

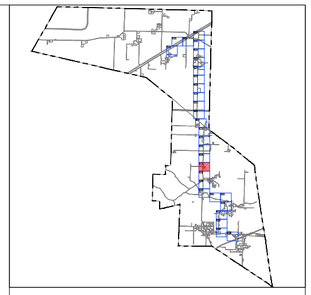

KEY PLAN

LEGEND:

110mm Ø PN - 8 HDPE PIPE

MS PIPE

SLUICE VALVE

WASHOUT VALVE

AIR RELEASE VALVE

PROPOSED STAND POST TYPE-I

PROPOSED TUBE WELL

BOUNDARY

VILLAGE:

Akanwali Khurd&Sher Mohammad&Khober&Kartar Singh(MVS)(BWN)

TITLE.

WATER SUPPLY SYSTEM LAYOUT PLAN-19

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	12-01-2026	DETAILED DESIGN	ASAD	ENGR. FAEIZ	ENGR. IHSAN-UL HAQ
02					
03					
04					
05					
06					
07					

DRAWING N°: PRMSC-BWN-AKK-WS-LP-19

SHEET 19 OF 29

REV 00

PROJECT:

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:

PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT

ASIAN CONSULTING ENGINEERS (PVT) LTD. www.asiancon.com

ENVIRONMENTAL TECHNOLOGIES

PRMSC-BWN-AKK-WS-LP-19

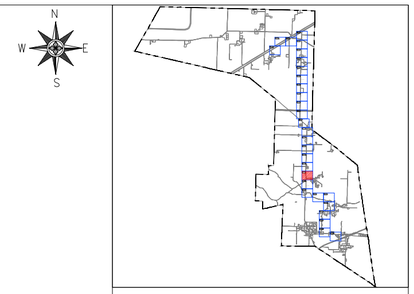

KEY PLAN

LEGEND:

110mm Ø PN - 8 HDPE PIPE

MS PIPE

SLUICE VALVE

WASHOUT VALVE

AIR RELEASE VALVE

PROPOSED STAND POST TYPE-I

PROPOSED TUBE WELL

BOUNDARY

STAND POST WW
SEEPAGE CHAMBER
REF:PRMSC-WS-TD-04A

Ø4" uPVC PIPE

STAND POST
TYPE - I
REF:PRMSC-WS-SP-C-02

Ø110mm

53'

Ø110mm

559'

VILLAGE:
Akanwali Khurd&Sher Mohammad&Khober&Kartar Singh(MVS)(BWN)

TITLE.
WATER SUPPLY SYSTEM
LAYOUT PLAN-20

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	12-01-2026	DETAILED DESIGN	ASAD	ENGR. FAEIZ	ENGR. IHSAN-UL HAQ
02					
03					
04					
05					
06					
07					

DRAWING N°:
PRMSC-BWN-AKK-WS-LP-20

SHEET
20 OF 29

REV
00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT
ASIAN CONSULTING ENGINEERS (PVT) LTD. www.asiancon.com

PRMSC-BWN-AKK-WS-LP-20

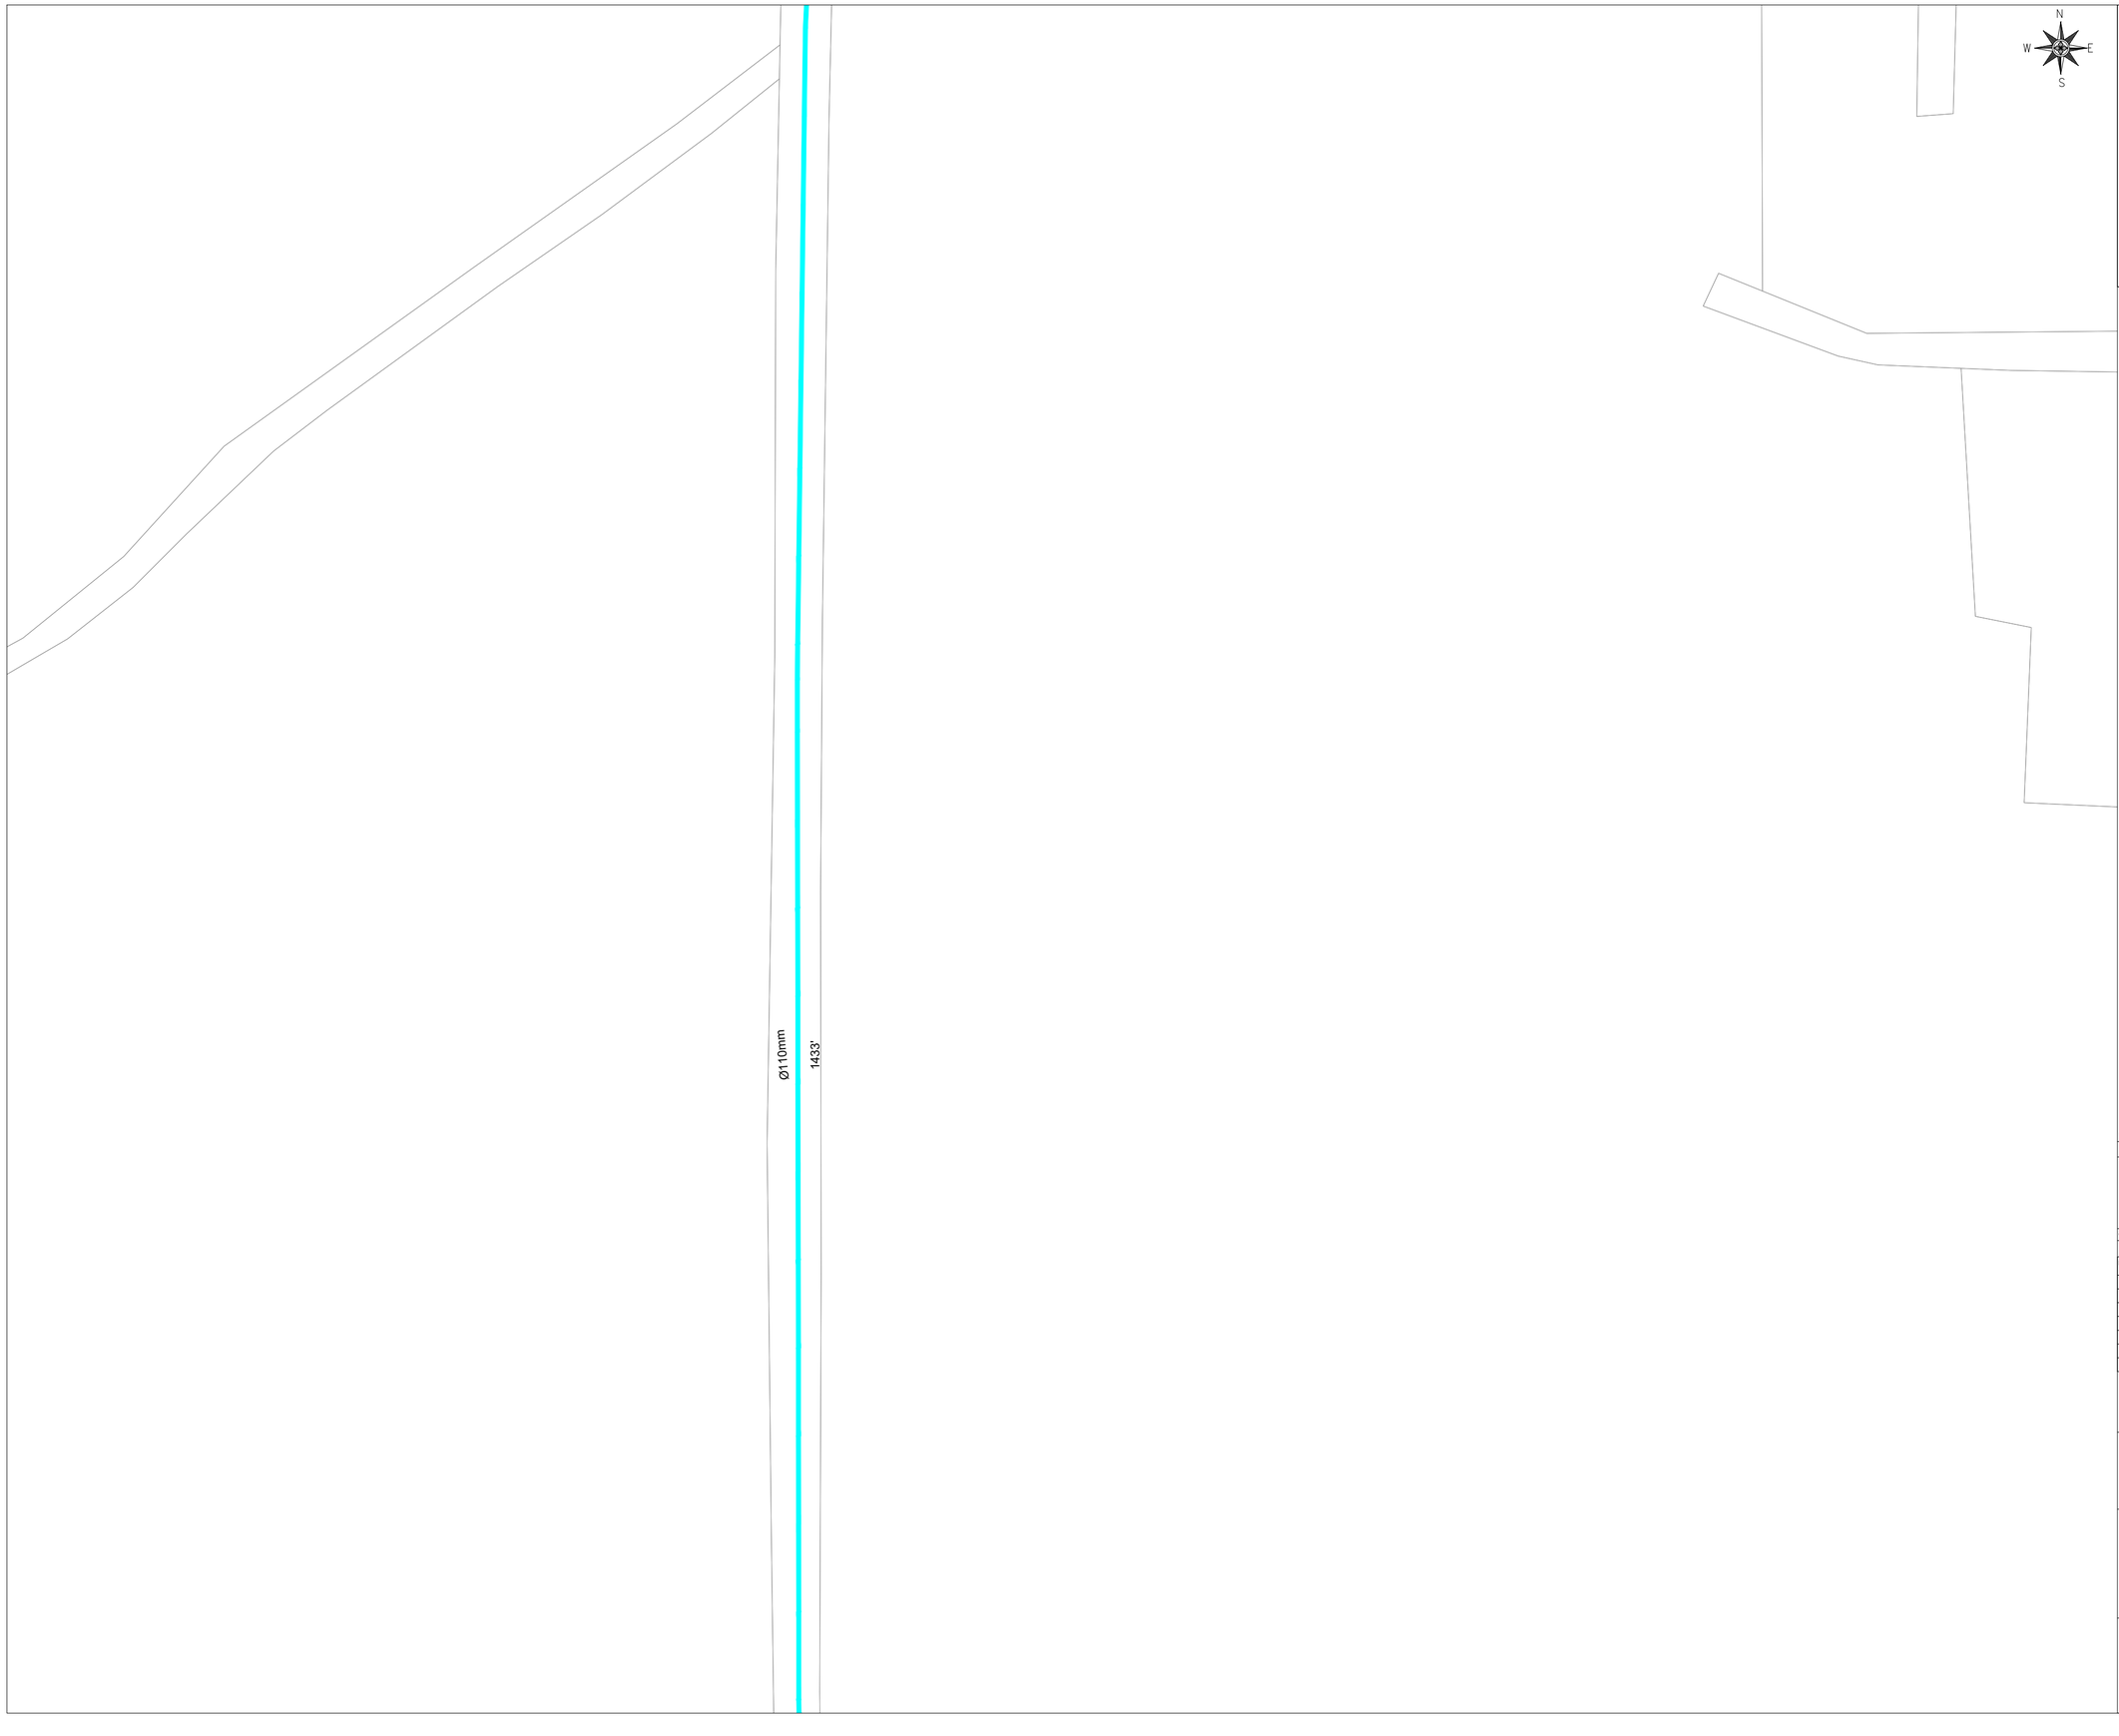

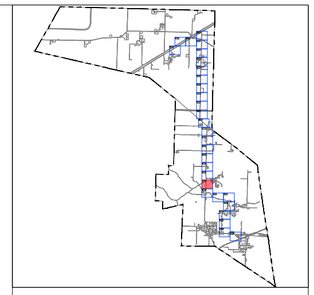

KEY PLAN

LEGEND:

- 110mm Ø PN - 8 HDPE PIPE
- MS PIPE
- SLUICE VALVE
- WASHOUT VALVE
- AIR RELEASE VALVE
- PROPOSED STAND POST TYPE-I
- PROPOSED TUBE WELL
- BOUNDARY

VILLAGE:

Akanwali Khurd&Sher Mohammad&Khober&Kartar Singh(MVS)(BWN)

TITLE.

WATER SUPPLY SYSTEM LAYOUT PLAN-21

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	12-01-2026	DETAILED DESIGN	ASAD	ENGR. FAEIZ	ENGR. IHSAN-UL HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-AKK-WS-LP-21	21 OF 29	00

PROJECT:

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:

PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT

ASIAN CONSULTING ENGINEERS www.asiancon.com

PRMSC-BWN-AKK-WS-LP-21

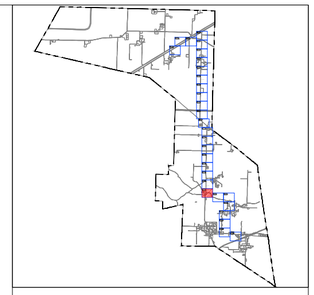

KEY PLAN

LEGEND:

- 110mm Ø PN - 8 HDPE PIPE
- MS PIPE
- SLUICE VALVE
- WASHOUT VALVE
- AIR RELEASE VALVE
- PROPOSED STAND POST TYPE-I
- PROPOSED TUBE WELL
- BOUNDARY

VILLAGE:

Akanwali Khurd&Sher Mohammad&Khober&Kartar Singh(MVS)(BWN)

TITLE.

WATER SUPPLY SYSTEM LAYOUT PLAN-22

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	12-01-2026	DETAILED DESIGN	ASAD	ENGR. FAEIZ	ENGR. IHSAN-UL HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº: PRMSC-BWN-AKK-WS-LP-22

SHEET 22 OF 29

REV 00

PROJECT:

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:

PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT

ASIAN CONSULTING ENGINEERS www.asiancon.com.pk

ENVIRONMENTAL TECHNOLOGIES

PRMSC-BWN-AKK-WS-LP-22

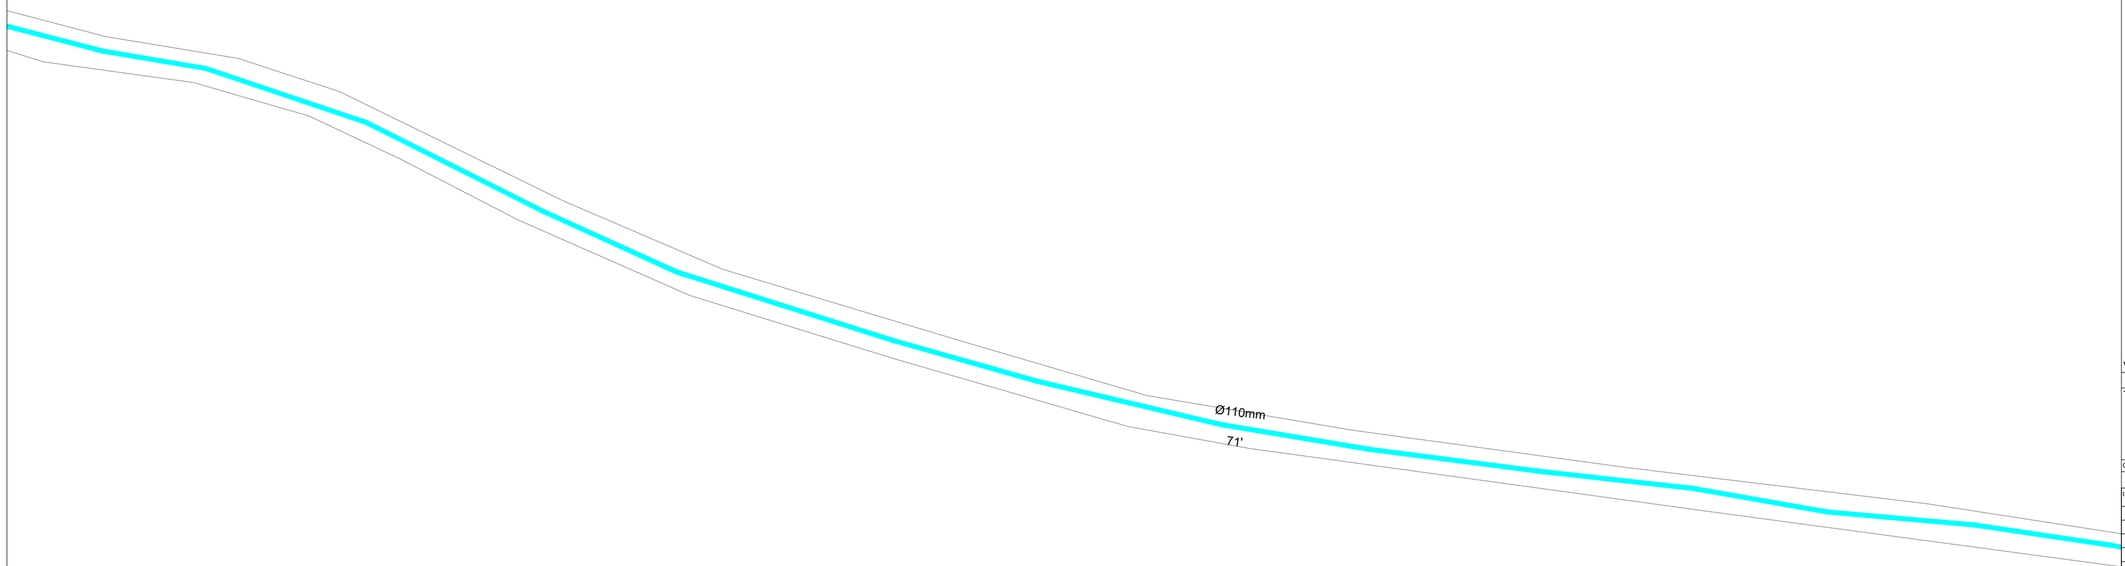

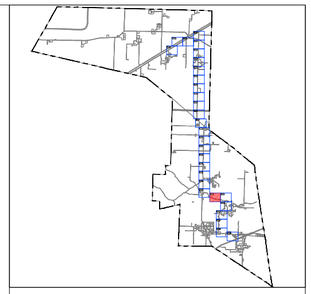

KEY PLAN

LEGEND:

110mm Ø PN - 8 HDPE PIPE

MS PIPE

SLUICE VALVE

WASHOUT VALVE

AIR RELEASE VALVE

PROPOSED STAND POST TYPE-I

PROPOSED TUBE WELL

BOUNDARY

VILLAGE:

Akanwali Khurd&Sher Mohammad&Khober&Kartar Singh(MVS)(BWN)

TITLE.

WATER SUPPLY SYSTEM LAYOUT PLAN-23

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	12-01-2026	DETAILED DESIGN	ASAD	ENGR. FAEIZ	ENGR. IHSAN-UL HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:

PRMSC-BWN-AKK-WS-LP-23

SHEET 23 OF 29

REV 00

PROJECT:

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:

PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT

ASIAN CONSULTING ENGINEERS www.asianconsultingengineers.com.pk

PRMSC-BWN-AKK-WS-LP-23

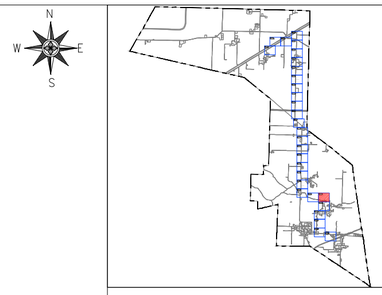

KEY PLAN

LEGEND:

110mm Ø PN - 8 HDPE PIPE

MS PIPE

SLUICE VALVE

WASHOUT VALVE

AIR RELEASE VALVE

PROPOSED STAND POST TYPE-I

PROPOSED TUBE WELL

BOUNDARY

PRMSC-BWN-AKK-WS-LP-24

VILLAGE:

Akanwali Khurd&Sher Mohammad&Khober&Kartar Singh(MVS)(BWN)

TITLE.

WATER SUPPLY SYSTEM LAYOUT PLAN-24

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	12-01-2026	DETAILED DESIGN	ASAD	ENGR. FAEIZ	ENGR. IHSAN-UL HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-AKK-WS-LP-24	24 OF 29	00

PROJECT:

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:

PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT

ASIAN CONSULTING ENGINEERS www.asiancon.com.pk

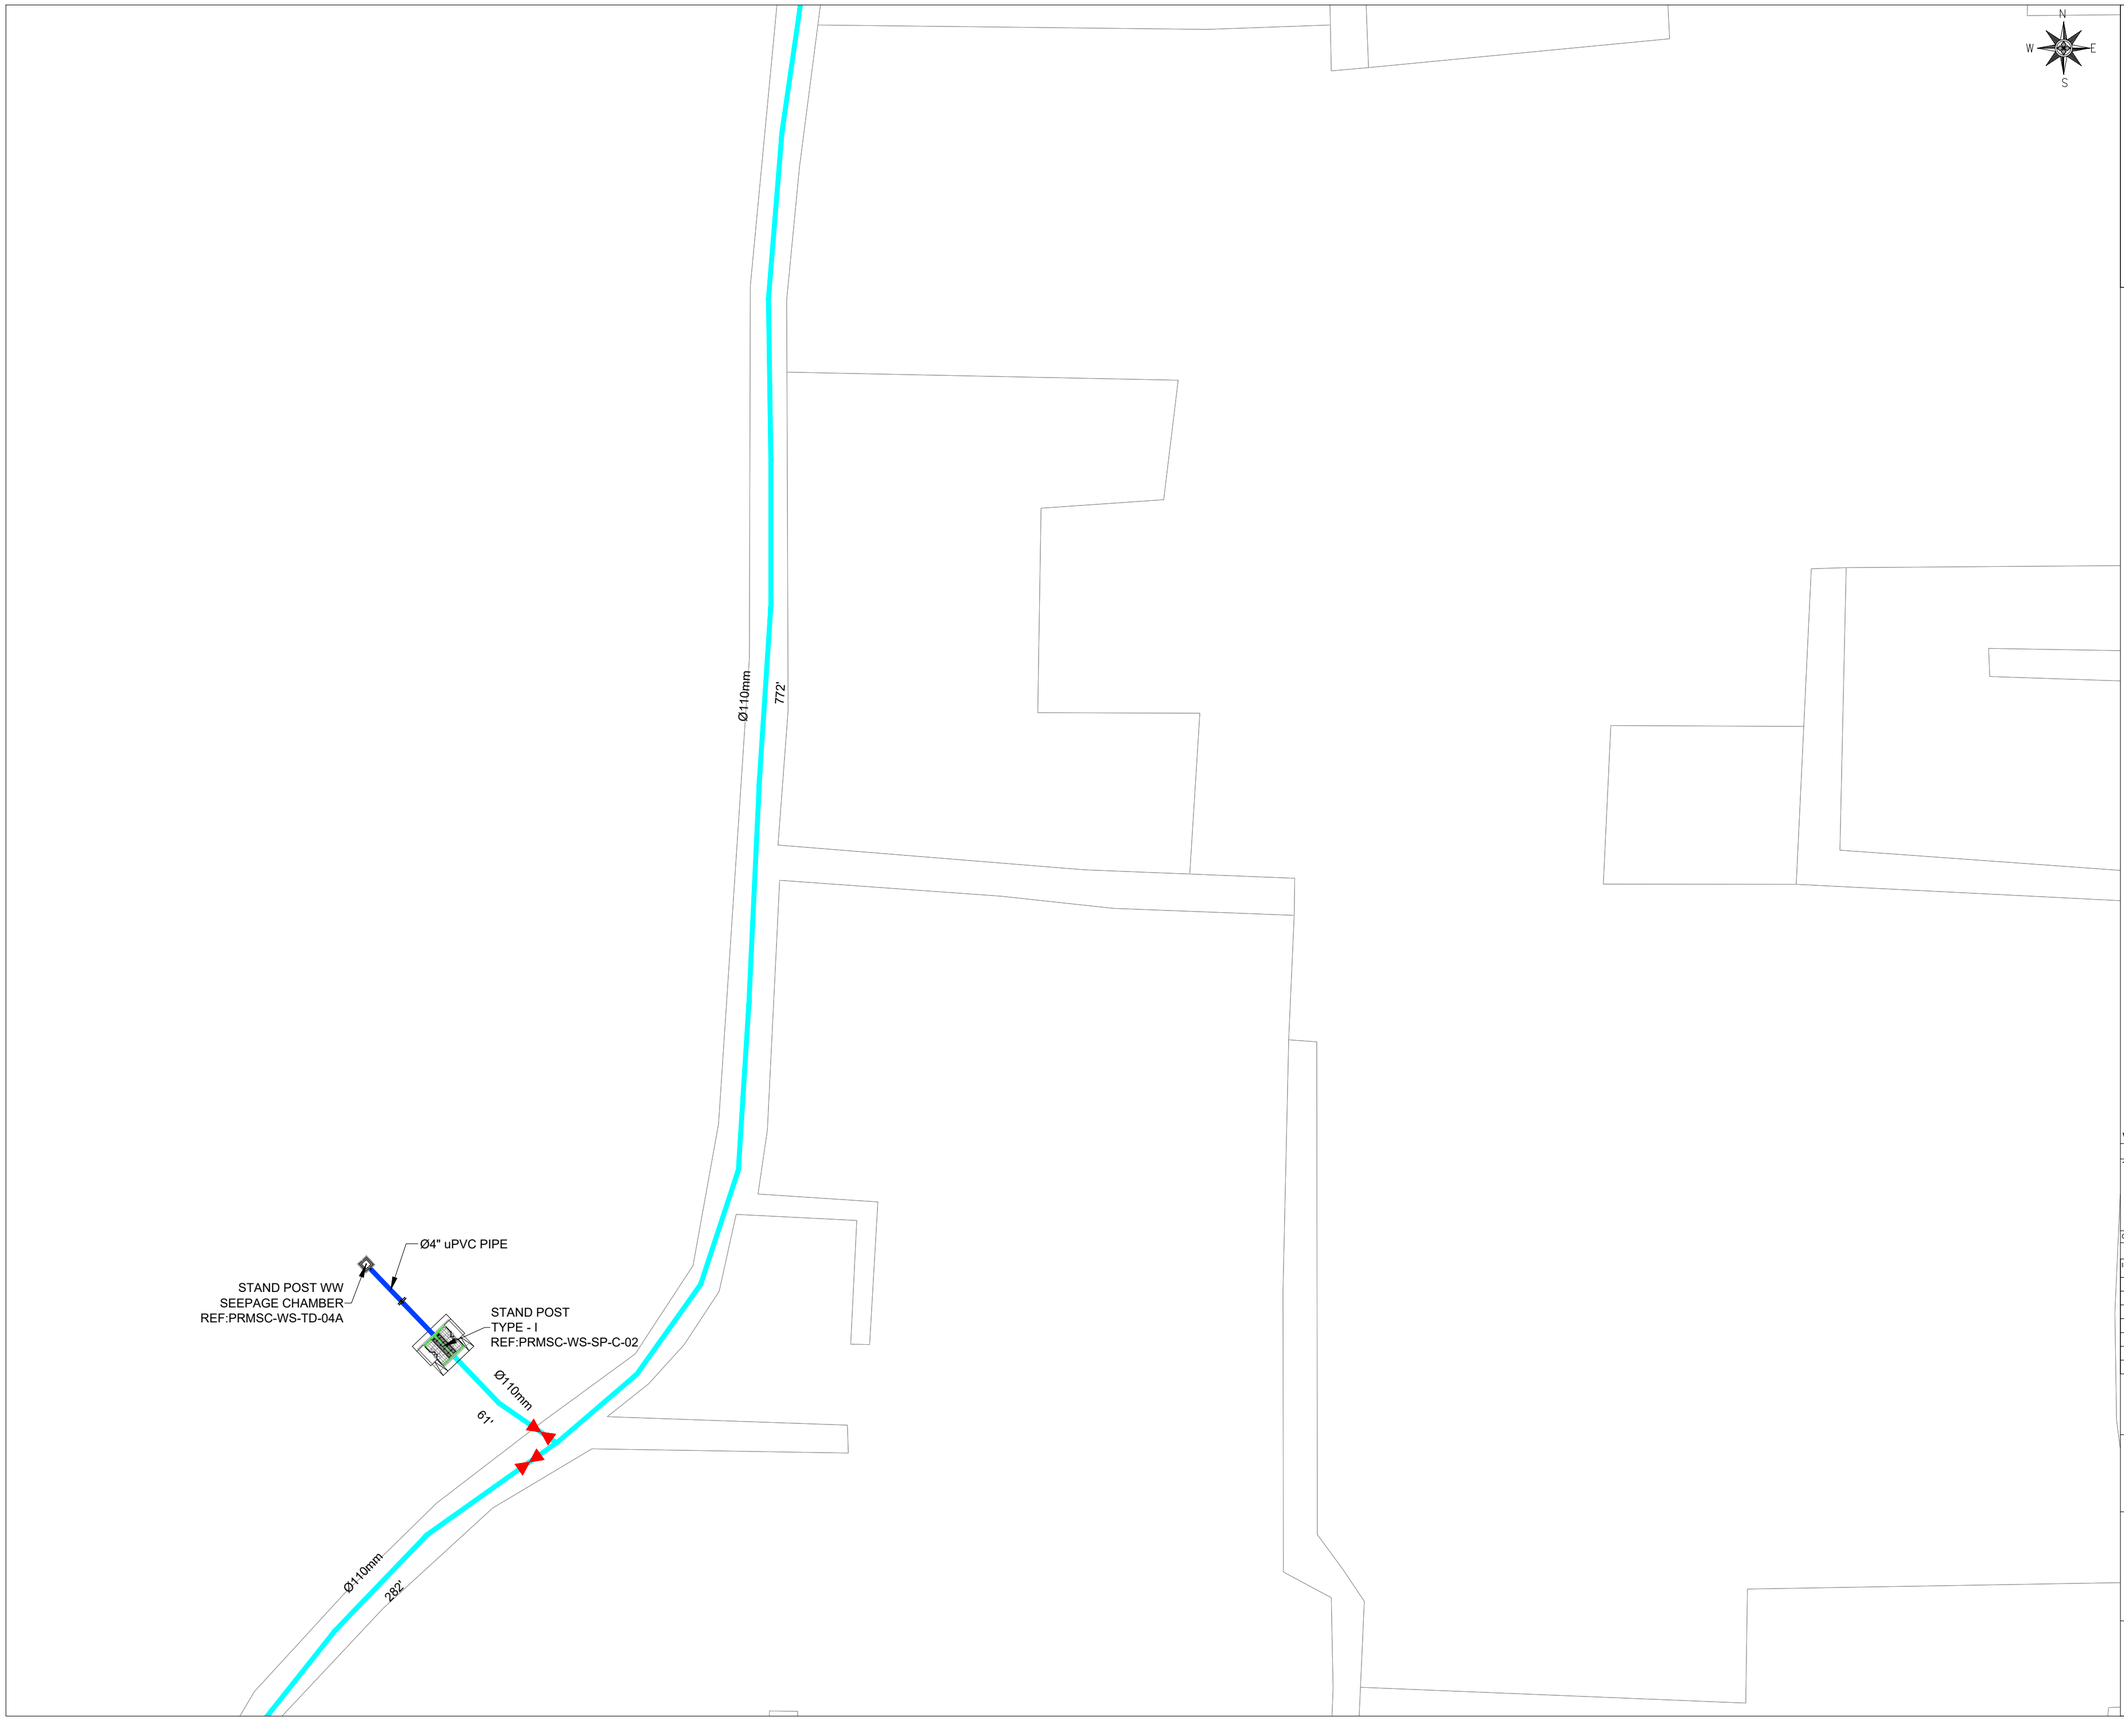

KEY PLAN

LEGEND:

- 110mm Ø PN - 8 HDPE PIPE
- MS PIPE
- SLUICE VALVE
- WASHOUT VALVE
- AIR RELEASE VALVE
- PROPOSED STAND POST TYPE-I
- PROPOSED TUBE WELL
- BOUNDARY

VILLAGE:

Akanwali Khurd&Sher Mohammad&Khober&Kartar Singh(MVS)(BWN)

TITLE:

WATER SUPPLY SYSTEM LAYOUT PLAN-25

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	12-01-2026	DETAILED DESIGN	ASAD	ENGR FARIZ	ENGR HSAN-UL HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-AKK-WS-LP-25	25 OF 29	00

PROJECT:

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:

PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT

ARE ENVIRONMENTAL RESOURCES | ASIAN CONSULTING ENGINEERS www.asiancon.com.pk

PRMSC-BWN-AKK-WS-LP-25

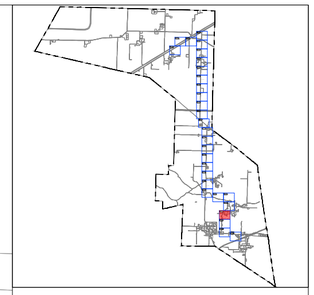

KEY PLAN

LEGEND:

- 110mm Ø PN - 8 HDPE PIPE
- MS PIPE
- SLUICE VALVE
- WASHOUT VALVE
- AIR RELEASE VALVE
- PROPOSED STAND POST TYPE-I
- PROPOSED TUBE WELL
- BOUNDARY

VILLAGE:

Akanwali Khurd&Sher Mohammad&Khober&Kartar Singh(MVS)(BWN)

TITLE.

WATER SUPPLY SYSTEM LAYOUT PLAN-26

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	12-01-2026	DETAILED DESIGN	ASAD	ENGR FAEIZ	ENGR IHSAN-UL HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-AKK-WS-LP-26	26 OF 29	00

PROJECT:

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:

PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT

ASIAN CONSULTING ENGINEERS www.asianceb.com

PRMSC-BWN-AKK-WS-LP-26

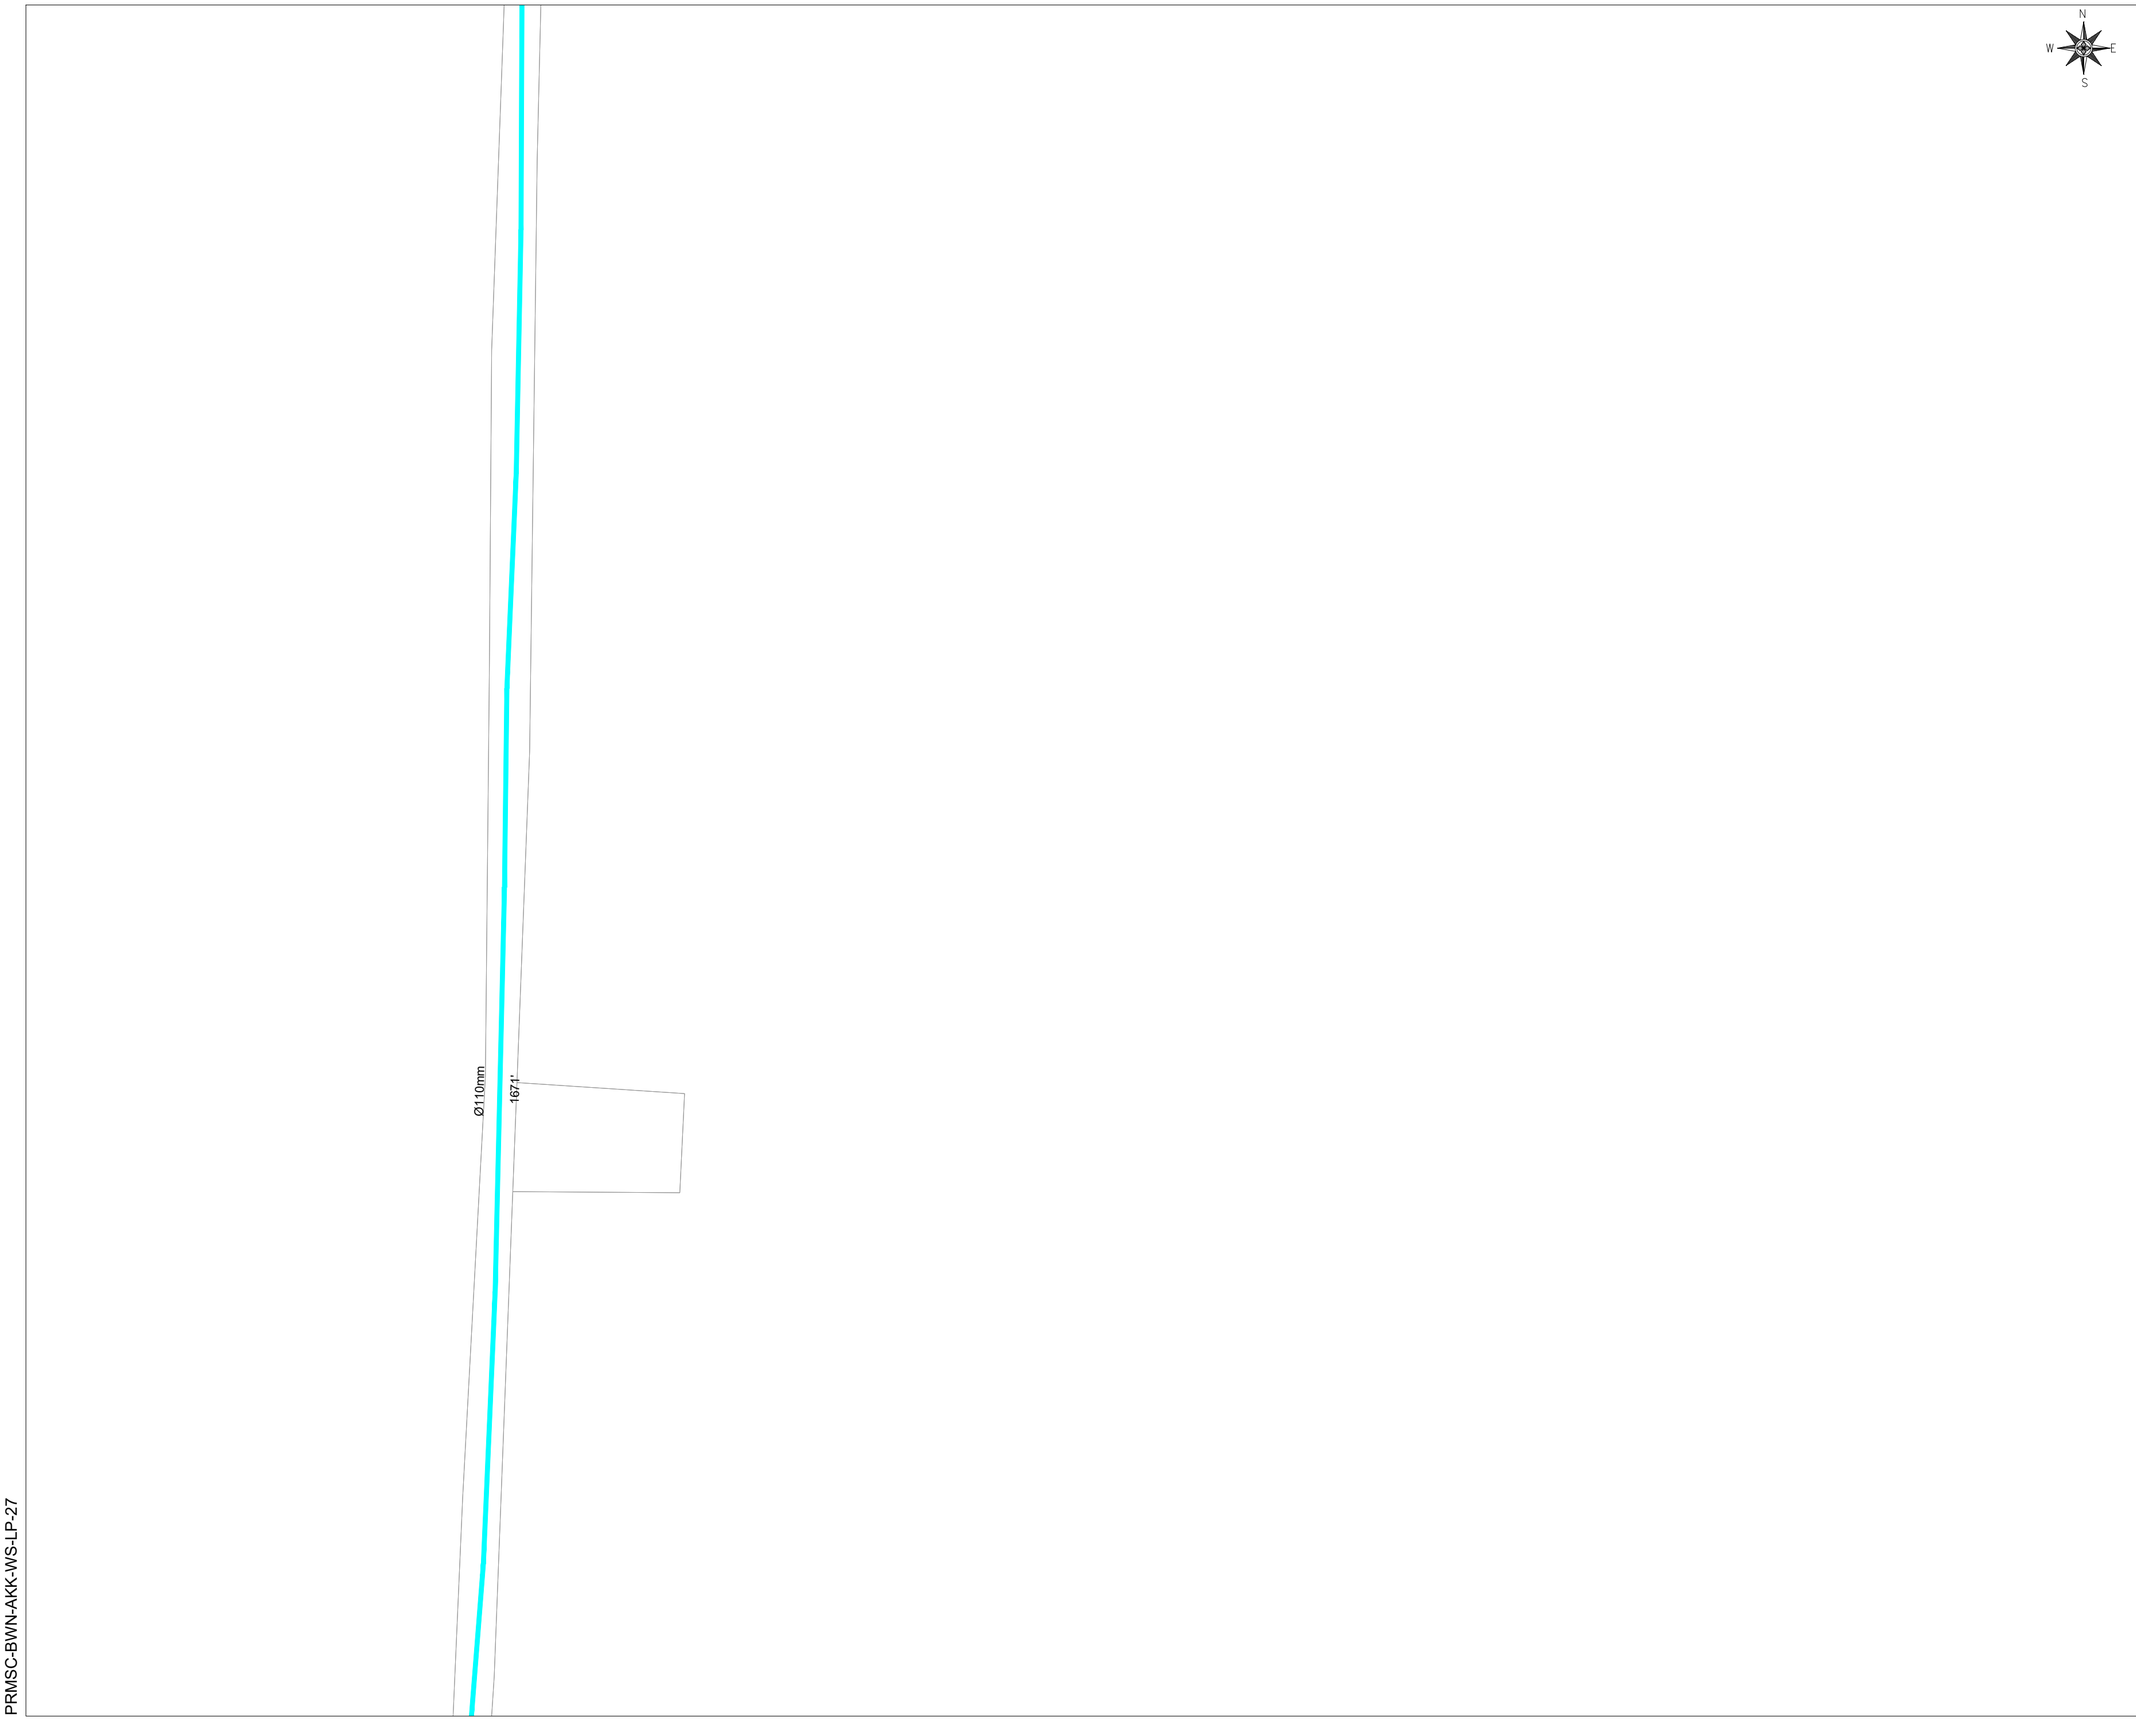

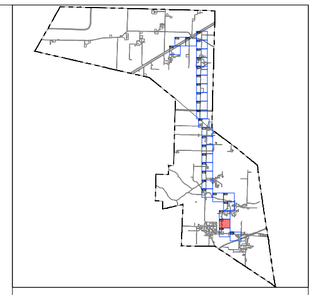

KEY PLAN

LEGEND:

110mm Ø PN - 8 HDPE PIPE

MS PIPE

SLUICE VALVE

WASHOUT VALVE

AIR RELEASE VALVE

PROPOSED STAND POST TYPE-I

PROPOSED TUBE WELL

BOUNDARY

VILLAGE:

Akanwali Khurd&Sher Mohammad&Khober&Kartar Singh(MVS)(BWN)

TITLE.

WATER SUPPLY SYSTEM LAYOUT PLAN-27

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	D E S C R I P T I O N	DRAWN	DESIGNED	APPROVED
01	12-01-2026	DETAILED DESIGN	ASAD	ENGR. FAEIZ	ENGR. IHSAN UL HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:

PRMSC-BWN-AKK-WS-LP-27

SHEET 27 OF 29

REV 00

PROJECT:

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:

PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT

ASIAN CONSULTING ENGINEERS www.asiancon.com

PRMSC-BWN-AKK-WS-LP-27

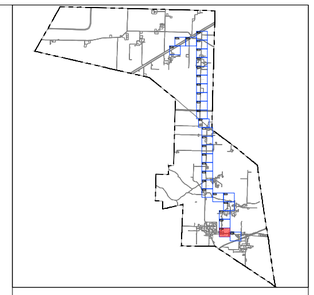

KEY PLAN

LEGEND:

- 110mm Ø PN - 8 HDPE PIPE
- MS PIPE
- SLUICE VALVE
- WASHOUT VALVE
- AIR RELEASE VALVE
- PROPOSED STAND POST TYPE-I
- PROPOSED TUBE WELL
- BOUNDARY

VILLAGE:
Akanwali Khurd&Sher Mohammad&Khober&Kartar Singh(MVS)(BWN)

TITLE.

WATER SUPPLY SYSTEM LAYOUT PLAN-28

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	12-01-2026	DETAILED DESIGN	ASAD	ENGR. FAEIZ	ENGR. IHSAN-UL HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-AKK-WS-LP-28	28 OF 29	00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT
ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

PRMSC-BWN-AKK-WS-LP-28

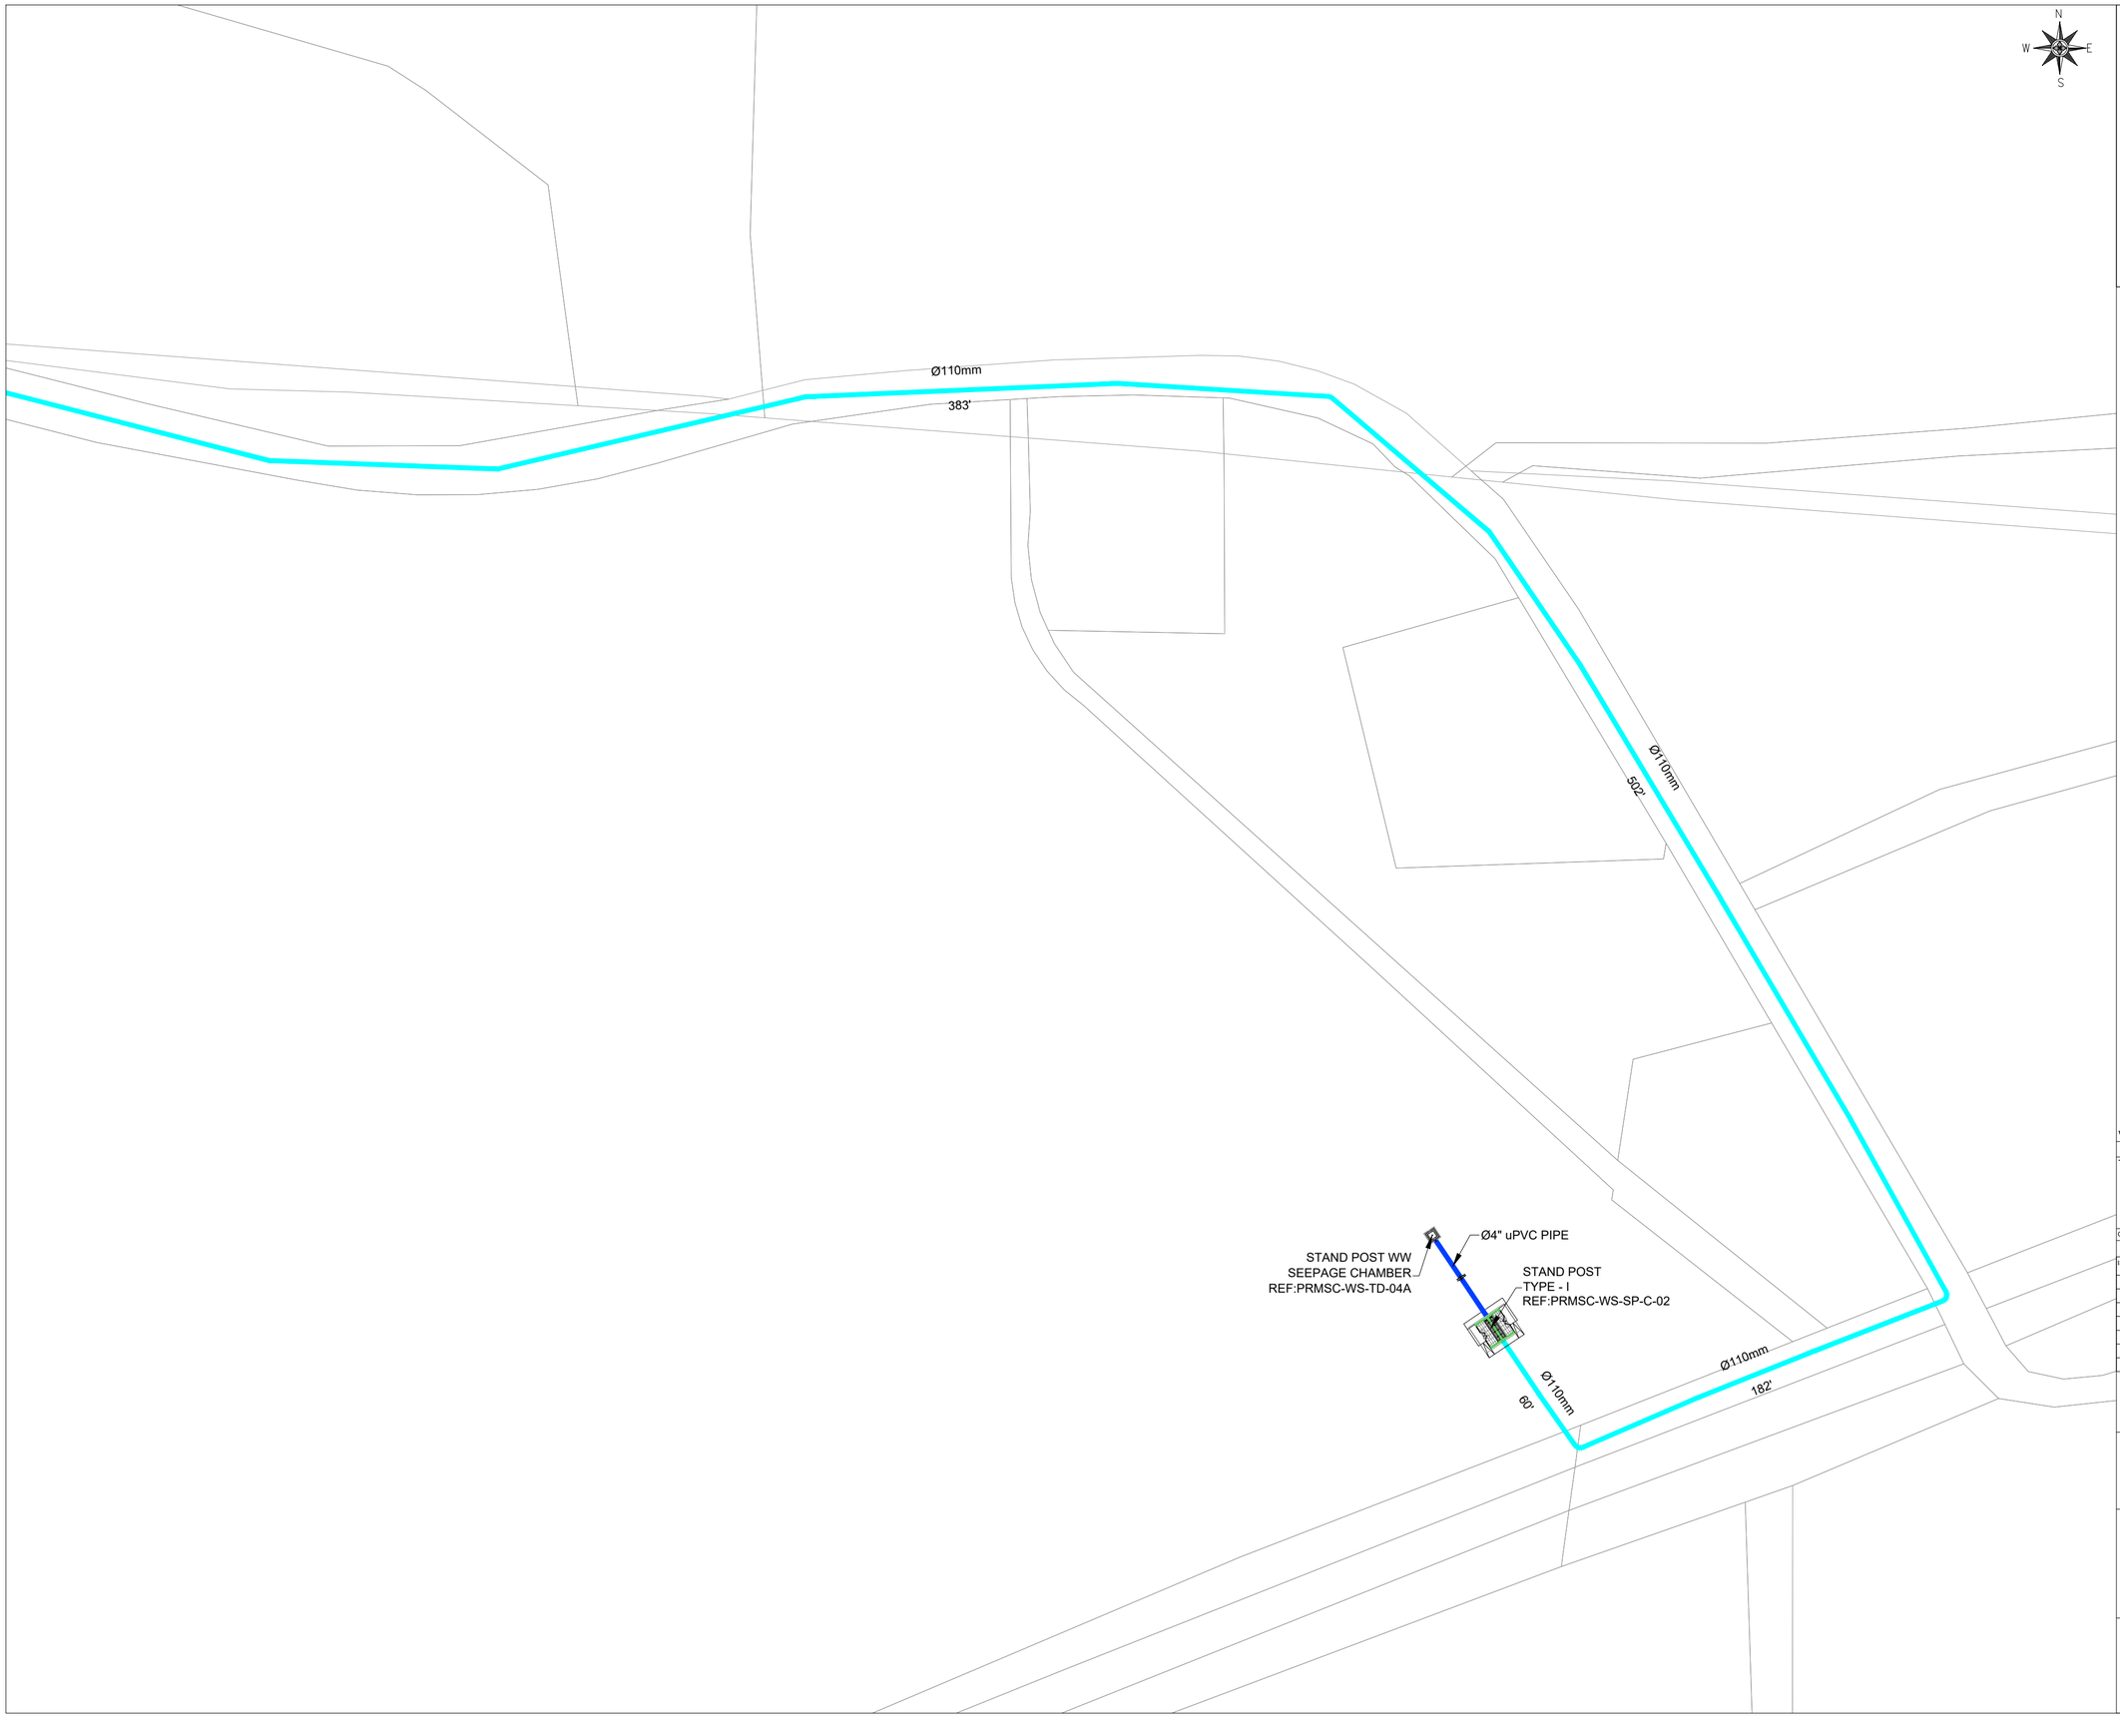

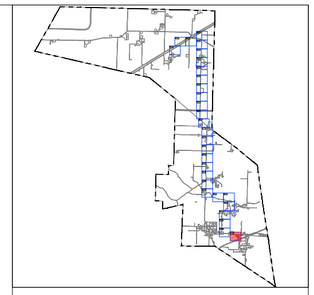

KEY PLAN

LEGEND:

- 110mm Ø PN - 8 HDPE PIPE
- MS PIPE
- SLUICE VALVE
- WASHOUT VALVE
- AIR RELEASE VALVE
- PROPOSED STAND POST TYPE-I
- PROPOSED TUBE WELL
- BOUNDARY

VILLAGE:

Akanwali Khurd&Sher Mohammad&Khober&Kartar Singh(MVS)(BWN)

TITLE.

WATER SUPPLY SYSTEM LAYOUT PLAN-29

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	12-01-2026	DETAILED DESIGN	ASAD	ENGR FAEIZ	ENGR IHSAN-UL HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-AKK-WS-LP-29	29 OF 29	00

PROJECT:

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:

PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT

ASIAN CONSULTING ENGINEERS www.asiancon.com

PRMSC-BWN-AKK-WS-LP-29

DHARAM PURA,HIRA BASHNOAI

KEY PLAN

Revenue Village: DS DP HB Settlement-1 Sheet-1

Title:
Proposed Water Supply Plan

Legend:

DISTRIBUTION NETWORK

90 mm Ø

SETTELMENT BOUNDARY

Scale: 1:1,700
1 inch = 142 feet
Paper Size: A3

0 40 80 160
Kilometers

Project:
Engineering Design & Construction Supervision, Punjab Rural Sustainable Water Supply & Sanitation Project, Cluster South-III

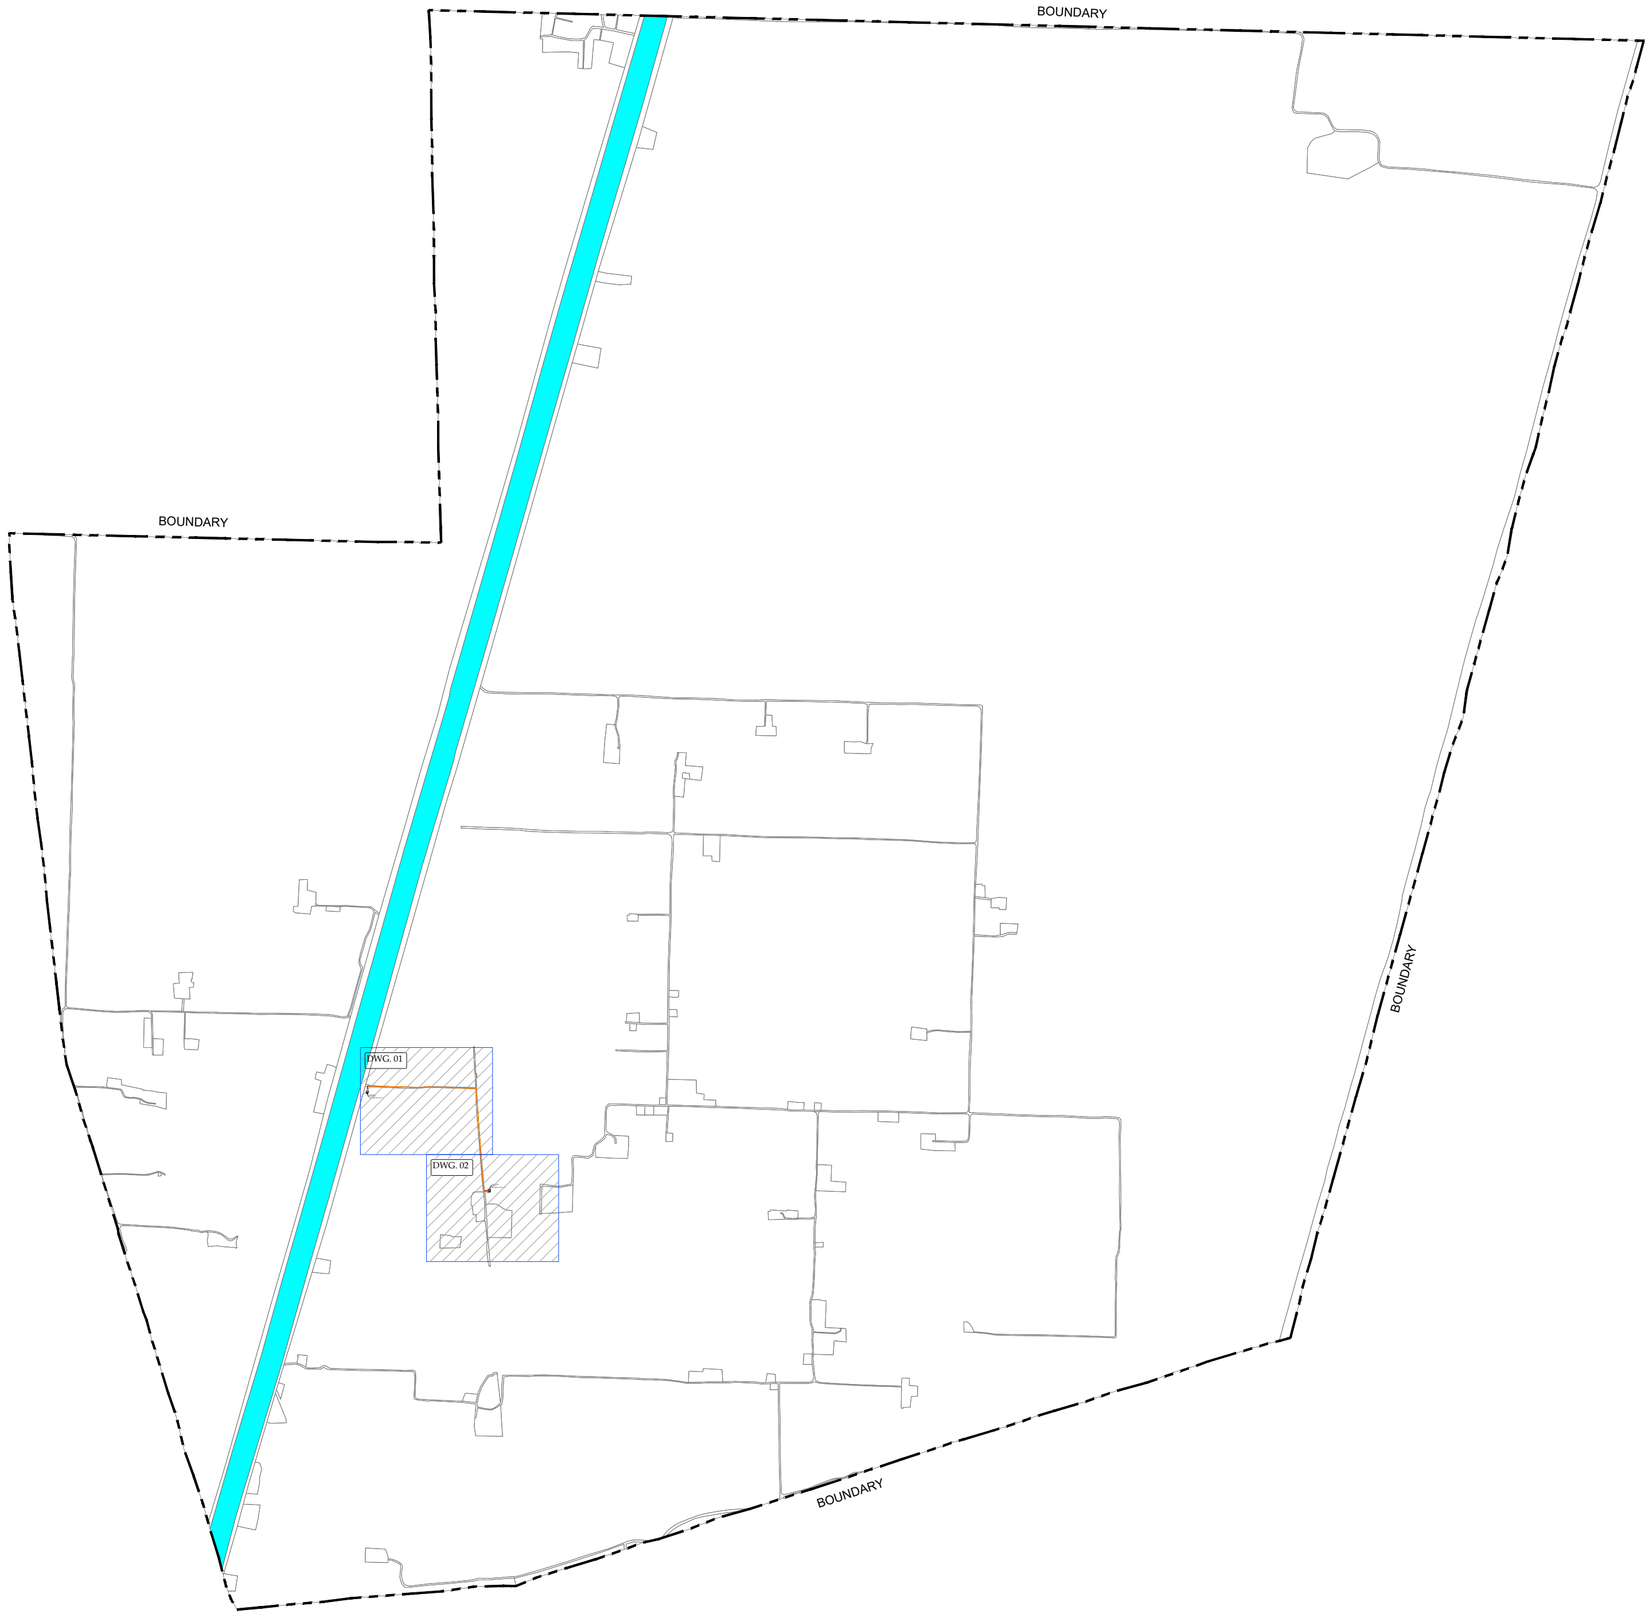

LEGEND:

- 90mm Ø HDPE PIPE
- SLUICE VALVE
- PROPOSED TUBE WELL
- PROPOSED STAND POST TYPE - I
- BOUNDARY

VILLAGE: DHARAM PURA & HIRA BASHNOI (BWN)

TITLE.

WATER SUPPLY SYSTEM KEY PLAN

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 800'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	19-02-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. HSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº: PRMSC-BWN-DPHB-WS-KP-00

SHEET 00 OF 00

REV 00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT
ASIAN CONSULTING ENGINEERS
www.asianconsultingengineers.com.pk

PRMSC-BWN-DPHB-WS-KP-00

LAYOUT PLAN

Revenue Village: DS DP HB Settlement-2 Sheet2

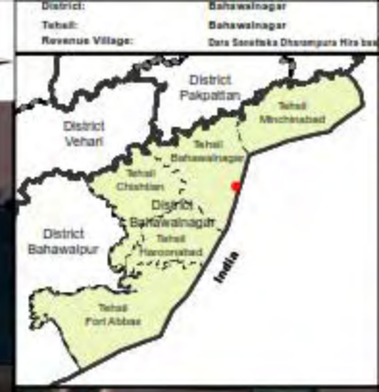

Title:
Proposed Water Supply Plan

Legend:

DISTRIBUTION NETWORK

- 90 mm Ø
- PROPOSED TUBEWELL
- STAND POST
- SETTELMENT BOUNDARY

Scale: 1:2,000
1 inch = 167 feet
Paper Size: A3

0 40 80 160
Kilometers

Project:
Engineering Design & Construction Supervision, Punjab Rural Sustainable Water Supply & Sanitation Project, Cluster South-III

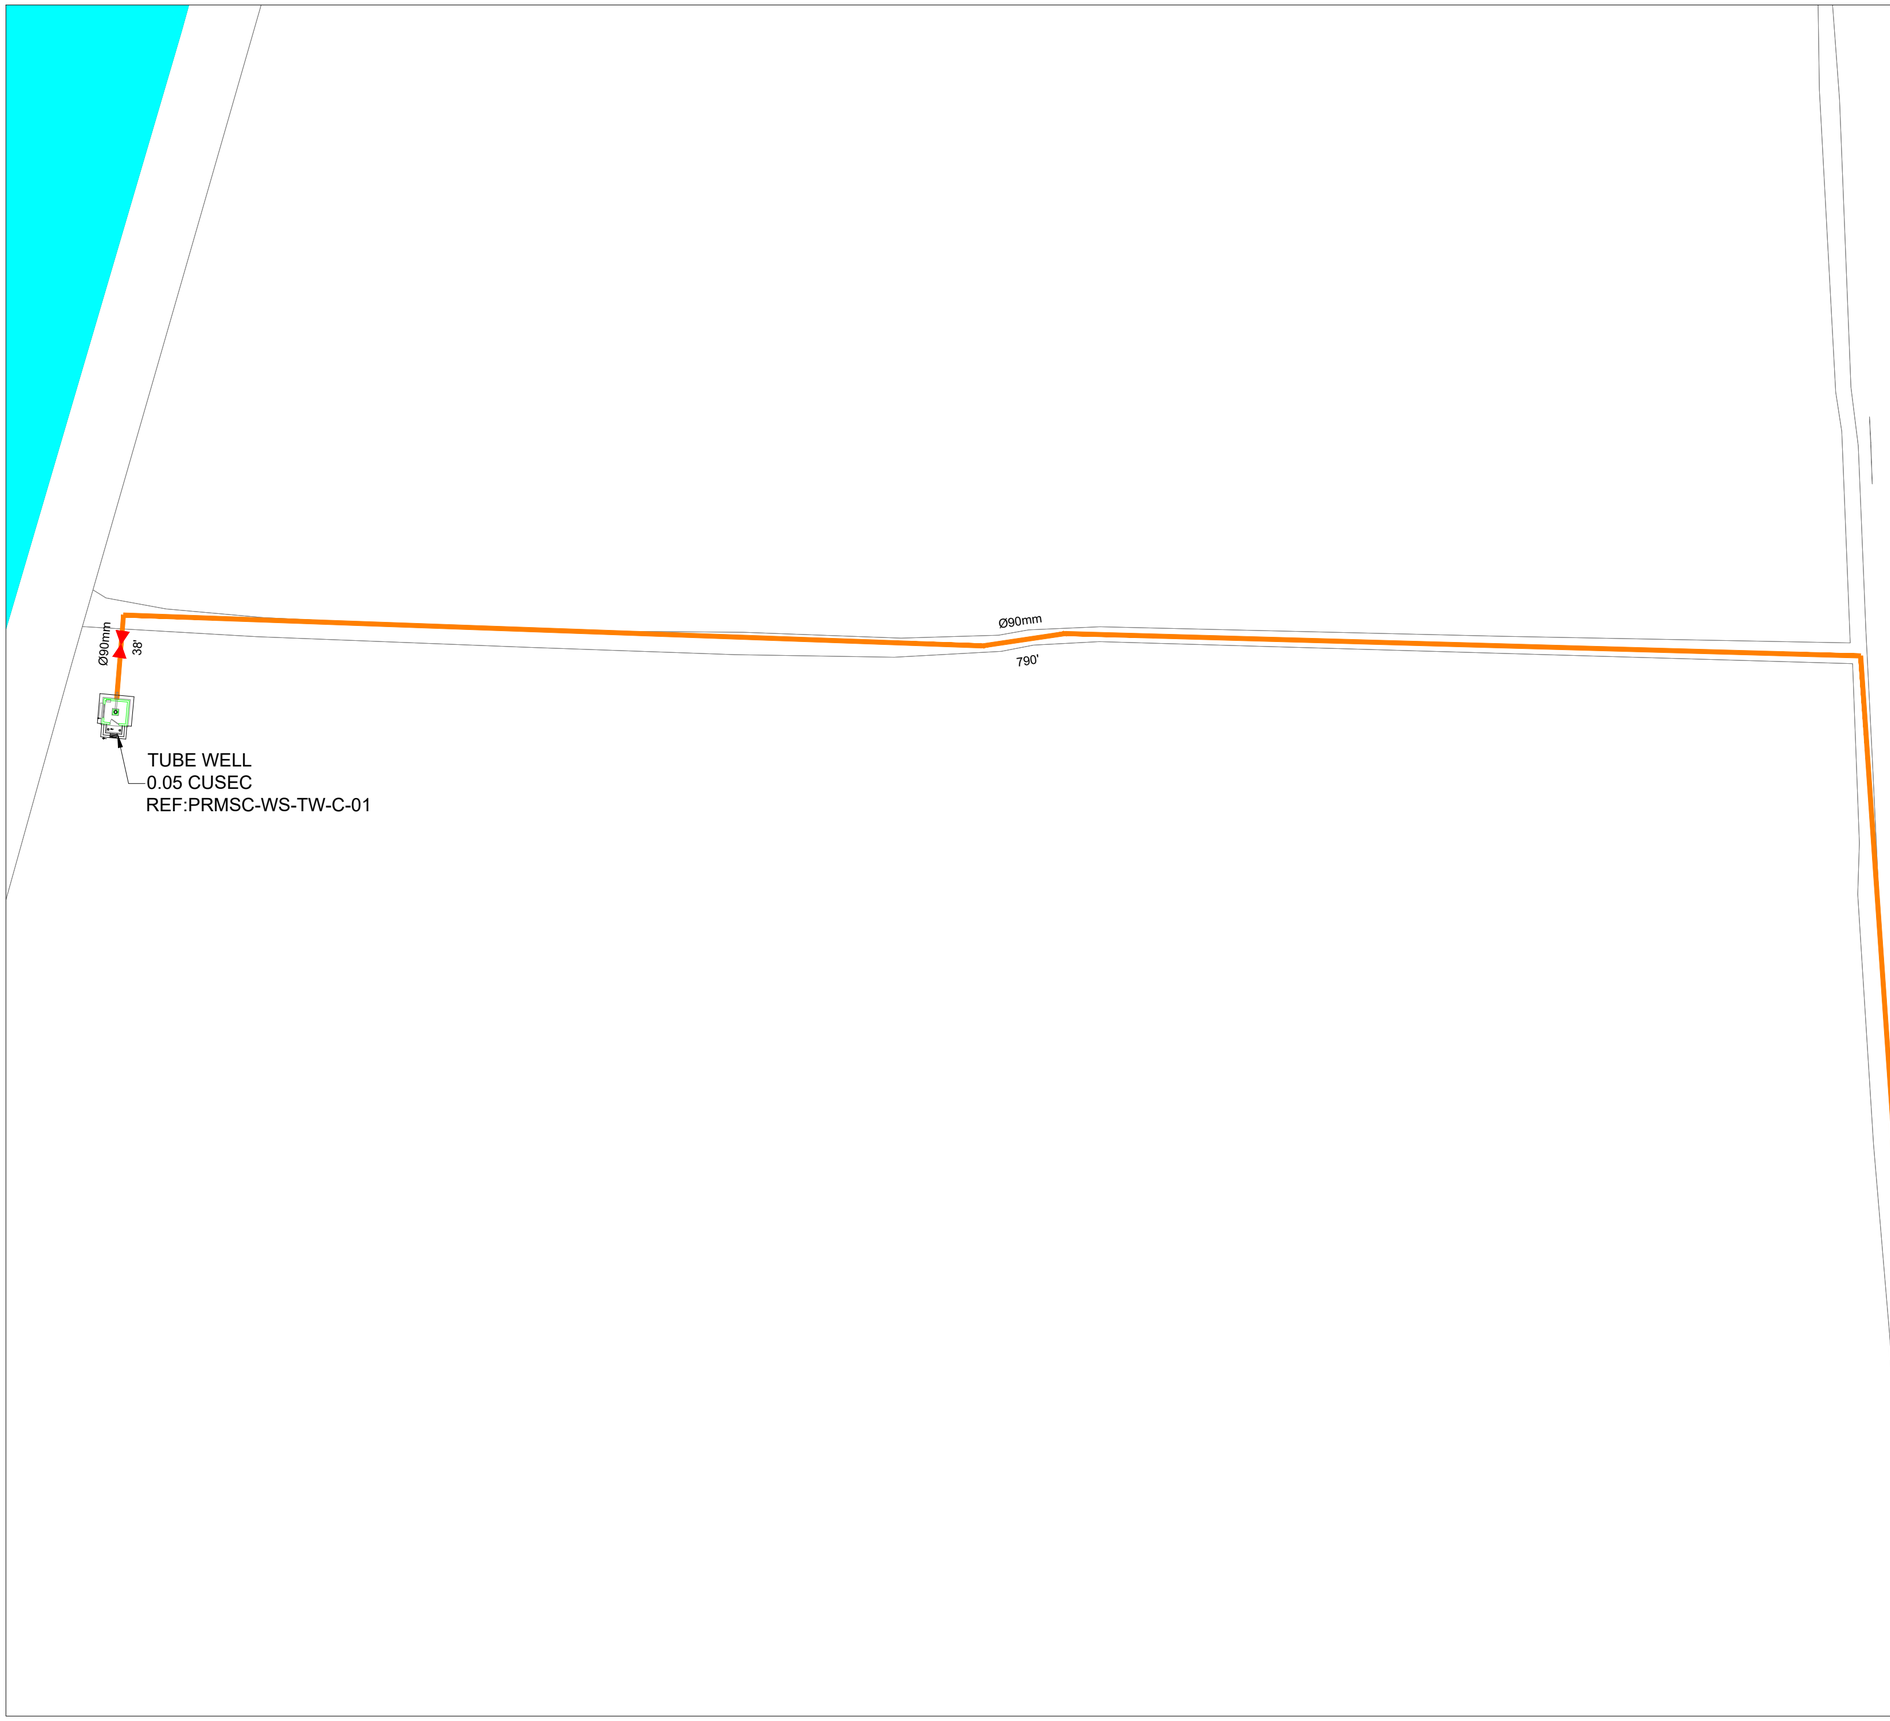

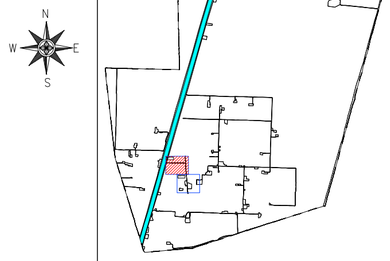

KEY PLAN

LEGEND:

- 90mm Ø HDPE PIPE
- SLUICE VALVE
- PROPOSED TUBE WELL
- PROPOSED STAND POST TYPE - I
- BOUNDARY

VILLAGE: DHARAM PURA & HIRA BASHNOI (BWN)

TITLE.

WATER SUPPLY SYSTEM LAYOUT PLAN-01

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	19-02-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-DPHB-WS-LP-01	01 OF 02	00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:
ASIAN CONSULTING ENGINEERS
www.asiancon.com.pv

PRMSC-BWN-DPHB-WS-LP-01

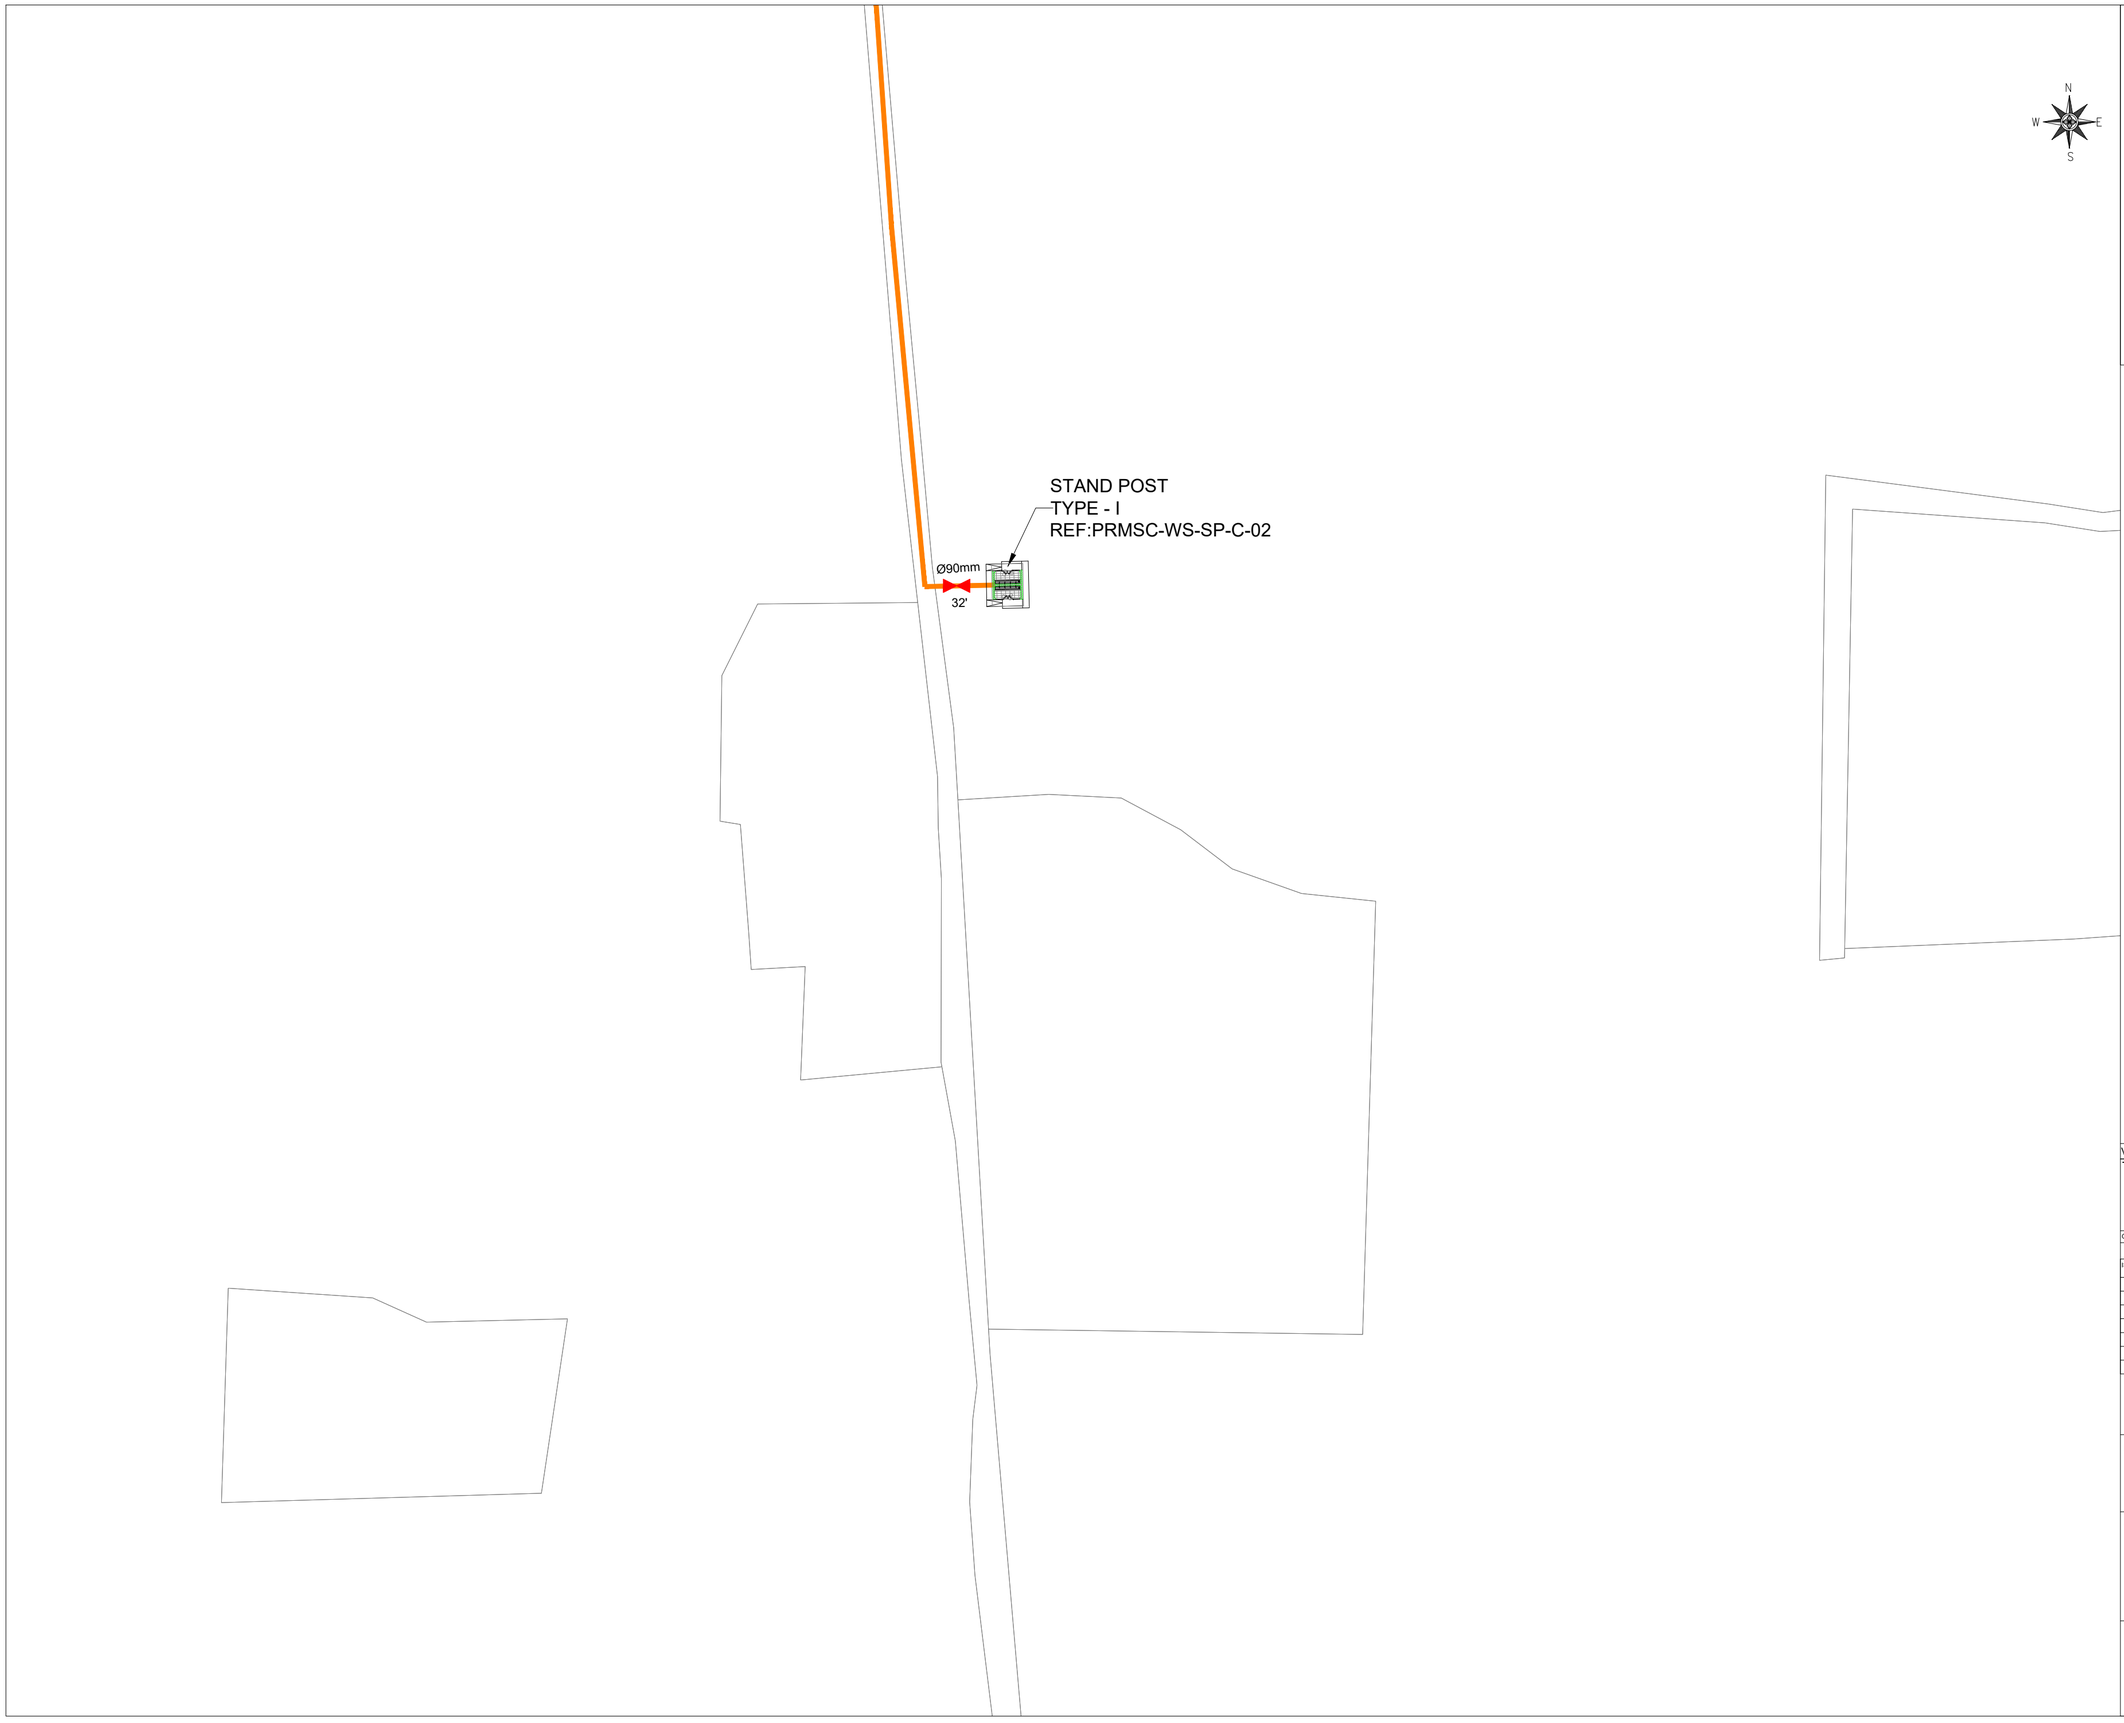

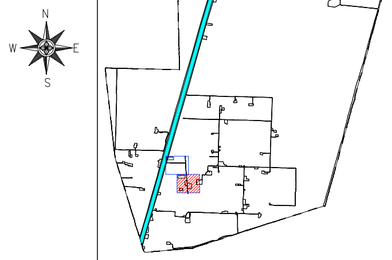

KEY PLAN

LEGEND:

- 90mm Ø HDPE PIPE
- SLUICE VALVE
- PROPOSED TUBE WELL
- PROPOSED STAND POST TYPE - I
- BOUNDARY

VILLAGE: DHARAM PURA & HIRA BASHNOI (BWN)

TITLE.

WATER SUPPLY SYSTEM LAYOUT PLAN-02

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	19-02-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-DPHB-WS-LP-02	02 OF 02	00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

PRMSC-BWN-DPHB-WS-LP-02

AMIN ABAD

KEY PLAN



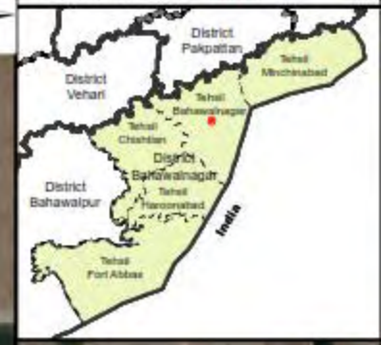

Title:
Proposed Water Supply Plan

Legend:

- SETTLEMENT
- RO PLANT
- SETTELMENT BOUNDARY

Scale: 1:1,000
1 inch = 83 feet
Paper Size: A3

0 40 80 160
Kilometers

Project:
Engineering Design & Construction Supervision, Punjab Rural Sustainable Water Supply & Sanitation Project, Cluster South-III

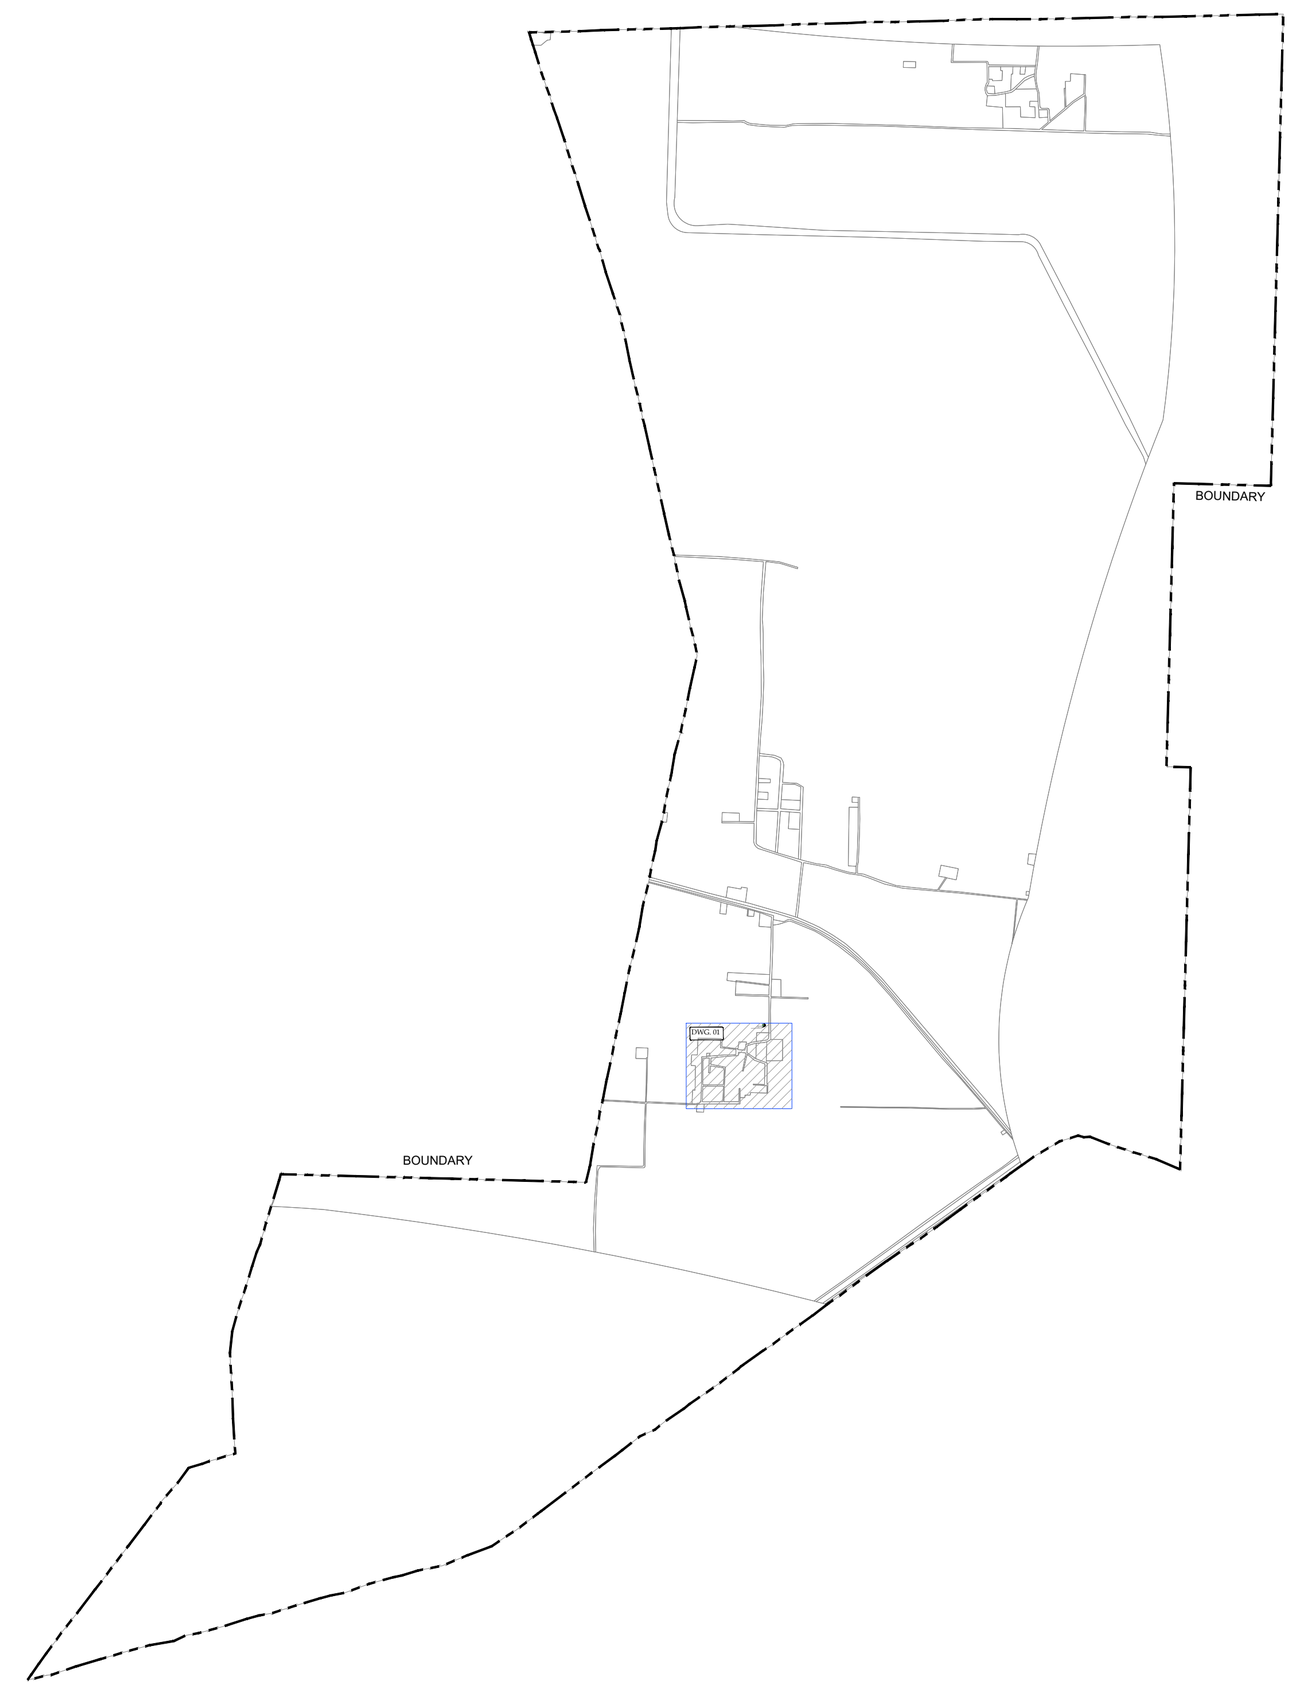

LEGEND:

RO PLANT

BOUNDARY

VILLAGE: AMIN ABAD(BWN)

TITLE.

WATER SUPPLY SYSTEM KEY PLAN

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 1000'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	02-12-2025	DETAILED DESIGN	ASAD	ENGR. FAIEZ	ENGR. IHSAN-UL HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº: PRMSC-BWN-AA-WS-KP-00

SHEET 00 OF 00

REV 00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT

ASIAN CONSULTING ENGINEERS (PVT) LTD. www.asiancon.com.pk

PRMSC-BWN-AA-WS-KP-00

LAYOUT PLAN

RO PLANT
CUSEC 0.05
REF:PRMSC-WS-SP-C-01

N
W
E
S

KEY PLAN

LEGEND:

RO PLANT

BOUNDARY

VILLAGE: AMIN ABAD (BHW)

TITLE.

WATER SUPPLY SYSTEM LAYOUT PLAN-01

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	D E S C R I P T I O N	DRAWN	DESIGNED	APPROVED
01	02-12-2025	DETAILED DESIGN	ASAD	ENGR. FAIEZ	ENGR. HSAN-UL HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº: PRMSC-BWN-AA-WS-LP-01

SHEET 01 OF 01

REV 00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT

ASIAN CONSULTING ENGINEERS
www.asianconsultingengineers.com

PRMSC-BWN-AA-WS-LP-01

BARASAJWAR KHAN

KEY PLAN

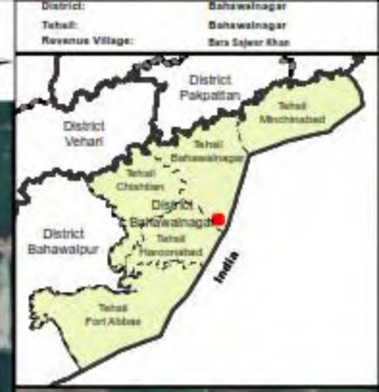

Title:
Proposed Water Supply Plan

Legend:

- SETTLEMENT
- PROPOSED TUBEWELL
- STAND POST

DISTRIBUTION NETWORK

- 90 mm Ø
- SETTELMENT BOUNDARY

Scale: 1:7,800
1 inch = 650 feet
Paper Size: A3

0 40 80 160
Kilometers

Project:
Engineering Design & Construction Supervision, Punjab Rural Sustainable Water Supply & Sanitation Project, Cluster South-III

LEGEND:

- 90mm Ø HDPE PIPE
- SLUICE VALVE
- WASHOUT VALVE
- AIR RELEASE VALVE
- PROPOSED STAND POST TYPE - I
- PROPOSED TUBE WELL
- BOUNDARY

VILLAGE: BARA SAJWAR KHAN (BWN)

TITLE.

WATER SUPPLY SYSTEM KEY PLAN

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 700'

ISSUE N°	DATE	D E S C R I P T I O N	DRAWN	DESIGNED	APPROVED
01	02-01-2026	DETAILED DESIGN	M.ASIF	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-BSK-WS-KP-00	00 OF 00	00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT
ASIAN CONSULTING ENGINEERS
www.asiancon.com

PRMSC-BWN-BSK-WS-KP-00

LAYOUT PLAN

KEY PLAN

LEGEND:

- 90mm Ø HDPE PIPE
- SLUICE VALVE
- WASHOUT VALVE
- AIR RELEASE VALVE
- PROPOSED STAND POST TYPE - I
- PROPOSED TUBE WELL
- BOUNDARY

VILLAGE: BARA SAJWAR KHAN (BWN)

TITLE.

WATAR SUPPLY SYSTEM LAYOUT PLAN-03

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	02-01-2026	DETAILED DESIGN	M.ASIF	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-BSK-WS-LP-03	03 OF 09	00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:
ASIAN CONSULTING ENGINEERS
www.asianconsult.com.pk

PRMSC-BWN-BSK-WS-LP-03

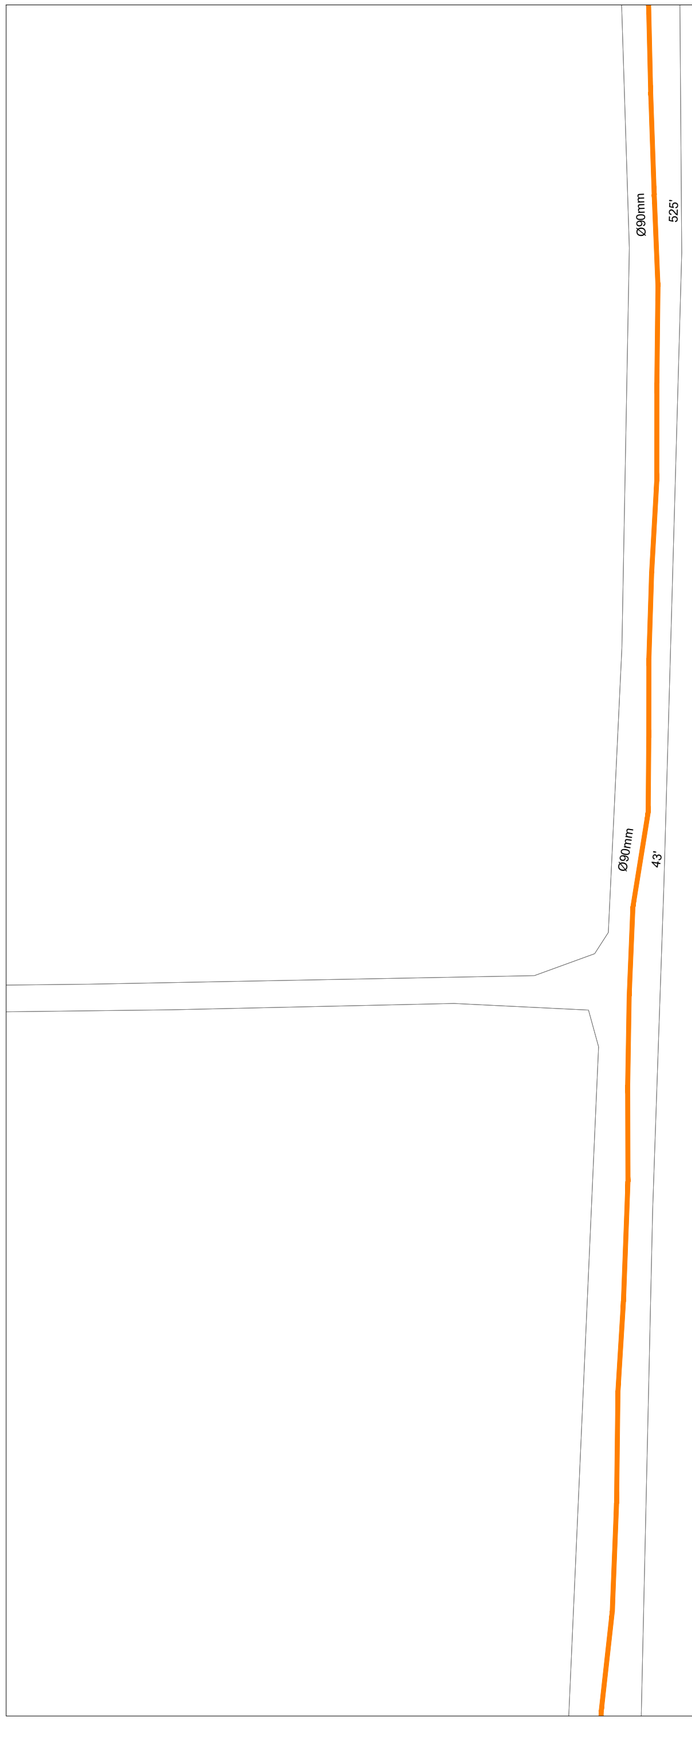

KEY PLAN

LEGEND:

- 90mm Ø HDPE PIPE
- SLUICE VALVE
- WASHOUT VALVE
- AIR RELEASE VALVE
- PROPOSED STAND POST TYPE - I
- PROPOSED TUBE WELL
- BOUNDARY

VILLAGE: BARA SAJWAR KHAN (BWN)

TITLE.

WATAR SUPPLY SYSTEM LAYOUT PLAN-04

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	02-01-2026	DETAILED DESIGN	M.ASIF	ENGR. FAIEZ	ENGR. HSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING N°: PRMSC-BWN-BSK-WS-LP-04

SHEET 04 OF 09

REV 00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:
ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

PRMSC-BWN-BSK-WS-LP-04

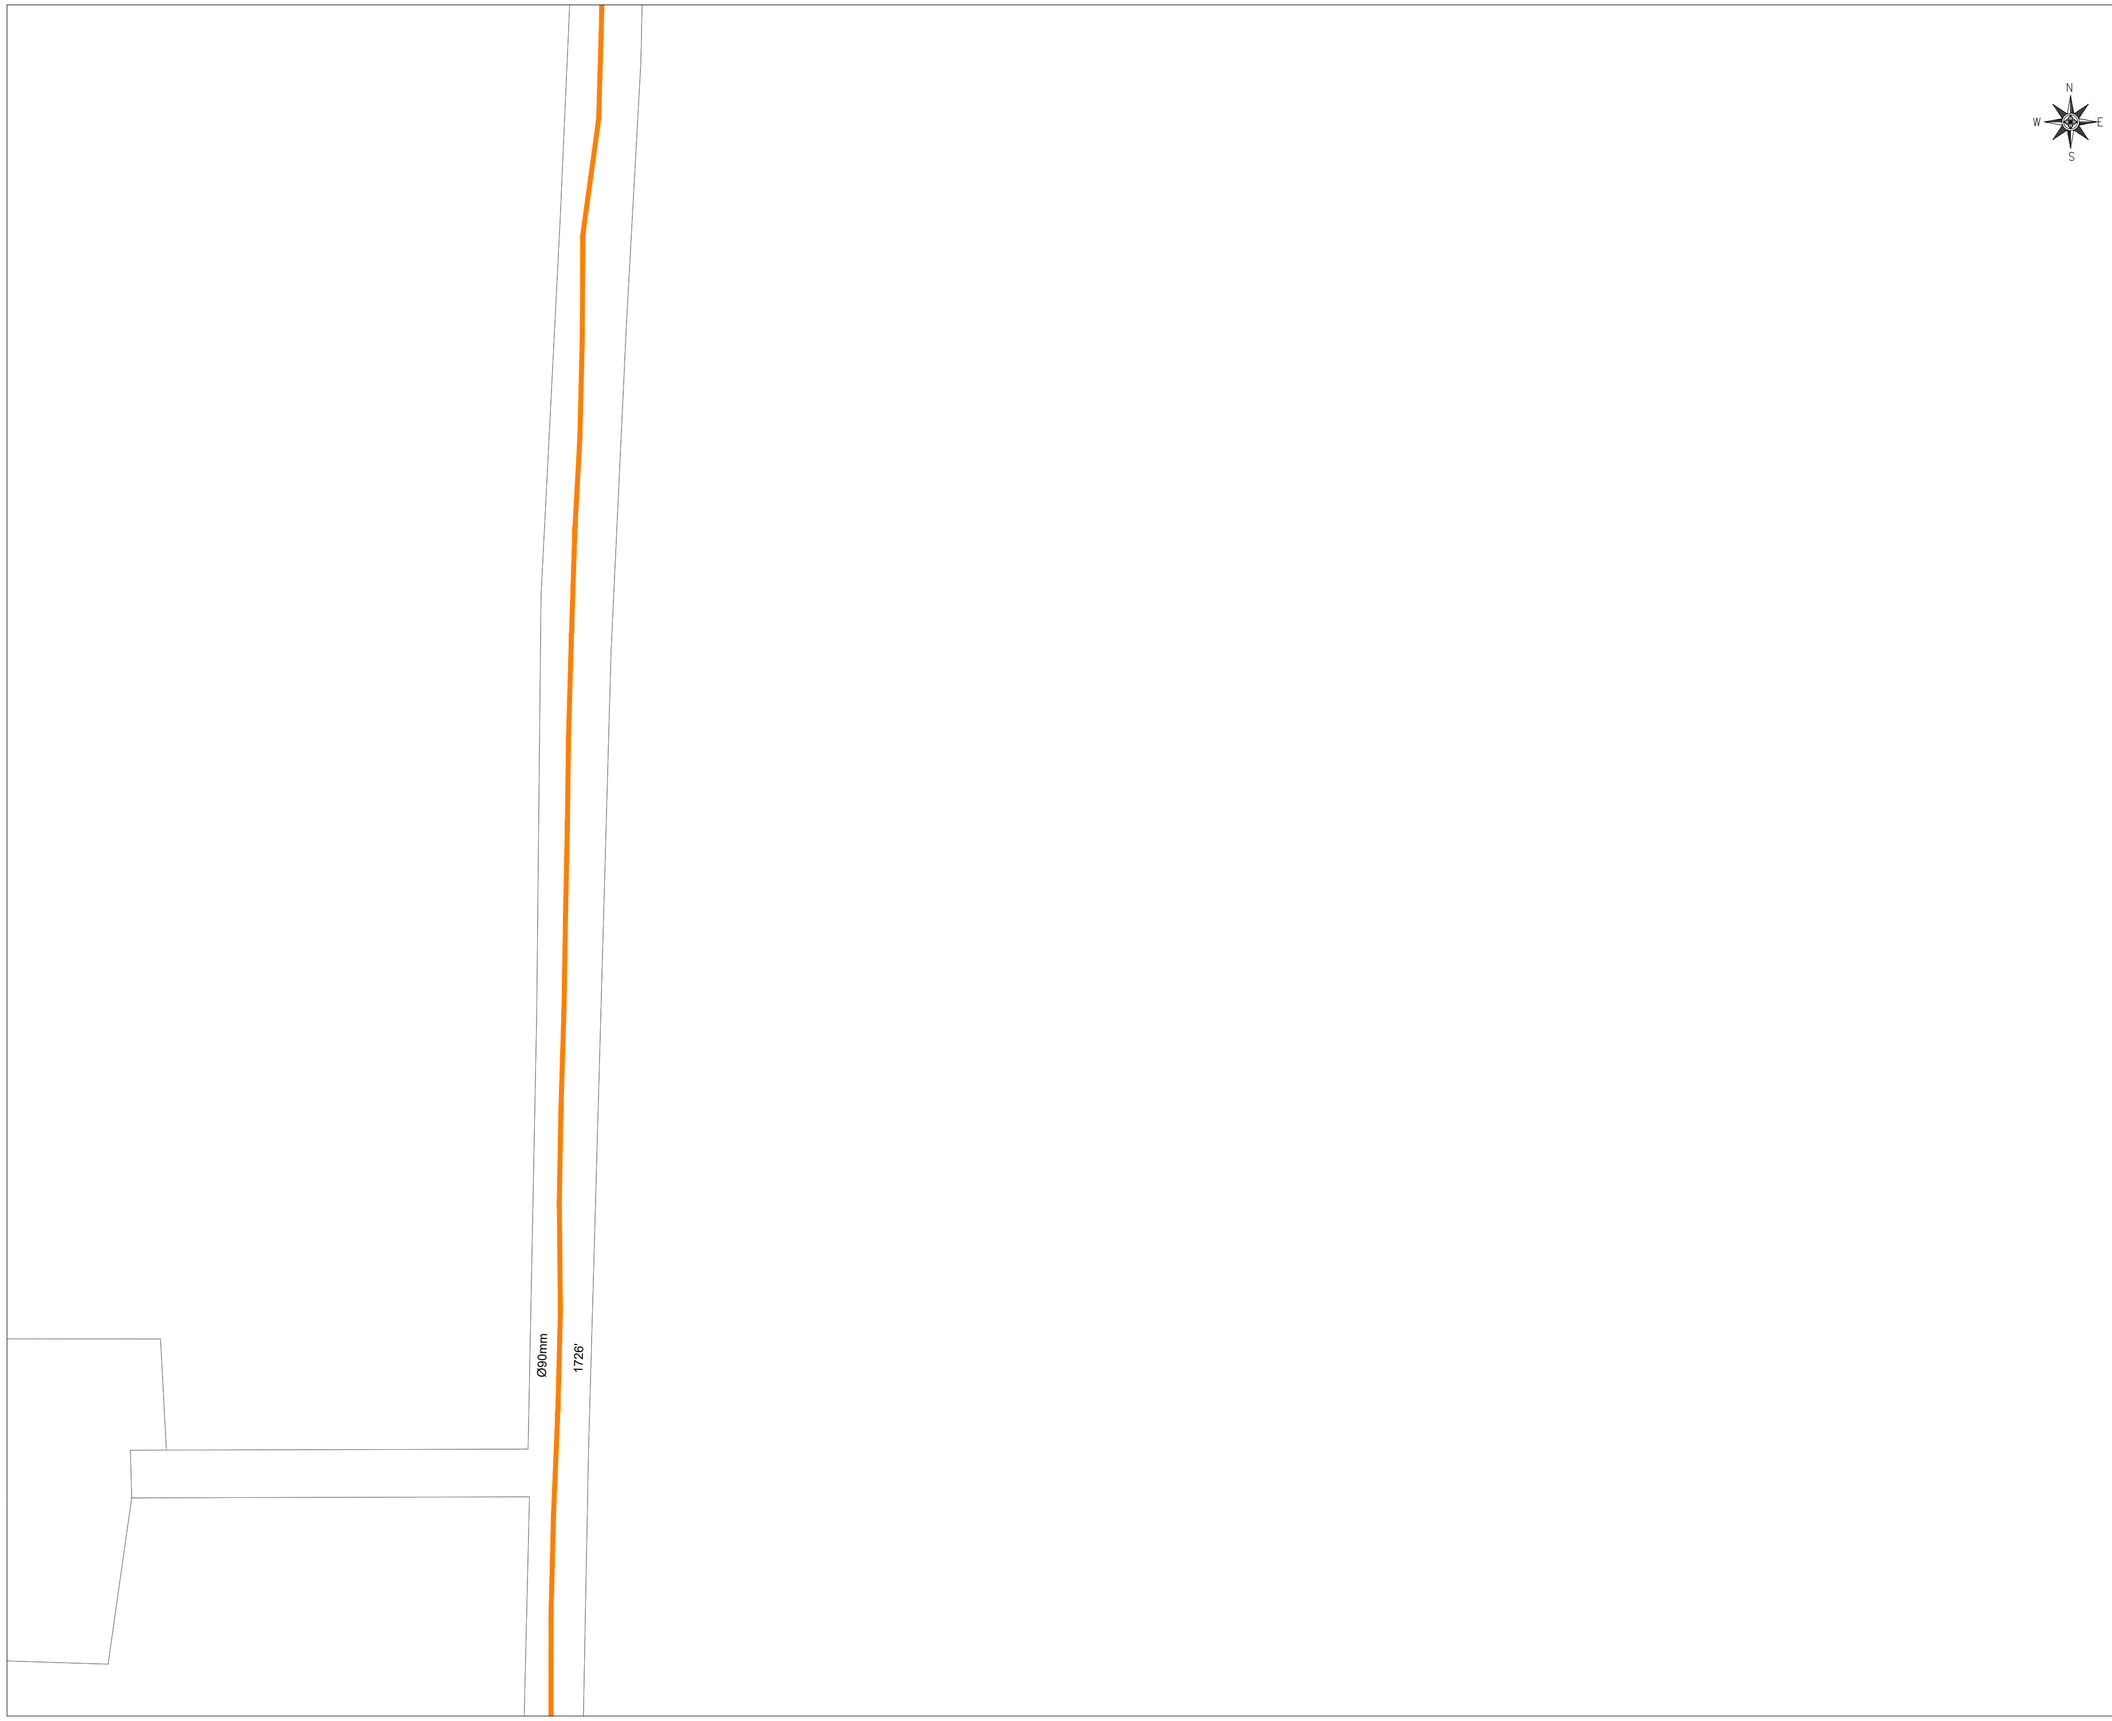

KEY PLAN

LEGEND:

- 90mm Ø HDPE PIPE
- SLUICE VALVE
- WASHOUT VALVE
- AIR RELEASE VALVE
- PROPOSED STAND POST TYPE - I
- PROPOSED TUBE WELL
- BOUNDARY

VILLAGE: BARA SAJWAR KHAN (BWN)

TITLE.

WATAR SUPPLY SYSTEM LAYOUT PLAN-05

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	D E S C R I P T I O N	DRAWN	DESIGNED	APPROVED
01	02-01-2026	DETAILED DESIGN	M.ASIF	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-BSK-WS-LP-05	05 OF 09	00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS www.asiancon.com

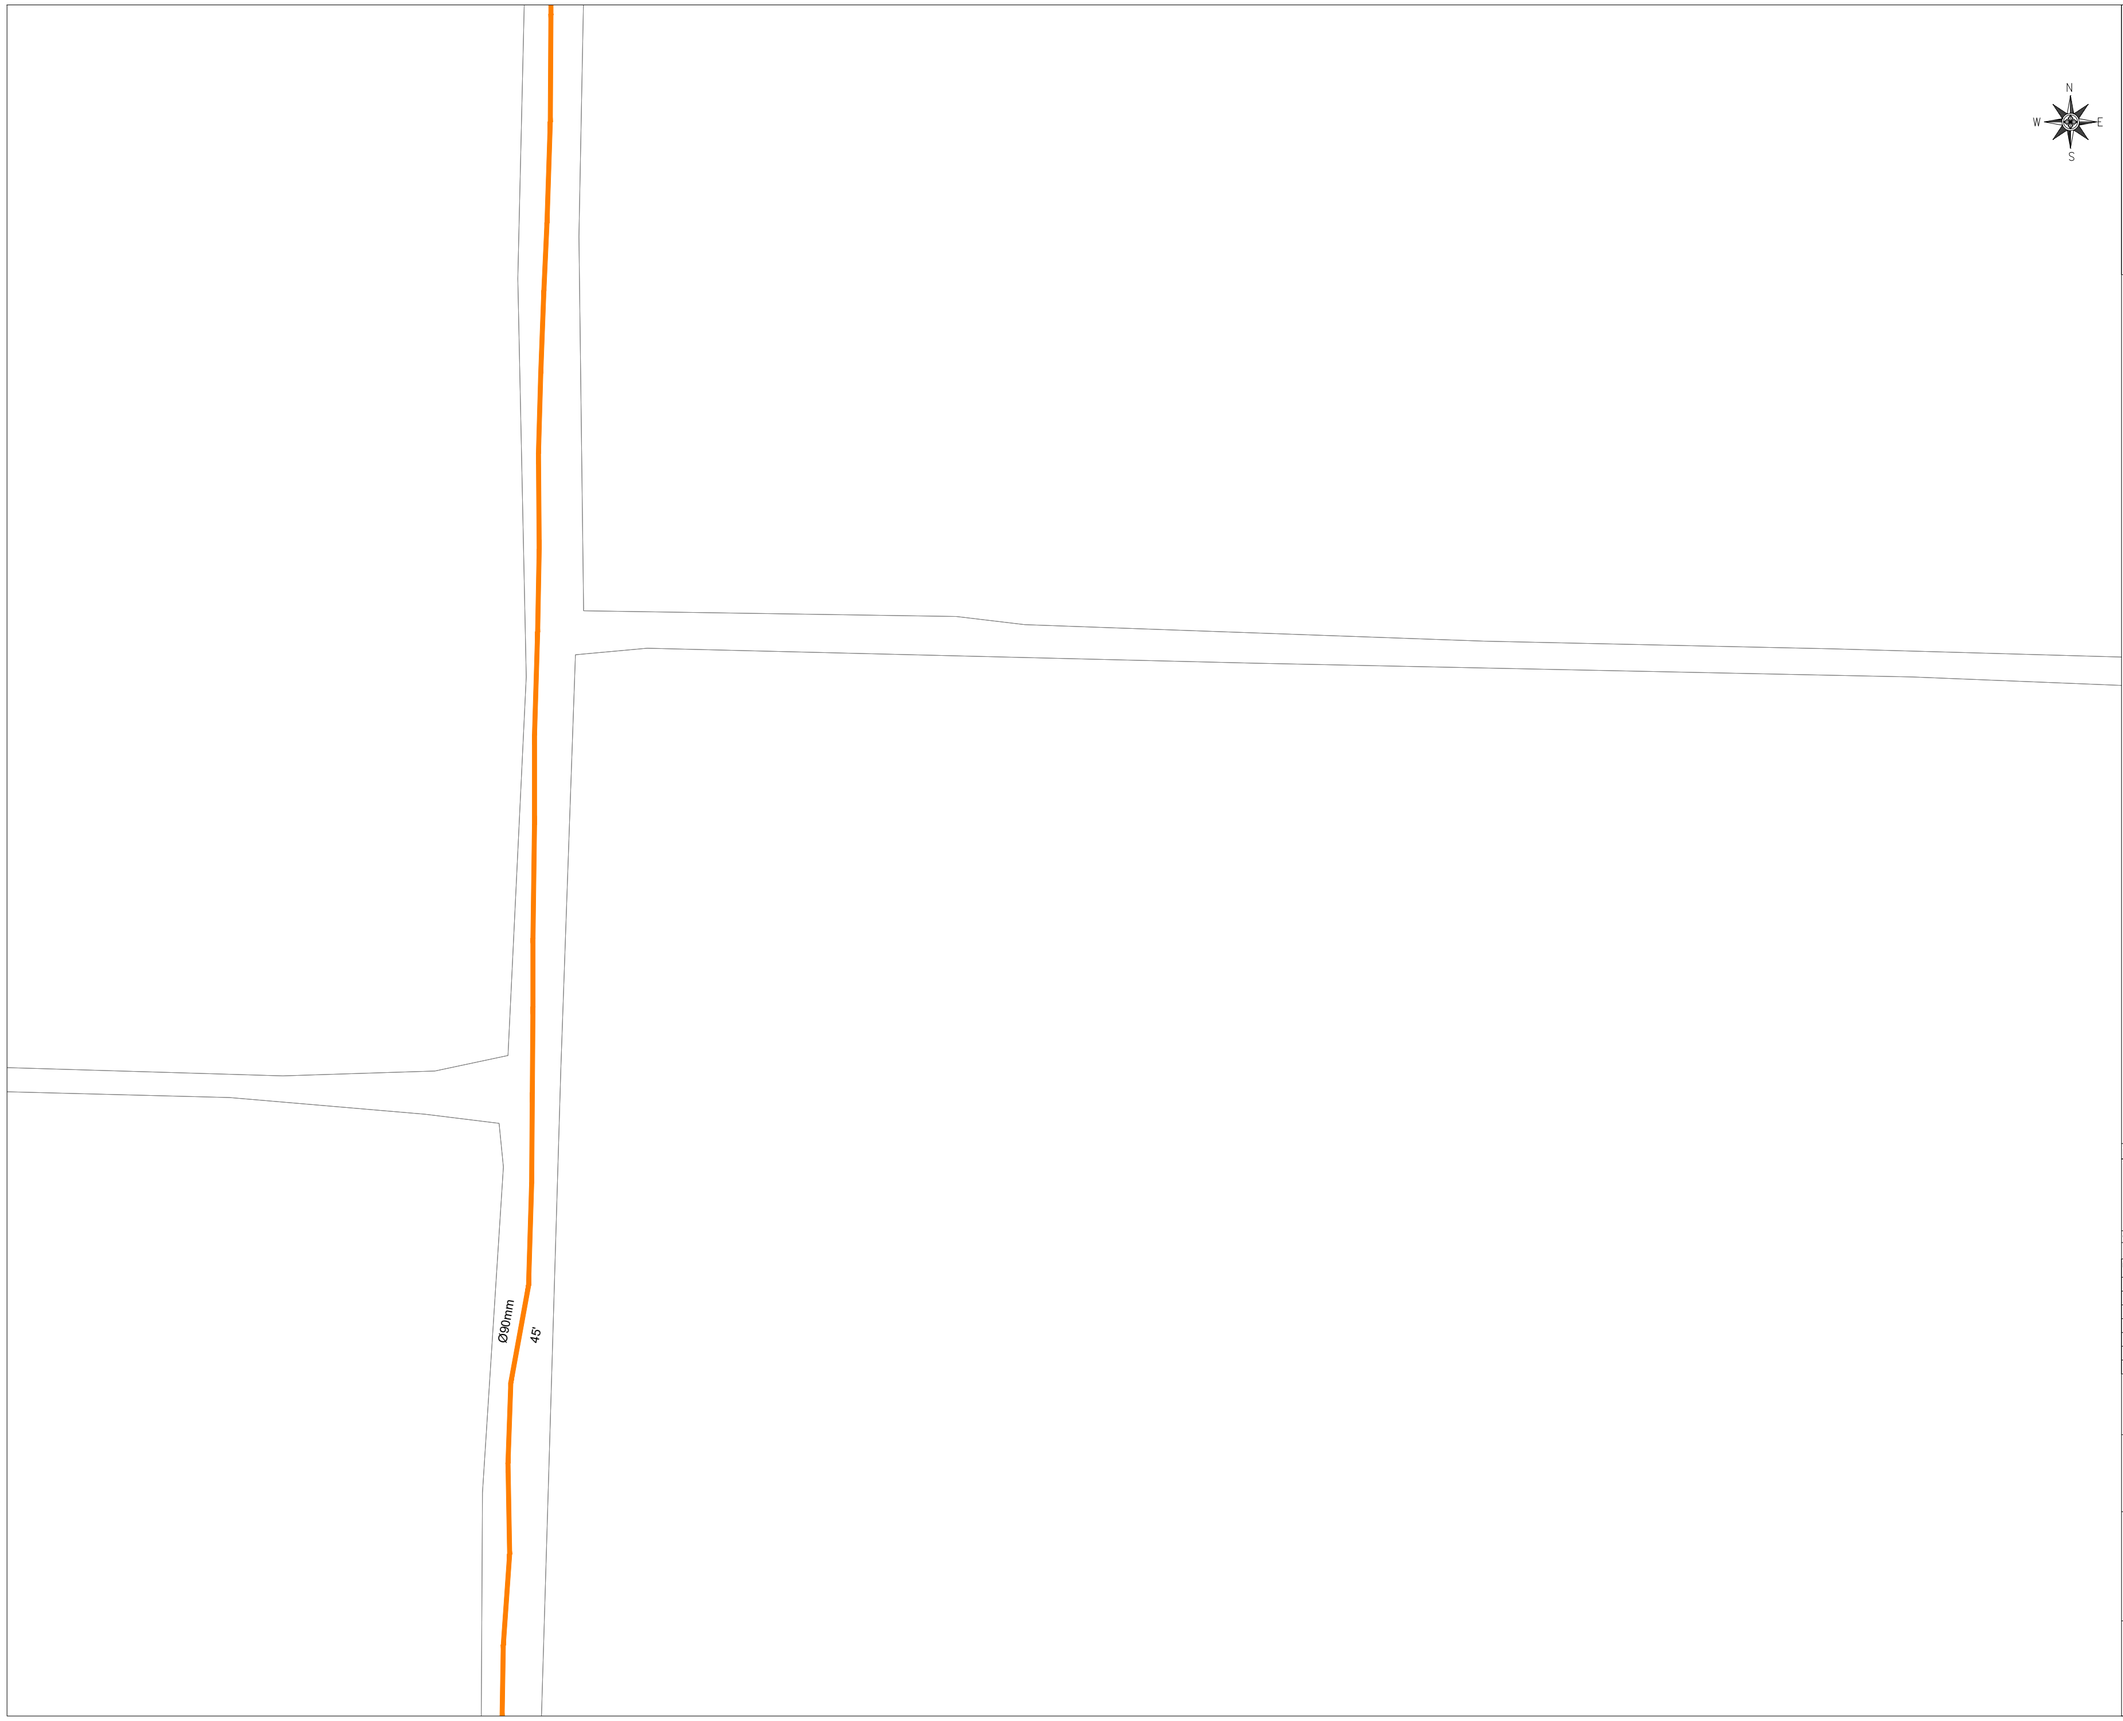

PRMSC-BWN-BSK-WS-LP-06

KEY PLAN

LEGEND:

- 90mm Ø HDPE PIPE
- SLUICE VALVE
- WASHOUT VALVE
- AIR RELEASE VALVE
- PROPOSED STAND POST TYPE - I
- PROPOSED TUBE WELL
- BOUNDARY

VILLAGE: BARA SAJWAR KHAN (BWN)

TITLE.

WATAR SUPPLY SYSTEM LAYOUT PLAN-06

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	02-01-2026	DETAILED DESIGN	M.ASIF	ENGR. FAIEZ	ENGR. HSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-BSK-WS-LP-06	06 OF 09	00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:
ASIAN CONSULTING ENGINEERS
www.asianconsultingengineers.com.pk

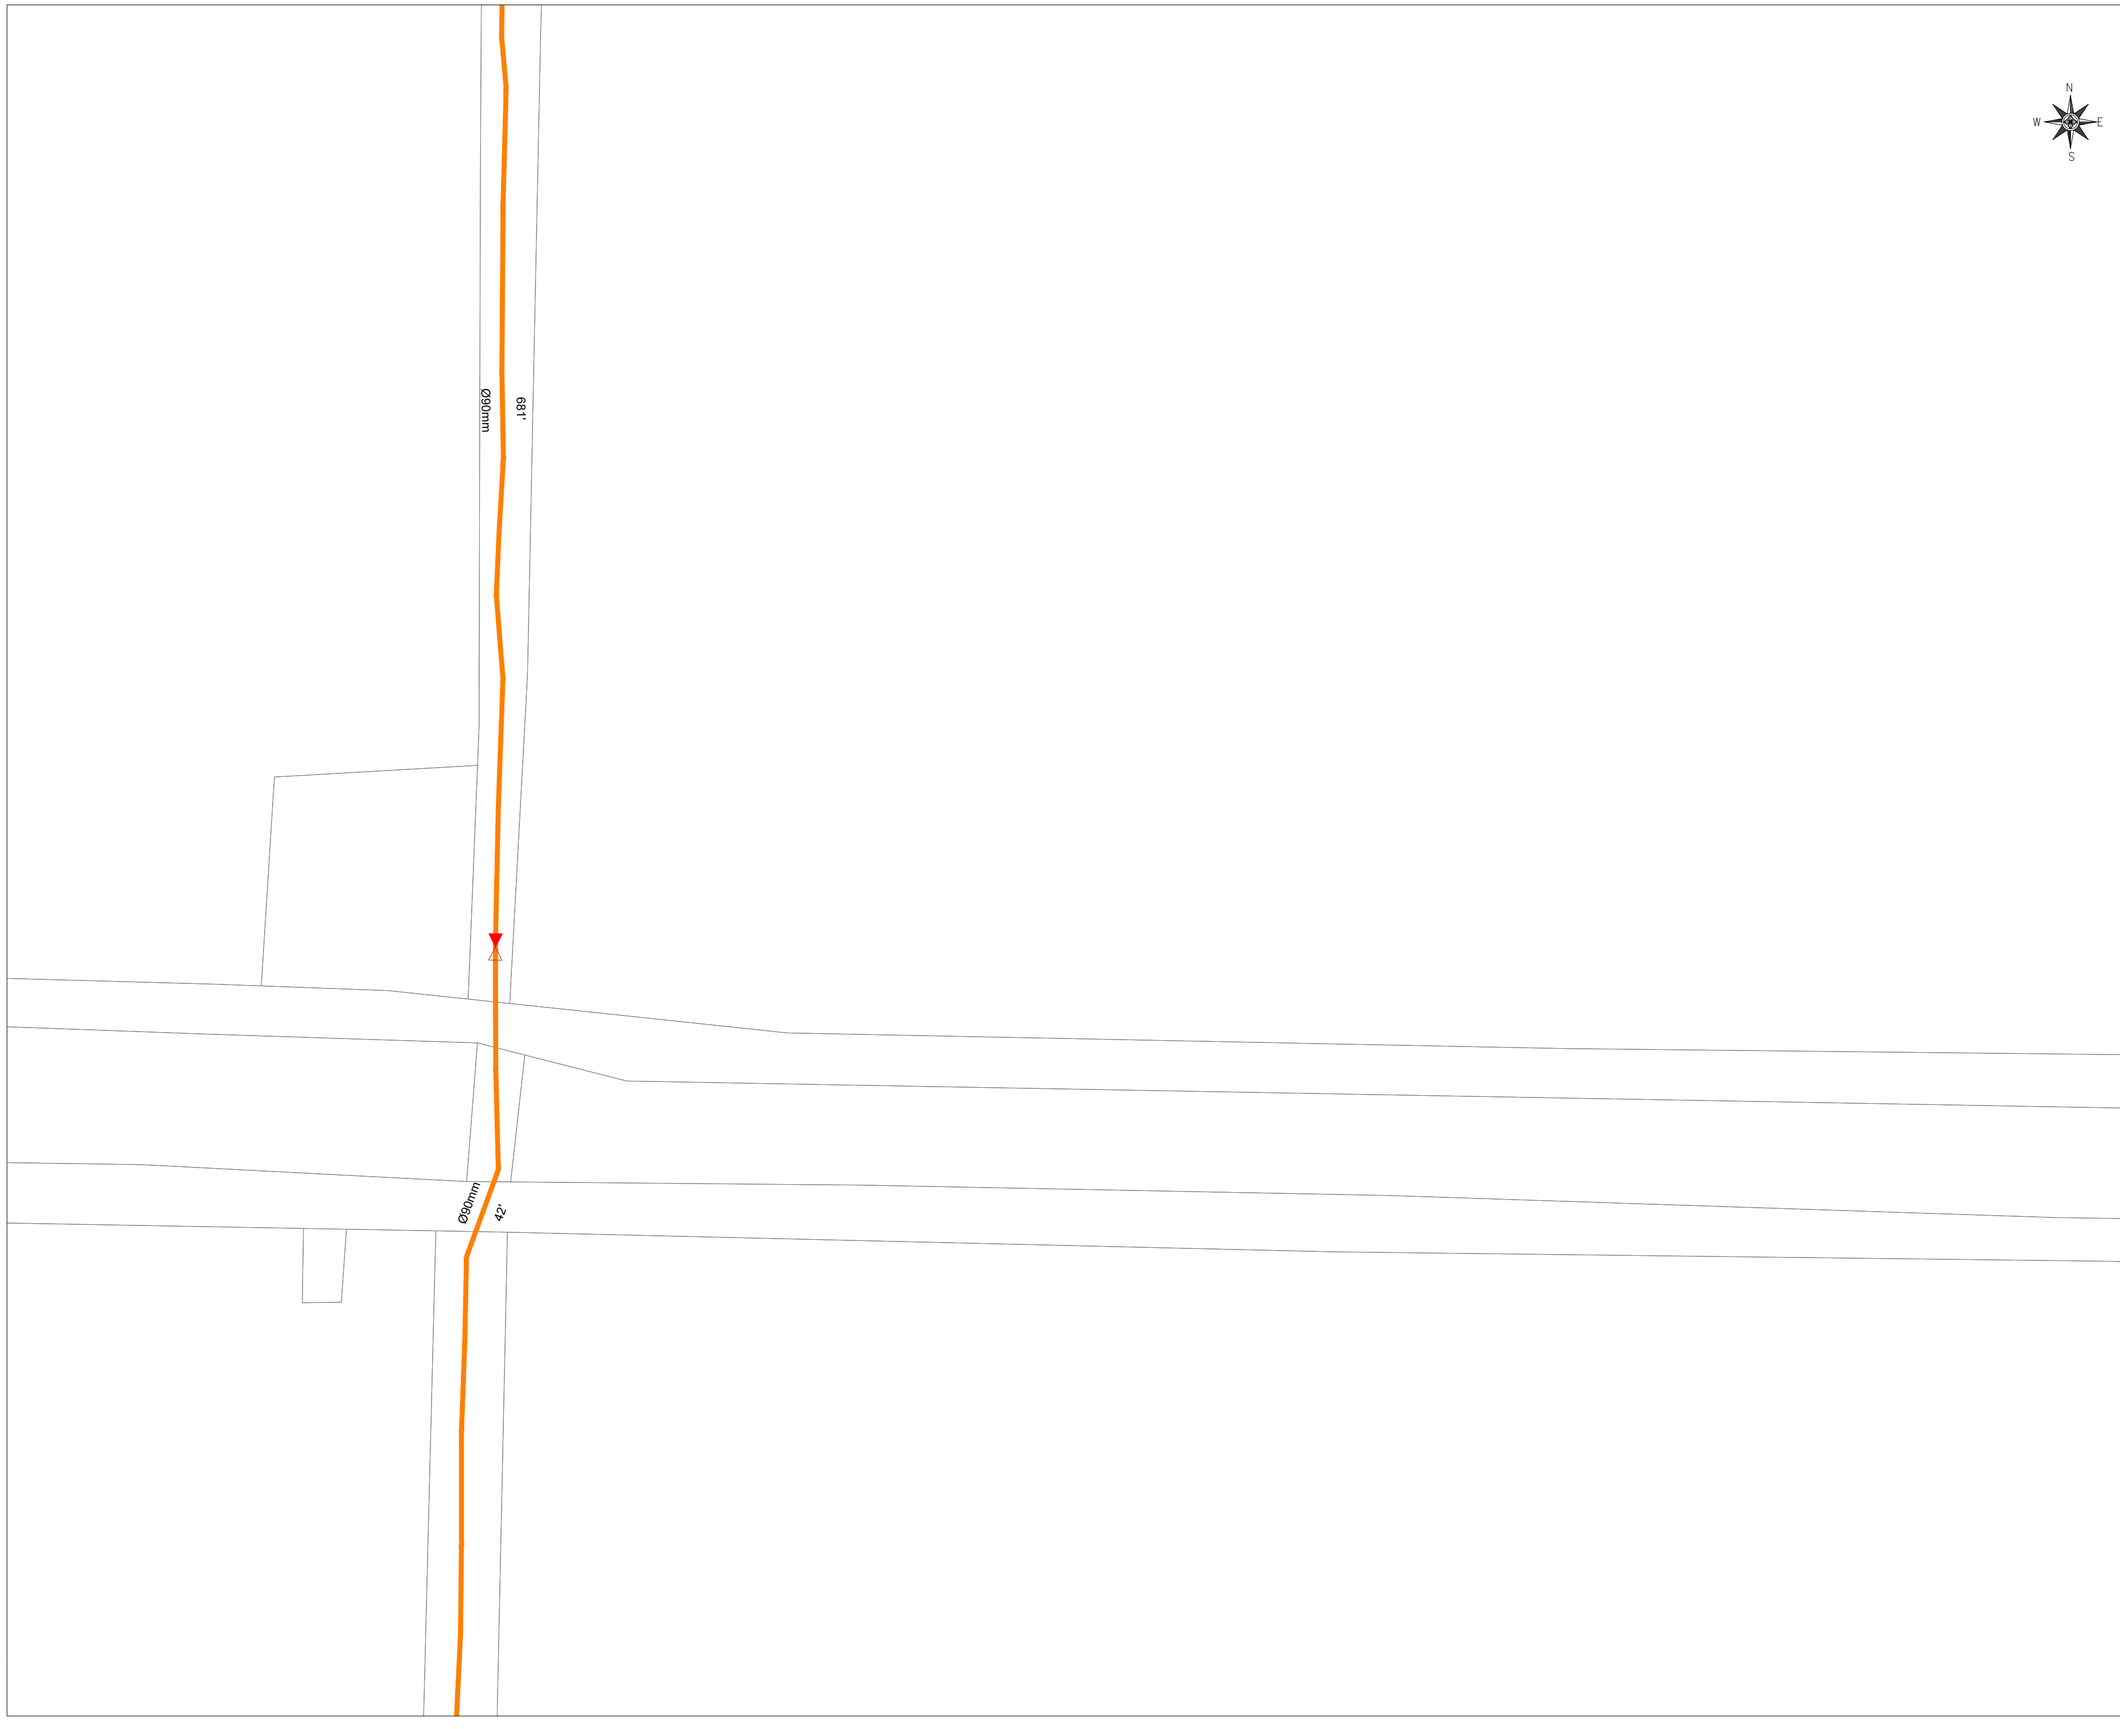

PRMSC-BWN-BSK-WS-LP-07

N
W
E
S

KEY PLAN

LEGEND:

- 90mm Ø HDPE PIPE
- SLUICE VALVE
- WASHOUT VALVE
- AIR RELEASE VALVE
- PROPOSED STAND POST TYPE - I
- PROPOSED TUBE WELL
- BOUNDARY

VILLAGE: BARA SAJWAR KHAN (BWN)

TITLE.

WATAR SUPPLY SYSTEM LAYOUT PLAN-07

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	02-01-2026	DETAILED DESIGN	M.ASIF	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING N°:	SHEET	REV
PRMSC-BWN-BSK-WS-LP-07	07 OF 09	00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:
ASIAN CONSULTING ENGINEERS
www.asianeon.com.pk

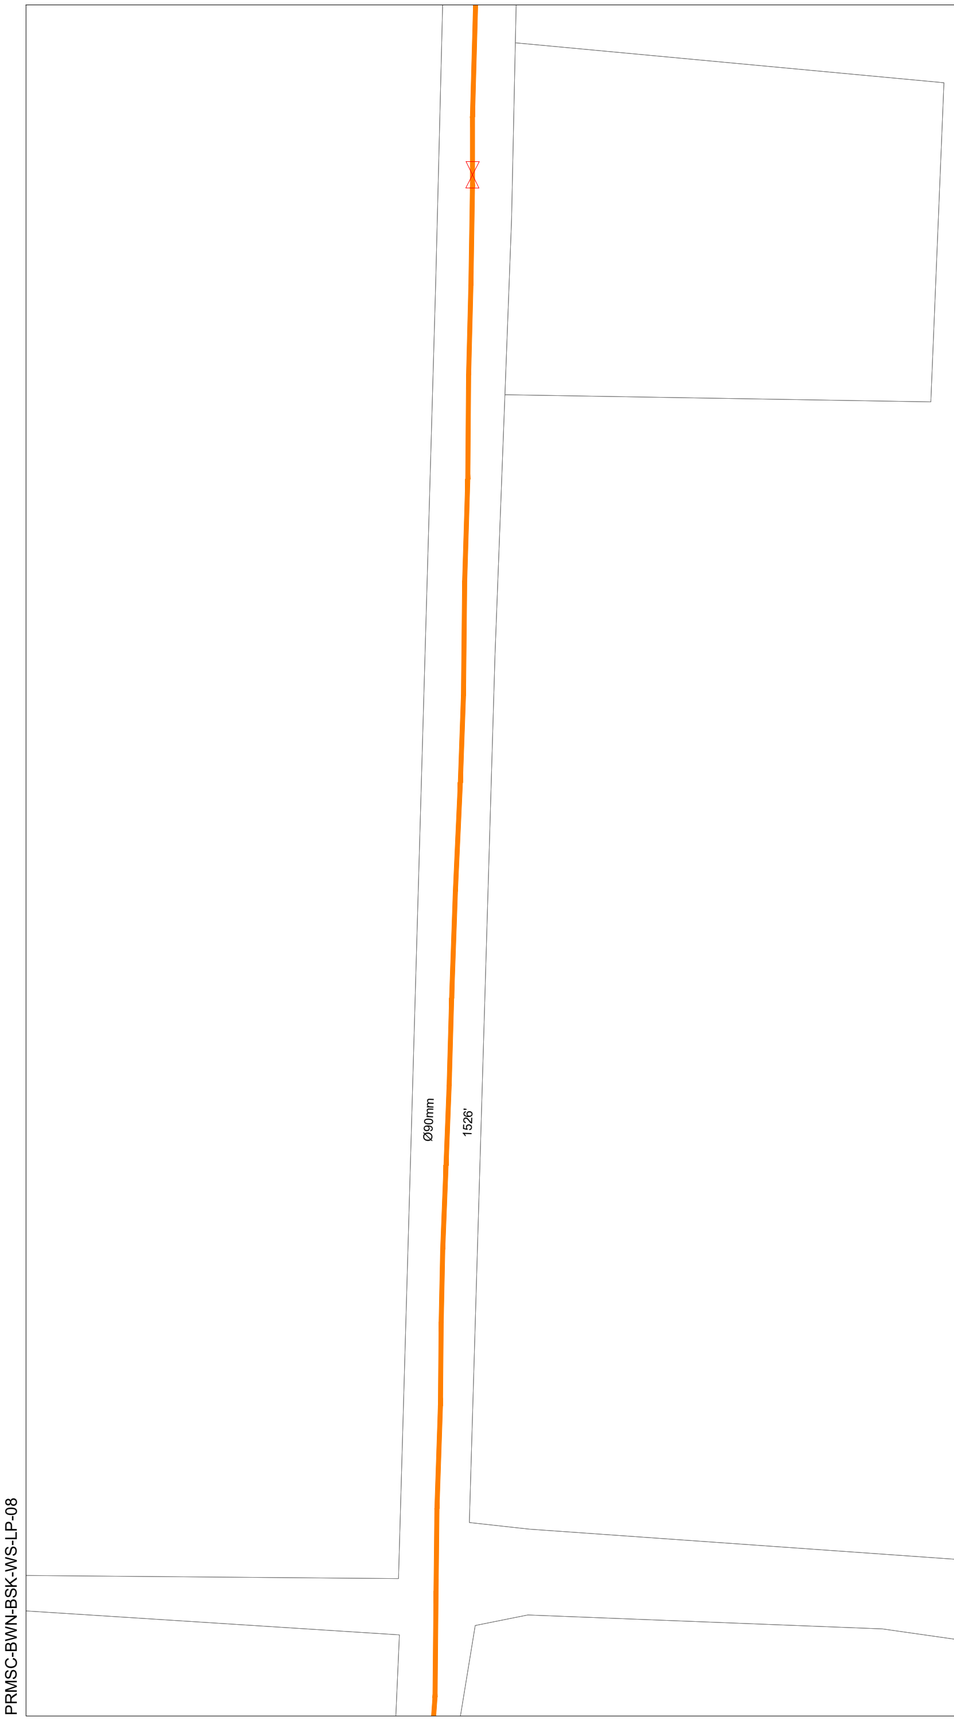

PRMSC-BWN-BSK-WS-LP-08

KEY PLAN

LEGEND:

- 90mm Ø HDPE PIPE
- SLUICE VALVE
- WASHOUT VALVE
- AIR RELEASE VALVE
- PROPOSED STAND POST TYPE - I
- PROPOSED TUBE WELL
- BOUNDARY

VILLAGE: BARA SAJWAR KHAN (BWN)

TITLE.

WATAR SUPPLY SYSTEM LAYOUT PLAN-08

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	02-01-2026	DETAILED DESIGN	M.ASIF	ENGR. FAIEZ	ENGR. HSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-BSK-WS-LP-08	08 OF 09	00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

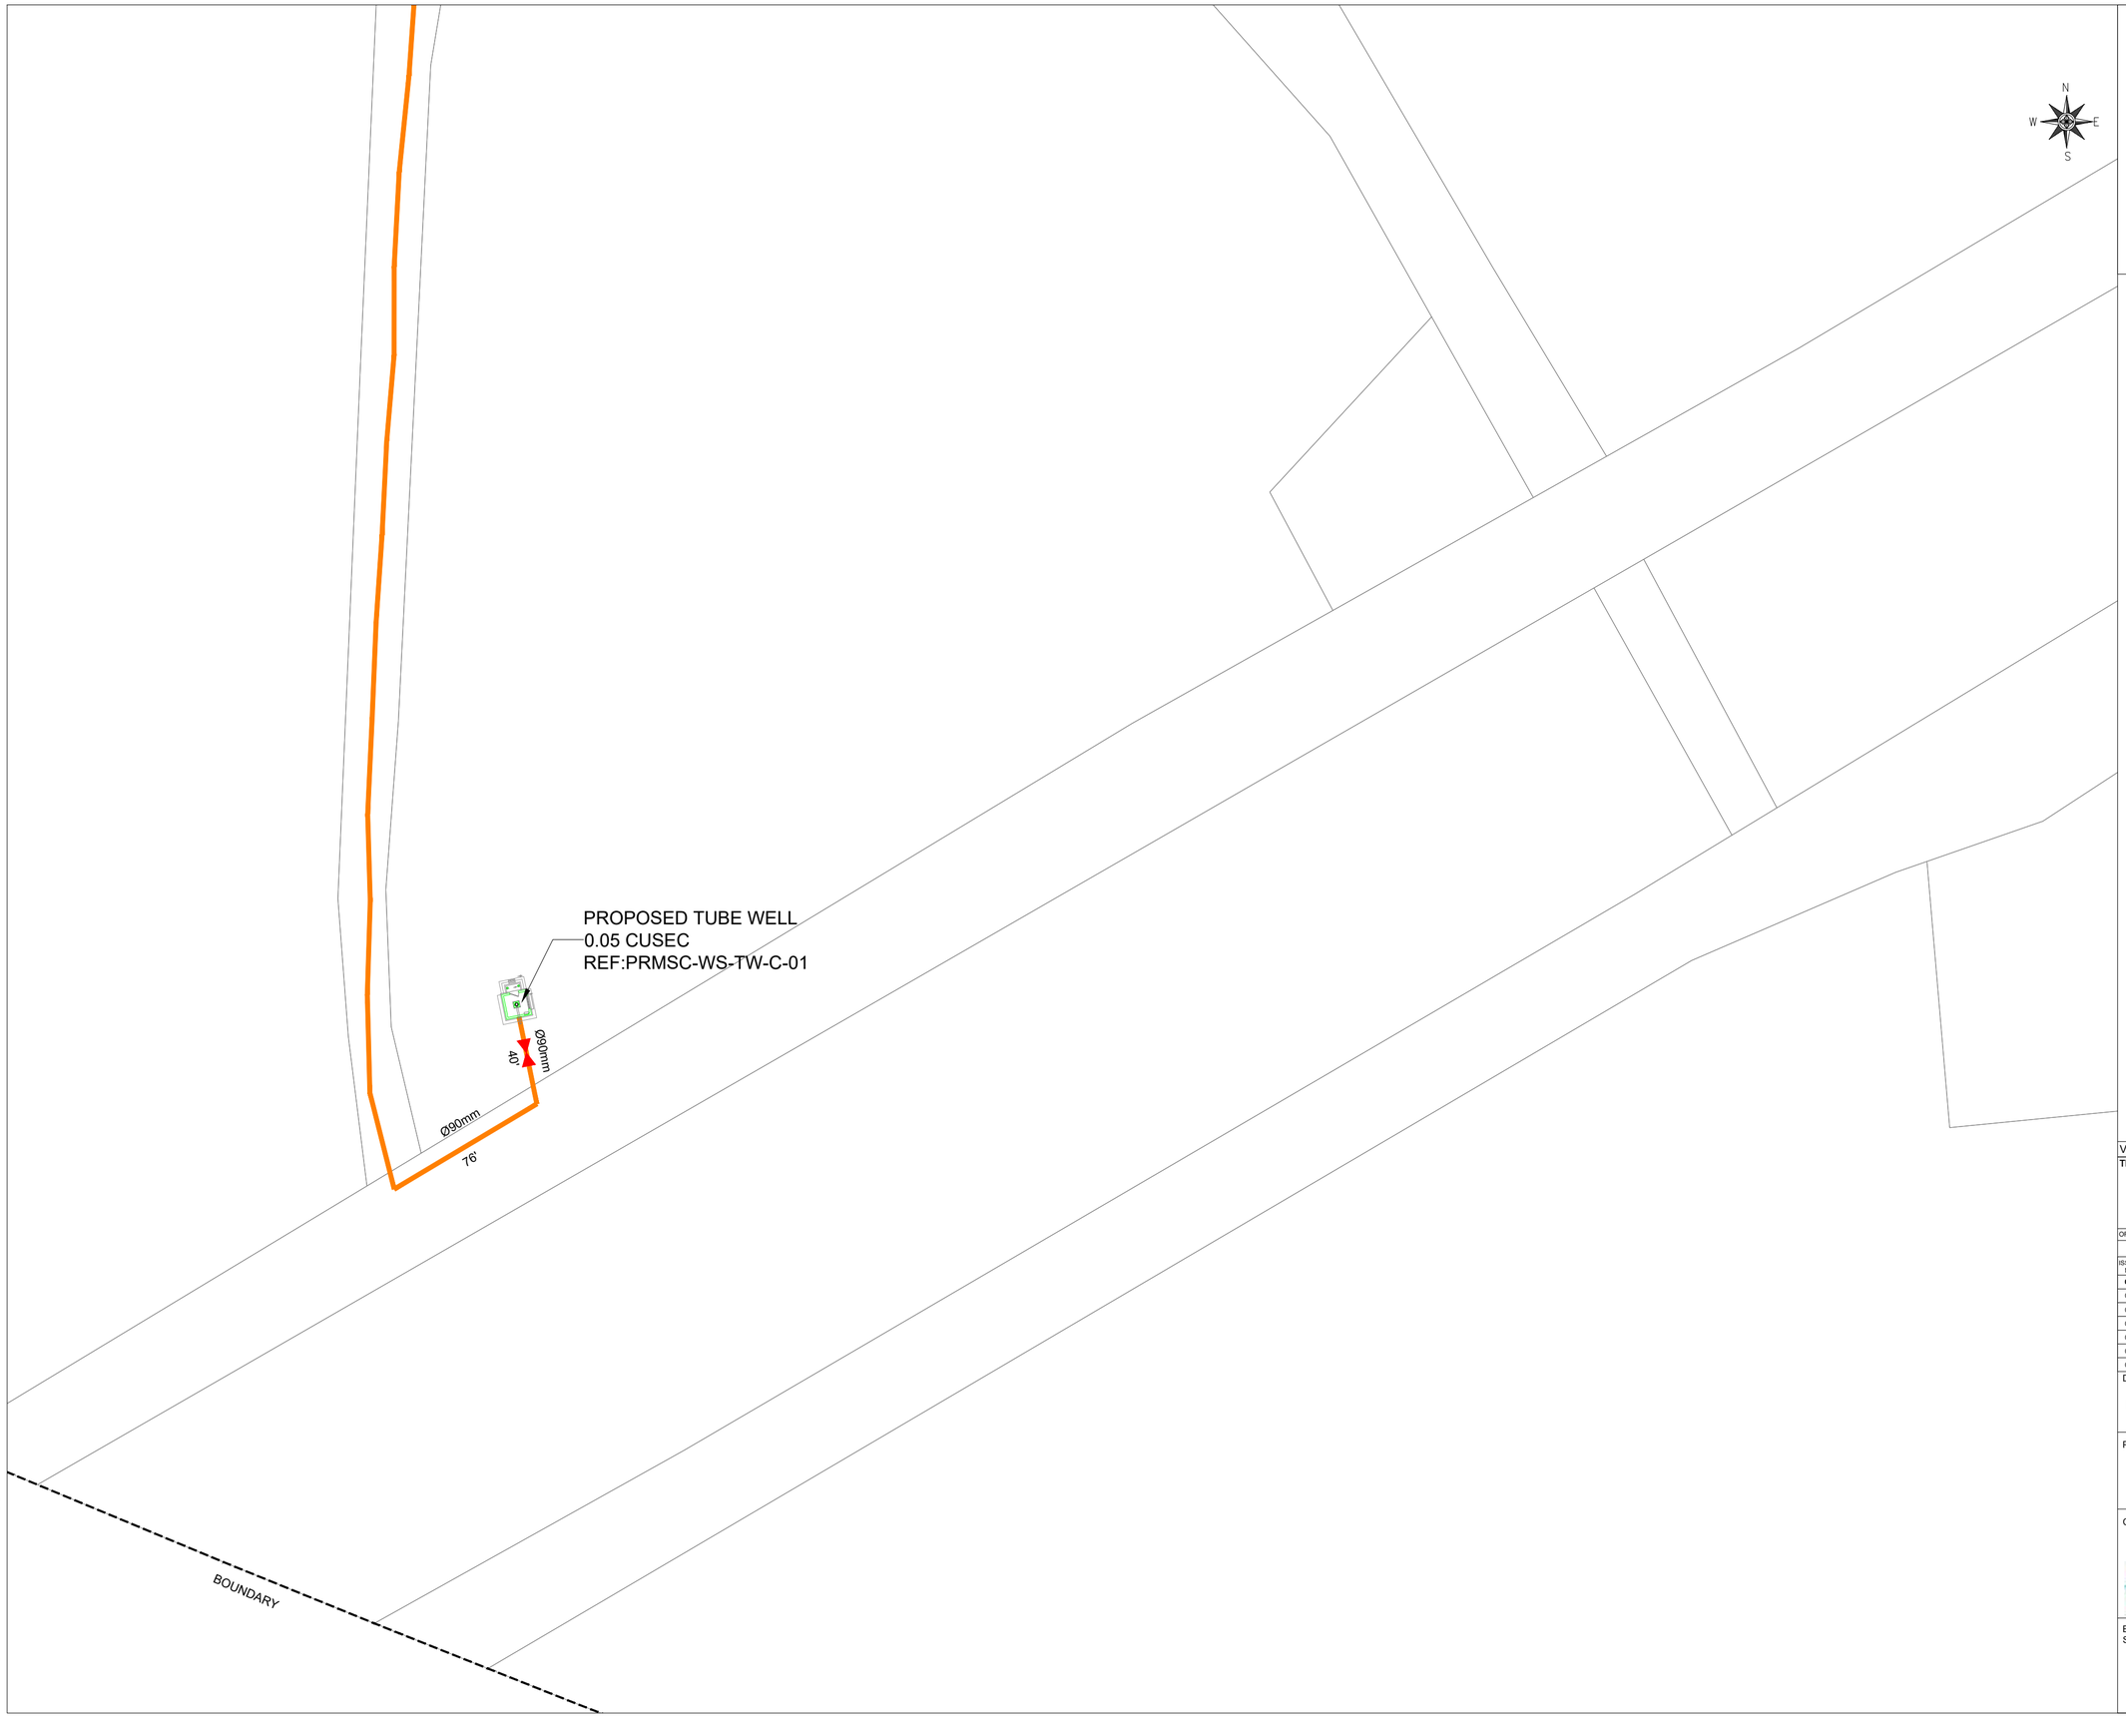

KEY PLAN

LEGEND:

- 90mm Ø HDPE PIPE
- SLUICE VALVE
- WASHOUT VALVE
- AIR RELEASE VALVE
- PROPOSED STAND POST TYPE - I
- PROPOSED TUBE WELL
- BOUNDARY

VILLAGE: BARA SAJWAR KHAN (BWN)

TITLE.

WATAR SUPPLY SYSTEM LAYOUT PLAN-09

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	02-01-2026	DETAILED DESIGN	M.ASIF	ENGR FAIEZ	ENGR HSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-BSK-WS-LP-09	09 OF 09	00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

DADOO MAMMUNKA

KEY PLAN

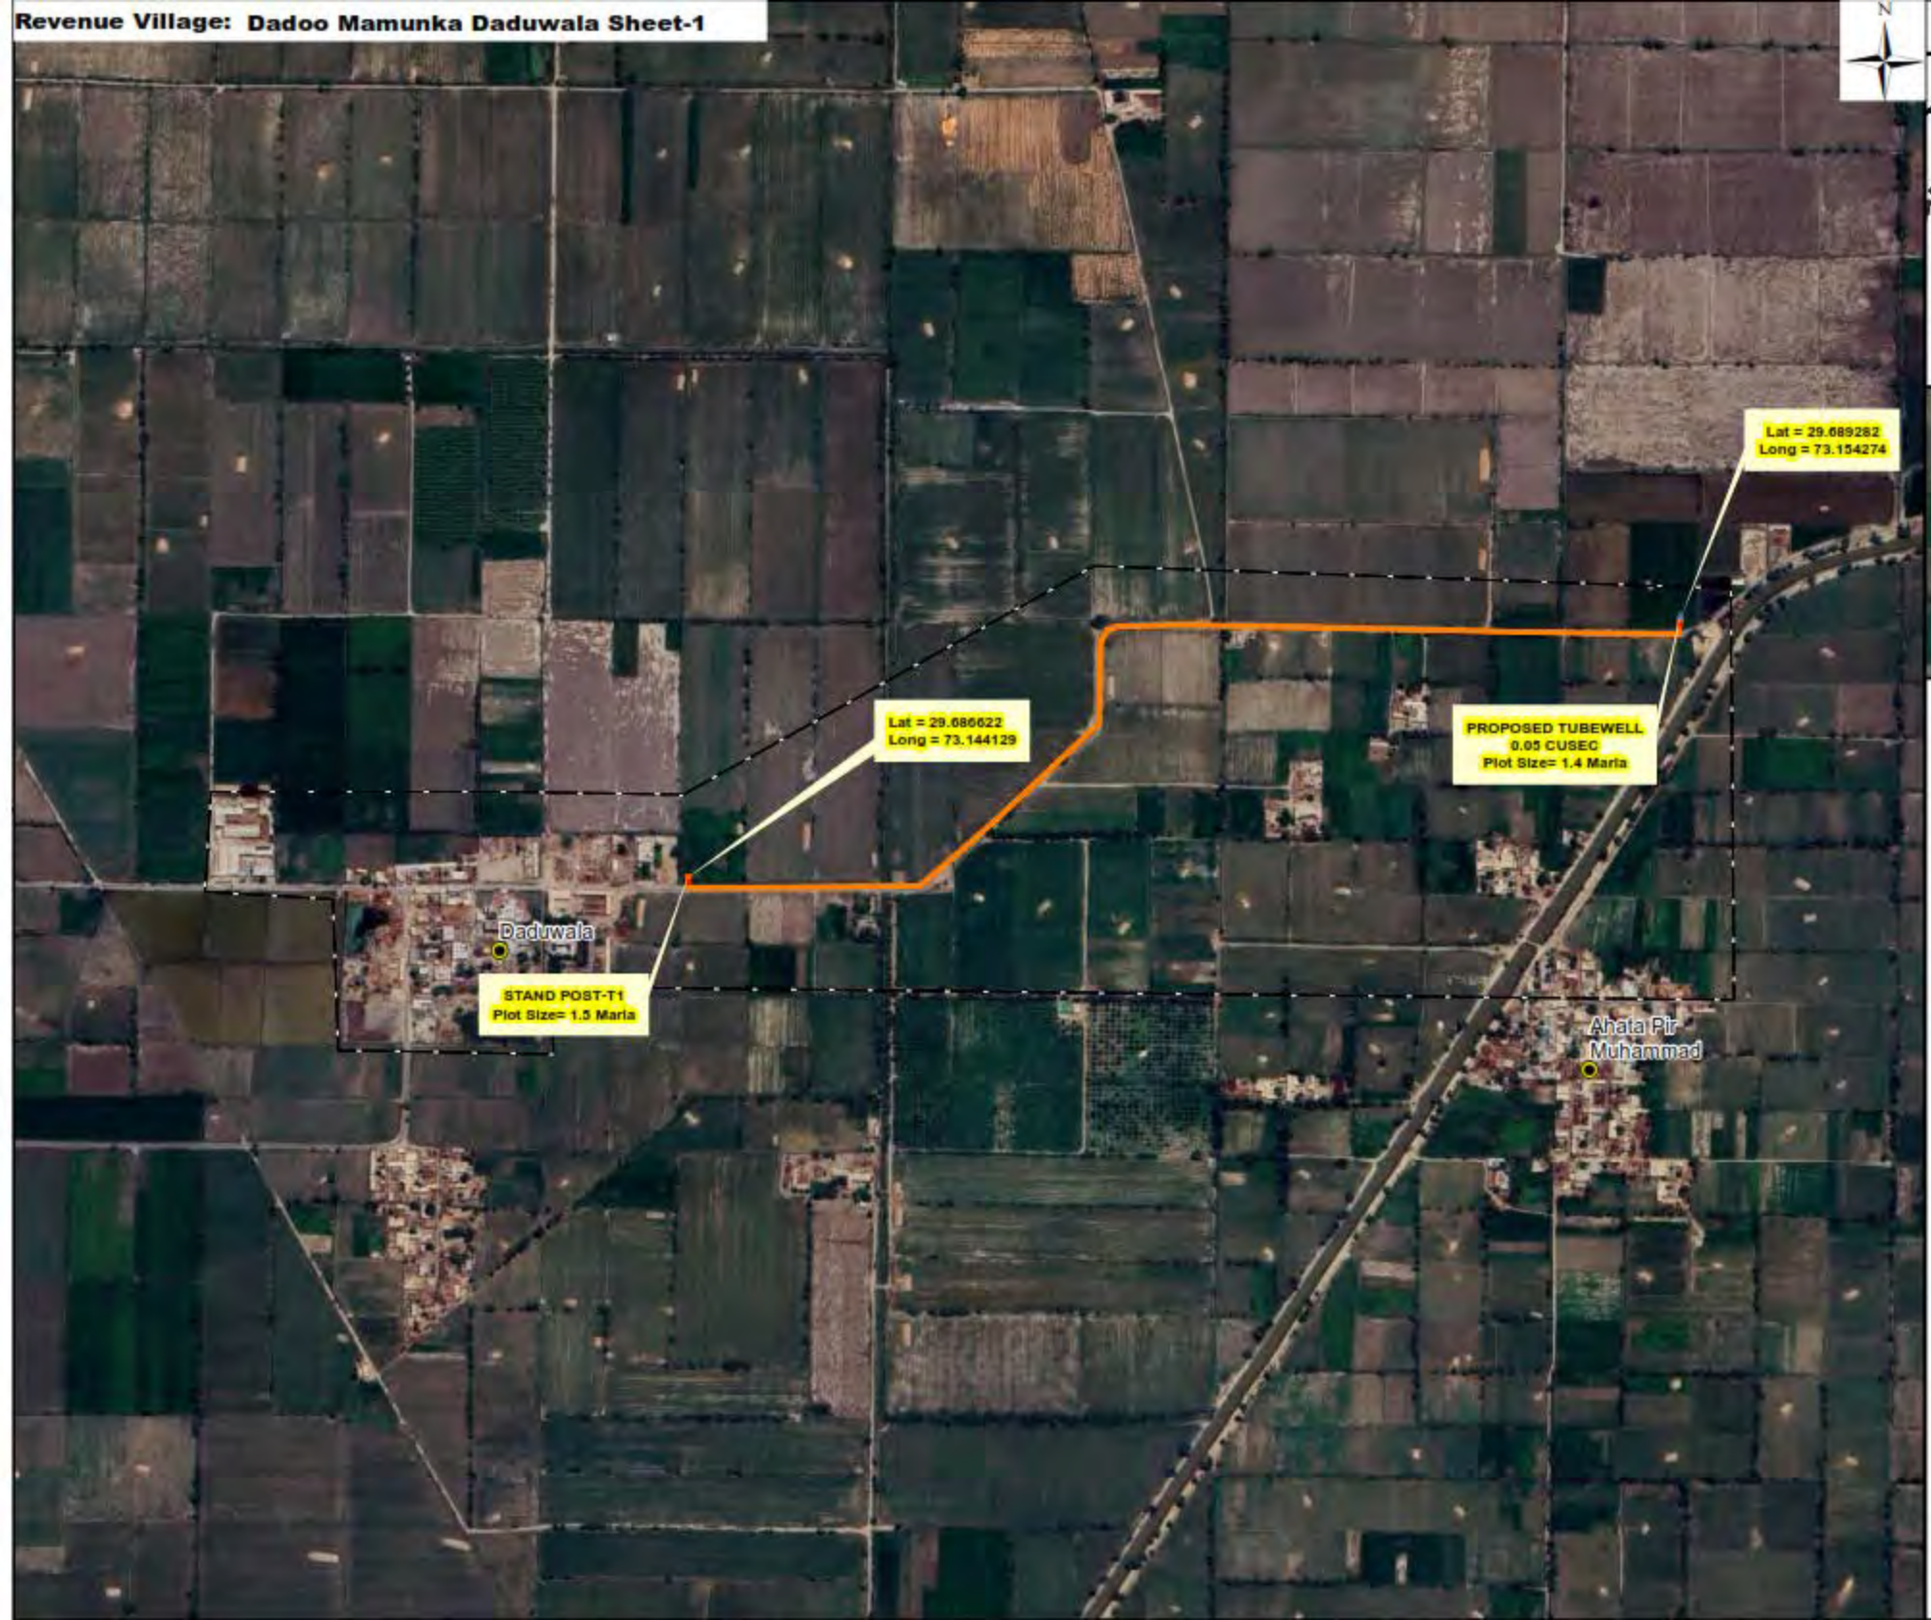

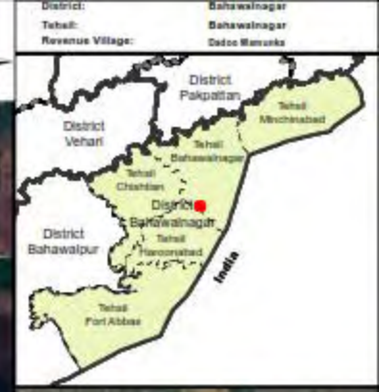

Title:
Proposed Water Supply Plan

Legend:

DISTRIBUTION NETWORK

- 90 mm Ø
- SETTLEMENT
- PROPOSED TUBEWELL
- STAND POST
- SETTELMENT BOUNDARY

Scale: 1:6,200
1 inch = 517 feet
Paper Size: A3

0 40 80 160
Kilometers

Project:
Engineering Design & Construction Supervision, Punjab Rural Sustainable Water Supply & Sanitation Project, Cluster South-III

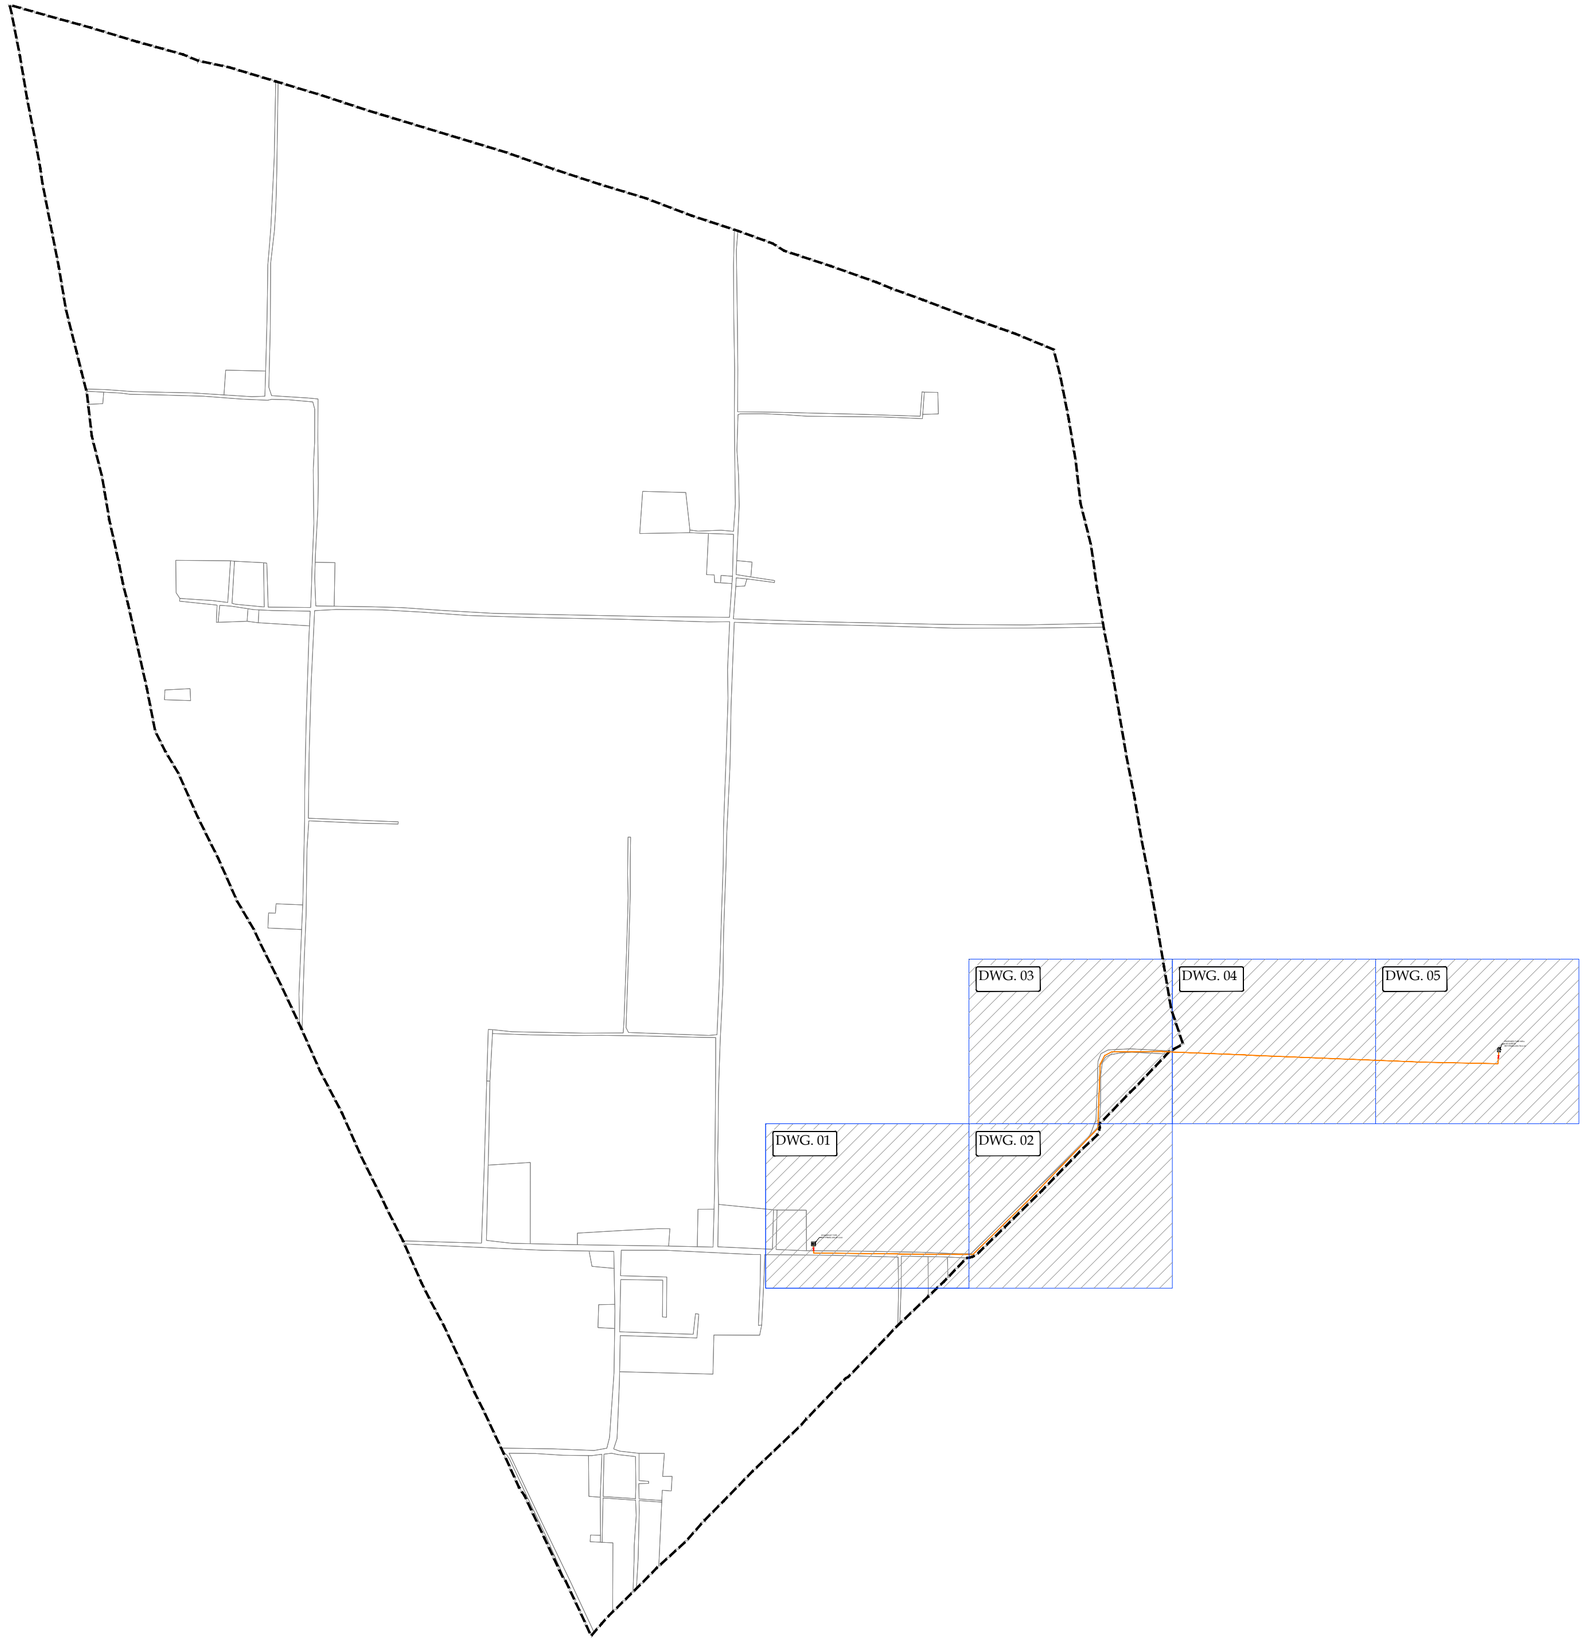

LEGEND:

- 90mm Ø HDPE PIPE
- SLUICE VALVE
- PROPOSED STAND POST TYPE - I
- PROPOSED TUBE WELL
- BOUNDARY

VILLAGE: DADOO MAMMUNKA (BWN)

TITLE.

WATER SUPPLY SYSTEM KEY PLAN

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 520'

ISSUE N°	DATE	D E S C R I P T I O N	DRAWN	DESIGNED	APPROVED
01	06-01-2026	DETAILED DESIGN	M.ASIF	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº: PRMSC-BWN-DM-WS-KP-00

SHEET 00 OF 00

REV 00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT
ASIAN CONSULTING ENGINEERS
www.asiancon.com

PRMSC-BWN-DM-WS-KP-00

LAYOUT PLAN

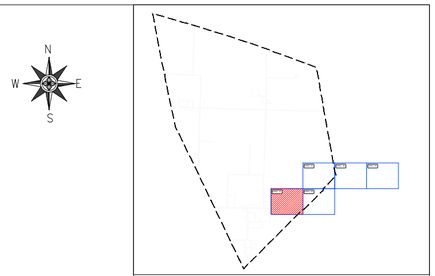

KEY PLAN

LEGEND:

90mm Ø HDPE PIPE	
SLUICE VALVE	
PROPOSED STAND POST TYPE - I	
PROPOSED TUBE WELL	
BOUNDARY	

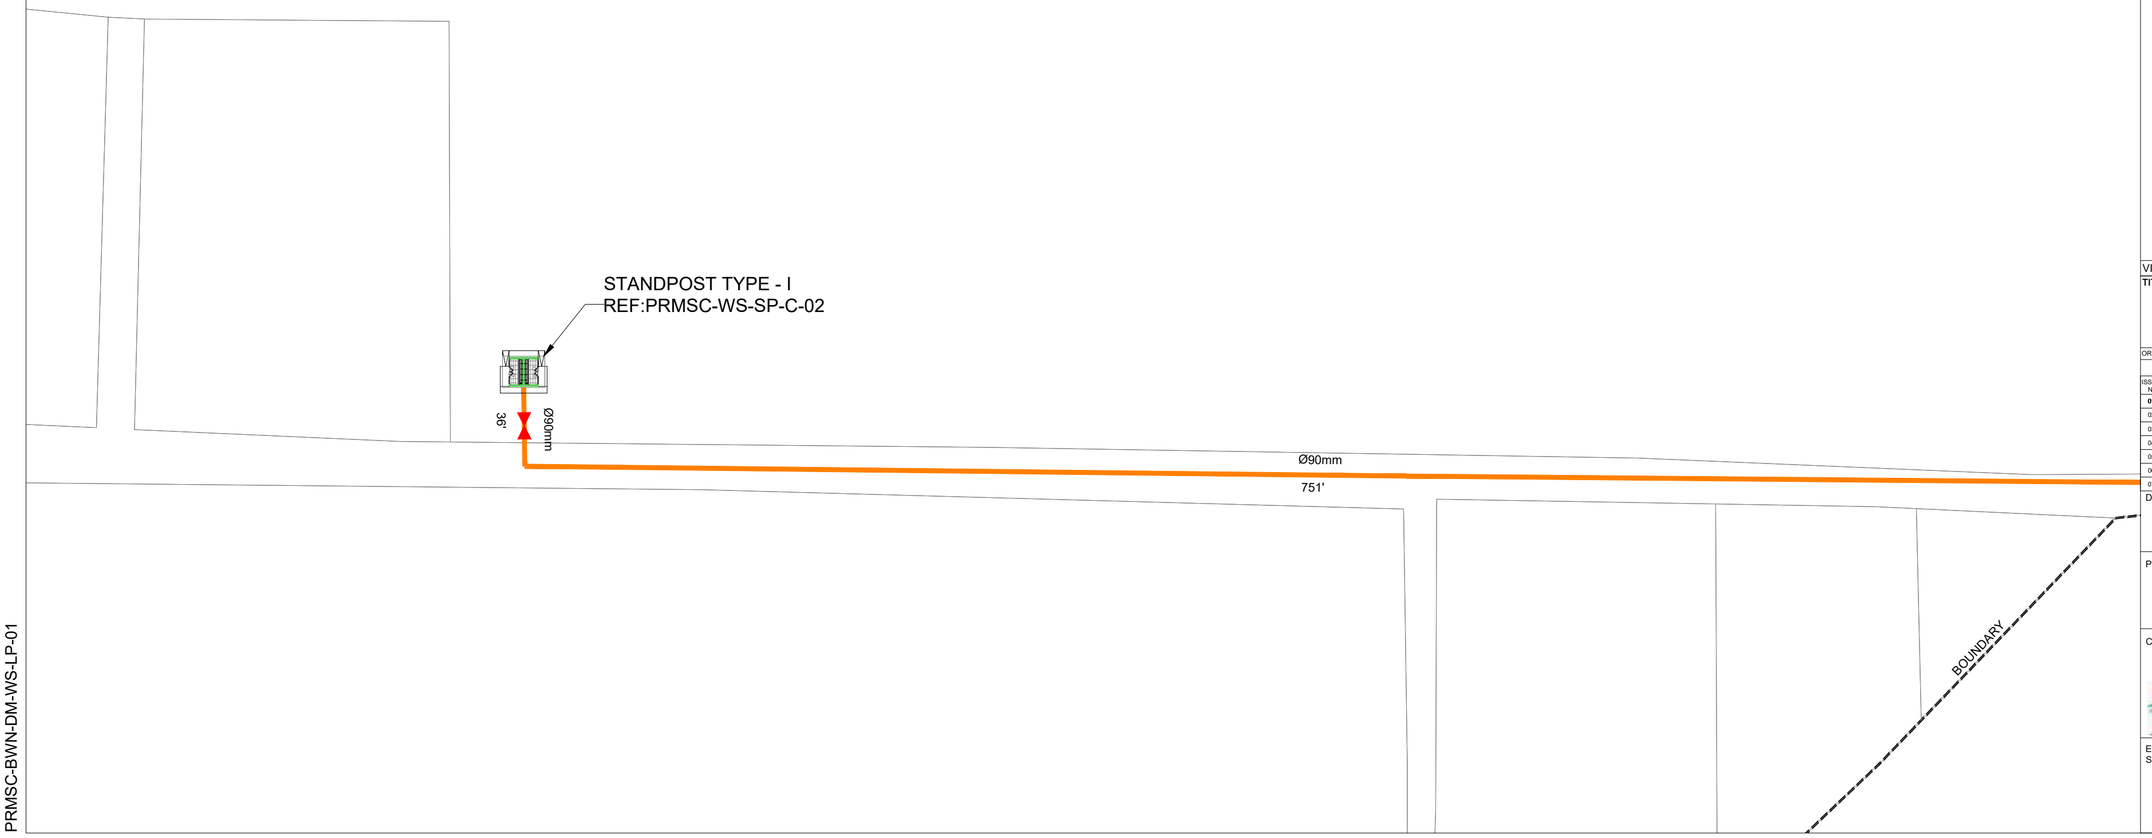

PRMSC-BWN-DM-WS-LP-01

VILLAGE: DADOO MAMMUNKA (BWN)

TITLE.

WATER SUPPLY SYSTEM LAYOUT PLAN-01

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	06-01-2026	DETAILED DESIGN	M.ASIF	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-DM-WS-LP-01	01 OF 05	00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

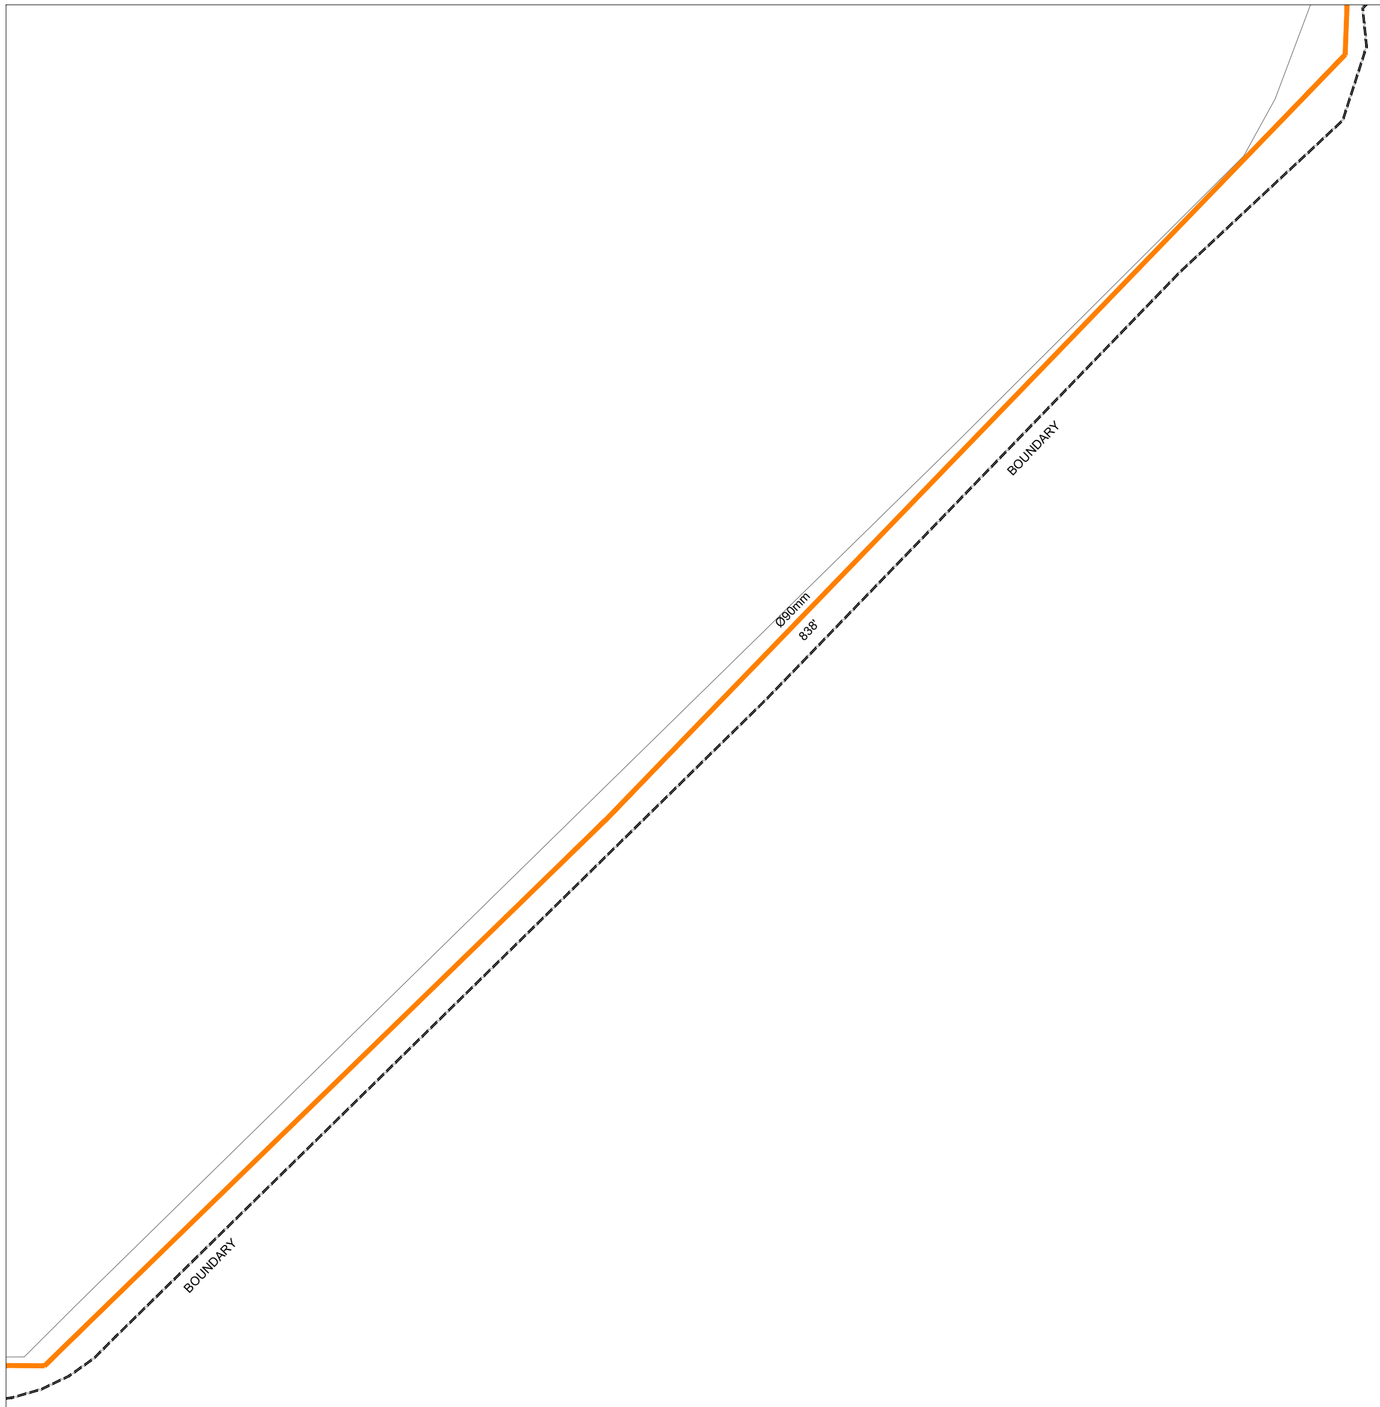

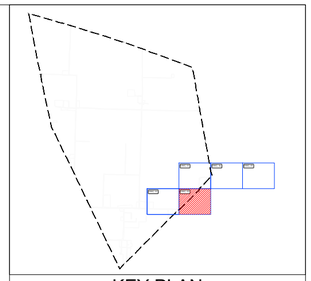

KEY PLAN

LEGEND:

90mm Ø HDPE PIPE

SLUICE VALVE

PROPOSED STAND POST TYPE - I

PROPOSED TUBE WELL

BOUNDARY

VILLAGE: DADOO MAMMUNKA (BWN)

TITLE.

WATER SUPPLY SYSTEM LAYOUT PLAN-02

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	06-01-2026	DETAILED DESIGN	M.ASIF	ENGR FAIEZ	ENGR IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº: PRMSC-BWN-DM-WS-LP-02

SHEET 02 OF 05

REV 00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:
ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

PRMSC-BWN-DM-WS-LP-02

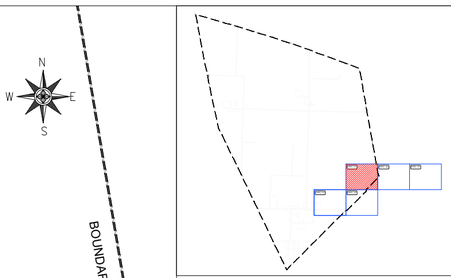

KEY PLAN

LEGEND:

90mm Ø HDPE PIPE

SLUICE VALVE

PROPOSED STAND POST TYPE - I

PROPOSED TUBE WELL

BOUNDARY

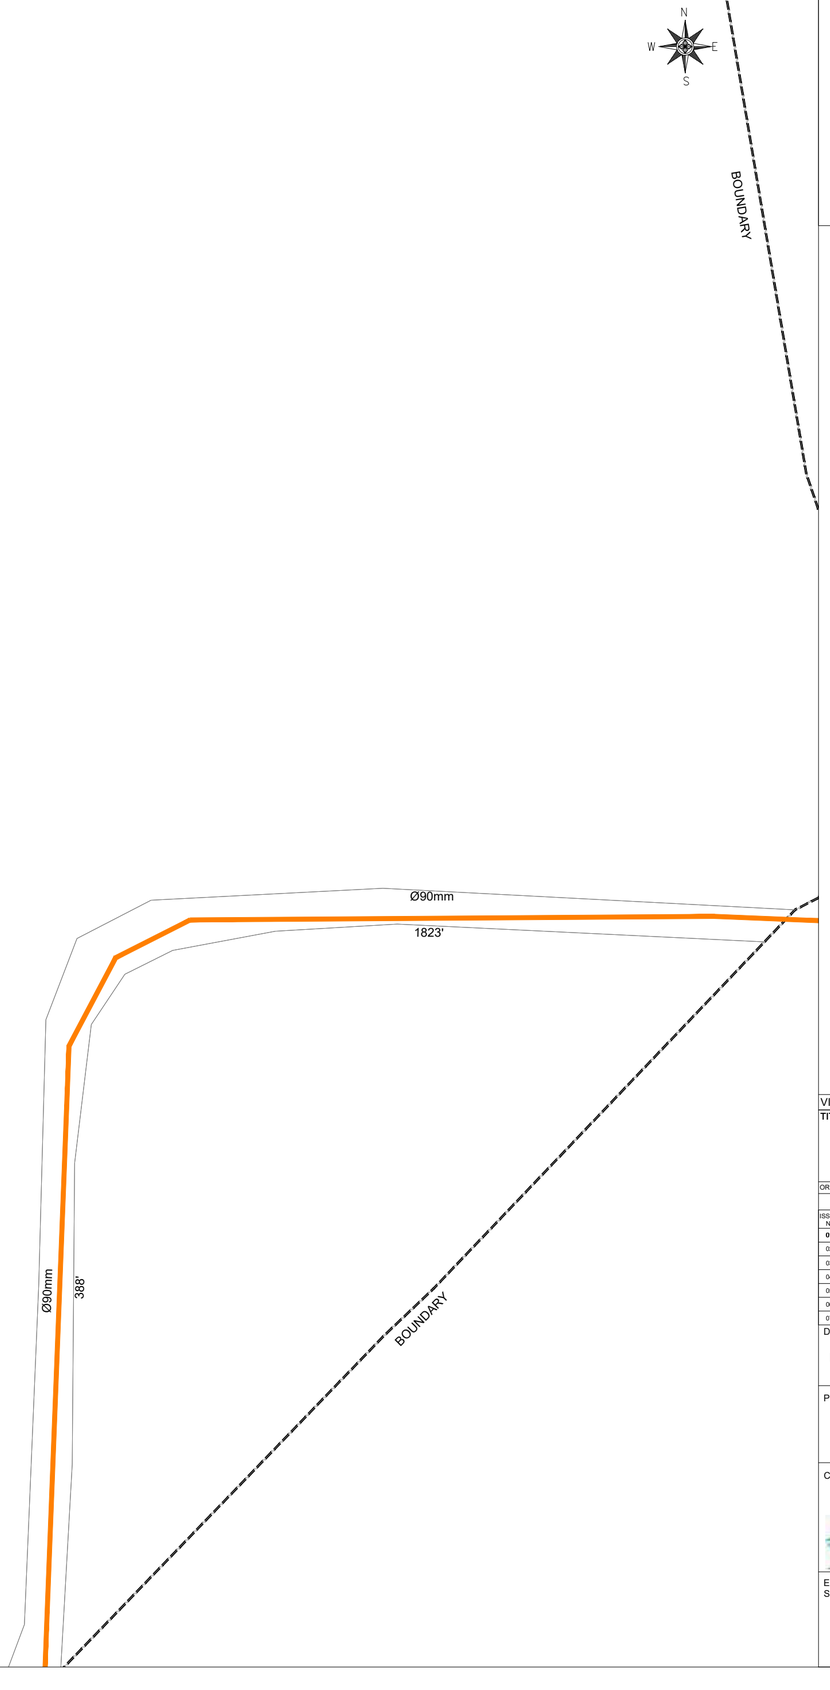

VILLAGE: DADOO MAMMUNKA (BWN)

TITLE.

WATER SUPPLY SYSTEM LAYOUT PLAN-03

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	D E S C R I P T I O N	DRAWN	DESIGNED	APPROVED
01	06-01-2026	DETAILED DESIGN	M.ASIF	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-DM-WS-LP-03	03 OF 05	00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:
ASIAN CONSULTING ENGINEERS
www.asianconsultingengineers.com

PRMSC-BWN-DM-WS-LP-03



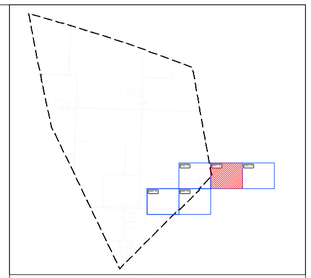

KEY PLAN

LEGEND:

- 90mm Ø HDPE PIPE
- SLUICE VALVE
- PROPOSED STAND POST TYPE - I
- PROPOSED TUBE WELL
- BOUNDARY

VILLAGE: DADOO MAMMUNKA (BWN)

TITLE.

WATER SUPPLY SYSTEM LAYOUT PLAN-04

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	D E S C R I P T I O N	DRAWN	DESIGNED	APPROVED
01	06-01-2026	DETAILED DESIGN	M.ASIF	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-DM-WS-LP-04	04 OF 05	00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:
ASIAN CONSULTING ENGINEERS
www.asianconsultants.com

PRMSC-BWN-DM-WS-LP-04

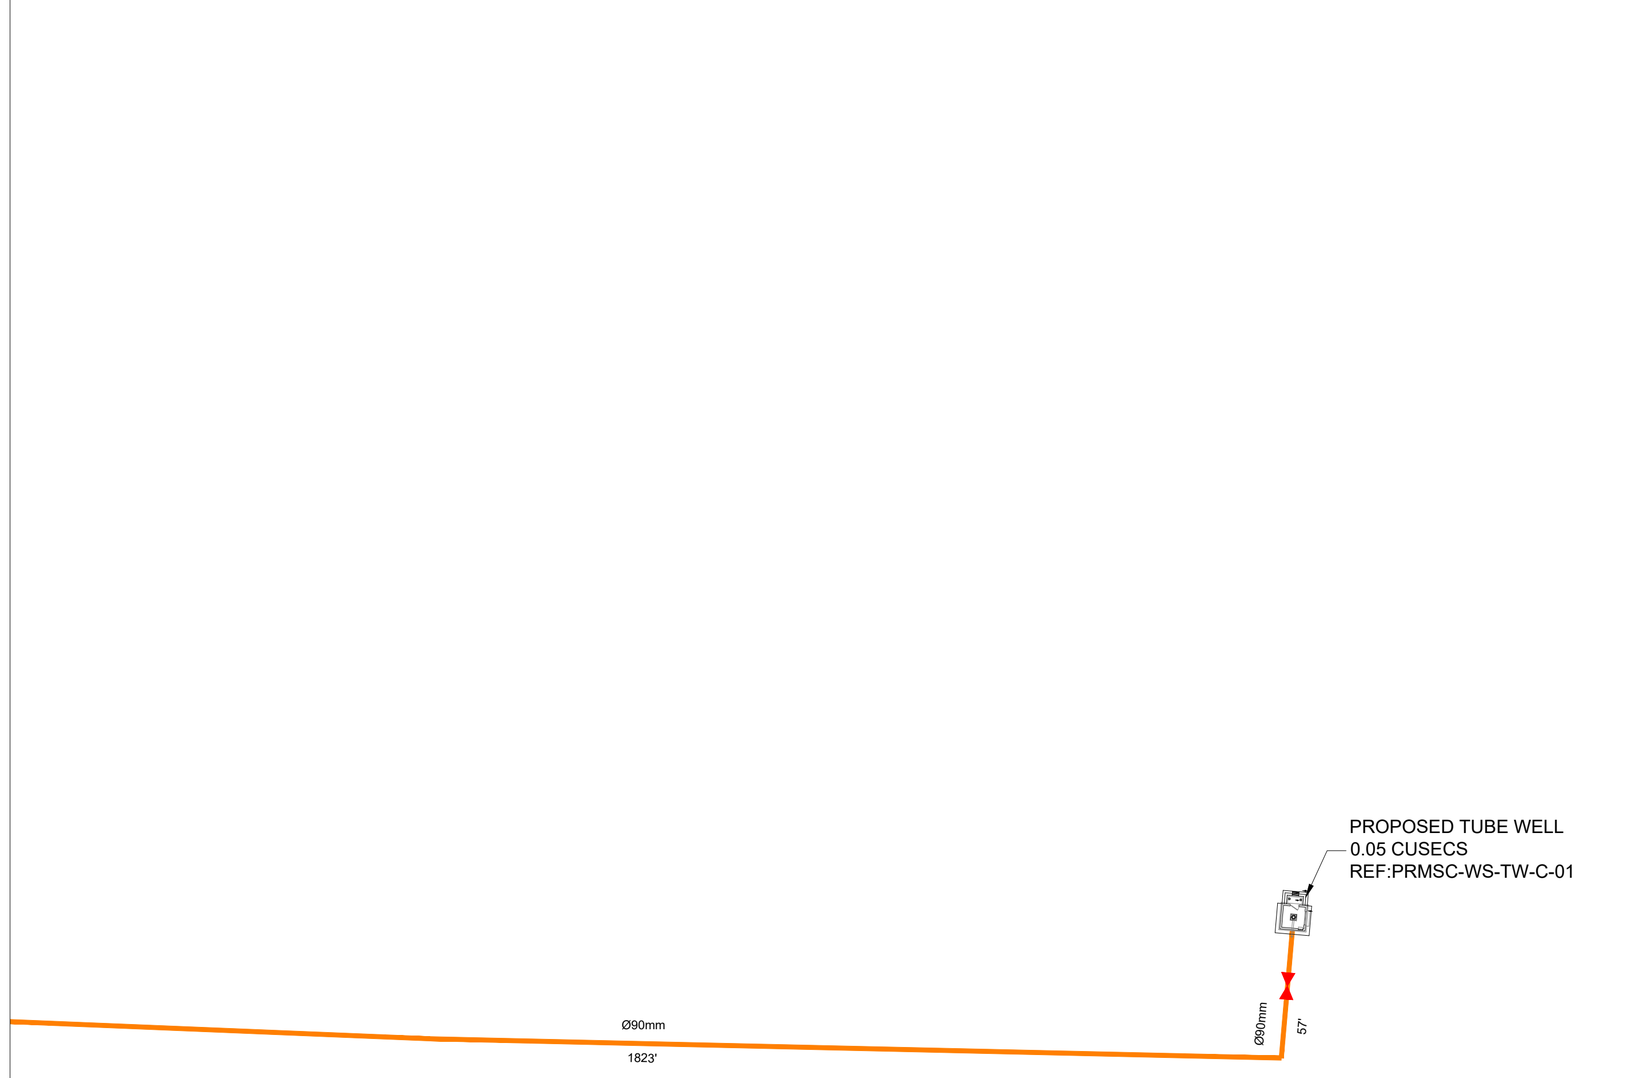

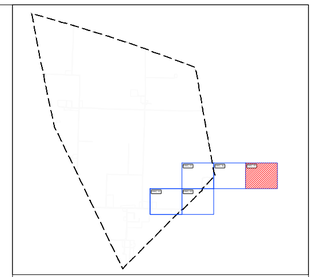

KEY PLAN

LEGEND:

90mm Ø HDPE PIPE

SLUICE VALVE

PROPOSED STAND POST TYPE - I

PROPOSED TUBE WELL

BOUNDARY

VILLAGE: DADOO MAMMUNKA (BWN)

TITLE.

WATER SUPPLY SYSTEM LAYOUT PLAN-05

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	06-01-2026	DETAILED DESIGN	M.ASIF	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-DM-WS-LP-05	05 OF 05	00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS (PVT) LTD. www.asiancon.com.pk

PRMSC-BWN-DM-WS-LP-05

HASAN RAIKA

KEY PLAN

Title:
Proposed Water Supply Plan

Legend:

- SETTLEMENT
- STAND POST
- SETTELMENT BOUNDARY

Scale: 1:3,100
1 inch = 258 feet
Paper Size: A3

0 40 80 160
Kilometers

Project:
Engineering Design & Construction Supervision, Punjab Rural Sustainable Water Supply & Sanitation Project, Cluster South-III

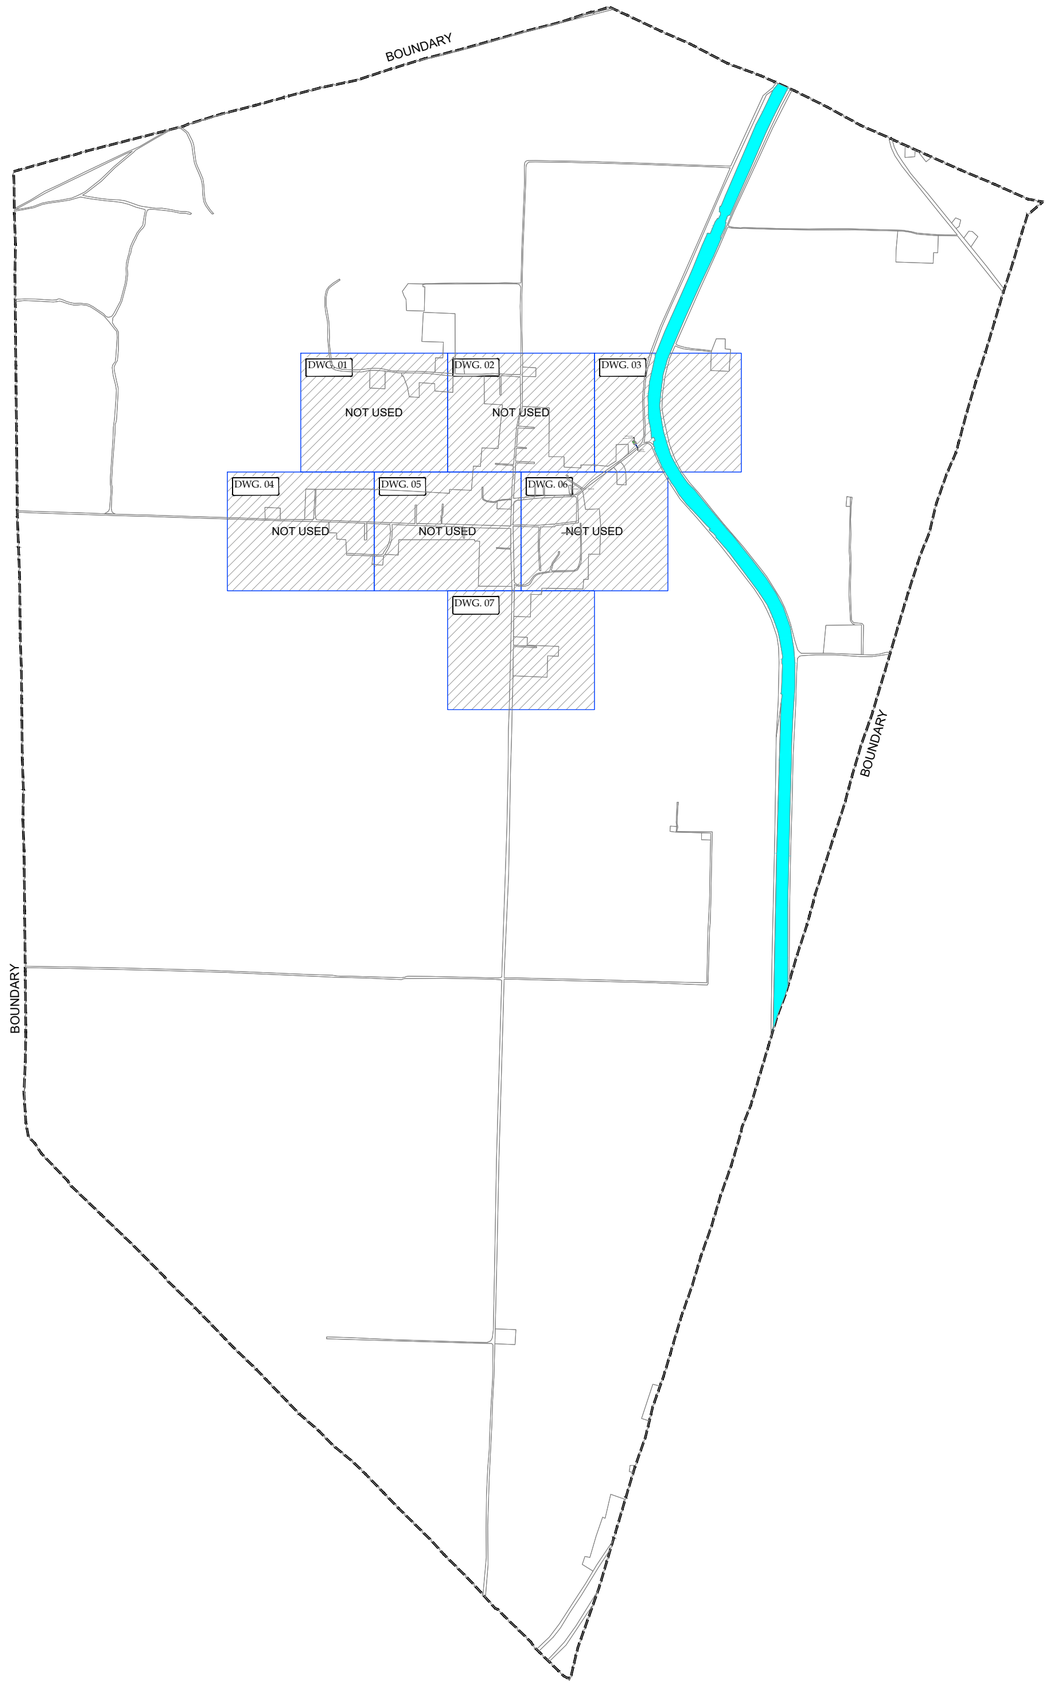

N
W
E
S

LEGEND:

PROPOSED STAND POST TYPE - II

BOUNDARY

VILLAGE: HASAN RAEKA (BWN)

TITLE.

WATER SUPPLY SYSTEM KEY PLAN

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 720'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	02-03-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING N°: PRMSC-BWN-HRK-WS-KP-00

SHEET 00 OF 00

REV 00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT
ASIAN CONSULTING ENGINEERS (PVT) LTD.
www.asiancon.com.pk

PRMSC-BWN-HRK-WS-KP-00

LAYOUT PLAN

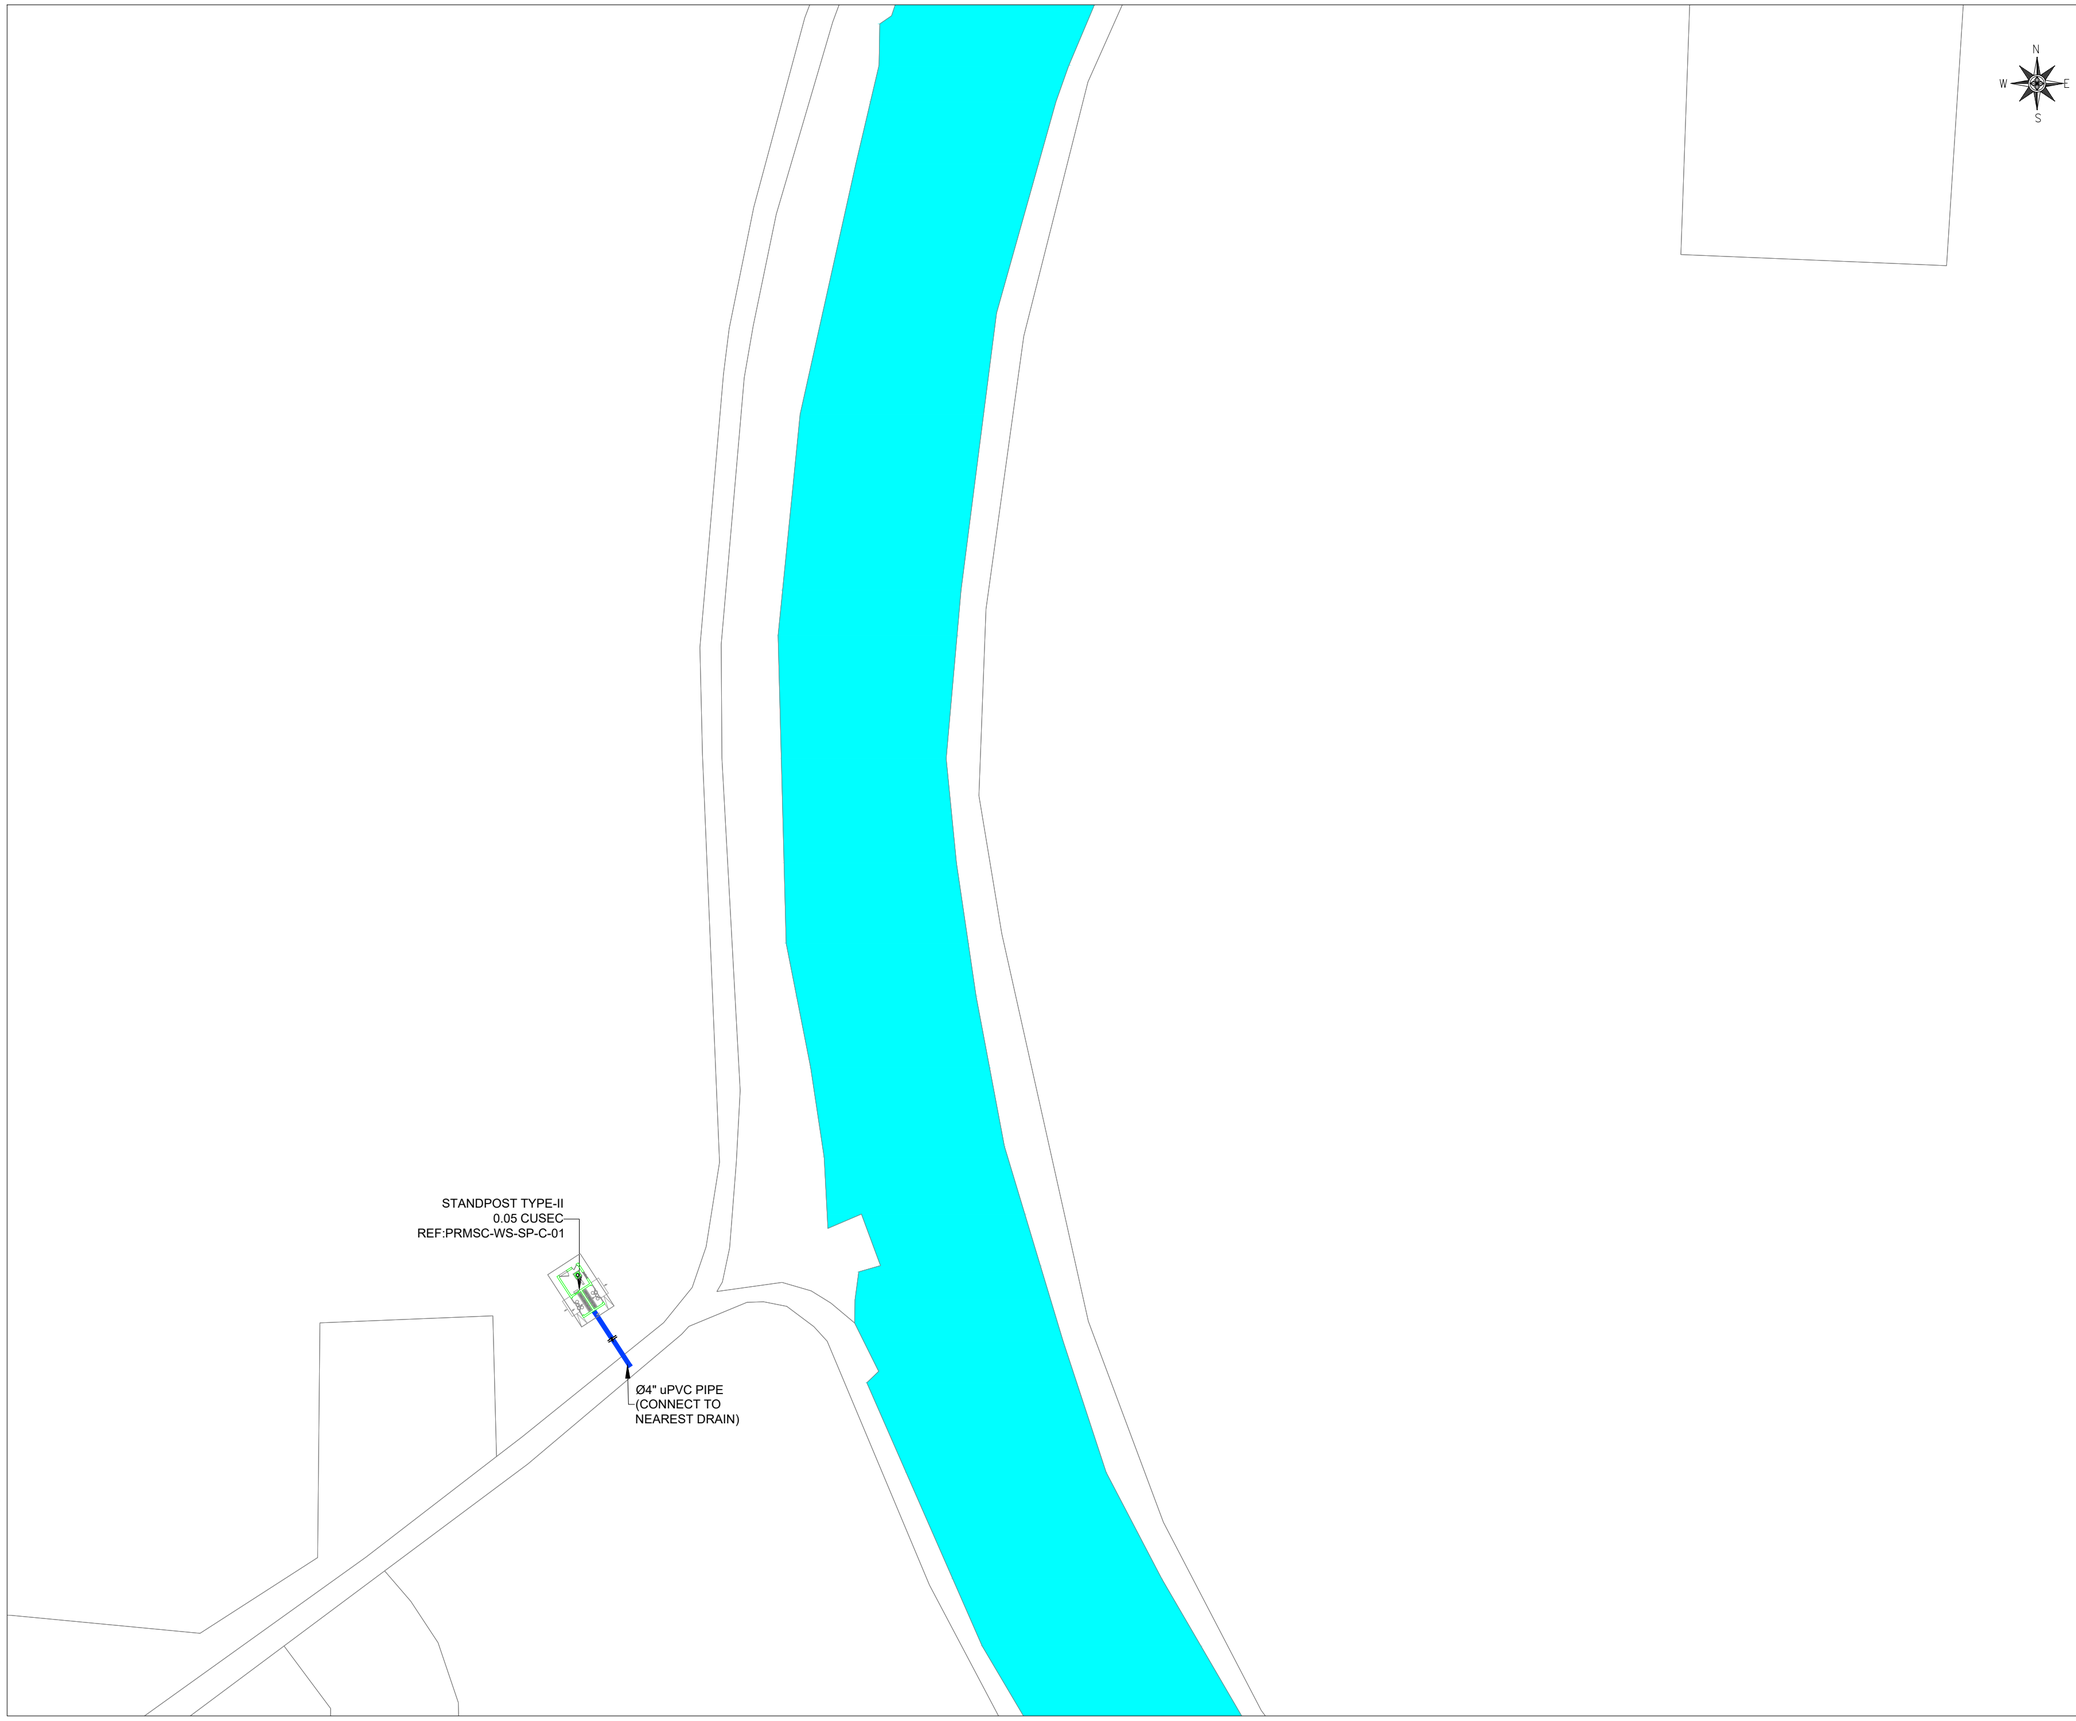



KEY PLAN

LEGEND:

PROPOSED STAND POST TYPE - II

BOUNDARY

VILLAGE: HASAN RAEKA (BWN)

TITLE.

WATER SUPPLY SYSTEM LAYOUT PLAN-03

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	D E S C R I P T I O N	DRAWN	DESIGNED	APPROVED
01	02-03-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº: PRMSC-BWN-HRK-WS-LP-03

SHEET 03 OF 07

REV 00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS www.asianeon.com

PRMSC-BWN-HRK-WS-LP-03

JAGGA SANATTEKA

KEY PLAN

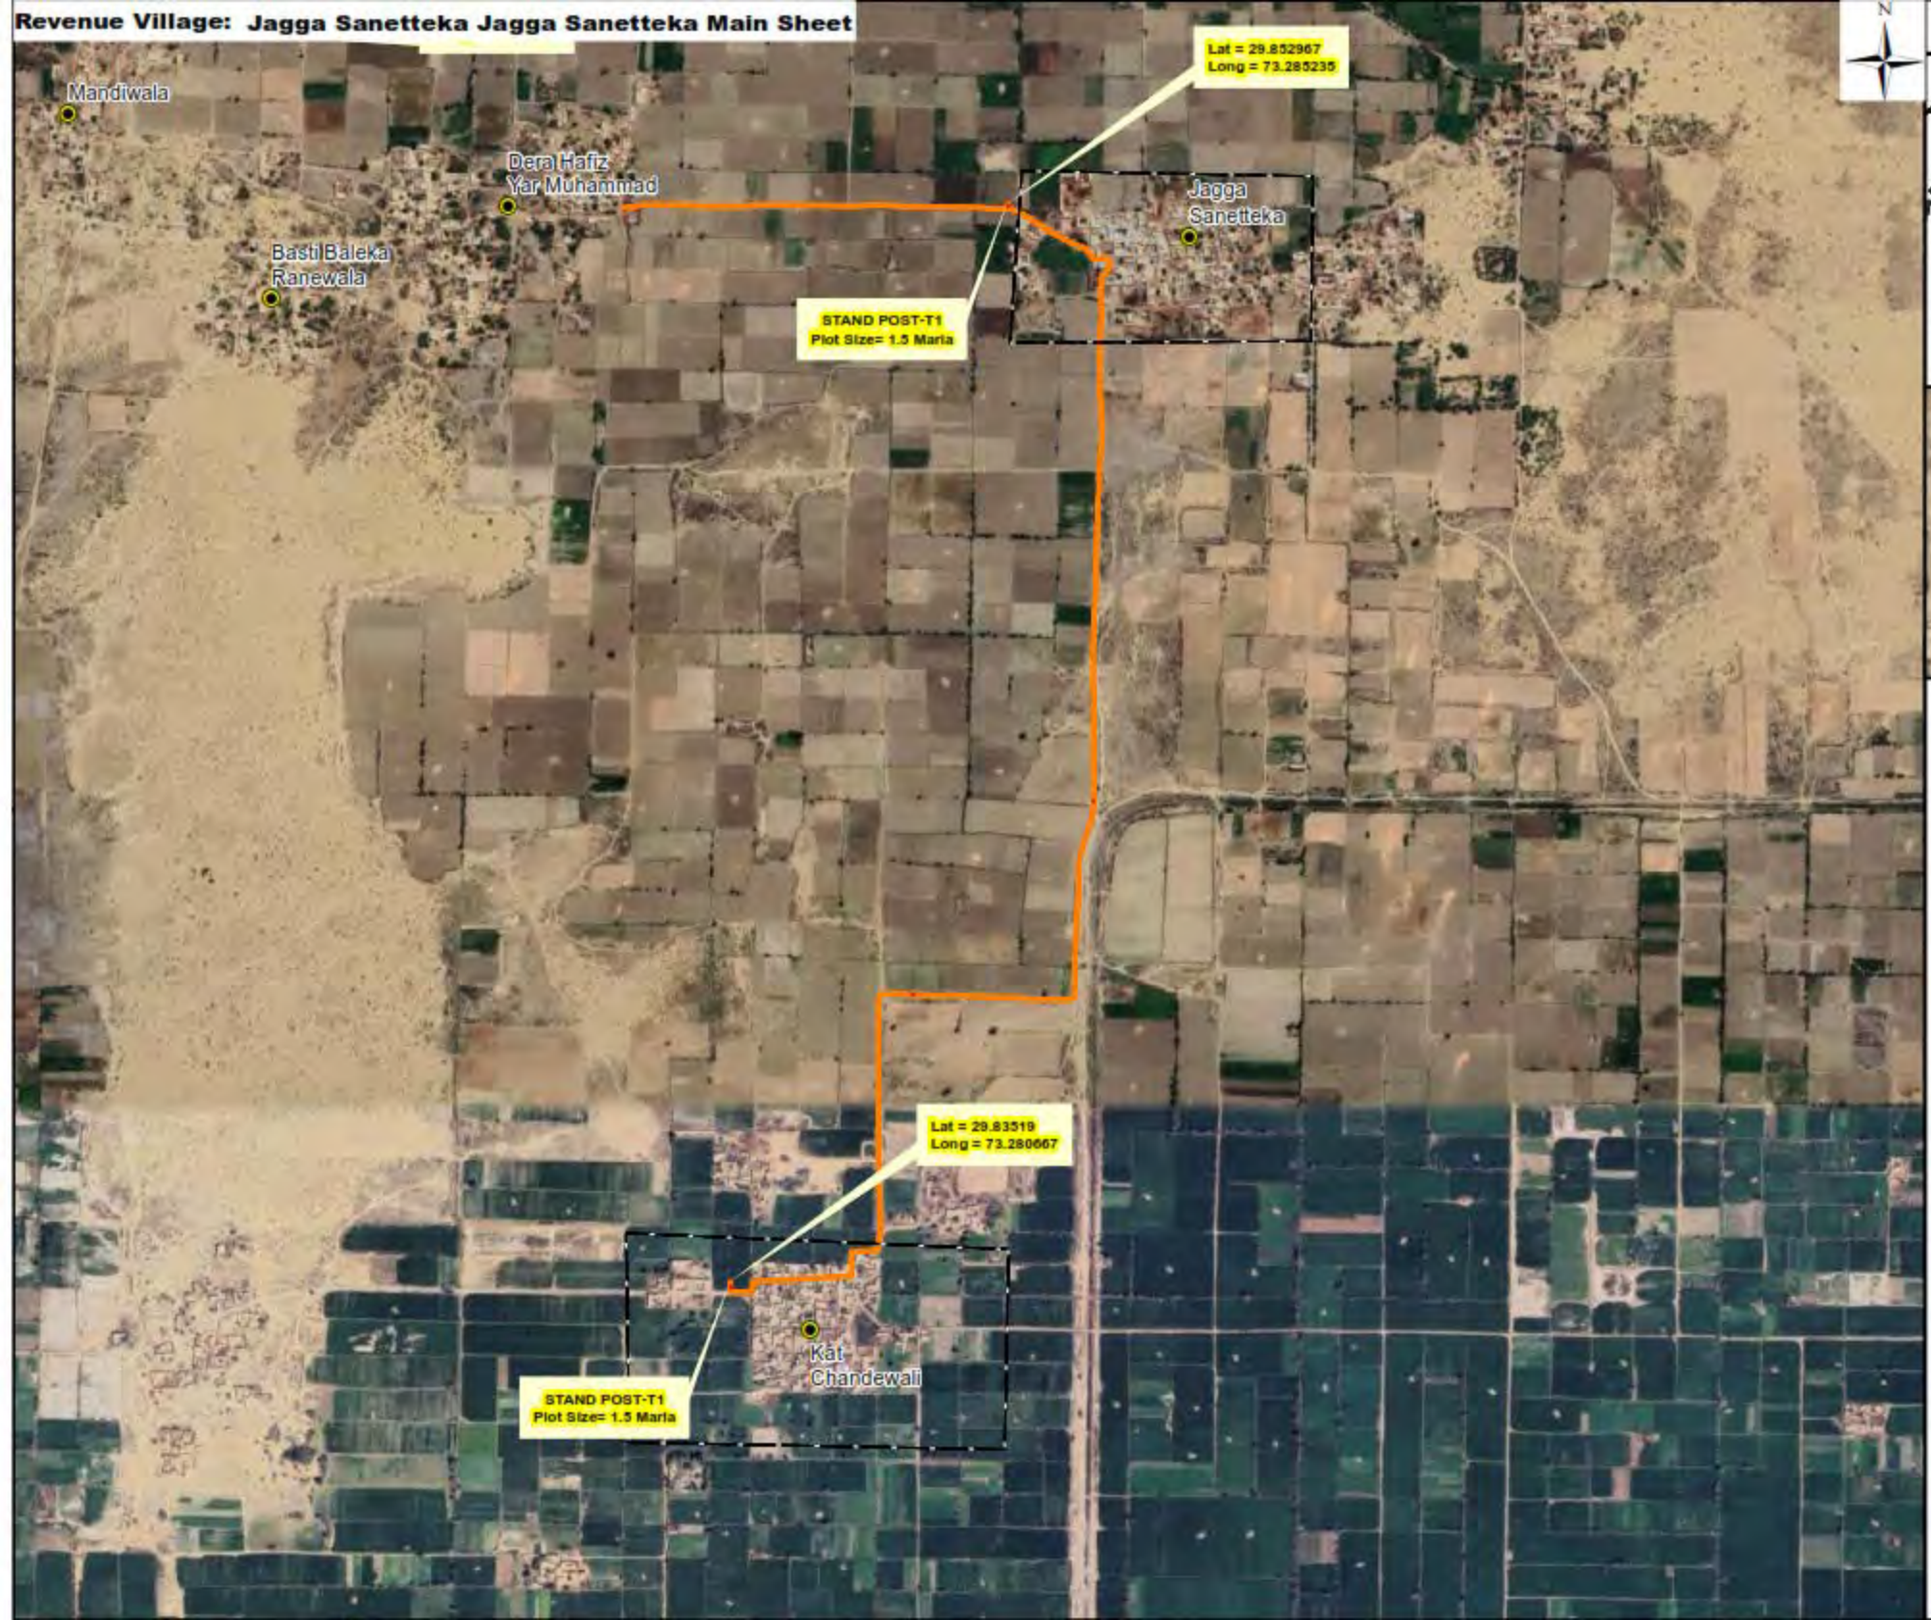

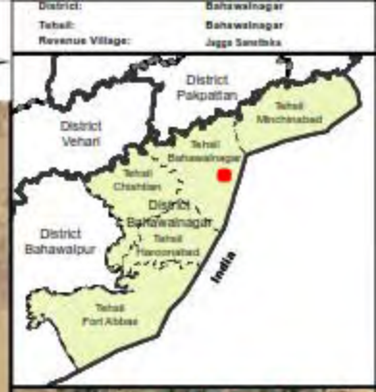

Title:
Proposed Water Supply Plan

Legend:

- SETTLEMENT

DISTRIBUTION NETWORK

- 90 mm Ø
- STAND POST
- SETTELMENT BOUNDARY

Scale: 1:10,000
1 inch = 833 feet
Paper Size: A3

0 40 80 160
Kilometers

Project:
Engineering Design & Construction Supervision, Punjab Rural Sustainable Water Supply & Sanitation Project, Cluster South-III

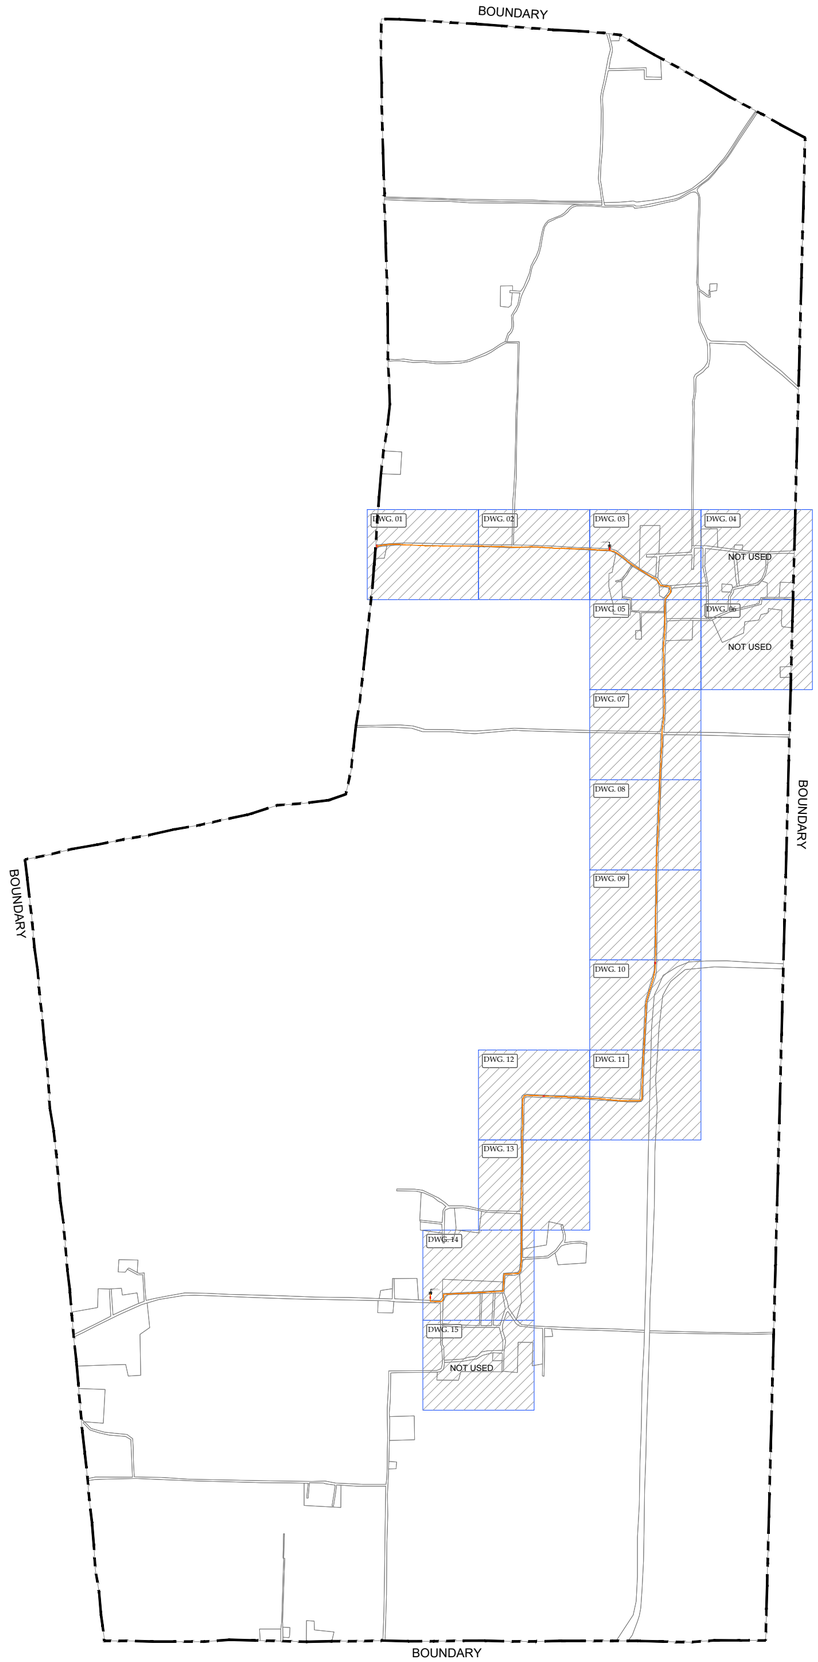

N
W E
S

LEGEND:

- 90mm Ø HDPE PIPE
- SLUICE VALVE
- WASHOUT VALVE
- AIR RELEASE VALVE
- STAND POST TYPE - I
- DEAD END
- BOUNDARY

VILLAGE: JAGGA SANETTEKA (BWN)

TITLE.

WATER SUPPLY SYSTEM KEY PLAN

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 950'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	16-12-2025	DETAILED DESIGN	ASAD	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº: PRMSC-BWN-JST-WS-KP-00

SHEET 00 OF 00

REV 00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT
ASIAN CONSULTING ENGINEERS
www.asiancon.com

PRMSC-BWN-JST-SEW-KP-00

LAYOUT PLANS

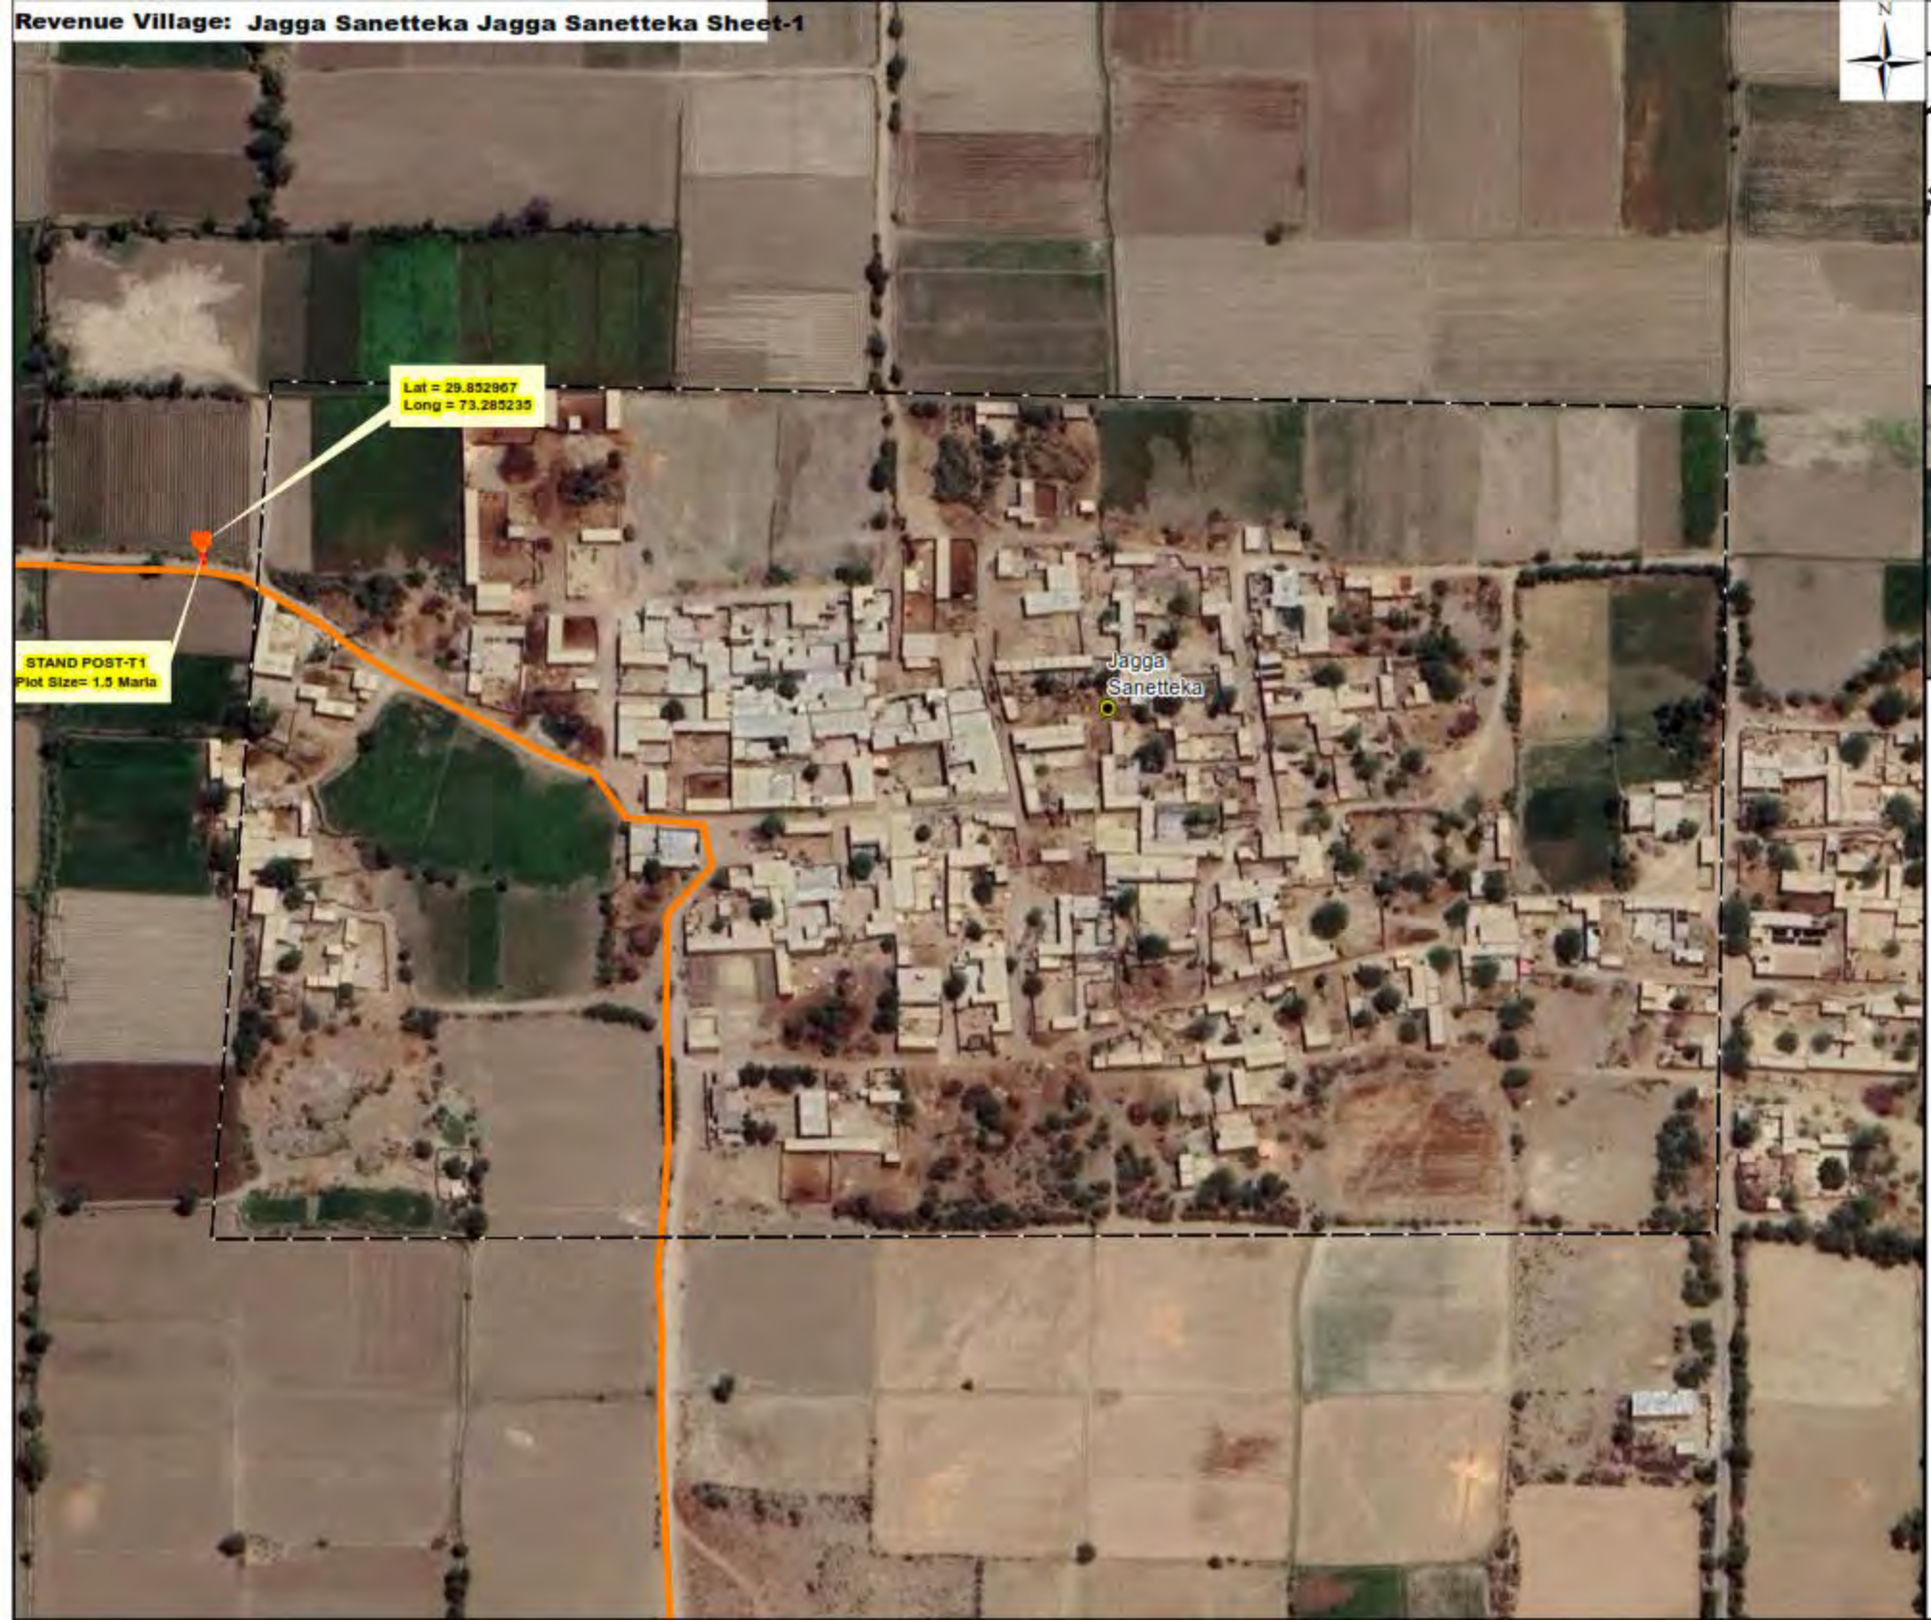



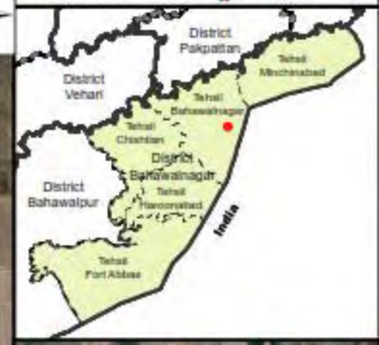

Title:
Proposed Water Supply Plan

Legend:

DISTRIBUTION NETWORK

- 90 mm Ø
- SETTLEMENT
- STAND POST
- SETTELMENT BOUNDARY

Scale: 1:2,000
1 inch = 167 feet
Paper Size: A3

0 40 80 160
Kilometers

Project:
Engineering Design & Construction Supervision, Punjab Rural Sustainable Water Supply & Sanitation Project, Cluster South-III

Title:
Proposed Water Supply Plan

Legend:

DISTRIBUTION NETWORK

- 90 mm Ø
- SETTLEMENT
- STAND POST
- SETTELMENT BOUNDARY

Scale: 1:2,500
1 inch = 208 feet
Paper Size: A3

0 40 80 160
Kilometers

Project:
Engineering Design & Construction Supervision, Punjab Rural Sustainable Water Supply & Sanitation Project, Cluster South-III

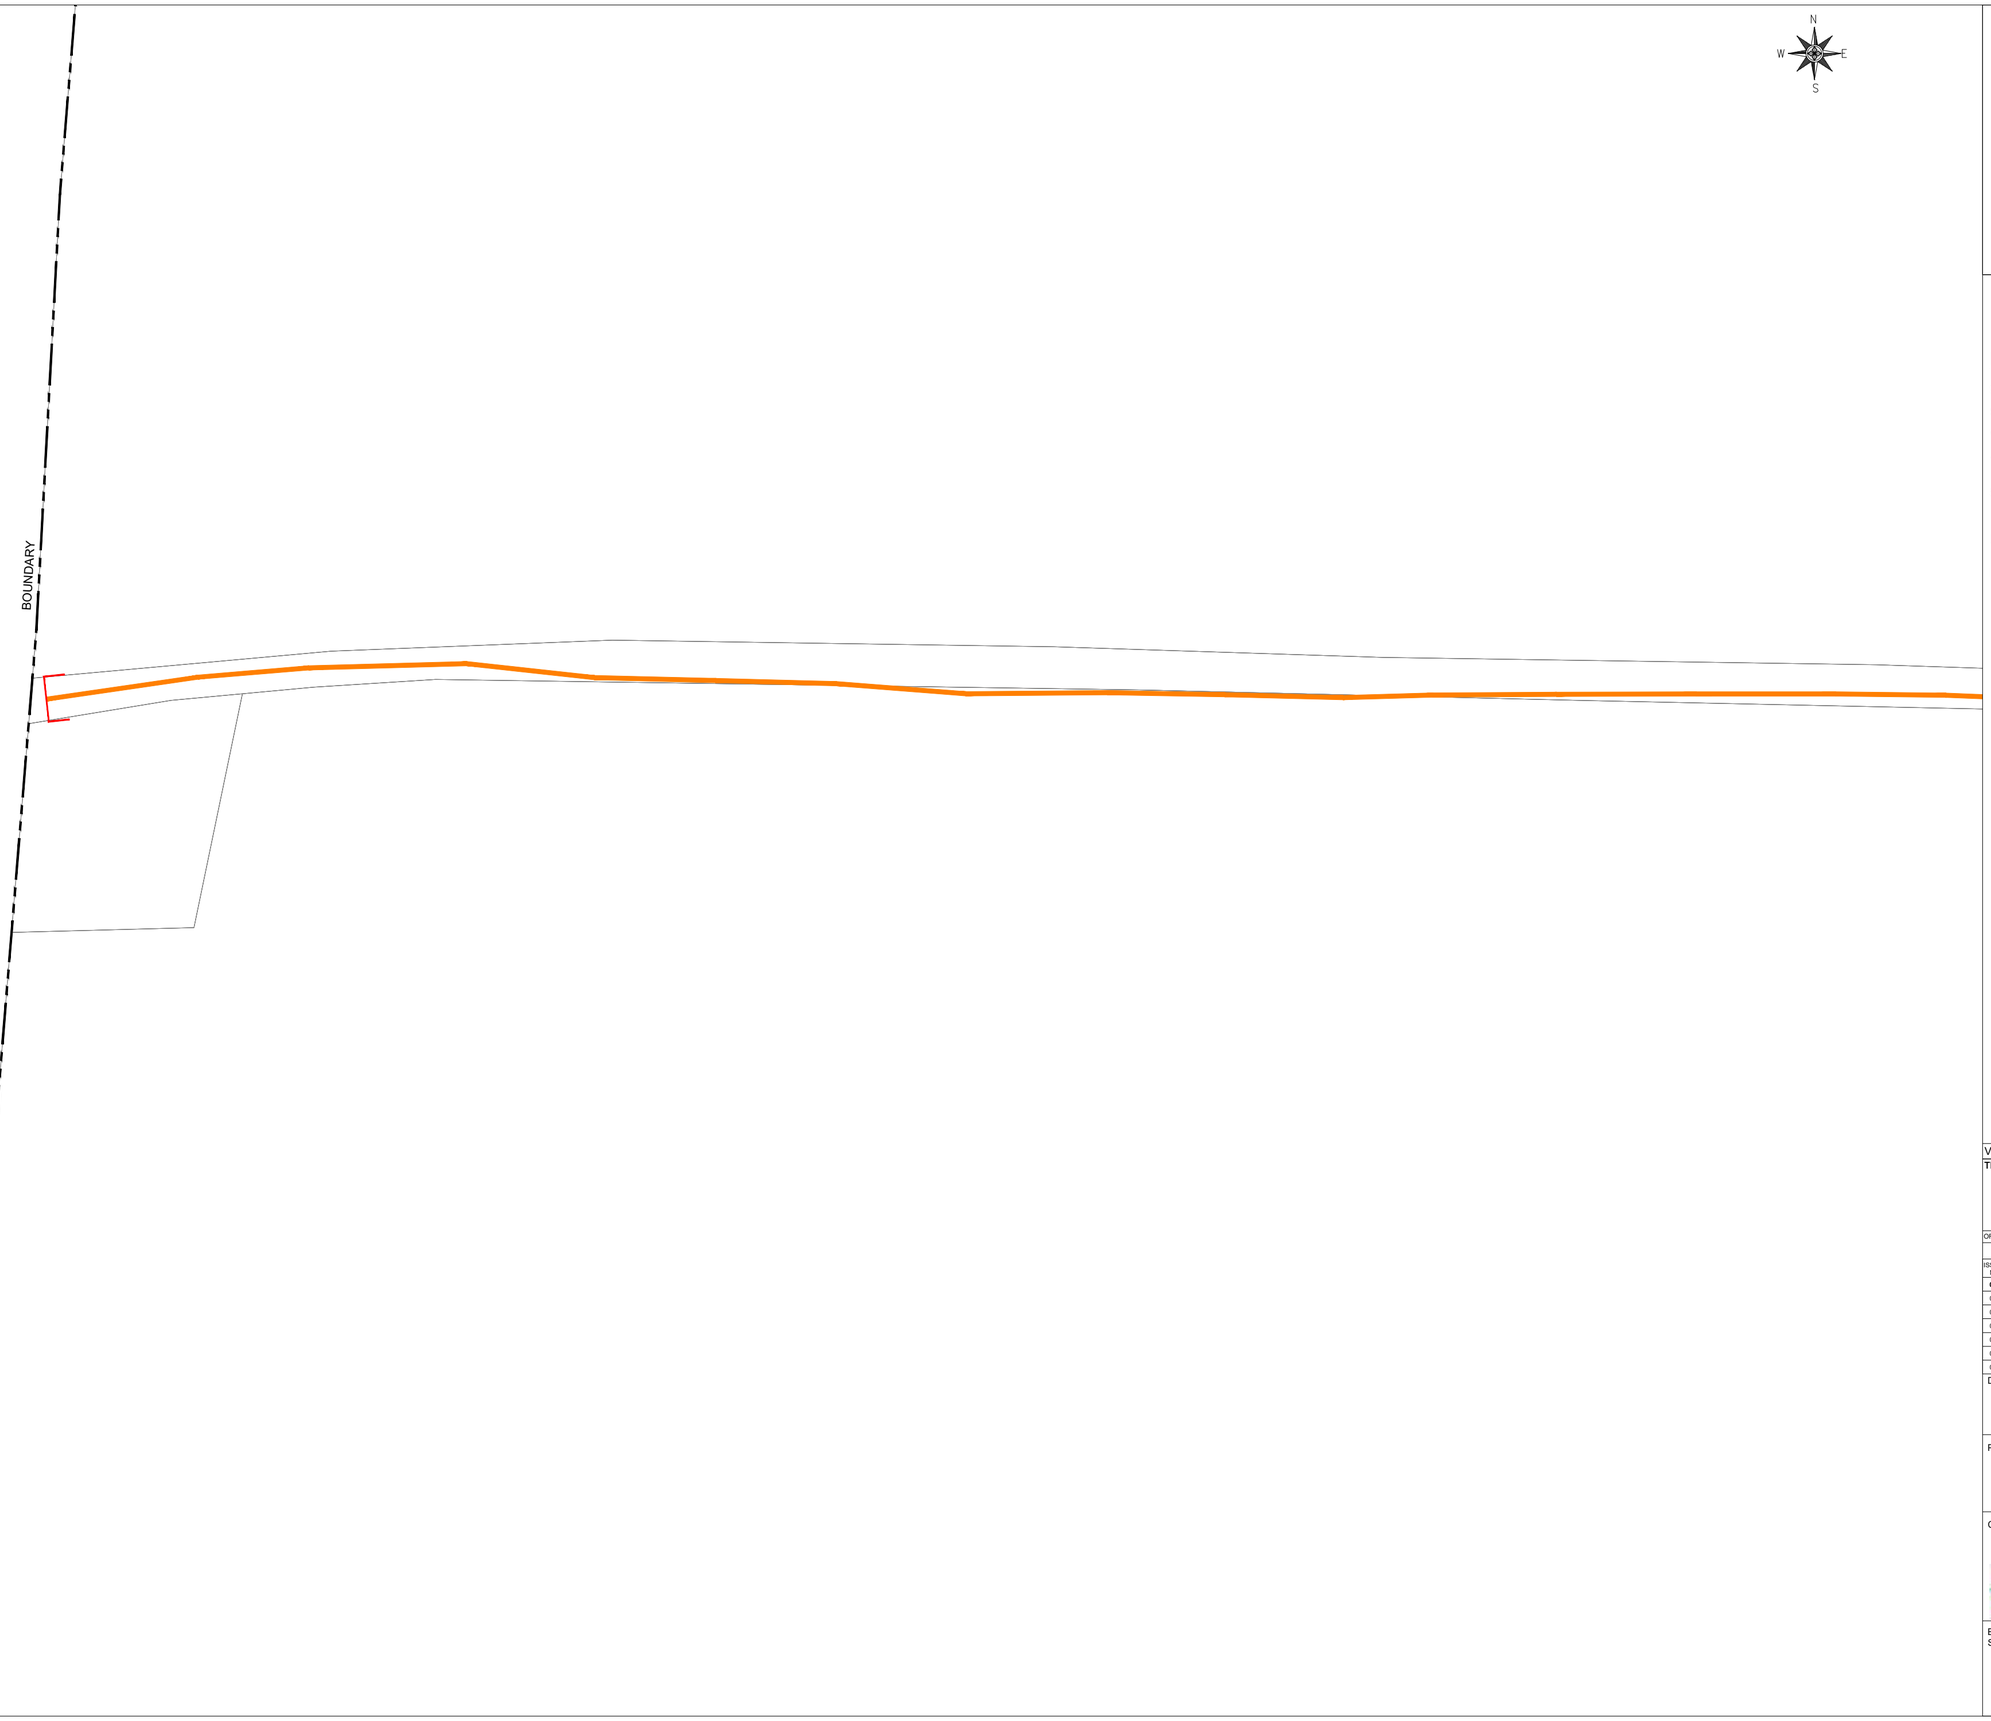

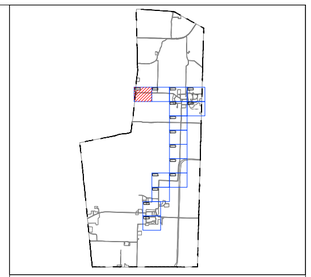

KEY PLAN

LEGEND:

- 90mm Ø HDPE PIPE
- SLUICE VALVE
- WASHOUT VALVE
- AIR RELEASE VALVE
- STAND POST TYPE - I
- DEAD END
- BOUNDARY

VILLAGE: JAGGA SANETTEKA (BWN)

TITLE.

WATER SUPPLY SYSTEM LAYOUT PLAN-01

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	16-12-2025	DETAILED DESIGN	ASAD	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº: PRMSC-BWN-JST-WS-LP-01

SHEET 01 OF 15

REV 00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:
ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

PRMSC-BWN-JST-WS-LP-01

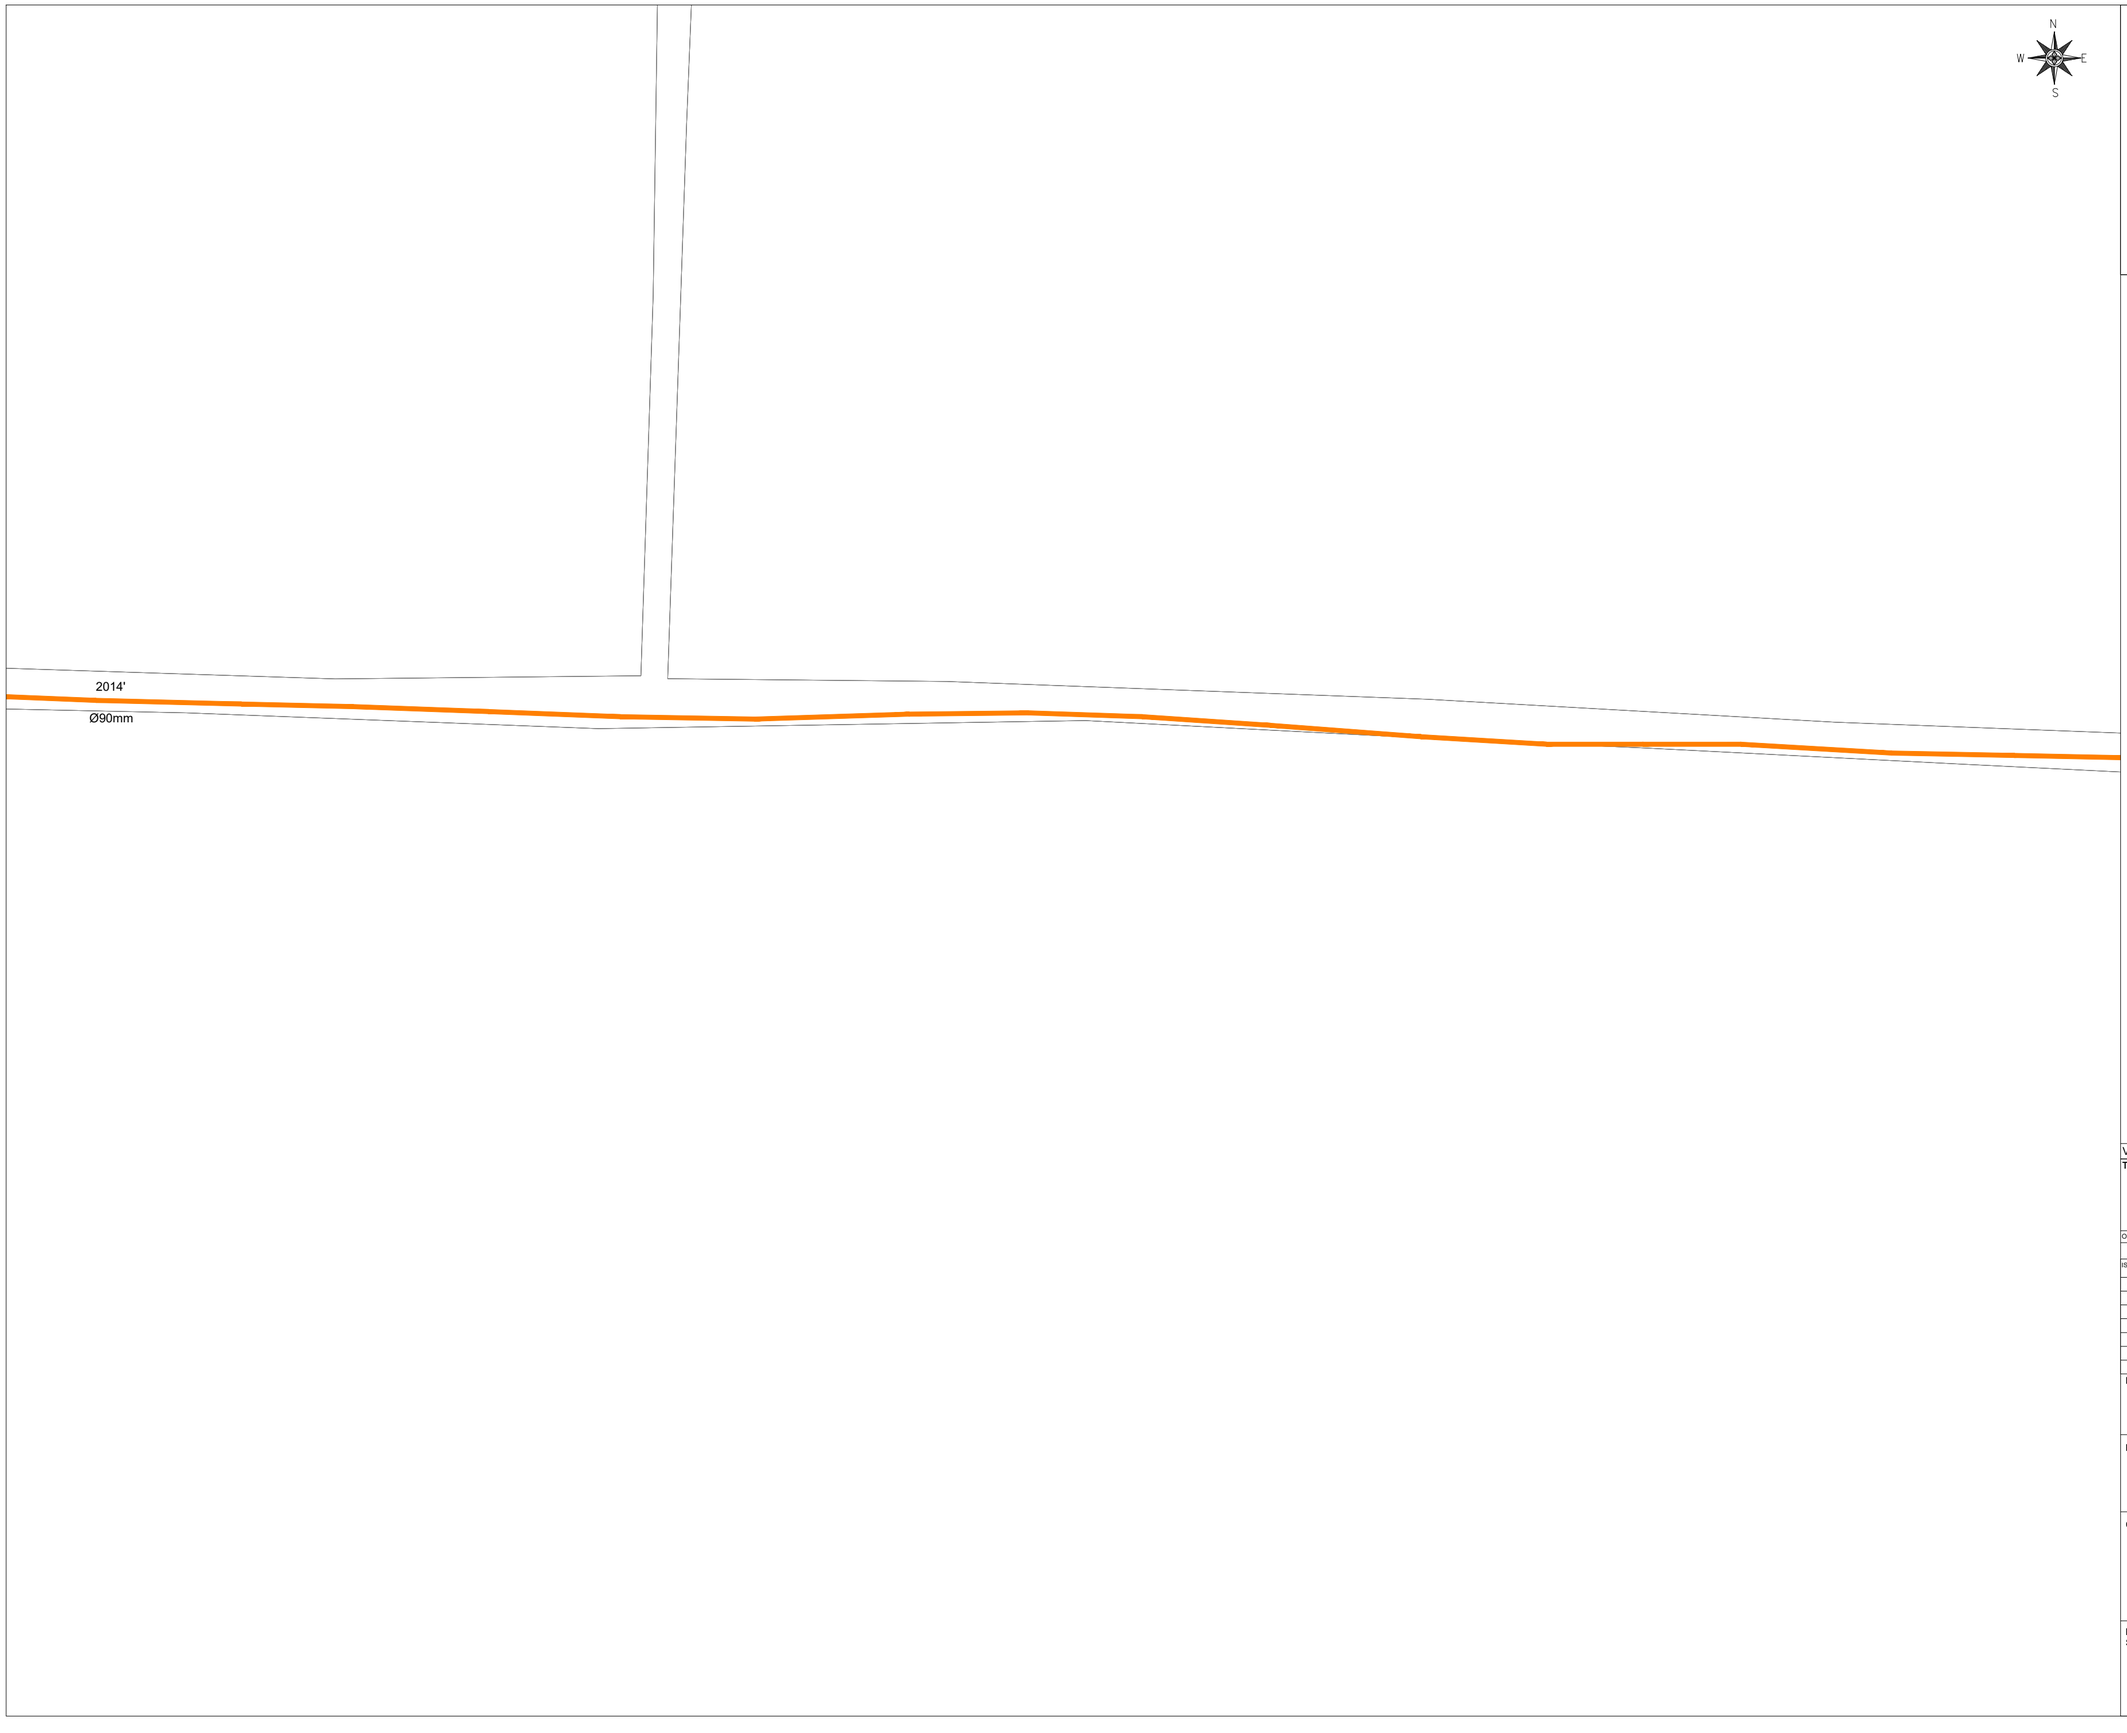

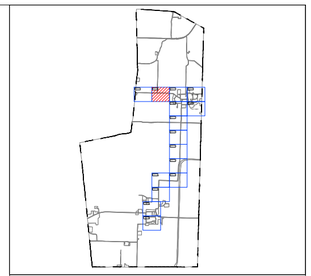

KEY PLAN

LEGEND:

- 90mm Ø HDPE PIPE
- SLUICE VALVE
- WASHOUT VALVE
- AIR RELEASE VALVE
- STAND POST TYPE - I
- DEAD END
- BOUNDARY

VILLAGE: JAGGA SANETTEKA (BWN)

TITLE.

WATER SUPPLY SYSTEM LAYOUT PLAN-02

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	16-12-2025	DETAILED DESIGN	ASAD	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-JST-WS-LP-02	02 OF 15	00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ENVIRONMENTAL MANAGEMENT — ASIAN CONSULTING ENGINEERS — www.asiancon.com.pk

PRMSC-BWN-JST-WS-LP-02

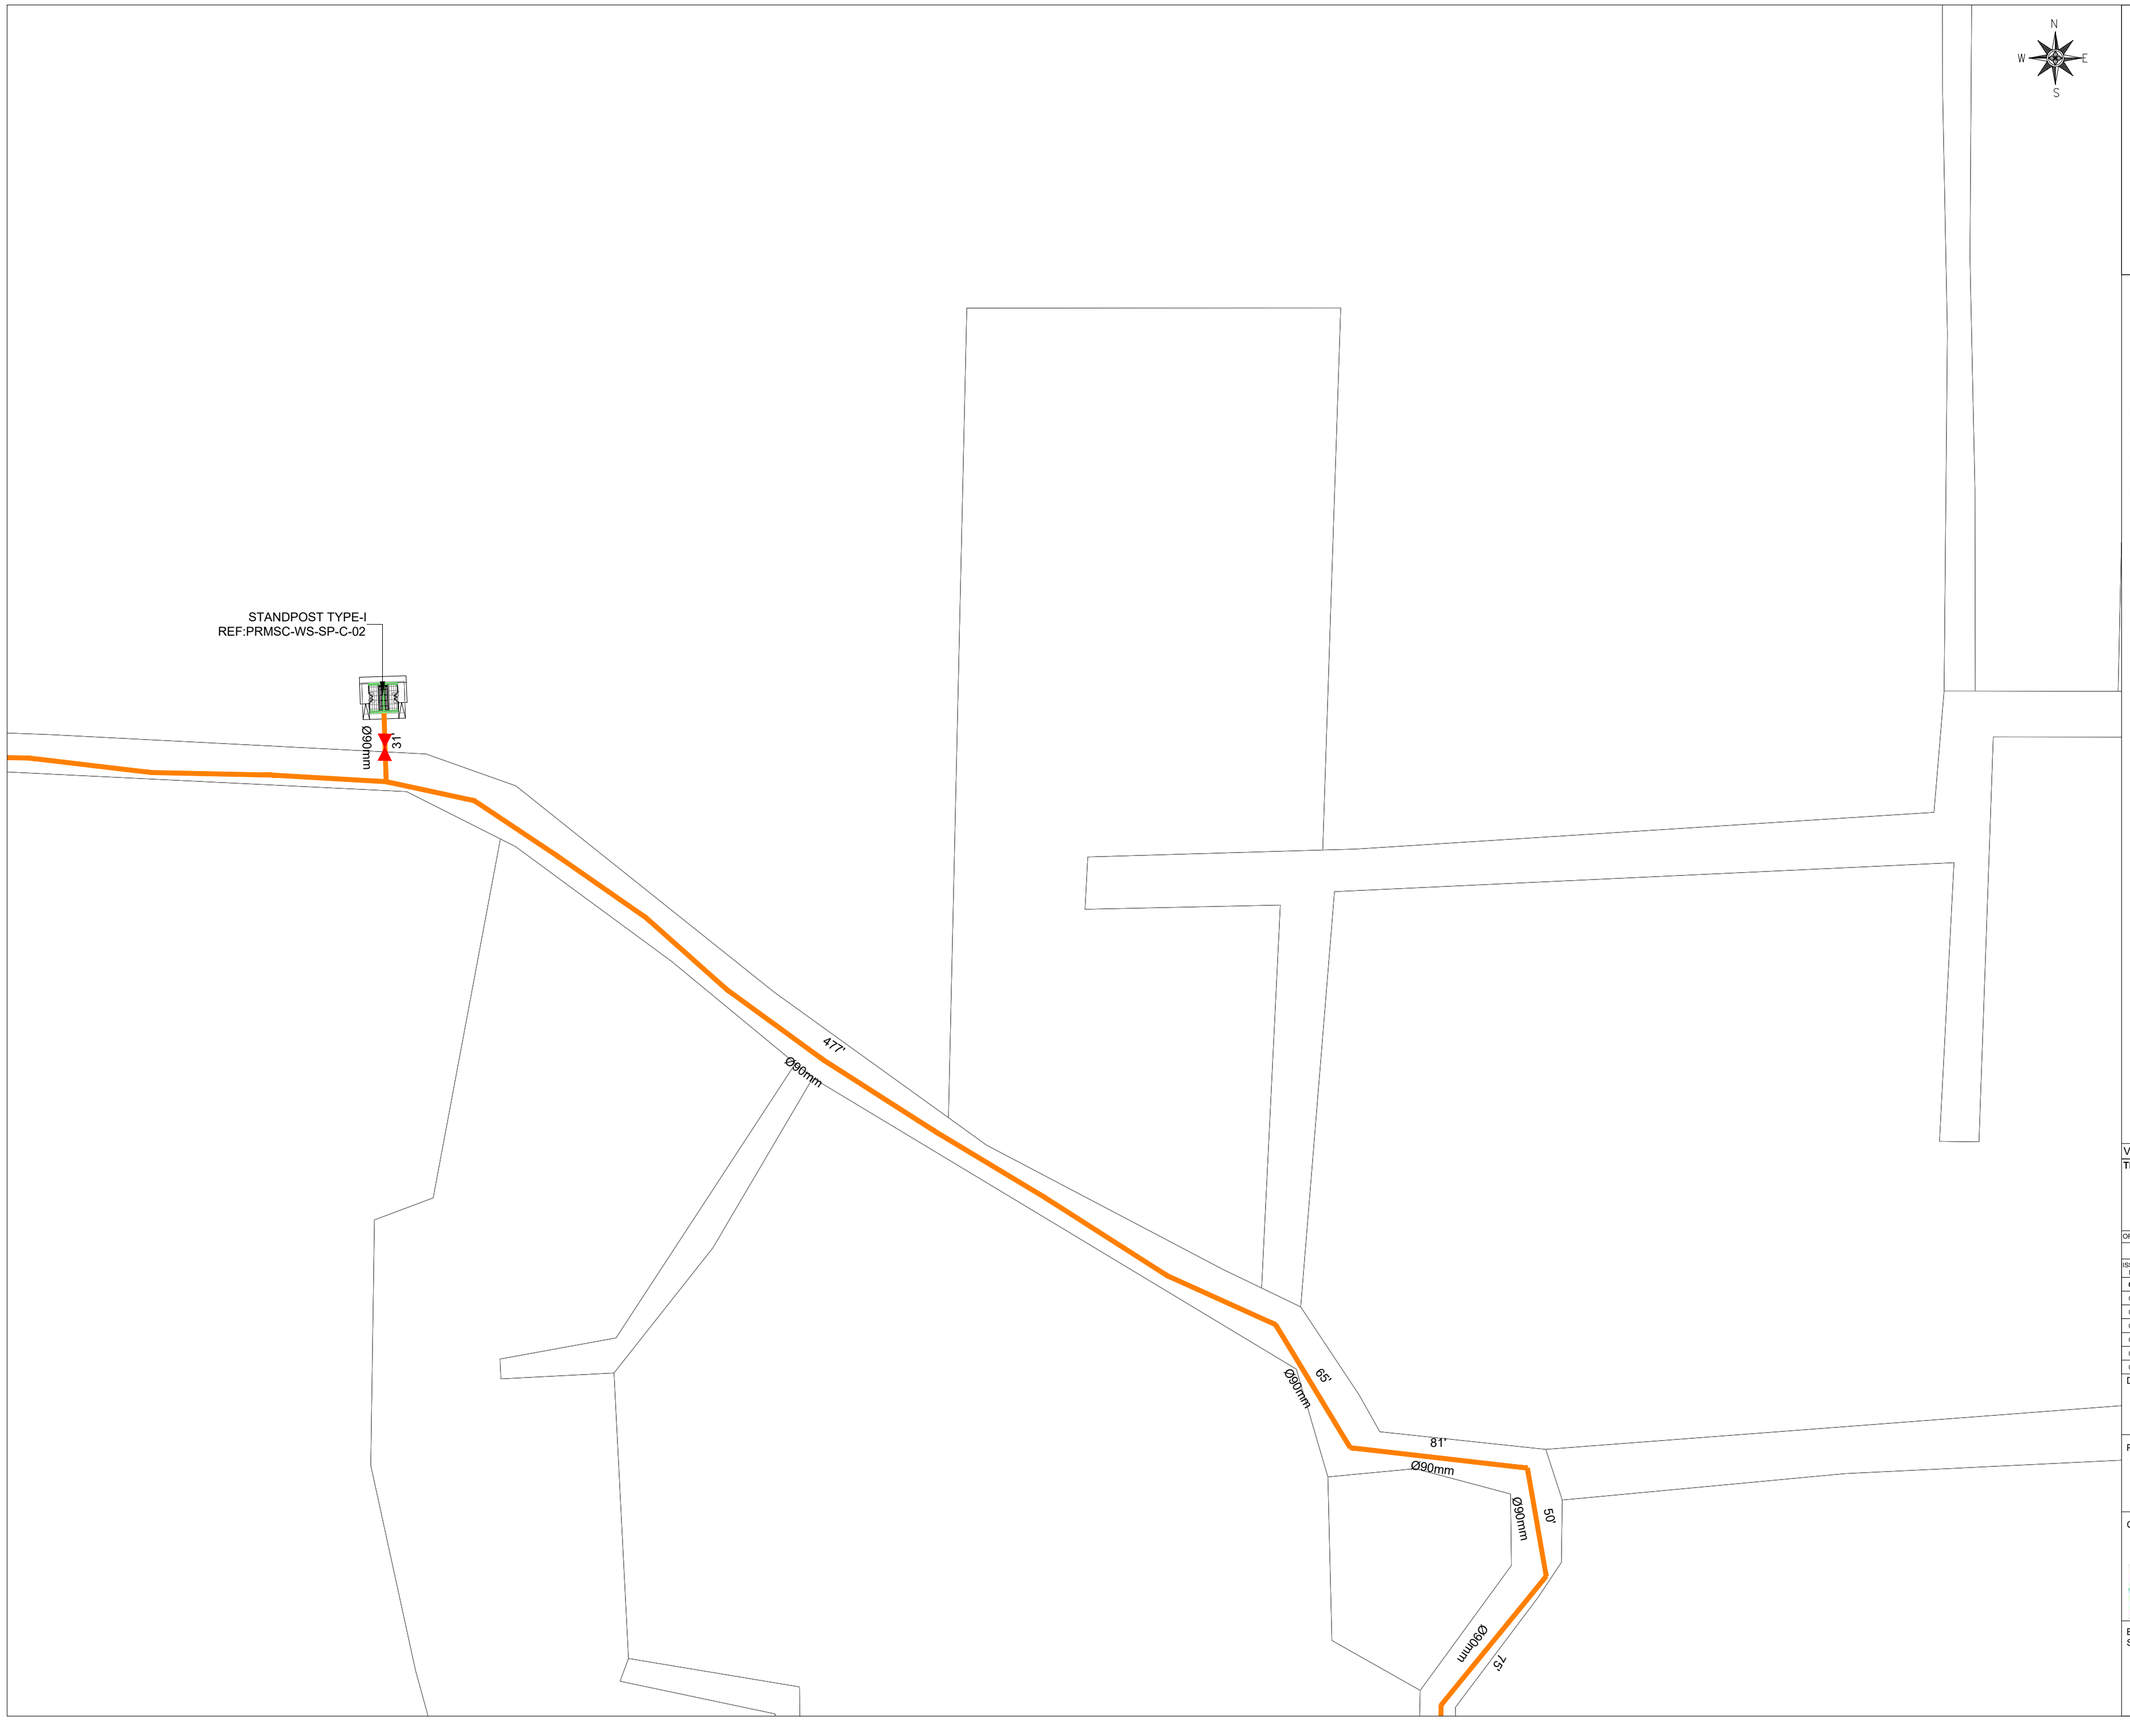

N
W
E
S

KEY PLAN

LEGEND:

- 90mm Ø HDPE PIPE
- SLUICE VALVE
- WASHOUT VALVE
- AIR RELEASE VALVE
- STAND POST TYPE - I
- DEAD END
- BOUNDARY

VILLAGE: JAGGA SANETTEKA (BWN)

TITLE.

WATER SUPPLY SYSTEM LAYOUT PLAN-03

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	16-12-2025	DETAILED DESIGN	ASAD	ENGR. FAIEZ	ENGR. HSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-JST-WS-LP-03	03 OF 15	00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:
ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

PRMSC-BWN-JST-WS-LP-03

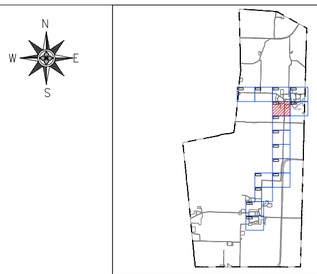

KEY PLAN

LEGEND:

90mm Ø HDPE PIPE

SLUICE VALVE

WASHOUT VALVE

AIR RELEASE VALVE

STAND POST TYPE - I

DEAD END

BOUNDARY

VILLAGE: JAGGA SANETTEKA (BWN)

TITLE.

WATER SUPPLY SYSTEM LAYOUT PLAN-05

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	16-12-2025	DETAILED DESIGN	ASAD	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-JST-WS-LP-05	05 OF 15	00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

PRMSC-BWN-JST-WS-LP-05

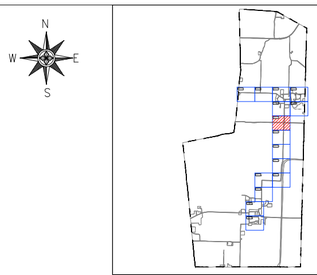

KEY PLAN

LEGEND:

90mm Ø HDPE PIPE

SLUICE VALVE

WASHOUT VALVE

AIR RELEASE VALVE

STAND POST TYPE - I

DEAD END

BOUNDARY

VILLAGE: JAGGA SANETTEKA (BWN)

TITLE.

WATER SUPPLY SYSTEM LAYOUT PLAN-07

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	16-12-2025	DETAILED DESIGN	ASAD	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº: PRMSC-BWN-JST-WS-LP-07

SHEET 07 OF 15

REV 00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:
ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

PRMSC-BWN-JST-WS-LP-07

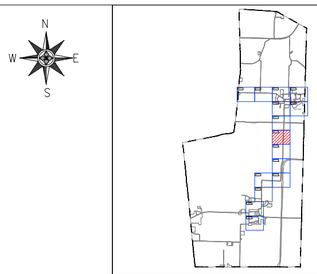

KEY PLAN

LEGEND:

90mm Ø HDPE PIPE

SLUICE VALVE

WASHOUT VALVE

AIR RELEASE VALVE

STAND POST TYPE - I

DEAD END

BOUNDARY

Ø90mm

3215'

VILLAGE: JAGGA SANETTEKA (BWN)

TITLE.

WATER SUPPLY SYSTEM LAYOUT PLAN-08

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	16-12-2025	DETAILED DESIGN	ASAD	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº: PRMSC-BWN-JST-WS-LP-08

SHEET 08 OF 15

REV 00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

PRMSC-BWN-JST-WS-LP-08

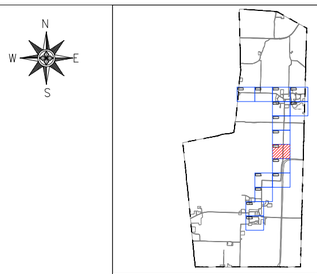

KEY PLAN

LEGEND:

90mm Ø HDPE PIPE

SLUICE VALVE

WASHOUT VALVE

AIR RELEASE VALVE

STAND POST TYPE - I

DEAD END

BOUNDARY

VILLAGE: JAGGA SANETTEKA (BWN)

TITLE.

WATER SUPPLY SYSTEM LAYOUT PLAN-09

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	16-12-2025	DETAILED DESIGN	ASAD	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-JST-WS-LP-09	09 OF 15	00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS
www.asianen.com.pk

PRMSC-BWN-JST-WS-LP-09

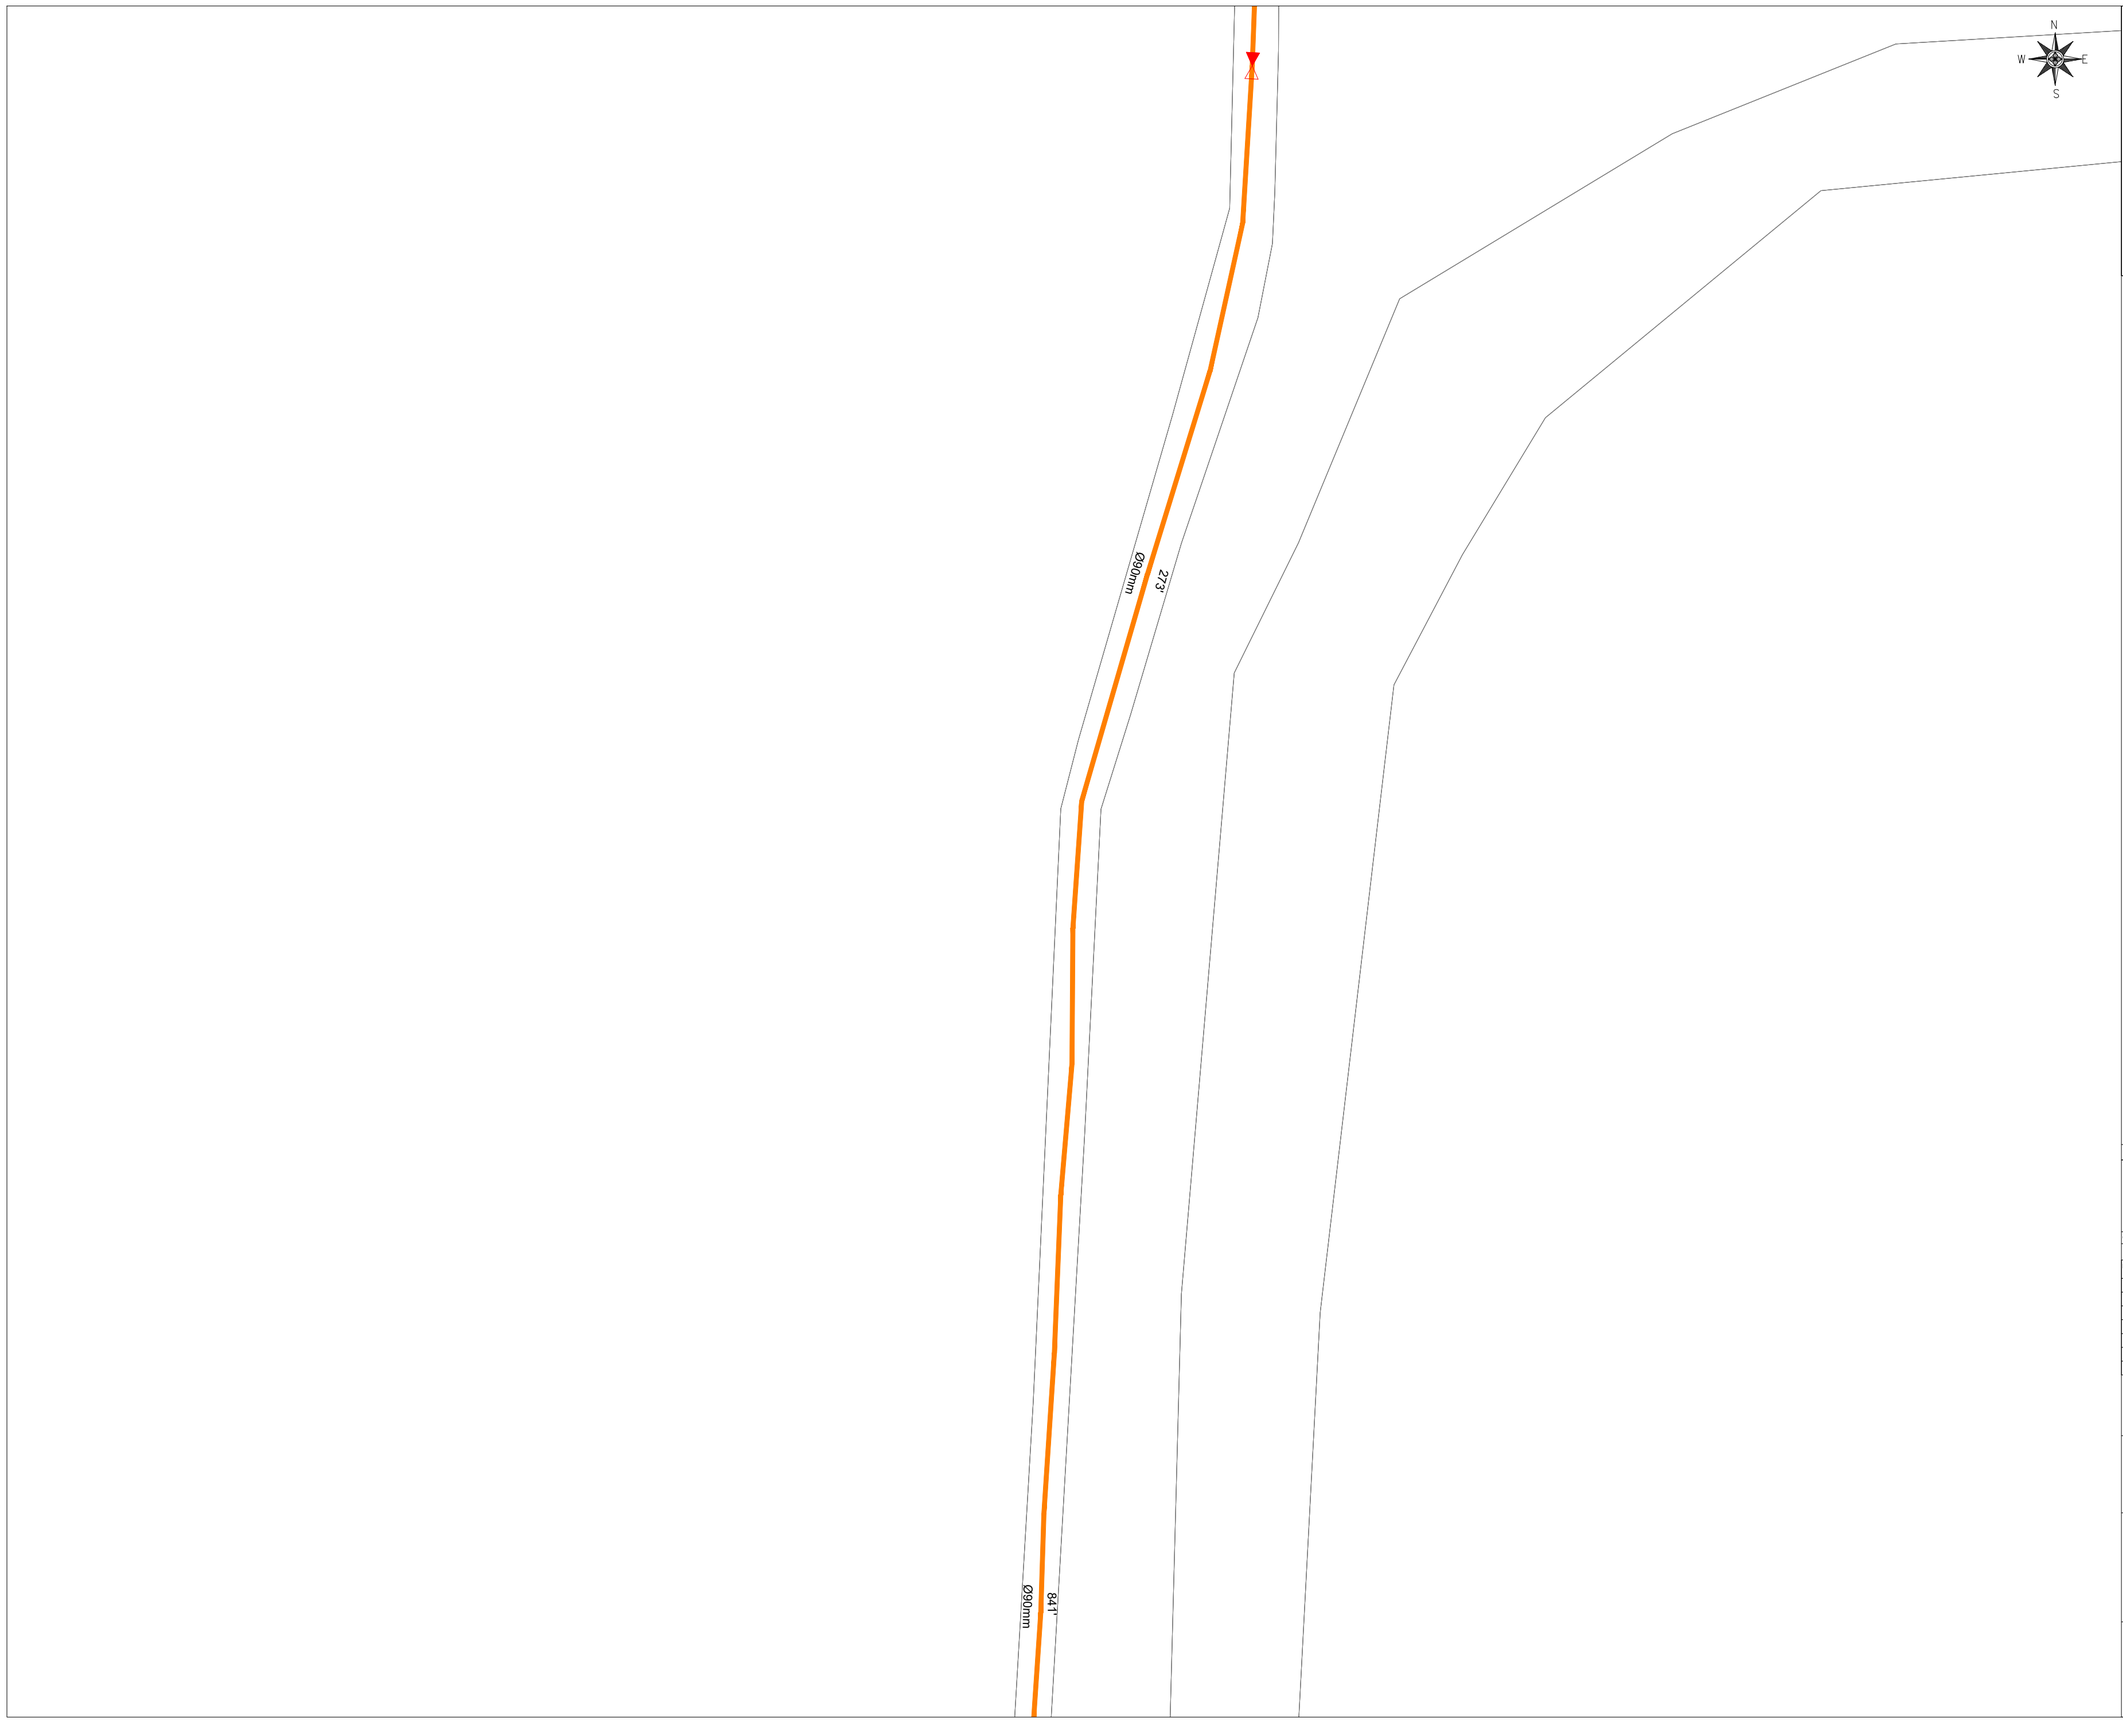

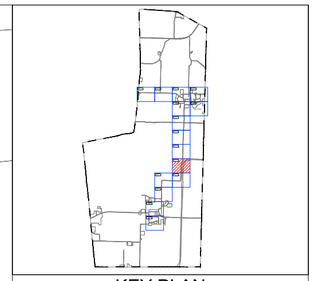

KEY PLAN

LEGEND:

- 90mm Ø HDPE PIPE
- SLUICE VALVE
- WASHOUT VALVE
- AIR RELEASE VALVE
- STAND POST TYPE - I
- DEAD END
- BOUNDARY

VILLAGE: JAGGA SANETTEKA (BWN)

TITLE.

WATER SUPPLY SYSTEM LAYOUT PLAN-10

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	16-12-2025	DETAILED DESIGN	ASAD	ENGR FAIEZ	ENGR IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº: PRMSC-BWN-JST-WS-LP-10

SHEET 10 OF 15

REV 00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

PRMSC-BWN-JST-WS-LP-10

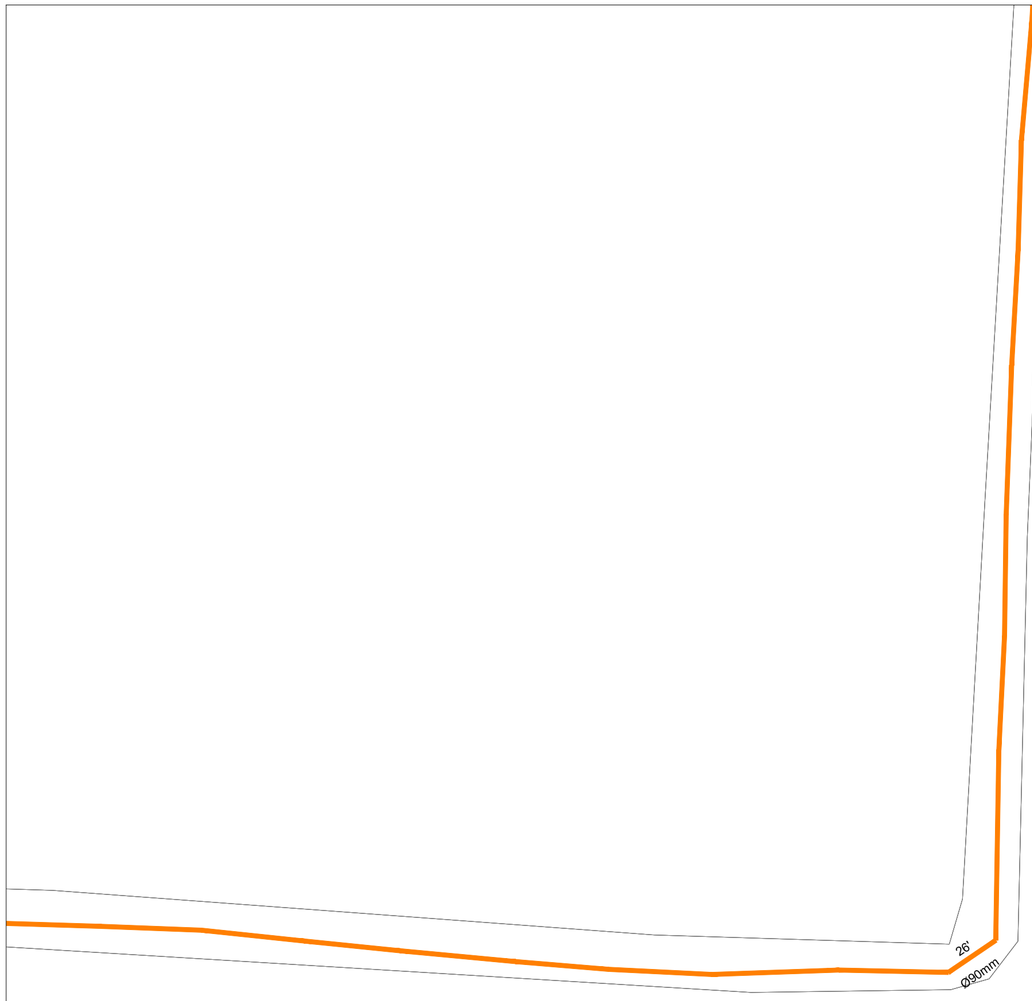



KEY PLAN

LEGEND:

- 90mm Ø HDPE PIPE
- SLUICE VALVE
- WASHOUT VALVE
- AIR RELEASE VALVE
- STAND POST TYPE - I
- DEAD END
- BOUNDARY

VILLAGE: JAGGA SANETTEKA (BWN)

TITLE:

WATER SUPPLY SYSTEM LAYOUT PLAN-11

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	16-12-2025	DETAILED DESIGN	ASAD	ENGR. FAIEZ	ENGR. HSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-JST-WS-LP-11	11 OF 15	00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:
ASIAN CONSULTING ENGINEERS
www.asianen.com.pk

PRMSC-BWN-JST-WS-LP-11

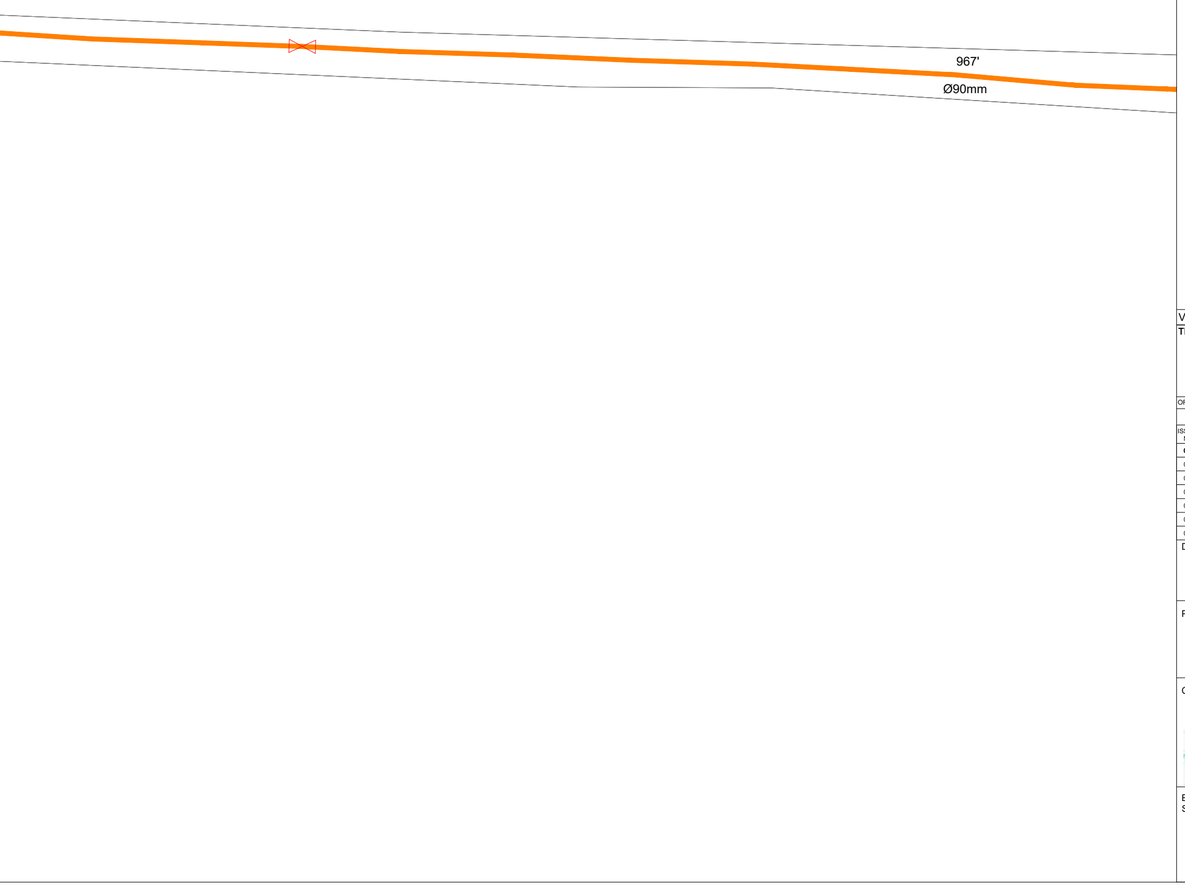

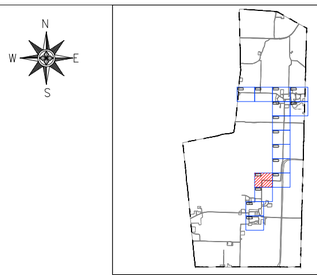

KEY PLAN

LEGEND:

90mm Ø HDPE PIPE	
SLUICE VALVE	
WASHOUT VALVE	
AIR RELEASE VALVE	
STAND POST TYPE - I	
DEAD END	
BOUNDARY	

VILLAGE: JAGGA SANETTEKA (BWN)

TITLE.

WATER SUPPLY SYSTEM LAYOUT PLAN-12

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	16-12-2025	DETAILED DESIGN	ASAD	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº: PRMSC-BWN-JST-WS-LP-12

SHEET 12 OF 15

REV 00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

PRMSC-BWN-JST-WS-LP-12



KEY PLAN

LEGEND:

- 90mm Ø HDPE PIPE
- SLUICE VALVE
- WASHOUT VALVE
- AIR RELEASE VALVE
- STAND POST TYPE - I
- DEAD END
- BOUNDARY

VILLAGE: JAGGA SANETTEKA (BWN)

TITLE.

WATER SUPPLY SYSTEM LAYOUT PLAN-13

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	16-12-2025	DETAILED DESIGN	ASAD	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-JST-WS-LP-13	13 OF 15	00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

PRMSC-BWN-JST-WS-LP-13

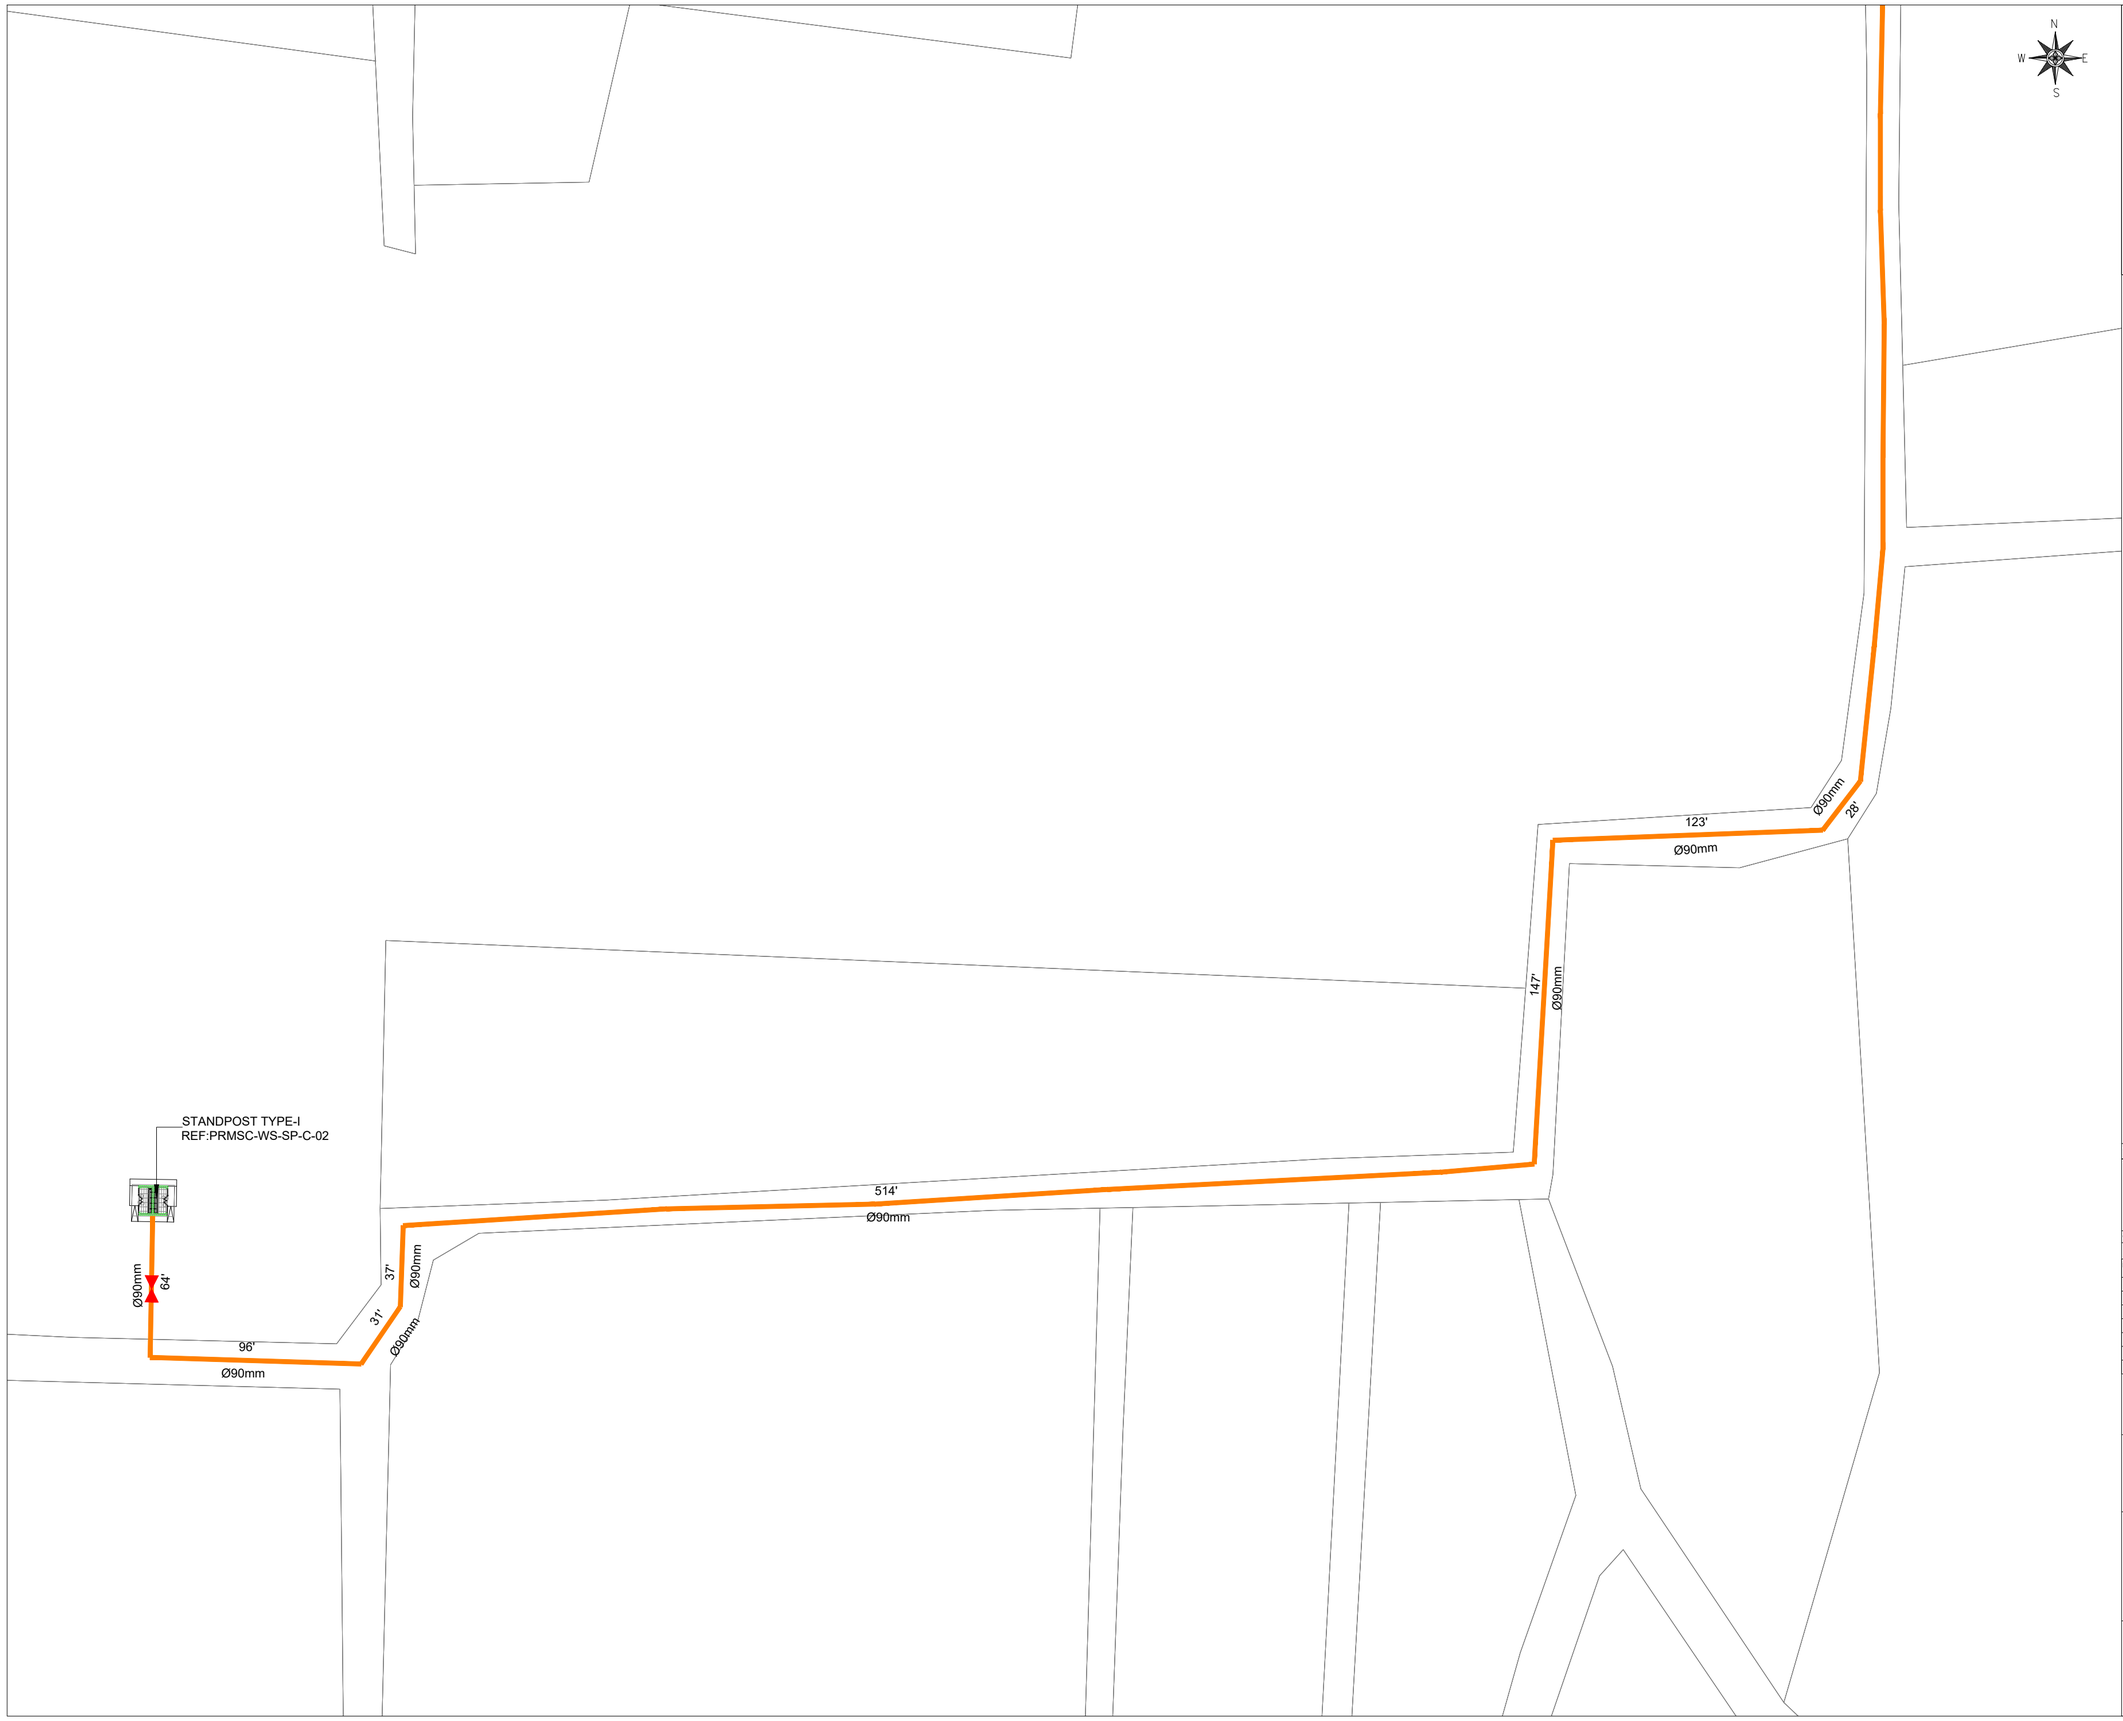



KEY PLAN

LEGEND:

- 90mm Ø HDPE PIPE
- SLUICE VALVE
- WASHOUT VALVE
- AIR RELEASE VALVE
- STAND POST TYPE - I
- DEAD END
- BOUNDARY

VILLAGE: JAGGA SANETTEKA (BWN)

TITLE:

WATER SUPPLY SYSTEM LAYOUT PLAN-14

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	16-12-2025	DETAILED DESIGN	ASAD	ENGR FAIEZ	ENGR HSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº: PRMSC-BWN-JST-WS-LP-14

SHEET 14 OF 15

REV 00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:
ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

PRMSC-BWN-JST-WS-LP-14

JALWALA

KEY PLAN

Revenue Village: Jalwala Jalwala Sheet-2

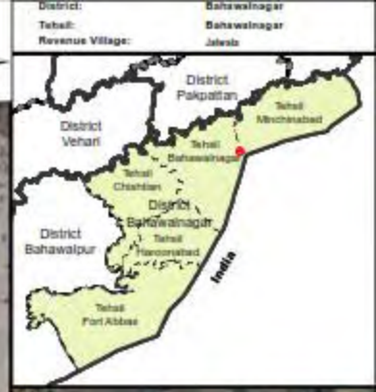

Title:
Proposed Water Supply Plan

Legend:

- SETTLEMENT
- STAND POST
- SETTELMENT BOUNDARY

Scale: 1:1,400
1 inch = 117 feet
Paper Size: A3

0 40 80 160
Kilometers

Project:
Engineering Design & Construction Supervision, Punjab Rural Sustainable Water Supply & Sanitation Project, Cluster South-III

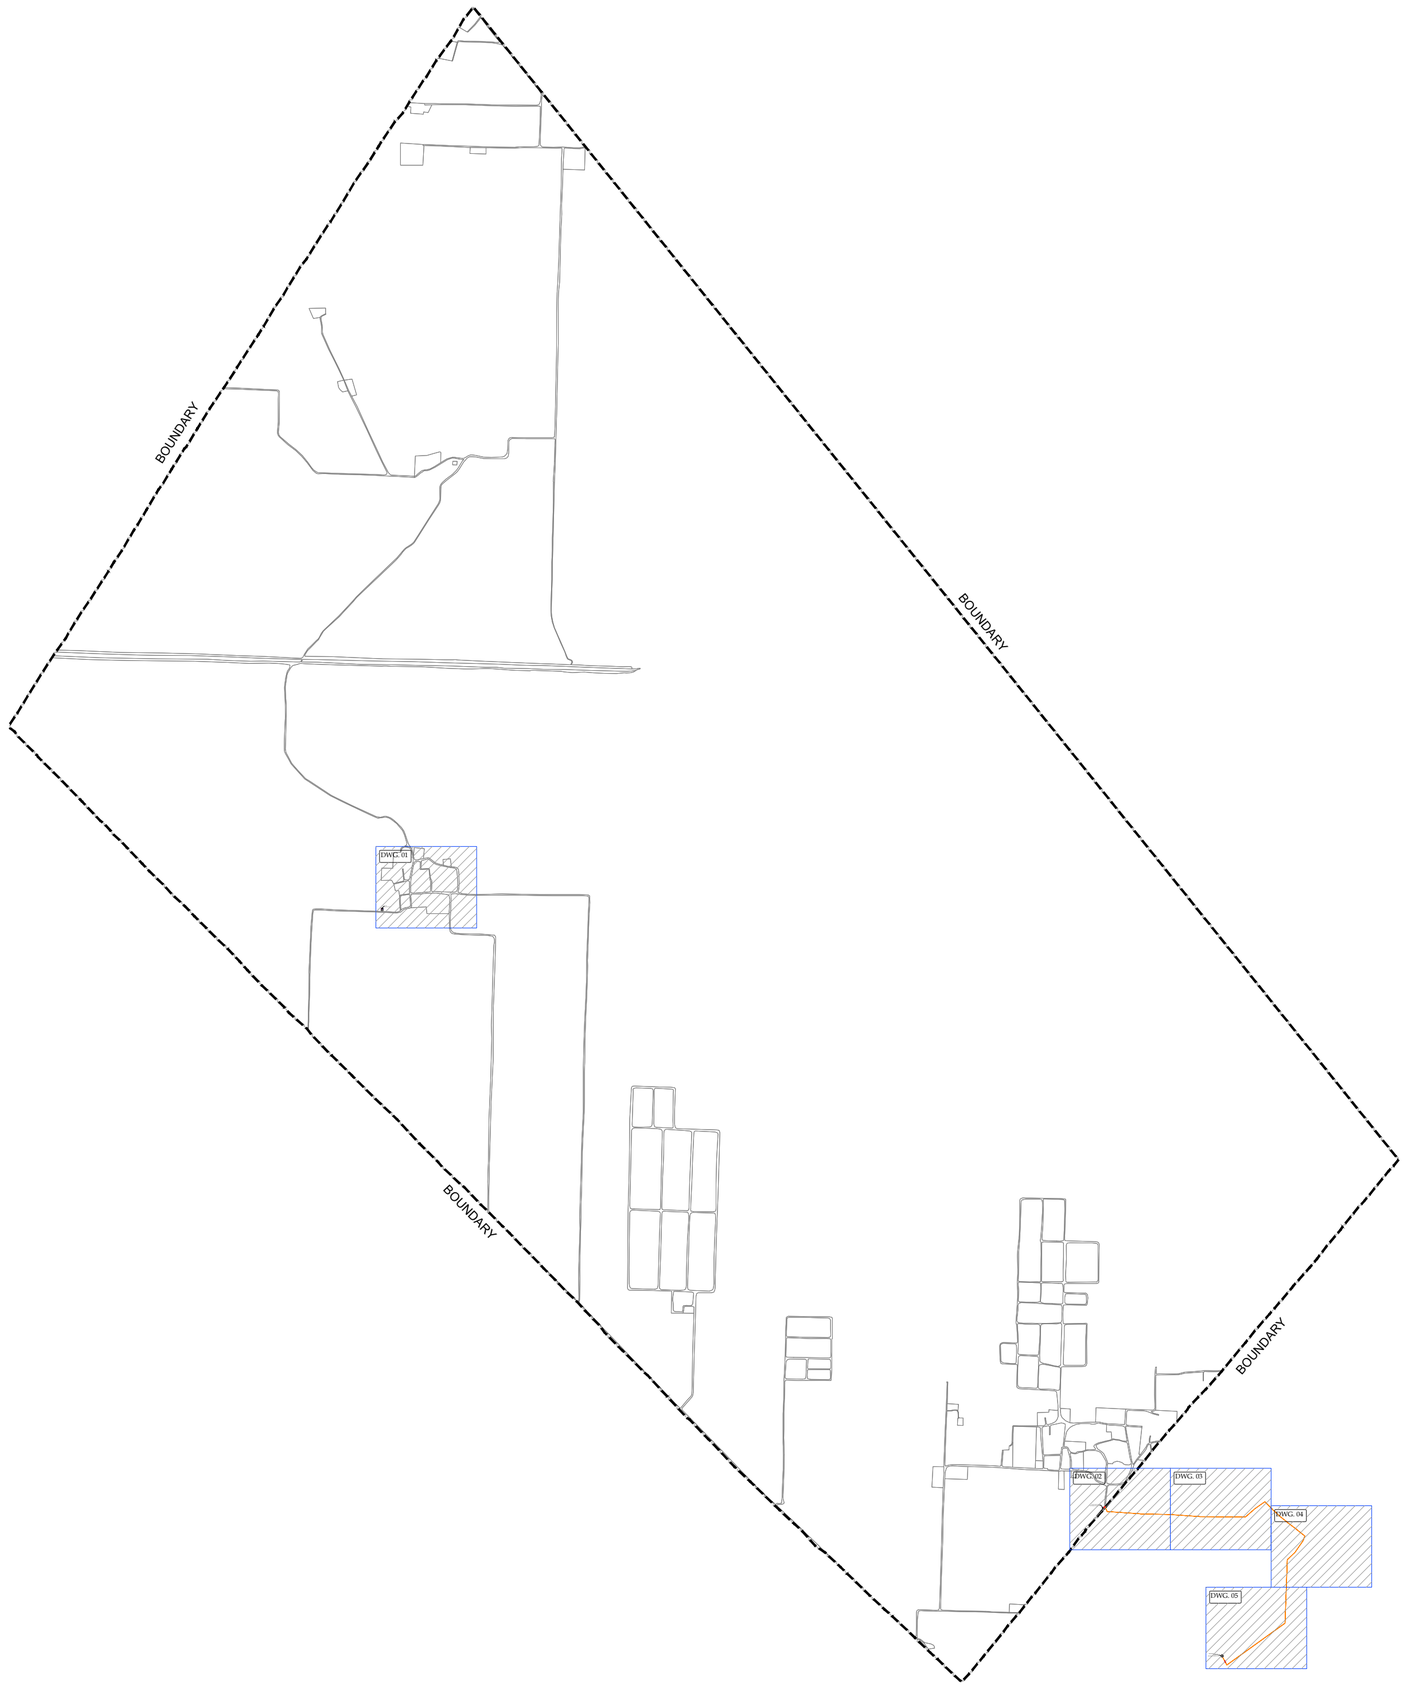

LEGEND:

- 90mm Ø HDPE PIPE
- SLUICE VALVE
- AIR RELEAS VALVE
- WASHOUT VALVE
- PROPOSED STAND POST TYPE-I
- PROPOSED TUBE WELL
- PROPOSED RO PLANT
- BOUNDARY

VILLAGE: JAALWALA (BWN)

TITLE.

WATER SUPPLY SYSTEM KEY PLAN

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 1050'

ISSUE N°	DATE	D E S C R I P T I O N	DRAWN	DESIGNED	APPROVED
01	02-01-2026	DETAILED DESIGN	HANNAN	ENGR. FAIEZ	ENGR. HSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº: PRMSC-BWN-JAW-WS-KP-00

SHEET 00 OF 00

REV 00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT
ASIAN CONSULTING ENGINEERS
www.asianeed.com.pk

PRMSC-BWN-JAW-WS-KP-00

LAYOUT PLANS

Revenue Village: Jalwala Jalwala Sheet-2

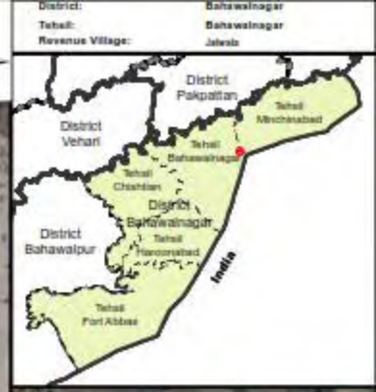

Title:
Proposed Water Supply Plan

Legend:

- SETTLEMENT
- STAND POST
- SETTELMENT BOUNDARY

Scale: 1:1,400
1 inch = 117 feet
Paper Size: A3

0 40 80 160
Kilometers

Project:
Engineering Design & Construction Supervision, Punjab Rural Sustainable Water Supply & Sanitation Project, Cluster South-III

N
W E
S

RO PLANT
REF:PRMSC-WS-SP-C-01



KEY PLAN

LEGEND:

90mm Ø HDPE PIPE	
SLUICE VALVE	
AIR RELEAS VALVE	
WASHOUT VALVE	
PROPOSED STAND POST TYPE-I	
PROPOSED TUBE WELL	
PROPOSED RO PLANT	
BOUNDARY	

VILLAGE: JAALWALA (BWN)

TITLE.

WATER SUPPLY SYSTEM LAYOUT PLAN-01

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	02-12-2025	DETAILED DESIGN	HANNAN	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº: PRMSC-BWN-JAW-WS-LP-01

SHEET 01 OF 05

REV 00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:
ASIAN CONSULTING ENGINEERS
www.asiancon.com

PRMSC-BWN-JAW-WS-LP-01

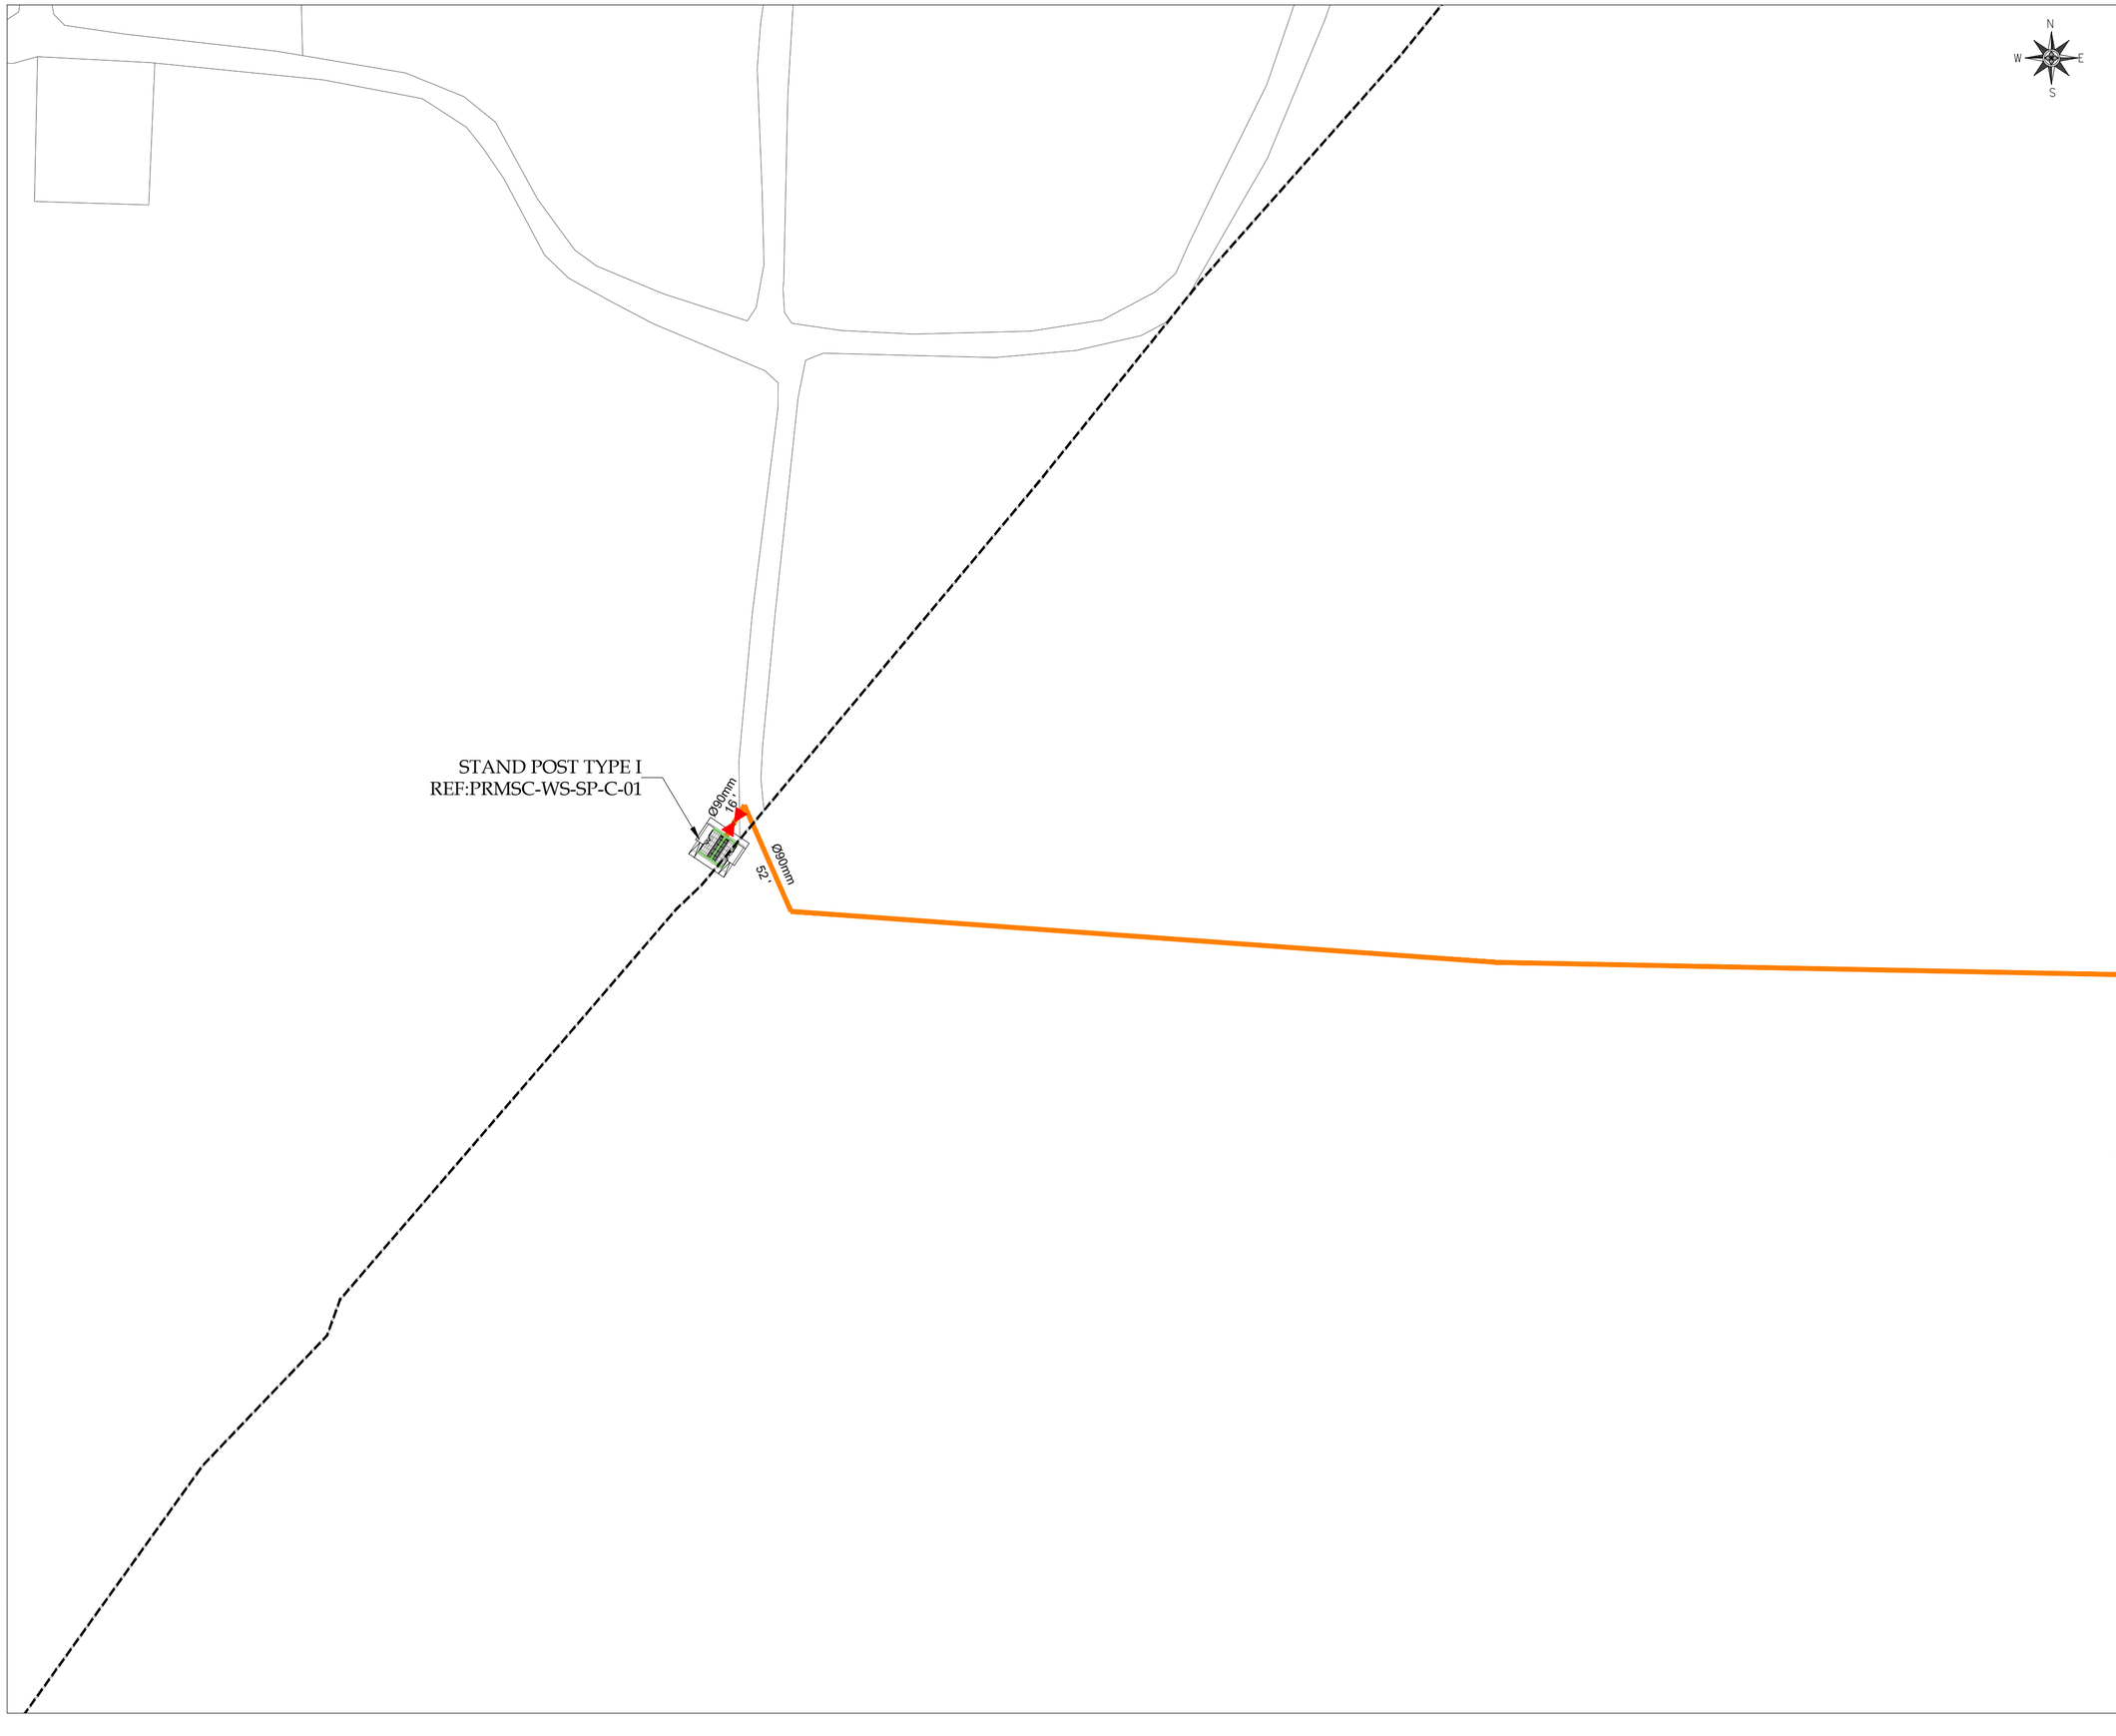



KEY PLAN

LEGEND:

- 90mm Ø HDPE PIPE
- SLUICE VALVE
- AIR RELEAS VALVE
- WASHOUT VALVE
- PROPOSED STAND POST TYPE-I
- PROPOSED TUBE WELL
- PROPOSED RO PLANT
- BOUNDARY

VILLAGE: JAALWALA (BWN)

TITLE.

WATER SUPPLY SYSTEM LAYOUT PLAN-02

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	02-12-2025	DETAILED DESIGN	HANNAN	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-JAW-WS-LP-02	02 OF 05	00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

PRMSC-BWN-JAW-WS-LP-02

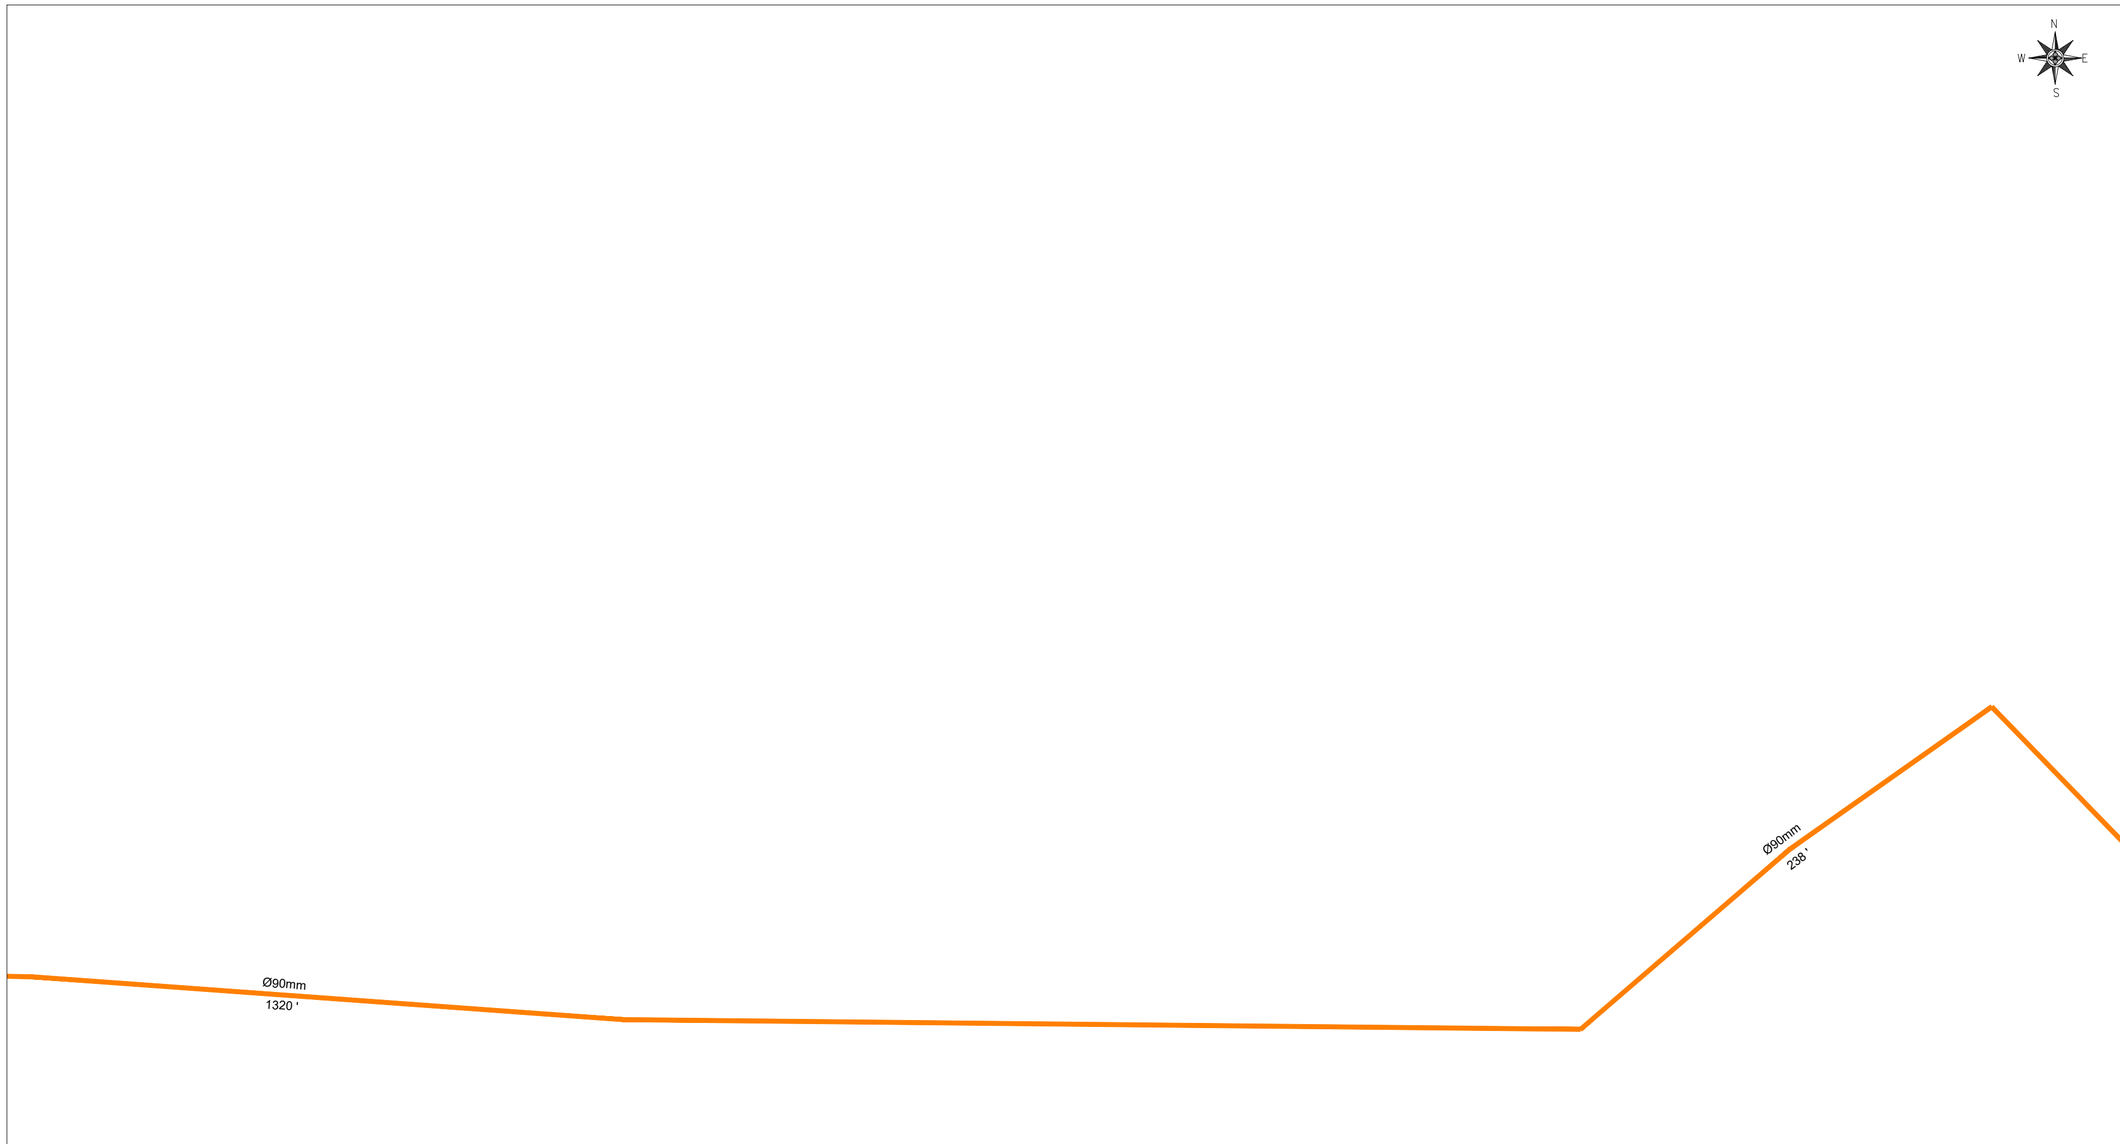

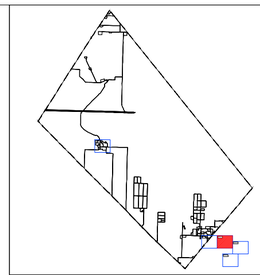

KEY PLAN

LEGEND:

90mm Ø HDPE PIPE

SLUICE VALVE

AIR RELEAS VALVE

WASHOUT VALVE

PROPOSED STAND POST TYPE-I

PROPOSED TUBE WELL

PROPOSED RO PLANT

BOUNDARY

VILLAGE: JAALWALA (BWN)

TITLE.

WATER SUPPLY SYSTEM LAYOUT PLAN-03

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	02-12-2025	DETAILED DESIGN	HANNAN	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº: PRMSC-BWN-JAW-WS-LP-03

SHEET 03 OF 05

REV 00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:
ASIAN CONSULTING ENGINEERS
www.asiacon.com.pk

PRMSC-BWN-JAW-WS-LP-03

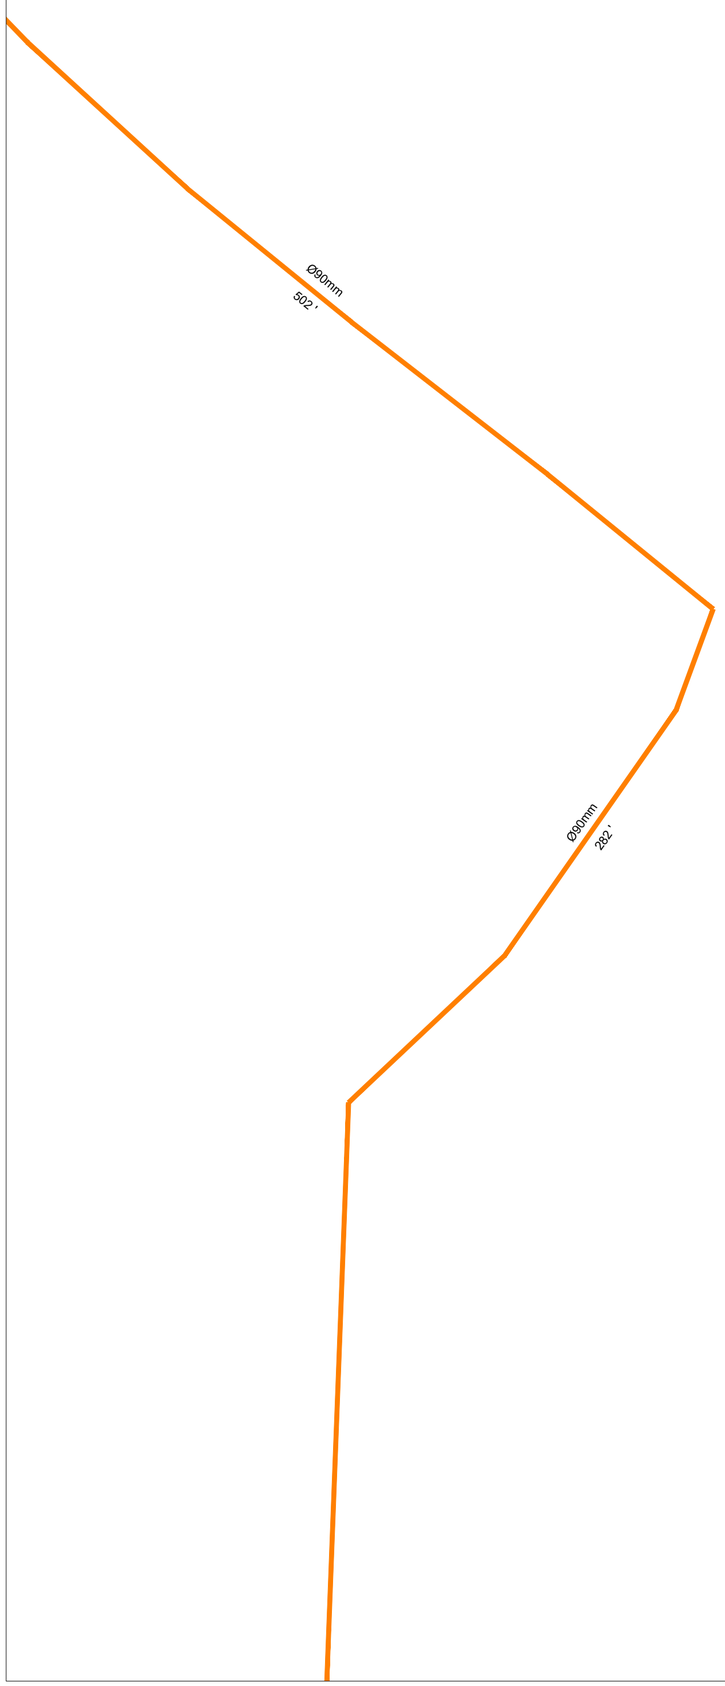

PRMSC-BWN-JAW-WS-LP-04

N
W
E
S



KEY PLAN

LEGEND:

- 90mm Ø HDPE PIPE
- SLUICE VALVE
- AIR RELEAS VALVE
- WASHOUT VALVE
- PROPOSED STAND POST TYPE-I
- PROPOSED TUBE WELL
- PROPOSED RO PLANT
- BOUNDARY

VILLAGE: JAALWALA (BWN)

TITLE.

WATER SUPPLY SYSTEM LAYOUT PLAN-04

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	02-12-2025	DETAILED DESIGN	HANNAN	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-JAW-WS-LP-04	04 OF 05	00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS
www.asiancon.com

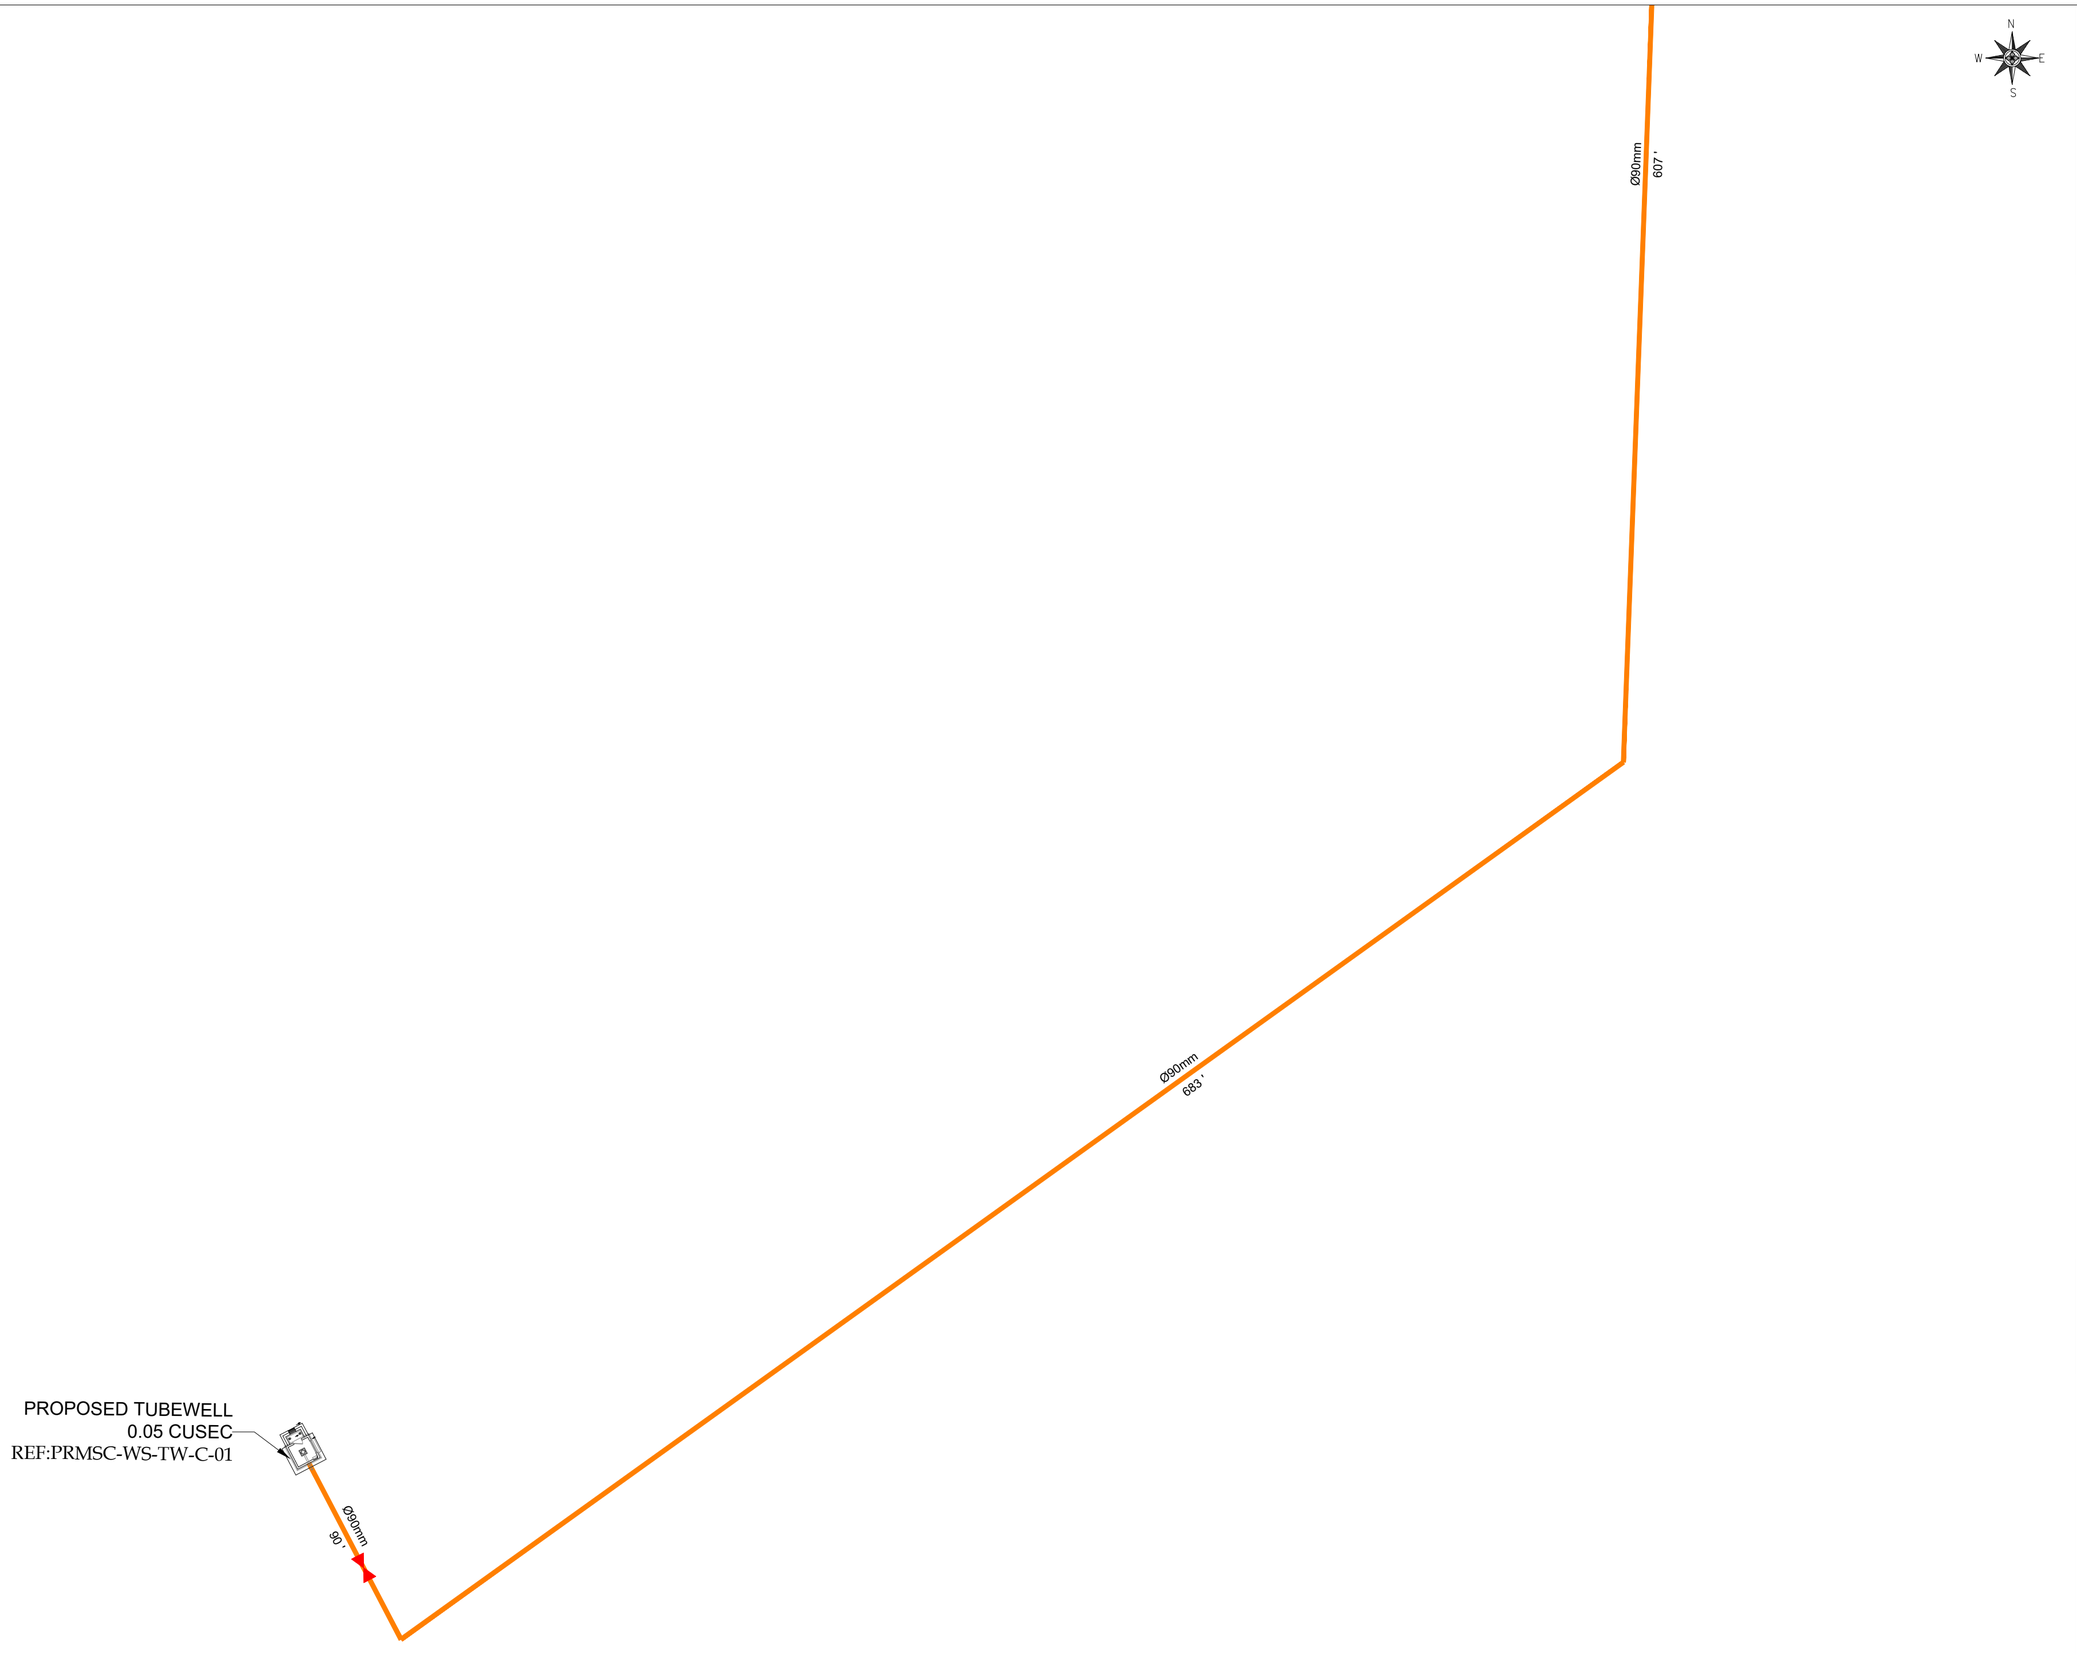

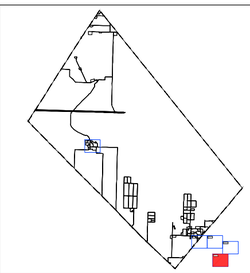

KEY PLAN

LEGEND:

- 90mm Ø HDPE PIPE
- SLUICE VALVE
- AIR RELEAS VALVE
- WASHOUT VALVE
- PROPOSED STAND POST TYPE-I
- PROPOSED TUBE WELL
- PROPOSED RO PLANT
- BOUNDARY

VILLAGE: JAALWALA (BWN)

TITLE.

WATER SUPPLY SYSTEM LAYOUT PLAN-05

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	02-12-2025	DETAILED DESIGN	HANNAN	ENGR FAIEZ	ENGR IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-JAW-WS-LP-05	05 OF 05	00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:
ASIAN CONSULTING ENGINEERS
www.asiaecon.com.pv

PRMSC-BWN-JAW-WS-LP-05

JANOOWALA

KEY PLAN



Title:
Proposed Water Supply Plan

Legend:

- SETTLEMENT
- STAND POST
- SETTELMENT BOUNDARY

Scale: 1:3,200
1 inch = 267 feet
Paper Size: A3

0 40 80 160
Kilometers

Project:
Engineering Design & Construction Supervision, Punjab Rural Sustainable Water Supply & Sanitation Project, Cluster South-III

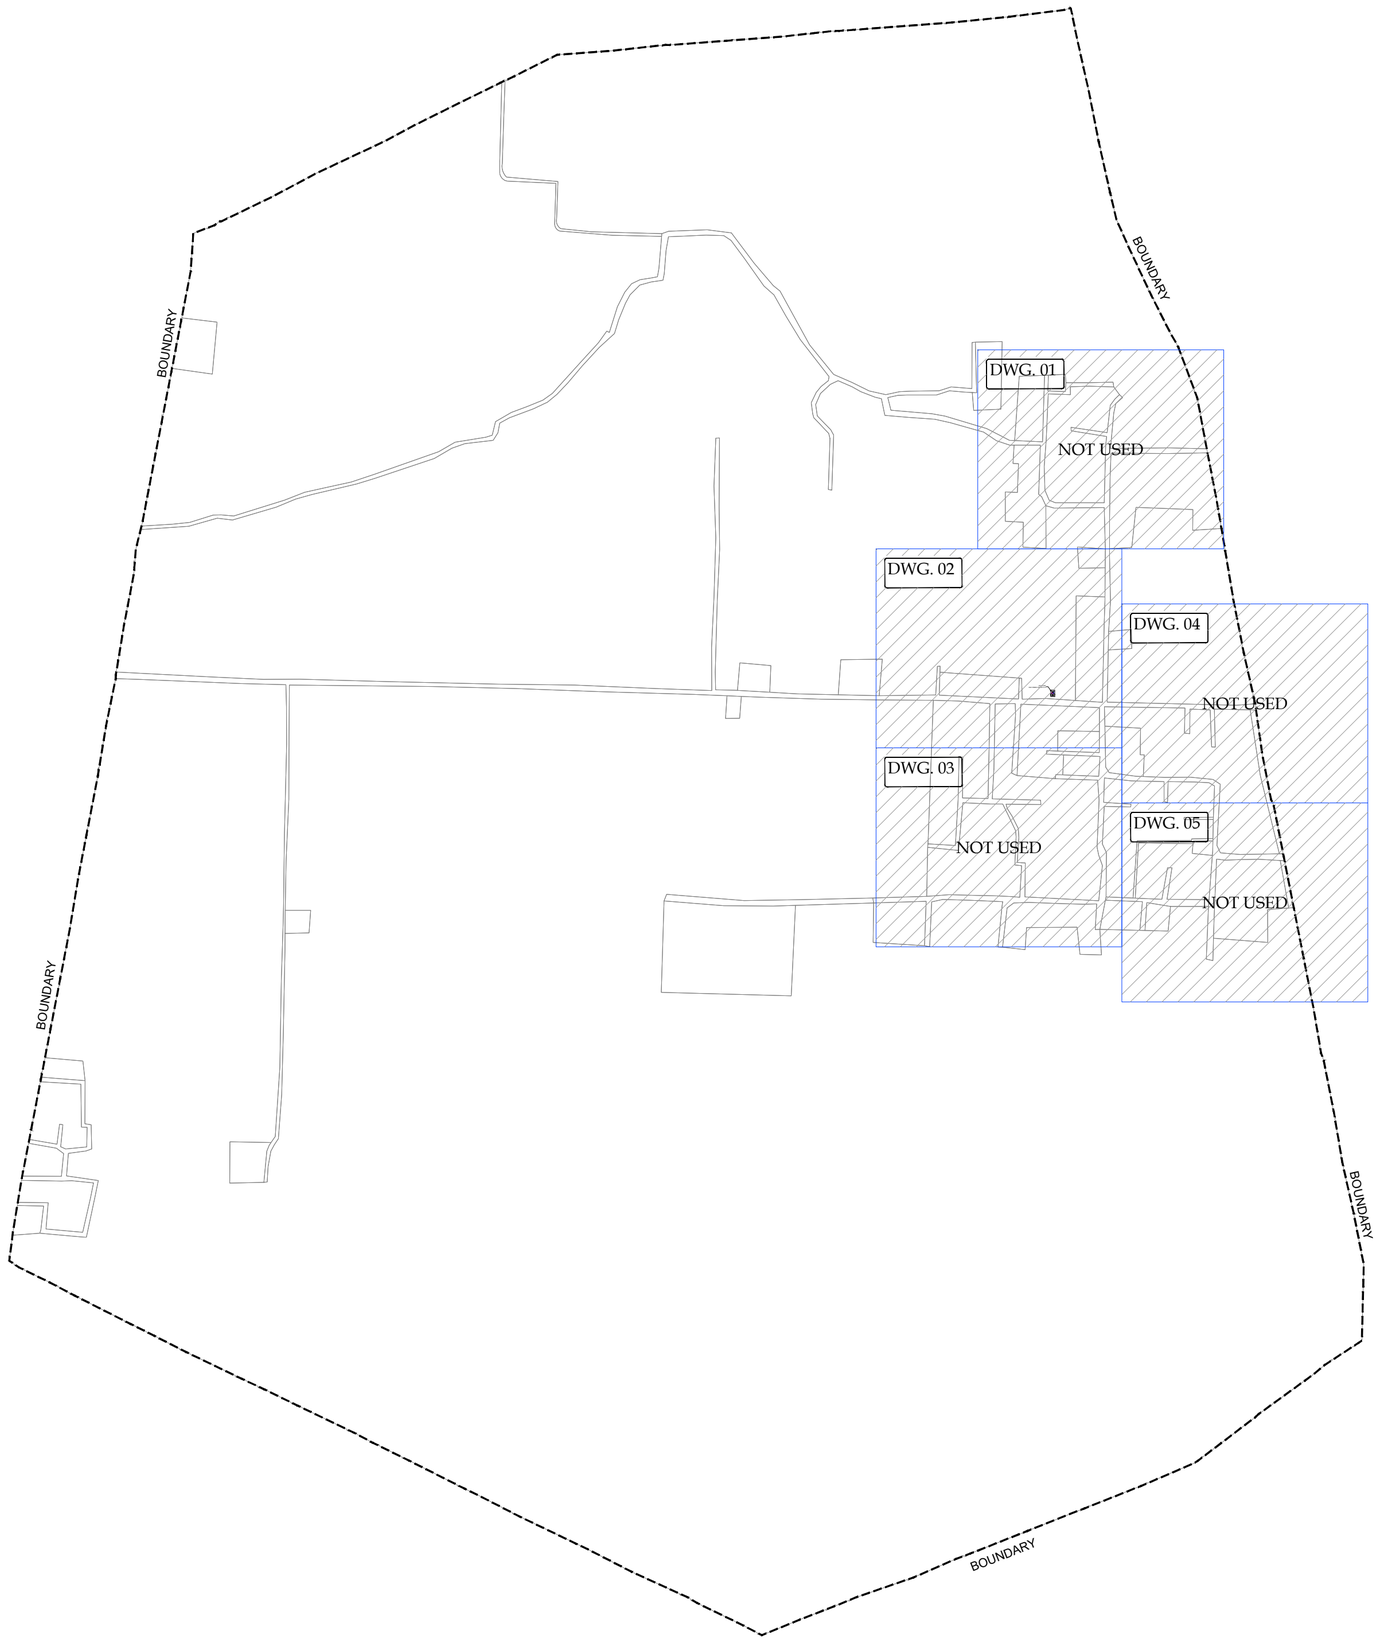

LEGEND:

PROPOSED RO PLANT

BOUNDARY

VILLAGE: JANOOWALA (BWN)

TITLE.

WATER SUPPLY SYSTEM KEY PLAN

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 430'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	02-01-2026	DETAILED DESIGN	HANNAN	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-JNW-WS-KP-00	00 OF 00	00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT
ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

PRMSC-BWN-JNW-WS-KP-00

LAYOUT PLANS

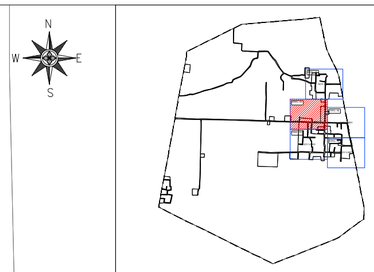

KEY PLAN

LEGEND:

PROPOSED RO PLANT

BOUNDARY

VILLAGE: KARTAR SINGH (BWN)

TITLE.

WATER SUPPLY SYSTEM LAYOUT PLAN-02

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	02-12-2025	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº: PRMSC-BWN-KTS-WS-LP-02

SHEET 02 OF 05

REV 00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

PRMSC-BWN-KTS-WS-LP-02

KHAWAJA BUX BODLA

KEY PLAN

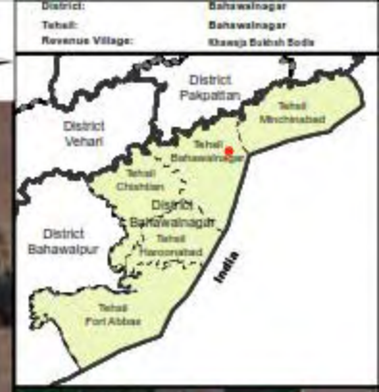

Title:
Proposed Water Supply Plan

Legend:

- SETTLEMENT
- STAND POST
- SETTELMENT BOUNDARY

Scale: 1:1,200
1 inch = 100 feet
Paper Size: A3

0 40 80 160
Kilometers

Project:
Engineering Design & Construction Supervision, Punjab Rural Sustainable Water Supply & Sanitation Project, Cluster South-III

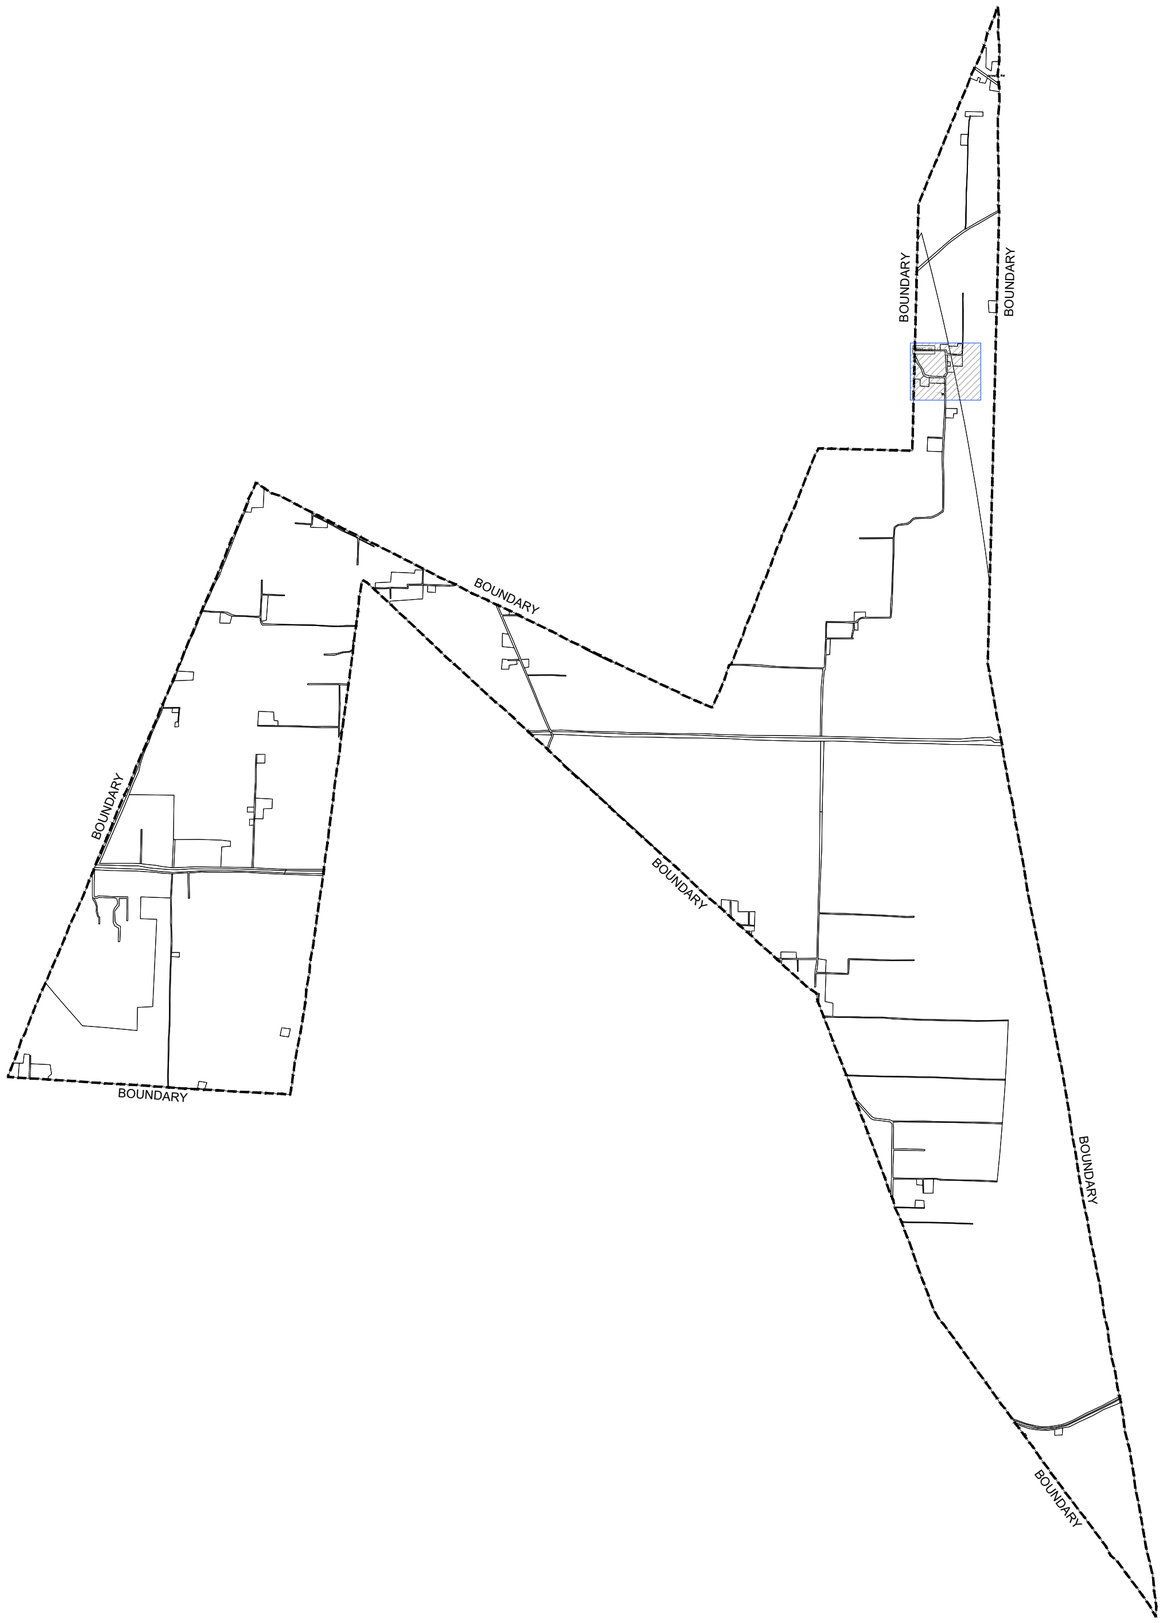

LEGEND:

RO PLANT

BOUNDARY

VILLAGE: KHAWAJA BAKHSH BODLA (BWN)

TITLE.

WATER SUPPLY SYSTEM KEY PLAN

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 1500'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	02-01-2026	DETAILED DESIGN	M.ASIF	ENGR. FAIEZ	ENGR. IHSAN UL HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº: PRMSC-BWN-KBB-WS-KP-00

SHEET 00 OF 00

REV 00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT

ASIAN CONSULTING ENGINEERS www.asiancon.com

PRMSC-BWN-KBB-WS-KP-00

LAYOUT PLANS

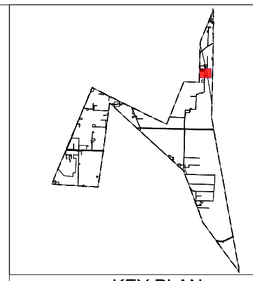

KEY PLAN

LEGEND:

RO PLANT

BOUNDARY

VILLAGE: KHAWAJA BAKHSH BODLA (BWN)

TITLE.

WATAR SUPPLY SYSTEM LAYOUT PLAN-01

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	D E S C R I P T I O N	DRAWN	DESIGNED	APPROVED
01	02-01-2026	DETAILED DESIGN	M ASIF	ENGR FAIEZ	ENGR IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-KBB-WS-LP-01	01 OF 01	00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS
www.asiancen.com

PRMSC-BWN-KBB-WS-LP-01

MALAK PURA

KEY PLAN

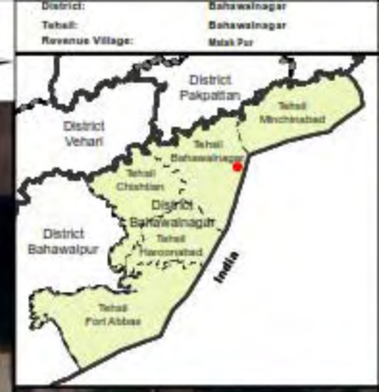

Title:
Proposed Water Supply Plan

Legend:

- SETTLEMENT
- STAND POST
- SETTELMENT BOUNDARY

Scale: 1:2,300
1 inch = 192 feet
Paper Size: A3

0 40 80 160
Kilometers

Project:
Engineering Design & Construction Supervision, Punjab Rural Sustainable Water Supply & Sanitation Project, Cluster South-III

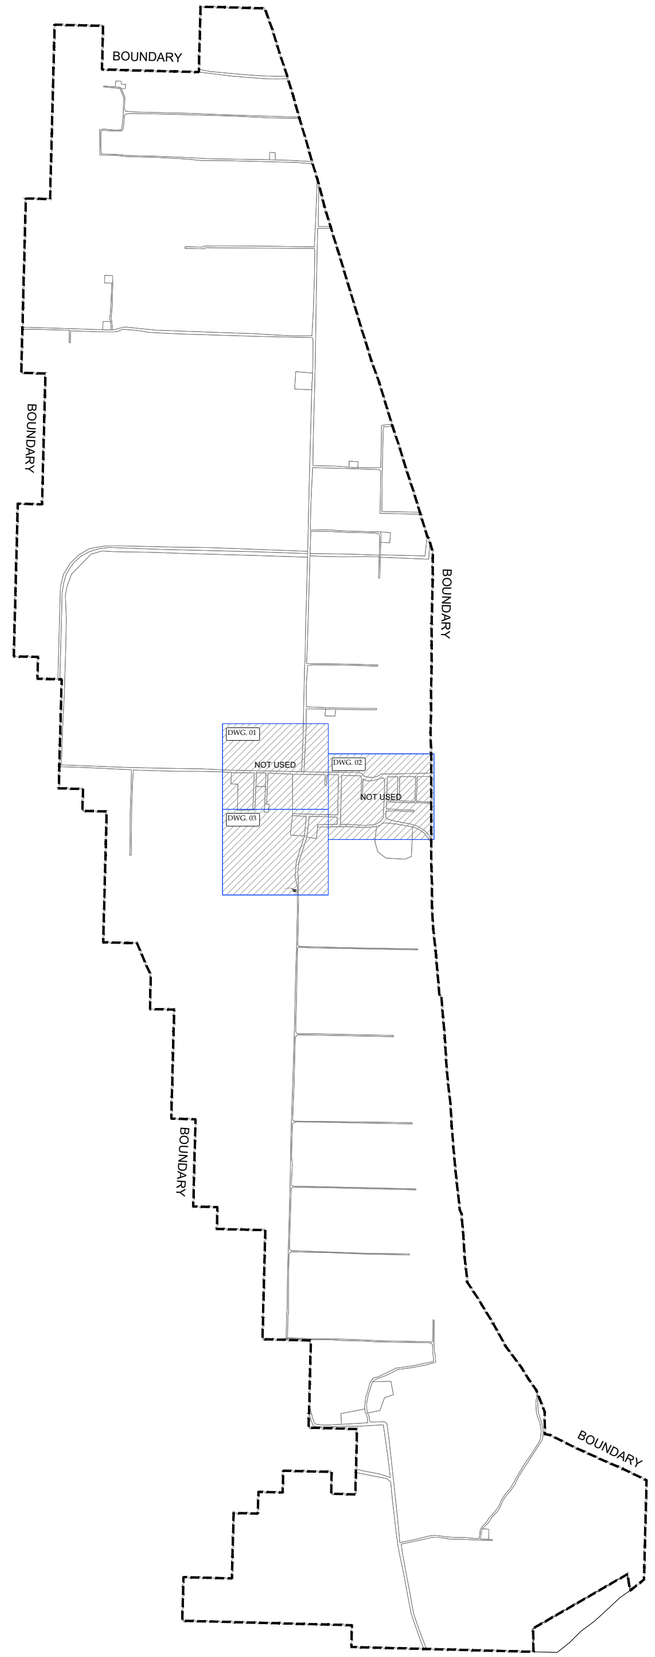

LEGEND:

RO PLANT

BOUNDARY

VILLAGE: MALAK PUR(BWN)

TITLE.

WATER SUPPLY SYSTEM KEY PLAN

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 1000'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	02-01-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-MLP-WS-KP-00	00 OF 00	00

PROJECT:

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:

PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT

ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

PRMSC-BWN-MLP-WS-KP-00

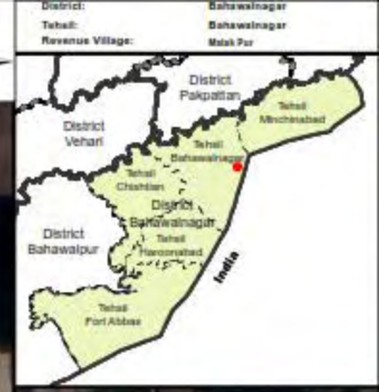

Title:
Proposed Water Supply Plan

Legend:

- SETTLEMENT
- STAND POST
- SETTELMENT BOUNDARY

Scale: 1:2,300
1 inch = 192 feet
Paper Size: A3

0 40 80 160
Kilometers

Project:
Engineering Design & Construction Supervision, Punjab Rural Sustainable Water Supply & Sanitation Project, Cluster South-III

LAYOUT PLANS



KEY PLAN

LEGEND:

RO PLANT

BOUNDARY

VILLAGE: MALAK PUR(BWN)

TITLE.

WATAR SUPPLY SYSTEM LAYOUT PLAN-03

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	02-01-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-MLP-WS-LP-03	03 OF 03	00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

PRMSC-BWN-MSL-WS-LP-03

MINA SANATTEKA

KEY PLAN

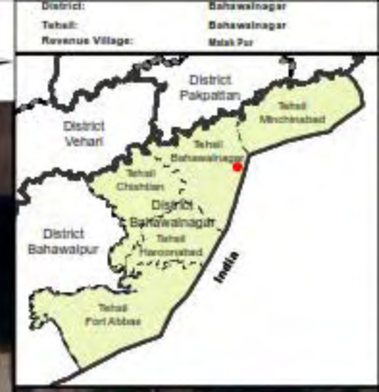

Title:
Proposed Water Supply Plan

Legend:

- SETTLEMENT
- STAND POST
- SETTELMENT BOUNDARY

Scale: 1:2,300
1 inch = 192 feet
Paper Size: A3

0 40 80 160
Kilometers

Project:
Engineering Design & Construction Supervision, Punjab Rural Sustainable Water Supply & Sanitation Project, Cluster South-III

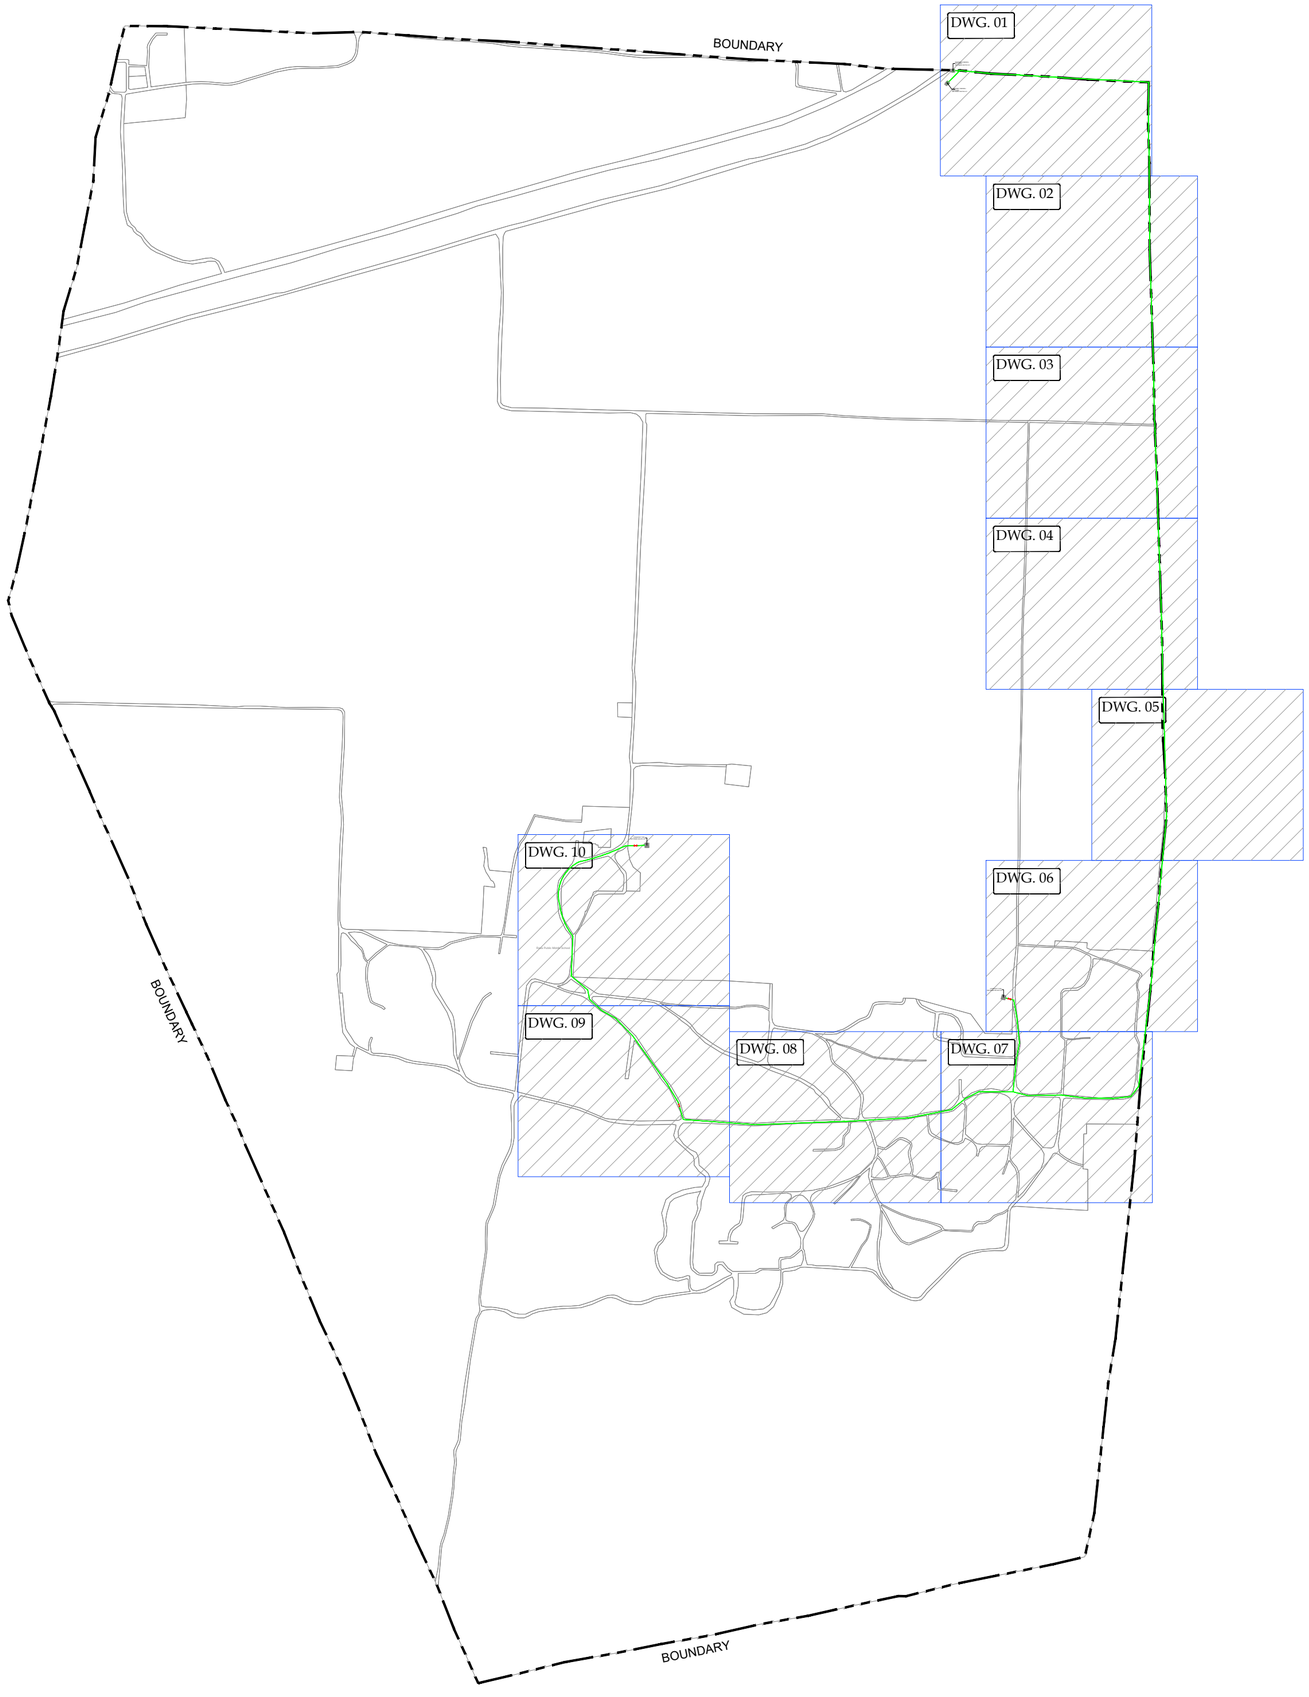

N
W
E
S

LEGEND:

- Ø150mm uPVC PIPE
- SLUICE VALVE
- AIR RELEASE VALVE
- PROPOSED TUBE WELL
- STAND POST TYPE - I
- DEAD END
- BOUNDARY

VILLAGE: MINA SANETTEKA (BWN)

TITLE.

WATER SUPPLY SYSTEM KEY PLAN

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 500'

ISSUE N°	DATE	D E S C R I P T I O N	DRAWN	DESIGNED	APPROVED
01	03-03-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-MST-WS-KP-00	00 OF 00	00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT
ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

PRMSC-BWN-MST-SEW-KP-00

LAYOUT PLANS

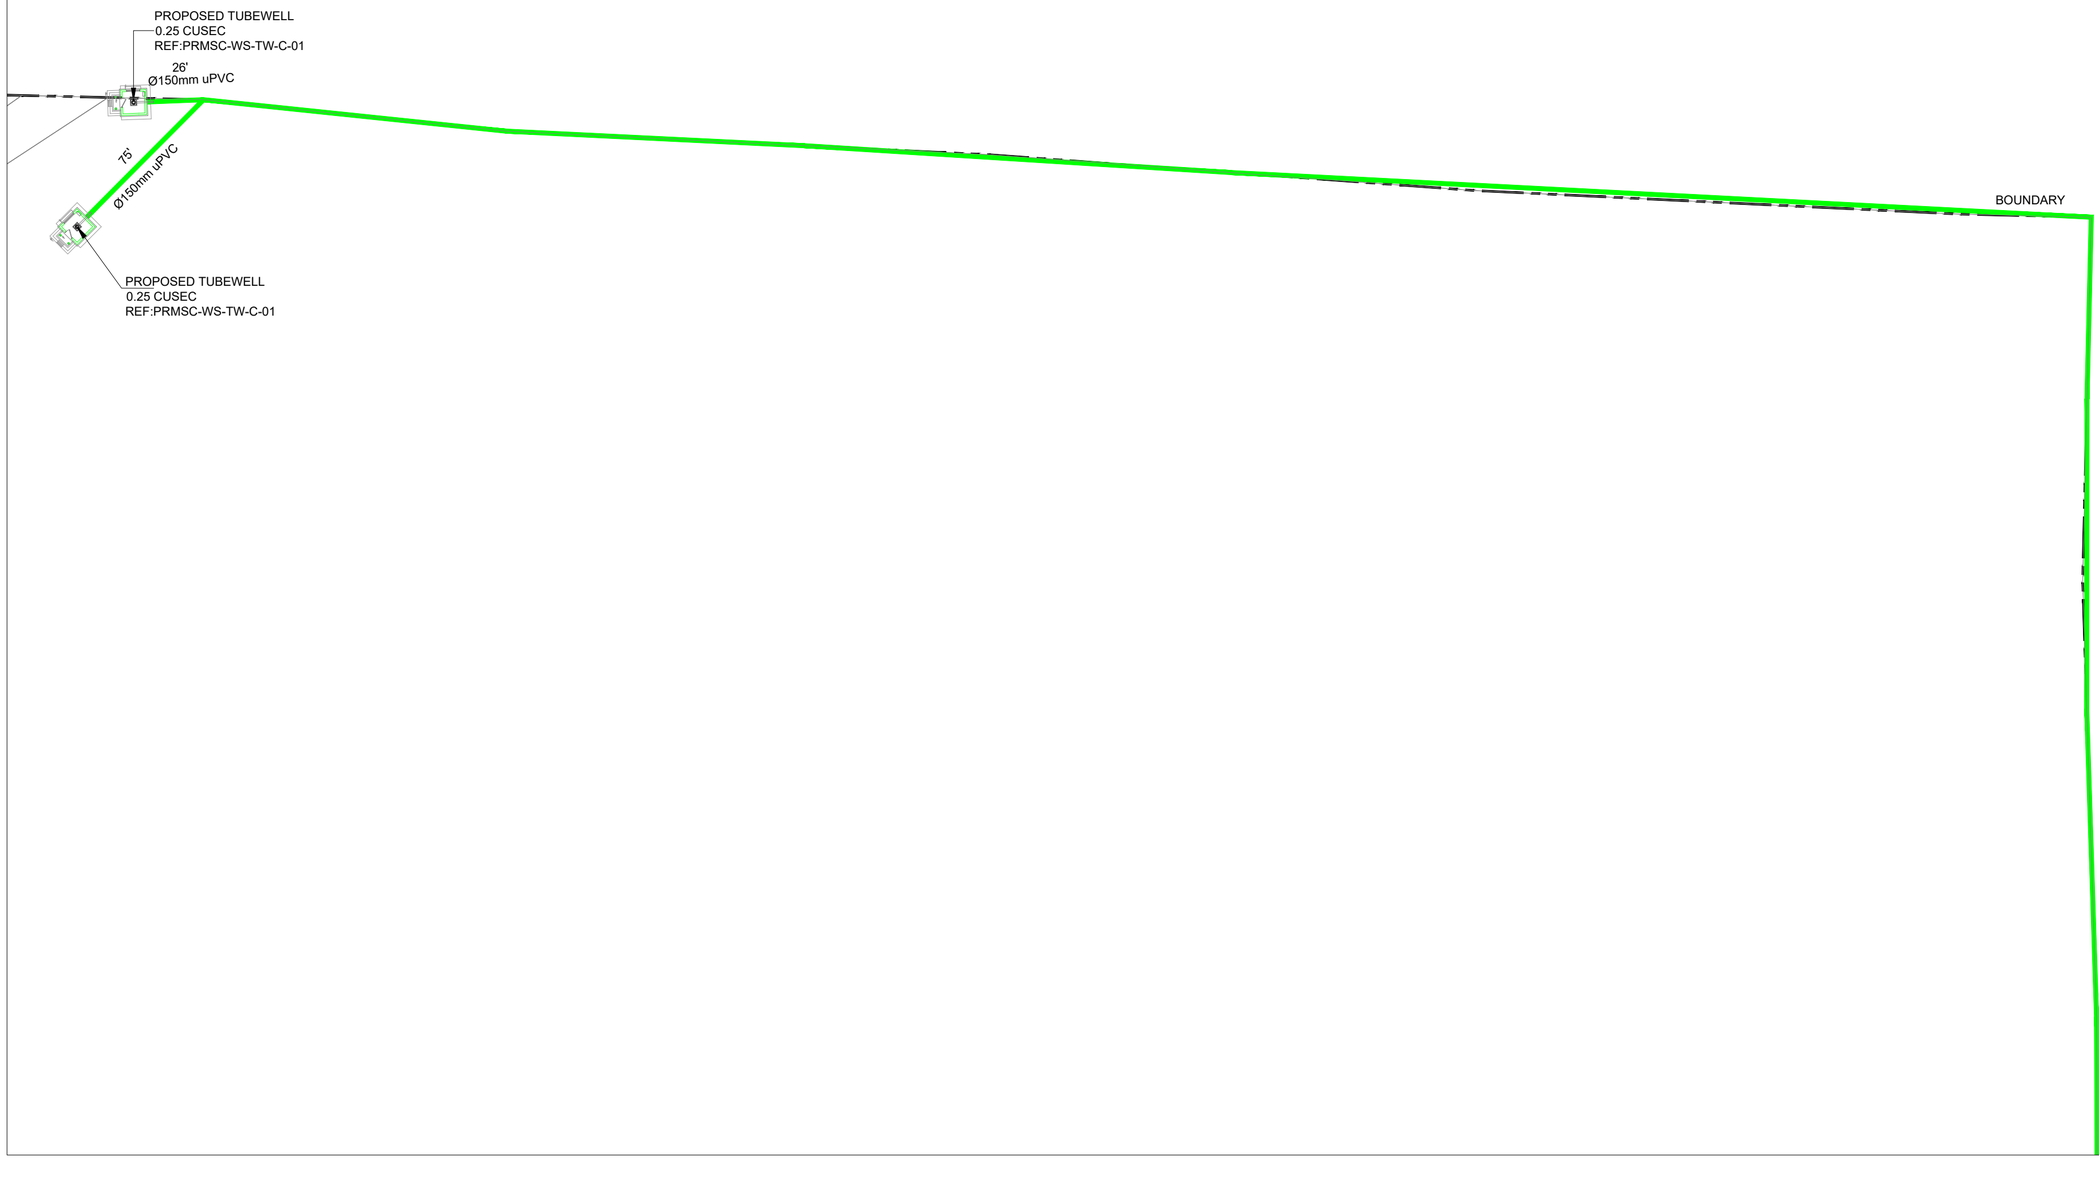

KEY PLAN

LEGEND:

- Ø150mm uPVC PIPE
- SLUICE VALVE
- AIR RELEASE VALVE
- PROPOSED TUBE WELL
- STAND POST TYPE - I
- DEAD END
- BOUNDARY

VILLAGE: MINA SANETTEKA (BWN)

TITLE.

WATER SUPPLY SYSTEM LAYOUT PLAN-01

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	D E S C R I P T I O N	DRAWN	DESIGNED	APPROVED
01	03-03-2026	DETAILED DESIGN	MUNEEB	ENGR FAIEZ	ENGR IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-MST-WS-LP-01	01 OF 10	00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:
ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

PRMSC-BWN-MST-WS-LP-01

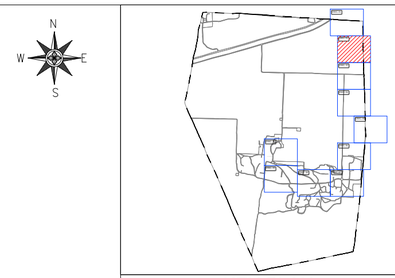

KEY PLAN

LEGEND:

Ø150mm uPVC PIPE

SLUICE VALVE

AIR RELEASE VALVE

PROPOSED TUBE WELL

STAND POST TYPE - I

DEAD END

BOUNDARY

BOUNDARY

5426'

Ø150mm uPVC

VILLAGE: MINA SANETTEKA (BWN)

TITLE.

WATER SUPPLY SYSTEM LAYOUT PLAN-02

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	D E S C R I P T I O N	DRAWN	DESIGNED	APPROVED
01	03-03-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. HSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-MST-WS-LP-02	02 OF 10	00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:
ASIAN CONSULTING ENGINEERS
www.asiancon.com

PRMSC-BWN-MST-WS-LP-02

KEY PLAN

LEGEND:

Ø150mm uPVC PIPE

SLUICE VALVE

AIR RELEASE VALVE

PROPOSED TUBE WELL

STAND POST TYPE - I

DEAD END

BOUNDARY

BOUNDARY

PRMSC-BWN-MST-WS-LP-03

VILLAGE: MINA SANETTEKA (BWN)

TITLE:

WATER SUPPLY SYSTEM LAYOUT PLAN-03

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	03-03-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. HSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-MST-WS-LP-03	03 OF 10	00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

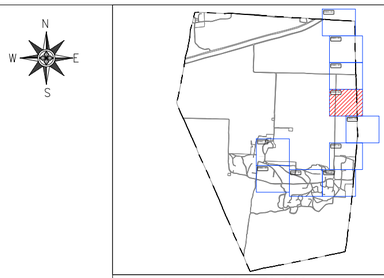

KEY PLAN

LEGEND:

Ø150mm uPVC PIPE

SLUICE VALVE

AIR RELEASE VALVE

PROPOSED TUBE WELL

STAND POST TYPE - I

DEAD END

BOUNDARY

BOUNDARY

PRMSC-BWN-MST-WS-LP-04

VILLAGE: MINA SANETTEKA (BWN)

TITLE.

WATER SUPPLY SYSTEM LAYOUT PLAN-04

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	03-03-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-MST-WS-LP-04	04 OF 10	00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

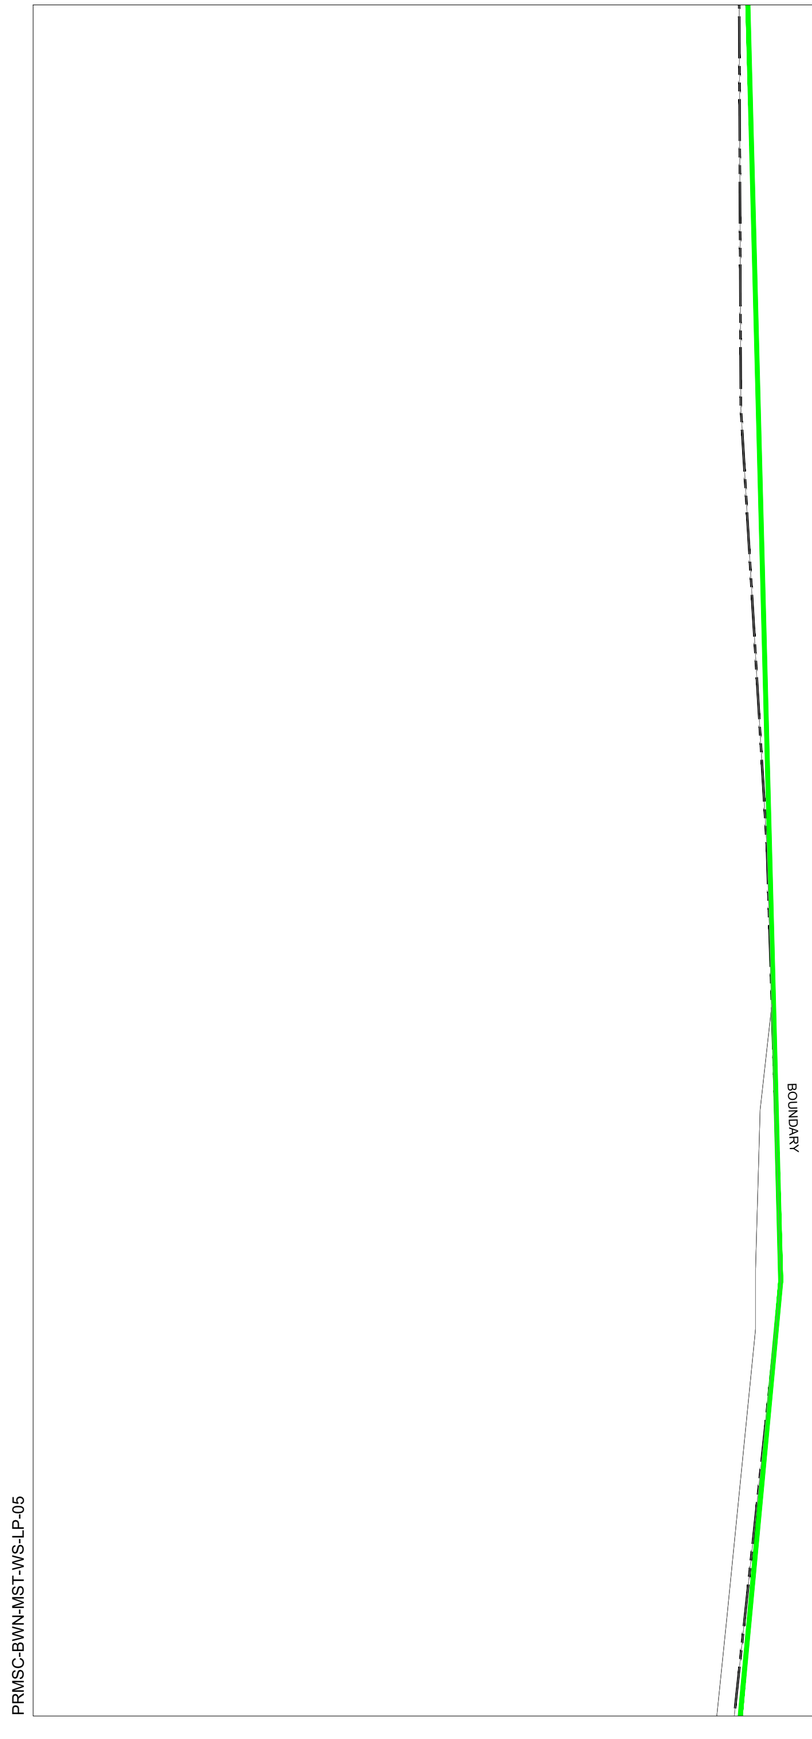

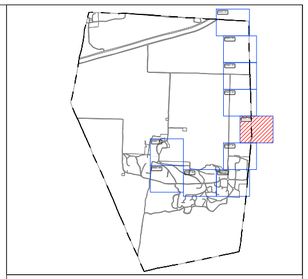

KEY PLAN

LEGEND:

- Ø150mm uPVC PIPE
- SLUICE VALVE
- AIR RELEASE VALVE
- PROPOSED TUBE WELL
- STAND POST TYPE - I
- DEAD END
- BOUNDARY

VILLAGE: MINA SANETTEKA (BWN)

TITLE.

WATER SUPPLY SYSTEM LAYOUT PLAN-05

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°.	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	03-03-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-MST-WS-LP-05	05 OF 10	00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:
ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

PRMSC-BWN-MST-WS-LP-05

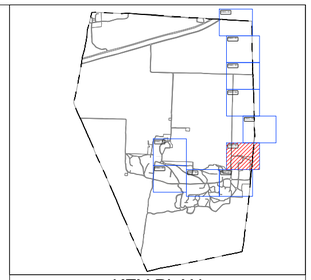

KEY PLAN

LEGEND:

- Ø150mm uPVC PIPE
- SLUICE VALVE
- AIR RELEASE VALVE
- PROPOSED TUBE WELL
- STAND POST TYPE - I
- DEAD END
- BOUNDARY

VILLAGE: MINA SANETTEKA (BWN)

TITLE.

WATER SUPPLY SYSTEM LAYOUT PLAN-06

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	03-03-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-MST-WS-LP-06	06 OF 10	00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

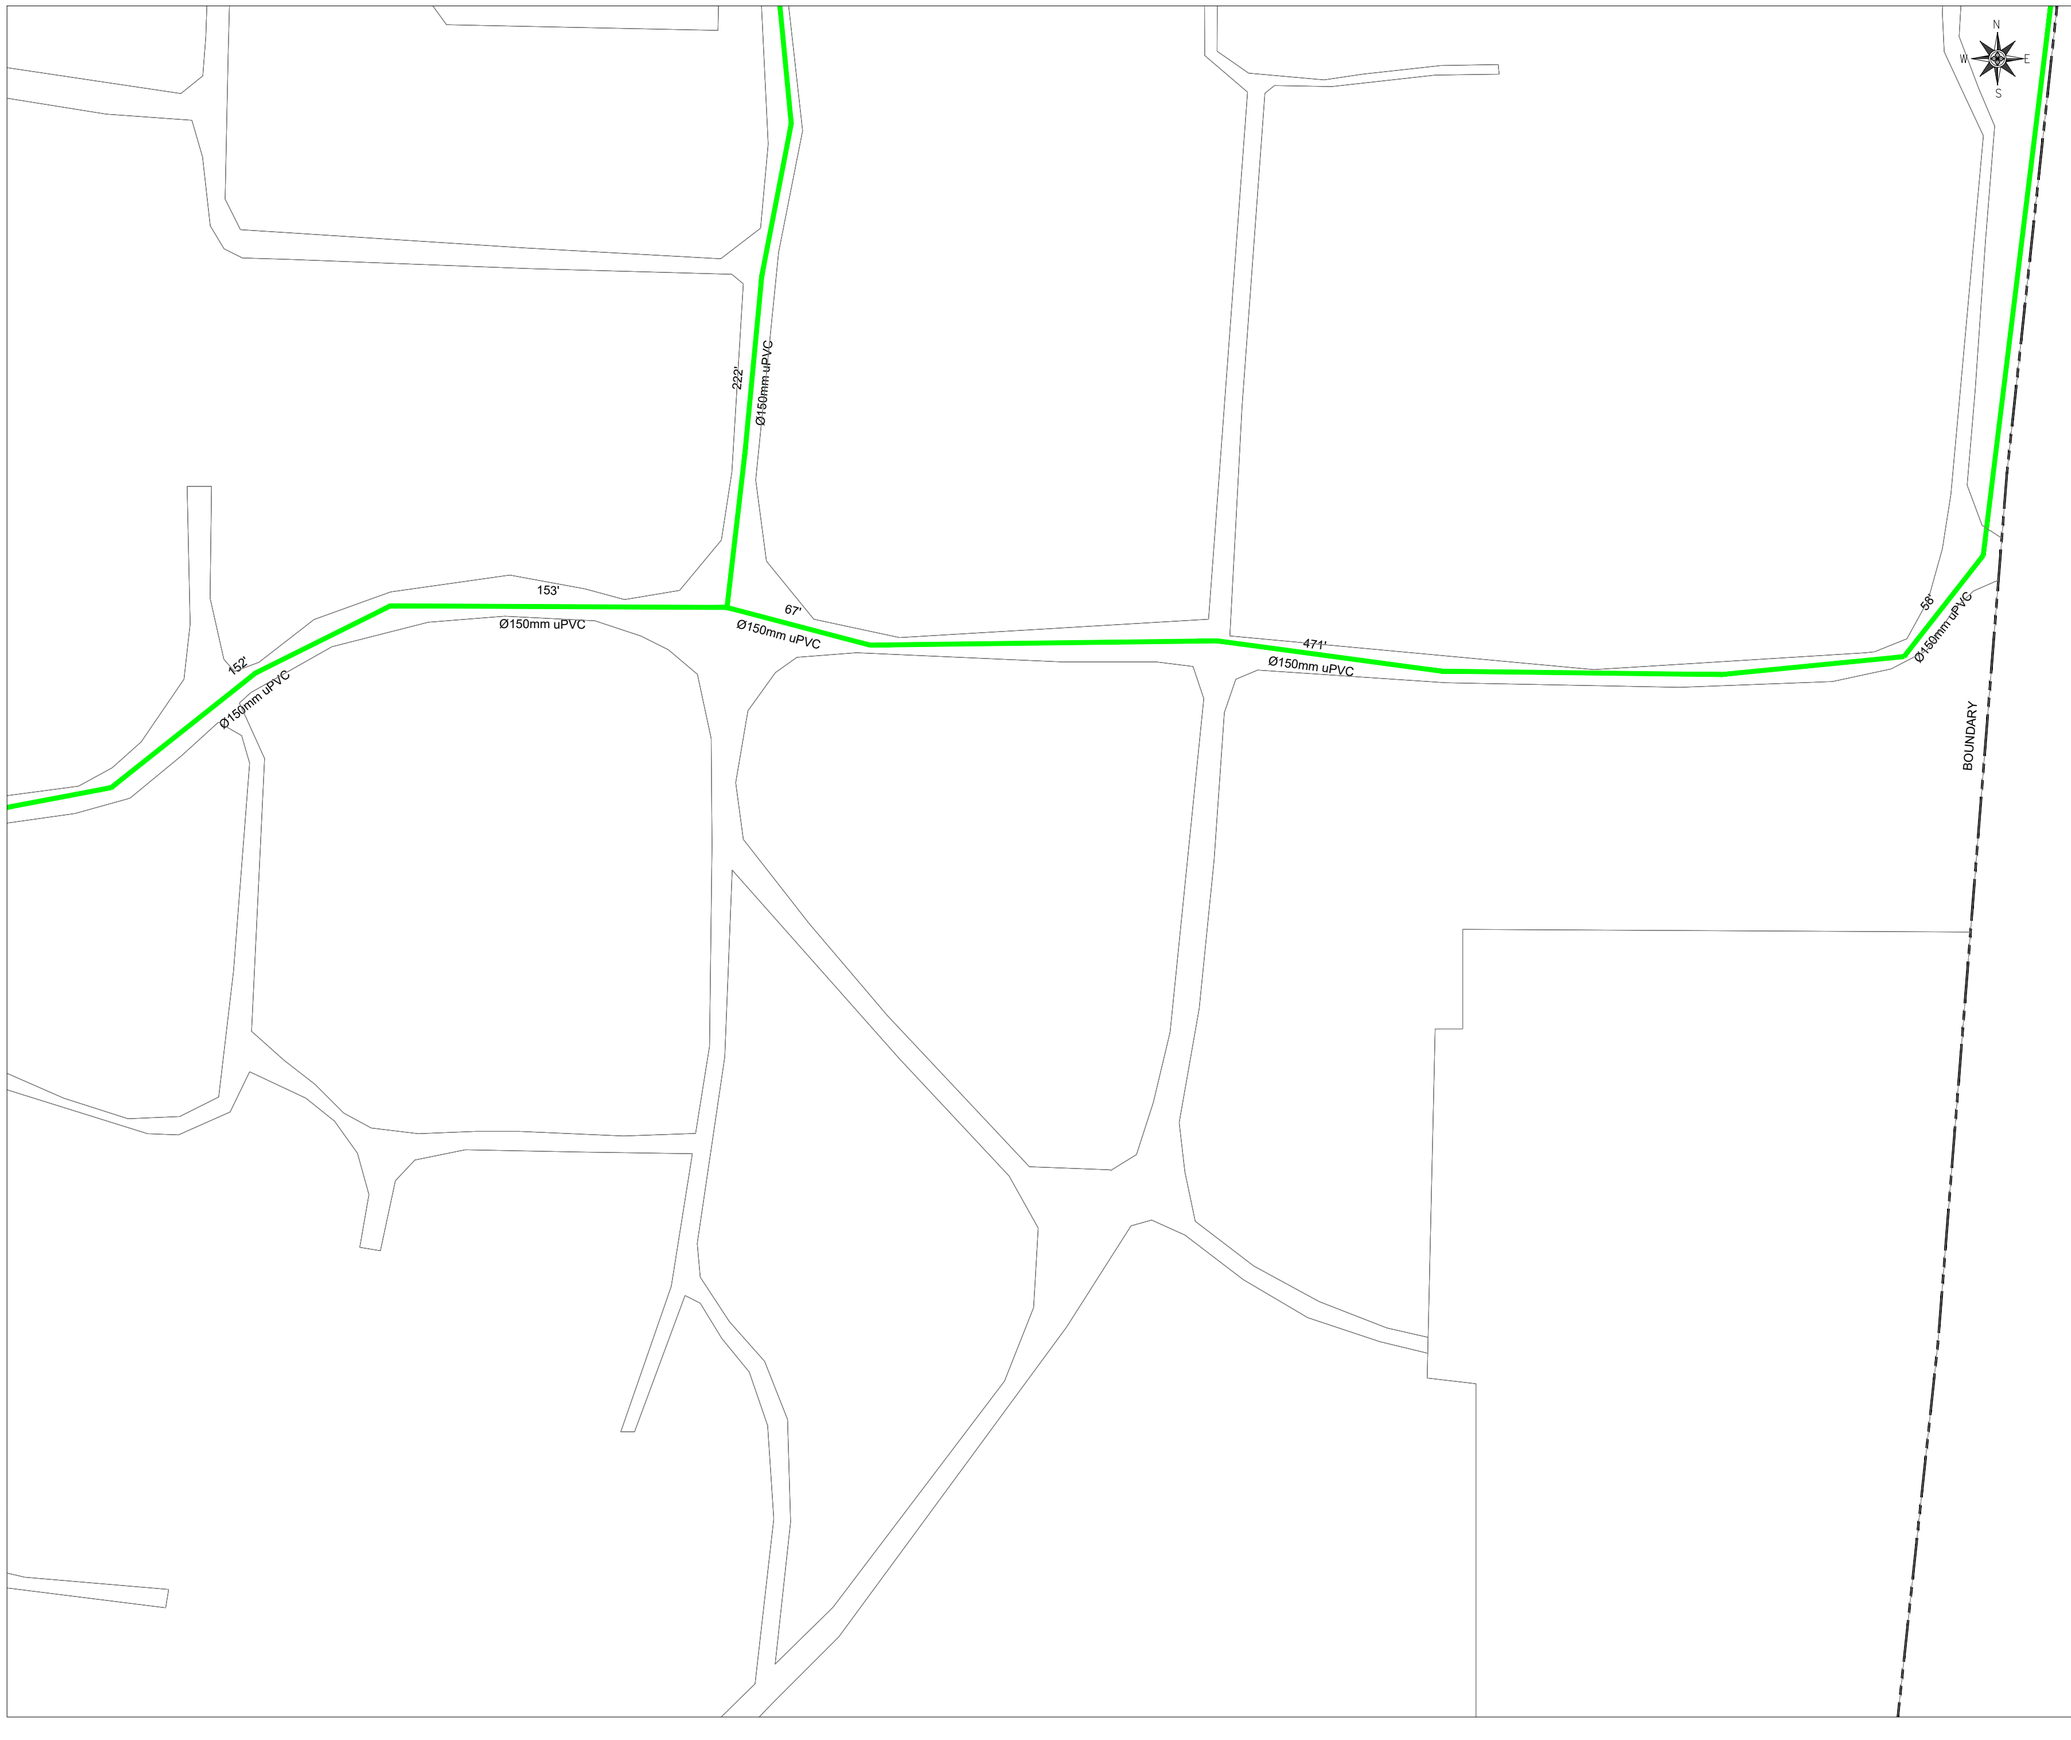

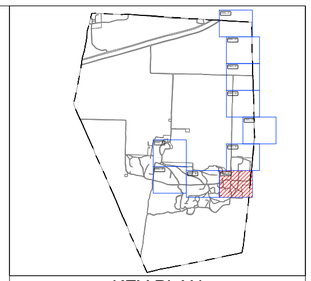

KEY PLAN

LEGEND:

- Ø150mm uPVC PIPE
- SLUICE VALVE
- AIR RELEASE VALVE
- PROPOSED TUBE WELL
- STAND POST TYPE - I
- DEAD END
- BOUNDARY

VILLAGE: MINA SANETTEKA (BWN)

TITLE.

WATER SUPPLY SYSTEM LAYOUT PLAN-07

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°.	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	03-03-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-MST-WS-LP-07	07 OF 10	00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:
ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

PRMSC-BWN-MST-WS-LP-07

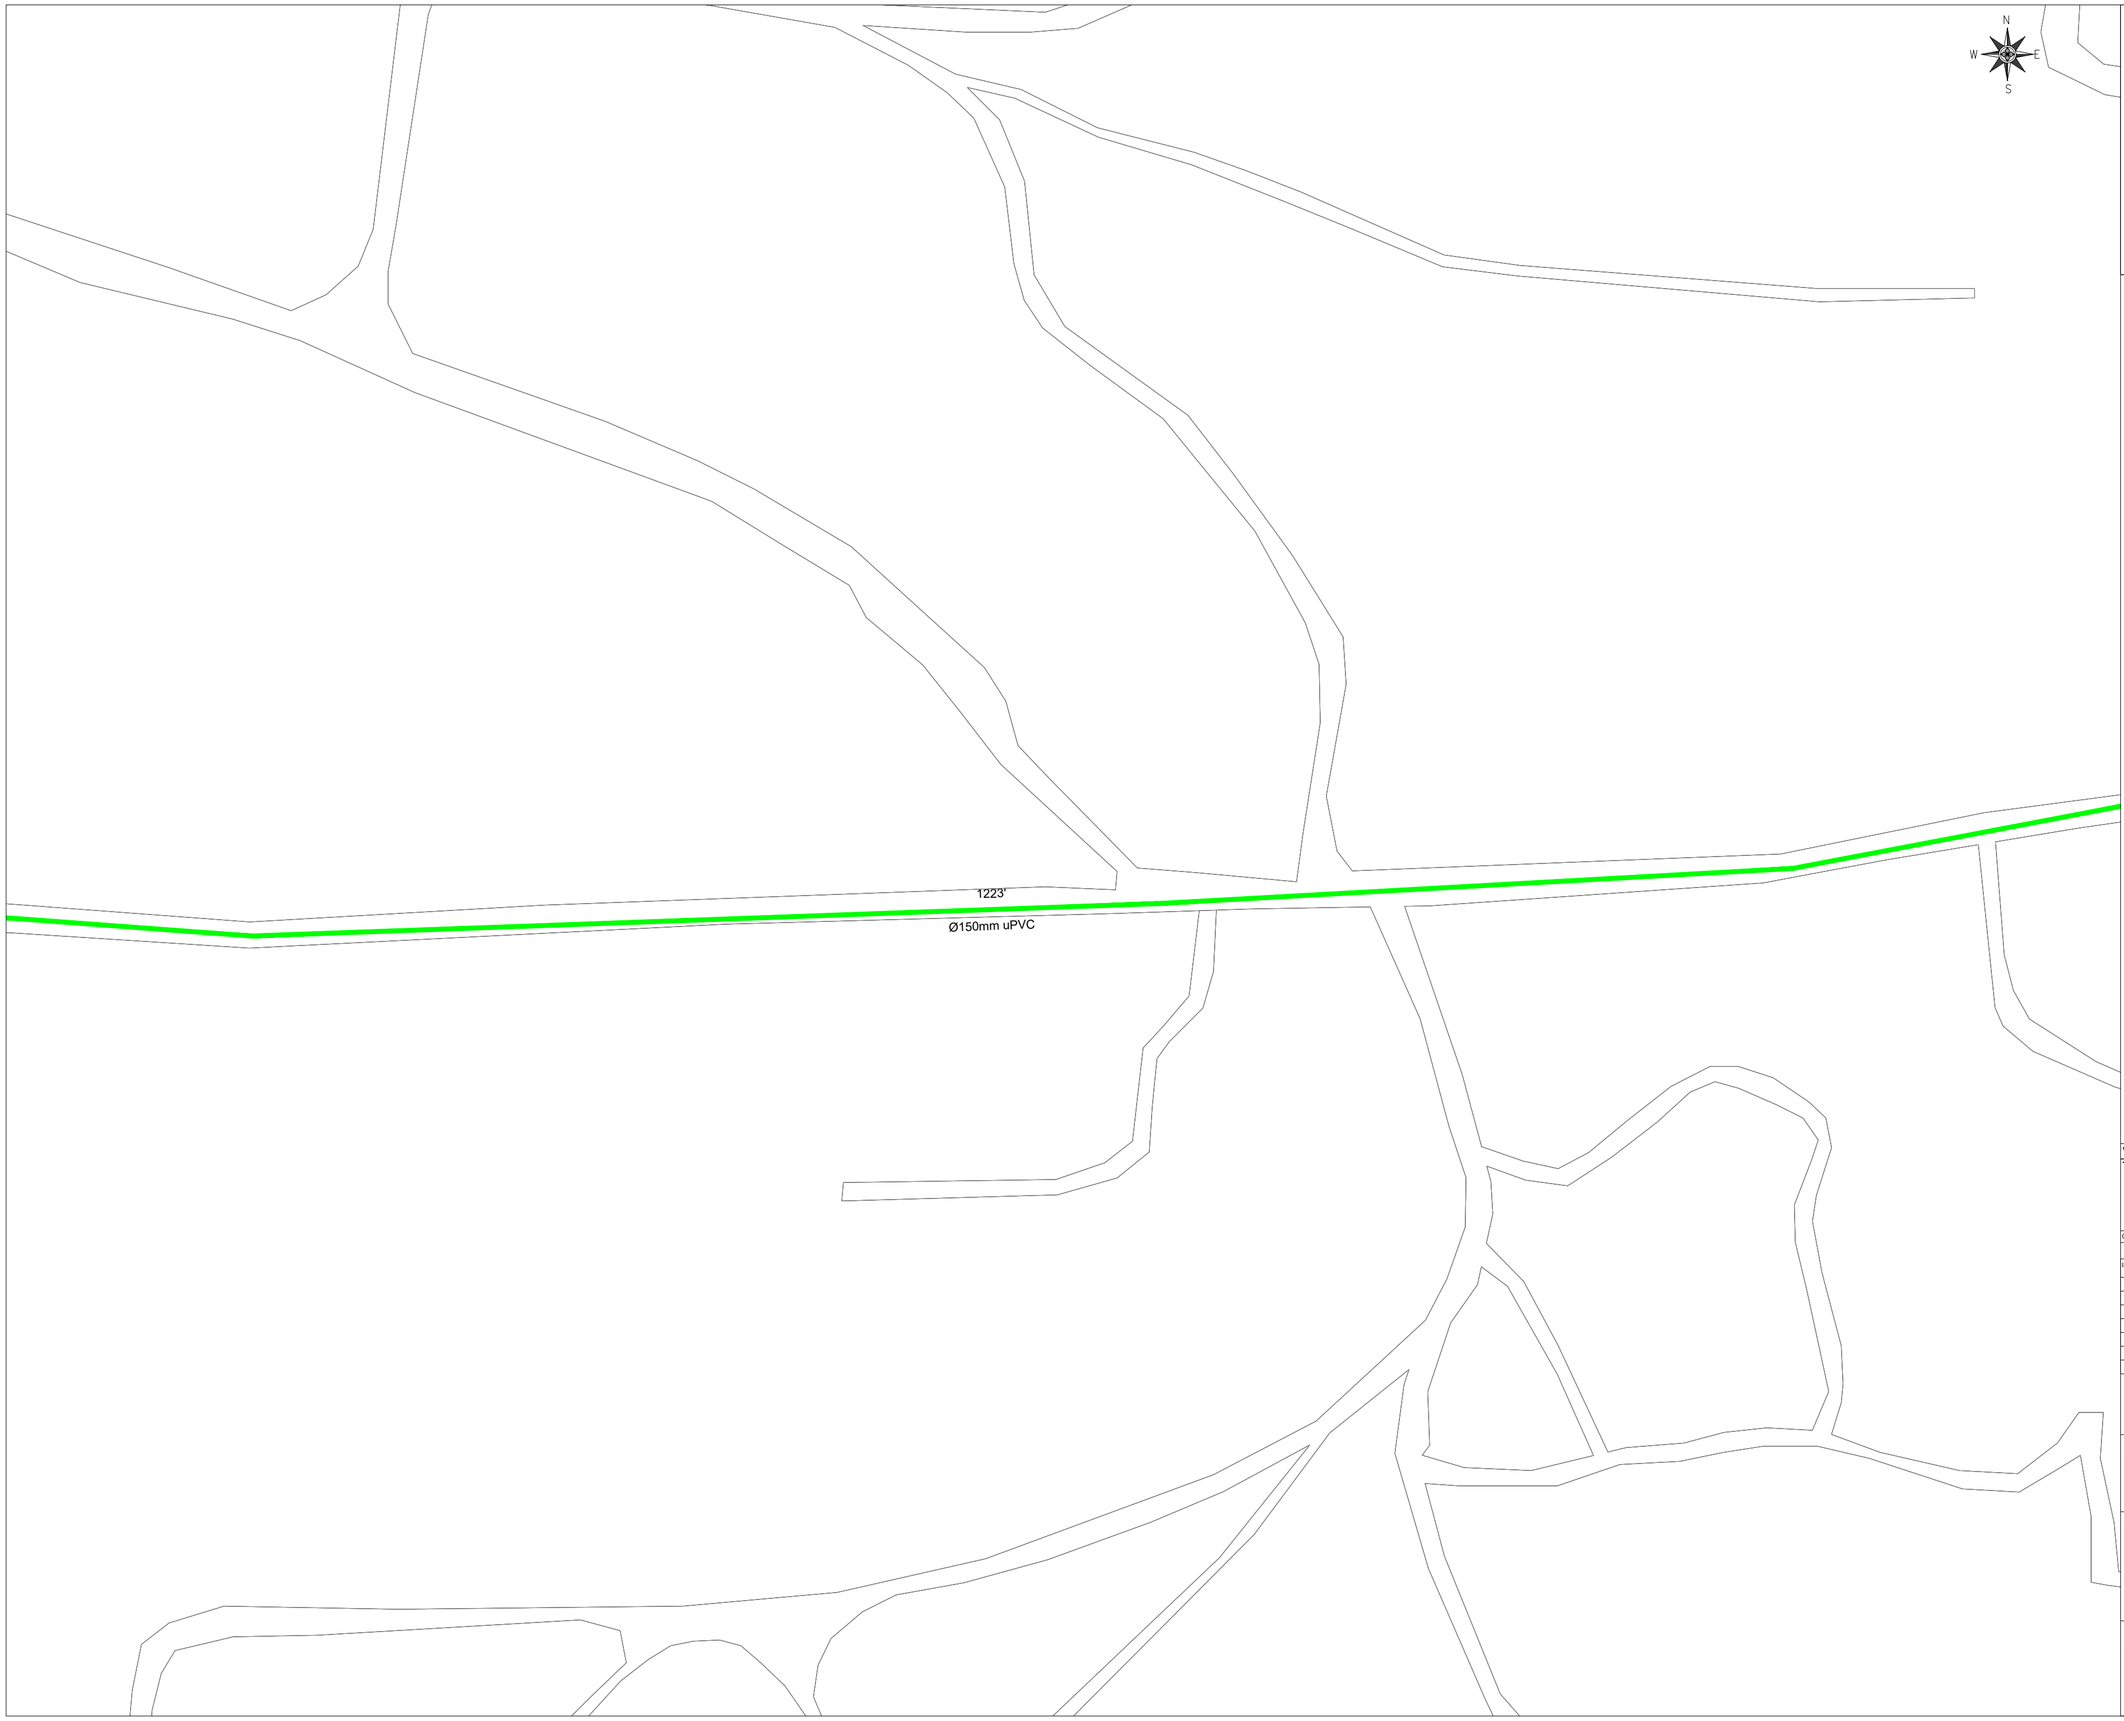

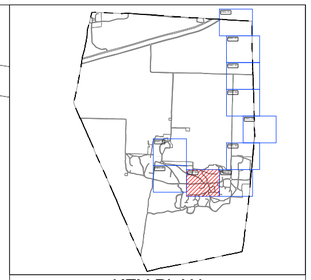

KEY PLAN

LEGEND:

- Ø150mm uPVC PIPE
- SLUICE VALVE
- AIR RELEASE VALVE
- PROPOSED TUBE WELL
- STAND POST TYPE - I
- DEAD END
- BOUNDARY

VILLAGE: MINA SANETTEKA (BWN)

TITLE.

WATER SUPPLY SYSTEM LAYOUT PLAN-08

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	D E S C R I P T I O N	DRAWN	DESIGNED	APPROVED
01	03-03-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº: PRMSC-BWN-MST-WS-LP-08

SHEET 08 OF 10

REV 00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:
ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

PRMSC-BWN-MST-WS-LP-08

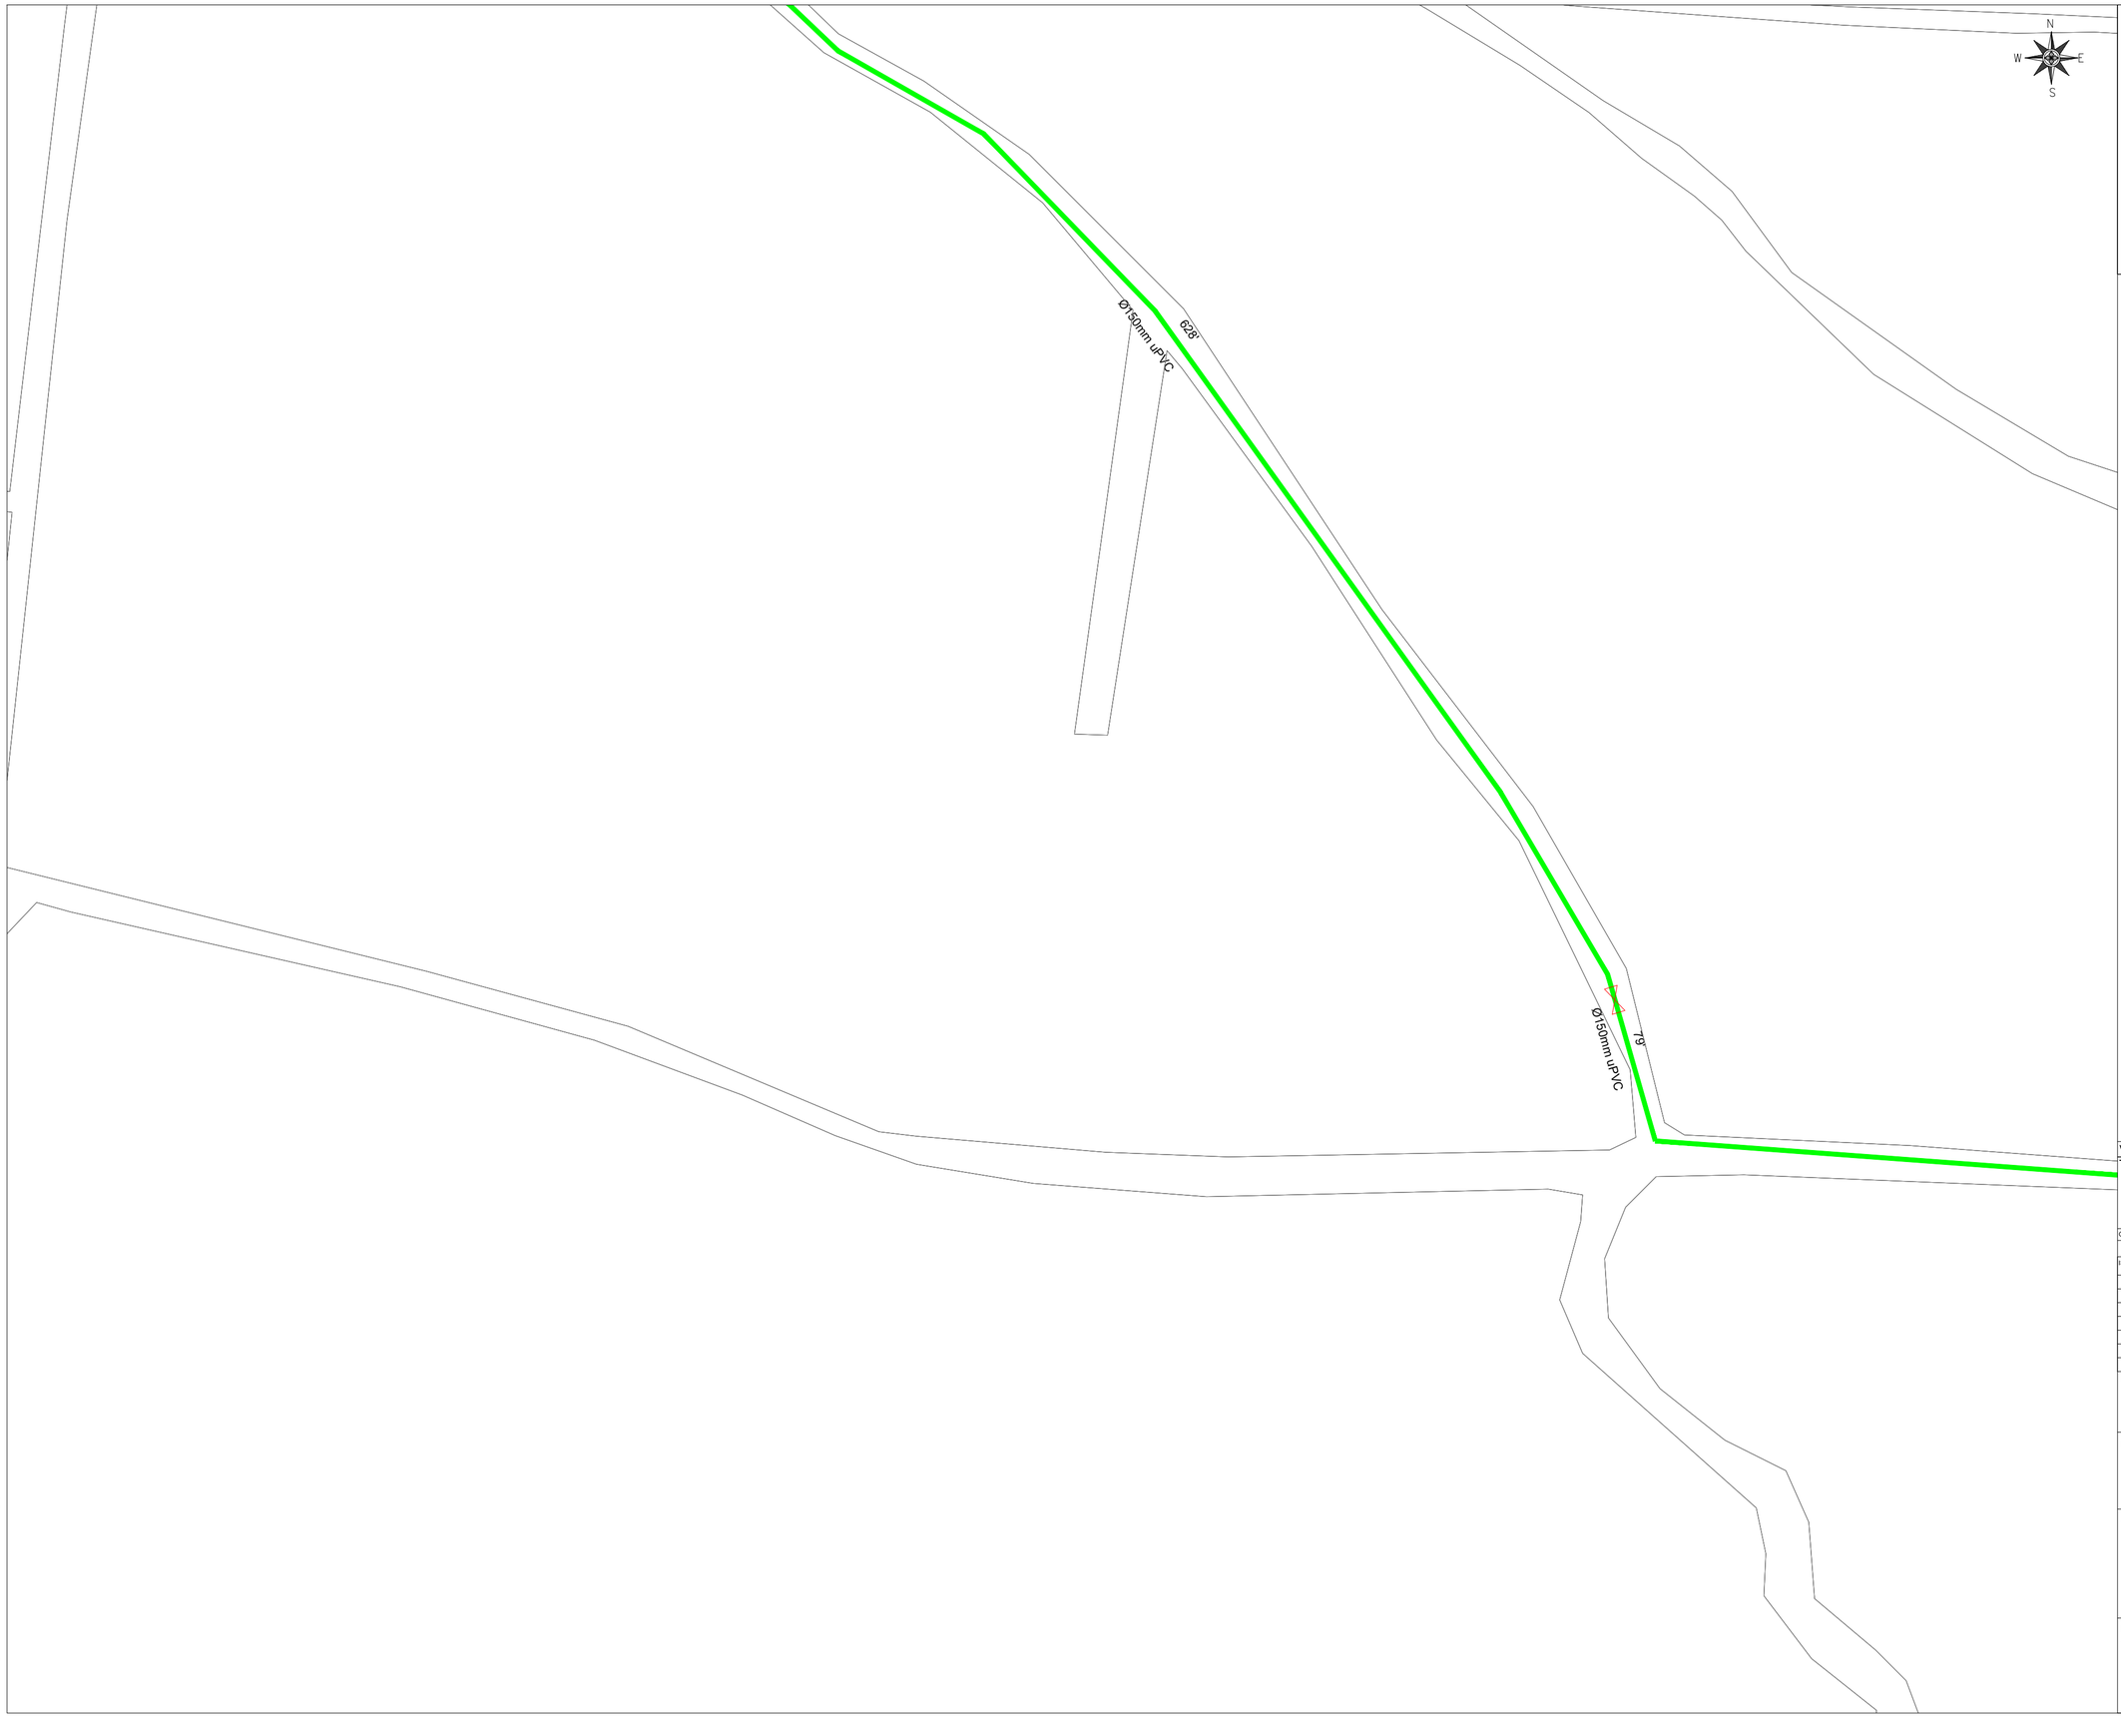

KEY PLAN

LEGEND:

- Ø150mm uPVC PIPE
- SLUICE VALVE
- AIR RELEASE VALVE
- PROPOSED TUBE WELL
- STAND POST TYPE - I
- DEAD END
- BOUNDARY

VILLAGE: MINA SANETTEKA (BWN)

TITLE.

WATER SUPPLY SYSTEM LAYOUT PLAN-09

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	03-03-2026	DETAILED DESIGN	MUNEEB	ENGR FAIEZ	ENGR IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-MST-WS-LP-09	09 OF 10	00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS (PVT) LTD. www.asiancon.com.pk

PRMSC-BWN-MST-WS-LP-09

STANDPOST TYPE-I
REF:PRMSC-WS-SP-C-02

92'
Ø150mm uPVC

611'
Ø150mm uPVC

Raza Public Middle School

179'
Ø150mm uPVC

100'
Ø150mm uPVC

41'
Ø150mm uPVC

PRMSC-BWN-MST-WS-LP-10

N
W
E
S



KEY PLAN

LEGEND:

- Ø150mm uPVC PIPE
- SLUICE VALVE
- AIR RELEASE VALVE
- PROPOSED TUBE WELL
- STAND POST TYPE - I
- DEAD END
- BOUNDARY

VILLAGE: MINA SANETTEKA (BWN)

TITLE.

WATER SUPPLY SYSTEM LAYOUT PLAN-10

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	03-03-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. HSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-MST-WS-LP-10	10 OF 10	00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:
ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

NOOR JAHANIAN

KEY PLAN

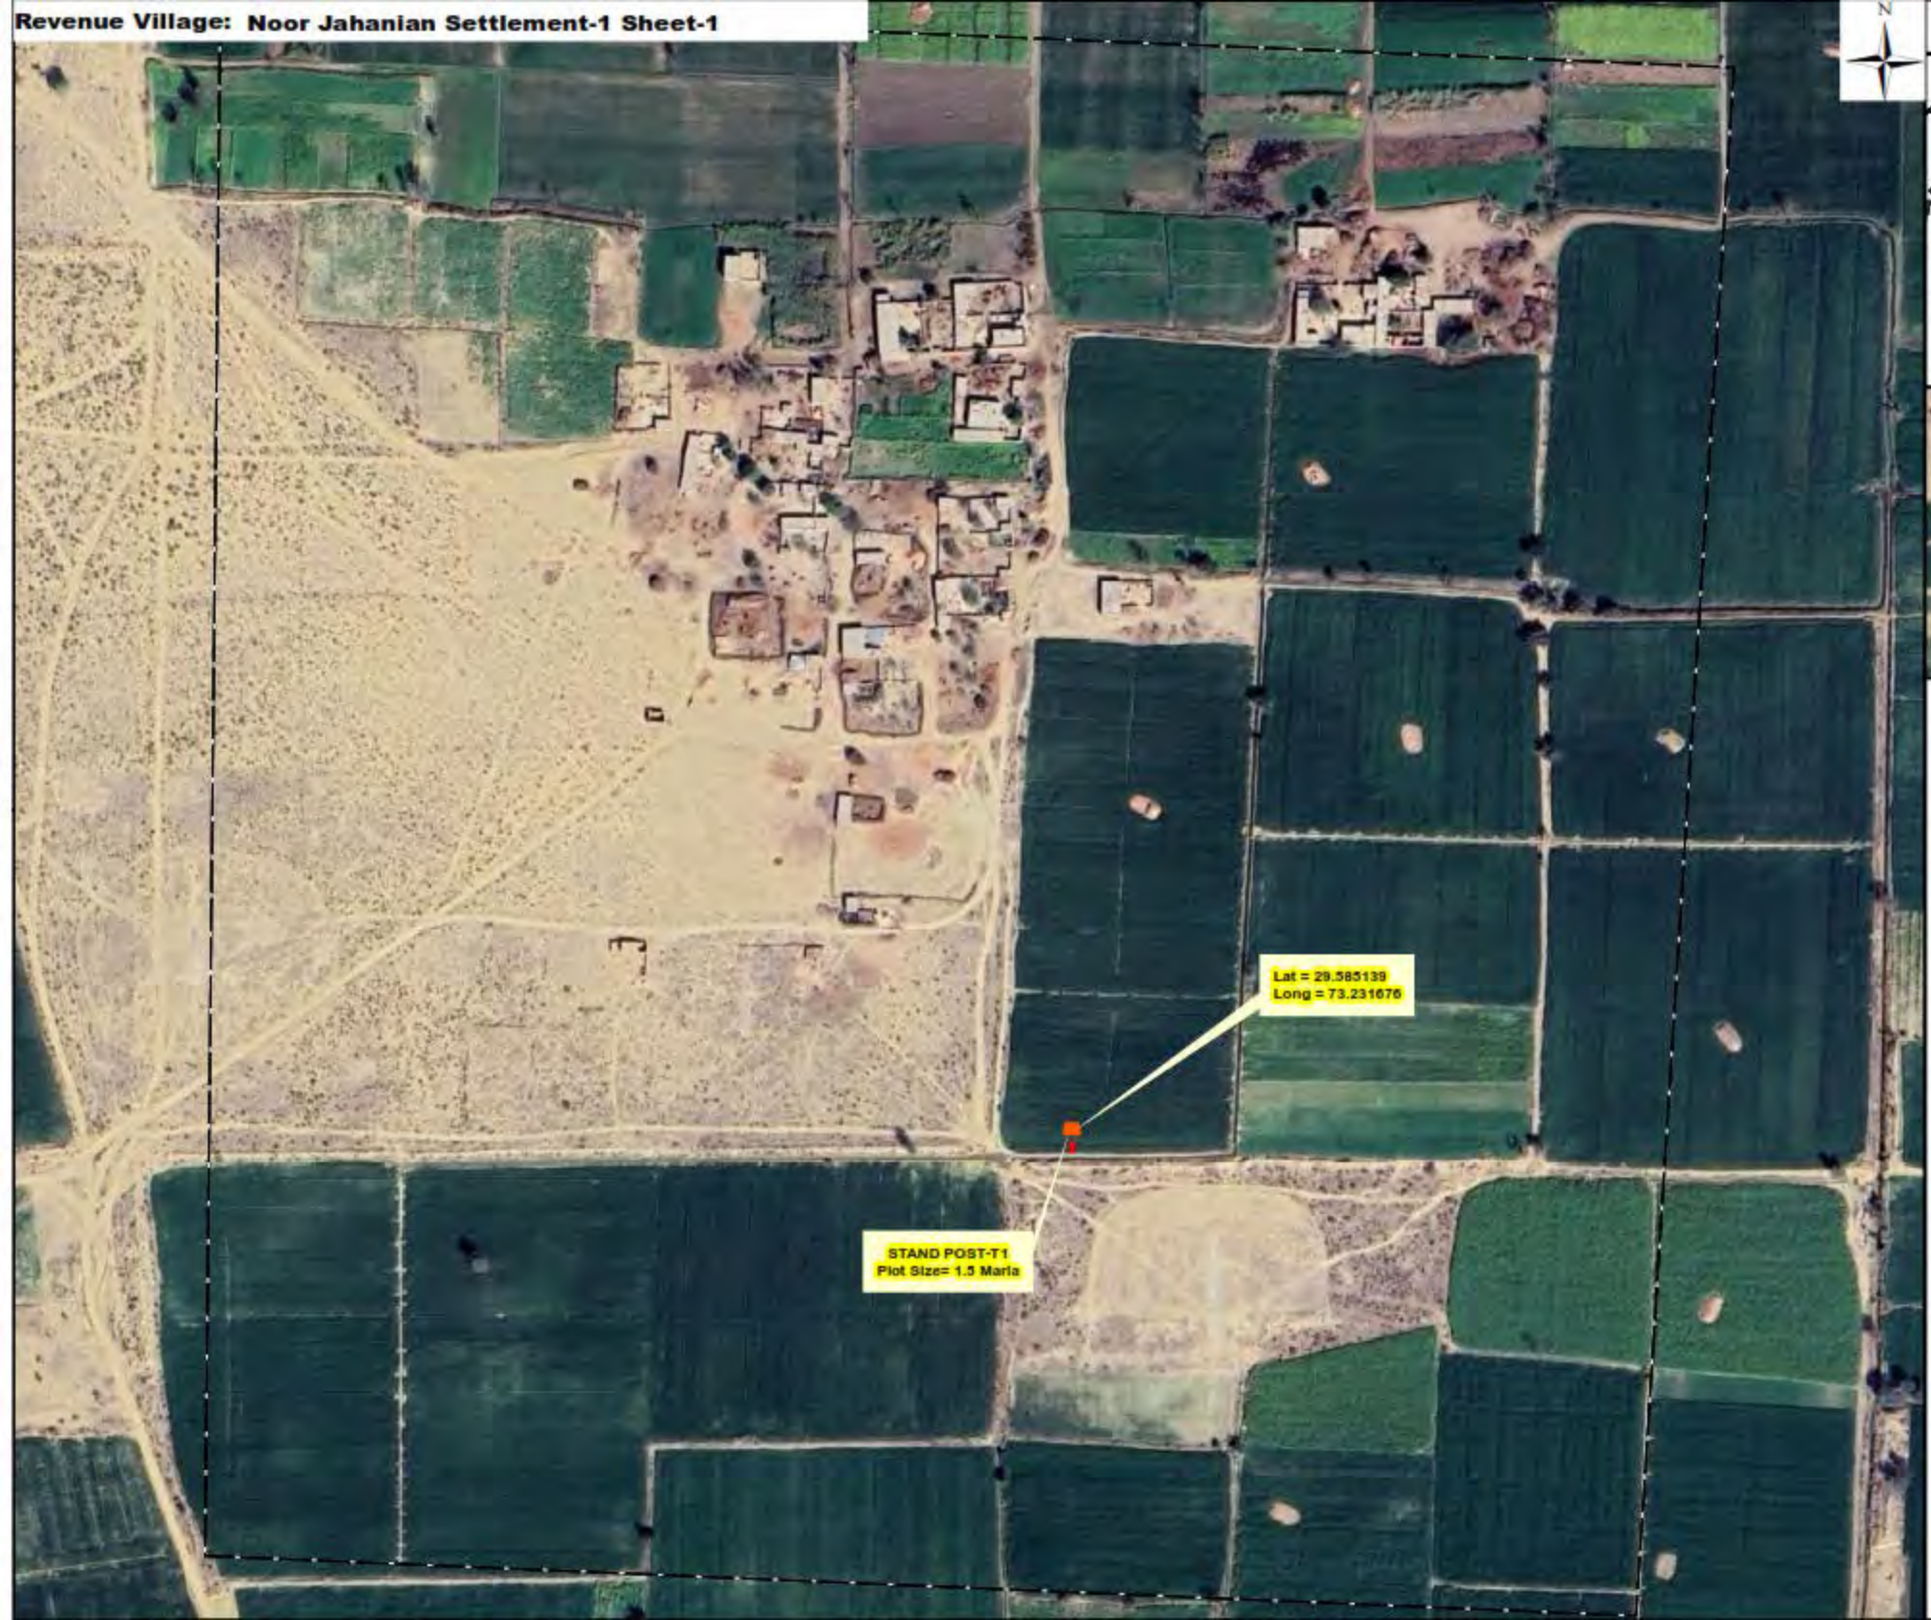



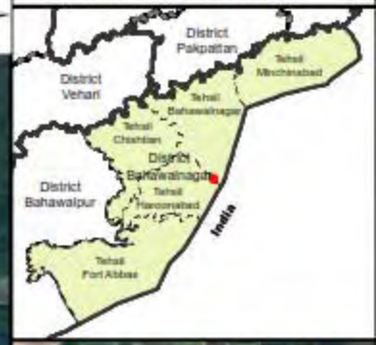

Title:
Proposed Water Supply Plan

Legend:

- STAND POST
- SETTELMENT BOUNDARY

Scale: 1:2,400
1 inch = 200 feet
Paper Size: A3

0 40 80 160
Kilometers

Project:
Engineering Design & Construction Supervision, Punjab Rural Sustainable Water Supply & Sanitation Project, Cluster South-III

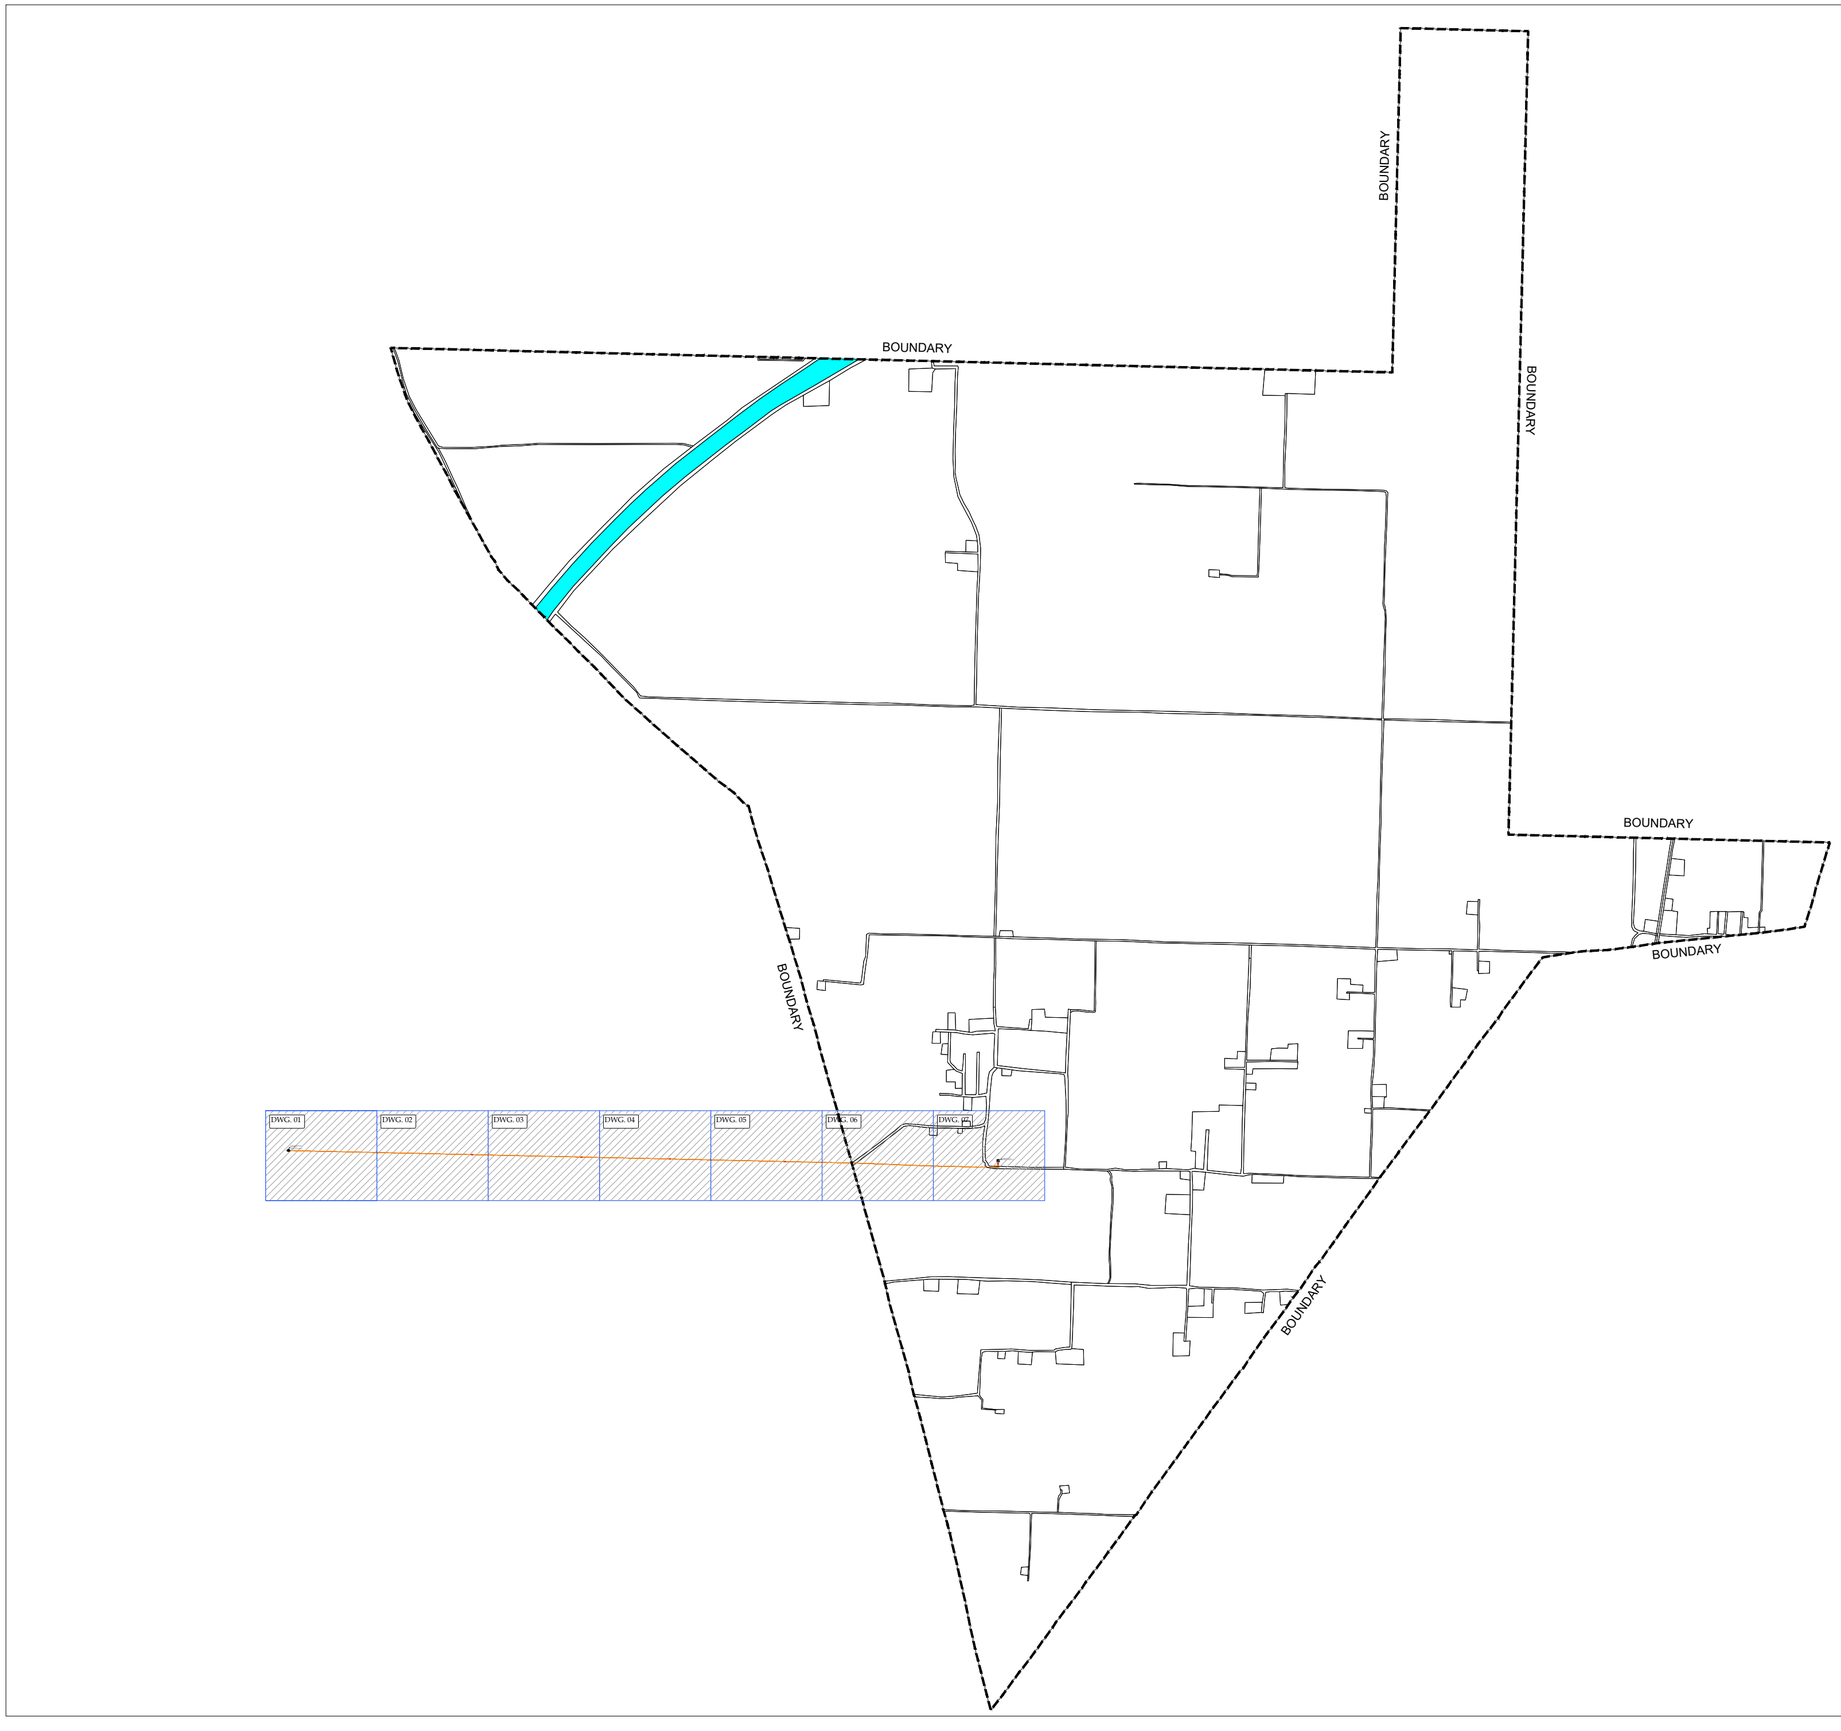

LEGEND:

- 90mm Ø HDPE PIPE
- SLUICE VALVE
- WASHOUT VALVE
- AIR RELEAS VALVE
- PROPOSED STAND POST TYPE - I
- PROPOSED TUBE WELL
- BOUNDARY

VILLAGE: NOOR JAHANIAN (BWN)

TITLE.

WATER SUPPLY SYSTEM KEY PLAN

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 950'

ISSUE N°	DATE	D E S C R I P T I O N	DRAWN	DESIGNED	APPROVED
01	02-01-2026	DETAILED DESIGN	M.ASIF	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº: PRMSC-BWN-NJN-WS-KP-00

SHEET 00 OF 00

REV 00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT
ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

PRMSC-BWN-NJN-WS-KP-00

LAYOUT PLANS

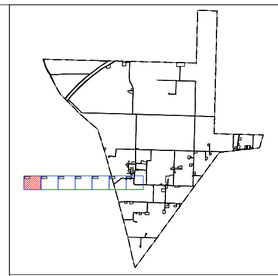

KEY PLAN

LEGEND:

- 90mm Ø HDPE PIPE
- SLUICE VALVE
- WASHOUT VALVE
- AIR RELEAS VALVE
- PROPOSED STAND POST TYPE - I
- PROPOSED TUBE WELL
- BOUNDARY

VILLAGE: NOOR JAHANIAN (BWN)

TITLE.

WATER SUPPLY SYSTEM LAYOUT PLAN-01

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	02-01-2026	DETAILED DESIGN	M.ASIF	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-NJN-WS-LP-01	01 OF 07	00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS www.asiancon.com

PRMSC-BWN-NJN-WS-LP-01



KEY PLAN

LEGEND:

- 90mm Ø HDPE PIPE
- SLUICE VALVE
- WASHOUT VALVE
- AIR RELEAS VALVE
- PROPOSED STAND POST TYPE - I
- PROPOSED TUBE WELL
- BOUNDARY

VILLAGE: NOOR JAHANIAN (BWN)

TITLE.

WATER SUPPLY SYSTEM LAYOUT PLAN-02

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	02-01-2026	DETAILED DESIGN	M.ASIF	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-NJN-WS-LP-02	02 OF 07	00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:
ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

PRMSC-BWN-NJN-WS-LP-02

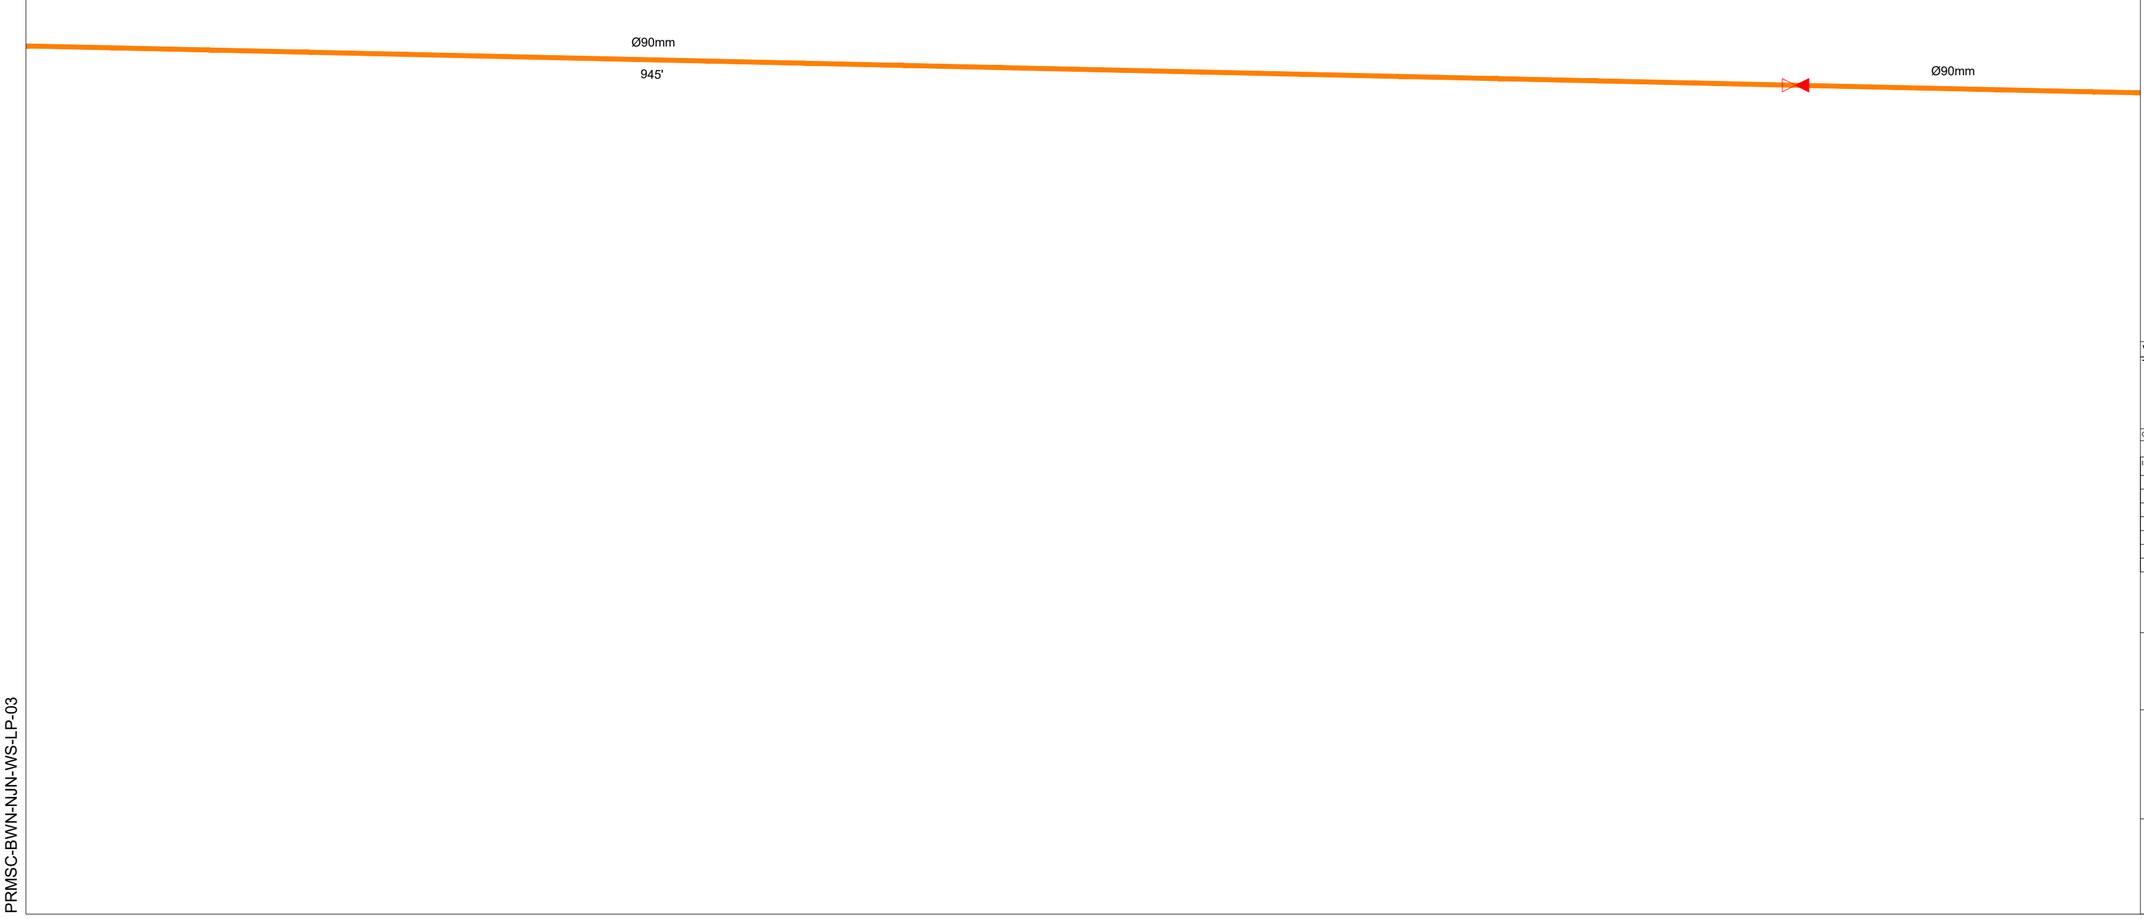

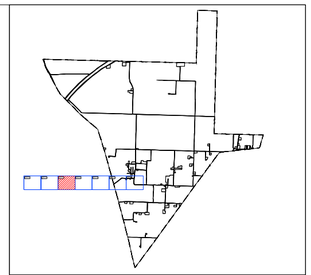

KEY PLAN

LEGEND:

- 90mm Ø HDPE PIPE
- SLUICE VALVE
- WASHOUT VALVE
- AIR RELEAS VALVE
- PROPOSED STAND POST TYPE - I
- PROPOSED TUBE WELL
- BOUNDARY

VILLAGE: NOOR JAHANIAN (BWN)

TITLE.

WATER SUPPLY SYSTEM LAYOUT PLAN-03

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	02-01-2026	DETAILED DESIGN	M.ASIF	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-NJN-WS-LP-03	03 OF 07	00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS
www.asiancon.com

PRMSC-BWN-NJN-WS-LP-03

KEY PLAN

LEGEND:

90mm Ø HDPE PIPE	
SLUICE VALVE	
WASHOUT VALVE	
AIR RELEAS VALVE	
PROPOSED STAND POST TYPE - I	
PROPOSED TUBE WELL	
BOUNDARY	

VILLAGE: NOOR JAHANIAN (BWN)

TITLE.

WATER SUPPLY SYSTEM LAYOUT PLAN-04

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	02-01-2026	DETAILED DESIGN	M.ASIF	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-NJN-WS-LP-04	04 OF 07	00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ENVIRONMENTAL MONITORING — ASIAN CONSULTING ENGINEERS — www.asiancon.com.pk

PRMSC-BWN-NJN-WS-LP-04

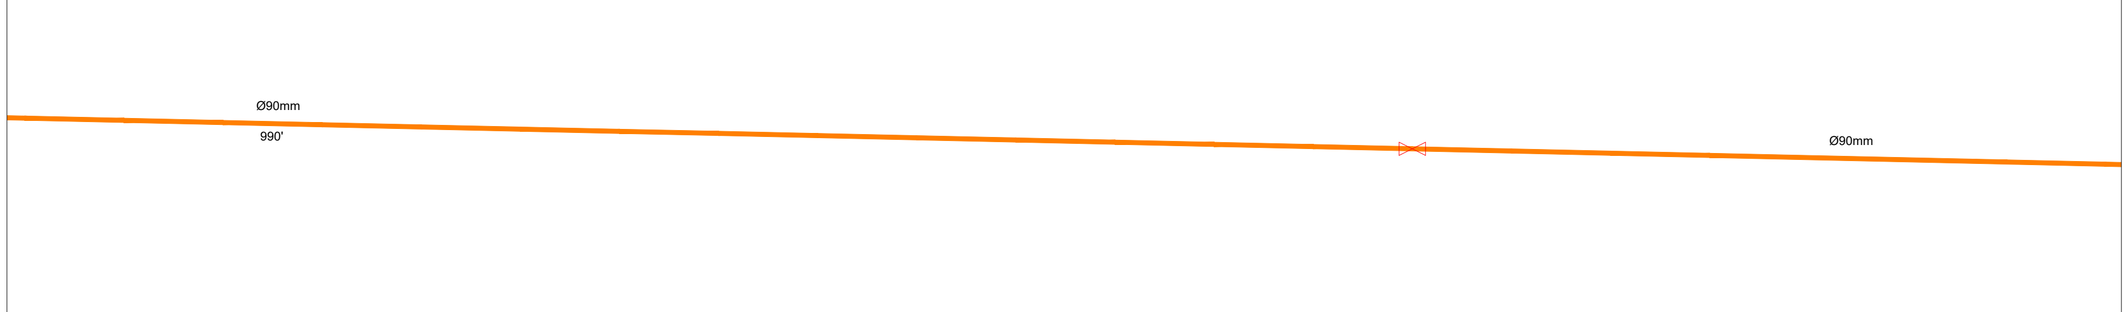



KEY PLAN

LEGEND:

- 90mm Ø HDPE PIPE
- SLUICE VALVE
- WASHOUT VALVE
- AIR RELEAS VALVE
- PROPOSED STAND POST TYPE - I
- PROPOSED TUBE WELL
- BOUNDARY

VILLAGE: NOOR JAHANIAN (BWN)

TITLE.

WATER SUPPLY SYSTEM LAYOUT PLAN-05

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	02-01-2026	DETAILED DESIGN	M.ASIF	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-NJN-WS-LP-05	05 OF 07	00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

PRMSC-BWN-NJN-WS-LP-05

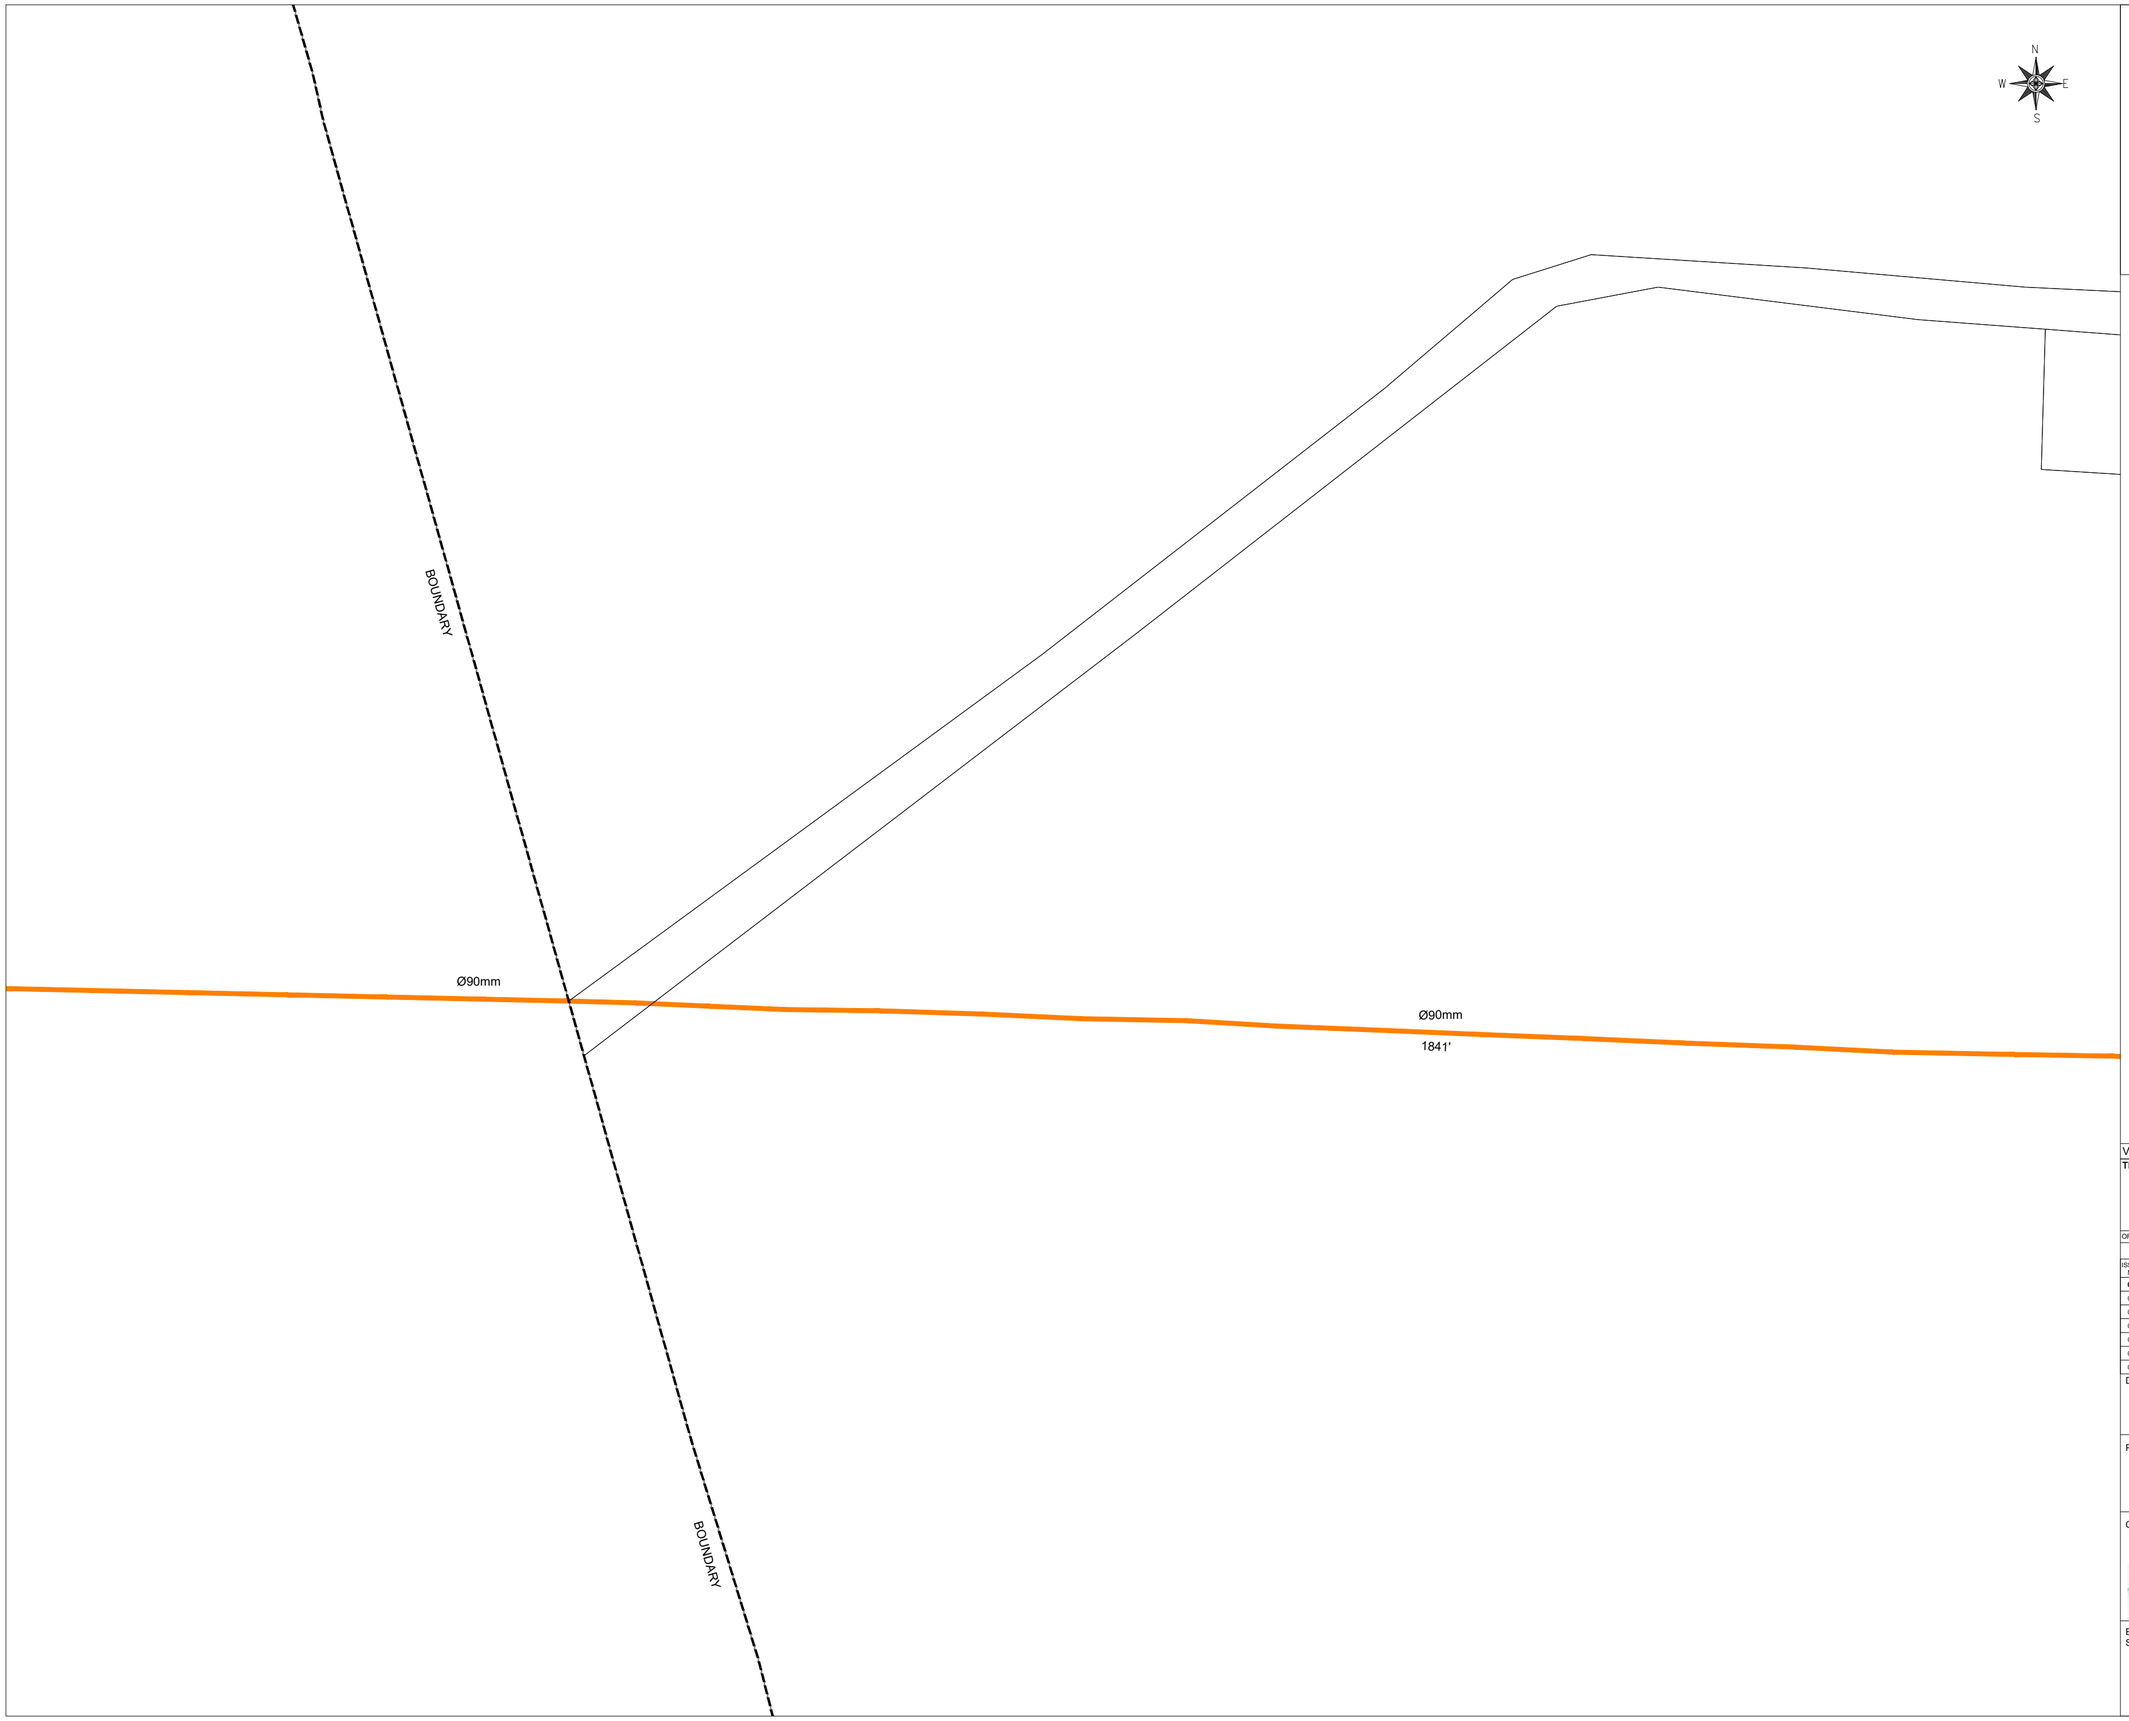

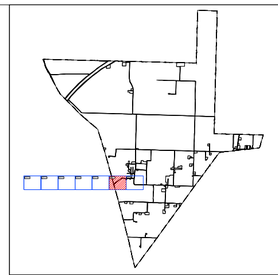

KEY PLAN

LEGEND:

- 90mm Ø HDPE PIPE
- SLUICE VALVE
- WASHOUT VALVE
- AIR RELEAS VALVE
- PROPOSED STAND POST TYPE - I
- PROPOSED TUBE WELL
- BOUNDARY

VILLAGE: NOOR JAHANIAN (BWN)

TITLE.

WATER SUPPLY SYSTEM LAYOUT PLAN-06

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	02-01-2026	DETAILED DESIGN	M.ASIF	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº: PRMSC-BWN-NJN-WS-LP-06

SHEET 06 OF 07

REV 00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:
ASIAN CONSULTING ENGINEERS
www.asianeon.com

PRMSC-BWN-NJN-WS-LP-06

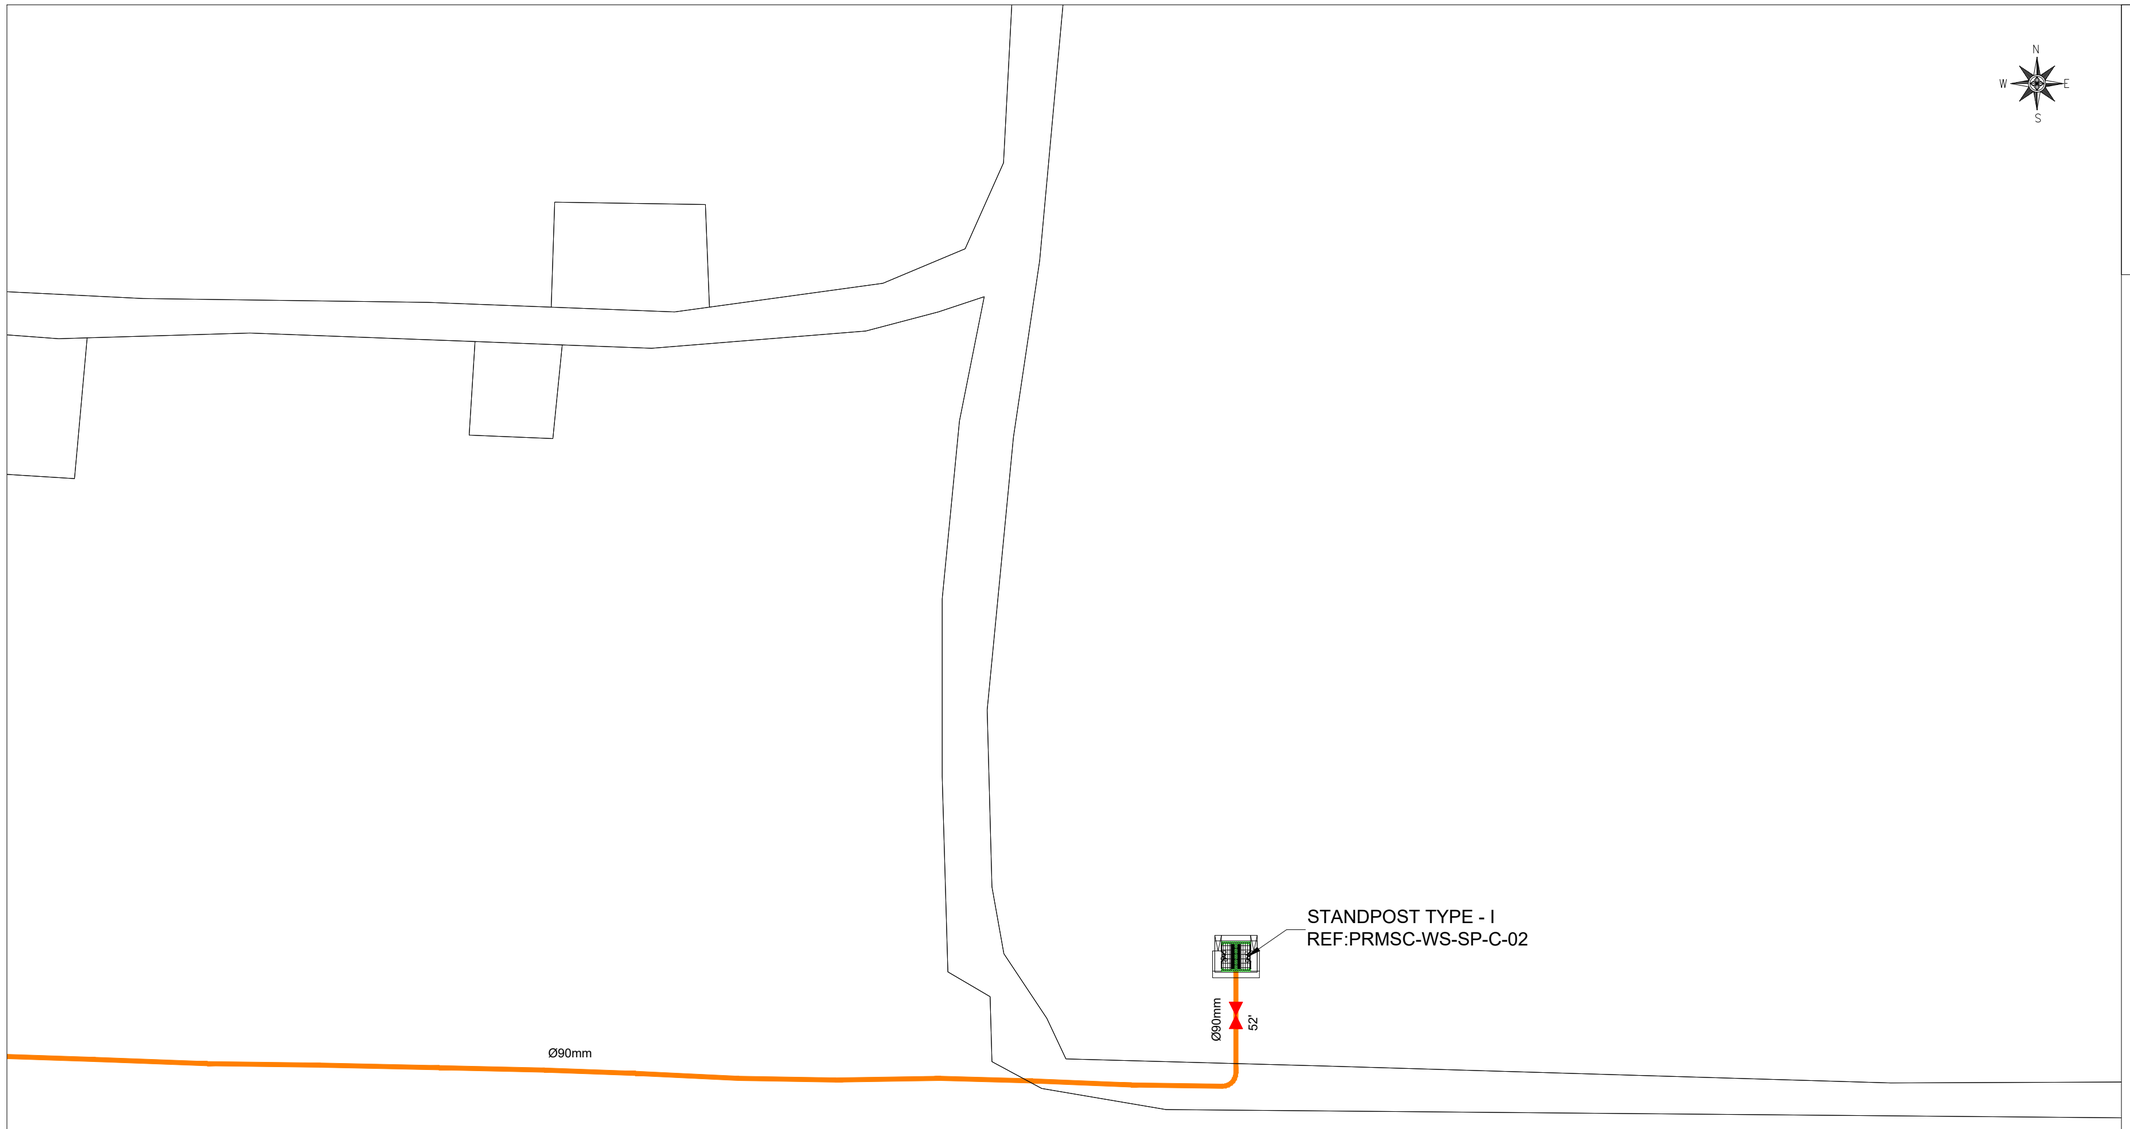

KEY PLAN

LEGEND:

- 90mm Ø HDPE PIPE
- SLUICE VALVE
- WASHOUT VALVE
- AIR RELEAS VALVE
- PROPOSED STAND POST TYPE - I
- PROPOSED TUBE WELL
- BOUNDARY

VILLAGE: NOOR JAHANIAN (BWN)

TITLE.

WATER SUPPLY SYSTEM LAYOUT PLAN-07

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	02-01-2026	DETAILED DESIGN	M.ASIF	ENGR. FAIEZ	ENGR. HSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-NJN-WS-LP-07	07 OF 07	00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:
ASIAN CONSULTING ENGINEERS
www.asianconsultingengineers.com

PRMSC-BWN-NJN-WS-LP-07

RAMNAGAR

KEY PLAN

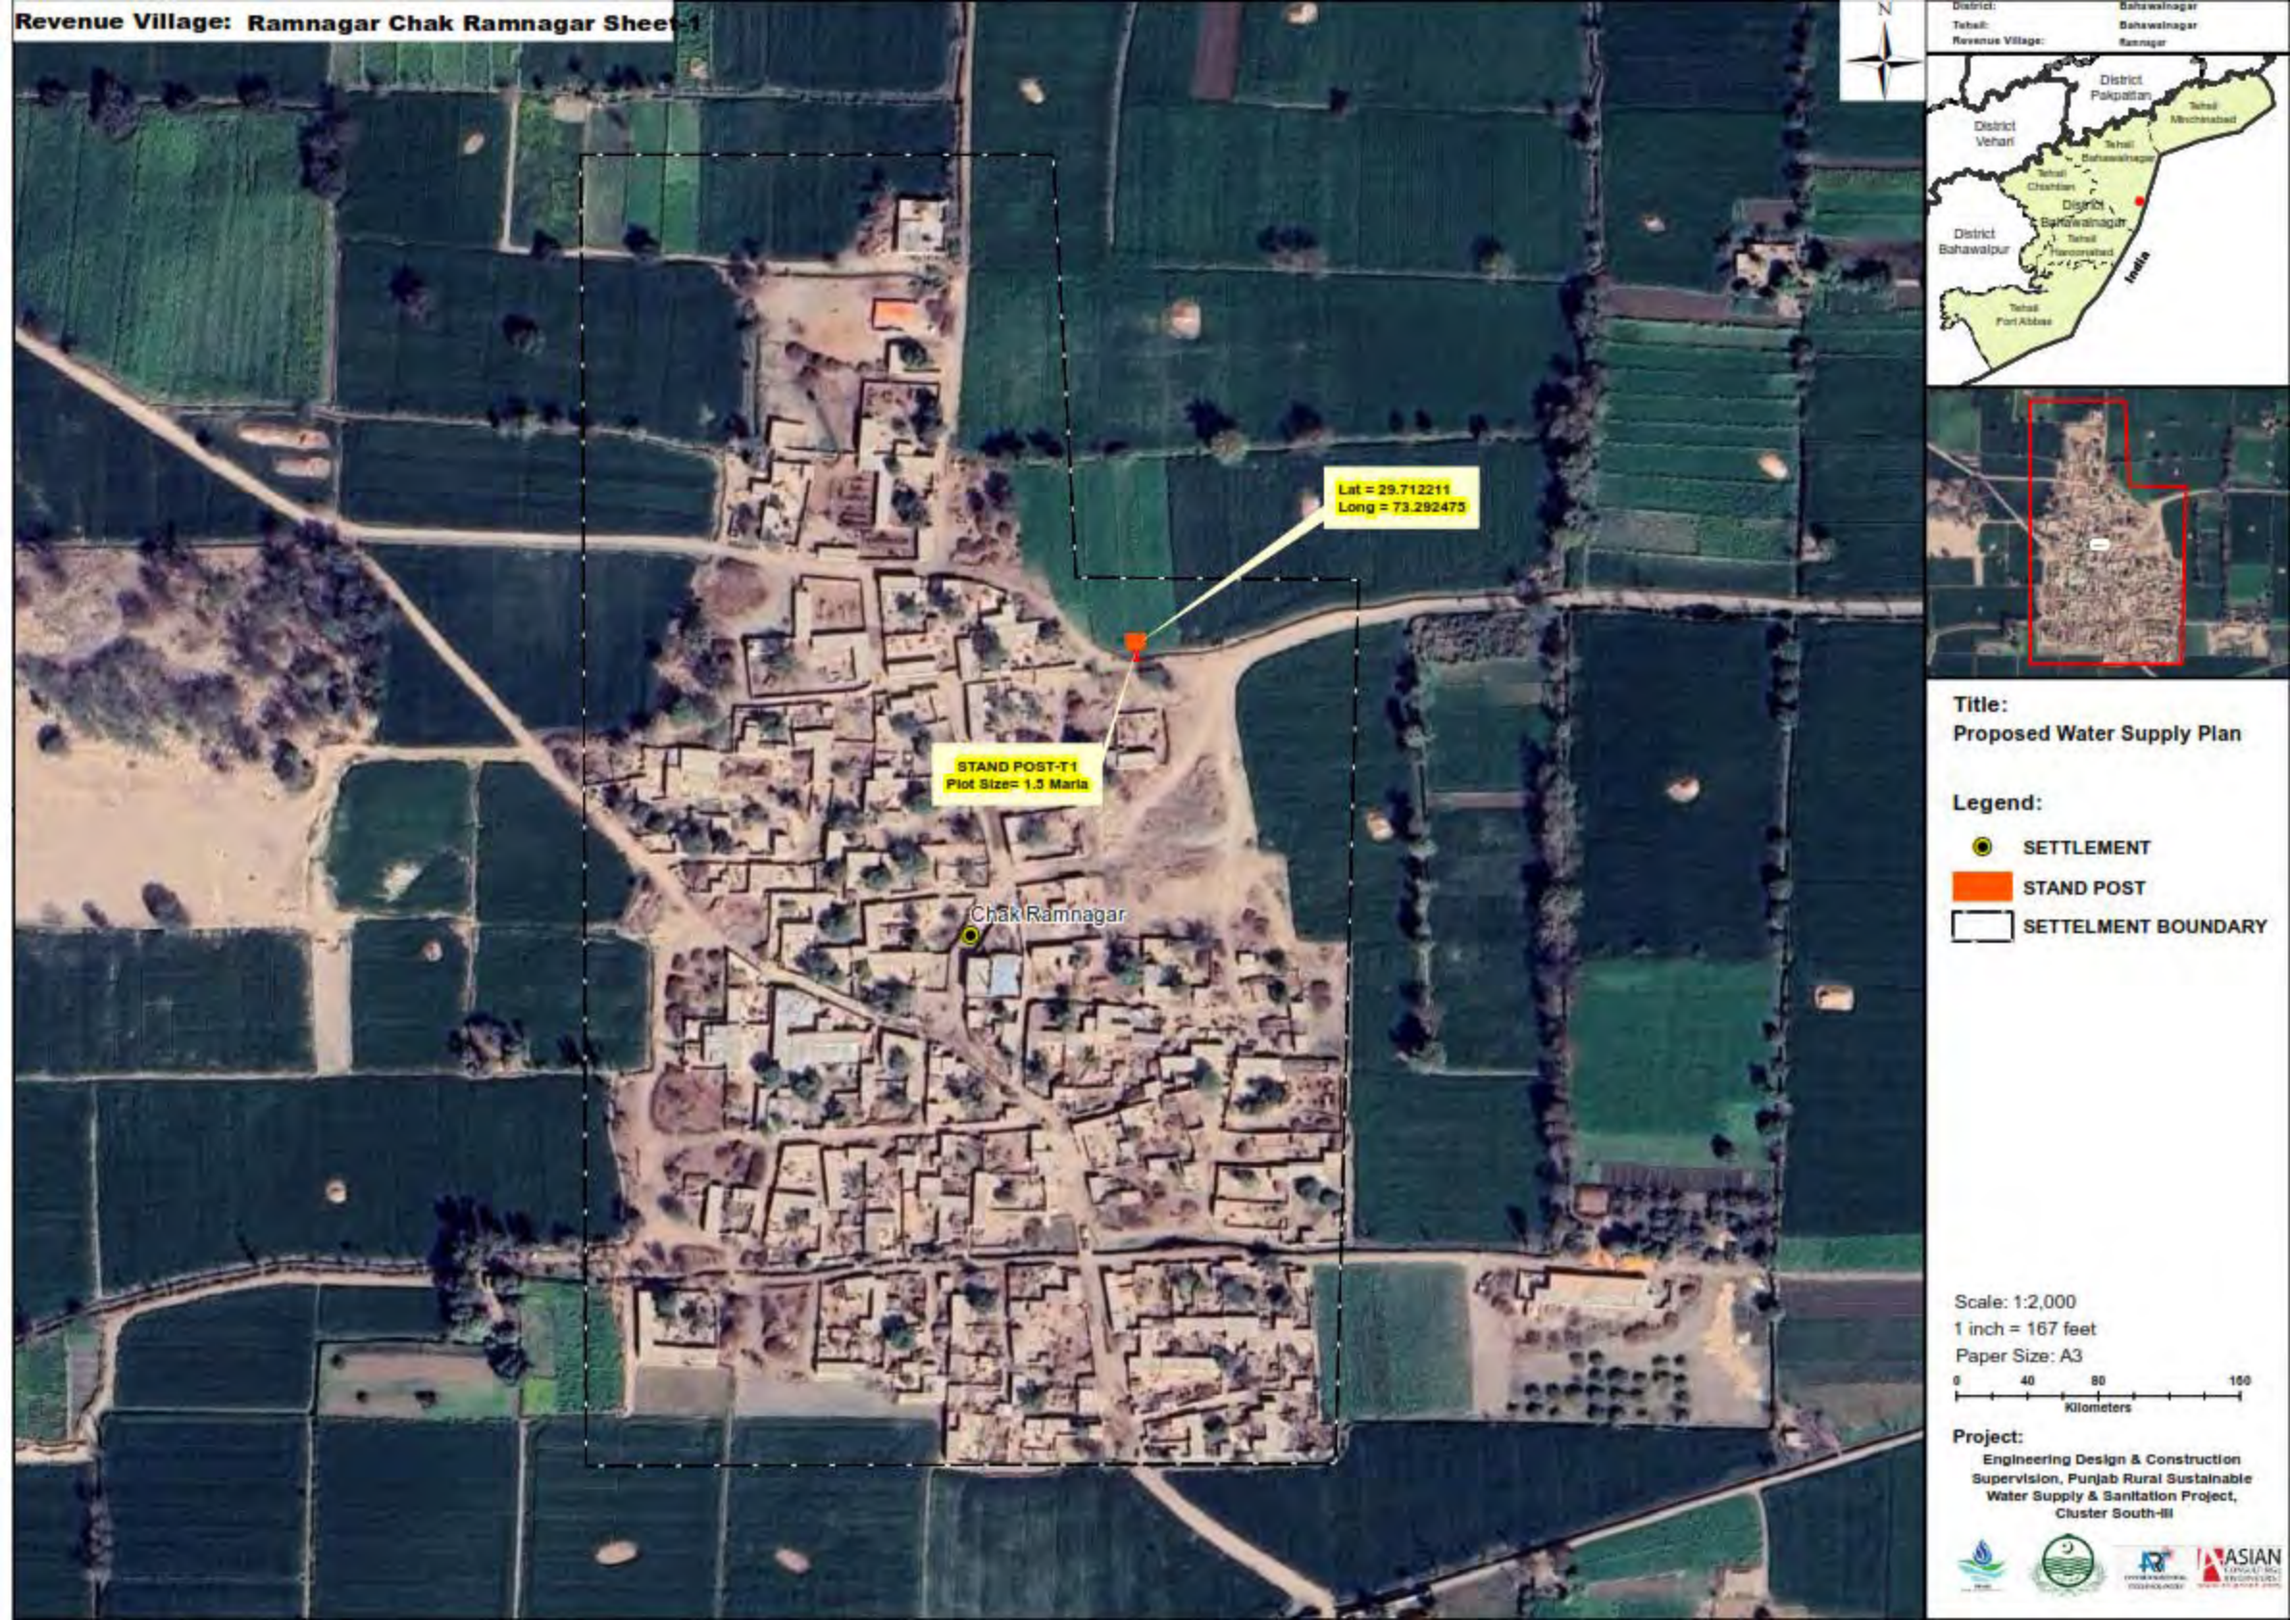
Revenue Village: Ramnagar Chak Ramnagar Sheet-1
Lat = 29.712211
Long = 73.292475
STAND POST-T1
Plot Size= 1.5 Marla
Chak Ramnagar
N
District:
Tehsil:
Revenue Village:
Bahawalnagar
Bahawalnagar
Ramnagar
District Pakpattan
Tehsil Minchinabad
District Vehari
Tehsil Bahawalnagar
Tehsil Chishtian
District Bahawalnagar
District Bahawalpur
Tehsil Haroonabad
Tehsil Fort Abbas
India
Title:
Proposed Water Supply Plan
Legend:
SETTLEMENT
STAND POST
SETTELMENT BOUNDARY
Scale: 1:2,000
1 inch = 167 feet
Paper Size: A3
0
40
80
160
Kilometers
Project:
Engineering Design & Construction Supervision, Punjab Rural Sustainable Water Supply & Sanitation Project, Cluster South-III

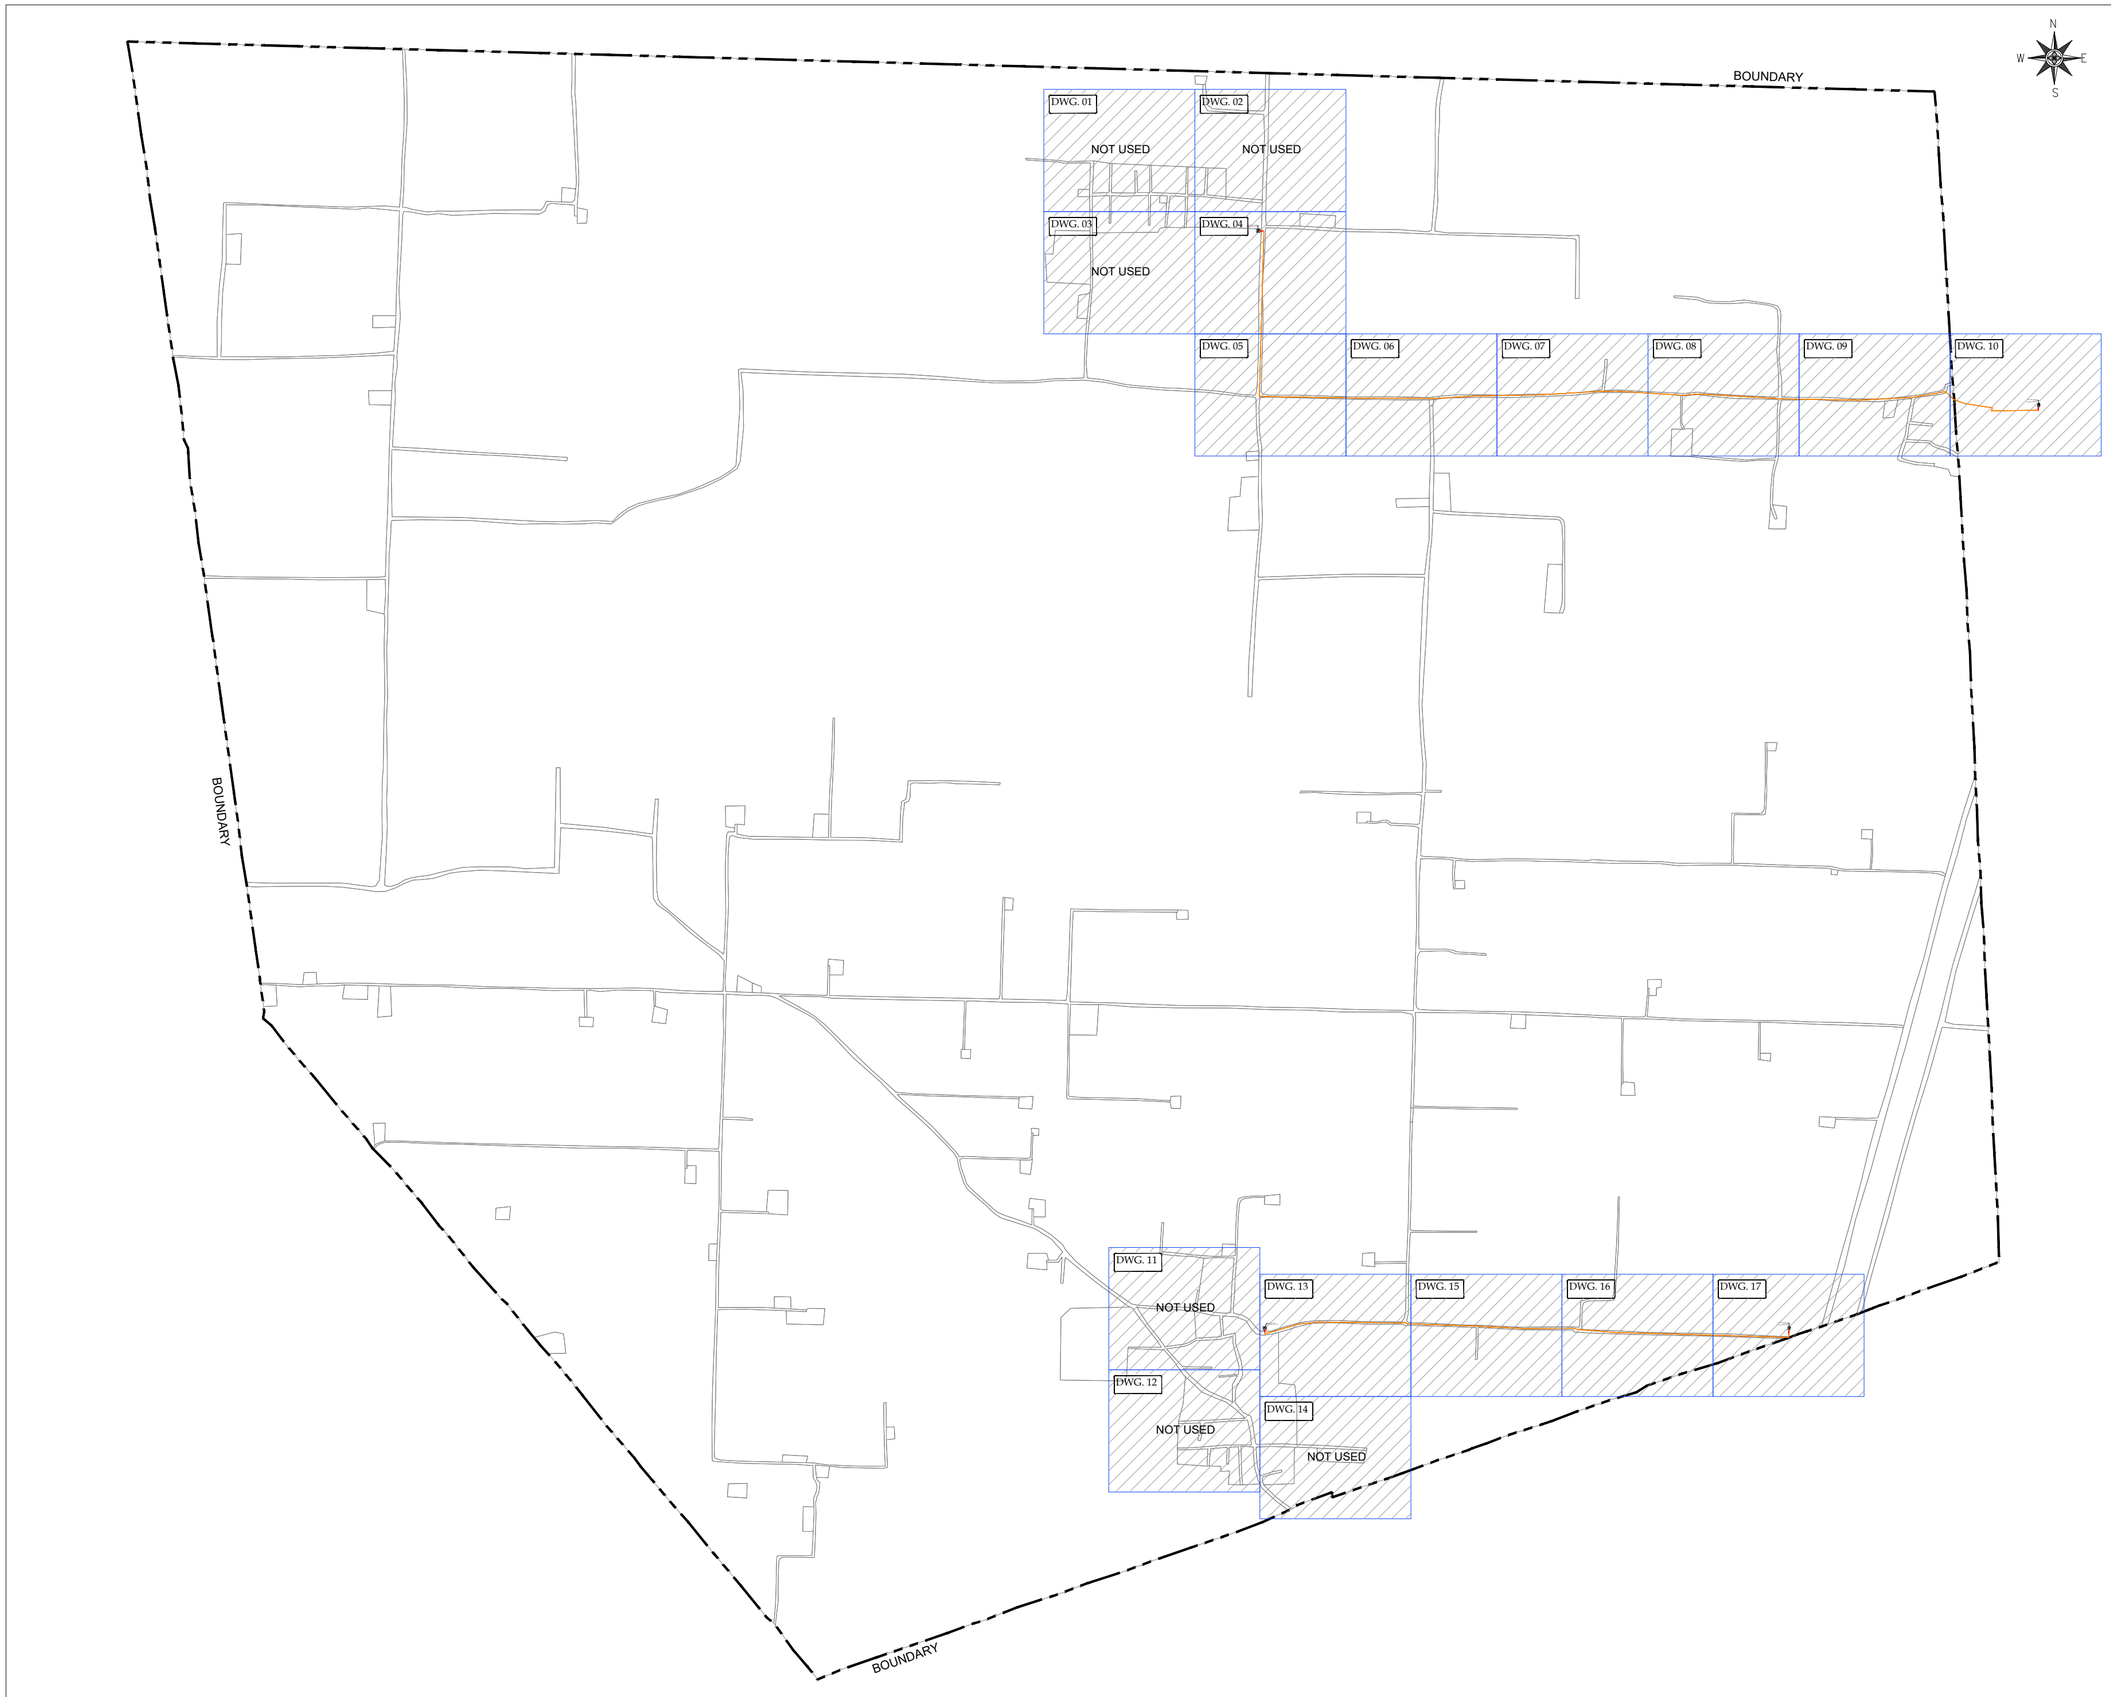

LEGEND:

- 90mm Ø HDPE PIPE
- SLUICE VALVE
- PROPOSED TUBE WELL
- STAND POST TYPE - I
- BOUNDARY

VILLAGE: RAMNAGAR (BWN)

TITLE.

WATER SUPPLY SYSTEM KEY PLAN

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 700'

ISSUE N°	DATE	D E S C R I P T I O N	DRAWN	DESIGNED	APPROVED
01	24-12-2025	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-RMG-WS-KP-00	00 OF 00	00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT
ASIAN CONSULTING ENGINEERS
www.asiancon.com IV

PRMSC-BWN-BIB-SEW-KP-00

LAYOUT PLANS

Revenue Village: Ramnagar Nai Abadi Sheet-1
Nai Abadi
Lat = 29.731382
Long = 73.29201
STAND POST-T1
Plot Size= 1.5 Marla
District:
Bahawalnagar
Tehsil:
Bahawalnagar
Revenue Village:
Ramnagar
District Pakpattan
Tehsil Minchinabad
District Vehari
Tehsil Bahawalnagar
Tehsil Chishtian
District Bahawalnagar
District Bahawalpur
Tehsil Haroonabad
India
Tehsil Fort Abbas
Title:
Proposed Water Supply Plan
Legend:
SETTLEMENT
STAND POST
SETTELMENT BOUNDARY
Scale: 1:1,700
1 inch = 142 feet
Paper Size: A3
0
40
80
160
Kilometers
Project:
Engineering Design & Construction Supervision, Punjab Rural Sustainable Water Supply & Sanitation Project, Cluster South-III

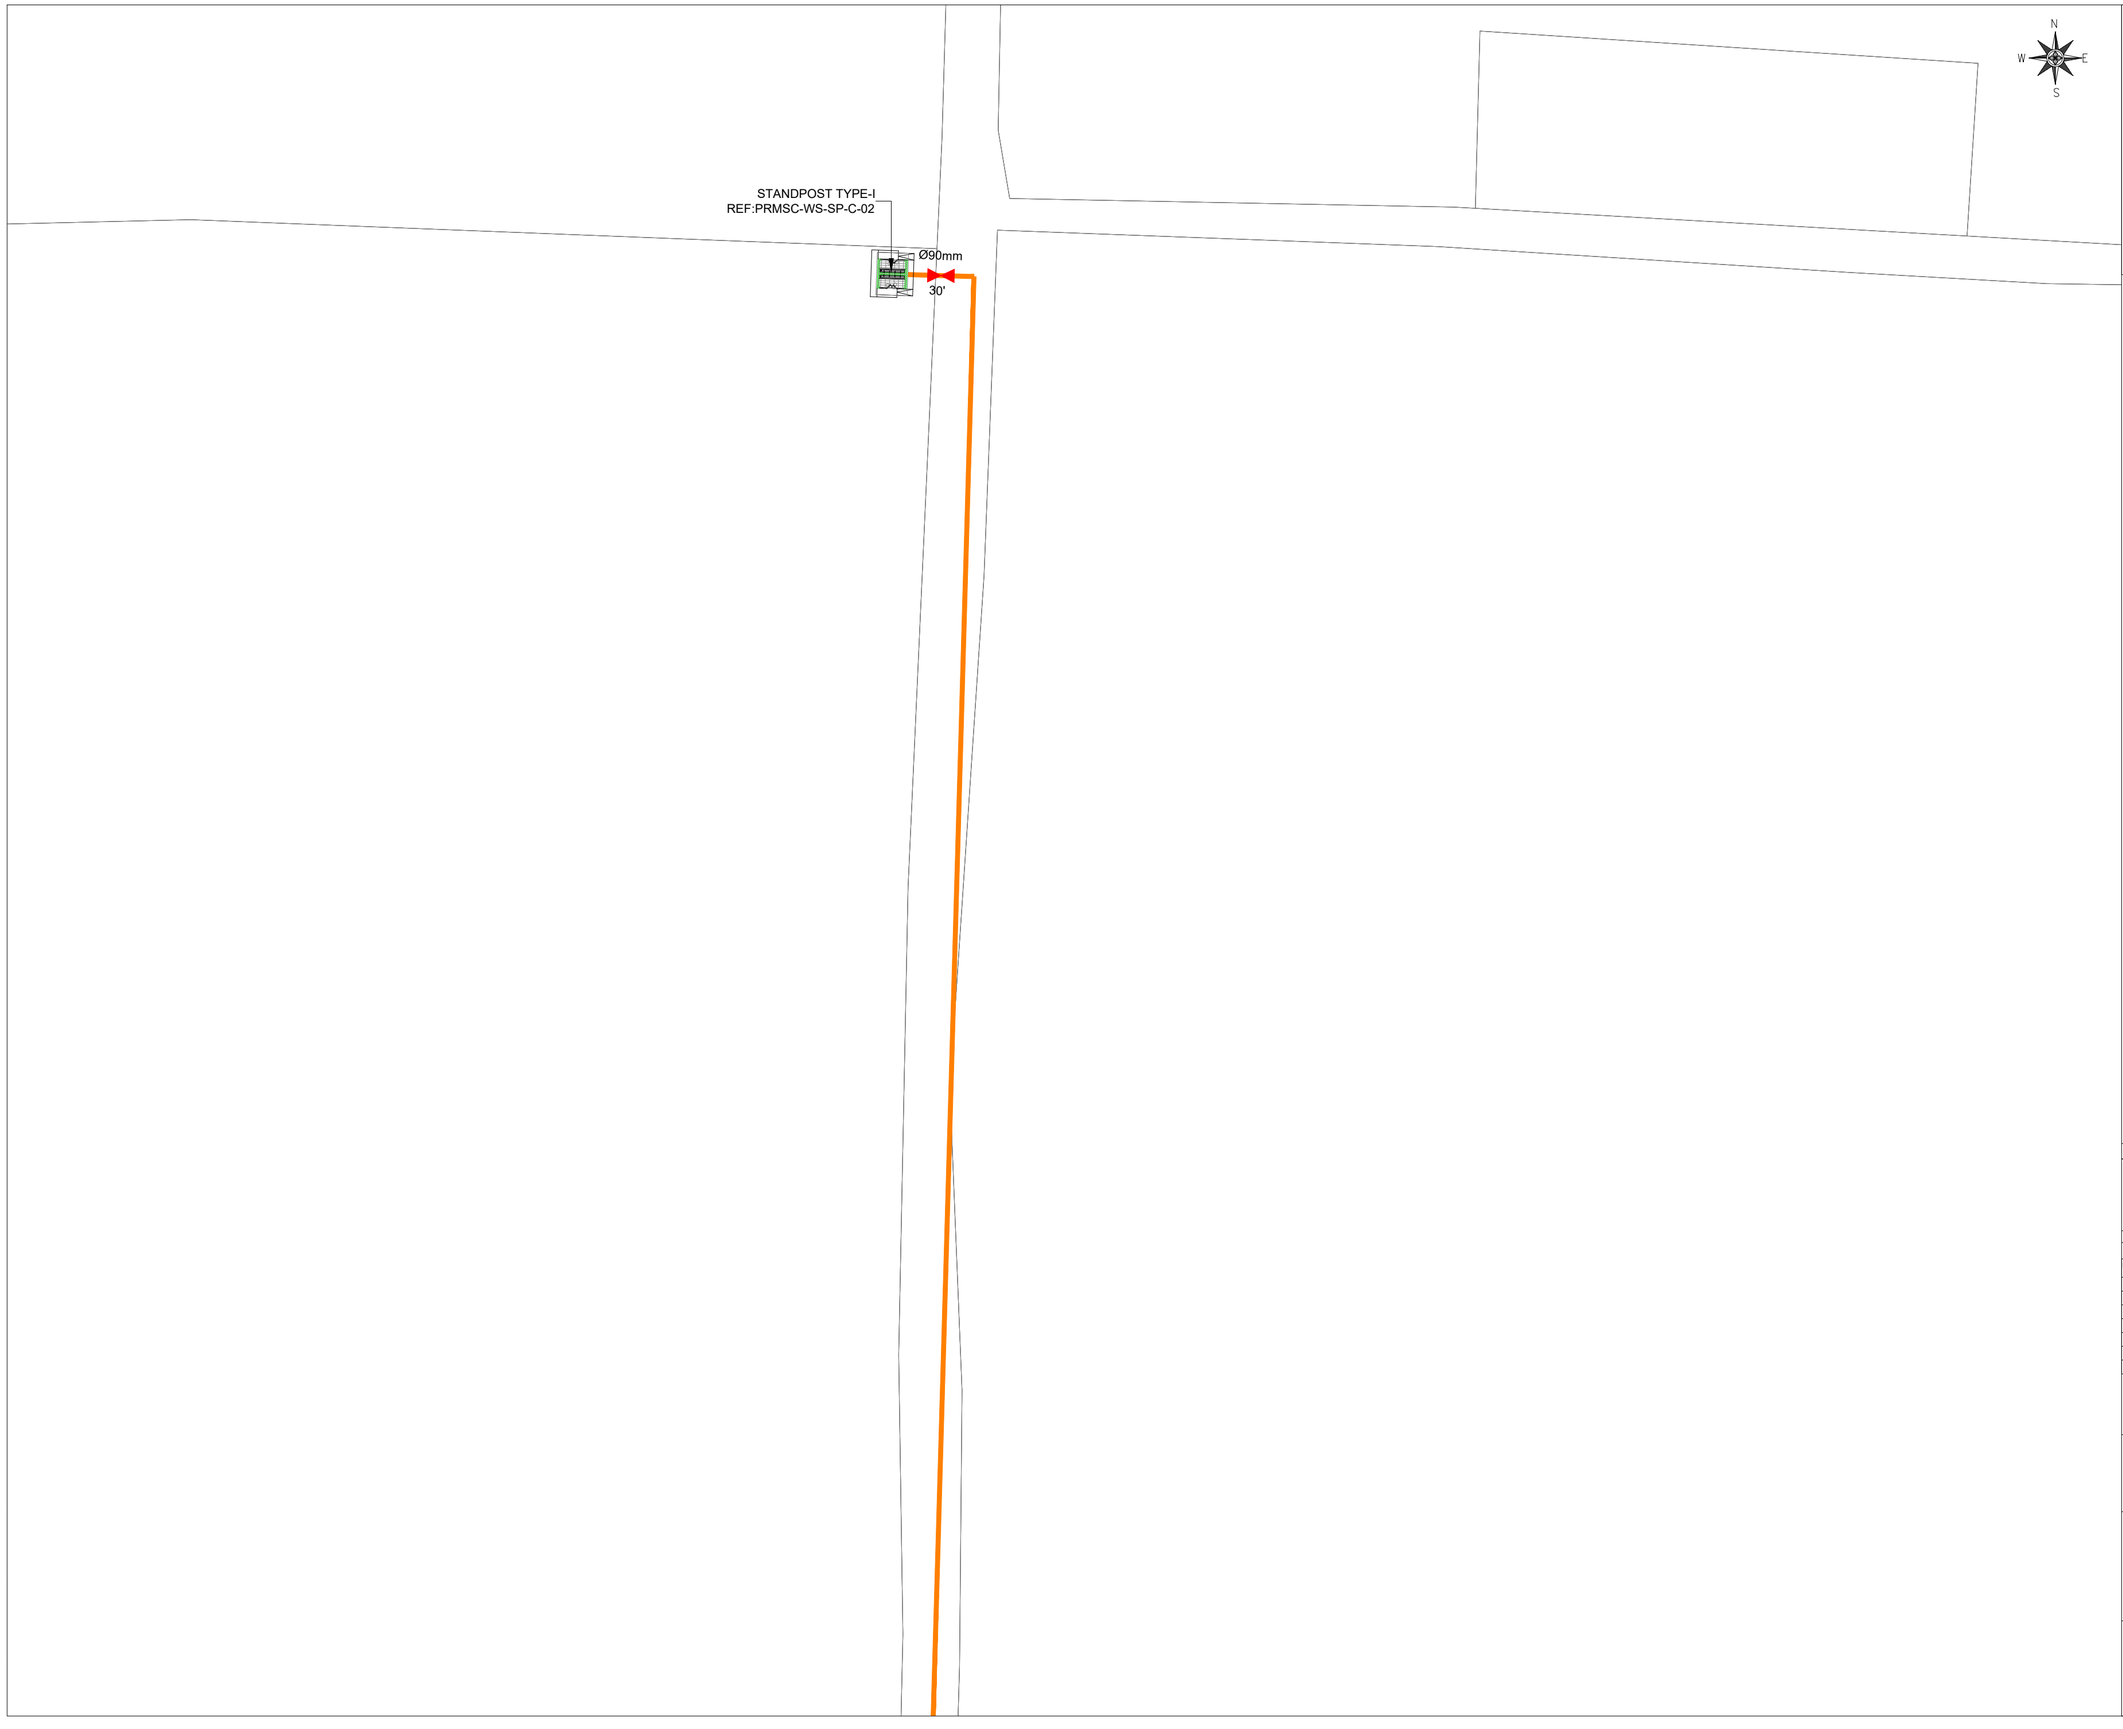

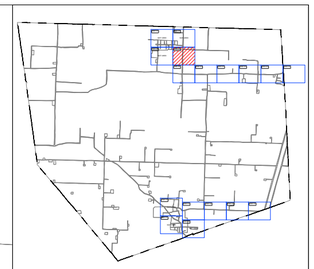

KEY PLAN

LEGEND:

90mm Ø HDPE PIPE

SLUICE VALVE

PROPOSED TUBE WELL

STAND POST TYPE - I

BOUNDARY

VILLAGE: RAMNAGAR (BWN)

TITLE.

WATER SUPPLY SYSTEM LAYOUT PLAN-04

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	D E S C R I P T I O N	DRAWN	DESIGNED	APPROVED
01	24-12-2025	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-RMG-WS-LP-04	04 OF 17	00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:
ASIAN CONSULTING ENGINEERS
www.asianeon.com

PRMSC-BWN-RMG-WS-LP-04

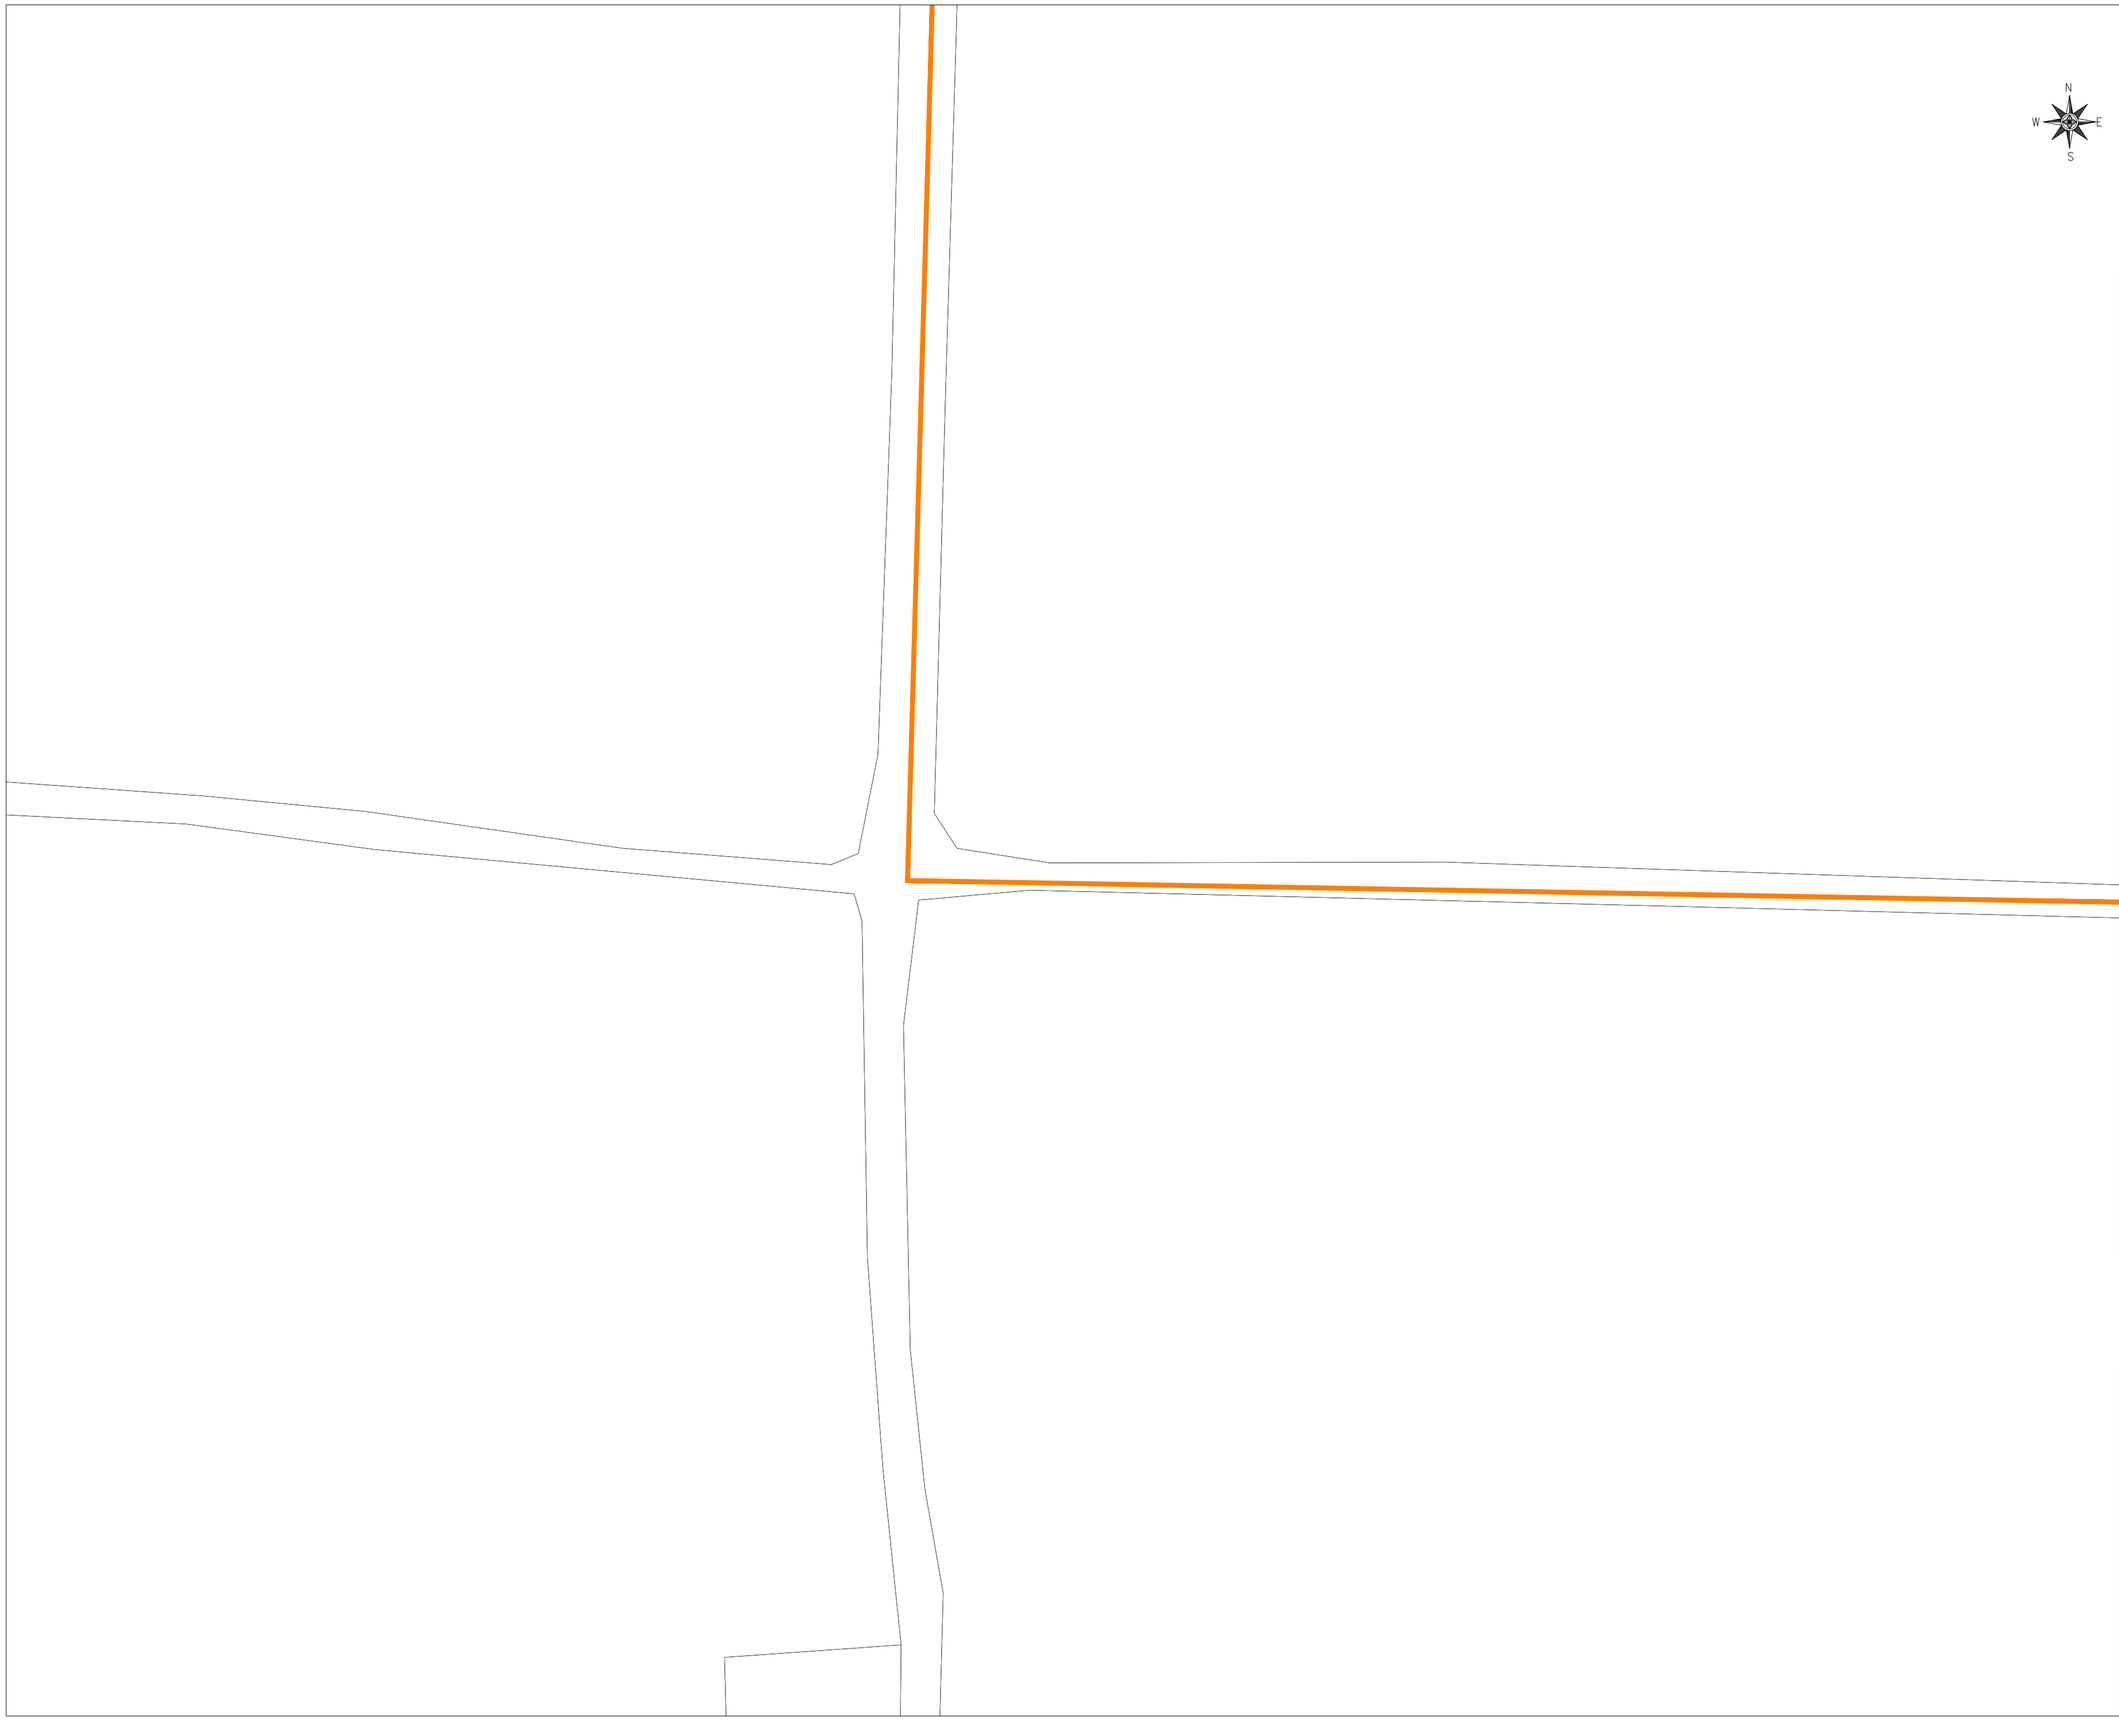

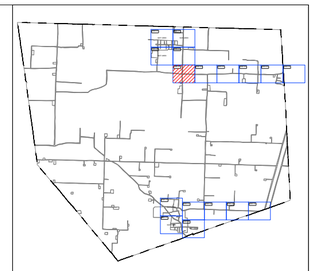

KEY PLAN

LEGEND:

90mm Ø HDPE PIPE

SLUICE VALVE

PROPOSED TUBE WELL

STAND POST TYPE - I

BOUNDARY

VILLAGE: RAMNAGAR (BWN)

TITLE.

WATER SUPPLY SYSTEM LAYOUT PLAN-05

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	D E S C R I P T I O N	DRAWN	DESIGNED	APPROVED
01	24-12-2025	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-RMG-WS-LP-05	05 OF 17	00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:
ASIAN CONSULTING ENGINEERS
www.asianeon.com

PRMSC-BWN-RMG-WS-LP-05

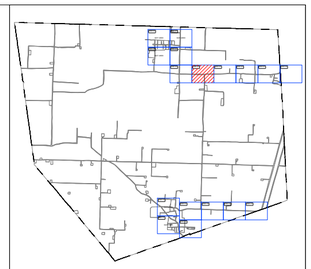

KEY PLAN

LEGEND:

90mm Ø HDPE PIPE

SLUICE VALVE

PROPOSED TUBE WELL

STAND POST TYPE - I

BOUNDARY

VILLAGE: RAMNAGAR (BWN)

TITLE.

WATER SUPPLY SYSTEM LAYOUT PLAN-06

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	24-12-2025	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-RMG-WS-LP-06	06 OF 17	00

PROJECT:

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ENVIRONMENTAL TECHNOLOGISTS

ASIAN CONSULTING ENGINEERS (PVT) LTD. www.asiancon.com.pk

PRMSC-BWN-RMG-WS-LP-06

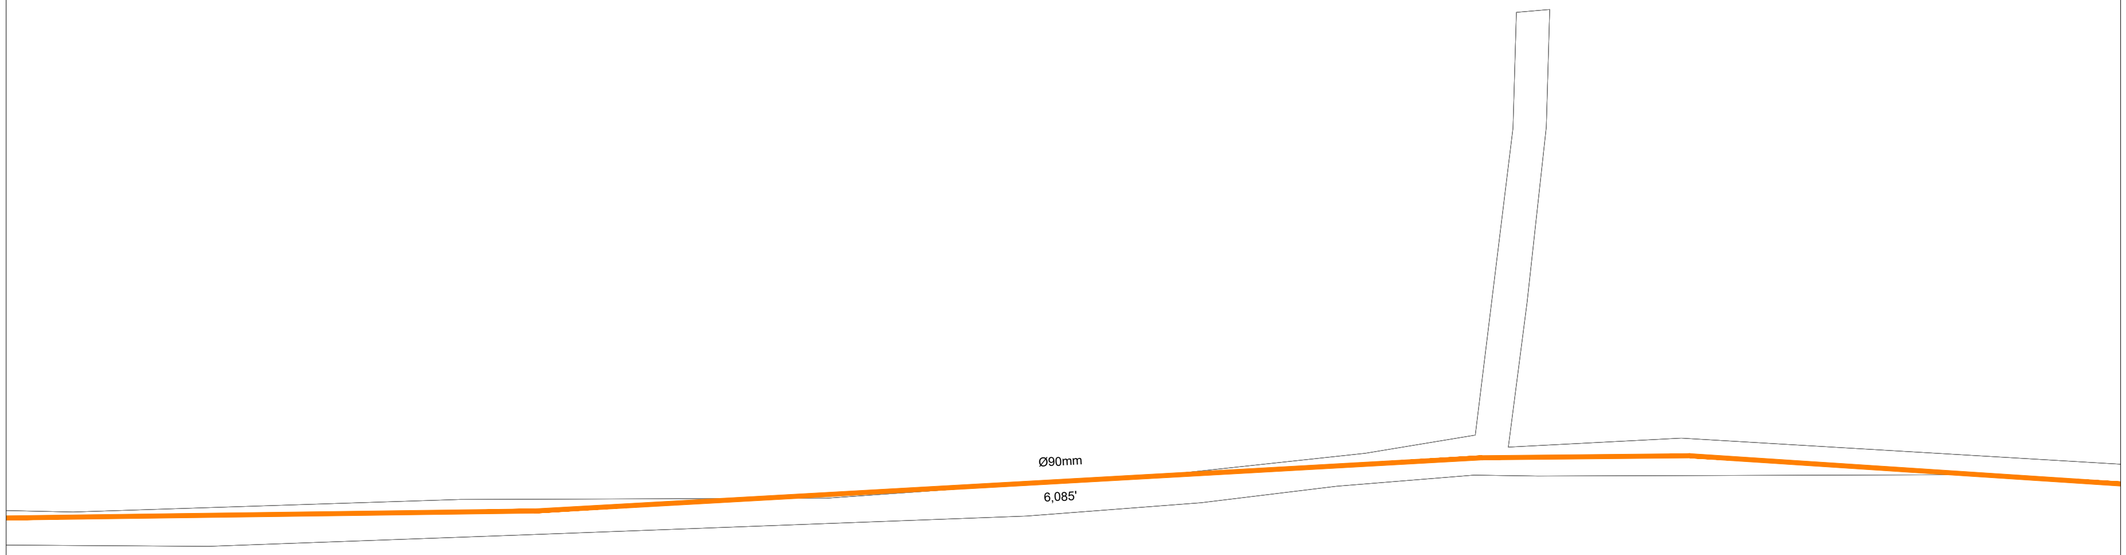

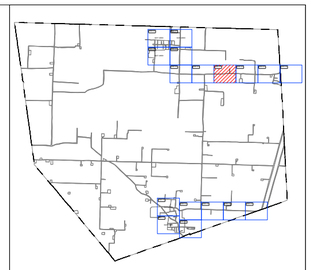

KEY PLAN

LEGEND:

90mm Ø HDPE PIPE

SLUICE VALVE

PROPOSED TUBE WELL

STAND POST TYPE - I

BOUNDARY

VILLAGE: RAMNAGAR (BWN)

TITLE.

WATER SUPPLY SYSTEM LAYOUT PLAN-07

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	D E S C R I P T I O N	DRAWN	DESIGNED	APPROVED
01	24-12-2025	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-RMG-WS-LP-07	07 OF 17	00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS (PVT) LTD. www.asiancon.com.pk

PRMSC-BWN-RMG-WS-LP-07

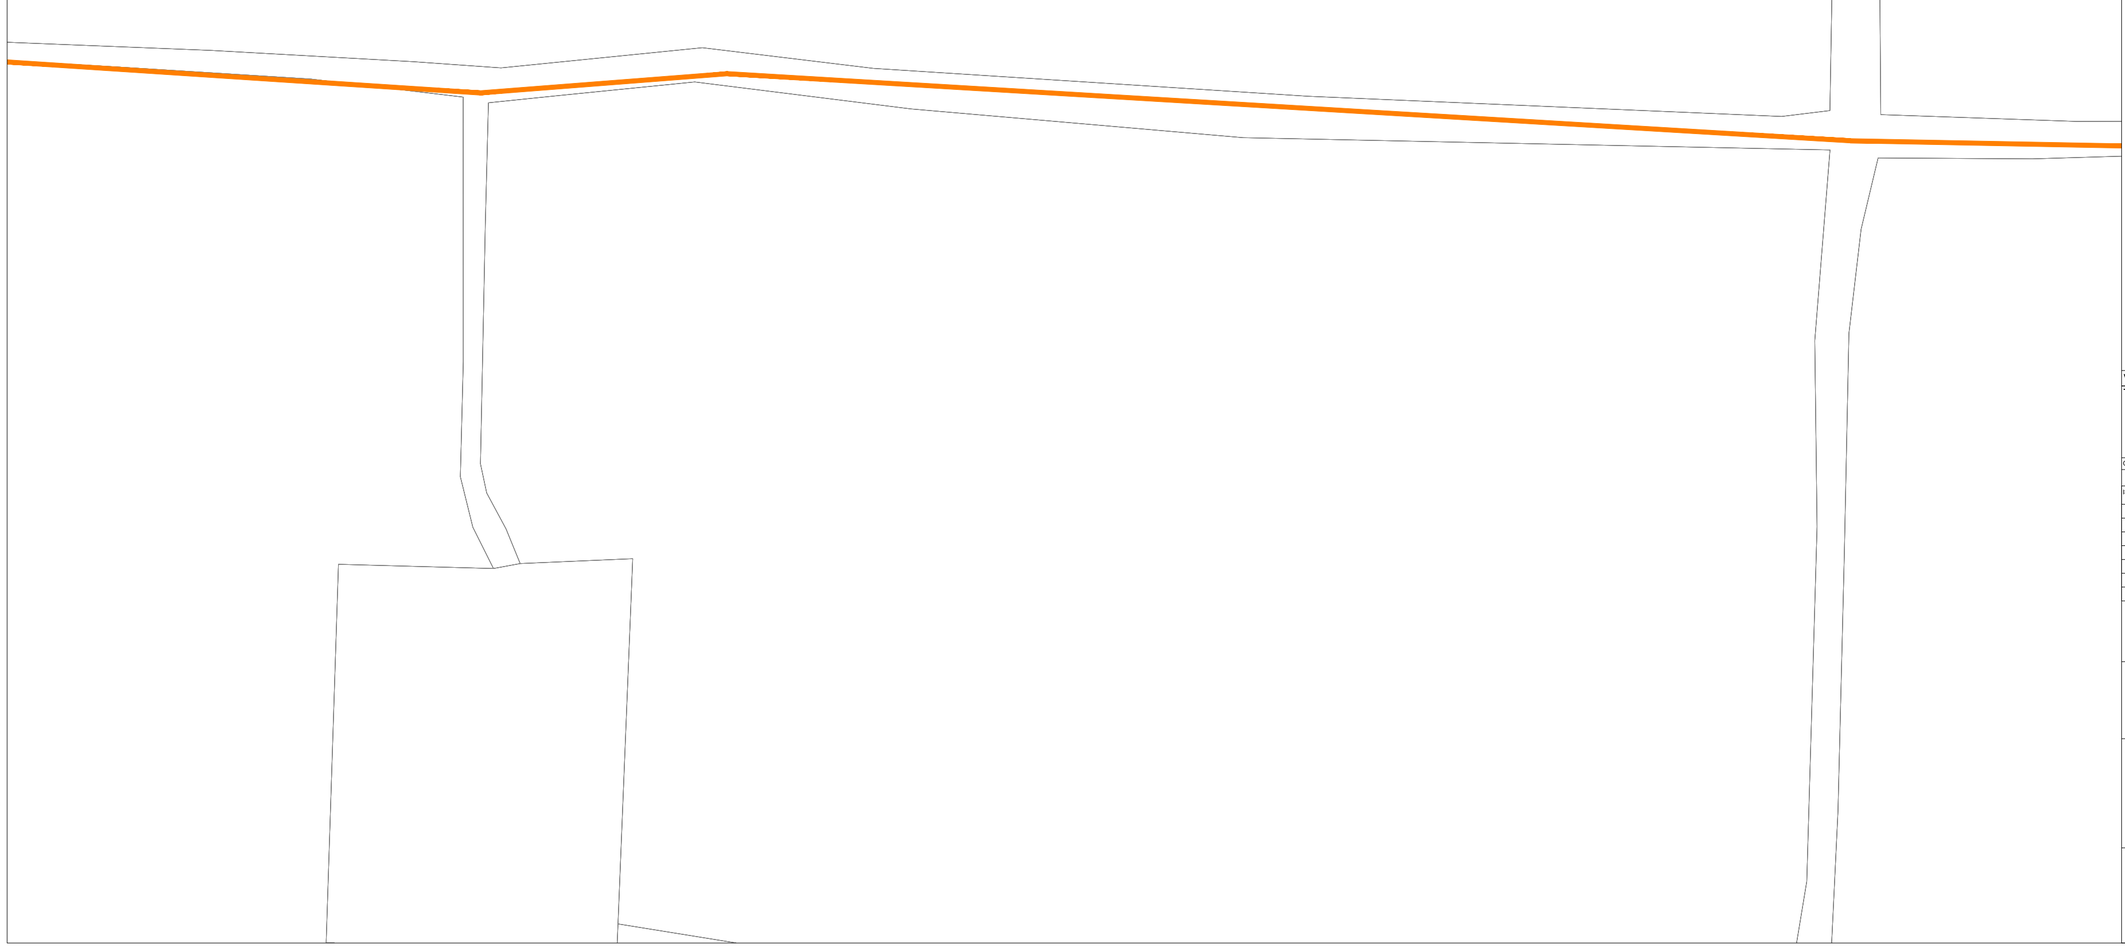

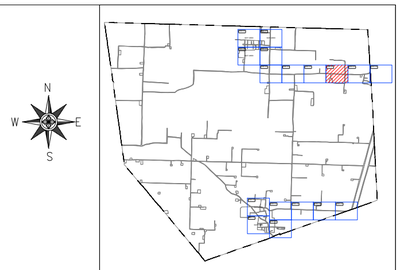

KEY PLAN

LEGEND:

90mm Ø HDPE PIPE

SLUICE VALVE

PROPOSED TUBE WELL

STAND POST TYPE - I

BOUNDARY

VILLAGE: RAMNAGAR (BWN)

TITLE.

WATER SUPPLY SYSTEM LAYOUT PLAN-08

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	D E S C R I P T I O N	DRAWN	DESIGNED	APPROVED
01	24-12-2025	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-RMG-WS-LP-08	08 OF 17	00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

PRMSC-BWN-RMG-WS-LP-08

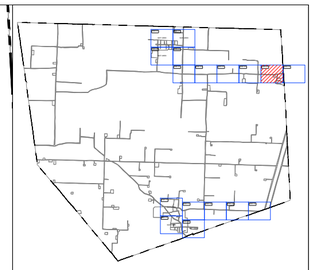

KEY PLAN

LEGEND:

90mm Ø HDPE PIPE

SLUICE VALVE

PROPOSED TUBE WELL

STAND POST TYPE - I

BOUNDARY

VILLAGE: RAMNAGAR (BWN)

TITLE.

WATER SUPPLY SYSTEM LAYOUT PLAN-09

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	D E S C R I P T I O N	DRAWN	DESIGNED	APPROVED
01	24-12-2025	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. HSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-RMG-WS-LP-09	09 OF 17	00

PROJECT:

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS www.asiancon.com.pk

PRMSC-BWN-RMG-WS-LP-09

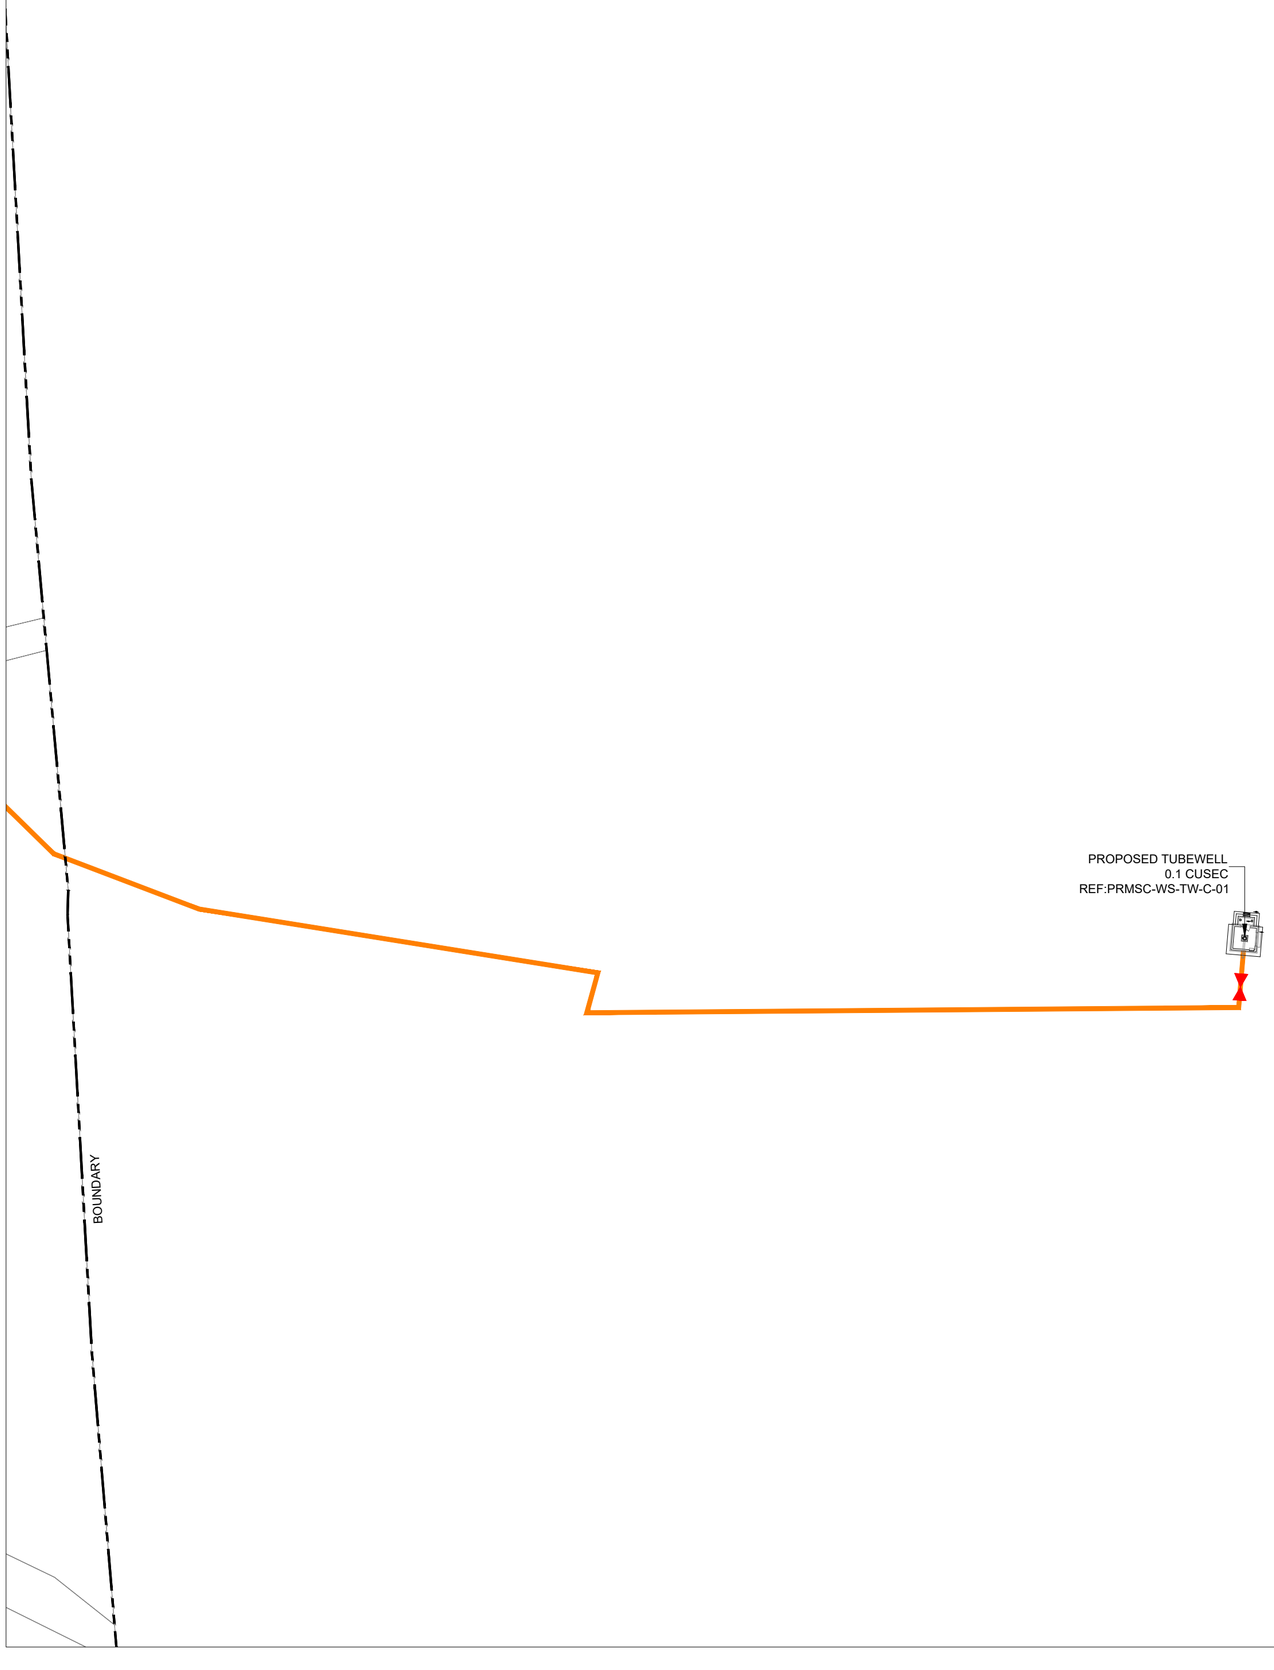

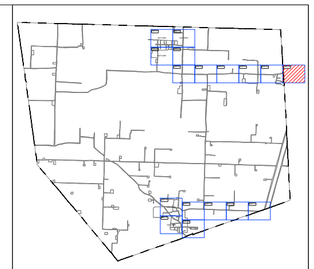

KEY PLAN

LEGEND:

90mm Ø HDPE PIPE

SLUICE VALVE

PROPOSED TUBE WELL

STAND POST TYPE - I

BOUNDARY

VILLAGE: RAMNAGAR (BWN)

TITLE.

WATER SUPPLY SYSTEM LAYOUT PLAN-10

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	24-12-2025	DETAILED DESIGN	MUNEEB	ENGR FAIEZ	ENGR IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-RMG-WS-LP-10	10 OF 17	00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

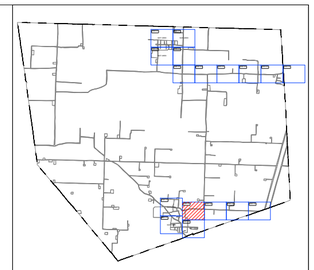

KEY PLAN

LEGEND:

90mm Ø HDPE PIPE

SLUICE VALVE

PROPOSED TUBE WELL

STAND POST TYPE - I

BOUNDARY

VILLAGE: RAMNAGAR (BWN)

TITLE.

WATER SUPPLY SYSTEM LAYOUT PLAN-13

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	D E S C R I P T I O N	DRAWN	DESIGNED	APPROVED
01	24-12-2025	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-RMG-WS-LP-13	13 OF 17	00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ENVIRONMENTAL TECHNOLOGIES
ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

PRMSC-BWN-RMG-WS-LP-13

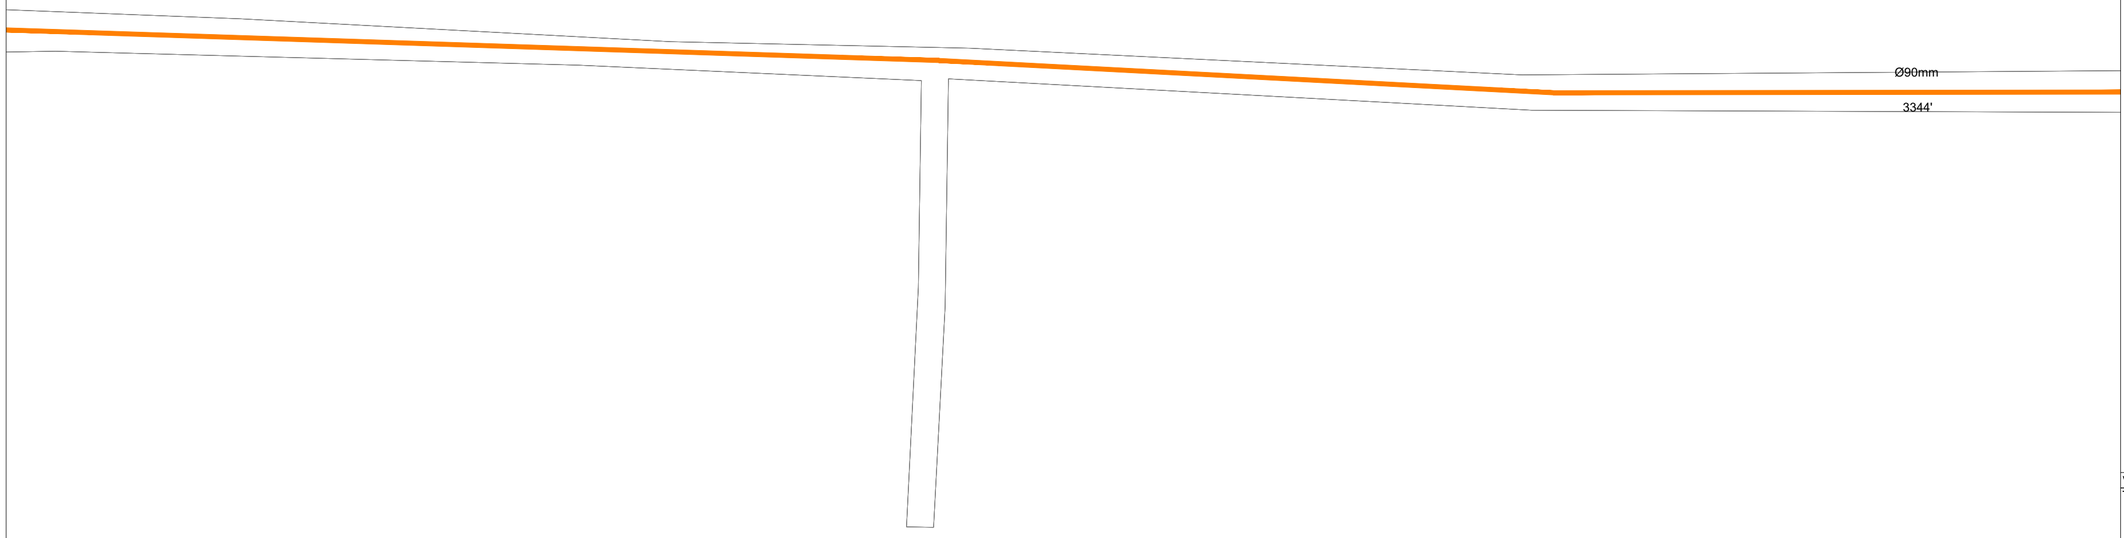

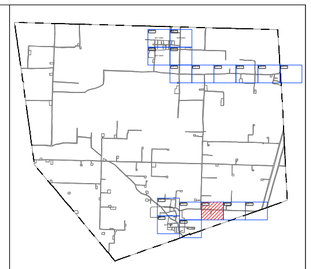

KEY PLAN

LEGEND:

90mm Ø HDPE PIPE

SLUICE VALVE

PROPOSED TUBE WELL

STAND POST TYPE - I

BOUNDARY

VILLAGE: RAMNAGAR (BWN)

TITLE.

WATER SUPPLY SYSTEM LAYOUT PLAN-15

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°.	DATE	D E S C R I P T I O N	DRAWN	DESIGNED	APPROVED
01	24-12-2025	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-RMG-WS-LP-15	15 OF 17	00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ENVIRONMENTAL TECHNOLOGIES
ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

PRMSC-BWN-RMG-WS-LP-15

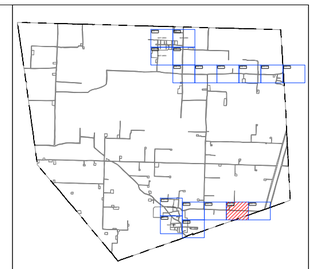

KEY PLAN

LEGEND:

- 90mm Ø HDPE PIPE
- SLUICE VALVE
- PROPOSED TUBE WELL
- STAND POST TYPE - I
- BOUNDARY

VILLAGE: RAMNAGAR (BWN)

TITLE.

WATER SUPPLY SYSTEM LAYOUT PLAN-16

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	D E S C R I P T I O N	DRAWN	DESIGNED	APPROVED
01	24-12-2025	DETAILED DESIGN	MUNEEB	ENGR FAIEZ	ENGR IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-RMG-WS-LP-16	16 OF 17	00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:
ASIAN CONSULTING ENGINEERS JV
www.asiancon.com

PRMSC-BWN-RMG-WS-LP-16

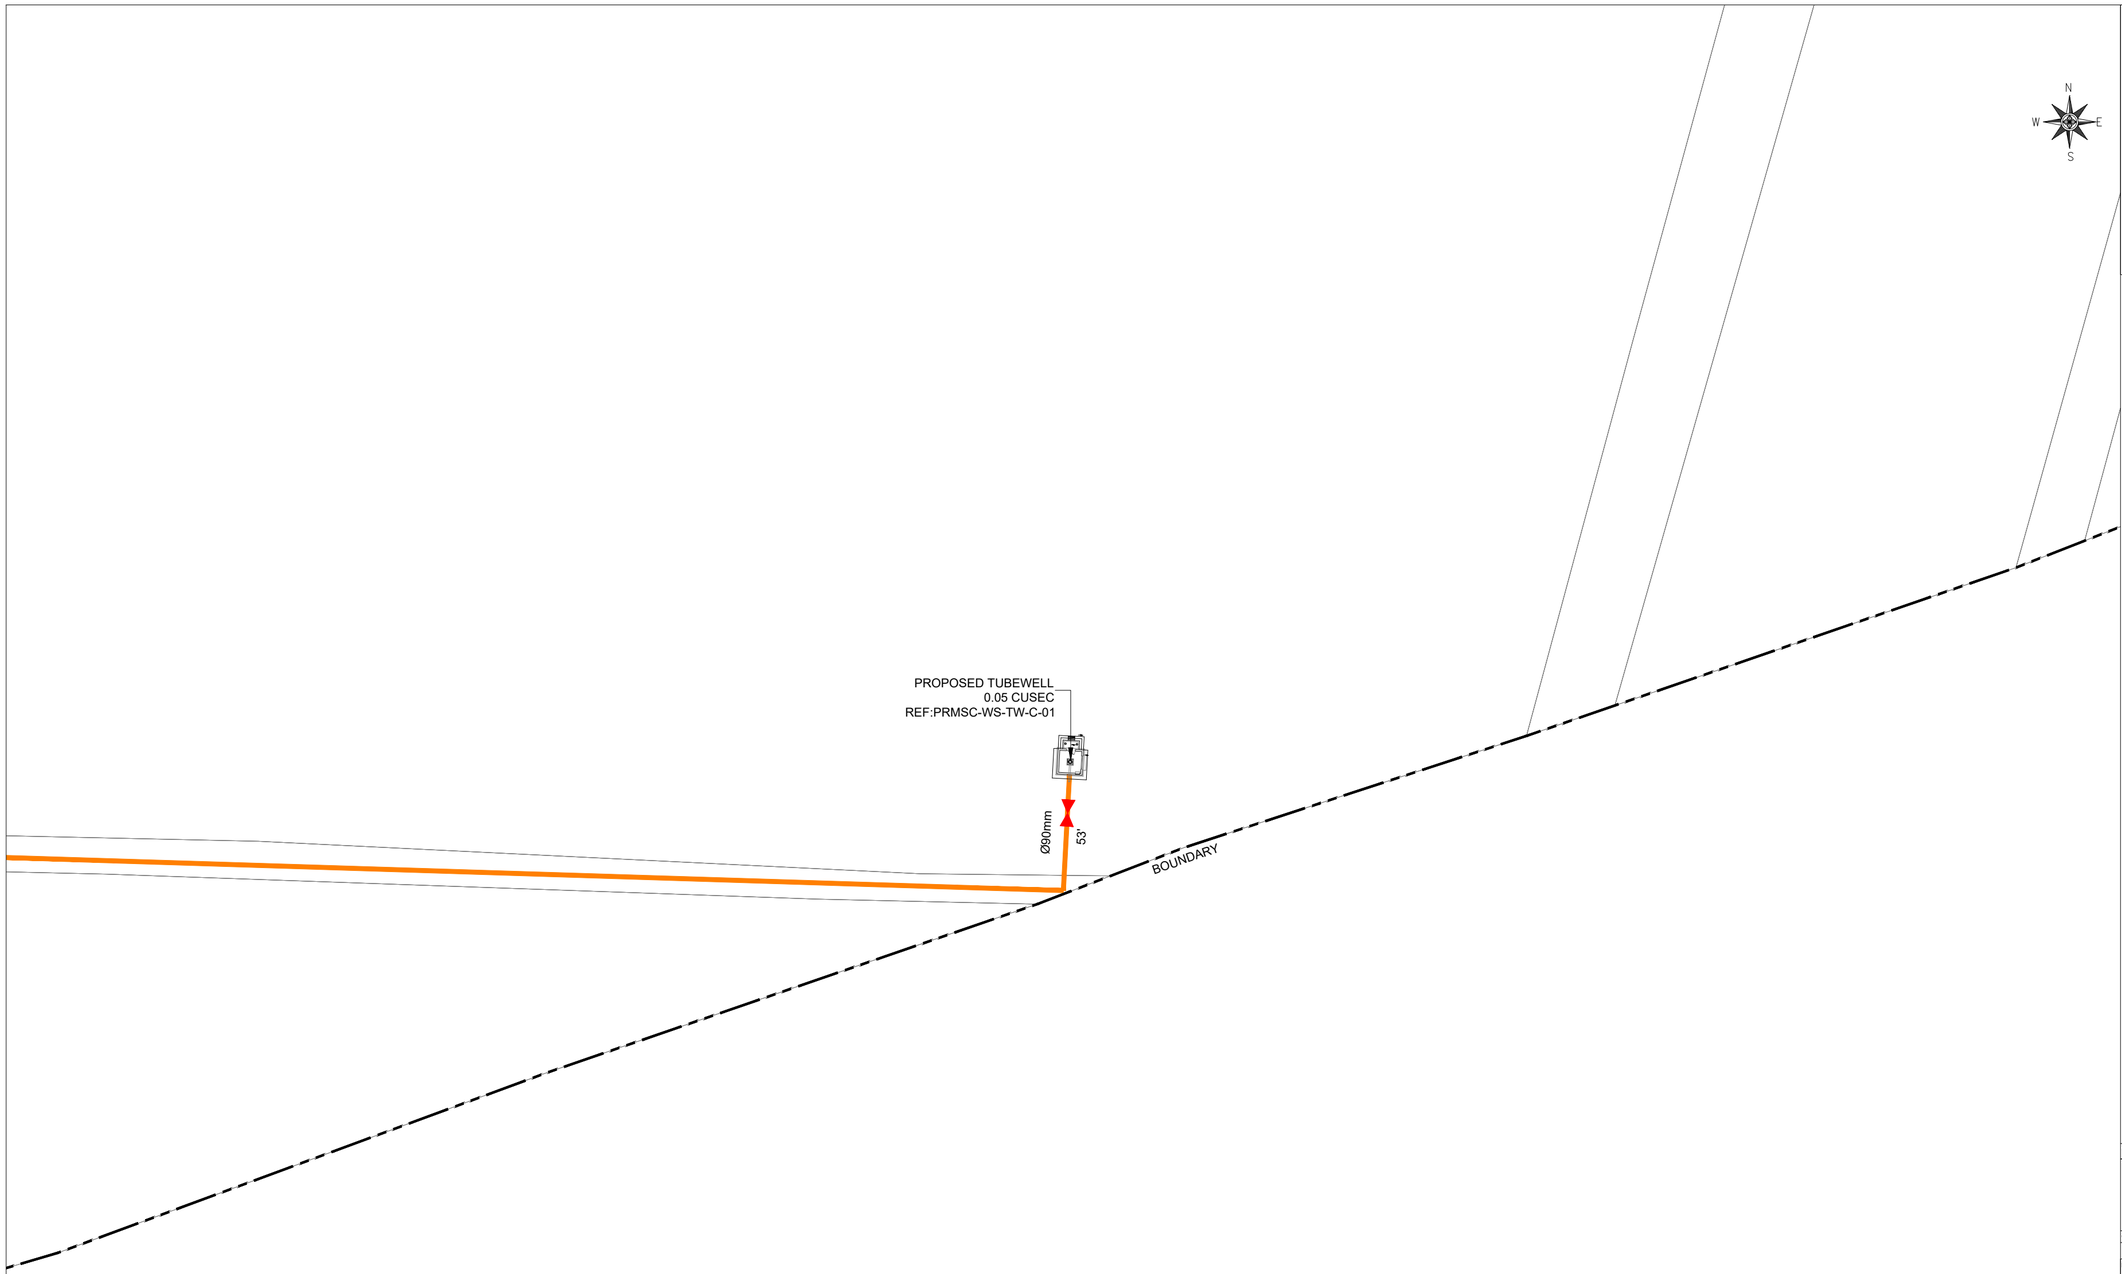

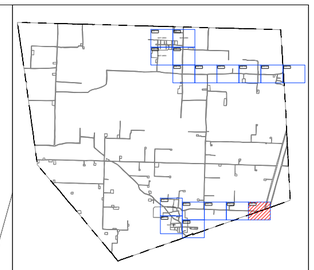

KEY PLAN

LEGEND:

90mm Ø HDPE PIPE

SLUICE VALVE

PROPOSED TUBE WELL

STAND POST TYPE - I

BOUNDARY

VILLAGE: RAMNAGAR (BWN)

TITLE.

WATER SUPPLY SYSTEM LAYOUT PLAN-17

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	D E S C R I P T I O N	DRAWN	DESIGNED	APPROVED
01	24-12-2025	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº: PRMSC-BWN-RMG-WS-LP-17

SHEET 17 OF 17

REV 00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS
www.asianeon.com

PRMSC-BWN-RMG-WS-LP-17

SANDAR BASHNOI

KEY PLAN

Revenue Village: Sandar Bashnoi Panwa Sheet-1

Title:
Proposed Water Supply Plan

Legend:

- SETTLEMENT
- PROPOSED TUBEWELL
- SETTELMENT BOUNDARY

Scale: 1:1,500
1 inch = 125 feet
Paper Size: A3

0 40 80 160
Kilometers

Project:
Engineering Design & Construction Supervision, Punjab Rural Sustainable Water Supply & Sanitation Project, Cluster South-III

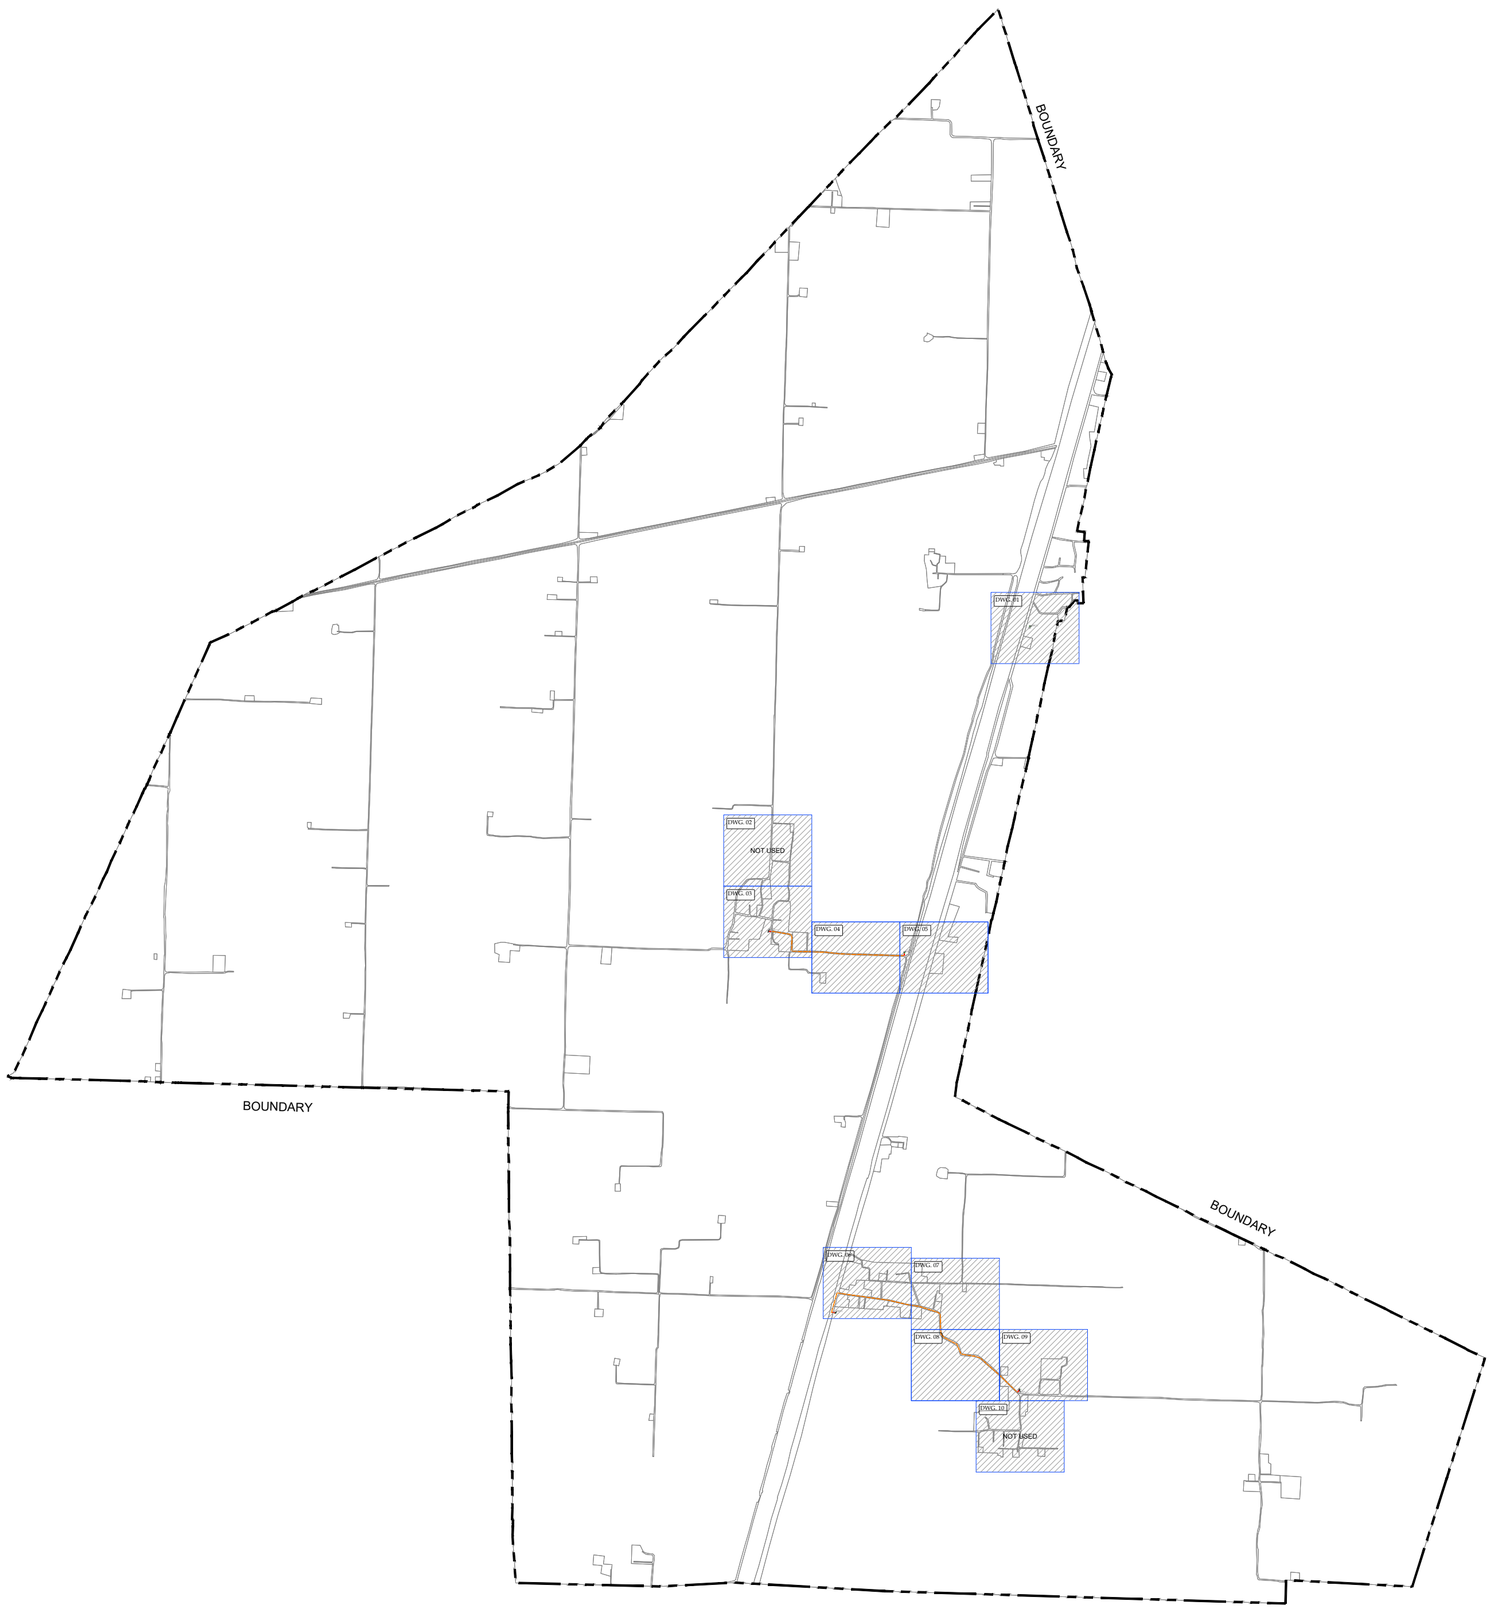

LEGEND:

- 90mm Ø HDPE PIPE
- SLUICE VALVE
- PROPOSED TUBE WELL
- STAND POST TYPE - I
- BOUNDARY

VILLAGE: SUNDAR BASHNOAI (BWN)

TITLE.

WATER SUPPLY SYSTEM KEY PLAN

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 1200'

ISSUE N°	DATE	D E S C R I P T I O N	DRAWN	DESIGNED	APPROVED
01	02-01-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING N°:	SHEET	REV
PRMSC-BWN-SBN-WS-KP-00	00 OF 00	00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT
ASIAN CONSULTING ENGINEERS
www.asianeng.com.pk

PRMSC-BWN-SBN-WS-KP-00

LAYOUT PLANS

Revenue Village: Sandar Bashnoi Dughanpura Sheet-2

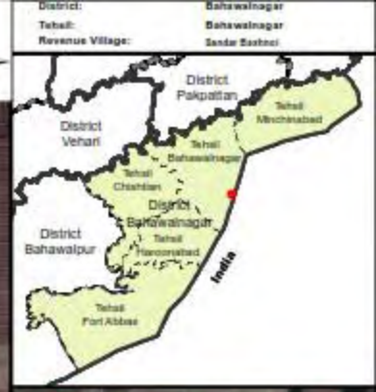

Title:
Proposed Water Supply Plan

Legend:

- SETTLEMENT
- STAND POST
- SETTELMENT BOUNDARY

Scale: 1:1,600
1 inch = 133 feet
Paper Size: A3

0 40 80 160
Kilometers

Project:
Engineering Design & Construction Supervision, Punjab Rural Sustainable Water Supply & Sanitation Project, Cluster South-III



Title:
Proposed Water Supply Plan

Legend:

- SETTLEMENT
- STAND POST
- SETTELMENT BOUNDARY

Scale: 1:3,500
1 inch = 292 feet
Paper Size: A3

0 40 80 160
Kilometers

Project:
Engineering Design & Construction Supervision, Punjab Rural Sustainable Water Supply & Sanitation Project, Cluster South-III

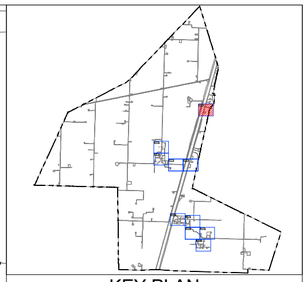

KEY PLAN

LEGEND:

- 90mm Ø HDPE PIPE
- SLUICE VALVE
- PROPOSED TUBE WELL
- STAND POST TYPE - I
- BOUNDARY

VILLAGE: SUNDAR BASHNOAI (BWN)

TITLE.

WATER SUPPLY SYSTEM LAYOUT PLAN-01

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	02-1-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-SBN-WS-LP-01	01 OF 10	00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

PRMSC-BWN-SBN-WS-LP-01

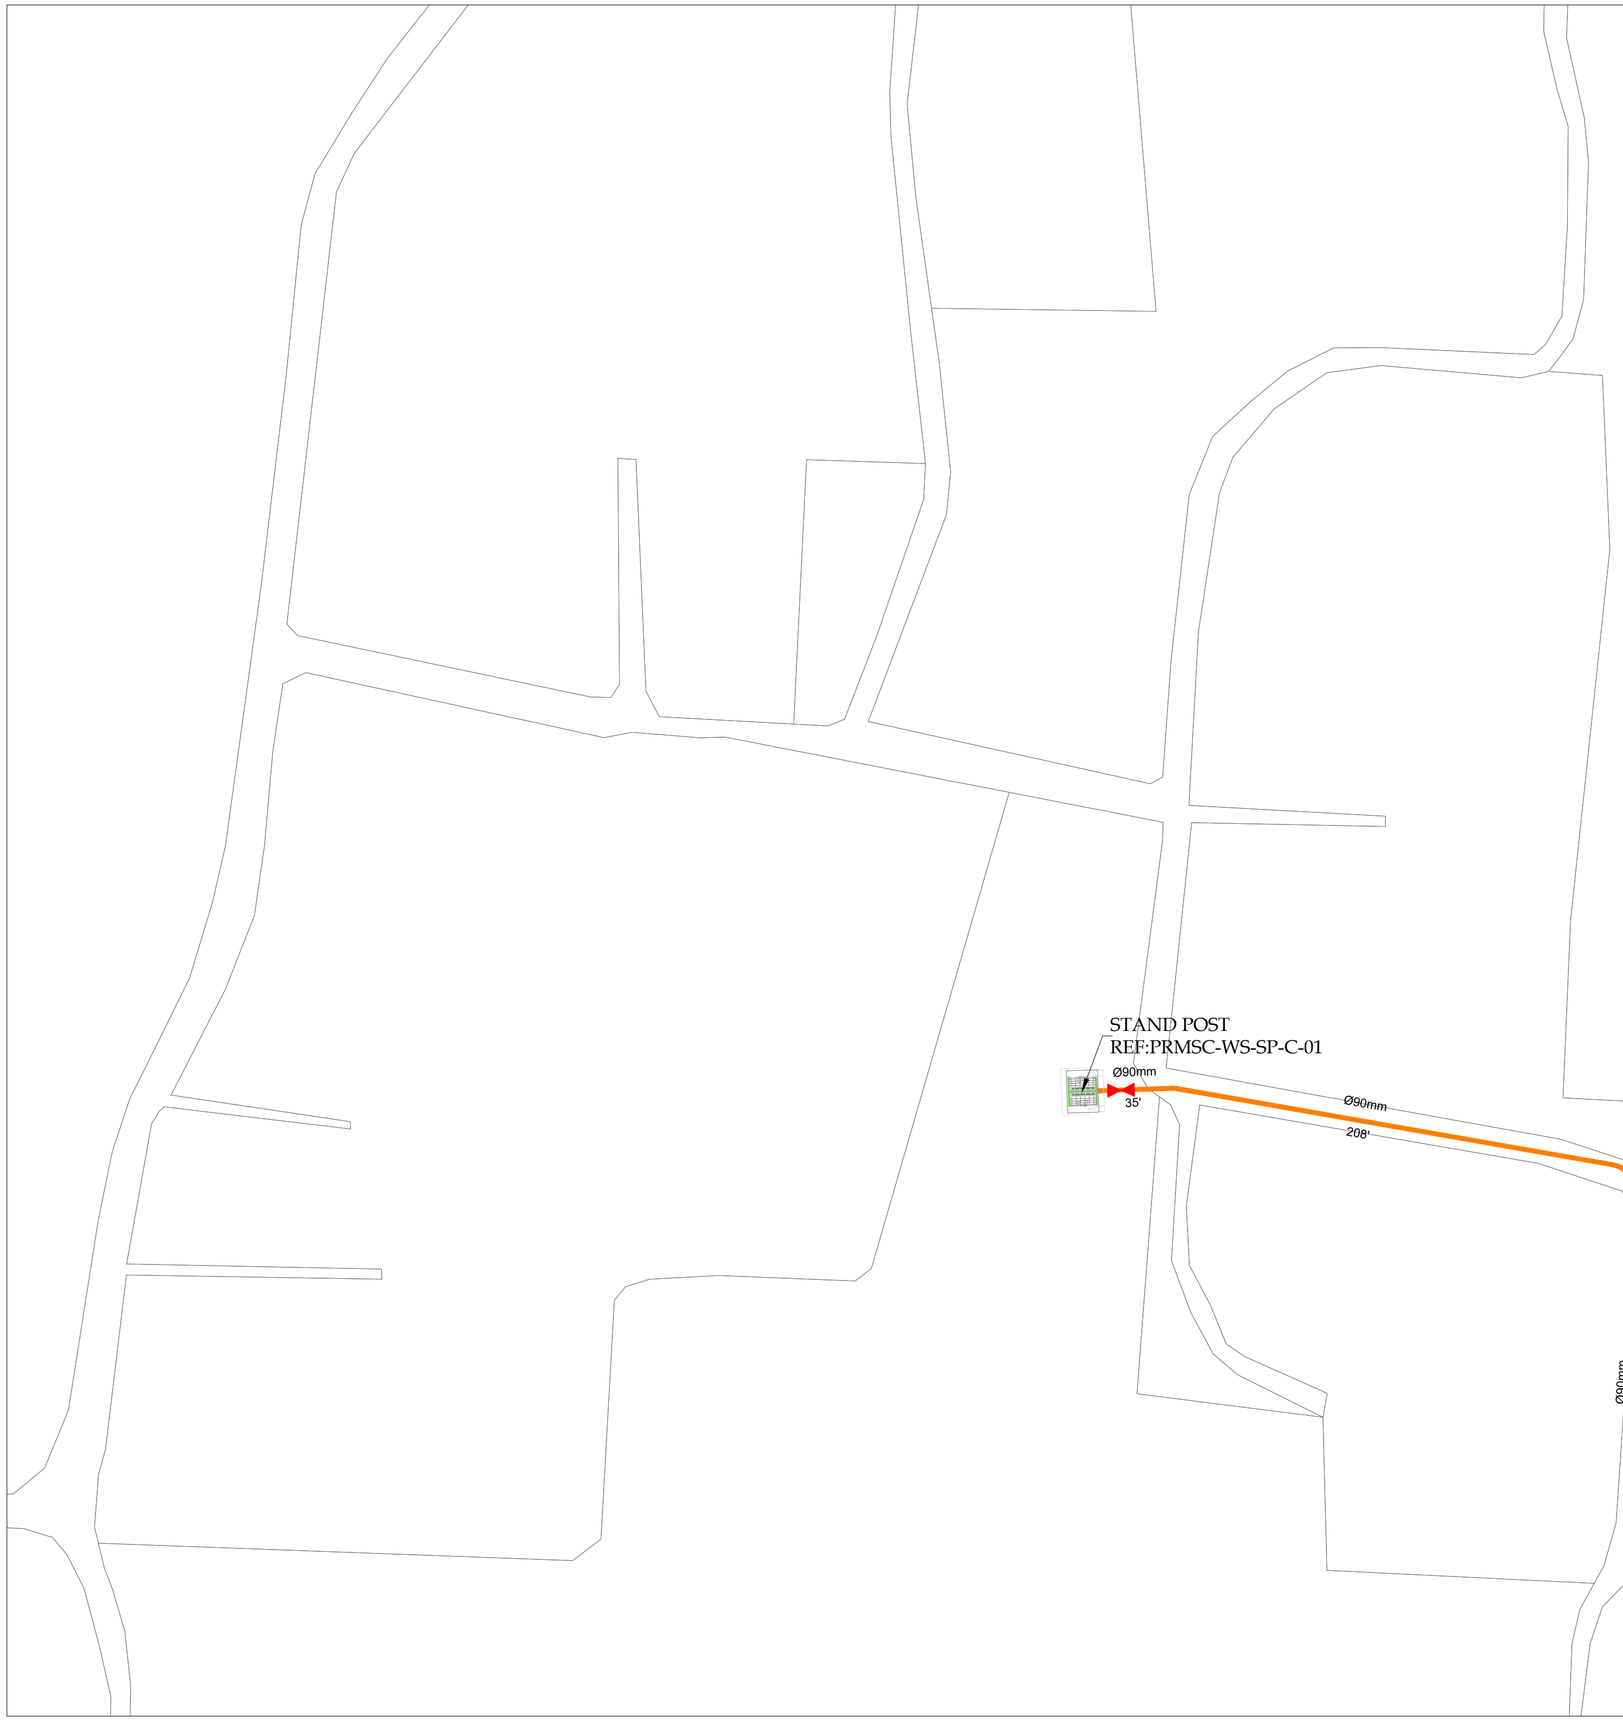

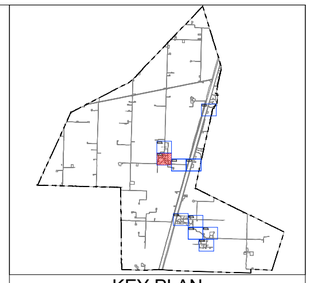

KEY PLAN

LEGEND:

- 90mm Ø HDPE PIPE
- SLUICE VALVE
- PROPOSED TUBE WELL
- STAND POST TYPE - I
- BOUNDARY

VILLAGE: SUNDAR BASHNOAI (BWN)

TITLE.

WATER SUPPLY SYSTEM LAYOUT PLAN-03

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	02-1-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:

PRMSC-BWN-SBN-WS-LP-03

SHEET 03 OF 10

REV 00

PROJECT:

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:

PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS JV
www.asiancon.com

PRMSC-BWN-SBN-WS-LP-03

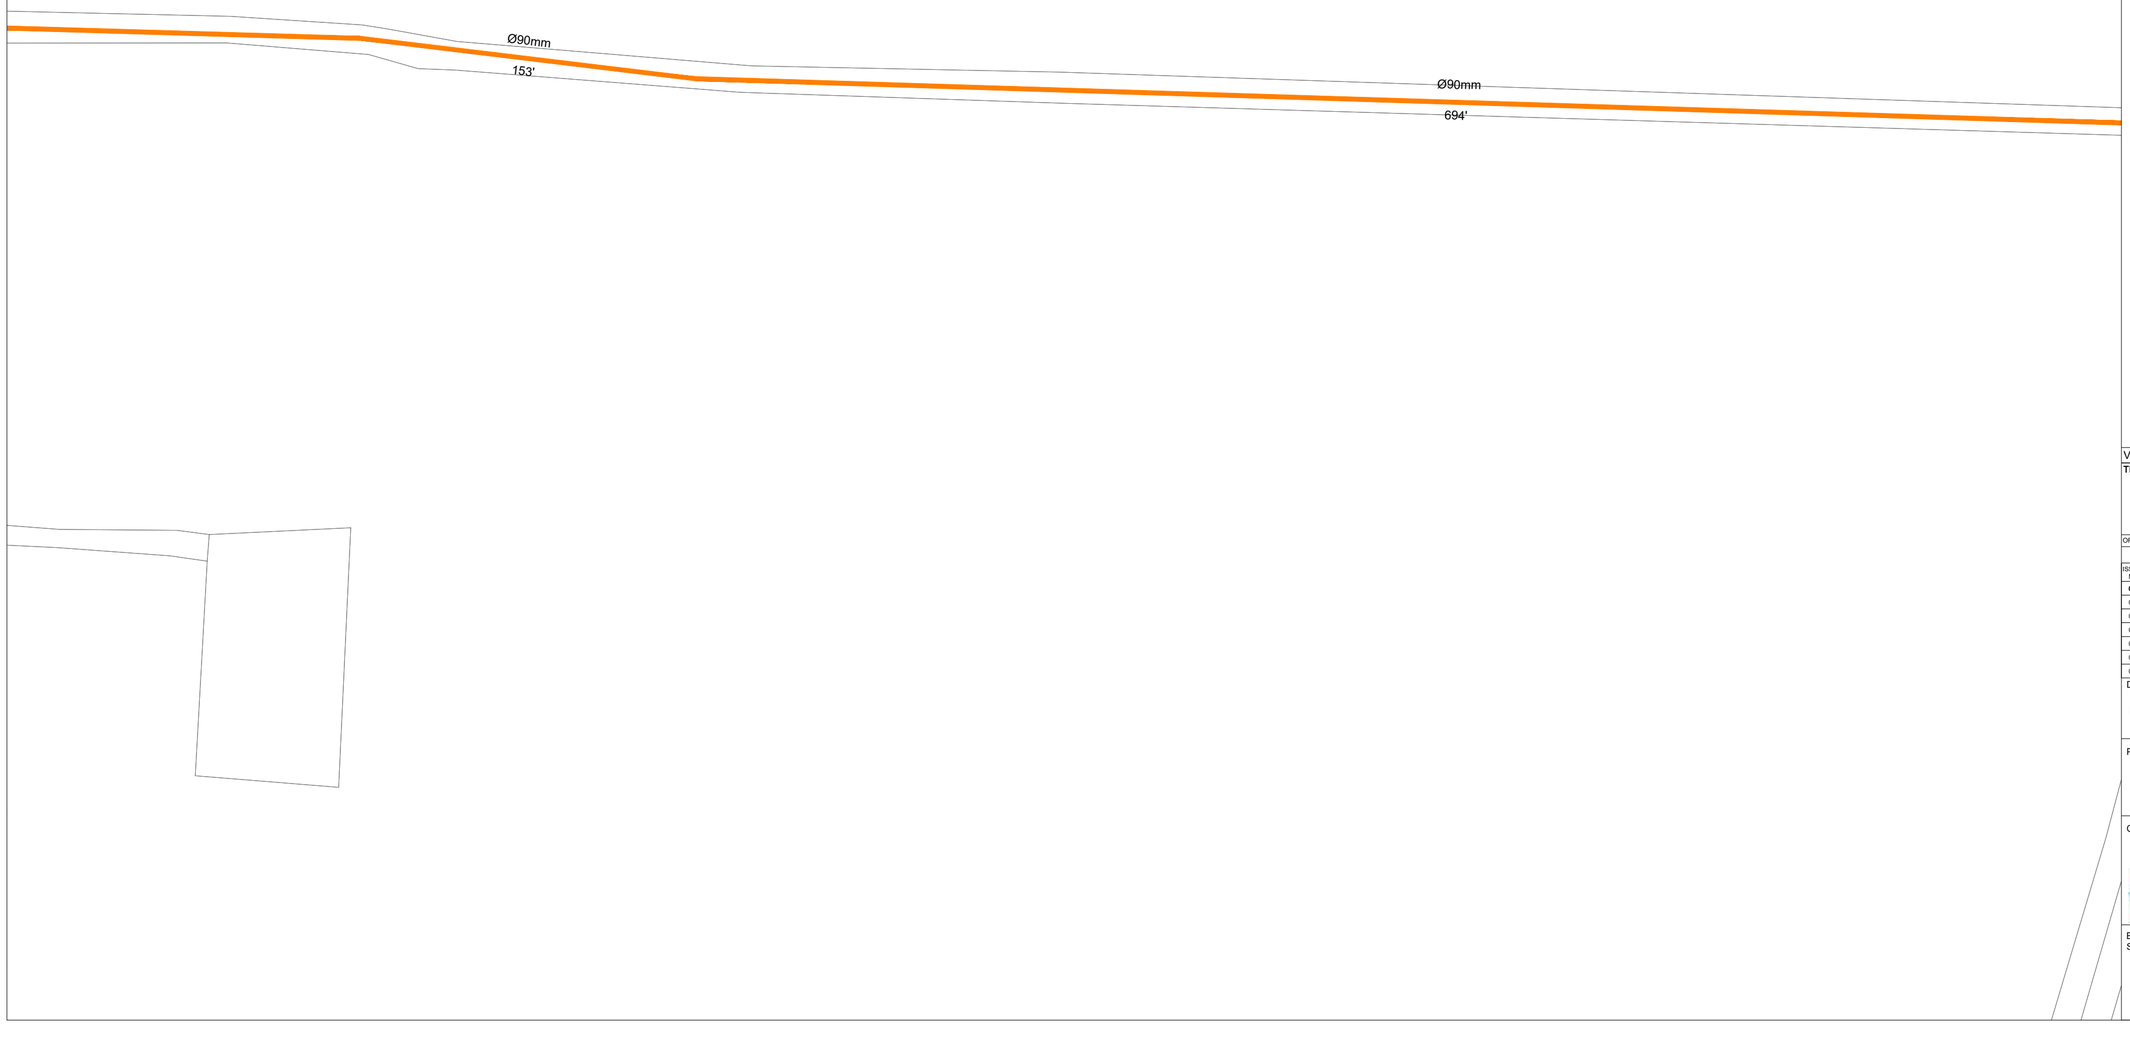

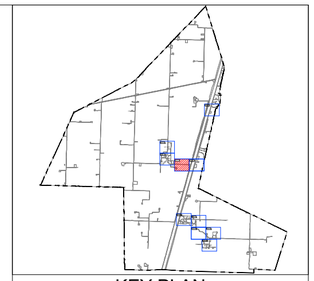

KEY PLAN

LEGEND:

- 90mm Ø HDPE PIPE
- SLUICE VALVE
- PROPOSED TUBE WELL
- STAND POST TYPE - I
- BOUNDARY

VILLAGE: SUNDAR BASHNOAI (BWN)

TITLE.

WATER SUPPLY SYSTEM LAYOUT PLAN-04

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	02-1-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-SBN-WS-LP-04	04 OF 10	00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:
ASIAN CONSULTING ENGINEERS
www.asiacon.com.pk

PRMSC-BWN-SBN-WS-LP-04

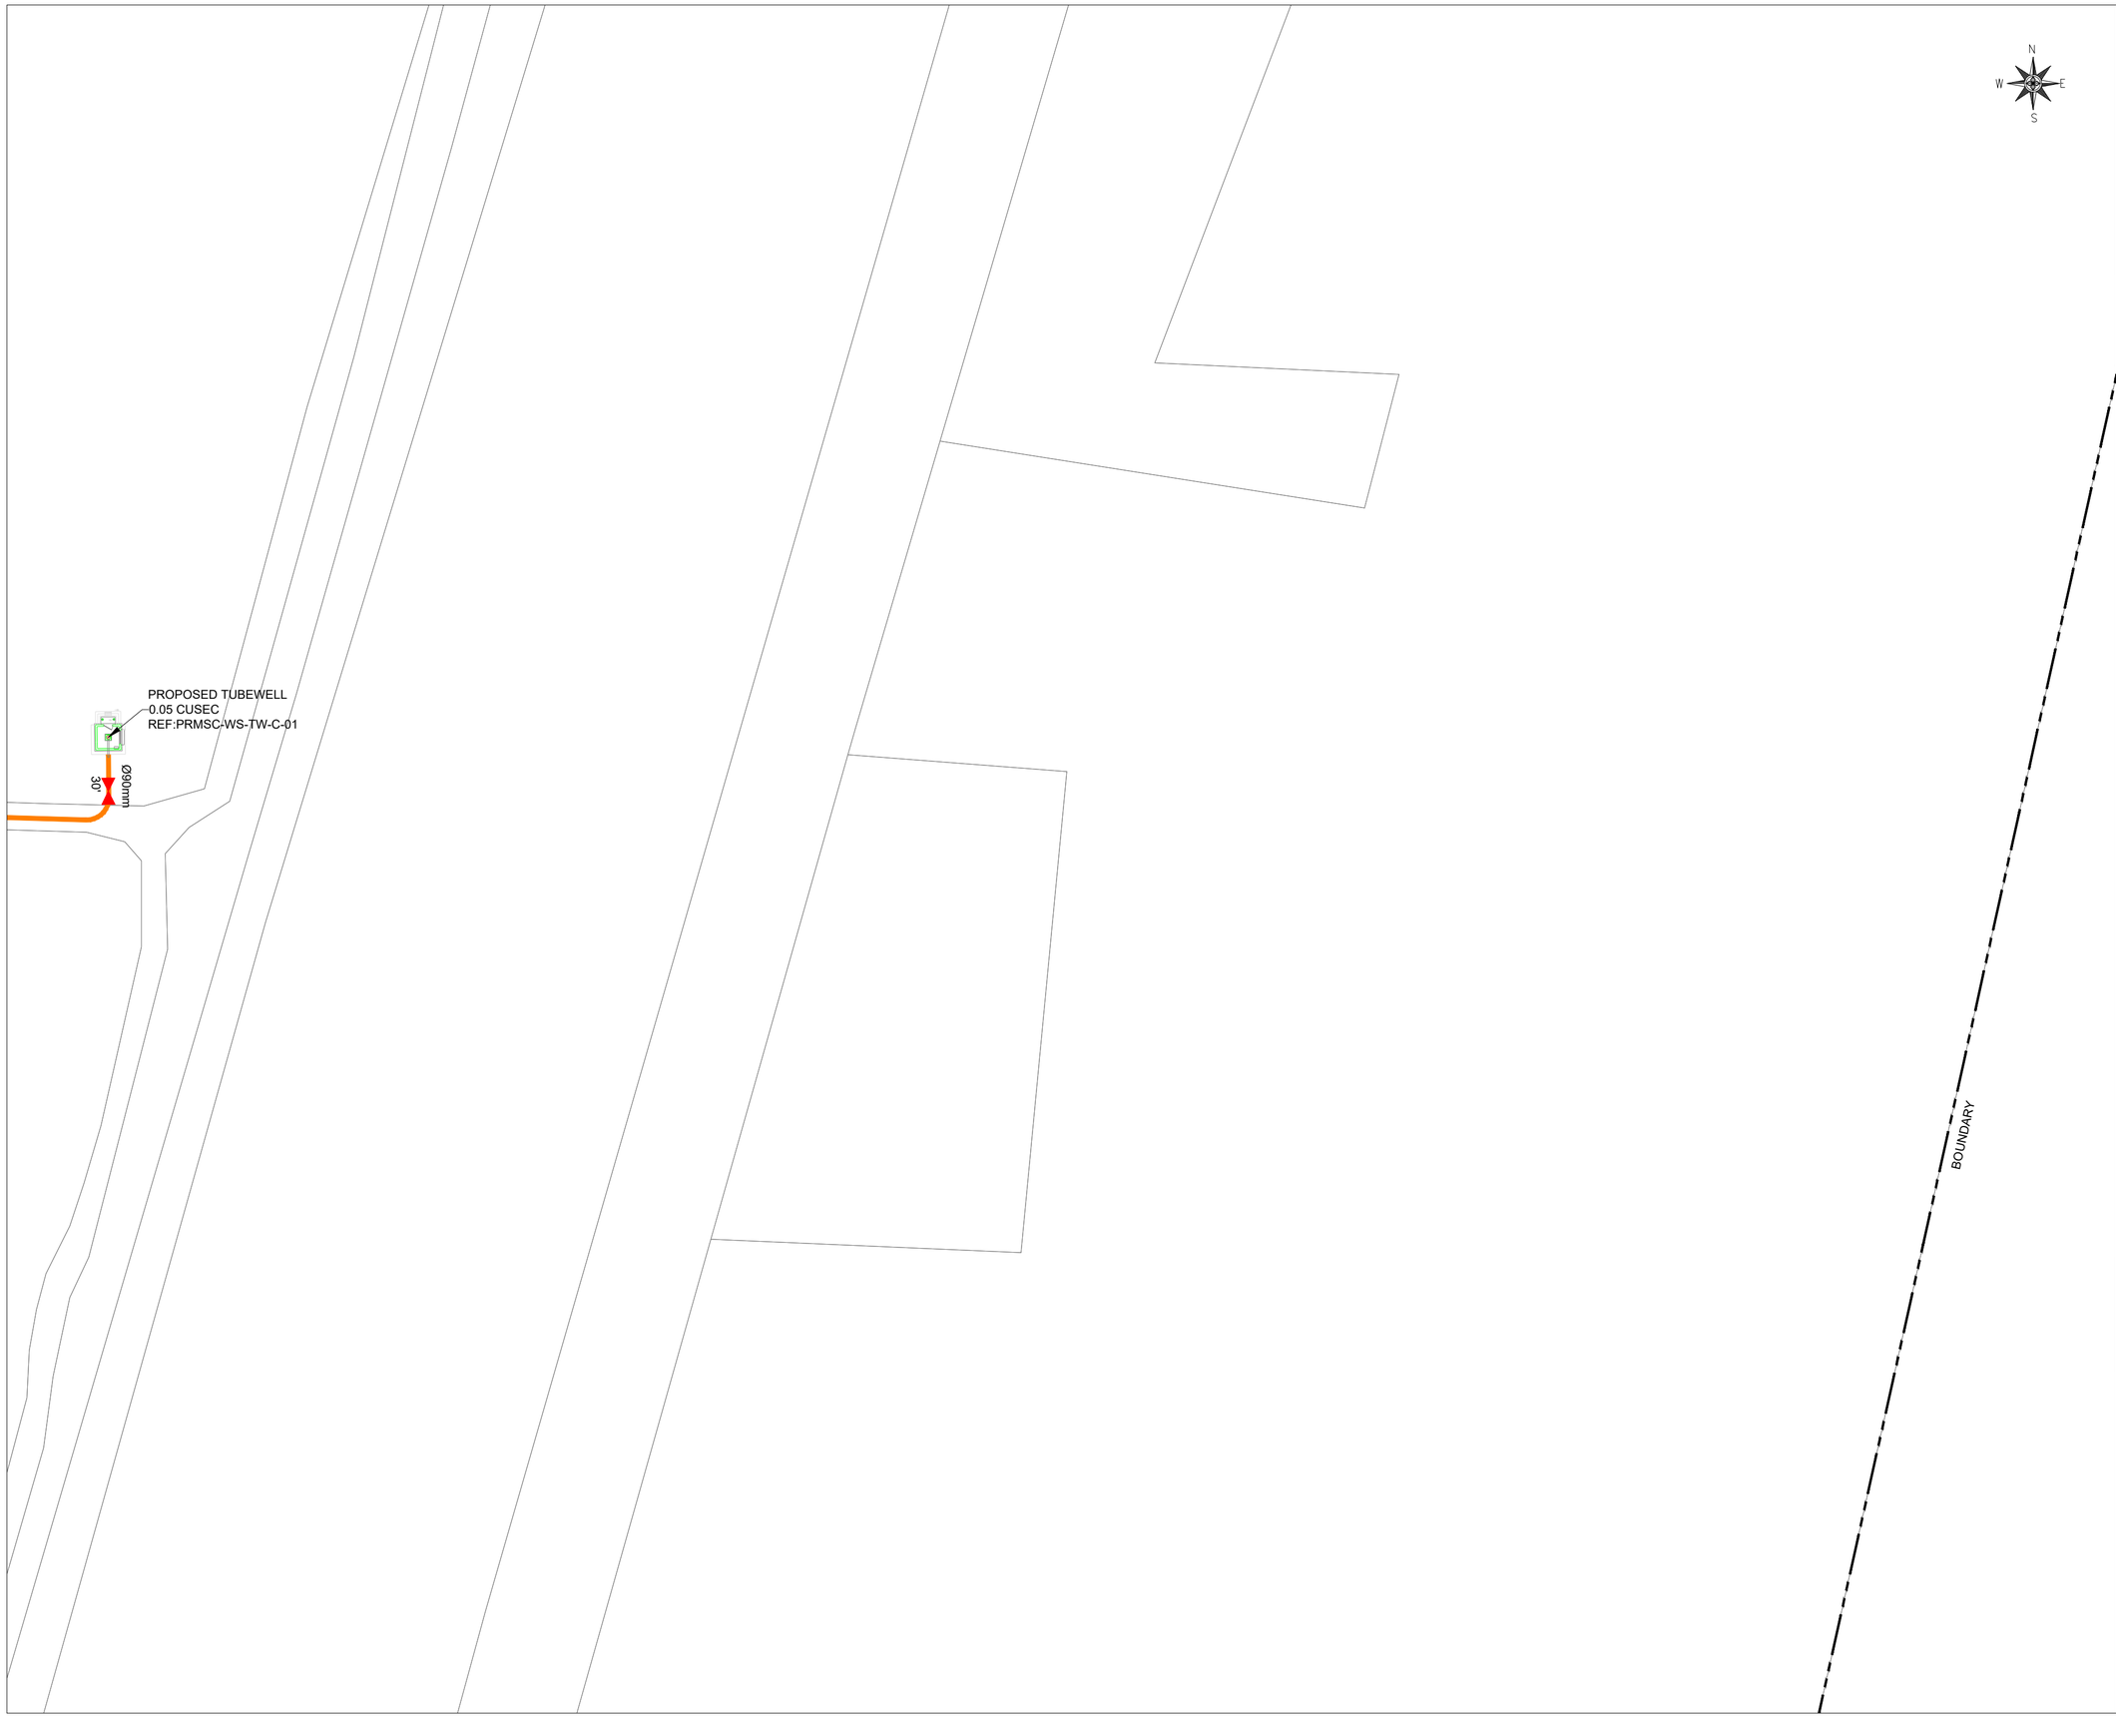

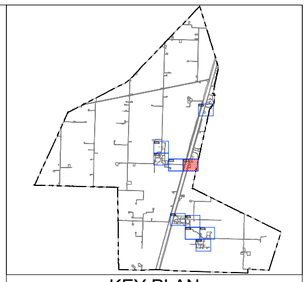

KEY PLAN

LEGEND:

- 90mm Ø HDPE PIPE
- SLUICE VALVE
- PROPOSED TUBE WELL
- STAND POST TYPE - I
- BOUNDARY

VILLAGE: SUNDAR BASHNOAI (BWN)

TITLE.

WATER SUPPLY SYSTEM LAYOUT PLAN-05

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	02-1-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-SBN-WS-LP-05	05 OF 10	00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS
www.asiancon.com JV

PRMSC-BWN-SBN-WS-LP-05

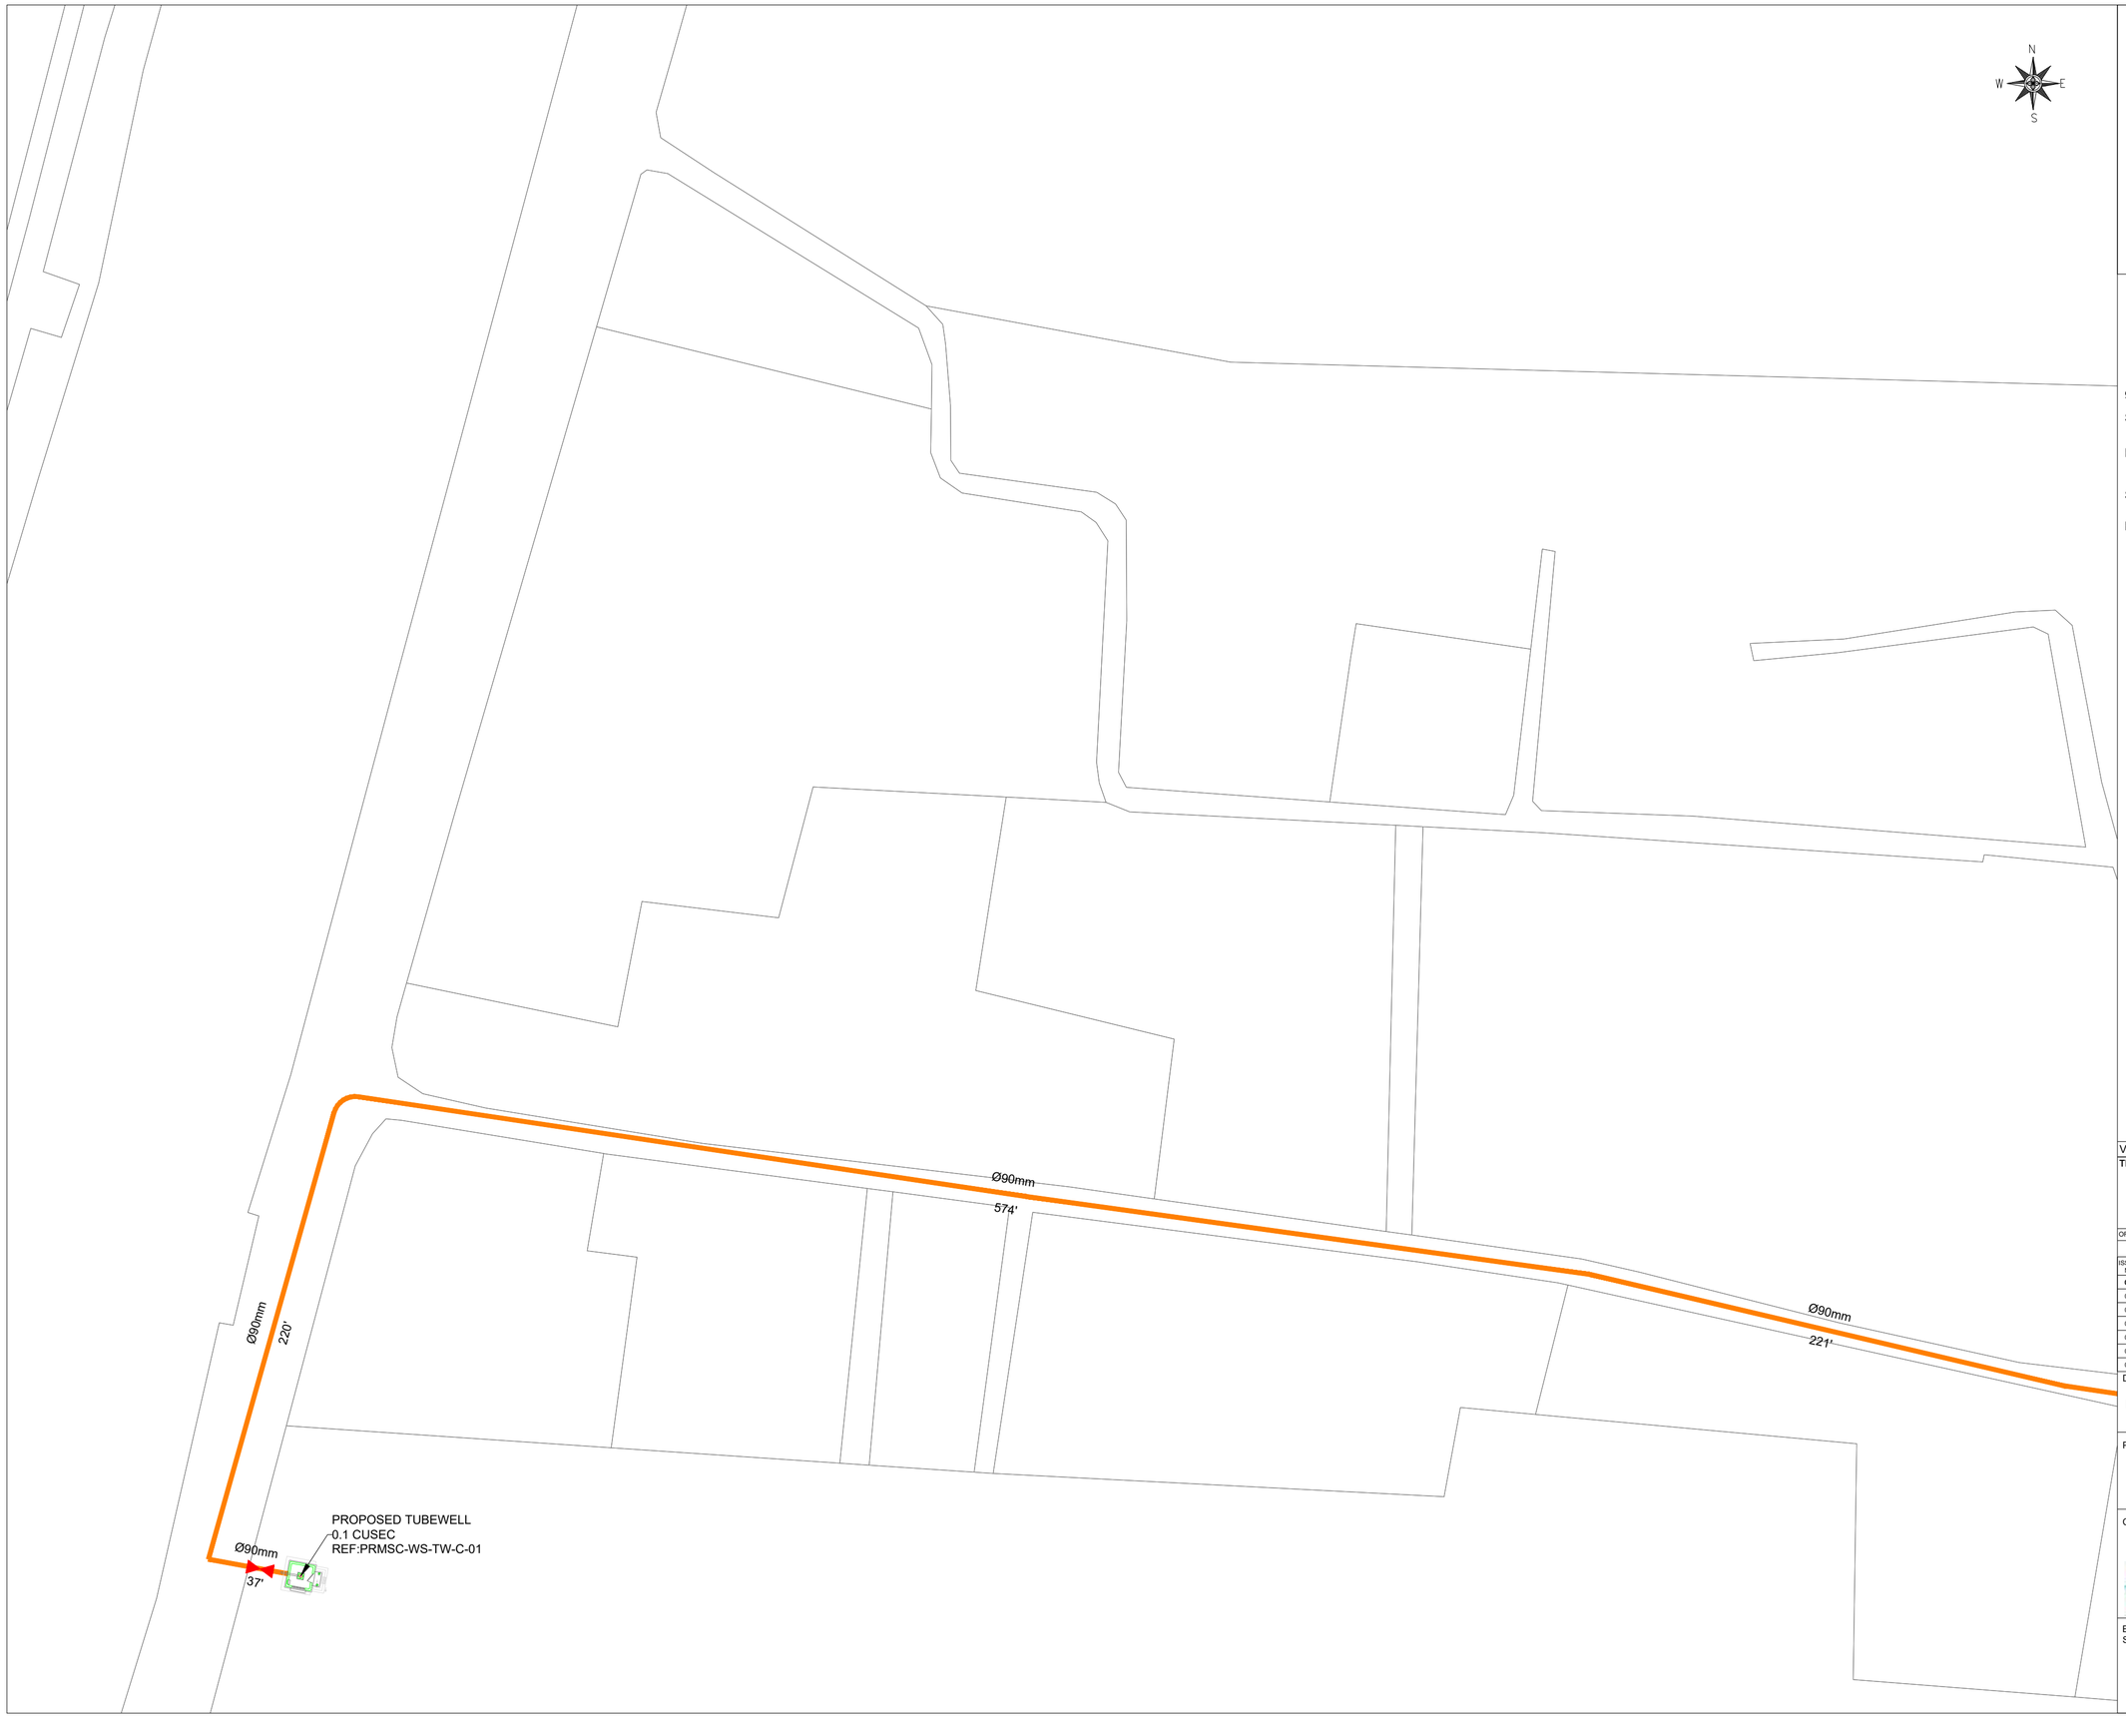

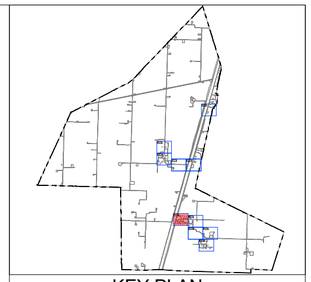

KEY PLAN

LEGEND:

90mm Ø HDPE PIPE

SLUICE VALVE

PROPOSED TUBE WELL

STAND POST TYPE - I

BOUNDARY

VILLAGE: SUNDAR BASHNOAI (BWN)

TITLE.

WATER SUPPLY SYSTEM LAYOUT PLAN-06

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	02-1-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING N°: PRMSC-BWN-SBN-WS-LP-06

SHEET 06 OF 10

REV 00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:
ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

PRMSC-BWN-SBN-WS-LP-06

PRMSC-BWN-SBN-WS-LP-07

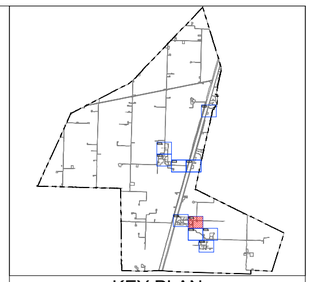

KEY PLAN

LEGEND:

90mm Ø HDPE PIPE

SLUICE VALVE

PROPOSED TUBE WELL

STAND POST TYPE - I

BOUNDARY

VILLAGE: SUNDAR BASHNOAI (BWN)

TITLE.

WATER SUPPLY SYSTEM LAYOUT PLAN-07

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	02-1-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-SBN-WS-LP-07	07 OF 10	00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

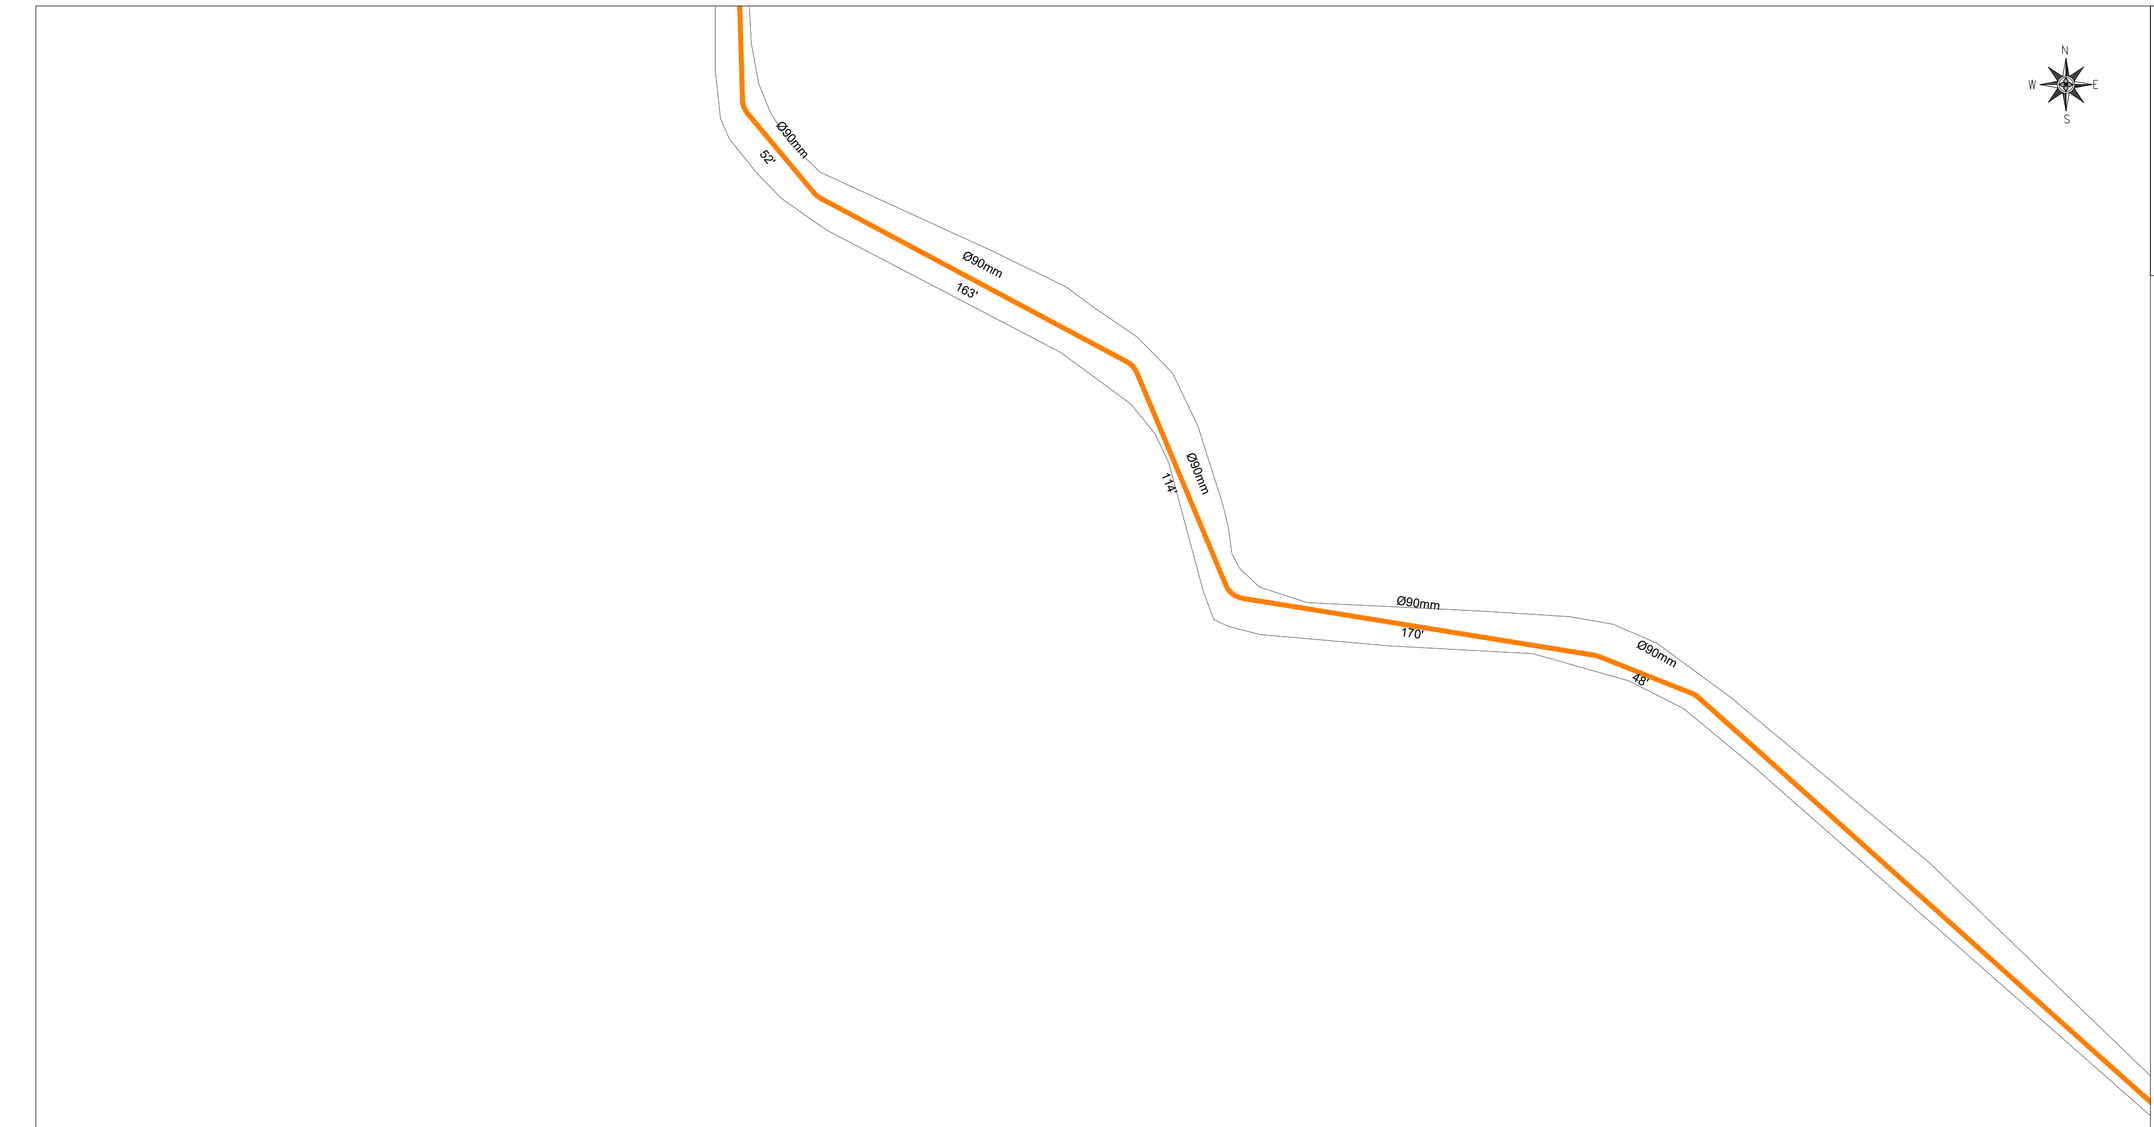

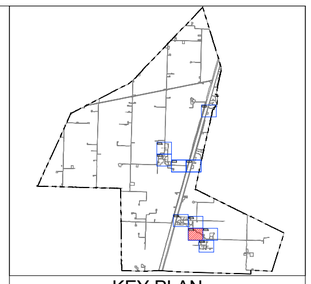

KEY PLAN

LEGEND:

- 90mm Ø HDPE PIPE
- SLUICE VALVE
- PROPOSED TUBE WELL
- STAND POST TYPE - I
- BOUNDARY

VILLAGE: SUNDAR BASHNOAI (BWN)

TITLE.

WATER SUPPLY SYSTEM LAYOUT PLAN-08

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	02-1-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-SBN-WS-LP-08	08 OF 10	00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS (PVT) LTD. www.asiacon.com.pk

PRMSC-BWN-SBN-WS-LP-08

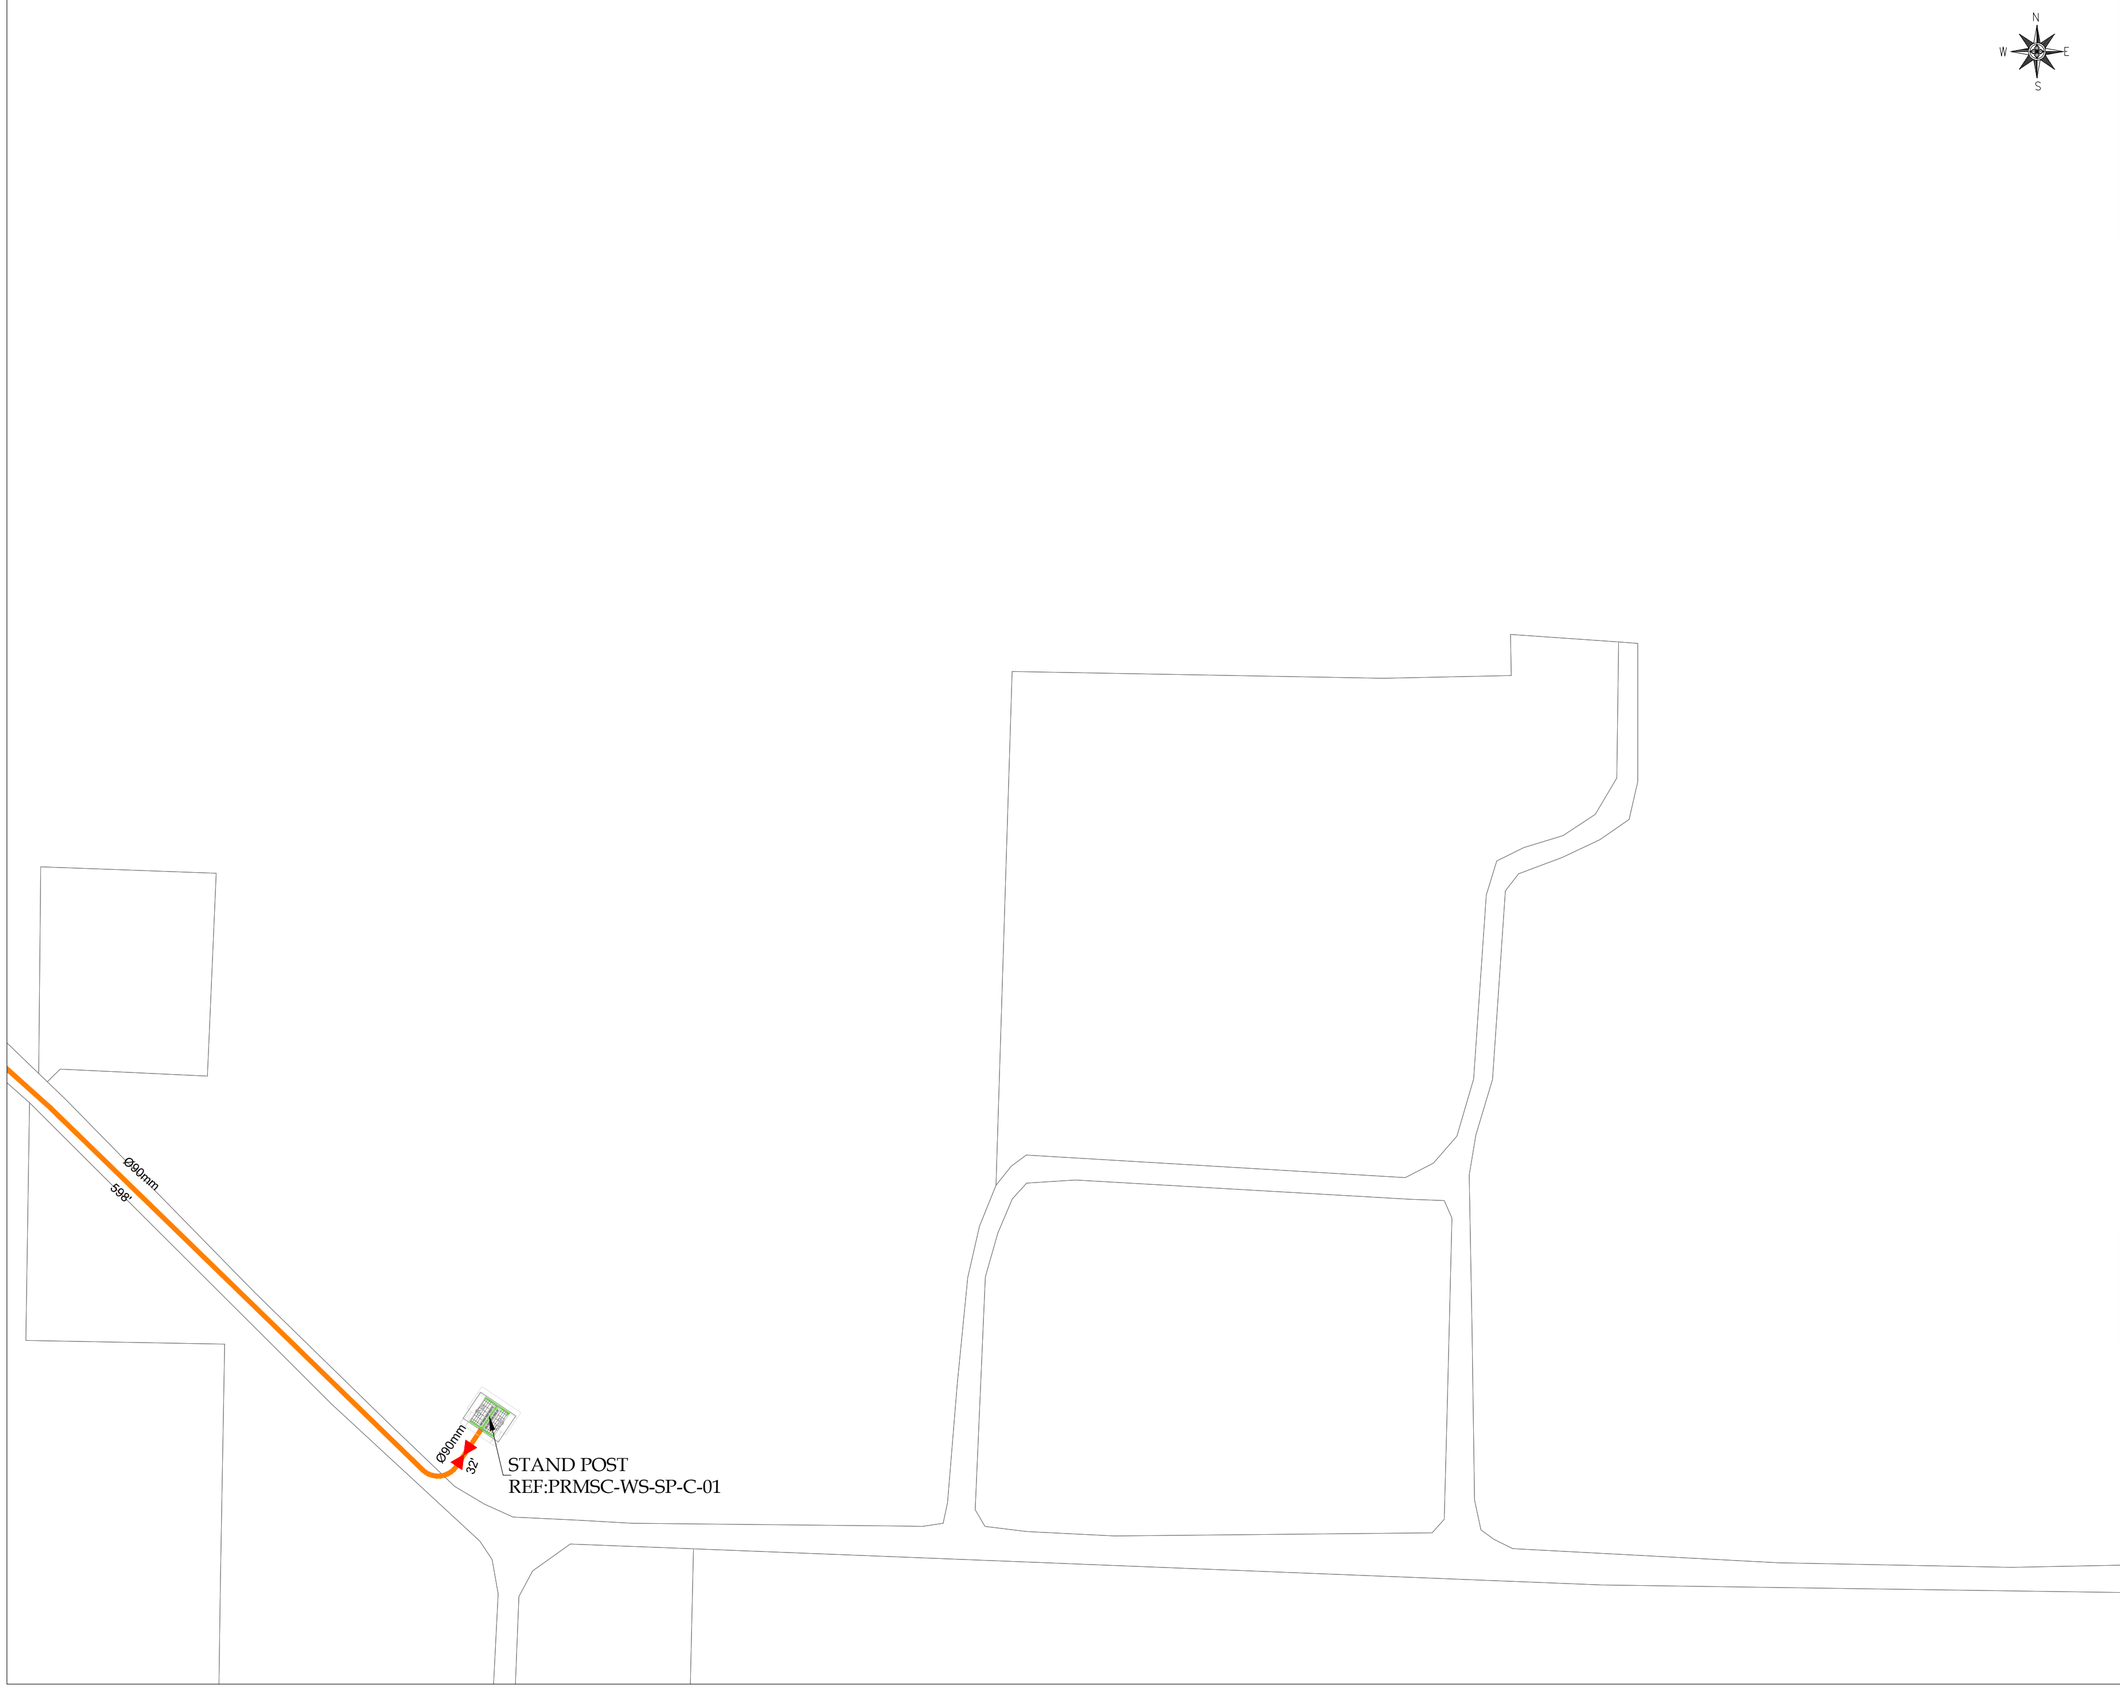

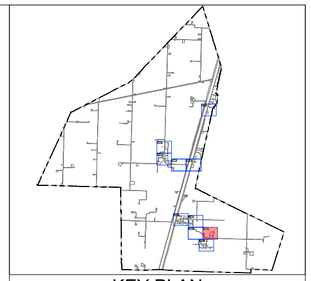

KEY PLAN

LEGEND:

- 90mm Ø HDPE PIPE
- SLUICE VALVE
- PROPOSED TUBE WELL
- STAND POST TYPE - I
- BOUNDARY

VILLAGE: SUNDAR BASHNOAI (BWN)

TITLE.

WATER SUPPLY SYSTEM LAYOUT PLAN-09

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	02-1-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. HSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-SBN-WS-LP-09	09 OF 10	00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

PRMSC-BWN-SBN-WS-LP-09

SHER SINGH WALA

KEY PLAN

Revenue Village: Sher Singh Wala Chak Ratni Khera Sheet-1
Lat = 29.653888
Long = 73.294855
STAND POST-T1
Plot Size= 1.5 Marla
Chak Ratni Khera
N
District:
Bahawalnagar
Tehsil:
Bahawalnagar
Revenue Village:
Sher Singh Wala
District Pakpattan
Tehsil Minchinabad
District Vehari
Tehsil Bahawalnagar
Tehsil Chishtian
District Bahawalnagar
District Bahawalpur
Tehsil Haroonabad
India
Tehsil Fort Abbas
Title:
Proposed Water Supply Plan
Legend:
SETTLEMENT
STAND POST
SETTELMENT BOUNDARY
Scale: 1:1,000
1 inch = 83 feet
Paper Size: A3
0
40
80
160
Kilometers
Project:
Engineering Design & Construction Supervision, Punjab Rural Sustainable Water Supply & Sanitation Project, Cluster South-III

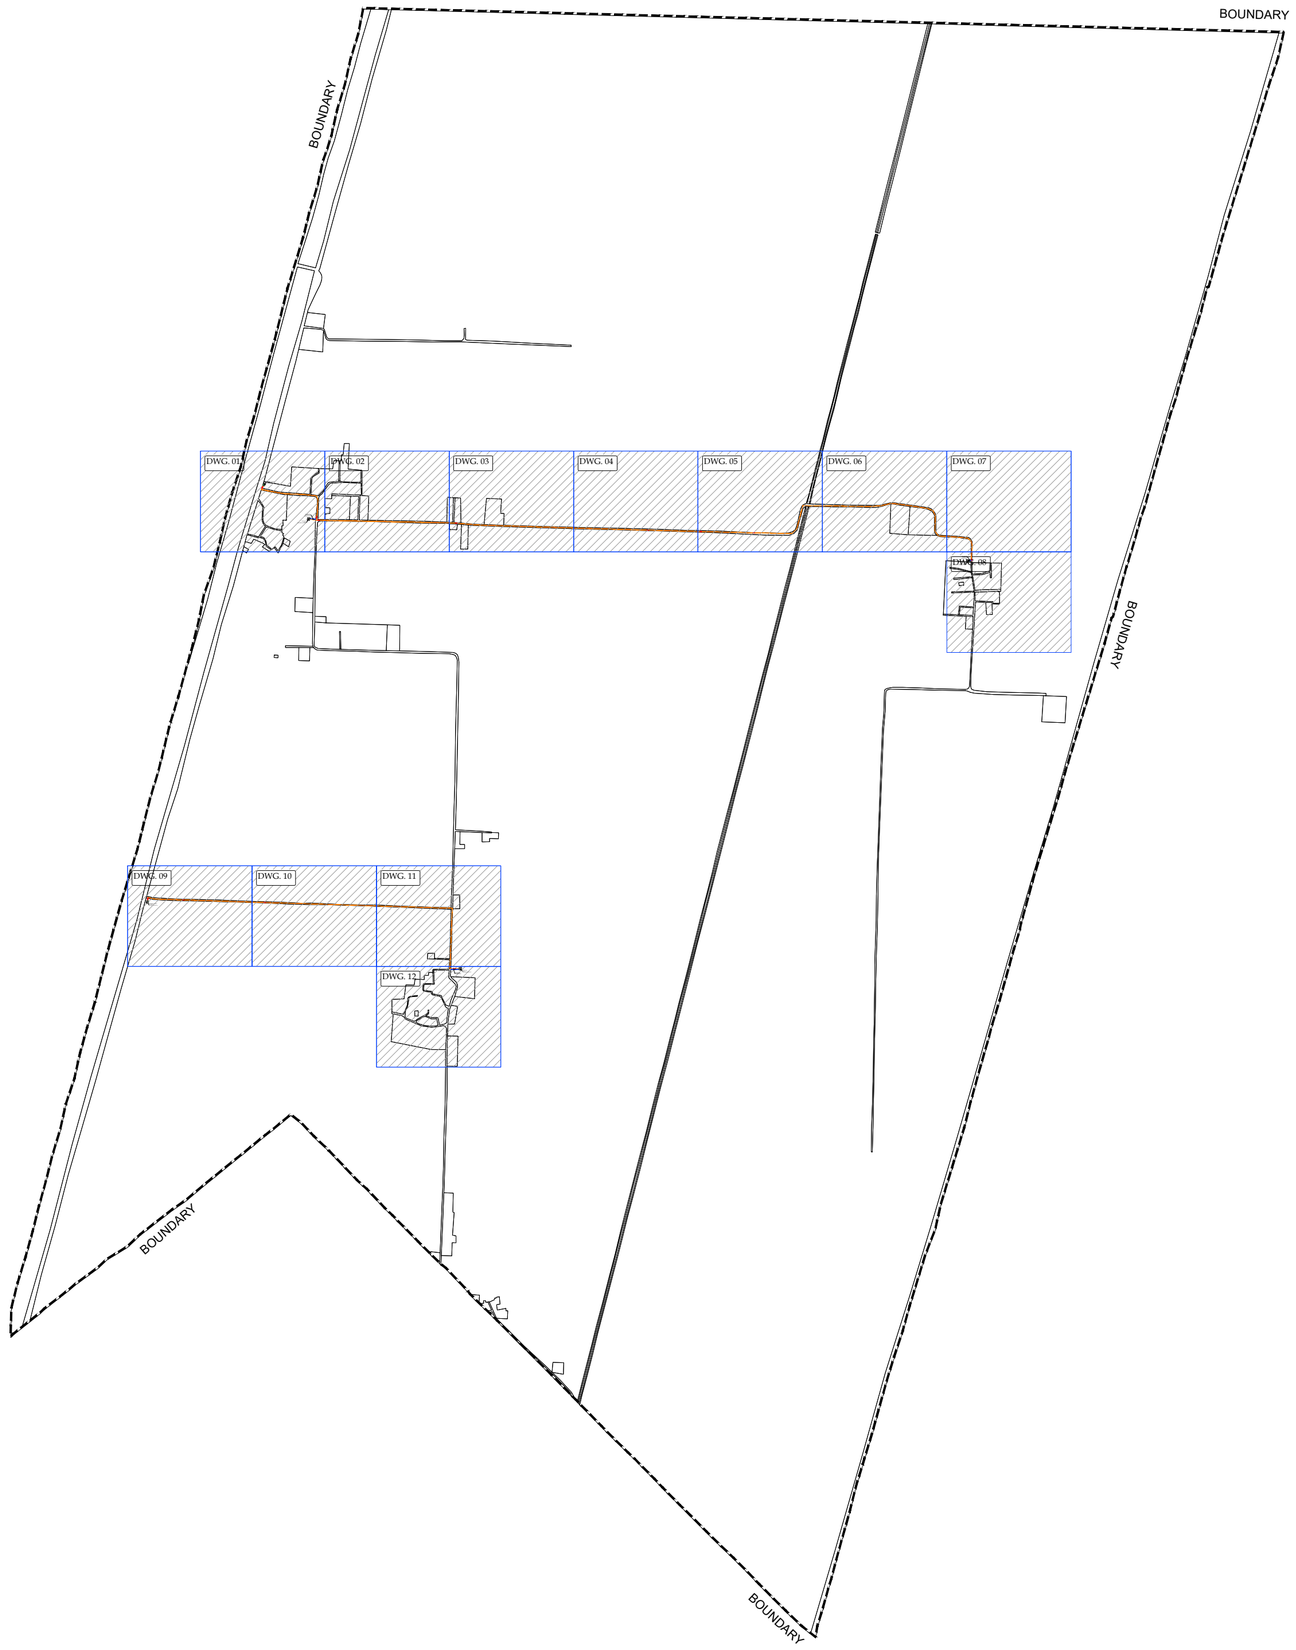

N
W
E
S

LEGEND:

- 90mm Ø PN - 8 HDPE PIPE
- SLUICE VALVE
- WASHOUT VALVE
- AIR RELEASE VALVE
- PROPOSED STAND POST TYPE-I
- PROPOSED TUBE WELL
- BOUNDARY

VILLAGE: SHER SINGH WALA (BWN)

TITLE.

WATER SUPPLY SYSTEM KEY PLAN

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 850'

ISSUE N°	DATE	D E S C R I P T I O N	DRAWN	DESIGNED	APPROVED
01	06-01-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-SSW-WS-KP-00	00 OF 00	00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT
ASIAN CONSULTING ENGINEERS
www.asiancon.com

PRMSC-BWN-SSW-SEW-KP-00

LAYOUT PLANS

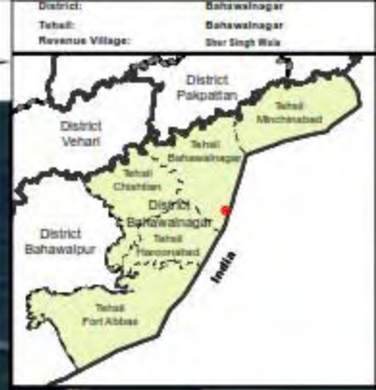

Title:
Proposed Water Supply Plan

Legend:

- PROPOSED TUBEWELL
- STAND POST
- SETTELMENT BOUNDARY

Scale: 1:1,000
1 inch = 83 feet
Paper Size: A3

0 40 80 160
Kilometers

Project:
Engineering Design & Construction Supervision, Punjab Rural Sustainable Water Supply & Sanitation Project, Cluster South-III

Revenue Village: Sher Singh Wala chak Sher Singh Wala Sheet-3

Lat = 29.662694
Long = 73.307036

STAND POST-T1
Plot Size= 1.5 Marla

Chak Sher Singh

N

District: Bahawalnagar
Tehsil: Bahawalnagar
Revenue Village: Sher Singh Wala

Title:
Proposed Water Supply Plan

Legend:

- SETTLEMENT
- STAND POST
- SETTELMENT BOUNDARY

Scale: 1:700
1 inch = 58 feet
Paper Size: A3

0 40 80 160
Kilometers

Project:
Engineering Design & Construction Supervision, Punjab Rural Sustainable Water Supply & Sanitation Project, Cluster South-III

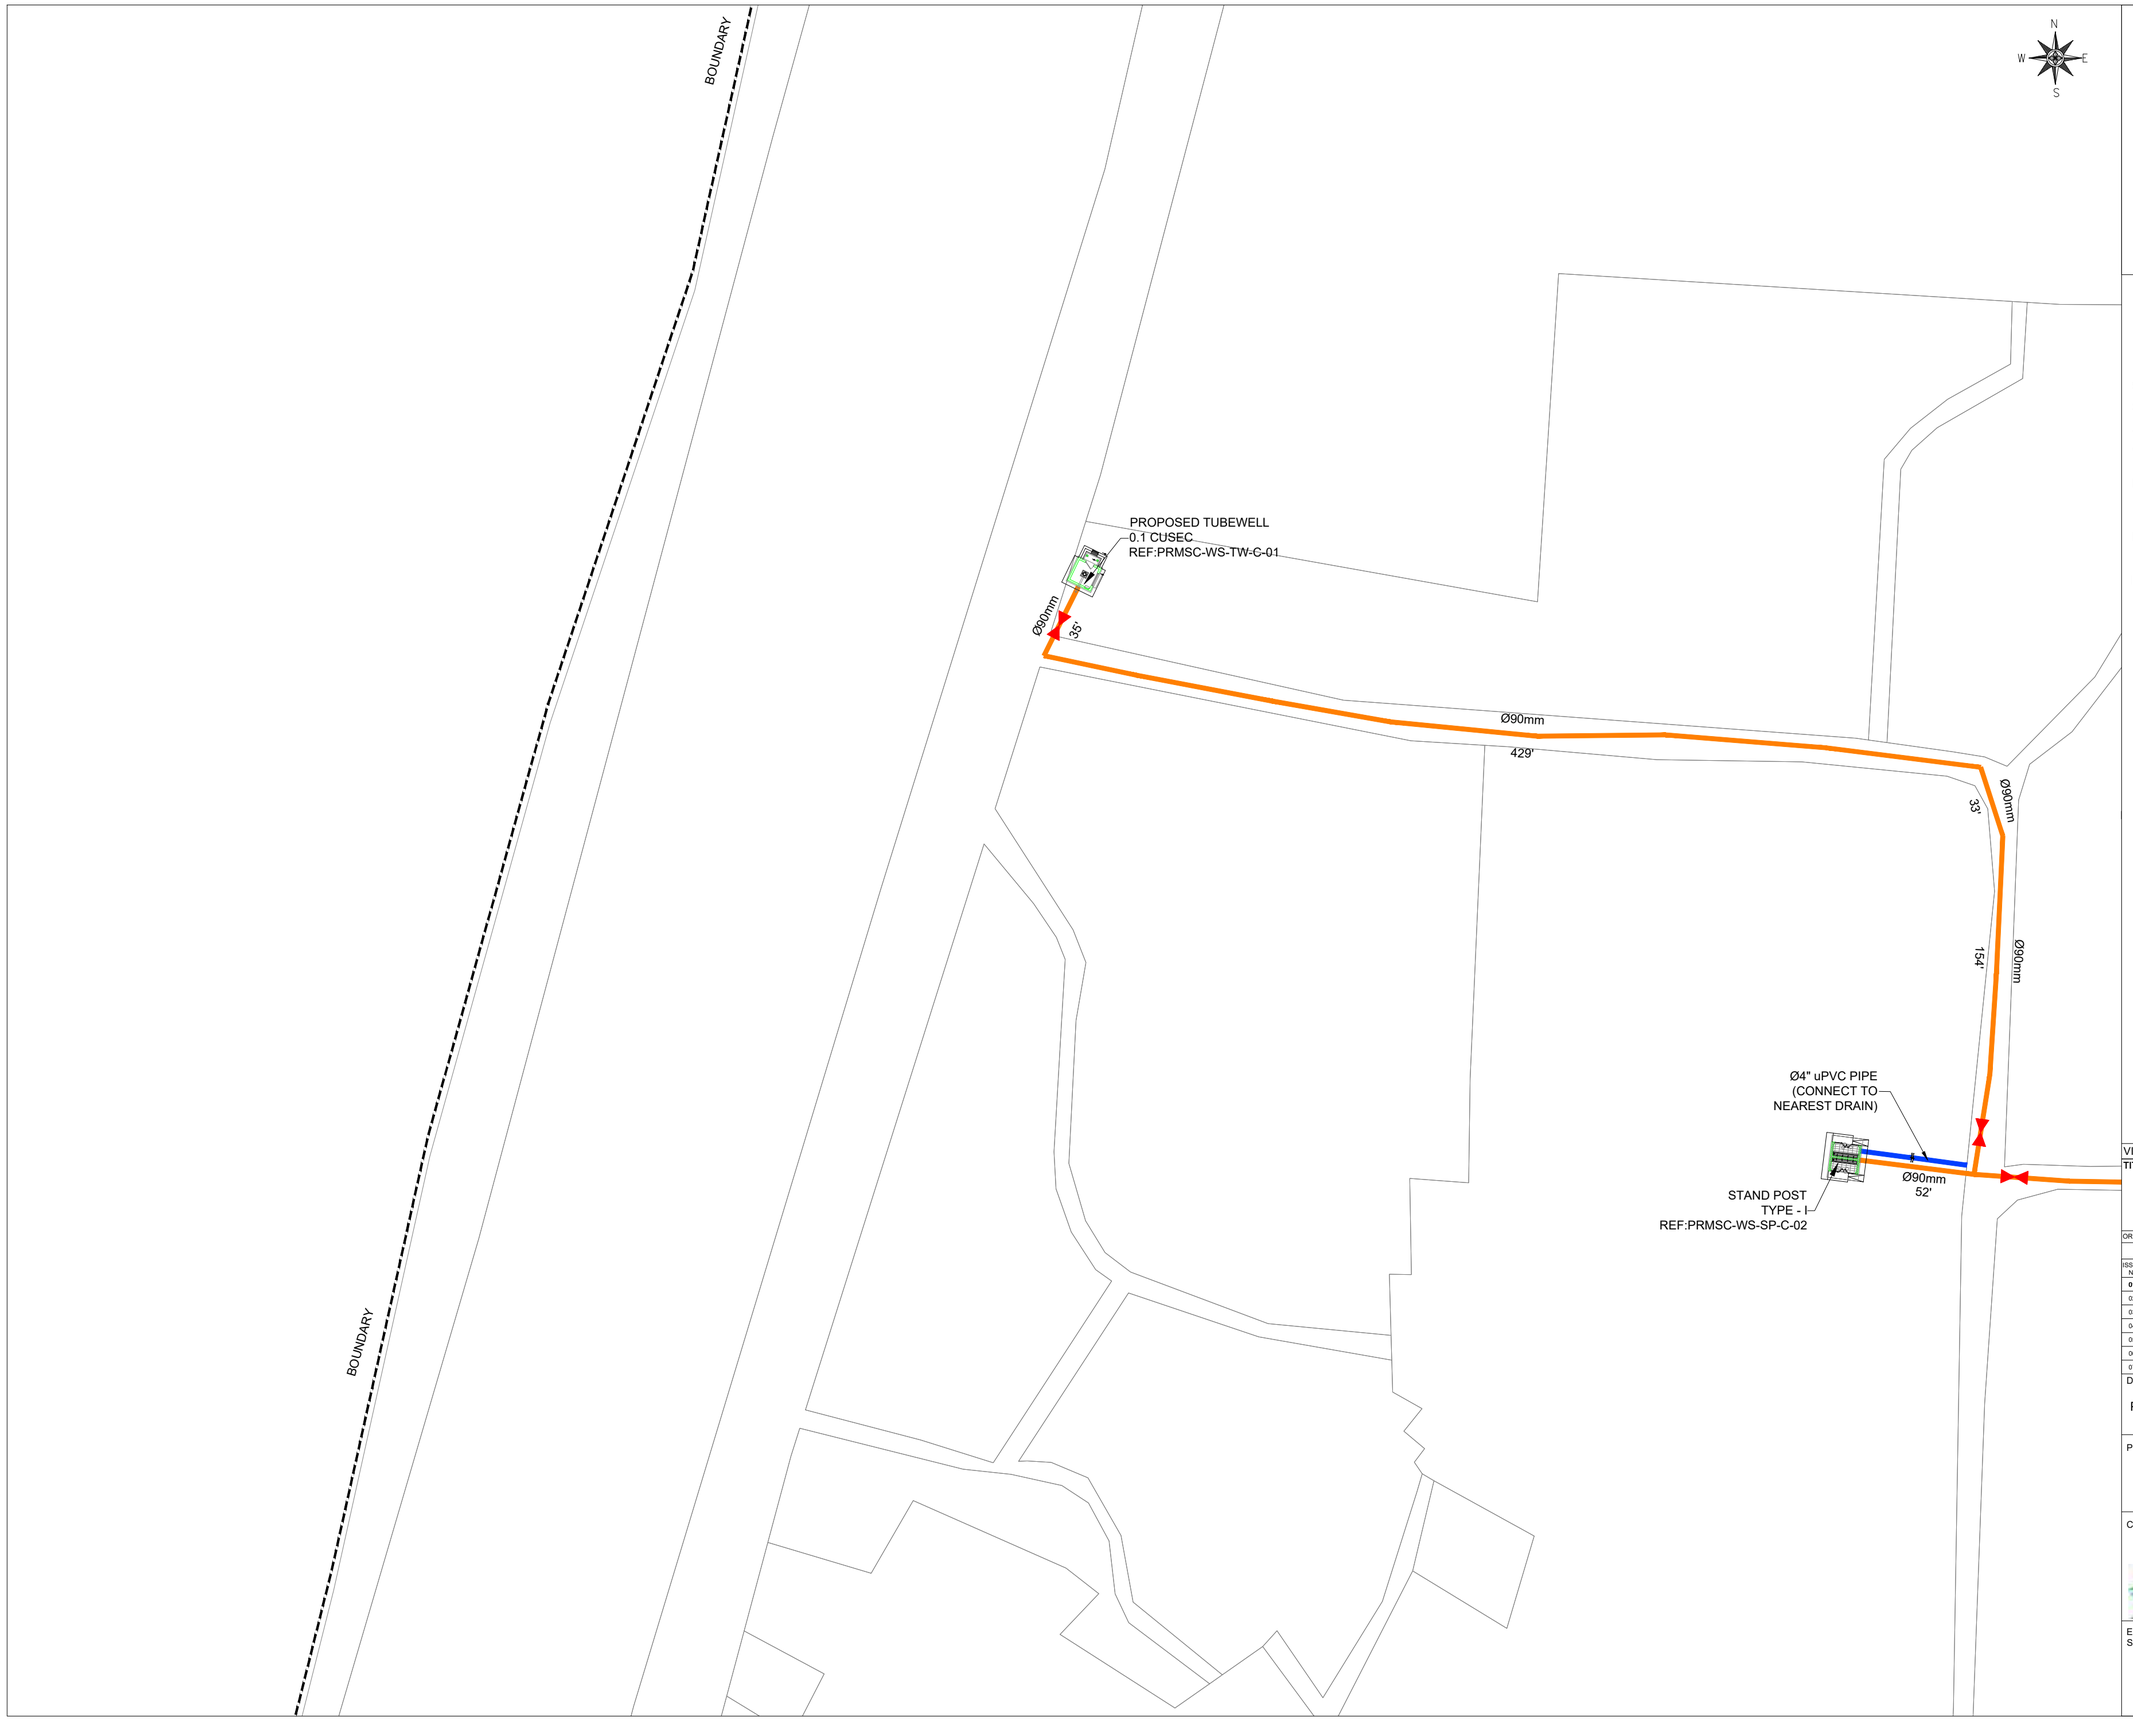



KEY PLAN

LEGEND:

- 90mm Ø HDPE PIPE
- SLUICE VALVE
- AIR RELEAS VALVE
- WASHOUT VALVE
- PROPOSED STAND POST TYPE-I
- PROPOSED TUBE WELL
- BOUNDARY

VILLAGE: SHER SINGH WALA (BWN)

TITLE.

WATER SUPPLY SYSTEM LAYOUT PLAN-01

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	02-01-2026	DETAILED DESIGN	MUNEEB	ENGR FAIEZ	ENGR IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº: PRMSC-BWN-SSW-WS-LP-01

SHEET 01 OF 12

REV 00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS
www.asiancon.com

PRMSC-BWN-SSW-SEW-LP-01

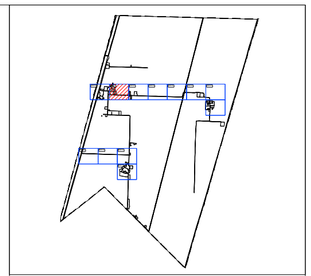

KEY PLAN

LEGEND:

90mm Ø HDPE PIPE

SLUICE VALVE

AIR RELEAS VALVE

WASHOUT VALVE

PROPOSED STAND POST TYPE-I

PROPOSED TUBE WELL

BOUNDARY

VILLAGE: SHER SINGH WALA (BWN)

TITLE.

WATER SUPPLY SYSTEM LAYOUT PLAN-02

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	02-01-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº: PRMSC-BWN-SSW-WS-LP-02

SHEET 02 OF 12

REV 00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:
ASIAN CONSULTING ENGINEERS
www.asianecon.com.pk

PRMSC-BWN-SSW-SEW-LP-02

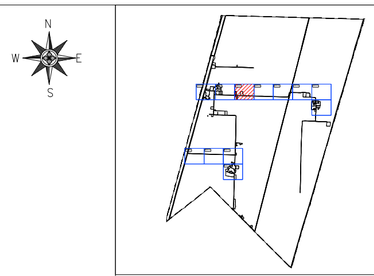

KEY PLAN

LEGEND:

90mm Ø HDPE PIPE

SLUICE VALVE

AIR RELEAS VALVE

WASHOUT VALVE

PROPOSED STAND POST TYPE-I

PROPOSED TUBE WELL

BOUNDARY

Ø90mm

3673'

PRMSC-BWN-SSW-SEW-LP-03

VILLAGE: SHER SINGH WALA (BWN)

TITLE.

WATER SUPPLY SYSTEM LAYOUT PLAN-03

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	02-01-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. HSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº: PRMSC-BWN-SSW-WS-LP-03

SHEET 03 OF 12

REV 00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS
www.asianconsultingengineers.com

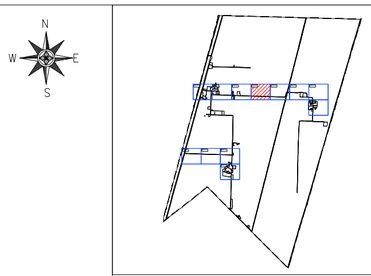

KEY PLAN

LEGEND:

90mm Ø HDPE PIPE

SLUICE VALVE

AIR RELEAS VALVE

WASHOUT VALVE

PROPOSED STAND POST TYPE-I

PROPOSED TUBE WELL

BOUNDARY

VILLAGE: SHER SINGH WALA (BWN)

TITLE.

WATER SUPPLY SYSTEM LAYOUT PLAN-04

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	02-01-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-SSW-WS-LP-04	04 OF 12	00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS (PVT) LTD. www.asiacon.com.pk

PRMSC-BWN-SSW-SEW-LP-04

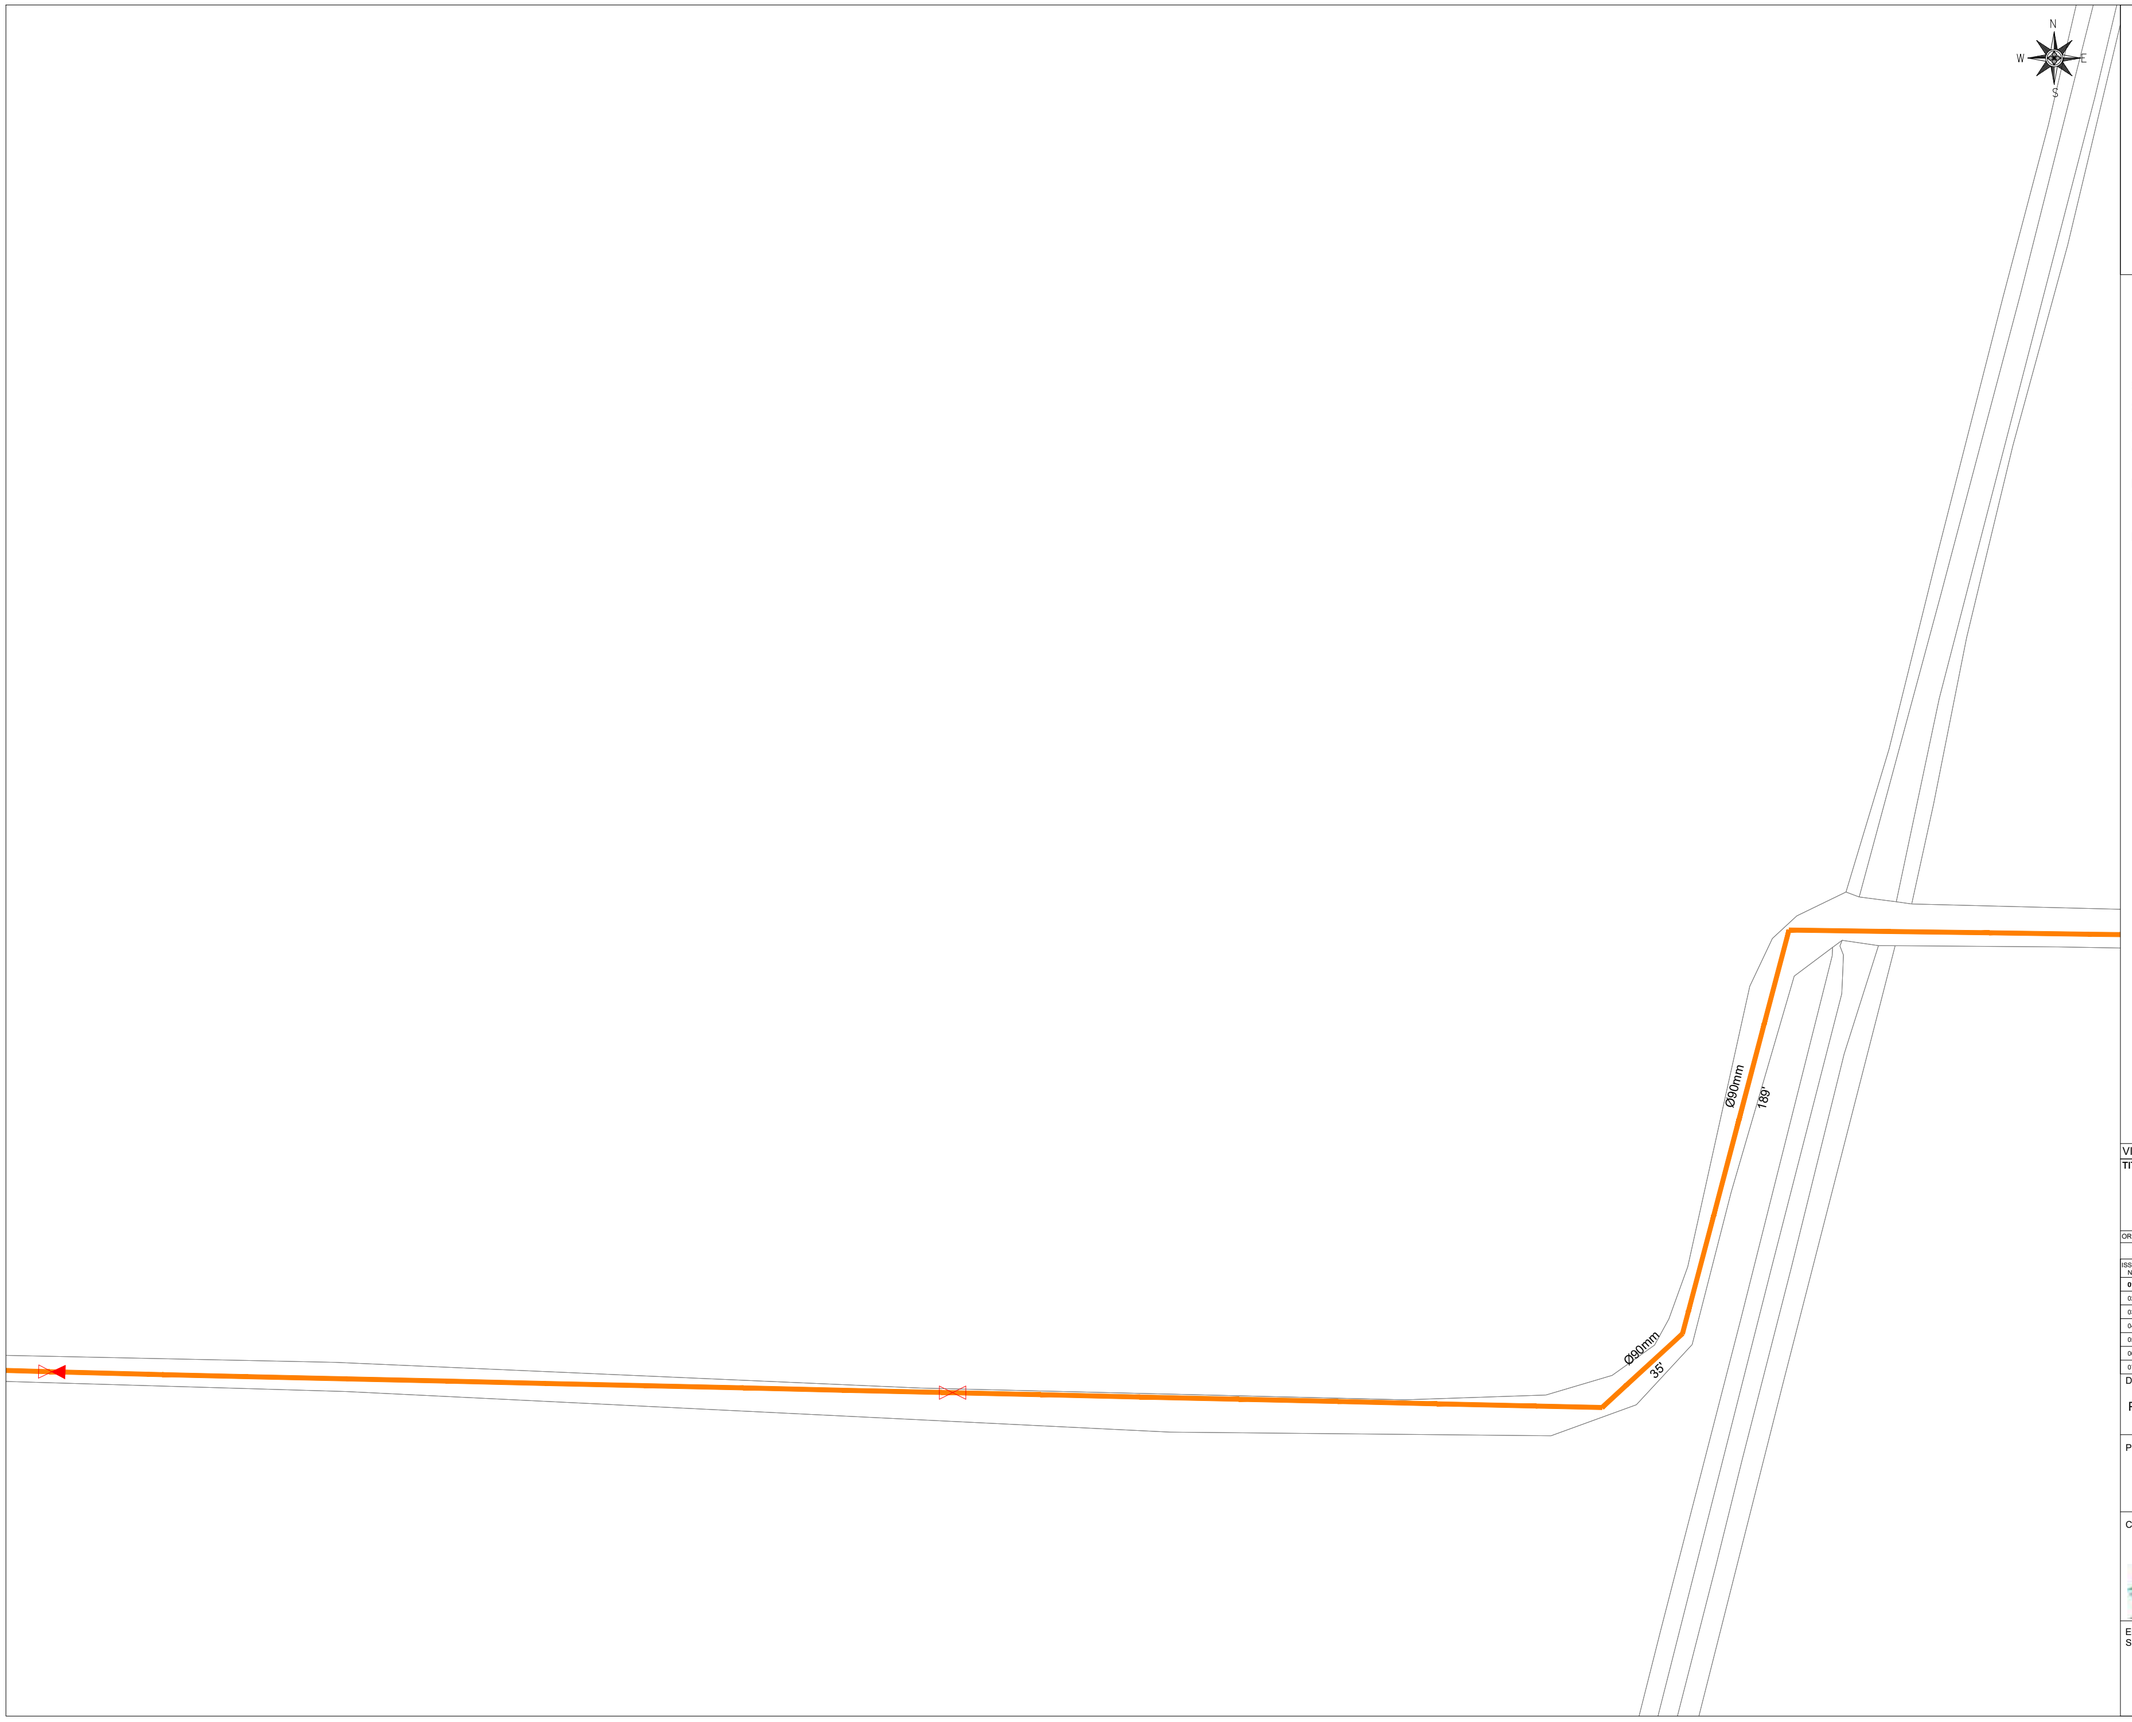

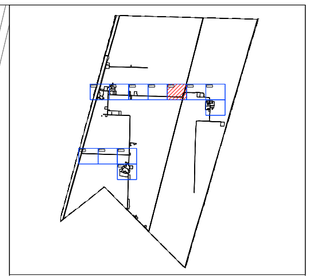

KEY PLAN

LEGEND:

90mm Ø HDPE PIPE

SLUICE VALVE

AIR RELEAS VALVE

WASHOUT VALVE

PROPOSED STAND POST TYPE-I

PROPOSED TUBE WELL

BOUNDARY

VILLAGE: SHER SINGH WALA (BWN)

TITLE.

WATER SUPPLY SYSTEM LAYOUT PLAN-05

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	02-01-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-SSW-WS-LP-05	05 OF 12	00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

PRMSC-BWN-ssw-SEW-LP-05

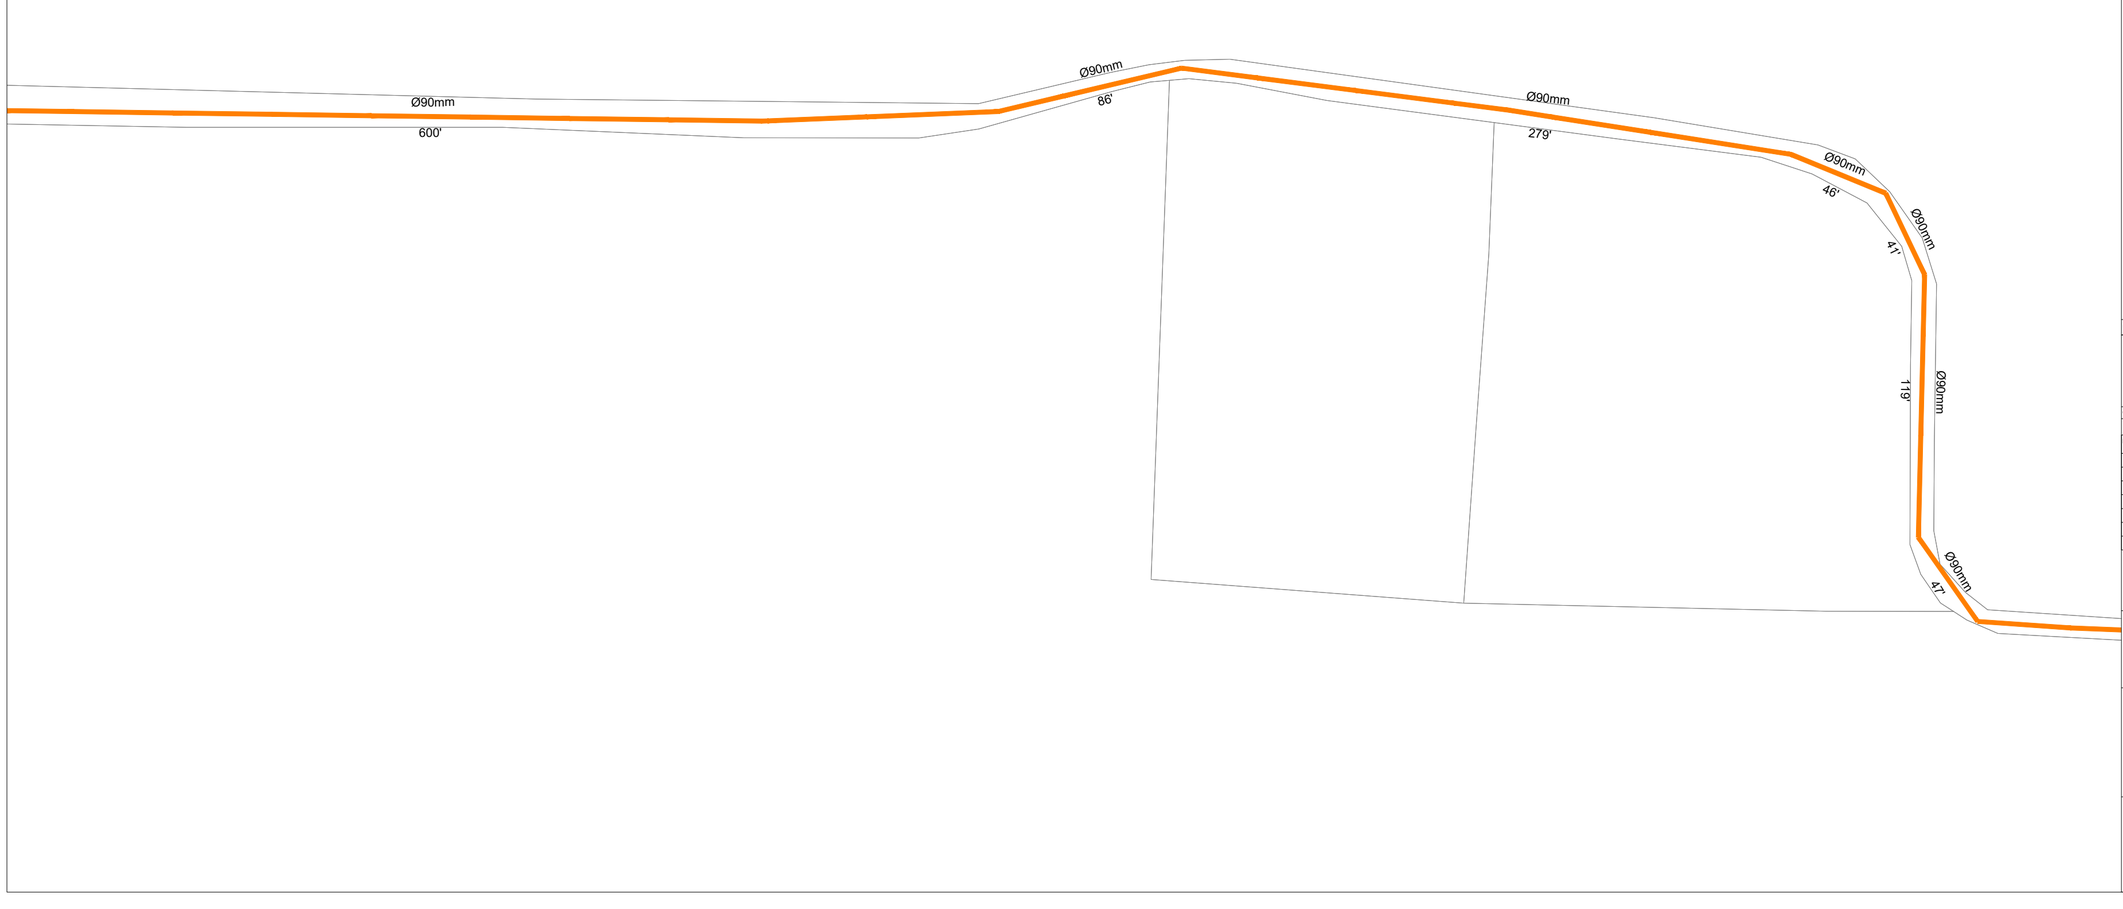

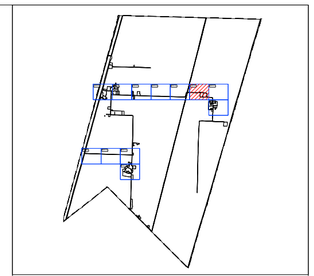

KEY PLAN

LEGEND:

- 90mm Ø HDPE PIPE
- SLUICE VALVE
- AIR RELEAS VALVE
- WASHOUT VALVE
- PROPOSED STAND POST TYPE-I
- PROPOSED TUBE WELL
- BOUNDARY

VILLAGE: SHER SINGH WALA (BWN)

TITLE.

WATER SUPPLY SYSTEM LAYOUT PLAN-06

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	02-01-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-SSW-WS-LP-06	06 OF 12	00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:
ASIAN CONSULTING ENGINEERS
www.asiacon.com.pk

PRMSC-BWN-SSW-SEW-LP-06

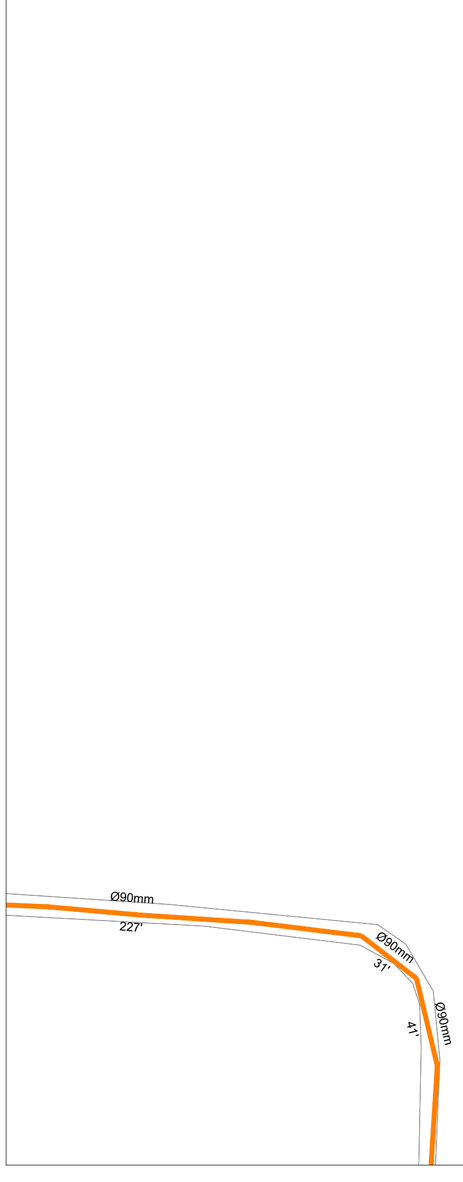

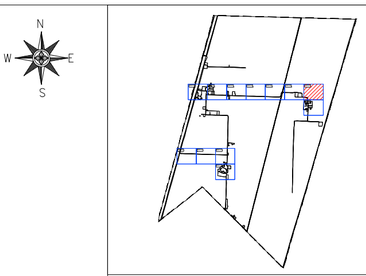

KEY PLAN

LEGEND:

- 90mm Ø HDPE PIPE
- SLUICE VALVE
- AIR RELEAS VALVE
- WASHOUT VALVE
- PROPOSED STAND POST TYPE-I
- PROPOSED TUBE WELL
- BOUNDARY

VILLAGE: SHER SINGH WALA (BWN)

TITLE.

WATER SUPPLY SYSTEM LAYOUT PLAN-07

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	02-01-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-SSW-WS-LP-07	07 OF 12	00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

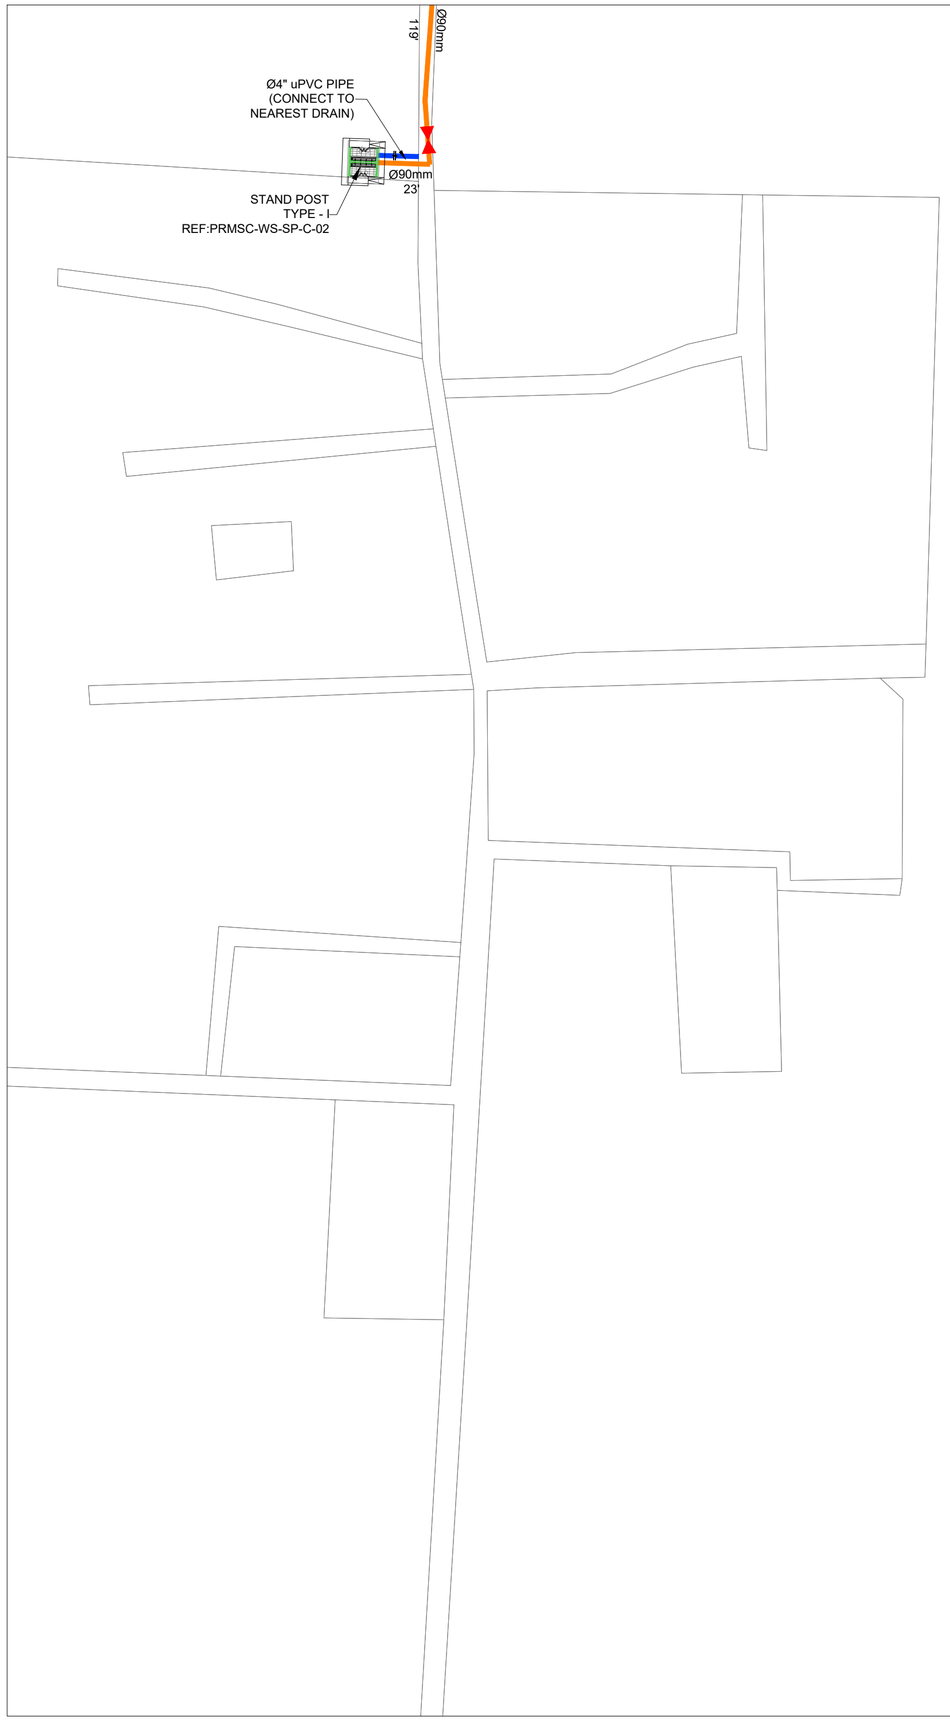

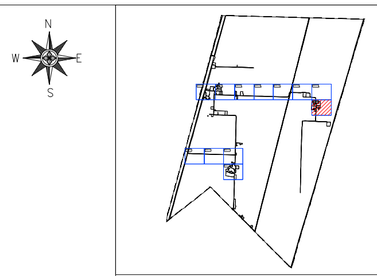

KEY PLAN

LEGEND:

- 90mm Ø HDPE PIPE
- SLUICE VALVE
- AIR RELEAS VALVE
- WASHOUT VALVE
- PROPOSED STAND POST TYPE-I
- PROPOSED TUBE WELL
- BOUNDARY

VILLAGE: SHER SINGH WALA (BWN)

TITLE.

WATER SUPPLY SYSTEM LAYOUT PLAN-08

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	02-01-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº: PRMSC-BWN-SSW-WS-LP-08

SHEET 08 OF 12

REV 00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:
ASIAN CONSULTING ENGINEERS
www.asiancon.com

PRMSC-BWN-SSW-SEW-LP-08

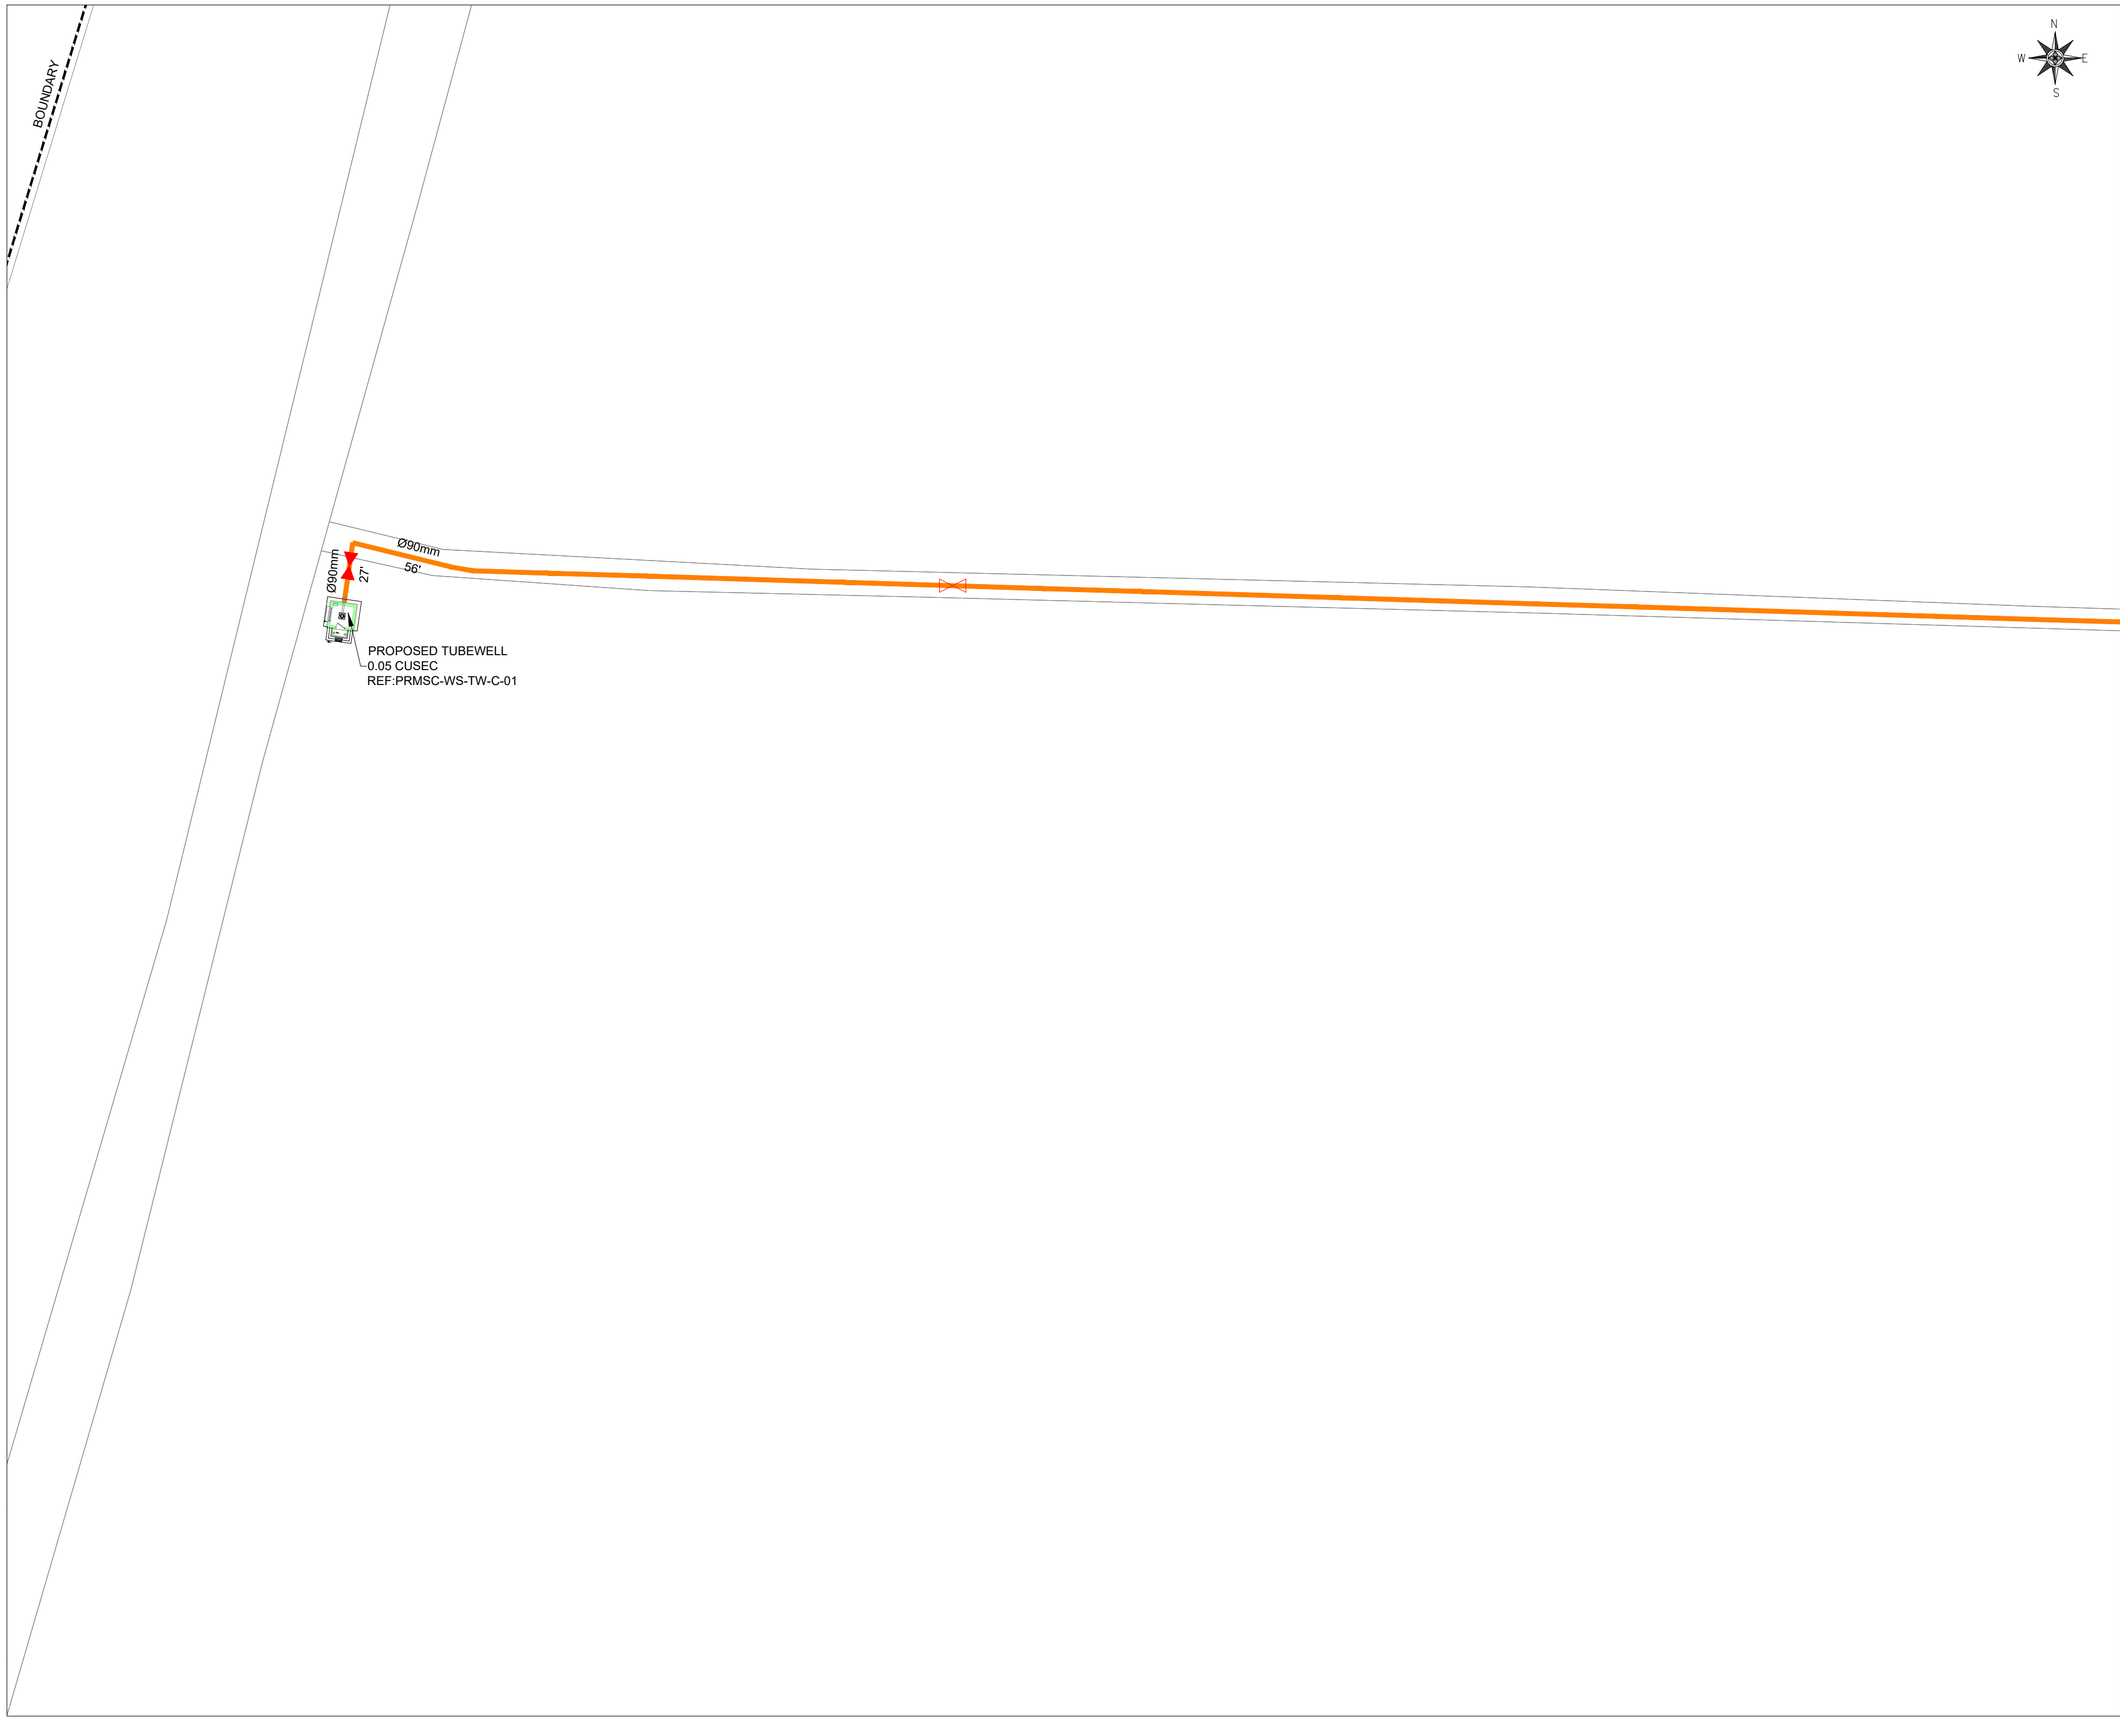



KEY PLAN

LEGEND:

- 90mm Ø HDPE PIPE
- SLUICE VALVE
- AIR RELEAS VALVE
- WASHOUT VALVE
- PROPOSED STAND POST TYPE-I
- PROPOSED TUBE WELL
- BOUNDARY

VILLAGE: SHER SINGH WALA (BWN)

TITLE.

WATER SUPPLY SYSTEM LAYOUT PLAN-09

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	02-01-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-SSW-WS-LP-09	09 OF 12	00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:
ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

PRMSC-BWN-SSW-WS-LP-9



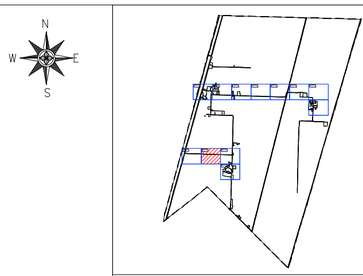

KEY PLAN

LEGEND:

90mm Ø HDPE PIPE

SLUICE VALVE

AIR RELEAS VALVE

WASHOUT VALVE

PROPOSED STAND POST TYPE-I

PROPOSED TUBE WELL

BOUNDARY

VILLAGE: SHER SINGH WALA (BWN)

TITLE.

WATER SUPPLY SYSTEM LAYOUT PLAN-10

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	02-01-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-SSW-WS-LP-10	10 OF 12	00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ENVIRONMENTAL MANAGEMENT

ASIAN CONSULTING ENGINEERS

www.asiancon.com.pk

PRMSC-BWN-SSW-WS-LP-10

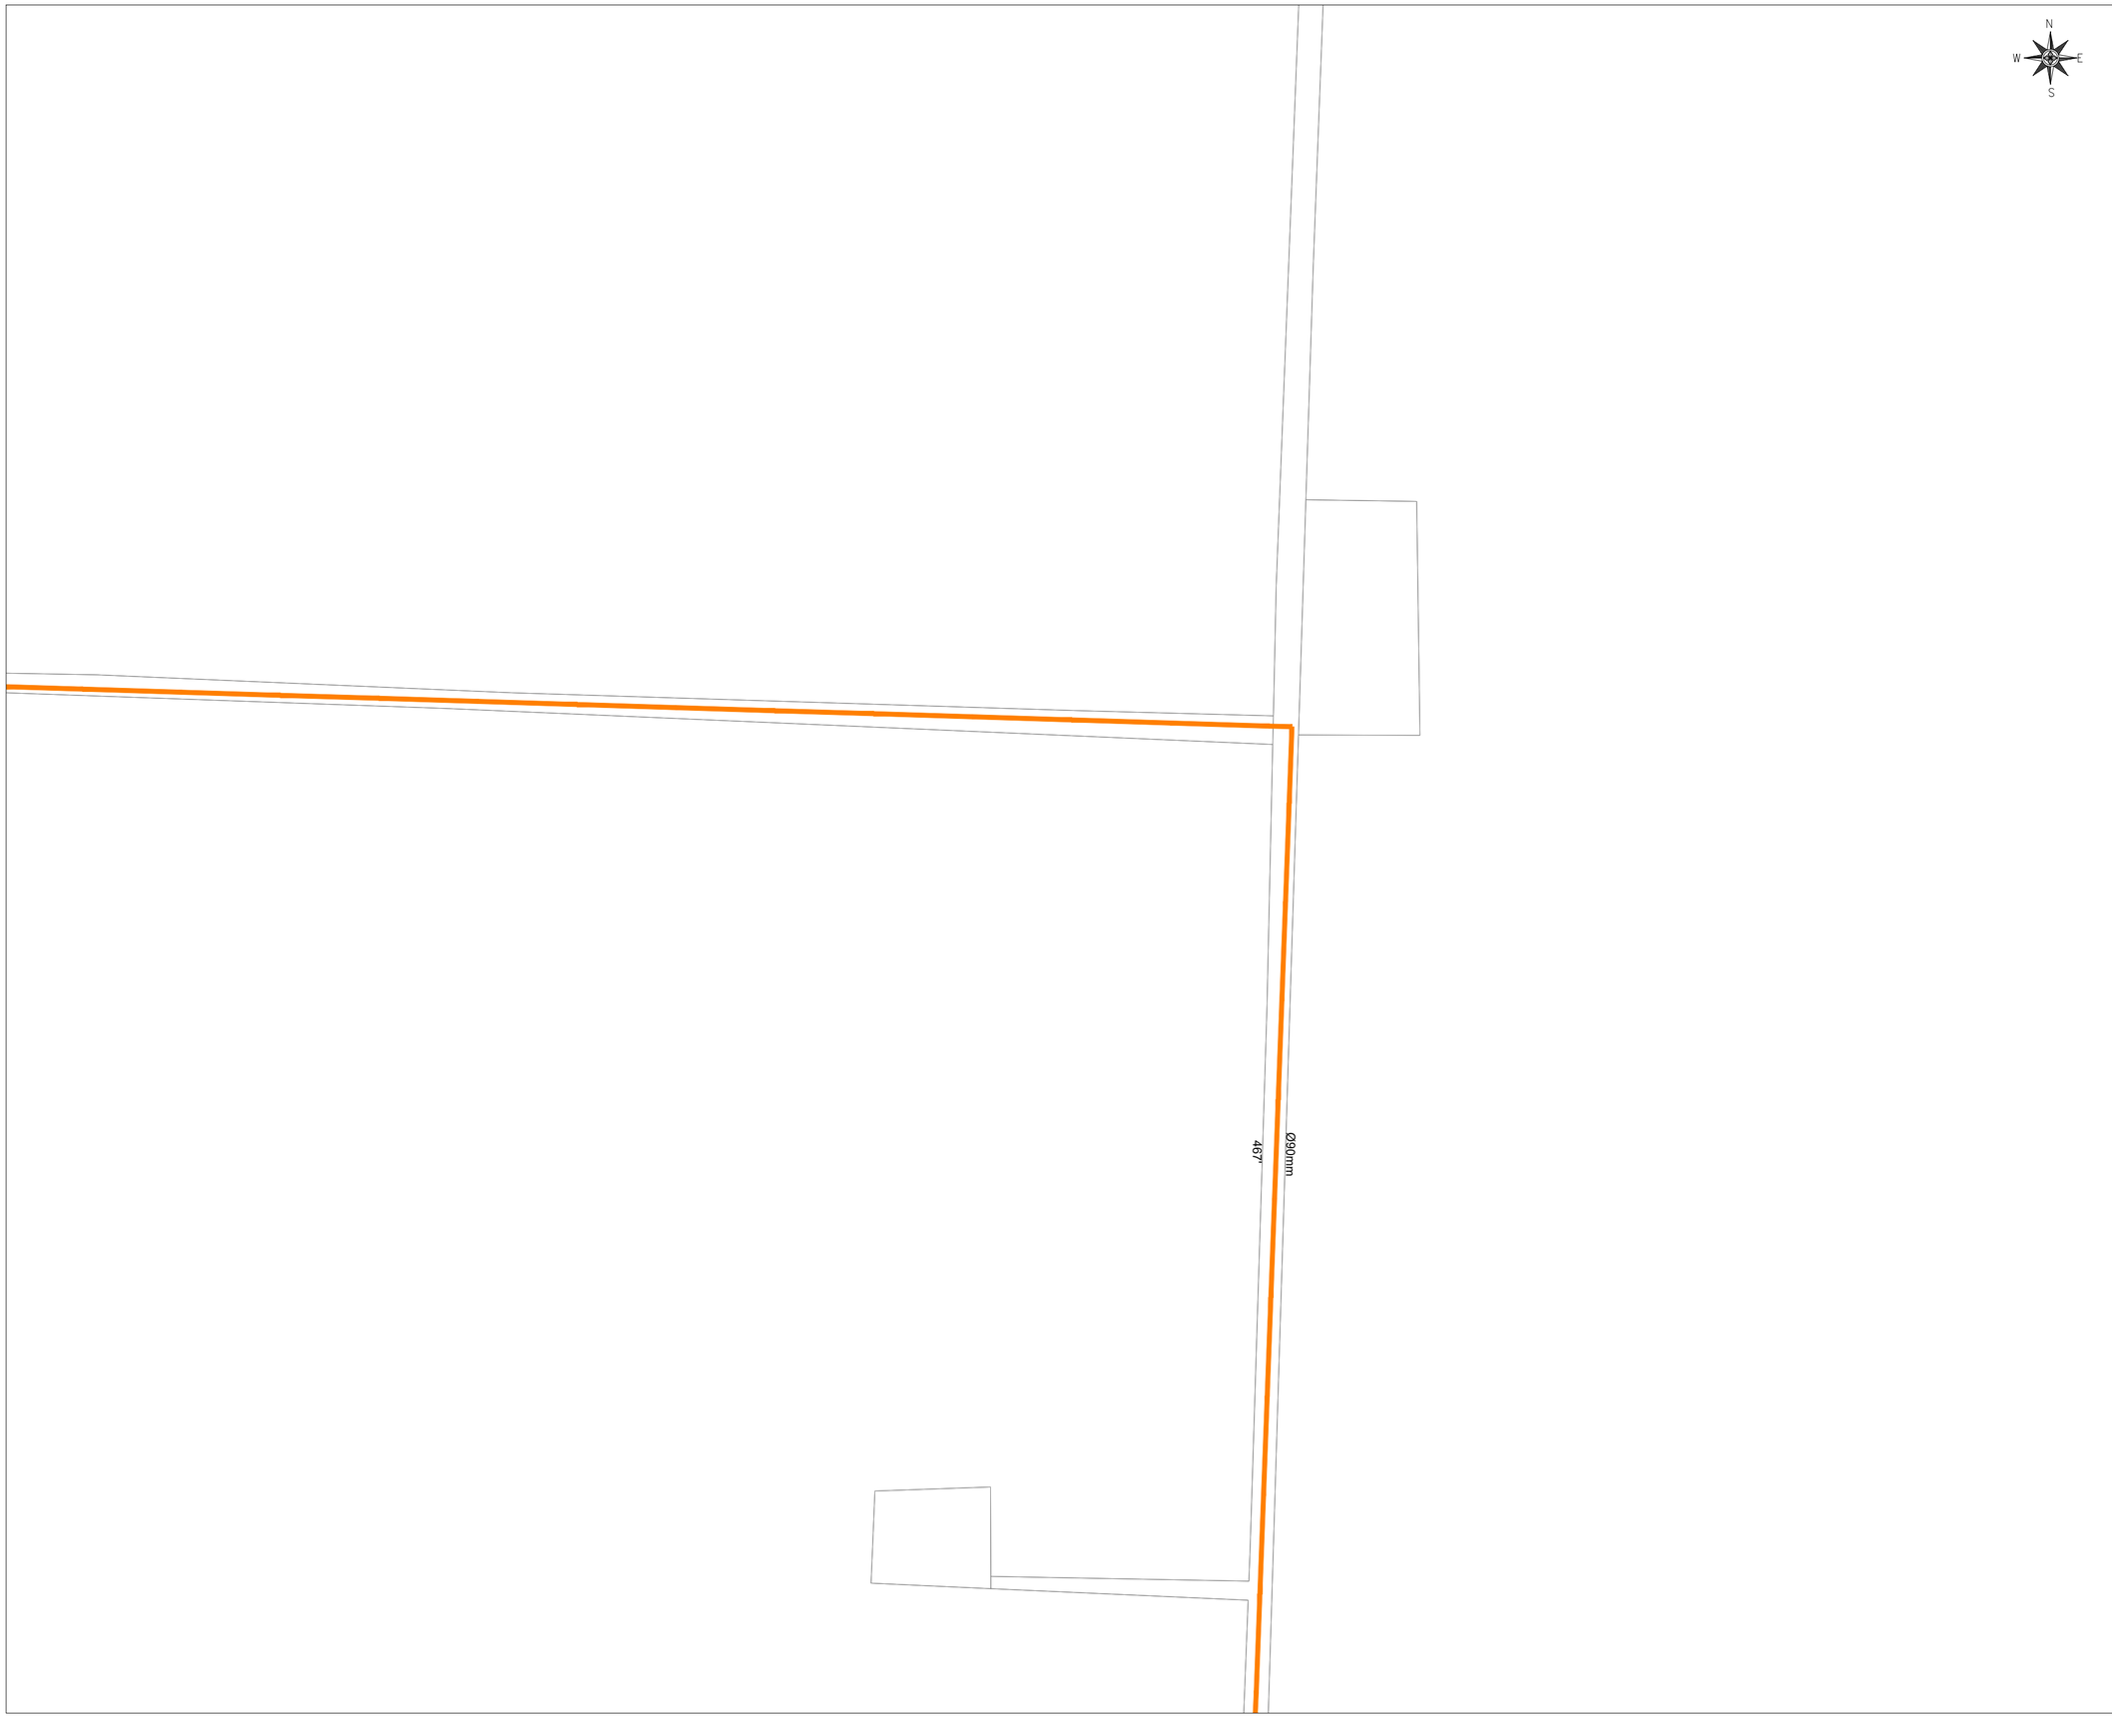

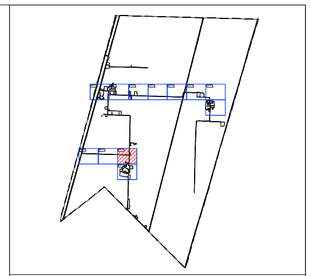

KEY PLAN

LEGEND:

- 90mm Ø HDPE PIPE
- SLUICE VALVE
- AIR RELEAS VALVE
- WASHOUT VALVE
- PROPOSED STAND POST TYPE-I
- PROPOSED TUBE WELL
- BOUNDARY

VILLAGE: SHER SINGH WALA (BWN)

TITLE.

WATER SUPPLY SYSTEM LAYOUT PLAN-11

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	02-01-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-SSW-WS-LP-11	11 OF 12	00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

PRMSC-BWN-SSW-WS-LP-11

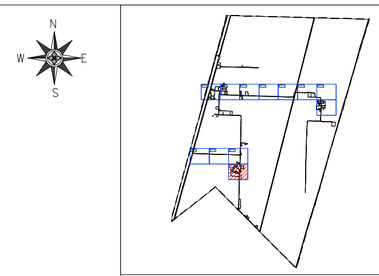

KEY PLAN

LEGEND:

- 90mm Ø HDPE PIPE
- SLUICE VALVE
- AIR RELEAS VALVE
- WASHOUT VALVE
- PROPOSED STAND POST TYPE-I
- PROPOSED TUBE WELL
- BOUNDARY

VILLAGE: SHER SINGH WALA (BWN)

TITLE.

WATER SUPPLY SYSTEM LAYOUT PLAN-12

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	02-01-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-SSW-WS-LP-12	12 OF 12	00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

PRMSC-BWN-SSW-WS-LP-12

TYPICAL DETAILS

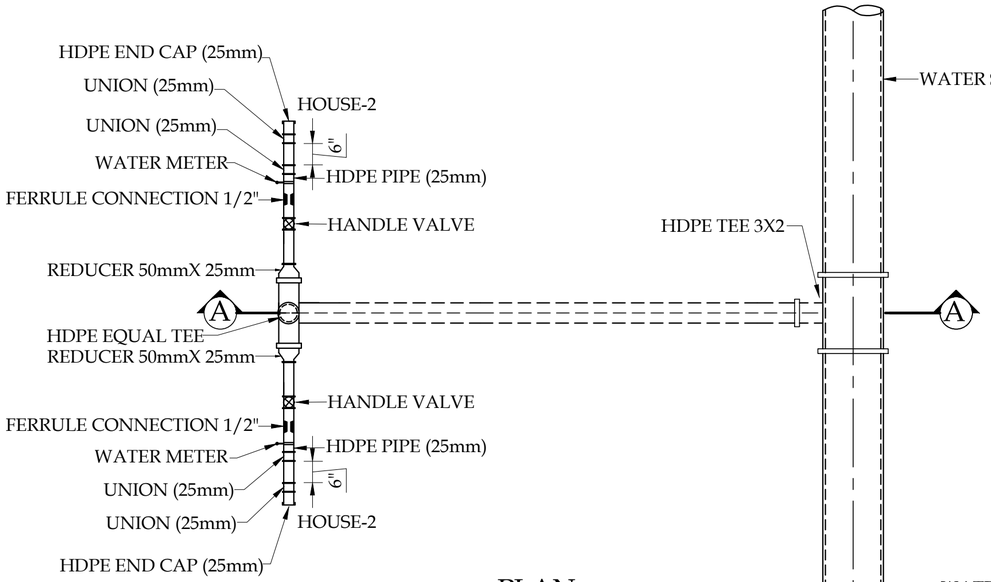

PLAN
DETAIL "A"

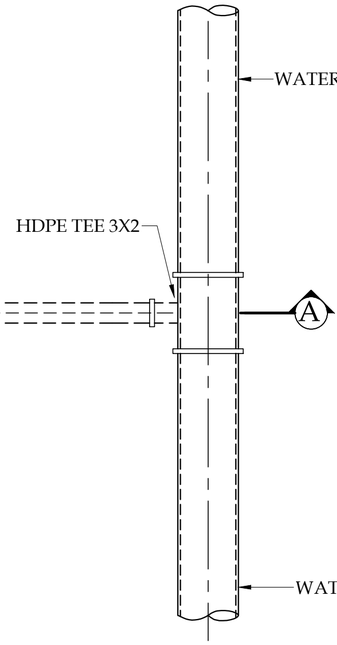

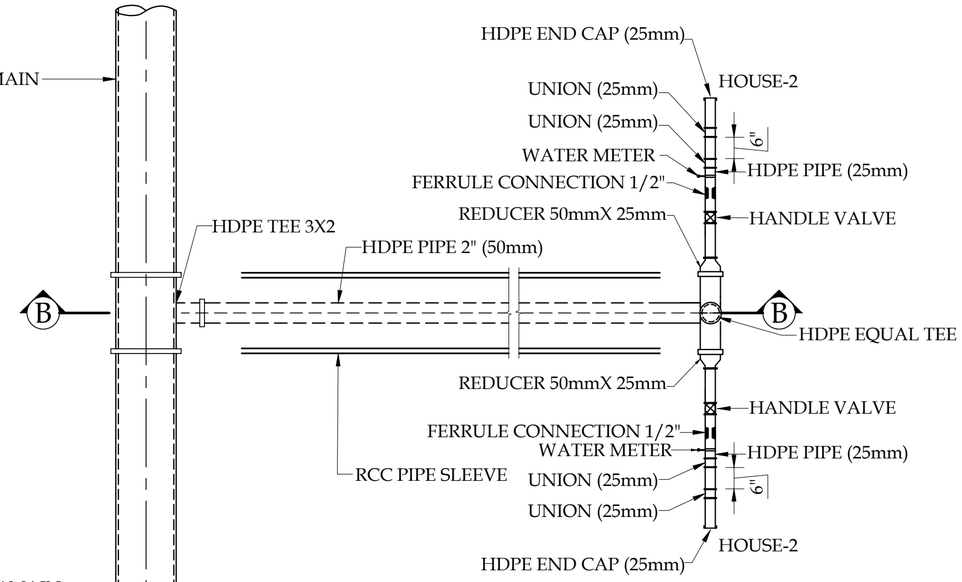

PLAN
DETAIL "B"

NOTES:-

1. ALL DIMENSIONS ARE IN FEET UNLESS OTHER STATED.
2. EXACT LOCATION OF WATER SUPPLY CHAMBER TO BE FINALIZED AND ADJUST AS PER SITE WITH PRIOR APPROVAL OF THE ENGINEER.
3. SULPHATE RESISTANT CEMENT SHALL BE USE FOR CONSTRUCTION OF THE CHAMBER.

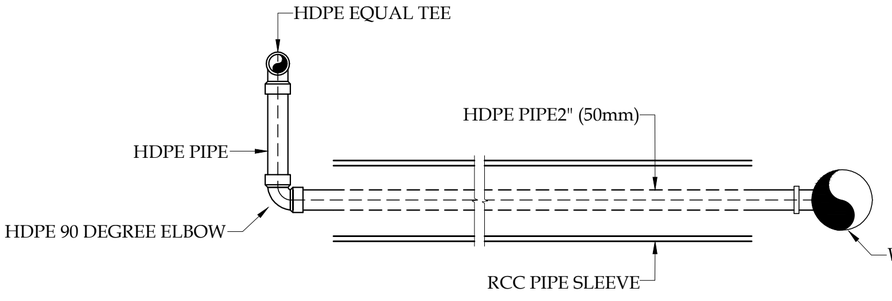

DETAIL FOR HOUSE CONNECTION (ADJACENT TO THE ROAD)
SECTION A-A
DETAIL "A"

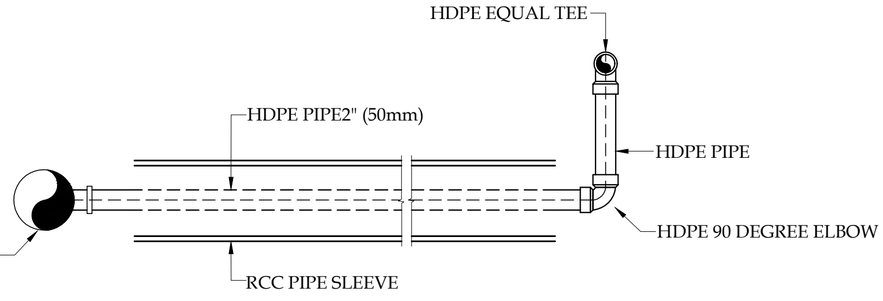

DETAIL FOR HOUSE CONNECTION (ACROSS THE ROAD)
SECTION B-B
DETAIL "B"

TITLE.
HOUSE CONNECTION DETAIL
DETAIL - (A & B)

ORIGINAL :		DATE :		SCALE :	
A2		JULY, 2025			
ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	02-12-2025	DETAILED DESIGN	ASAD	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING N°: PRMSC-WS-TD-01 | SHEET | REV 00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:
ASIAN CONSULTING ENGINEERS
www.asinco.com.pk

PRMSC-WS-TD-01

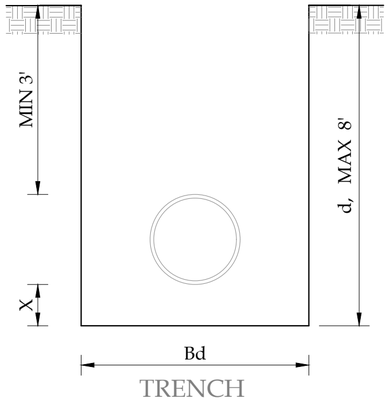

TRENCH

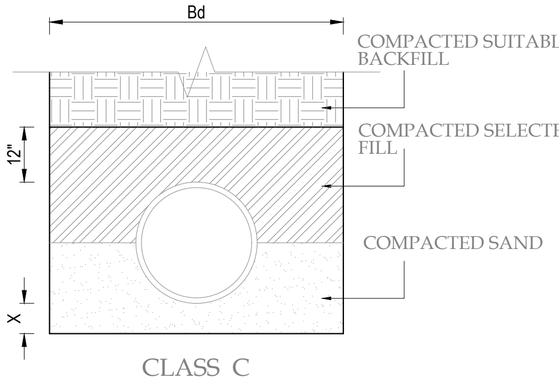

CLASS C

SCALE:- 1" = 1'-0"

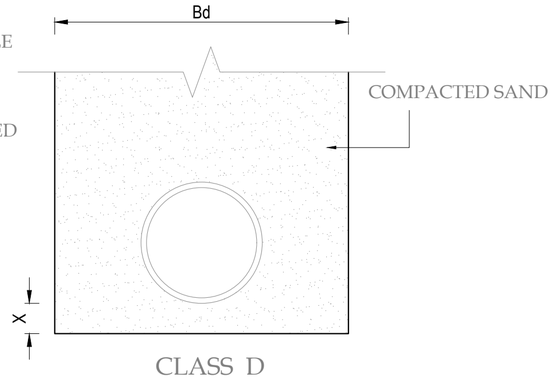

CLASS D

SCALE:- 1" = 1'-0"

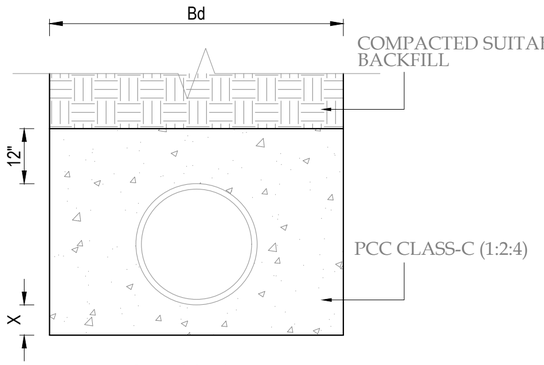

CLASS A

SCALE:- 1" = 1'-0"

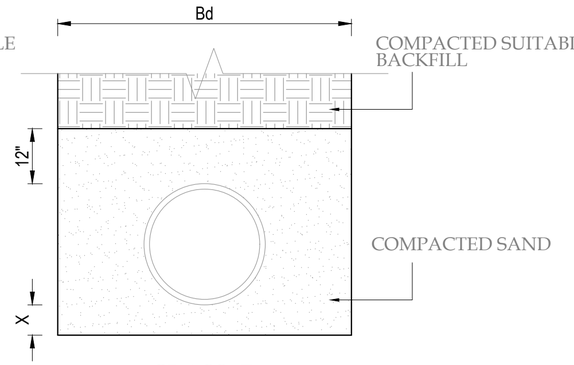

CLASS B

SCALE:- 1" = 1'-0"

(P&D REQUIREMENT)

NOTES:

1. 'Bd' IS TRENCH WIDTH.
2. USE CLASS 'C' BEDDING UNDER NORMAL COVER OF 3' AND LIGHT TRAFFIC.
3. USE CLASS 'B' BEDDING UNDER NORMAL COVER OF 3' AND HEAVY TRAFFIC.
4. USE CLASS 'A' BEDDING WHERE COVER IS LESS THAN 3' AND HEAVY TRAFFIC.
5. ALLOW CONCRETE TO ATTAIN STRENGTH OF AT LEAST 2,000 PSI BEFORE BACKFILLING THE TRENCH
6. VALUES OF 'X' ARE PRESENT IN TABLE.

PIPE DIA	TRENCH WIDTH (Bd)	X
90mm - 180mm	1'-6"	4"
200mm	2'-0"	4"
250mm	2'-0"	5"
280mm	2'-0"	6"
315mm	2'-6"	7"
355mm	2'-6"	8"

TITLE.

TYPICAL DETAILS
TRENCH & BEDDING DETAILS

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 1'-0"

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	02-12-2025	DETAILED DESIGN	ASAD	ENGR. FAIEZ	ENGR. HSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING N°: PRMSC-WS-TD-02

SHEET 1 OF 1

REV 00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ENVIRONMENTAL TECHNOLOGIES

ASIAN CONSULTING ENGINEERS www.asiancon.com

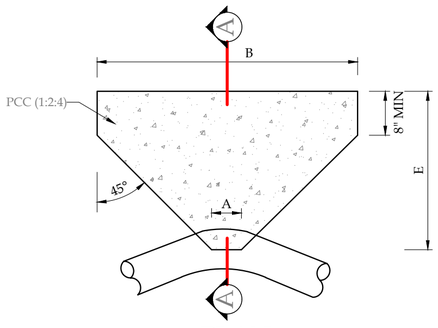

PLAN

SCALE:- 1/2" = 1'-0"

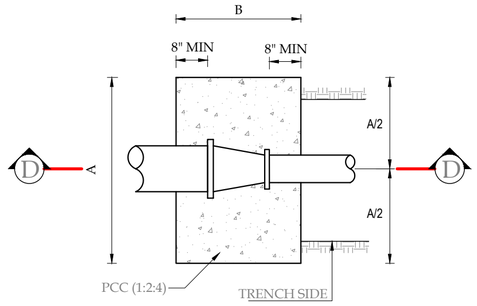

PLAN

SCALE:- 1/2" = 1'-0"

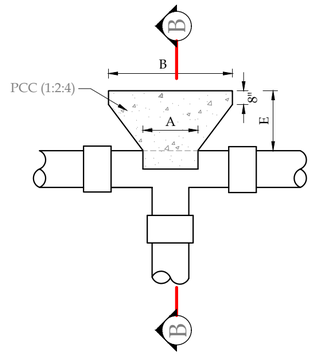

PLAN

SCALE:- 1/2" = 1'-0"

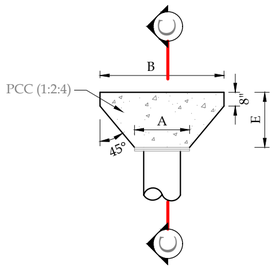

PLAN

SCALE:- 1/2" = 1'-0"



SECTION A-A

SCALE:- 1/2" = 1'-0"

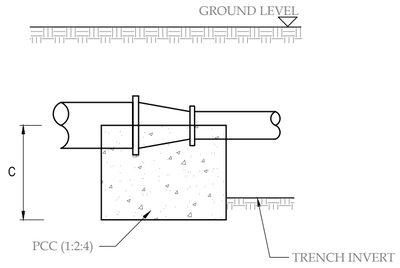

SECTION D-D

SCALE:- 1/2" = 1'-0"



SECTION B-B

SCALE:- 1/2" = 1'-0"

TEES



SECTION C-C

SCALE:- 1/2" = 1'-0"

DEAD END

PIPE DIA (mm)	BEND	11.25 °	22.50 °	45.00 °	90.00 °
90	H	1'-6"	1'-6"	1'-6"	1'-6"
	A	6"	6"	6"	8"
	B	1'	1'	1'	1'-4"
	E	11"	11"	11"	12"
110	H	1'-6"	1'-6"	1'-6"	1'-6"
	A	6"	6"	9"	1'-0"
	B	12"	12"	1'-3"	2'-0"
	E	11"	11"	11"	1'-2"
160	H	2'-0"	2'-0"	2'-0"	2'-0"
	A	6"	12"	1'-3"	1'-4"
	B	12"	1'-6"	2'-3"	3'-0"
	E	11"	11"	1'-2"	1'-6"
200	H	2'-0"	2'-0"	2'-0"	2'-0"
	A	10"	12"	1'-4"	1'-5"
	B	1'-6"	2'	3'-0"	3'-9"
	E	12"	1'-2"	1'-6"	1'-10"
250	H	2'-6"	2'-6"	2'-6"	2'-6"
	A	12"	1'-5"	1'-5"	1'-10"
	B	2'-0"	2'-9"	3'-9"	5'-0"
	E	1'-2"	1'-4"	1'-10"	2'-3"
315	H	2'-6"	2'-6"	2'-6"	2'-6"
	A	1'-4"	1'-4"	1'-10"	2'-10"
	B	2'-6"	3'-0"	4'-6"	6'-0"
	E	1'-3"	1'-6"	2'-0"	2'-9"

TAPER SIZE (mm)	DIMENSIONS	
110-90	A	3'-0"
	B	1'-9"
	C	1'-6"
160-90	A	3'-9"
	B	2'-6"
	C	1'-9"
160-110	A	3'-3"
	B	2'-6"
	C	1'-9"
200-110	A	4'-0"
	B	2'-6"
	C	1'-9"
200-160	A	4'-0"
	B	2'-6"
	C	1'-9"
250-160	A	5'-0"
	B	2'-6"
	C	2'-0"
250-200	A	4'-3"
	B	2'-6"
	C	2'-0"
315-160	A	6'-6"
	B	2'-9"
	C	2'-3"
315-200	A	6'-0"
	B	2'-9"
	C	2'-3"
315-250	A	4'-9"
	B	2'-9"
	C	2'-3"

TEES

PIPE DIA (mm)	DIMENSIONS	
90	H	1'-6"
	A	11"
	B	1'-9"
	E	1'-1"
110	H	1'-6"
	A	11"
	B	2'-3"
	E	1'-4"
160	H	2'-0"
	A	10"
	B	3'-0"
	E	1'-9"
200	H	2'-0"
	A	1'-4"
	B	4'-6"
	E	2'-3"
250	H	2'-6"
	A	1'-10"
	B	6'-0"
	E	2'-9"
315	H	2'-6"
	A	1'-10"
	B	7'-0"
	E	3'-3"

DEAD ENDS

PIPE DIA (mm)	DIMENSIONS	
90	H	1'-6"
	A	7"
	B	1'-3"
	E	12"
110	H	1'-6"
	A	10"
	B	1'-6"
	E	12"
160	H	2'-0"
	A	10"
	B	2'-6"
	E	1'-6"
200	H	2'-0"
	A	1'-2"
	B	3'
	E	1'-7"
250	H	2'-6"
	A	1'-5"
	B	3'-9"
	E	1'-10"
315	H	2'-6"
	A	1'-4"
	B	4'-6"
	E	2'-3"

TITLE.

TYPICAL DETAILS THRUST BLOCKS - HORIZONTAL

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1/2" = 1'-0"

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	02-12-2025	DETAILED DESIGN	ASAD	ENGR. FAIEZ	ENGR. IRSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº: PRMSC-WS-TD-03 | SHEET 1 OF 1 | REV 00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:
ASIAN CONSULTING ENGINEERS www.asiancon.com

PRMSC-WS-TD-03

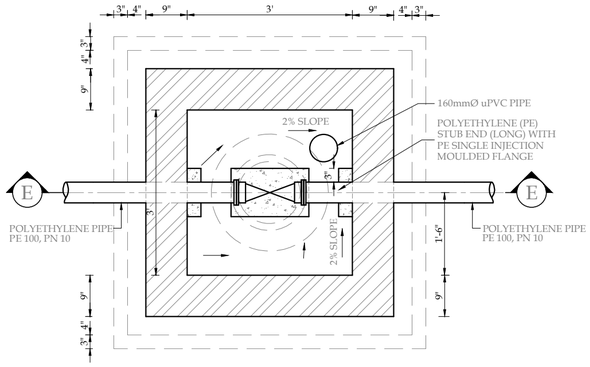

SECTIONAL PLAN
GATE VALVE

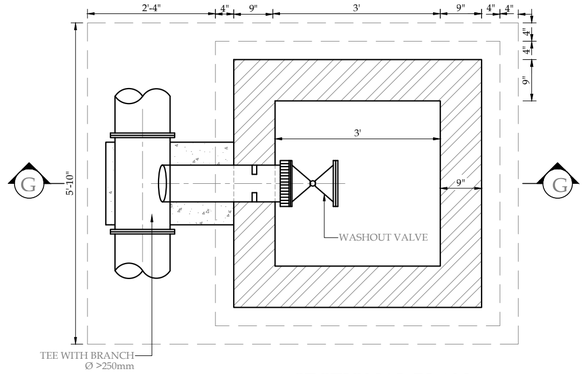

SECTIONAL PLAN
WASHOUT VALVE

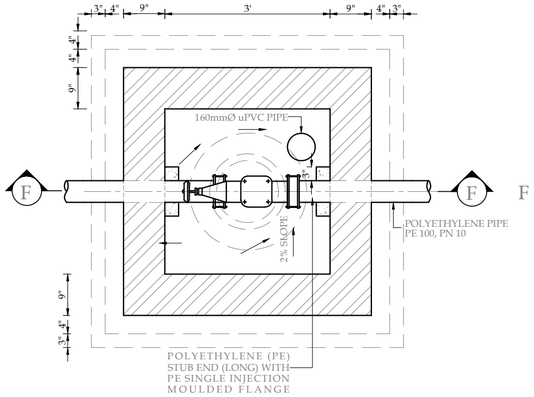

SECTIONAL PLAN
AIR RELEASE VALVE

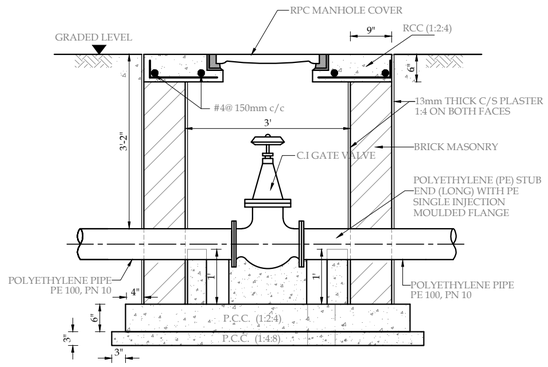

SECTION E-E

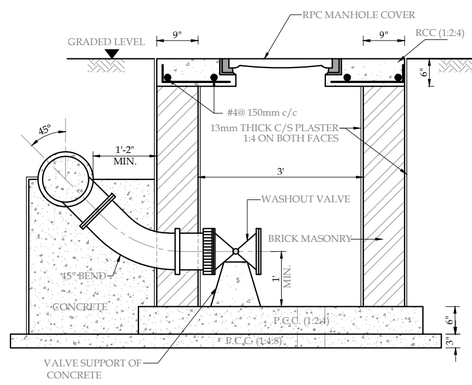

SECTION G-G

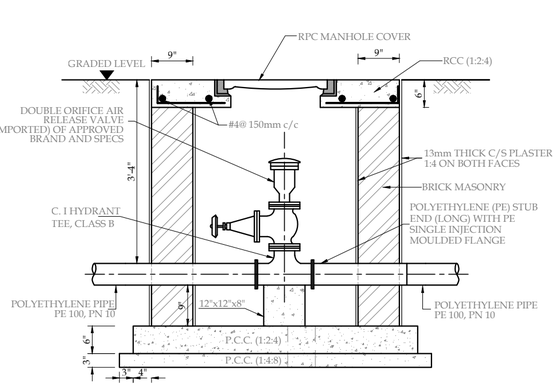

SECTION F-F

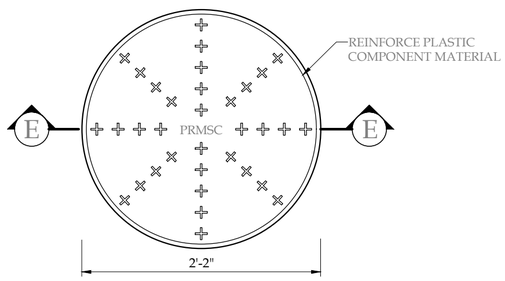

RPC MANHOLE COVER PLAN
SCALE:- 1" = 1'-0"



SECTION AT E-E
SCALE:- 1" = 1'-0"

TITLE.
TYPICAL DETAILS
VALVE CHAMBER &
MANHOLE COVER DETAILS

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	02-12-2025	DETAILED DESIGN	ASAD	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING N°: PRMSC-WS-TD-04
SHEET 1 OF 1
REV 00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:
ASIAN CONSULTING ENGINEERS
www.asiancon.com

PRMSC-WS-TD-04

STAND POST TYPE - I

VIEW-I

VIEW-II

VIEW-III

CUT OUT PLAN

TITLE.

3D IMAGES

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	05-12-2025	DETAILED DESIGN	ASAD	ENGR. FAEIZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-WS-SP-C-01		00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

Images

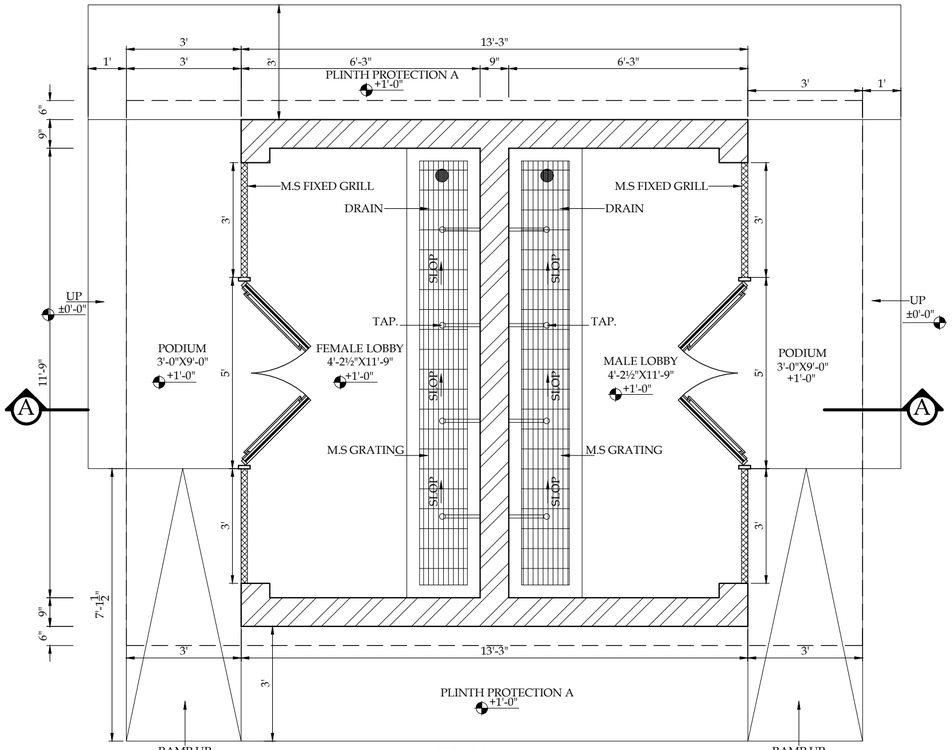

PLAN

SCALE:- 3/8" = 1'-0"

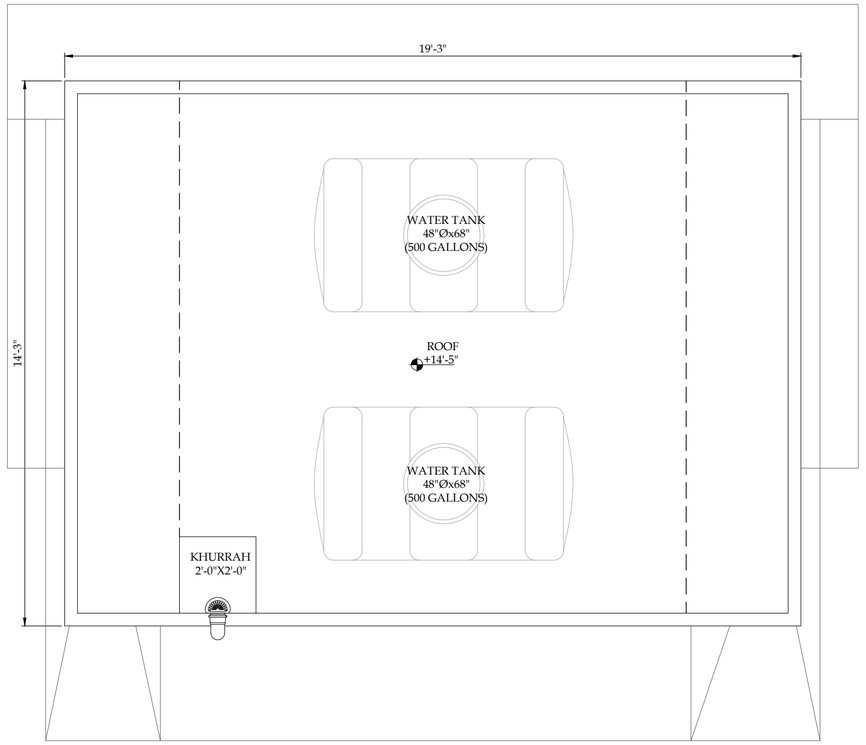

ROOF PLAN

SCALE:- 3/8" = 1'-0"

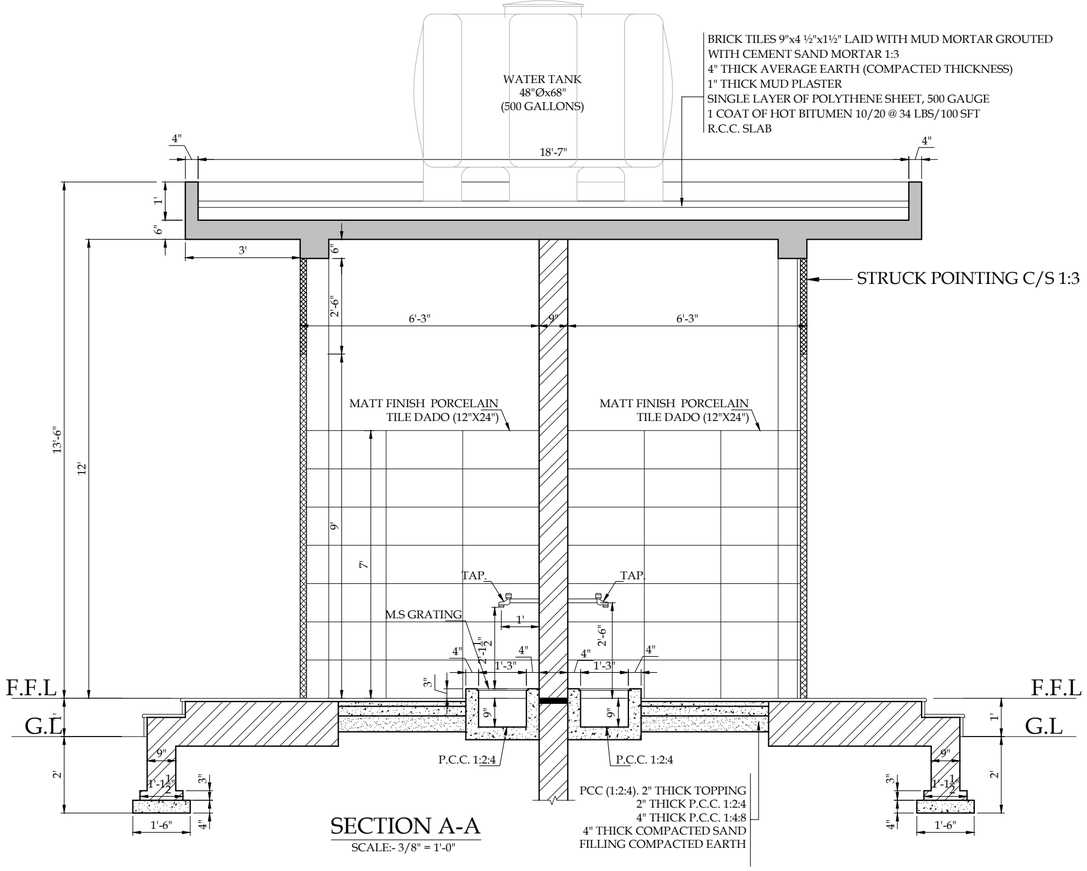

SECTION A-A

SCALE:- 3/8" = 1'-0"

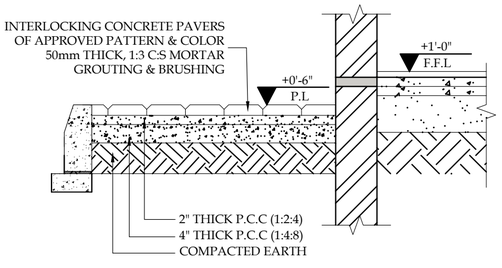

PLINTH PROTECTION DETAIL

SCALE:- 1/2" = 1'-0"

TITLE.

STAND POST
PLAN & SECTION

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	05-12-2025	DETAILED DESIGN	ASAD	ENGR. FAEIZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº: PRMSC-WS-SP-C-02 | SHEET | REV 00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:
ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

01

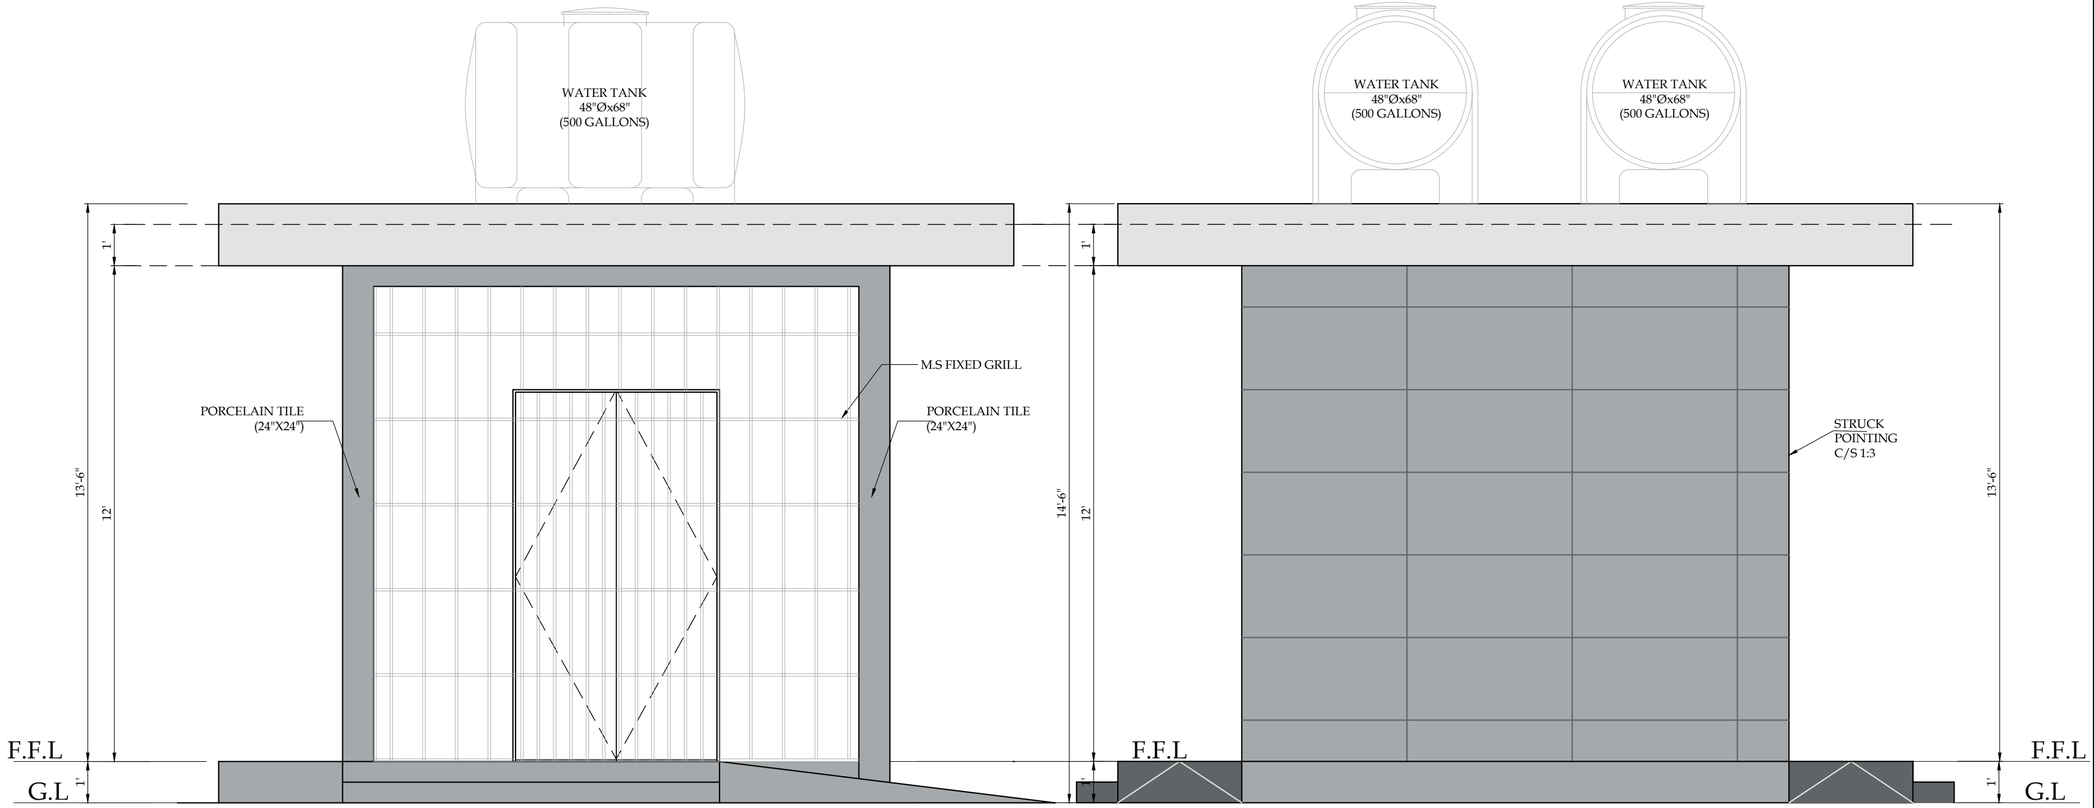

FRONT ELEVATION

SCALE:- 3/8" = 1'-0"

SIDE ELEVATION

SCALE:- 3/8" = 1'-0"

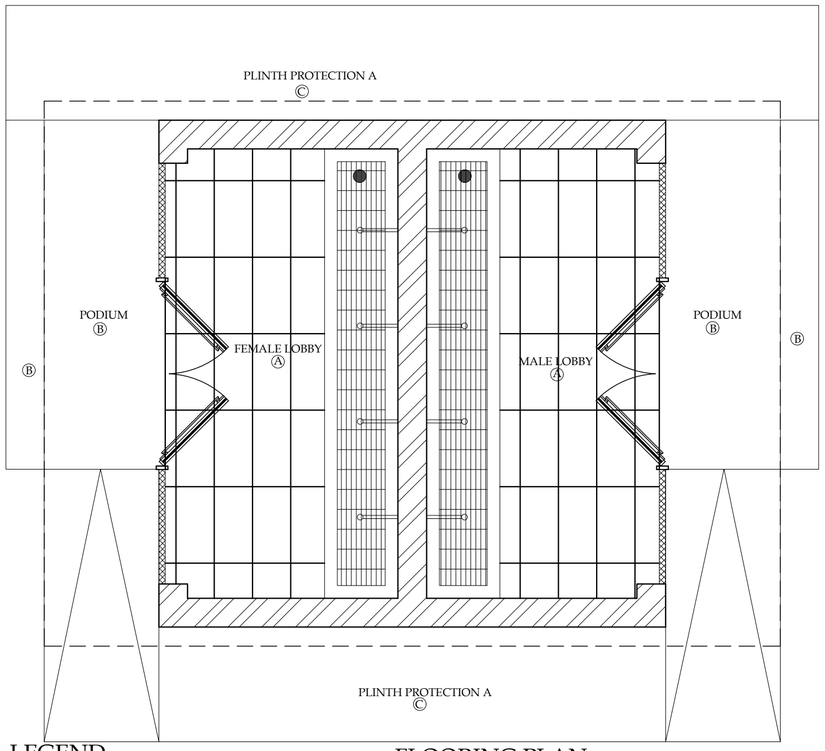

LEGEND

A=MATT FINISH PORCELAIN TILE (12"X24")
B=3/4" TH. CHINA VERONA MARBLE SLAB
C=50mm CONCRETE PAVERS

FLOORING PLAN

SCALE:- 3/8" = 1'-0"

TITLE.

STAND POST
FRONT,SIDE ELEVATIONS &
FLOORING PLAN

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	05-12-2025	DETAILED DESIGN	ASAD	ENGR. FAEIZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº: PRMSC-WS-SP-C-02

SHEET

REV 00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

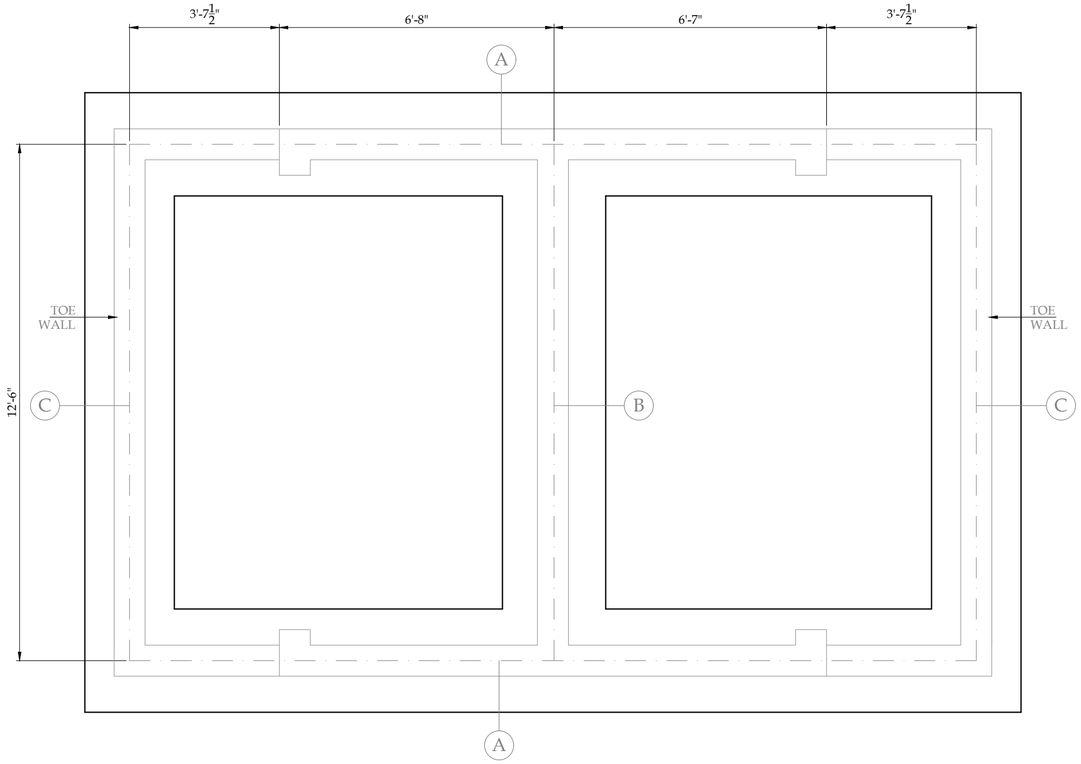

FOUNDATION LAYOUT PLAN

SCALE:- 3/8" = 1'-0"

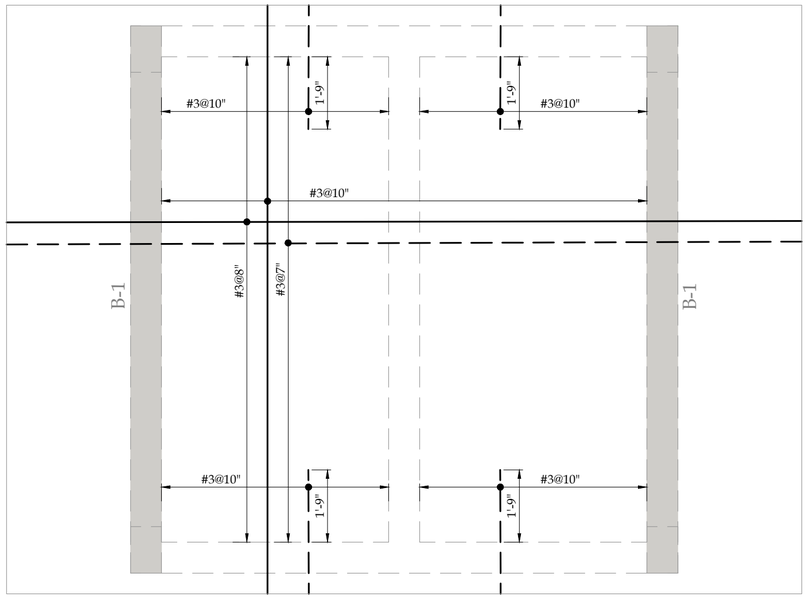

ROOF SLAB REINFORCEMENT PLAN

SCALE:- 3/8" = 1'-0"

NOTE:

1. THICKNESS OF ALL SLABS IS 6" UNLESS OTHERWISE NOTED.
2. DISTRIBUTION TOP BARS #3@12"c/c.

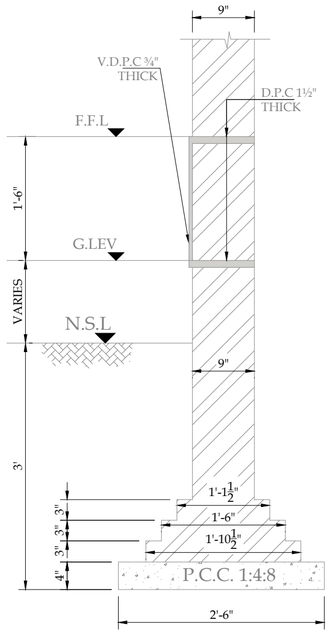

TYPE-A

SCALE:- 3/4" = 1'-0"

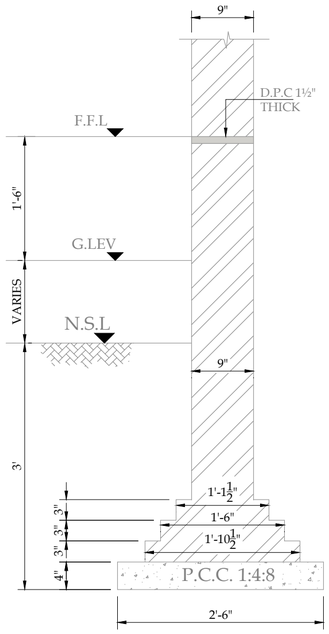

TYPE-B

SCALE:- 3/4" = 1'-0"

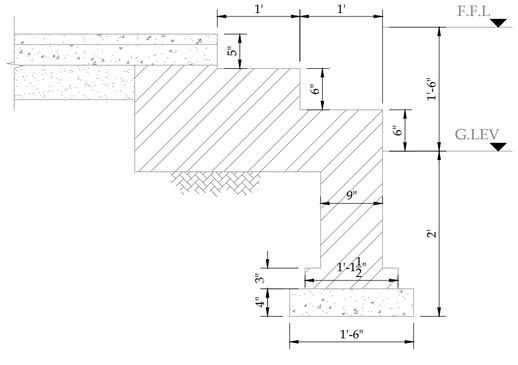

TYPE-C

SCALE:- 3/4" = 1'-0"

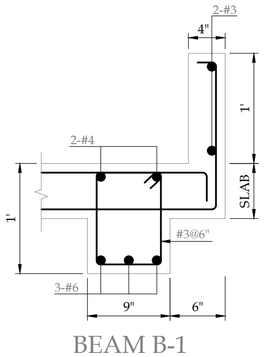

BEAM B-1

SCALE:- 1" = 1'-0"

TITLE.

FOUNDATION LAYOUT PLAN & SECTIONAL DETAILS

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	05-12-2025	DETAILED DESIGN	ASAD	ENGR. FAEIZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-WS-SP-S-01		00

PROJECT:

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS www.asiancon.com.pk

S-01

" LIGHT "						
NO.	SYMBOL	DESCRIPTION	TYPE / DETAIL / SPEC			
			COLOR TEMP.	LUMENS	CRI	P.F
1	⊕	CEILING MOUNTED LED DOWN LIGHT ROUND WITH 18 WATT.	5000-5500K	> 80lm/w	> 80	> .95

" FAN "				
NO.	SYMBOL	DESCRIPTION	SIZE	DETAIL
1		CEILING FAN 56" SWEEP WITH M.S HOOK	56" Ø	99.9% COPPER

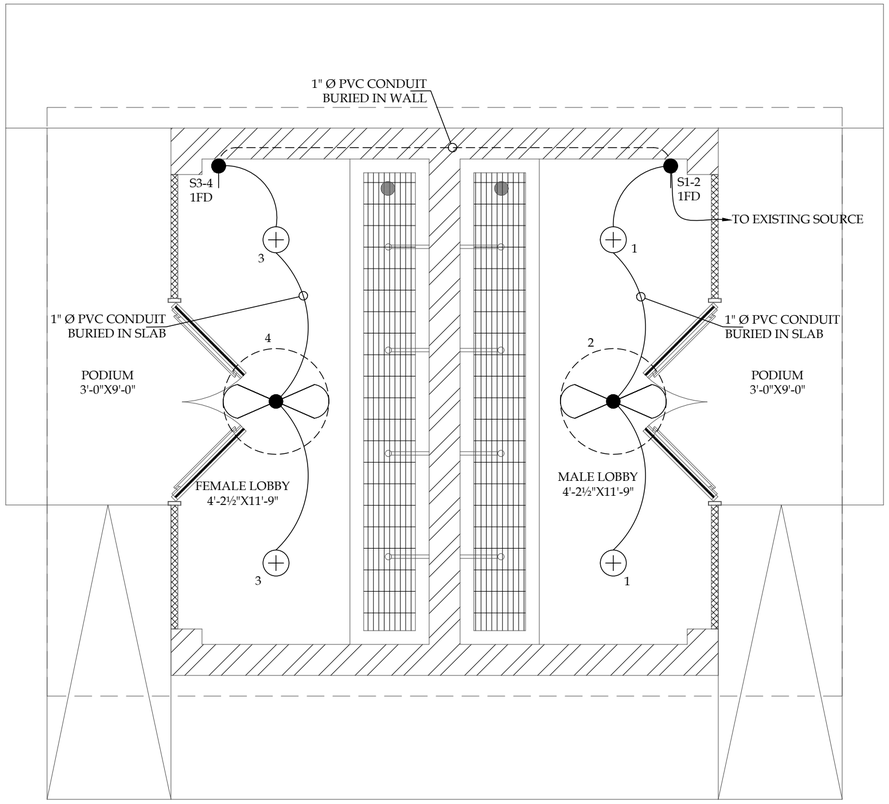

PLAN

TITLE.

ELECTRICAL LIGHTING LAYOUT PLAN (OPTION-I)

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	

ISSUE N°	DATE	D E S C R I P T I O N	DRAWN	DESIGNED	APPROVED
01	05-12-2025	DETAILED DESIGN	ASAD	ENGR. FAEQ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:

PRMSC-WS-SP-E-01

SHEET

REV 00

PROJECT:

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:

PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS www.asiancon.com.pk

GENERAL NOTES

- ALL PLUMBING WORKS SHALL BE EXECUTED STRICTLY IN ACCORDANCE WITH THE LATEST APPLICABLE CODES (E.G., IPC, UPC, ASME, ASTM, AND LOCAL AUTHORITY REQUIREMENTS).
- THE CONTRACTOR SHALL VERIFY ALL DIMENSIONS, LEVELS, SITE CONDITIONS, AND UTILITY CONNECTION POINTS BEFORE COMMENCING ANY WORK.
- DO NOT SCALE DRAWINGS. ANY DISCREPANCIES BETWEEN DRAWINGS, SITE, AND SPECIFICATIONS MUST BE BROUGHT TO THE ATTENTION OF THE ENGINEER BEFORE EXECUTION.
- COORDINATE ALL WORK WITH ARCHITECTURAL, STRUCTURAL, HVAC, ELECTRICAL, AND FIRE PROTECTION DRAWINGS BEFORE INSTALLATION.
- ALL PENETRATIONS THROUGH SLABS, WALLS, AND BEAMS SHALL BE COORDINATED WITH THE STRUCTURAL ENGINEER. USE SLEEVES WITH ANNULAR SPACE FILLED WITH APPROVED FIRE-STOPPING MATERIAL FOR FIRE-RATED ASSEMBLIES.
- ALL PIPES PASSING THROUGH WET AREAS OR UNDERGROUND SHALL BE WRAPPED OR SLEEVED WITH PROTECTIVE SLEEVES TO PREVENT CORROSION AND LEAKAGE.
- PROVIDE PIPE SUPPORTS, BRACKETS, HANGERS, AND ANCHORS AS PER MANUFACTURER'S RECOMMENDATIONS AND APPLICABLE CODES (E.G., MSS SP-58). ENSURE THERMAL EXPANSION AND CONTRACTION ALLOWANCES.
- ALL DRAINAGE AND VENT PIPING SHALL BE INSTALLED WITH REQUIRED SLOPES TO ENSURE SELF-CLEANING VELOCITY AND AVOID ACCUMULATION.
- AIR ADMITTANCE VALVES ARE NOT PERMITTED UNLESS APPROVED IN WRITING BY THE AUTHORITY HAVING JURISDICTION.
- ALL WATER SUPPLY PIPING MUST BE PRESSURE TESTED WITH POTABLE WATER TO 150% OF OPERATING PRESSURE OR MINIMUM 10 BAR (WHICHEVER IS HIGHER) FOR AT LEAST 2 HOURS WITH NO PRESSURE DROP.
- SANITARY DRAINAGE AND VENT PIPING MUST BE TESTED WITH A 10-FOOT HEAD OF WATER OR 5 PSI OF AIR PRESSURE FOR A MINIMUM OF 15 MINUTES WITHOUT LOSS.
- HOT WATER RECIRCULATION PIPING, IF REQUIRED, SHALL BE INSTALLED TO MINIMIZE WAITING TIME AT REMOTE FIXTURES. INSTALL BALANCING VALVES AND THERMAL TRAPS AS NEEDED.
- PROVIDE NON-RETURN VALVES, PRESSURE-REDUCING VALVES, STRAINERS, AND ISOLATION VALVES AT ALL STRATEGIC LOCATIONS.
- ALL PLUMBING FIXTURES AND FITTINGS MUST BE WATER-CONSERVING TYPE AND SHALL MEET RELEVANT LEED/GREEN BUILDING OR LOCAL SUSTAINABILITY REQUIREMENTS, WHERE APPLICABLE.
- WATER HEATERS (ELECTRIC, GAS, OR SOLAR) MUST BE INSTALLED WITH SAFETY VALVES, DRAIN PANS, AND THERMAL INSULATION. COORDINATE VENTING WITH MECHANICAL DRAWINGS.
- PROVIDE TRAP PRIMERS FOR FLOOR DRAINS IN DRY AREAS TO PREVENT TRAP SEAL EVAPORATION.
- ENSURE ANTI-SIPHON VACUUM BREAKERS AND BACKFLOW PREVENTERS ARE INSTALLED WHERE REQUIRED TO PROTECT POTABLE WATER SUPPLY.
- ALL PLUMBING ACCESSORIES (E.G., FAUCETS, VALVES, HOSES, DRAINS) SHALL BE OF HEAVY-DUTY COMMERCIAL GRADE AND APPROVED BY THE CONSULTANT.
- PROVIDE SEDIMENT TRAPS AT CONNECTIONS TO GAS APPLIANCES (IF APPLICABLE).
- WHERE PLUMBING SYSTEMS ARE INSTALLED IN CEILING SPACES, PROVIDE ADEQUATE ACCESS PANELS FOR MAINTENANCE OF CONCEALED FITTINGS AND VALVES.
- INSULATE ALL DOMESTIC HOT WATER AND CHILLED WATER PIPING AS PER PROJECT SPECIFICATIONS AND ENERGY CODE REQUIREMENTS.
- UNDERGROUND PIPING MUST BE LAID ON COMPACTED SAND BEDDING AND COVERED WITH FINE SAND BEFORE BACKFILLING WITH SELECTED MATERIAL.
- IDENTIFY ALL EXPOSED PIPING AND VALVES WITH COLOR-CODED LABELS, PIPE MARKERS, AND TAGS AS PER PIPING IDENTIFICATION SCHEDULE.
- COORDINATE FINAL FIXTURE LOCATIONS WITH ARCHITECTURAL INTERIOR DRAWINGS AND SITE MOCKUPS PRIOR TO INSTALLATION.
- CONTRACTOR IS RESPONSIBLE FOR ALL TRENCHING, EXCAVATION, CORE DRILLING, BACKFILLING, AND MAKING GOOD ALL DISTURBED SURFACES.
- PROVIDE ALL NECESSARY CLEANOUTS, VENT TERMINALS, AND INSPECTION CHAMBERS AS SHOWN ON DRAWINGS OR AS REQUIRED BY CODE.
- STORMWATER PIPING SHALL BE SEPARATE FROM SANITARY DRAINAGE AND DESIGNED FOR 100-YEAR RETURN PERIOD UNLESS OTHERWISE NOTED.
- CONTRACTOR SHALL PREPARE AND SUBMIT COMPLETE AS-BUILT DRAWINGS SHOWING EXACT LOCATIONS, PIPE SIZES, AND VALVE TYPES UPON PROJECT COMPLETION.
- PERFORM FULL FLUSHING, CLEANING, DISINFECTION, AND COMMISSIONING OF ALL SYSTEMS BEFORE HANDING OVER TO THE CLIENT.
- SUBMIT OPERATION & MAINTENANCE MANUALS, WARRANTIES, AND TRAINING SCHEDULES TO FACILITY MANAGEMENT TEAM AT PROJECT CLOSEOUT.
- THE CONTRACTOR SHALL ARRANGE FOR ALL REQUIRED INSPECTIONS AND APPROVALS FROM RELEVANT AUTHORITIES DURING AND AFTER CONSTRUCTION.
- ALL WORKMANSHIP SHALL BE NEAT, CLEAN, AND PROFESSIONAL. ANY POORLY EXECUTED WORK SHALL BE REMOVED AND REINSTALLED AT CONTRACTOR'S EXPENSE.

LEGEND AND ABBREVIATIONS

ABRV.	DESCRIPTION
CW	COLD WATER SUPPLY
HW	HOT WATER SUPPLY
HWR	HOT WATER RETURN
WP	WASTE WATER LINE
SP	SOIL WATER LINE
V	VENT PIPE
RWP	RAIN WATER PIPE
AIR	AIR VENT
DCW	DOMESTIC COLD WATER
DHW	DOMESTIC HOT WATER
HDR	HEADER PIPE
PPR	POLYPROPYLENE RANDOM PIPE
CPVC	CHLORINATED POLYVINYL CHLORIDE PIPE

UPVC	UNPLASTICIZED PVC PIPE
CI	CAST IRON PIPE
HDPE	HIGH-DENSITY POLYETHYLENE PIPE
GI	GALVANIZED IRON PIPE
PVC	POLYVINYL CHLORIDE PIPE
SS	STAINLESS STEEL PIPE
CU	COPPER PIPE
ROD	ROD-OUT POINT
TS	TEST STATION
BP	BOOSTER PUMP

PIPE SLOPES

300mm	Ø12"	1 IN 330
225mm	Ø9"	1 IN 225
160mm	Ø6"	1 IN 180
110mm	Ø4"	1 IN 100
75mm	Ø3"	1 IN 75
50mm	Ø2"	1 IN 50

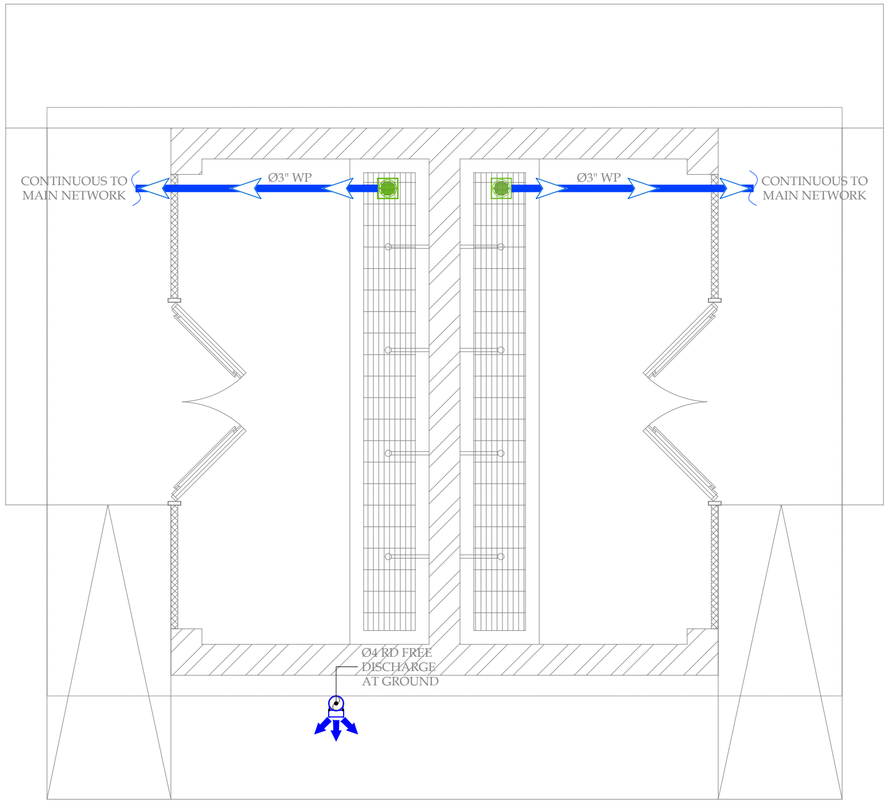

1 GROUND FLOOR LAYOUT
Scale: 3/8" = 1' - 0"

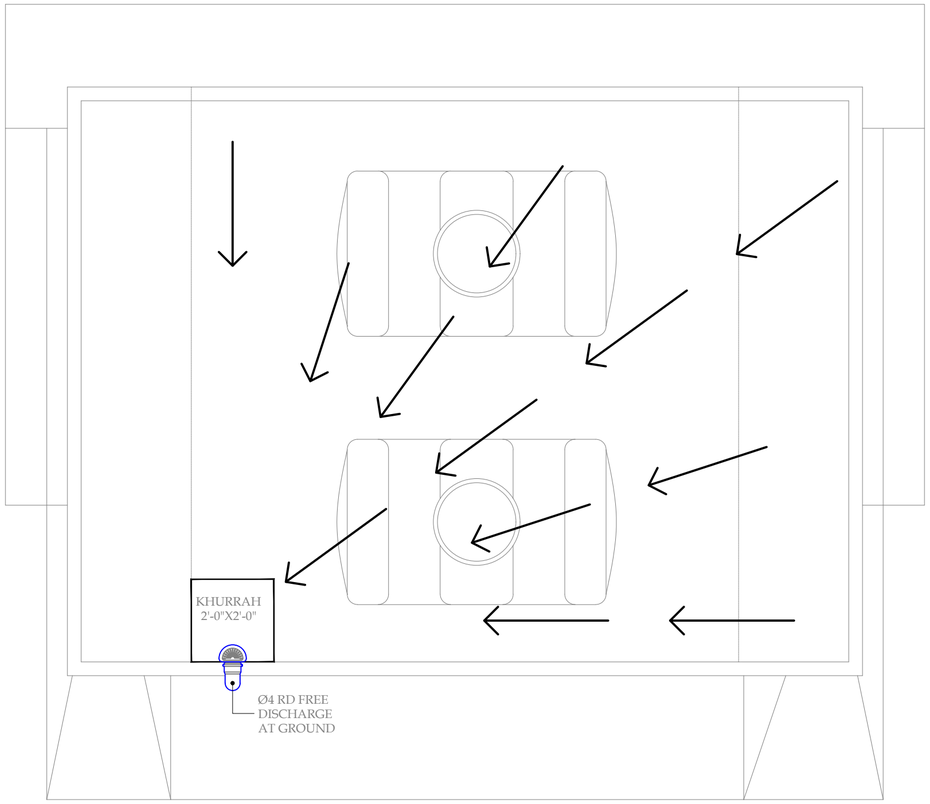

1 ROOF LAYOUT
Scale: 3/8" = 1' - 0"

TITLE.

STAND POST
DRAINAGE SYSTEM LAYOUT

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	05-12-2025	DETAILED DESIGN	ASAD	ENGR. FAEIZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº: PRMSC-WS-SP-P-01

SHEET

REV 00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:
ASIAN CONSULTING ENGINEERS
www.asianconsultants.com.pk

P-01

GENERAL NOTES

- ALL PLUMBING WORKS SHALL BE EXECUTED STRICTLY IN ACCORDANCE WITH THE LATEST APPLICABLE CODES (E.G., IPC, UPC, ASME, ASTM, AND LOCAL AUTHORITY REQUIREMENTS).
- THE CONTRACTOR SHALL VERIFY ALL DIMENSIONS, LEVELS, SITE CONDITIONS, AND UTILITY CONNECTION POINTS BEFORE COMMENCING ANY WORK.
- DO NOT SCALE DRAWINGS. ANY DISCREPANCIES BETWEEN DRAWINGS, SITE, AND SPECIFICATIONS MUST BE BROUGHT TO THE ATTENTION OF THE ENGINEER BEFORE EXECUTION.
- COORDINATE ALL WORK WITH ARCHITECTURAL, STRUCTURAL, HVAC, ELECTRICAL, AND FIRE PROTECTION DRAWINGS BEFORE INSTALLATION.
- ALL PENETRATIONS THROUGH SLABS, WALLS, AND BEAMS SHALL BE COORDINATED WITH THE STRUCTURAL ENGINEER. USE SLEEVES WITH ANNULAR SPACE FILLED WITH APPROVED FIRE-STOPPING MATERIAL FOR FIRE-RATED ASSEMBLIES.
- ALL PIPES PASSING THROUGH WET AREAS OR UNDERGROUND SHALL BE WRAPPED OR SLEEVED WITH PROTECTIVE SLEEVES TO PREVENT CORROSION AND LEAKAGE.
- PROVIDE PIPE SUPPORTS, BRACKETS, HANGERS, AND ANCHORS AS PER MANUFACTURER'S RECOMMENDATIONS AND APPLICABLE CODES (E.G., MSS SP-58). ENSURE THERMAL EXPANSION AND CONTRACTION ALLOWANCES.
- ALL DRAINAGE AND VENT PIPING SHALL BE INSTALLED WITH REQUIRED SLOPES TO ENSURE SELF-CLEANING VELOCITY AND AVOID ACCUMULATION.
- AIR ADMITTANCE VALVES ARE NOT PERMITTED UNLESS APPROVED IN WRITING BY THE AUTHORITY HAVING JURISDICTION.
- ALL WATER SUPPLY PIPING MUST BE PRESSURE TESTED WITH POTABLE WATER TO 150% OF OPERATING PRESSURE OR MINIMUM 10 BAR (WHICHEVER IS HIGHER) FOR AT LEAST 2 HOURS WITH NO PRESSURE DROP.
- SANITARY DRAINAGE AND VENT PIPING MUST BE TESTED WITH A 10-FOOT HEAD OF WATER OR 5 PSI OF AIR PRESSURE FOR A MINIMUM OF 15 MINUTES WITHOUT LOSS.
- HOT WATER RECIRCULATION PIPING, IF REQUIRED, SHALL BE INSTALLED TO MINIMIZE WAITING TIME AT REMOTE FIXTURES. INSTALL BALANCING VALVES AND THERMAL TRAPS AS NEEDED.
- PROVIDE NON-RETURN VALVES, PRESSURE-REDUCING VALVES, STRAINERS, AND ISOLATION VALVES AT ALL STRATEGIC LOCATIONS.
- ALL PLUMBING FIXTURES AND FITTINGS MUST BE WATER-CONSERVING TYPE AND SHALL MEET RELEVANT LEED/GREEN BUILDING OR LOCAL SUSTAINABILITY REQUIREMENTS, WHERE APPLICABLE.
- WATER HEATERS (ELECTRIC, GAS, OR SOLAR) MUST BE INSTALLED WITH SAFETY VALVES, DRAIN PANS, AND THERMAL INSULATION. COORDINATE VENTING WITH MECHANICAL DRAWINGS.
- PROVIDE TRAP PRIMERS FOR FLOOR DRAINS IN DRY AREAS TO PREVENT TRAP SEAL EVAPORATION.
- ENSURE ANTI-SIPHON VACUUM BREAKERS AND BACKFLOW PREVENTERS ARE INSTALLED WHERE REQUIRED TO PROTECT POTABLE WATER SUPPLY.
- ALL PLUMBING ACCESSORIES (E.G., FAUCETS, VALVES, HOSES, DRAINS) SHALL BE OF HEAVY-DUTY COMMERCIAL GRADE AND APPROVED BY THE CONSULTANT.
- PROVIDE SEDIMENT TRAPS AT CONNECTIONS TO GAS APPLIANCES (IF APPLICABLE).
- WHERE PLUMBING SYSTEMS ARE INSTALLED IN CEILING SPACES, PROVIDE ADEQUATE ACCESS PANELS FOR MAINTENANCE OF CONCEALED FITTINGS AND VALVES.
- INSULATE ALL DOMESTIC HOT WATER AND CHILLED WATER PIPING AS PER PROJECT SPECIFICATIONS AND ENERGY CODE REQUIREMENTS.
- UNDERGROUND PIPING MUST BE LAID ON COMPACTED SAND BEDDING AND COVERED WITH FINE SAND BEFORE BACKFILLING WITH SELECTED MATERIAL.
- IDENTIFY ALL EXPOSED PIPING AND VALVES WITH COLOR-CODED LABELS, PIPE MARKERS, AND TAGS AS PER PIPING IDENTIFICATION SCHEDULE.
- COORDINATE FINAL FIXTURE LOCATIONS WITH ARCHITECTURAL INTERIOR DRAWINGS AND SITE MOCKUPS PRIOR TO INSTALLATION.
- CONTRACTOR IS RESPONSIBLE FOR ALL TRENCHING, EXCAVATION, CORE DRILLING, BACKFILLING, AND MAKING GOOD ALL DISTURBED SURFACES.
- PROVIDE ALL NECESSARY CLEANOUTS, VENT TERMINALS, AND INSPECTION CHAMBERS AS SHOWN ON DRAWINGS OR AS REQUIRED BY CODE.
- STORMWATER PIPING SHALL BE SEPARATE FROM SANITARY DRAINAGE AND DESIGNED FOR 100-YEAR RETURN PERIOD UNLESS OTHERWISE NOTED.
- CONTRACTOR SHALL PREPARE AND SUBMIT COMPLETE AS-BUILT DRAWINGS SHOWING EXACT LOCATIONS, PIPE SIZES, AND VALVE TYPES UPON PROJECT COMPLETION.
- PERFORM FULL FLUSHING, CLEANING, DISINFECTION, AND COMMISSIONING OF ALL SYSTEMS BEFORE HANDING OVER TO THE CLIENT.
- SUBMIT OPERATION & MAINTENANCE MANUALS, WARRANTIES, AND TRAINING SCHEDULES TO FACILITY MANAGEMENT TEAM AT PROJECT CLOSEOUT.
- THE CONTRACTOR SHALL ARRANGE FOR ALL REQUIRED INSPECTIONS AND APPROVALS FROM RELEVANT AUTHORITIES DURING AND AFTER CONSTRUCTION.
- ALL WORKMANSHIP SHALL BE NEAT, CLEAN, AND PROFESSIONAL. ANY POORLY EXECUTED WORK SHALL BE REMOVED AND REINSTALLED AT CONTRACTOR'S EXPENSE.

LEGEND AND ABBREVIATIONS

ABRV.	DESCRIPTION
CW	COLD WATER SUPPLY
HW	HOT WATER SUPPLY
HWR	HOT WATER RETURN
WP	WASTE WATER LINE
SP	SOIL WATER LINE
V	VENT PIPE
RWP	RAIN WATER PIPE
AIR	AIR VENT
DCW	DOMESTIC COLD WATER
DHW	DOMESTIC HOT WATER
HDR	HEADER PIPE
PPR	POLYPROPYLENE RANDOM PIPE
CPVC	CHLORINATED POLYVINYL CHLORIDE PIPE

UPVC	UNPLASTICIZED PVC PIPE
CI	CAST IRON PIPE
HDPE	HIGH-DENSITY POLYETHYLENE PIPE
GI	GALVANIZED IRON PIPE
PVC	POLYVINYL CHLORIDE PIPE
SS	STAINLESS STEEL PIPE
CU	COPPER PIPE
ROD	ROD-OUT POINT
TS	TEST STATION
BP	BOOSTER PUMP

PIPE SLOPES

300mm	Ø12"	1 IN 330
225mm	Ø9"	1 IN 225
160mm	Ø6"	1 IN 180
110mm	Ø4"	1 IN 100
75mm	Ø3"	1 IN 75
50mm	Ø2"	1 IN 50

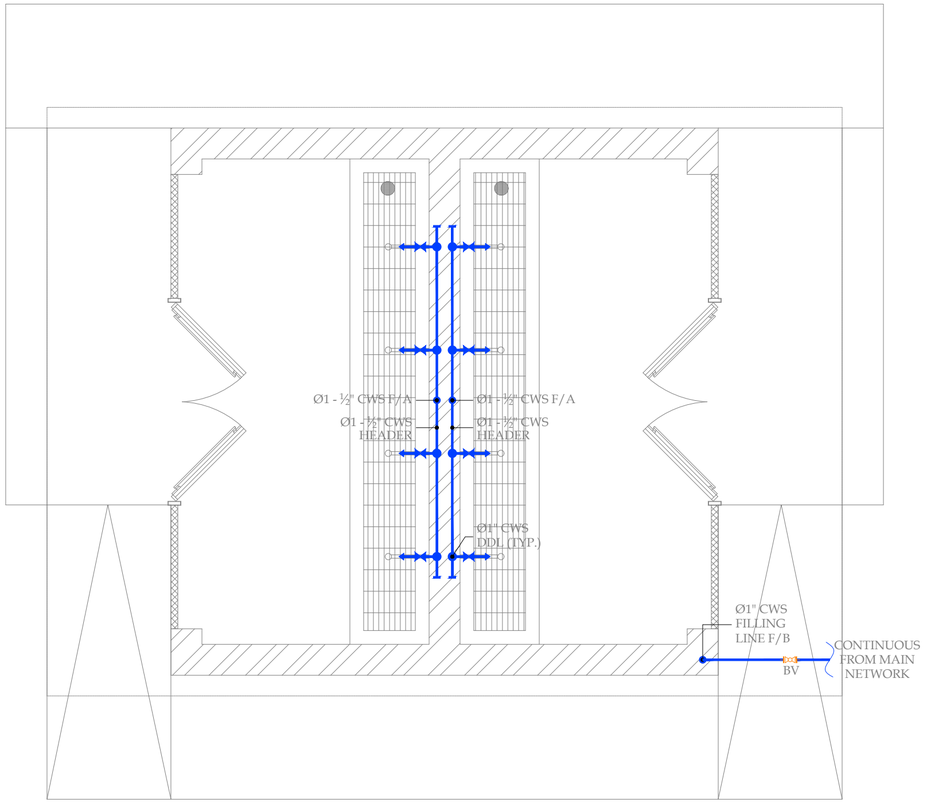

1 GROUND FLOOR LAYOUT
Scale: 3/8" = 1' - 0"

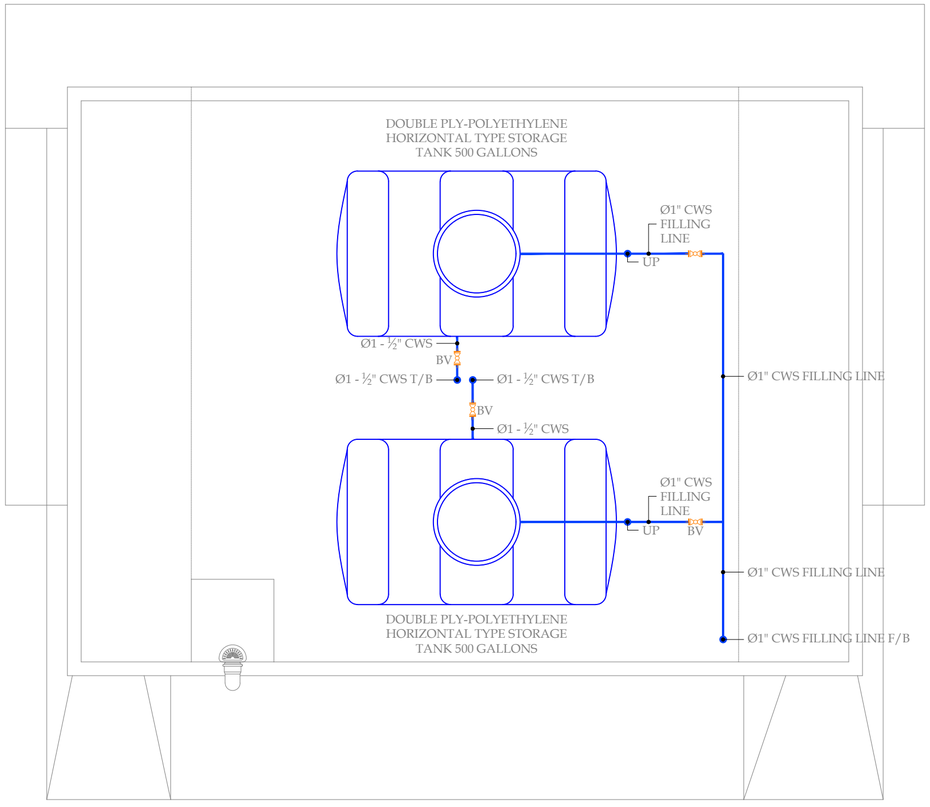

1 ROOF LAYOUT
Scale: 3/8" = 1' - 0"

TITLE.

STAND POST
WATER SUPPLY SYSTEM LAYOUT

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	05-12-2025	DETAILED DESIGN	ASAD	ENGR. FAEIZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:
PRMSC-WS-SP-P-02

SHEET

REV
00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:
ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

STAND POST TYPE - II

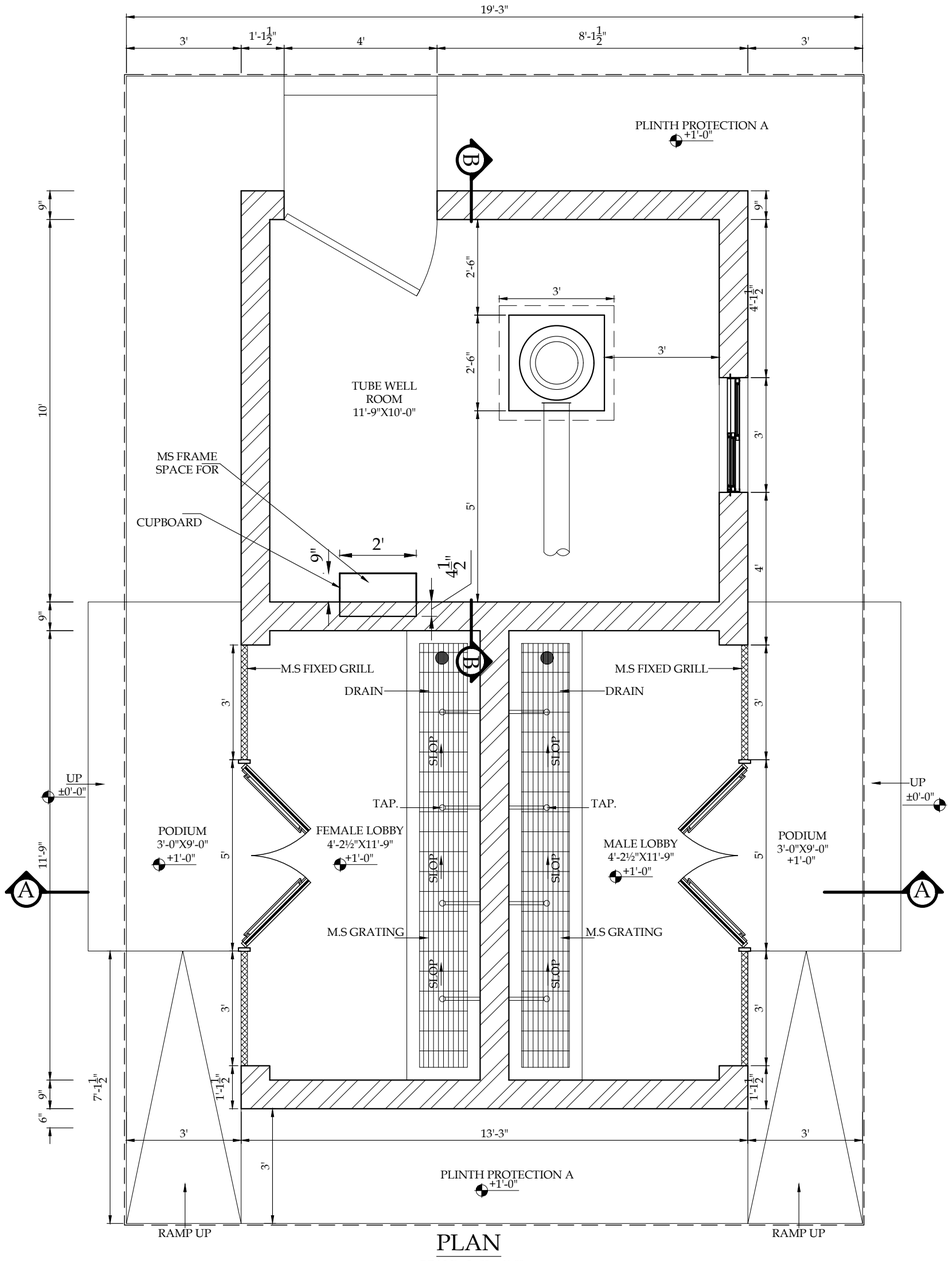

PLAN

SCALE:- 3/8" = 1'-0"

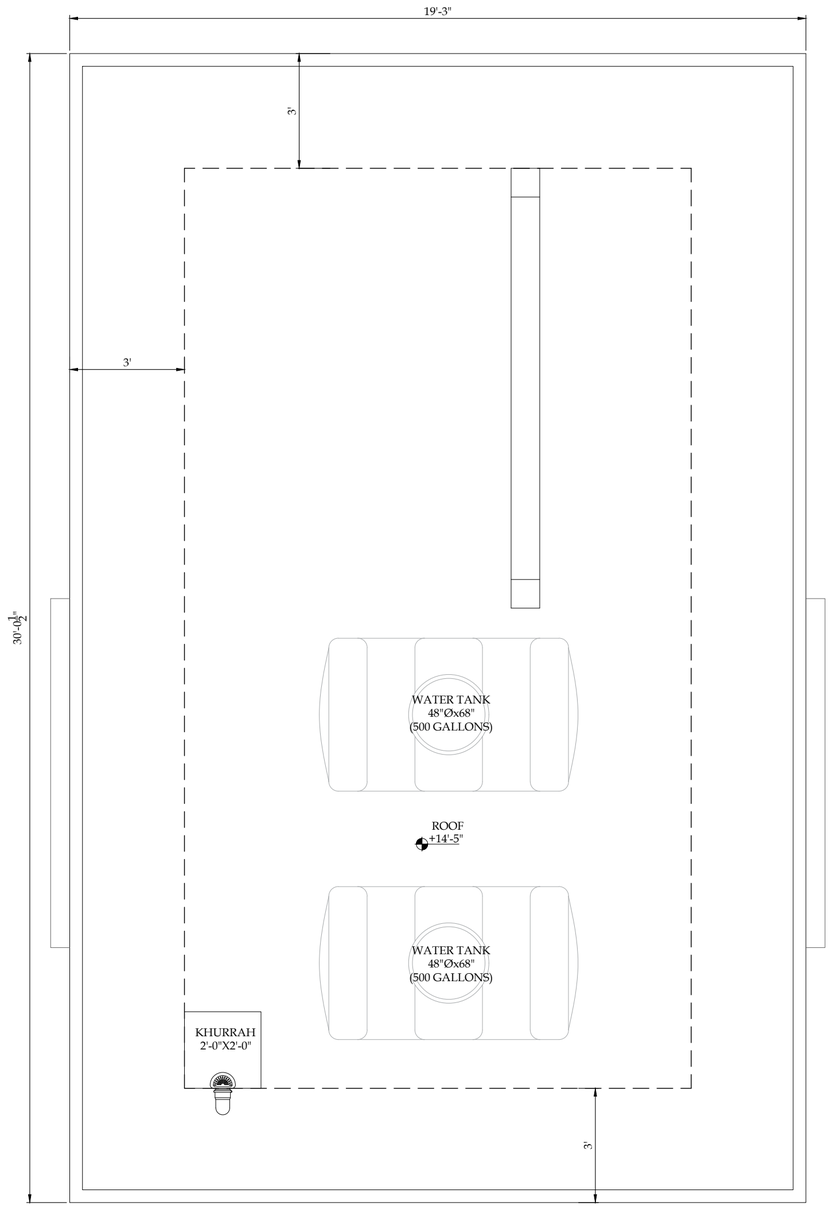

ROOF PLAN

SCALE:- 3/8" = 1'-0"

TITLE.

STAND POST TYPE-II
PLAN & SECTION

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	10-12-2025	DETAILED DESIGN	ASAD	ENGR. FAEIZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:

PRMSC-WS-SP-C-01

SHEET

REV
00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

01

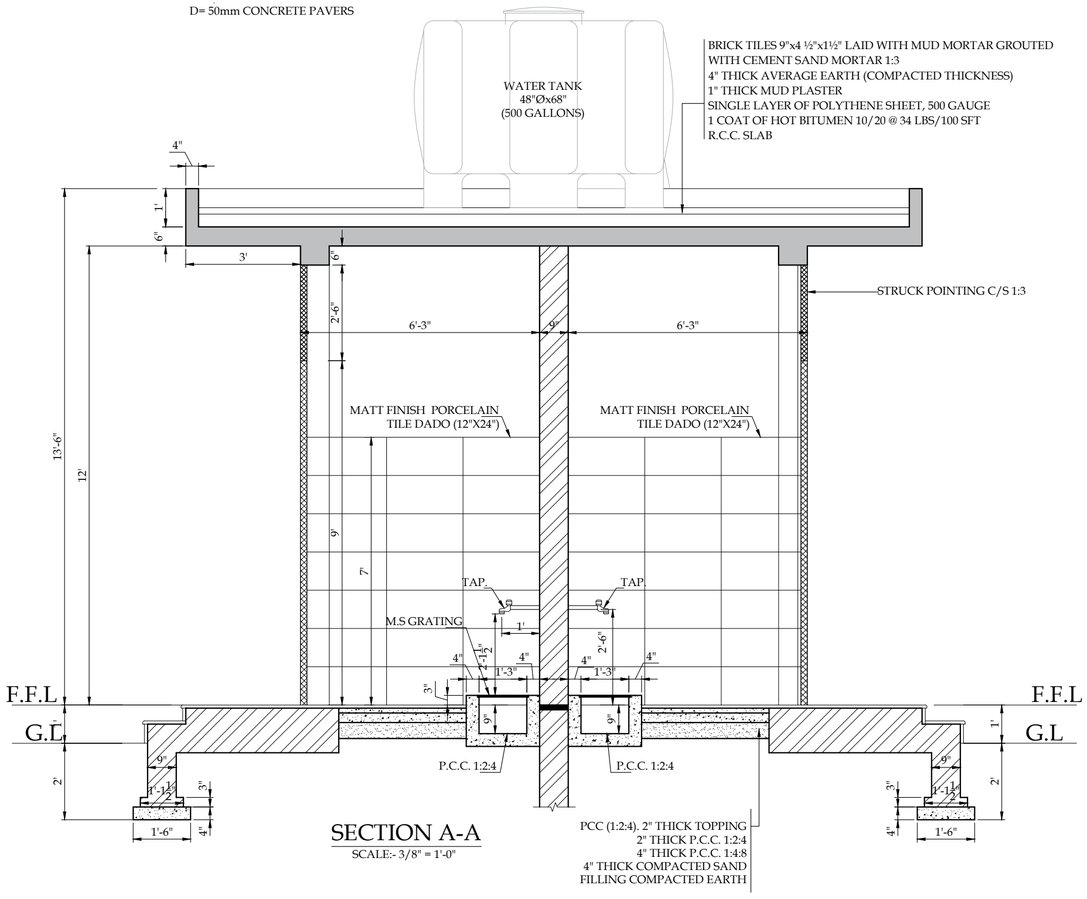

SECTION A-A

SCALE:- 3/8" = 1'-0"

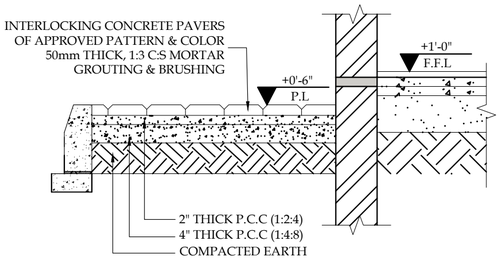

PLINTH PROTECTION DETAIL

SCALE:- 1/2" = 1'-0"

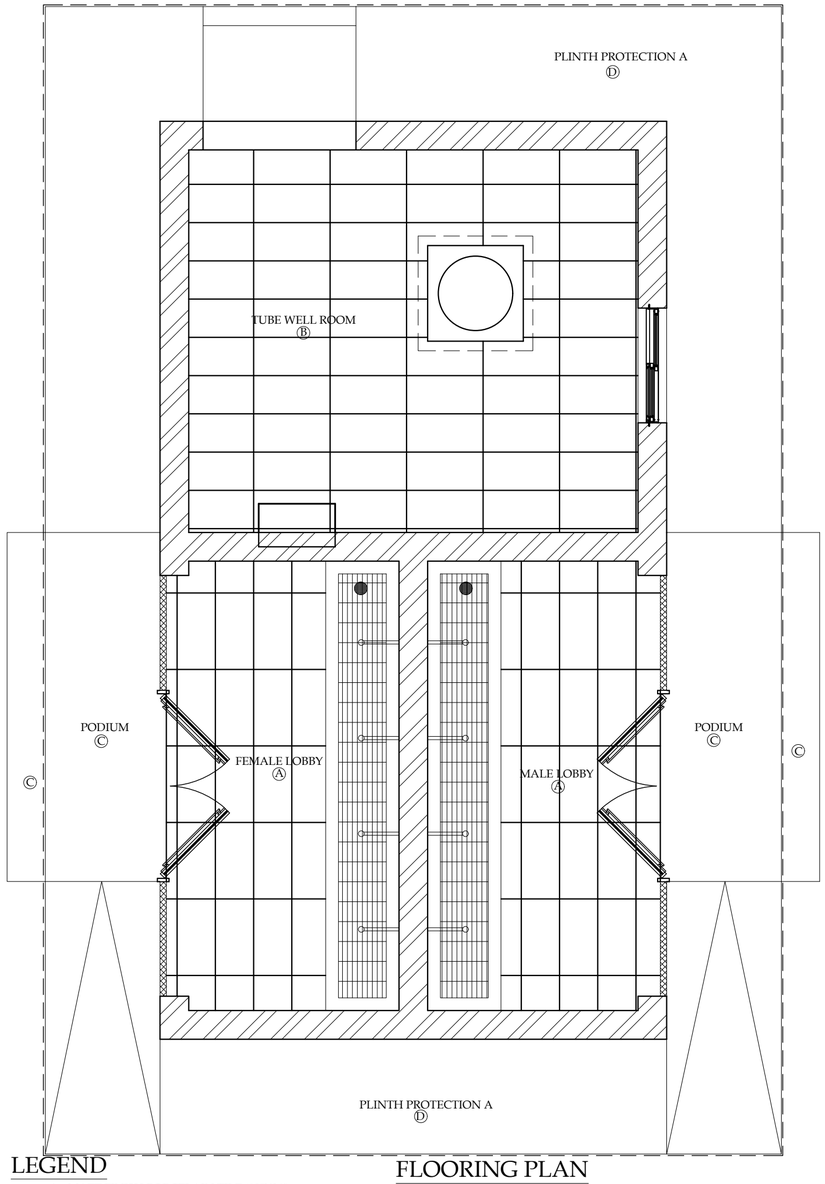

LEGEND

A= MATT FINISH PORCELAIN TILE (12"X24")
B=1/2" THICK MOSAIC FLOORING
C= 3/4" TH. CHINA VERONA MARBLE SLAB

FLOORING PLAN

SCALE:- 3/8" = 1'-0"

TITLE.

STAND POST TYPE-II
FRONT,SIDE ELEVATIONS &
FLOORING PLAN

ORIGINAL :		DATE :		SCALE :	
A2		JULY, 2025			

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	10-12-2025	DETAILED DESIGN	ASAD	ENGR. FAEIZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:

PRMSC-WS-SP-C-02

SHEET

REV
00

PROJECT:

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:

PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

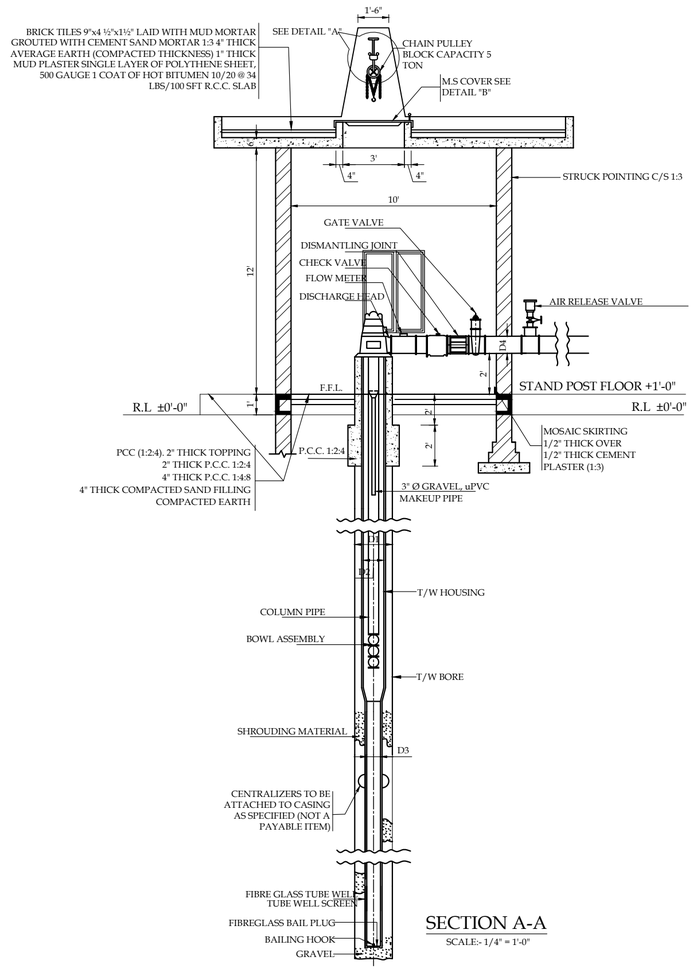

SECTION A-A

SCALE:- 1/4" = 1'-0"

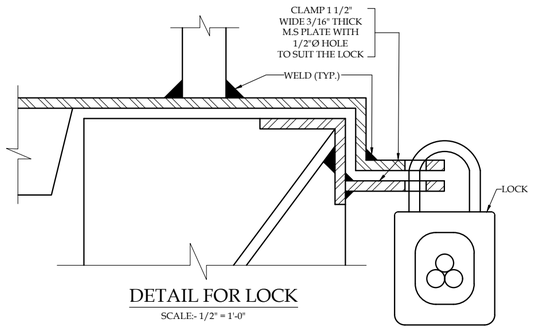

DETAIL FOR LOCK

SCALE:- 1/2" = 1'-0"

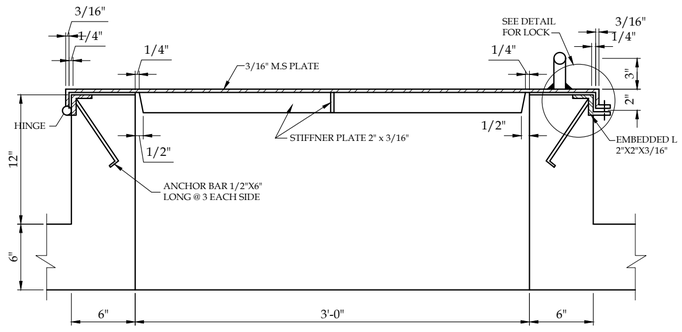

SECTION D-D

SCALE:- 1/2" = 1'-0"

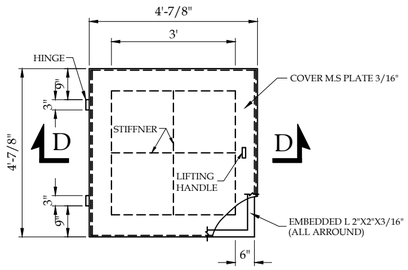

DETAIL "B"

SCALE:- 1/2" = 1'-0"

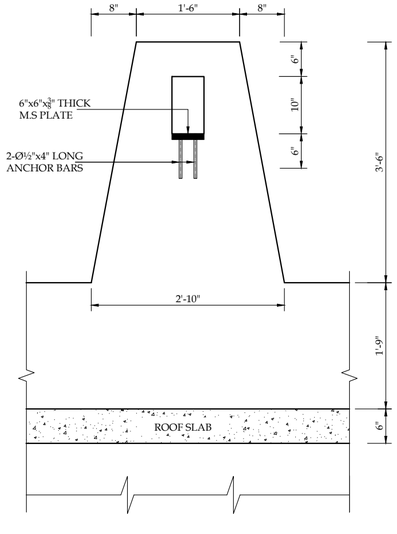

SIDE ELEVATION OF GIRDER LIFT WALL DETAIL-A

SCALE:- 3/4" = 1'-0"



REDUCER DETAIL

SCALE:- 3/4" = 1'-0"

BRICK TILES 9"x4 ½"x1½" LAID WITH MUD MORTAR GROUTED WITH CEMENT SAND MORTAR 1:3 4" THICK AVERAGE EARTH (COMPACTED THICKNESS) 1" THICK MUD PLASTER SINGLE LAYER OF POLYTHENE SHEET, 500 GAUGE 1 COAT OF HOT BITUMEN 10/20 @ 34 LBS/100 SFT R.C.C. SLAB

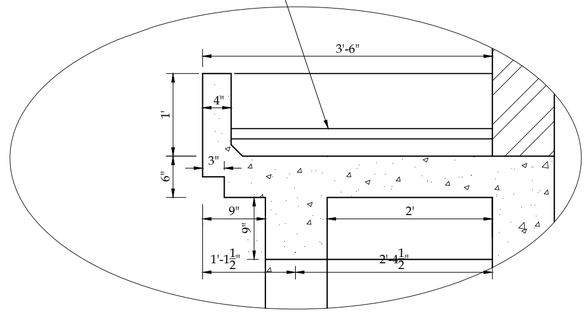

DETAIL "X"

SCALE:- 3/4" = 1'-0"

SCHEDULE OF TUBE WELL

DESCRIPTION	SIZE PUMP-1	SIZE PUMP-2
TUBEWELL CAPACITY	0.05 CUSEC	0.15-0.5 CUSEC
D1	8"	18"
D2	6"	12"
D3	4"	8"
D4	4"	6"
SETTING DEPTH	60'	80'
STRAINER LENGTH	10'	50'
BAIL PLUG	10'	10'
BORE DEPTH	90'±	200'±

TITLE:

TUBE WELL
PLAN & SECTION

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	10-12-2025	DETAILED DESIGN	ASAD	ENGR FAEIZ	ENGR IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:

PRMSC-WS-SP-C-02A

SHEET

REV 00

PROJECT:

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS www.asiancon.com.pk

2A

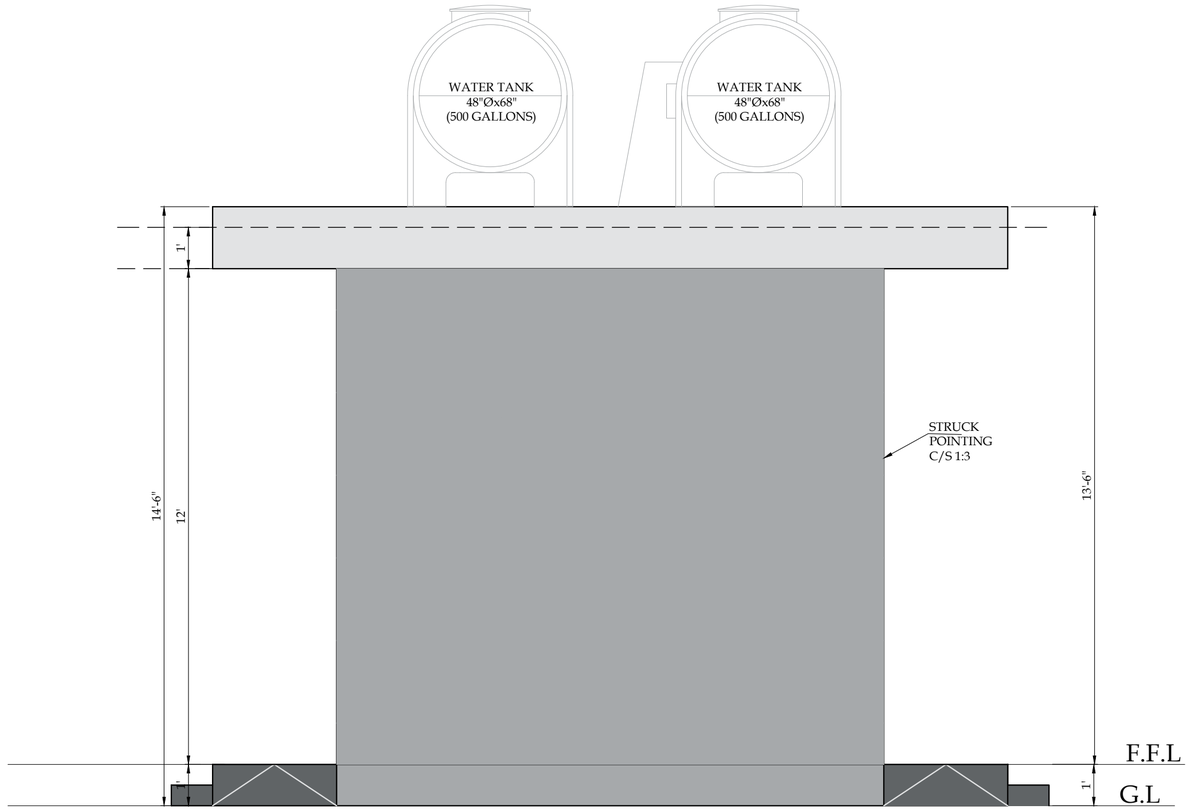

SIDE ELEVATION

SCALE:- 3/8" = 1'-0"

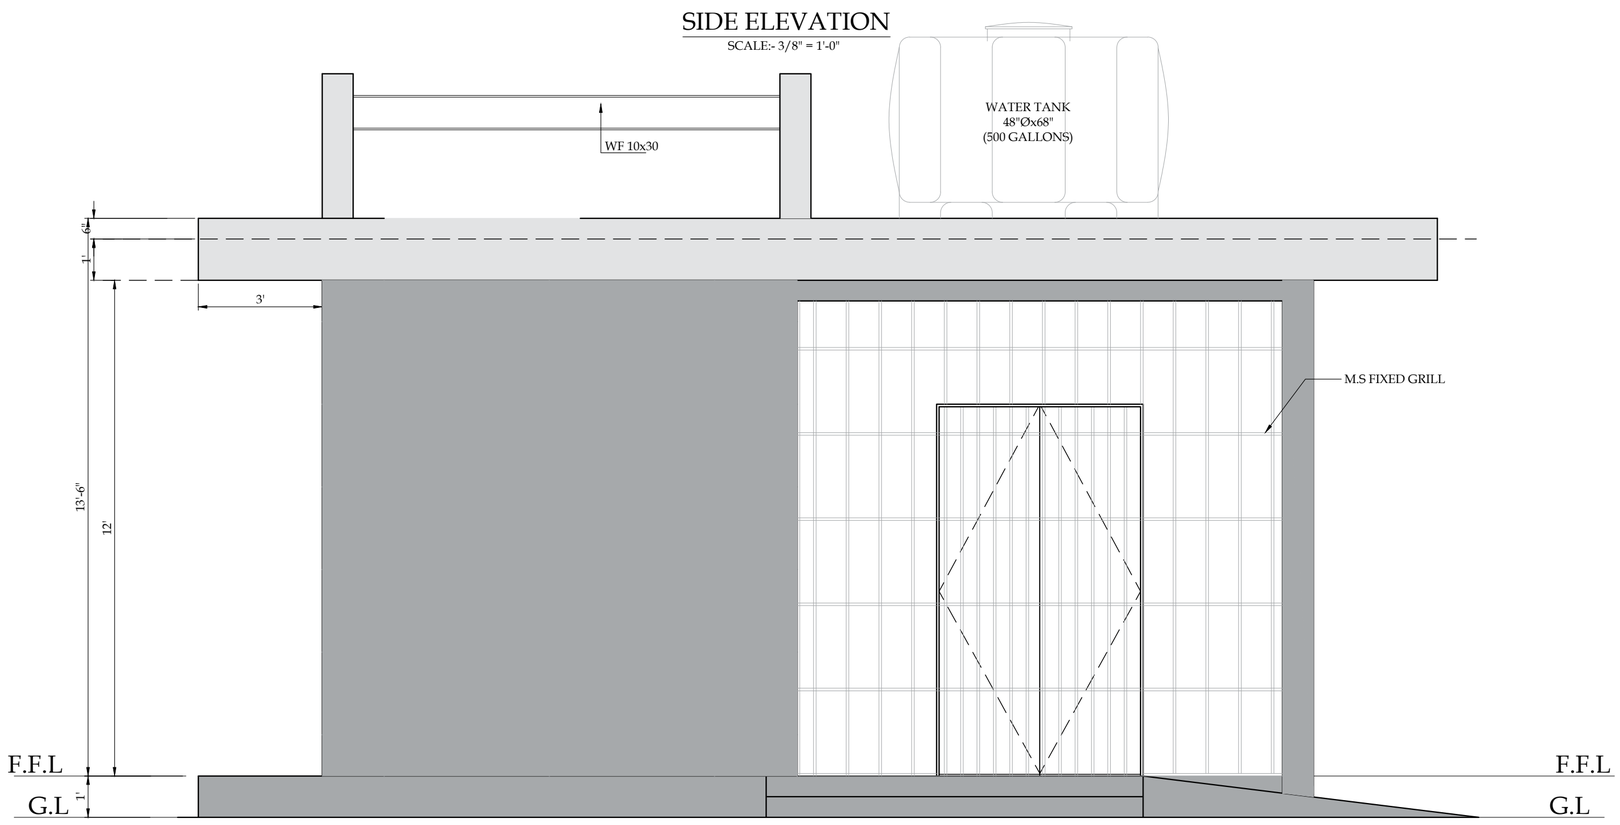

FRONT ELEVATION

SCALE:- 3/8" = 1'-0"

TITLE.

STAND POST TYPE-II
FRONT,SIDE ELEVATIONS &
FLOORING PLAN

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	10-12-2025	DETAILED DESIGN	ASAD	ENGR. FAEIZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-WS-SP-C-03		00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

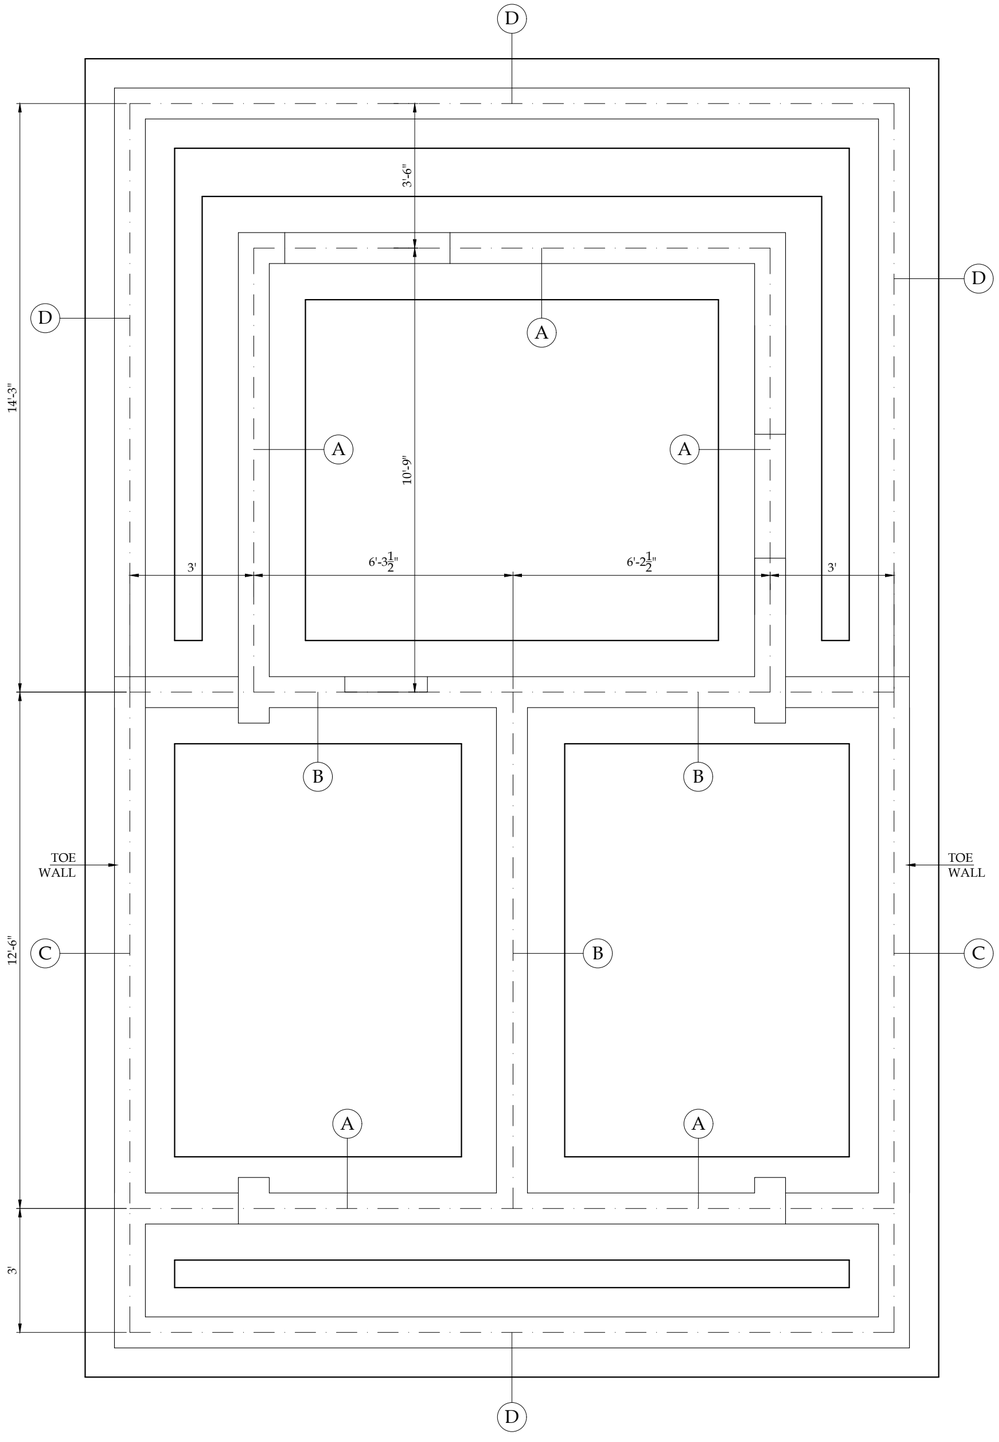

FOUNDATION LAYOUT PLAN
SCALE:- 3/8" = 1'-0"

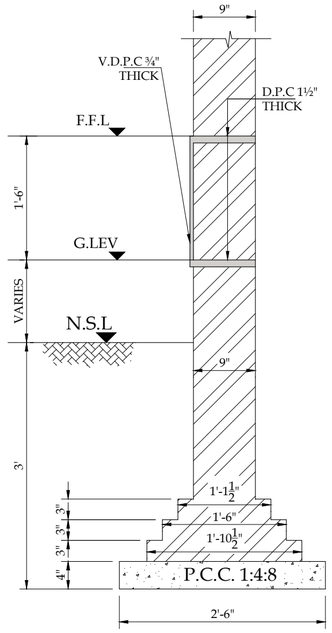

TYPE-A
SCALE:- 3/4" = 1'-0"

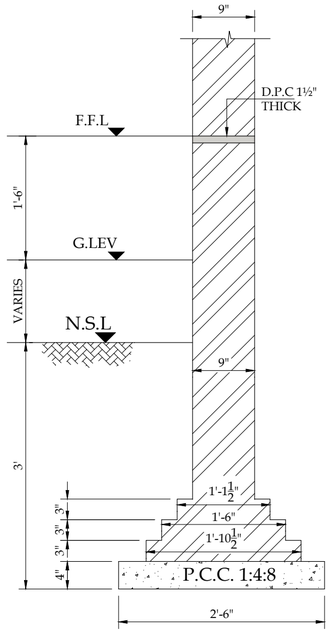

TYPE-B
SCALE:- 3/4" = 1'-0"

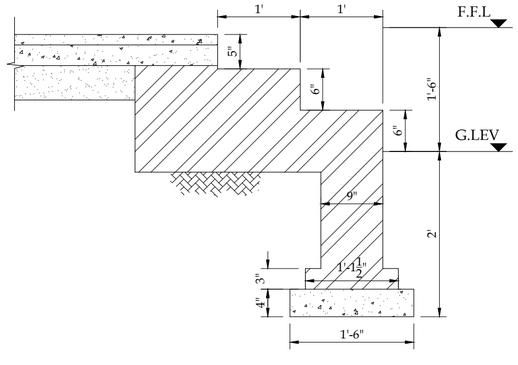

TYPE-C
SCALE:- 3/4" = 1'-0"

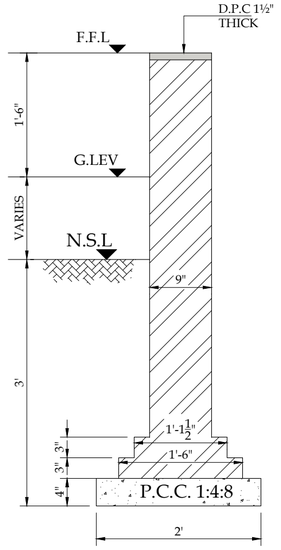

TYPE-D
SCALE:- 3/4" = 1'-0"

TITLE.
FOUNDATION LAYOUT PLAN
& SECTIONAL DETAILS

ORIGINAL :		DATE :		SCALE :	
A2		JULY, 2025			

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	10-12-2025	DETAILED DESIGN	ASAD	ENGR. FAEIZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING N°: PRMSC-WS-SP-S-01 | SHEET | REV 00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:
ASIAN CONSULTING ENGINEERS www.asiancon.com.pk

S-01

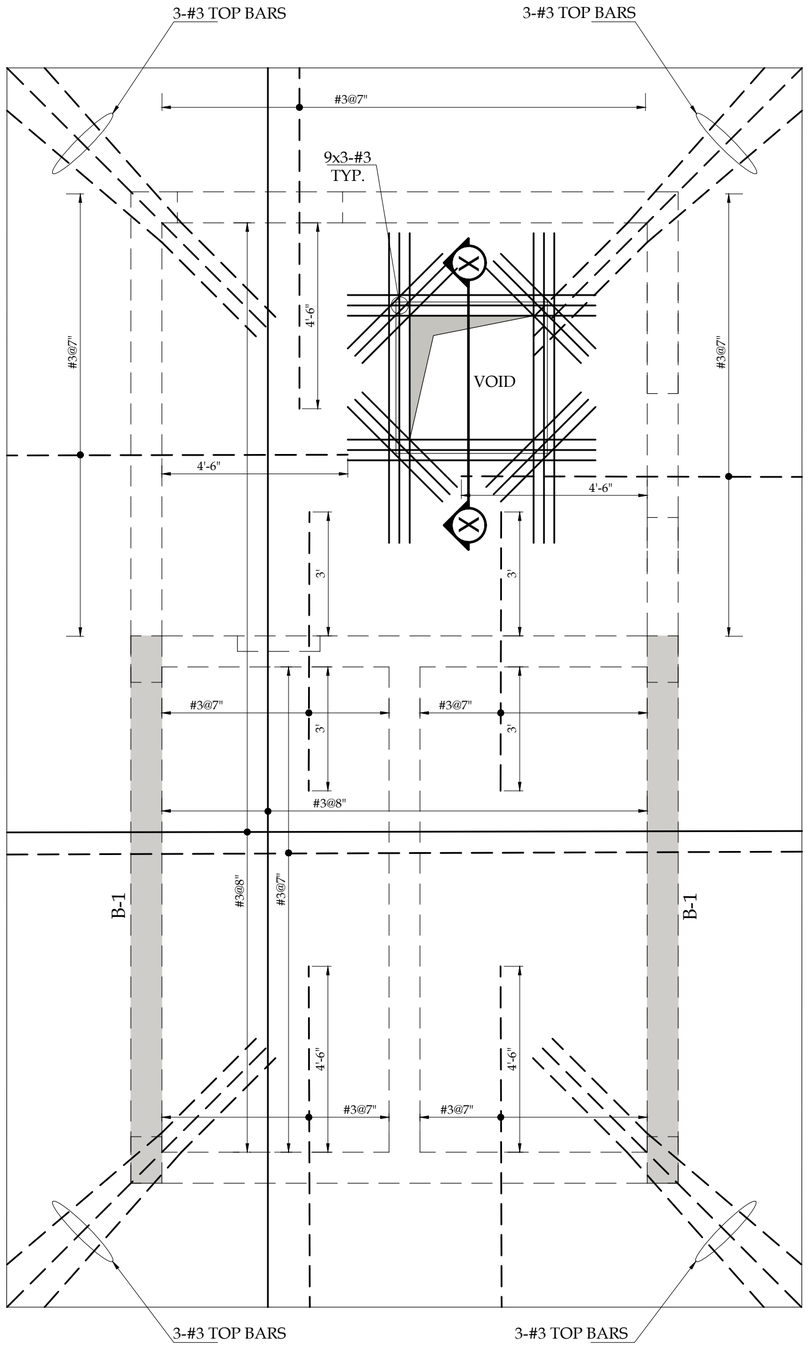

ROOF SLAB REINFORCEMENT PLAN

SCALE:- 3/8" = 1'-0"

NOTE:

1. THICKNESS OF ALL SLABS IS 6" UNLESS OTHERWISE NOTED.
2. DISTRIBUTION TOP BARS #3@12"c/c.

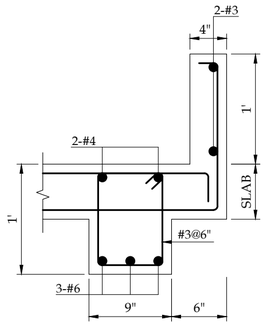

BEAM B-1

SCALE:- 1" = 1'-0"

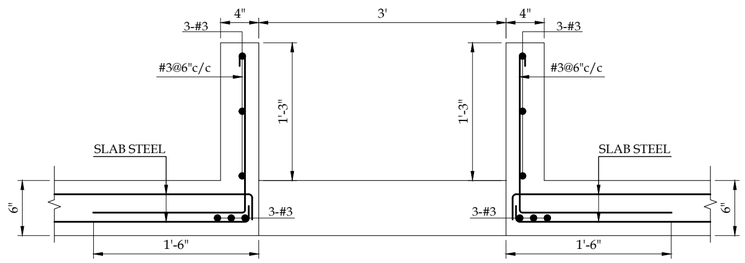

SECTION X-X

SCALE:- 1" = 1'-0"

TITLE.

ROOF SLAB REINFORCEMENT PLAN & SECTIONAL DETAILS

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	10-12-2025	DETAILED DESIGN	ASAD	ENGR. FAEIZ	ENGR. IRSAN UL HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-WS-SP-S-02		00

PROJECT:

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS www.asiancon.com

S-01

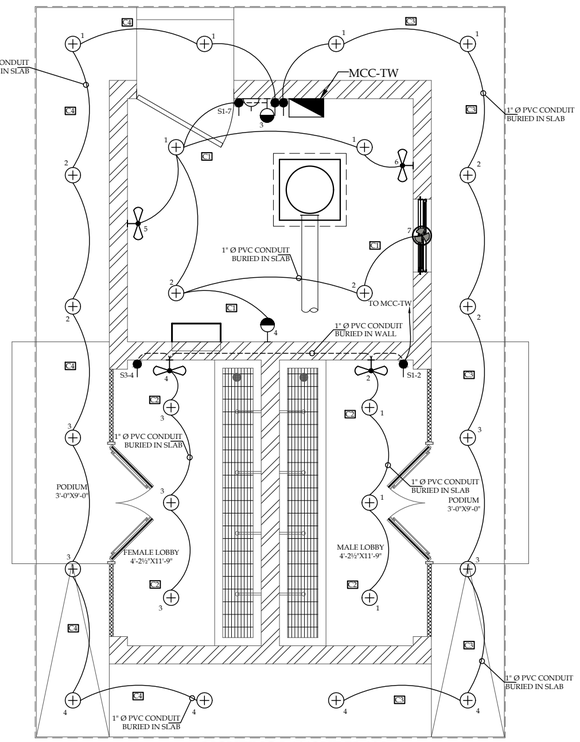

LIGHTING LAYOUT PLAN

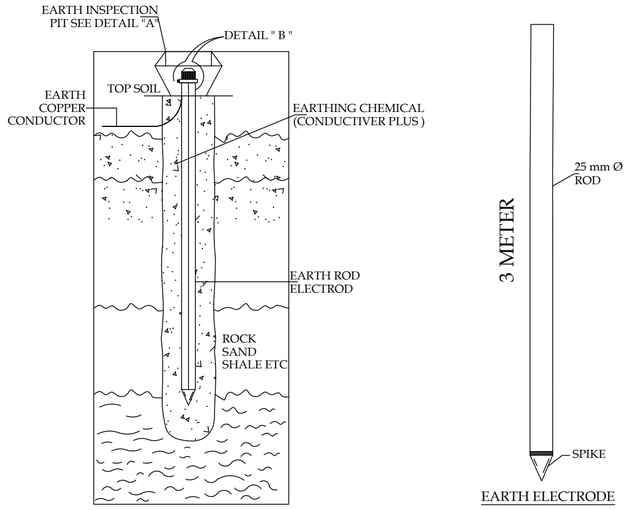

EARTH ROD INSTALLATION DETAIL

EARTH ELECTRODE COPPER ROD



EARTH INSPECTION PIT DETAIL "A"



DETAIL " B "

U BOND CONNECTION EARTHING

NOTES FOR EARTHING SYSTEM

1- EARTH BORE SHALL BE MADE AT 6'-0" AWAY FROM R.C.C FOUNDATION.

2- DISTANCE BETWEEN 2 EARTH BORES SHALL NOT BE LESS THEN 10'-0"

3- COPPER CONDUCTOR AT TOP SHALL BE BOLTED WITH THIMBLES, BRASS NUTS,BOLTS ETC/WELD POWDER.

4- JOINTS SHALL BE COVERED WITH HEAT SHRINKABLE TAPE.

5- CONTRACTOR TO MEASURE EARTHING RESISTANCE IN THE PRESENCE OF SITE ENGINEER. BOTH THE SITE ENGINEER AND CONTRACTOR SHALL SIGN THE EARTH TESTING RESULT AND SUBMIT IT TO THE CLIENT FOR RECORD WITH EQUIPMENT CALIBRATION CERTIFICATE.

6-THE EARTH RESISTANCE VALUE AFTER INSTALLATION SHALL BE LESS THAN THREE (3) OHM.

7-ALL MATERIAL OF THE ELECTRODE WILL BE OF COPPER.

8-THE EARLY STEAMER ROD WILL BE HANGED WITH PROPER HANGING ARRANGEMENT.

" LIGHTS "						
NO.	SYMBOL	DESCRIPTION	TYPE / DETAIL / SPEC			
			COLOR TEMP.	LUMENS	CRI	P.F
1		WALL LIGHT WITH 12 WATT LED	5000-5500K	> 80lm/w	> 80	> .95
2		LED DOWN LIGHT WITH 18 WATT	5000-5500K	> 100lm/w	> 80	> .95

" F A N S "				
NO.	SYMBOL	DESCRIPTION	SIZE	DETAIL
1		WALL MOUNTED LOUVRE BRACKET FAN	18" Ø	99.9% COPPER
2		EXHAUST FAN WITH STEEL BODY WITH 18" Ø	18" Ø	99.9% COPPER

" SWITCH & LIGHT PLUG "			
NO.	SYMBOL	DESCRIPTION	TYPE
1		10 AMP; 1 WAY FLUSH TYPE SWITCH (SWITCH BOARD).	GANG TYPE SWITCH
2		10 AMP WALL SOCKET RECESSED TYPE.	2 PIN

" POWER "			
NO.	SYMBOL	DESCRIPTION	HEIGHT
1		20 AMP POWER SOCKET	4'-0" ABOVE F.F.L
2		13 AMP POWER SOCKET UNIVERSAL TYPE	1'-0" ABOVE F.F.L
3		MCC-TW	4'-0" ABOVE F.F.L
4		MAN HOLE 24"X24"X36"	R.C.C/ BRICK
5		EARTHING SET (ROD TYPE)	ROD TYPE

GENERAL NOTES:-

01 ELECTRICAL WORKS

ALL ELECTRICAL WORKS PERTAINING TO WIRING OF ELECTRICAL SYSTEMS SHALL STRICTLY CONFORM TO BS CODES (BS 7671) .

02 ELECTRICAL CONDUITING

ALL WIRING SHALL BE DONE IN PVC CONDUIT TO BE CONCEALED IN FALSE CEILING,WALLS, SLABS,COLUMNS AND FLOOR & RGS CONDUIT IS OPEN OR AS SHOWN ON DRAWINGS.

03 ELECTRICAL WIRING

THE WIRING SHOULD BE STARTED ONLY AFTER INSPECTION OF THE CONDUIT SYSTEM HAS BEEN COMPLETED AND ALL OUTLET BOXES ARE FIXED AT THEIR RESPECTIVE POSITIONS.

04 PVC CONDUITS

ALL PVC CONDUITS SHALL BE OF AS PER MENTIONED IN DRAWINGS & EVERY CONDUIT SHOULD BE 20% FREE SPACE (DEPENDING UPON NUMBER OF WIRES) FROM SWITCH BOARD TO LIGHT POINTS & 1" DIA FROM DBs TO SWITCH BOARDS AND POWER SOCKETS OR AS SHOWN ON DRAWINGS.

05 COLOUR CODING

COLOUR CODING FOR WIRING SHALL BE AS FOLLOWS: RED,YELLOW AND BLUE FOR PHASES,BLACK FOR NEUTRAL AND GREEN / YELLOW FOR CPC (EARTH).

06 EARTHING OF POINTS

ALL LIGHT POINTS AND POWER SOCKETS SHALL BE PROPERLY EARTHED WITH SAME SIZE PVC INSULATED WIRES OF COLOUR YELLOW/GREEN FOR PHASE & NEUTRAL.

07 CAPACITY OF CONDUITS

THE NUMBER OF WIRES TO BE PULLED IN ANY CONDUIT FOR WIRING PURPOSES SHALL CONFORM TO BS CODES (BS EN 61386-25:2011) & HAVE 30% CLEARANCE.

08 OTHER SYSTEMS

1" DIA PVC CONDUIT SHALL BE USED FOR WIRING OF ALL OTHER SYSTEMS UNLESS OTHERWISE MENTIONED ON PLANS OR AS SPECIFIED IN BOQ.

09 ELECTRICAL CONSULTANT

ELECTRICAL CONTRACTOR TO CONSULT ELECTRICAL CONSULTANT/ENGINEER FOR ANY FURTHER CLARIFICATIONS.NO ASSUMPTIONS SHOULD BE MADE.

10 FERRULING

FERRULING SHOULD BE DONE ON ALL CIRCUITS FOR LIGHT & POWER & FERRULING SAMPLE SHOULD BE APPROVED BY THE ENGINEER / CONSULTANT.

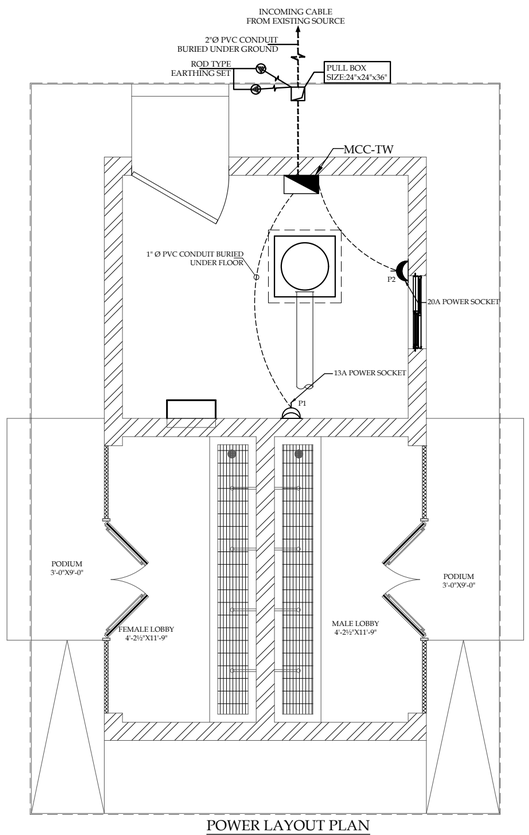

POWER LAYOUT PLAN

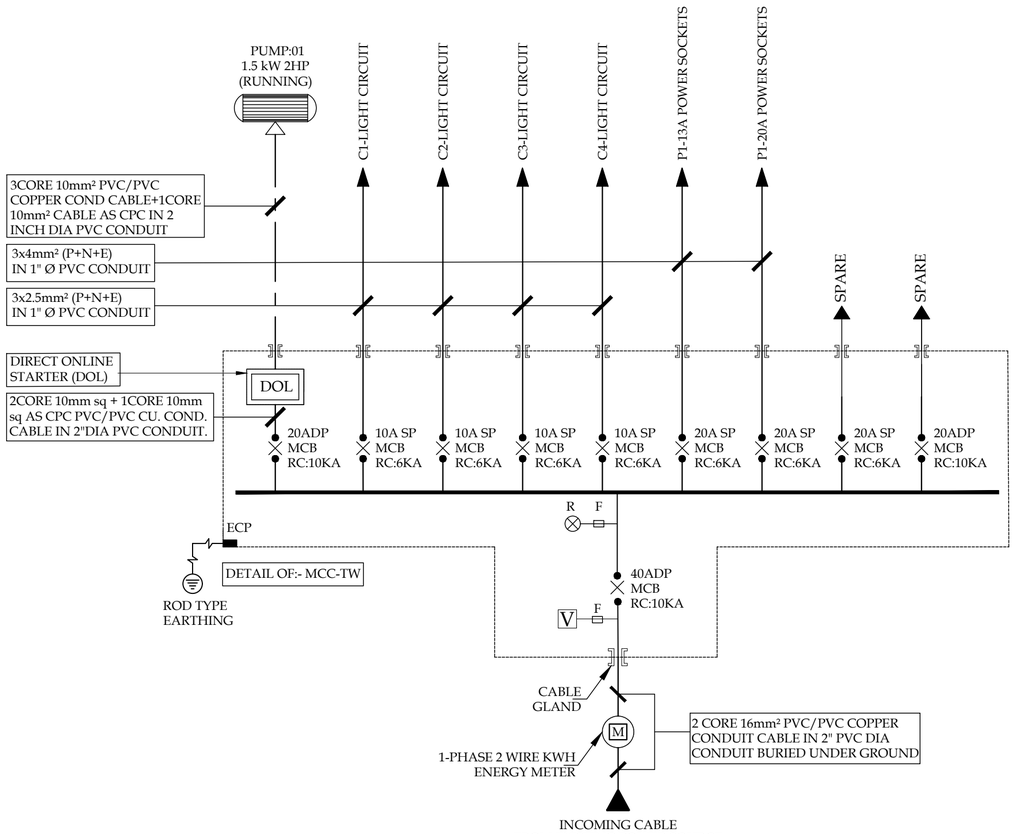

TITLE.

ELECTRICAL LIGHTING & POWER LAYOUT PLAN (TYPE-II)

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	10-12-2025	DETAILED DESIGN	ASAD	ENGR. FAEIZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING N°: PRMSC-WS-SP-E-01 | SHEET | REV 00

PROJECT: ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT: ASIAN CONSULTING ENGINEERS www.asiancon.com.pk

E-01

LEGEND AND ABBREVIATIONS

ABRV.	DESCRIPTION
CW	COLD WATER SUPPLY
HW	HOT WATER SUPPLY
HWR	HOT WATER RETURN
WP	WASTE WATER LINE
SP	SOIL WATER LINE
V	VENT PIPE
RWP	RAIN WATER PIPE
AIR	AIR VENT
DCW	DOMESTIC COLD WATER
DHW	DOMESTIC HOT WATER

HDR	HEADER PIPE
PPR	POLYPROPYLENE RANDOM PIPE
CPVC	CHLORINATED POLYVINYL CHLORIDE PIPE
UPVC	UNPLASTICIZED PVC PIPE
CI	CAST IRON PIPE
HDPE	HIGH-DENSITY POLYETHYLENE PIPE
GI	GALVANIZED IRON PIPE
PVC	POLYVINYL CHLORIDE PIPE
SS	STAINLESS STEEL PIPE
CU	COPPER PIPE
ROD	ROD-OUT POINT
TS	TEST STATION
BP	BOOSTER PUMP

PIPE SLOPES

300mm	Ø12"	1 IN 330
225mm	Ø9"	1 IN 225
160mm	Ø6"	1 IN 180
110mm	Ø4"	1 IN 100
75mm	Ø3"	1 IN 75
50mm	Ø2"	1 IN 50

GENERAL NOTES

- ALL PLUMBING WORKS SHALL BE EXECUTED STRICTLY IN ACCORDANCE WITH THE LATEST APPLICABLE CODES (E.G., IPC, UPC, ASME, ASTM, AND LOCAL AUTHORITY REQUIREMENTS).
- THE CONTRACTOR SHALL VERIFY ALL DIMENSIONS, LEVELS, SITE CONDITIONS, AND UTILITY CONNECTION POINTS BEFORE COMMENCING ANY WORK.
- DO NOT SCALE DRAWINGS. ANY DISCREPANCIES BETWEEN DRAWINGS, SITE, AND SPECIFICATIONS MUST BE BROUGHT TO THE ATTENTION OF THE ENGINEER BEFORE EXECUTION.
- COORDINATE ALL WORK WITH ARCHITECTURAL, STRUCTURAL, HVAC, ELECTRICAL, AND FIRE PROTECTION DRAWINGS BEFORE INSTALLATION.
- ALL PENETRATIONS THROUGH SLABS, WALLS, AND BEAMS SHALL BE COORDINATED WITH THE STRUCTURAL ENGINEER. USE SLEEVES WITH ANNULAR SPACE FILLED WITH APPROVED FIRE-STOPPING MATERIAL FOR FIRE-RATED ASSEMBLIES.
- ALL PIPES PASSING THROUGH WET AREAS OR UNDERGROUND SHALL BE WRAPPED OR SLEEVED WITH PROTECTIVE SLEEVES TO PREVENT CORROSION AND LEAKAGE.
- PROVIDE PIPE SUPPORTS, BRACKETS, HANGERS, AND ANCHORS AS PER MANUFACTURER'S RECOMMENDATIONS AND APPLICABLE CODES (E.G., MSS SP-58). ENSURE THERMAL EXPANSION AND CONTRACTION ALLOWANCES.
- ALL DRAINAGE AND VENT PIPING SHALL BE INSTALLED WITH REQUIRED SLOPES TO ENSURE SELF-CLEANING VELOCITY AND AVOID ACCUMULATION.
- AIR ADMITTANCE VALVES ARE NOT PERMITTED UNLESS APPROVED IN WRITING BY THE AUTHORITY HAVING JURISDICTION.
- ALL WATER SUPPLY PIPING MUST BE PRESSURE TESTED WITH POTABLE WATER TO 150% OF OPERATING PRESSURE OR MINIMUM 10 BAR (WHICHEVER IS HIGHER) FOR AT LEAST 2 HOURS WITH NO PRESSURE DROP.
- SANITARY DRAINAGE AND VENT PIPING MUST BE TESTED WITH A 10-FOOT HEAD OF WATER OR 5 PSI OF AIR PRESSURE FOR A MINIMUM OF 15 MINUTES WITHOUT LOSS.
- HOT WATER RECIRCULATION PIPING, IF REQUIRED, SHALL BE INSTALLED TO MINIMIZE WAITING TIME AT REMOTE FIXTURES. INSTALL BALANCING VALVES AND THERMAL TRAPS AS NEEDED.
- PROVIDE NON-RETURN VALVES, PRESSURE-REDUCING VALVES, STRAINERS, AND ISOLATION VALVES AT ALL STRATEGIC LOCATIONS.
- ALL PLUMBING FIXTURES AND FITTINGS MUST BE WATER-CONSERVING TYPE AND SHALL MEET RELEVANT LEED/GREEN BUILDING OR LOCAL SUSTAINABILITY REQUIREMENTS, WHERE APPLICABLE.
- WATER HEATERS (ELECTRIC, GAS, OR SOLAR) MUST BE INSTALLED WITH SAFETY VALVES, DRAIN PANS, AND THERMAL INSULATION. COORDINATE VENTING WITH MECHANICAL DRAWINGS.
- PROVIDE TRAP PRIMERS FOR FLOOR DRAINS IN DRY AREAS TO PREVENT TRAP SEAL EVAPORATION.
- ENSURE ANTI-SIPHON VACUUM BREAKERS AND BACKFLOW PREVENTERS ARE INSTALLED WHERE REQUIRED TO PROTECT POTABLE WATER SUPPLY.
- ALL PLUMBING ACCESSORIES (E.G., FAUCETS, VALVES, HOSES, DRAINS) SHALL BE OF HEAVY-DUTY COMMERCIAL GRADE AND APPROVED BY THE CONSULTANT.
- PROVIDE SEDIMENT TRAPS AT CONNECTIONS TO GAS APPLIANCES (IF APPLICABLE).
- WHERE PLUMBING SYSTEMS ARE INSTALLED IN CEILING SPACES, PROVIDE ADEQUATE ACCESS PANELS FOR MAINTENANCE OF CONCEALED FITTINGS AND VALVES.
- INSULATE ALL DOMESTIC HOT WATER AND CHILLED WATER PIPING AS PER PROJECT SPECIFICATIONS AND ENERGY CODE REQUIREMENTS.
- UNDERGROUND PIPING MUST BE LAID ON COMPACTED SAND BEDDING AND COVERED WITH FINE SAND BEFORE BACKFILLING WITH SELECTED MATERIAL.
- IDENTIFY ALL EXPOSED PIPING AND VALVES WITH COLOR-CODED LABELS, PIPE MARKERS, AND TAGS AS PER PIPING IDENTIFICATION SCHEDULE.
- COORDINATE FINAL FIXTURE LOCATIONS WITH ARCHITECTURAL INTERIOR DRAWINGS AND SITE MOCKUPS PRIOR TO INSTALLATION.
- CONTRACTOR IS RESPONSIBLE FOR ALL TRENCHING, EXCAVATION, CORE DRILLING, BACKFILLING, AND MAKING GOOD ALL DISTURBED SURFACES.
- PROVIDE ALL NECESSARY CLEANOUTS, VENT TERMINALS, AND INSPECTION CHAMBERS AS SHOWN ON DRAWINGS OR AS REQUIRED BY CODE.
- STORMWATER PIPING SHALL BE SEPARATE FROM SANITARY DRAINAGE AND DESIGNED FOR 100-YEAR RETURN PERIOD UNLESS OTHERWISE NOTED.
- CONTRACTOR SHALL PREPARE AND SUBMIT COMPLETE AS-BUILT DRAWINGS SHOWING EXACT LOCATIONS, PIPE SIZES, AND VALVE TYPES UPON PROJECT COMPLETION.
- PERFORM FULL FLUSHING, CLEANING, DISINFECTION, AND COMMISSIONING OF ALL SYSTEMS BEFORE HANDING OVER TO THE CLIENT.
- SUBMIT OPERATION & MAINTENANCE MANUALS, WARRANTIES, AND TRAINING SCHEDULES TO FACILITY MANAGEMENT TEAM AT PROJECT CLOSEOUT.
- THE CONTRACTOR SHALL ARRANGE FOR ALL REQUIRED INSPECTIONS AND APPROVALS FROM RELEVANT AUTHORITIES DURING AND AFTER CONSTRUCTION.
- ALL WORKMANSHIP SHALL BE NEAT, CLEAN, AND PROFESSIONAL. ANY POORLY EXECUTED WORK SHALL BE REMOVED AND REINSTALLED AT CONTRACTOR'S EXPENSE.

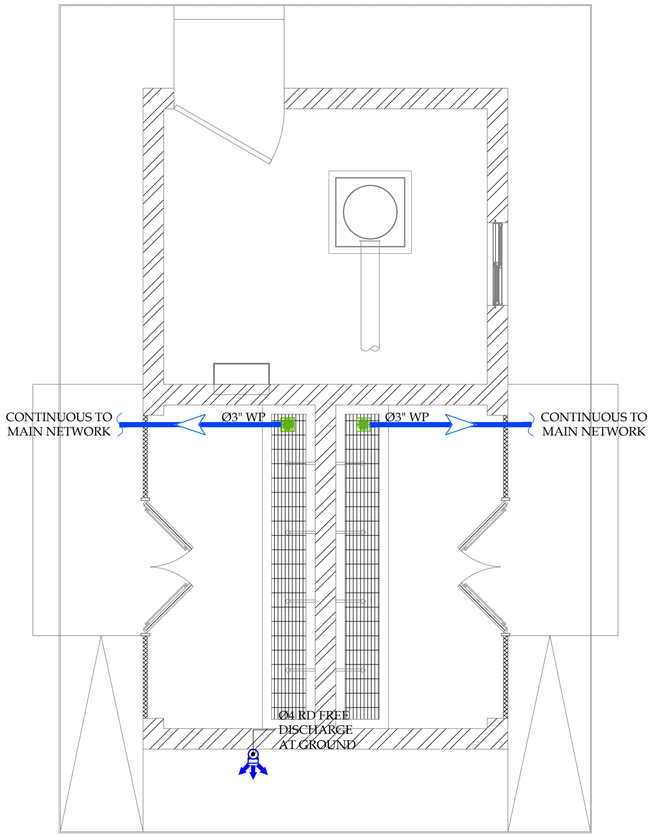

1 GROUND FLOOR LAYOUT
Scale: 3/8" = 1' - 0"

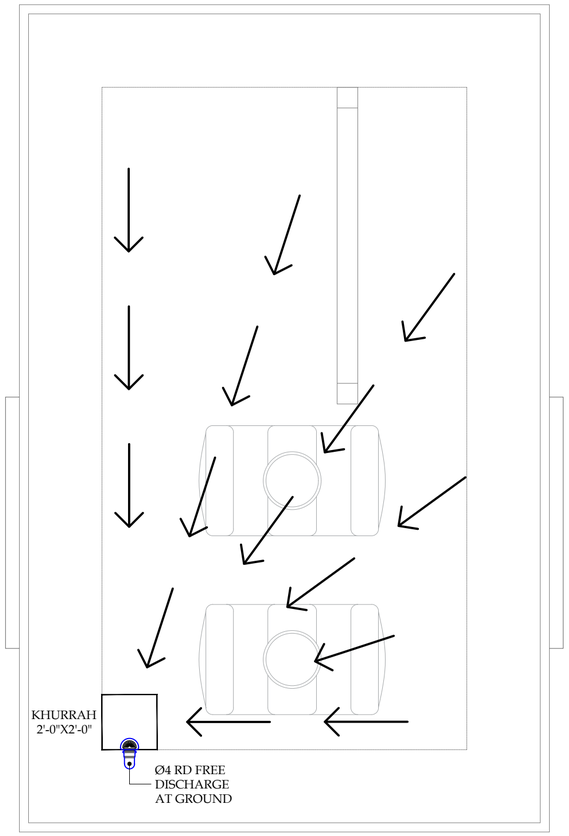

1 ROOF LAYOUT
Scale: 3/8" = 1' - 0"

TITLE.
STAND POST
DRAINAGE SYSTEM LAYOUT

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	10-12-2025	DETAILED DESIGN	ASAD	ENGR. FAEIZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº: PRMSC-WS-SP-P-01
SHEET
REV 00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:
ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

P-01

LEGEND AND ABBREVIATIONS

ABRV.	DESCRIPTION
CW	COLD WATER SUPPLY
HW	HOT WATER SUPPLY
HWR	HOT WATER RETURN
WP	WASTE WATER LINE
SP	SOIL WATER LINE
V	VENT PIPE
RWP	RAIN WATER PIPE
AIR	AIR VENT
DCW	DOMESTIC COLD WATER
DHW	DOMESTIC HOT WATER

HDR	HEADER PIPE
PPR	POLYPROPYLENE RANDOM PIPE
CPVC	CHLORINATED POLYVINYL CHLORIDE PIPE
UPVC	UNPLASTICIZED PVC PIPE
CI	CAST IRON PIPE
HDPE	HIGH-DENSITY POLYETHYLENE PIPE
GI	GALVANIZED IRON PIPE
PVC	POLYVINYL CHLORIDE PIPE
SS	STAINLESS STEEL PIPE
CU	COPPER PIPE
ROD	ROD-OUT POINT
TS	TEST STATION
BP	BOOSTER PUMP

PIPE SLOPES

300mm	Ø12"	1 IN 330
225mm	Ø9"	1 IN 225
160mm	Ø6"	1 IN 180
110mm	Ø4"	1 IN 100
75mm	Ø3"	1 IN 75
50mm	Ø2"	1 IN 50

GENERAL NOTES

- ALL PLUMBING WORKS SHALL BE EXECUTED STRICTLY IN ACCORDANCE WITH THE LATEST APPLICABLE CODES (E.G., IPC, UPC, ASME, ASTM, AND LOCAL AUTHORITY REQUIREMENTS).
- THE CONTRACTOR SHALL VERIFY ALL DIMENSIONS, LEVELS, SITE CONDITIONS, AND UTILITY CONNECTION POINTS BEFORE COMMENCING ANY WORK.
- DO NOT SCALE DRAWINGS. ANY DISCREPANCIES BETWEEN DRAWINGS, SITE, AND SPECIFICATIONS MUST BE BROUGHT TO THE ATTENTION OF THE ENGINEER BEFORE EXECUTION.
- COORDINATE ALL WORK WITH ARCHITECTURAL, STRUCTURAL, HVAC, ELECTRICAL, AND FIRE PROTECTION DRAWINGS BEFORE INSTALLATION.
- ALL PENETRATIONS THROUGH SLABS, WALLS, AND BEAMS SHALL BE COORDINATED WITH THE STRUCTURAL ENGINEER. USE SLEEVES WITH ANNULAR SPACE FILLED WITH APPROVED FIRE-STOPPING MATERIAL FOR FIRE-RATED ASSEMBLIES.
- ALL PIPES PASSING THROUGH WET AREAS OR UNDERGROUND SHALL BE WRAPPED OR SLEEVED WITH PROTECTIVE SLEEVES TO PREVENT CORROSION AND LEAKAGE.
- PROVIDE PIPE SUPPORTS, BRACKETS, HANGERS, AND ANCHORS AS PER MANUFACTURER'S RECOMMENDATIONS AND APPLICABLE CODES (E.G., MSS SP-58). ENSURE THERMAL EXPANSION AND CONTRACTION ALLOWANCES.
- ALL DRAINAGE AND VENT PIPING SHALL BE INSTALLED WITH REQUIRED SLOPES TO ENSURE SELF-CLEANING VELOCITY AND AVOID ACCUMULATION.
- AIR ADMITTANCE VALVES ARE NOT PERMITTED UNLESS APPROVED IN WRITING BY THE AUTHORITY HAVING JURISDICTION.
- ALL WATER SUPPLY PIPING MUST BE PRESSURE TESTED WITH POTABLE WATER TO 150% OF OPERATING PRESSURE OR MINIMUM 10 BAR (WHICHEVER IS HIGHER) FOR AT LEAST 2 HOURS WITH NO PRESSURE DROP.
- SANITARY DRAINAGE AND VENT PIPING MUST BE TESTED WITH A 10-FOOT HEAD OF WATER OR 5 PSI OF AIR PRESSURE FOR A MINIMUM OF 15 MINUTES WITHOUT LOSS.
- HOT WATER RECIRCULATION PIPING, IF REQUIRED, SHALL BE INSTALLED TO MINIMIZE WAITING TIME AT REMOTE FIXTURES. INSTALL BALANCING VALVES AND THERMAL TRAPS AS NEEDED.
- PROVIDE NON-RETURN VALVES, PRESSURE-REDUCING VALVES, STRAINERS, AND ISOLATION VALVES AT ALL STRATEGIC LOCATIONS.
- ALL PLUMBING FIXTURES AND FITTINGS MUST BE WATER-CONSERVING TYPE AND SHALL MEET RELEVANT LEED/GREEN BUILDING OR LOCAL SUSTAINABILITY REQUIREMENTS, WHERE APPLICABLE.
- WATER HEATERS (ELECTRIC, GAS, OR SOLAR) MUST BE INSTALLED WITH SAFETY VALVES, DRAIN PANS, AND THERMAL INSULATION. COORDINATE VENTING WITH MECHANICAL DRAWINGS.
- PROVIDE TRAP PRIMERS FOR FLOOR DRAINS IN DRY AREAS TO PREVENT TRAP SEAL EVAPORATION.
- ENSURE ANTI-SIPHON VACUUM BREAKERS AND BACKFLOW PREVENTERS ARE INSTALLED WHERE REQUIRED TO PROTECT POTABLE WATER SUPPLY.
- ALL PLUMBING ACCESSORIES (E.G., FAUCETS, VALVES, HOSES, DRAINS) SHALL BE OF HEAVY-DUTY COMMERCIAL GRADE AND APPROVED BY THE CONSULTANT.
- PROVIDE SEDIMENT TRAPS AT CONNECTIONS TO GAS APPLIANCES (IF APPLICABLE).
- WHERE PLUMBING SYSTEMS ARE INSTALLED IN CEILING SPACES, PROVIDE ADEQUATE ACCESS PANELS FOR MAINTENANCE OF CONCEALED FITTINGS AND VALVES.
- INSULATE ALL DOMESTIC HOT WATER AND CHILLED WATER PIPING AS PER PROJECT SPECIFICATIONS AND ENERGY CODE REQUIREMENTS.
- UNDERGROUND PIPING MUST BE LAID ON COMPACTED SAND BEDDING AND COVERED WITH FINE SAND BEFORE BACKFILLING WITH SELECTED MATERIAL.
- IDENTIFY ALL EXPOSED PIPING AND VALVES WITH COLOR-CODED LABELS, PIPE MARKERS, AND TAGS AS PER PIPING IDENTIFICATION SCHEDULE.
- COORDINATE FINAL FIXTURE LOCATIONS WITH ARCHITECTURAL INTERIOR DRAWINGS AND SITE MOCKUPS PRIOR TO INSTALLATION.
- CONTRACTOR IS RESPONSIBLE FOR ALL TRENCHING, EXCAVATION, CORE DRILLING, BACKFILLING, AND MAKING GOOD ALL DISTURBED SURFACES.
- PROVIDE ALL NECESSARY CLEANOUTS, VENT TERMINALS, AND INSPECTION CHAMBERS AS SHOWN ON DRAWINGS OR AS REQUIRED BY CODE.
- STORMWATER PIPING SHALL BE SEPARATE FROM SANITARY DRAINAGE AND DESIGNED FOR 100-YEAR RETURN PERIOD UNLESS OTHERWISE NOTED.
- CONTRACTOR SHALL PREPARE AND SUBMIT COMPLETE AS-BUILT DRAWINGS SHOWING EXACT LOCATIONS, PIPE SIZES, AND VALVE TYPES UPON PROJECT COMPLETION.
- PERFORM FULL FLUSHING, CLEANING, DISINFECTION, AND COMMISSIONING OF ALL SYSTEMS BEFORE HANDING OVER TO THE CLIENT.
- SUBMIT OPERATION & MAINTENANCE MANUALS, WARRANTIES, AND TRAINING SCHEDULES TO FACILITY MANAGEMENT TEAM AT PROJECT CLOSEOUT.
- THE CONTRACTOR SHALL ARRANGE FOR ALL REQUIRED INSPECTIONS AND APPROVALS FROM RELEVANT AUTHORITIES DURING AND AFTER CONSTRUCTION.
- ALL WORKMANSHIP SHALL BE NEAT, CLEAN, AND PROFESSIONAL. ANY POORLY EXECUTED WORK SHALL BE REMOVED AND REINSTALLED AT CONTRACTOR'S EXPENSE.

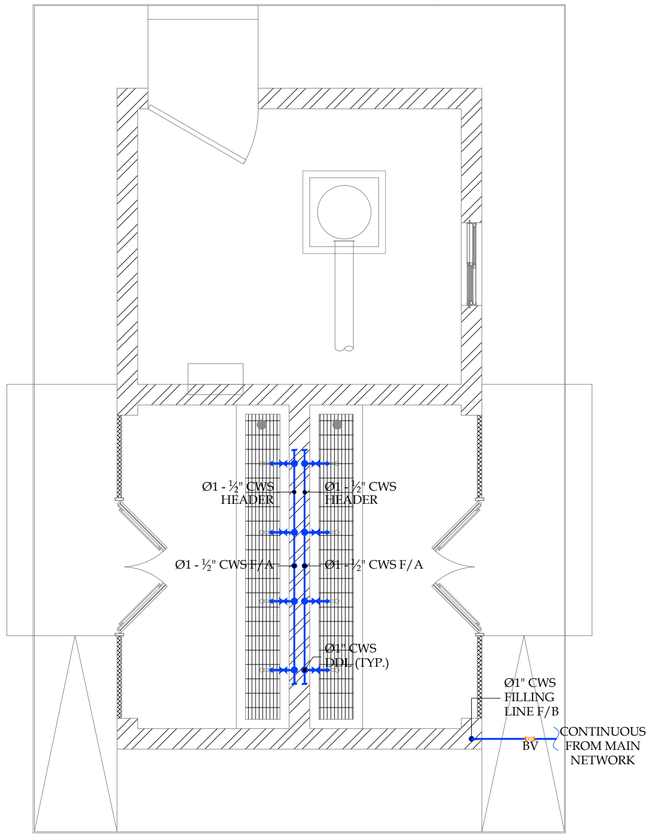

1 GROUND FLOOR LAYOUT
Scale: 3/8" = 1' - 0"

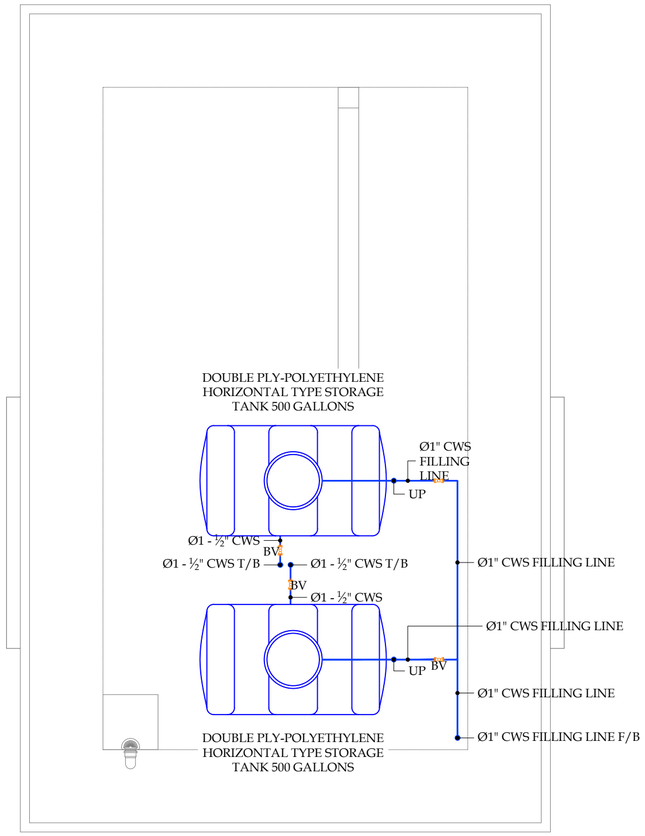

1 ROOF LAYOUT
Scale: 3/8" = 1' - 0"

TITLE.
STAND POST
WATER SUPPLY SYSTEM LAYOUT

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	10-12-2025	DETAILED DESIGN	ASAD	ENGR. FAEIZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº: PRMSC-WS-SP-P-02 | SHEET | REV 00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:
ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

RO PLANT

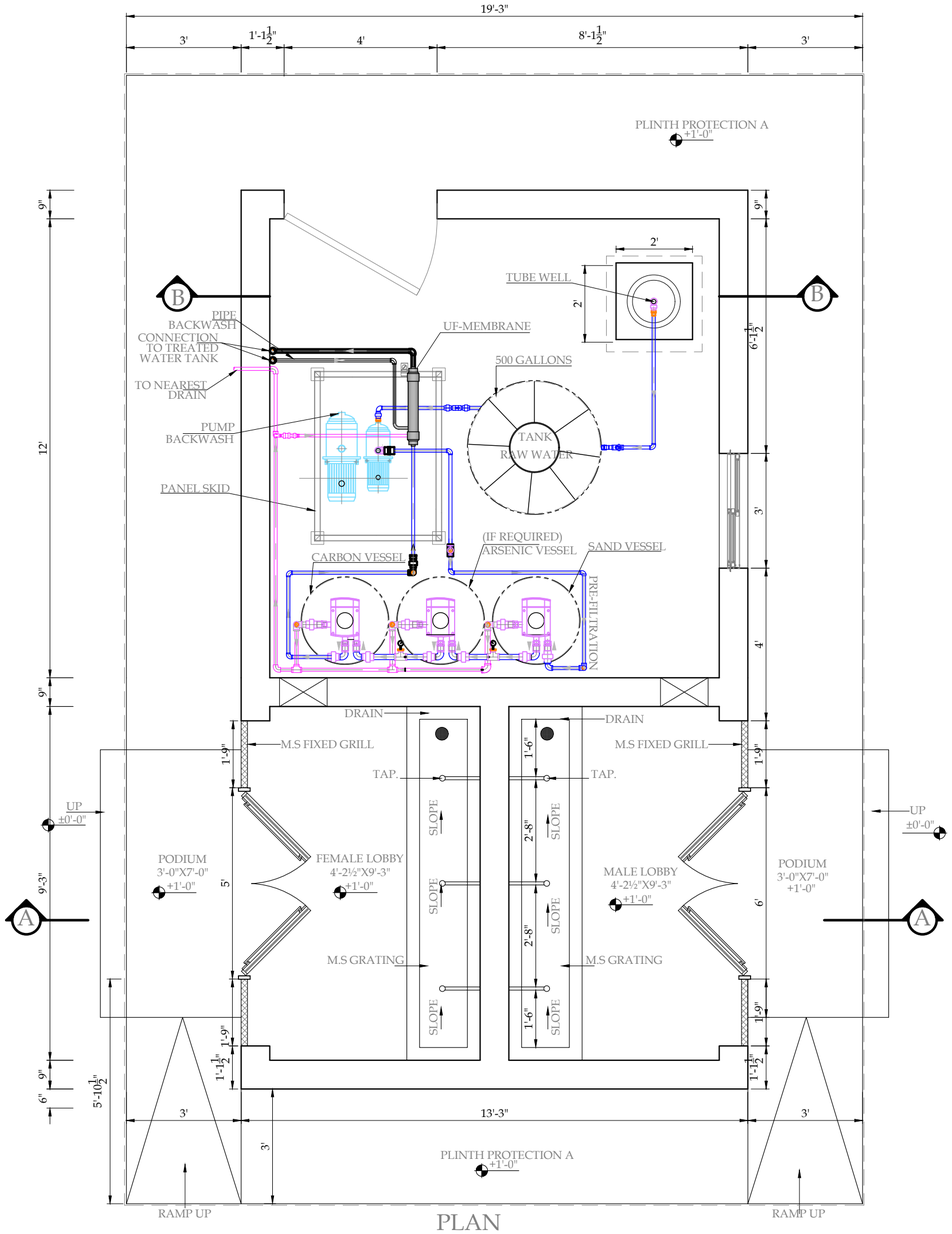

PLAN

SCALE:- 3/8" = 1'-0"

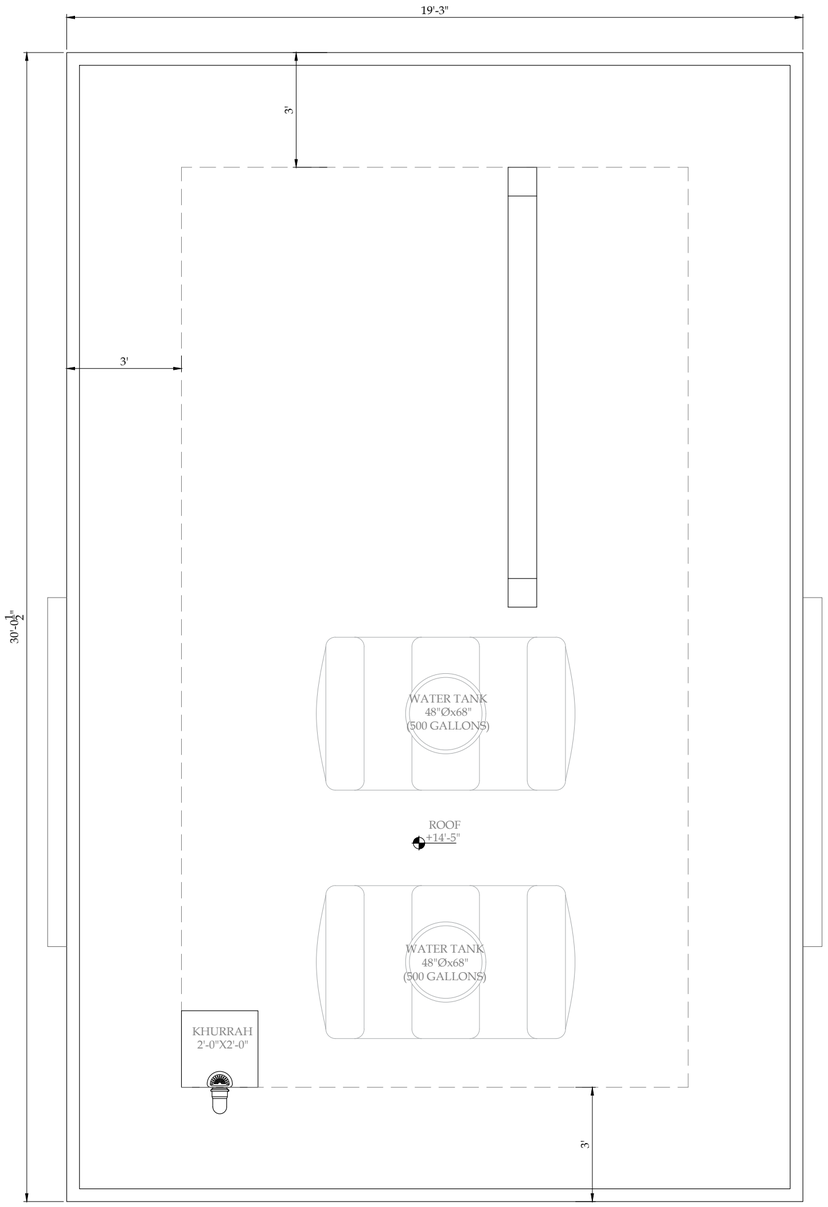

ROOF PLAN

SCALE:- 3/8" = 1'-0"

LEGEND

- FEED PIPE (uPVC 1")
- DRAIN PIPE (uPVC 3/4")
- PRODUCT PIPE (uPVC 3/4")
- BACKWASH PIPE (PPRC 1")

TITLE.

RO PLANT
PLAN & SECTION

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	10-12-2025	DETAILED DESIGN	ASAD	ENGR. FAEIZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:

PRMSC-WS-SP-C-01

SHEET

REV 00

PROJECT:

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:

PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS www.asianconsultingengineers.com

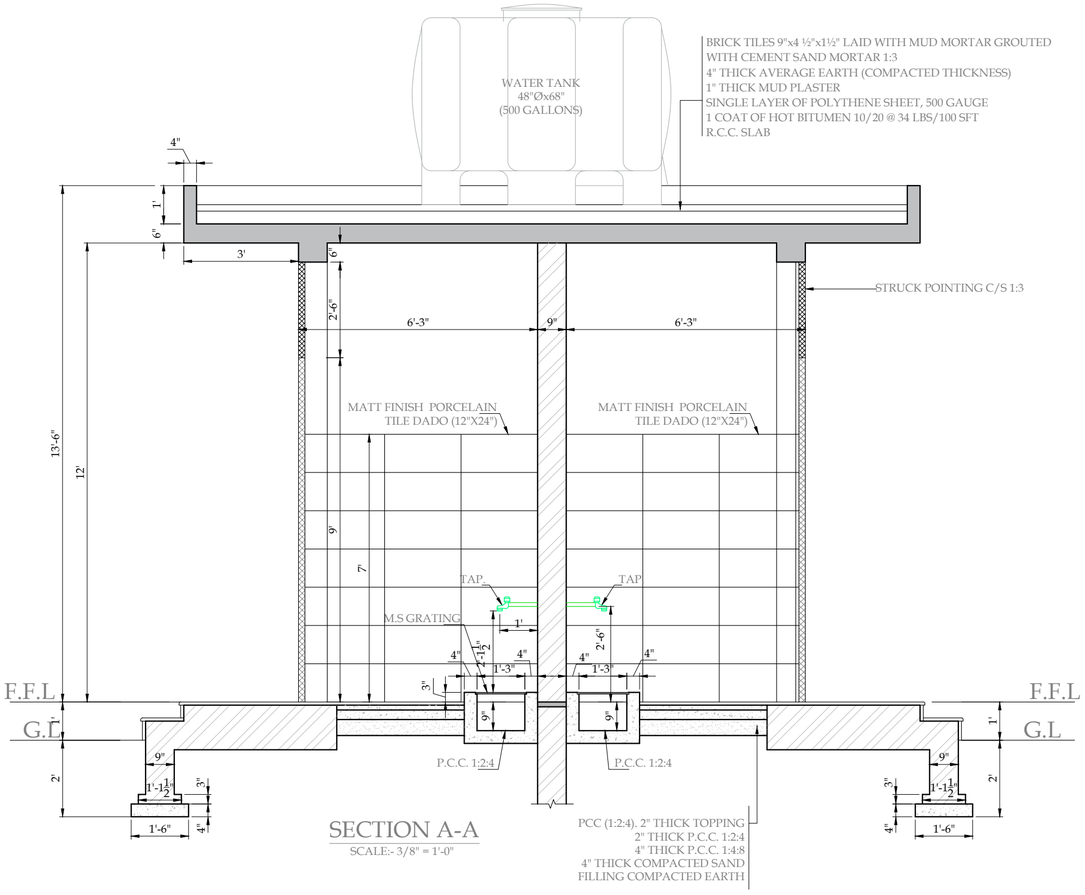

SECTION A-A

SCALE:- 3/8" = 1'-0"

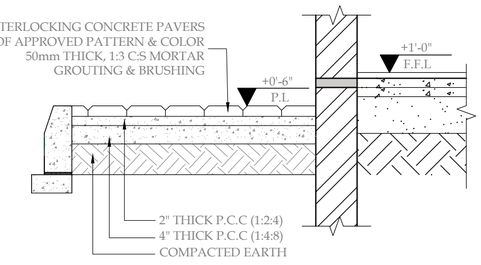

PLINTH PROTECTION DETAIL

SCALE:- 1/2" = 1'-0"

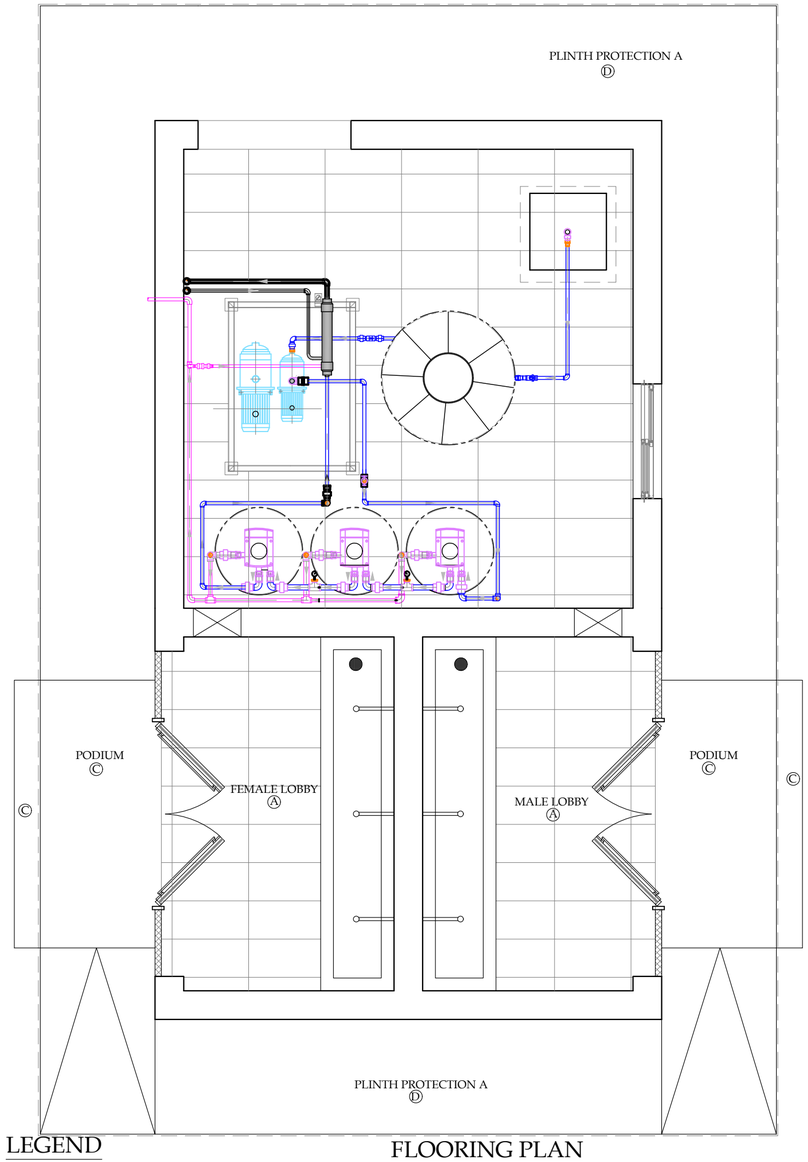

LEGEND

A= MATT FINISH PORCELAIN TILE (12"X24")
B=1/2" THICK MOSAIC FLOORING
C= 3/4" TH. CHINA VERONA MARBLE SLAB
D= 50mm CONCRETE PAVERS

FLOORING PLAN

SCALE:- 3/8" = 1'-0"

TITLE.

RO PLANT
FRONT,SIDE ELEVATIONS & FLOORING PLAN

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	10-12-2025	DETAILED DESIGN	ASAD	ENGR. FAEIZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING N°: PRMSC-WS-SP-C-02

SHEET

REV 00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS www.asiancon.com.pk

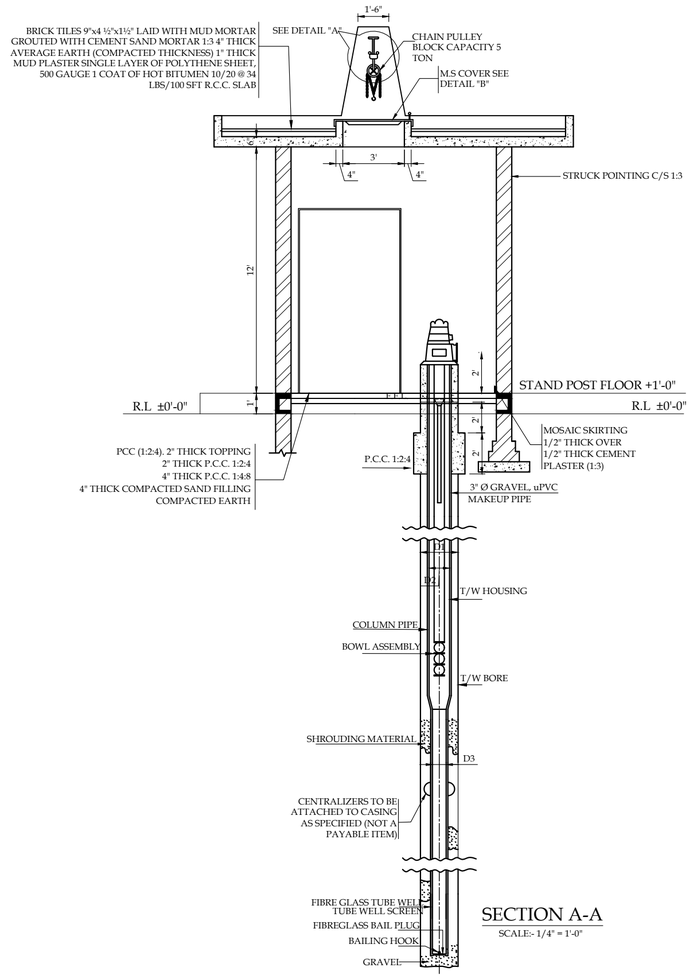

SECTION A-A

SCALE:- 1/4" = 1'-0"

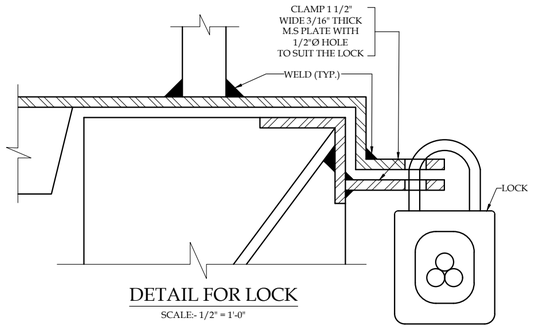

DETAIL FOR LOCK

SCALE:- 1/2" = 1'-0"

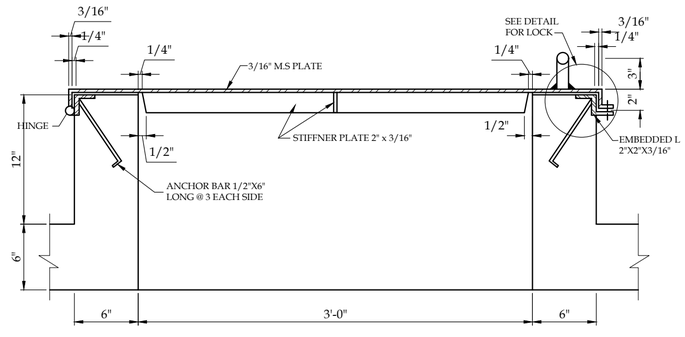

SECTION D-D

SCALE:- 1/2" = 1'-0"

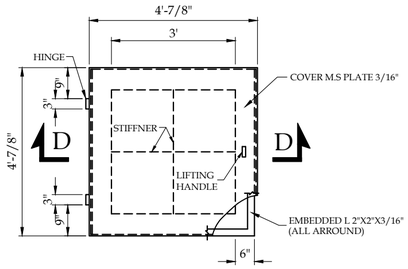

DETAIL "B"

SCALE:- 1/2" = 1'-0"

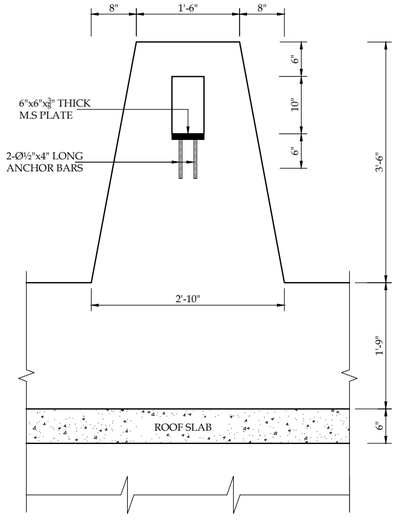

SIDE ELEVATION OF GIRDER LIFT WALL DETAIL-A

SCALE:- 3/4" = 1'-0"



REDUCER DETAIL

SCALE:- 3/4" = 1'-0"

BRICK TILES 9"x4 ½"x1½" LAID WITH MUD MORTAR GROUTED WITH CEMENT SAND MORTAR 1:3 4" THICK AVERAGE EARTH (COMPACTED THICKNESS) 1" THICK MUD PLASTER SINGLE LAYER OF POLYTHENE SHEET, 500 GAUGE 1 COAT OF HOT BITUMEN 10/20 @ 34 LBS/100 SFT R.C.C. SLAB

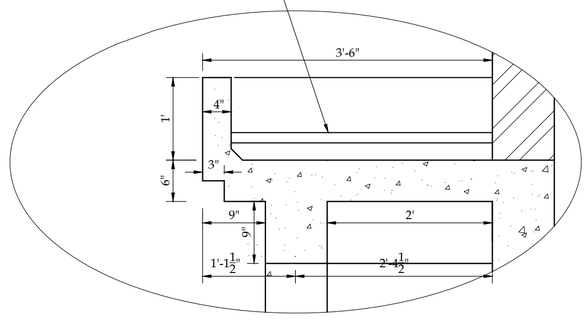

DETAIL "X"

SCALE:- 3/4" = 1'-0"

SCHEDULE OF TUBE WELL

DESCRIPTION	SIZE PUMP-1	SIZE PUMP-2
TUBEWELL CAPACITY	0.05 CUSEC	0.15-0.5 CUSEC
D1	8"	18"
D2	6"	12"
D3	4"	8"
D4	4"	6"
SETTING DEPTH	60'	80'
STRAINER LENGTH	10'	50'
BAIL PLUG	10'	10'
BORE DEPTH	90'±	200'±

TITLE.

TUBE WELL
PLAN & SECTION

ORIGINAL :		DATE :		SCALE :	
A2		JULY, 2025			
ISSUE N°.	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	10-12-2025	DETAILED DESIGN	ASAD	ENGR. FAEIZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:

PRMSC-WS-SP-C-02A

SHEET

REV 00

PROJECT:

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:

PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

2A

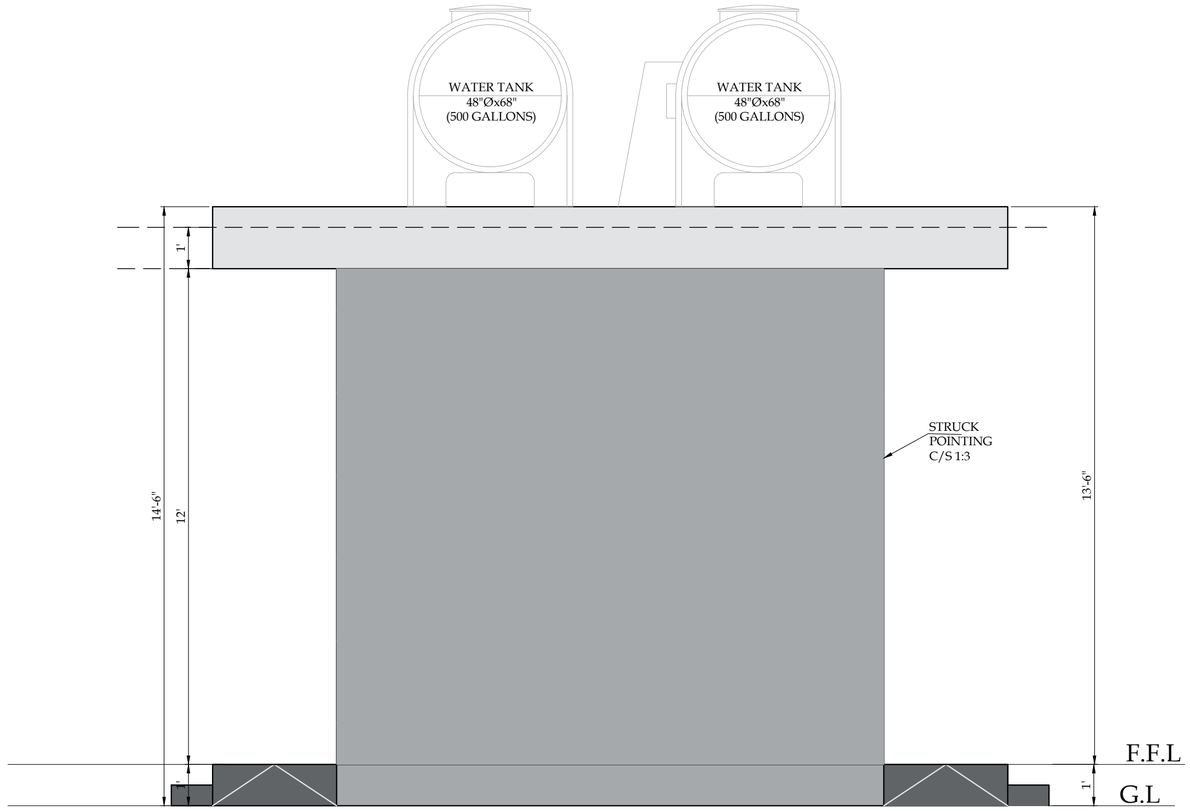

SIDE ELEVATION

SCALE:- 3/8" = 1'-0"

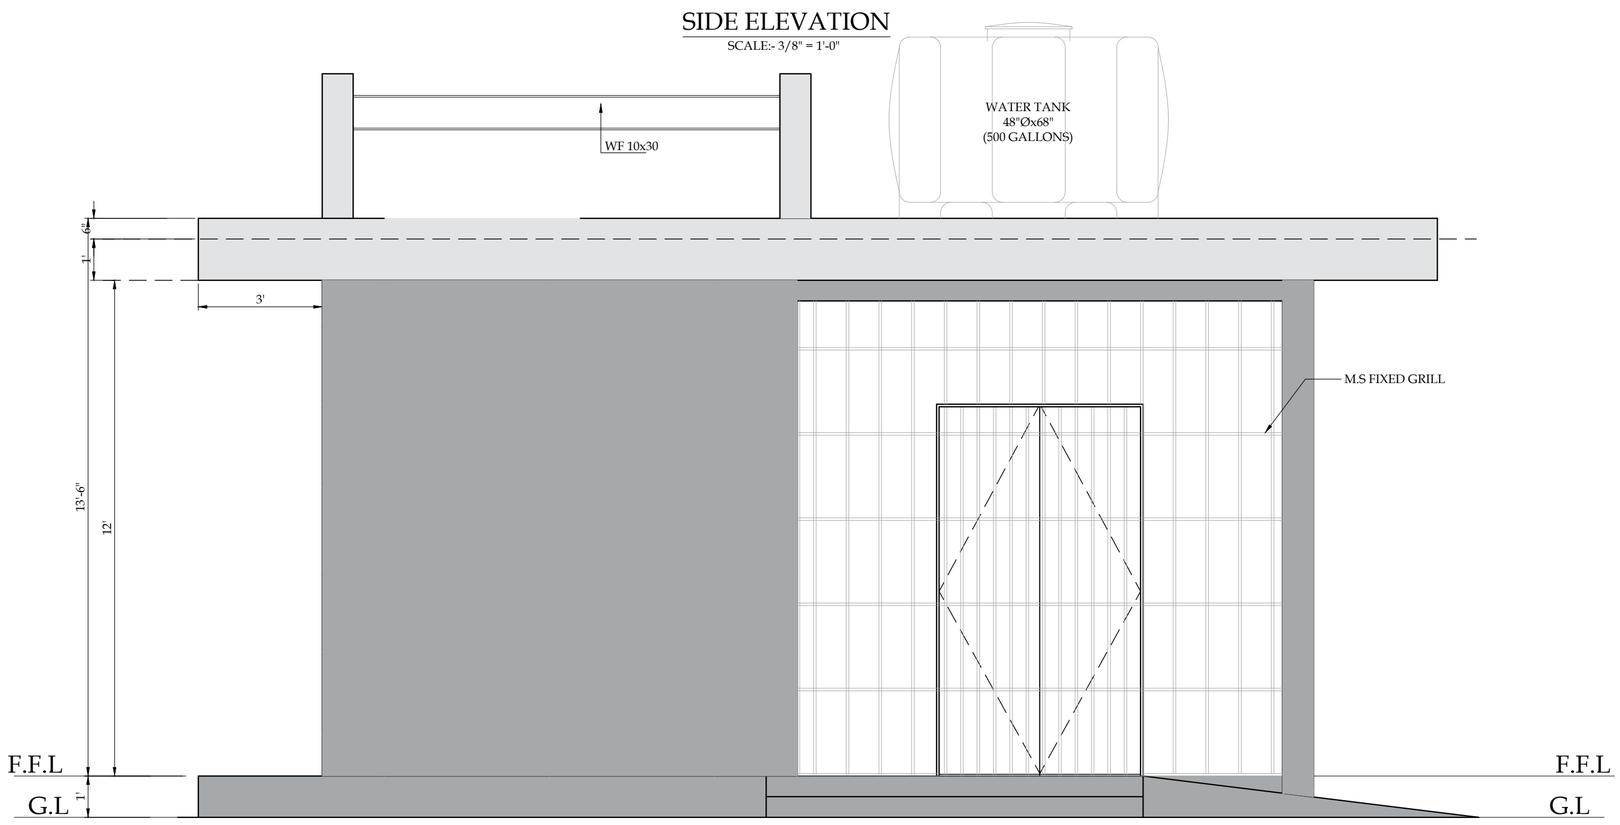

FRONT ELEVATION

SCALE:- 3/8" = 1'-0"

TITLE.

STAND POST TYPE-II
FRONT,SIDE ELEVATIONS &
FLOORING PLAN

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	10-12-2025	DETAILED DESIGN	ASAD	ENGR. FAEIZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-WS-SP-C-03		00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

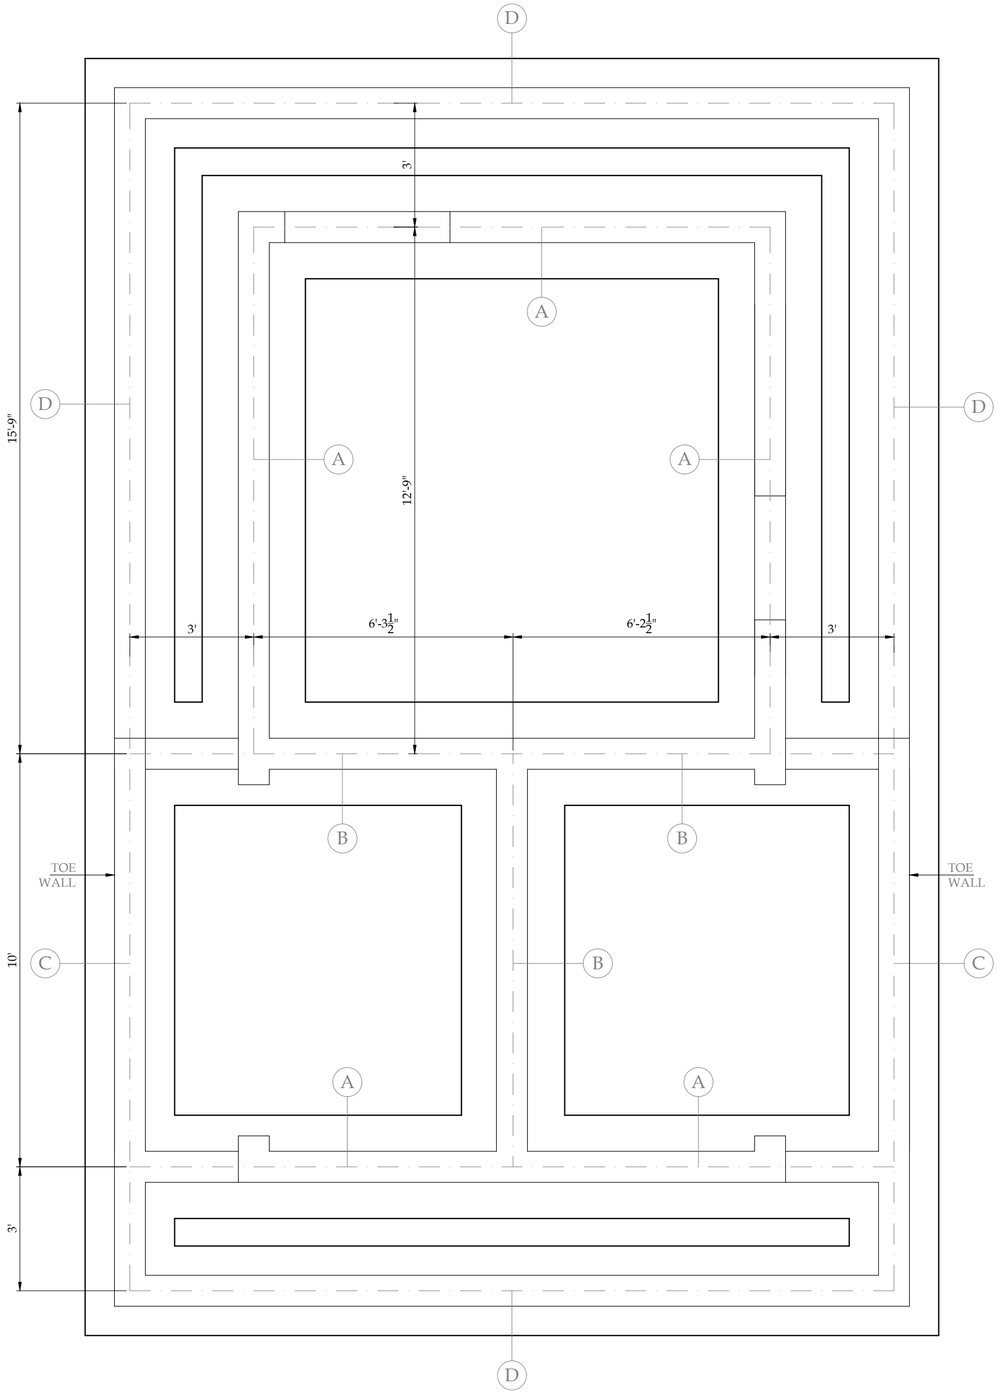

FOUNDATION LAYOUT PLAN

SCALE:- 3/8" = 1'-0"

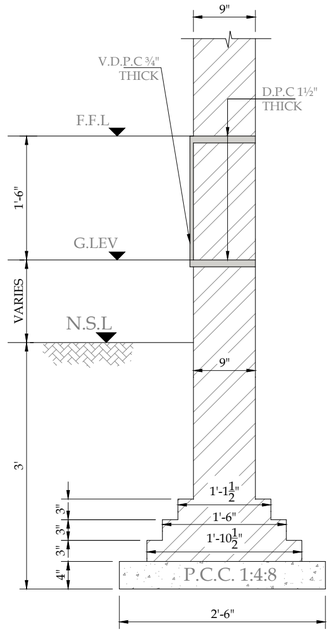

TYPE-A

SCALE:- 3/4" = 1'-0"

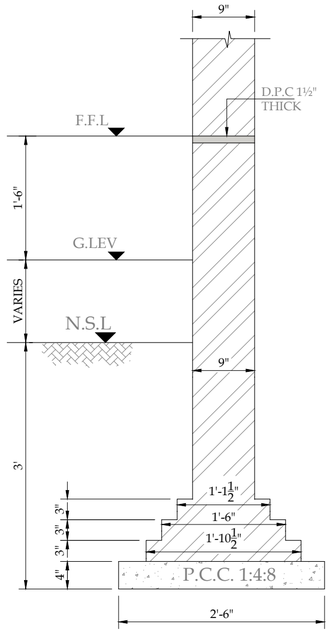

TYPE-B

SCALE:- 3/4" = 1'-0"

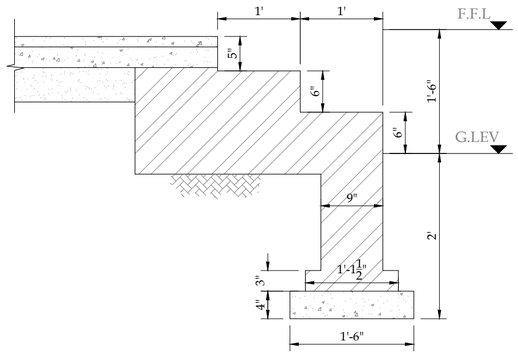

TYPE-C

SCALE:- 3/4" = 1'-0"

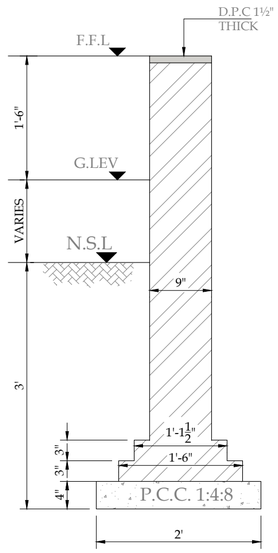

TYPE-D

SCALE:- 3/4" = 1'-0"

TITLE.

FOUNDATION LAYOUT PLAN & SECTIONAL DETAILS

ORIGINAL :		DATE :		SCALE :		
A2		JULY, 2025				
ISSUE N°	DATE	DESCRIPTION		DRAWN	DESIGNED	APPROVED
01	10-12-2025	DETAILED DESIGN		ASAD	ENGR FAEIZ	ENGR IHSAN-UL-HAQ
02						
03						
04						
05						
06						
07						

DRAWING Nº:

PRMSC-WS-SP-S-01

SHEET

REV 00

PROJECT:

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS www.asiancon.com

S-01

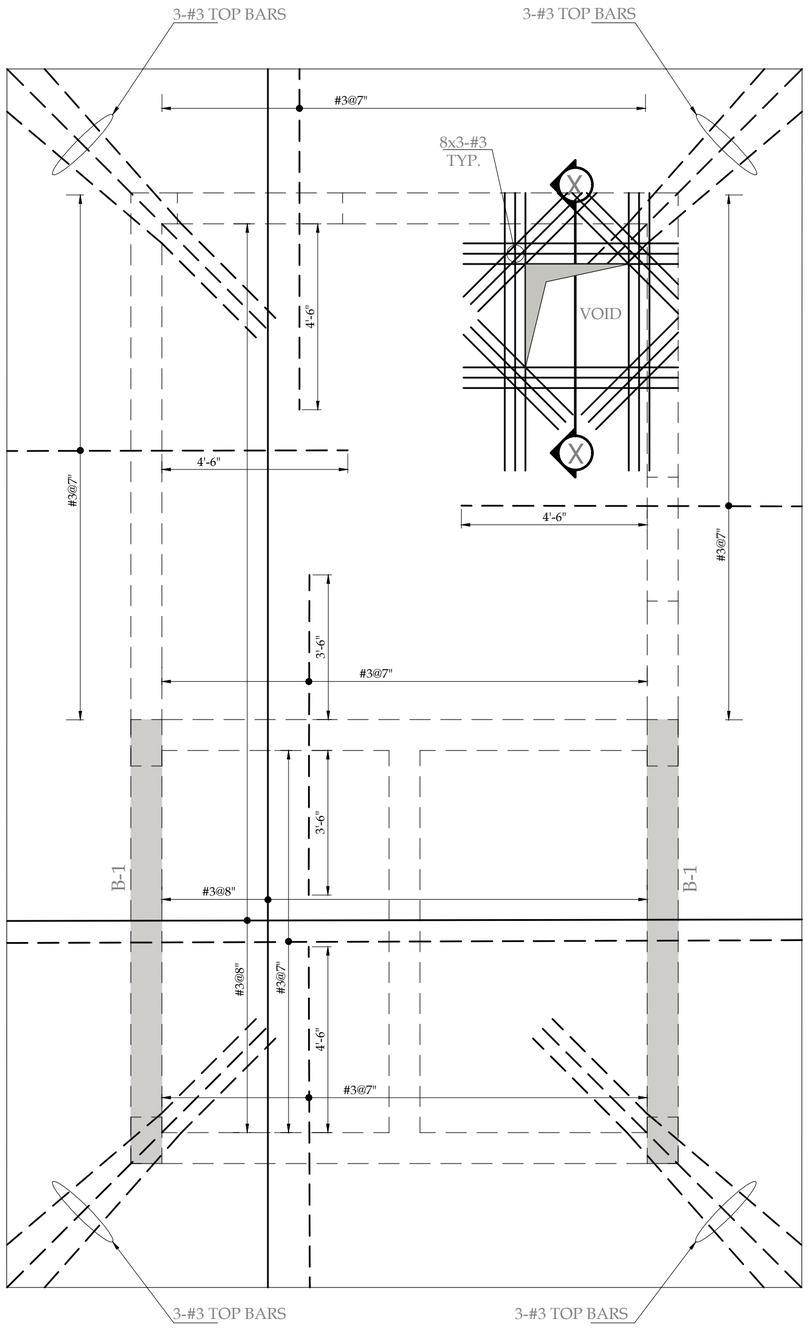

ROOF SLAB REINFORCEMENT PLAN

SCALE:- 3/8" = 1'-0"

NOTE:

1. THICKNESS OF ALL SLABS IS 6" UNLESS OTHERWISE NOTED.
2. DISTRIBUTION TOP BARS #3@12"c/c.

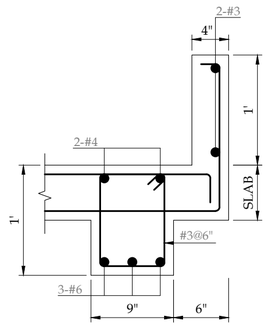

BEAM B-1

SCALE:- 1" = 1'-0"

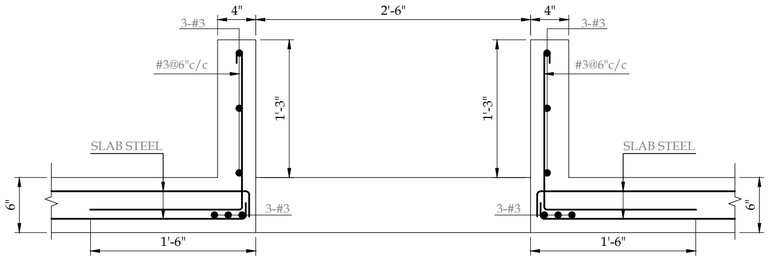

SECTION X-X

SCALE:- 1" = 1'-0"

TITLE.

ROOF SLAB REINFORCEMENT PLAN & SECTIONAL DETAILS

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	10-12-2025	DETAILED DESIGN	ASAD	ENGR. FAEIZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº: PRMSC-WS-SP-S-02 | SHEET | REV 00

PROJECT: ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS www.asiancon.com.pk

S-02

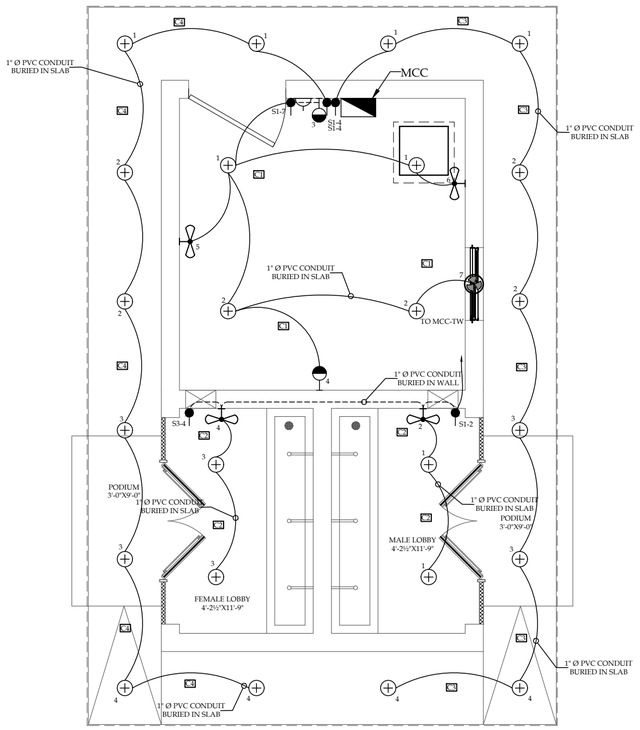

LIGHTING LAYOUT PLAN

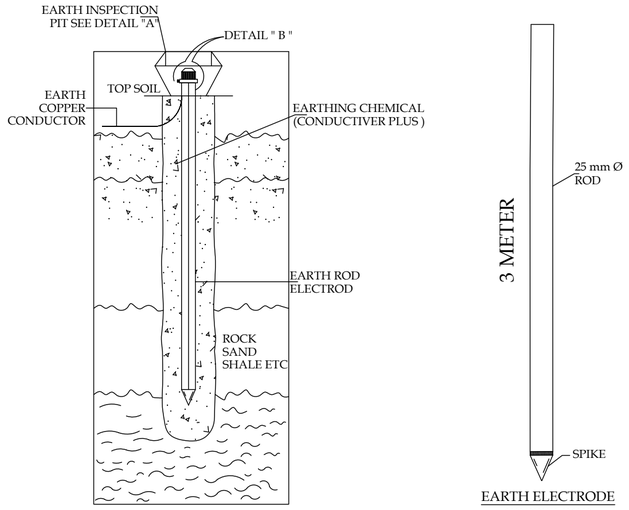

EARTH ROD INSTALLATION DETAIL

EARTH ELECTRODE COPPER ROD



EARTH INSPECTION PIT DETAIL "A"



DETAIL " B "

U BOND CONNECTION EARTHING

NOTES FOR EARTHING SYSTEM

1- EARTH BORE SHALL BE MADE AT 6'-0" AWAY FROM R.C.C FOUNDATION.

2- DISTANCE BETWEEN 2 EARTH BORES SHALL NOT BE LESS THEN 10'-0"

3- COPPER CONDUCTOR AT TOP SHALL BE BOLTED WITH THIMBLES, BRASS NUTS,BOLTS ETC/WELD POWDER.

4- JOINTS SHALL BE COVERED WITH HEAT SHRINKABLE TAPE.

5- CONTRACTOR TO MEASURE EARTHING RESISTANCE IN THE PRESENCE OF SITE ENGINEER. BOTH THE SITE ENGINEER AND CONTRACTOR SHALL SIGN THE EARTH TESTING RESULT AND SUBMIT IT TO THE CLIENT FOR RECORD WITH EQUIPMENT CALIBRATION CERTIFICATE.

6-THE EARTH RESISTANCE VALUE AFTER INSTALLATION SHALL BE LESS THAN THREE (3) OHM.

7-ALL MATERIAL OF THE ELECTRODE WILL BE OF COPPER.

" L I G H T S "

NO.	SYMBOL	DESCRIPTION	TYPE / DETAIL / SPEC			
			COLOR TEMP.	LUMENS	CRI	P.F
1		WALL LIGHT WITH 12 WATT LED	5000-5500K	> 80lm/w	> 80	> .95
2		LED DOWN LIGHT WITH 18 WATT	5000-5500K	> 100lm/w	> 80	> .95

" F A N S "

NO.	SYMBOL	DESCRIPTION	SIZE	DETAIL
1		WALL MOUNTED LOUVRE BRACKET FAN	18" Ø	99.9% COPPER
2		EXHAUST FAN WITH STEEL BODY WITH 18" Ø	18" Ø	99.9% COPPER

" SWITCH & LIGHT PLUG "

NO.	SYMBOL	DESCRIPTION	TYPE
1		10 AMP; 1 WAY FLUSH TYPE SWITCH (SWITCH BOARD).	GANG TYPE SWITCH
2		10 AMP WALL SOCKET RECESSED TYPE.	2 PIN

" P O W E R "

NO.	SYMBOL	DESCRIPTION	HEIGHT
1		20 AMP POWER SOCKET	4'-0" ABOVE F.F.L
2		13 AMP POWER SOCKET UNIVERSAL TYPE	1'-0" ABOVE F.F.L
3		MCC	4'-0" ABOVE F.F.L
4		MAN HOLE 24"X24"X36"	R.C.C/ BRICK
5		EARTHING SET (ROD TYPE)	ROD TYPE

GENERAL NOTES:-

01 ELECTRICAL WORKS

ALL ELECTRICAL WORKS PERTAINING TO WIRING OF ELECTRICAL SYSTEMS SHALL STRICTLY CONFORM TO BS CODES (BS 7671) .

02 ELECTRICAL CONDUITING

ALL WIRING SHALL BE DONE IN PVC CONDUIT TO BE CONCEALED IN FALSE CEILING,WALLS, SLABS,COLUMNS AND FLOOR & RGS CONDUIT IS OPEN OR AS SHOWN ON DRAWINGS.

03 ELECTRICAL WIRING

THE WIRING SHOULD BE STARTED ONLY AFTER INSPECTION OF THE CONDUIT SYSTEM HAS BEEN COMPLETED AND ALL OUTLET BOXES ARE FIXED AT THEIR RESPECTIVE POSITIONS.

04 PVC CONDUITS

ALL PVC CONDUITS SHALL BE OF AS PER MENTIONED IN DRAWINGS & EVERY CONDUIT SHOULD BE 20% FREE SPACE (DEPENDING UPON NUMBER OF WIRES) FROM SWITCH BOARD TO LIGHT POINTS & 1" DIA FROM DBs TO SWITCH BOARDS AND POWER SOCKETS OR AS SHOWN ON DRAWINGS.

05 COLOUR CODING

COLOUR CODING FOR WIRING SHALL BE AS FOLLOWS: RED,YELLOW AND BLUE FOR PHASES,BLACK FOR NEUTRAL AND GREEN / YELLOW FOR CPC (EARTH).

06 EARTHING OF POINTS

ALL LIGHT POINTS AND POWER SOCKETS SHALL BE PROPERLY EARTHED WITH SAME SIZE PVC INSULATED WIRES OF COLOUR YELLOW/GREEN FOR PHASE & NEUTRAL.

07 CAPACITY OF CONDUITS

THE NUMBER OF WIRES TO BE PULLED IN ANY CONDUIT FOR WIRING PURPOSES SHALL CONFORM TO BS CODES (BS EN 61386-25:2011) & HAVE 30% CLEARANCE.

08 OTHER SYSTEMS

1" DIA PVC CONDUIT SHALL BE USED FOR WIRING OF ALL OTHER SYSTEMS UNLESS OTHERWISE MENTIONED ON PLANS OR AS SPECIFIED IN BOQ.

09 ELECTRICAL CONSULTANT

ELECTRICAL CONTRACTOR TO CONSULT ELECTRICAL CONSULTANT/ENGINEER FOR ANY FURTHER CLARIFICATIONS.NO ASSUMPTIONS SHOULD BE MADE.

10 FERRULING

FERRULING SHOULD BE DONE ON ALL CIRCUITS FOR LIGHT & POWER & FERRULING SAMPLE SHOULD BE APPROVED BY THE ENGINEER / CONSULTANT.

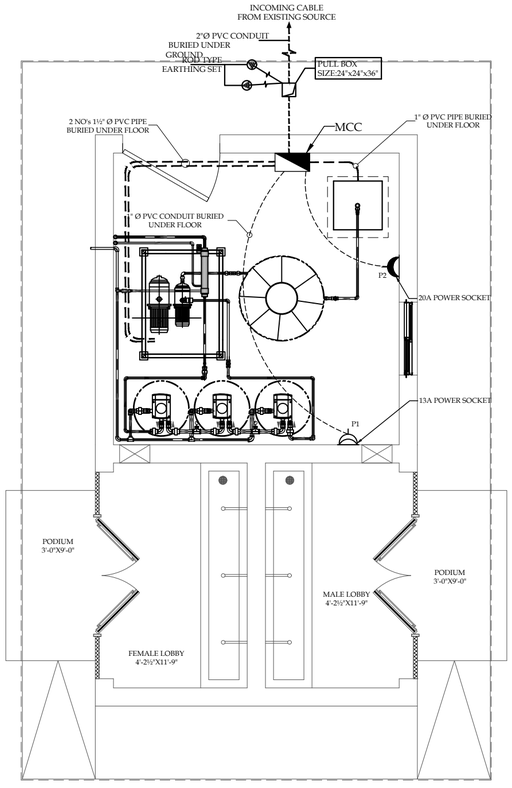

POWER LAYOUT PLAN

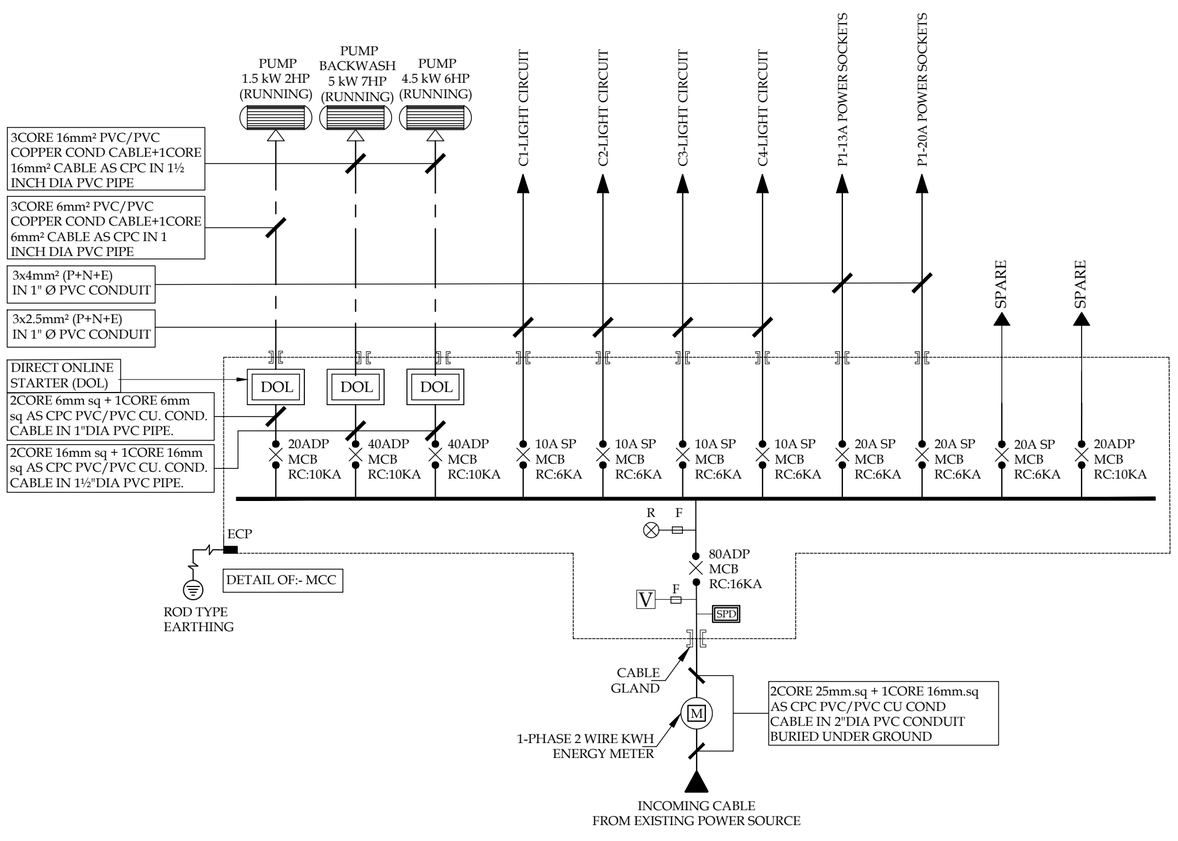

TITLE.

ELECTRICAL LIGHTING & POWER LAYOUT PLAN (TYPE-II)

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	

ISSUE N°	DATE	D E S C R I P T I O N	DRAWN	DESIGNED	APPROVED
01	10-12-2025	DETAILED DESIGN	ASAD	ENGR. FAEIZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING N°: PRMSC-WS-SP-E-01 | SHEET | REV 00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:
ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

E-01

LEGEND AND ABBREVIATIONS

ABRV.	DESCRIPTION
CW	COLD WATER SUPPLY
HW	HOT WATER SUPPLY
HWR	HOT WATER RETURN
WP	WASTE WATER LINE
SP	SOIL WATER LINE
V	VENT PIPE
RWP	RAIN WATER PIPE
AIR	AIR VENT
DCW	DOMESTIC COLD WATER
DHW	DOMESTIC HOT WATER

HDR	HEADER PIPE
PPR	POLYPROPYLENE RANDOM PIPE
CPVC	CHLORINATED POLYVINYL CHLORIDE PIPE
UPVC	UNPLASTICIZED PVC PIPE
CI	CAST IRON PIPE
HDPE	HIGH-DENSITY POLYETHYLENE PIPE
GI	GALVANIZED IRON PIPE
PVC	POLYVINYL CHLORIDE PIPE
SS	STAINLESS STEEL PIPE
CU	COPPER PIPE
ROD	ROD-OUT POINT
TS	TEST STATION
BP	BOOSTER PUMP

PIPE SLOPES

300mm	Ø12"	1 IN 330
225mm	Ø9"	1 IN 225
160mm	Ø6"	1 IN 180
110mm	Ø4"	1 IN 100
75mm	Ø3"	1 IN 75
50mm	Ø2"	1 IN 50

GENERAL NOTES

- ALL PLUMBING WORKS SHALL BE EXECUTED STRICTLY IN ACCORDANCE WITH THE LATEST APPLICABLE CODES (E.G., IPC, UPC, ASME, ASTM, AND LOCAL AUTHORITY REQUIREMENTS).
- THE CONTRACTOR SHALL VERIFY ALL DIMENSIONS, LEVELS, SITE CONDITIONS, AND UTILITY CONNECTION POINTS BEFORE COMMENCING ANY WORK.
- DO NOT SCALE DRAWINGS. ANY DISCREPANCIES BETWEEN DRAWINGS, SITE, AND SPECIFICATIONS MUST BE BROUGHT TO THE ATTENTION OF THE ENGINEER BEFORE EXECUTION.
- COORDINATE ALL WORK WITH ARCHITECTURAL, STRUCTURAL, HVAC, ELECTRICAL, AND FIRE PROTECTION DRAWINGS BEFORE INSTALLATION.
- ALL PENETRATIONS THROUGH SLABS, WALLS, AND BEAMS SHALL BE COORDINATED WITH THE STRUCTURAL ENGINEER. USE SLEEVES WITH ANNULAR SPACE FILLED WITH APPROVED FIRE-STOPPING MATERIAL FOR FIRE-RATED ASSEMBLIES.
- ALL PIPES PASSING THROUGH WET AREAS OR UNDERGROUND SHALL BE WRAPPED OR SLEEVED WITH PROTECTIVE SLEEVES TO PREVENT CORROSION AND LEAKAGE.
- PROVIDE PIPE SUPPORTS, BRACKETS, HANGERS, AND ANCHORS AS PER MANUFACTURER'S RECOMMENDATIONS AND APPLICABLE CODES (E.G., MSS SP-58). ENSURE THERMAL EXPANSION AND CONTRACTION ALLOWANCES.
- ALL DRAINAGE AND VENT PIPING SHALL BE INSTALLED WITH REQUIRED SLOPES TO ENSURE SELF-CLEANING VELOCITY AND AVOID ACCUMULATION.
- AIR ADMITTANCE VALVES ARE NOT PERMITTED UNLESS APPROVED IN WRITING BY THE AUTHORITY HAVING JURISDICTION.
- ALL WATER SUPPLY PIPING MUST BE PRESSURE TESTED WITH POTABLE WATER TO 150% OF OPERATING PRESSURE OR MINIMUM 10 BAR (WHICHEVER IS HIGHER) FOR AT LEAST 2 HOURS WITH NO PRESSURE DROP.
- SANITARY DRAINAGE AND VENT PIPING MUST BE TESTED WITH A 10-FOOT HEAD OF WATER OR 5 PSI OF AIR PRESSURE FOR A MINIMUM OF 15 MINUTES WITHOUT LOSS.
- HOT WATER RECIRCULATION PIPING, IF REQUIRED, SHALL BE INSTALLED TO MINIMIZE WAITING TIME AT REMOTE FIXTURES. INSTALL BALANCING VALVES AND THERMAL TRAPS AS NEEDED.
- PROVIDE NON-RETURN VALVES, PRESSURE-REDUCING VALVES, STRAINERS, AND ISOLATION VALVES AT ALL STRATEGIC LOCATIONS.
- ALL PLUMBING FIXTURES AND FITTINGS MUST BE WATER-CONSERVING TYPE AND SHALL MEET RELEVANT LEED/GREEN BUILDING OR LOCAL SUSTAINABILITY REQUIREMENTS, WHERE APPLICABLE.
- WATER HEATERS (ELECTRIC, GAS, OR SOLAR) MUST BE INSTALLED WITH SAFETY VALVES, DRAIN PANS, AND THERMAL INSULATION. COORDINATE VENTING WITH MECHANICAL DRAWINGS.
- PROVIDE TRAP PRIMERS FOR FLOOR DRAINS IN DRY AREAS TO PREVENT TRAP SEAL EVAPORATION.
- ENSURE ANTI-SIPHON VACUUM BREAKERS AND BACKFLOW PREVENTERS ARE INSTALLED WHERE REQUIRED TO PROTECT POTABLE WATER SUPPLY.
- ALL PLUMBING ACCESSORIES (E.G., FAUCETS, VALVES, HOSES, DRAINS) SHALL BE OF HEAVY-DUTY COMMERCIAL GRADE AND APPROVED BY THE CONSULTANT.
- PROVIDE SEDIMENT TRAPS AT CONNECTIONS TO GAS APPLIANCES (IF APPLICABLE).
- WHERE PLUMBING SYSTEMS ARE INSTALLED IN CEILING SPACES, PROVIDE ADEQUATE ACCESS PANELS FOR MAINTENANCE OF CONCEALED FITTINGS AND VALVES.
- INSULATE ALL DOMESTIC HOT WATER AND CHILLED WATER PIPING AS PER PROJECT SPECIFICATIONS AND ENERGY CODE REQUIREMENTS.
- UNDERGROUND PIPING MUST BE LAID ON COMPACTED SAND BEDDING AND COVERED WITH FINE SAND BEFORE BACKFILLING WITH SELECTED MATERIAL.
- IDENTIFY ALL EXPOSED PIPING AND VALVES WITH COLOR-CODED LABELS, PIPE MARKERS, AND TAGS AS PER PIPING IDENTIFICATION SCHEDULE.
- COORDINATE FINAL FIXTURE LOCATIONS WITH ARCHITECTURAL INTERIOR DRAWINGS AND SITE MOCKUPS PRIOR TO INSTALLATION.
- CONTRACTOR IS RESPONSIBLE FOR ALL TRENCHING, EXCAVATION, CORE DRILLING, BACKFILLING, AND MAKING GOOD ALL DISTURBED SURFACES.
- PROVIDE ALL NECESSARY CLEANOUTS, VENT TERMINALS, AND INSPECTION CHAMBERS AS SHOWN ON DRAWINGS OR AS REQUIRED BY CODE.
- STORMWATER PIPING SHALL BE SEPARATE FROM SANITARY DRAINAGE AND DESIGNED FOR 100-YEAR RETURN PERIOD UNLESS OTHERWISE NOTED.
- CONTRACTOR SHALL PREPARE AND SUBMIT COMPLETE AS-BUILT DRAWINGS SHOWING EXACT LOCATIONS, PIPE SIZES, AND VALVE TYPES UPON PROJECT COMPLETION.
- PERFORM FULL FLUSHING, CLEANING, DISINFECTION, AND COMMISSIONING OF ALL SYSTEMS BEFORE HANDING OVER TO THE CLIENT.
- SUBMIT OPERATION & MAINTENANCE MANUALS, WARRANTIES, AND TRAINING SCHEDULES TO FACILITY MANAGEMENT TEAM AT PROJECT CLOSEOUT.
- THE CONTRACTOR SHALL ARRANGE FOR ALL REQUIRED INSPECTIONS AND APPROVALS FROM RELEVANT AUTHORITIES DURING AND AFTER CONSTRUCTION.
- ALL WORKMANSHIP SHALL BE NEAT, CLEAN, AND PROFESSIONAL. ANY POORLY EXECUTED WORK SHALL BE REMOVED AND REINSTALLED AT CONTRACTOR'S EXPENSE.

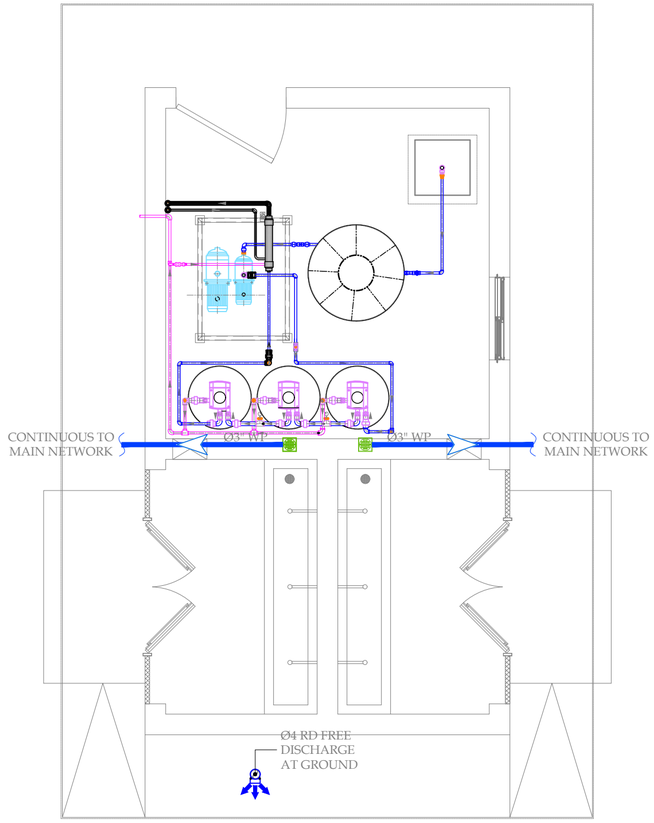

1 GROUND FLOOR LAYOUT
Scale: 3/8" = 1' - 0"

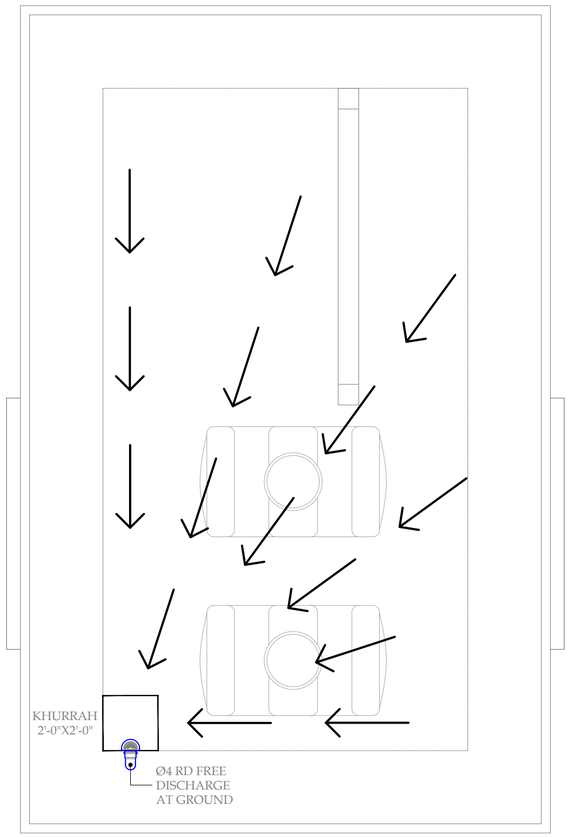

1 ROOF LAYOUT
Scale: 3/8" = 1' - 0"

TITLE.
STAND POST
DRAINAGE SYSTEM LAYOUT

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	10-12-2025	DETAILED DESIGN	ASAD	ENGR FARIZ	ENGR HSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº: PRMSC-WS-SP-P-01
SHEET
REV 00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:
ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

P-01

LEGEND AND ABBREVIATIONS

ABRV.	DESCRIPTION
CW	COLD WATER SUPPLY
HW	HOT WATER SUPPLY
HWR	HOT WATER RETURN
WP	WASTE WATER LINE
SP	SOIL WATER LINE
V	VENT PIPE
RWP	RAIN WATER PIPE
AIR	AIR VENT
DCW	DOMESTIC COLD WATER
DHW	DOMESTIC HOT WATER

HDR	HEADER PIPE
PPR	POLYPROPYLENE RANDOM PIPE
CPVC	CHLORINATED POLYVINYL CHLORIDE PIPE
UPVC	UNPLASTICIZED PVC PIPE
CI	CAST IRON PIPE
HDPE	HIGH-DENSITY POLYETHYLENE PIPE
GI	GALVANIZED IRON PIPE
PVC	POLYVINYL CHLORIDE PIPE
SS	STAINLESS STEEL PIPE
CU	COPPER PIPE
ROD	ROD-OUT POINT
TS	TEST STATION
BP	BOOSTER PUMP

PIPE SLOPES

300mm	Ø12"	1 IN 330
225mm	Ø9"	1 IN 225
160mm	Ø6"	1 IN 180
110mm	Ø4"	1 IN 100
75mm	Ø3"	1 IN 75
50mm	Ø2"	1 IN 50

GENERAL NOTES

- ALL PLUMBING WORKS SHALL BE EXECUTED STRICTLY IN ACCORDANCE WITH THE LATEST APPLICABLE CODES (E.G., IPC, UPC, ASME, ASTM, AND LOCAL AUTHORITY REQUIREMENTS).
- THE CONTRACTOR SHALL VERIFY ALL DIMENSIONS, LEVELS, SITE CONDITIONS, AND UTILITY CONNECTION POINTS BEFORE COMMENCING ANY WORK.
- DO NOT SCALE DRAWINGS. ANY DISCREPANCIES BETWEEN DRAWINGS, SITE, AND SPECIFICATIONS MUST BE BROUGHT TO THE ATTENTION OF THE ENGINEER BEFORE EXECUTION.
- COORDINATE ALL WORK WITH ARCHITECTURAL, STRUCTURAL, HVAC, ELECTRICAL, AND FIRE PROTECTION DRAWINGS BEFORE INSTALLATION.
- ALL PENETRATIONS THROUGH SLABS, WALLS, AND BEAMS SHALL BE COORDINATED WITH THE STRUCTURAL ENGINEER. USE SLEEVES WITH ANNULAR SPACE FILLED WITH APPROVED FIRE-STOPPING MATERIAL FOR FIRE-RATED ASSEMBLIES.
- ALL PIPES PASSING THROUGH WET AREAS OR UNDERGROUND SHALL BE WRAPPED OR SLEEVED WITH PROTECTIVE SLEEVES TO PREVENT CORROSION AND LEAKAGE.
- PROVIDE PIPE SUPPORTS, BRACKETS, HANGERS, AND ANCHORS AS PER MANUFACTURER'S RECOMMENDATIONS AND APPLICABLE CODES (E.G., MSS SP-58). ENSURE THERMAL EXPANSION AND CONTRACTION ALLOWANCES.
- ALL DRAINAGE AND VENT PIPING SHALL BE INSTALLED WITH REQUIRED SLOPES TO ENSURE SELF-CLEANING VELOCITY AND AVOID ACCUMULATION.
- AIR ADMITTANCE VALVES ARE NOT PERMITTED UNLESS APPROVED IN WRITING BY THE AUTHORITY HAVING JURISDICTION.
- ALL WATER SUPPLY PIPING MUST BE PRESSURE TESTED WITH POTABLE WATER TO 150% OF OPERATING PRESSURE OR MINIMUM 10 BAR (WHICHEVER IS HIGHER) FOR AT LEAST 2 HOURS WITH NO PRESSURE DROP.
- SANITARY DRAINAGE AND VENT PIPING MUST BE TESTED WITH A 10-FOOT HEAD OF WATER OR 5 PSI OF AIR PRESSURE FOR A MINIMUM OF 15 MINUTES WITHOUT LOSS.
- HOT WATER RECIRCULATION PIPING, IF REQUIRED, SHALL BE INSTALLED TO MINIMIZE WAITING TIME AT REMOTE FIXTURES. INSTALL BALANCING VALVES AND THERMAL TRAPS AS NEEDED.
- PROVIDE NON-RETURN VALVES, PRESSURE-REDUCING VALVES, STRAINERS, AND ISOLATION VALVES AT ALL STRATEGIC LOCATIONS.
- ALL PLUMBING FIXTURES AND FITTINGS MUST BE WATER-CONSERVING TYPE AND SHALL MEET RELEVANT LEED/GREEN BUILDING OR LOCAL SUSTAINABILITY REQUIREMENTS, WHERE APPLICABLE.
- WATER HEATERS (ELECTRIC, GAS, OR SOLAR) MUST BE INSTALLED WITH SAFETY VALVES, DRAIN PANS, AND THERMAL INSULATION. COORDINATE VENTING WITH MECHANICAL DRAWINGS.
- PROVIDE TRAP PRIMERS FOR FLOOR DRAINS IN DRY AREAS TO PREVENT TRAP SEAL EVAPORATION.
- ENSURE ANTI-SIPHON VACUUM BREAKERS AND BACKFLOW PREVENTERS ARE INSTALLED WHERE REQUIRED TO PROTECT POTABLE WATER SUPPLY.
- ALL PLUMBING ACCESSORIES (E.G., FAUCETS, VALVES, HOSES, DRAINS) SHALL BE OF HEAVY-DUTY COMMERCIAL GRADE AND APPROVED BY THE CONSULTANT.
- PROVIDE SEDIMENT TRAPS AT CONNECTIONS TO GAS APPLIANCES (IF APPLICABLE).
- WHERE PLUMBING SYSTEMS ARE INSTALLED IN CEILING SPACES, PROVIDE ADEQUATE ACCESS PANELS FOR MAINTENANCE OF CONCEALED FITTINGS AND VALVES.
- INSULATE ALL DOMESTIC HOT WATER AND CHILLED WATER PIPING AS PER PROJECT SPECIFICATIONS AND ENERGY CODE REQUIREMENTS.
- UNDERGROUND PIPING MUST BE LAID ON COMPACTED SAND BEDDING AND COVERED WITH FINE SAND BEFORE BACKFILLING WITH SELECTED MATERIAL.
- IDENTIFY ALL EXPOSED PIPING AND VALVES WITH COLOR-CODED LABELS, PIPE MARKERS, AND TAGS AS PER PIPING IDENTIFICATION SCHEDULE.
- COORDINATE FINAL FIXTURE LOCATIONS WITH ARCHITECTURAL INTERIOR DRAWINGS AND SITE MOCKUPS PRIOR TO INSTALLATION.
- CONTRACTOR IS RESPONSIBLE FOR ALL TRENCHING, EXCAVATION, CORE DRILLING, BACKFILLING, AND MAKING GOOD ALL DISTURBED SURFACES.
- PROVIDE ALL NECESSARY CLEANOUTS, VENT TERMINALS, AND INSPECTION CHAMBERS AS SHOWN ON DRAWINGS OR AS REQUIRED BY CODE.
- STORMWATER PIPING SHALL BE SEPARATE FROM SANITARY DRAINAGE AND DESIGNED FOR 100-YEAR RETURN PERIOD UNLESS OTHERWISE NOTED.
- CONTRACTOR SHALL PREPARE AND SUBMIT COMPLETE AS-BUILT DRAWINGS SHOWING EXACT LOCATIONS, PIPE SIZES, AND VALVE TYPES UPON PROJECT COMPLETION.
- PERFORM FULL FLUSHING, CLEANING, DISINFECTION, AND COMMISSIONING OF ALL SYSTEMS BEFORE HANDING OVER TO THE CLIENT.
- SUBMIT OPERATION & MAINTENANCE MANUALS, WARRANTIES, AND TRAINING SCHEDULES TO FACILITY MANAGEMENT TEAM AT PROJECT CLOSEOUT.
- THE CONTRACTOR SHALL ARRANGE FOR ALL REQUIRED INSPECTIONS AND APPROVALS FROM RELEVANT AUTHORITIES DURING AND AFTER CONSTRUCTION.
- ALL WORKMANSHIP SHALL BE NEAT, CLEAN, AND PROFESSIONAL. ANY POORLY EXECUTED WORK SHALL BE REMOVED AND REINSTALLED AT CONTRACTOR'S EXPENSE.

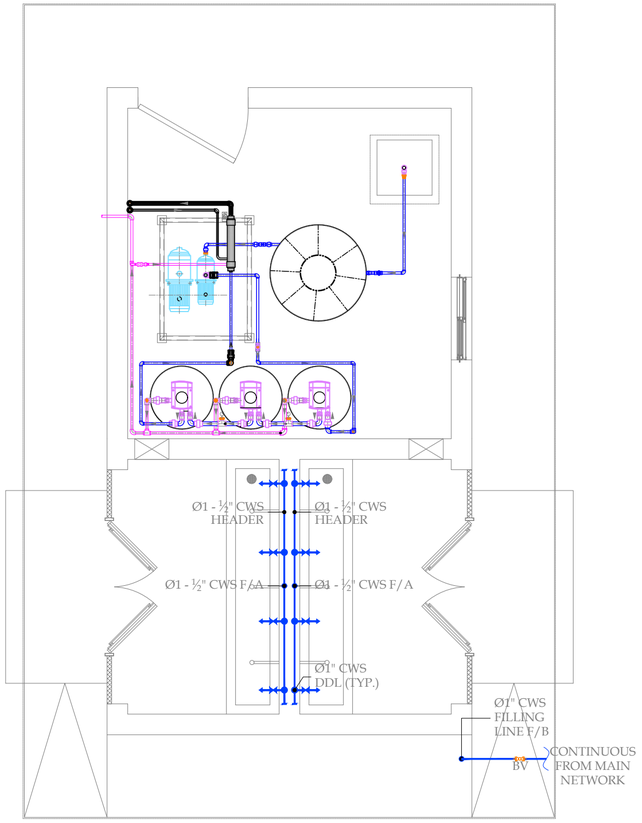

1 GROUND FLOOR LAYOUT
Scale: 3/8" = 1' - 0"

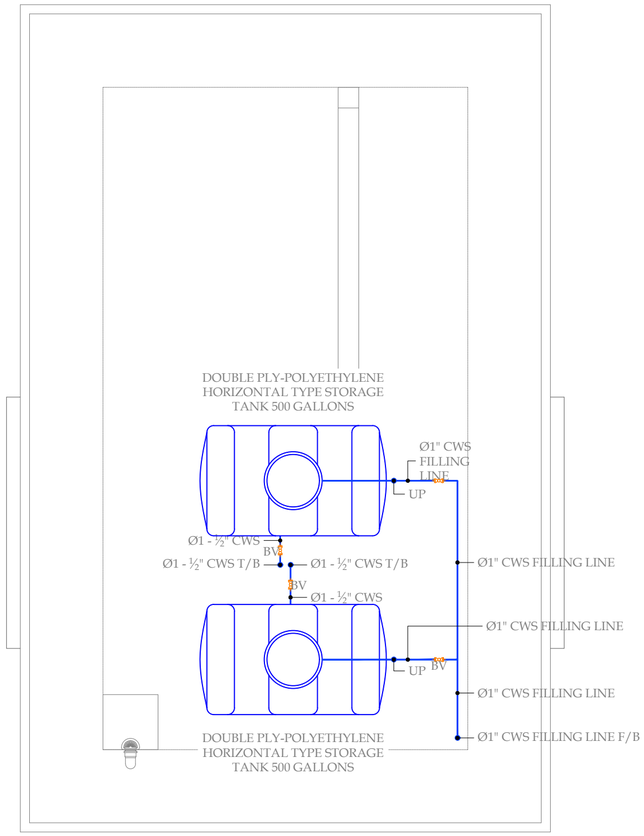

1 ROOF LAYOUT
Scale: 3/8" = 1' - 0"

TITLE.
STAND POST
WATER SUPPLY SYSTEM LAYOUT

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	10-12-2025	DETAILED DESIGN	ASAD	ENGR. FARIZ	ENGR. HSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING N°: PRMSC-WS-SP-P-02
SHEET
REV 00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:
ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

TUBE WELL

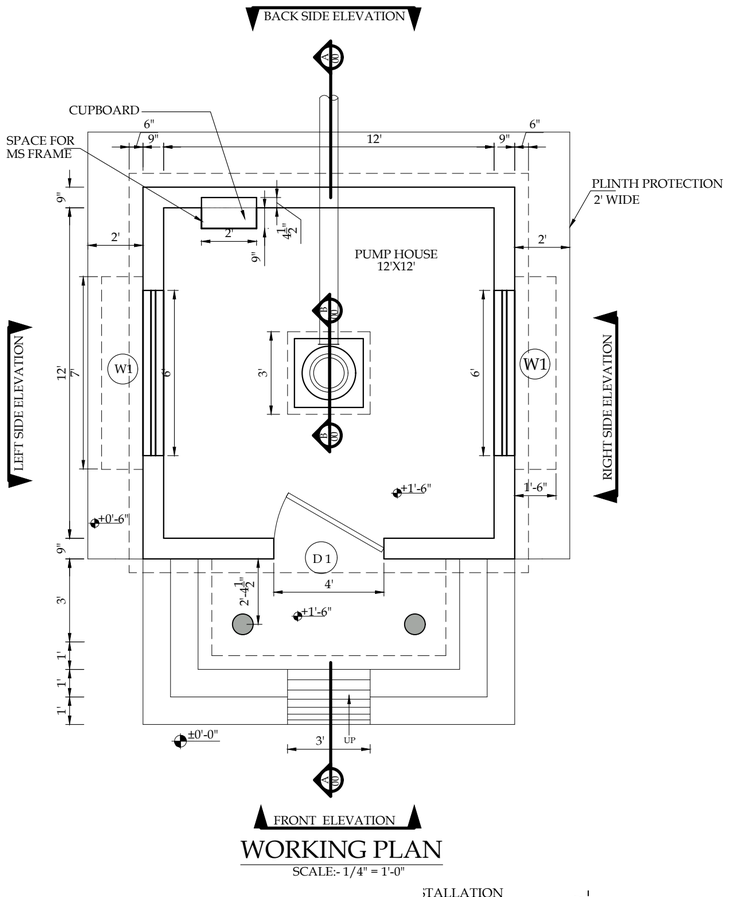

WORKING PLAN

SCALE:- 1/4" = 1'-0"

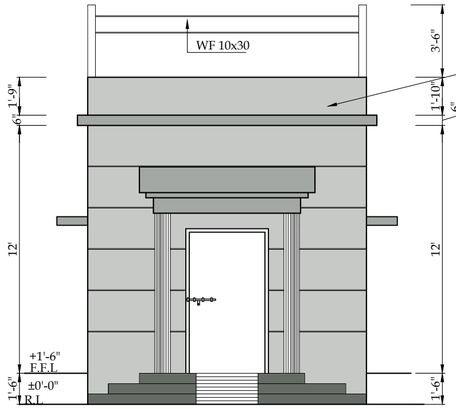

FRONT ELEVATION

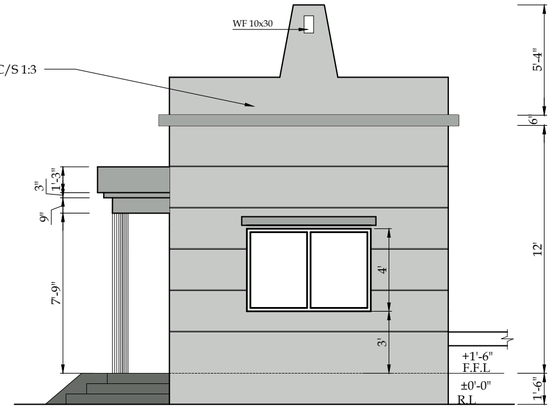

RIGHT SIDE ELEVATION

SCALE:- 3/16" = 1'-0"

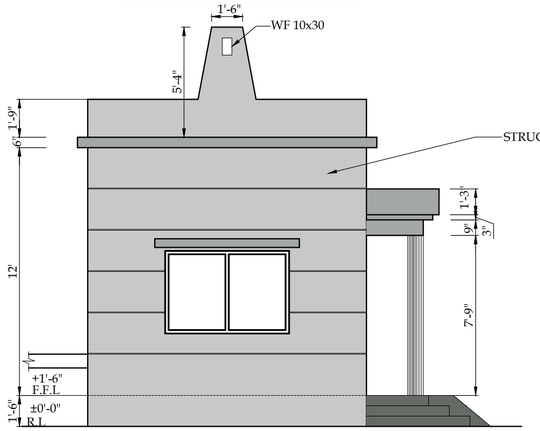

LEFT SIDE ELEVATION

SCALE:- 3/16" = 1'-0"

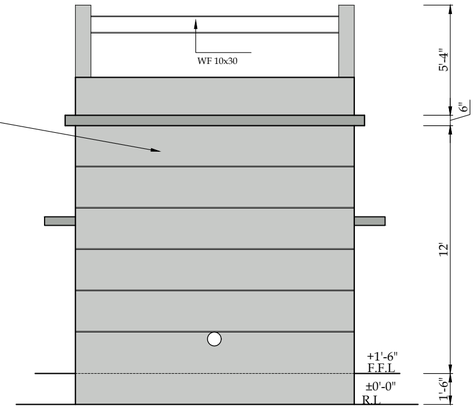

BACK SIDE ELEVATION

SCALE:- 3/16" = 1'-0"

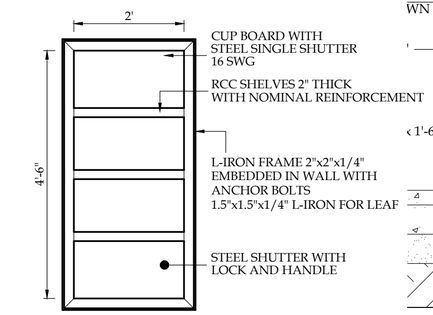

CUP BOARD DETAIL

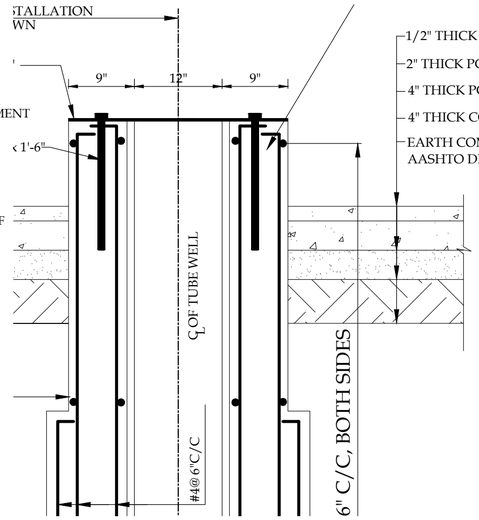

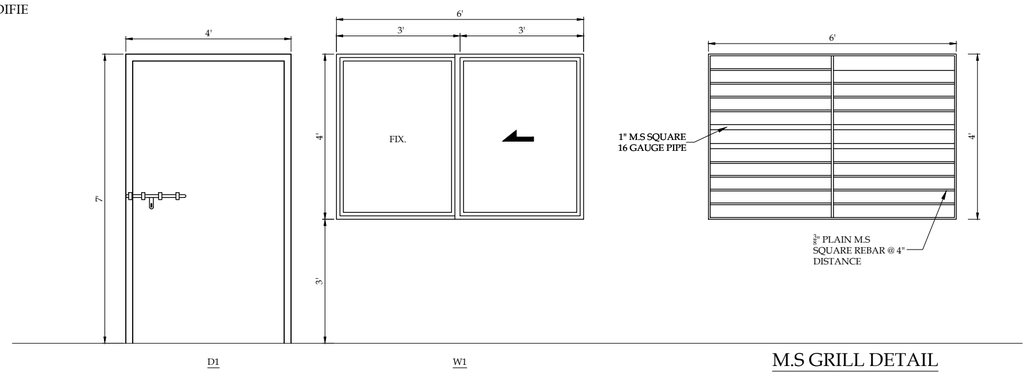

M.S GRILL DETAIL

DOOR & WINDOW SCHEDULE

Sr No.	TYPE	SIZE	SILL	QTY.	DESCRIPTION
1	D1	4'-0"x 7'-0"	0'-0"	01	16 GAUGE M.S. DOOR
2	W1	6'-0"x 4'-0"	3'-0"	01	M.S. WINDOW (16SWG) OF TUBULAR PIPE 1.5"X1.5" (40X40 mm) WITH 5mm GLASS PANNELS WITH M.S. GRILL
3	V1	2'-0"x 2'-0"	5'-0"	01	

NOTE

1. TUBE WELL DESIGN IS TENTATIVE. ACTUAL CONSTRUCTION/INSTALLATION SHALL CONFORM TO SITE SITUATION AND AS PER INSTRUCTIONS OF THE PROJECT MANAGER.
2. PLINTH OF CHAMBER TO BE DECIDED IN CONSULTATION WITH THE PROJECT MANAGER.

TITLE.

TUBE WELL
PLAN & SECTION

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	29-08-2025	DETAILED DESIGN	ASAD	ENGR. TANA	ENGR. HASAN UL HAQ
02					
03					
04					
05					
06					
07					

DRAWING N°: PRMSC-WS-TW-C-01 | SHEET | REV 00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

01

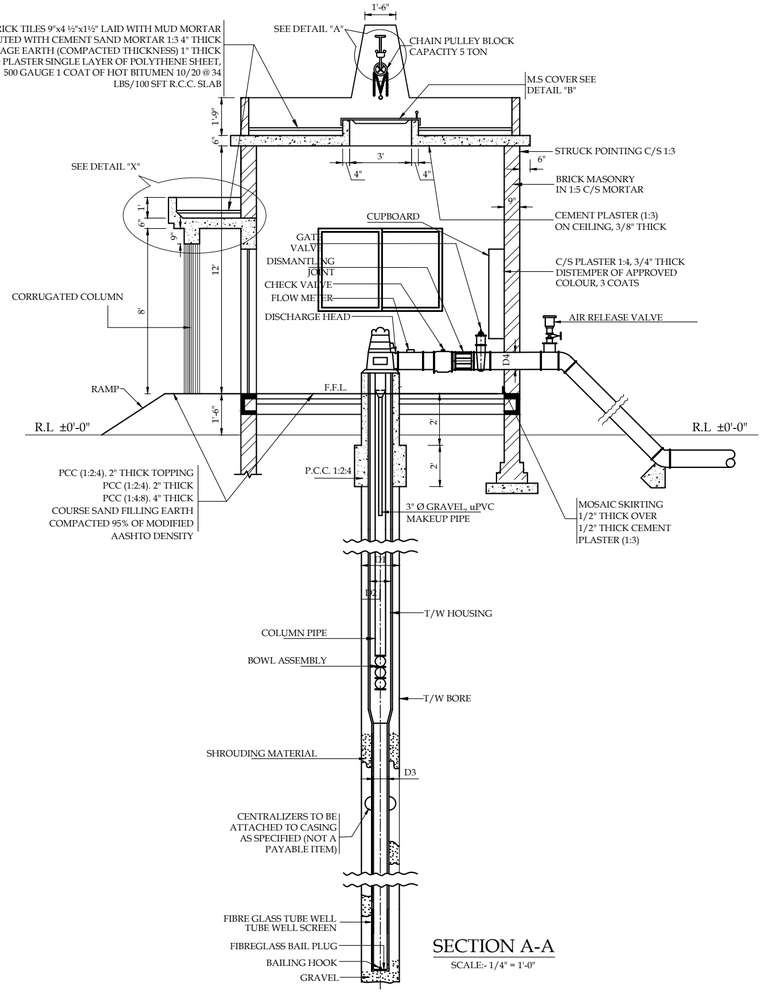

SECTION A-A

SCALE:- 1/4" = 1'-0"

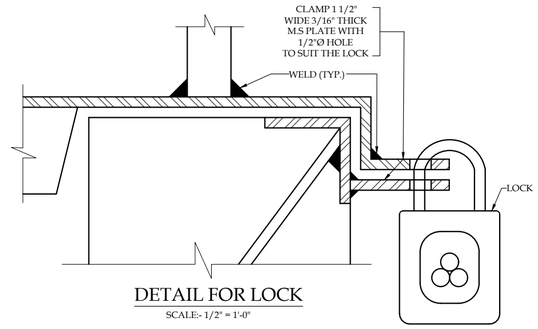

DETAIL FOR LOCK

SCALE:- 1/2" = 1'-0"

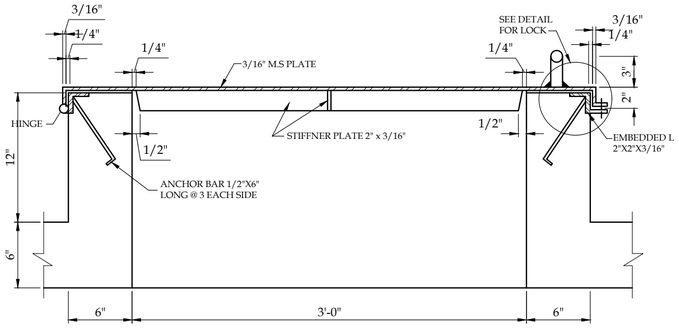

SECTION D-D

SCALE:- 1/2" = 1'-0"

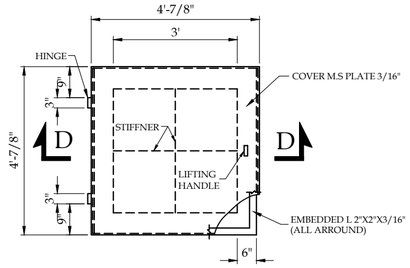

DETAIL "B"

SCALE:- 1/2" = 1'-0"

SCHEDULE OF TUBE WELL

DESCRIPTION	SIZE PUMP-1	SIZE PUMP-2
TUBEWELL CAPACITY	0.5 CUSEC	0.6 CUSEC
D1	18"	18"
D2	12"	12"
D3	8"	8"
D4	6"	6"
SETTING DEPTH	110'	60'
STRAINER LENGTH	60'	60'
BAIL PLUG	10'	10'
BORE DEPTH	350'±	200'±

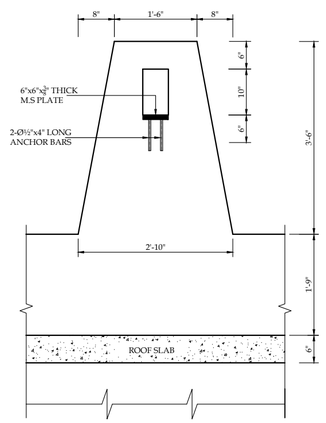

SIDE ELEVATION OF GIRDER LIFT WALL DETAIL-A

SCALE:- 3/4" = 1'-0"



REDUCER DETAIL

SCALE:- 3/4" = 1'-0"

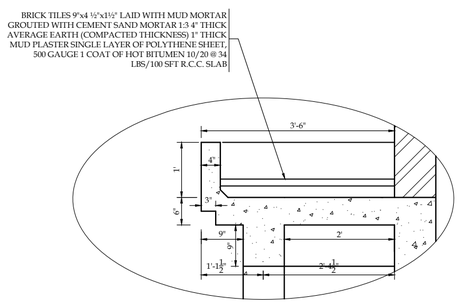

DETAIL "X"

SCALE:- 3/4" = 1'-0"

TITLE.

TUBE WELL
PLAN & SECTION

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	10-12-2025	DETAILED DESIGN	ASAD	ENGR. TANIA	ENGR. ISRAR-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING N°: PRMSC-WS-TW-C-02 | SHEET | REV 00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER CENTRAL

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:
ASIAN CONSULTING ENGINEERS www.asiancon.com

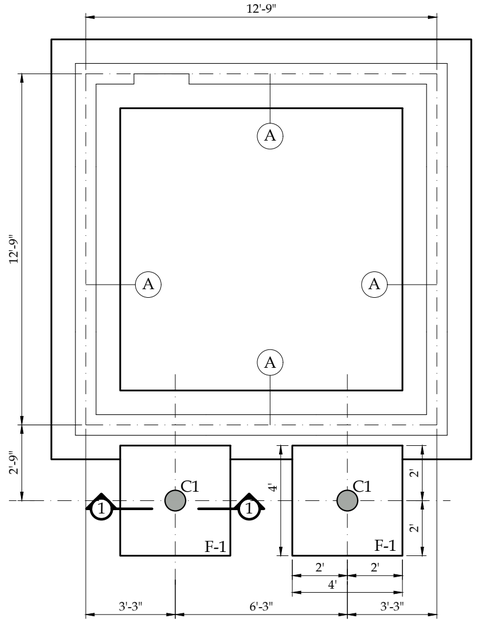

FOUNDATION LAYOUT PLAN

SCALE:- 1/4" = 1'-0"

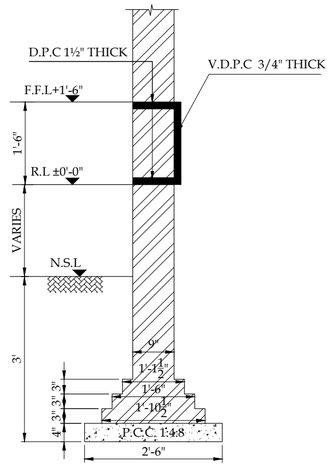

TYPE -A

SCALE:- 1/2" = 1'-0"

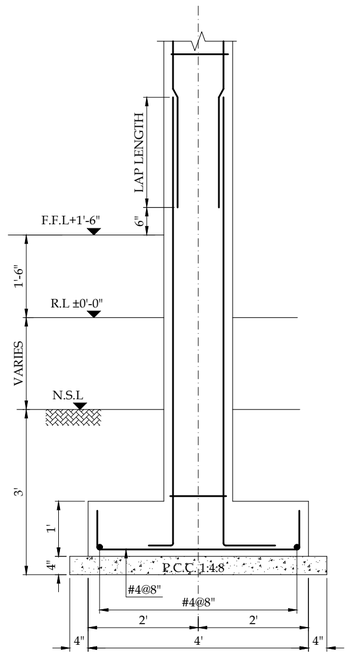

SECTION 1-1 FOR FOOTING F-1

SCALE:- 1/2" = 1'-0"



COLUMN C1

SCALE:- 1" = 8"

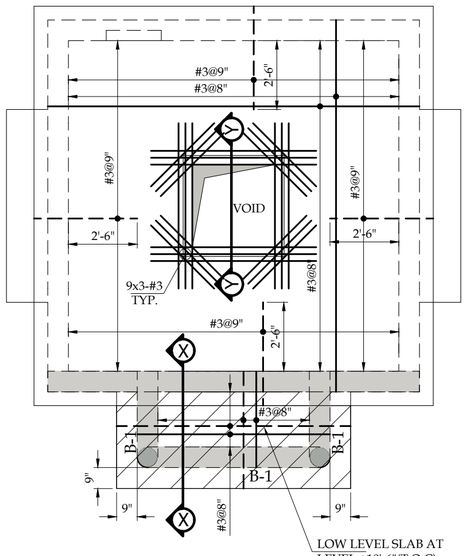

SLAB AT LEVEL (+)14'-6" (T.O.C)

SCALE:- 1/4" = 1'-0"

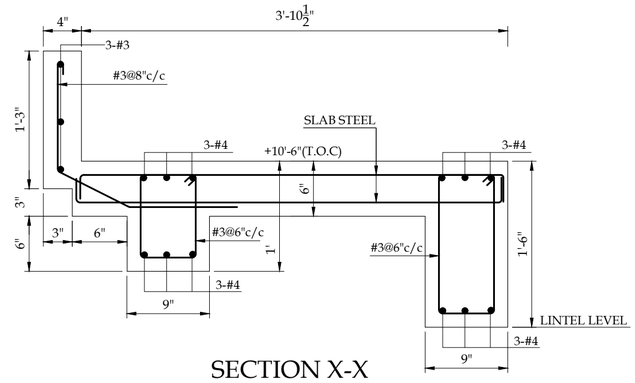

SECTION X-X

SCALE:- 1" = 1'-0"

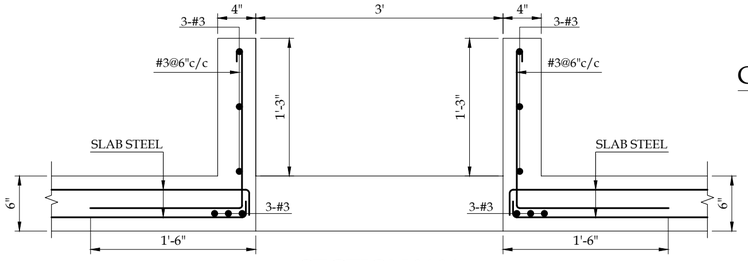

SECTION Y-Y

SCALE:- 1" = 1'-0"

NOTE:

1. THICKNESS OF ALL SLABS IS 6" UNLESS OTHERWISE NOTED.
2. DISTRIBUTION TOP BARS #3@12"c/c.

GENERAL NOTES:-

1. ALL STRUCTURAL CONCRETE SHALL CONFORM TO ACI (AMERICAN CONCRETE INSTITUTE) REQUIREMENTS.
2. MINIMUM COMPRESSIVE CYLINDER STRENGTH AT 28 DAYS SHALL BE 4000 Psi FOR ALL STRUCTURAL MEMBERS.
3. ALL REINFORCING STEEL SHALL BE DEFORMED BARS CONFORMING TO ASTM A615 HAVING MINIMUM YIELD OF STRENGTH OF 60,000 PSI
4. CONCRETE COVER

I. FOUNDATION BOTTOM = 2" TOP = 2" SIDES = 3"

II. BEAMS = 1-1/2"

II. COLUMN = 1-1/2"

5. BRICK MASNORY IN SUB STRUCTURE WILL BE 1:6 CEMENT SAND MORTAR AND SUPER STRUCTURE WILL BE 1:5.
6. HORIZONTAL D.P.C. WILL BE 1½" TH. P.C.C (1:2:4) WITH 1 COAT OF HOT BITUMEN 10/20@20 LBS/100SFT ON ONE LAYER OF POLYTHENE SHEET, 500 GAUGE.

TITLE.

TUBE WELL
STRUCTURAL DETAILS

ORIGINAL :		DATE :		SCALE :	
A2		JULY, 2025			
ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	10-12-2025	DETAILED DESIGN	ASAD	ENGR. TAHA	ENGR. IHSANULHAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:

PRMSC-WS-TW-S-01

SHEET

REV 00

PROJECT:

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER CENTRAL

CLIENT:

PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS www.asiancon.com.pk

S1

" LIGHTS "

NO.	SYMBOL	DESCRIPTION	TYPE / DETAIL / SPEC			
			COLOR TEMP.	LUMENS	CRI	P.F
1		CEILING MOUNTED LED DOWN LIGHT ROUND WITH 18 WATT.	5000-5500K	> 80lm/w	> 80	> .95
2		BULK HEAD LIGHT ROUND WITH 18 WATT.	5000-5500K	> 100lm/w	> 80	> .95

" F A N S "

NO.	SYMBOL	DESCRIPTION	SIZE	DETAIL
1		WALL MOUNTED LOUVRE BRACKET FAN	18" Ø	99.9% COPPER

"-SWITCH & LIGHT PLUG "

NO.	SYMBOL	DESCRIPTION	HEIGHT
1		10 AMP: 1 WAY FLUSH TYPE SWITCH (SWITCH BOARD).	4'-0" ABOVE F.F.L
2		10/13 AMP LIGHT PLUG.	1'-0" ABOVE F.F.L

" POWER & L.T SWITCH GEAR "

NO.	SYMBOL	DESCRIPTION	TYPE
1		13 AMP UNIVERSAL POWER SOCKET RECESS TYPE.	----------
2		DISTRIBUTION BOARD "LIGHT & POWER "	IP54 - INDOOR TYPE
3		EARTHING SET	ROD TYPE
4		MANHOLE	SIZE :-24"x24"x36"

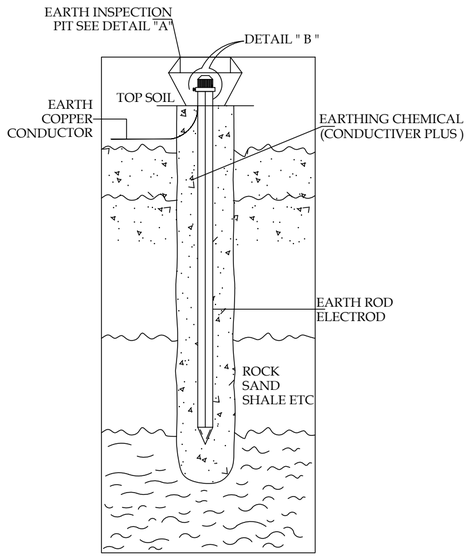

EARTH ROD INSTALLATION DETAIL



EARTH ELECTRODE COPPER ROD



DETAIL " B "

U BOND CONNECTION EARTHING

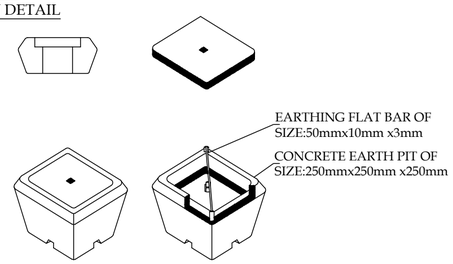

EARTH INSPECTION PIT DETAIL "A"

NOTES FOR EARTHING SYSTEM

1- EARTH BORE SHALL BE MADE AT 6'-0" AWAY FROM R.C.C FOUNDATION.

2- DISTANCE BETWEEN 2 EARTH BORES SHALL NOT BE LESS THEN 10'-0"

3- COPPER CONDUCTOR AT TOP SHALL BE BOLTED WITH THIMBLES, BRASS NUTS,BOLTS ETC/WELD POWDER.

4- JOINTS SHALL BE COVERED WITH HEAT SHRINKABLE TAPE.

5- CONTRACTOR TO MEASURE EARTHING RESISTANCE IN THE PRESENCE OF SITE ENGINEER. BOTH THE SITE ENGINEER AND CONTRACTOR SHALL SIGN THE EARTH TESTING RESULT AND SUBMIT IT TO THE CLIENT FOR RECORD WITH EQUIPMENT CALIBRATION CERTIFICATE.

6-THE EARTH RESISTANCE VALUE AFTER INSTALLATION SHALL BE LESS THAN THREE (3) OHM.

7-ALL MATERIAL OF THE ELECTRODE WILL BE OF COPPER.

8-THE EARLY STEAMER ROD WILL BE HANGED WITH PROPER HANGING ARRANGEMENT.

GENERAL NOTES:-

01 ELECTRICAL WORKS

ALL ELECTRICAL WORKS PERTAINING TO WIRING OF ELECTRICAL SYSTEMS SHALL STRICTLY CONFORM TO BS CODES (BS 7671) .

02 ELECTRICAL CONDUITING

ALL WIRING SHALL BE DONE IN PVC CONDUIT TO BE CONCEALED IN FALSE CEILING,WALLS, SLABS,COLUMNS AND FLOOR & RGS CONDUIT IS OPEN OR AS SHOWN ON DRAWINGS.

03 ELECTRICAL WIRING

THE WIRING SHOULD BE STARTED ONLY AFTER INSPECTION OF THE CONDUIT SYSTEM HAS BEEN COMPLETED AND ALL OUTLET BOXES ARE FIXED AT THEIR RESPECTIVE POSITIONS.

04 PVC CONDUITS

ALL PVC CONDUITS SHALL BE OF AS PER MENTIONED IN DRAWINGS & EVERY CONDUIT SHOULD BE 20% FREE SPACE (DEPENDING UPON NUMBER OF WIRES) FROM SWITCH BOARD TO LIGHT POINTS & 1" DIA FROM DBs TO SWITCH BOARDS AND POWER SOCKETS OR AS SHOWN ON DRAWINGS.

05 COLOUR CODING

COLOUR CODING FOR WIRING SHALL BE AS FOLLOWS: RED,YELLOW AND BLUE FOR PHASES,BLACK FOR NEUTRAL AND GREEN / YELLOW FOR CPC (EARTH).

06 EARTHING OF POINTS

ALL LIGHT POINTS AND POWER SOCKETS SHALL BE PROPERLY EARTHED WITH SAME SIZE PVC INSULATED WIRES OF COLOUR YELLOW/GREEN FOR PHASE & NEUTRAL.

07 CAPACITY OF CONDUITS

THE NUMBER OF WIRES TO BE PULLED IN ANY CONDUIT FOR WIRING PURPOSES SHALL CONFORM TO BS CODES (BS EN 61386-25:2011) & HAVE 30% CLEARANCE.

08 OTHER SYSTEMS

1" DIA PVC CONDUIT SHALL BE USED FOR WIRING OF ALL OTHER SYSTEMS UNLESS OTHERWISE MENTIONED ON PLANS OR AS SPECIFIED IN BOQ.

09 ELECTRICAL CONSULTANT

ELECTRICAL CONTRACTOR TO CONSULT ELECTRICAL CONSULTANT /ENGINEER FOR ANY FURTHER CLARIFICATIONS.NO ASSUMPTIONS SHOULD BE MADE.

10 FERRULING

FERRULING SHOULD BE DONE ON ALL CIRCUITS FOR LIGHT & POWER & FERRULING SAMPLE SHOULD BE APPROVED BY THE ENGINEER / CONSULTANT.

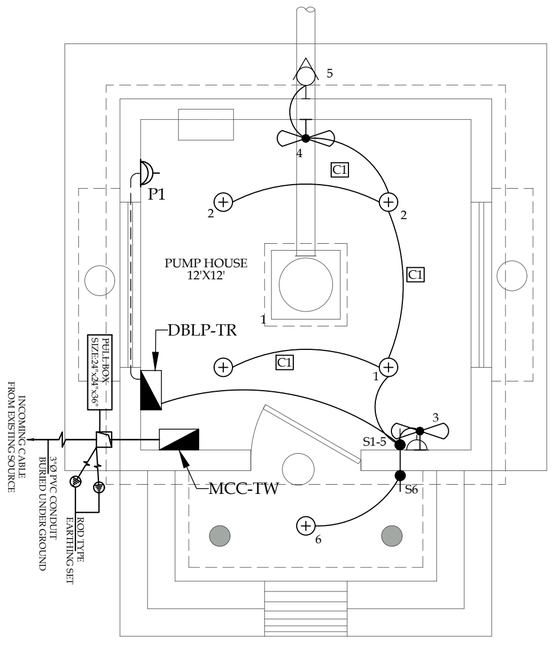

WORKING PLAN

SCALE:- 1/4" = 1'-0"

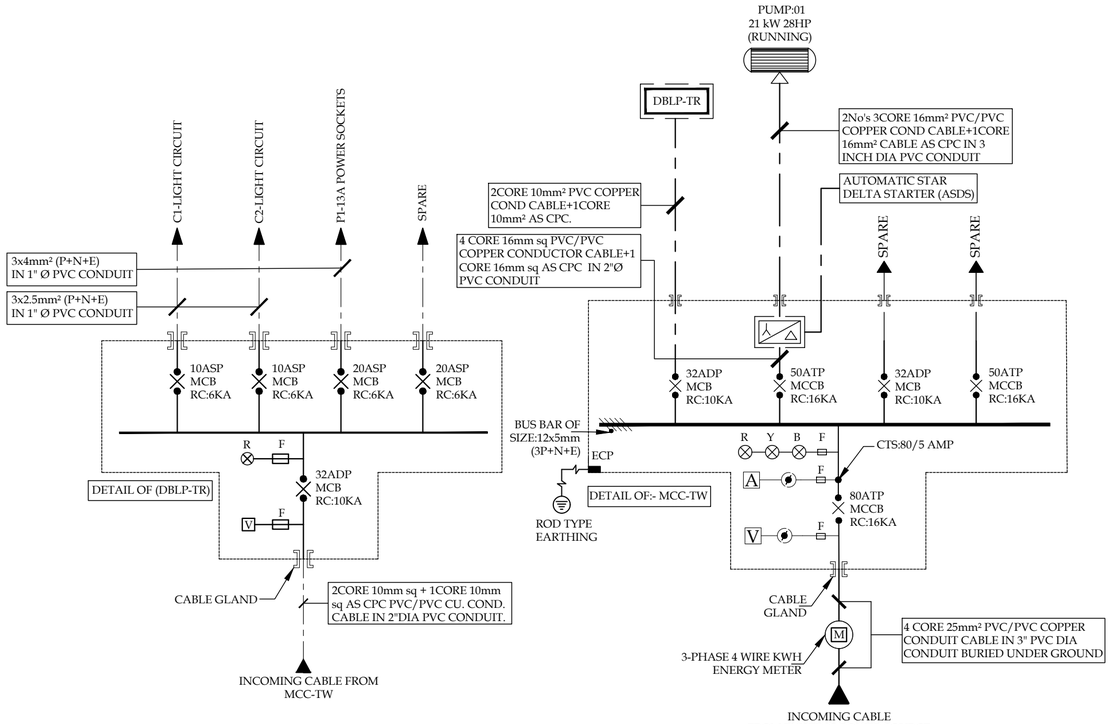

TITLE.

ELECTRICAL LAYOUT PLAN FOR 0.5 CUSEC

ORIGINAL :		DATE :		SCALE :	
	A2	JULY, 2025			

ISSUE N°	DATE	D E S C R I P T I O N	DRAWN	DESIGNED	APPROVED
01	10-12-2025	DETAILED DESIGN	SHERAZ AHMED	ENGR. FARHAN	ENGR MUNEEB
02					
03					
04					
05					
06					
07					

DRAWING N°: PRMSC-WS-TW-E-01 | SHEET | REV 00

PROJECT: ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER CENTRAL

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT: ASIAN CONSULTING ENGINEERS www.asiancon.com.pk

E-01

" LIGHTS "

NO.	SYMBOL	DESCRIPTION	TYPE / DETAIL / SPEC			
			COLOR TEMP.	LUMENS	CRI	P.F
1		CEILING MOUNTED LED DOWN LIGHT ROUND WITH 18 WATT.	5000-5500K	> 80lm/w	> 80	> .95
2		BULK HEAD LIGHT ROUND WITH 18 WATT.	5000-5500K	> 100lm/w	> 80	> .95

" F A N S "

NO.	SYMBOL	DESCRIPTION	SIZE	DETAIL
1		WALL MOUNTED LOUVRE BRACKET FAN	18" Ø	99.9% COPPER

"-SWITCH & LIGHT PLUG "

NO.	SYMBOL	DESCRIPTION	HEIGHT
1		10 AMP: 1 WAY FLUSH TYPE SWITCH (SWITCH BOARD).	4'-0" ABOVE F.F.L
2		10/13 AMP LIGHT PLUG.	1'-0" ABOVE F.F.L

" POWER & L.T SWITCH GEAR "

NO.	SYMBOL	DESCRIPTION	TYPE
1		13 AMP UNIVERSAL POWER SOCKET RECESS TYPE.	----------
2		DISTRIBUTION BOARD "LIGHT & POWER "	IP54 - INDOOR TYPE
3		EARTHING SET	ROD TYPE
4		MANHOLE	SIZE :-24"x24"x36"

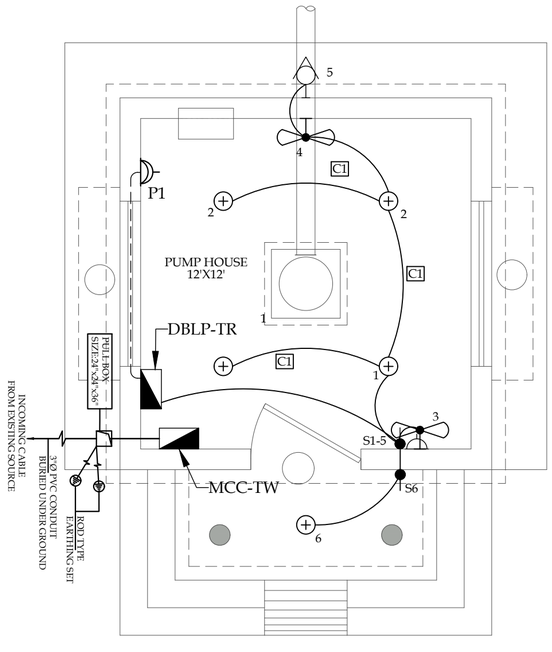

WORKING PLAN

SCALE:- 1/4" = 1'-0"

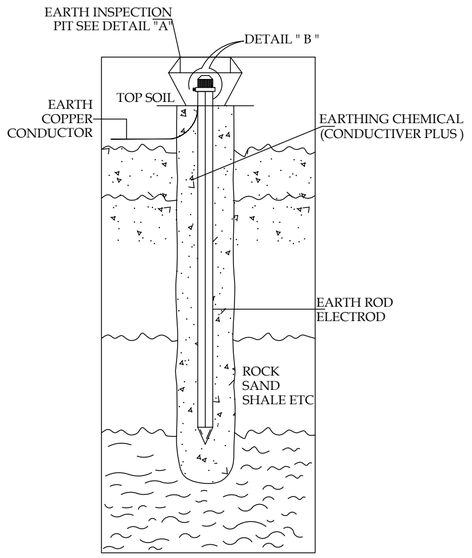

EARTH ROD INSTALLATION DETAIL



EARTH ELECTRODE COPPER ROD

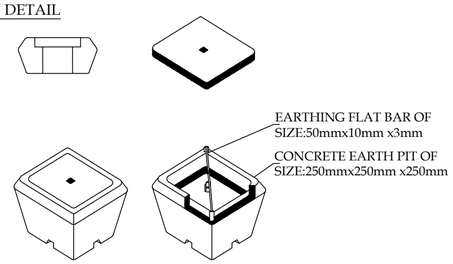

EARTH INSPECTION PIT DETAIL "A"



DETAIL " B "

U BOND CONNECTION EARTHING

NOTES FOR EARTHING SYSTEM

1- EARTH BORE SHALL BE MADE AT 6'-0" AWAY FROM R.C.C FOUNDATION.

2- DISTANCE BETWEEN 2 EARTH BORES SHALL NOT BE LESS THEN 10'-0"

3- COPPER CONDUCTOR AT TOP SHALL BE BOLTED WITH THIMBLES, BRASS NUTS,BOLTS ETC/WELD POWDER.

4- JOINTS SHALL BE COVERED WITH HEAT SHRINKABLE TAPE.

5- CONTRACTOR TO MEASURE EARTHING RESISTANCE IN THE PRESENCE OF SITE ENGINEER. BOTH THE SITE ENGINEER AND CONTRACTOR SHALL SIGN THE EARTH TESTING RESULT AND SUBMIT IT TO THE CLIENT FOR RECORD WITH EQUIPMENT CALIBRATION CERTIFICATE.

6-THE EARTH RESISTANCE VALUE AFTER INSTALLATION SHALL BE LESS THAN THREE (3) OHM.

7-ALL MATERIAL OF THE ELECTRODE WILL BE OF COPPER.

8-THE EARLY STEAMER ROD WILL BE HANGED WITH PROPER HANGING ARRANGEMENT.

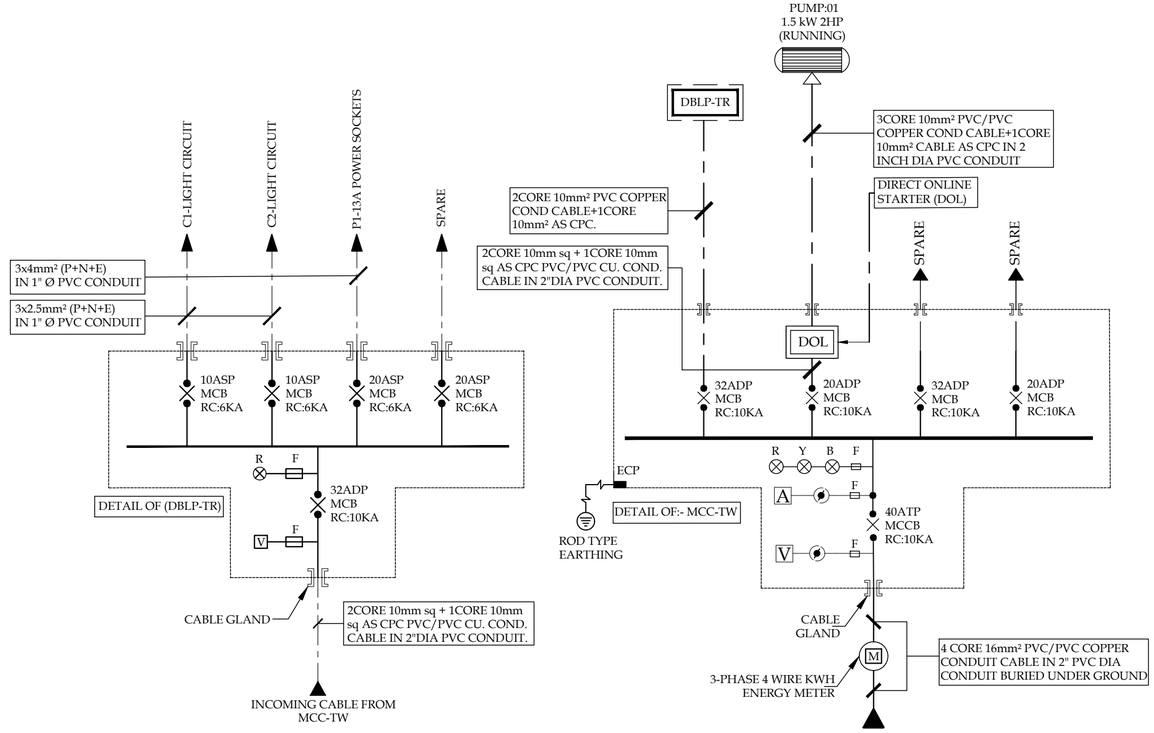

GENERAL NOTES:-

01 ELECTRICAL WORKS

ALL ELECTRICAL WORKS PERTAINING TO WIRING OF ELECTRICAL SYSTEMS SHALL STRICTLY CONFORM TO BS CODES (BS 7671) .

02 ELECTRICAL CONDUITING

ALL WIRING SHALL BE DONE IN PVC CONDUIT TO BE CONCEALED IN FALSE CEILING,WALLS, SLABS,COLUMNS AND FLOOR & RGS CONDUIT IS OPEN OR AS SHOWN ON DRAWINGS.

03 ELECTRICAL WIRING

THE WIRING SHOULD BE STARTED ONLY AFTER INSPECTION OF THE CONDUIT SYSTEM HAS BEEN COMPLETED AND ALL OUTLET BOXES ARE FIXED AT THEIR RESPECTIVE POSITIONS.

04 PVC CONDUITS

ALL PVC CONDUITS SHALL BE OF AS PER MENTIONED IN DRAWINGS & EVERY CONDUIT SHOULD BE 20% FREE SPACE (DEPENDING UPON NUMBER OF WIRES) FROM SWITCH BOARD TO LIGHT POINTS & 1" DIA FROM DBs TO SWITCH BOARDS AND POWER SOCKETS OR AS SHOWN ON DRAWINGS.

05 COLOUR CODING

COLOUR CODING FOR WIRING SHALL BE AS FOLLOWS: RED,YELLOW AND BLUE FOR PHASES,BLACK FOR NEUTRAL AND GREEN / YELLOW FOR CPC (EARTH).

06 EARTHING OF POINTS

ALL LIGHT POINTS AND POWER SOCKETS SHALL BE PROPERLY EARTHED WITH SAME SIZE PVC INSULATED WIRES OF COLOUR YELLOW/GREEN FOR PHASE & NEUTRAL.

07 CAPACITY OF CONDUITS

THE NUMBER OF WIRES TO BE PULLED IN ANY CONDUIT FOR WIRING PURPOSES SHALL CONFORM TO BS CODES (BS EN 61386-25:2011) & HAVE 30% CLEARANCE.

08 OTHER SYSTEMS

1" DIA PVC CONDUIT SHALL BE USED FOR WIRING OF ALL OTHER SYSTEMS UNLESS OTHERWISE MENTIONED ON PLANS OR AS SPECIFIED IN BOQ.

09 ELECTRICAL CONSULTANT

ELECTRICAL CONTRACTOR TO CONSULT ELECTRICAL CONSULTANT /ENGINEER FOR ANY FURTHER CLARIFICATIONS.NO ASSUMPTIONS SHOULD BE MADE.

10 FERRULING

FERRULING SHOULD BE DONE ON ALL CIRCUITS FOR LIGHT & POWER & FERRULING SAMPLE SHOULD BE APPROVED BY THE ENGINEER / CONSULTANT.

TITLE.

ELECTRICAL LAYOUT PLAN FOR 0.05 CUSEC

ORIGINAL :		DATE :		SCALE :	
A2		JULY, 2025			
ISSUE N°	DATE	D E S C R I P T I O N	DRAWN	DESIGNED	APPROVED
01	10-12-2025	DETAILED DESIGN	SHERAZ AHMED	ENGR. FARHAN	ENGR MUNEEB
02					
03					
04					
05					
06					
07					

DRAWING N°: PRMSC-WS-TW-E-02 | SHEET | REV 00

PROJECT: ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER CENTRAL

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS www.asiancon.com.pk

E-02

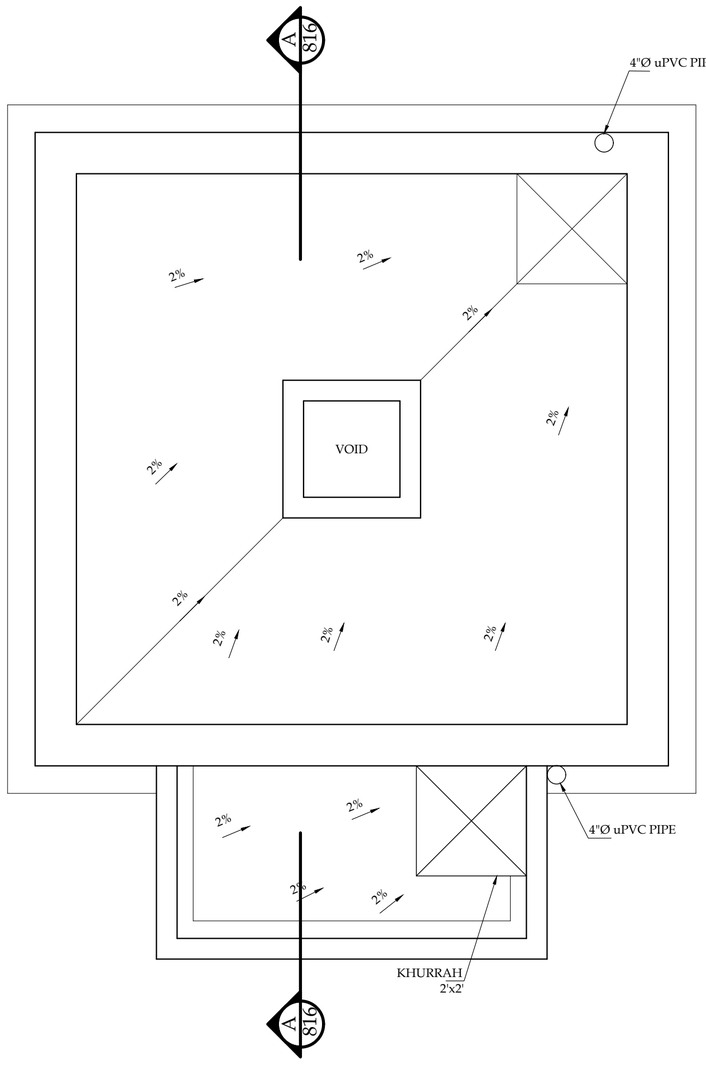

ROOF DRAINAGE PLAN

SCALE:- 1/2" = 1'-0"

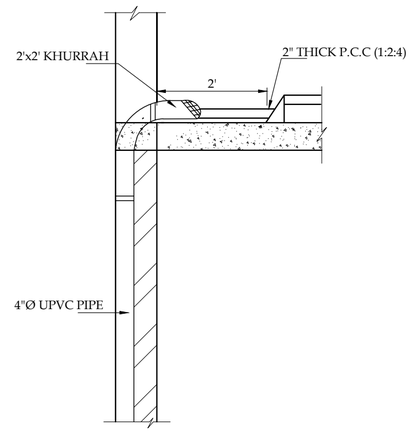

SECTION AA

SCALE:- 1/2" = 1'-0"

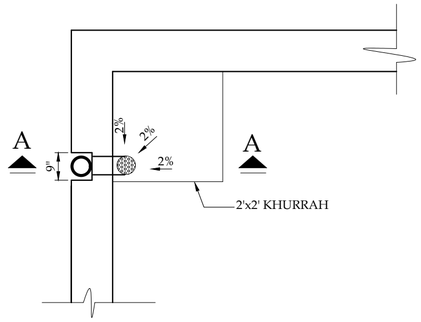

ROOF KHURRAH PLAN

SCALE:- 1/2" = 1'-0"

TITLE.

TUBE WELL
PLAN & SECTION

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	10-12-2025	DETAILED DESIGN	ASAD	ENGR. TAHA	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:

PRMSC-WS-TW-P-01

SHEET

REV
00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER CENTRAL

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

P1

BOUNDARY WALL

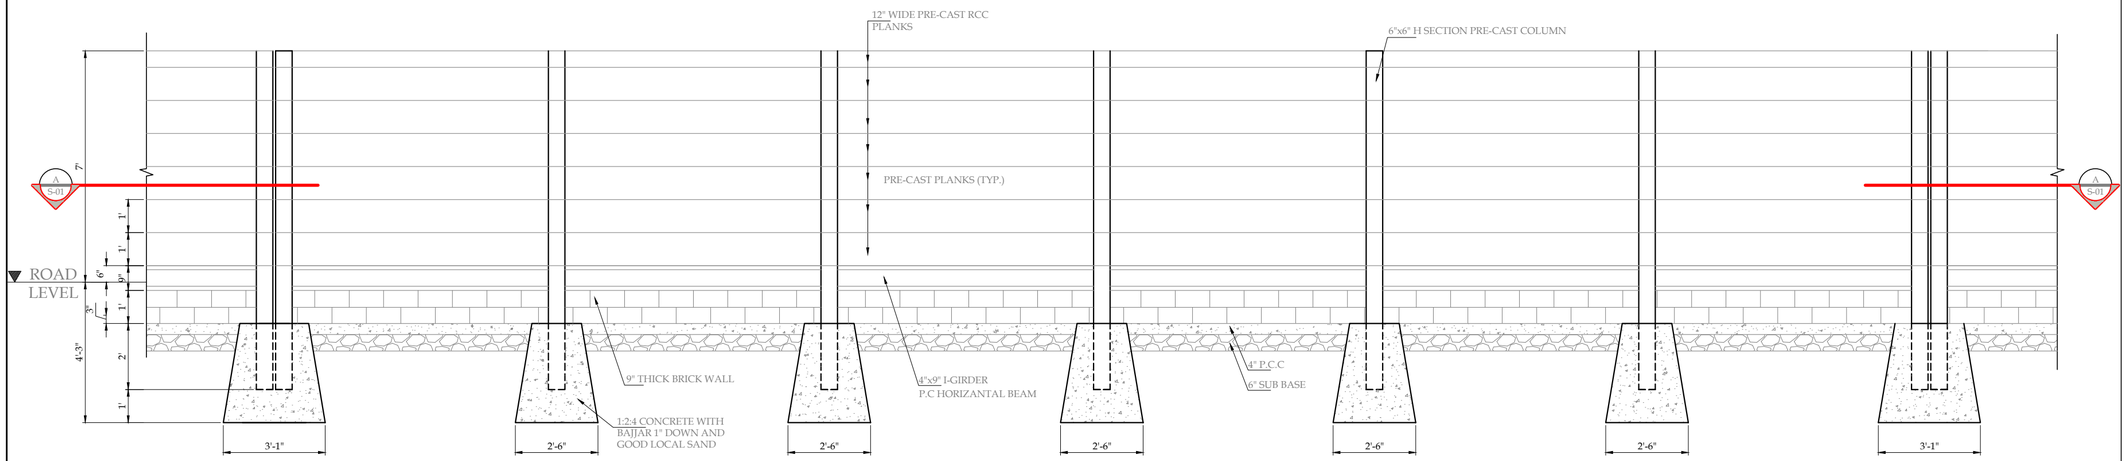

FRONT ELEVATION

SCALE:- 3/8" = 1'-0"

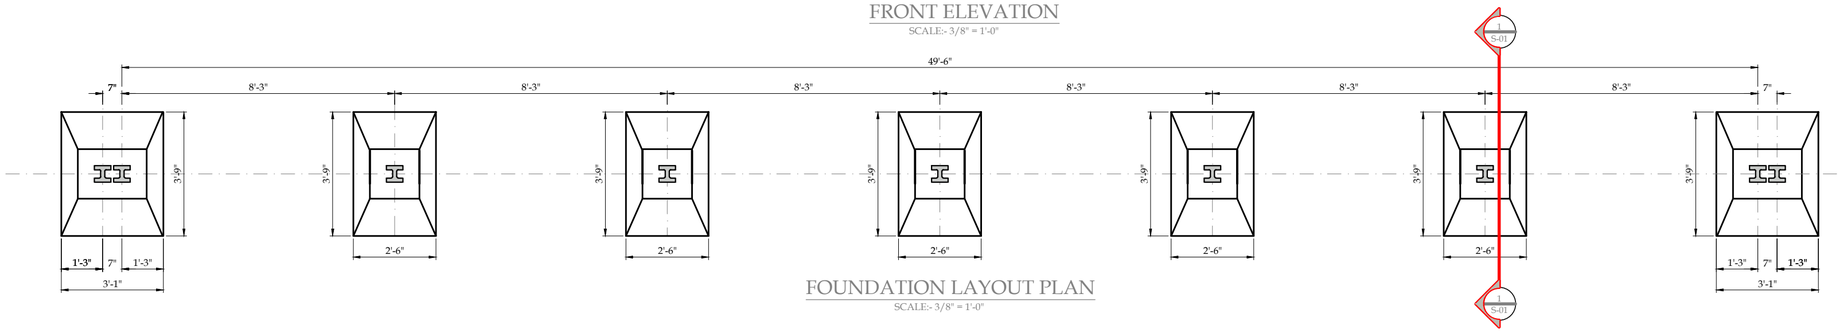

FOUNDATION LAYOUT PLAN

SCALE:- 3/8" = 1'-0"



SECTION A-A

SCALE:- 3/8" = 1'-0"

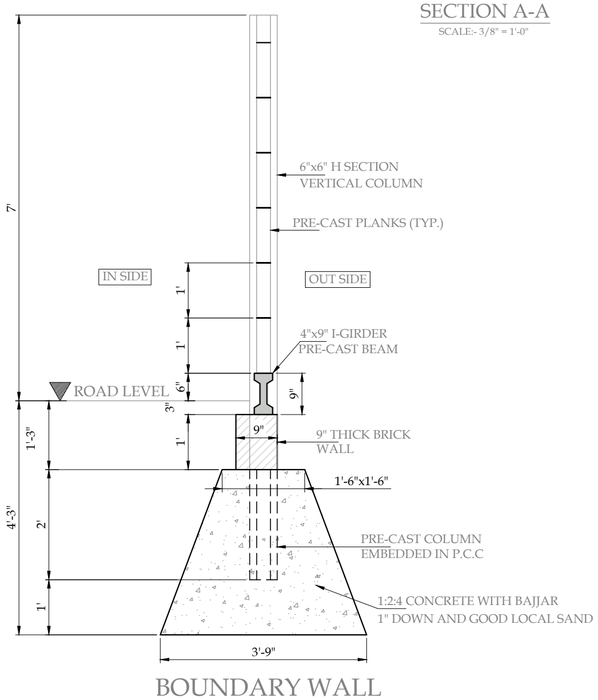

BOUNDARY WALL SECTION B-B

SCALE:- 1/2" = 1'-0"

TITLE.

BOUNDARY WALL STRUCTURAL DETAILS

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	----

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	31-12-2025	DETAILED DESIGN	ASAD	ENGR. FAEIZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING N°:

PRMSC-WS-BW-C-01

SHEET

REV

PROJECT:

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS www.asiancon.com JV

S-24

PRMSC
Punjab Rural Municipal Services Company

Punjab Rural Municipal Services Company (PRMSC)

“Engineering, Design &
Construction Supervision Consultant (Cluster South - III")
Detailed Design Drawings

BAHAWALNAGAR
[DRAIN SYSTEM]

AKKANWALI KHURD,SHER MOHD(MVS),KARTAR SINGH,KHOBER,DHARAM PURA,HIRA BASHNOAI (MVS) ALLAHABAD,AMIN ABAD,BARASAJWAR KHAN,CHAK ABDUL HAQ, DADOO MAMMUNKA,DARA SANATTEKA,DHANRAJ PURA,HASAN RAIKA,JAGGA SANATTEKA,JALWALA,JANOOWALA,KHAWAJA BUX BODLA,MAHNI BEGKA,MALAK PURA,MINA SANATTEKA,MUHAMMAD ASAD KHAN,MUHSAN PURA,NOOR JAHANIAN,PARAN WALA,RAMNAGAR,SANDAR BASHNOI,SHER SINGH WALA,TOBI QAMAR-UD-DIN,

MAY-2026

ENVIRONMENTAL TECHNOLOGIES

ASIAN CONSULTING ENGINEERS (PVT.) LTD
www.asiancon.com

Head Office:
C-3, Jhelum Block, Green Fort-II, Lahore.
Phone: +92 42 35450914-15
Fax: +92 42 35450916,
Email: arslan@asiancon.com

ACS REGISTRARS Quality Assurance ISO 9001 UKAS 229

Project Location Map (Bahawalnagar)

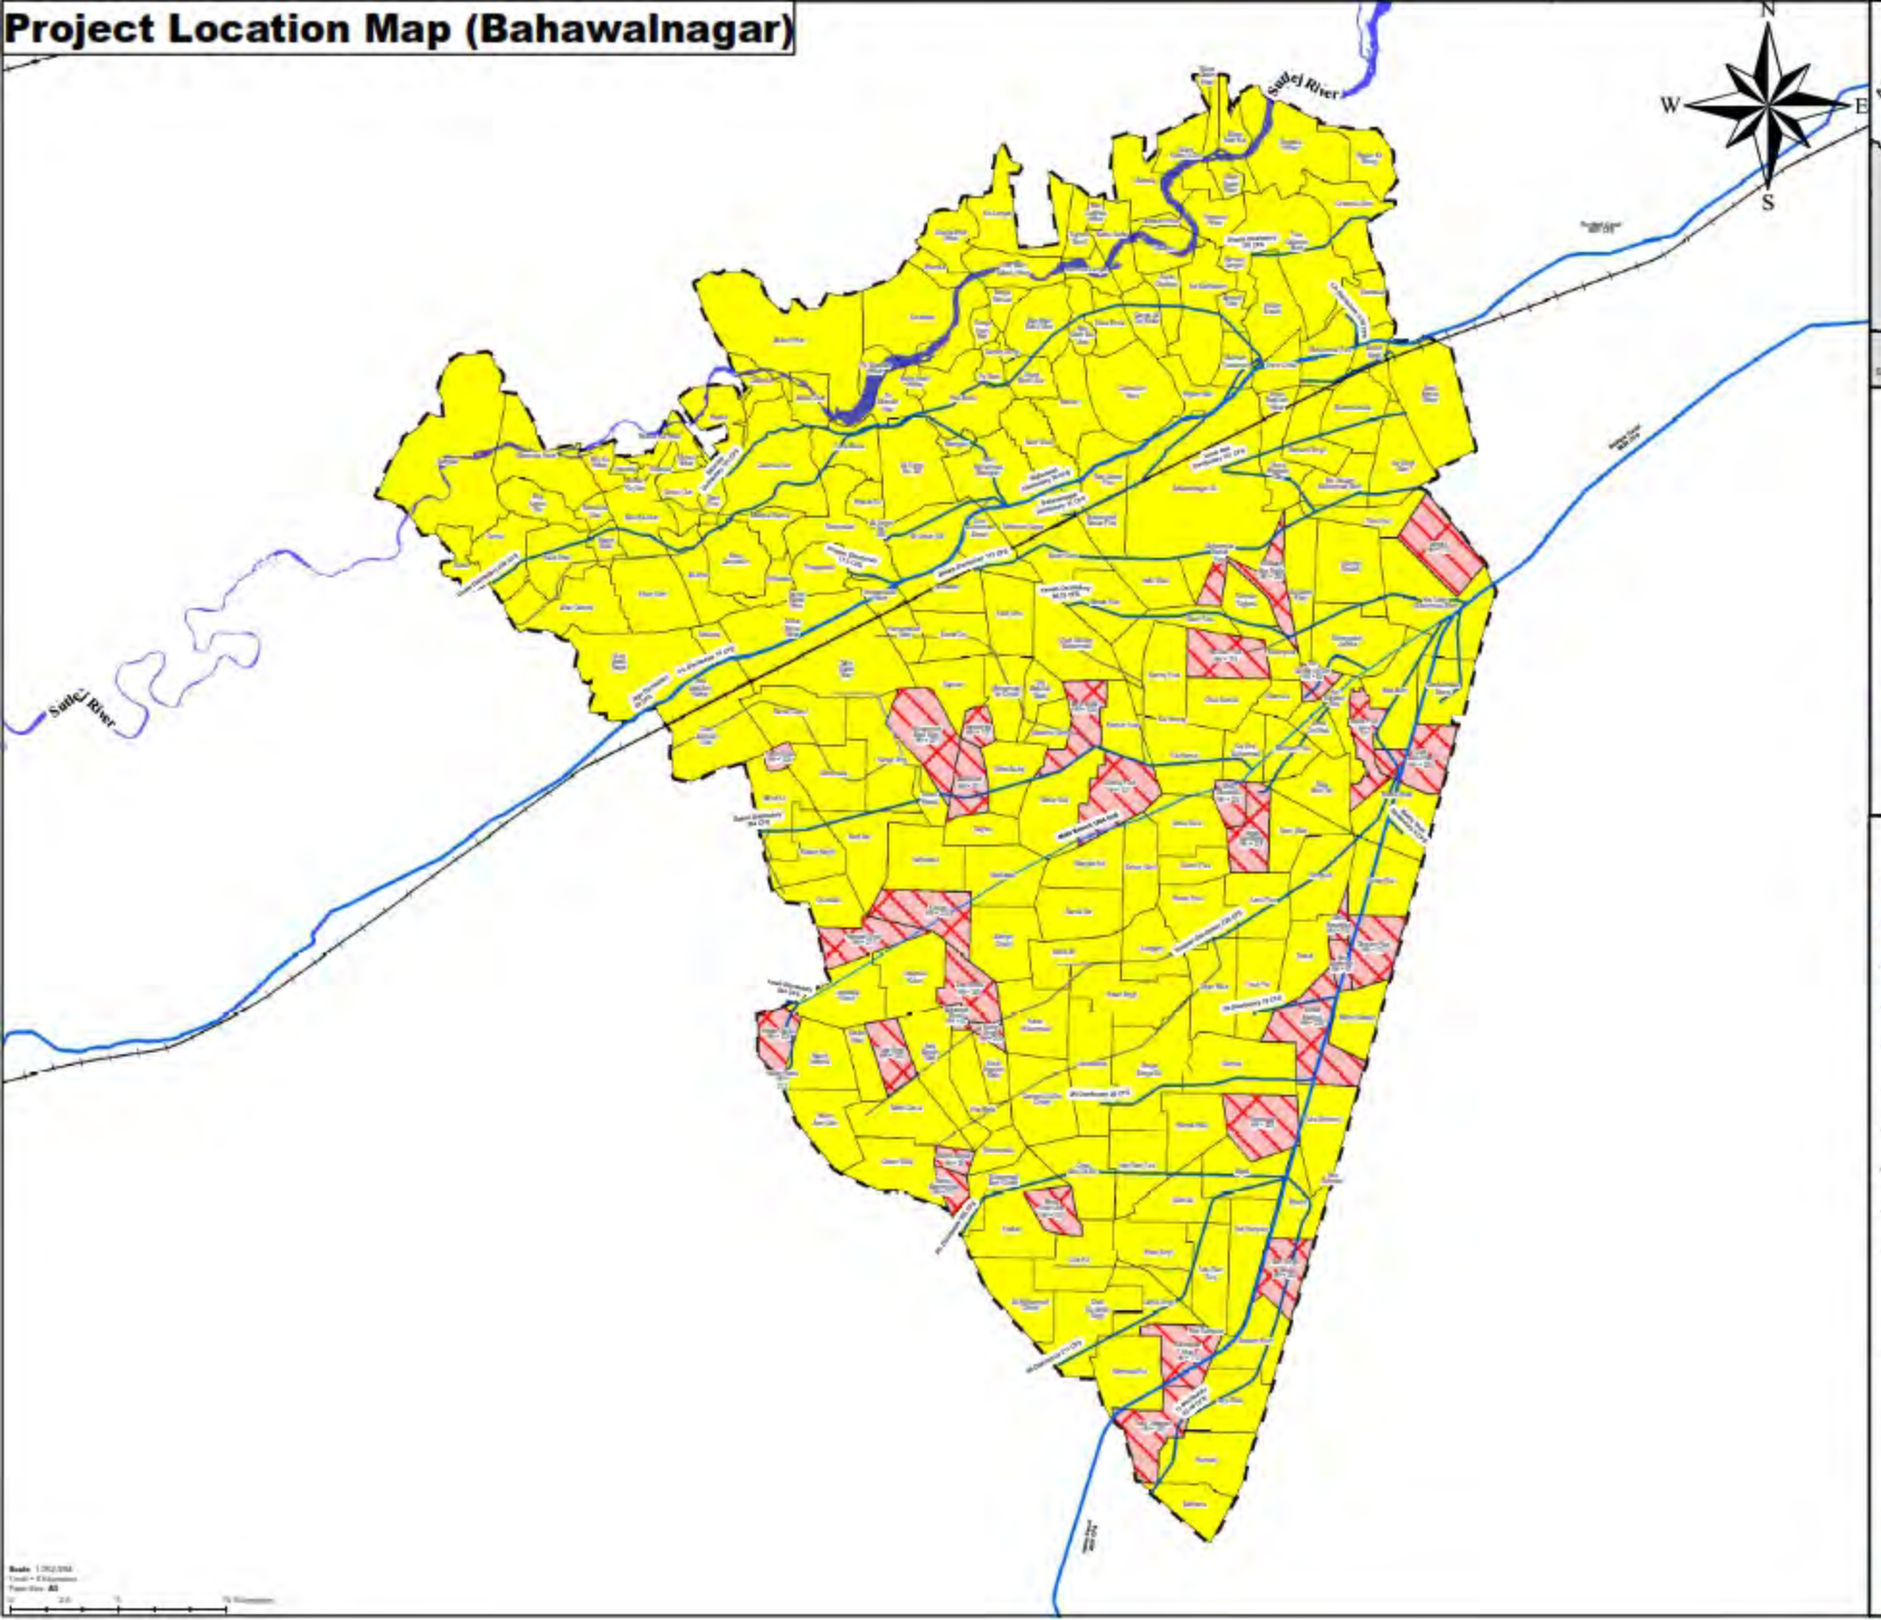

Legend

- Main Canals
- Distributary
- Branch Canals
- Minors
- Sub Minors
- Railway Line
- Provincial Boundary
- Division Boundary
- District Boundary
- Province Punjab
- Project District
- Project Tehsil
- River
- Projected Village
- Tehsil Boundary

Project:

Engineering Design & Construction Supervision,Punjab Rural Sustainable Water Supply & Sanitation Project Cluster South-III

TEHSIL BAHAWALNAGAR

MAUZA AKKANWALI KHURD

LATITUDE: 29.768
LONGITUDE: 73.14

LEGEND

- CENTER
- MAJOR SETTELMENT
- CANAL
- SETTELMENT BOUNDARY
- PROJECT AREA BOUNDARY

TITLE:
SATELLITE MAPS

PROJECT:
Engineering Design & Construction Supervision, Punjab Rural Sustainable Water Supply & Sanitation Project, Cluster South-III

DATE:	02-03-26
DRAWN:	ASAD
DESGIN:	ENGR.FAIEZ
APPROVED:	ENGR. IHSAN UL HAQ

TITLE:
PRMSC-BWN-AK-SM-01

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

INFRASTRUCTURE CONSULTANT
ENVIRONMENTAL TECHNOLOGIES
ASIAN CONSULTING ENGINEERS
www.asiancon.com

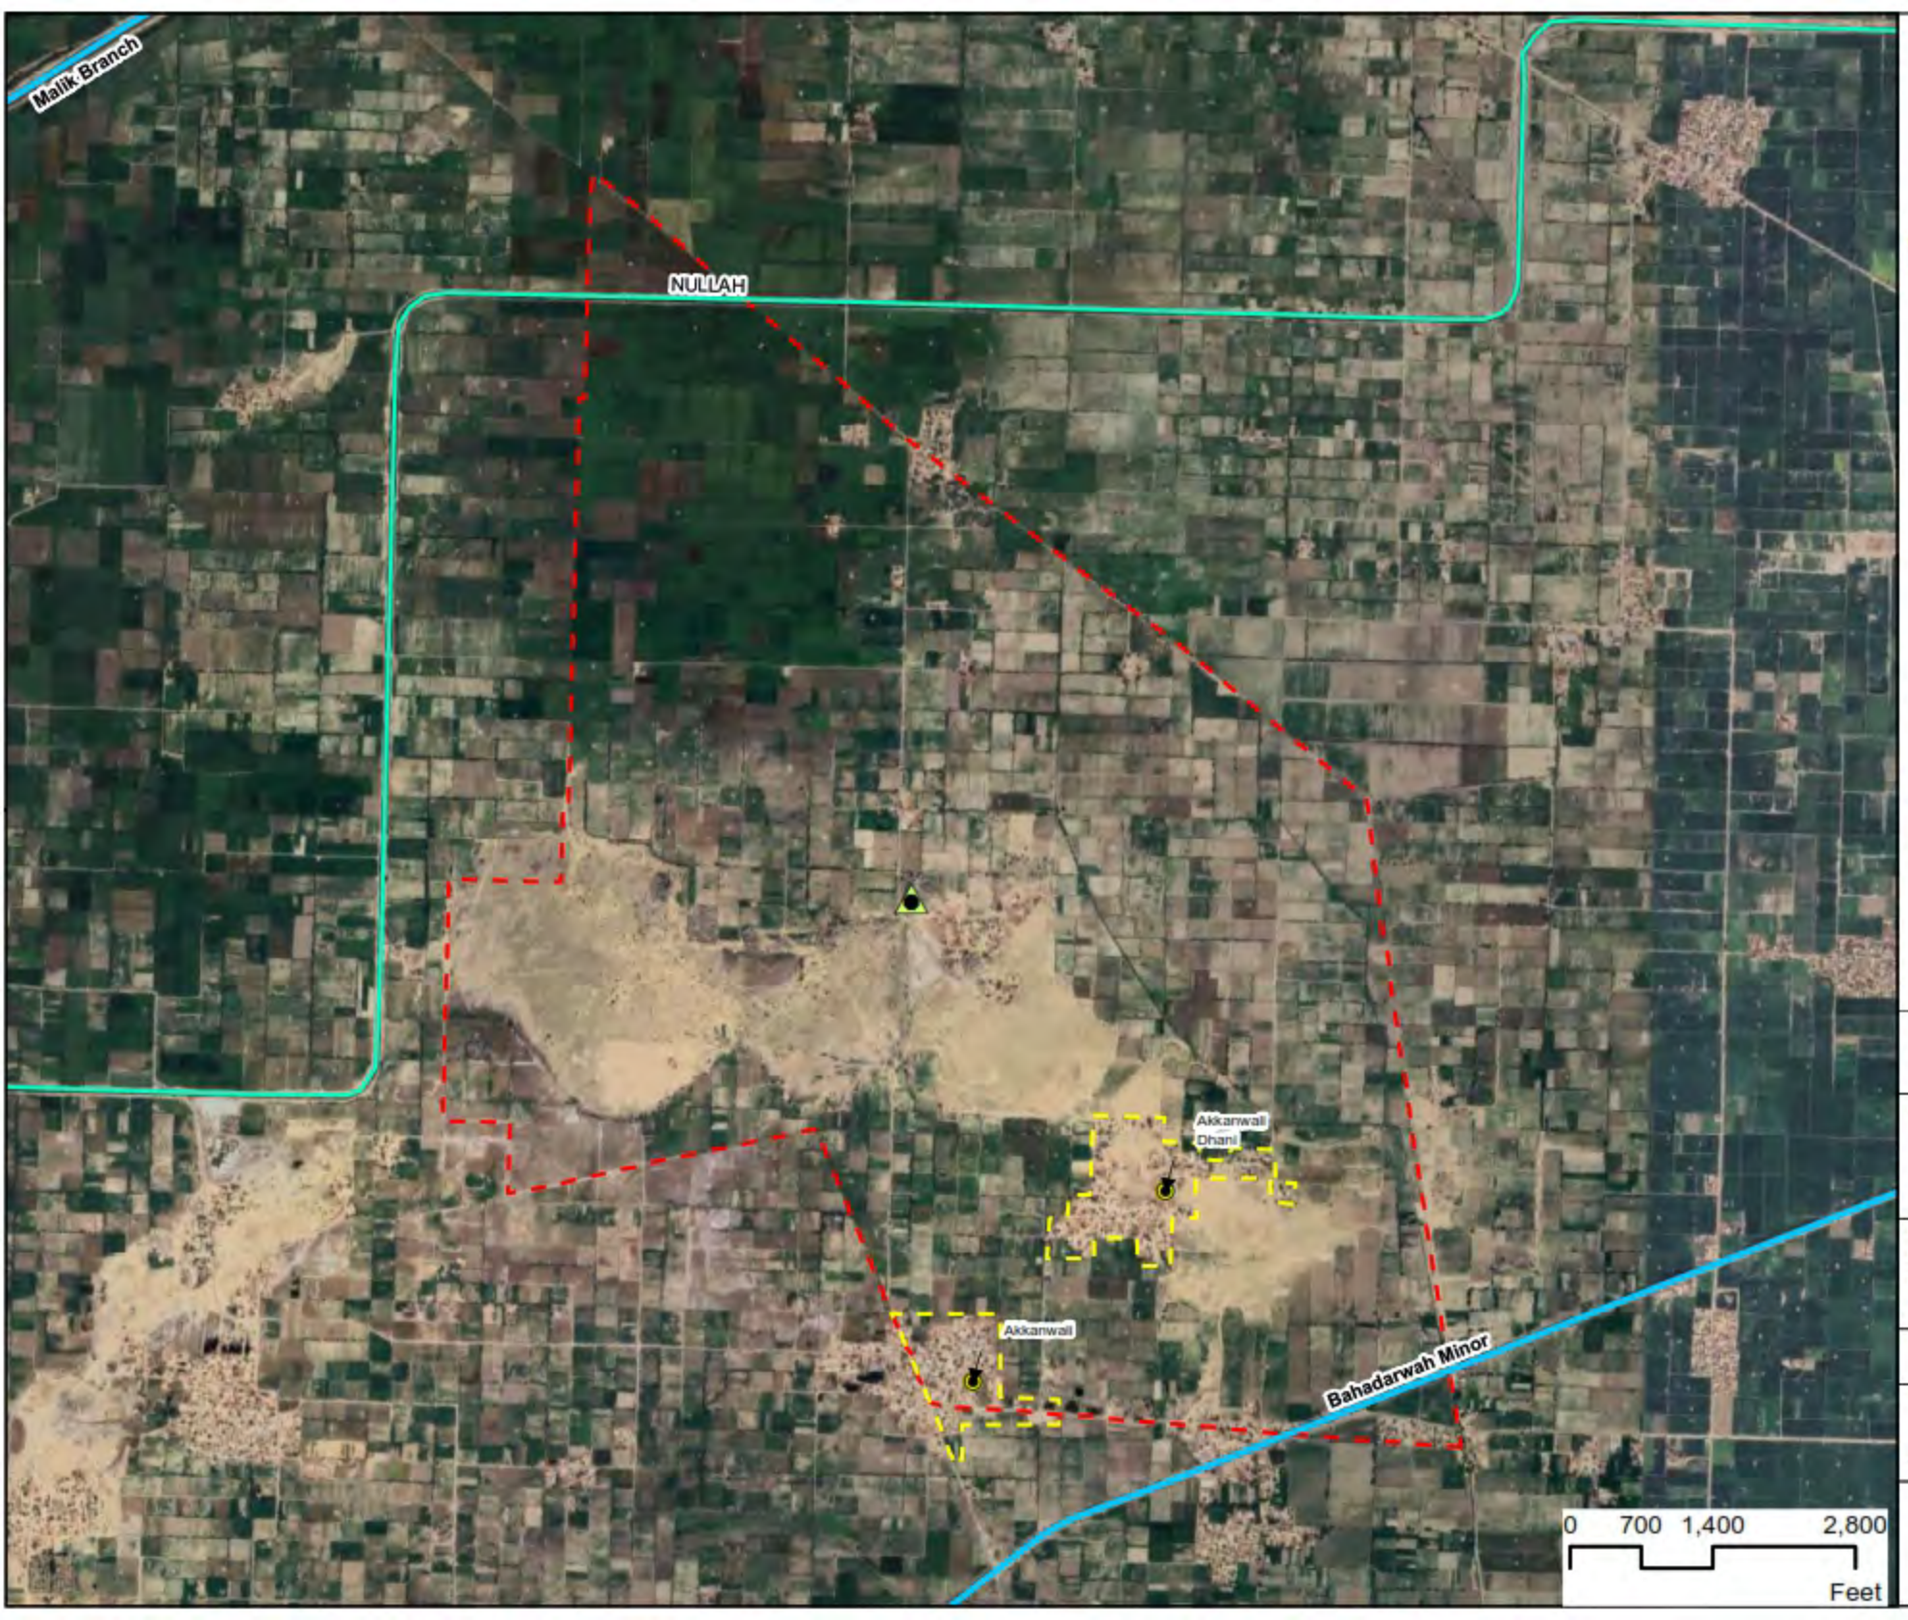

TEHSIL BAHAWALNAGAR

MAUZA SHER MOHD

LATITUDE: 29.786
LONGITUDE: 73.136

LEGEND

- CENTER
- MAJOR SETTELMENT
- NULLAH
- CANAL
- SETTELMENT BOUNDARY
- PROJECT AREA BOUNDARY

TITLE:
SATELLITE MAPS

PROJECT:
Engineering Design & Construction Supervision, Punjab Rural Sustainable Water Supply & Sanitation Project, Cluster South-III

DATE:	02-03-26
DRAWN:	ASAD
DESGIN:	ENGR.FAIEZ
APPROVED:	ENGR. IHSAN UL HAQ

TITLE:
PRMSC-BWN-SM-SM-01

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

INFRASTRUCTURE CONSULTANT
ENVIRONMENTAL TECHNOLOGIES
ASIAN CONSULTING ENGINEERS
www.asiancon.com

N
W E
S

TEHSIL BAHAWALNAGAR

MAUZA KARTAR SINGH

LATITUDE: 29.763
LONGITUDE: 73.15

LEGEND

- CENTER
- MAJOR SETTELMENT
- CANAL
- SETTELMENT BOUNDARY
- PROJECT AREA BOUNDARY

TITLE:
SATELLITE MAPS

PROJECT:
Engineering Design & Construction Supervision, Punjab Rural Sustainable Water Supply & Sanitation Project, Cluster South-III

DATE:	02-03-26
DRAWN:	ASAD
DESGIN:	ENGR.FAIEZ
APPROVED:	ENGR. IHSAN UL HAQ

TITLE:
PRMSC-BWN-KS-SM-01

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

INFRASTRUCTURE CONSULTANT
ENVIRONMENTAL TECHNOLOGIES
ASIAN CONSULTING ENGINEERS
www.asiancon.com

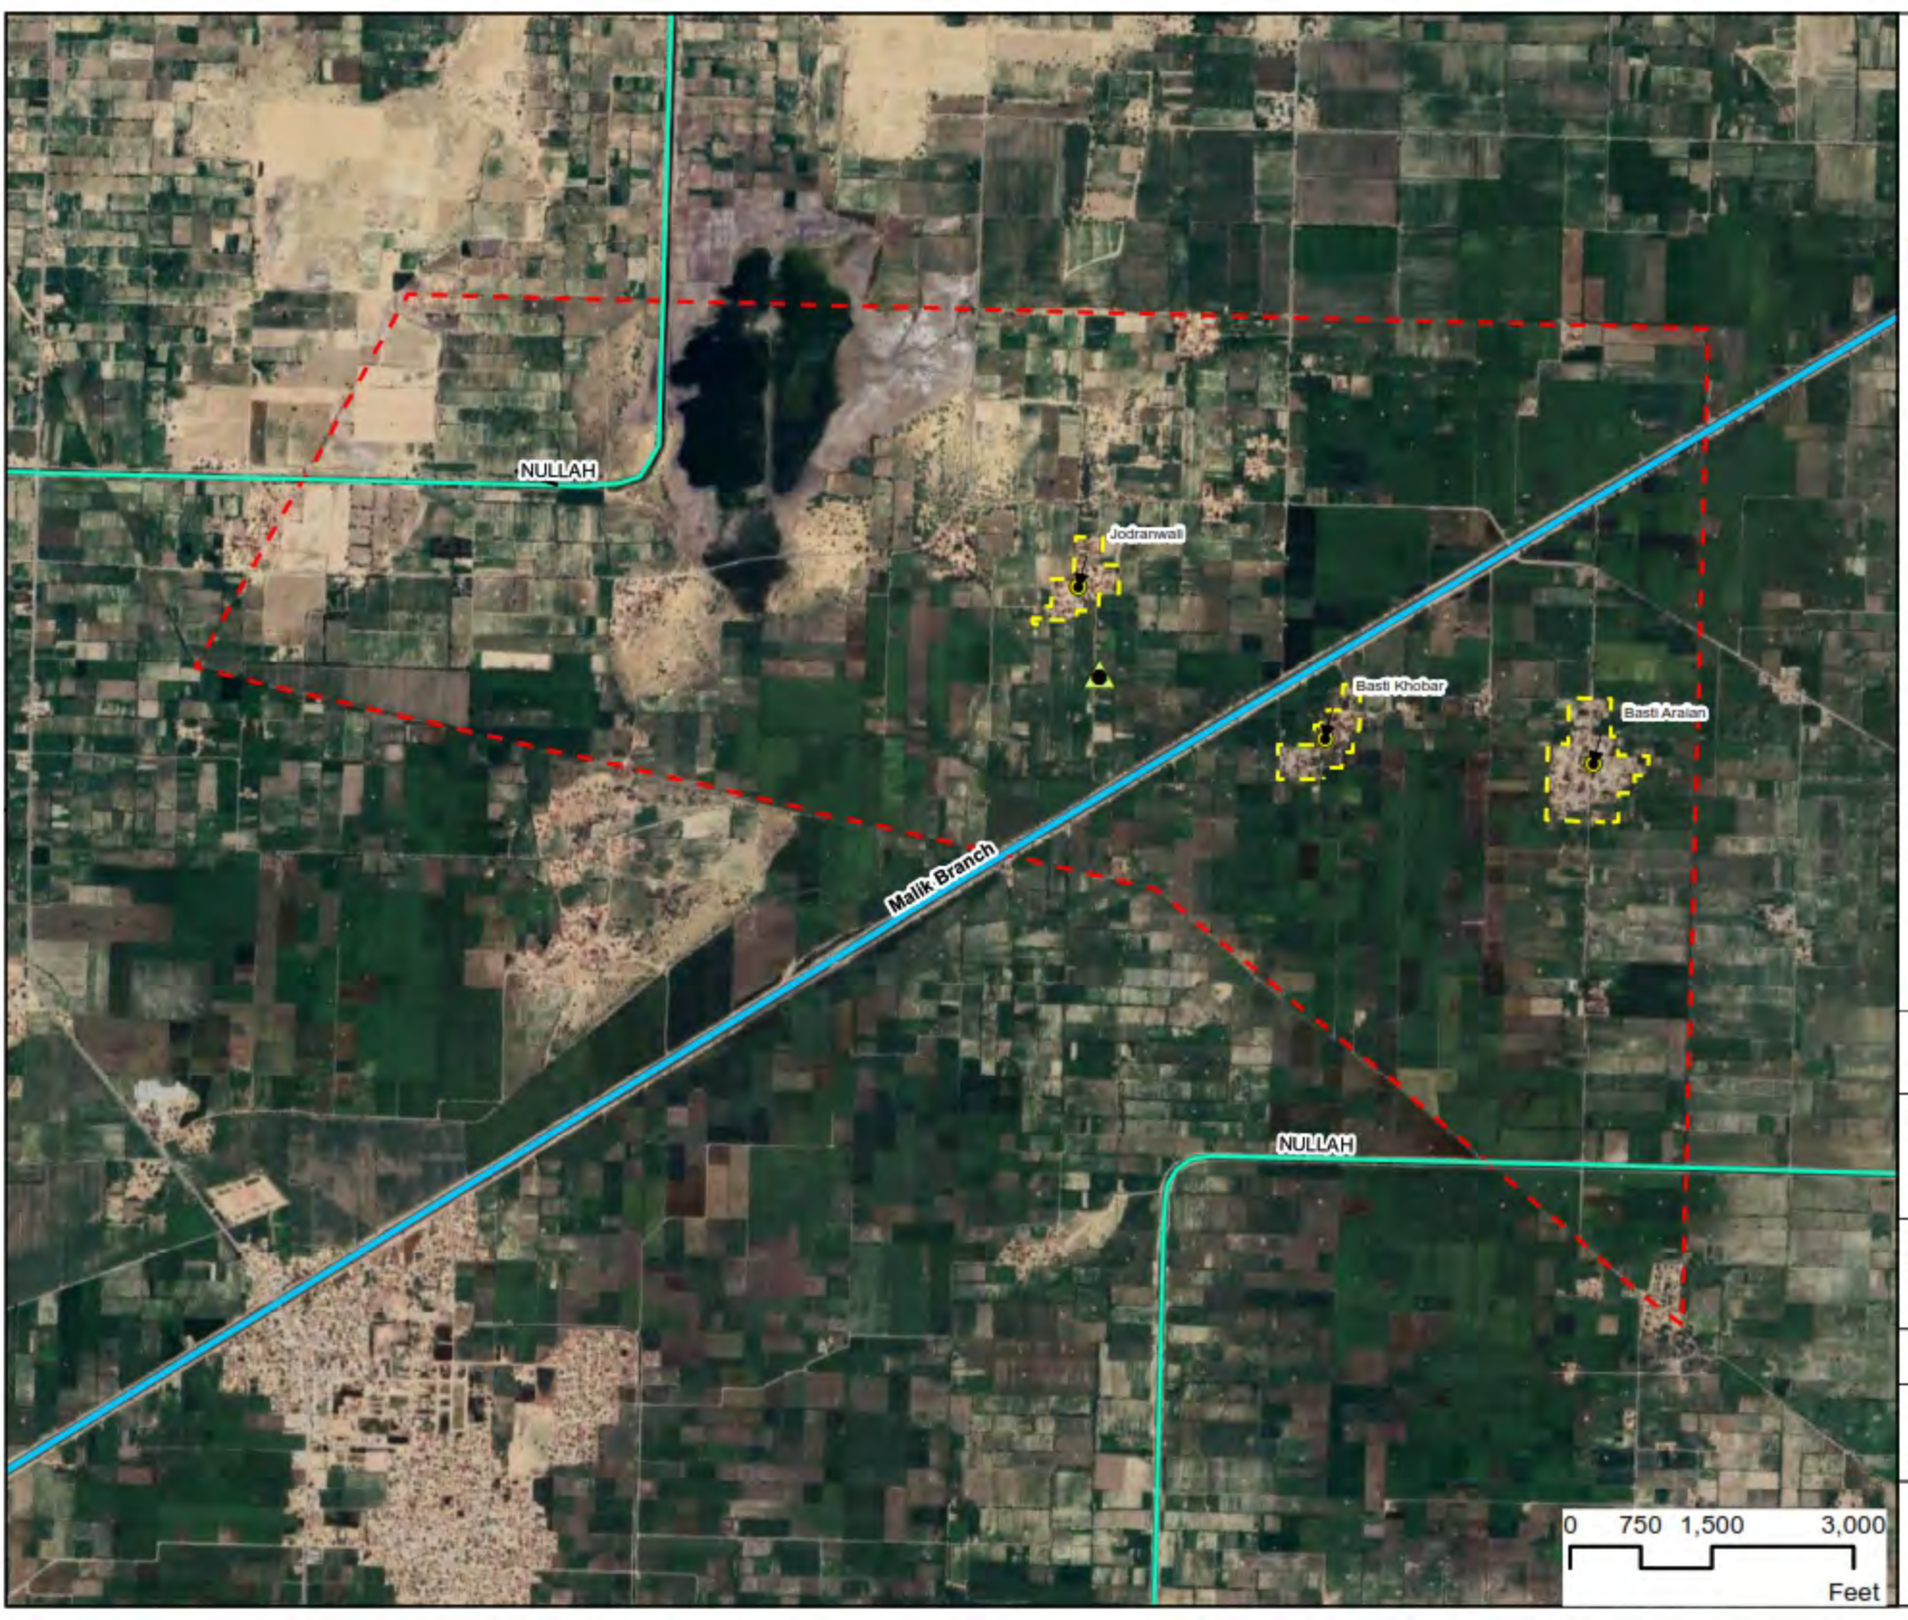

TEHSIL BAHAWALNAGAR

MAUZA KHOBER

LATITUDE: 29.818
LONGITUDE: 73.107

LEGEND

- CENTER
- MAJOR SETTELMENT
- NULLAH
- CANAL
- SETTELMENT BOUNDARY
- PROJECT AREA BOUNDARY

TITLE:
SATELLITE MAPS

PROJECT:
Engineering Design & Construction Supervision, Punjab Rural Sustainable Water Supply & Sanitation Project, Cluster South-III

DATE:	02-03-26
DRAWN:	ASAD
DESGIN:	ENGR.FAIEZ
APPROVED:	ENGR. IHSAN UL HAQ

TITLE:
PRMSC-BWN-K-SM-01

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

INFRASTRUCTURE CONSULTANT
ENVIRONMENTAL TECHNOLOGIES
ASIAN CONSULTING ENGINEERS
www.asiancon.com

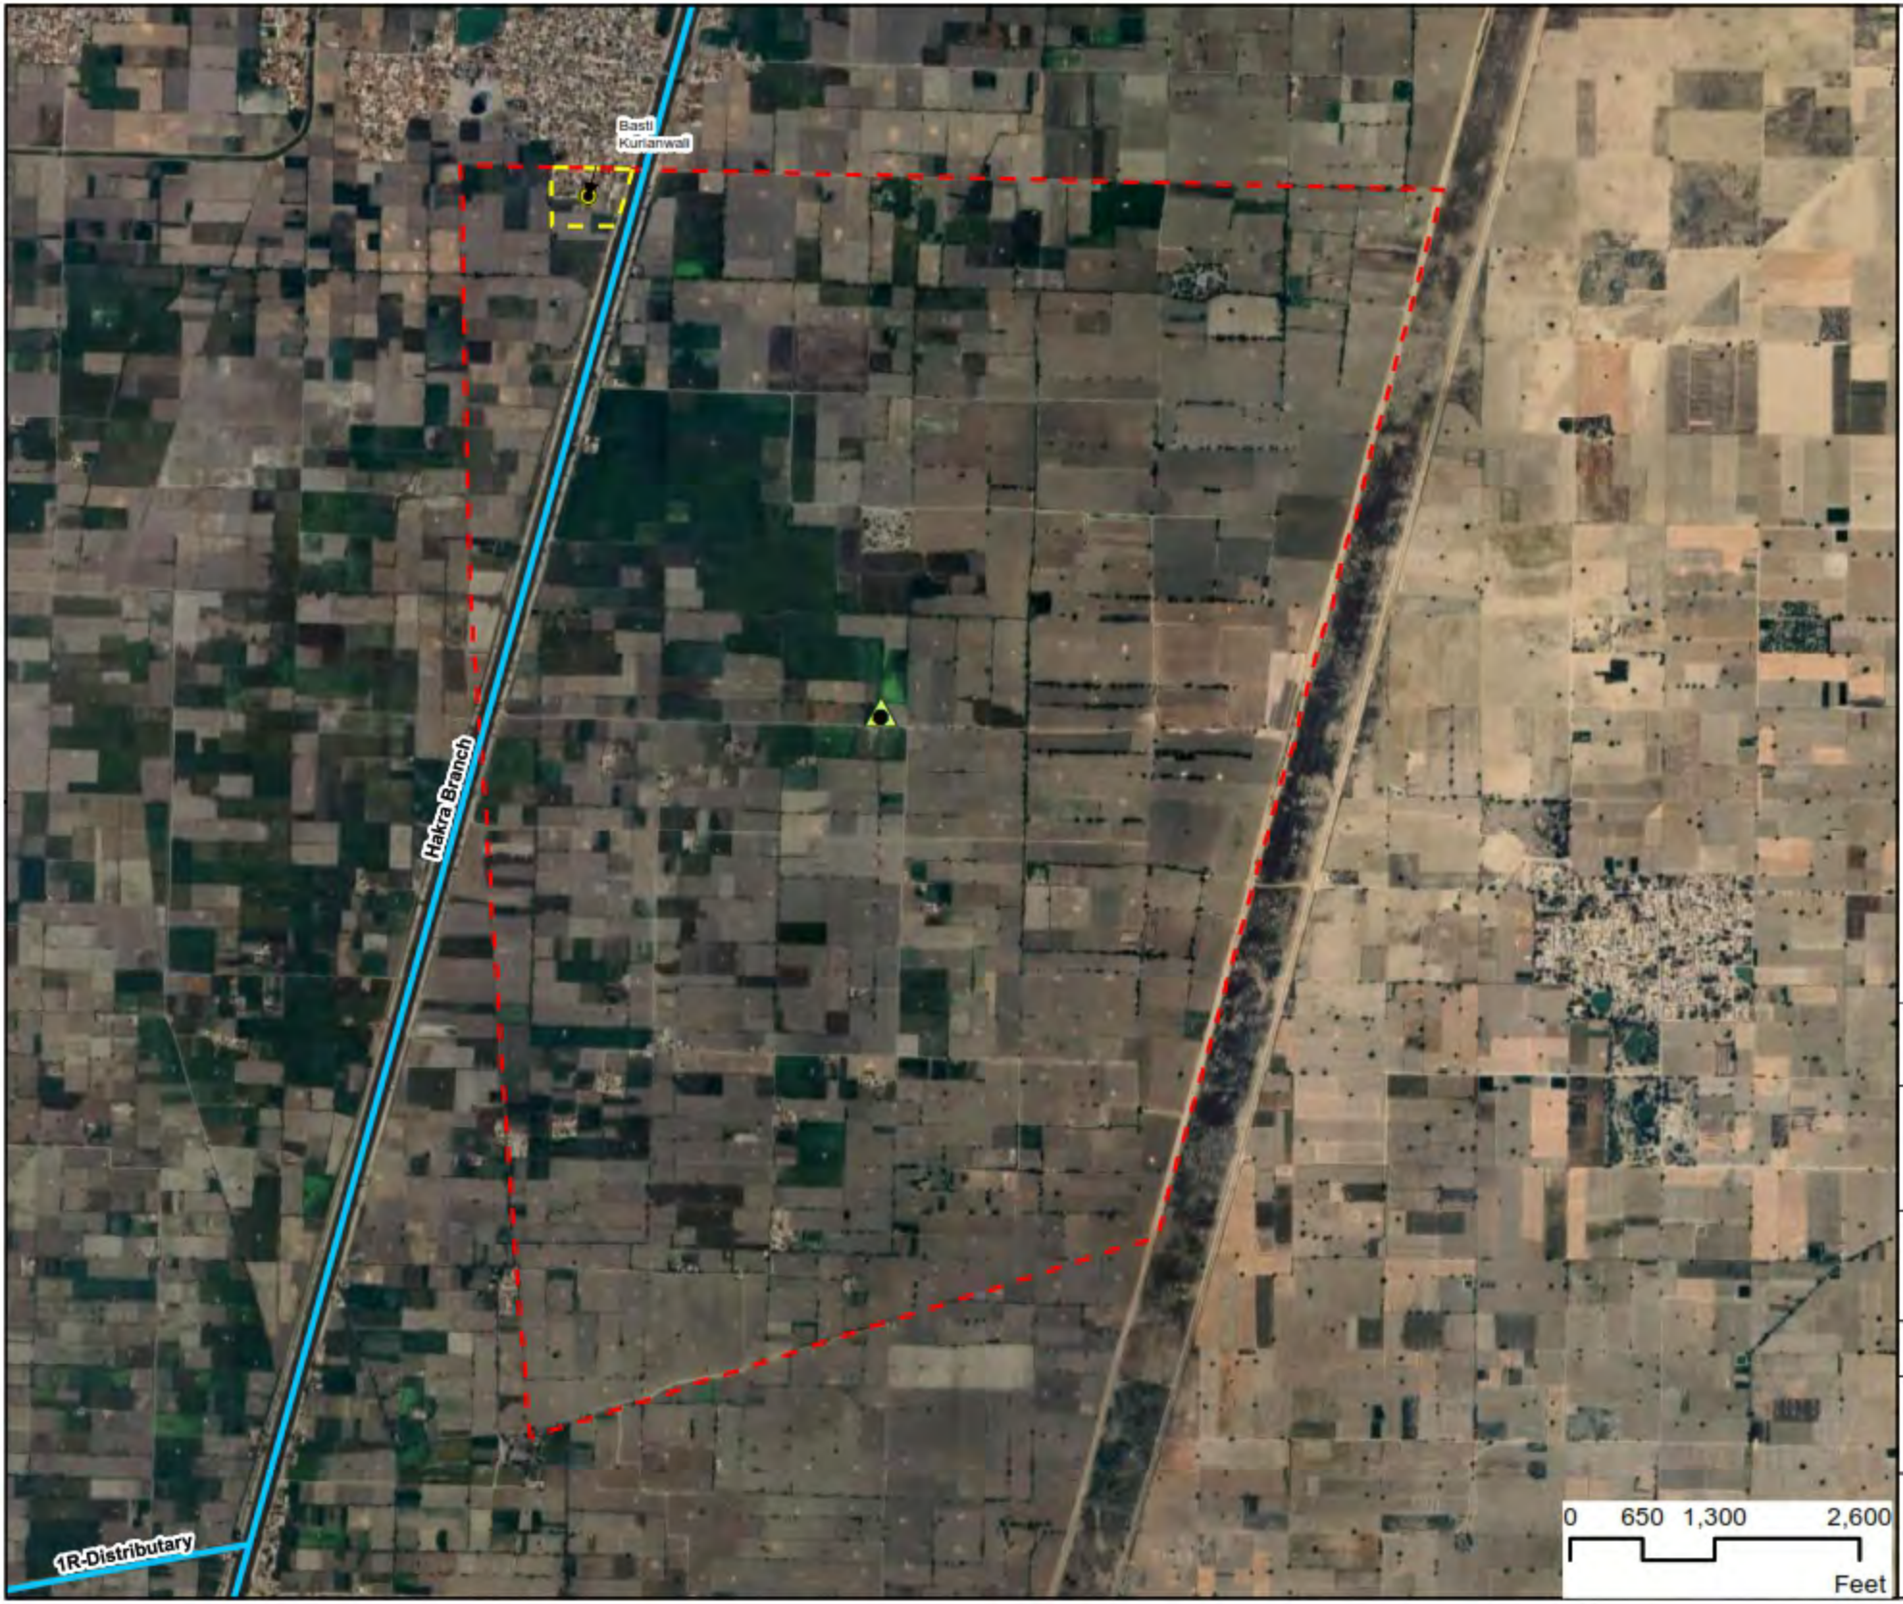

N
W E
S

TEHSIL BAHAWALNAGAR

MAUZA DHARAM PURA

LATITUDE: 29.81
LONGITUDE: 73.35

LEGEND

- CENTER
- MAJOR SETTELMENT
- CANAL
- SETTELMENT BOUNDARY
- PROJECT AREA BOUNDARY

TITLE:
SATELLITE MAPS

PROJECT:
Engineering Design & Construction Supervision, Punjab Rural Sustainable Water Supply & Sanitation Project, Cluster South-III

DATE:	02-03-26
DRAWN:	ASAD
DESGIN:	ENGR.FAIEZ
APPROVED:	ENGR. IHSAN UL HAQ

TITLE:
PRMSC-BWN-DP-SM-01

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

INFRASTRUCTURE CONSULTANT
ENVIRONMENTAL TECHNOLOGIES
ASIAN CONSULTING ENGINEERS
www.asiancon.com

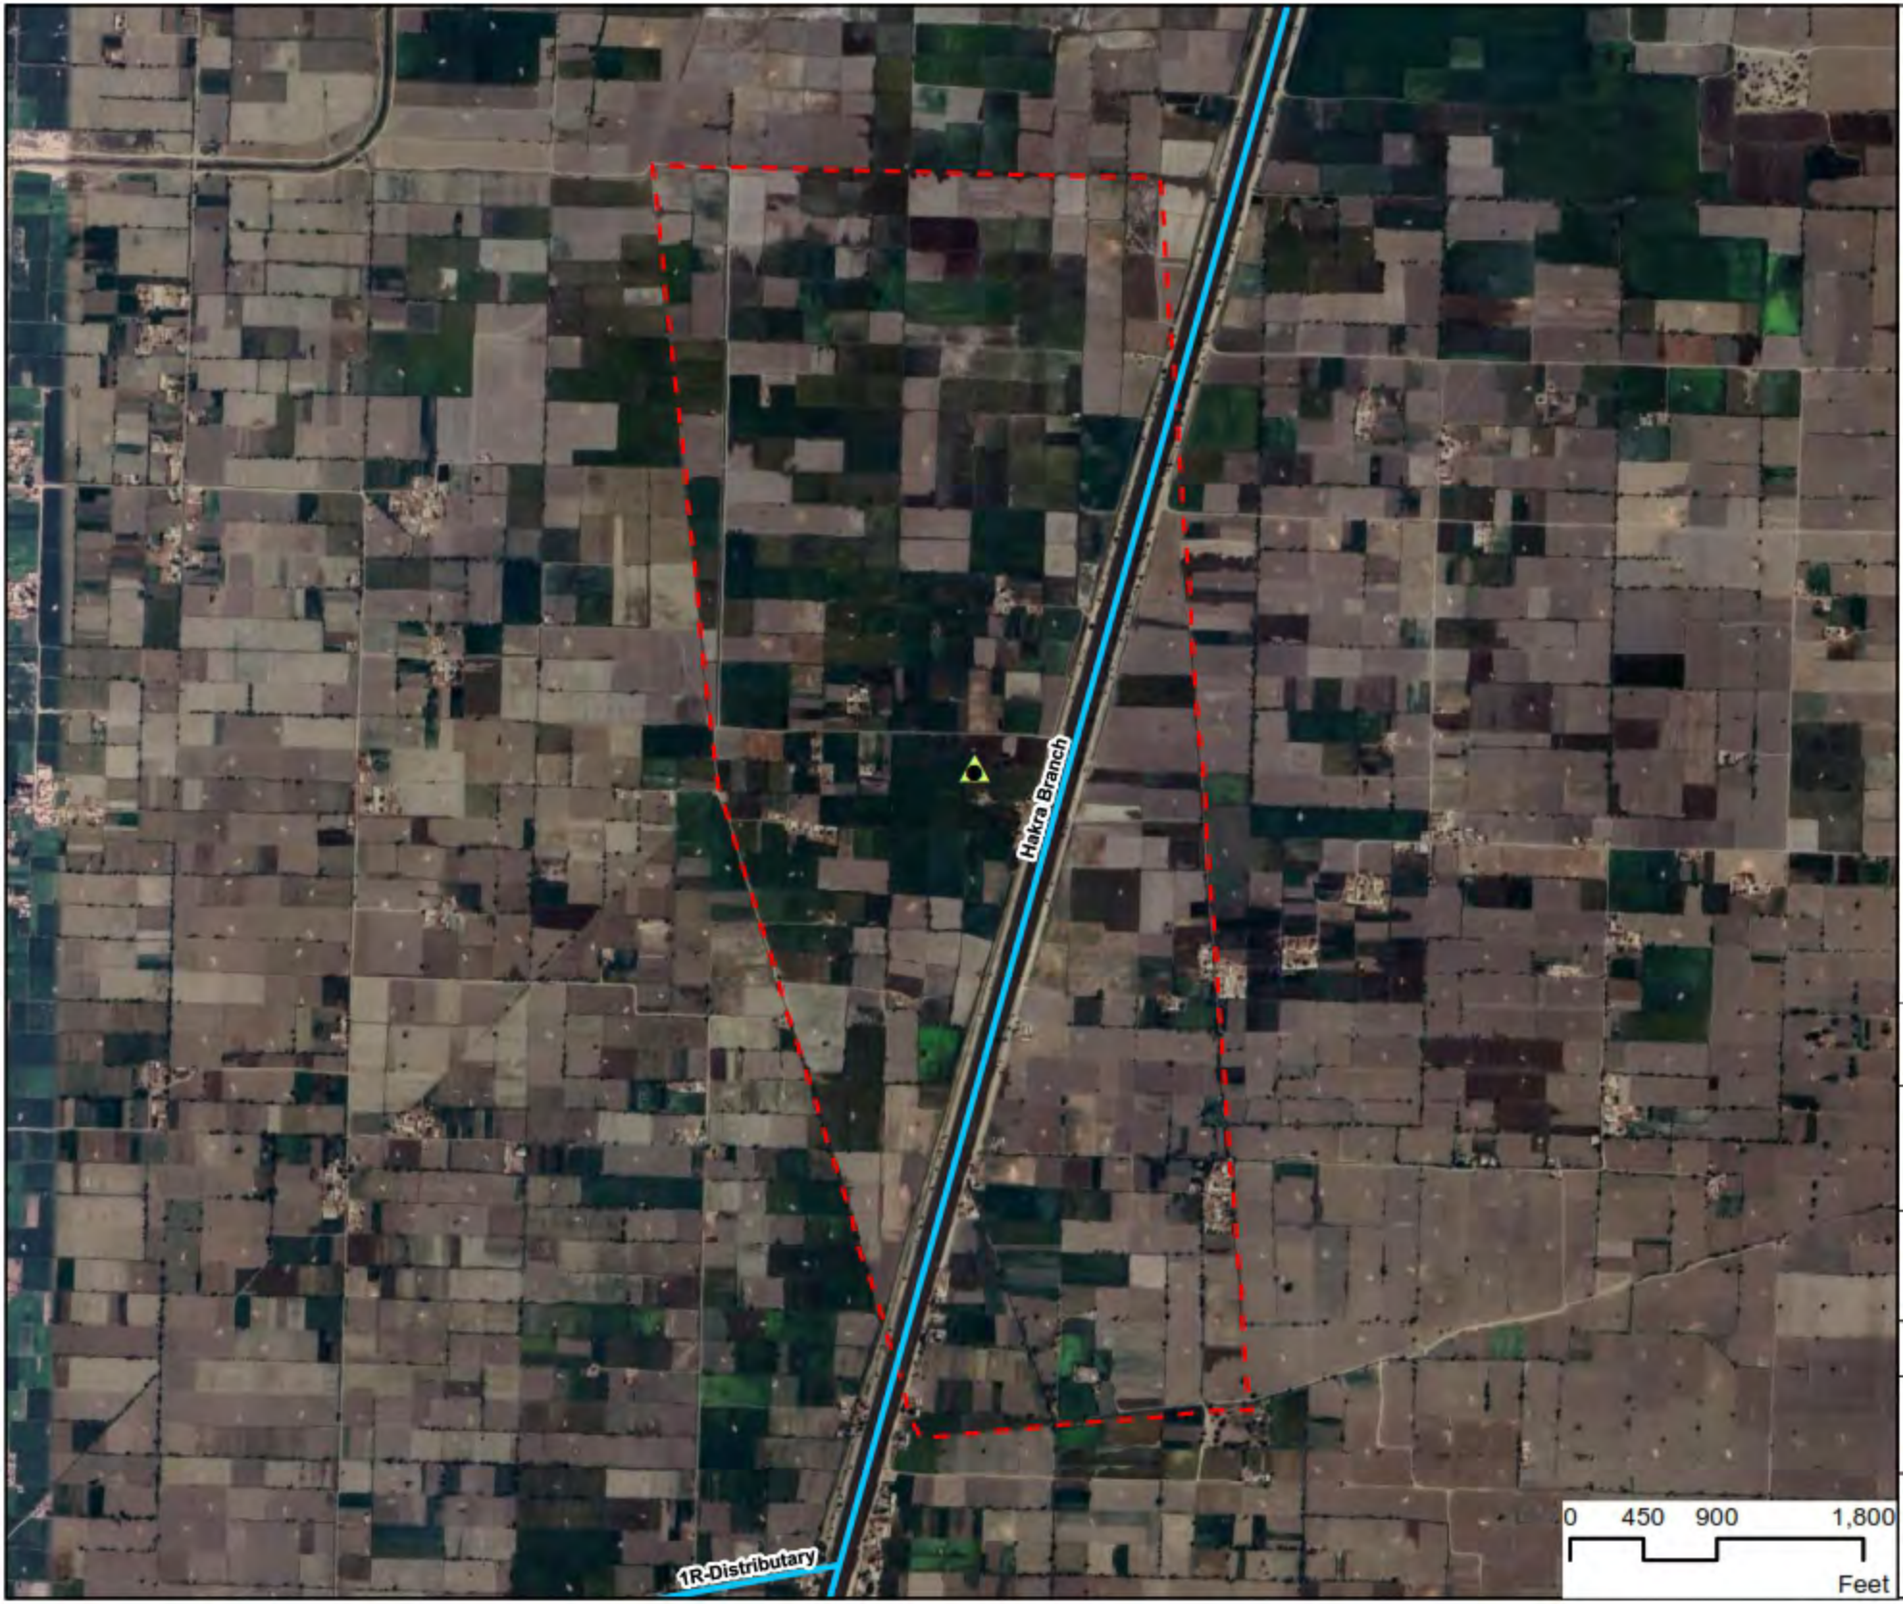

N
W E
S

TEHSIL BAHAWALNAGAR

MAUZA HIRA BASHNOAI

LATITUDE: 29.799
LONGITUDE: 73.327

LEGEND

- CENTER
- CANAL
- PROJECT AREA BOUNDARY

TITLE:
SATELLITE MAPS

PROJECT:
Engineering Design & Construction Supervision, Punjab Rural Sustainable Water Supply & Sanitation Project, Cluster South-III

DATE:	02-03-26
DRAWN:	ASAD
DESGIN:	ENGR.FAIEZ
APPROVED:	ENGR. IHSAN UL HAQ

TITLE:
PRMSC-BWN-HB-SM-01

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

INFRASTRUCTURE CONSULTANT
ENVIRONMENTAL TECHNOLOGIES
ASIAN CONSULTING ENGINEERS
www.asiancon.com

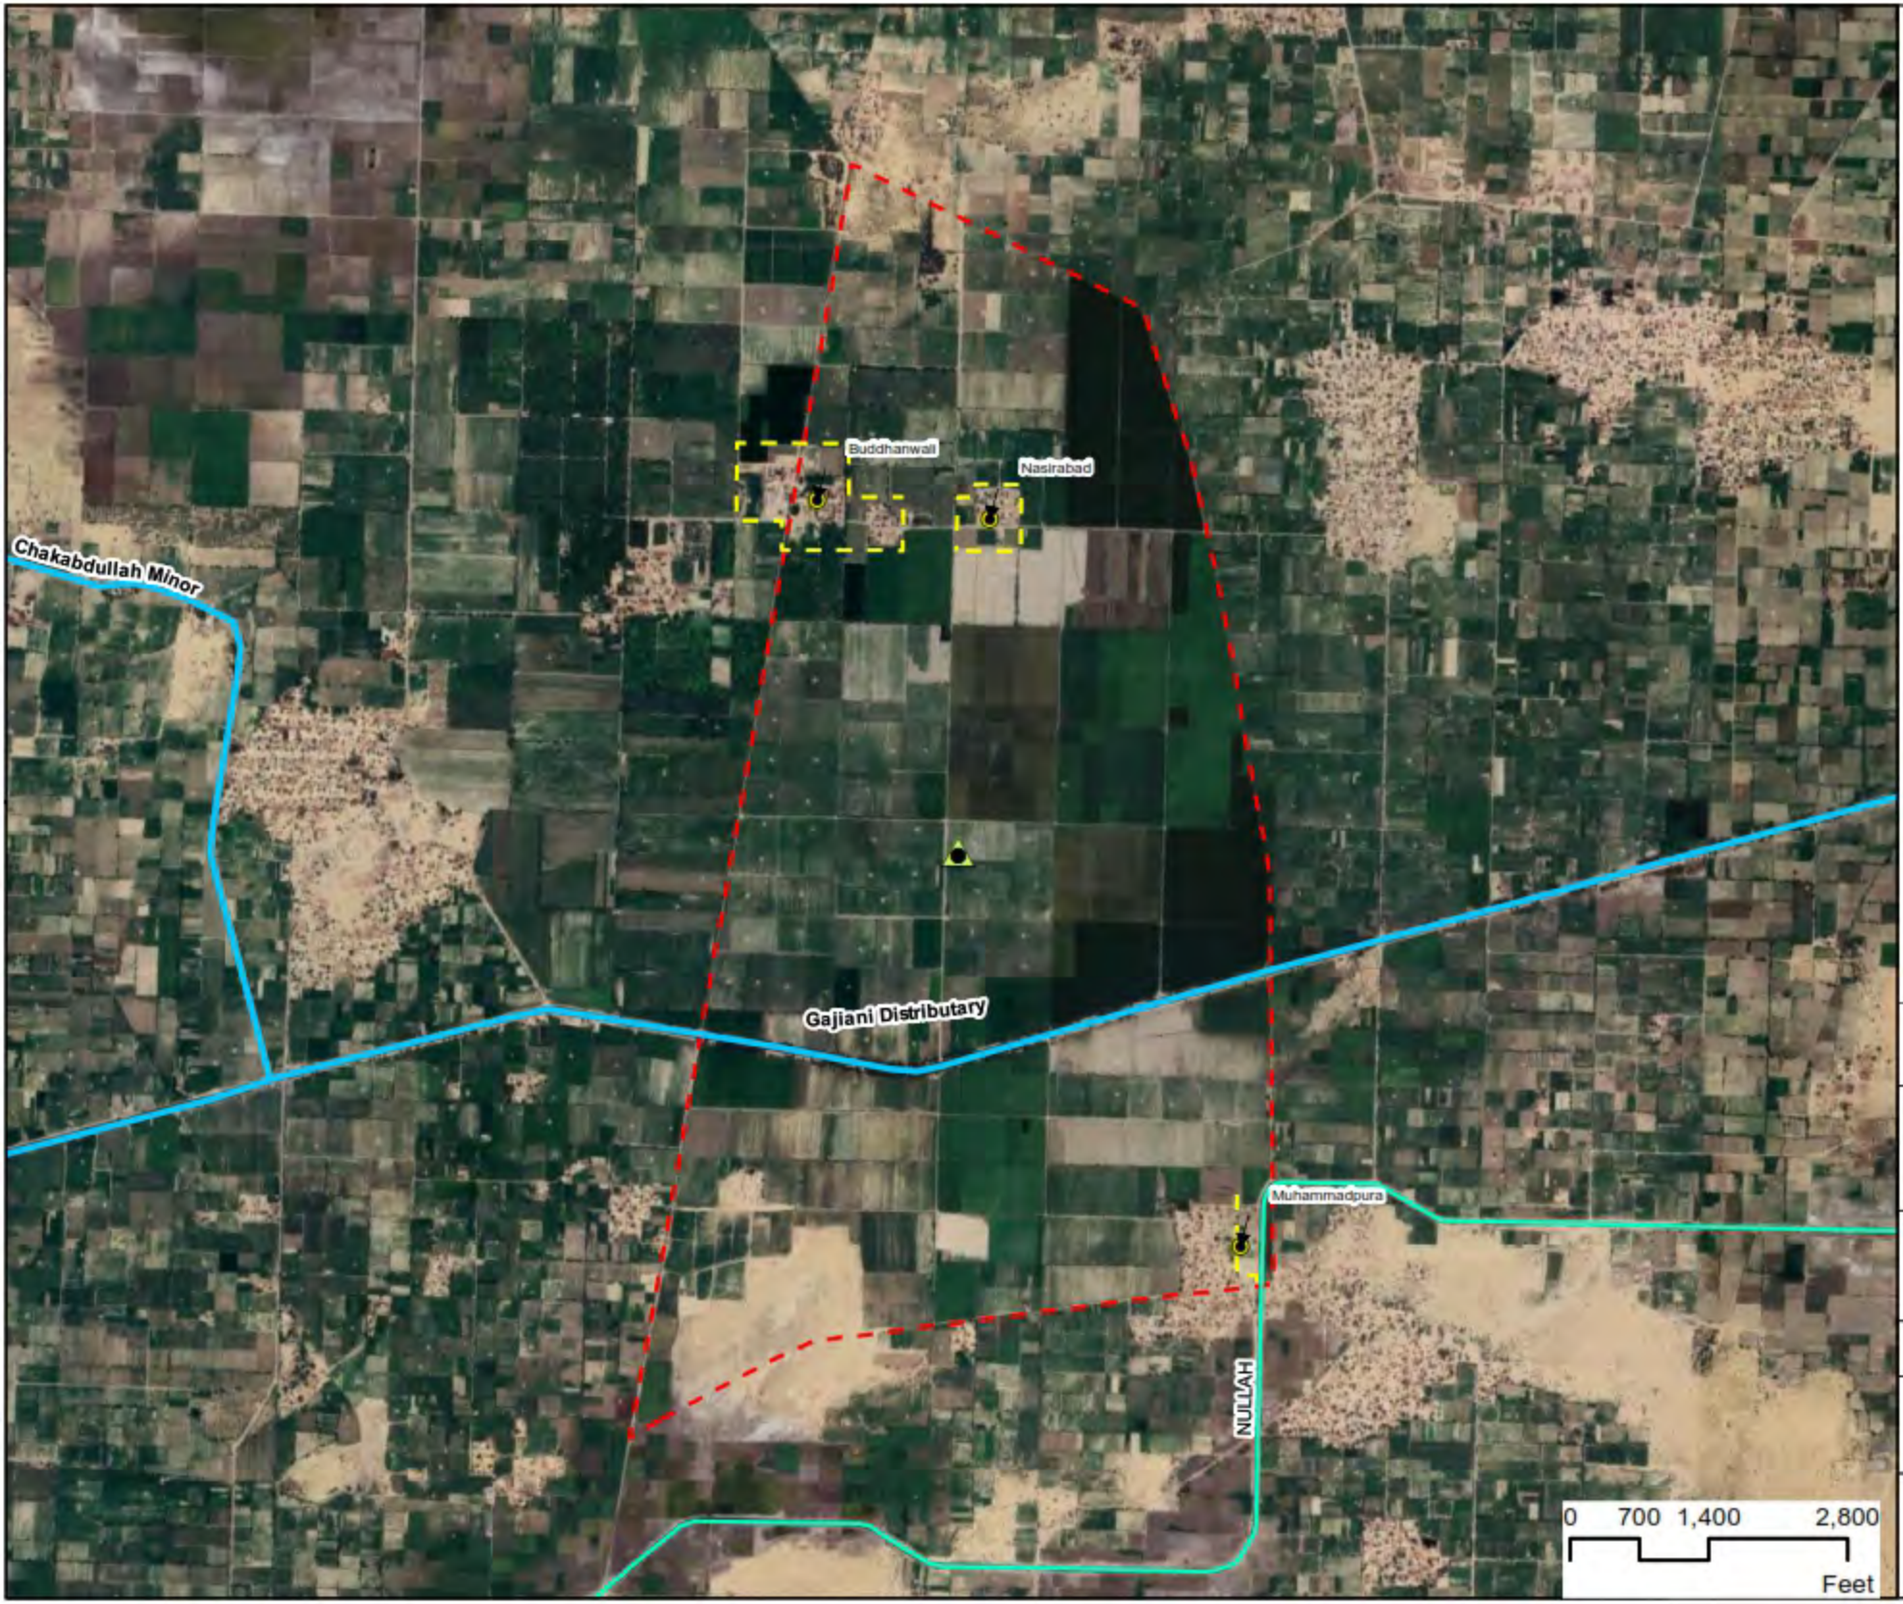

TEHSIL BAHAWALNAGAR

MAUZA ALLAHABAD

LATITUDE: 29.878
LONGITUDE: 73.151

LEGEND

- CENTER
- MAJOR SETTELMENT
- NULLAH
- CANAL
- SETTELMENT BOUNDARY
- PROJECT AREA BOUNDARY

TITLE: SATELLITE MAPS

PROJECT: Engineering Design & Construction Supervision, Punjab Rural Sustainable Water Supply & Sanitation Project, Cluster South-III

DATE:	02-03-26
DRAWN:	ASAD
DESGIN:	ENGR.FAIEZ
APPROVED:	ENGR. IHSAN UL HAQ

TITLE: PRMSC-BWN-A-SM-01

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

INFRASTRUCTURE CONSULTANT

ENVIRONMENTAL TECHNOLOGIES

ASIAN CONSULTING ENGINEERS www.asiancon.com

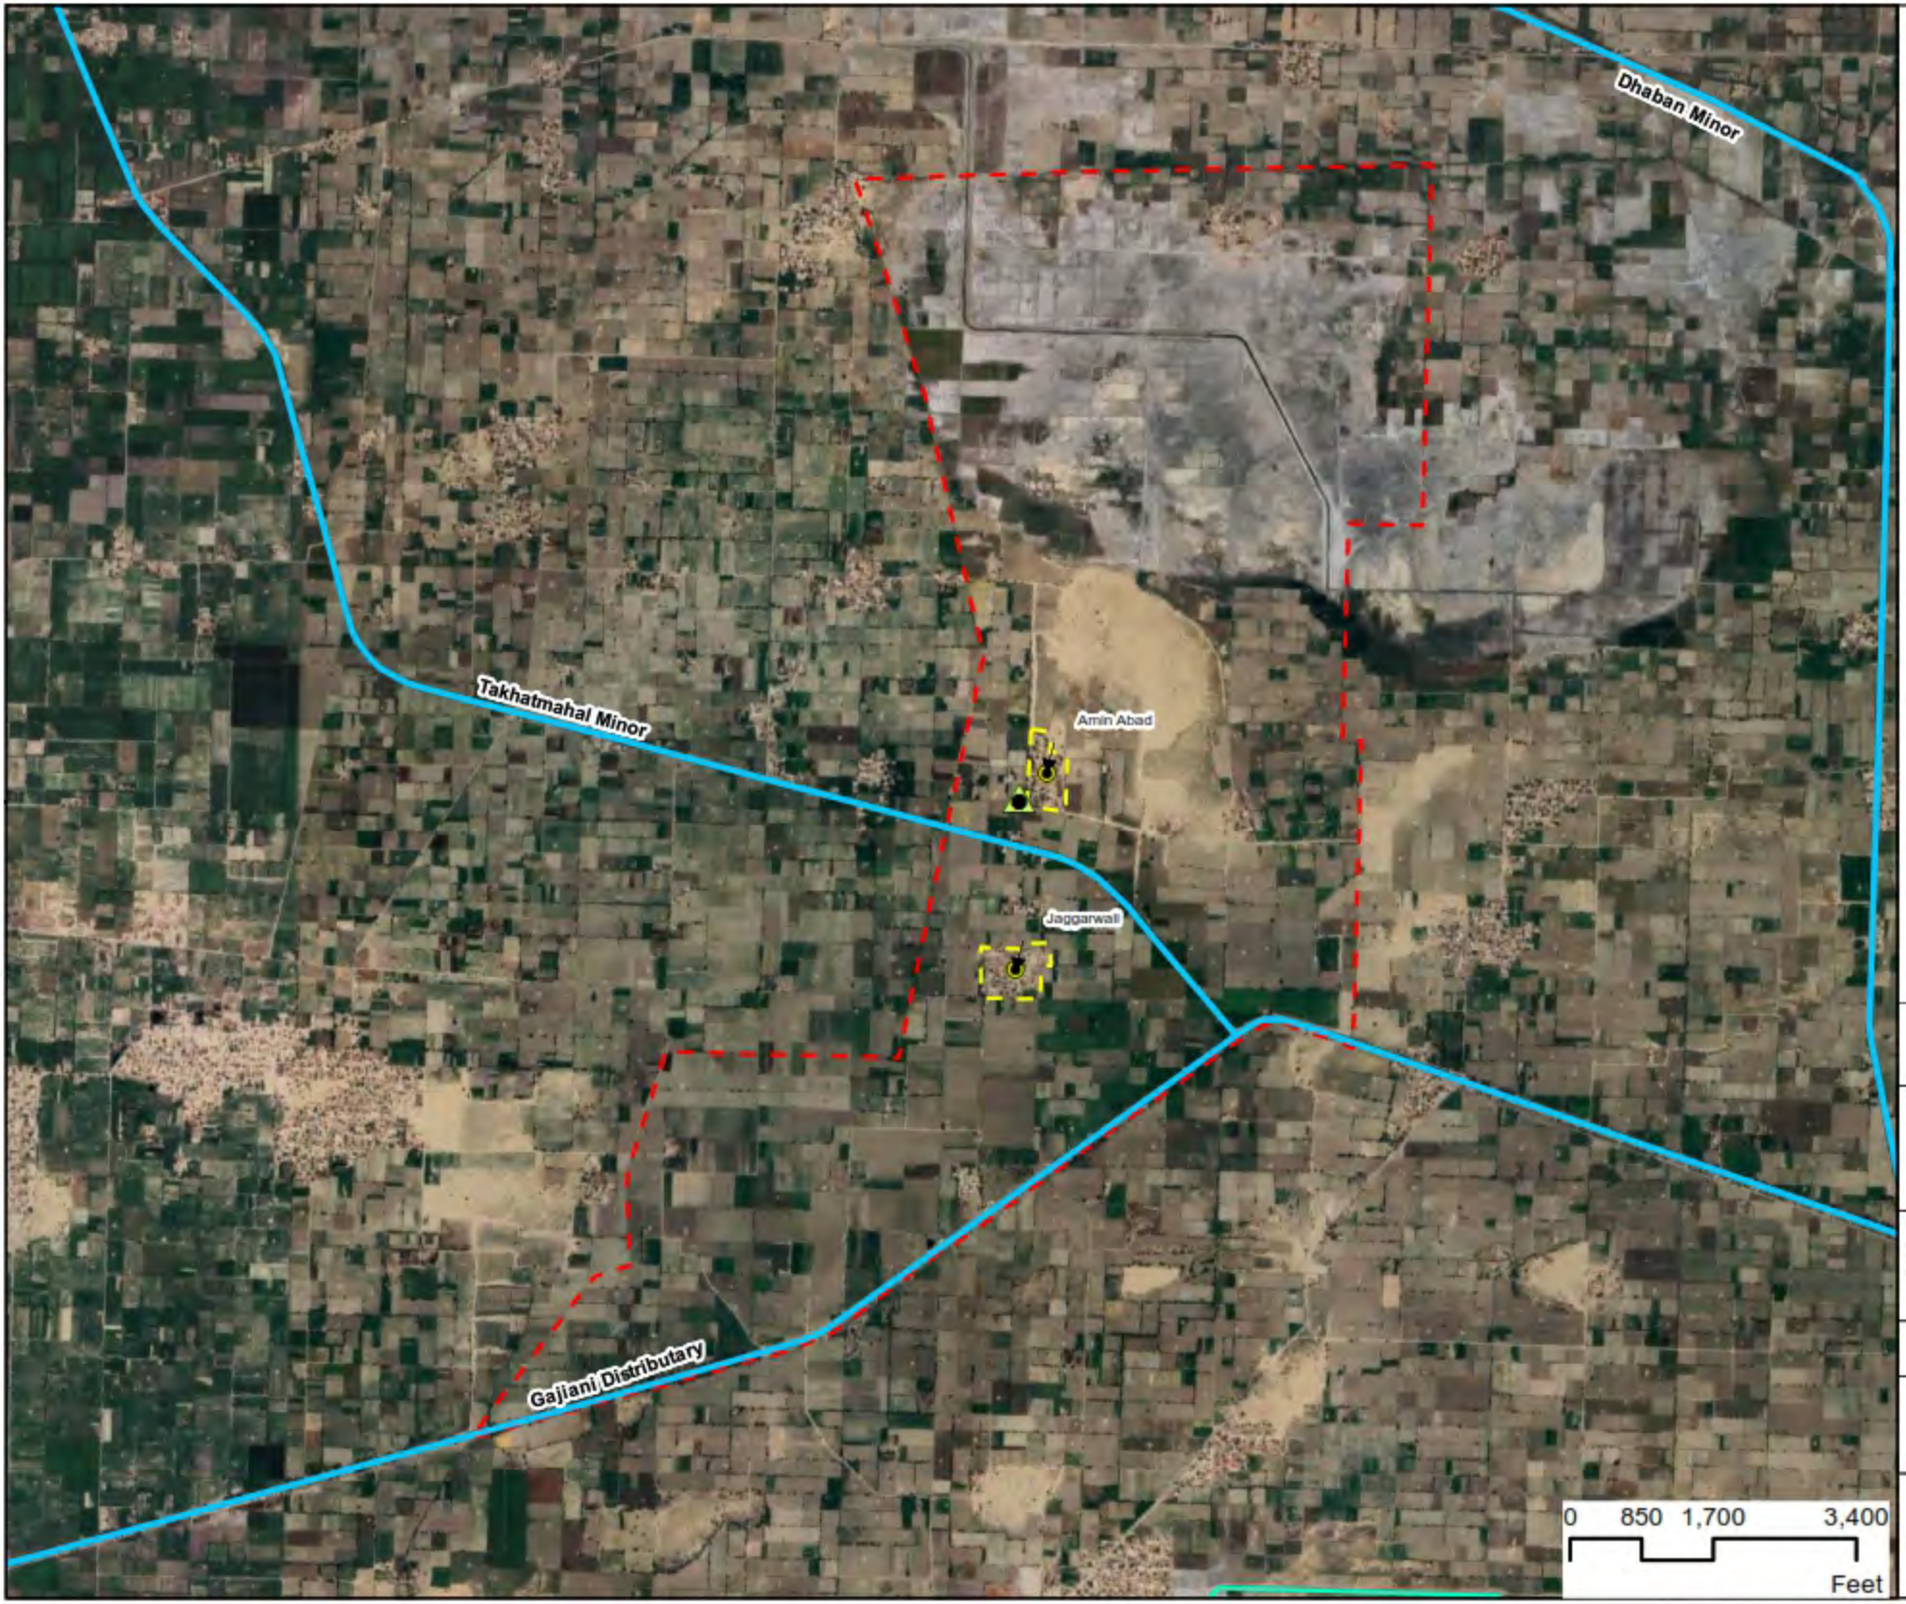

N
W E
S

TEHSIL BAHAWALNAGAR

MAUZA AMIN ABAD

LATITUDE: 29.905
LONGITUDE: 73.19

LEGEND

- CENTER
- MAJOR SETTELMENT
- NULLAH
- CANAL
- SETTELMENT BOUNDARY
- PROJECT AREA BOUNDARY

TITLE:
SATELLITE MAPS

PROJECT:
Engineering Design & Construction Supervision, Punjab Rural Sustainable Water Supply & Sanitation Project, Cluster South-III

DATE:	02-03-26
DRAWN:	ASAD
DESGIN:	ENGR.FAIEZ
APPROVED:	ENGR. IHSAN UL HAQ

TITLE:
PRMSC-BWN-AA-SM-01

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

INFRASTRUCTURE CONSULTANT
ENVIRONMENTAL TECHNOLOGIES
ASIAN CONSULTING ENGINEERS
www.asiancon.com

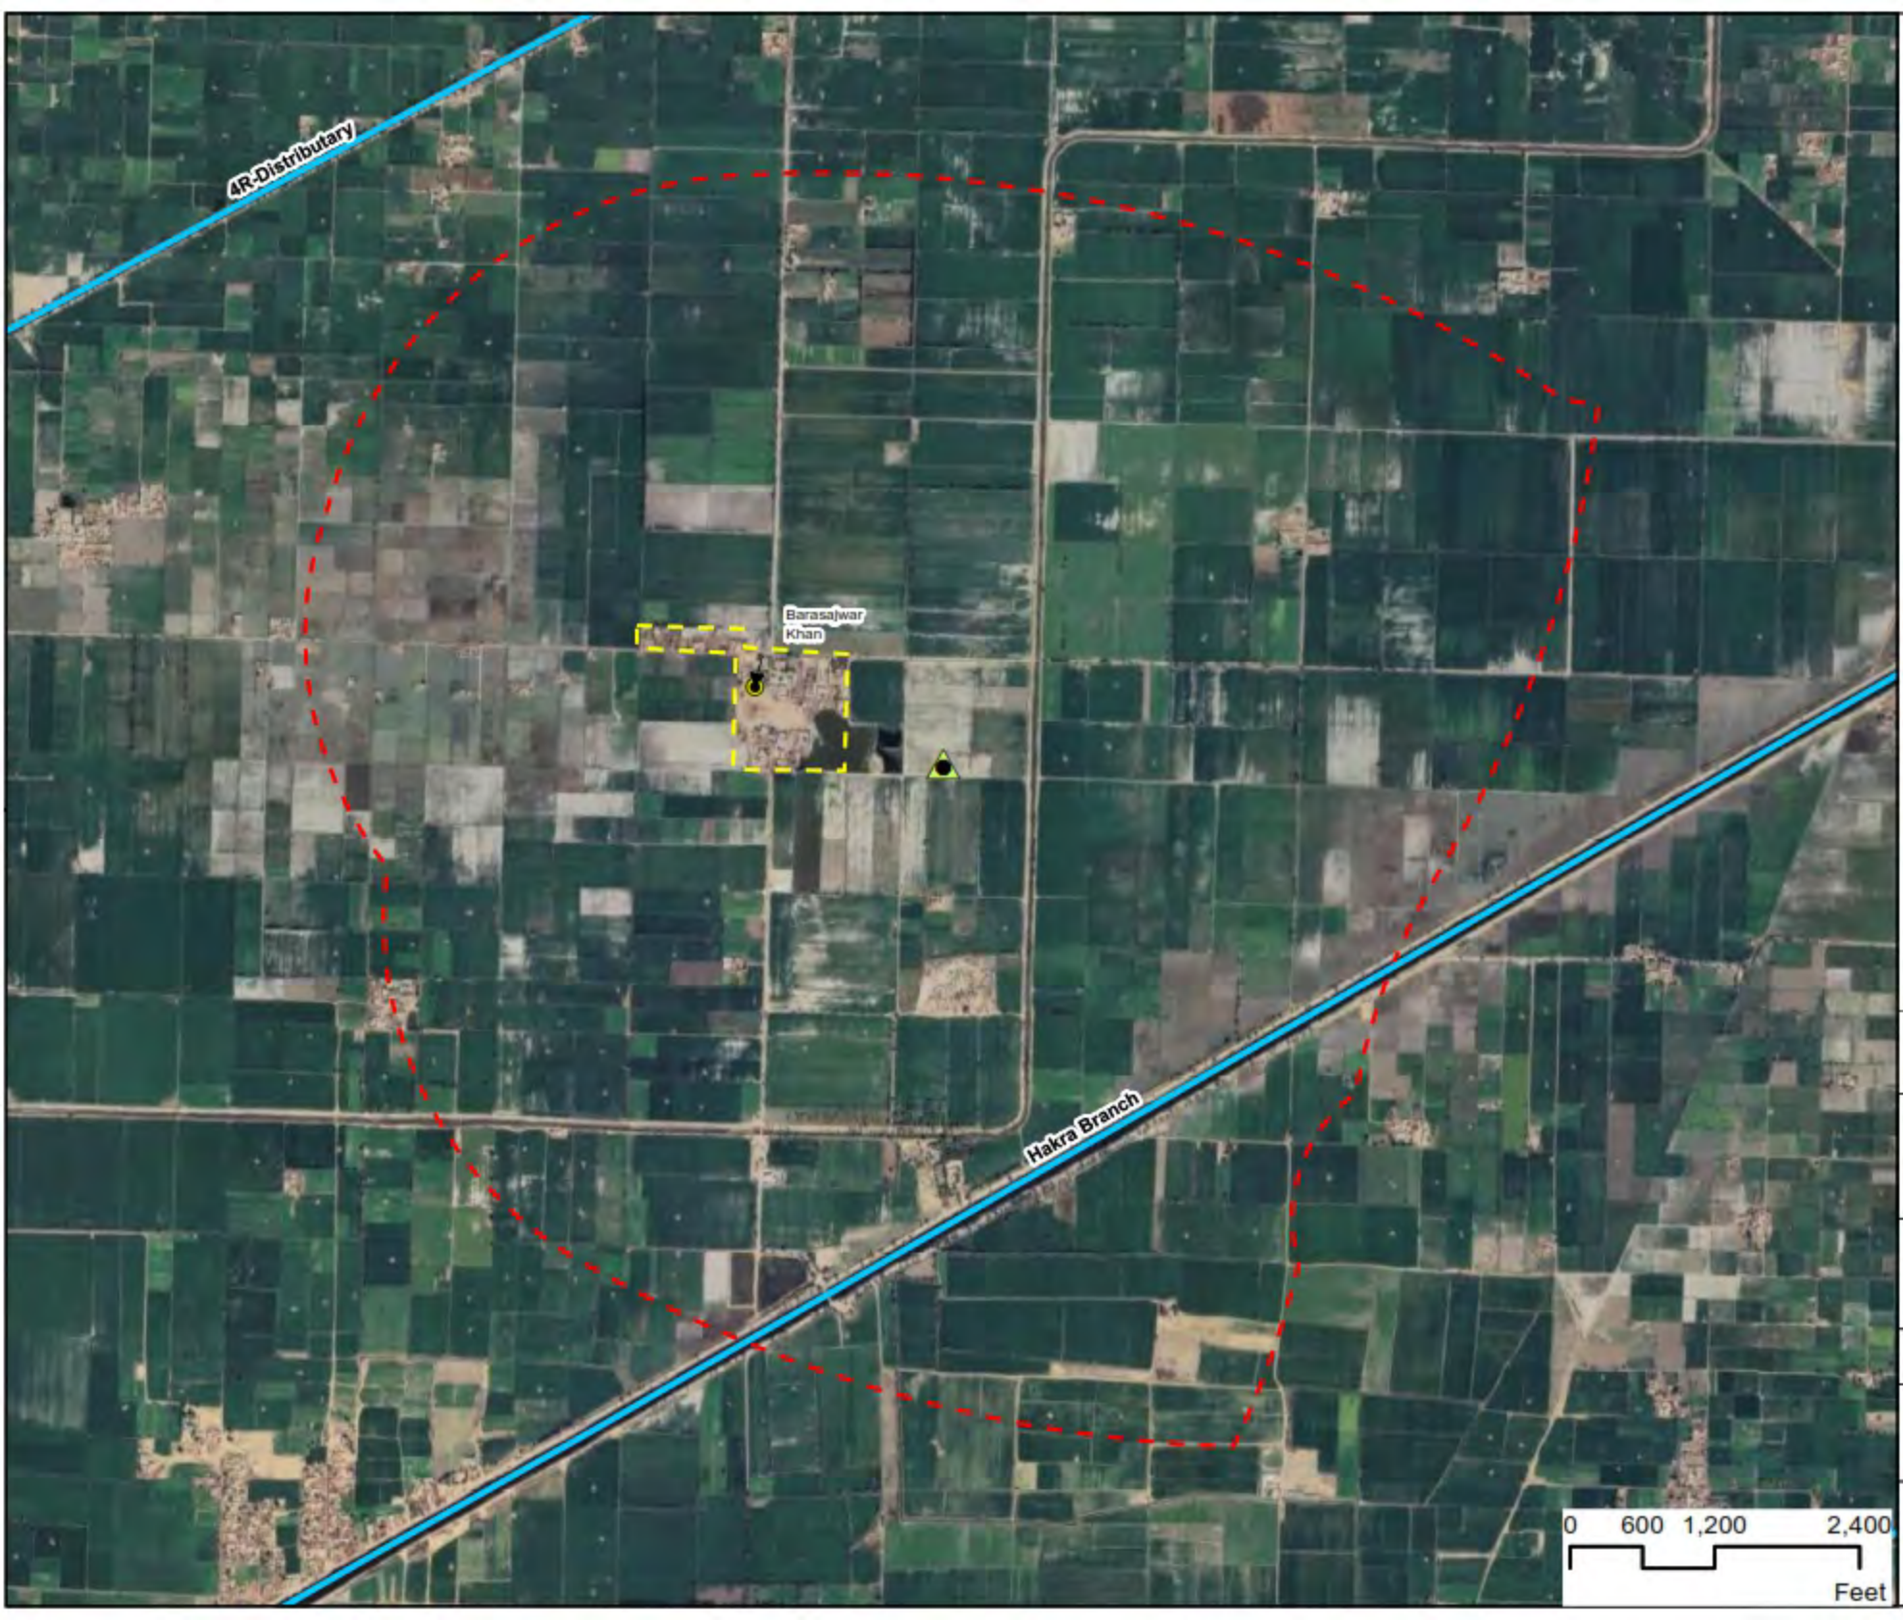

N
W E
S

TEHSIL BAHAWALNAGAR

MAUZA BARASAJWAR KHAN

LATITUDE: 29.636
LONGITUDE: 73.236

LEGEND

- CENTER
- MAJOR SETTELMENT
- CANAL
- SETTELMENT BOUNDARY
- PROJECT AREA BOUNDARY

TITLE:
SATELLITE MAPS

PROJECT:
Engineering Design & Construction Supervision, Punjab Rural Sustainable Water Supply & Sanitation Project, Cluster South-III

DATE:	02-03-26
DRAWN:	ASAD
DESGIN:	ENGR.FAIEZ
APPROVED:	ENGR. IHSAN UL HAQ

TITLE:
PRMSC-BWN-BK-SM-01

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

INFRASTRUCTURE CONSULTANT
ENVIRONMENTAL TECHNOLOGIES
ASIAN CONSULTING ENGINEERS
www.asiancon.com

N
W E
S

TEHSIL BAHAWALNAGAR

MAUZA CHAK ABDUL HAQ

LATITUDE: 29.89
LONGITUDE: 73.378

LEGEND

- CENTER
- MAJOR SETTELMENT
- CANAL
- SETTELMENT BOUNDARY
- PROJECT AREA BOUNDARY

TITLE:
SATELLITE MAPS

PROJECT:
Engineering Design & Construction Supervision, Punjab Rural Sustainable Water Supply & Sanitation Project, Cluster South-III

DATE:	02-03-26
DRAWN:	ASAD
DESGIN:	ENGR.FAIEZ
APPROVED:	ENGR. IHSAN UL HAQ

TITLE:
PRMSC-BWN-CAH-SM-01

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

INFRASTRUCTURE CONSULTANT
ENVIRONMENTAL TECHNOLOGIES
ASIAN CONSULTING ENGINEERS
www.asiancon.com

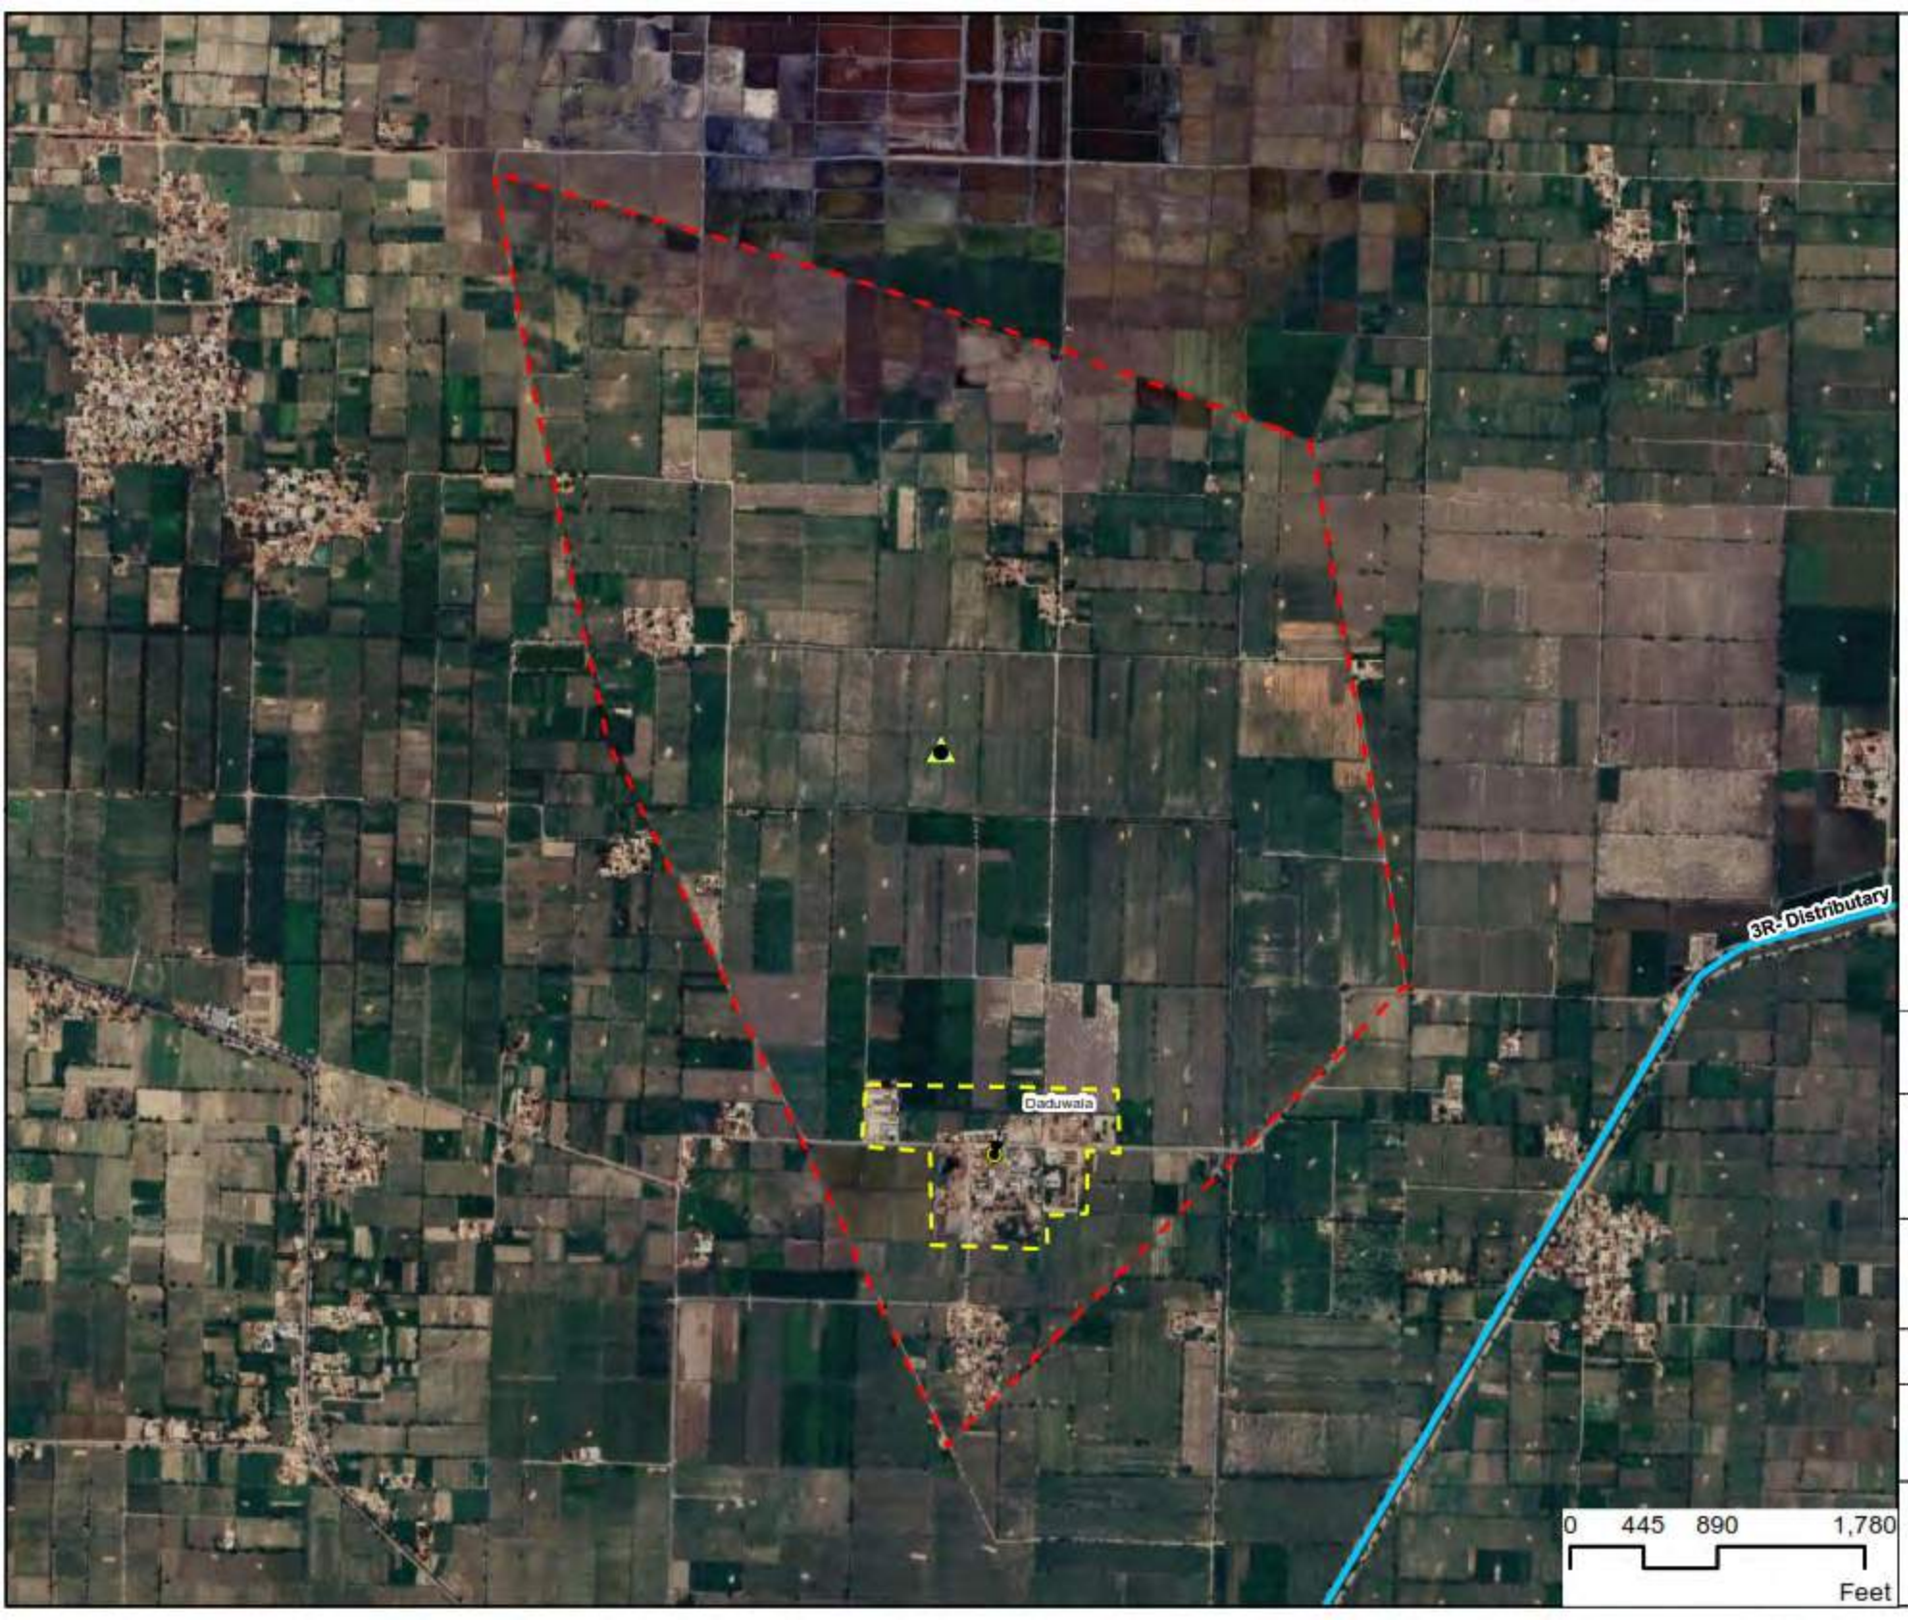

N
W E
S

TEHSIL BAHAWALNAGAR

MAUZA DADOO MAMMUNKA

LATITUDE: 29.689
LONGITUDE: 73.137

LEGEND

- CENTER
- MAJOR SETTELMENT
- CANAL
- SETTELMENT BOUNDARY
- PROJECT AREA BOUNDARY

TITLE:
SATELLITE MAPS

PROJECT:
Engineering Design & Construction Supervision, Punjab Rural Sustainable Water Supply & Sanitation Project, Cluster South-III

DATE:	02-03-26
DRAWN:	ASAD
DESGIN:	ENGR.FAIEZ
APPROVED:	ENGR. IHSAN UL HAQ

TITLE:
PRMSC-BWN-DM-SM-01

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

INFRASTRUCTURE CONSULTANT
ENVIRONMENTAL TECHNOLOGIES
ASIAN CONSULTING ENGINEERS
www.asiancon.com

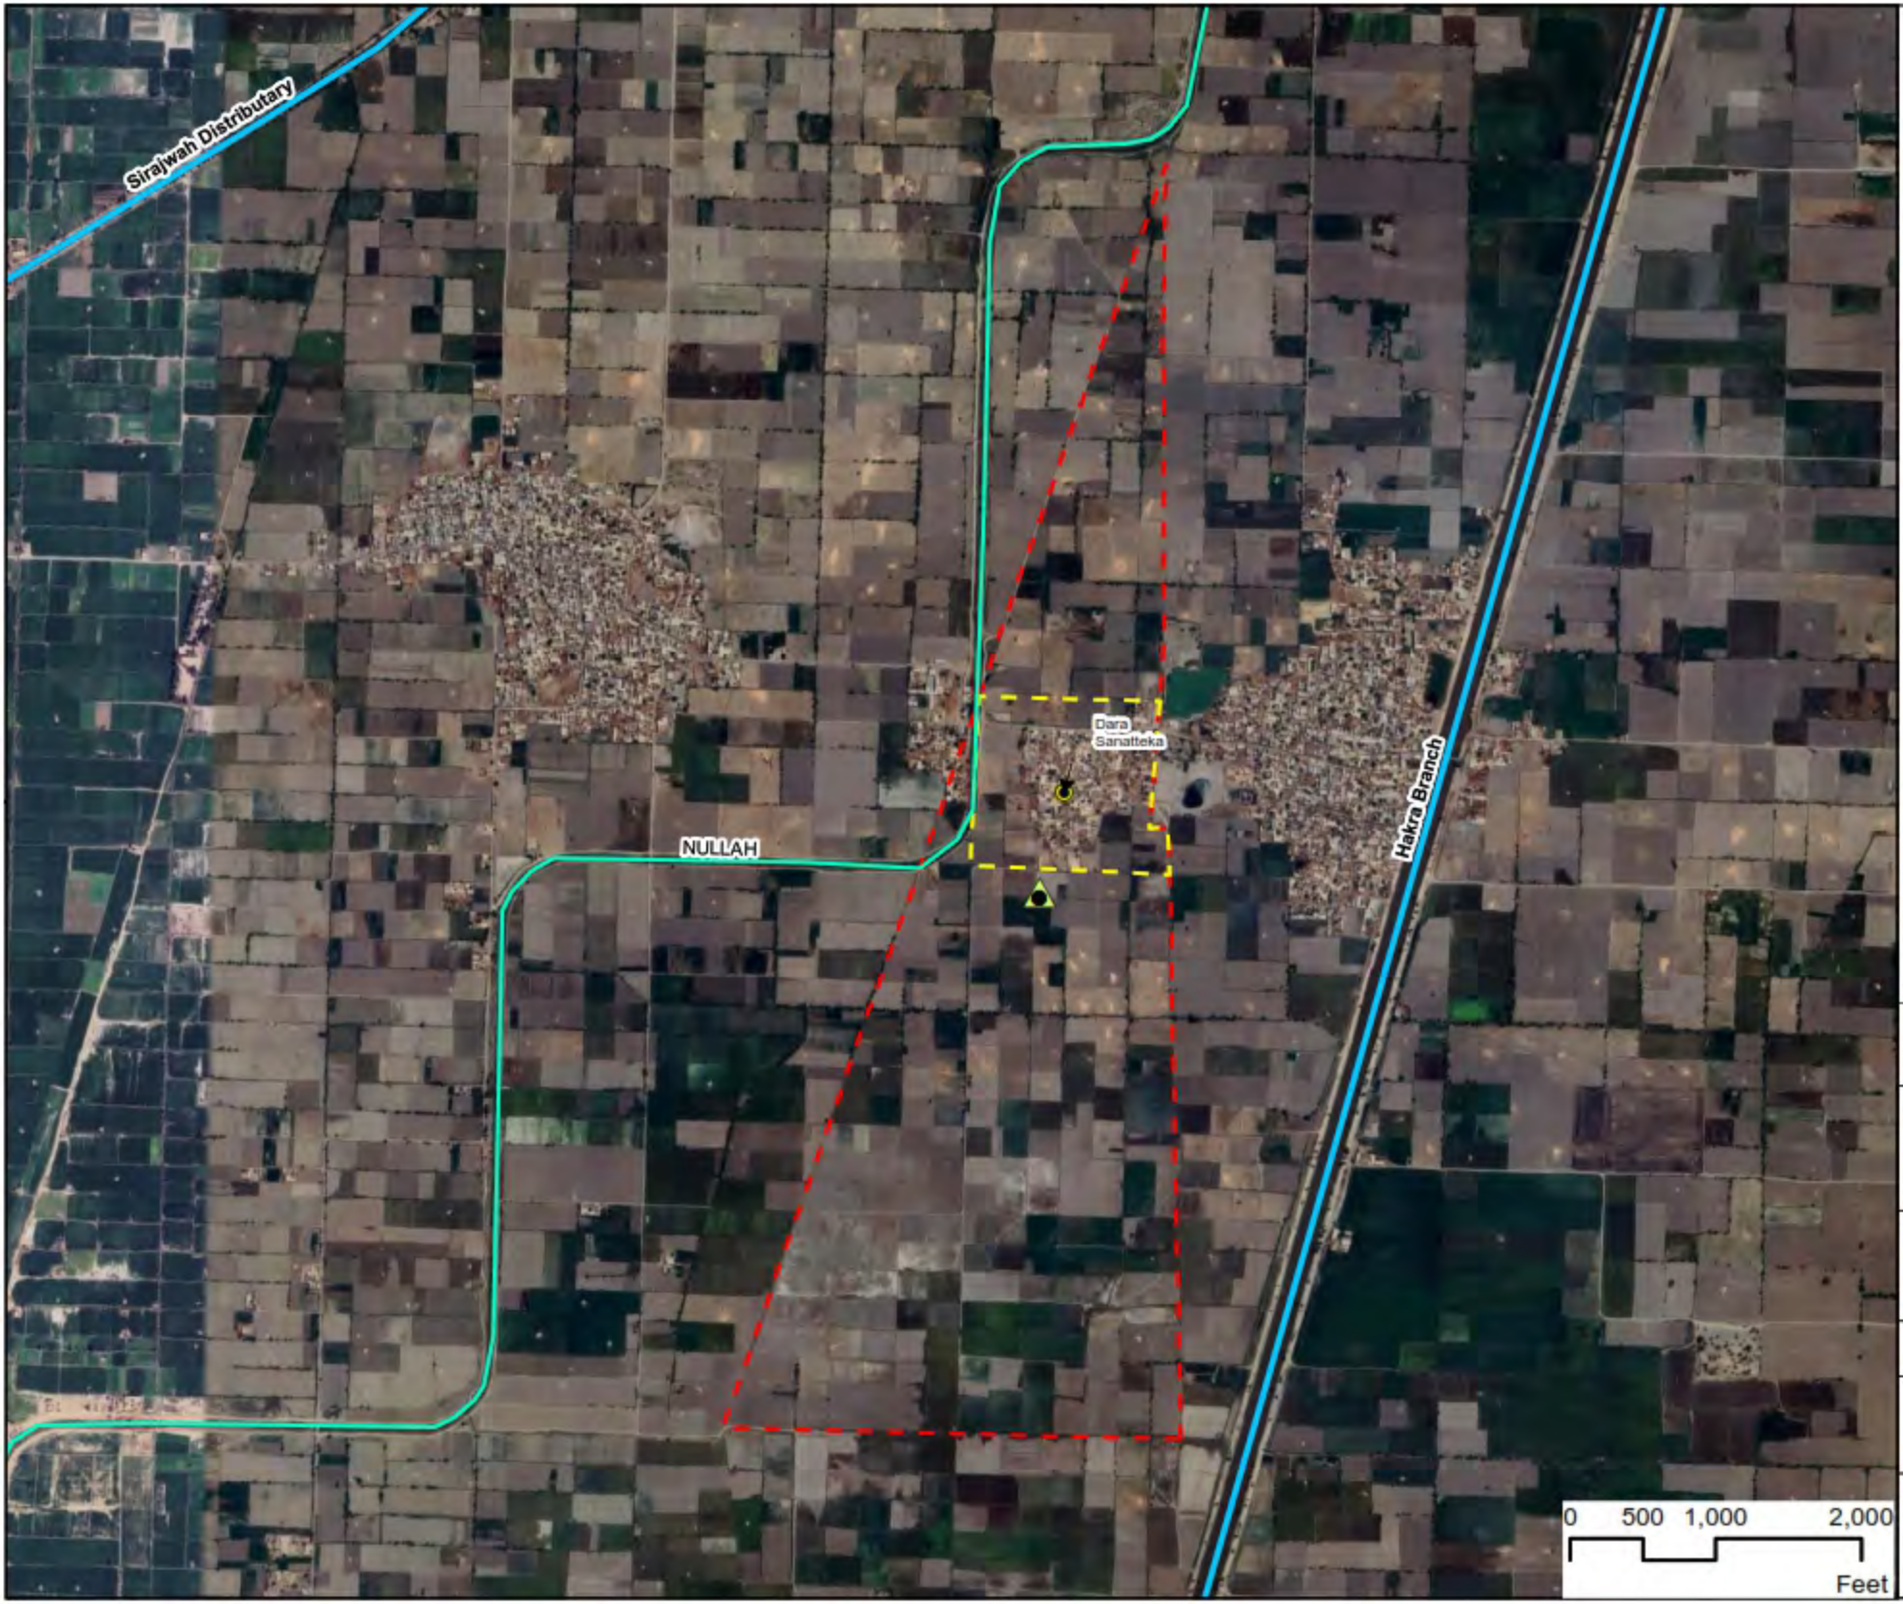

N
W E
S

TEHSIL BAHAWALNAGAR

MAUZA DARA SANATTEKA

LATITUDE: 29.818
LONGITUDE: 73.326

LEGEND

- CENTER
- MAJOR SETTELMENT
- NULLAH
- CANAL
- SETTELMENT BOUNDARY
- PROJECT AREA BOUNDARY

TITLE:
SATELLITE MAPS

PROJECT:
Engineering Design & Construction Supervision, Punjab Rural Sustainable Water Supply & Sanitation Project, Cluster South-III

DATE:	02-03-26
DRAWN:	ASAD
DESGIN:	ENGR.FAIEZ
APPROVED:	ENGR. IHSAN UL HAQ

TITLE:
PRMSC-BWN-DS-SM-01

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

INFRASTRUCTURE CONSULTANT
ENVIRONMENTAL TECHNOLOGIES
ASIAN CONSULTING ENGINEERS
www.asiancon.com

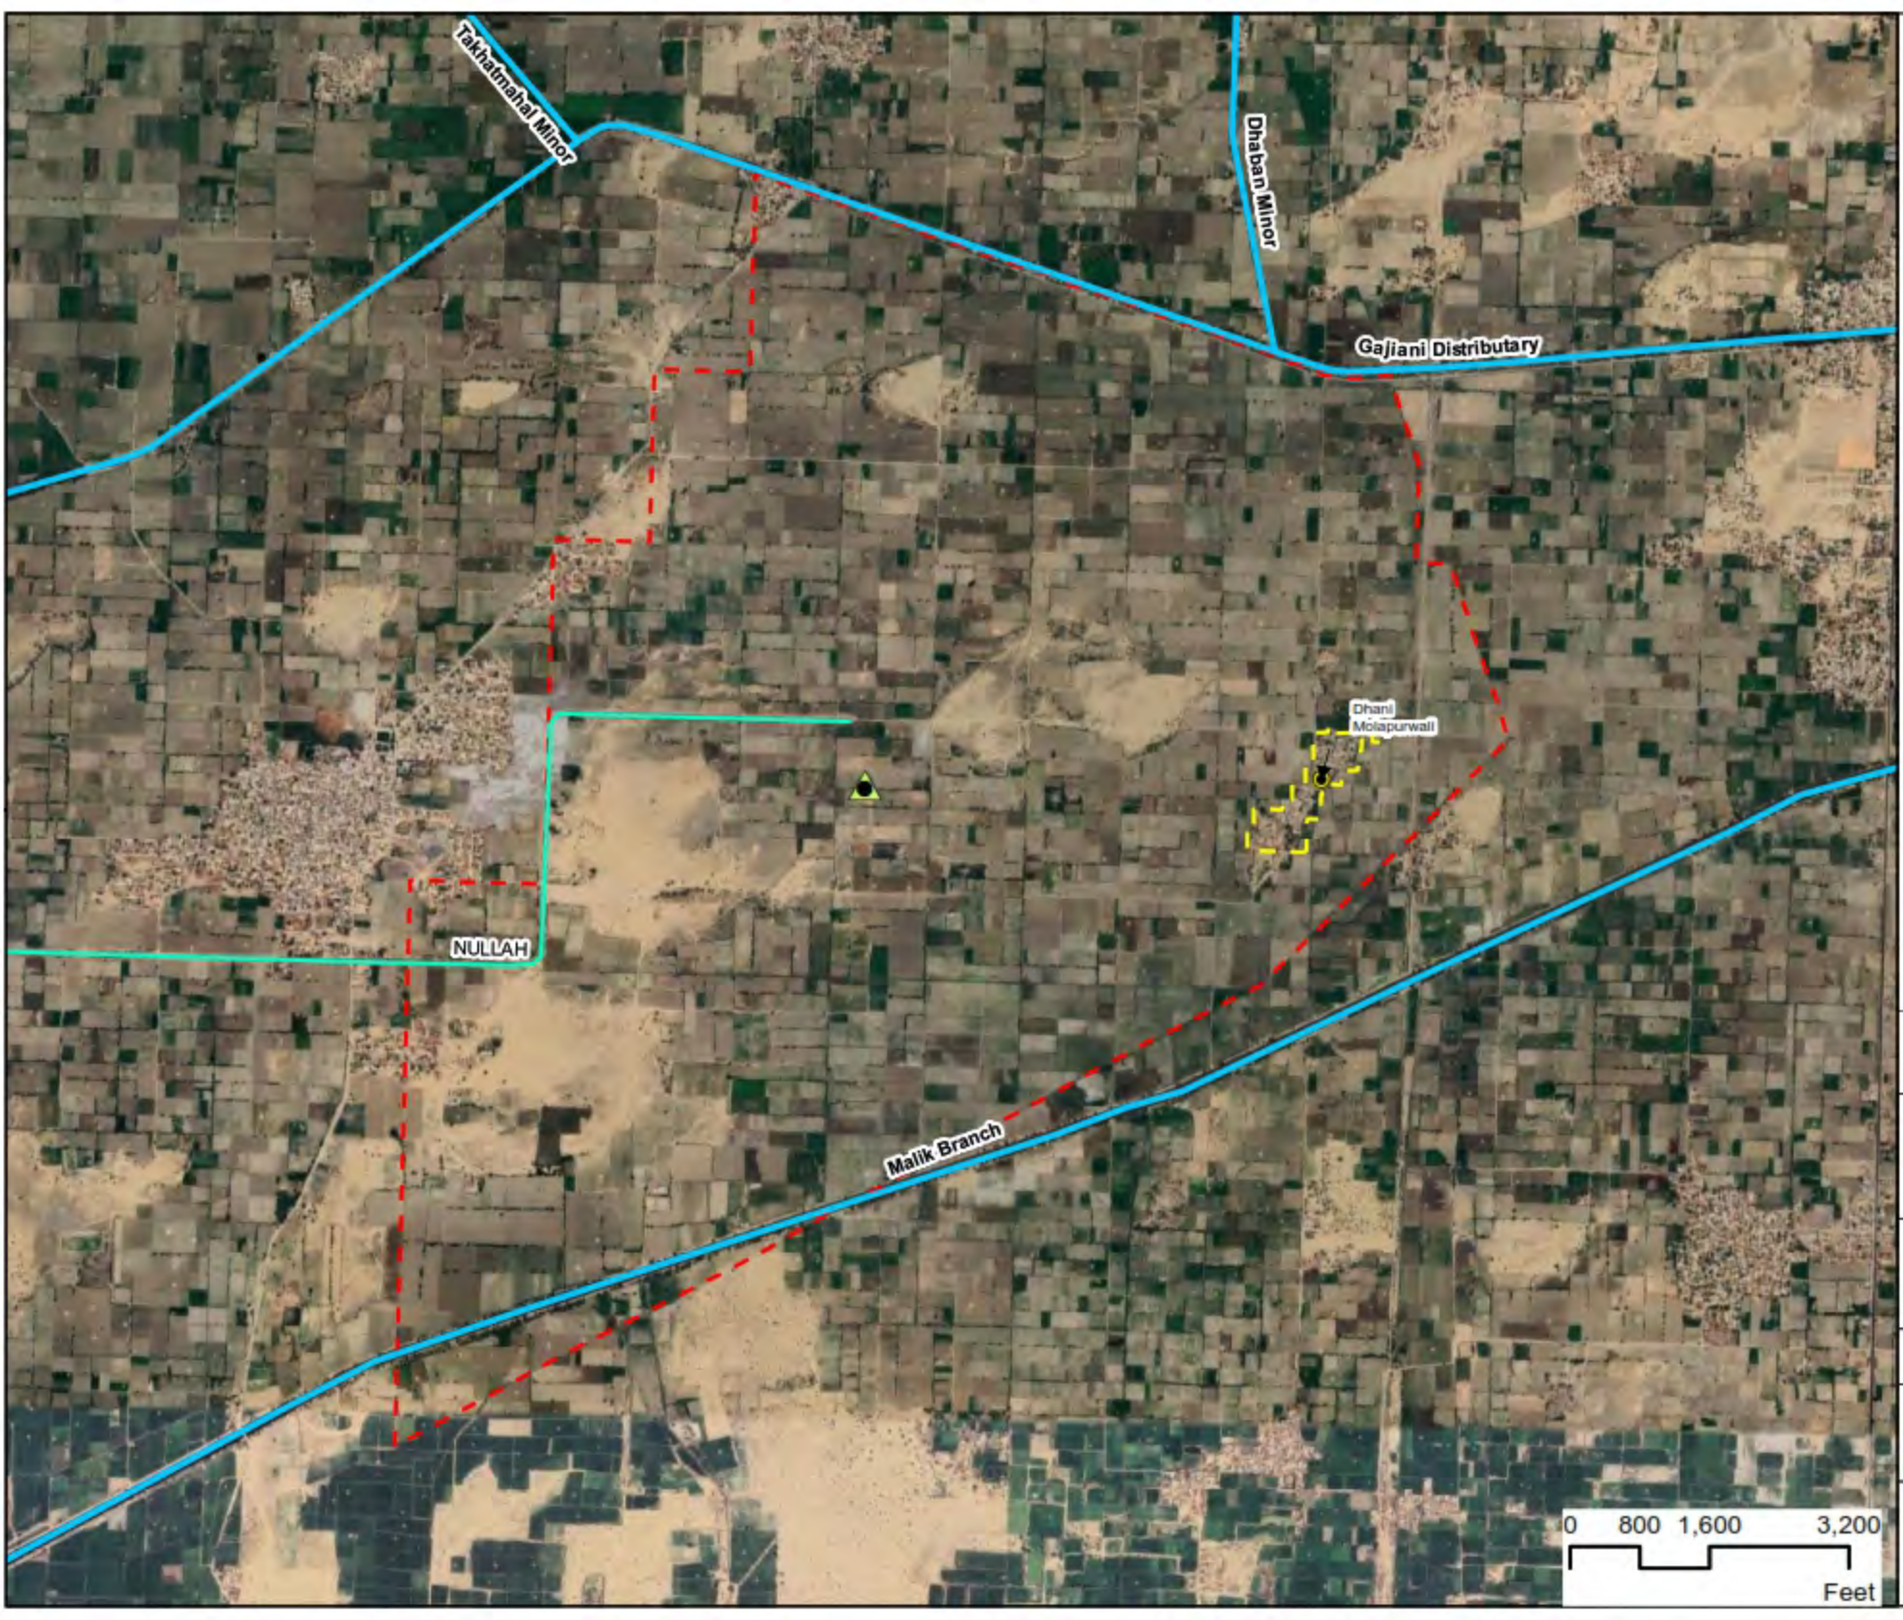

TEHSIL BAHAWALNAGAR

MAUZA DHANRAJ PURA

LATITUDE: 29.839
LONGITUDE: 73.198

LEGEND

- CENTER
- MAJOR SETTELMENT
- NULLAH
- CANAL
- SETTELMENT BOUNDARY
- PROJECT AREA BOUNDARY

TITLE:
SATELLITE MAPS

PROJECT:
Engineering Design & Construction Supervision, Punjab Rural Sustainable Water Supply & Sanitation Project, Cluster South-III

DATE:	02-03-26
DRAWN:	ASAD
DESGIN:	ENGR.FAIEZ
APPROVED:	ENGR. IHSAN UL HAQ

TITLE:
PRMSC-BWN-DHP-SM-01

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

INFRASTRUCTURE CONSULTANT
ENVIRONMENTAL TECHNOLOGIES
ASIAN CONSULTING ENGINEERS
www.asiancon.com

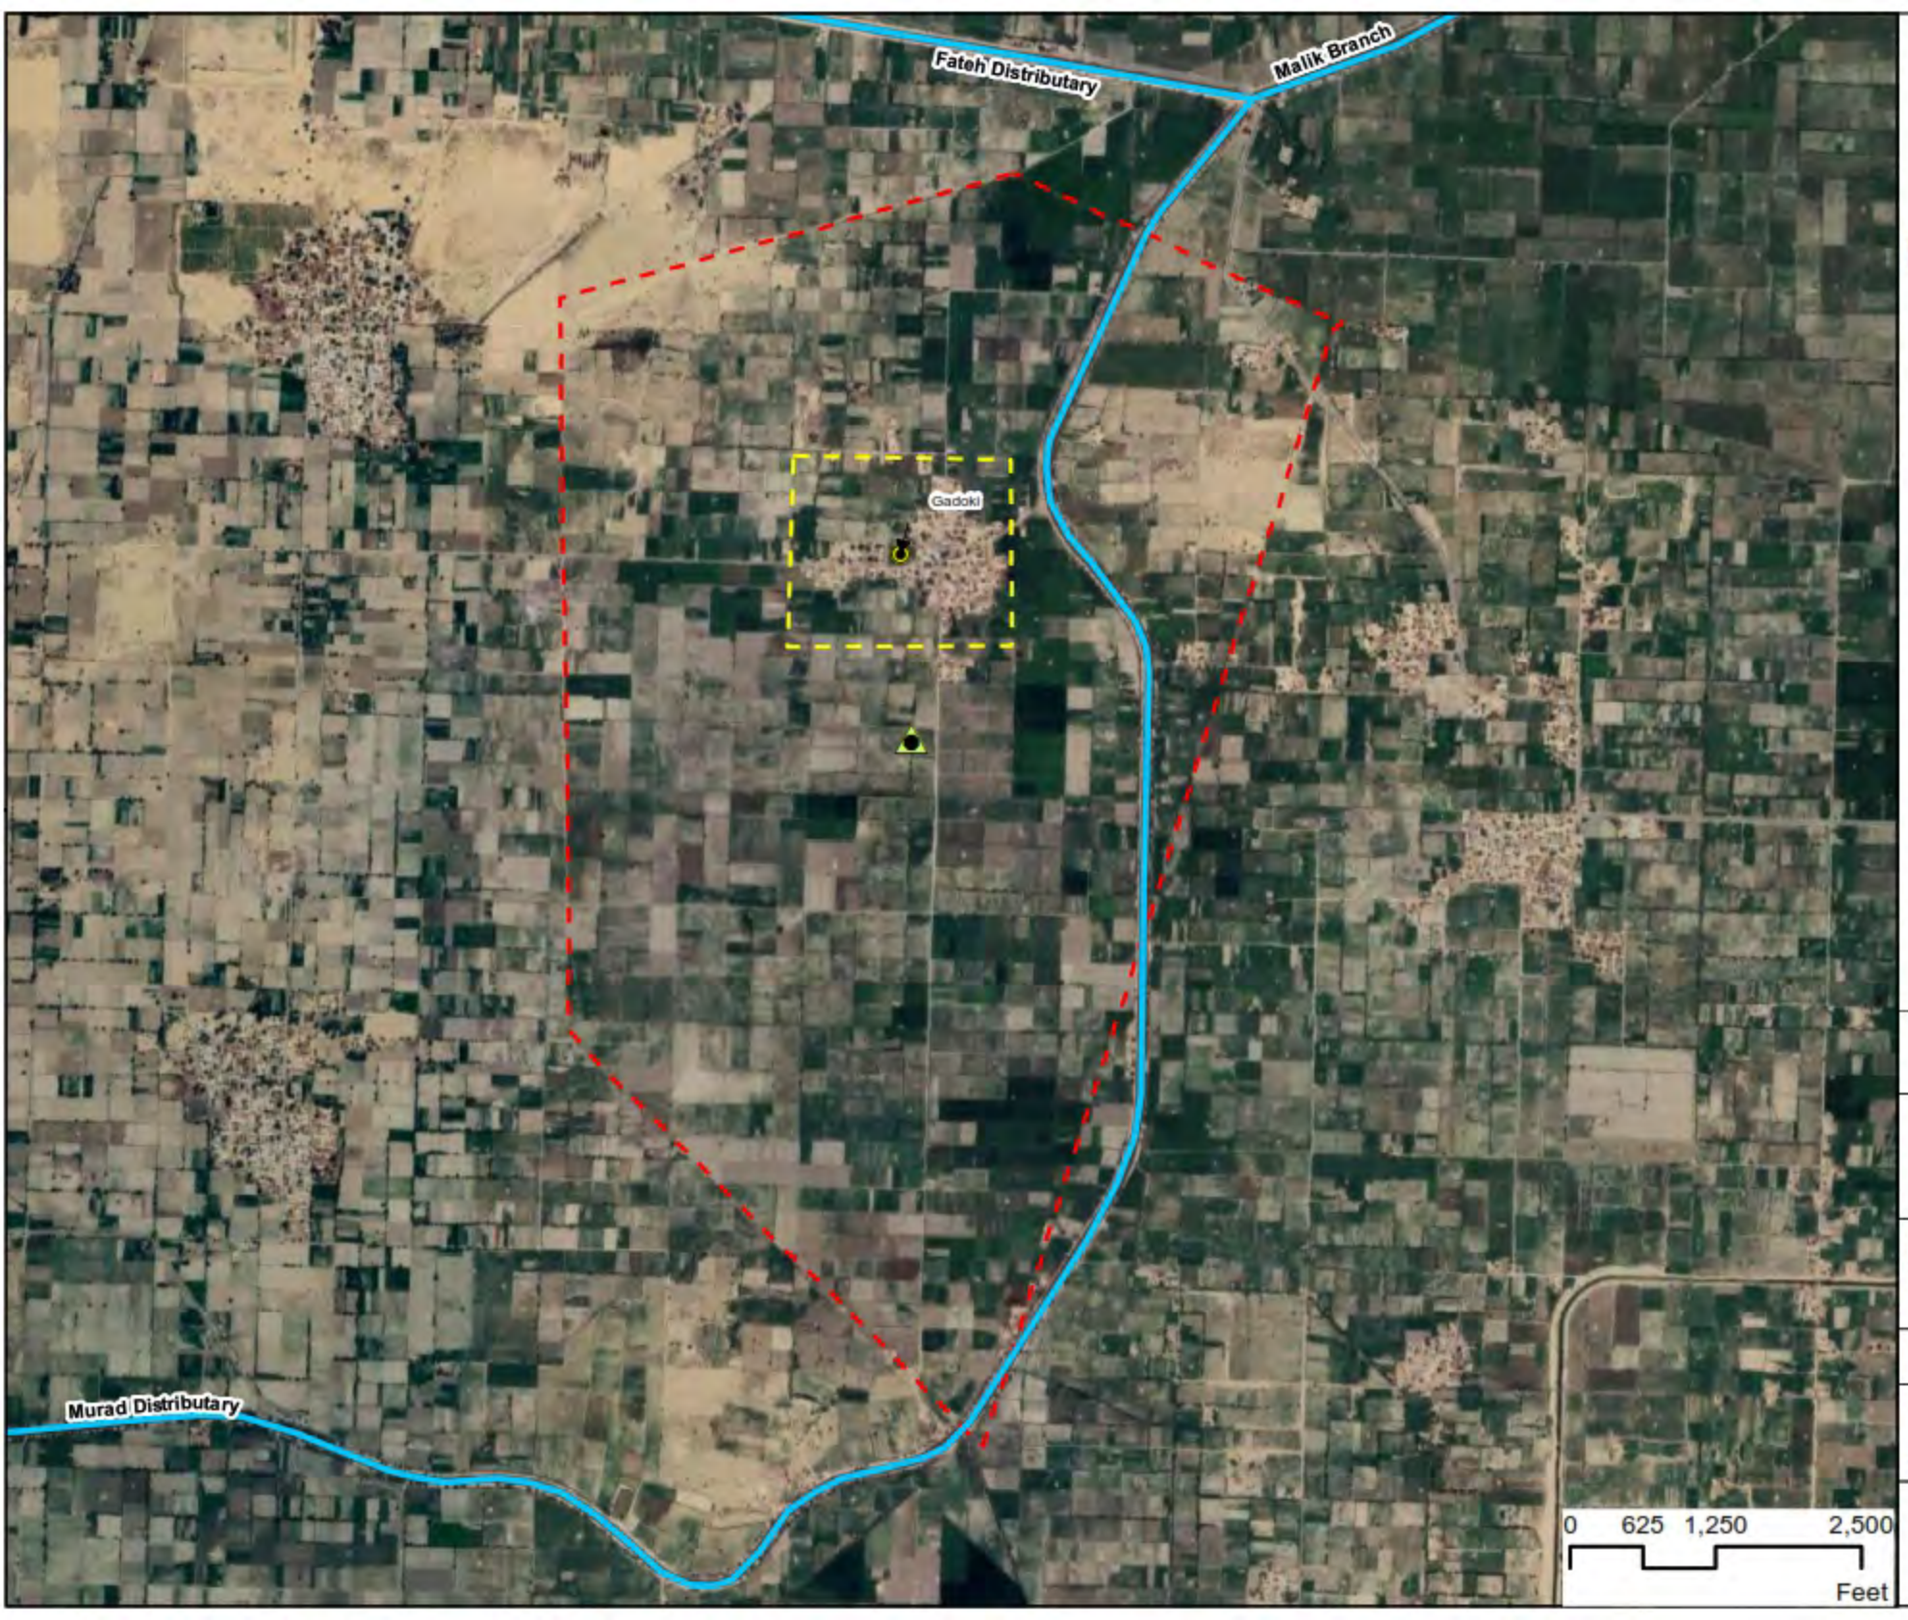

N
W E
S

TEHSIL BAHAWALNAGAR

MAUZA HASAN RAIKA

LATITUDE: 29.739
LONGITUDE: 73.056

LEGEND

- CENTER
- MAJOR SETTELMENT
- CANAL
- SETTELMENT BOUNDARY
- PROJECT AREA BOUNDARY

TITLE:
SATELLITE MAPS

PROJECT:
Engineering Design & Construction Supervision, Punjab Rural Sustainable Water Supply & Sanitation Project, Cluster South-III

DATE:	02-03-26
DRAWN:	ASAD
DESGIN:	ENGR.FAIEZ
APPROVED:	ENGR. IHSAN UL HAQ

TITLE:
PRMSC-BWN-HR-SM-01

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

INFRASTRUCTURE CONSULTANT
ENVIRONMENTAL TECHNOLOGIES
ASIAN CONSULTING ENGINEERS
www.asiancon.com

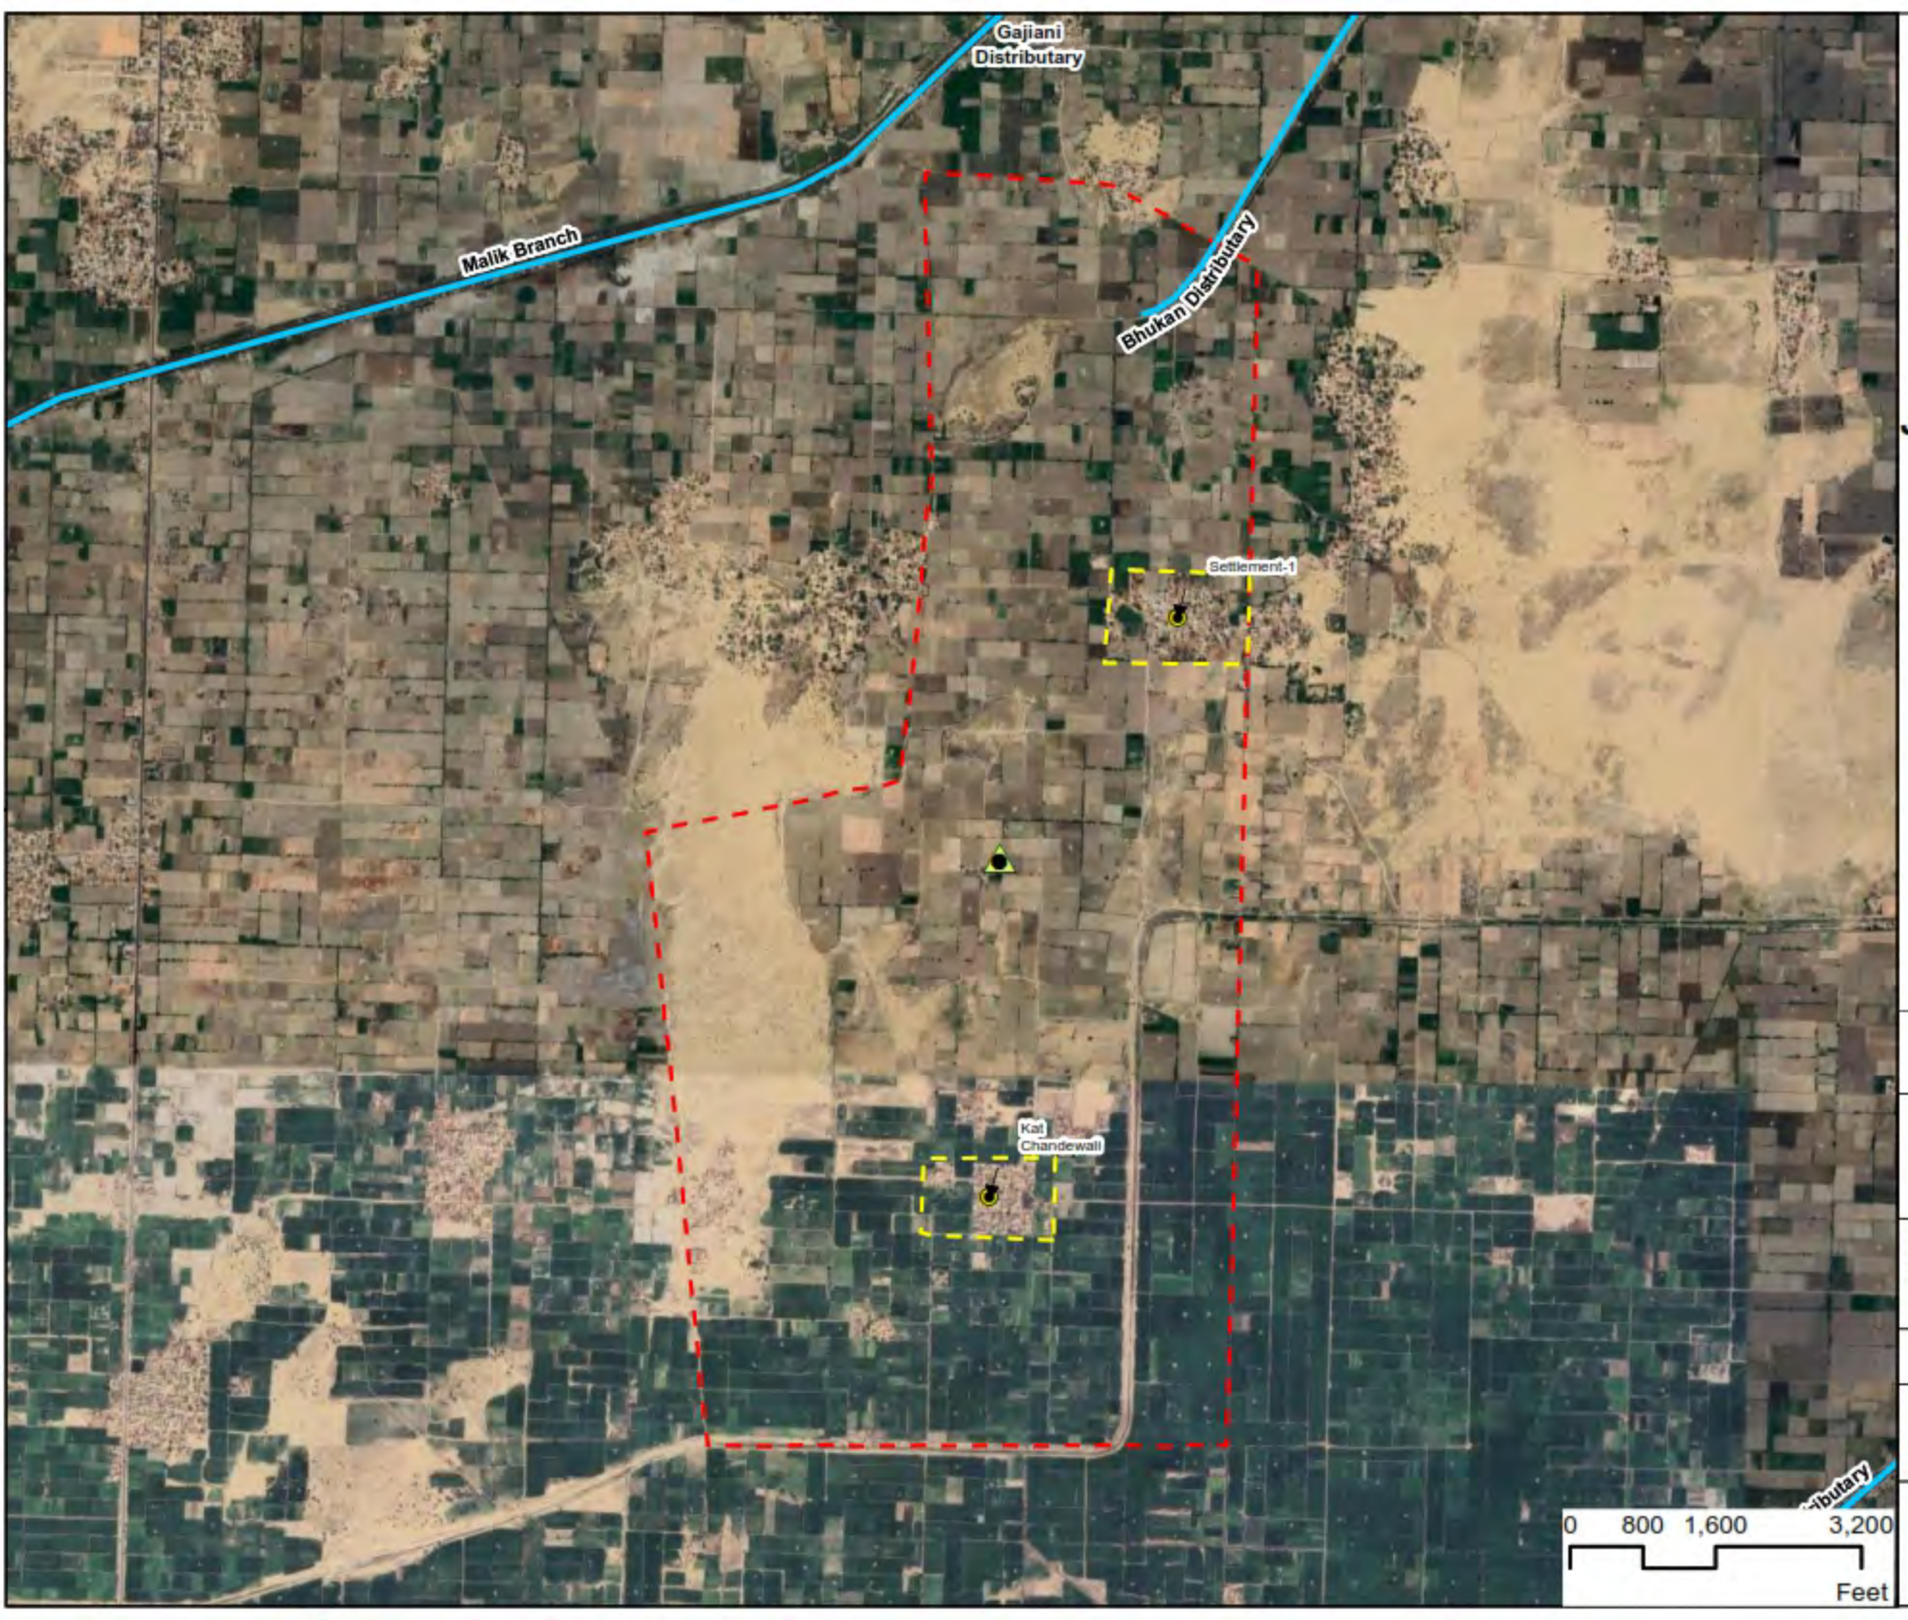

N
W E
S

TEHSIL BAHAWALNAGAR

MAUZA JAGGA SANETTEKA

LATITUDE: 29.857
LONGITUDE: 73.279

LEGEND

- CENTER
- MAJOR SETTELMENT
- CANAL
- SETTELMENT BOUNDARY
- PROJECT AREA BOUNDARY

TITLE:
SATELLITE MAPS

PROJECT:
Engineering Design & Construction Supervision, Punjab Rural Sustainable Water Supply & Sanitation Project, Cluster South-III

DATE:	02-03-26
DRAWN:	ASAD
DESGIN:	ENGR.FAIEZ
APPROVED:	ENGR. IHSAN UL HAQ

TITLE:
PRMSC-BWN-JS-SM-01

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

INFRASTRUCTURE CONSULTANT
ENVIRONMENTAL TECHNOLOGIES
ASIAN CONSULTING ENGINEERS
www.asiancon.com

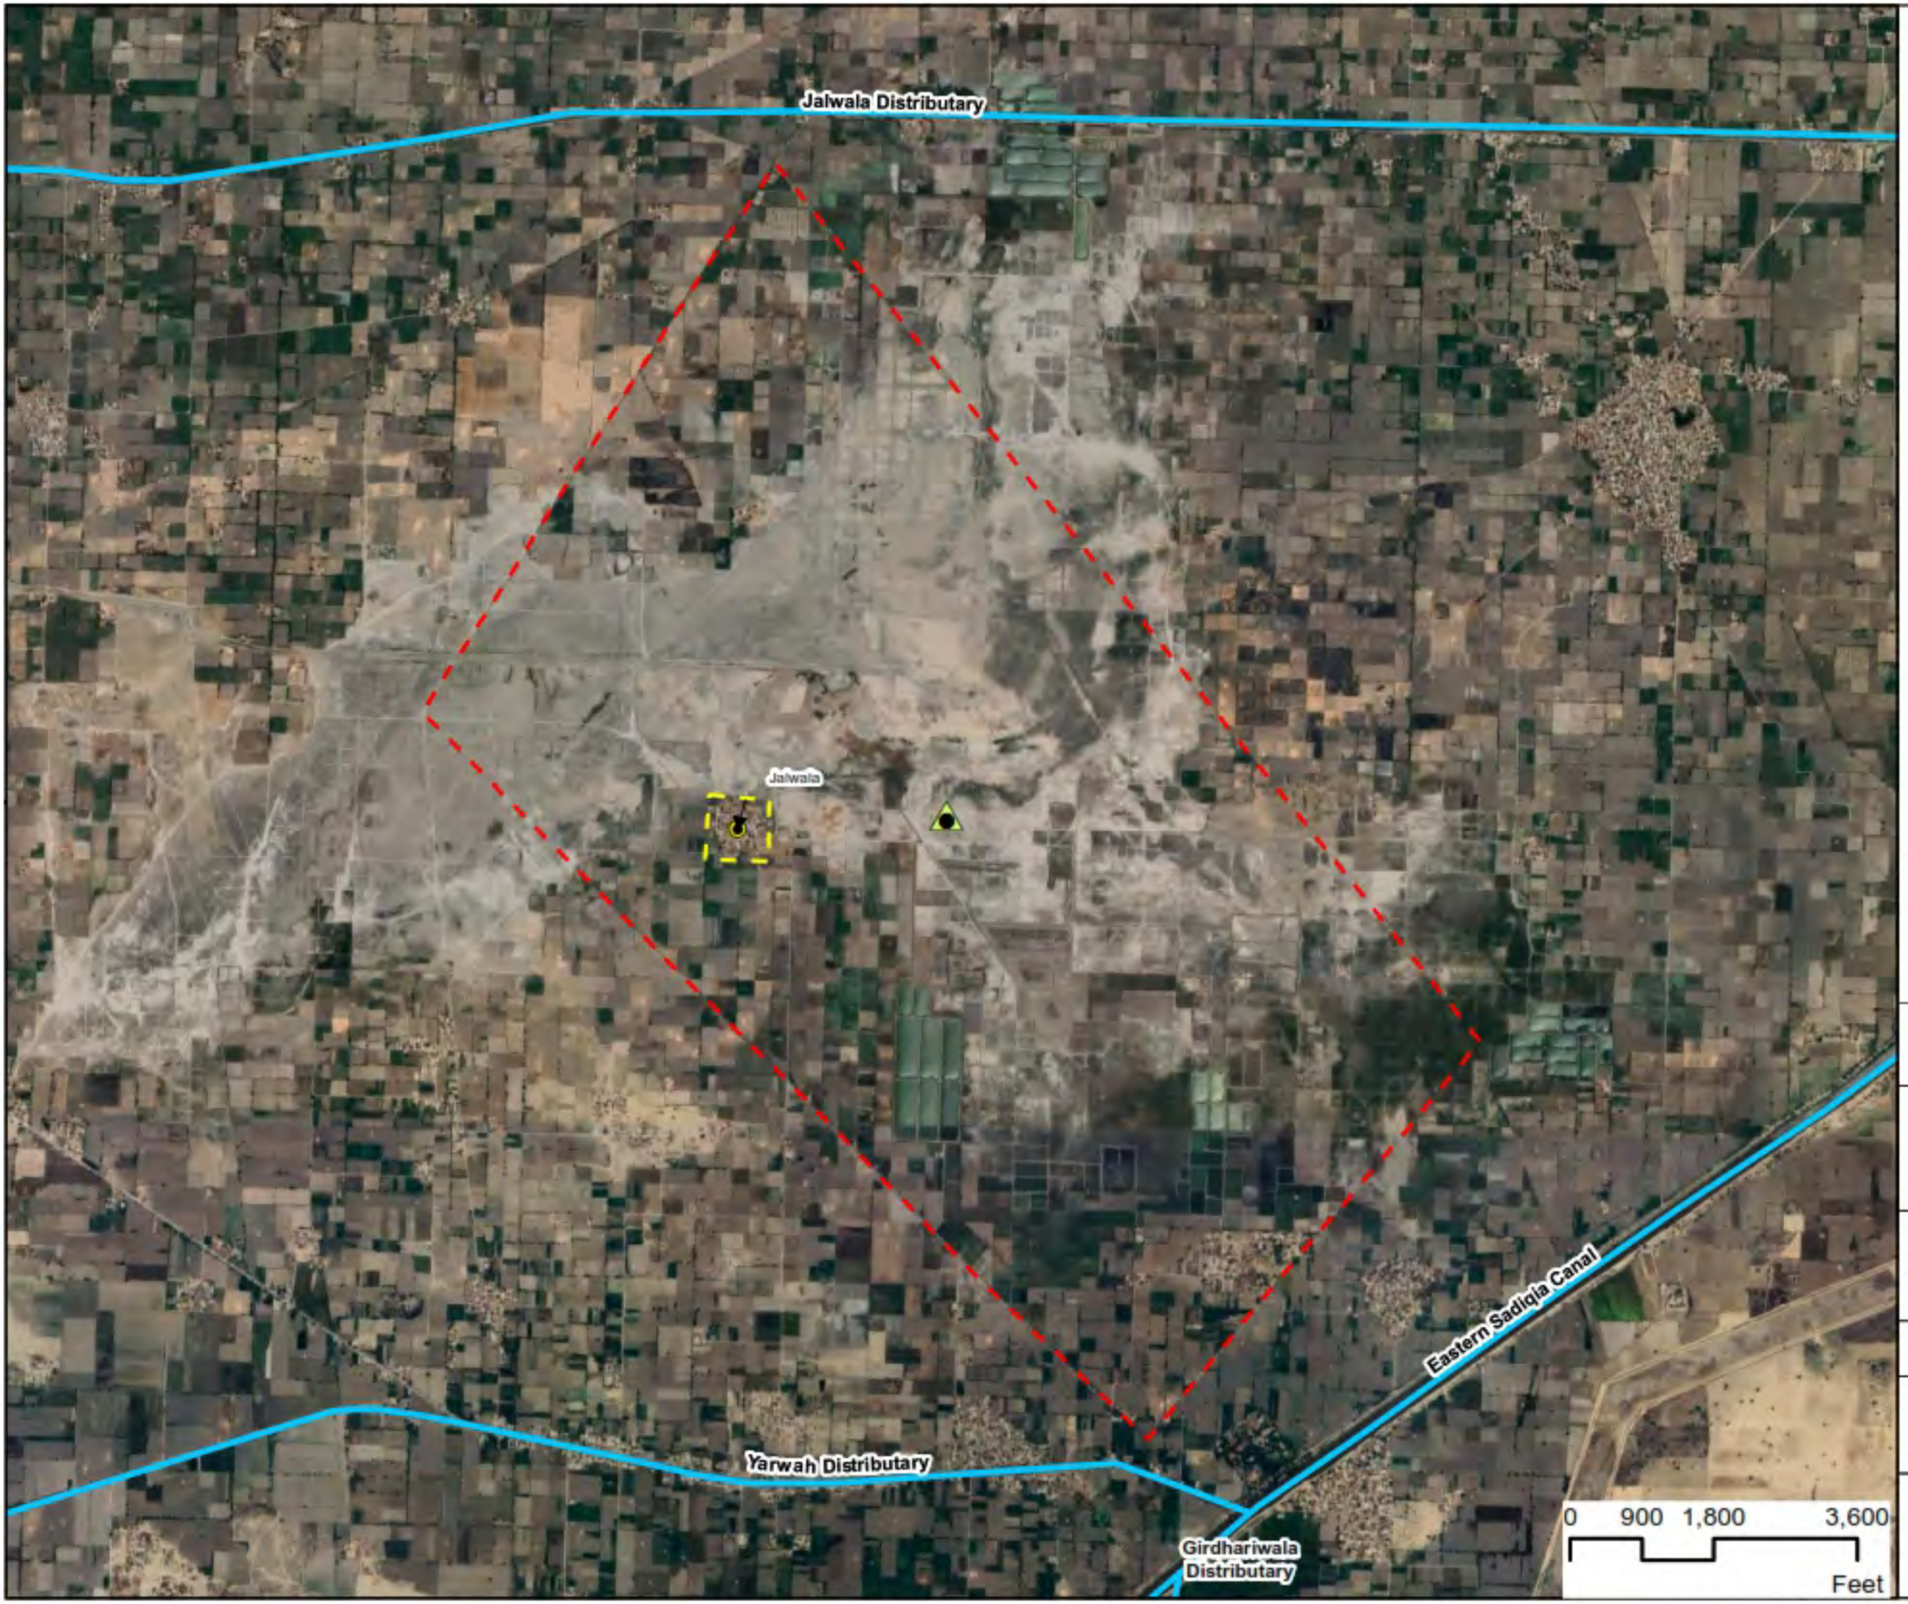

N
W E
S

TEHSIL BAHAWALNAGAR

MAUZA JALWALA

LATITUDE: 29.944
LONGITUDE: 73.378

LEGEND

- CENTER
- MAJOR SETTELMENT
- CANAL
- SETTELMENT BOUNDARY
- PROJECT AREA BOUNDARY

TITLE:
SATELLITE MAPS

PROJECT:
Engineering Design & Construction Supervision, Punjab Rural Sustainable Water Supply & Sanitation Project, Cluster South-III

DATE:	02-03-26
DRAWN:	ASAD
DESGIN:	ENGR.FAIEZ
APPROVED:	ENGR. IHSAN UL HAQ

TITLE:
PRMSC-BWN-J-SM-01

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

INFRASTRUCTURE CONSULTANT
ENVIRONMENTAL TECHNOLOGIES
ASIAN CONSULTING ENGINEERS
www.asiancon.com

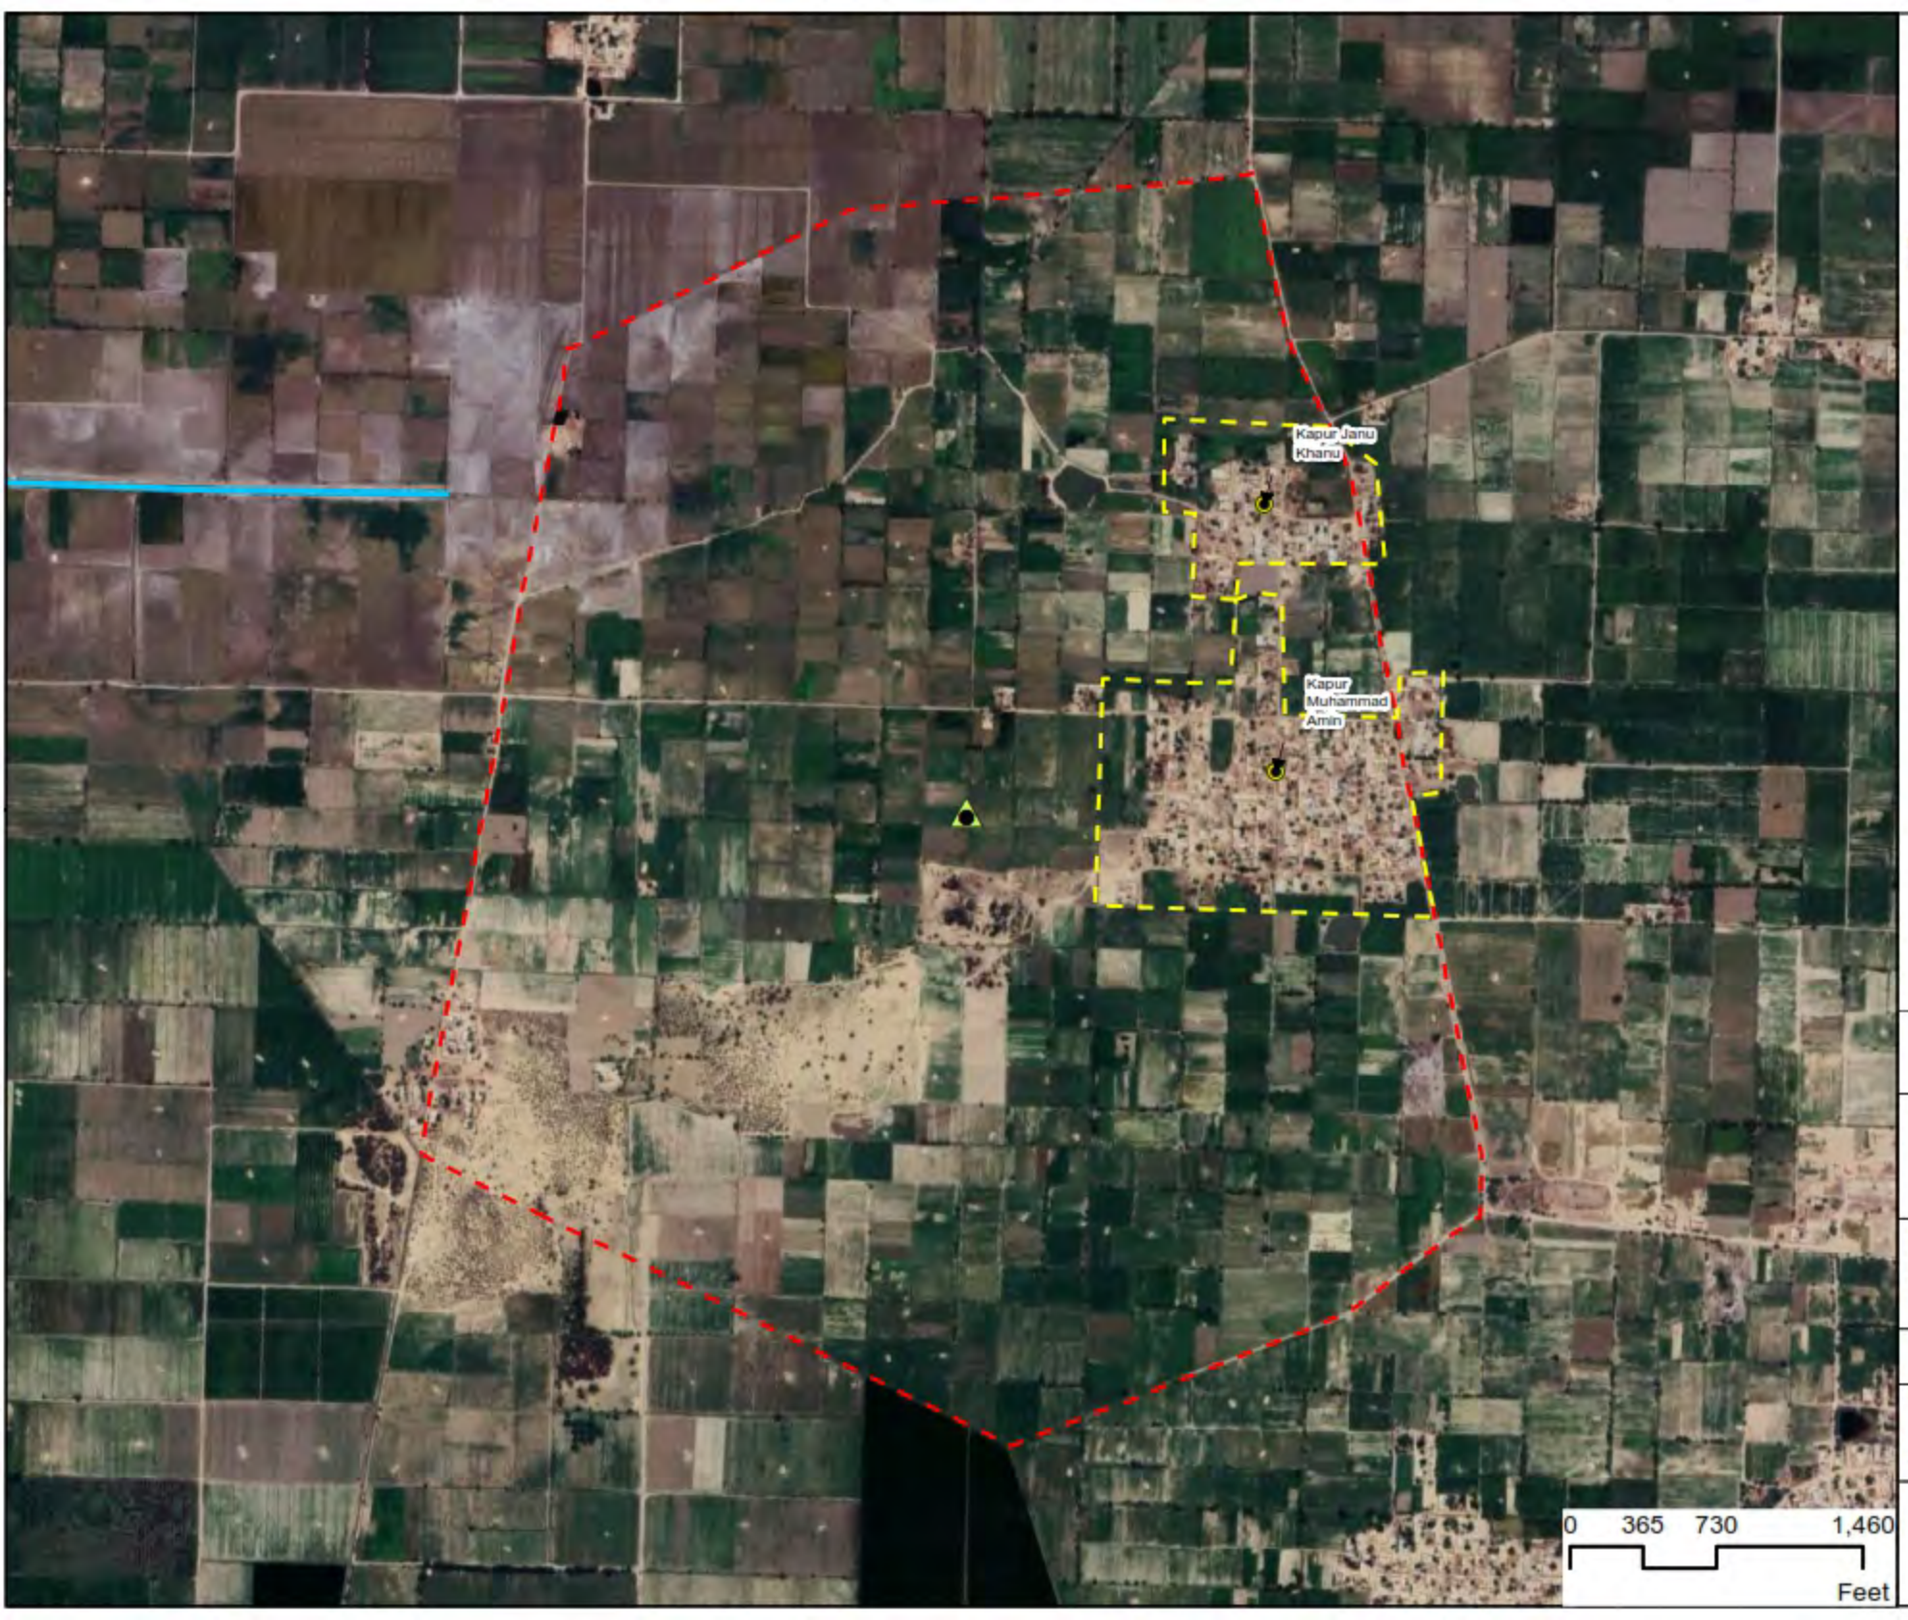

N
W E
S

TEHSIL BAHAWALNAGAR

MAUZA JANOOWALA

LATITUDE: 29.892
LONGITUDE: 73.155

LEGEND

- CENTER
- MAJOR SETTELMENT
- CANAL
- SETTELMENT BOUNDARY
- PROJECT AREA BOUNDARY

TITLE:
SATELLITE MAPS

PROJECT:
Engineering Design & Construction Supervision, Punjab Rural Sustainable Water Supply & Sanitation Project, Cluster South-III

DATE:	02-03-26
DRAWN:	ASAD
DESGIN:	ENGR.FAIEZ
APPROVED:	ENGR. IHSAN UL HAQ

TITLE:
PRMSC-BWN-J-SM-01

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

INFRASTRUCTURE CONSULTANT
ENVIRONMENTAL TECHNOLOGIES
ASIAN CONSULTING ENGINEERS
www.asiancon.com

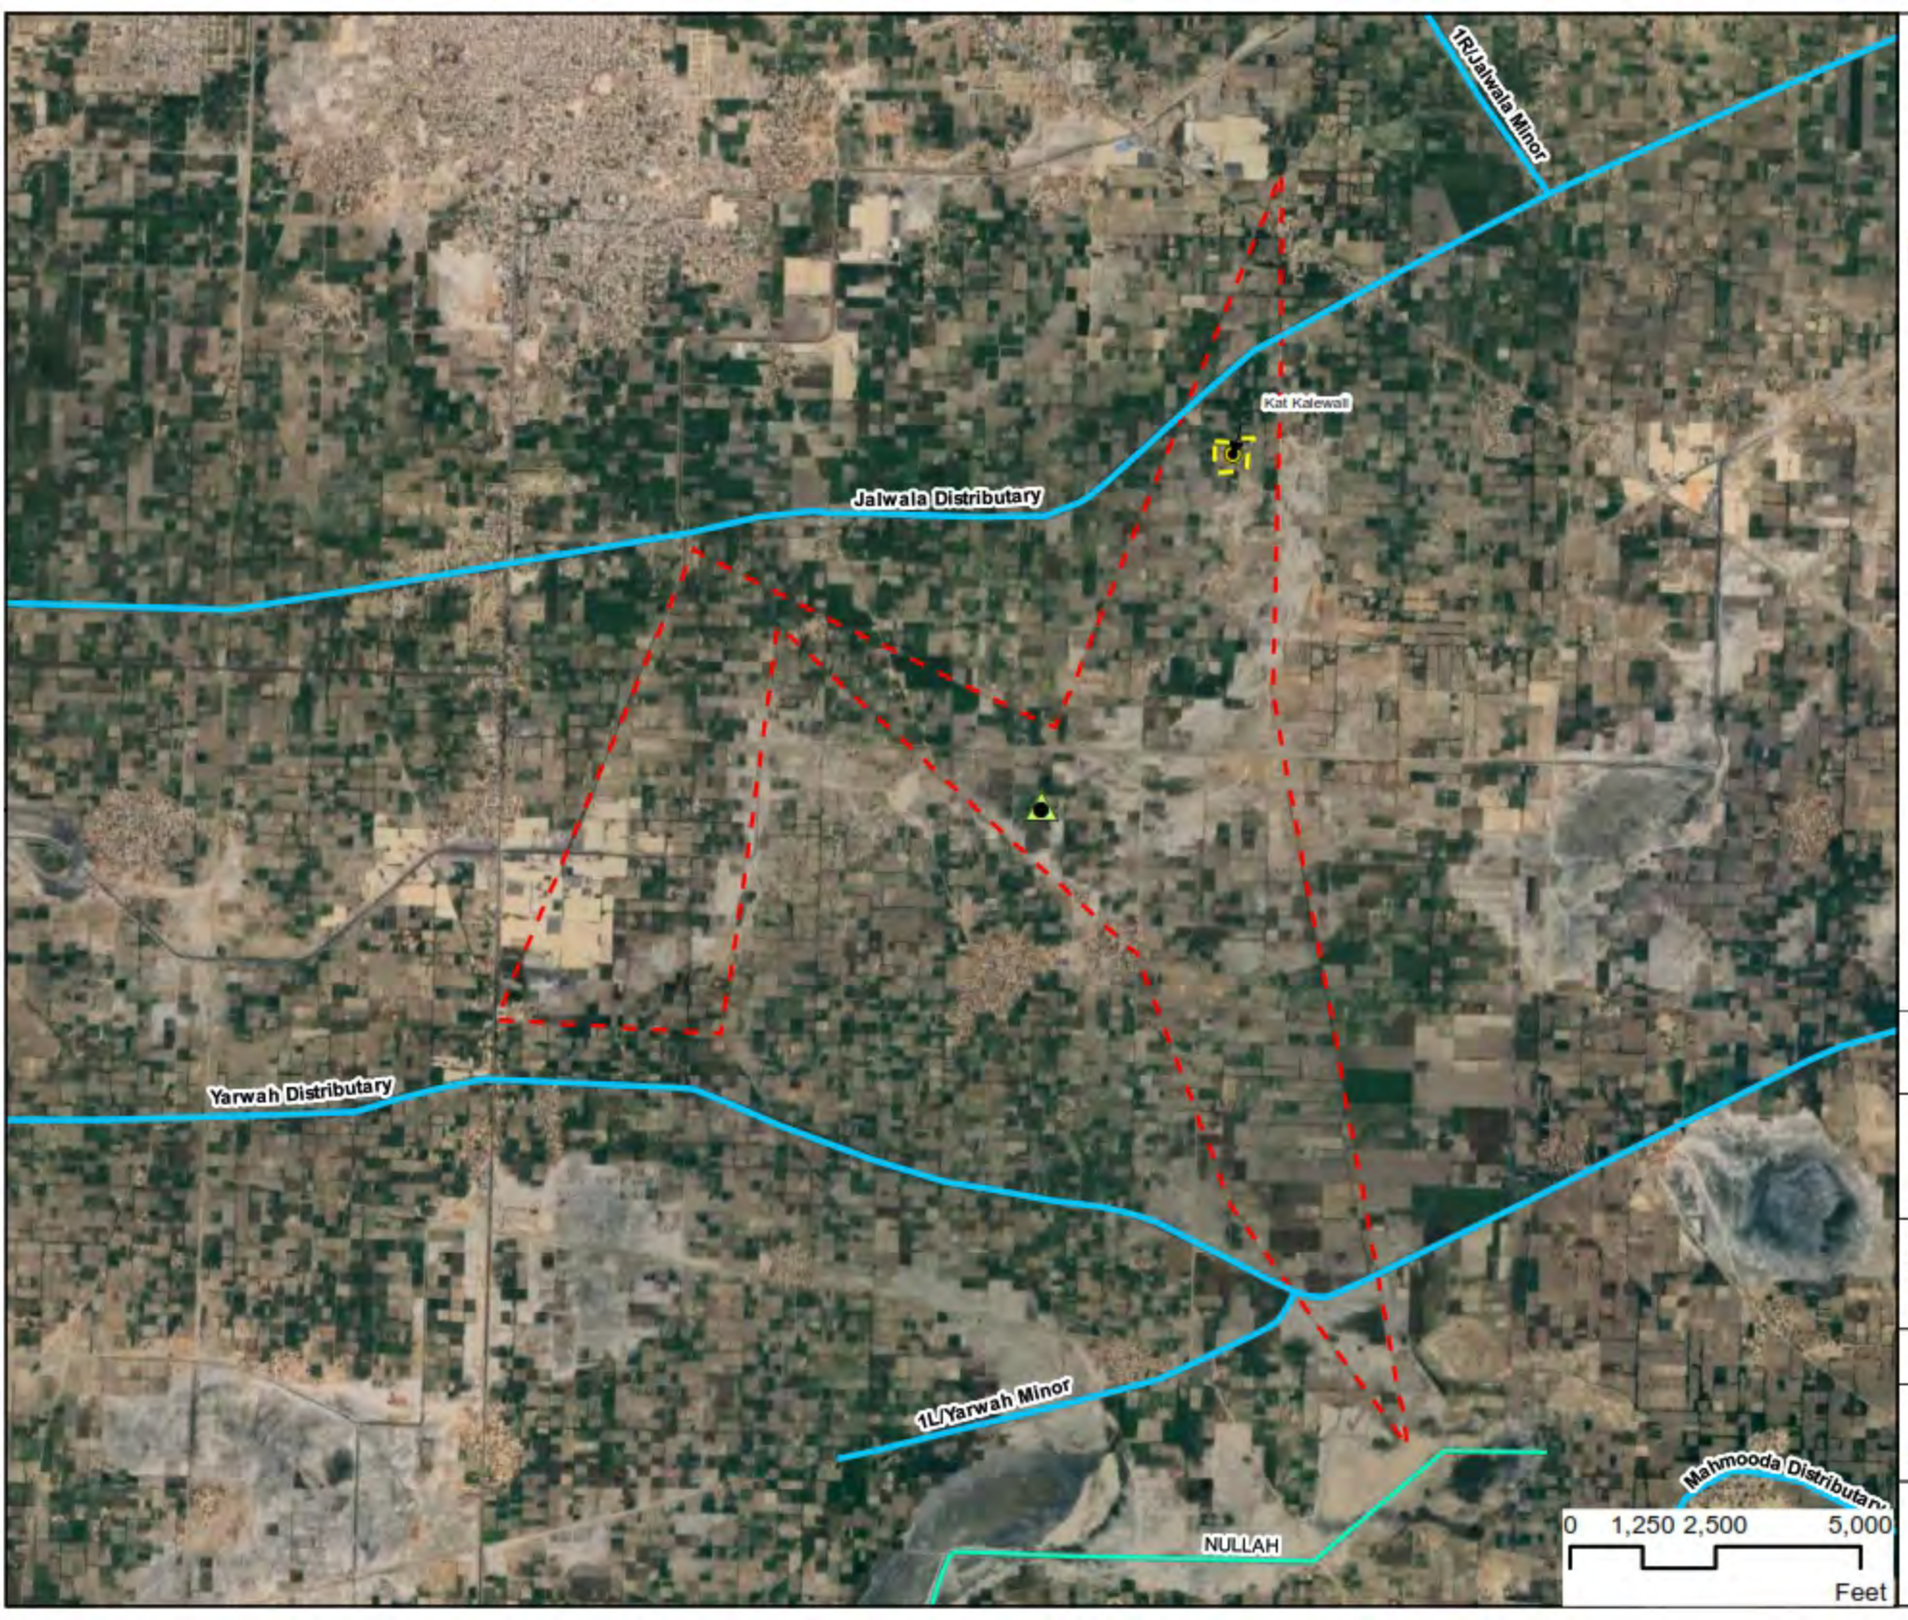

N
W E
S

TEHSIL BAHAWALNAGAR

MAUZA KHAWAJA BUX BODLA

LATITUDE: 29.94
LONGITUDE: 73.289

LEGEND

- CENTER
- MAJOR SETTELMENT
- NULLAH
- CANAL
- SETTELMENT BOUNDARY
- PROJECT AREA BOUNDARY

TITLE:
SATELLITE MAPS

PROJECT:
Engineering Design & Construction Supervision, Punjab Rural Sustainable Water Supply & Sanitation Project, Cluster South-III

DATE:	02-03-26
DRAWN:	ASAD
DESGIN:	ENGR.FAIEZ
APPROVED:	ENGR. IHSAN UL HAQ

TITLE:
PRMSC-BWN-KBB-SM-01

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

INFRASTRUCTURE CONSULTANT
ENVIRONMENTAL TECHNOLOGIES
ASIAN CONSULTING ENGINEERS
www.asiancon.com

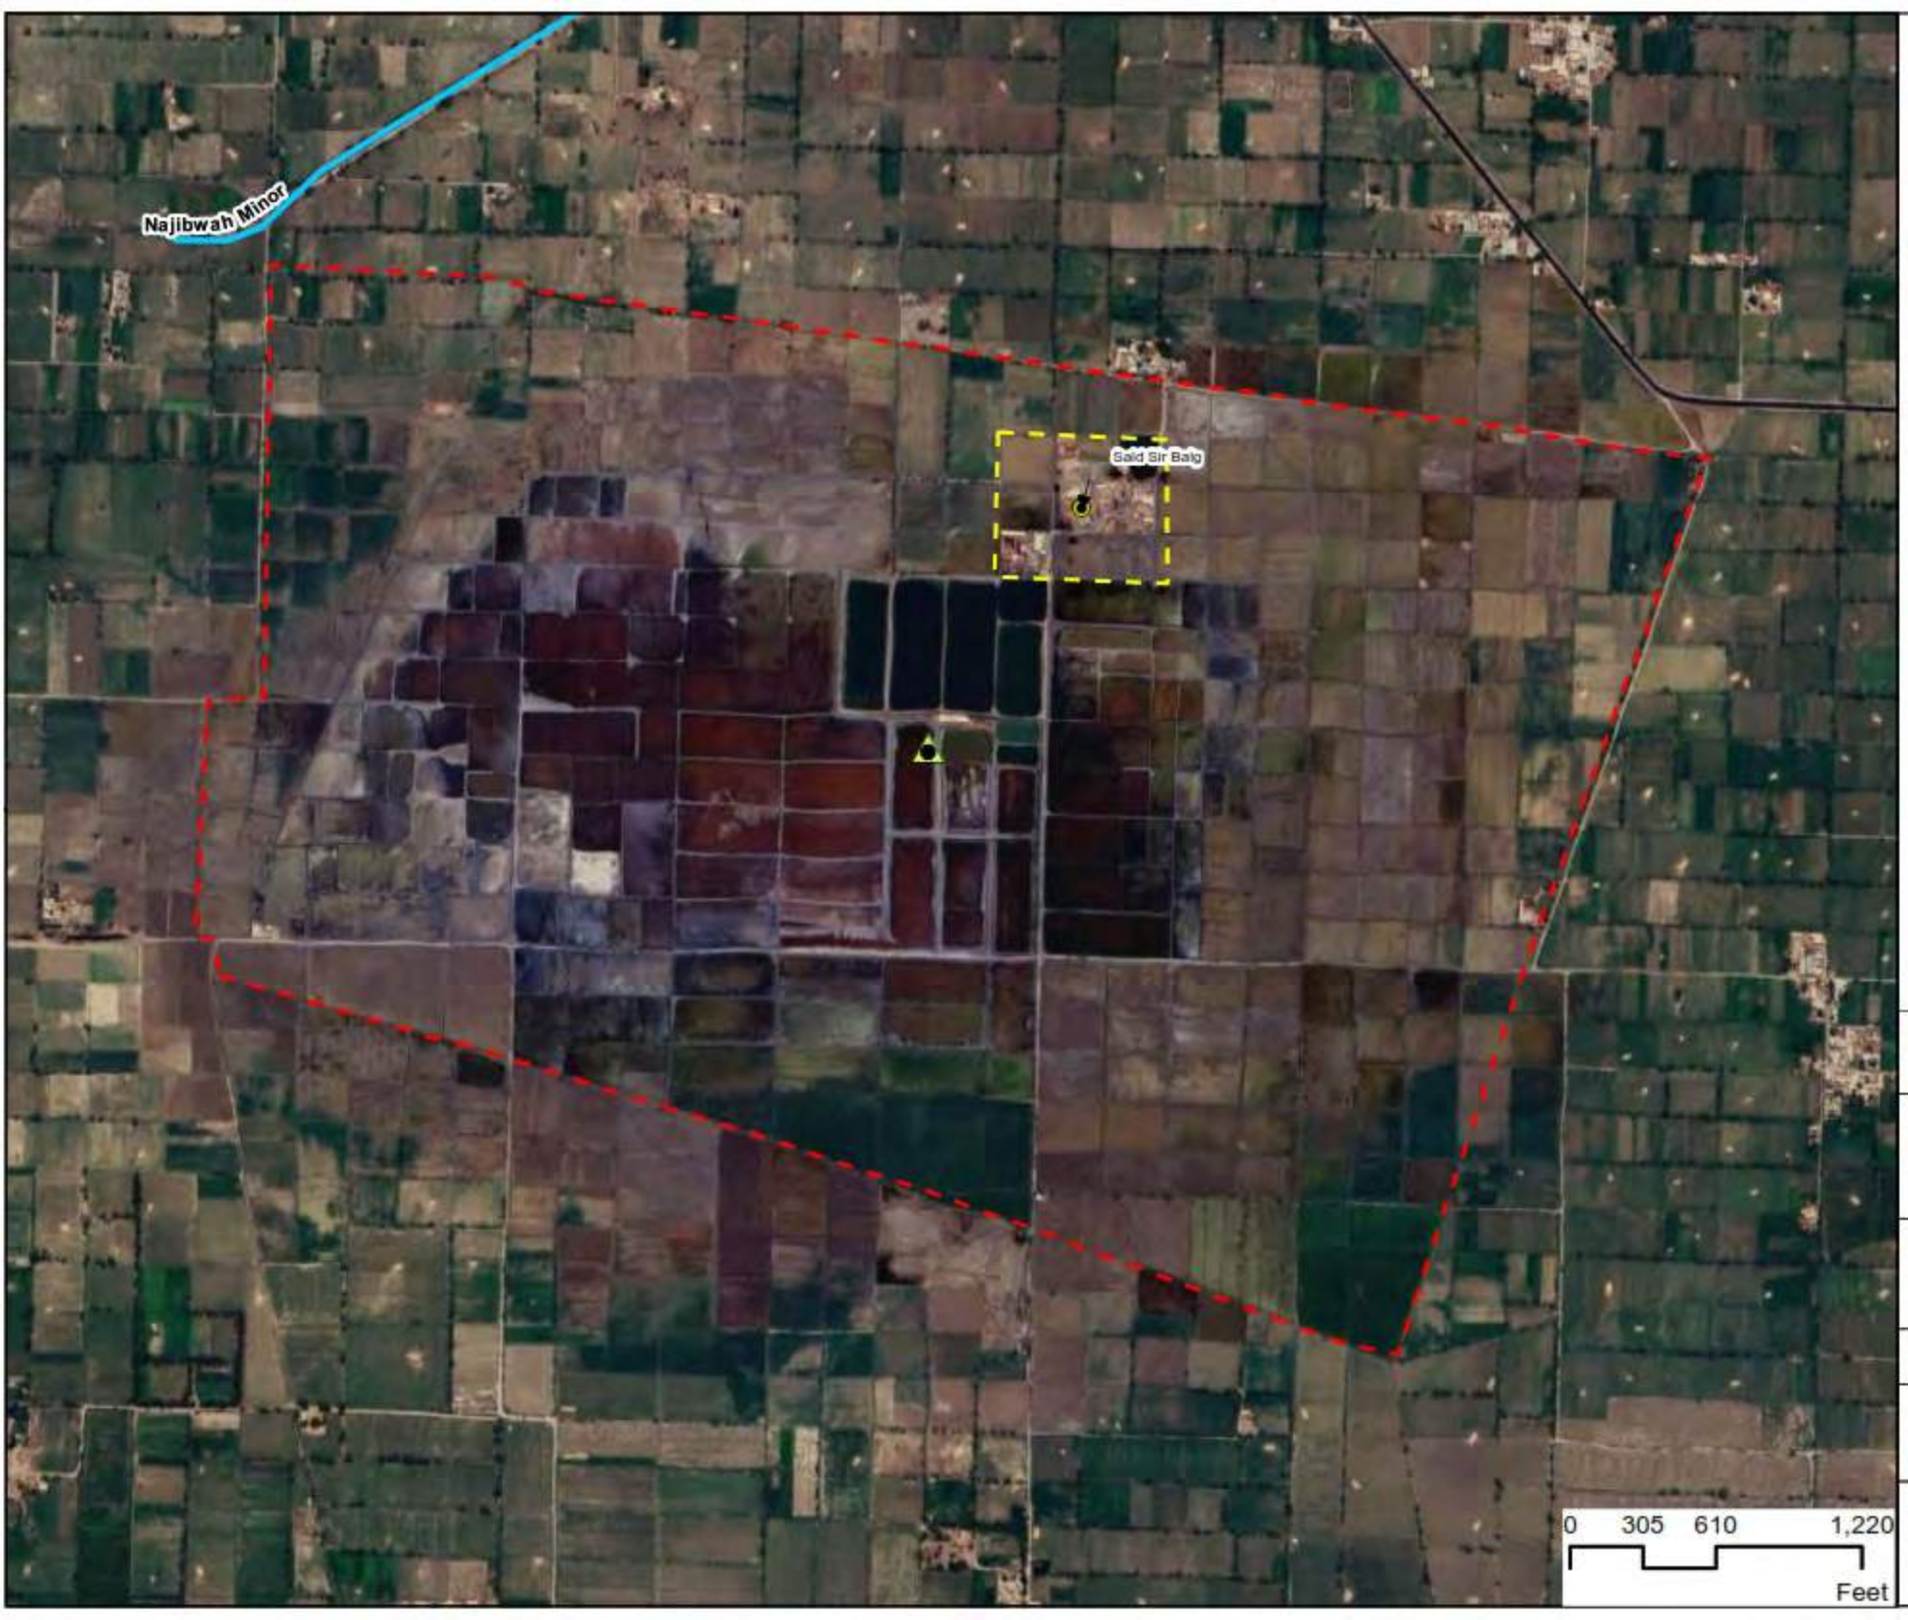

TEHSIL BAHAWALNAGAR

MAUZA MAHNI BEGKA

LATITUDE: 29.709
LONGITUDE: 73.151

LEGEND

- CENTER
- MAJOR SETTELMENT
- CANAL
- SETTELMENT BOUNDARY
- PROJECT AREA BOUNDARY

0 305 610 1,220
Feet

TITLE:
SATELLITE MAPS

PROJECT:
Engineering Design & Construction Supervision, Punjab Rural Sustainable Water Supply & Sanitation Project, Cluster South-III

DATE:	02-03-26
DRAWN:	ASAD
DESGIN:	ENGR.FAIEZ
APPROVED:	ENGR. IHSAN UL HAQ

TITLE:
PRMSC-BWN-MB-SM-01

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

INFRASTRUCTURE CONSULTANT
ENVIRONMENTAL TECHNOLOGIES
ASIAN CONSULTING ENGINEERS
www.asiancon.com

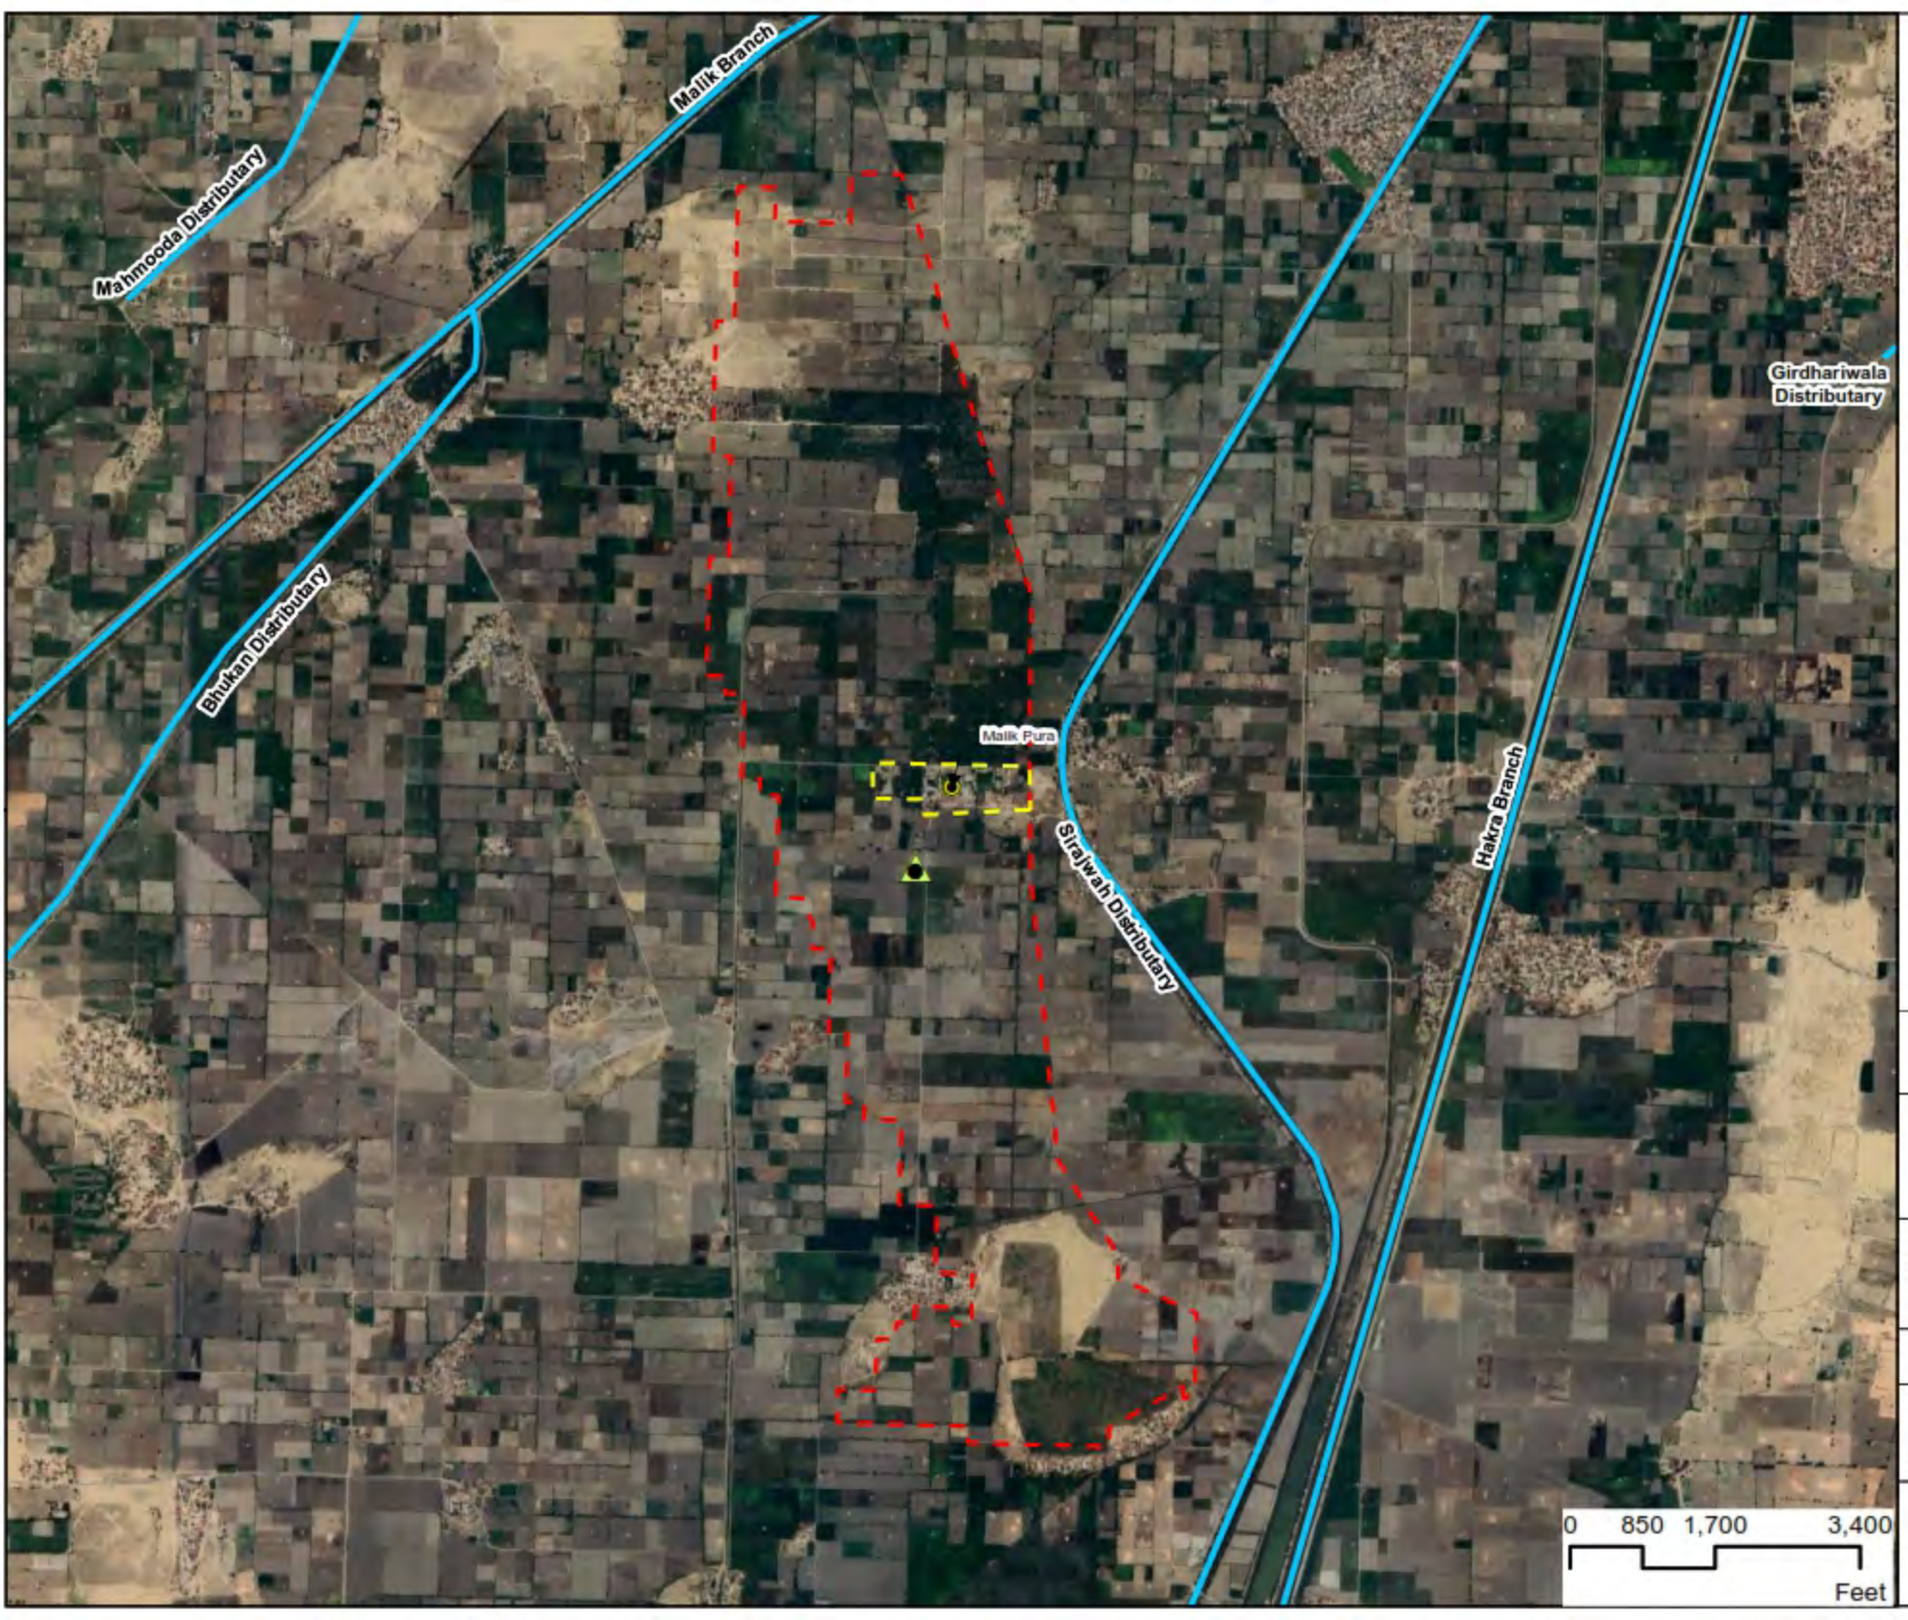

N
W E
S

TEHSIL BAHAWALNAGAR

MAUZA MALAK PURA

LATITUDE: 29.896
LONGITUDE: 73.328

LEGEND

- CENTER
- MAJOR SETTELMENT
- CANAL
- SETTELMENT BOUNDARY
- PROJECT AREA BOUNDARY

TITLE:
SATELLITE MAPS

PROJECT:
Engineering Design & Construction Supervision, Punjab Rural Sustainable Water Supply & Sanitation Project, Cluster South-III

DATE:	02-03-26
DRAWN:	ASAD
DESGIN:	ENGR.FAIEZ
APPROVED:	ENGR. IHSAN UL HAQ

TITLE:
PRMSC-BWN-MP-SM-01

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

INFRASTRUCTURE CONSULTANT
ENVIRONMENTAL TECHNOLOGIES
ASIAN CONSULTING ENGINEERS
www.asiancon.com

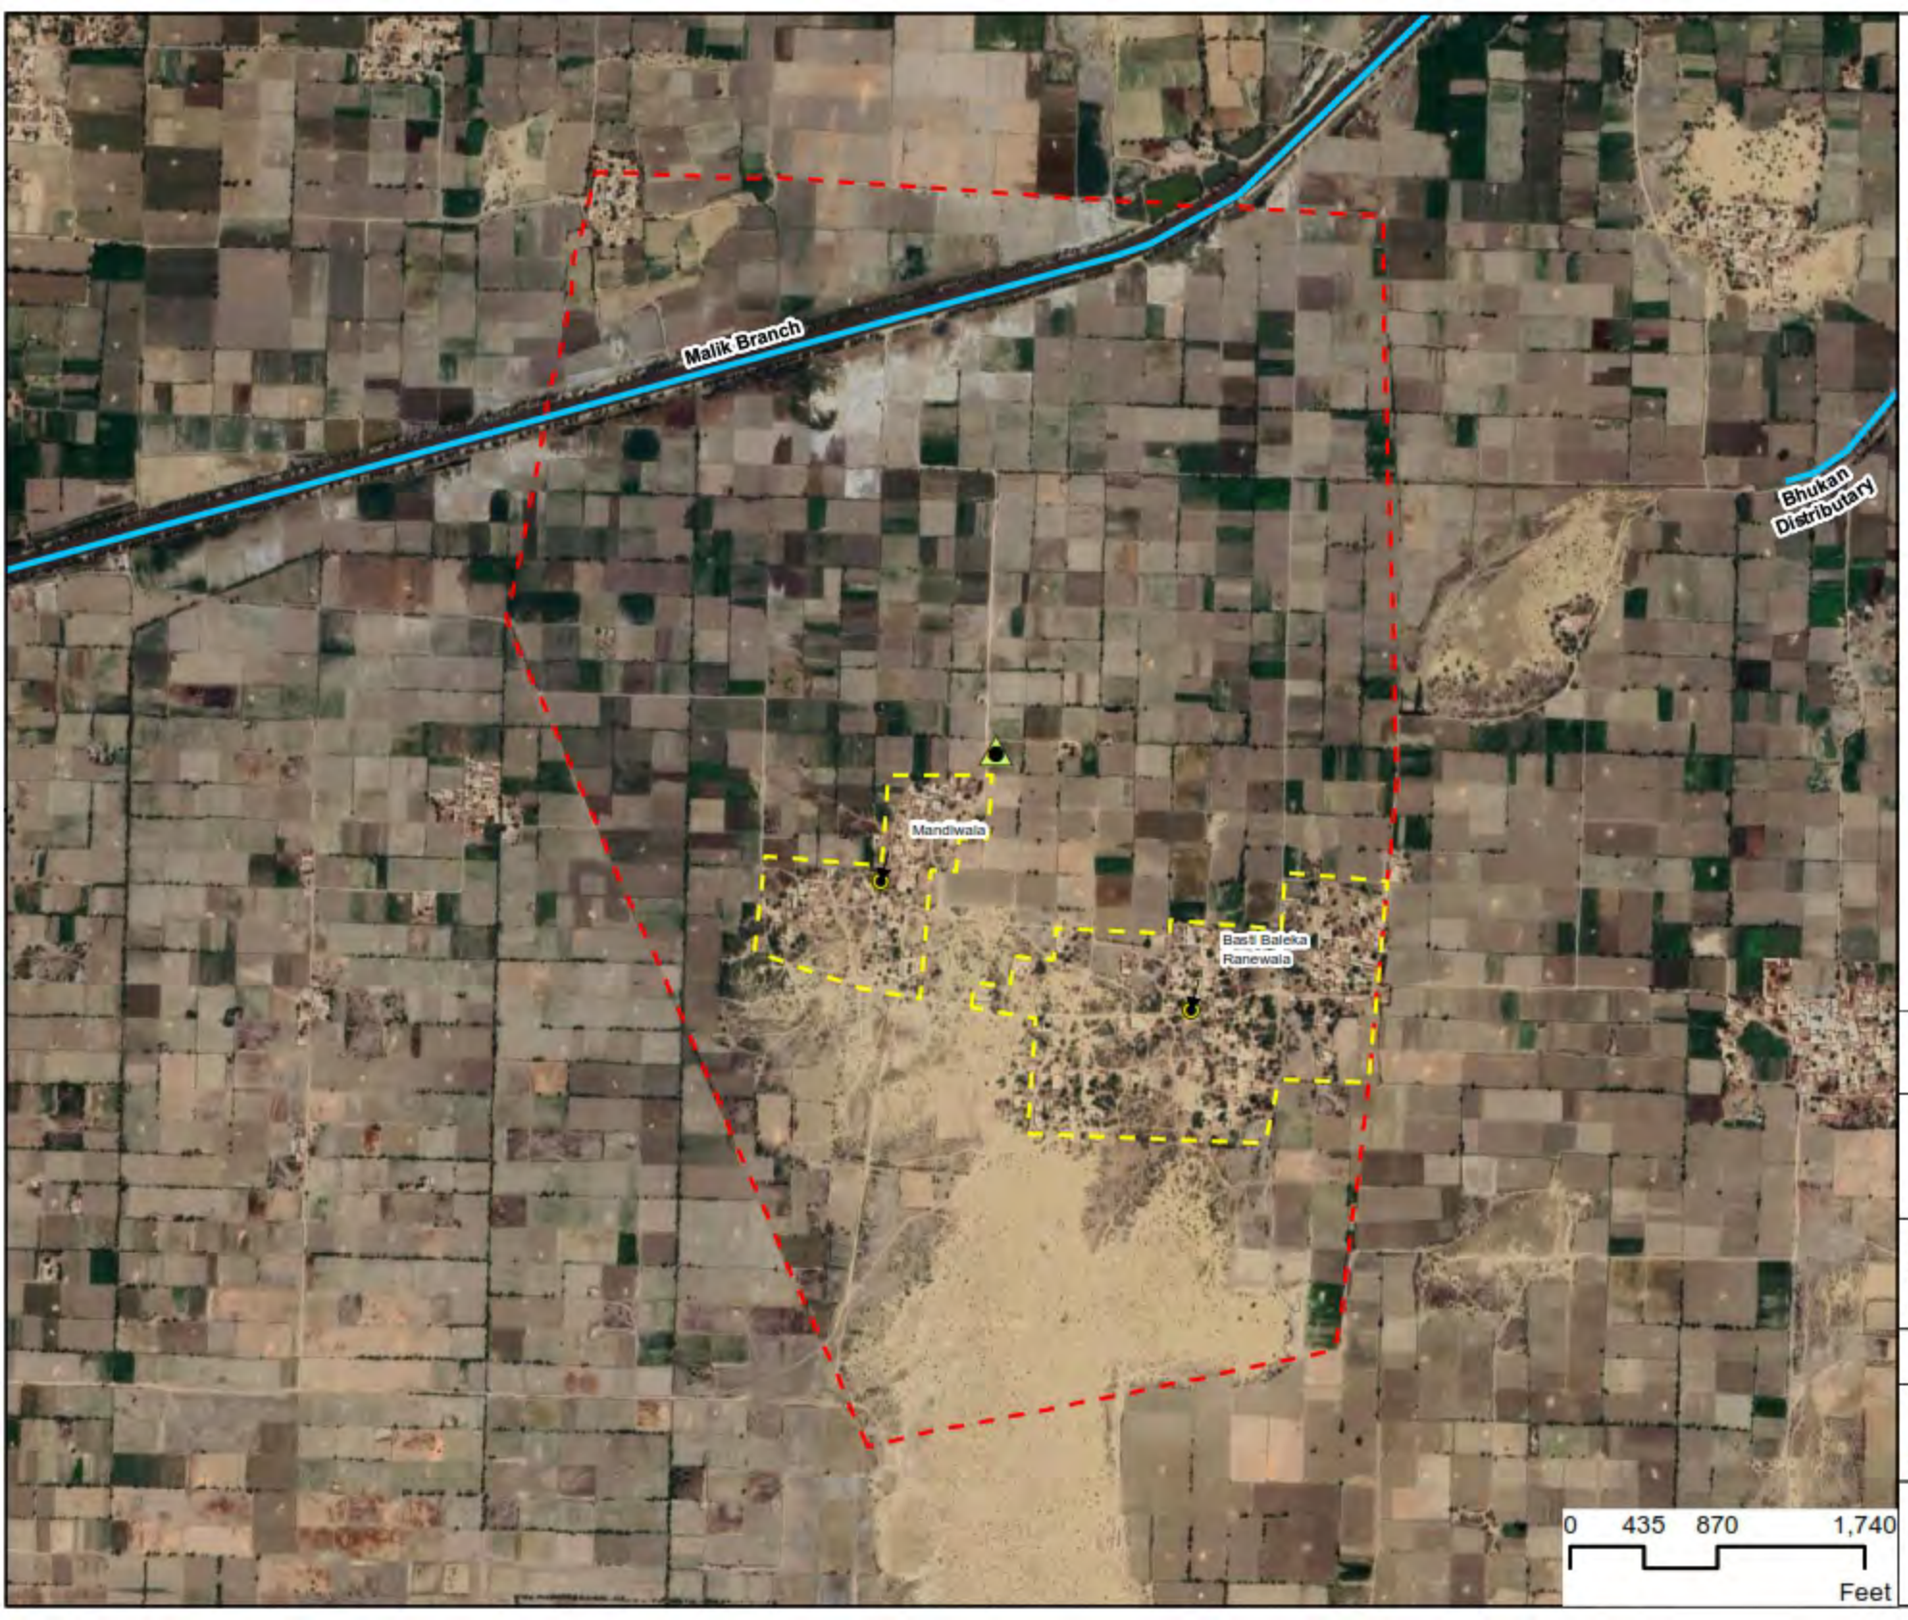

N
W E
S

TEHSIL BAHAWALNAGAR

MAUZA MINA SANATTEKA

LATITUDE: 29.866
LONGITUDE: 73.274

LEGEND

- CENTER
- MAJOR SETTELMENT
- CANAL
- SETTELMENT BOUNDARY
- PROJECT AREA BOUNDARY

TITLE:
SATELLITE MAPS

PROJECT:
Engineering Design & Construction Supervision, Punjab Rural Sustainable Water Supply & Sanitation Project, Cluster South-III

DATE:	02-03-26
DRAWN:	ASAD
DESGIN:	ENGR.FAIEZ
APPROVED:	ENGR. IHSAN UL HAQ

TITLE:
PRMSC-BWN-MS-SM-01

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

INFRASTRUCTURE CONSULTANT
ENVIRONMENTAL TECHNOLOGIES
ASIAN CONSULTING ENGINEERS
www.asiancon.com

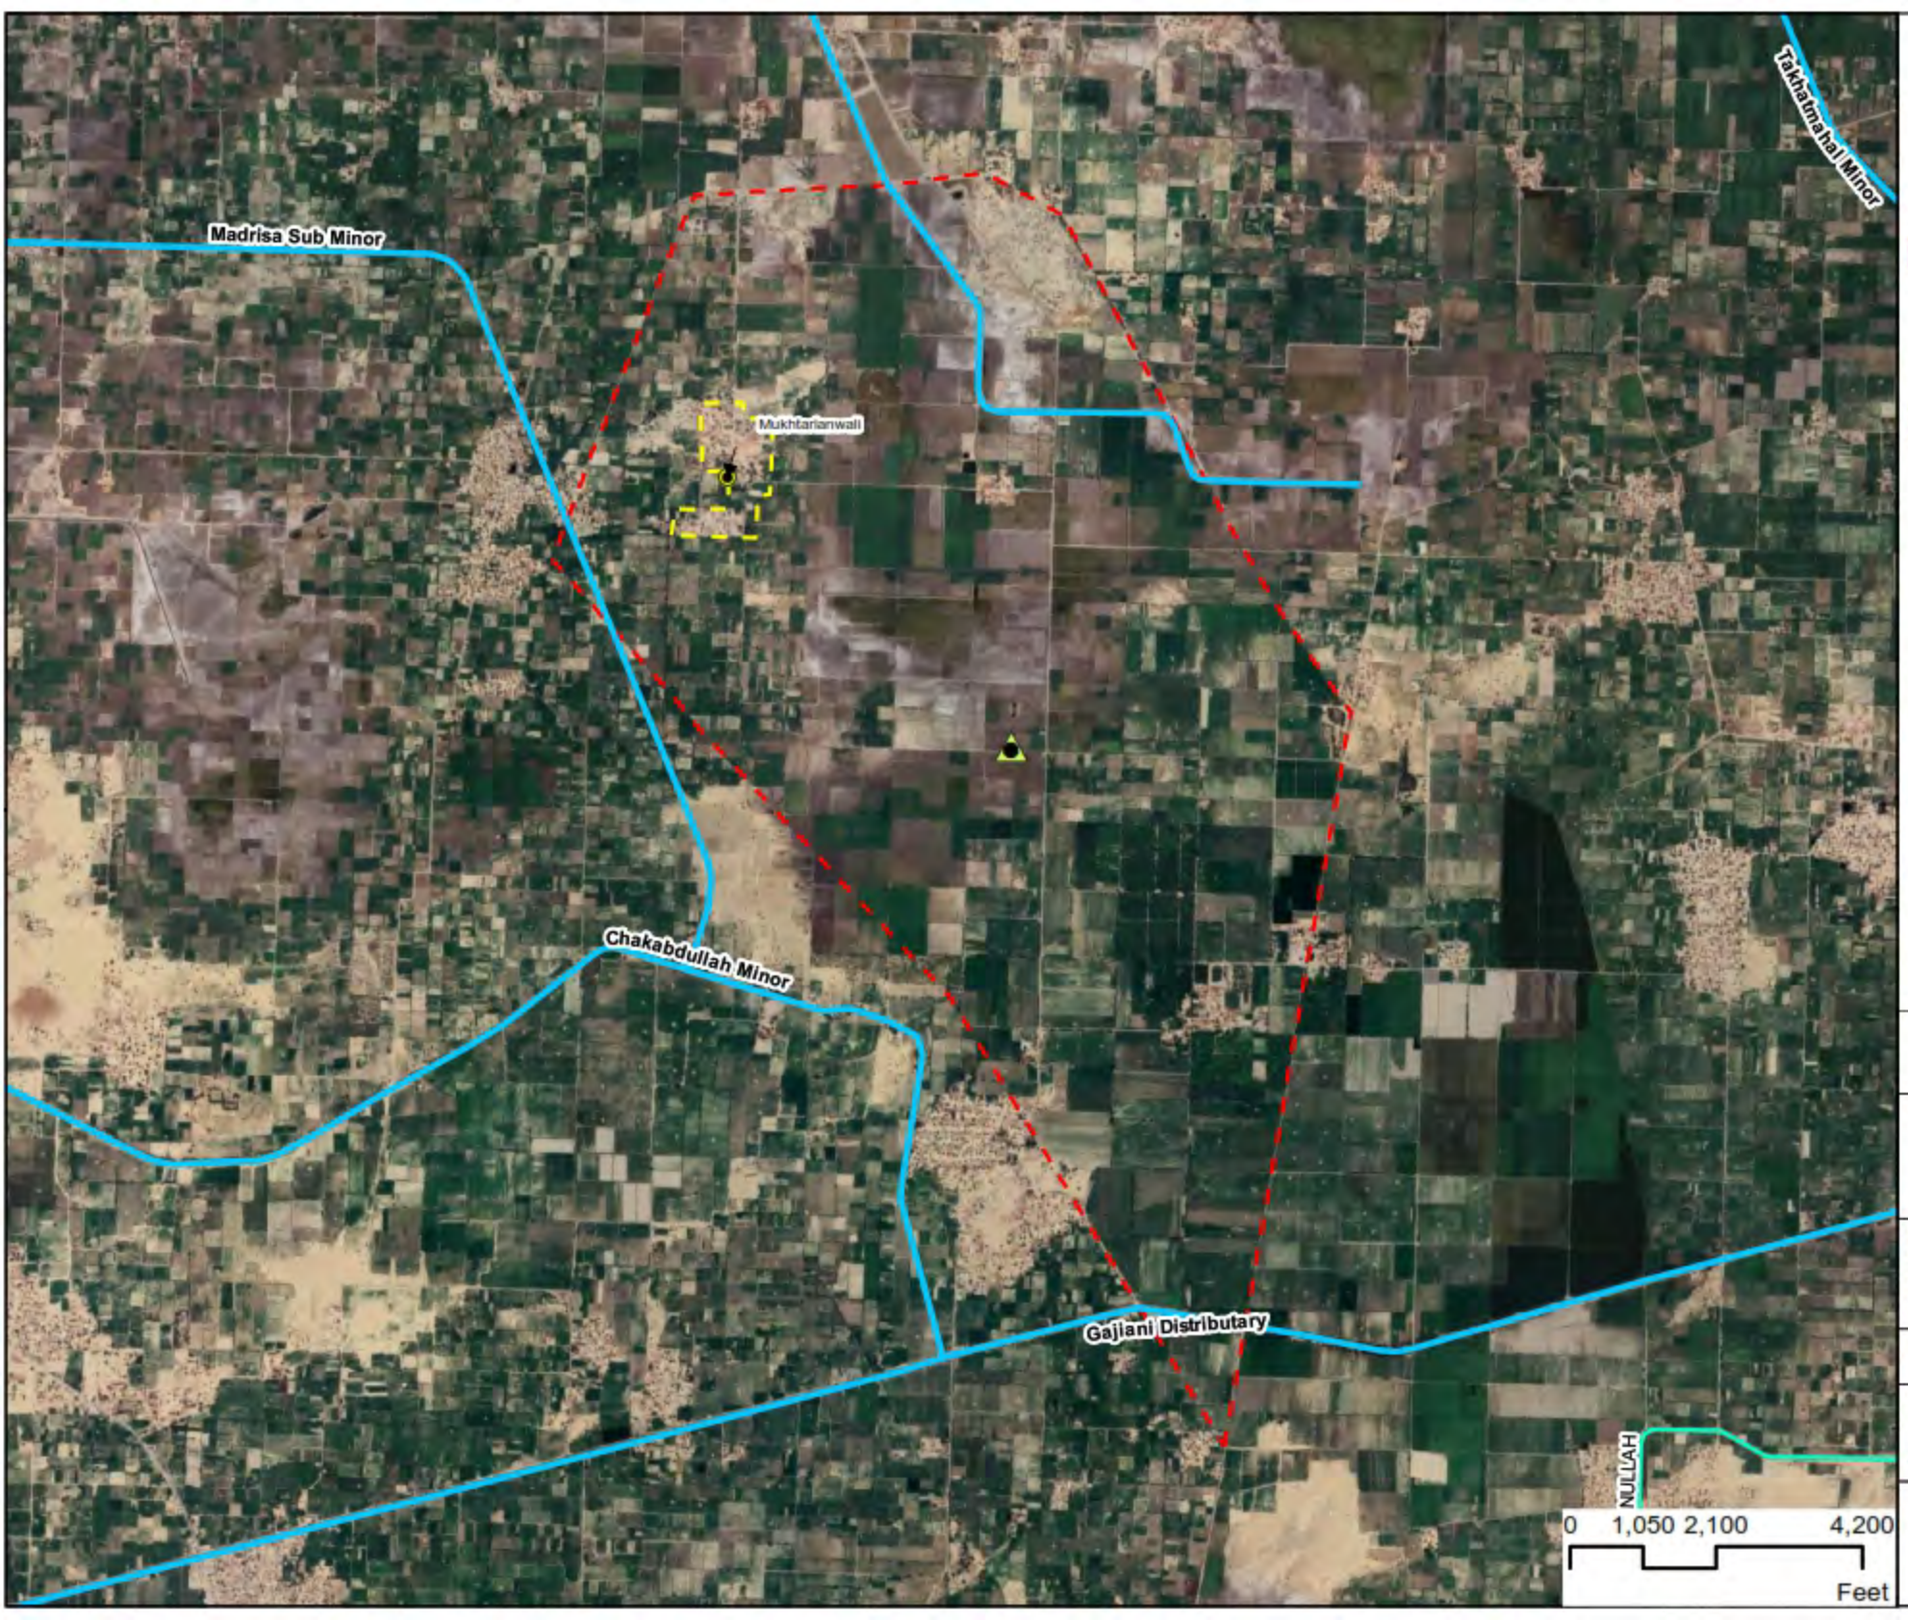

N
W E
S

TEHSIL BAHAWALNAGAR

MAUZA MUHAMMAD ASAD KHAN

LATITUDE: 29.902
LONGITUDE: 73.115

LEGEND

- CENTER
- MAJOR SETTELMENT
- NULLAH
- CANAL
- SETTELMENT BOUNDARY
- PROJECT AREA BOUNDARY

TITLE:
SATELLITE MAPS

PROJECT:
Engineering Design & Construction Supervision, Punjab Rural Sustainable Water Supply & Sanitation Project, Cluster South-III

DATE:	02-03-26
DRAWN:	ASAD
DESGIN:	ENGR.FAIEZ
APPROVED:	ENGR. IHSAN UL HAQ

TITLE:
PRMSC-BWN-MAK-SM-01

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

INFRASTRUCTURE CONSULTANT
ENVIRONMENTAL TECHNOLOGIES
ASIAN CONSULTING ENGINEERS
www.asiancon.com

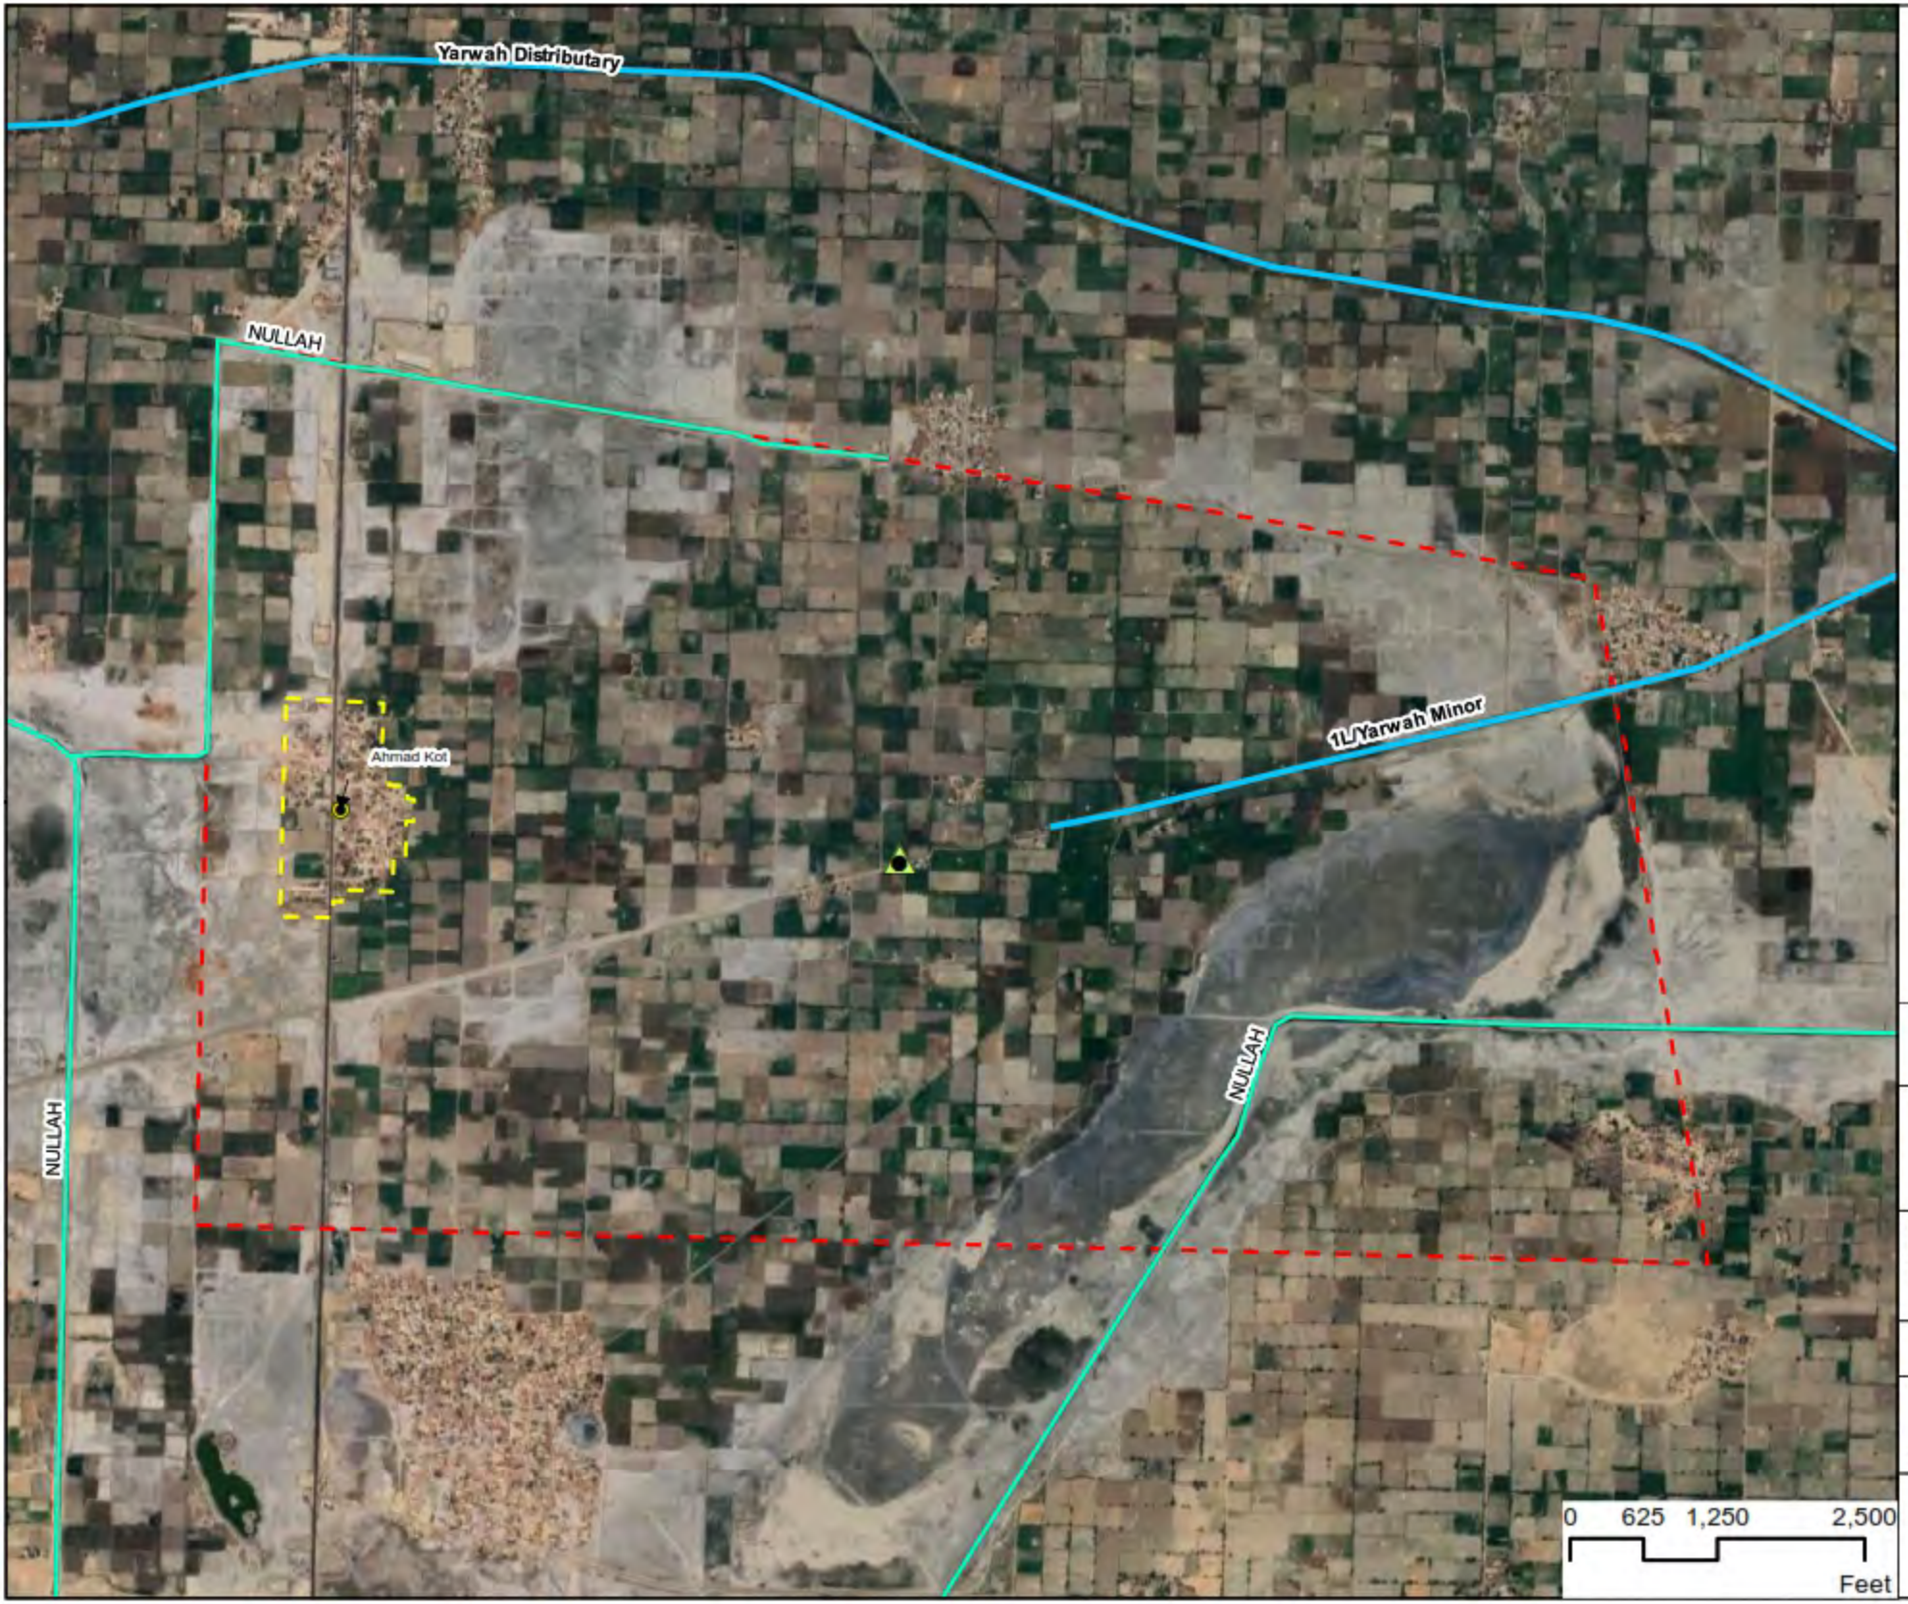

N
W E
S

TEHSIL BAHAWALNAGAR

MAUZA MUHSAN PURA

LATITUDE: 29.909
LONGITUDE: 73.264

LEGEND

- CENTER
- MAJOR SETTELMENT
- NULLAH
- CANAL
- SETTELMENT BOUNDARY
- PROJECT AREA BOUNDARY

TITLE:
SATELLITE MAPS

PROJECT:
Engineering Design & Construction Supervision, Punjab Rural Sustainable Water Supply & Sanitation Project, Cluster South-III

DATE:	02-03-26
DRAWN:	ASAD
DESGIN:	ENGR.FAIEZ
APPROVED:	ENGR. IHSAN UL HAQ

TITLE:
PRMSC-BWN-MHP-SM-01

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

INFRASTRUCTURE CONSULTANT
ENVIRONMENTAL TECHNOLOGIES
ASIAN CONSULTING ENGINEERS
www.asiancon.com

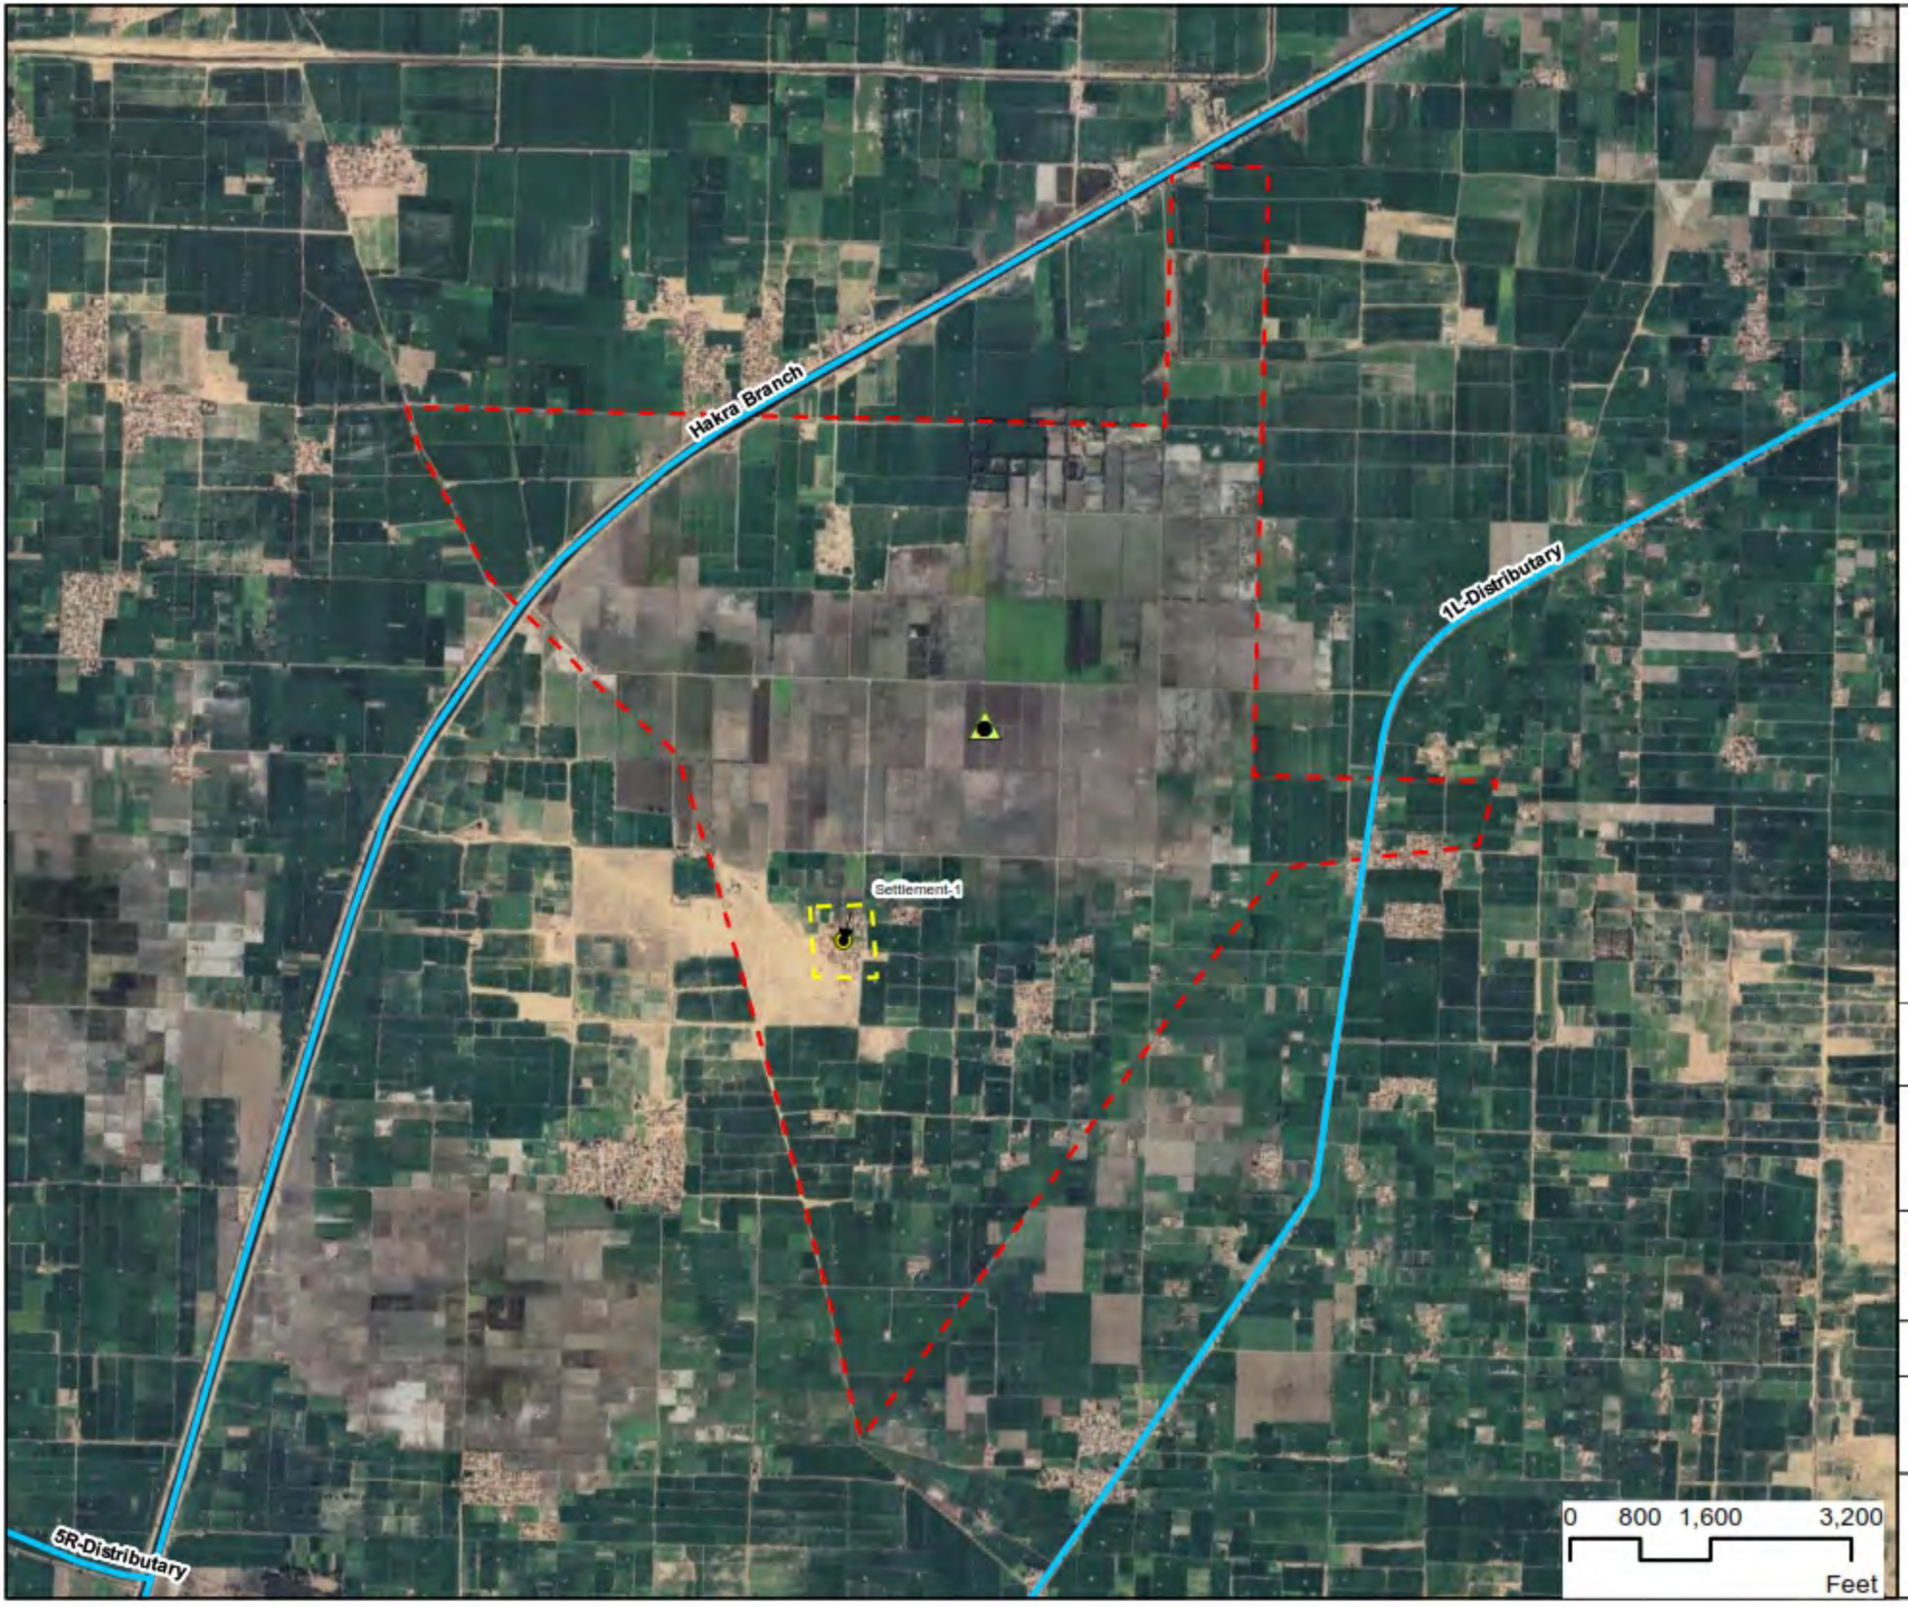

TEHSIL BAHAWALNAGAR

MAUZA NOOR JAHANIA

LATITUDE: 29.587
LONGITUDE: 73.227

LEGEND

- CENTER
- MAJOR SETTELMENT
- CANAL
- SETTELMENT BOUNDARY
- PROJECT AREA BOUNDARY

TITLE: SATELLITE MAPS

PROJECT: Engineering Design & Construction Supervision, Punjab Rural Sustainable Water Supply & Sanitation Project, Cluster South-III

DATE:	02-03-26
DRAWN:	ASAD
DESGIN:	ENGR.FAIEZ
APPROVED:	ENGR. IHSAN UL HAQ

TITLE: PRMSC-BWN-NJ-SM-01

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

INFRASTRUCTURE CONSULTANT

ENVIRONMENTAL TECHNOLOGIES

ASIAN CONSULTING ENGINEERS www.asiancon.com

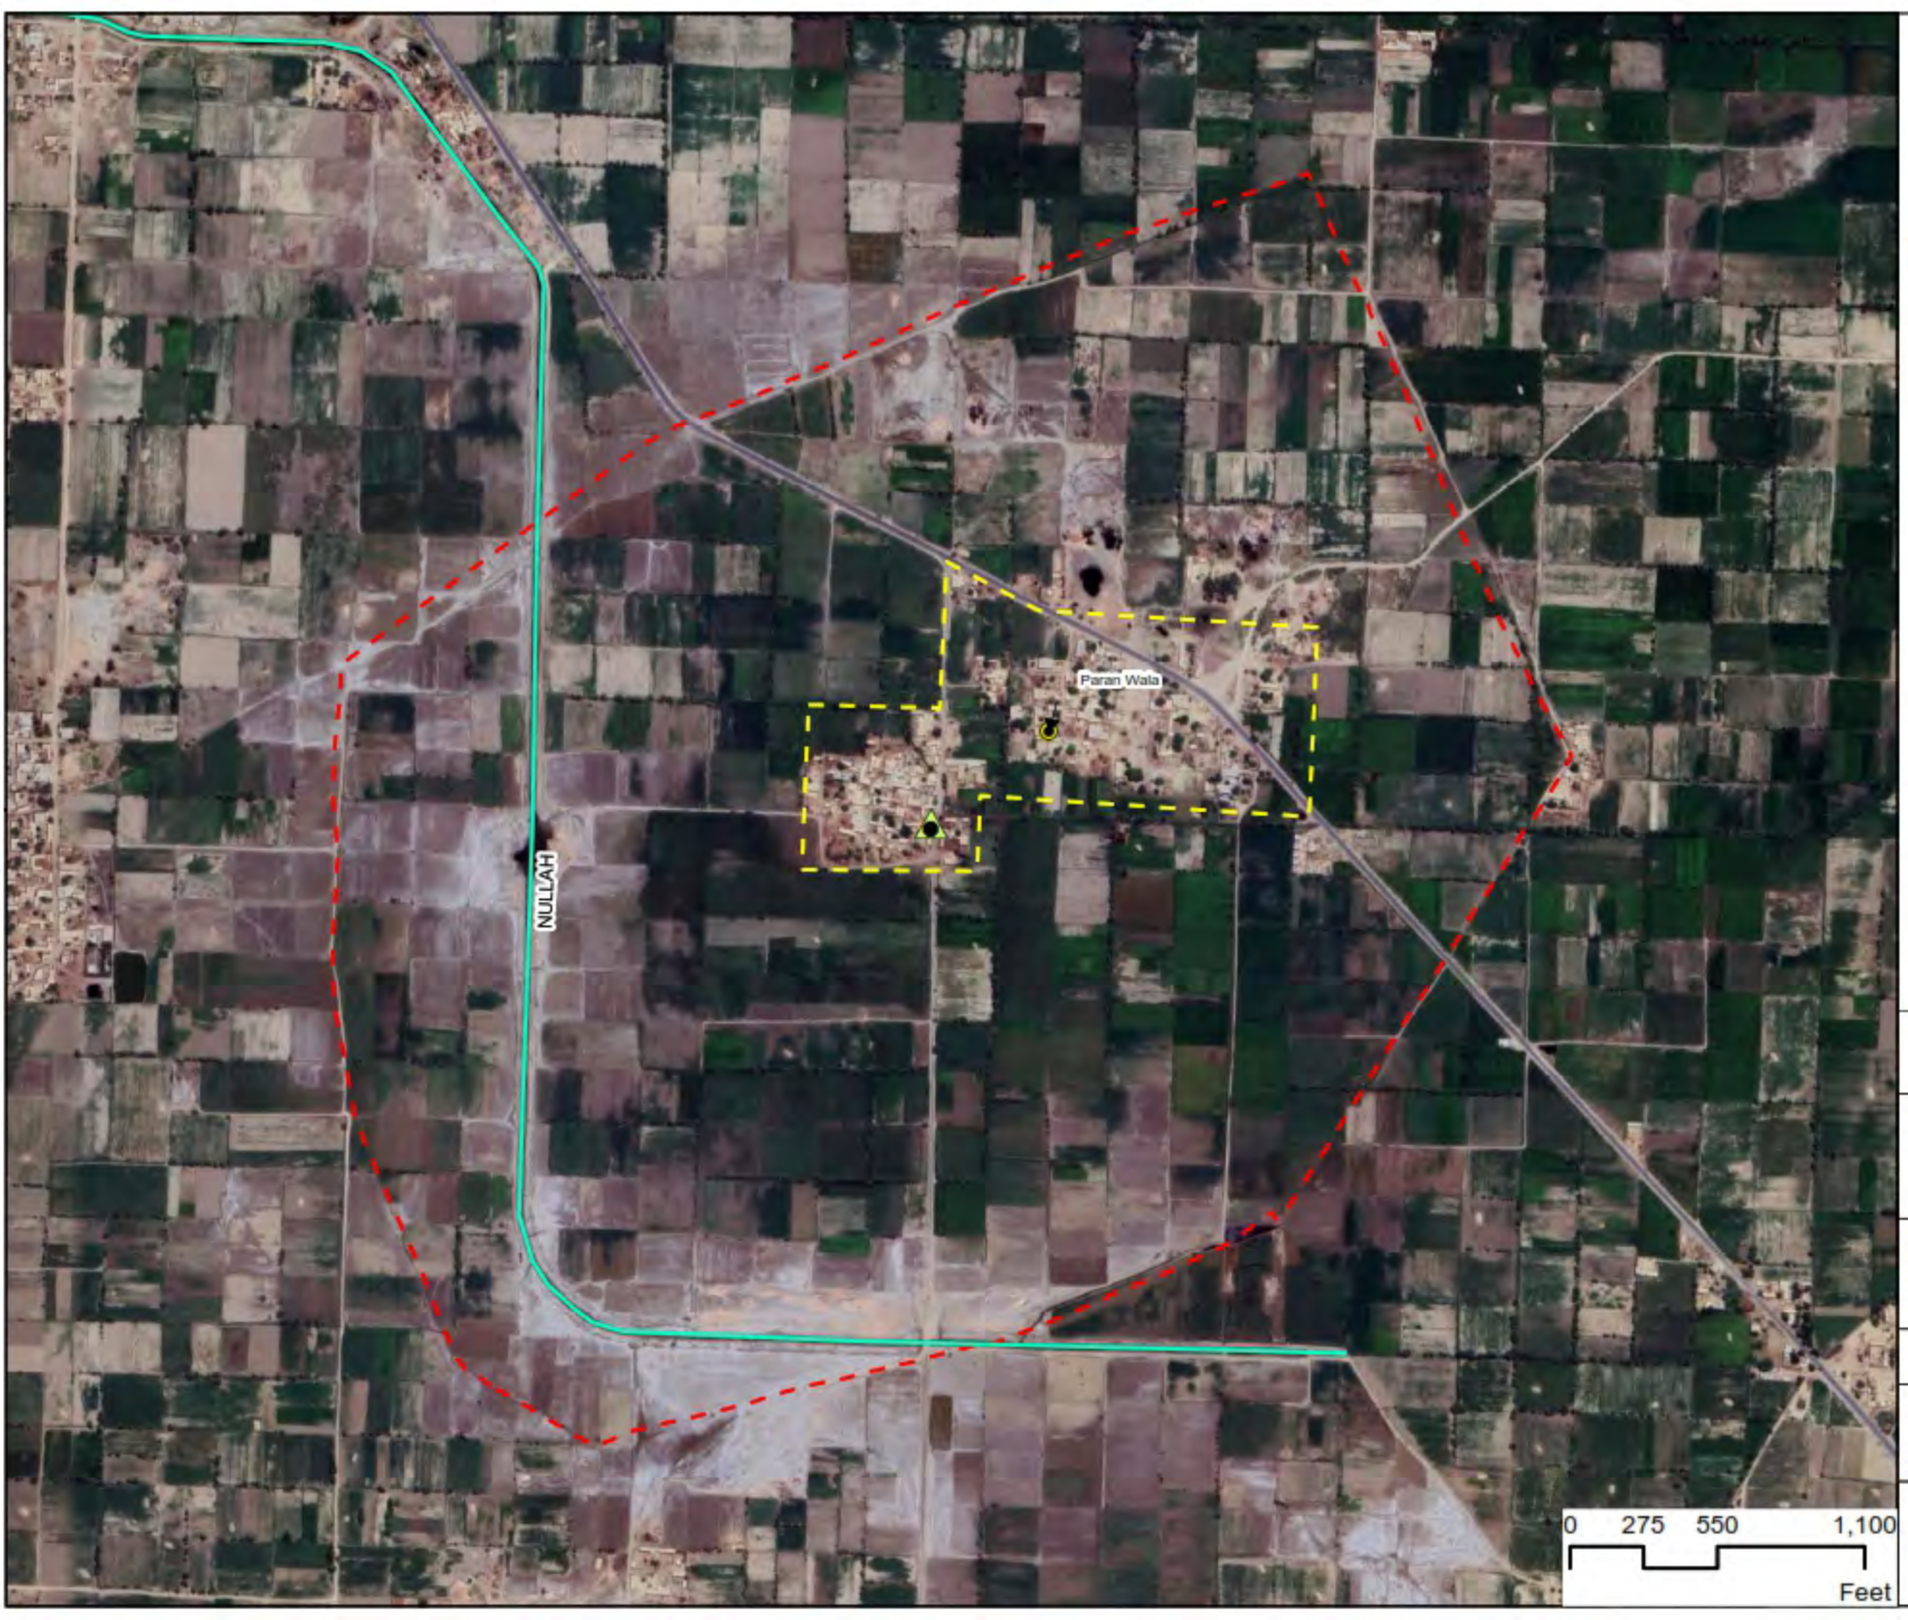

N
W E
S

TEHSIL BAHAWALNAGAR

MAUZA PARAN WALA

LATITUDE: 29.878
LONGITUDE: 73.059

LEGEND

- CENTER
- MAJOR SETTELMENT
- NULLAH
- SETTELMENT BOUNDARY
- PROJECT AREA BOUNDARY

TITLE:
SATELLITE MAPS

PROJECT:
Engineering Design & Construction Supervision, Punjab Rural Sustainable Water Supply & Sanitation Project, Cluster South-III

DATE:	02-03-26
DRAWN:	ASAD
DESGIN:	ENGR.FAIEZ
APPROVED:	ENGR. IHSAN UL HAQ

TITLE:
PRMSC-BWN-PW-SM-01

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

INFRASTRUCTURE CONSULTANT
ENVIRONMENTAL TECHNOLOGIES
ASIAN CONSULTING ENGINEERS
www.asiancon.com

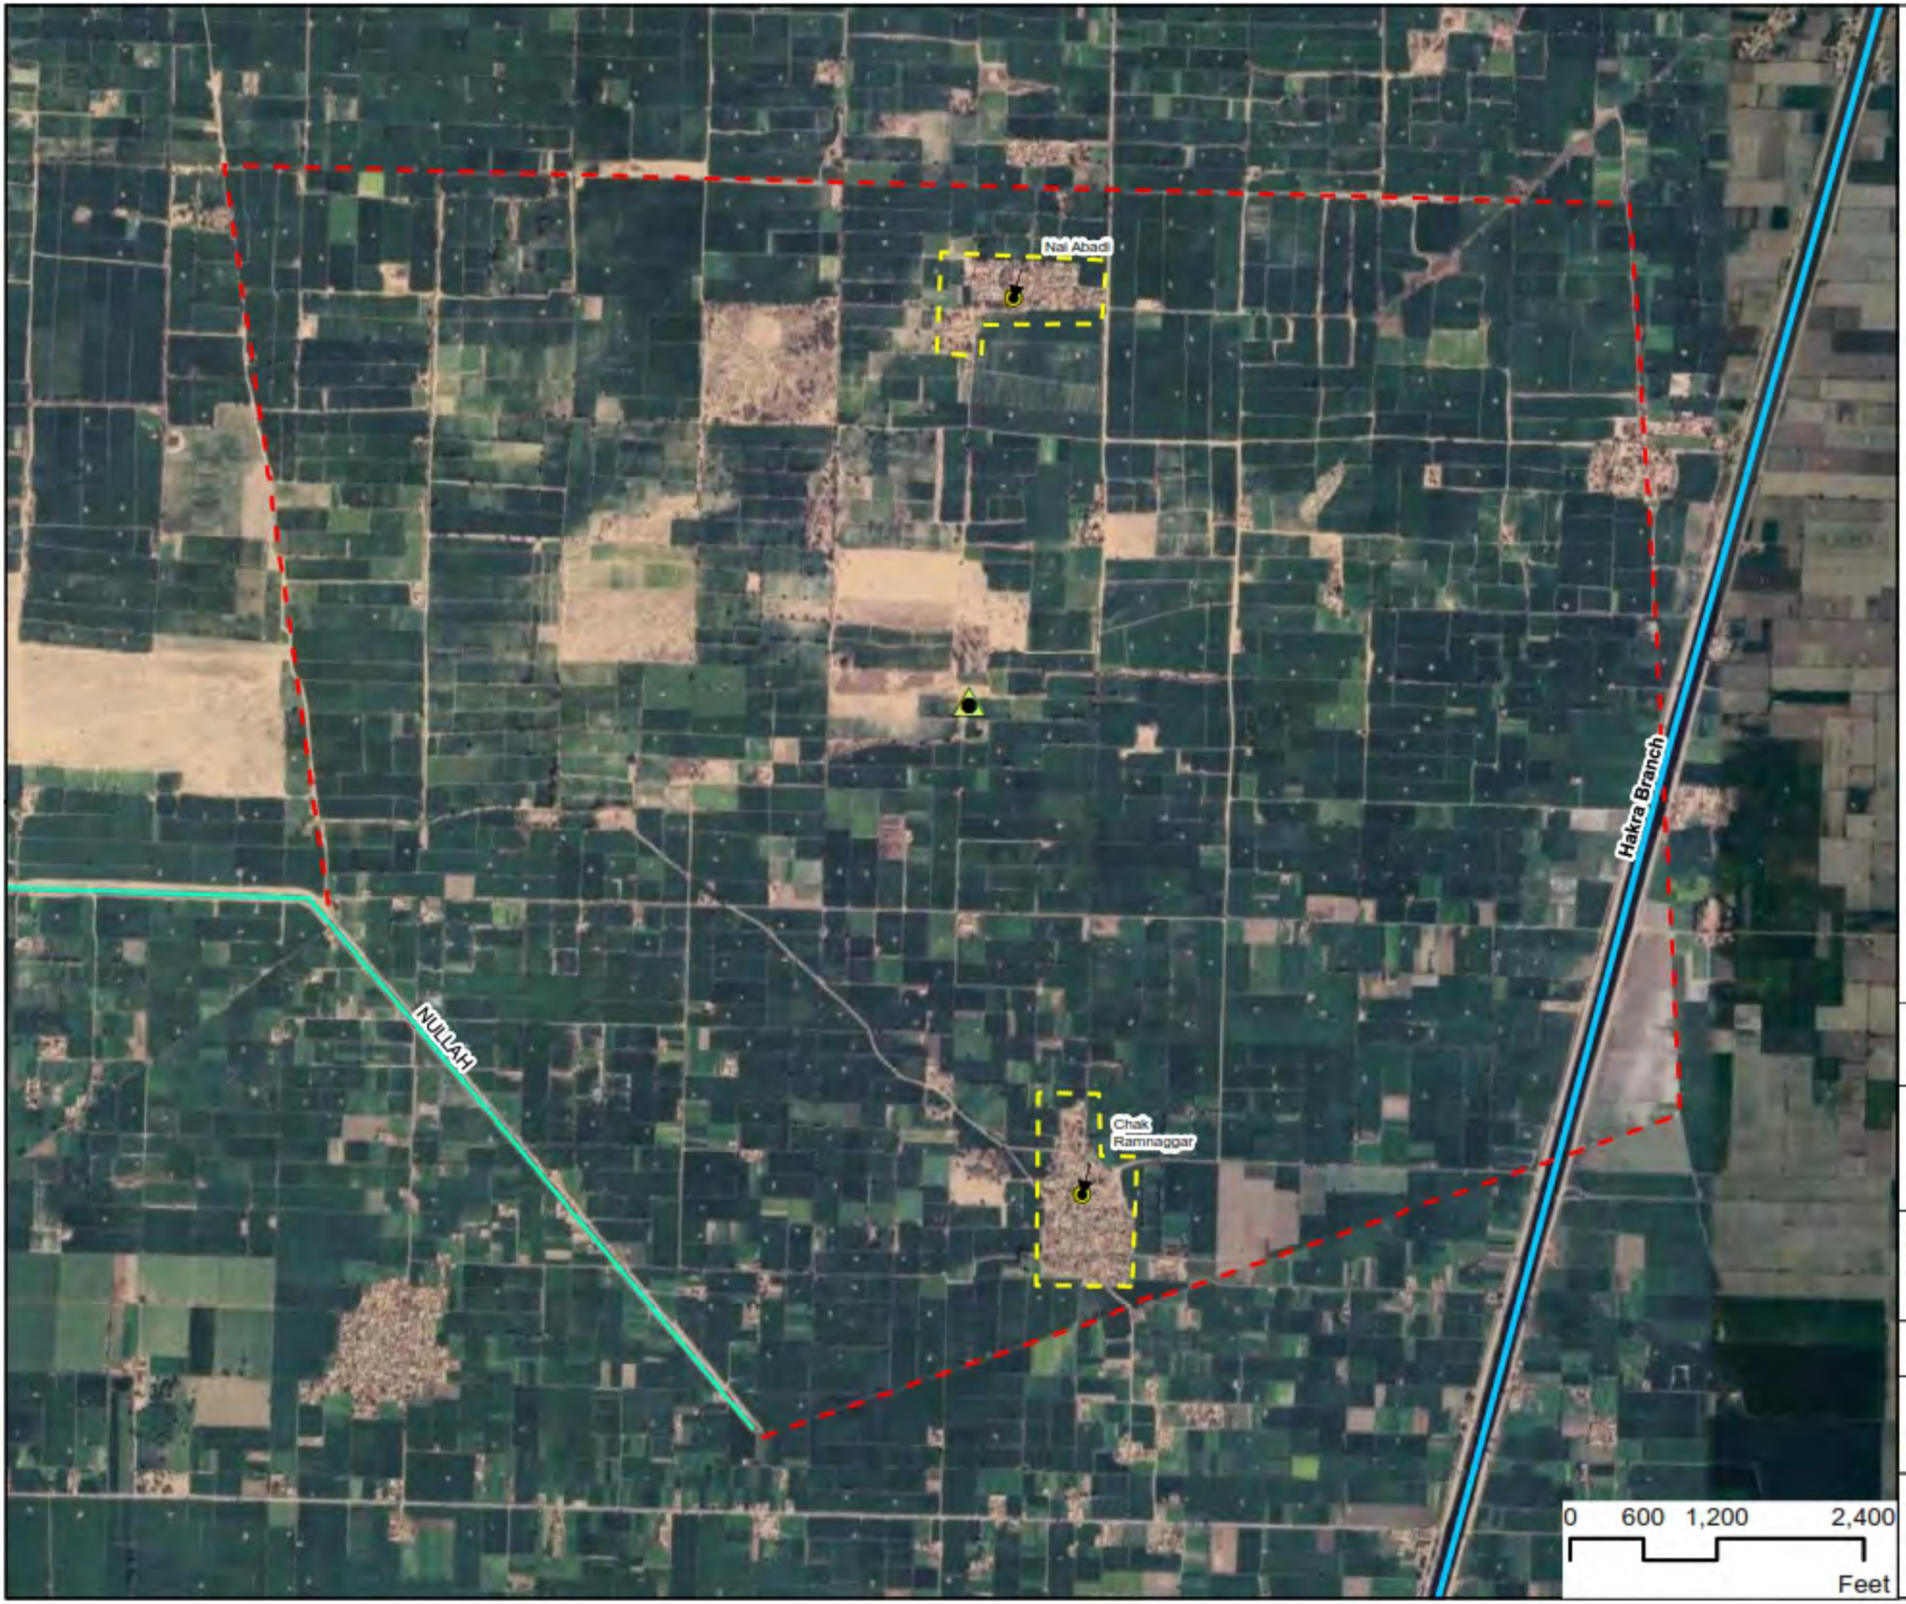

TEHSIL BAHAWALNAGAR

MAUZA RAMNAGAR

LATITUDE: 29.728
LONGITUDE: 73.306

LEGEND

- CENTER
- MAJOR SETTELMENT
- NULLAH
- CANAL
- SETTELMENT BOUNDARY
- PROJECT AREA BOUNDARY

0 600 1,200 2,400
Feet

TITLE:
SATELLITE MAPS

PROJECT:
Engineering Design & Construction Supervision, Punjab Rural Sustainable Water Supply & Sanitation Project, Cluster South-III

DATE:	02-03-26
DRAWN:	ASAD
DESGIN:	ENGR.FAIEZ
APPROVED:	ENGR. IHSAN UL HAQ

TITLE:
PRMSC-BWN-R-SM-01

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

INFRASTRUCTURE CONSULTANT
ENVIRONMENTAL TECHNOLOGIES
ASIAN CONSULTING ENGINEERS
www.asiancon.com

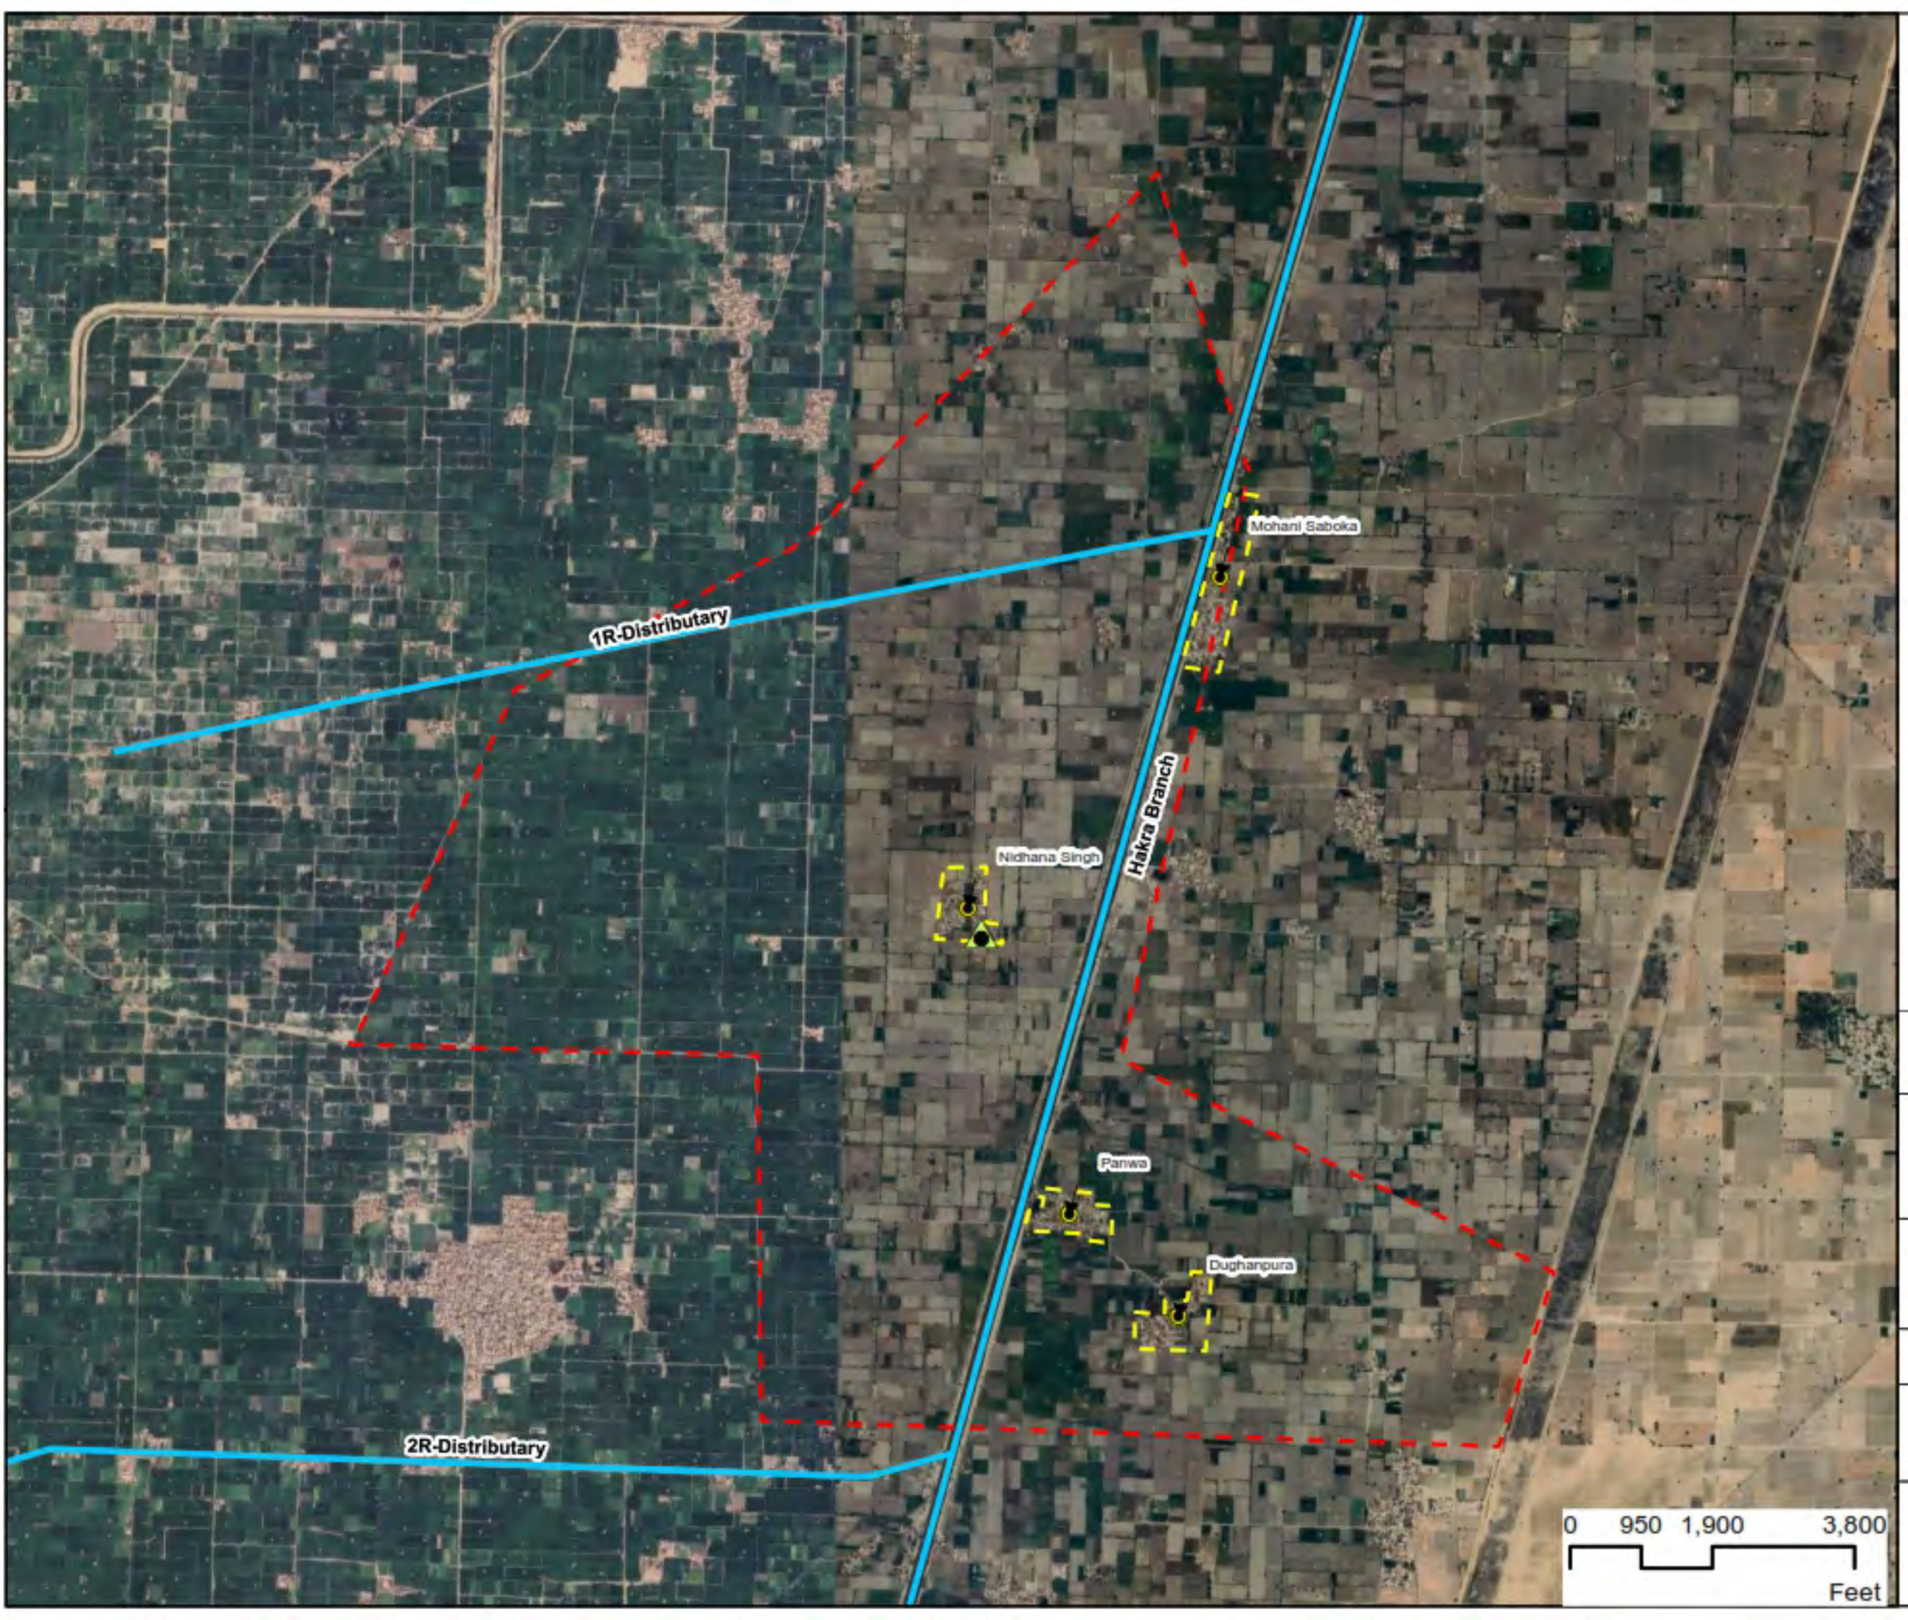

TEHSIL BAHAWALNAGAR

MAUZA SANDAR BASHNOI

LATITUDE: 29.756
LONGITUDE: 73.3

LEGEND

- CENTER
- MAJOR SETTELMENT
- CANAL
- SETTELMENT BOUNDARY
- PROJECT AREA BOUNDARY

TITLE:
SATELLITE MAPS

PROJECT:
Engineering Design & Construction Supervision, Punjab Rural Sustainable Water Supply & Sanitation Project, Cluster South-III

DATE:	02-03-26
DRAWN:	ASAD
DESGIN:	ENGR.FAIEZ
APPROVED:	ENGR. IHSAN UL HAQ

TITLE:
PRMSC-BWN-SB-SM-01

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

INFRASTRUCTURE CONSULTANT
ENVIRONMENTAL TECHNOLOGIES
ASIAN CONSULTING ENGINEERS
www.asiancon.com

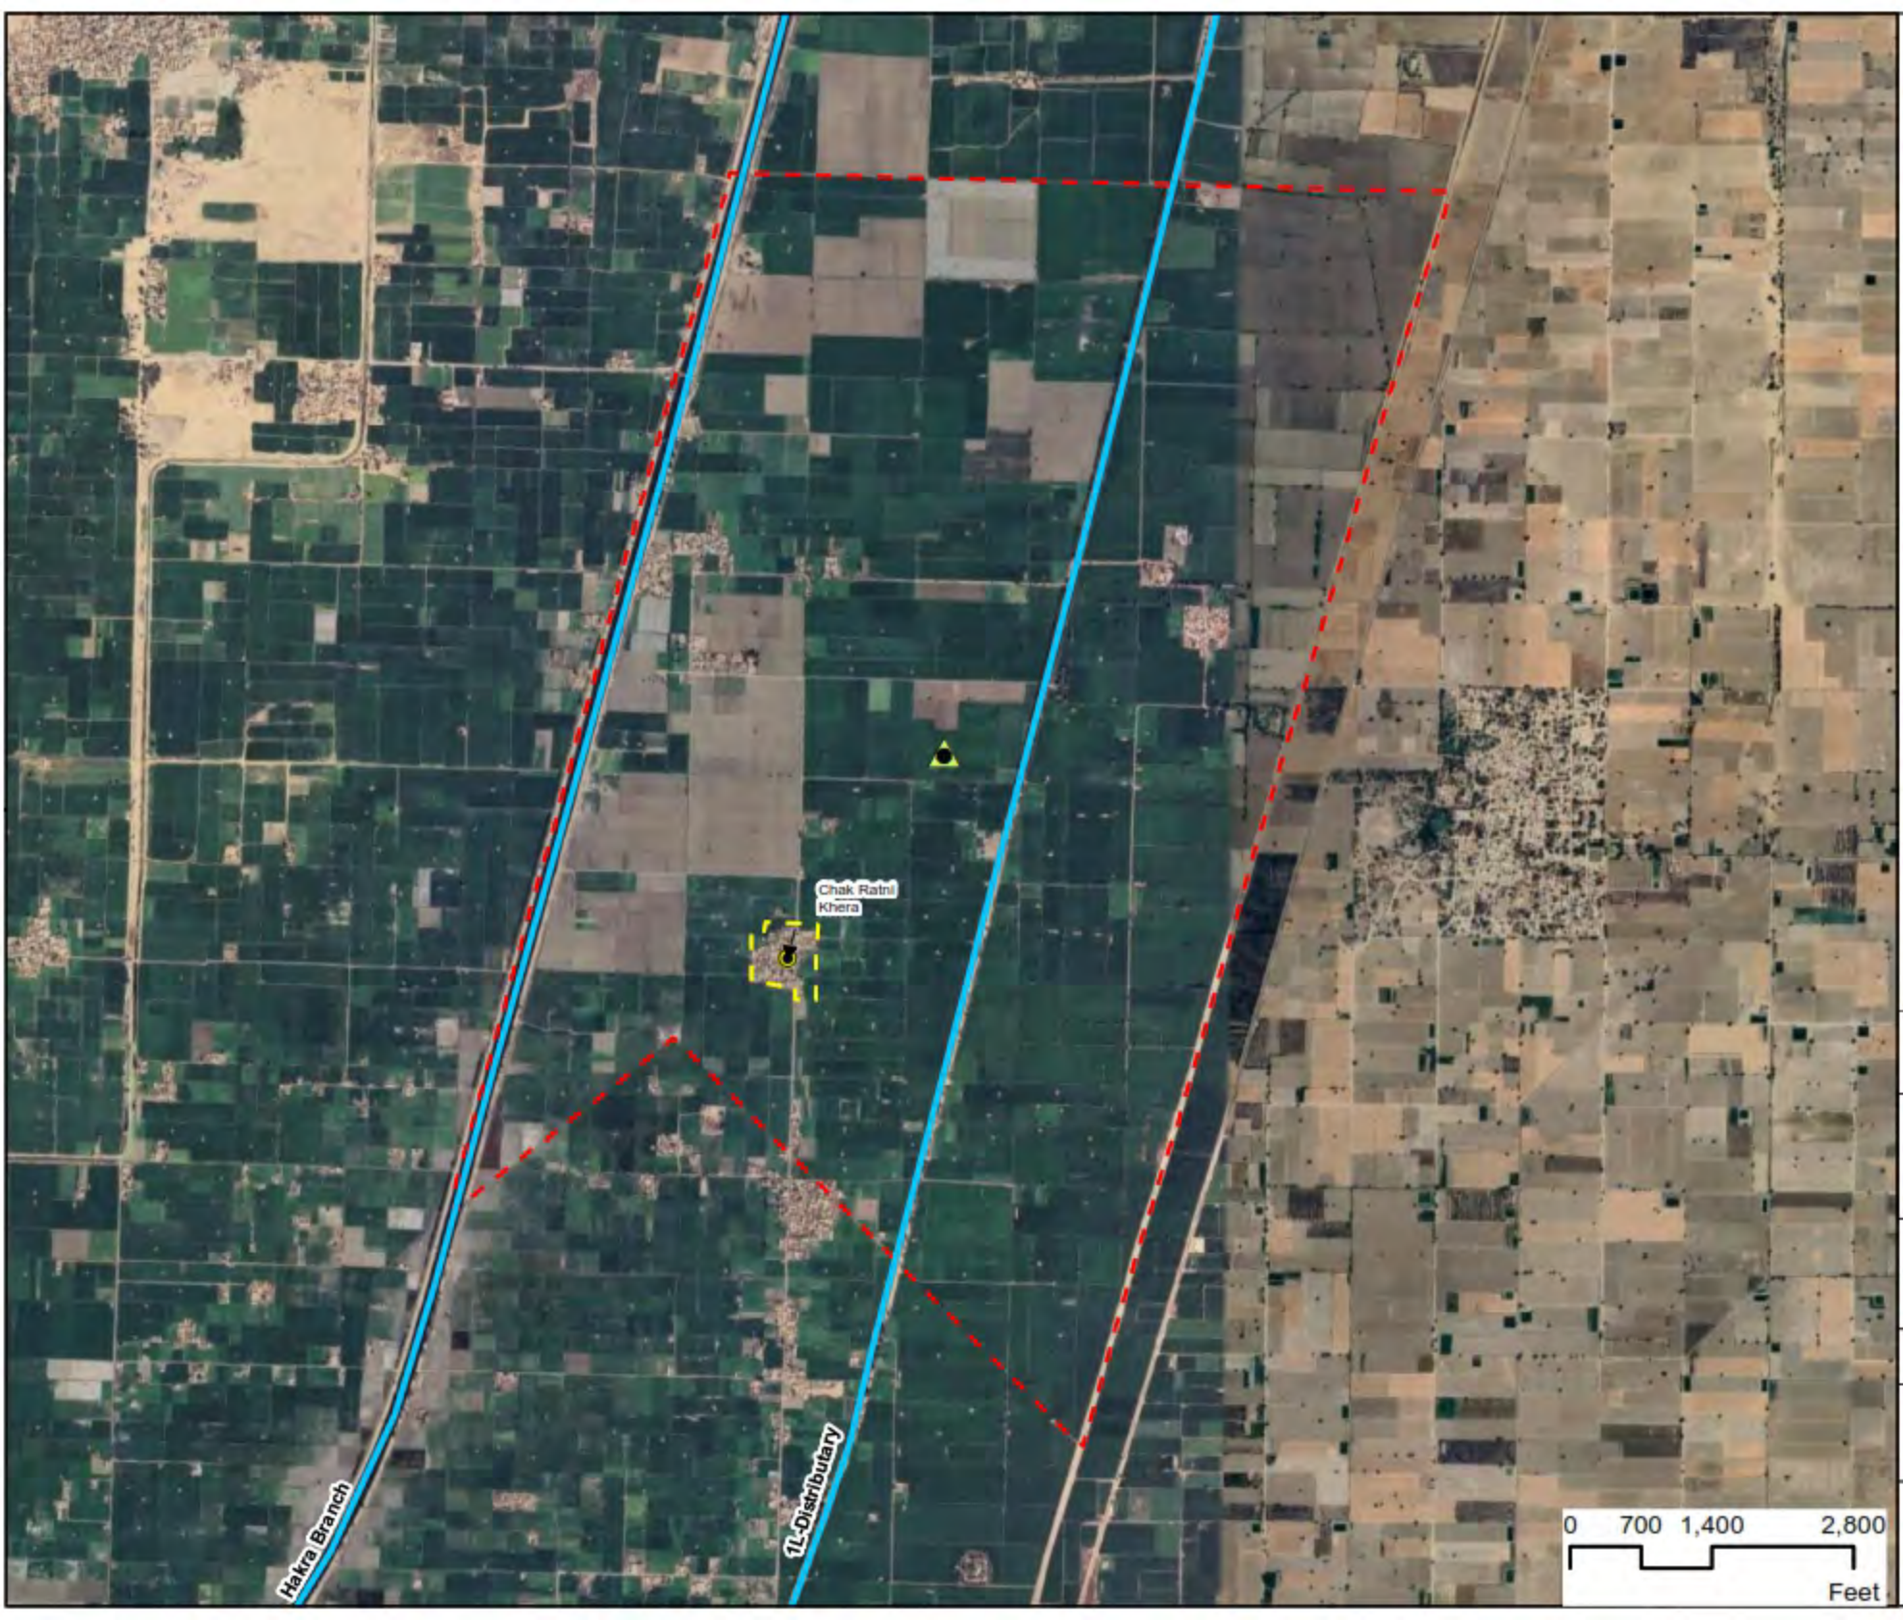

N
W E
S

TEHSIL BAHAWALNAGAR

MAUZA SHER SINGH WALA

LATITUDE: 29.656
LONGITUDE: 73.287

LEGEND

- CENTER
- MAJOR SETTELMENT
- CANAL
- SETTELMENT BOUNDARY
- PROJECT AREA BOUNDARY

TITLE:
SATELLITE MAPS

PROJECT:
Engineering Design & Construction Supervision, Punjab Rural Sustainable Water Supply & Sanitation Project, Cluster South-III

DATE:	02-03-26
DRAWN:	ASAD
DESGIN:	ENGR.FAIEZ
APPROVED:	ENGR. IHSAN UL HAQ

TITLE:
PRMSC-BWN-SSW-SM-01

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

INFRASTRUCTURE CONSULTANT
ENVIRONMENTAL TECHNOLOGIES
ASIAN CONSULTING ENGINEERS
www.asiancon.com

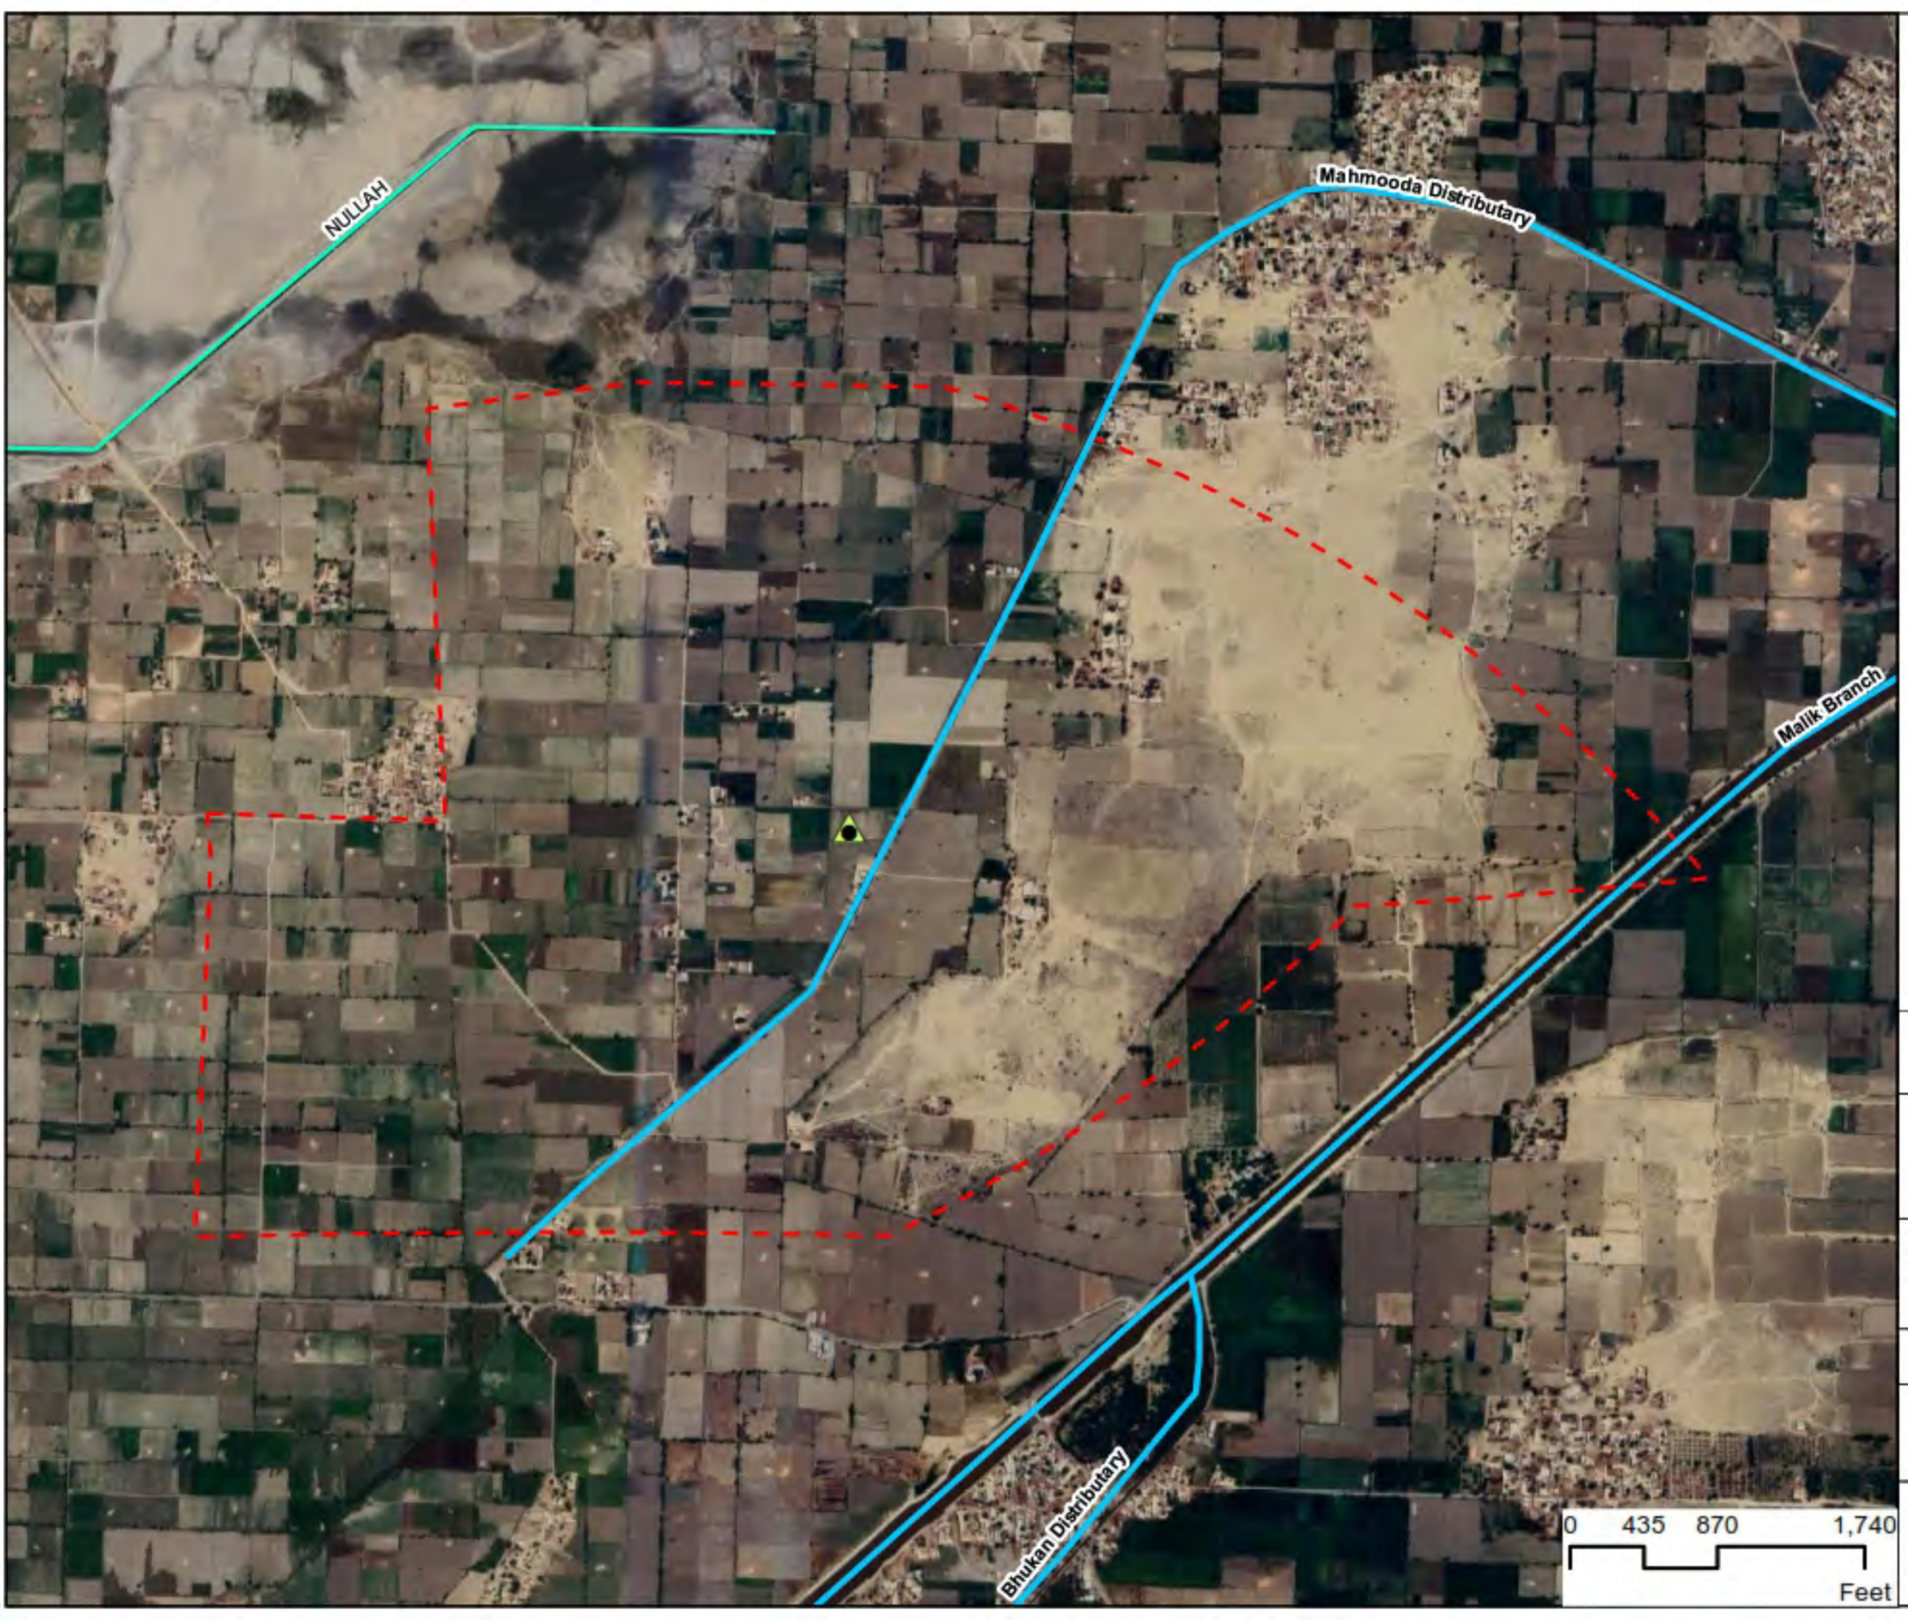

N
W E
S

TEHSIL BAHAWALNAGAR

MAUZA TOBI QAMAR-UD-DIN

LATITUDE: 29.908
LONGITUDE: 73.328

LEGEND

- CENTER
- NULLAH
- CANAL
- PROJECT AREA BOUNDARY

TITLE:
SATELLITE MAPS

PROJECT:
Engineering Design & Construction Supervision, Punjab Rural Sustainable Water Supply & Sanitation Project, Cluster South-III

DATE:	02-03-26
DRAWN:	ASAD
DESGIN:	ENGR.FAIEZ
APPROVED:	ENGR. IHSAN UL HAQ

TITLE:
PRMSC-BWN-TQ-SM-01

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

INFRASTRUCTURE CONSULTANT
ENVIRONMENTAL TECHNOLOGIES
ASIAN CONSULTING ENGINEERS
www.asiancon.com

AKKANWALI KHURD&SHER MOHD(MVS)

KEY PLAN

Revenue Village: Mvs Akanwali Khurd & Sher Mohammad Main Sheet

District:	Bahawalnagar
Tehsil:	Bahawalnagar
Revenue Village:	Mvs Akanwali Khurd & Sher Mo

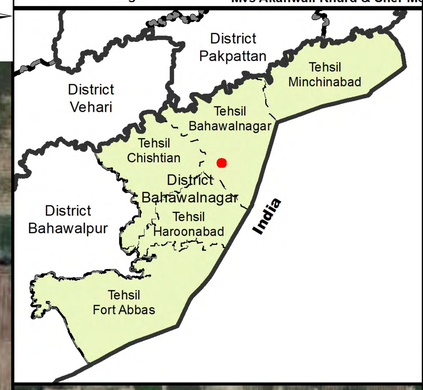

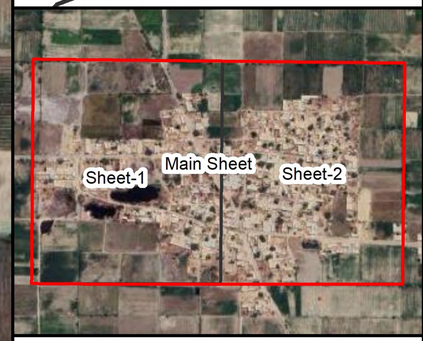

GL=508.00
IL=506.25

SEPTIC TANK-T1
Plot Size =
1.59 Marla

GL=506.00
IL=504.37

SEPTIC TANK-T4
Plot Size =
3.04 Marla

GL=507.58
IL=506.23

SEPTIC TANK-T1
Plot Size =
1.59 Marla

3" HDPE ULTIMATE DISPOSAL TO WATER COURSE

Akanwali

Title:
Proposed Drainage Network Plan

Legend:

- SETTLEMENT
- NODE
- 3" HDPE PIPE
- DRAIN TYPE-1
- EXISTING SULLAGE CARRIER
- SEPTIC TANK
- SETTLEMENT BOUNDARY

Drain Type 1=8980 Rft

Sullage Carrier=6438 Rft

Scale: 1:2,100
1 inch = 175 feet
Paper Size: A3

0 40 80 160
Kilometers

Project:

Engineering Design & Construction Supervision, Punjab Rural Sustainable Water Supply & Sanitation Project, Cluster South III

PRWSC

ENVIRONMENTAL TECHNOLOGIES

ASIAN CONSULTING ENGINEERS www.asiancon.com

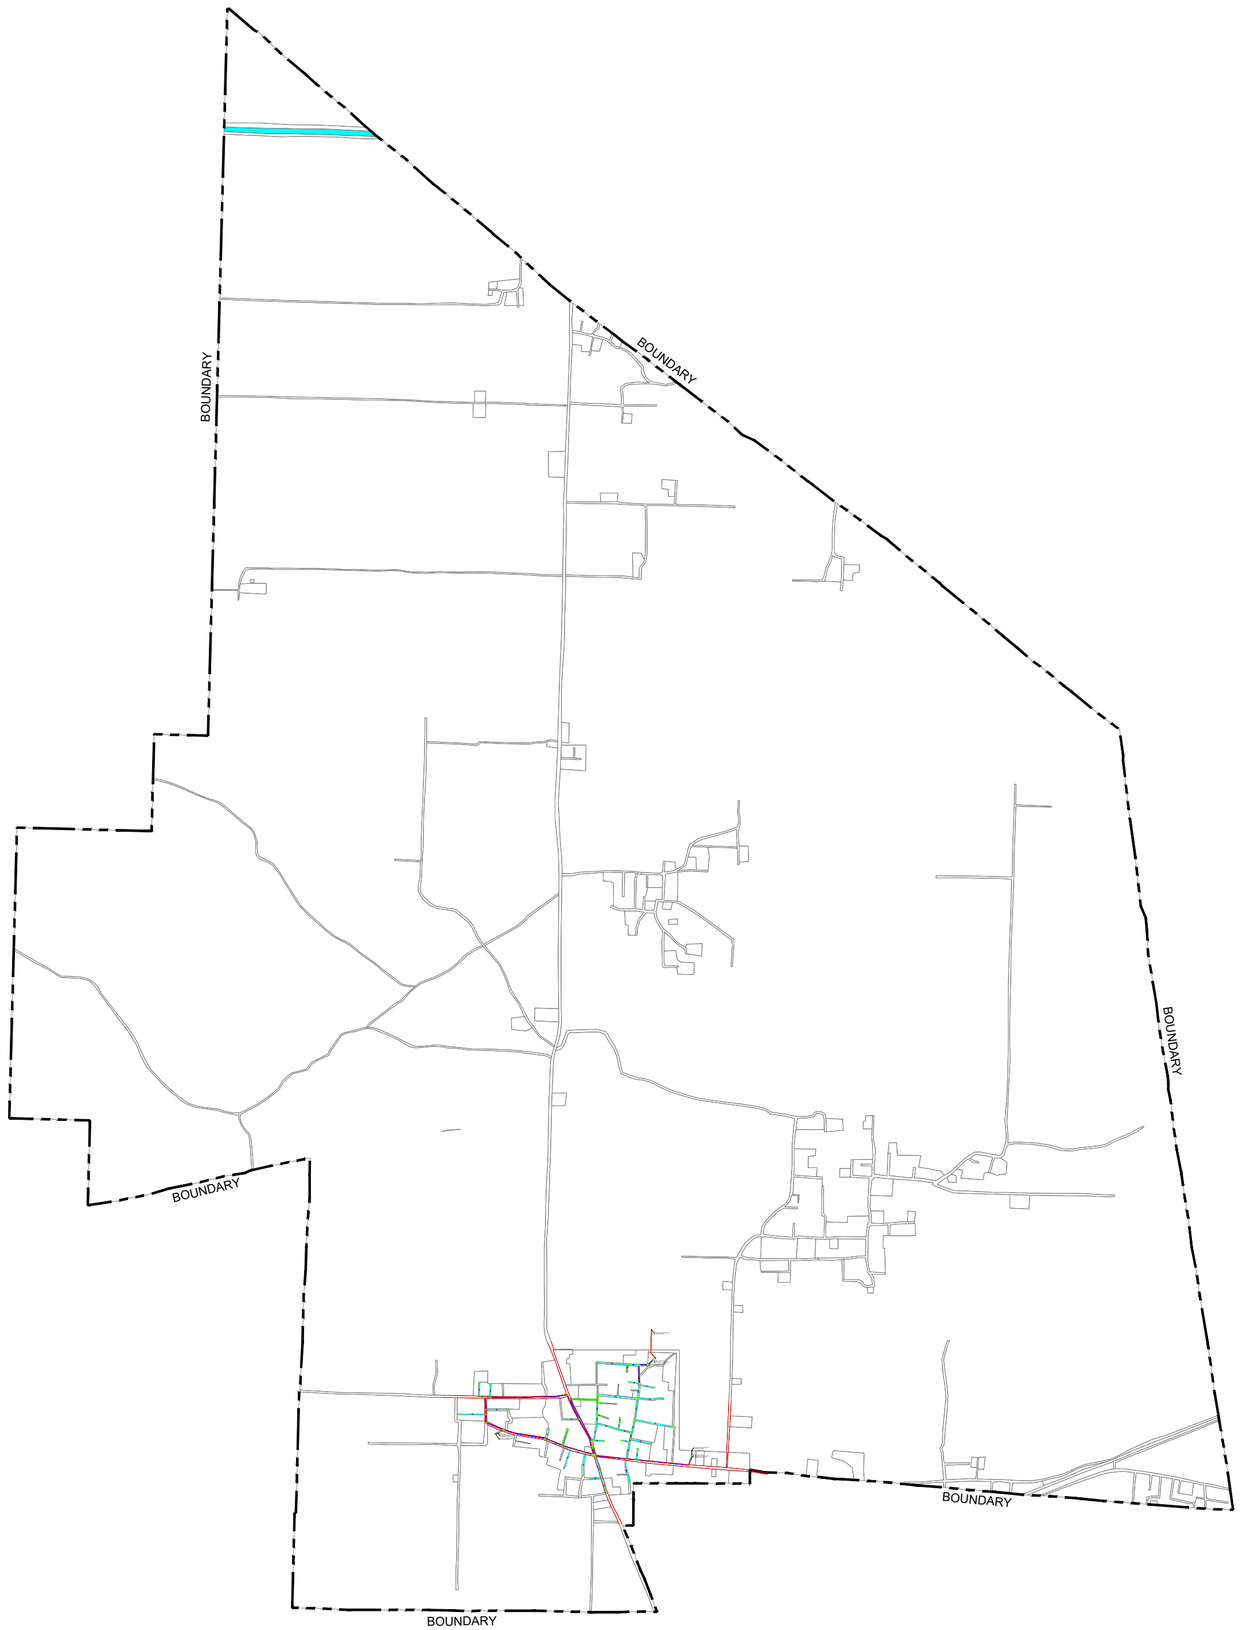

LEGEND:

- DRAIN TYPE-I
- SULLAGE CARRIER
- Ø3" HDPE PIPE
- EXISTING SOLING
- METALLED ROAD
- PROPOSED CULVERT
- BOUNDARY

VILLAGE: AKKANWALI KHURD&SHER MUHAMMAD (MVS)(BWN)

TITLE.

DRAINAGE SYSTEM KEY PLAN

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 900'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	02-01-2026	DETAILED DESIGN	MUNEEB	ENGR. FAEIZ	ENGR. IHSAN-UL-HAQ
02	12-02-2026	DETAILED DESIGN	MUNEEB	ENGR. FAEIZ	ENGR. IHSAN-UL-HAQ
03	19-04-2026	DETAILED DESIGN	HANNAN	ENGR. FAEIZ	ENGR. IHSAN-UL-HAQ
04					
05					
06					
07					

DRAWING Nº: PRMSC-BWN-AWS-SEW-KP-00

SHEET 00 OF 00

REV 01

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT
ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

PRMSC-BWN-AWS-SEW-KP-00

LAYOUT PLAN

Revenue Village: Mvs Akanwali Khurd & Sher Mohammad Sheet-1

SEPTIC TANK-T4
Plot Size =
3.04 Marla

District:	Bahawalnagar
Tehsil:	Bahawalnagar
Revenue Village:	Mvs Akanwali Khurd & Sher Mo

Title:
Proposed Drainage Network Plan

Legend:

- NODE
- 6" uPVC PIPE
- DRAIN TYPE-1
- EXISTING SULLAGE CARRIER
- SEPTIC TANK
- SETTLEMENT BOUNDARY

Drain Type 1=8980 Rft
Sullage Carrier=6438 Rft

Scale: 1:1,500
1 inch = 125 feet
Paper Size: A3

0 40 80 160
Kilometers

Project:
Engineering Design & Construction Supervision, Punjab Rural Sustainable Water Supply & Sanitation Project, Cluster South III

Revenue Village: Mvs Akanwali Khurd & Sher Mohammad Sheet-2

District:	Bahawalnagar
Tehsil:	Bahawalnagar
Revenue Village:	Mvs Akanwali Khurd & Sher Mo

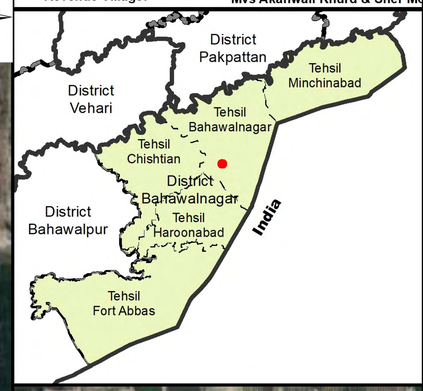

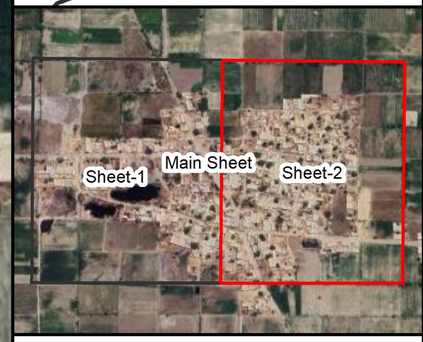

GL=508.00
IL=506.25

SEPTIC TANK-T1
Plot Size =
1.59 Marla

GL=507.7
IL=506.2

SEPTIC TANK-T1
Plot Size =
1.59 Marla

Akanwali

Title:
Proposed Drainage Network Plan

Legend:

- SETTLEMENT
- NODE
- 3" HDPE PIPE
- DRAIN TYPE-1
- EXISTING SULLAGE CARRIER
- SEPTIC TANK
- SETTLEMENT BOUNDARY

Drain Type 1=8980 Rft

Sullage Carrier=6438 Rft

Scale: 1:1,500
1 inch = 125 feet
Paper Size: A3

0 40 80 160
Kilometers

Project:
Engineering Design & Construction Supervision, Punjab Rural Sustainable Water Supply & Sanitation Project, Cluster South III

PRMSC ENVIRONMENTAL TECHNOLOGIES ASIAN CONSULTING ENGINEERS www.asiancon.com

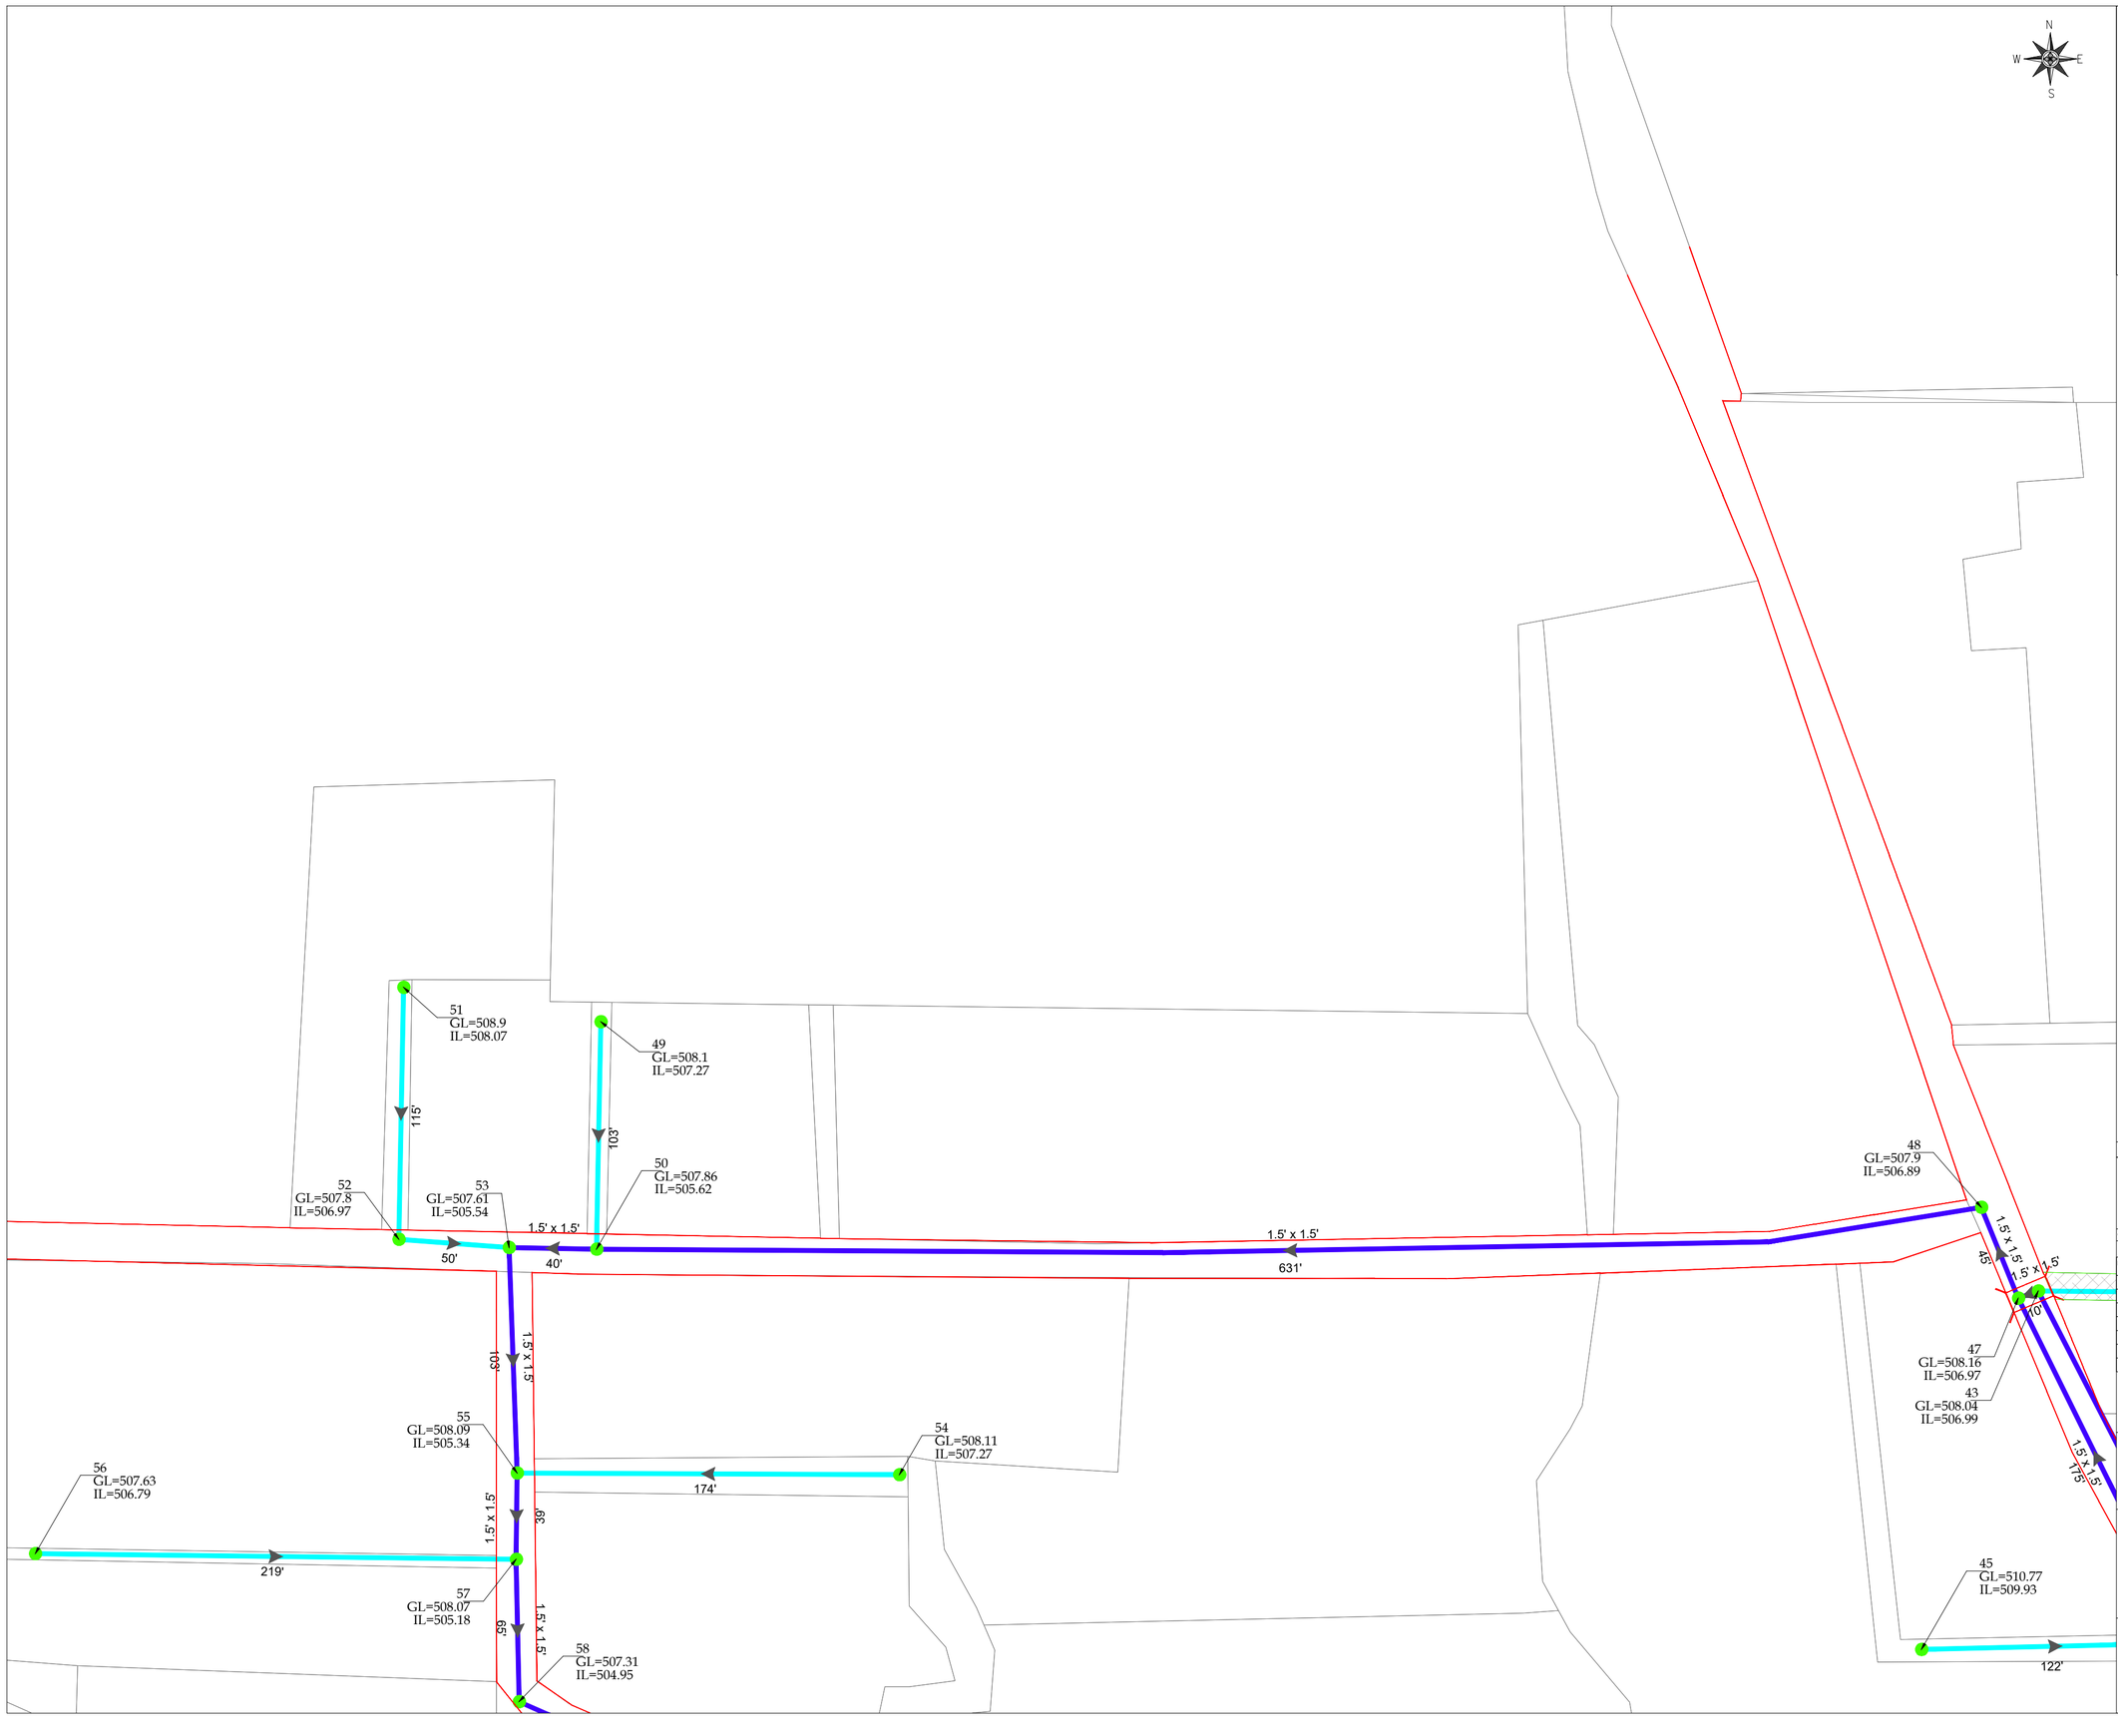

KEY PLAN

LEGEND:

- DRAIN TYPE-I
- SULLAGE CARRIER
- Ø3" HDPE PIPE
- EXISTING SOLING
- METALLED ROAD
- PROPOSED CULVERT
- BOUNDARY

VILLAGE: AKKANWALI KHURD&SHER MUHAMMAD (MVS)(BWN)

TITLE.

DRAINAGE SYSTEM LAYOUT PLAN-01

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	02-01-2026	DETAILED DESIGN	MUNEEB	ENGR FAIEZ	ENGR IHSAN-UL-HAQ
02	12-02-2026	DETAILED DESIGN	MUNEEB	ENGR FAIEZ	ENGR IHSAN-UL-HAQ
03	19-04-2026	DETAILED DESIGN	HANNAN	ENGR FAIEZ	ENGR IHSAN-UL-HAQ
04					
05					
06					
07					

DRAWING N°:	SHEET	REV
PRMSC-BWN-AWS-SEW-LP-01	01 OF 04	01

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS
www.asiacon.com.pk

PRMSC-BWN-AWS-SEW-LP-01

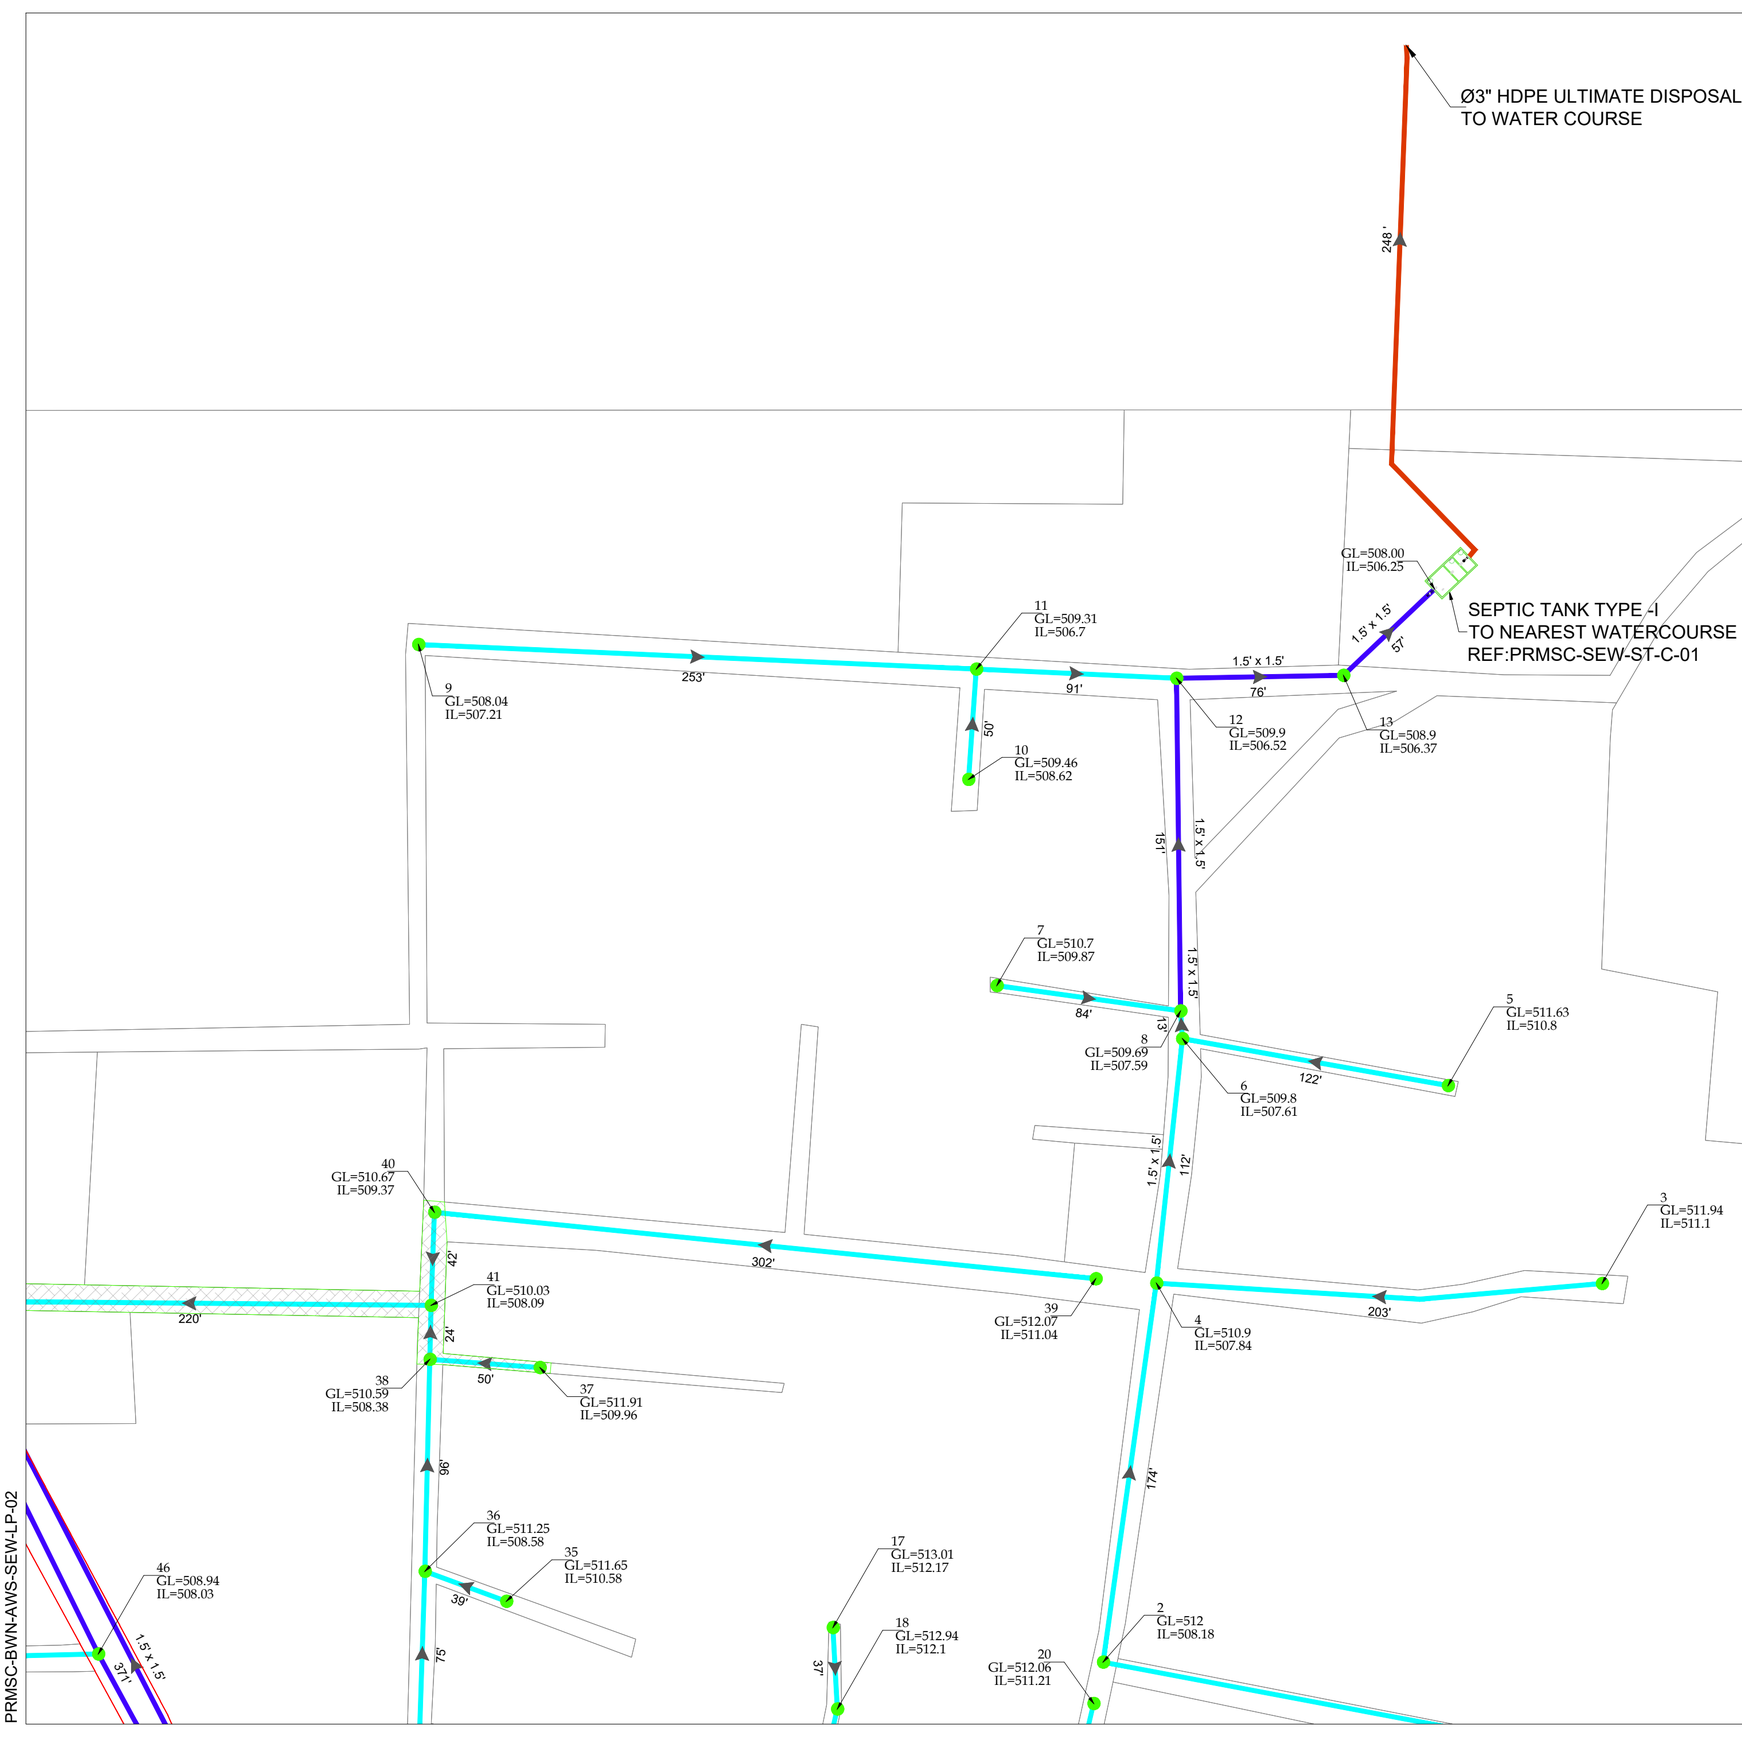

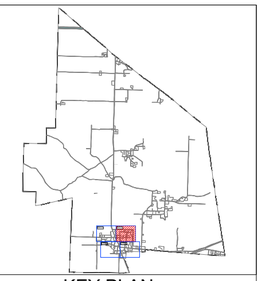

KEY PLAN

LEGEND:

- DRAIN TYPE-I
- SULLAGE CARRIER
- Ø3" HDPE PIPE
- EXISTING SOLING
- METALLED ROAD
- PROPOSED CULVERT
- BOUNDARY

VILLAGE: AKKANWALI KHURD&SHER MUHAMMAD (MVS)(BWN)

TITLE.

DRAINAGE SYSTEM LAYOUT PLAN-02

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	02-01-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN UL HAQ
02	12-02-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN UL HAQ
03	19-04-2026	DETAILED DESIGN	HANNAN	ENGR. FAIEZ	ENGR. IHSAN UL HAQ
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-AWS-SEW-LP-02	02 OF 04	01

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

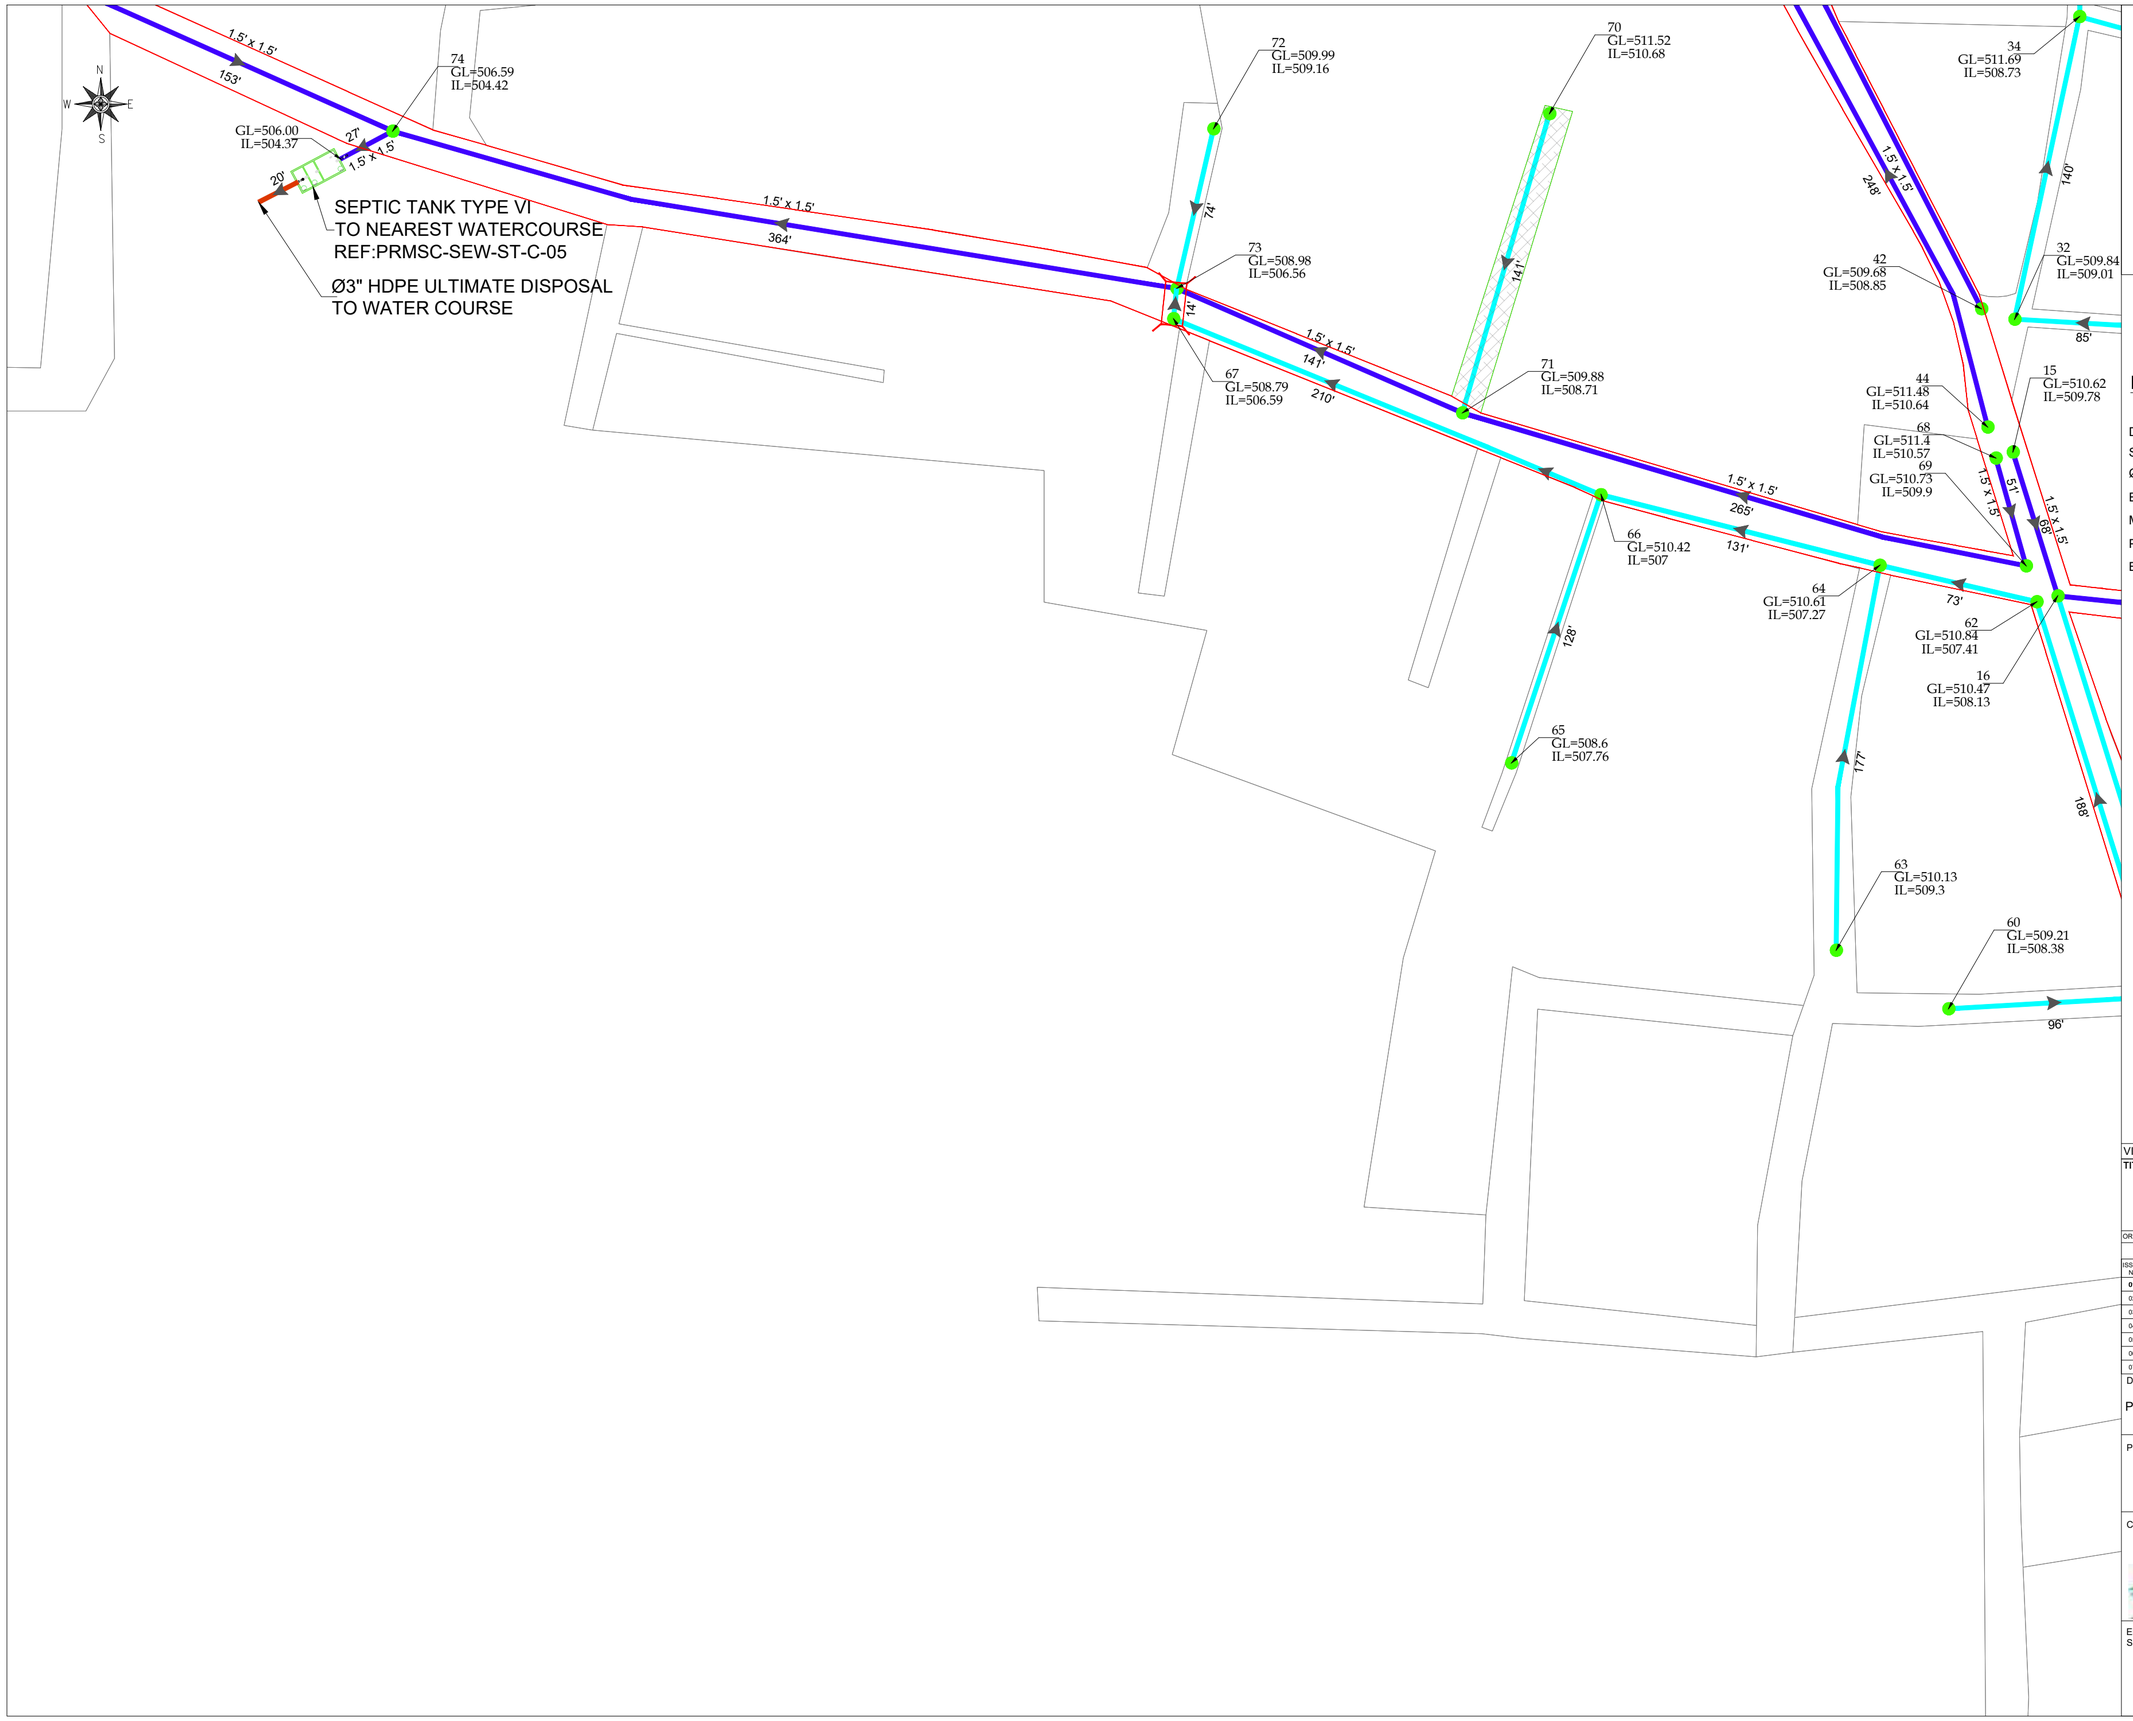

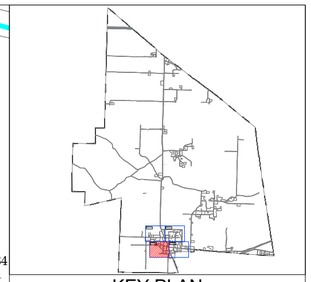

KEY PLAN

LEGEND:

- DRAIN TYPE-I
- SULLAGE CARRIER
- Ø3" HDPE PIPE
- EXISTING SOLING
- METALLED ROAD
- PROPOSED CULVERT
- BOUNDARY

VILLAGE: AKKANWALI KHURD&SHER MUHAMMAD (MVS)(BWN)

TITLE.

DRAINAGE SYSTEM LAYOUT PLAN-03

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	02-01-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02	12-02-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
03	19-04-2026	DETAILED DESIGN	HANNAN	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-AWS-SEW-LP-03	03 OF 04	01

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:
ASIAN CONSULTING ENGINEERS
www.asiancon.com.pv

PRMSC-BWN-AWS-SEW-LP-03

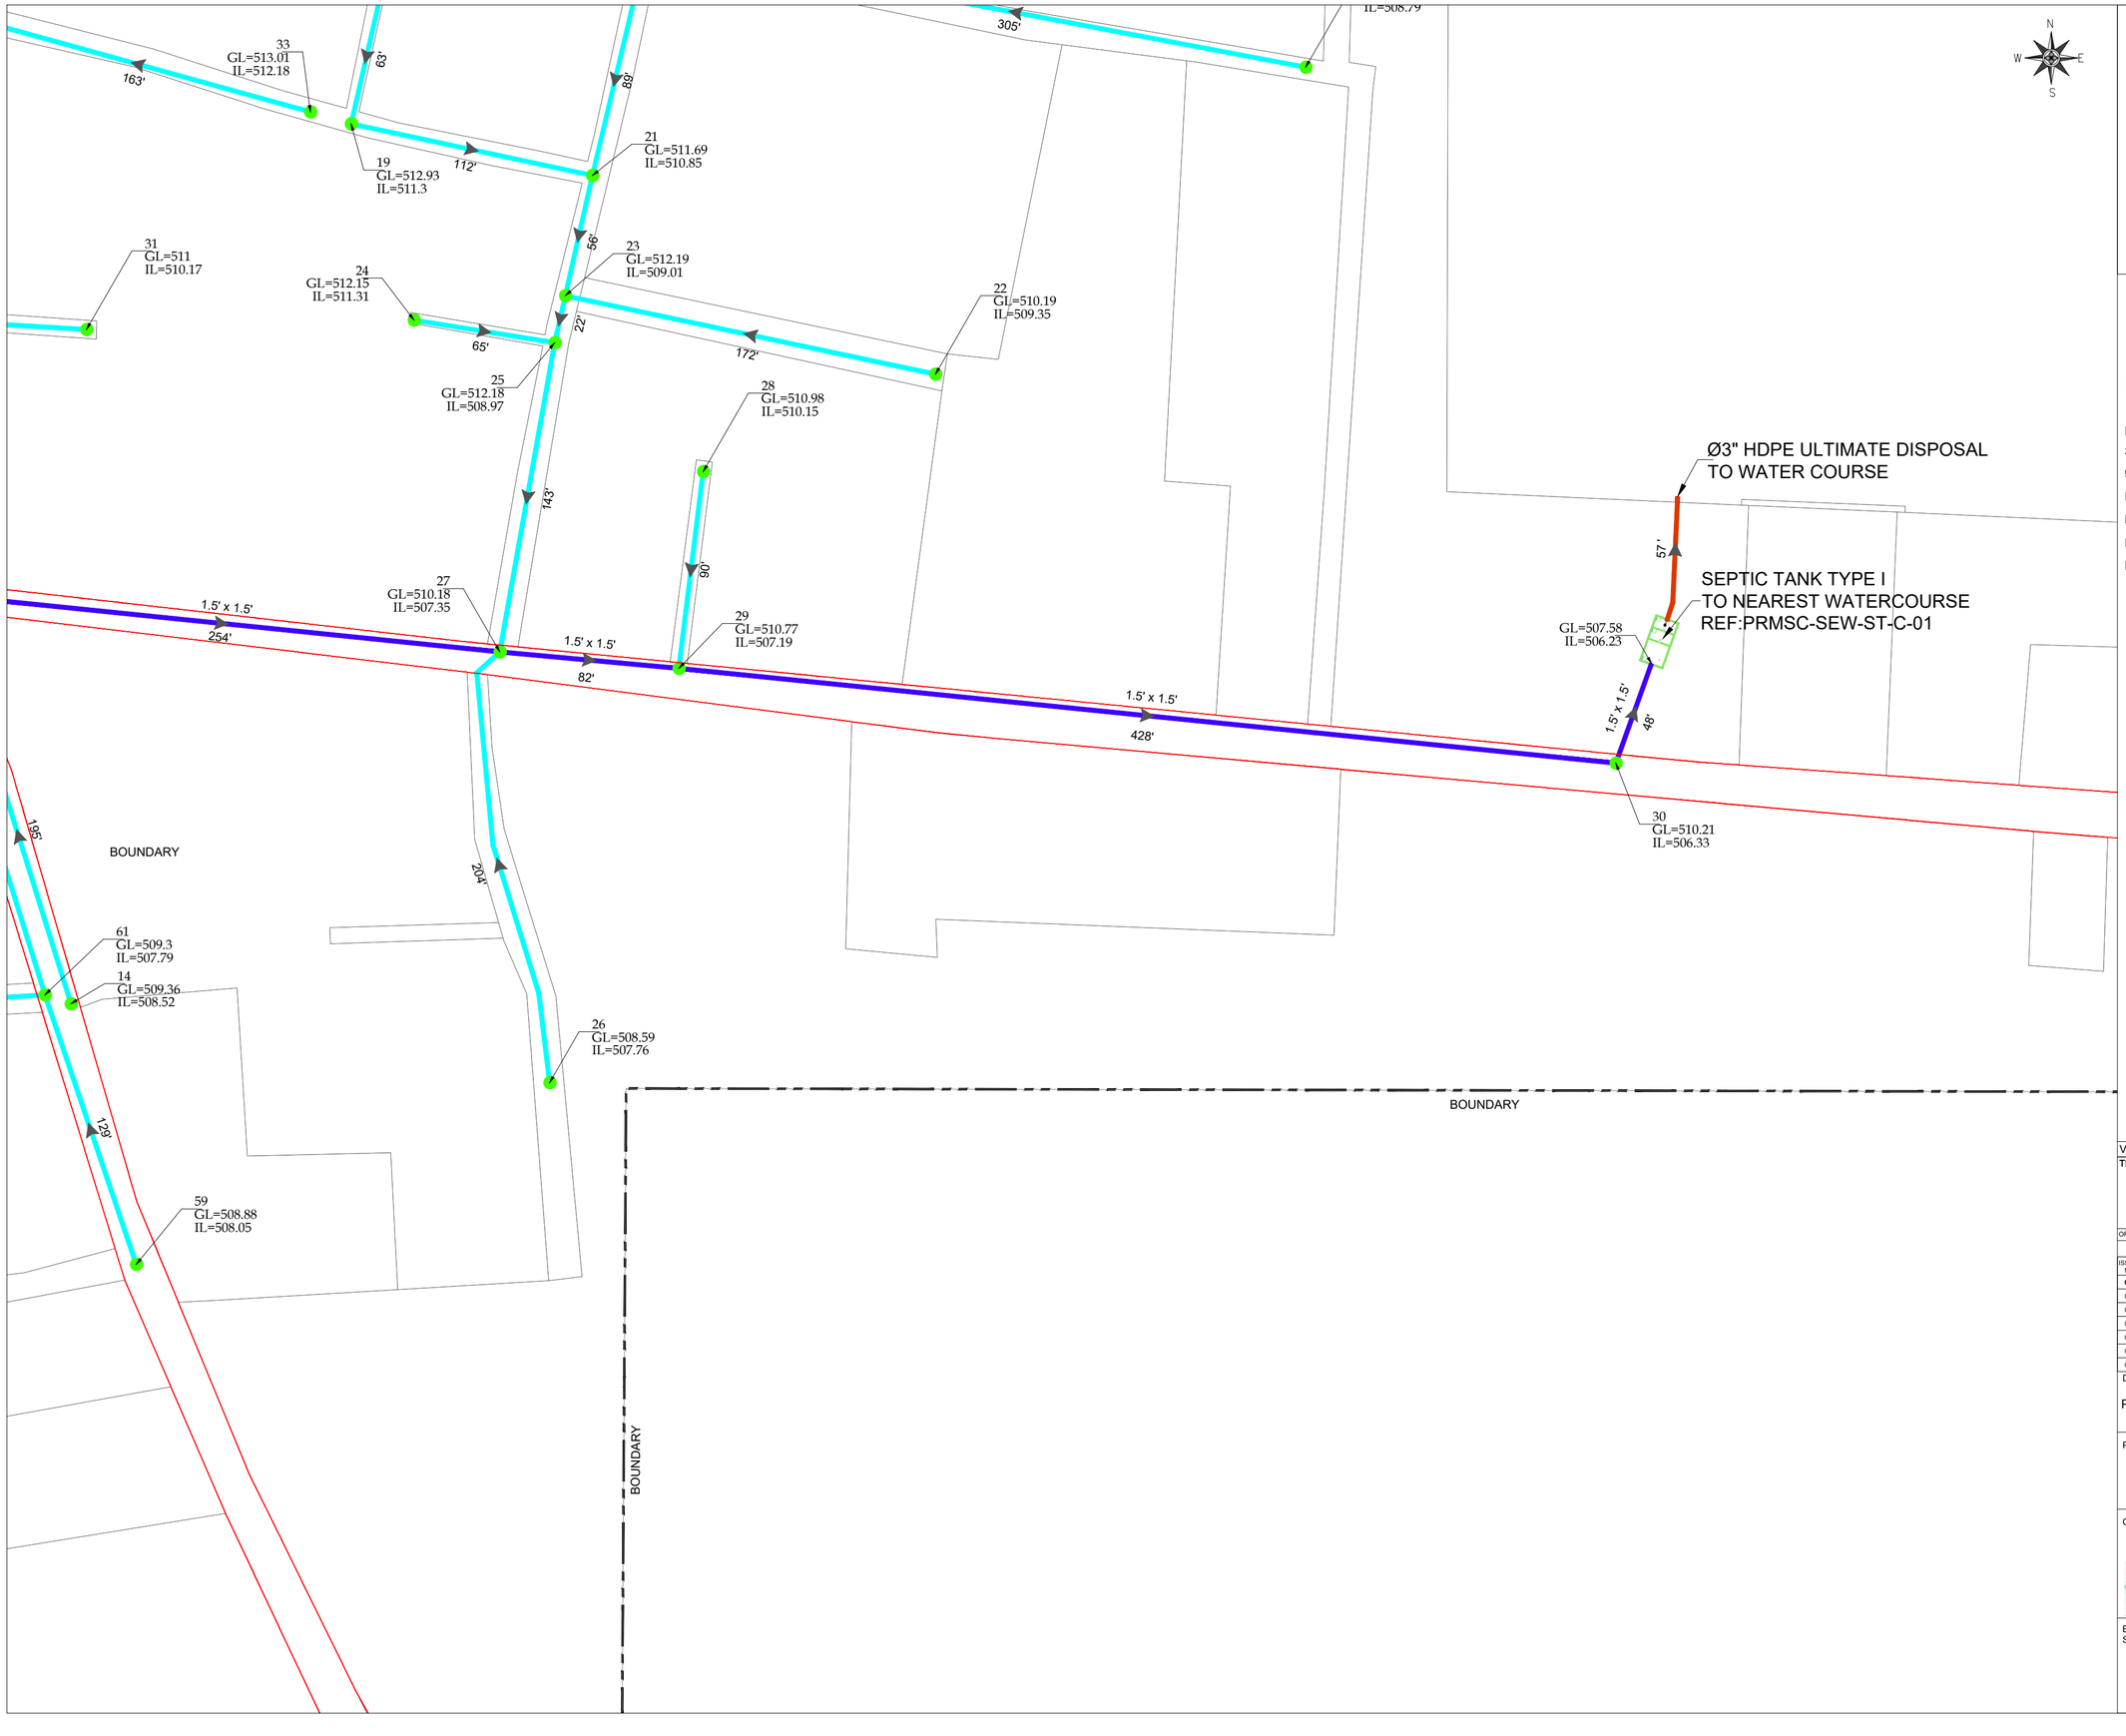

VILLAGE: AKKANWALI KHURD&SHER MUHAMMAD (MVS)(BWN)

TITLE.

DRAINAGE SYSTEM LAYOUT PLAN-04

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	02-01-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02	12-02-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
03	19-04-2026	DETAILED DESIGN	HANNAN	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
04					
05					
06					
07					

DRAWING N°: PRMSC-BWN-AWS-SEW-LP-04

SHEET 04 OF 04

REV 01

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS
www.asianconsultants.com JV

HYDRAULIC STATEMENT

Node		Length	Slope	Elevation Ground	Elevation Ground	Invert	Invert	Depth
FROM	TO	ft	ft/ft	U/S	D/S	U/S	D/S	ft
1	2	305	0.002	509.63	512	508.79	508.18	0.83
2	4	174	0.002	512	510.9	508.18	507.84	3.82
3	4	203	0.016	511.94	510.9	511.1	507.84	0.83
4	6	112	0.002	510.9	509.8	507.84	507.61	3.06
5	6	122	0.026	511.63	509.8	510.8	507.61	0.83
6	8	13	0.002	509.8	509.69	507.61	507.59	2.19
7	8	84	0.027	510.7	509.69	509.87	507.59	0.83
8	12	151	0.002	509.69	509.9	507.59	507.29	2.1
9	11	253	0.002	508.04	509.31	507.21	506.7	0.83
10	11	50	0.003	509.46	509.31	508.62	508.48	0.83
11	12	91	0.002	509.31	509.9	506.7	506.52	2.61
12	13	76	0.002	509.9	508.9	506.52	506.37	3.39
13	Septic Tank Type-I (HH=45)	57	0.002	508.9	508	506.37	506.25	2.53
14	16	195	0.002	509.36	510.47	508.52	508.13	0.83
15	16	68	0.0022	510.62	510.47	509.78	509.64	0.83
16	27	254	0.0031	510.47	510.18	508.13	507.35	2.34
17	18	37	0.002	513.01	512.94	512.17	512.1	0.83
18	19	63	0.002	512.94	512.93	512.1	511.98	0.84
19	21	112	0.004	512.93	511.69	511.3	510.85	1.63
20	21	89	0.004	512.06	511.69	511.21	510.85	0.85
21	23	56	0.002	511.69	512.19	510.85	510.74	0.83
22	23	172	0.002	510.19	512.19	509.35	509.01	0.83
23	25	22	0.002	512.19	512.18	509.01	508.97	3.18
24	25	65	0.002	512.15	512.18	511.31	511.18	0.83
25	27	143	0.002	512.18	510.18	508.97	508.68	3.21
26	27	204	0.002	508.59	510.18	507.76	507.35	0.83
27	29	82	0.002	510.18	510.77	507.35	507.19	2.83
28	29	90	0.0023	510.98	510.77	510.15	509.94	0.83
29	30	428	0.002	510.77	510.21	507.19	506.33	3.59
30	Septic Tank Type-I (HH=45)	48	0.002	510.21	507.58	506.33	506.23	3.87
31	32	85	0.0137	511	509.84	510.17	509.01	0.83
32	34	140	0.002	509.84	511.69	509.01	508.73	0.83
33	34	163	0.0212	513.01	511.69	512.18	508.73	0.83
34	36	75	0.002	511.69	511.25	508.73	508.58	2.96
35	36	39	0.004	511.65	511.25	510.58	510.42	1.08
36	38	96	0.002	511.25	510.59	508.58	508.38	2.68
37	38	50	0.004	511.91	510.59	509.96	509.76	1.95

HYDRAULIC STATEMENT

Node		Length	Slope	Elevation Ground	Elevation Ground	Invert	Invert	Depth
FROM	TO	ft	ft/ft	U/S	D/S	U/S	D/S	ft
38	41	24	0.002	510.59	510.03	508.38	508.34	2.21
39	40	302	0.004	512.07	510.67	511.04	509.83	1.03
40	41	42	0.004	510.67	510.03	509.37	509.2	1.3
41	43	220	0.004	510.03	508.04	508.09	507.21	1.94
42	43	371	0.005	509.68	508.04	508.85	506.99	0.83
43	47	10	0.002	508.04	508.16	506.99	506.97	1.05
44	46	248	0.0105	511.48	508.94	510.64	508.03	0.83
45	46	122	0.0157	510.77	508.94	509.93	508.03	0.83
46	47	175	0.004	508.94	508.16	508.03	507.33	0.91
47	48	45	0.002	508.16	507.9	506.97	506.89	1.19
48	50	631	0.002	507.9	507.86	506.89	505.62	1.02
49	50	103	0.0023	508.1	507.86	507.27	507.03	0.83
50	53	40	0.002	507.86	507.61	505.62	505.54	2.24
51	52	115	0.0096	508.9	507.8	508.07	506.97	0.83
52	53	50	0.0037	507.8	507.61	506.97	506.78	0.83
53	55	103	0.002	507.61	508.09	505.54	505.34	2.07
54	55	174	0.002	508.11	508.09	507.27	506.93	0.83
55	57	39	0.0039	508.09	508.07	505.34	505.18	2.75
56	57	219	0.002	507.63	508.07	506.79	506.36	0.83
57	58	65	0.0036	508.07	507.31	505.18	504.95	2.88
58	74	153	0.0035	507.31	506.59	504.95	504.42	2.36
59	61	129	0.002	508.88	509.3	508.05	507.79	0.83
60	61	96	0.002	509.21	509.3	508.38	508.19	0.83
61	62	188	0.002	509.3	510.84	507.79	507.41	1.51
62	64	73	0.002	510.84	510.61	507.41	507.27	3.43
63	64	177	0.002	510.13	510.61	509.3	508.95	0.83
64	66	131	0.002	510.61	510.42	507.27	507	3.34
65	66	129	0.002	508.6	510.42	507.76	507.51	0.83
66	67	210	0.002	510.42	508.79	507	506.59	3.42
67	73	14	0.002	508.79	508.98	506.59	506.56	2.2
68	69	51	0.0131	511.4	510.73	510.57	509.9	0.83
69	71	265	0.0032	510.73	509.88	509.9	509.04	0.83
70	71	141	0.014	511.52	509.88	510.68	508.71	0.83
71	73	141	0.004	509.88	508.98	508.71	508.14	1.17
72	73	74	0.0349	509.99	508.98	509.16	506.56	0.83
73	74	364	0.0022	508.98	506.59	506.56	505.75	2.42
74	Septic Tank Type-VI (HH=140)	27	0.002	506.59	506	504.42	504.37	2.17

VILLAGE: AKKANWALI KHURD&SHER MUHAMMAD (MVS)(BWN)

TITLE.

HYDRAULIC STATEMENT

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	02-01-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ HSAN	ENGR. HSAN-UL-HAQ
02	12-02-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ HSAN	ENGR. HSAN-UL-HAQ
03	19-04-2026	DETAILED DESIGN	HANNAN	ENGR. FAIEZ HSAN	ENGR. HSAN-UL-HAQ
04					
05					
06					
07					

DRAWING Nº:

PRMSC-KPT-MTI-SEW-KP-00

SHEET 00 OF 00

REV 00

PROJECT:

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER CENTRAL

CLIENT:

PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ENVIROLEVEL TECHNOLOGIES ASIAN CONSULTING ENGINEERS www.asiancon.com

PRMSC-KPT-MK-SEW-HS-00

KARTAR SINGH

KEY PLAN

Revenue Village: Kartar Singh Main Sheet

GL=537.00
IL=534.90

SEPTIC TANK-T1
Plot Size=1.59
Marla

GL=531.23
IL=530.39

SEPTIC TANK-T5
Plot Size=3.42
Marla

Kat Mehr Singh

District:	Bahawalnagar
Tehsil:	Bahawalnagar
Revenue Village:	Kartar Singh



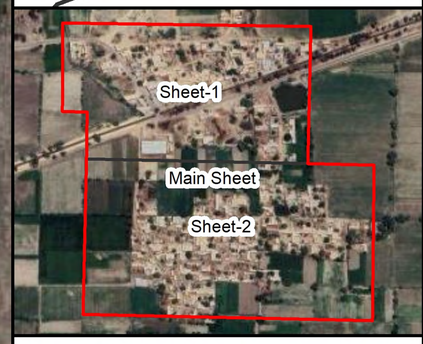

Title:
Proposed Drainage Network Plan

Legend:

- SETTLEMENT
- NODE
- 3" HDPE PIPE
- DRAIN TYPE-1
- SULLAGE CARRIER
- SEPTIC TANK
- SETTLEMENT BOUNDARY

Drain Type 1=8980 Rft

Sullage Carrier= 6438 Rft

Scale: 1:1,800
1 inch = 150 feet
Paper Size: A3

0 40 80 160
Kilometers

Project:

Engineering Design & Construction Supervision, Punjab Rural Sustainable Water Supply & Sanitation Project, Cluster South III

PRWSC
ENVIRONMENTAL TECHNOLOGIES
ASIAN CONSULTING ENGINEERS www.asiancon.com

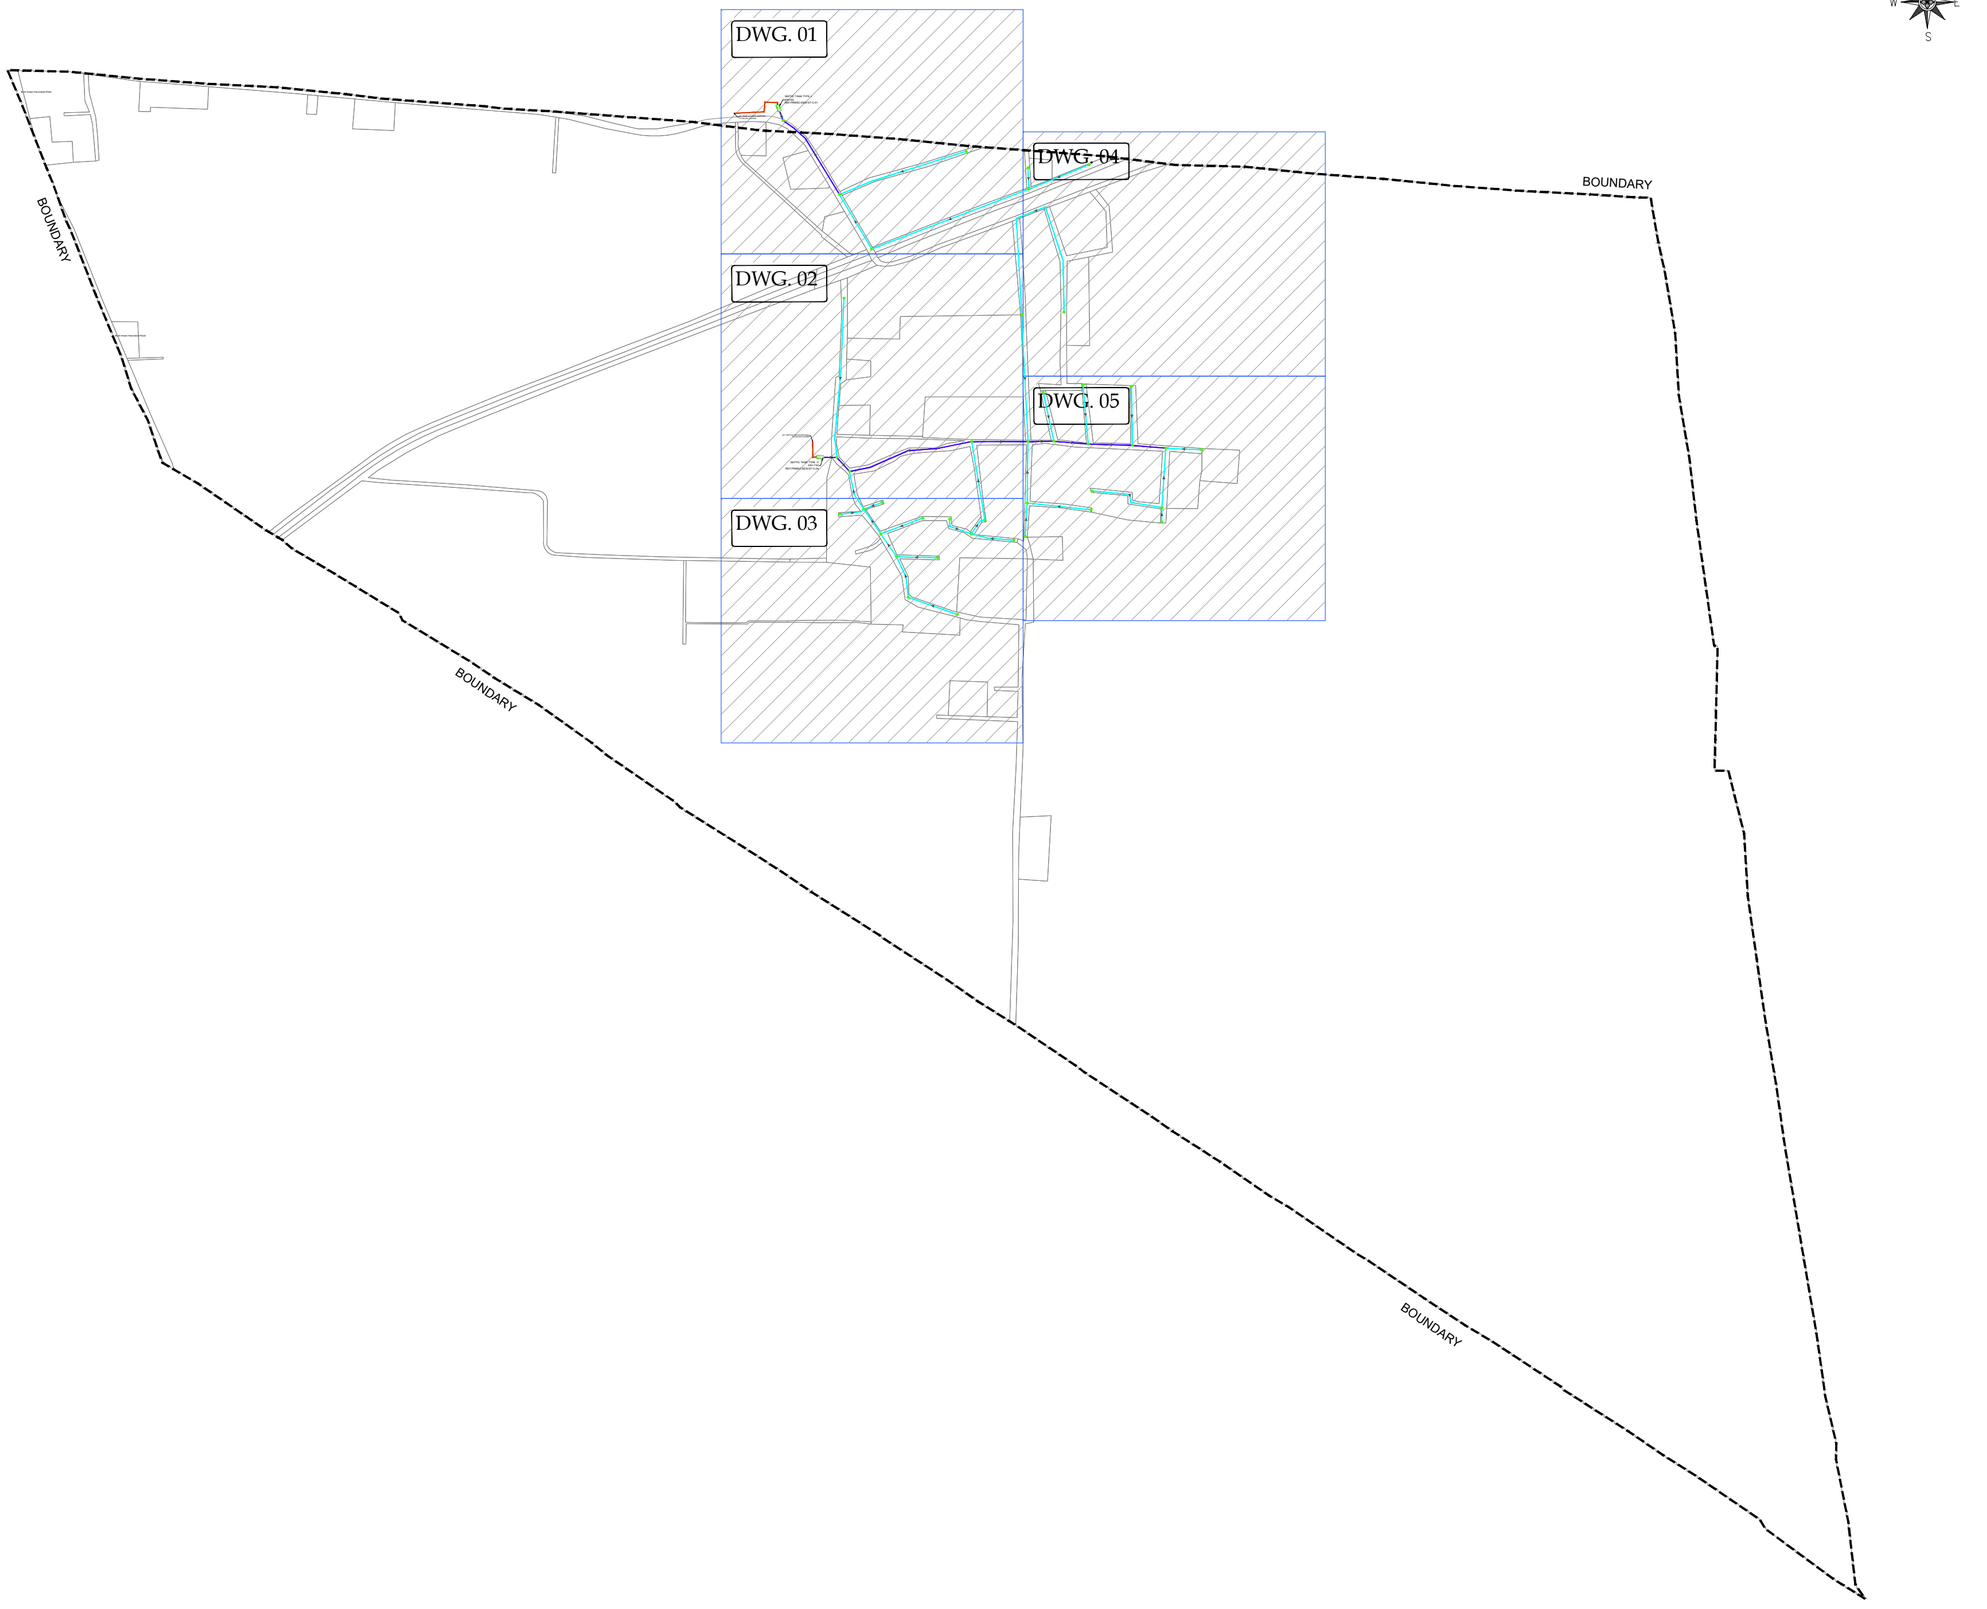

LEGEND:

- DRAIN TYPE - I
- SULLAGE CARRIER
- Ø3" HDPE PIPE
- BOUNDARY

VILLAGE: KARTAR SINGH (BWN)

TITLE.

DRAINAGE SYSTEM KEY PLAN

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 350'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	20-04-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-KTS-SEW-KP-00	00 OF 00	00

PROJECT:

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:

PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT

ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

PRMSC-BWN-KTS-SEW-KP-00

LAYOUT PLAN

Revenue Village: Kartar Singh Sheet-1

GL=537.00
IL=534.90

SEPTIC TANK-T1
Plot Size=1.59 Marla

3" HDPE ULTIMATE DISPOSAL TO WATER COURSE

ND-7
GL=538.1
IL=534.96

ND-6
GL=539.77
IL=535.56

ND-5
GL=539.27
IL=537.30

ND-4
GL=538.9
IL=535.96

ND-2
GL=539.3
IL=537.75

ND-1
GL=538.28
IL=537.45

ND-3
GL=538.37
IL=537.05

ND-40
GL=533.41
IL=532.58

ND-9
GL=536.83
IL=535.99

ND-8
GL=539.04
IL=538.7

ND-10
GL=539.01
IL=536.48

ND-37
GL=538.4
IL=536.64

N

District: Bahawalnagar
Tehsil: Bahawalnagar
Revenue Village: Kartar Singh

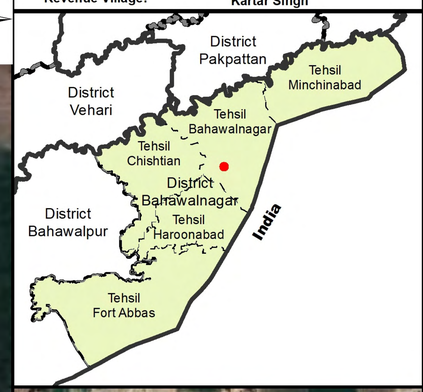

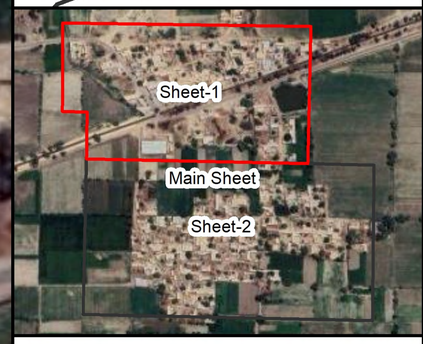

Title:
Proposed Drainage Network Plan

Legend:

- NODE
- 3" HDPE PIPE
- DRAIN TYPE-1
- SULLAGE CARRIER
- SEPTIC TANK
- SETTLEMENT BOUNDARY

Drain Type 1=8980 Rft
Sullage Carrier= 6438 Rft

Scale: 1:1,300
1 inch = 108 feet
Paper Size: A3

0 40 80 160
Kilometers

Project:
Engineering Design & Construction Supervision, Punjab Rural Sustainable Water Supply & Sanitation Project, Cluster South III

PRWSC
ENVIRONMENTAL TECHNOLOGIES
ASIAN CONSULTING ENGINEERS
www.asiancon.com

Revenue Village: Kartar Singh Sheet-2

District:	Bahawalnagar
Tehsil:	Bahawalnagar
Revenue Village:	Kartar Singh

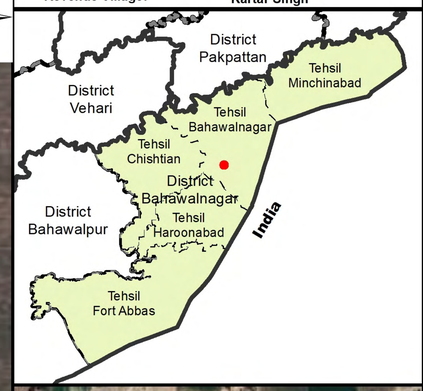

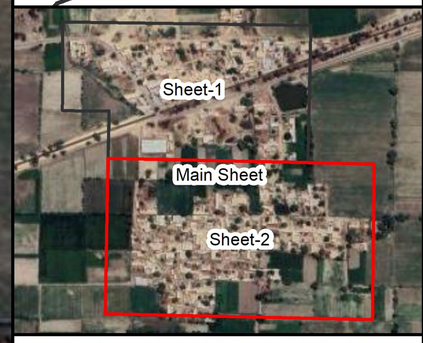

Title:
Proposed Drainage Network Plan

Legend:

- SETTLEMENT
- NODE
- 3" HDPE PIPE
- DRAIN TYPE-1
- SULLAGE CARRIER
- SEPTIC TANK
- SETTLEMENT BOUNDARY

Drain Type 1=8980 Rft

Sullage Carrier= 6438 Rft

Scale: 1:1,400
1 inch = 117 feet
Paper Size: A3

0 40 80 160
Kilometers

Project:

Engineering Design & Construction Supervision, Punjab Rural Sustainable Water Supply & Sanitation Project, Cluster South III

PRWSC ENVIRONMENTAL TECHNOLOGIES ASIAN CONSULTING ENGINEERS www.asiancon.com

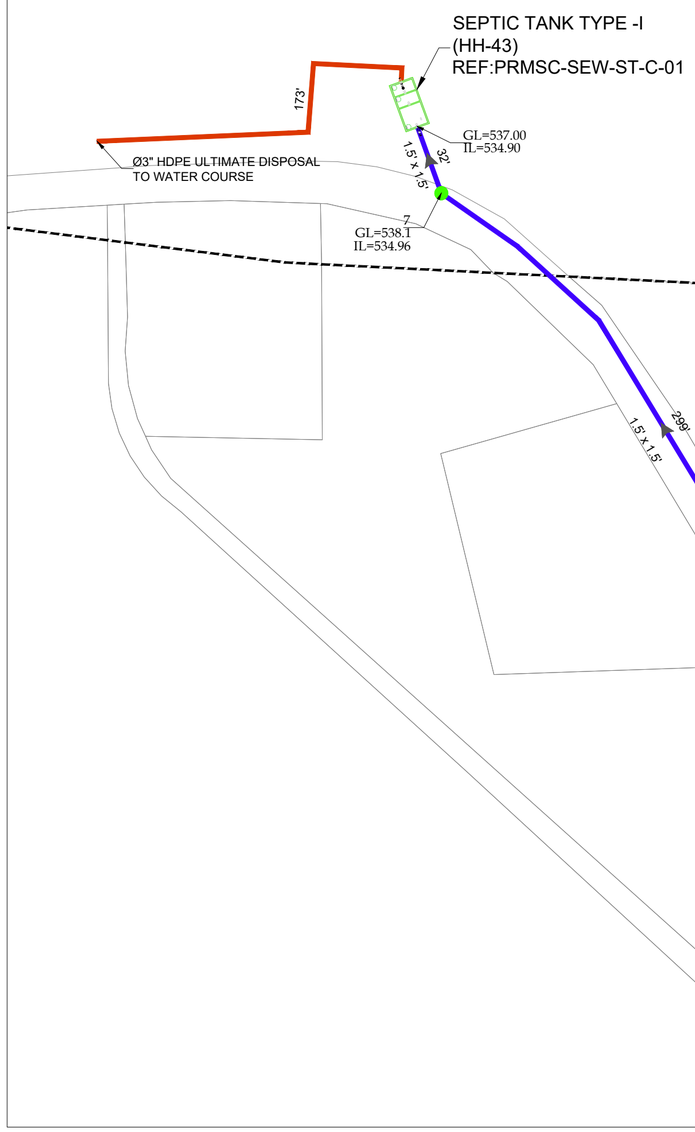

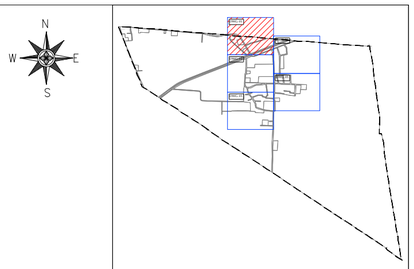

KEY PLAN

LEGEND:

- DRAIN TYPE - I
- SULLAGE CARRIER
- Ø3" HDPE PIPE
- BOUNDARY

VILLAGE: KARTAR SINGH (BWN)

TITLE.

DRAINAGE SYSTEM LAYOUT PLAN-01

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	20-04-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº: PRMSC-BWN-KTS-SEW-LP-01

SHEET 01 OF 05

REV 00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:
ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

PRMSC-BWN-KTS-SEW-LP-01

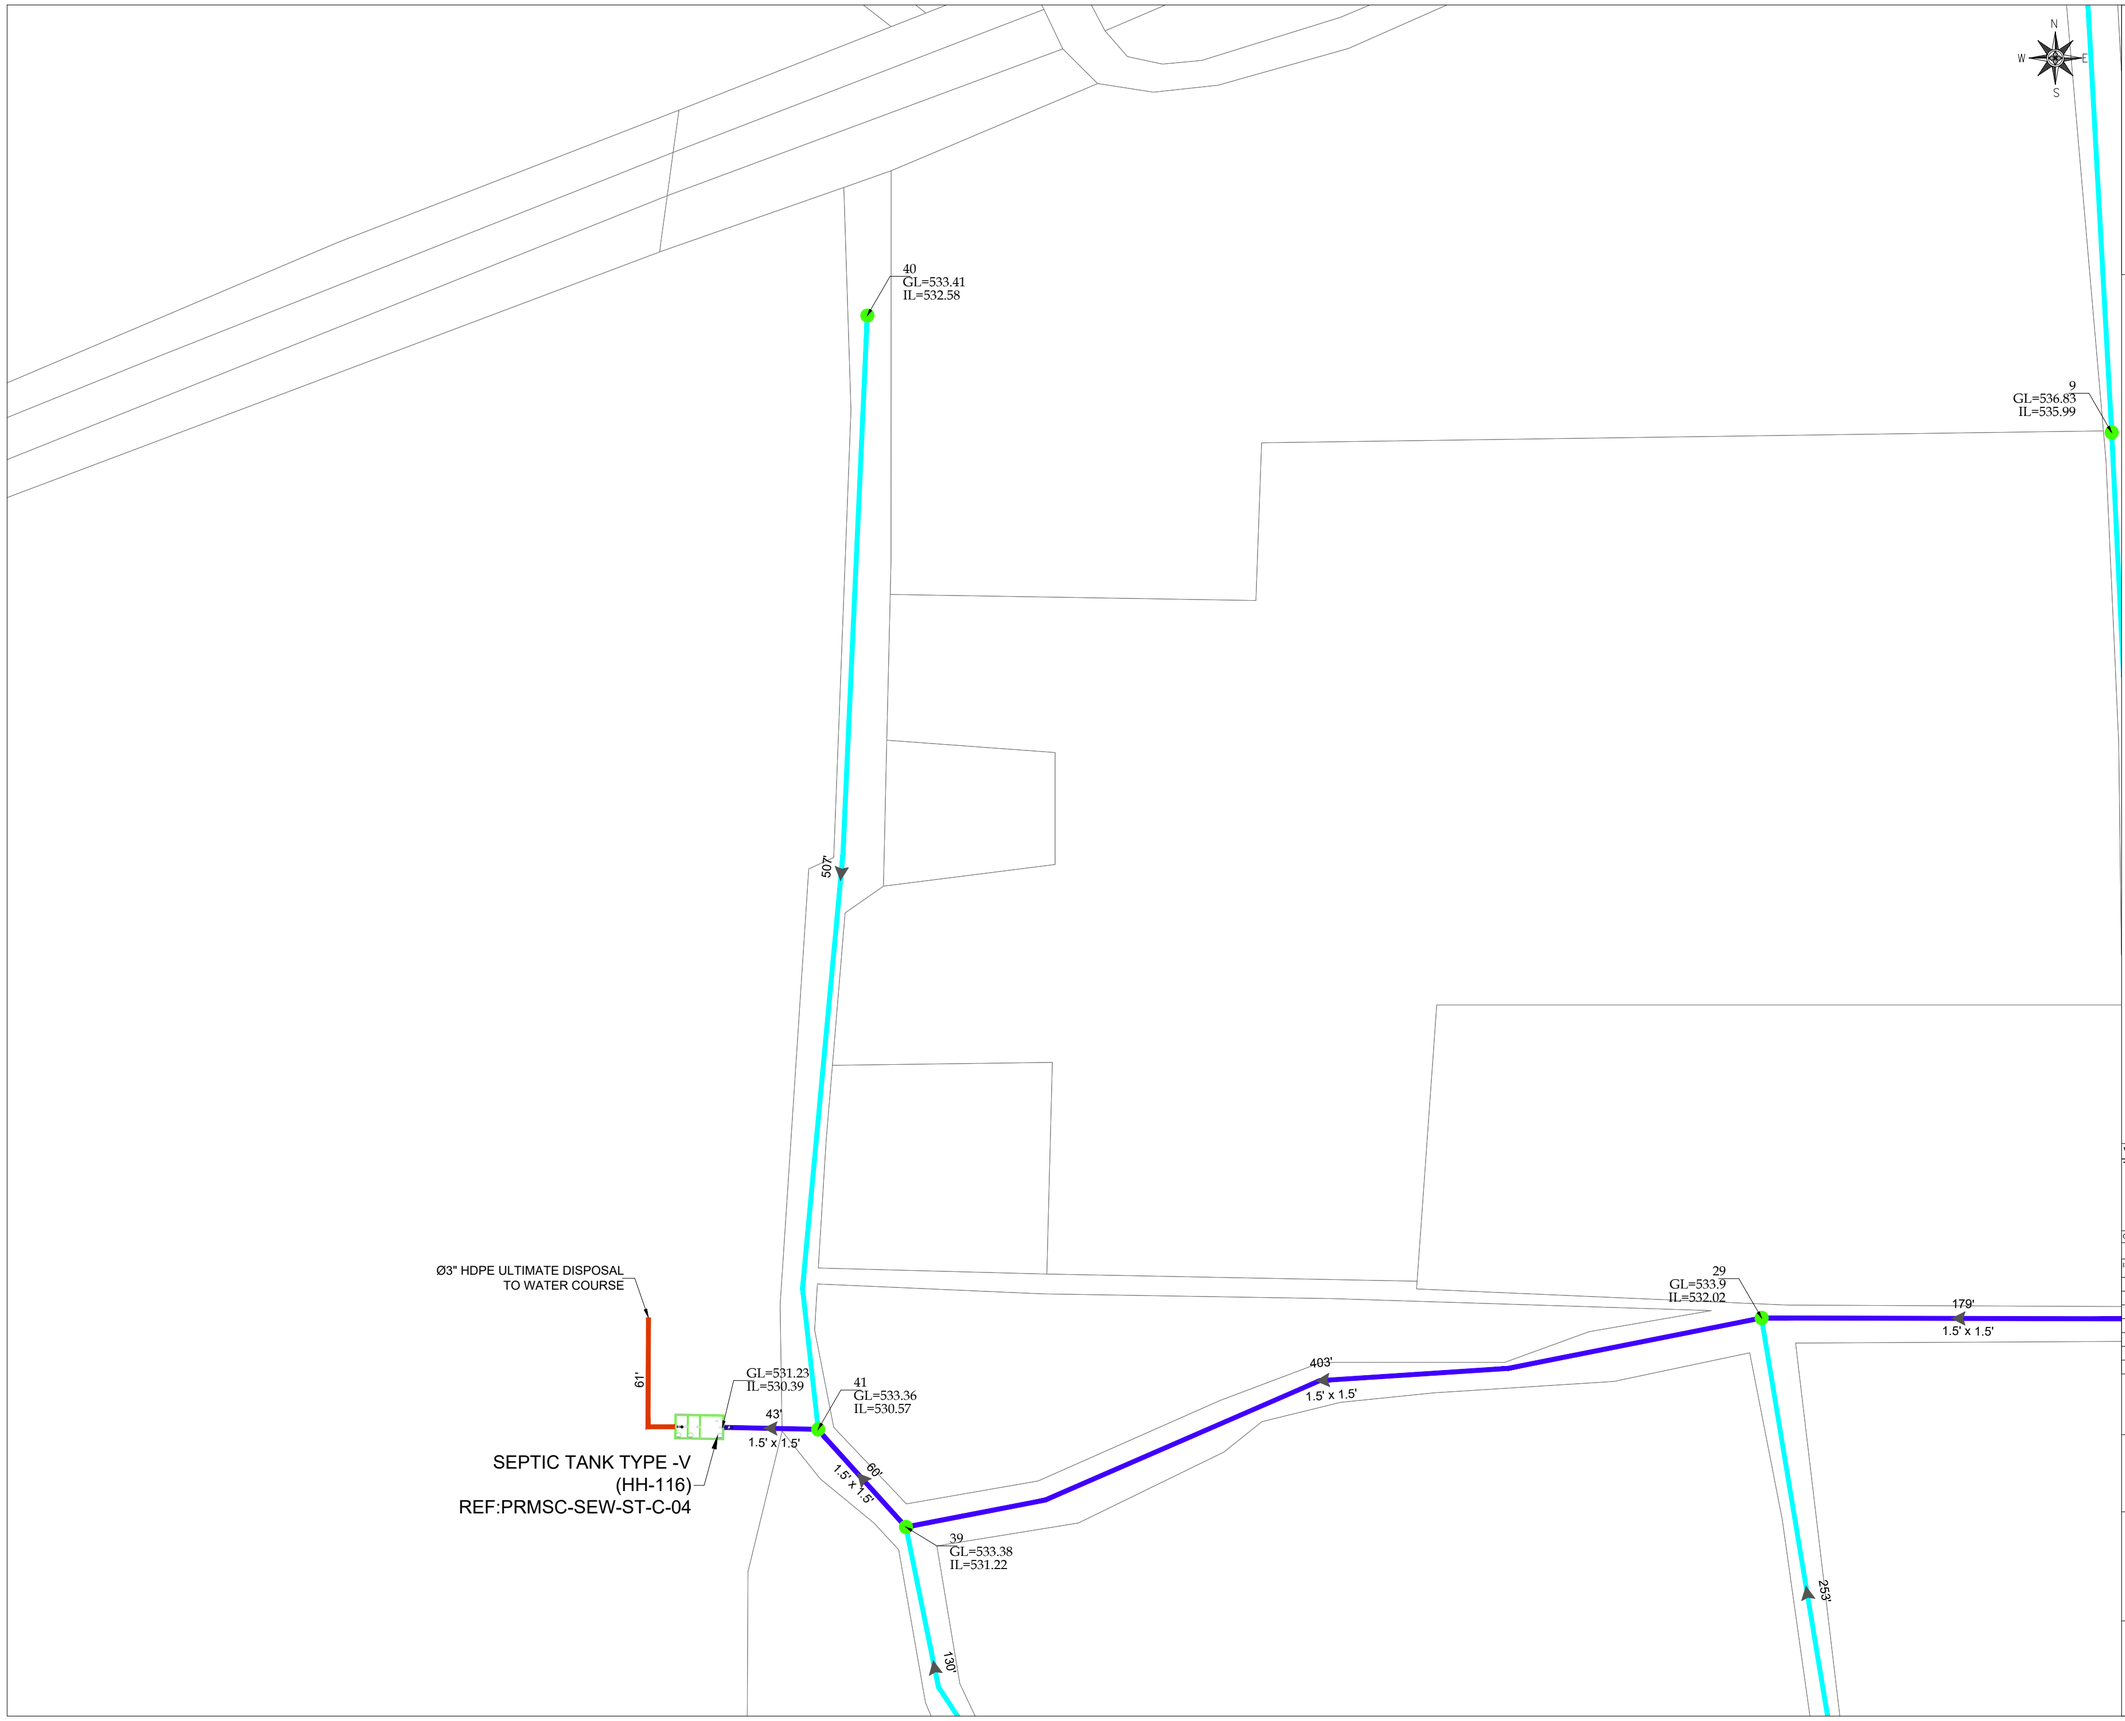

KEY PLAN

LEGEND:

- DRAIN TYPE - I
- SULLAGE CARRIER
- Ø3" HDPE PIPE
- BOUNDARY

VILLAGE: KARTAR SINGH (BWN)

TITLE.

DRAINAGE SYSTEM LAYOUT PLAN-02

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	20-04-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:

PRMSC-BWN-KTS-SEW-LP-02

SHEET 02 OF 05

REV 00

PROJECT:

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:

PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

PRMSC-BWN-KTS-SEW-LP-02

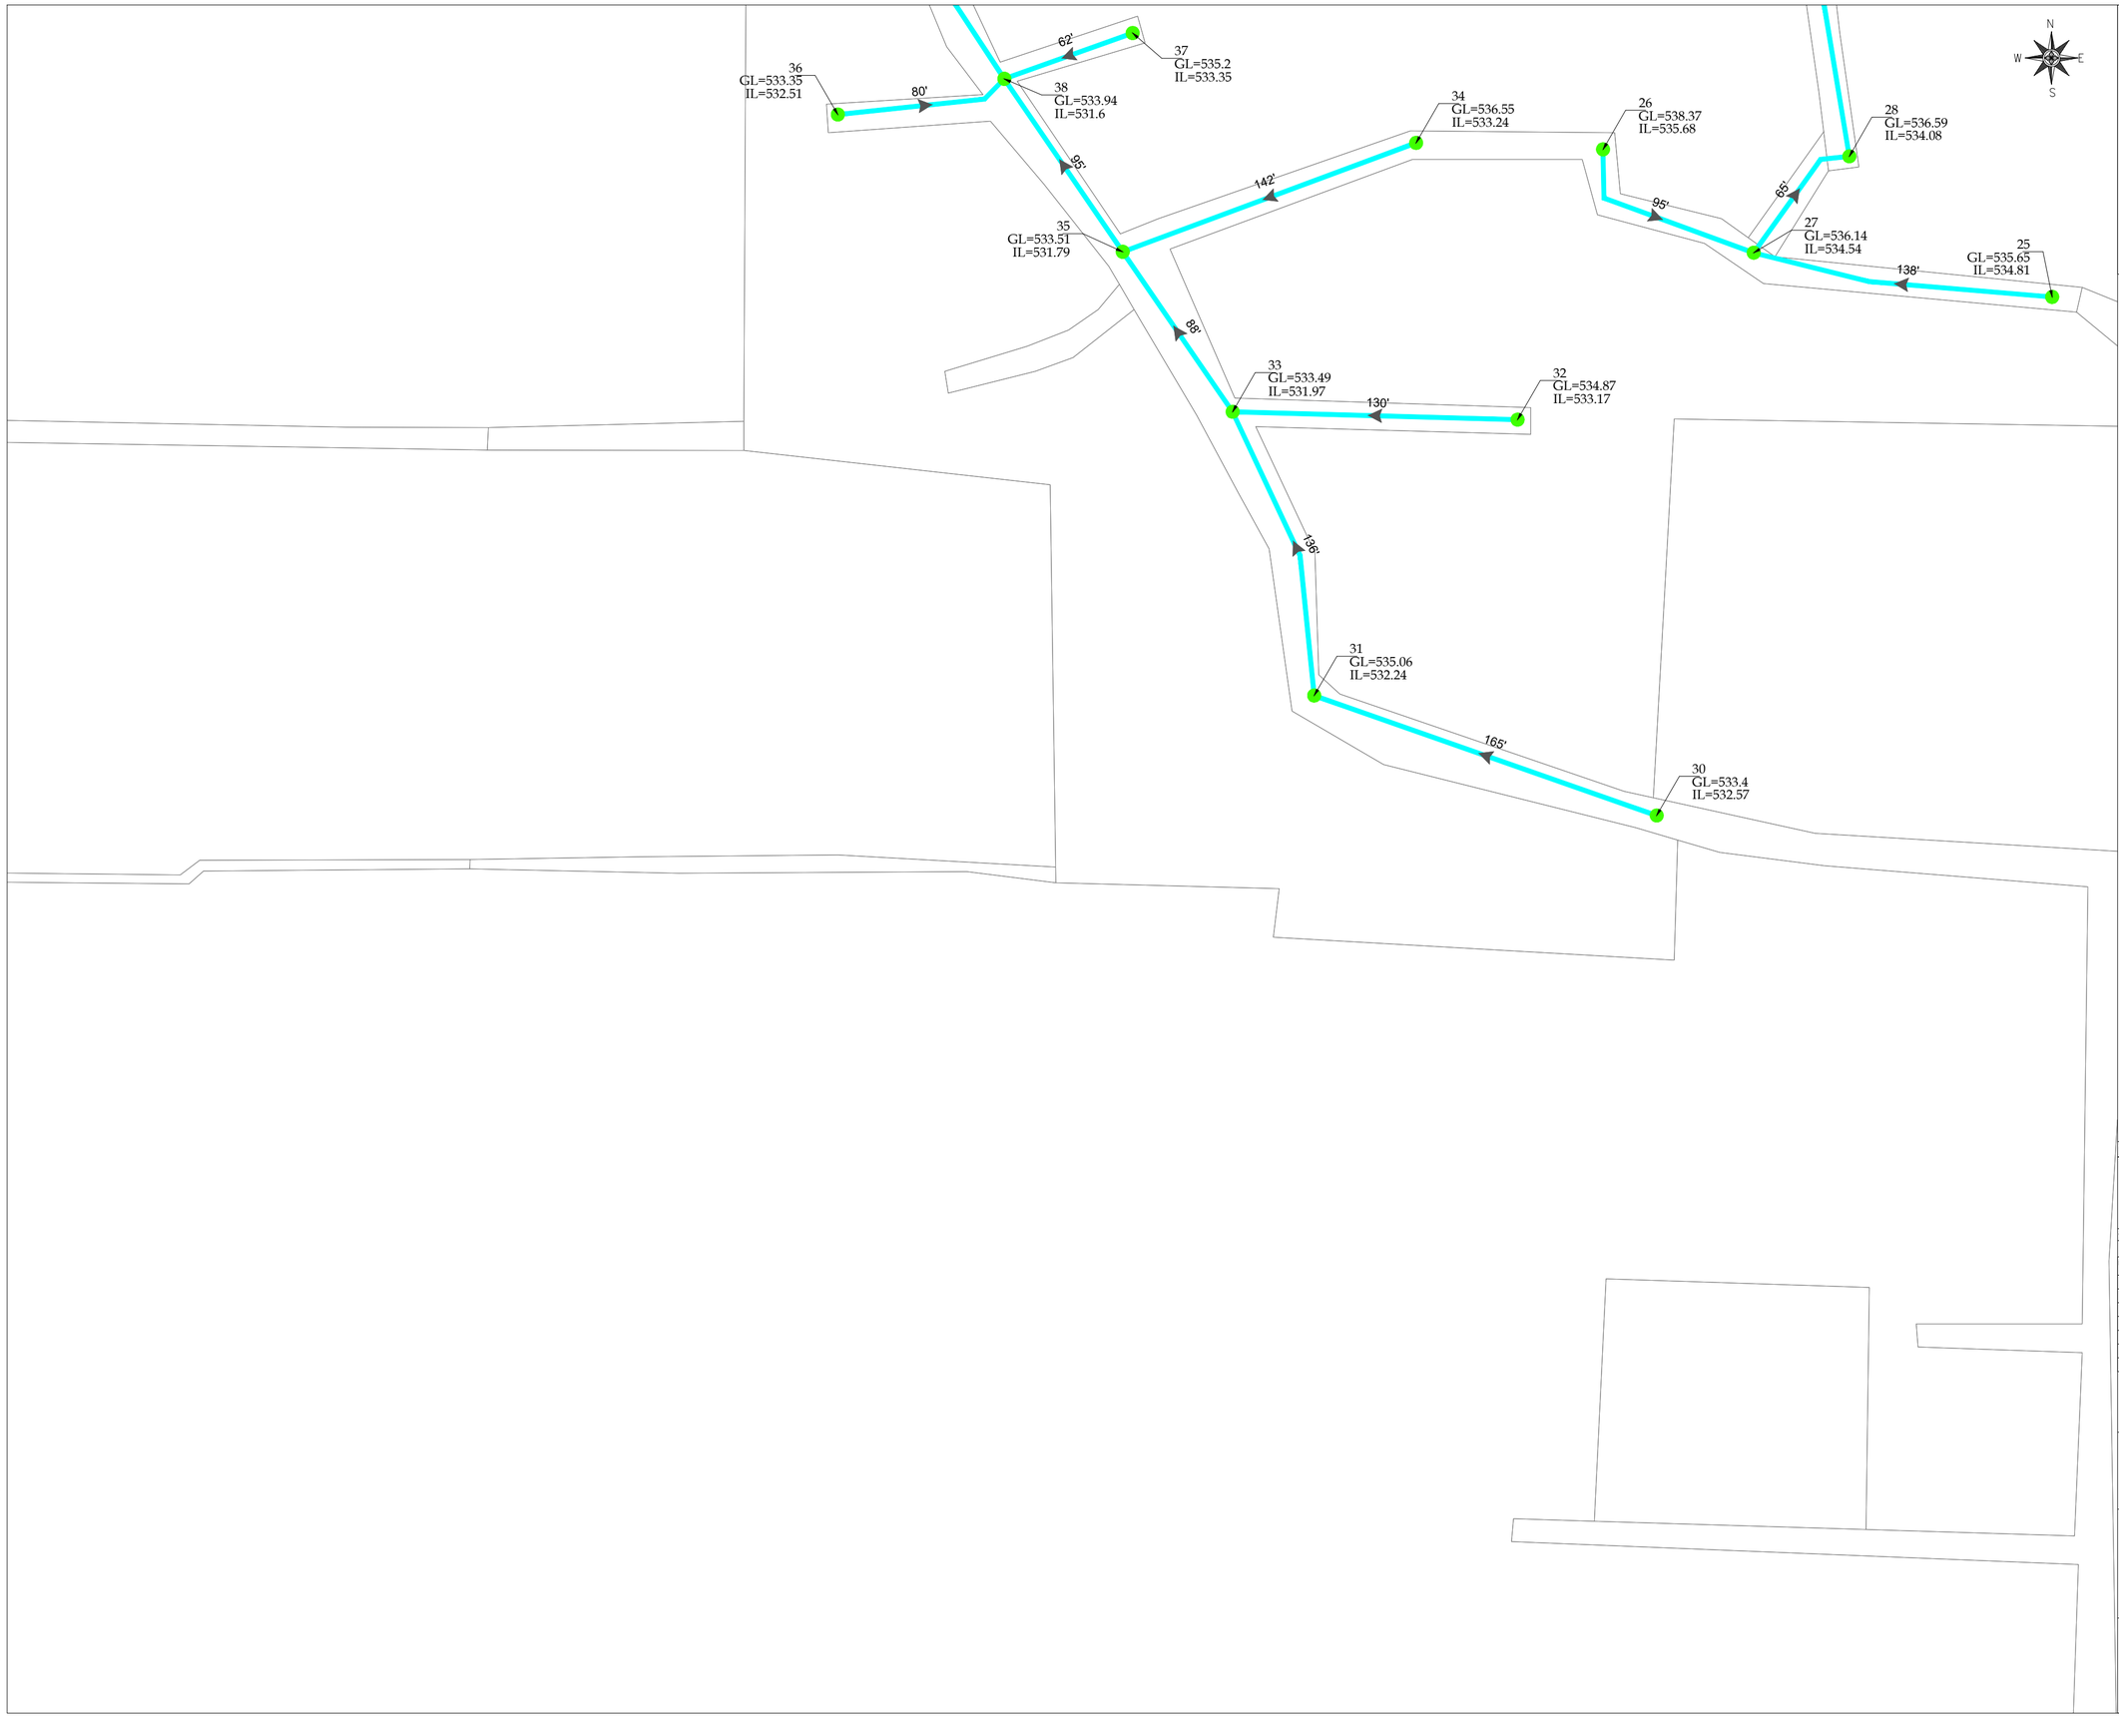

KEY PLAN

LEGEND:

- DRAIN TYPE - I
- SULLAGE CARRIER
- Ø3" HDPE PIPE
- BOUNDARY

VILLAGE: KARTAR SINGH (BWN)

TITLE.

DRAINAGE SYSTEM LAYOUT PLAN-03

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	20-04-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-KTS-SEW-LP-03	03 OF 05	00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

PRMSC-BWN-KTS-SEW-LP-03

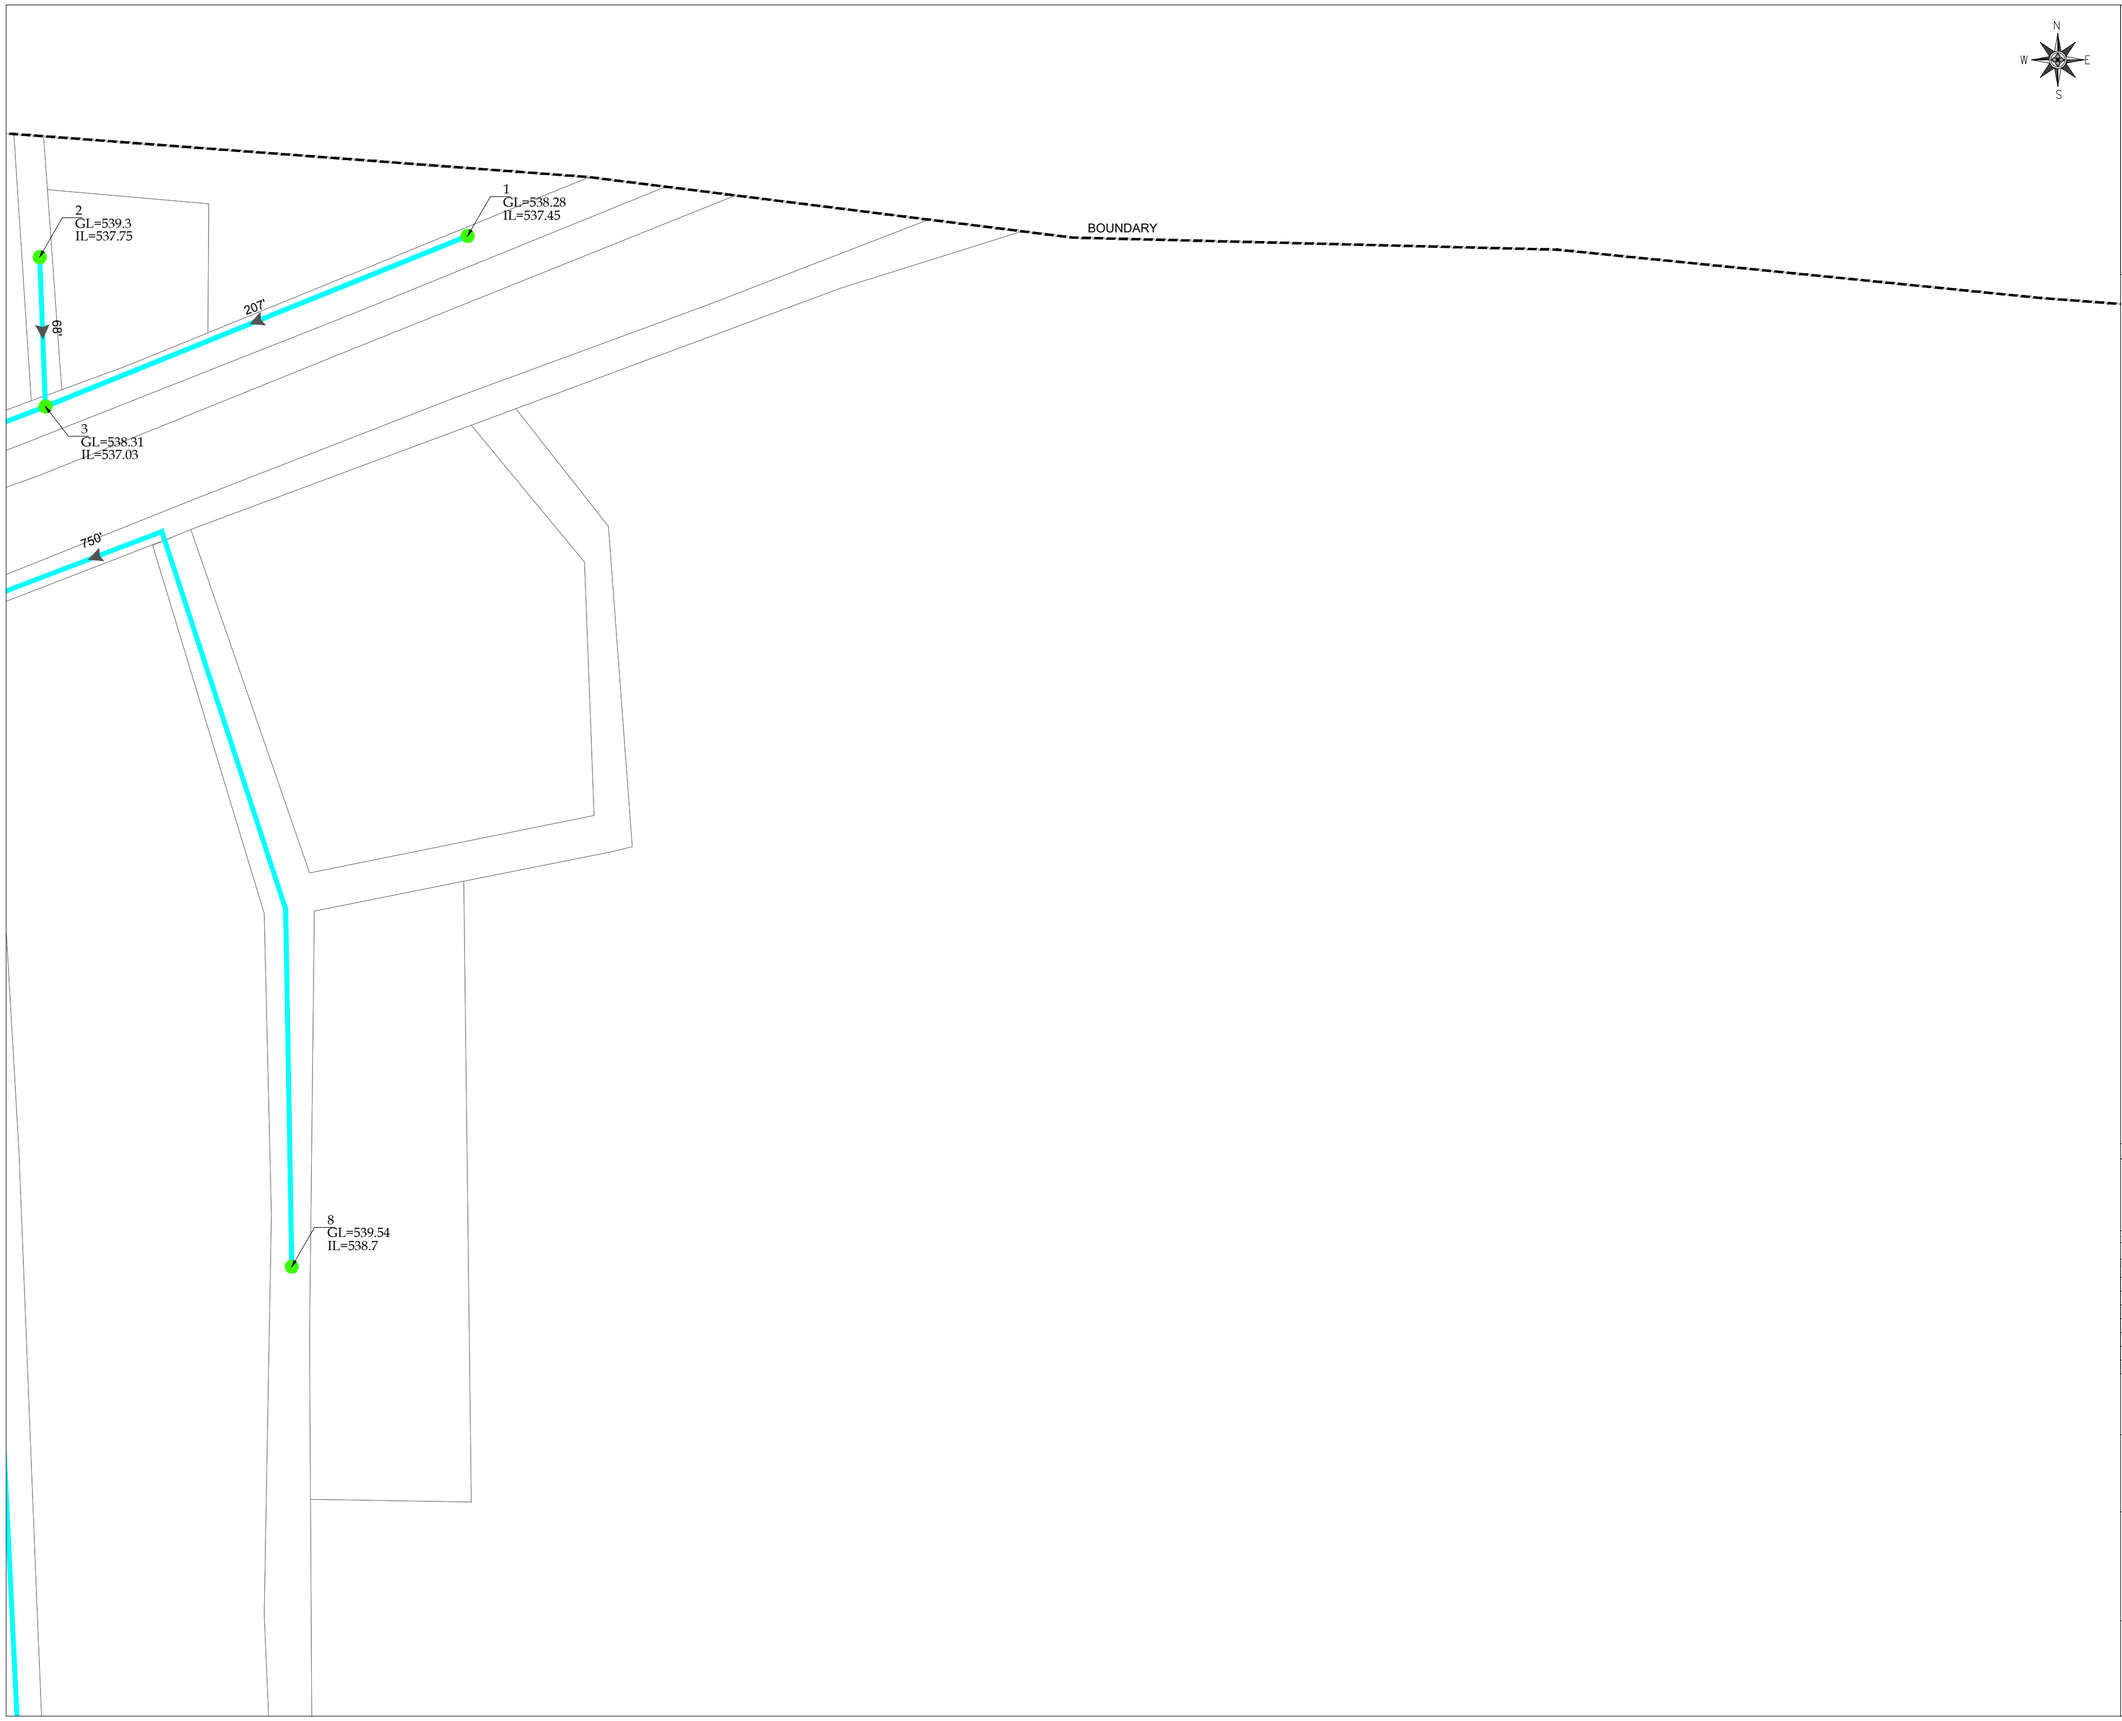

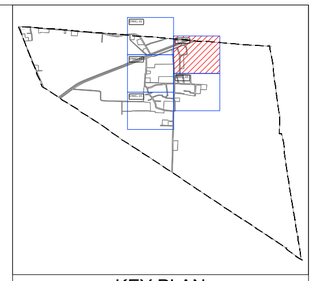

KEY PLAN

LEGEND:

- DRAIN TYPE - I
- SULLAGE CARRIER
- Ø3" HDPE PIPE
- BOUNDARY

VILLAGE: KARTAR SINGH (BWN)

TITLE.

DRAINAGE SYSTEM LAYOUT PLAN-04

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	20-04-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-KTS-SEW-LP-04	04 OF 05	00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

PRMSC-BWN-KTS-SEW-LP-04

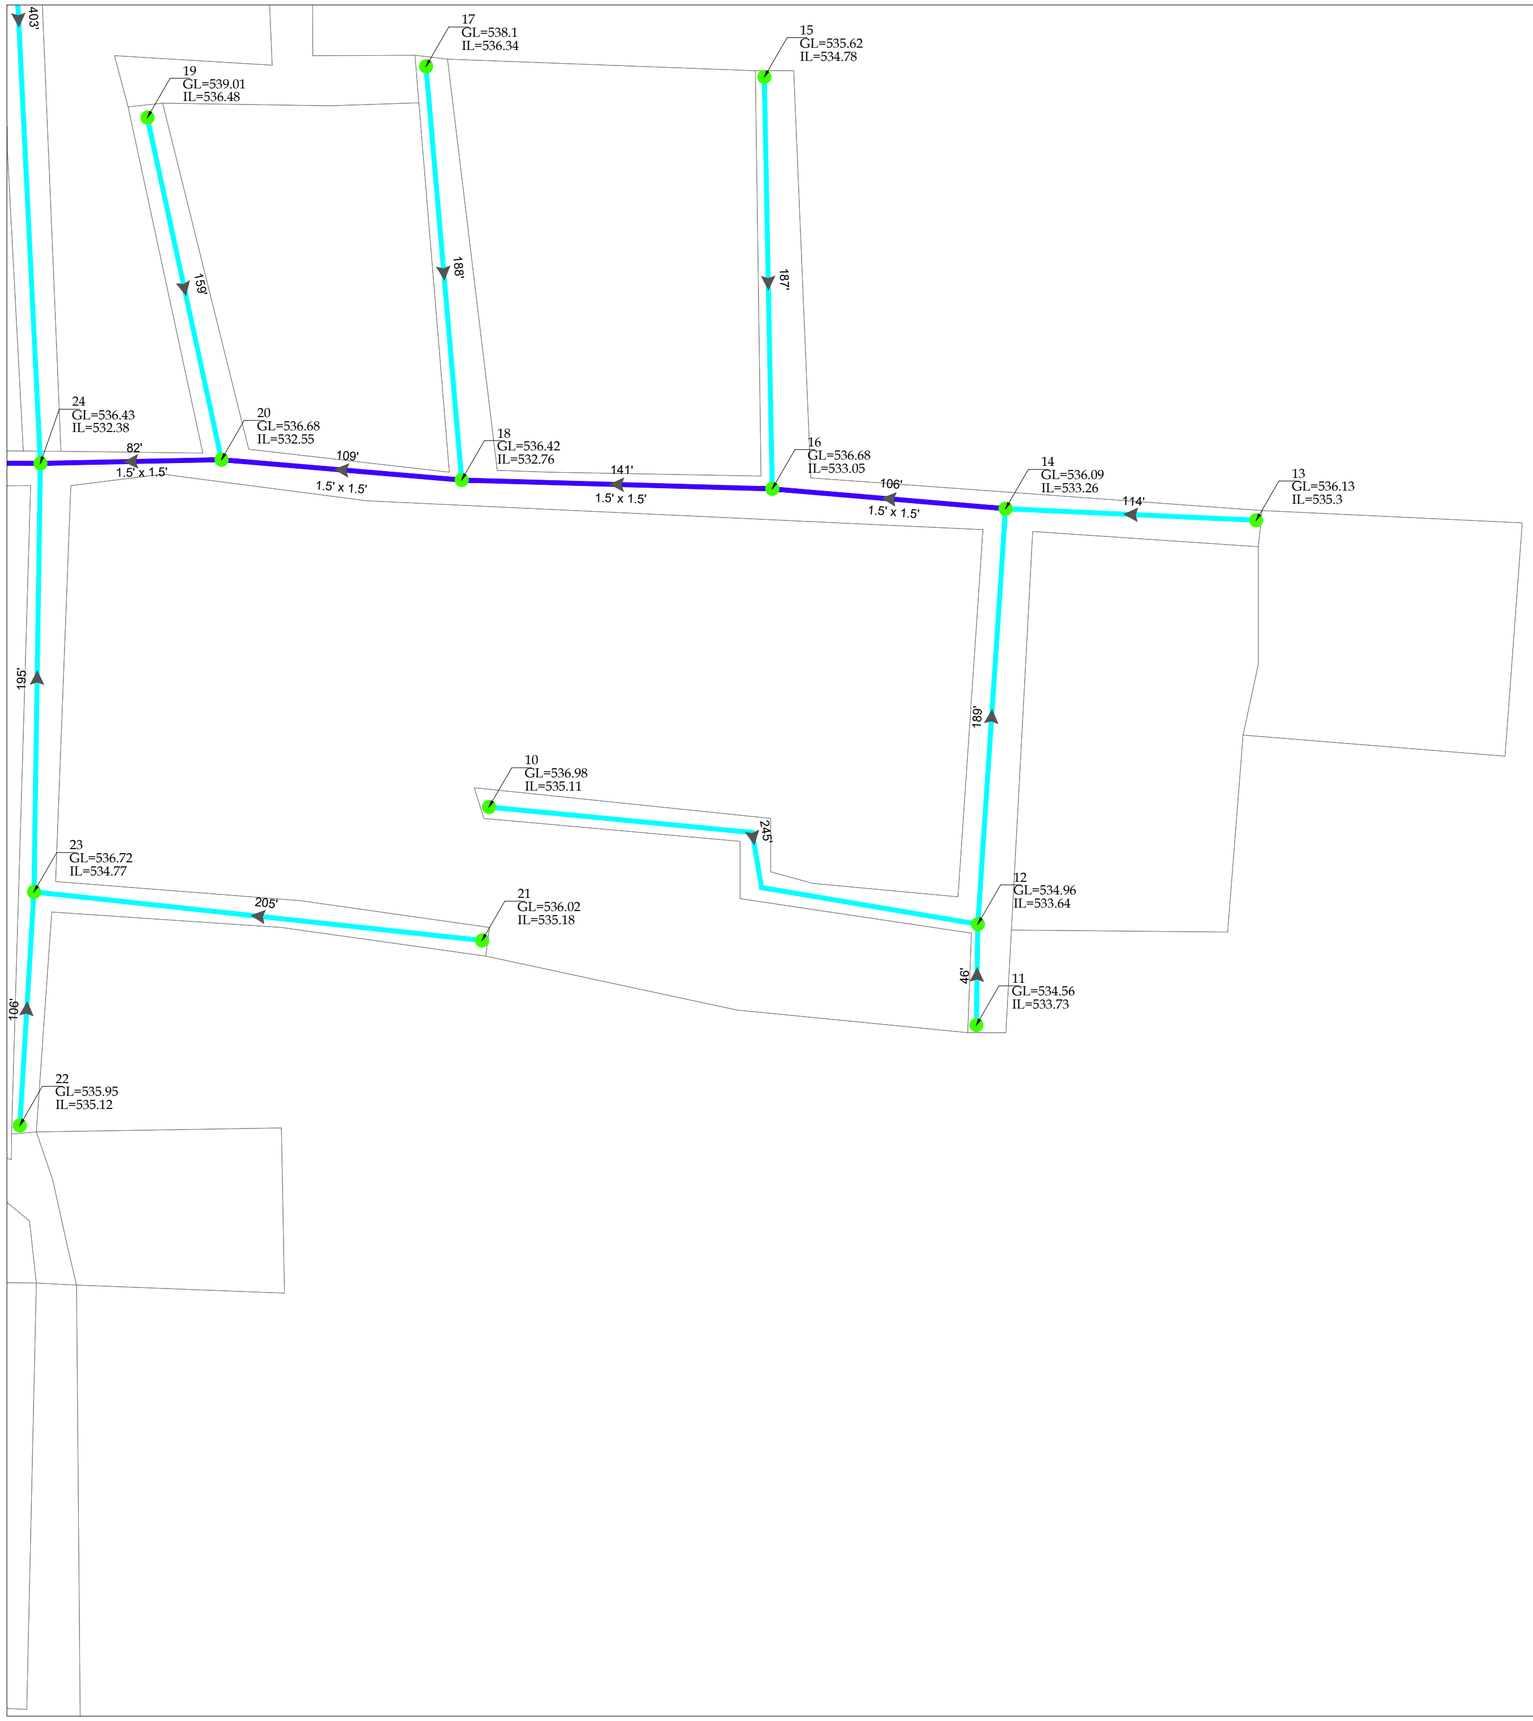

PRMSC-BWN-KTS-SEW-LP-05

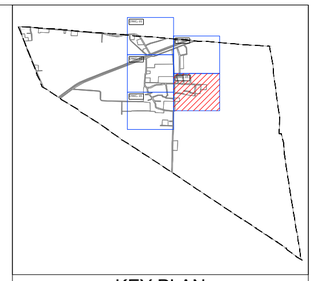

KEY PLAN

LEGEND:

- DRAIN TYPE - I
- SULLAGE CARRIER
- Ø3" HDPE PIPE
- BOUNDARY

VILLAGE: KARTAR SINGH (BWN)

TITLE.

DRAINAGE SYSTEM LAYOUT PLAN-05

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	20-04-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING N°: PRMSC-BWN-KTS-SEW-LP-05

SHEET 05 OF 05

REV 00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS
www.asianeon.com.pk

HYDRAULIC STATEMENT

Node		Length	Slope	Elevation Ground	Elevation Ground	Elevation Invert	Elevation Invert	Depth
FROM	TO	ft	ft/ft	U/S	D/S	U/S	D/S	ft
1	3	207	0.002	538.28	538.31	537.45	537.03	0.83
2	3	68	0.004	539.3	538.31	537.75	537.48	1.55
3	4	535	0.002	538.31	538.9	537.03	535.96	1.28
4	6	201	0.002	538.9	539.77	535.96	535.56	2.93
5	6	426	0.002	538.22	539.77	537.39	536.54	0.83
6	7	299	0.002	539.77	538.1	535.56	534.96	4.21
7	ST Type-I (HH=43)	32	0.002	538.1	537	534.96	534.9	3.14
8	9	750	0.004	539.54	536.83	538.7	535.99	0.83
9	24	403	0.002	536.83	536.43	535.99	535.19	0.83
10	12	245	0.004	536.98	534.96	535.11	534.13	1.88
11	12	46	0.002	534.56	534.96	533.73	533.64	0.83
12	14	189	0.002	534.96	536.09	533.64	533.26	1.33
13	14	114	0.002	536.13	536.09	535.3	535.07	0.83
14	16	106	0.002	536.09	536.68	533.26	533.05	2.83
15	16	187	0.002	535.62	536.68	534.78	534.41	0.83
16	18	141	0.002	536.68	536.42	533.05	532.76	3.63
17	18	188	0.004	538.1	536.42	536.34	535.58	1.76
18	20	109	0.002	536.42	536.68	532.76	532.55	3.65
19	20	159	0.004	539.01	536.68	536.48	535.84	2.53
20	24	82	0.002	536.68	536.43	532.55	532.38	4.13
21	23	205	0.002	536.02	536.72	535.18	534.77	0.83
22	23	106	0.003	535.95	536.72	535.12	534.77	0.83
23	24	195	0.002	536.72	536.43	534.77	534.39	1.95
24	29	179	0.002	536.43	533.9	532.38	532.02	4.05
25	27	138	0.002	535.65	536.14	534.81	534.54	0.83
26	27	95	0.004	538.37	536.14	535.68	535.31	2.69
27	28	65	0.002	536.14	536.59	534.54	534.41	1.6
28	29	253	0.004	536.59	533.9	534.08	533.06	2.51
29	39	403	0.002	533.9	533.38	532.02	531.22	1.87
30	31	165	0.002	533.4	535.06	532.57	532.24	0.83
31	33	136	0.002	535.06	533.49	532.24	531.97	2.82
32	33	130	0.004	534.87	533.49	533.17	532.66	1.69
33	35	88	0.002	533.49	533.51	531.97	531.79	1.52
34	35	142	0.004	536.55	533.51	533.24	532.67	3.31
35	38	95	0.002	533.51	533.94	531.79	531.6	1.71
36	38	80	0.002	533.35	533.94	532.51	532.35	0.83
37	38	62	0.004	535.2	533.94	533.35	533.1	1.85
38	39	130	0.003	533.94	533.38	531.6	531.22	2.33
39	41	60	0.002	533.38	533.36	531.22	531.1	2.17
40	41	507	0.004	533.41	533.36	532.58	530.57	0.83
41	ST Type-V (HH=116)	43	0.004	533.36	531.23	530.57	530.39	2.8

VILLAGE: KARTAR SINGH (BWN)

TITLE.

HYDRAULIC STATEMENT

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	20-04-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº: PRMSC-BWN-KTS-SEW-HS-00

SHEET 00 OF 00

REV 00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT
ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

PRMSC-BWN-KTS-SEW-HS-00

KHOBER

KEY PLAN

Revenue Village: Khober Sheet-1

District:	Bahawalnagar
Tehsil:	Bahawalnagar
Revenue Village:	Khober

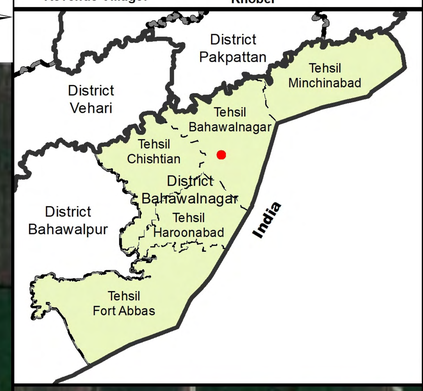

ND-1 GL=545.35 IL=544.32
ND-14 GL=545.32 IL=544.49
ND-16 GL=544.71 IL=542.09
ND-15 GL=545.21 IL=542.38
ND-2 GL=544.56 IL=543.53
ND-3 GL=544.75 IL=543.12
ND-4 GL=546.14 IL=545.3
ND-5 GL=544.74 IL=542.9
ND-17 GL=545 IL=541.5
ND-13 GL=543.58 IL=542.75
Araian di Basti
ND-6 GL=548.95 IL=548.12
ND-19 GL=543.25 IL=541.2
ND-7 GL=544.95 IL=542.43
ND-18 GL=547.5 IL=546.66
ND-23 GL=544.76 IL=543.93
ND-9 GL=544.66 IL=541.56
ND-12 GL=543.98 IL=540.86
ND-20 GL=544.01 IL=540.84
ND-24 GL=543.32 IL=542.34
GL=542.41 IL=540.02
SEPTIC TANK-T3 Plot Size=2.62 Marla
ND-25 GL=542.62 IL=540.12
ND-22 GL=544.57 IL=540.66
ND-8 GL=542.75 IL=541.92
ND-10 GL=544.51 IL=543.67
ND-11 GL=544.54 IL=543.27
ND-21 GL=543.69 IL=542.86

Title:
Proposed Drainage Network Plan

Legend:

- SETTLEMENT
- NODE
- 3" HDPE PIPE
- DRAIN TYPE-1
- SULLAGE CARRIER
- SEPTIC TANK
- SETTLEMENT BOUNDARY

Drain Type 1=8980 Rft

Sullage Carrier= 6438 Rft

Scale: 1:1,500

1 inch = 125 feet

Paper Size: A3

0 40 80 160

Kilometers

Project:

Engineering Design & Construction Supervision, Punjab Rural Sustainable Water Supply & Sanitation Project, Cluster South III

PRWSC

ENVIRONMENTAL TECHNOLOGIES

ASIAN CONSULTING ENGINEERS www.asianconi.com

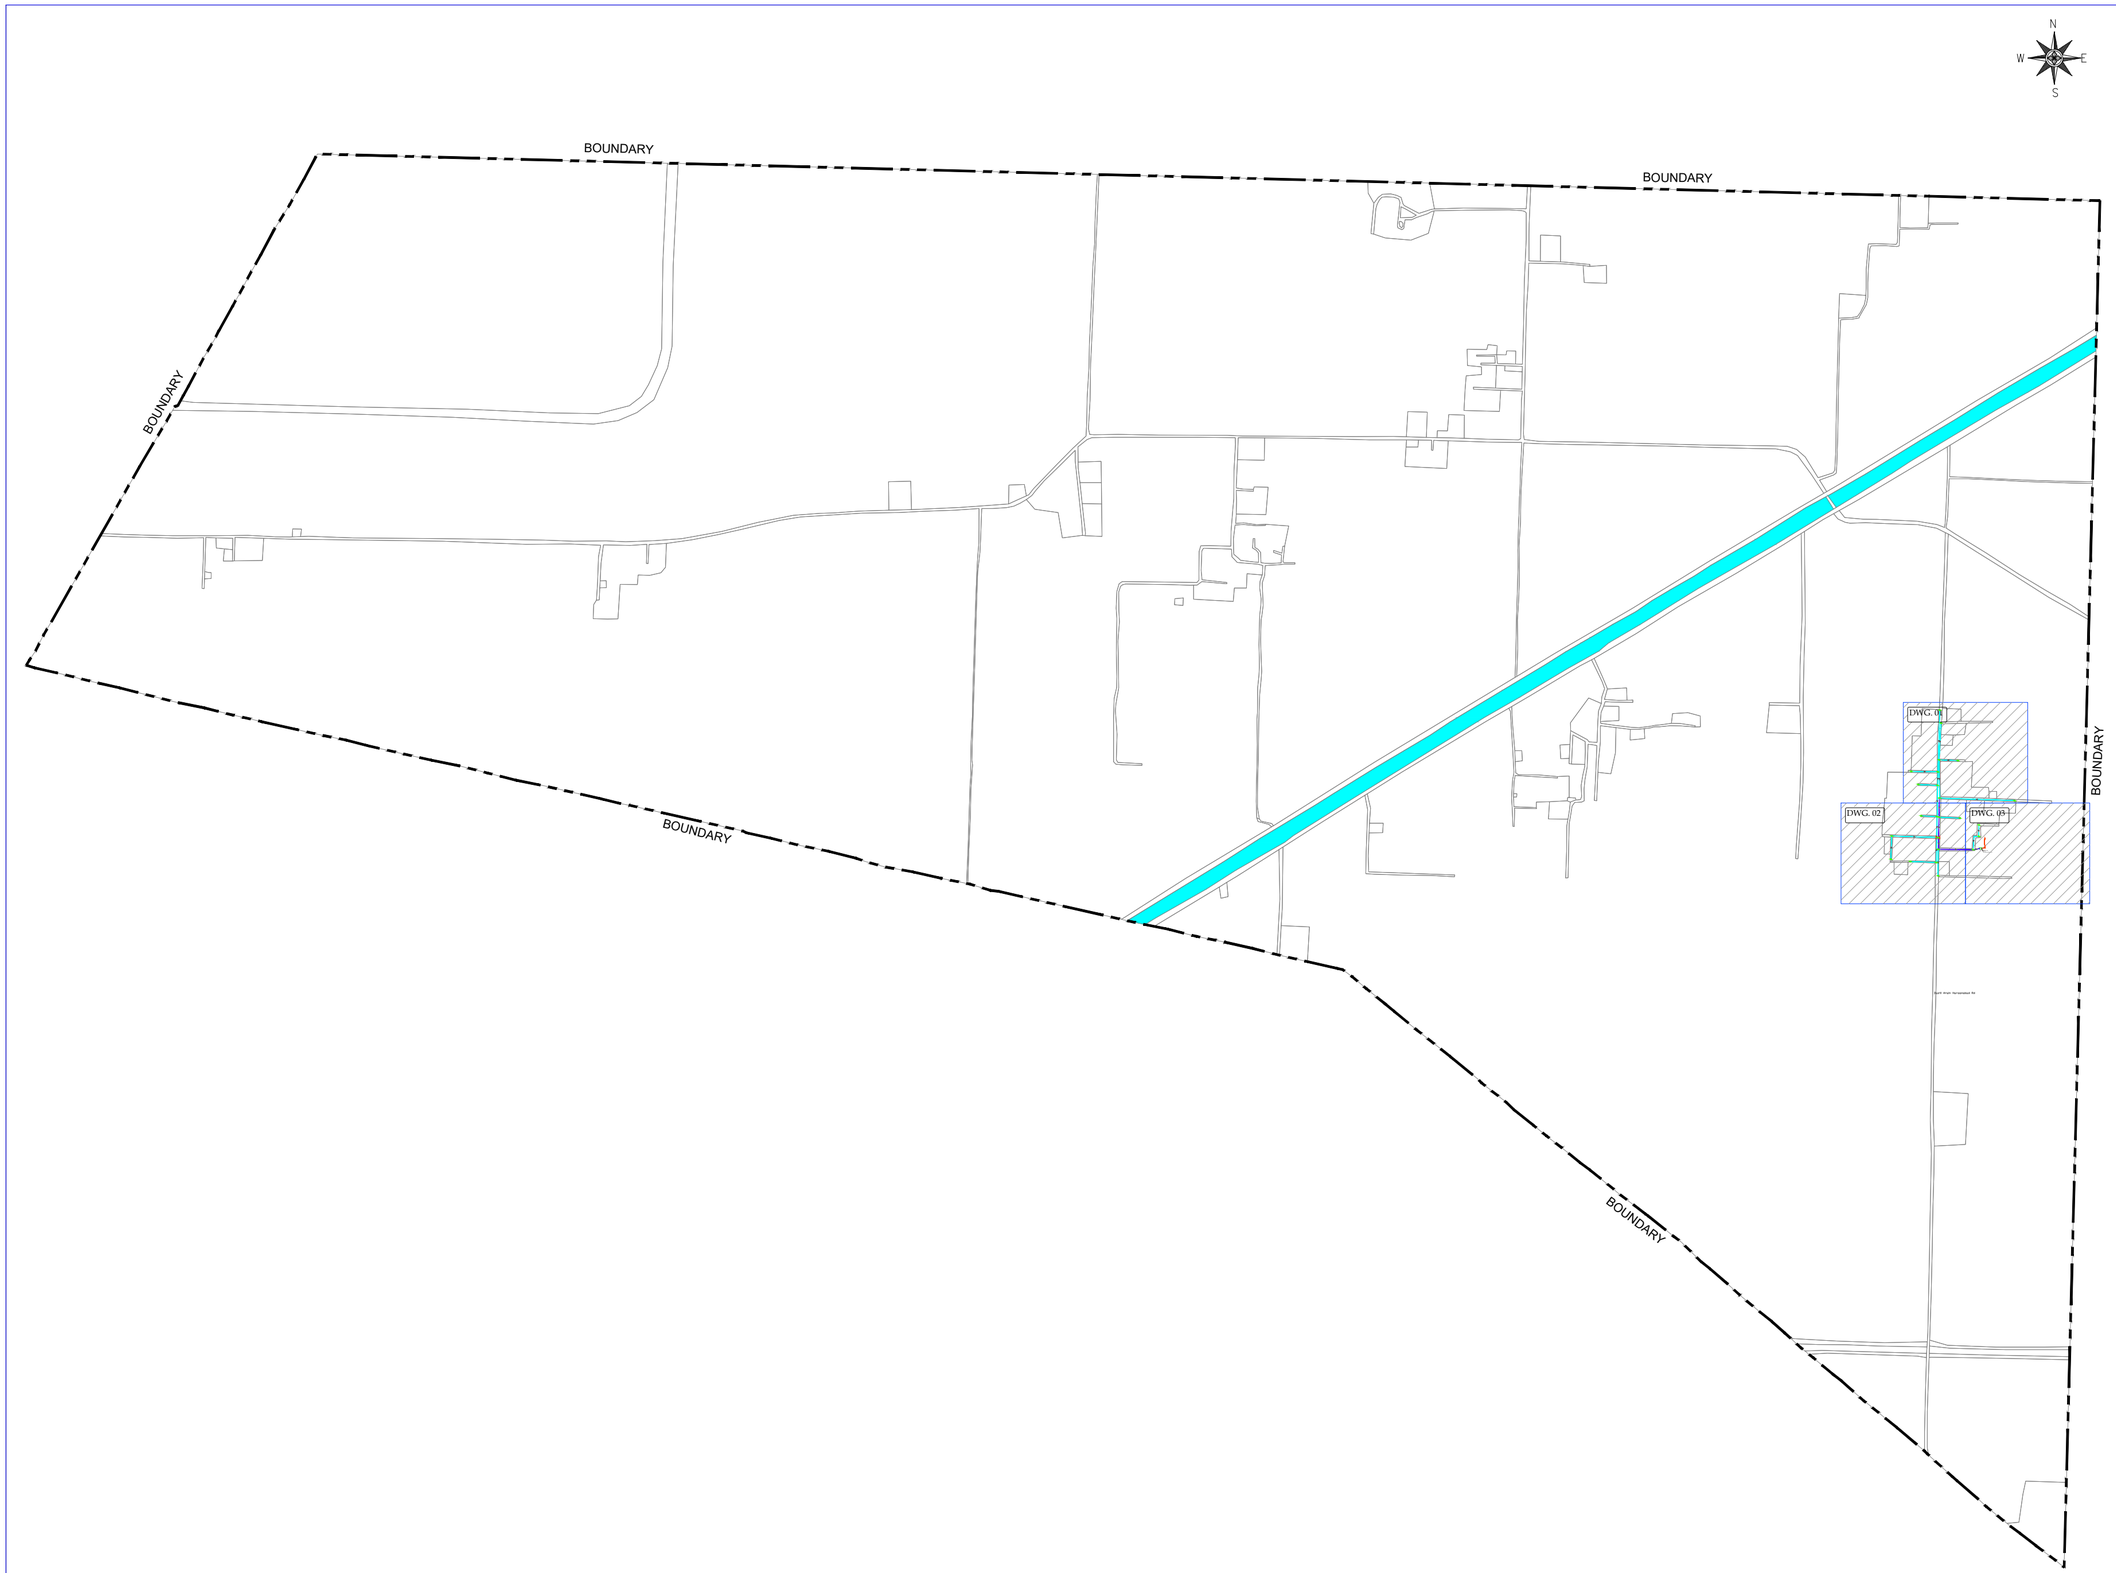

LEGEND:

- DRAIN TYPE - I
- SULLAGE CARRIER
- Ø3" HDPE PIPE
- PROPOSED CULVERT
- BOUNDARY

VILLAGE: KHOBER (BWN)

TITLE.

DRAINAGE SYSTEM KEY PLAN

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 850'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	02-01-2026	DETAILED DESIGN	MUNEEB	ENGR. FAEIZ	ENGR. IHSAN-UL-HAQ
02	20-04-2026	DETAILED DESIGN	MUNEEB	ENGR. FAEIZ	ENGR. IHSAN-UL-HAQ
03					
04					
05					
06					
07					

DRAWING Nº: PRMSC-BWN-KHB-SEW-KP-00

SHEET 00 OF 00

REV 01

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT
ASIAN CONSULTING ENGINEERS
www.asianceb.com

PRMSC-BWN-KHB-SEW-KP-00

LAYOUT PLAN

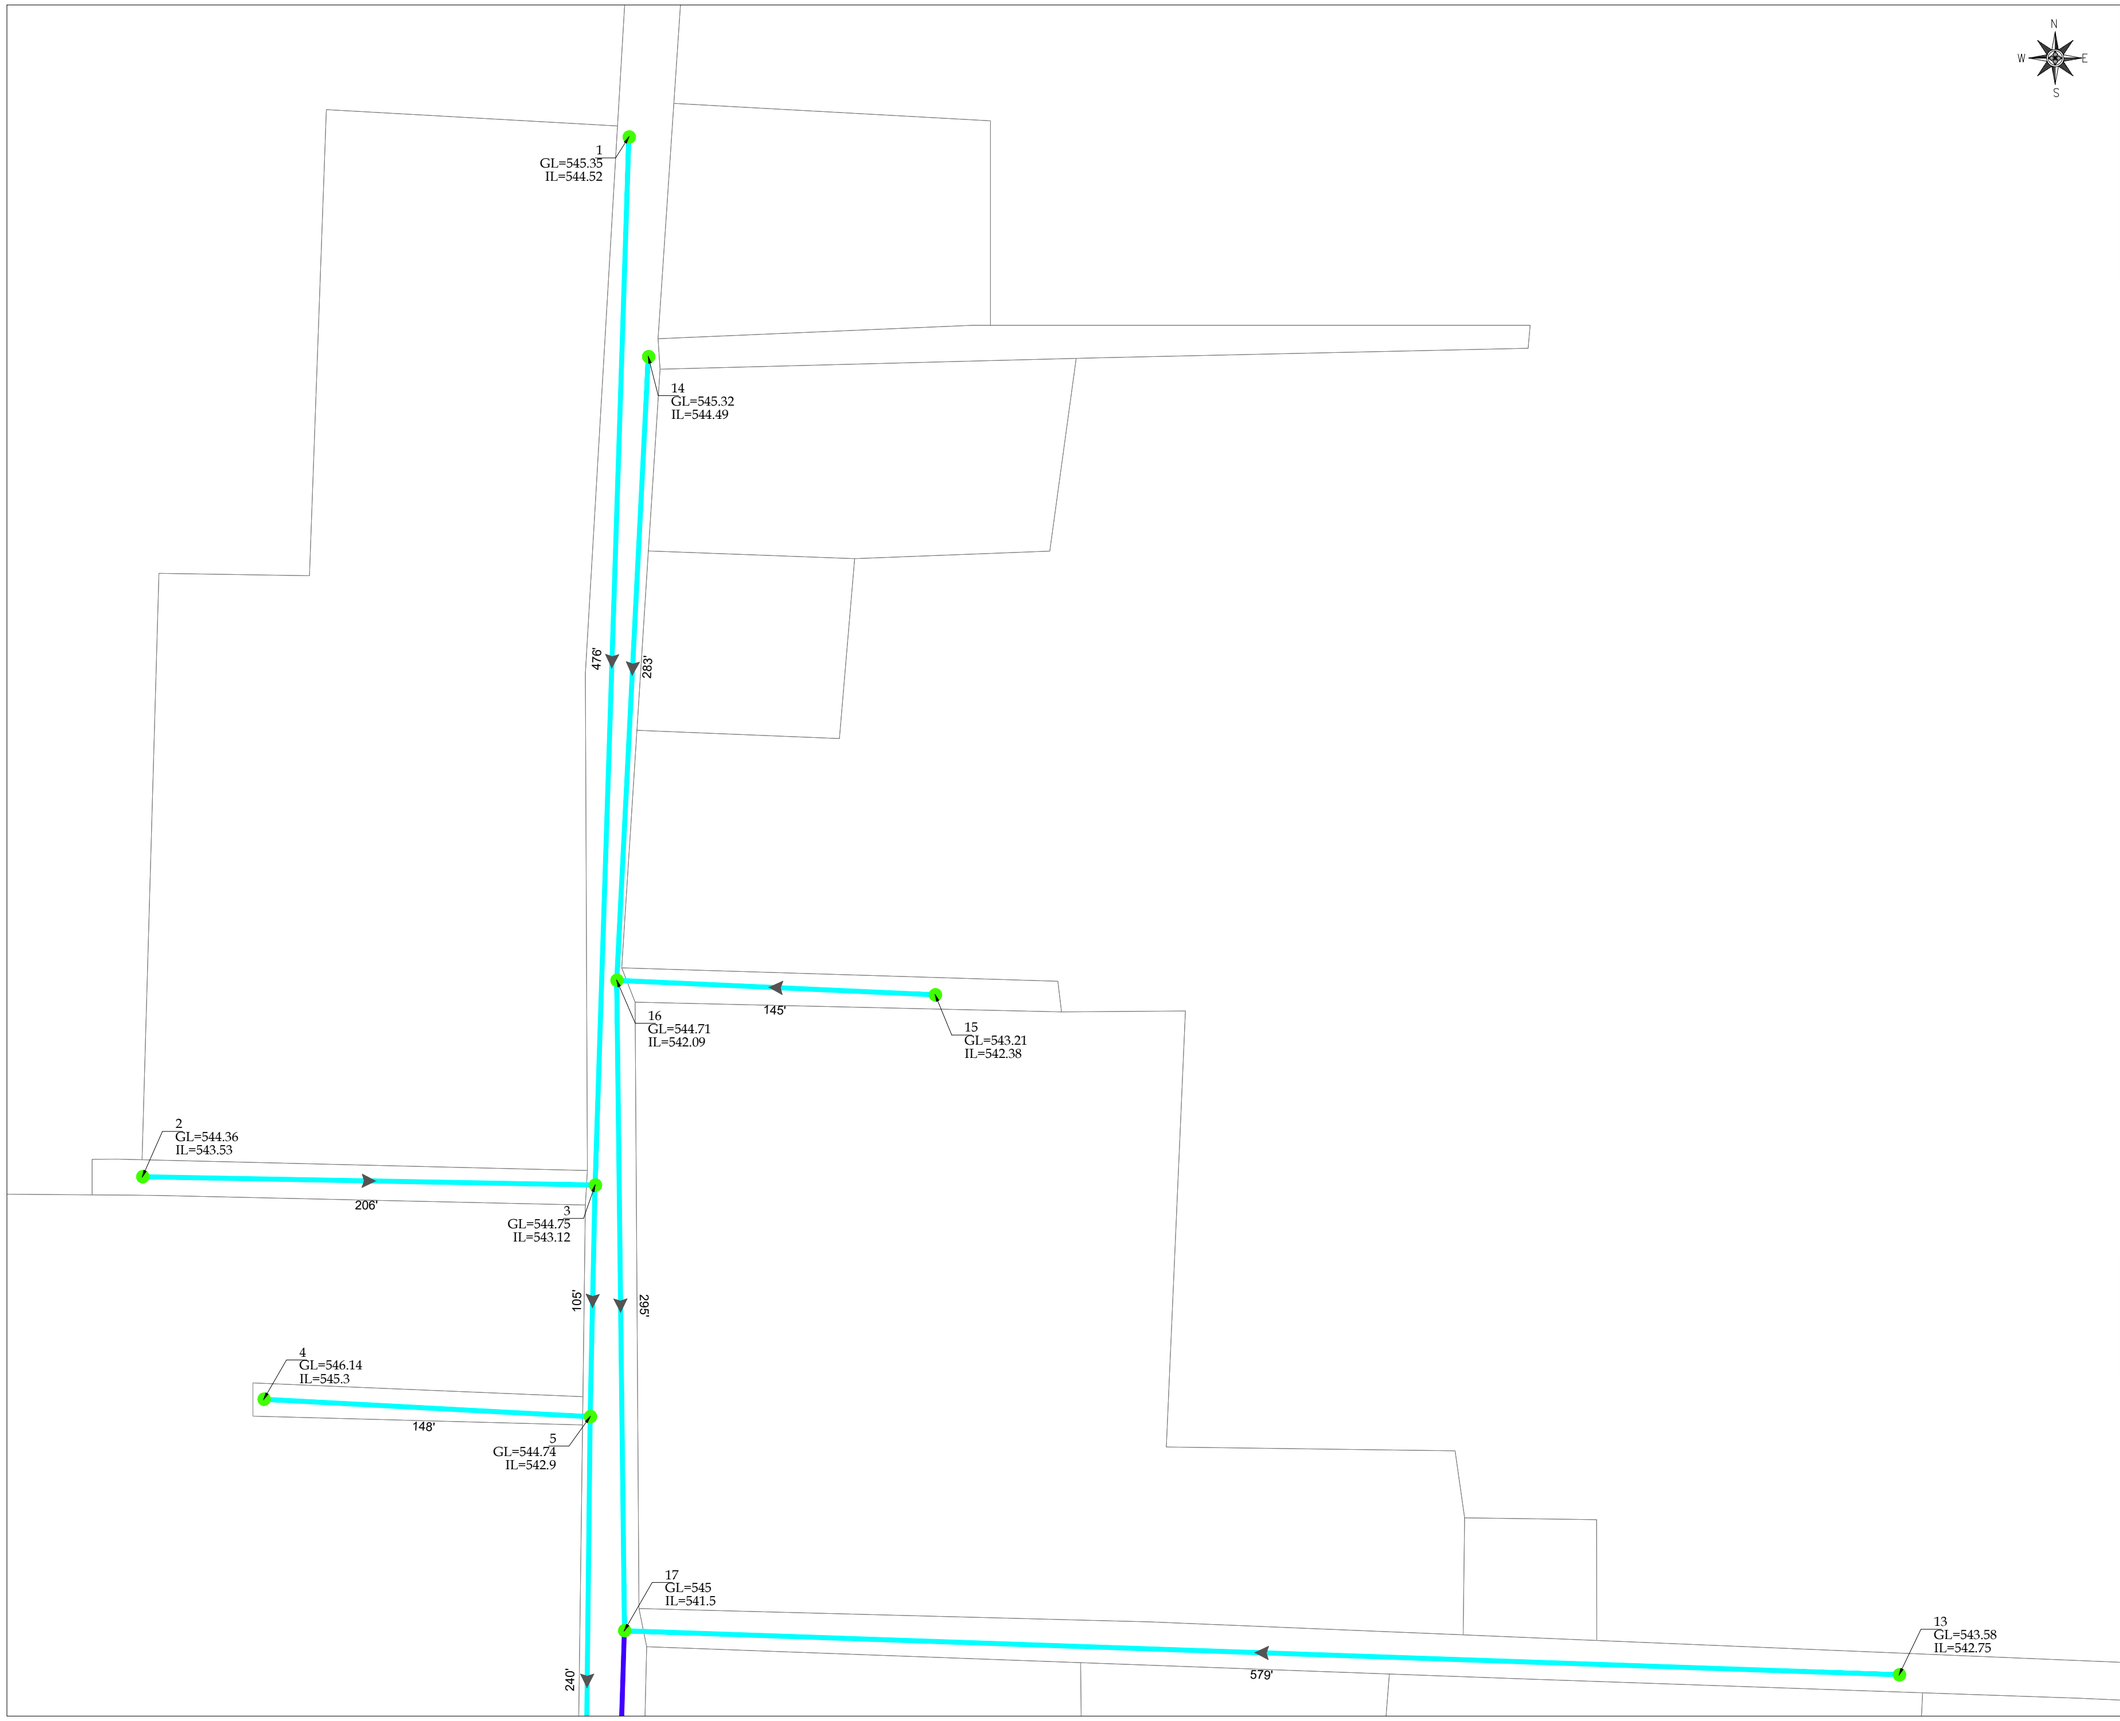

PRMSC-BWN-KHB-SEW-LP-01

N
W
E
S

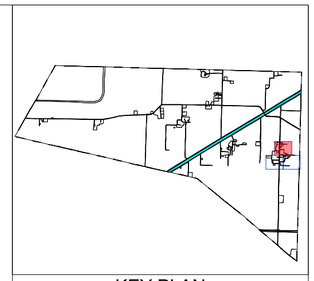

KEY PLAN

LEGEND:

- DRAIN TYPE - I
- SULLAGE CARRIER
- Ø3" HDPE PIPE
- PROPOSED CULVERT
- BOUNDARY

VILLAGE: KHOBAR (BWN)

TITLE.

DRAINAGE SYSTEM LAYOUT PLAN-01

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	02-01-2026	DETAILED DESIGN	MUNEEB	ENGR FAIEZ	ENGR IHSAN-UL-HAQ
02	20-04-2026	DETAILED DESIGN	MUNEEB	ENGR FAIEZ	ENGR IHSAN-UL-HAQ
03					
04					
05					
06					
07					

DRAWING Nº: PRMSC-BWN-KHB-SEW-LP-01

SHEET 01 OF 03

REV 01

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:
ASIAN CONSULTING ENGINEERS
www.asiacon.com.pv

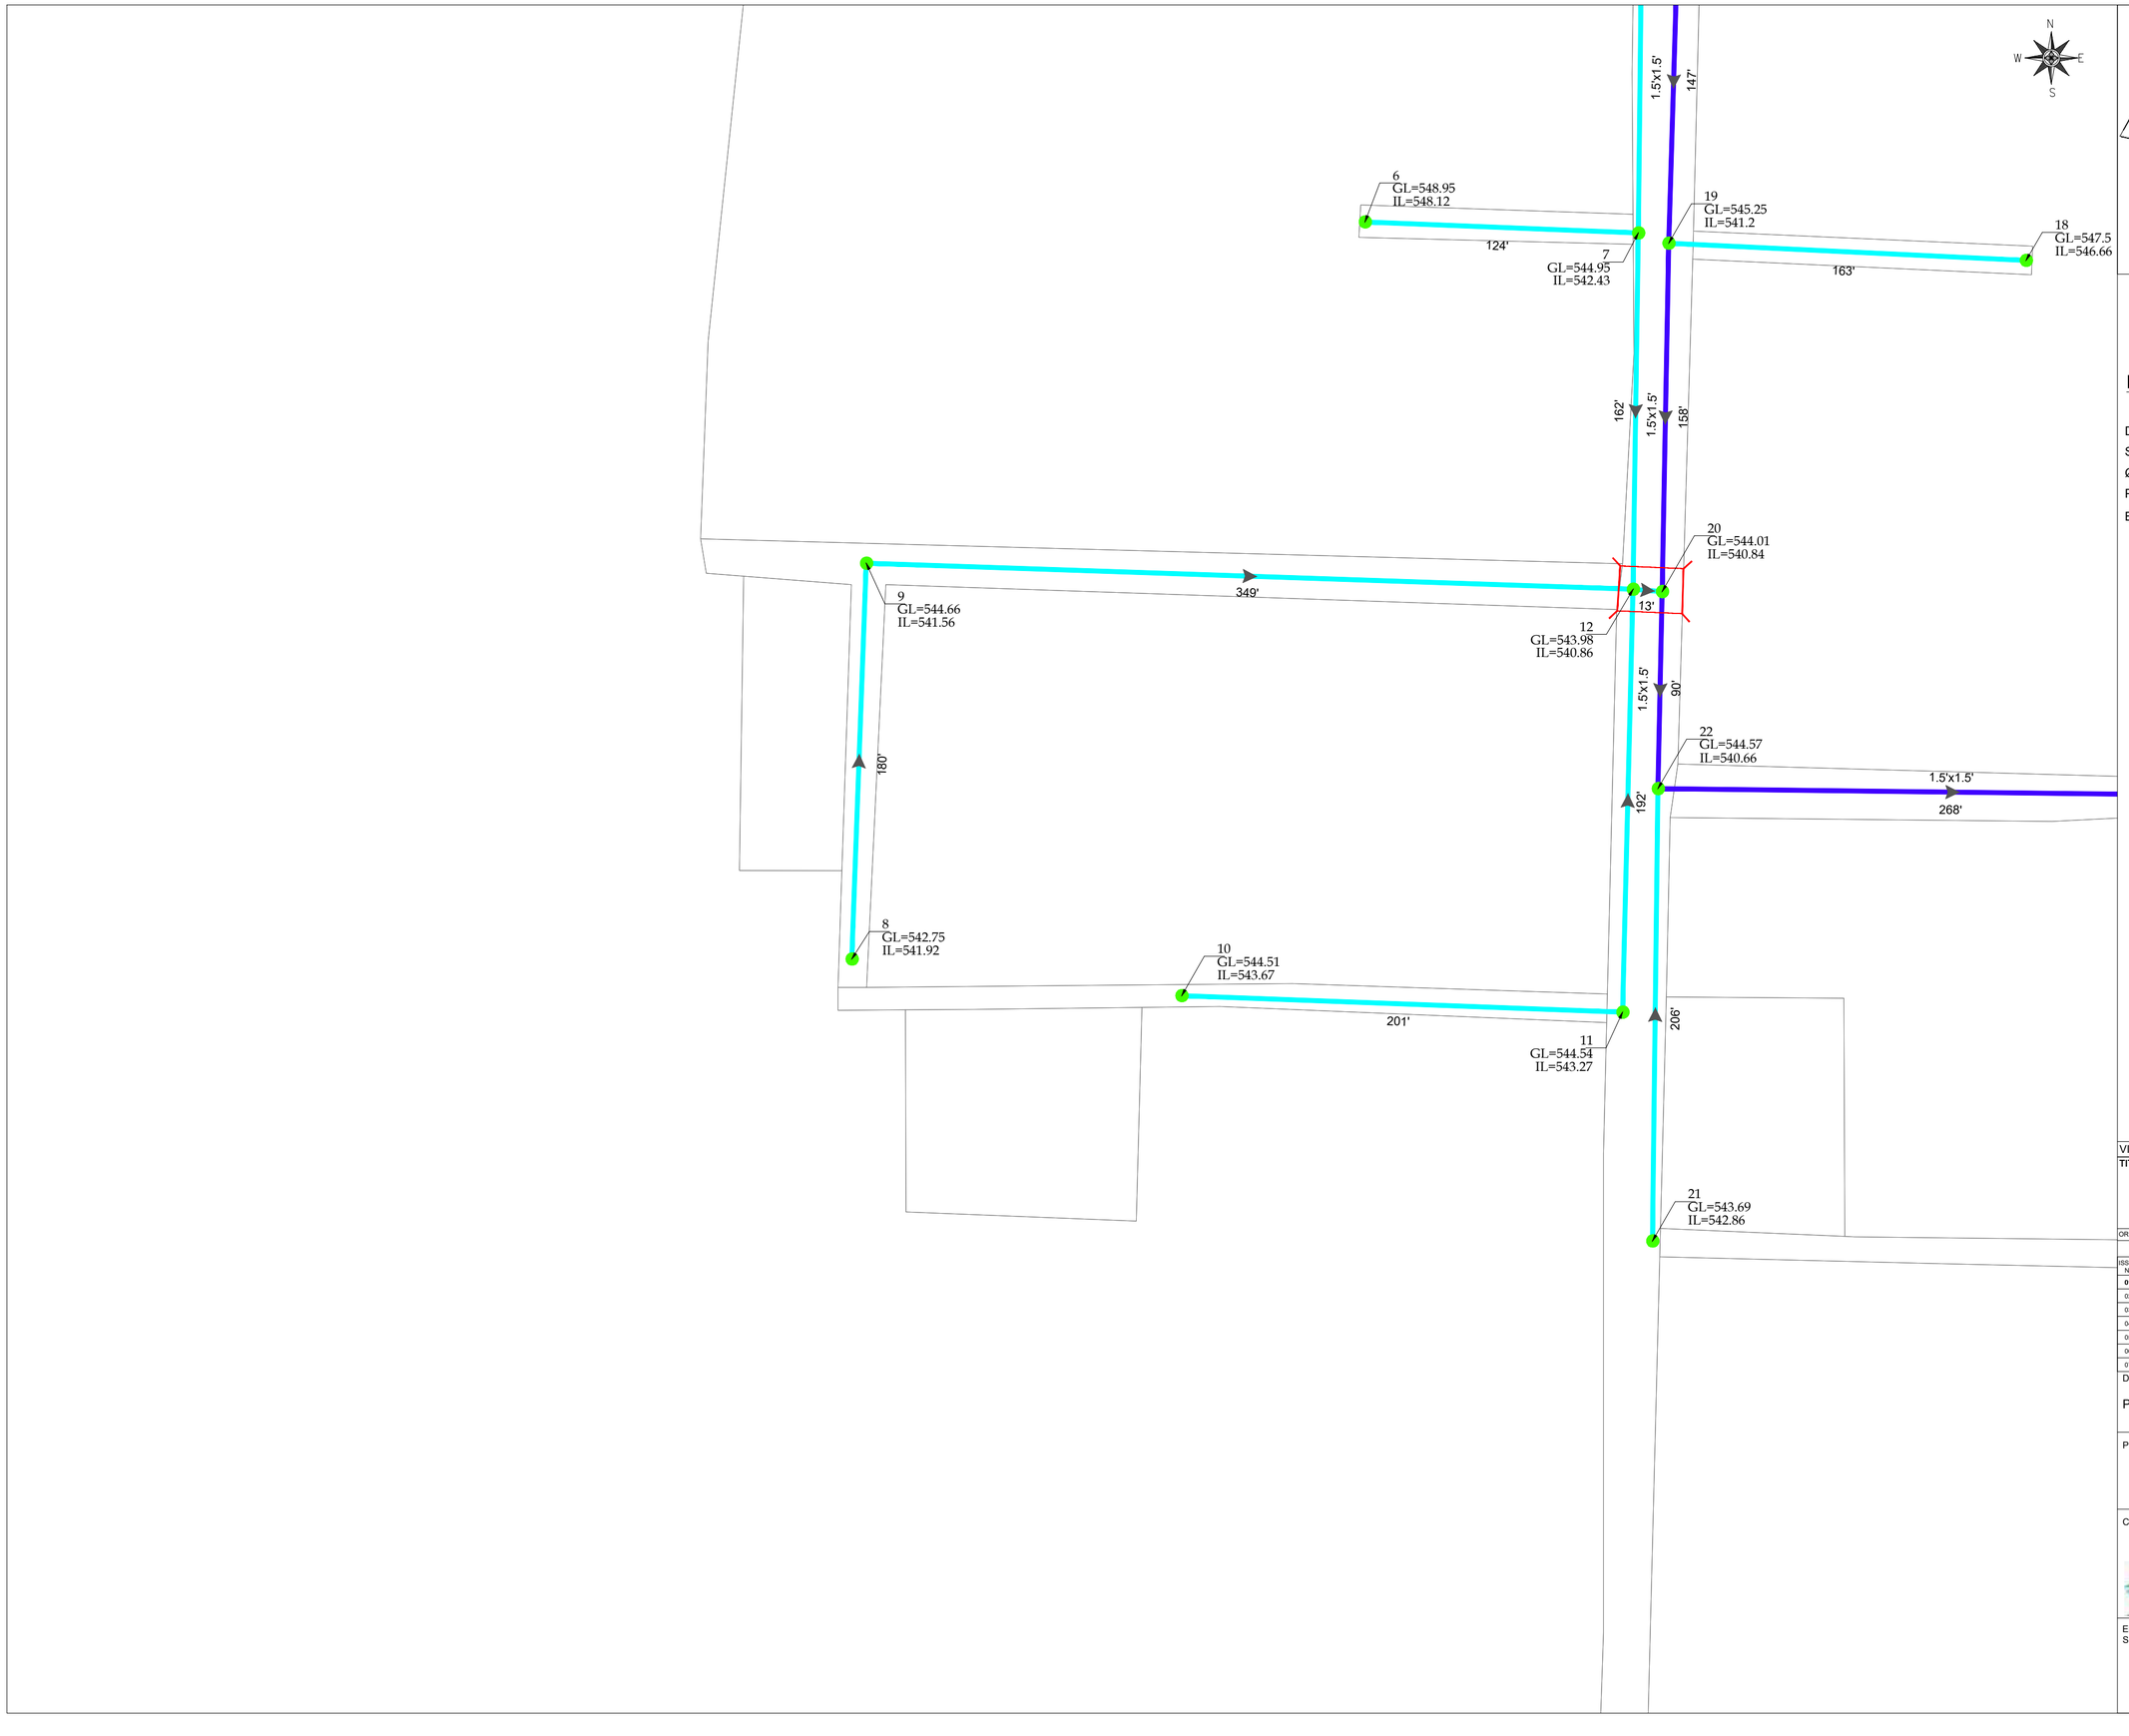

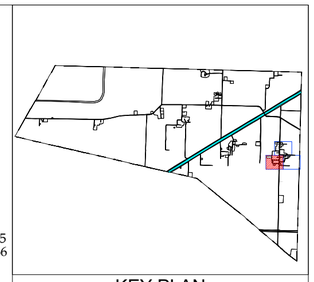

KEY PLAN

LEGEND:

DRAIN TYPE - I
SULLAGE CARRIER
Ø3" HDPE PIPE
PROPOSED CULVERT
BOUNDARY

VILLAGE: KHOBAR (BWN)

TITLE.

DRAINAGE SYSTEM LAYOUT PLAN-02

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	02-01-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02	20-04-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
03					
04					
05					
06					
07					

DRAWING N°:	SHEET	REV
PRMSC-BWN-KHB-SEW-LP-02	02 OF 03	01

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

PRMSC-BWN-KHB-SEW-LP-02

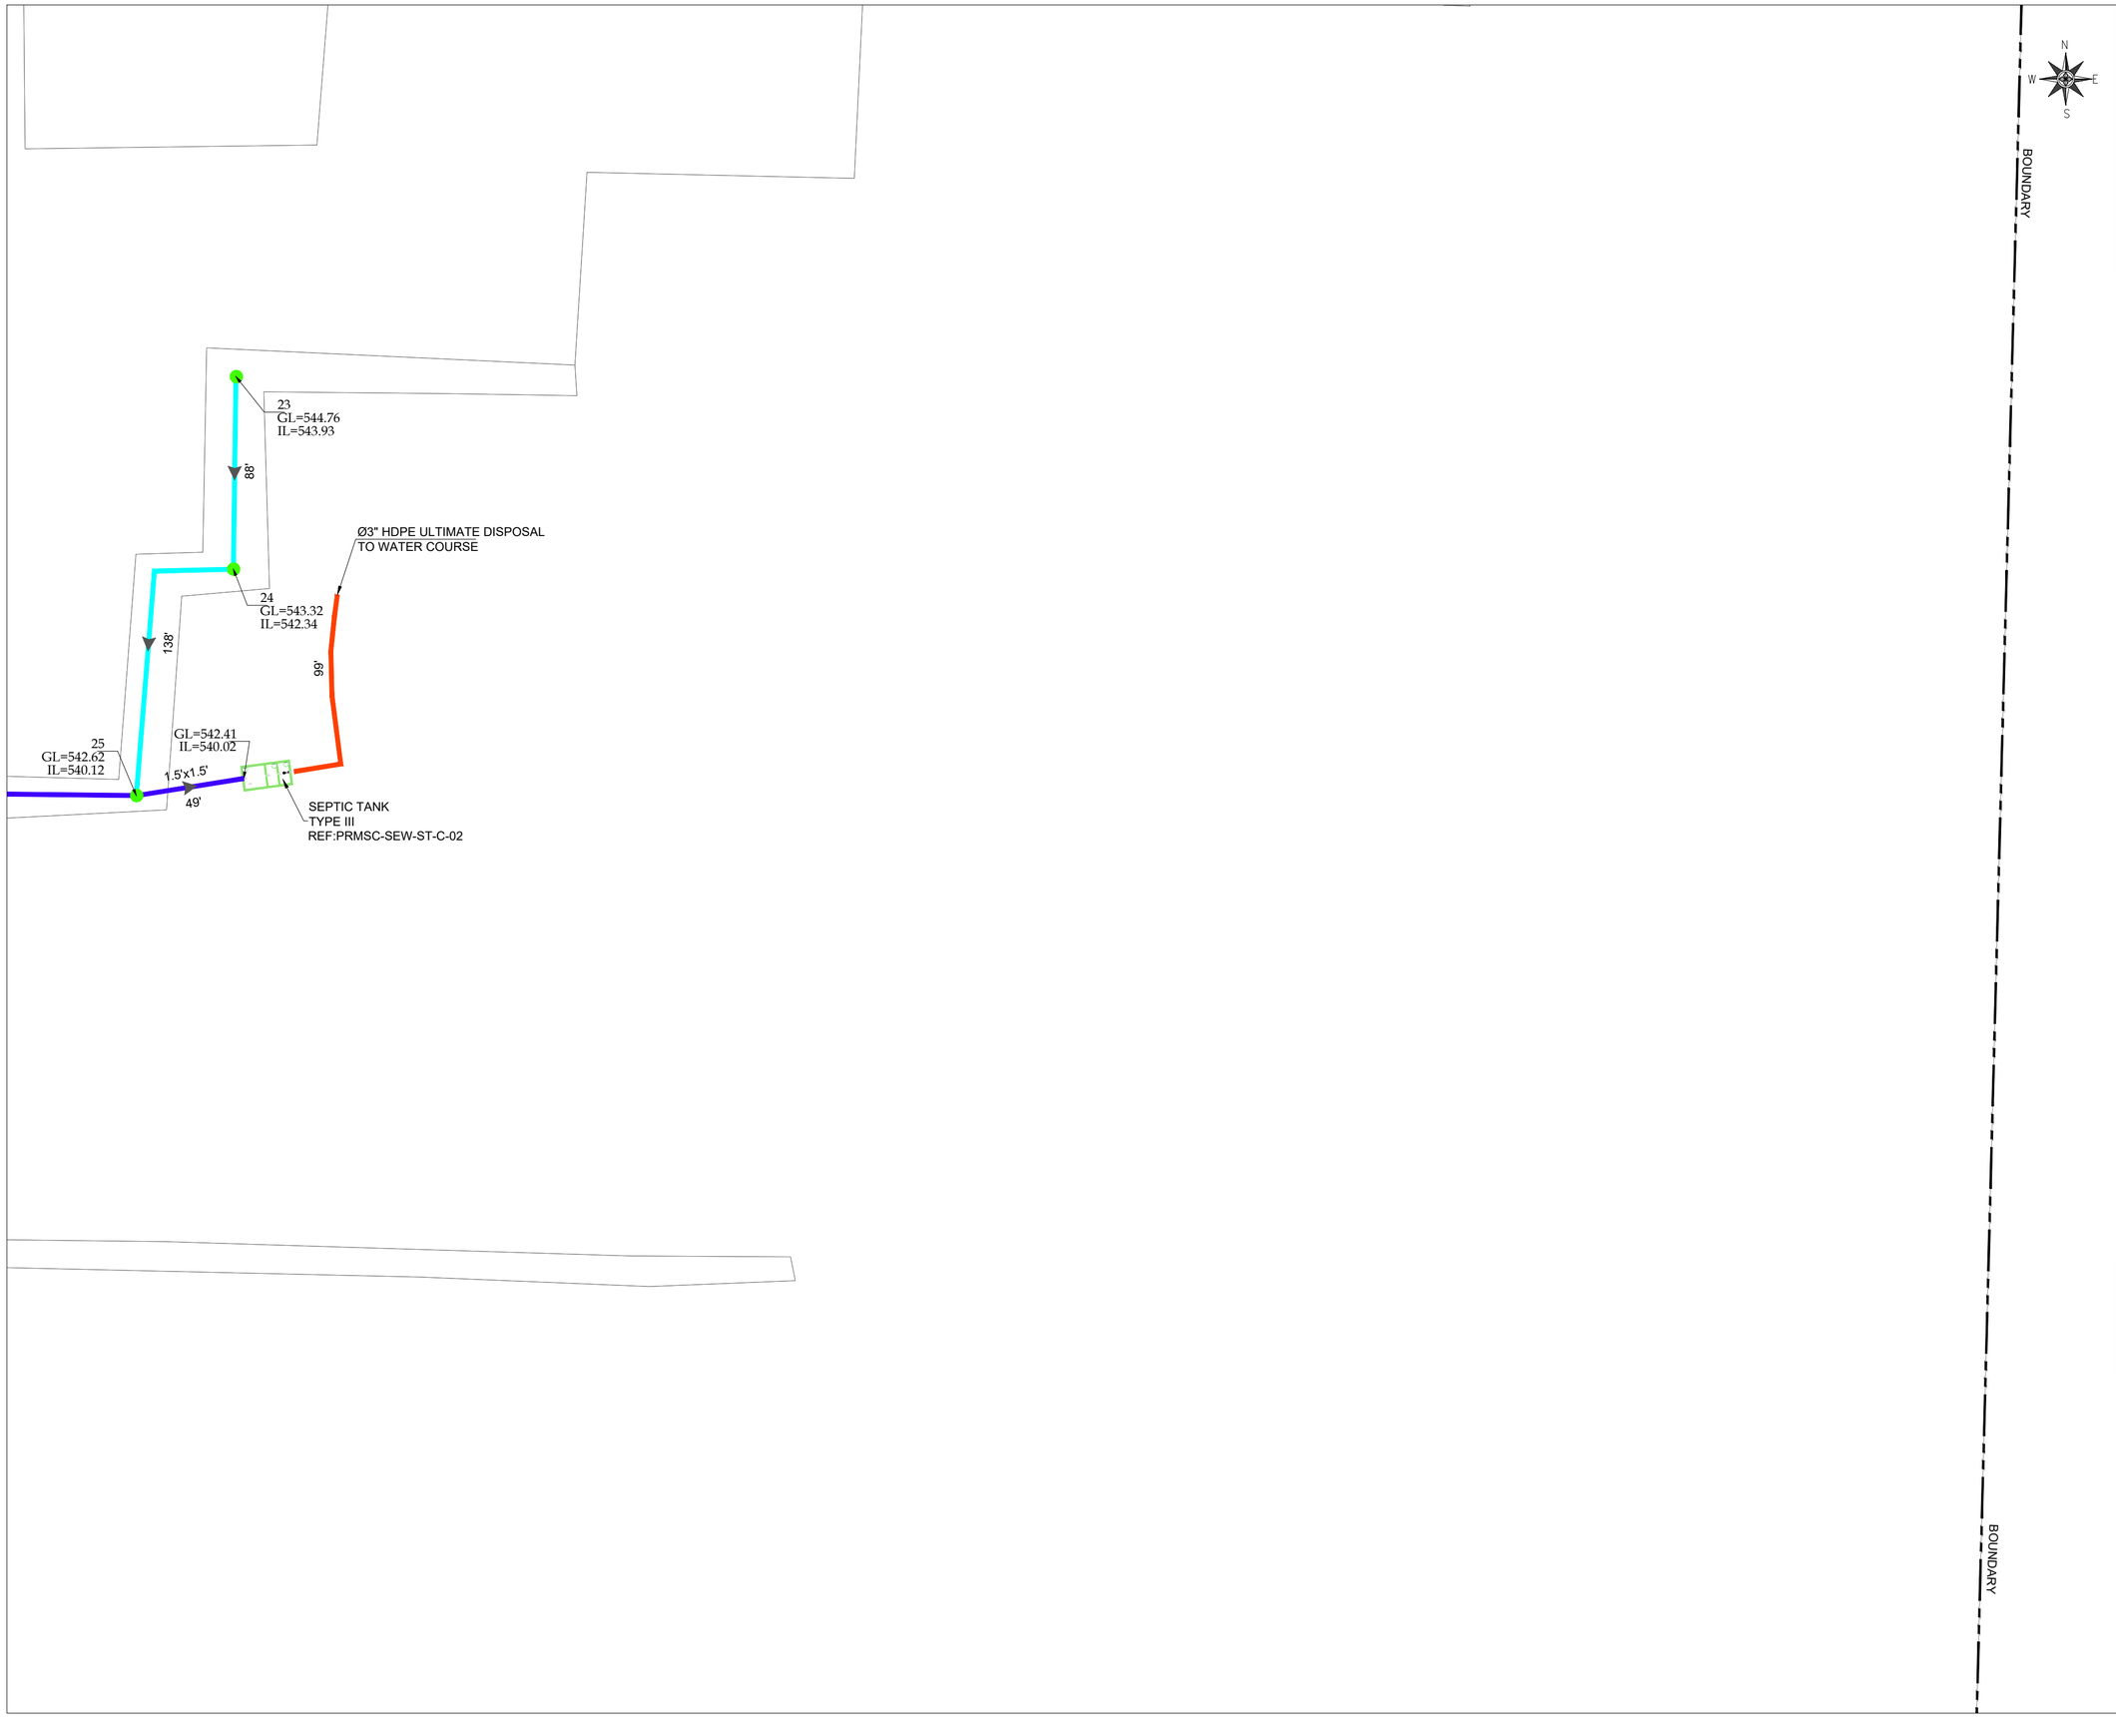

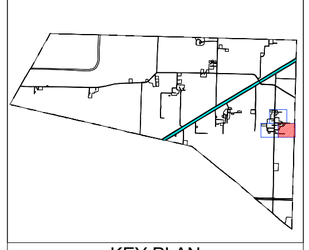

KEY PLAN

LEGEND:

DRAIN TYPE - I

SULLAGE CARRIER

Ø3" HDPE PIPE

PROPOSED CULVERT

BOUNDARY

VILLAGE: KHOBAR (BWN)

TITLE.

DRAINAGE SYSTEM LAYOUT PLAN-03

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	02-01-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02	20-04-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-KHB-SEW-LP-03	03 OF 03	01

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:
ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

PRMSC-BWN-KHB-SEW-LP-03

HYDRAULIC STATEMENT

Node		Length	Slope	Elevation Ground	Elevation Ground	Invert	Invert	Depth
FROM	TO	ft	ft/ft	U/S	D/S	U/S	D/S	ft
1	3	476	0.003	545.35	544.75	544.52	543.12	0.83
2	3	206	0.002	544.36	544.75	543.53	543.12	0.83
3	5	105	0.002	544.75	544.74	543.12	542.9	1.63
4	5	148	0.016	546.14	544.74	545.3	542.9	0.83
5	7	240	0.002	544.74	544.95	542.9	542.43	1.84
6	7	124	0.046	548.95	544.95	548.12	542.43	0.83
7	12	162	0.002	544.95	543.98	542.43	542.1	2.52
8	9	180	0.002	542.75	544.66	541.92	541.56	0.83
9	12	349	0.002	544.66	543.98	541.56	540.86	3.1
10	11	201	0.002	544.51	544.54	543.67	543.27	0.83
11	12	192	0.002	544.54	543.98	543.27	542.89	1.27
12	20	13	0.002	543.98	544.01	540.86	540.84	3.12
13	17	579	0.002	543.58	545	542.75	541.5	0.83
14	16	283	0.002	545.32	544.71	544.49	543.88	0.83
15	16	145	0.002	543.21	544.71	542.38	542.09	0.83
16	17	295	0.002	544.71	545	542.09	541.5	2.63
17	19	147	0.002	545	545.25	541.5	541.2	3.5
18	19	163	0.034	547.5	545.25	546.66	541.2	0.83
19	20	158	0.002	545.25	544.01	541.2	540.84	4
20	22	90	0.002	544.01	544.57	540.84	540.66	3.18
21	22	206	0.002	543.69	544.57	542.86	542.45	0.83
22	25	268	0.002	544.57	542.62	540.66	540.12	3.91
23	24	88	0.018	544.76	543.32	543.93	542.34	0.83
24	25	138	0.004	543.32	542.62	542.34	541.78	0.98
25	Septic Tank Type-III	49	0.002	542.62	542.41	540.12	540.02	2.5

VILLAGE: KHOBER (BWN)

TITLE.

HYDRAULIC STATEMENT

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	02-01-2026	DETAILED DESIGN	MUNEEB	ENGR. FAEIZ	ENGR. HSANULHAQ
02	20-04-2026	DETAILED DESIGN	MUNEEB	ENGR. FAEIZ	ENGR. HSANULHAQ
03					
04					
05					
06					
07					

DRAWING Nº: PRMSC-BWN-KHB-SEW-HS-01

SHEET 01 OF 01

REV 01

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT
ASIAN CONSULTING ENGINEERS
www.asianeon.com.pk

PRMSC-BWN-KHB-SEW-HS-00

ALLAHABAD

KEY PLAN

Revenue Village: Allahabad Sheet-1

N

District:	Bahawalnagar
Tehsil:	Bahawalnagar
Revenue Village:	Allahabad

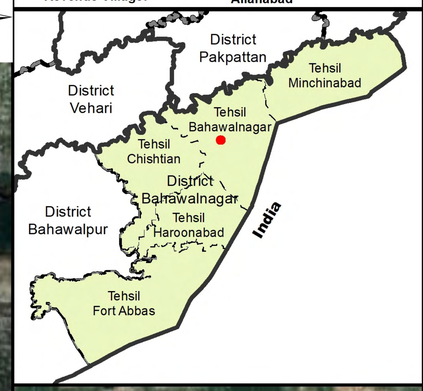

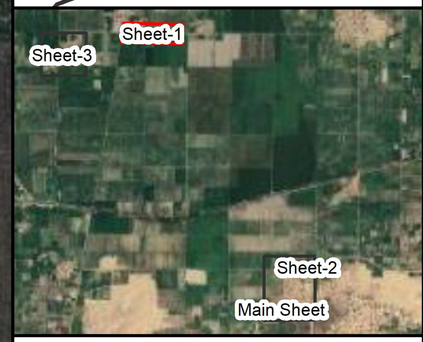

Buddhanwali

ND-1 GL=512.29 IL=511.46
30'
ND-2 GL=513.01 IL=510.65
33'
ND-3 GL=512.62 IL=510.39
262'
ND-7 GL=513.45 IL=509.86
24'
ND-4 GL=512.26 IL=511.43
45'
ND-5 GL=514.07 IL=511.11
520'
1.5'X1.5'
ND-6 GL=513 IL=512.17
ND-8 GL=511.78 IL=508.62
136'
GL=510.87 IL=509.55
127'
3" HDPE PIPE ULTIMATE DISPOSAL TO WATER COURSE
SEPTIC TANK-T1 Plot Size=1.59 Marla

Title:
Proposed Drainage Network Plan

Legend:

- SETTLEMENT
- NODE
- 3"HDPE PIPE
- DRAIN TYPE-1
- SULLAGE CARRIER
- SEPTIC TANK
- SETTLEMENT BOUNDARY

Drain Type 1=8808 Rft
Sullage Carrier= 3324 Rft

Scale: 1:1,700
1 inch = 142 feet
Paper Size: A3

0 40 80 160
Kilometers

Project:
Engineering Design & Construction Supervision, Punjab Rural Sustainable Water Supply & Sanitation Project, Cluster South III

PRWSC
ENVIRONMENTAL TECHNOLOGIES
ASIAN CONSULTING ENGINEERS www.asiancon.com

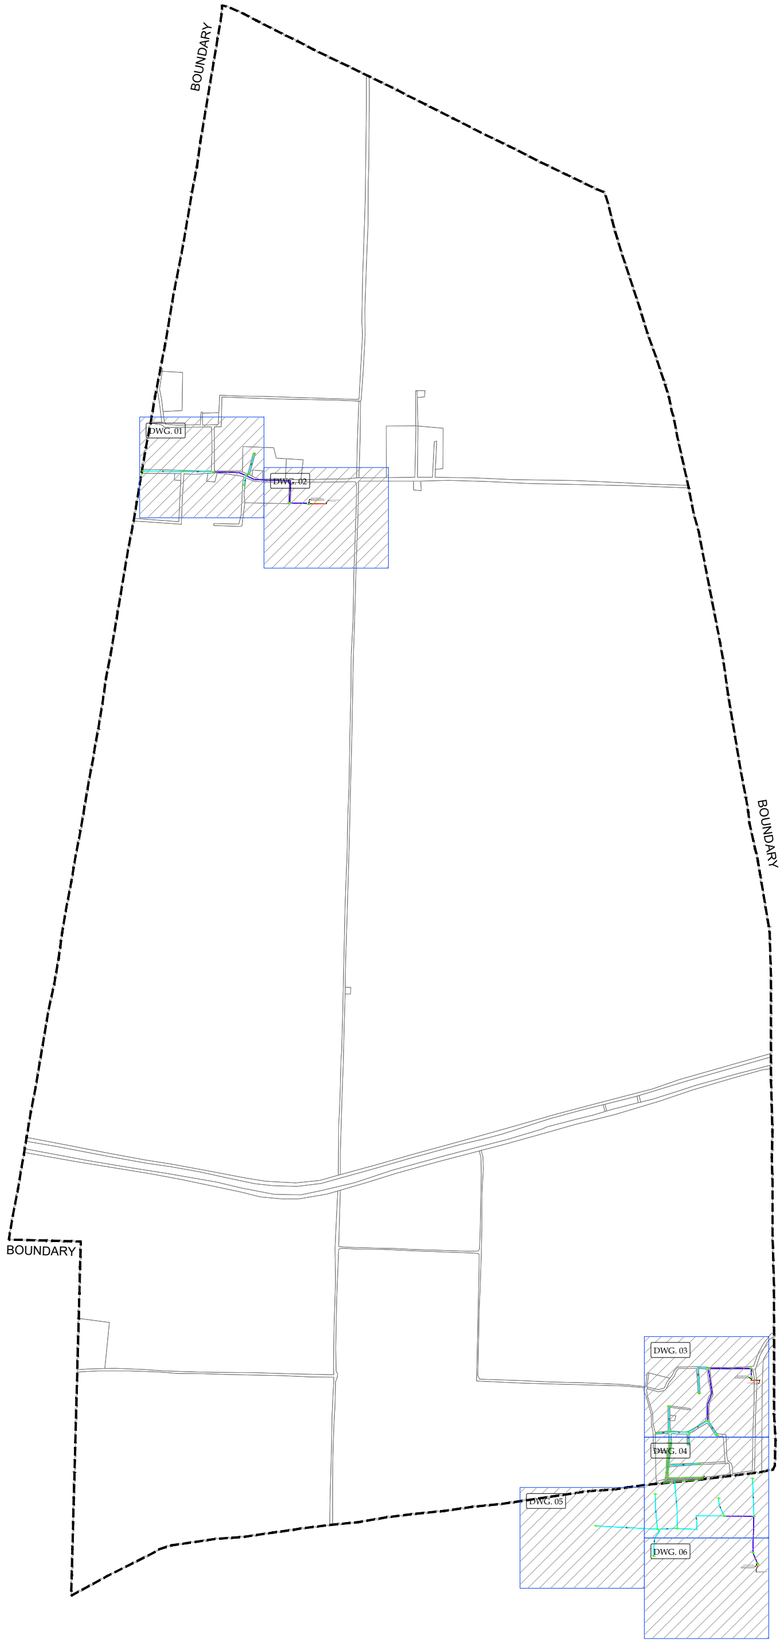

N
W
E
S

LEGEND:

- DRAIN TYPE - I
- SULLAGE CARRIER
- Ø3" HDPE PIPE
- EXISTING SOLING
- BOUNDARY

VILLAGE: ALLAHABAD (BWN)

TITLE.

DRAINAGE SYSTEM KEY PLAN

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 850'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	21-04-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-AB-SEW-KP-00	00 OF 00	00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT
ASIAN CONSULTING ENGINEERS
www.asianeon.com

PRMSC-BWN-AB-SEW-KP-00

LAYOUT PLAN

Revenue Village: Allahabad Sheet-2

N

District:	Bahawalnagar
Tehsil:	Bahawalnagar
Revenue Village:	Allahabad

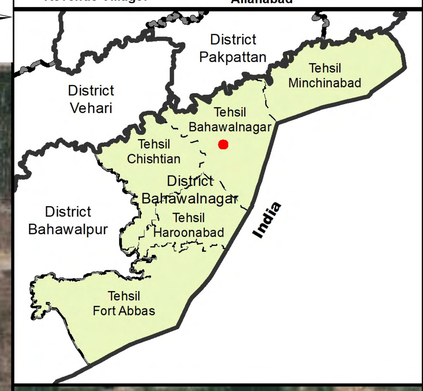

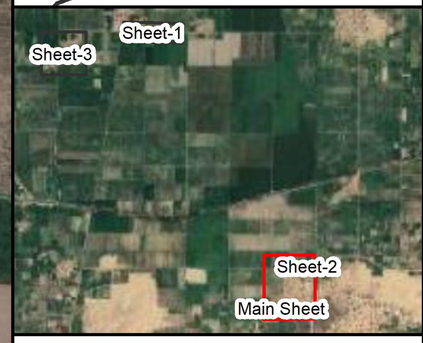

ND-20 GL=513.26 IL=510.64
ND-21 GL=512.28 IL=509.95
SEPTIC TANK-T3 Plot Size=2.62 Marla
3" HDPE PIPE TO ULTIMATE DISPOSAL TO WATER COURSE
GL=510.55 IL=509.72
ND-19 GL=519.96 IL=519.12
ND-12 GL=517.66 IL=516.83
ND-18 GL=512.3 IL=511.46
ND-13 GL=513.42 IL=512.59
ND-14 GL=516.37 IL=512.39
ND-16 GL=515.42 IL=512.41
ND-17 GL=514.21 IL=513.37
ND-15 GL=516.98 IL=516.14
Muhammadpura
ND-9 GL=518.64 IL=517.81
ND-11 GL=519.51 IL=516.68
ND-10 GL=519.35 IL=518.51
ND-26 GL=519.87 IL=519.04
ND-30 GL=510.53 IL=509.5
ND-23 GL=518.48 IL=517.65
ND-28 GL=515.72 IL=514.88
ND-29 GL=509.32 IL=508.49
ND-31 GL=511 IL=508.03
ND-22 GL=515.38 IL=514.52
ND-25 GL=515.72 IL=512.23
ND-27 GL=512.45 IL=510.38
ND-24 GL=519.86 IL=519.19
ND-32 GL=510.22 IL=507.46
SEPTIC TANK-T1 Plot Size=1.59 Marla
GL=509.21 IL=507.30
3" HDPE ULTIMATE DISPOSAL TO WATER COURSE

Title:
Proposed Drainage Network Plan

Legend:

- SETTLEMENT
- NODE
- 3" HDPE PIPE
- DRAIN TYPE-1
- SULLAGE CARRIER
- SEPTIC TANK
- SETTLEMENT BOUNDARY

Drain Type 1=8808 Rft

Sullage Carrier= 3324 Rft

Scale: 1:2,100

1 inch = 175 feet

Paper Size: A3

0 40 80 160

Kilometers

Project:

Engineering Design & Construction Supervision, Punjab Rural Sustainable Water Supply & Sanitation Project, Cluster South III

PRMSC

ENVIRONMENTAL TECHNOLOGIES

ASIAN CONSULTING ENGINEERS www.asiancon.com

KEY PLAN

LEGEND:

- DRAIN TYPE - I
- SULLAGE CARRIER
- Ø3" HDPE PIPE
- EXISTING SOLING
- BOUNDARY

VILLAGE: ALLAHABAD (BWN)

TITLE.

DRAINAGE SYSTEM LAYOUT PLAN-01

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	21-04-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-AB-SEW-LP-01	01 OF 06	00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:
ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

PRMSC-BWN-AB-SEW-LP-01

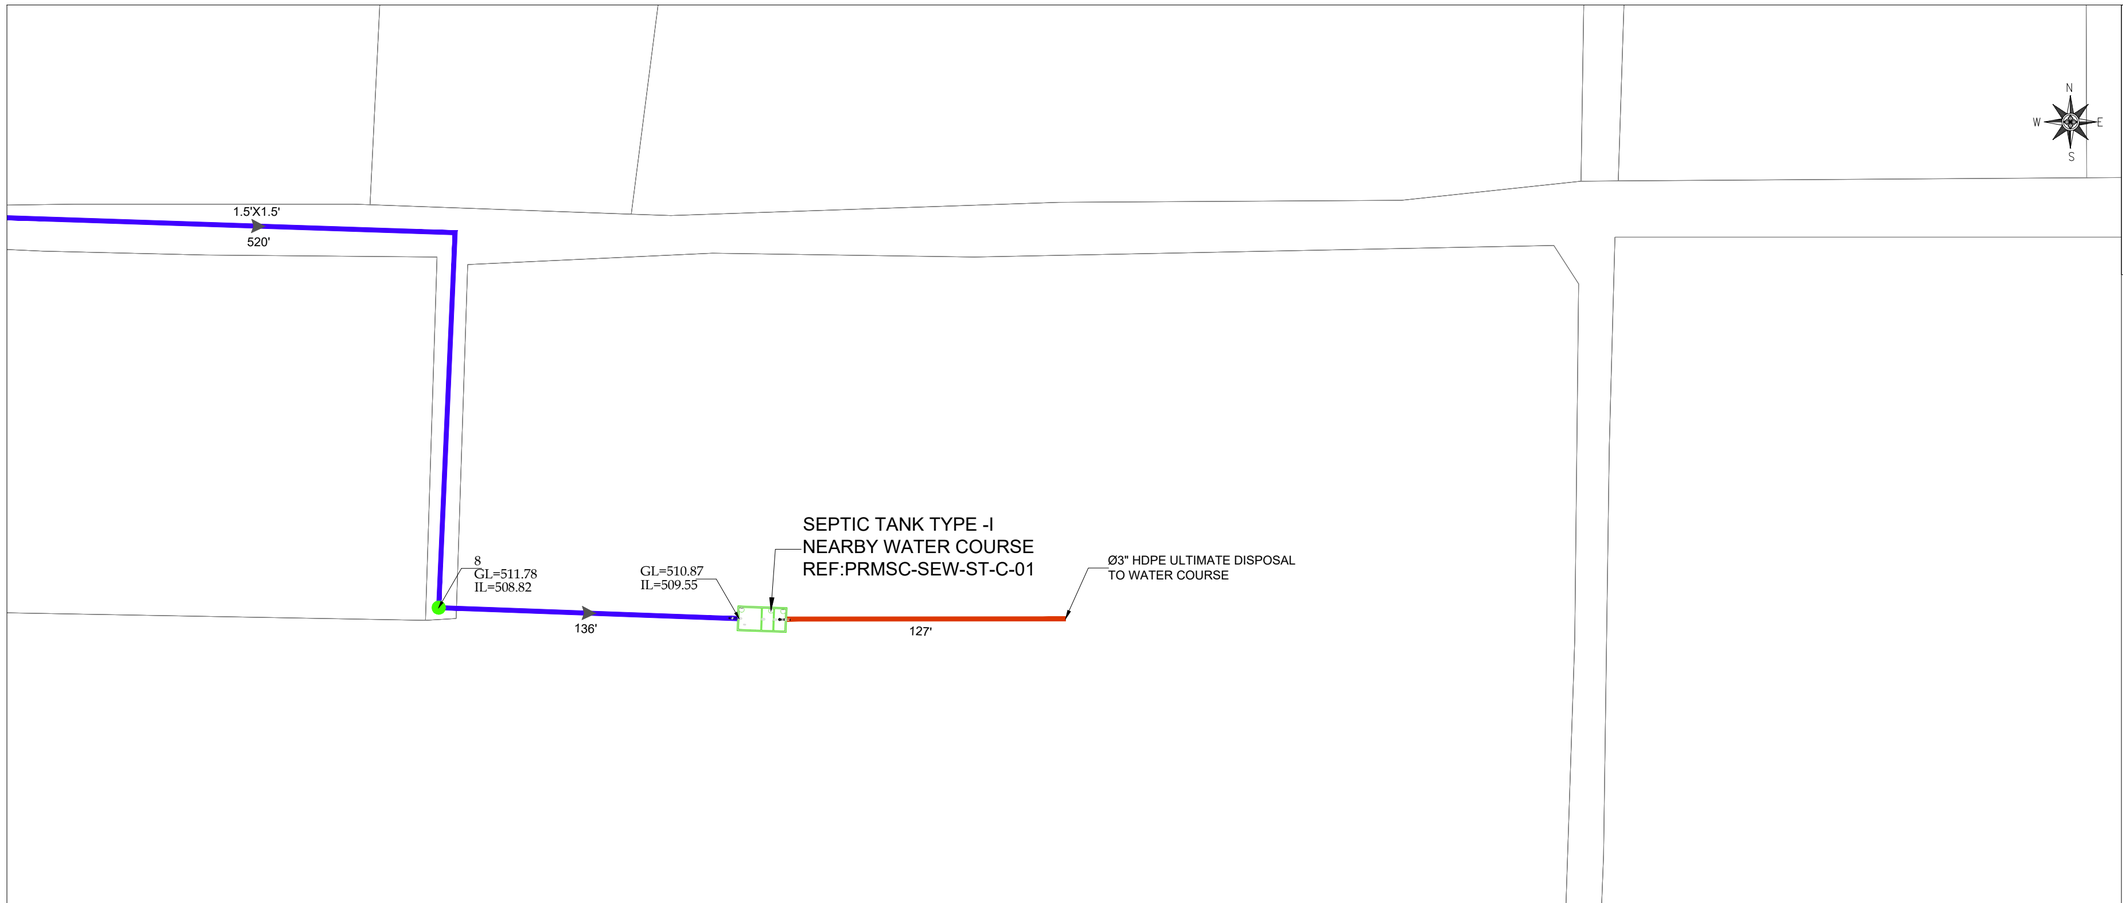

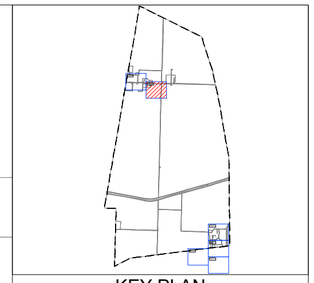

KEY PLAN

LEGEND:

- DRAIN TYPE - I
- SULLAGE CARRIER
- Ø3" HDPE PIPE
- EXISTING SOLING
- BOUNDARY

VILLAGE: ALLAHABAD (BWN)

TITLE.

DRAINAGE SYSTEM LAYOUT PLAN-02

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	21-04-2026	DETAILED DESIGN	MUNEEB	ENGR FAIEZ	ENGR IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-AB-SEW-LP-02	02 OF 06	00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

PRMSC-BWN-AB-SEW-LP-02

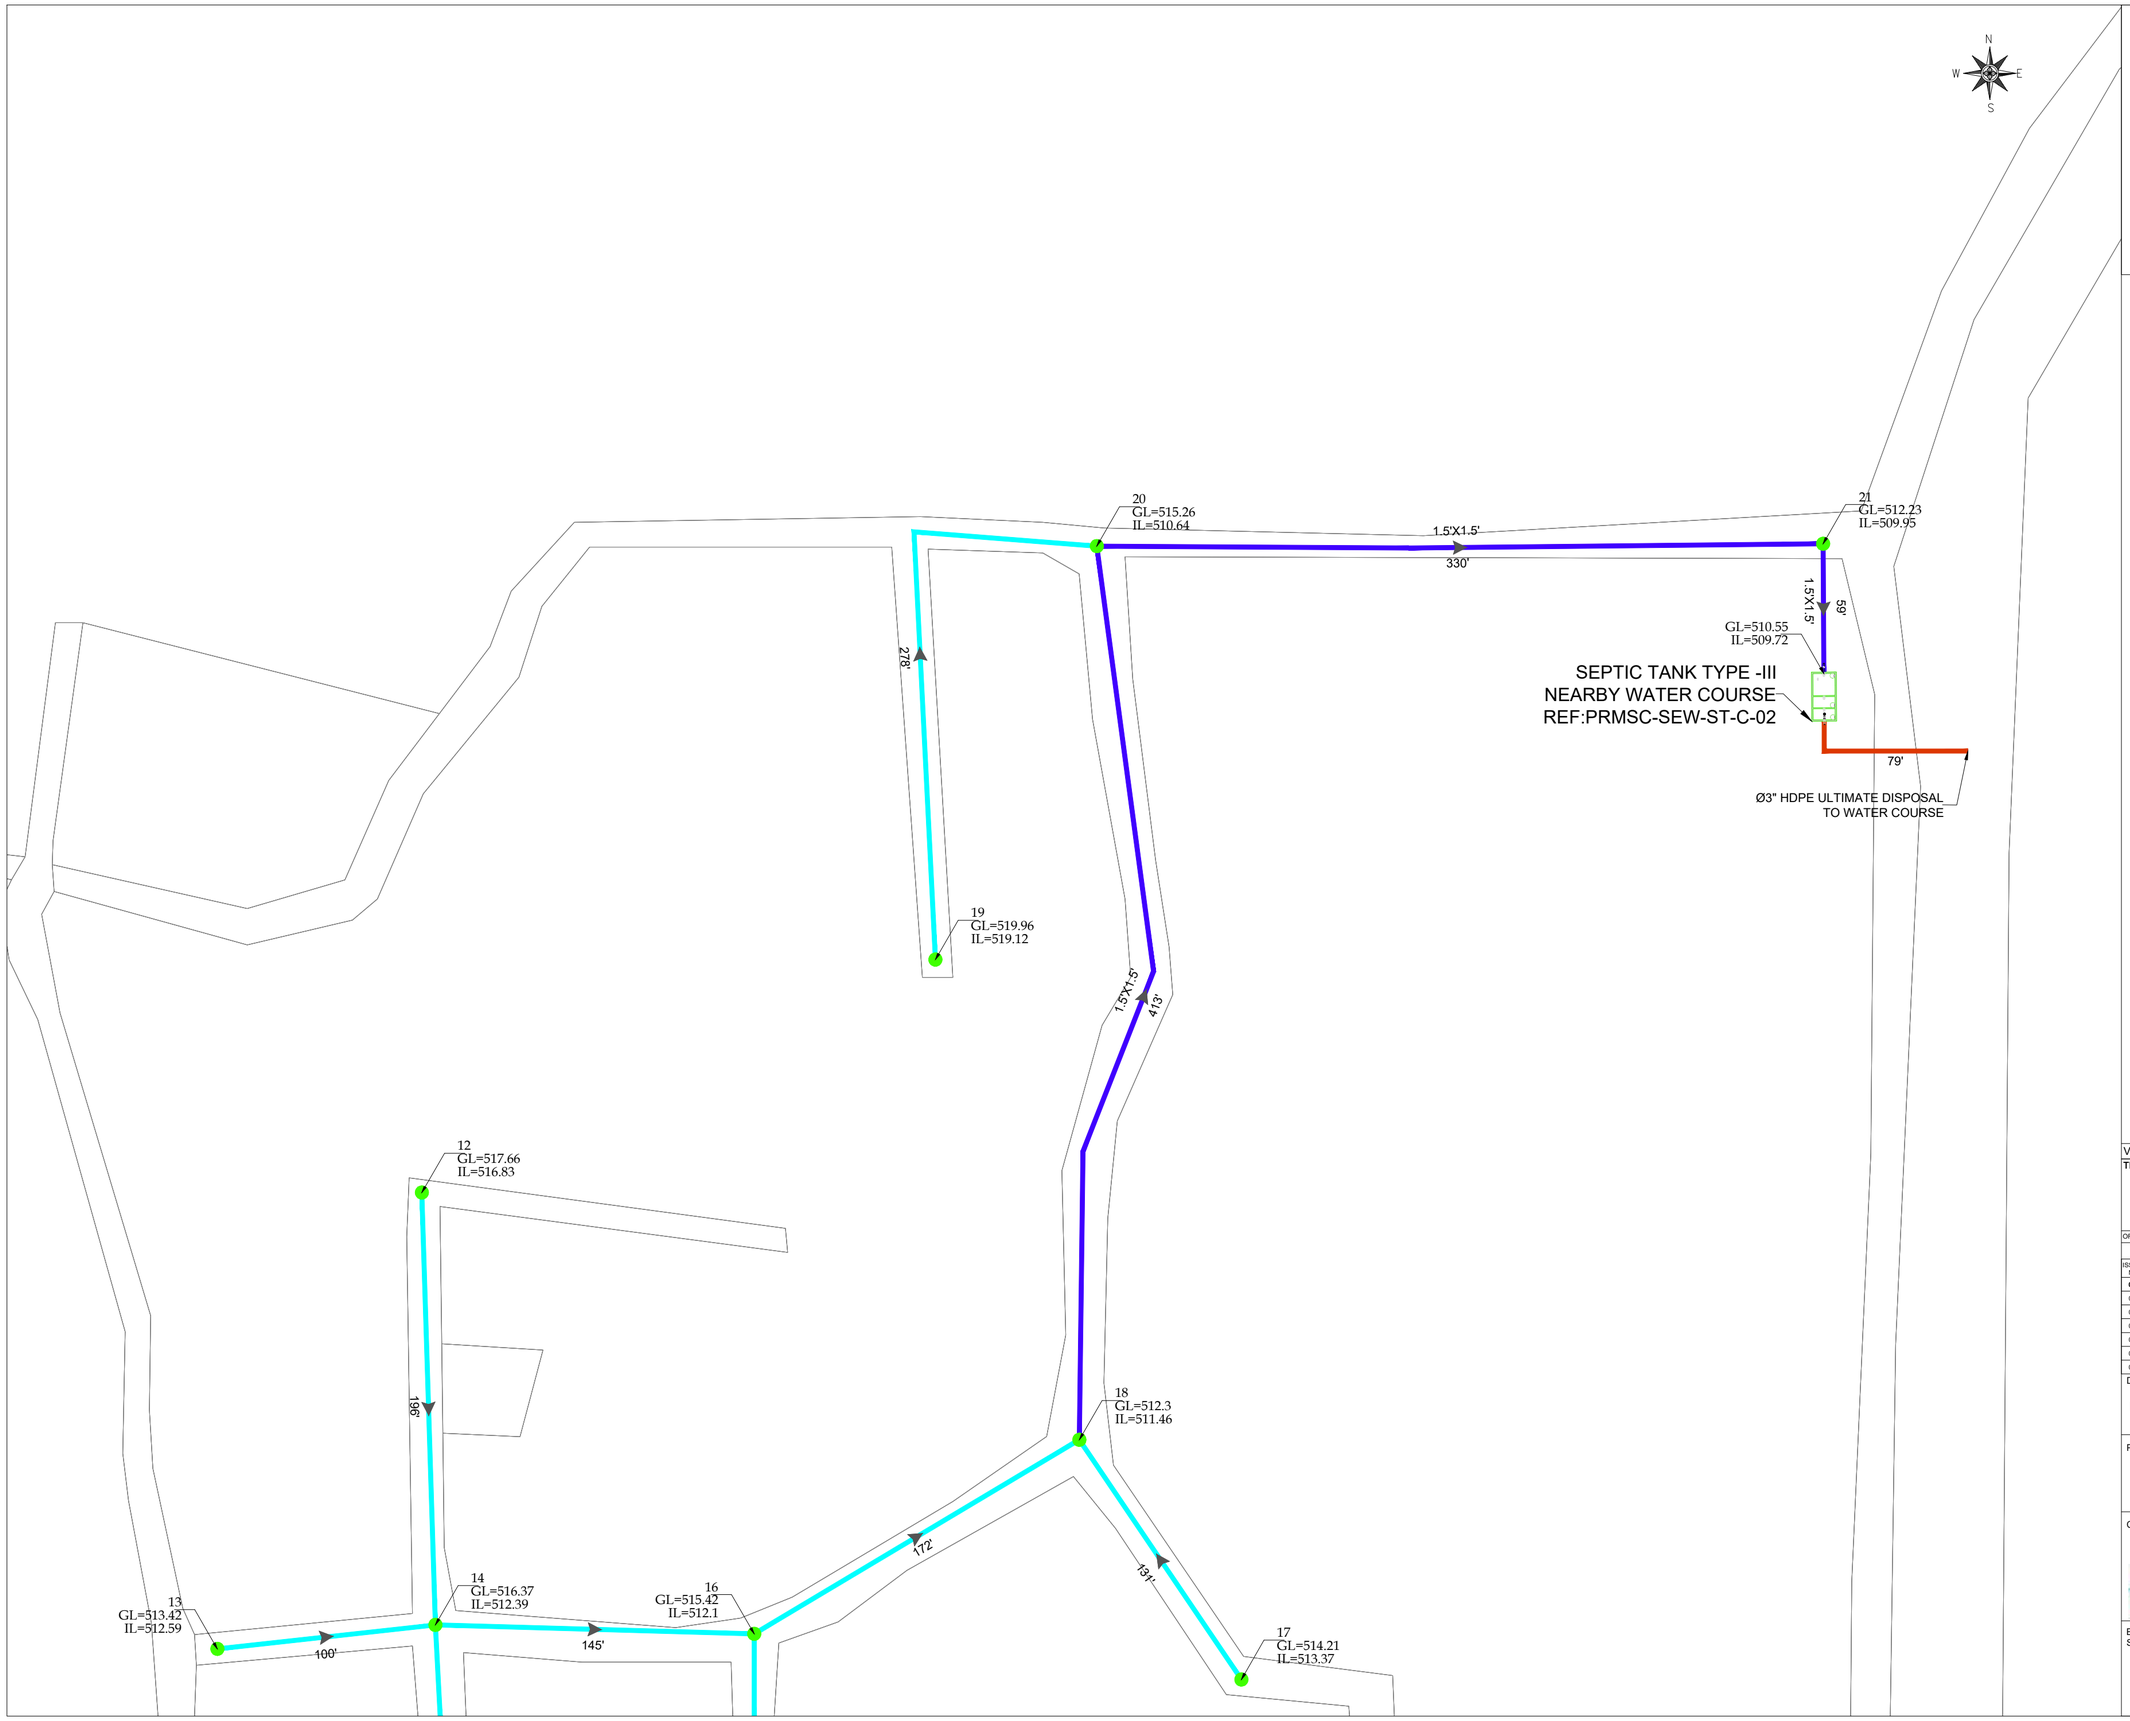

PRMSC-BWN-AB-SEW-LP-03



KEY PLAN

LEGEND:

- DRAIN TYPE - I
- SULLAGE CARRIER
- Ø3" HDPE PIPE
- EXISTING SOLING
- BOUNDARY

VILLAGE: ALLAHABAD (BWN)

TITLE.

DRAINAGE SYSTEM LAYOUT PLAN-03

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	21-04-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. HSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING N°: PRMSC-BWN-AB-SEW-LP-03

SHEET 03 OF 06

REV 00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS
www.asianeon.com.pv

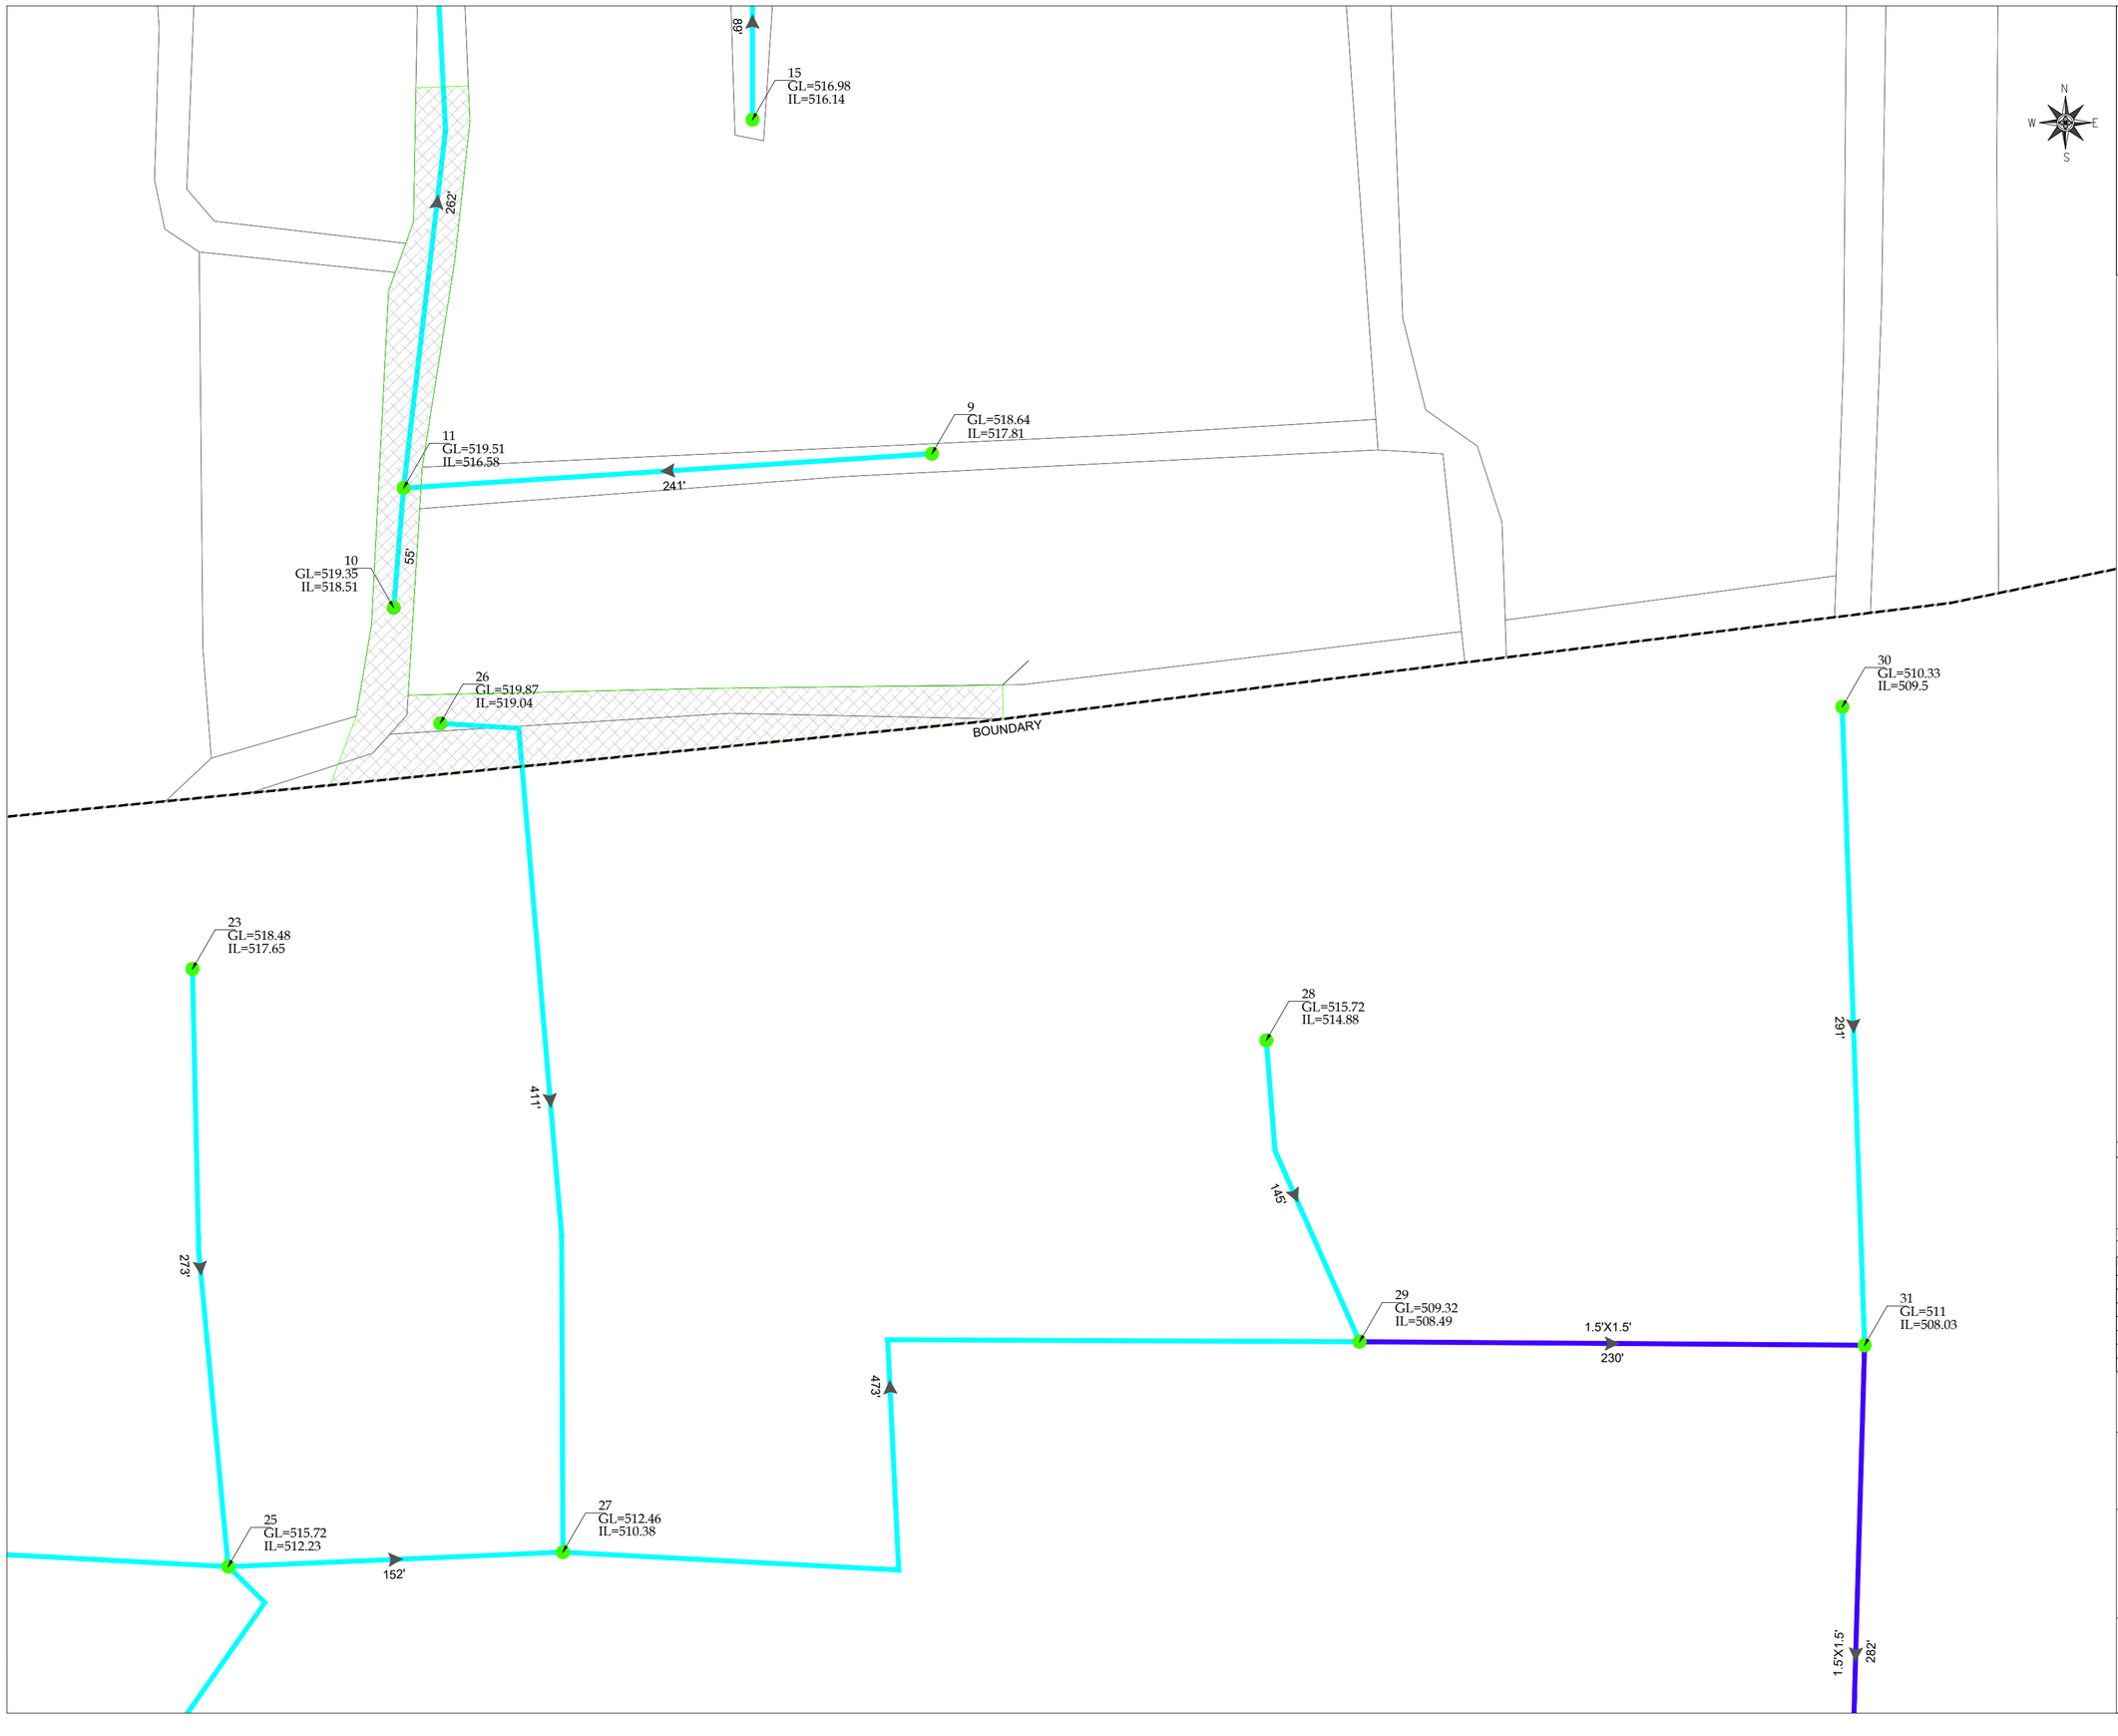

KEY PLAN

LEGEND:

- DRAIN TYPE - I
- SULLAGE CARRIER
- Ø3" HDPE PIPE
- EXISTING SOLING
- BOUNDARY

VILLAGE: ALLAHABAD (BWN)

TITLE.

DRAINAGE SYSTEM LAYOUT PLAN-04

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	21-04-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING N°:	SHEET	REV
PRMSC-BWN-AB-SEW-LP-04	04 OF 06	00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS
www.asiacon.com.pk

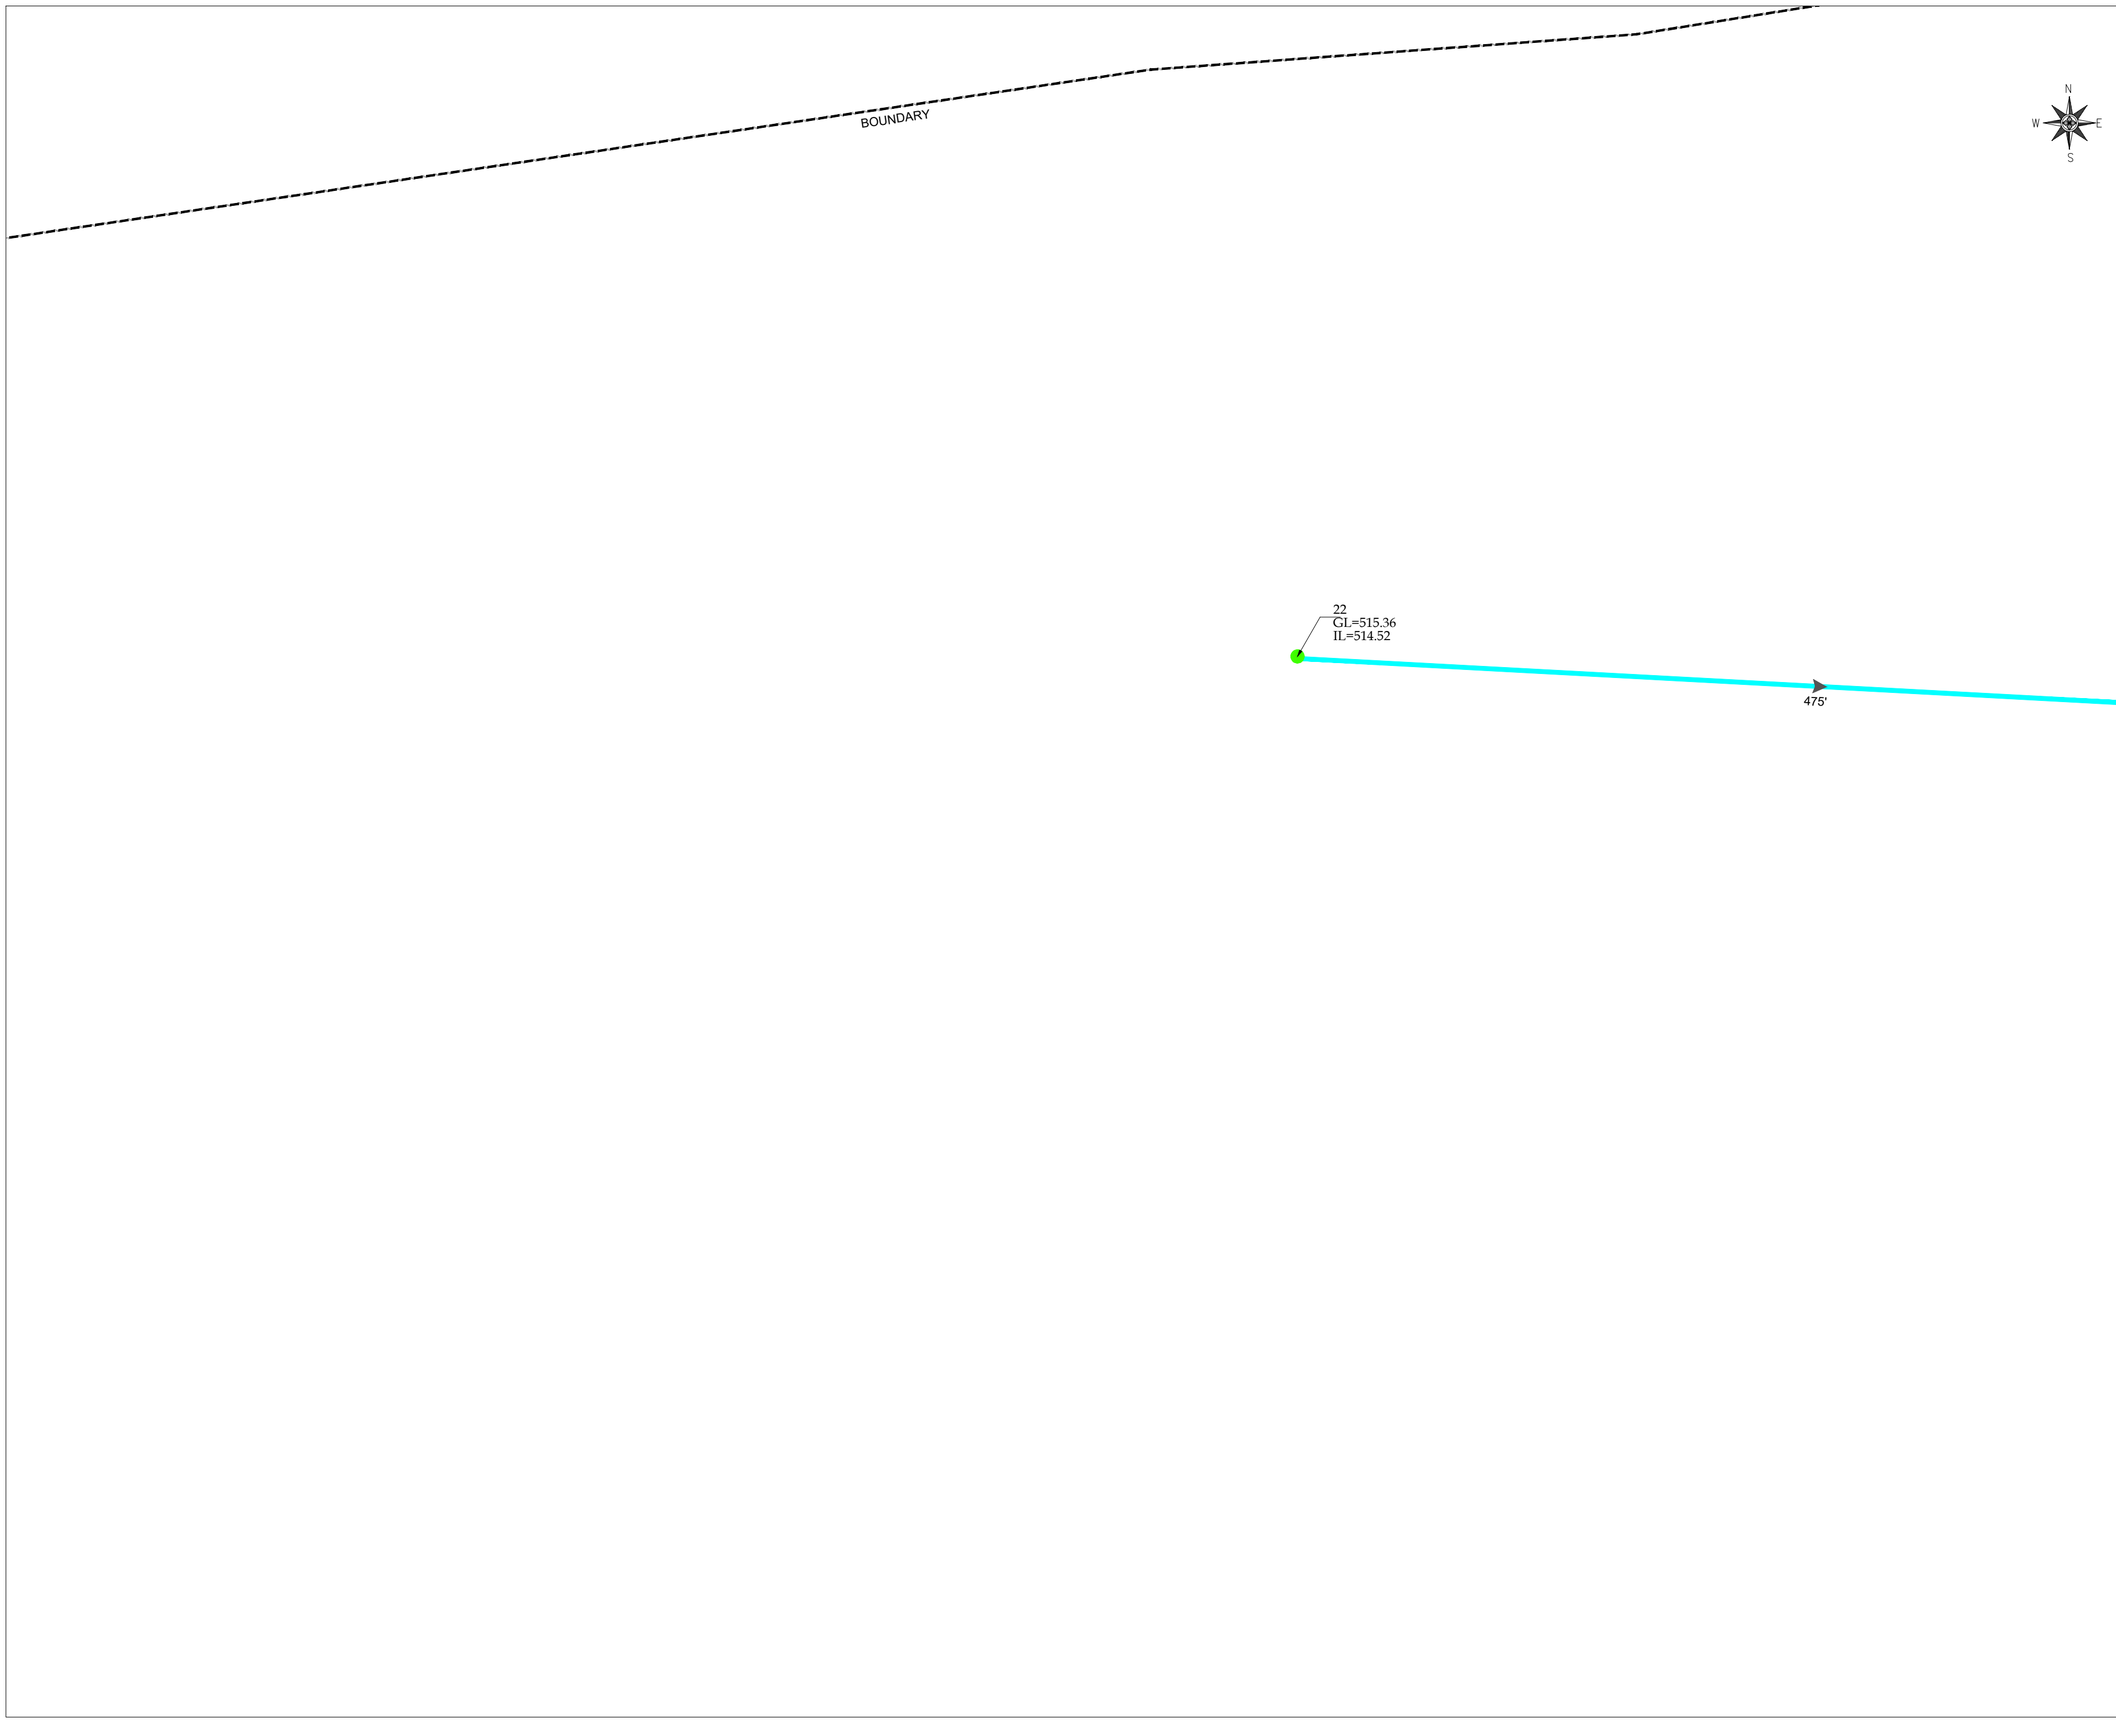

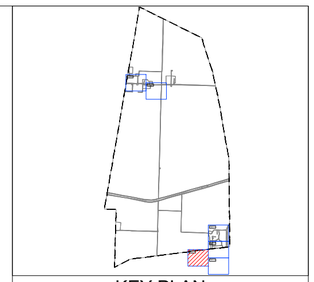

KEY PLAN

LEGEND:

- DRAIN TYPE - I
- SULLAGE CARRIER
- Ø3" HDPE PIPE
- EXISTING SOLING
- BOUNDARY

VILLAGE: ALLAHABAD (BWN)

TITLE.

DRAINAGE SYSTEM LAYOUT PLAN-05

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	21-04-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-AB-SEW-LP-05	05 OF 06	00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS
www.asiacon.com.pk

PRMSC-BWN-AB-SEW-LP-05

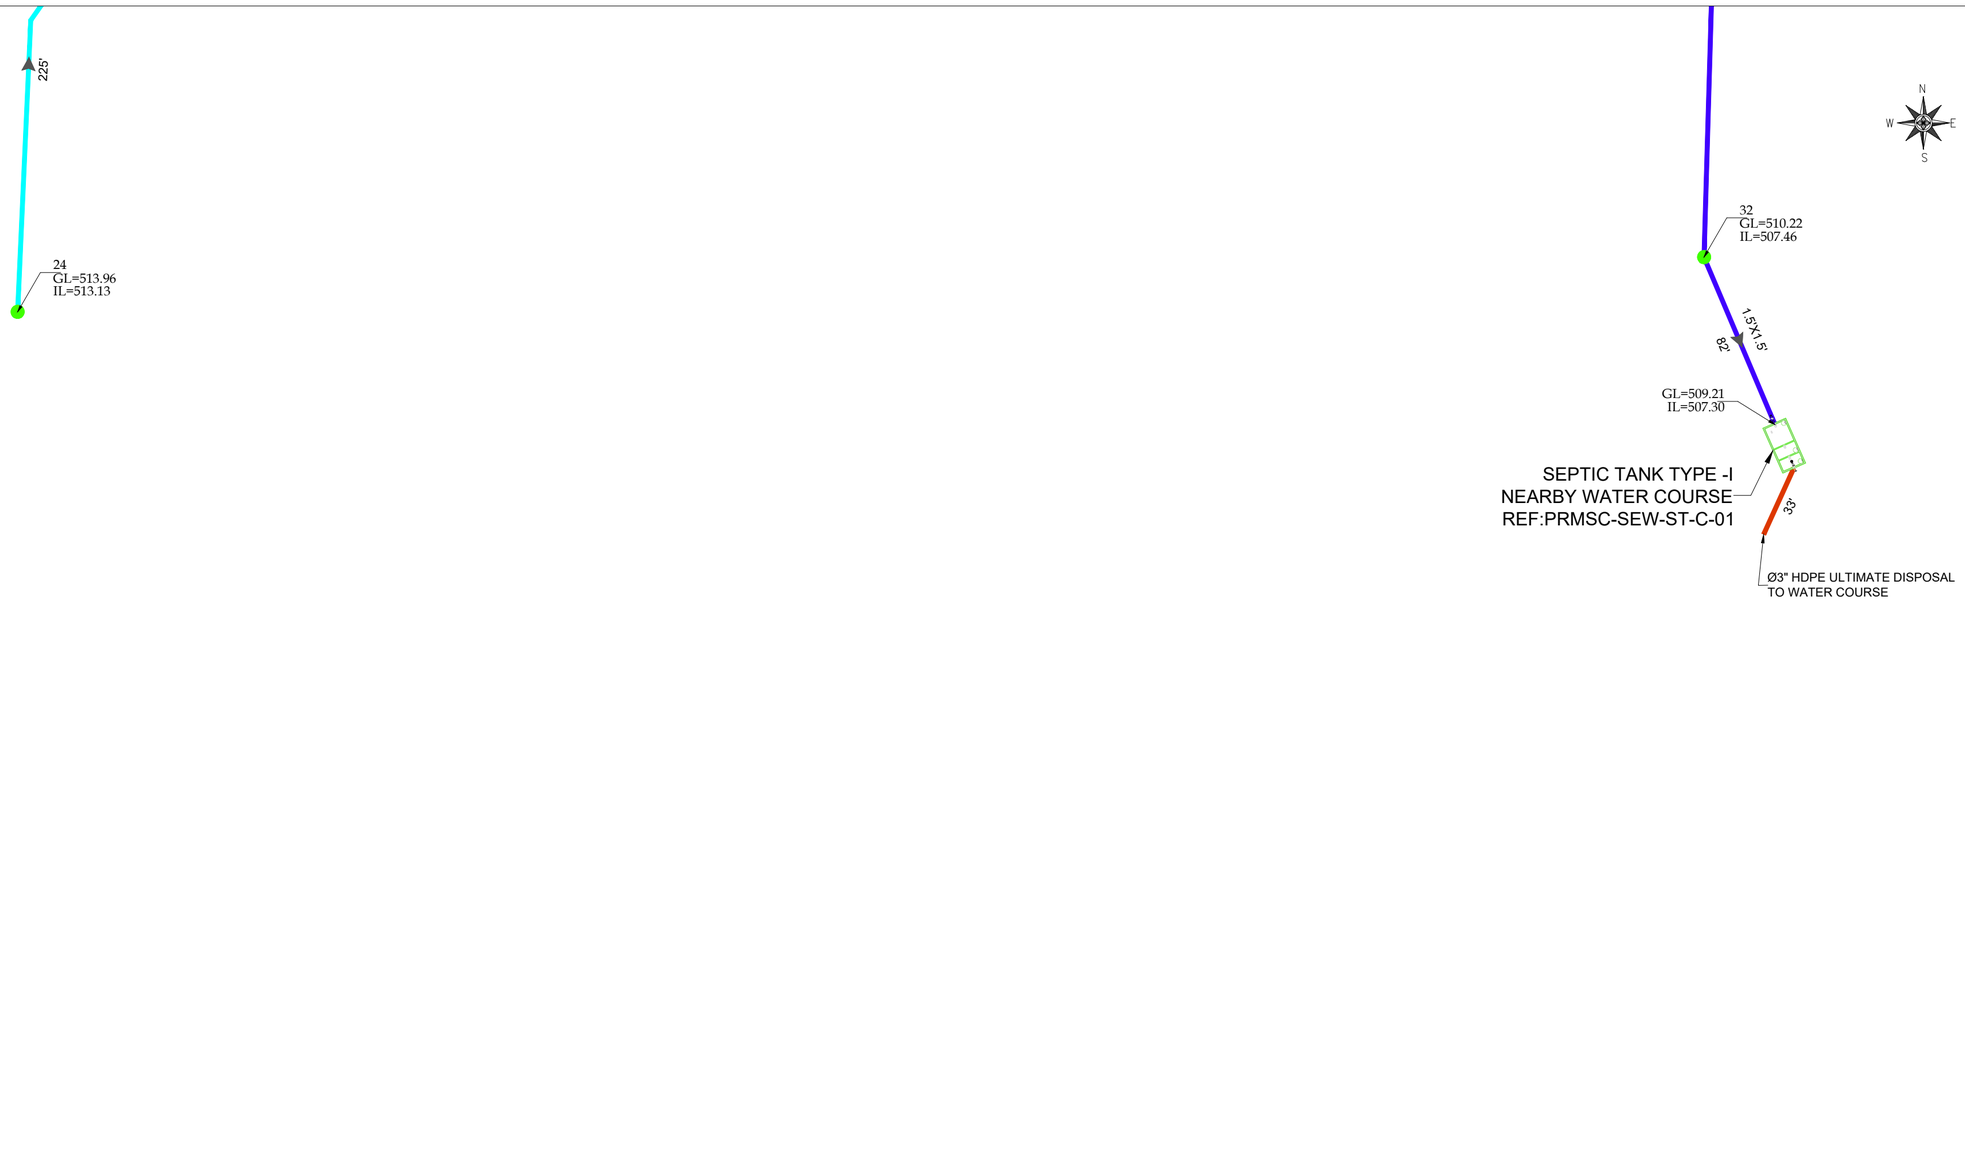

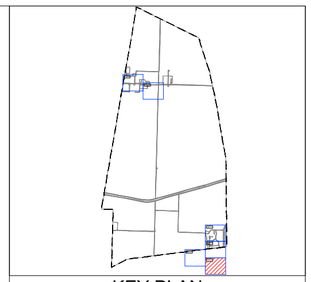

KEY PLAN

LEGEND:

- DRAIN TYPE - I
- SULLAGE CARRIER
- Ø3" HDPE PIPE
- EXISTING SOLING
- BOUNDARY

VILLAGE: ALLAHABAD (BWN)

TITLE.

DRAINAGE SYSTEM LAYOUT PLAN-06

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	21-04-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-AB-SEW-LP-06	06 OF 06	00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS
www.asiacon.com.pk

PRMSC-BWN-AB-SEW-LP-06

HYDRAULIC STATEMENT								
Node		Length	Slope	Elevation Ground	Elevation Ground	Elevation Invert	Elevation Invert	Depth
FROM	TO	ft	ft/ft	U/S	D/S	U/S	D/S	ft
1	2	305	0.002	512.29	513.01	511.46	510.85	0.83
2	3	232	0.002	513.01	512.62	510.85	510.39	2.16
3	7	262	0.002	512.62	513.45	510.39	509.86	2.23
4	5	158	0.002	512.26	514.07	511.43	511.11	0.83
5	7	24	0.002	514.07	513.45	511.11	511.06	2.96
6	7	75	0.002	513	513.45	512.17	512.01	0.83
7	8	520	0.002	513.45	511.78	509.86	508.82	3.59
8	ST Type I	136	0.002	511.78	510.87	508.82	508.55	2.96
9	11	241	0.002	518.64	519.51	517.81	517.33	0.83
10	11	55	0.002	519.35	519.51	518.51	518.41	0.83
11	14	262	0.004	519.51	516.37	516.58	515.53	2.93
12	14	196	0.023	517.66	516.37	516.83	512.39	0.83
13	14	100	0.002	513.42	516.37	512.59	512.39	0.83
14	16	145	0.002	516.37	515.42	512.39	512.1	3.98
15	16	89	0.045	516.98	515.42	516.14	512.1	0.83
16	18	172	0.004	515.42	512.3	512.1	511.46	3.32
17	18	131	0.015	514.21	512.3	513.37	511.46	0.83
18	20	413	0.002	512.3	515.26	511.46	510.64	0.83
19	20	278	0.031	519.96	515.26	519.12	510.64	0.83
20	21	330	0.002	515.26	512.23	510.64	509.95	4.62
21	ST Type III	59	0.004	512.23	510.55	509.95	509.72	2.28
22	25	475	0.002	515.36	515.72	510.55	513.57	0.83
23	25	273	0.02	518.48	515.72	517.65	512.23	0.83
24	25	225	0.004	513.96	515.72	513.13	512.23	0.83
25	27	152	0.004	515.72	512.46	512.23	511.62	3.49
26	27	411	0.021	519.87	512.46	519.04	510.38	0.83
27	29	473	0.004	512.46	509.32	510.38	508.49	2.08
28	29	145	0.044	515.72	509.32	514.88	508.49	0.83
29	31	230	0.002	509.32	511	508.49	508.03	0.83
30	31	291	0.004	510.33	511	509.5	508.34	0.83
31	32	282	0.002	511	510.22	508.03	507.46	2.97
32	ST Type I	82	0.002	510.22	509.21	507.46	507.3	2.76

VILLAGE: ALLAHABAD (BWN)

TITLE.

HYDRAULIC STATEMENT

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	21-04-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-AB-SEW-HS-00	00 OF 00	00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER CENTRAL

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS www.asianeng.com

PRMSC-BWN-AB-SEW-HS-00

AMIN ABAD

KEY PLAN

Revenue Village: Amin Abad Sheet-1

District:	Bahawalnagar
Tehsil:	Bahawalnagar
Revenue Village:	Amin Abad

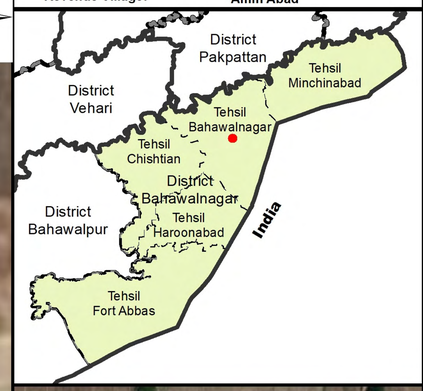

ND-9 GL=543 IL=542.17
206'
ND-10 GL=543.05 IL=541.75
75'
ND-11 GL=545.59 IL=541.61
141'
ND-12 GL=542.71 IL=541.33
ND-13 GL=543.62 IL=540.48
75'
90'
ND-14 GL=543.14 IL=540.4
ND-5 GL=543.6 IL=542.76
ND-6 GL=543.55 IL=542.5
132'
75'
ND-8 GL=543.94 IL=540.64
ND-20 GL=542.68 IL=539.78
75'
ND-19 GL=543.38 IL=538.93
229'
106'
ND-4 GL=543.1 IL=540.85
99'
ND-3 GL=541.88 IL=541.05
ND-18 GL=543.62 IL=542.76
132'
ND-16 GL=544.98 IL=543.32
ND-15 GL=545.72 IL=544.24
64'
ND-17 GL=544.09 IL=543.04
Jagarwali
ND-28 GL=546.73 IL=545.92
ND-7 GL=548.04 IL=543.78
197'
405'
ND-1 GL=543.35 IL=542.27
102'
ND-2 GL=542.7 IL=541.82
ND-21 GL=544.72 IL=543.89
434'
122'
GL=539.51 IL=537.93
SEPTIC TANK-T2 Plot Size=2 Marla
ND-25 GL=542.64 IL=539.74
192'
ND-24 GL=542.4 IL=540.79
147'
ND-22 GL=541.92 IL=541.08
148'
316'
2 RMF/FF ULTIMATE DISPOSAL TO WATER COURSE

N

Title:
Proposed Drainage Network Plan

Legend:

- SETTLEMENT
- NODE
- 3"HDPE PIPE
- DRAIN TYPE-1
- SULLAGE CARRIER
- SEPTIC TANK
- SETTLEMENT BOUNDARY

Drain Type 1=2336 Rft
Sullage Carrier= 1518 Rft

Scale: 1:1,000
1 inch = 83 feet
Paper Size: A3

0 40 80 160
Kilometers

Project:
Engineering Design & Construction Supervision, Punjab Rural Sustainable Water Supply & Sanitation Project, Cluster South III

PRMSC
ENVIRONMENTAL TECHNOLOGIES
ASIAN CONSULTING ENGINEERS www.asiancon.com

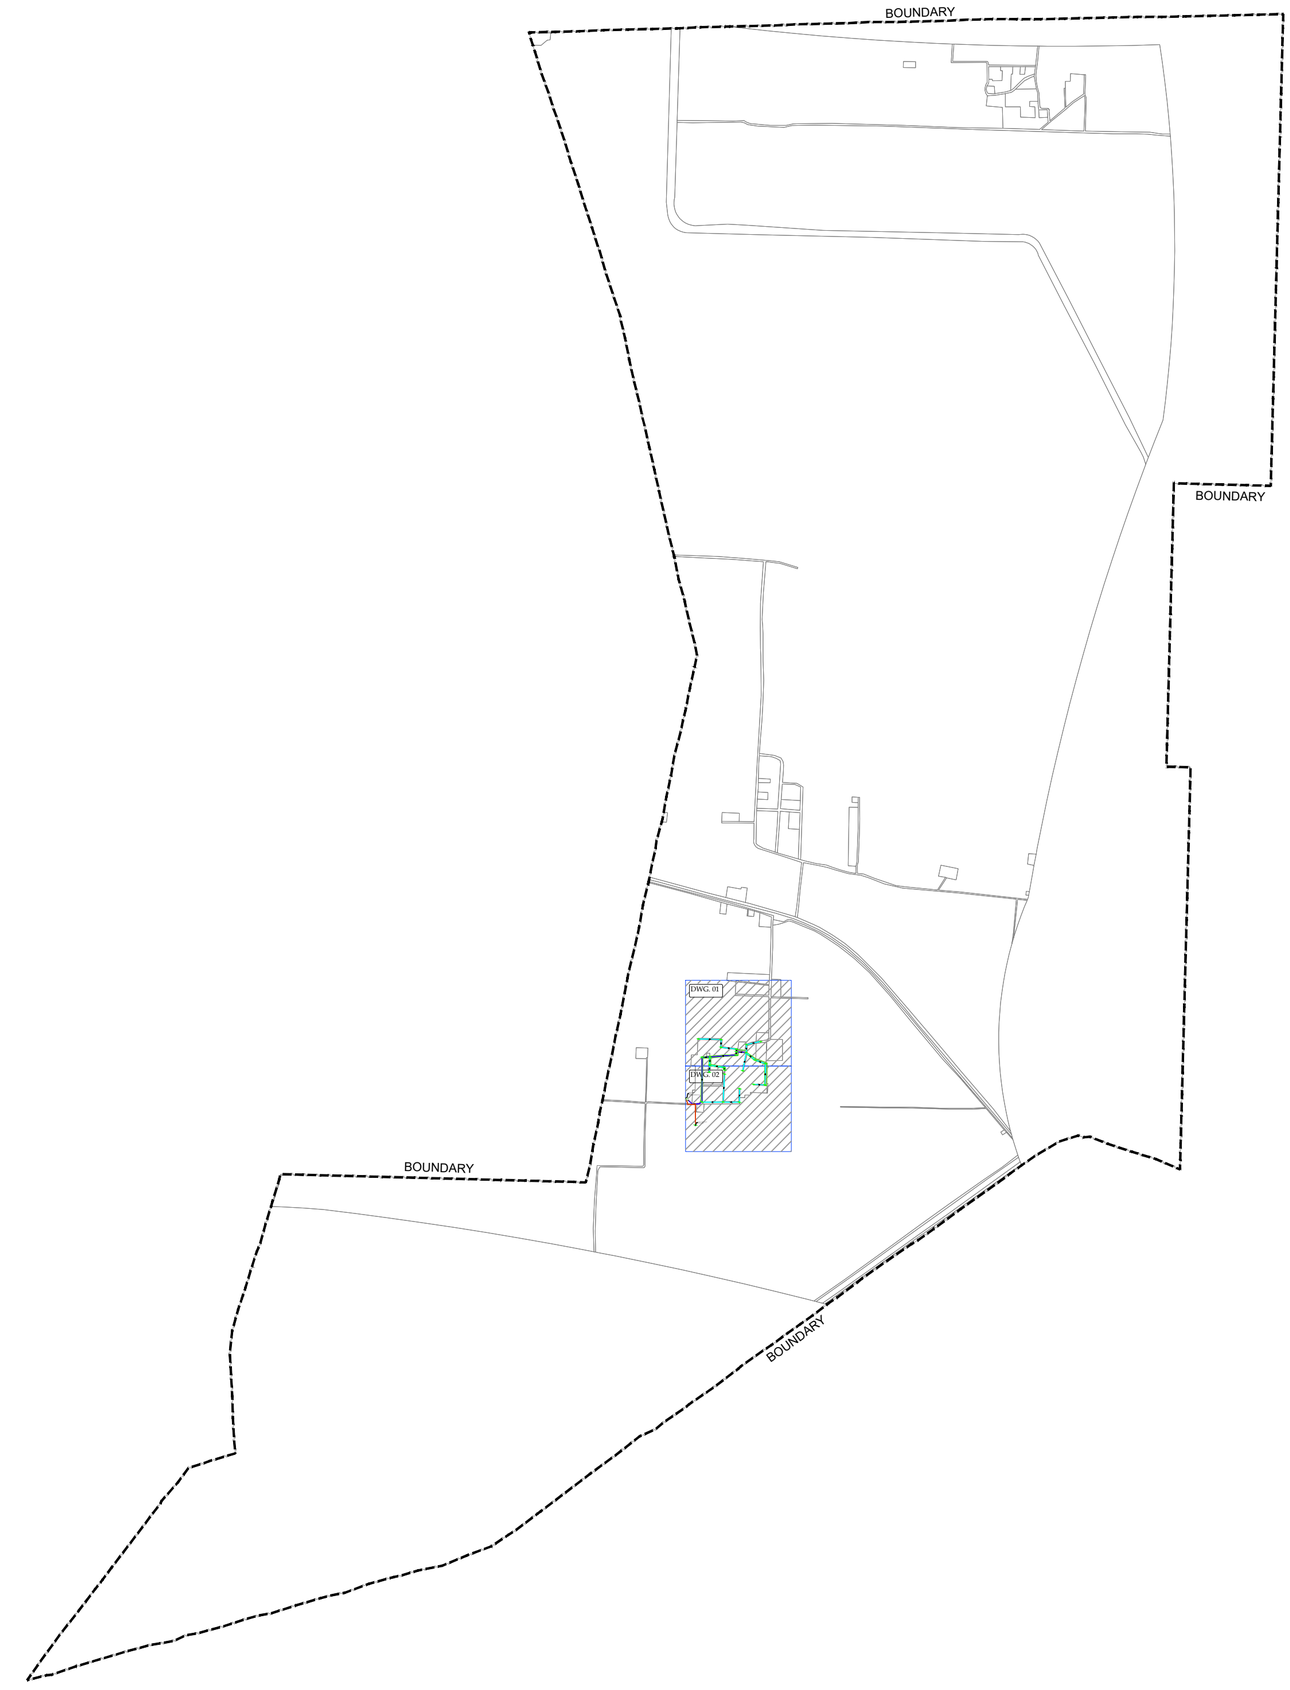

LEGEND:

- DRAIN TYPE - I
- SULLAGE CARRIER
- Ø3" HDPE PIPE
- EXISTING SOLING
- BOUNDARY

VILLAGE: AMIN ABAD(BWN)

TITLE.

DRAINAGE SYSTEM KEY PLAN

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 1000'

ISSUE N°	DATE	D E S C R I P T I O N	DRAWN	DESIGNED	APPROVED
01	21-04-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. HSAN-UL HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-AA-SEW-KP-00	00 OF 00	01

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT
ASIAN CONSULTING ENGINEERS
www.asiancen.com

PRMSC-BWN-AA-SEW-KP-00

LAYOUT PLAN

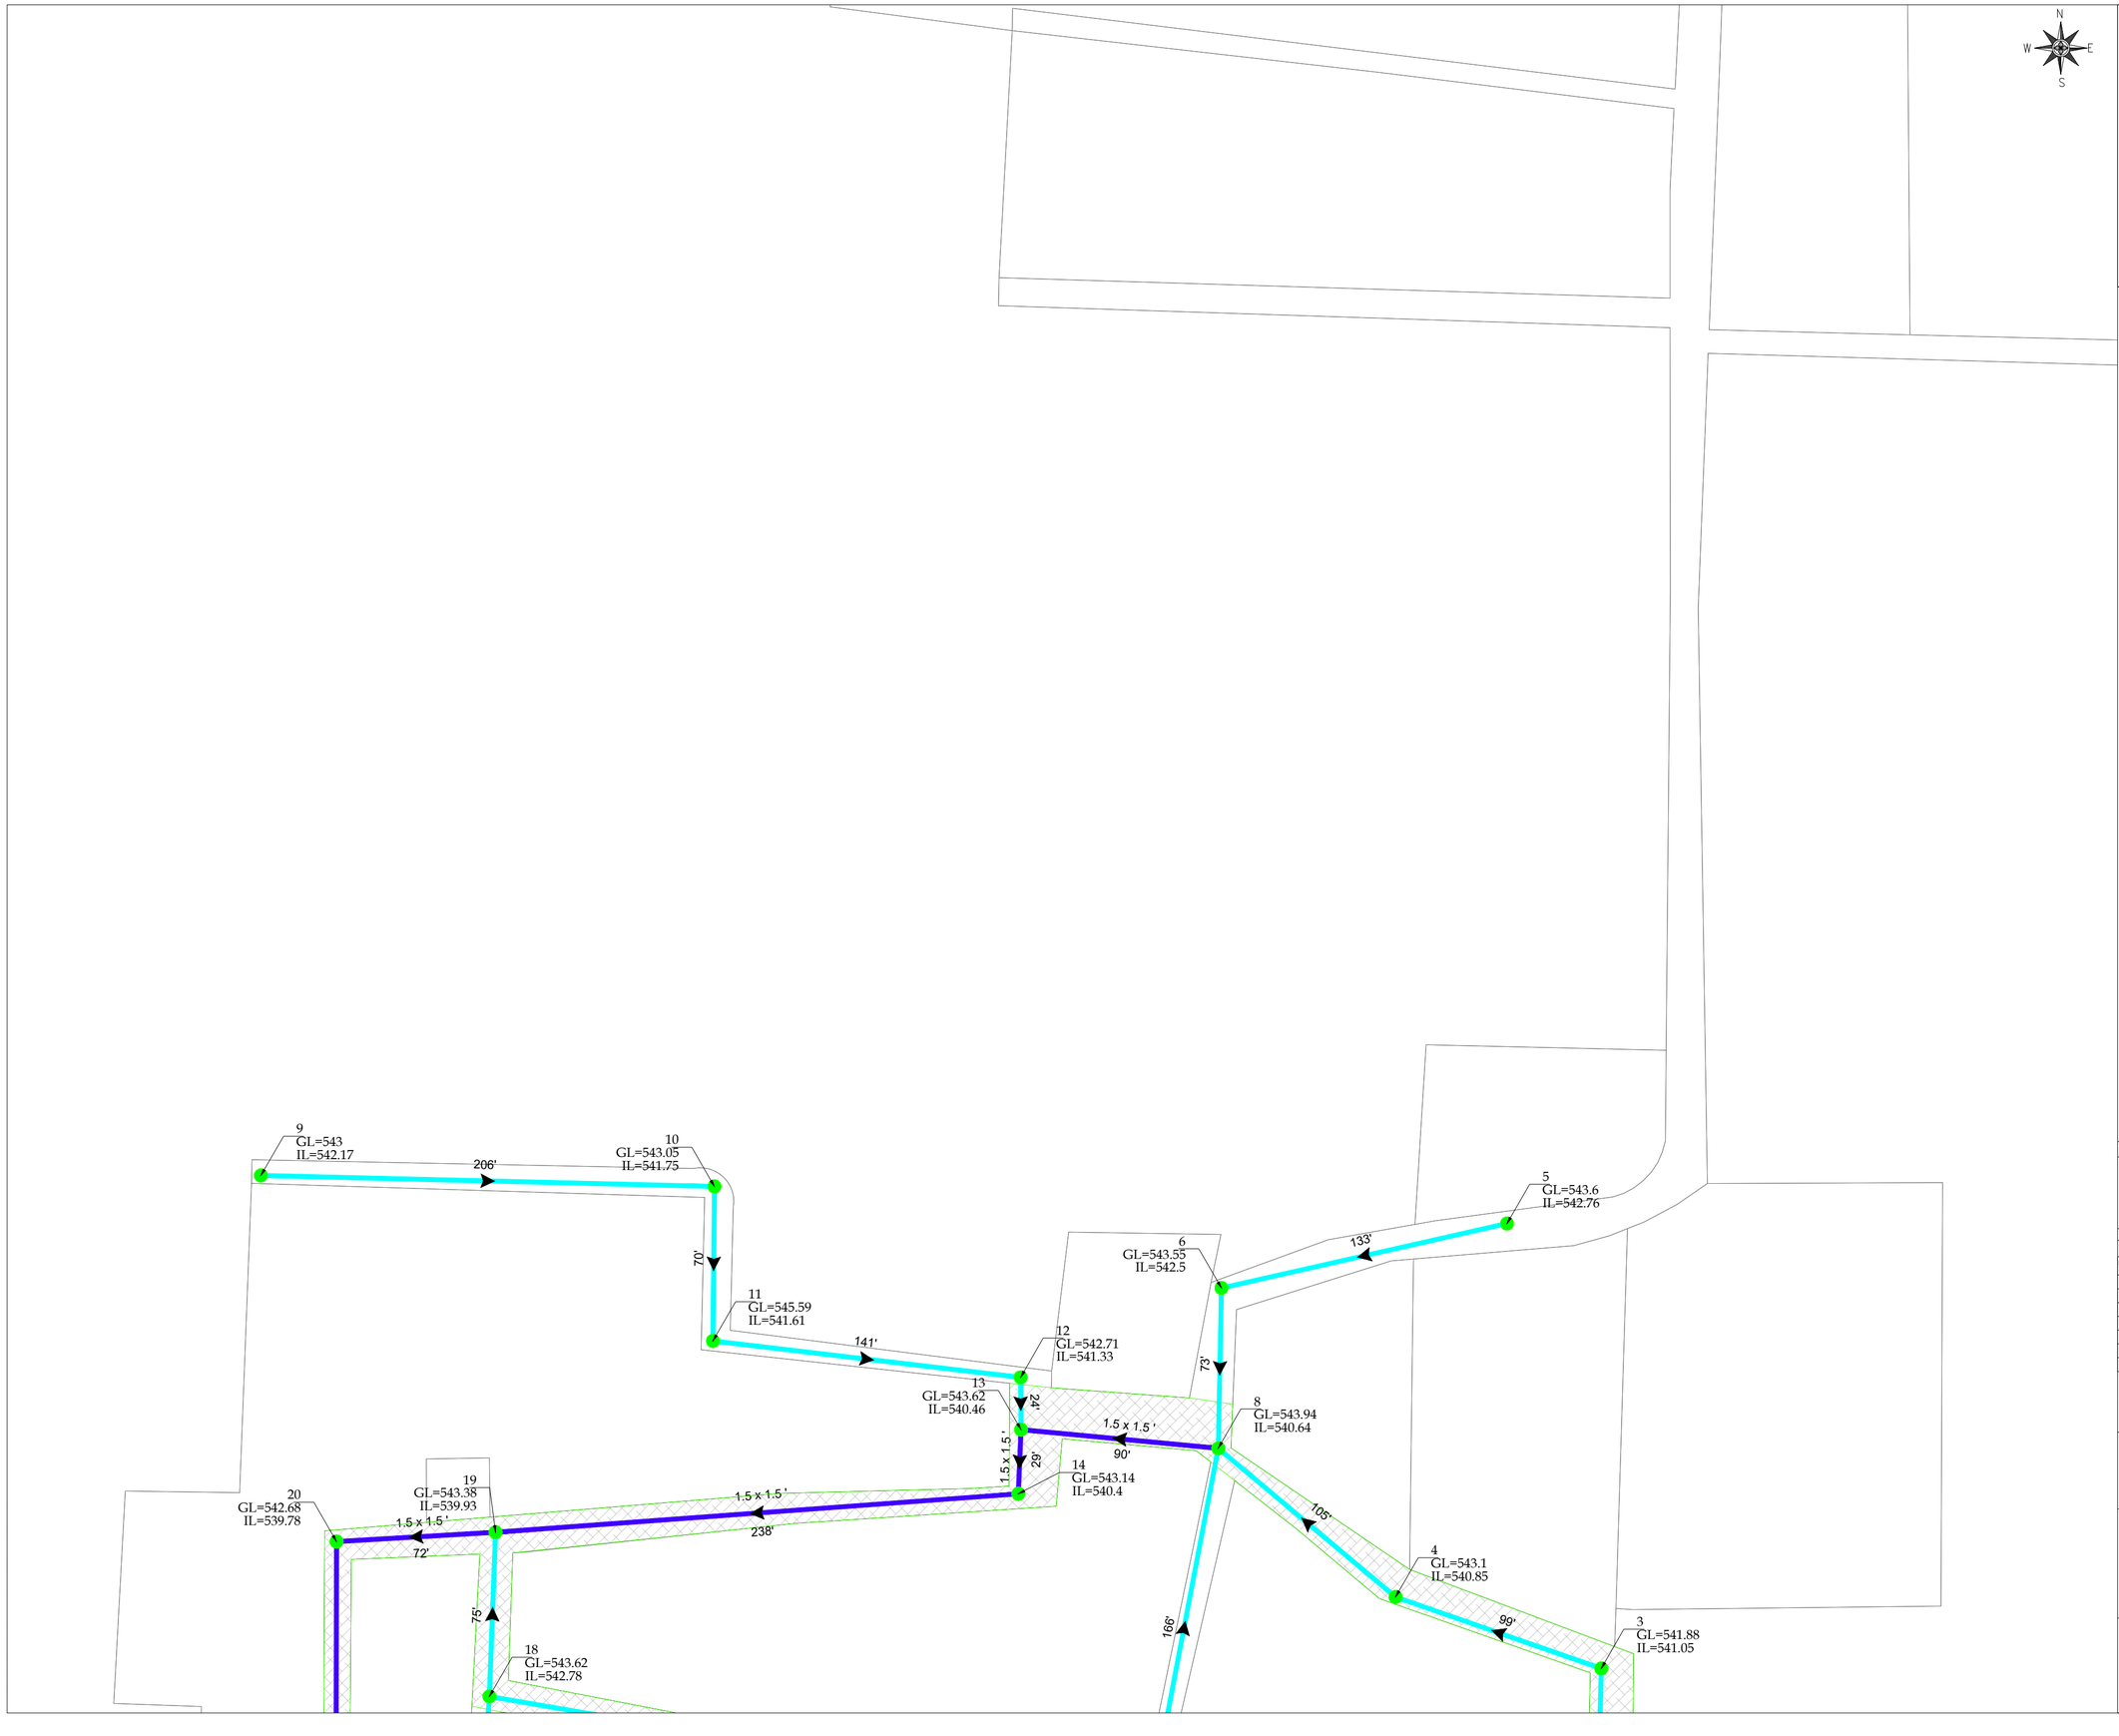

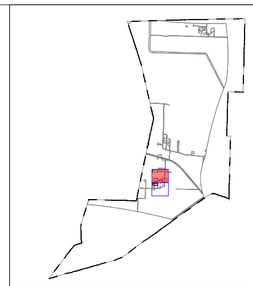

KEY PLAN

LEGEND:

- DRAIN TYPE - I
- SULLAGE CARRIER
- Ø3" HDPE PIPE
- EXISTING SOLING
- BOUNDARY

VILLAGE: AMIN ABAD (BHW)

TITLE.

DRAINAGE SYSTEM LAYOUT PLAN-01

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	21-04-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. HSAN-UL HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-AA-SEW-LP-01	01 OF 02	01

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT
ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

PRMSC-BWN-AA-SEW-LP-01

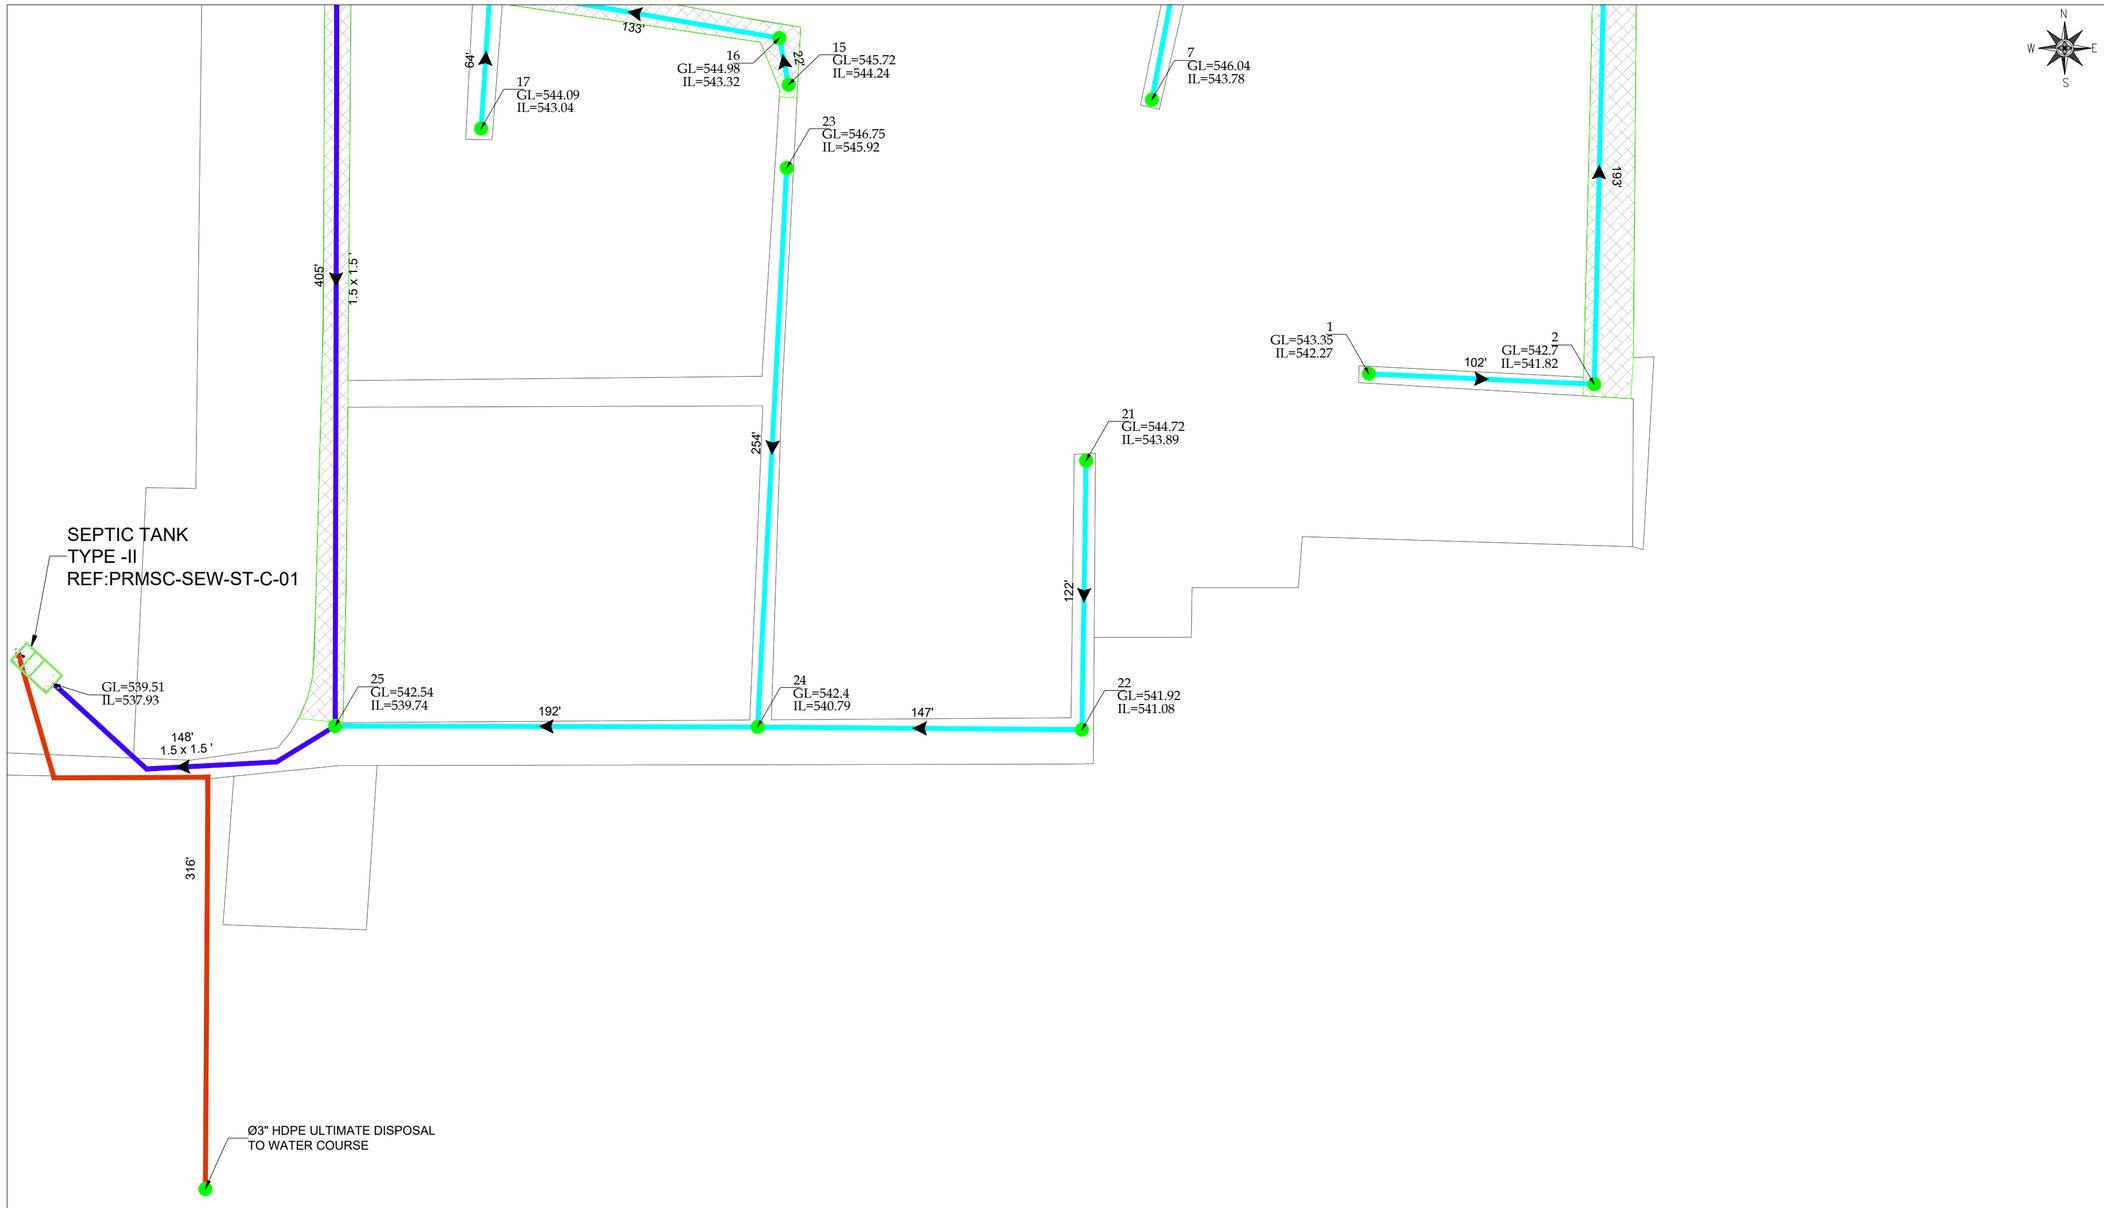



KEY PLAN

LEGEND:

- DRAIN TYPE - I
- SULLAGE CARRIER
- Ø3" HDPE PIPE
- EXISTING SOLING
- BOUNDARY

VILLAGE: AMIN ABAD (BHW)

TITLE.

DRAINAGE SYSTEM LAYOUT PLAN-02

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	21-04-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-AA-SEW-LP-02	02 OF 02	01

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT

ENVIRONMENTAL ENGINEERS (PVT) LTD.
ASIAN CONSULTING ENGINEERS (PVT) LTD. www.asiancon.com

PRMSC-BWN-AA-SEW-LP-02

HYDRAULIC STATEMENT								
Node		Length	Slope	Elevation Ground	Elevation Ground	Elevation Invert	Elevation Invert	Depth
FROM	TO	ft	ft/ft	U/S	D/S	U/S	D/S	ft
1	2	102	0.004	543.35	542.7	542.27	541.86	1.08
2	3	193	0.004	542.7	541.88	541.82	541.05	0.87
3	4	99	0.002	541.88	543.1	541.05	540.85	0.83
4	8	105	0.002	543.1	543.94	540.85	540.64	2.25
5	6	133	0.002	543.6	543.55	542.76	542.5	0.83
6	8	73	0.002	543.55	543.94	542.5	542.35	1.05
7	8	166	0.004	546.04	543.94	543.78	543.11	2.26
8	13	90	0.002	543.94	543.62	540.64	540.46	3.3
9	10	206	0.002	543	543.05	542.17	541.75	0.83
10	11	70	0.002	543.05	545.59	541.75	541.61	1.3
11	12	141	0.002	545.59	542.71	541.61	541.33	3.97
12	13	24	0.002	542.71	543.62	541.33	541.28	1.38
13	14	29	0.002	543.62	543.14	540.46	540.4	3.16
14	19	238	0.002	543.14	543.38	540.4	539.93	2.73
15	16	22	0.004	545.72	544.98	544.24	544.15	1.49
16	18	133	0.004	544.98	543.62	543.32	542.78	1.67
17	18	64	0.004	544.09	543.62	543.04	542.78	1.05
18	19	75	0.003	543.62	543.38	542.78	542.55	0.83
19	20	72	0.002	543.38	542.68	539.93	539.78	3.45
20	25	405	0	542.68	542.54	539.78	539.74	2.9
21	22	122	0.023	544.72	541.92	543.89	541.08	0.83
22	24	147	0.002	541.92	542.4	541.08	540.79	0.83
23	24	254	0.02	546.75	542.4	545.92	540.79	0.83
24	25	192	0.005	542.4	542.54	540.79	539.74	1.61
25	ST-TYPE-II	148	0.012	542.54	539.51	539.74	537.93	2.8

VILLAGE: AMIN ABAD (BWN)

TITLE.

HYDRAULIC STATEMENT

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	21-04-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. HASEEB
02					
03					
04					
05					
06					
07					

DRAWING Nº: PRMSC-BWN-AA-SEW-HS-00

SHEET 00 OF 00

REV 00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT
ENVIRONMENTAL TECHNOLOGIES
ASIAN CONSULTING ENGINEERS
www.asiancon.com

PRMSC-BWN-AA-SEW-HS-00

BARASAJWAR KHAN

KEY PLAN

N
W
E
S

LEGEND:

- DRAIN TYPE - I
- SULLAGE CARRIER
- Ø3" HDPE PIPE
- METALLED ROAD
- BOUNDARY

VILLAGE: BARA SAJWAR KHAN (BWN)

TITLE.

DRAINAGE SYSTEM KEY PLAN

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 700'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	02-01-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02	21-04-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-BSK-SEW-KP-00	00 OF 00	01

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT
ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

PRMSC-BWN-BSK-SEW-KP-00

LAYOUT PLAN

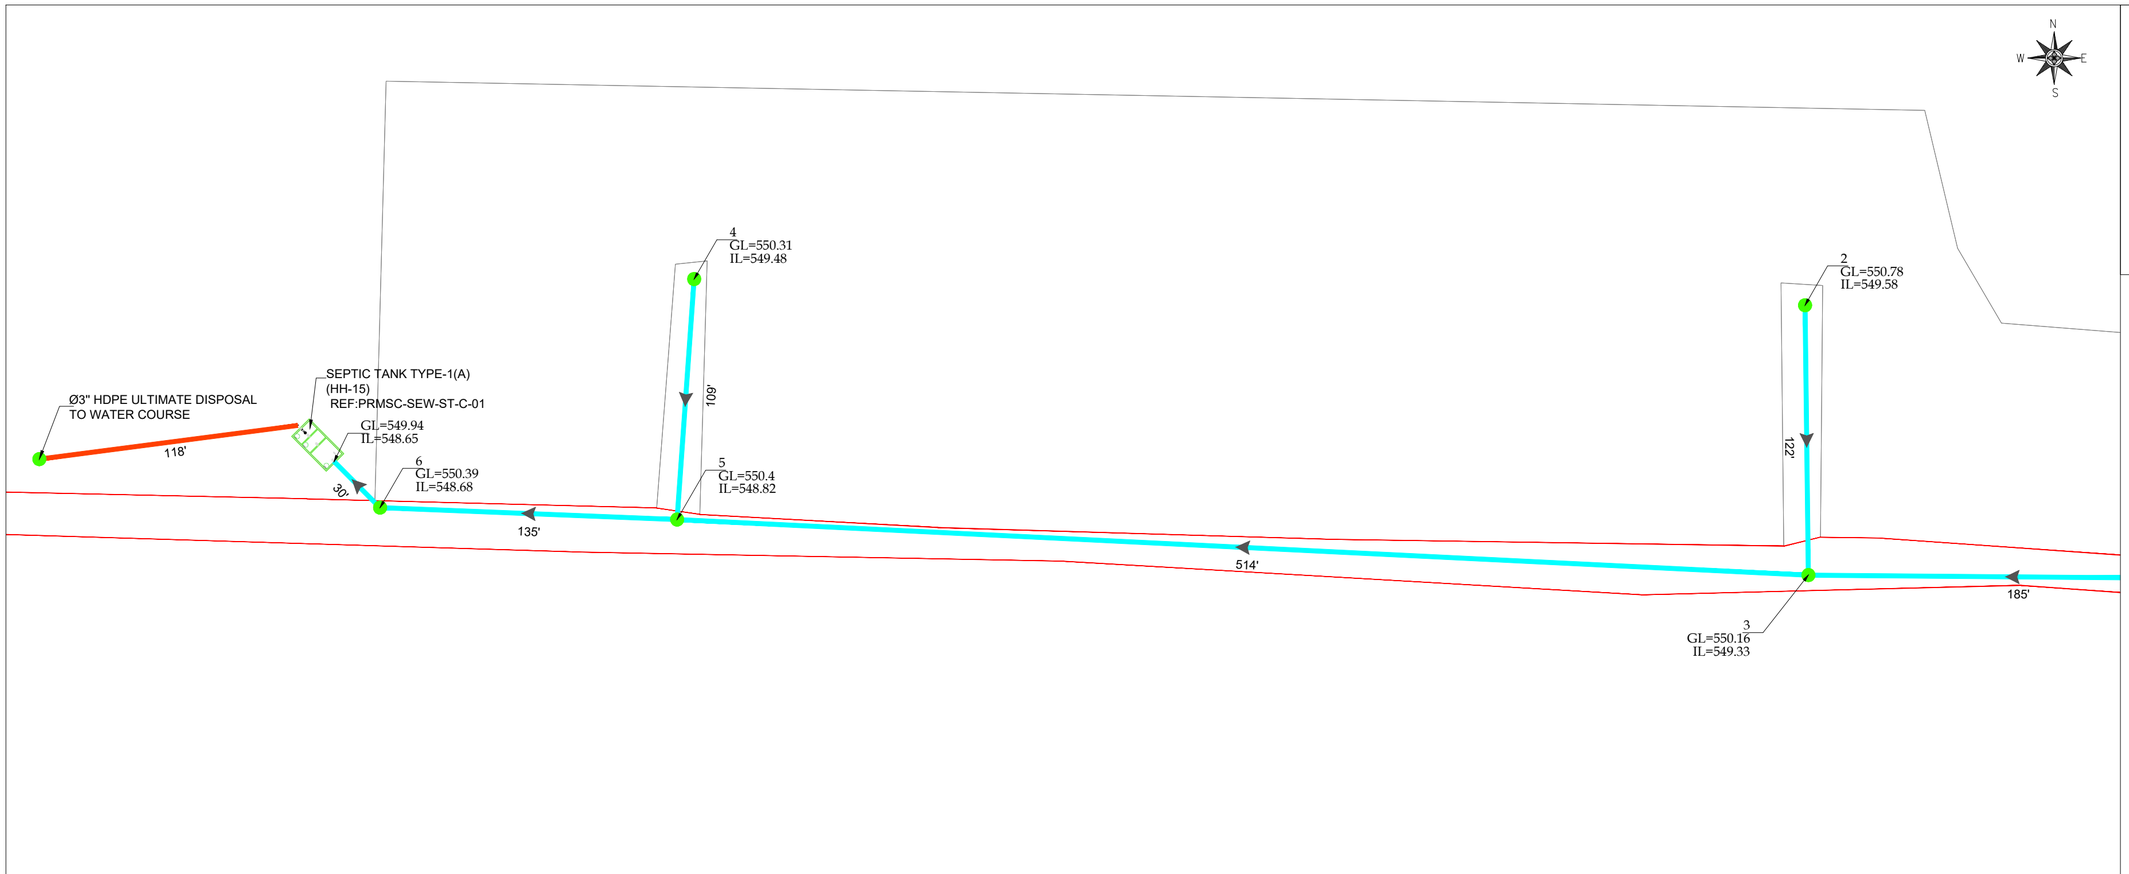

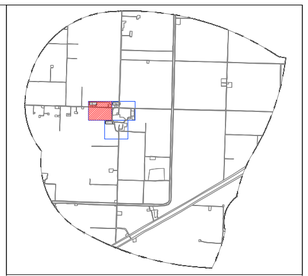

KEY PLAN

LEGEND:

- DRAIN TYPE - I
- SULLAGE CARRIER
- Ø3" HDPE PIPE
- METALLED ROAD
- BOUNDARY

VILLAGE: BARA SAJWAR KHAN (BWN)

TITLE.

DRAINAGE SYSTEM LAYOUT PLAN-01

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	02-01-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02	21-04-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-BSK-SEW-LP-01	01 OF 03	01

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS
www.asiacon.com.pk

PRMSC-BWN-BSK-SEW-LP-01

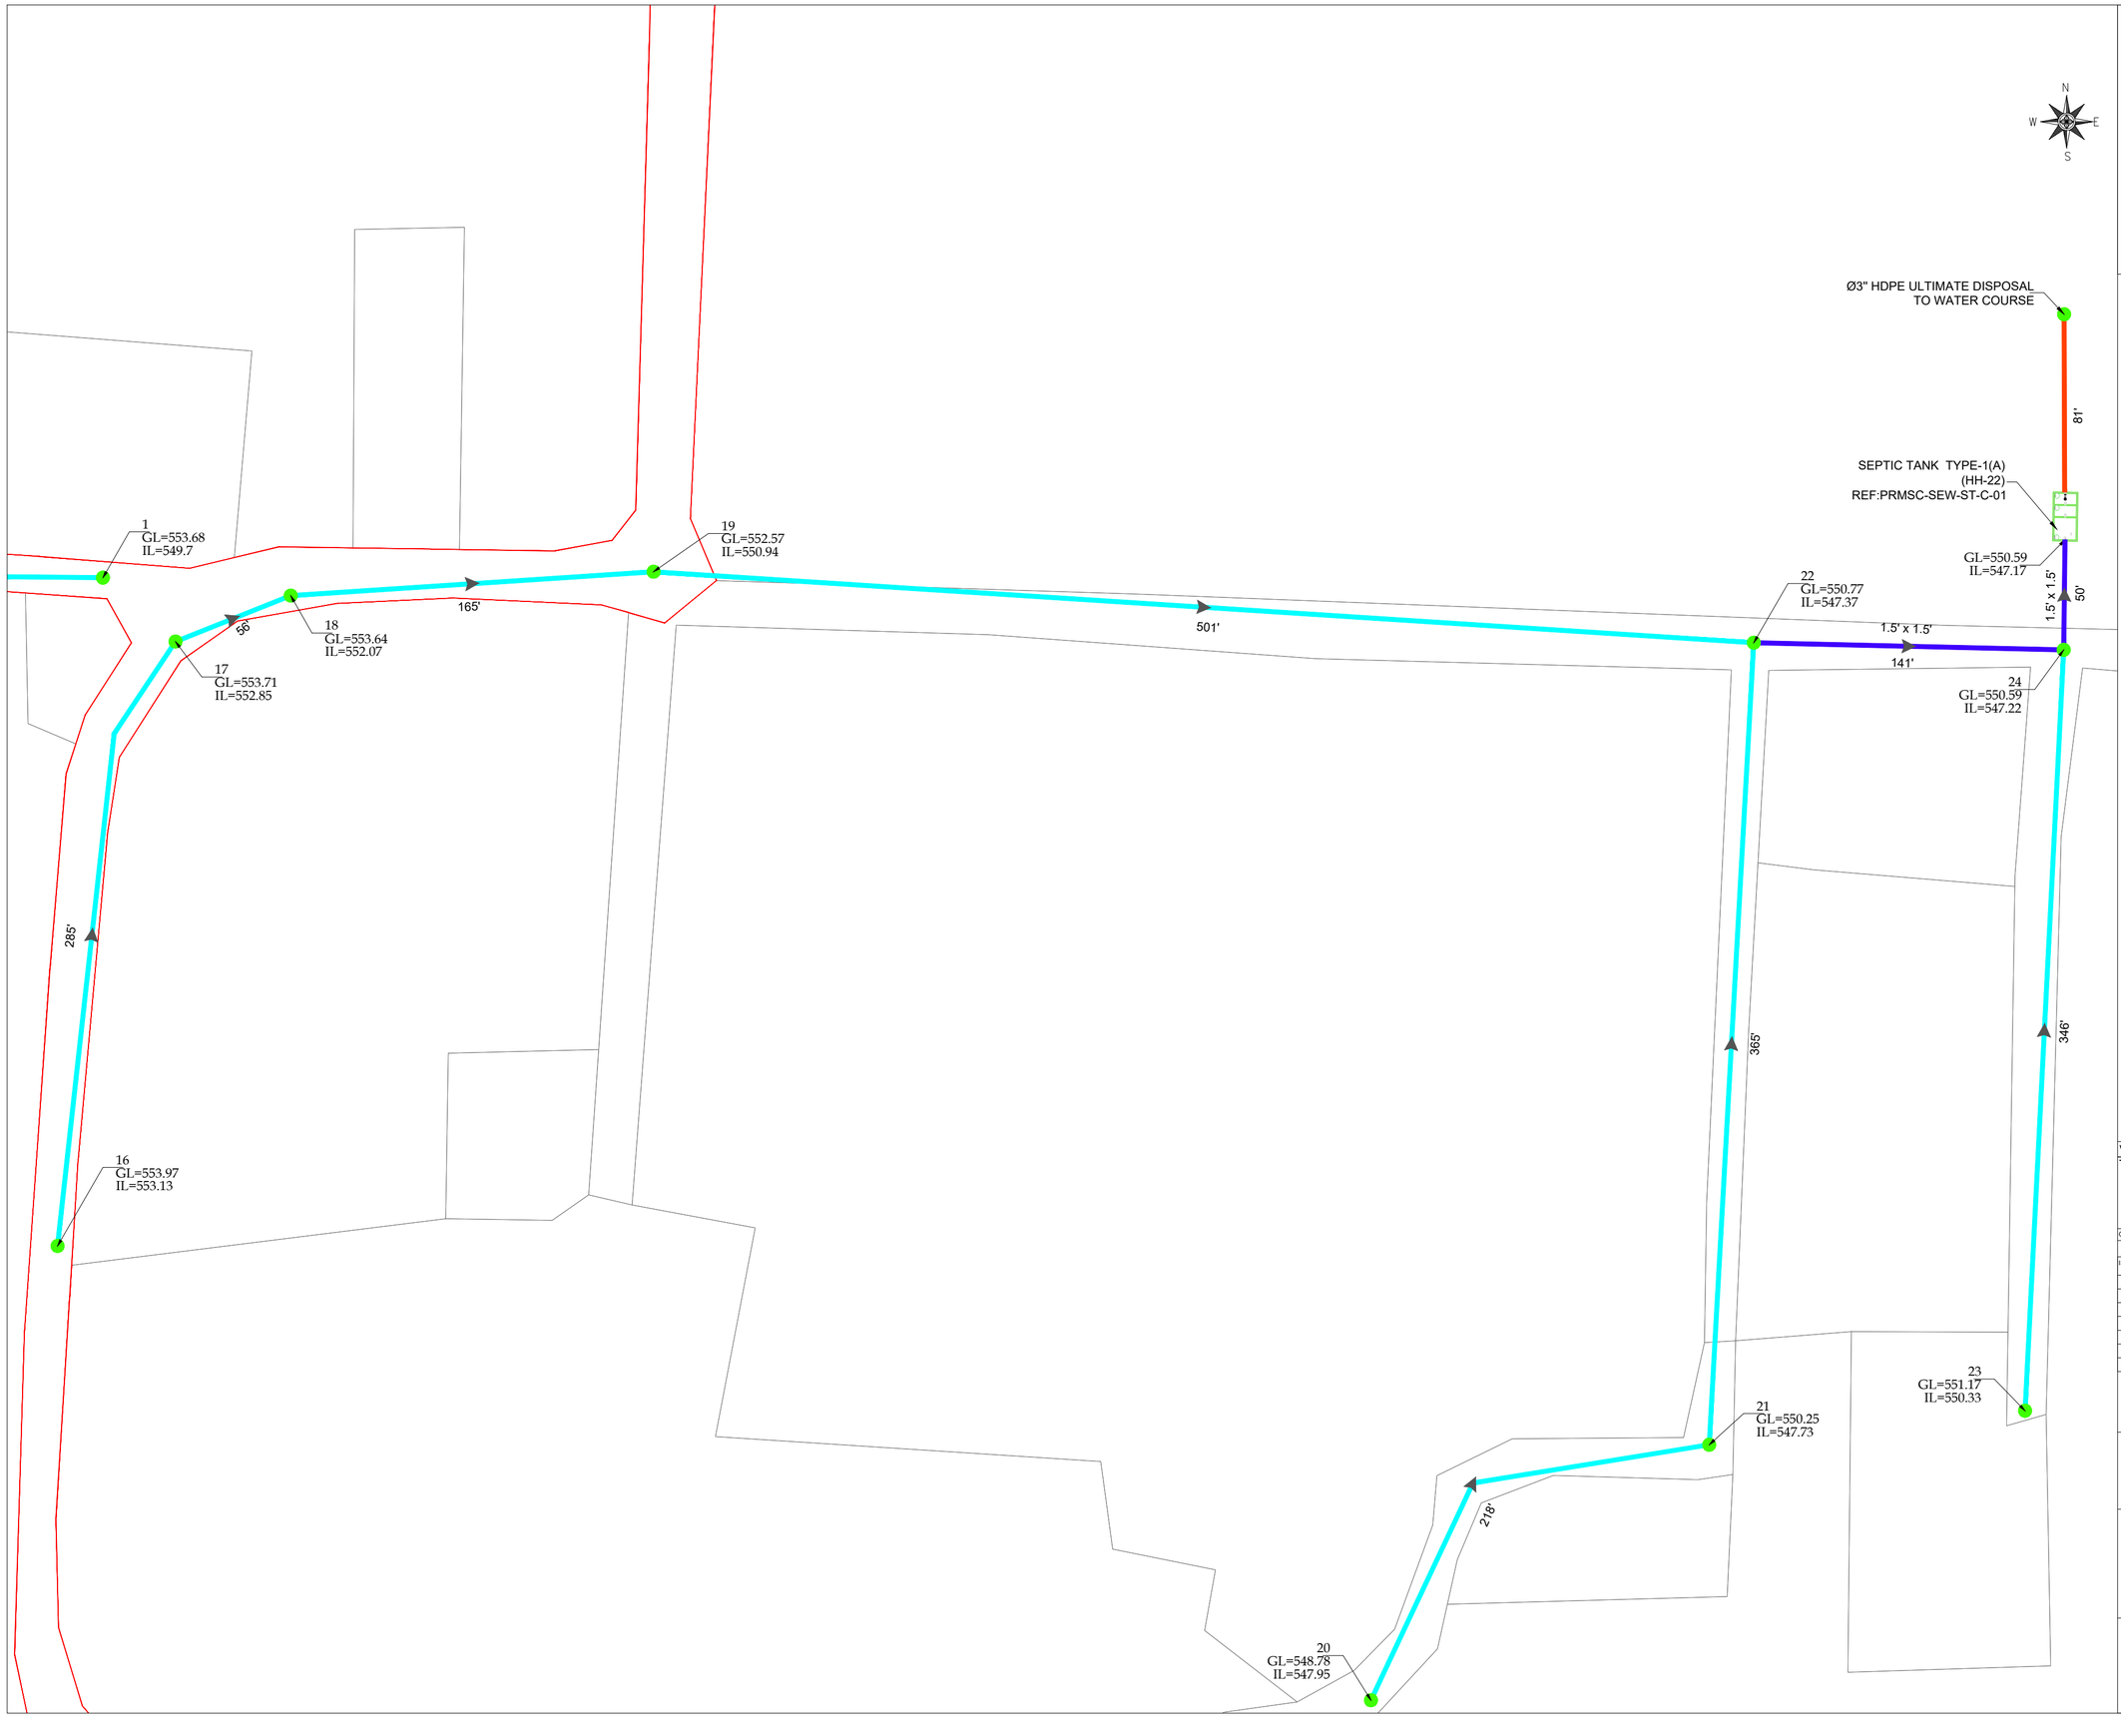

PRMSC-BWN-BSK-SEW-LP-02

KEY PLAN

LEGEND:

- DRAIN TYPE - I
- SULLAGE CARRIER
- Ø3" HDPE PIPE
- METALLED ROAD
- BOUNDARY

VILLAGE: BARA SAJWAR KHAN (BWN)

TITLE.

DRAINAGE SYSTEM LAYOUT PLAN-02

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	02-01-2026	DETAILED DESIGN	MUNEEB	ENGR FAIEZ	ENGR IHSAN-UL-HAQ
02	21-04-2026	DETAILED DESIGN	MUNEEB	ENGR FAIEZ	ENGR IHSAN-UL-HAQ
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-BSK-SEW-LP-02	02 OF 03	01

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

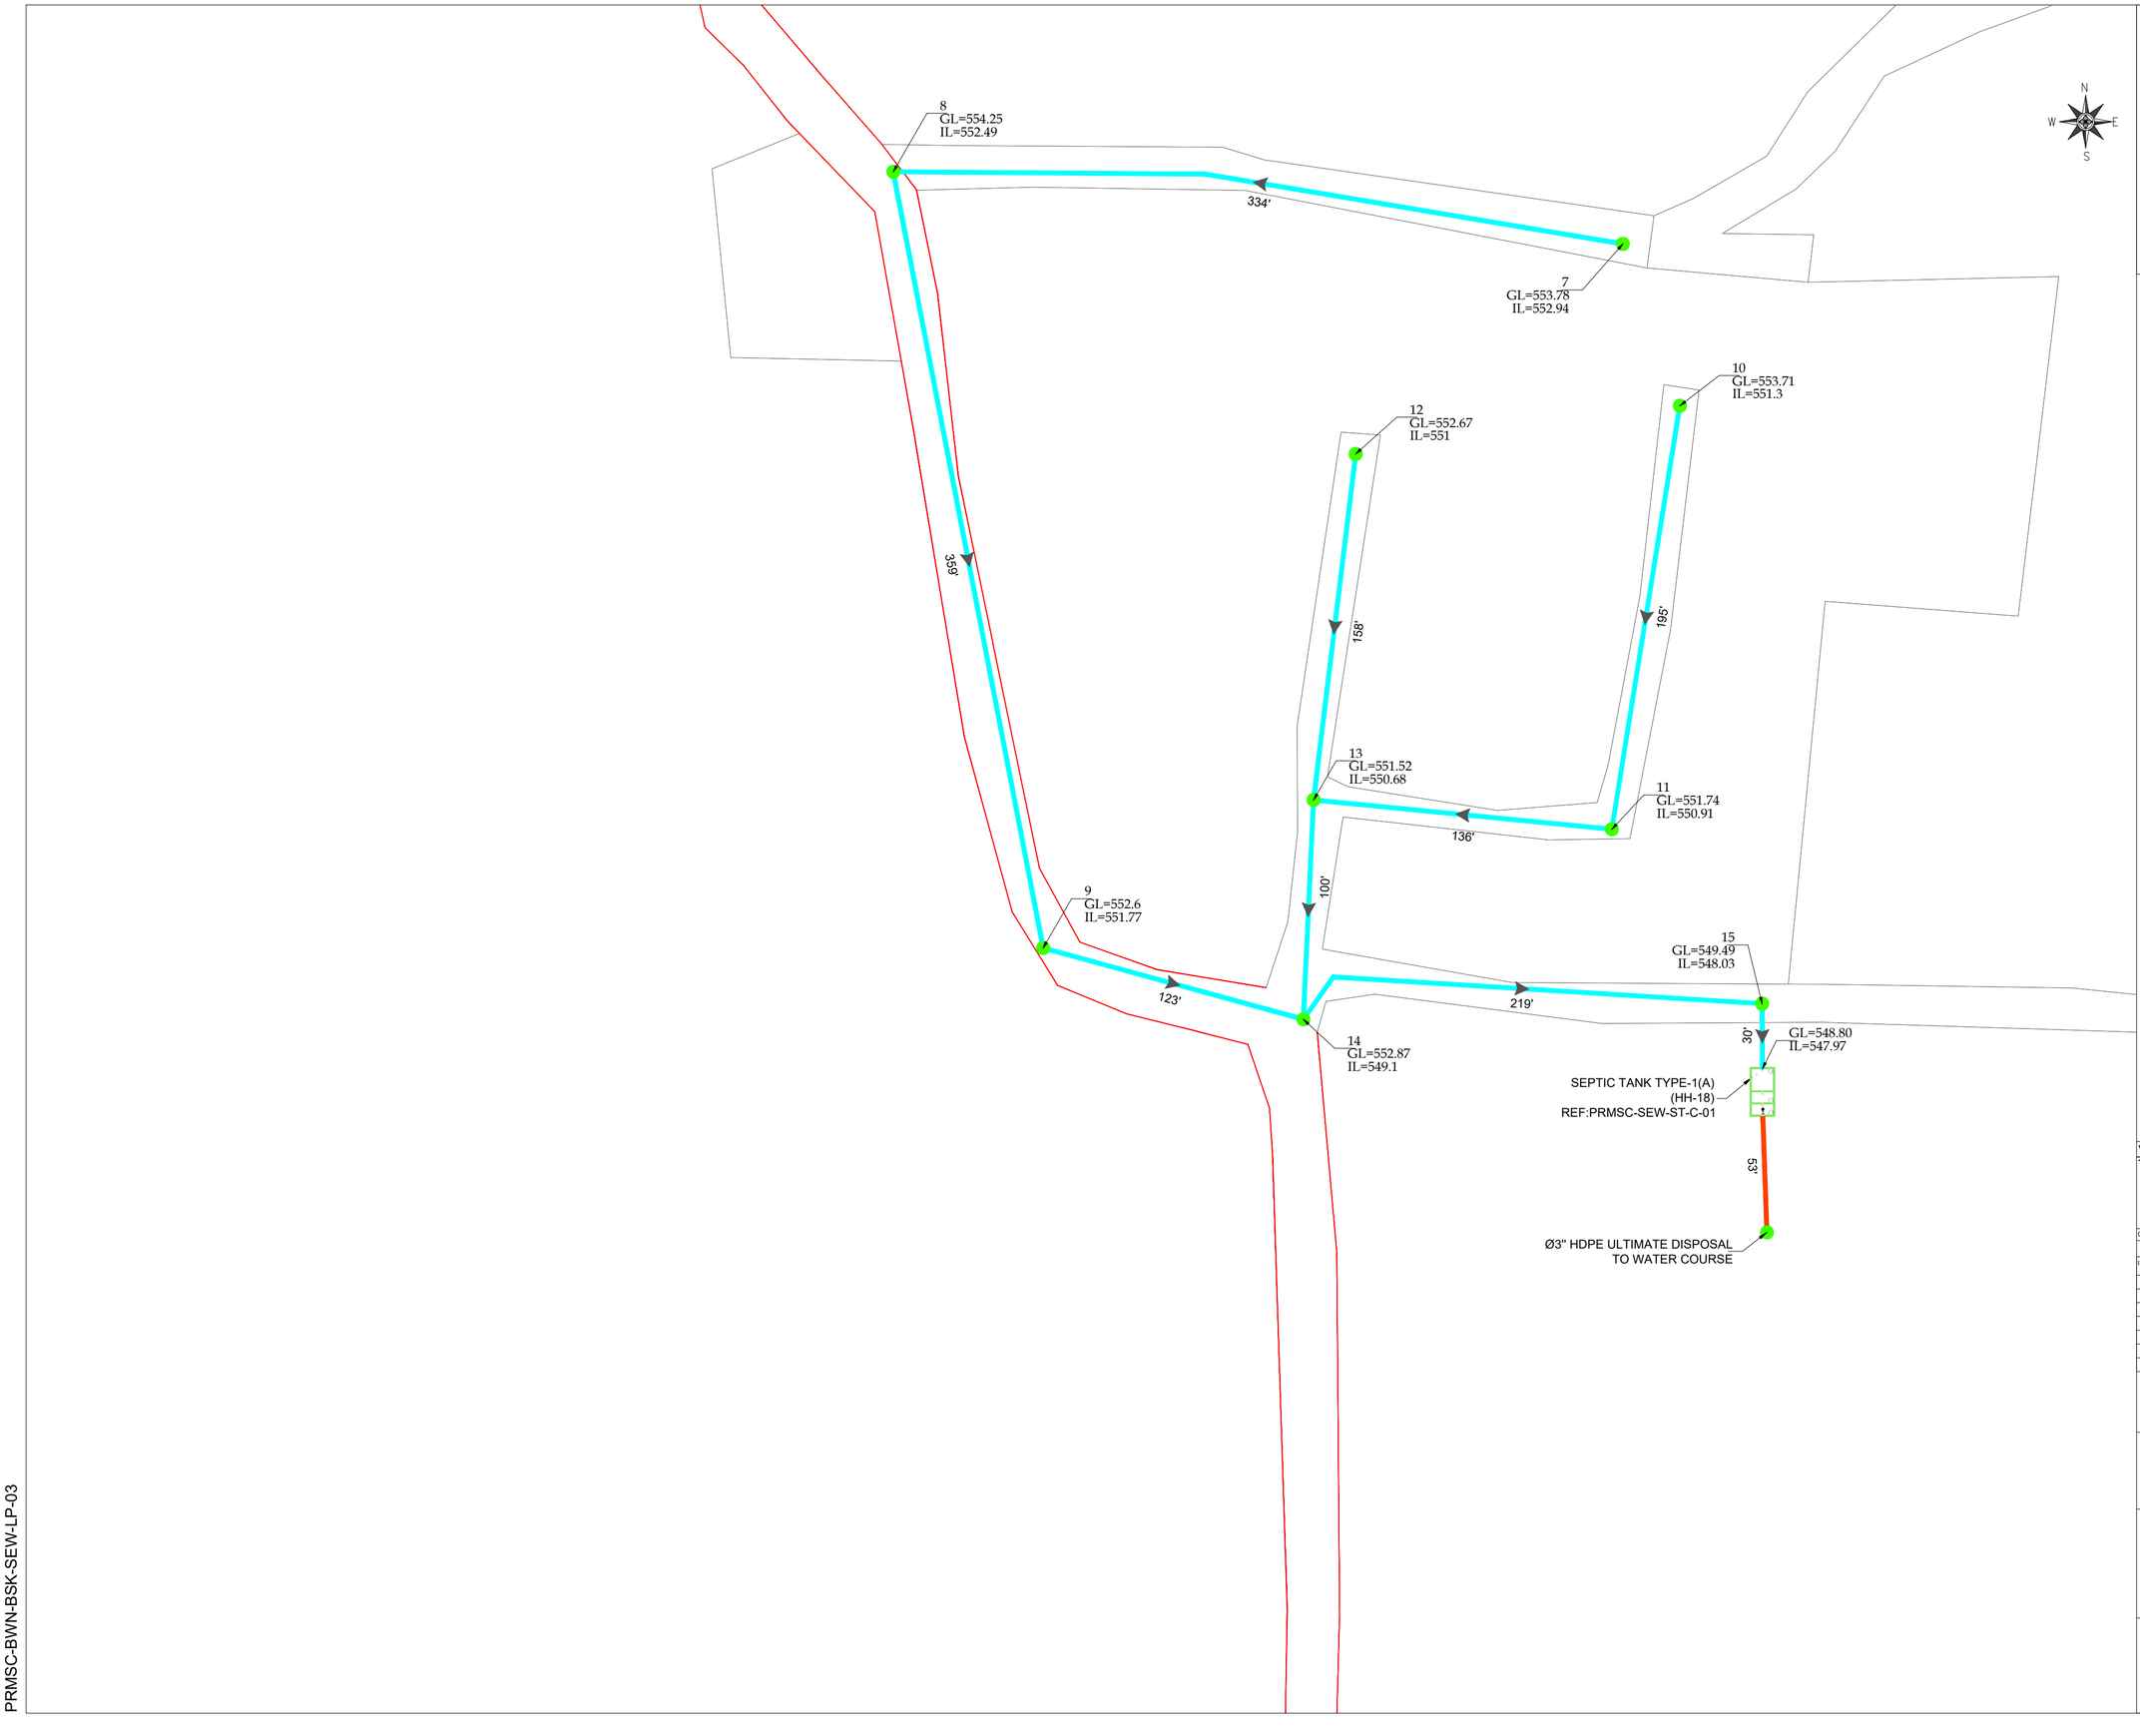

KEY PLAN

LEGEND:

- DRAIN TYPE - I
- SULLAGE CARRIER
- Ø3" HDPE PIPE
- METALLED ROAD
- BOUNDARY

VILLAGE: BARA SAJWAR KHAN (BWN)

TITLE.

DRAINAGE SYSTEM LAYOUT PLAN-03

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	02-01-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. HSAN-UL-HAQ
02	21-04-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. HSAN-UL-HAQ
03					
04					
05					
06					
07					

DRAWING N°:	SHEET	REV
PRMSC-BWN-BSK-SEW-LP-03	03 OF 03	01

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

PRMSC-BWN-BSK-SEW-LP-03

HYDRAULIC STATEMENT

Node		Length	Slope	Elevation Ground	Elevation Ground	Elevation Invert	Elevation Invert	Depth
FROM	TO	ft	ft/ft	U/S	D/S	U/S	D/S	ft
1	3	185	0.002	553.68	550.16	549.7	549.33	3.98
2	3	122	0.002	550.78	550.16	549.58	549.33	1.2
3	5	514	0.001	550.16	550.4	549.33	548.82	0.83
4	5	109	0.001	550.31	550.4	549.48	549.37	0.83
5	6	135	0.001	550.4	550.39	548.82	548.68	1.58
6	Septic Tank (HH-15)	30	0.001	550.39	549.94	548.68	548.65	1.71
7	8	334	0.00135	553.78	554.25	552.94	552.49	0.84
8	9	359	0.002	554.25	552.6	552.49	551.77	1.76
9	14	123	0.001	552.6	552.87	551.77	551.65	0.83
10	11	195	0.002	553.71	551.74	551.3	550.91	2.41
11	13	136	0.00167	551.74	551.52	550.91	550.68	0.83
12	13	158	0.002	552.67	551.52	551	550.68	1.67
13	14	100	0.001	551.52	552.87	550.68	550.58	0.84
14	15	219	0.002	552.87	549.49	549.1	548.66	3.77
15	Septic Tank (HH-18)	30	0.002	549.49	548.8	548.03	547.97	1.46
16	17	285	0.001	553.97	553.71	553.13	552.85	0.84
17	18	56	0.001	553.71	553.64	552.85	552.79	0.86
18	19	165	0.002	553.64	552.57	552.07	551.74	1.57
19	22	501	0.002	552.57	550.77	550.94	549.93	1.63
20	21	218	0.001	548.78	550.25	547.95	547.73	0.83
21	22	365	0.001	550.25	550.77	547.73	547.37	2.52
22	24	141	0.001	550.77	550.59	547.37	547.22	3.4
23	24	346	0.00166	551.17	550.59	550.33	549.76	0.84
24	Septic Tank (HH-22)	50	0.001	550.59	550.59	547.22	547.17	3.37

VILLAGE: BARA SAJWAR KHAN (BWN)

TITLE.

HYDRAULIC STATEMENT

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	02-01-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. HSAN-UL-HAQ
02	21-04-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. HSAN-UL-HAQ
03					
04					
05					
06					
07					

DRAWING Nº: PRMSC-BWN-BSK-SEW-HS-01

SHEET 01 OF 01

REV 01

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT
ASIAN CONSULTING ENGINEERS
www.asiancon.com

PRMSC-BWN-BSK-SEW-HS-01

CHAK ABDUL HAQ

KEY PLAN

Revenue Village: Chak Abdul Haq Main Sheet

District:	Bahawalnagar
Tehsil:	Bahawalnagar
Revenue Village:	Chak Abdul Haq

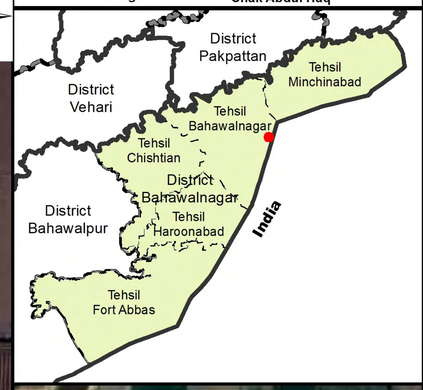

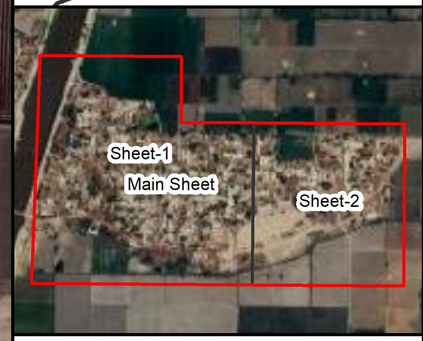

Title:
Proposed Drainage Network Plan

Legend:

- SETTLEMENT
- NODE
- 3" HDPE PIPE
- DRAIN TYPE-1
- SULLAGE CARRIER
- SEPTIC TANK
- SETTLEMENT BOUNDARY

Drain Type 1=7701 Rft

Sullage Carrier= 3244 Rft

Scale: 1:2,300

1 inch = 192 feet

Paper Size: A3

0 40 80 160

Kilometers

Project:
Engineering Design & Construction Supervision, Punjab Rural Sustainable Water Supply & Sanitation Project, Cluster South III

PRWSC

ENVIRONMENTAL TECHNOLOGIES

ASIAN CONSULTING ENGINEERS www.asiancon.com

LEGEND:

- DRAIN TYPE - I
- SULLAGE CARRIER
- Ø3" HDPE PIPE
- BOUNDARY

VILLAGE: CHAK ABDUL HAQ (BWN)

TITLE.

DRAINAGE SYSTEM KEY PLAN

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 750'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	20-04-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-CAH-SEW-KP-00	00 OF 00	00

PROJECT:

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:

PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT

ASIAN CONSULTING ENGINEERS
www.asiancon.com

PRMSC-BWN-CAH-SEW-KP-00

LAYOUT PLAN

Revenue Village: Chak Abdul Haq Sheet-1

District:	Bahawalnagar
Tehsil:	Bahawalnagar
Revenue Village:	Chak Abdul Haq

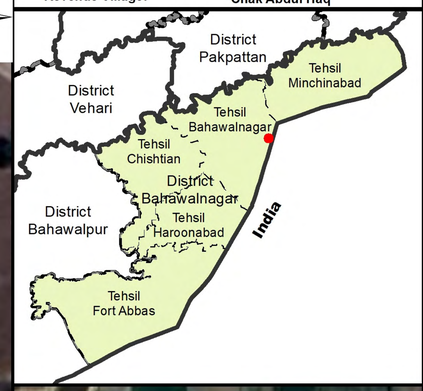

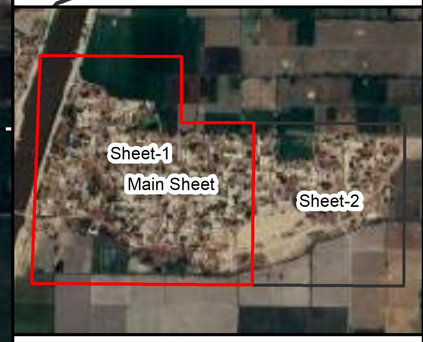

GL=577.32
IL=574.53
FOR FINAL ULTIMATE DISPOSAL TO WATER COURSE
414'
ND-29
GL=577.23
IL=574.61
SEPTIC TANK-T1
Plot Size=1.59 Marla
ND-27
GL=578.47
IL=576.62
ND-28
GL=579.93
IL=576.83
ND-09
GL=578.55
IL=574.65
ND-25
GL=577.93
IL=576.69
ND-26
GL=578.1
IL=574.67
ND-24
GL=578.93
IL=574.83
ND-23
GL=577.05
IL=574.18
ND-19
GL=578.84
IL=576.59
ND-17
GL=577.79
IL=574.49
ND-21
GL=578.89
IL=578.04
ND-36
GL=584.91
IL=582.66
ND-22
GL=580.73
IL=578.84
ND-35
GL=592.03
IL=589.78
ND-34
GL=592.08
IL=589.83
ND-9
GL=600.66
IL=597.81
ND-31
GL=600.71
IL=598.46
ND-33
GL=592.2
IL=589.75
Ghaitanwali
ND-20
GL=576.75
IL=573.28
GL=577.73
IL=573.18
SEPTIC TANK-T2
Plot Size=2 Marla
FOR FINAL ULTIMATE DISPOSAL TO WATER COURSE
ND-18
GL=576.56
IL=573.85
ND-14
GL=587.73
IL=585.48
ND-12
GL=587.5
IL=585.25
ND-10
GL=588.42
IL=587.17
ND-16
GL=576.85
IL=574.16
ND-15
GL=577.93
IL=574.91
ND-13
GL=578.58
IL=575.08
ND-11
GL=577.77
IL=575.52

Title:
Proposed Drainage Network Plan

Legend:

- SETTLEMENT
- NODE
- 3" HDPE PIPE
- DRAIN TYPE-1
- SULLAGE CARRIER
- SEPTIC TANK
- SETTLEMENT BOUNDARY

Drain Type 1=7701 Rft
Sullage Carrier= 3244 Rft

Scale: 1:1,700
1 inch = 142 feet
Paper Size: A3

0 40 80 160
Kilometers

Project:
Engineering Design & Construction Supervision, Punjab Rural Sustainable Water Supply & Sanitation Project, Cluster South III

PRMSC
ENVIRONMENTAL TECHNOLOGIES
ASIAN CONSULTING ENGINEERS www.asiancon.com

Revenue Village: Chak Abdul Haq Sheet-2

N

District:	Bahawalnagar
Tehsil:	Bahawalnagar
Revenue Village:	Chak Abdul Haq

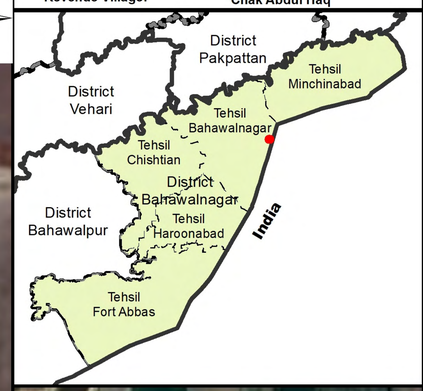

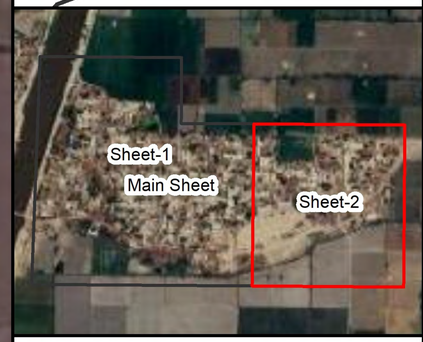

ND-35 GL=592.03 IL=589.79
ND-36 GL=594.91 IL=592.66
ND-31 GL=590.71 IL=588.46
ND-33 GL=592.2 IL=589.95
ND-4 GL=590.71 IL=587.99
ND-5 GL=590.08 IL=587.02
ND-6 GL=588.9 IL=582.83
ND-1 GL=586.38 IL=584.13
ND-2 GL=583.6 IL=580.73
ND-3 GL=577.84 IL=575.09
ND-32 GL=590.44 IL=588.19
ND-7 GL=575.72 IL=573.47
ND-8 GL=575.54 IL=573.28
GL=577.32 IL=573.15
SEPTIC TANK-T1(A) Plot Size=1.15 Marla
F.H.D.P.E. PIPE ULTIMATE DISPOSAL TO WATER COURSE
ND-11 GL=577.77 IL=575.52

Title:
Proposed Drainage Network Plan

Legend:

- NODE
- 3" HDPE PIPE
- DRAIN TYPE-1
- SULLAGE CARRIER
- SEPTIC TANK
- SETTLEMENT BOUNDARY

Drain Type 1=7701 Rft

Sullage Carrier= 3244 Rft

Scale: 1:1,200

1 inch = 100 feet

Paper Size: A3

0 40 80 160

Kilometers

Project:

Engineering Design & Construction Supervision, Punjab Rural Sustainable Water Supply & Sanitation Project, Cluster South III

PRWSC

ENVIRONMENTAL TECHNOLOGIES

ASIAN CONSULTING ENGINEERS www.asiancon.com

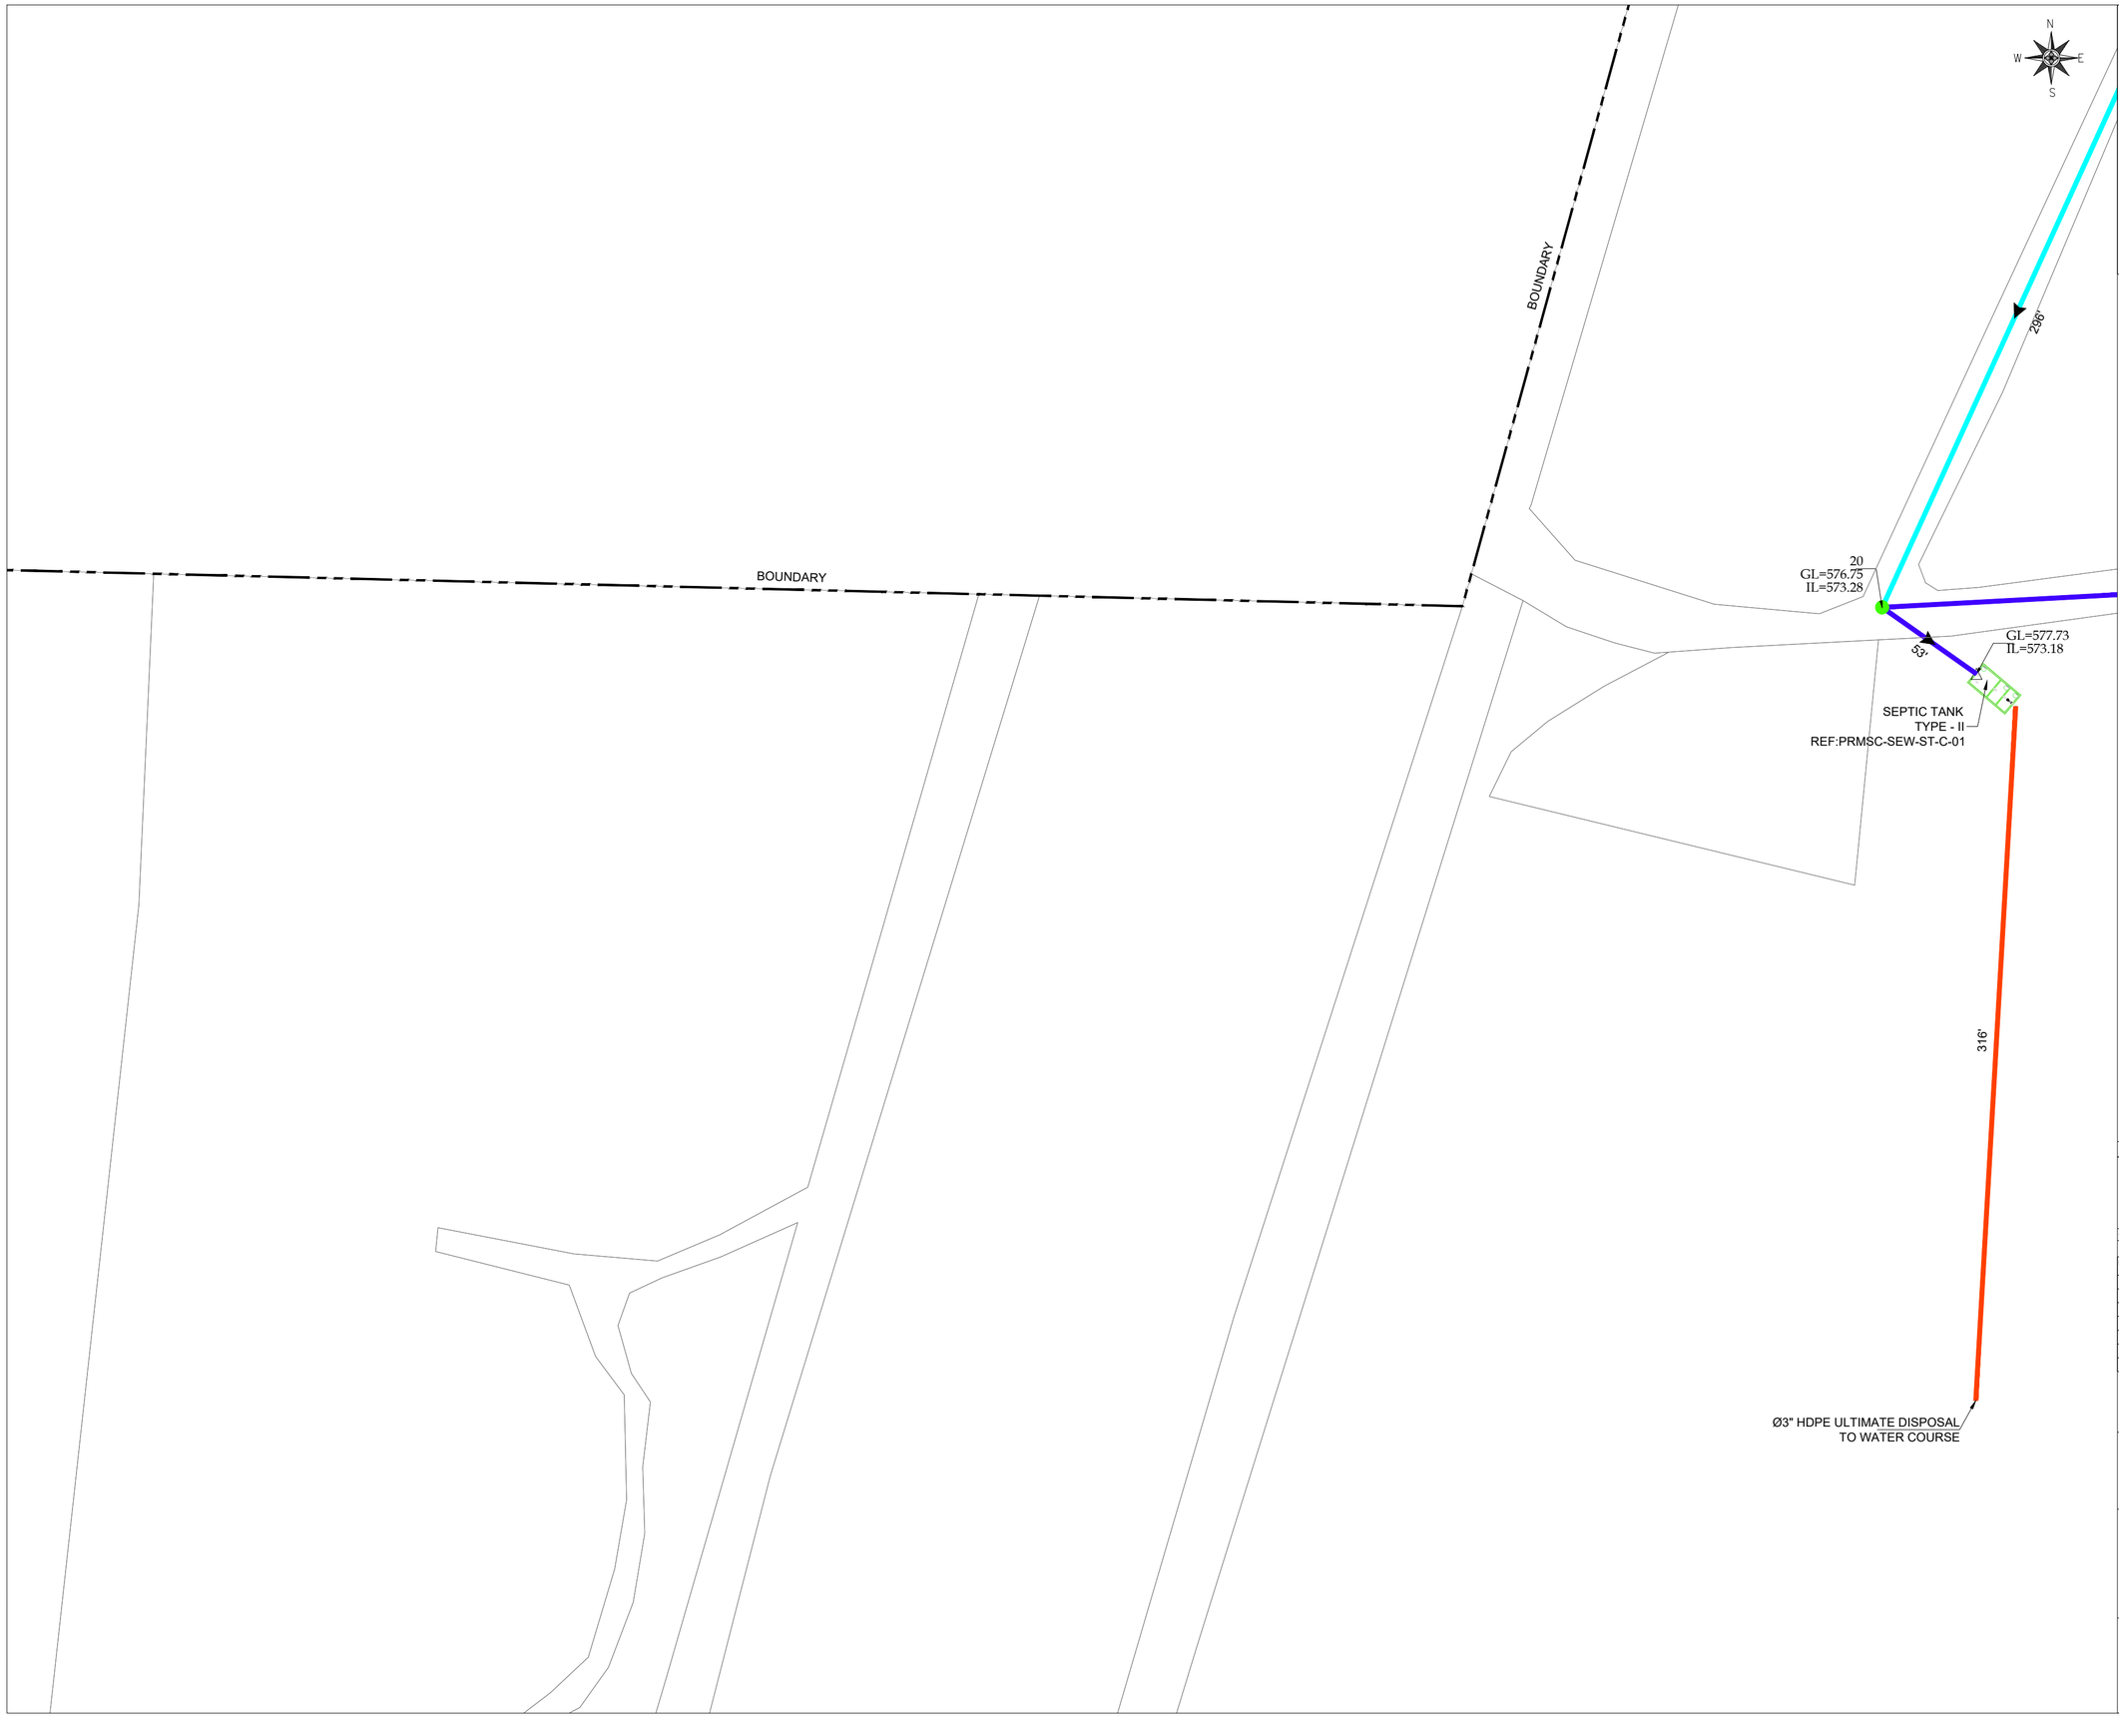

KEY PLAN

LEGEND:

- DRAIN TYPE - I
- SULLAGE CARRIER
- Ø3" HDPE PIPE
- BOUNDARY

VILLAGE: CHAK ABDUL HAQ (BWN)

TITLE.

DRAINAGE SYSTEM LAYOUT PLAN-01

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	20-04-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-CAH-SEW-LP-01	01 OF 05	00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS
www.asiaecon.com.pv

PRMSC-BWN-CAH-SEW-LP-01

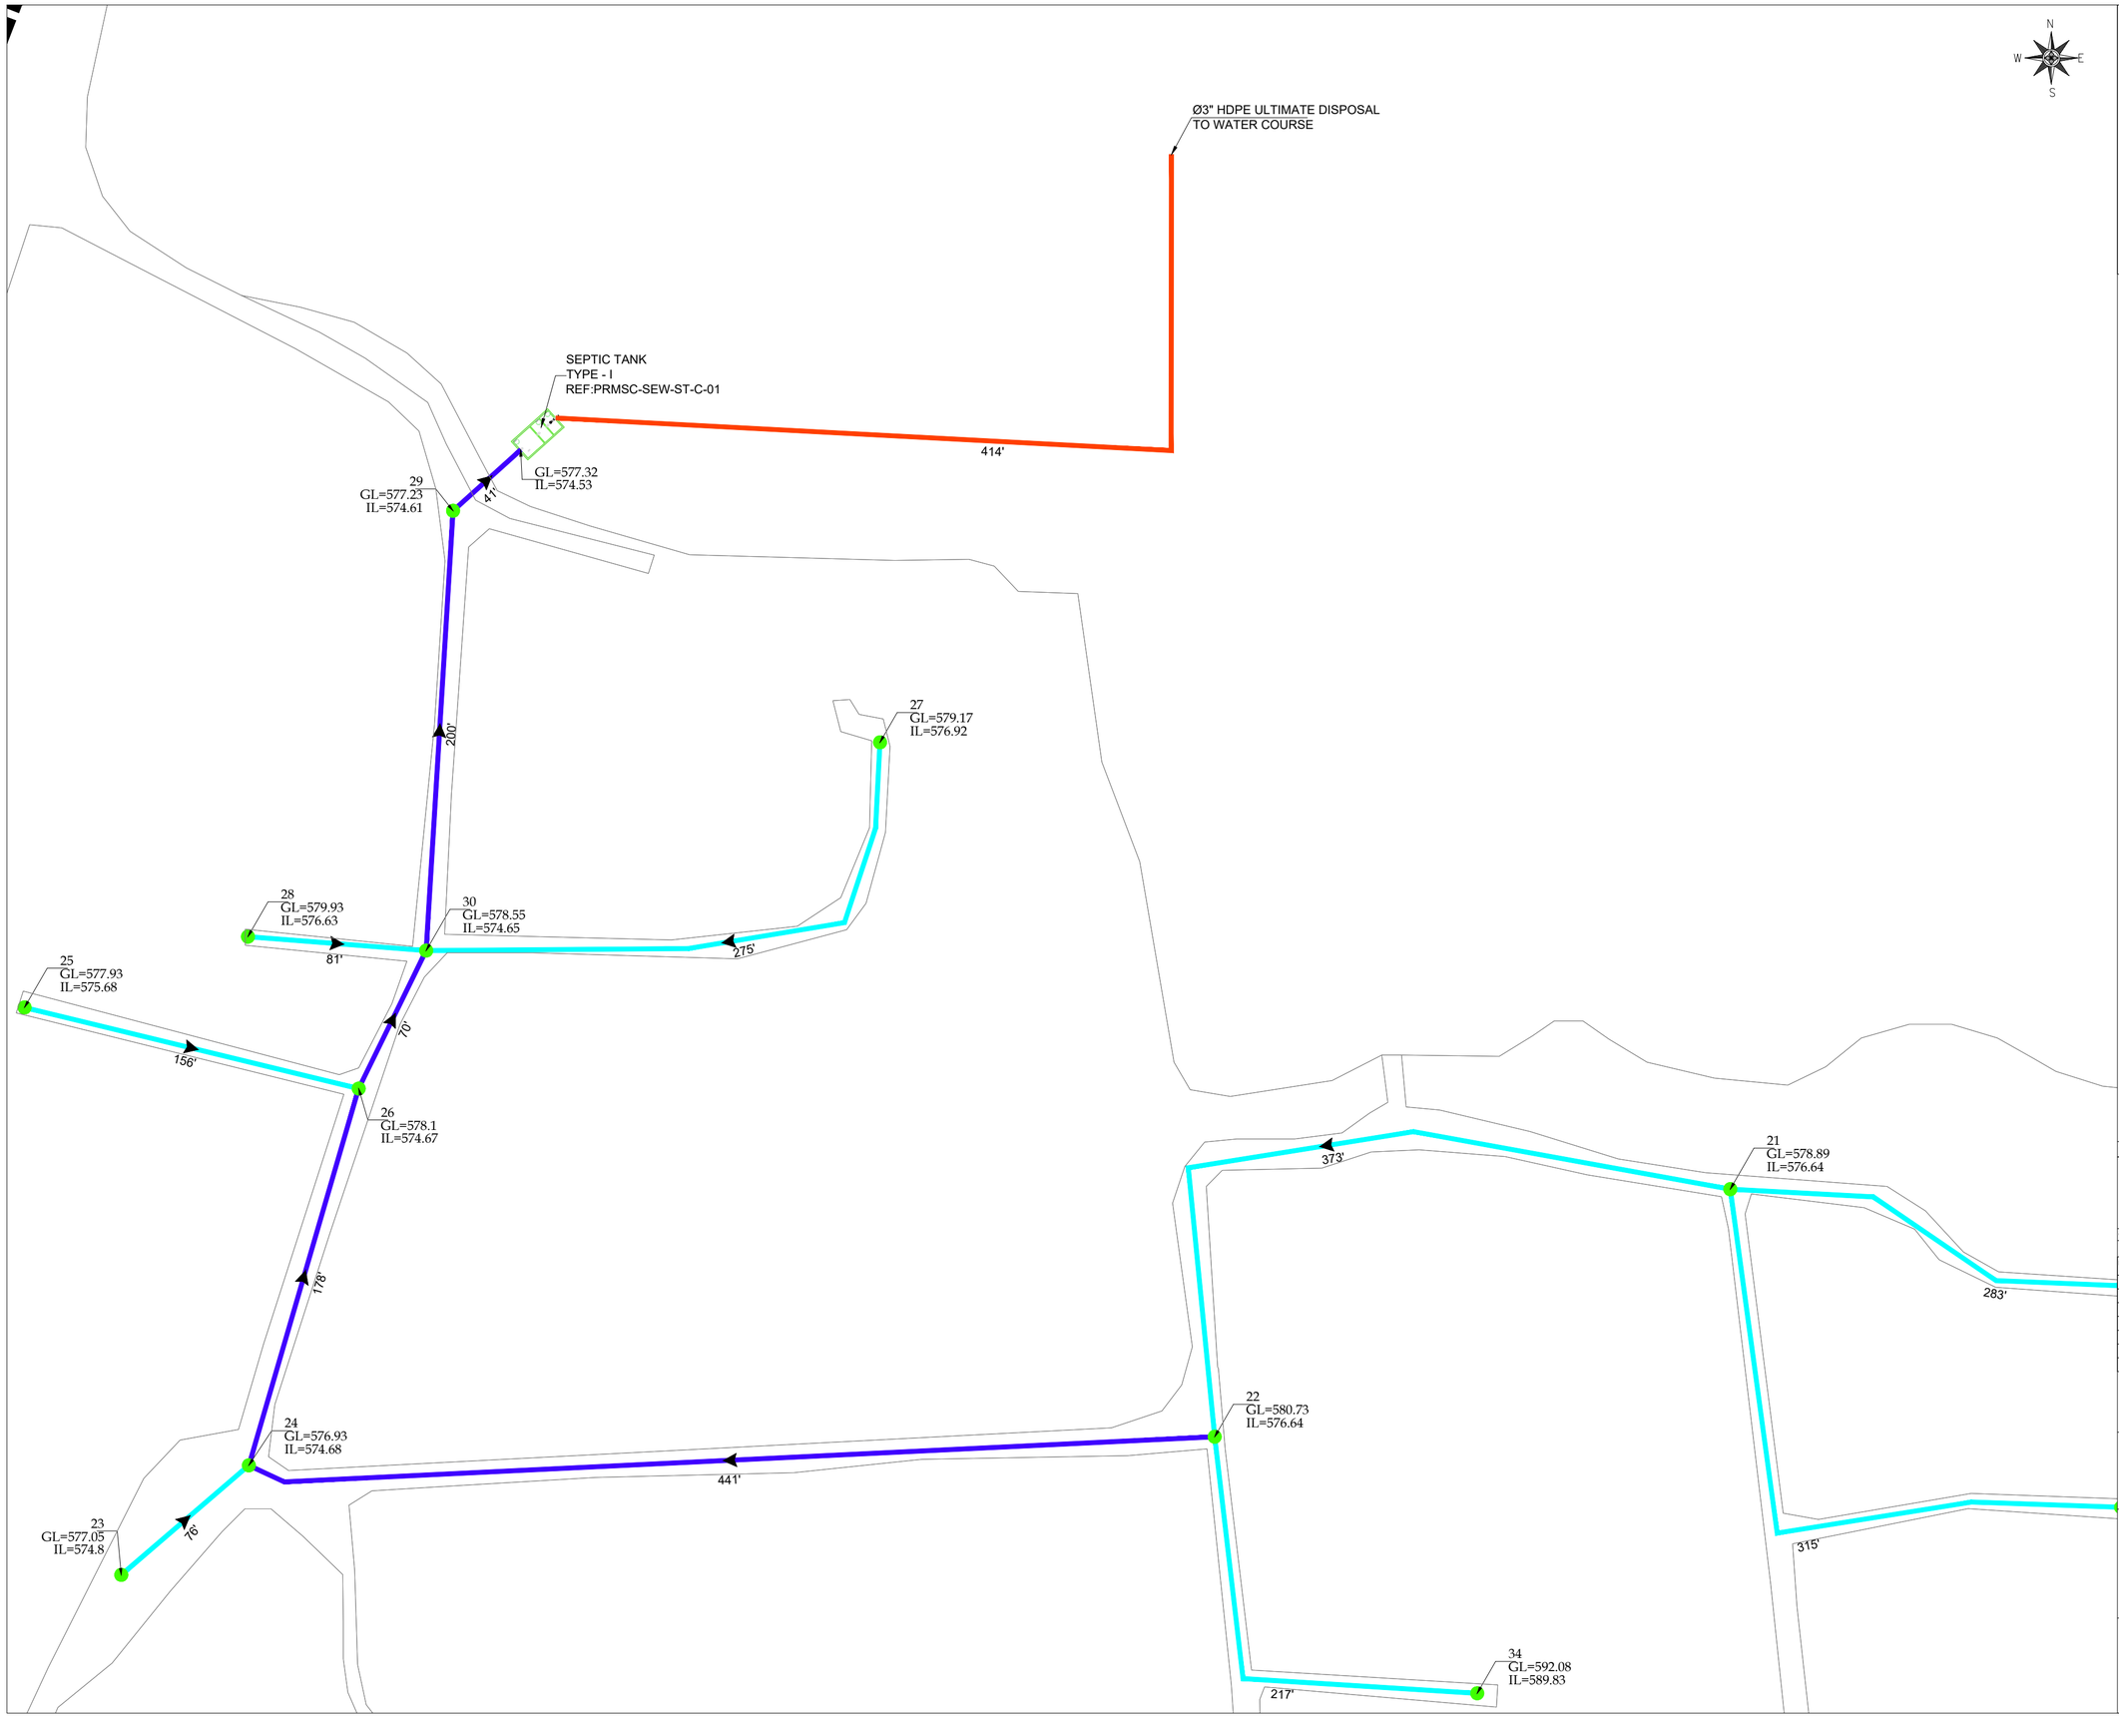

KEY PLAN

LEGEND:

- DRAIN TYPE - I
- SULLAGE CARRIER
- Ø3" HDPE PIPE
- BOUNDARY

VILLAGE: CHAK ABDUL HAQ (BWN)

TITLE.

DRAINAGE SYSTEM LAYOUT PLAN-02

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	20-04-2026	DETAILED DESIGN	MUNEEB	ENGR FAIEZ	ENGR IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-CAH-SEW-LP-02	02 OF 05	00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS
www.asiancon.com JV

PRMSC-BWN-CAH-SEW-LP-02

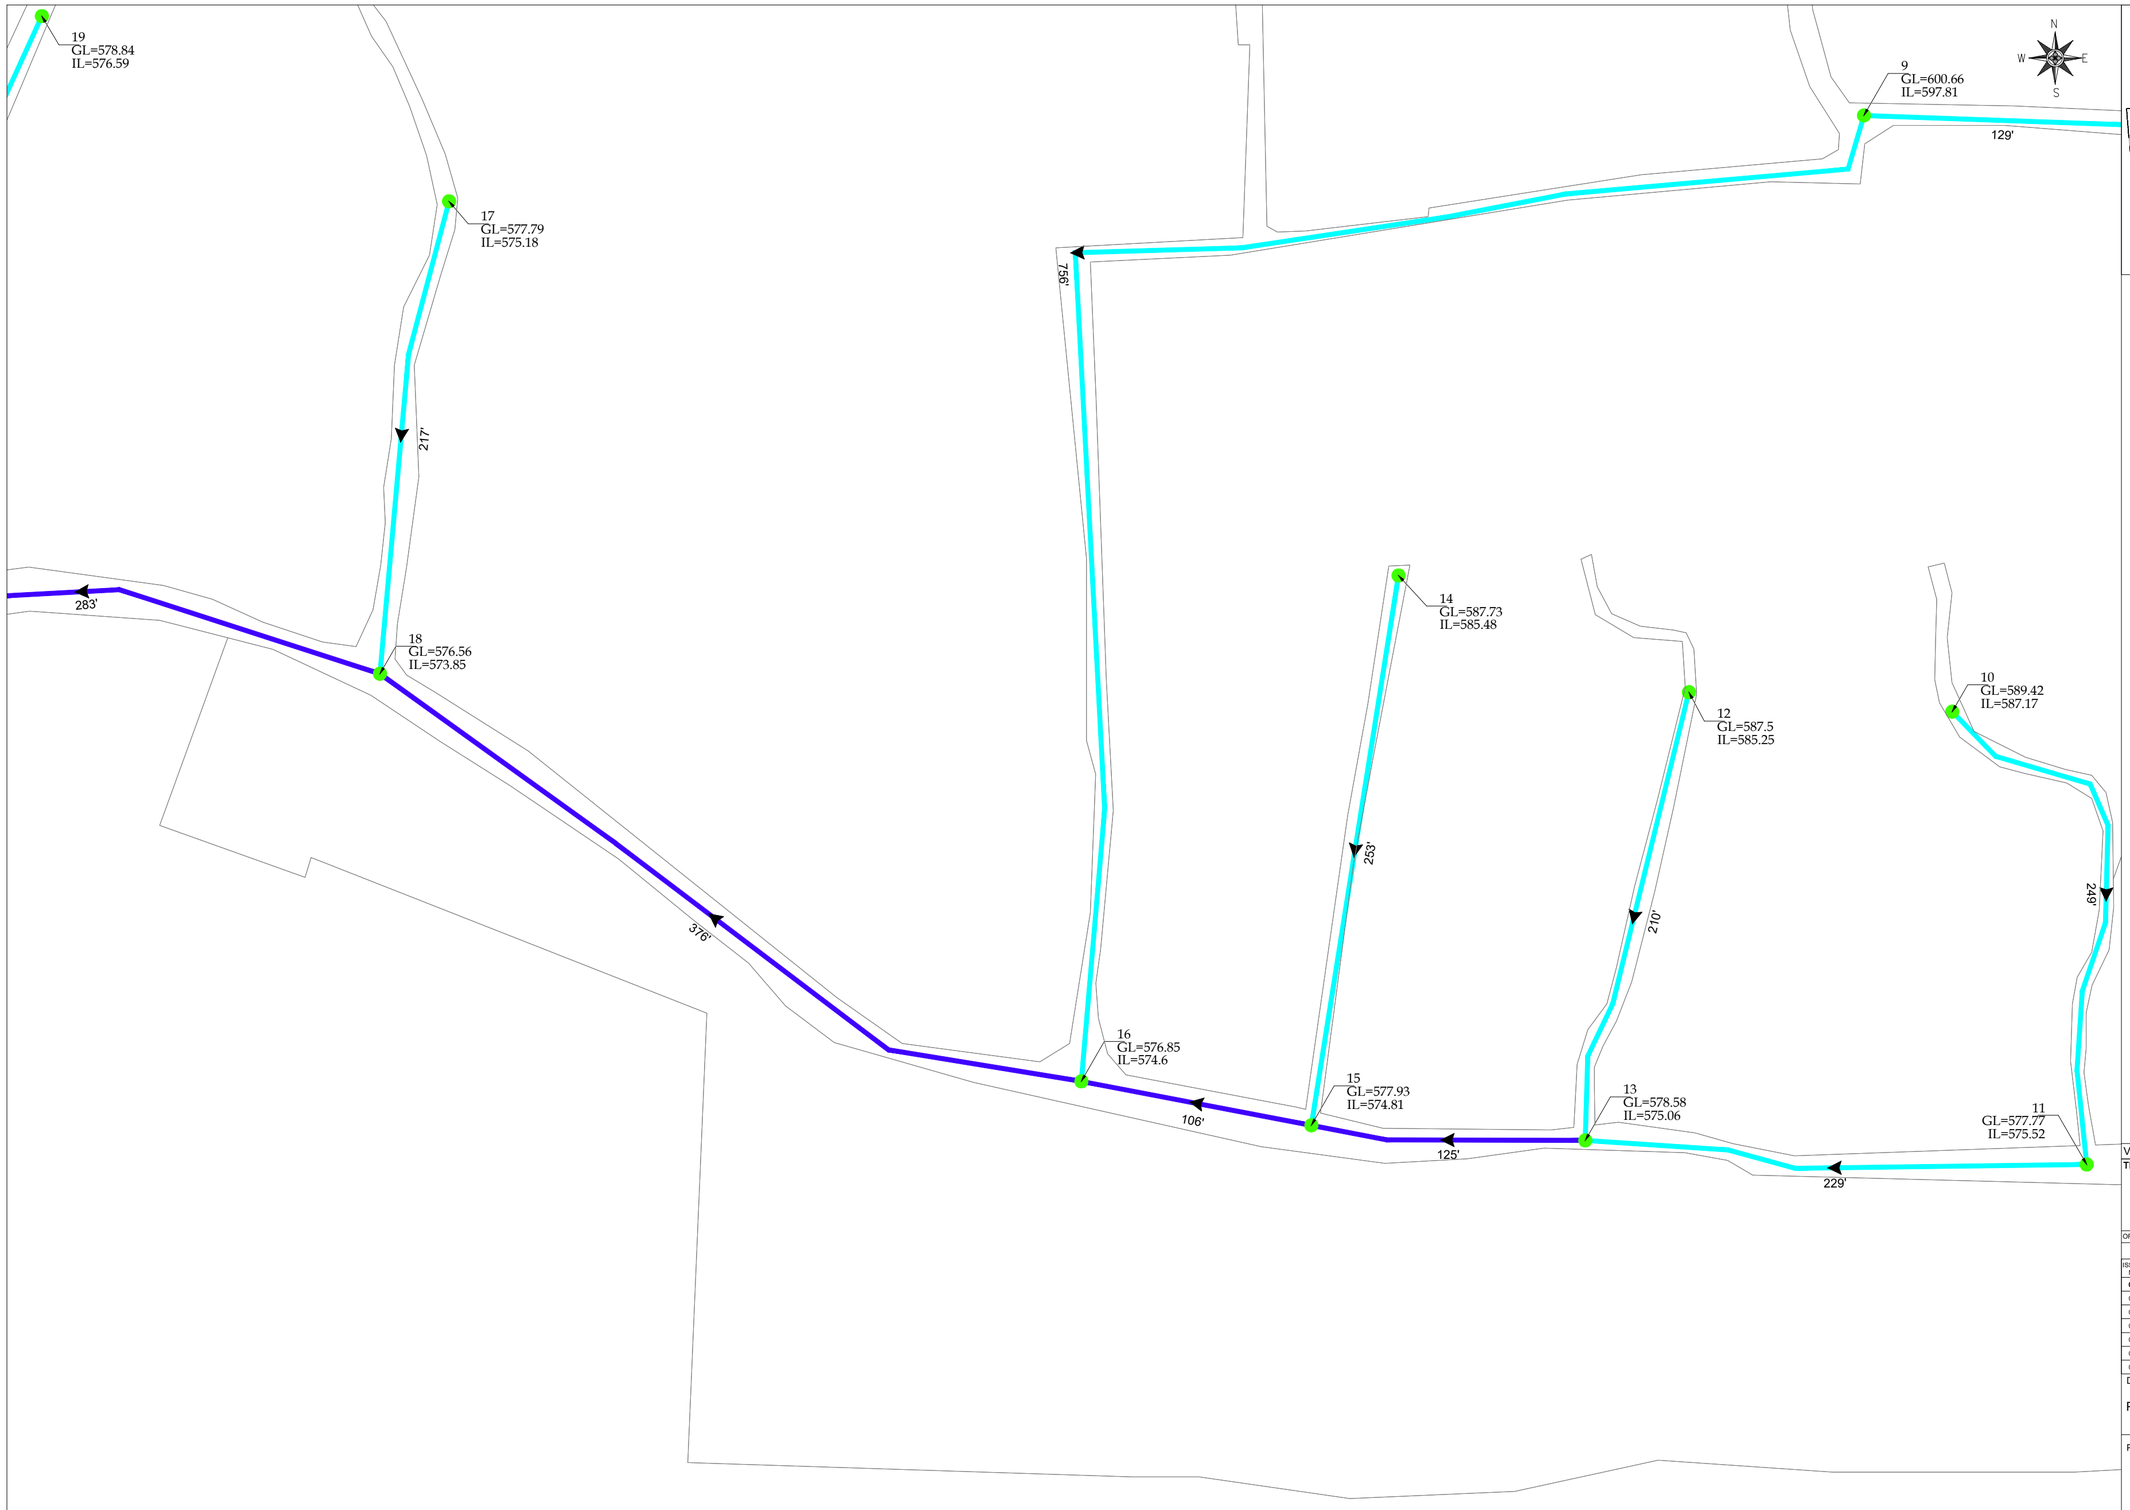

KEY PLAN

LEGEND:

- DRAIN TYPE - I
- SULLAGE CARRIER
- Ø3" HDPE PIPE
- BOUNDARY

VILLAGE: CHAK ABDUL HAQ (BWN)

TITLE.

DRAINAGE SYSTEM LAYOUT PLAN-03

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	20-04-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-CAH-SEW-LP-03	03 OF 05	00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

PRMSC-BWN-CAH-SEW-LP-03

KEY PLAN

LEGEND:

DRAIN TYPE - I

SULLAGE CARRIER

Ø3" HDPE PIPE

BOUNDARY

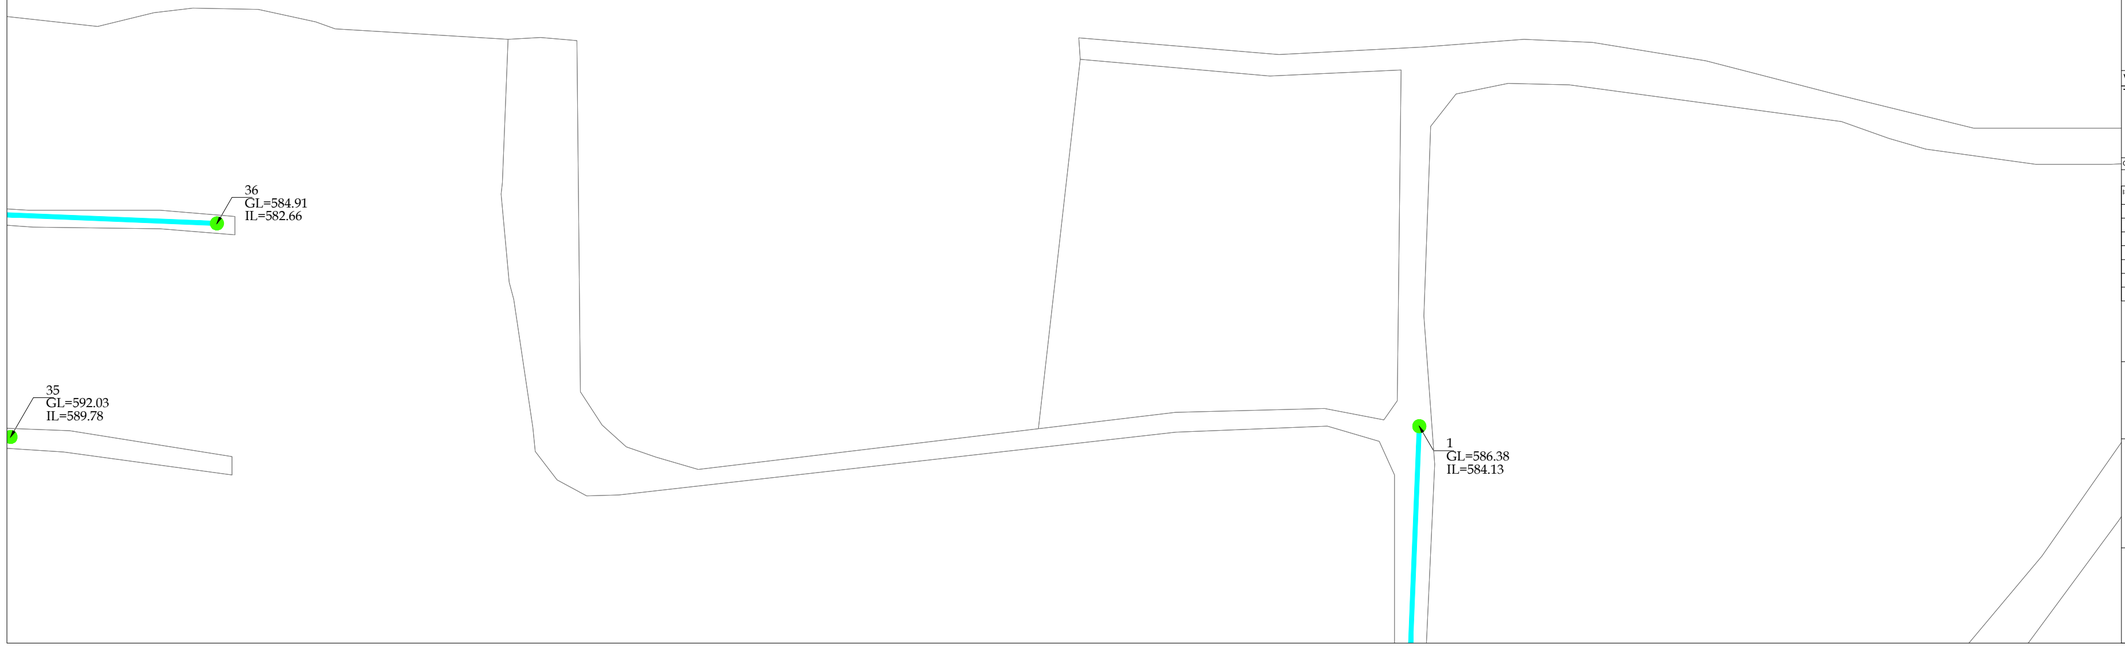

VILLAGE: CHAK ABDUL HAQ (BWN)

TITLE.

DRAINAGE SYSTEM LAYOUT PLAN-04

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	20-04-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-CAH-SEW-LP-04	04 OF 05	00

PROJECT:

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS
www.asiacon.com.pk

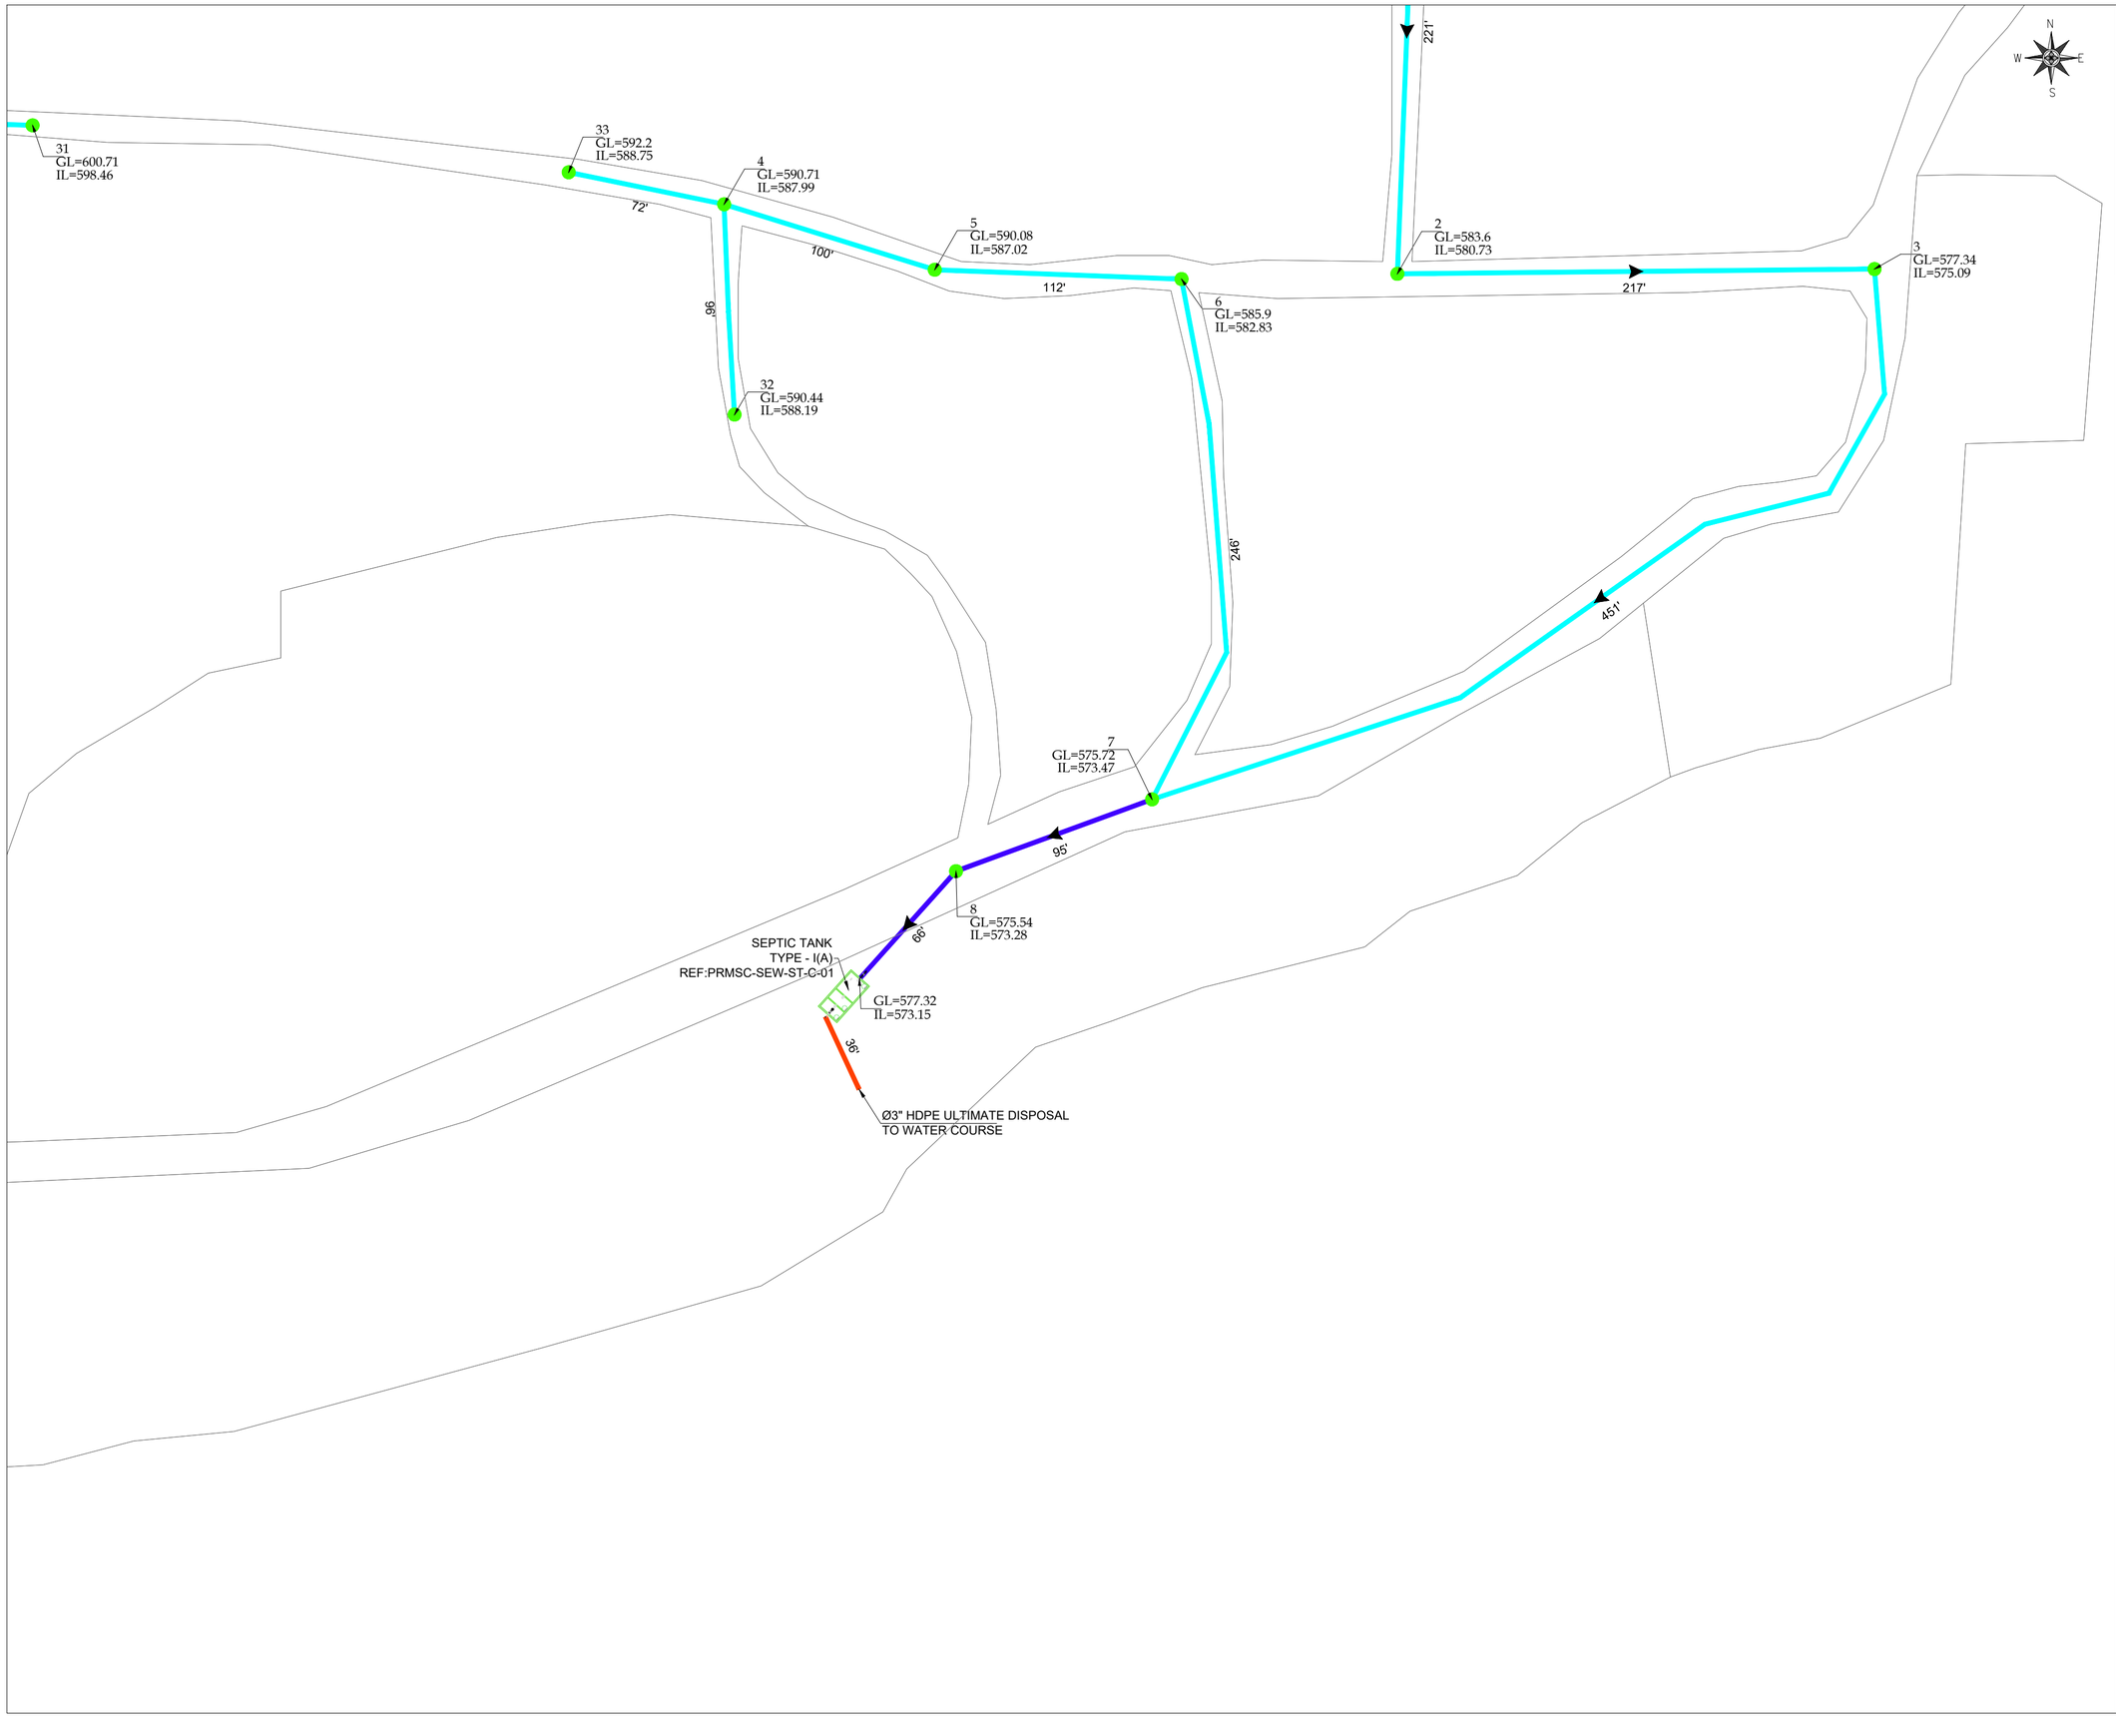

KEY PLAN

LEGEND:

- DRAIN TYPE - I
- SULLAGE CARRIER
- Ø3" HDPE PIPE
- BOUNDARY

VILLAGE: CHAK ABDUL HAQ (BWN)

TITLE.

DRAINAGE SYSTEM LAYOUT PLAN-05

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	20-04-2026	DETAILED DESIGN	MUNEEB	ENGR FAIEZ	ENGR IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº: PRMSC-BWN-CAH-SEW-LP-05

SHEET 05 OF 05

REV 00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

PRMSC-BWN-CAH-SEW-LP-05

HYDRAULIC STATEMENT								
Node		Length	Slope	Elevation Ground	Elevation Ground	Elevation Invert	Elevation Invert	Depth
FROM	TO	ft	ft/ft	U/S	D/S	U/S	D/S	ft
1	2	221	0.01536	586.38	583.6	584.13	580.73	2.25
2	3	217	0.026	583.6	577.34	580.73	575.09	2.87
3	7	451	0.00359	577.34	575.72	575.09	573.47	2.25
32	4	96	0.002	590.44	590.71	587.99	588.19	2.71
33	4	72	0.004	592.2	590.71	588.46	588.75	3.07
4	5	100	0.002	590.71	590.08	587.79	587.99	3.07
5	6	112	0.03	590.08	585.9	583.65	587.02	2.25
6	7	246	0.038	585.9	575.72	573.47	582.83	2.27
7	8	95	0.002	575.72	575.54	573.47	573.28	2.84
8	ST-TYPE-IA	66	0.002	575.54	577.32	573.28	573.15	2.25
31	9	129	0.005	600.71	600.66	597.81	598.46	2.25
9	16	756	0.03072	600.66	576.85	597.81	574.6	2.25
10	11	249	0.0467	589.42	577.77	587.17	575.52	3.52
11	13	229	0.002	577.77	578.58	575.52	575.06	2.25
12	13	210	0.04847	587.5	578.58	585.25	575.06	3.12
13	15	125	0.002	578.58	577.93	575.06	574.81	2.26
14	15	253	0.04222	587.73	577.93	585.48	574.81	2.6
15	16	106	0.002	577.93	576.85	574.81	574.6	2.72
16	18	376	0.002	576.85	576.56	574.6	573.85	2.25
17	18	217	0.004	577.79	576.56	575.18	574.31	3.47
18	20	283	0.002	576.56	576.75	573.85	573.28	2.25
19	20	296	0.0112	578.84	576.75	576.59	573.28	4.09
20	ST-TYPE-II	53	0.002	576.75	577.73	573.28	573.18	2.25
35	21	315	0.04165	592.03	578.89	576.64	589.78	2.25
36	21	283	0.02121	584.91	578.89	576.64	582.66	2.25
21	22	373	0.00002	578.89	580.73	576.64	576.64	3.43
34	22	217	0.05221	592.08	580.73	578.48	589.83	2.25
22	24	441	0.00442	580.73	576.93	576.64	574.68	3.3
23	24	76	0.00153	577.05	576.93	574.8	574.68	2.62
24	26	178	0.0001	576.93	578.1	574.68	574.67	3.9
25	26	156	0.002	577.93	578.1	575.68	575.37	2.25
26	30	70	0.0002	578.1	578.55	574.67	574.65	2.25
27	30	275	0.00225	579.17	578.55	576.92	576.3	3.45
28	30	81	0.004	579.93	578.55	576.63	576.3	2.25
30	29	200	0.0002	578.55	577.23	574.61	574.65	2.25
29	ST-TYPE-I	41	0.002	577.23	577.32	574.61	574.53	2.25

VILLAGE: CHAK ABDUL HAQ (BWN)

TITLE.

HYDRAULIC STATEMENT

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	20-04-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº: PRMSC-BWN-CAH-SEW-HS-01

SHEET 01 OF 01

REV 00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT
ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

PRMSC-BWN-CAH-SEW-HS-00

DADOO MAMMUNKA

KEY PLAN

Revenue Village: Dadoo Mamunka Sheet-1

N

District:	Bahawalnagar
Tehsil:	Bahawalnagar
Revenue Village:	Dadoo Mamunka

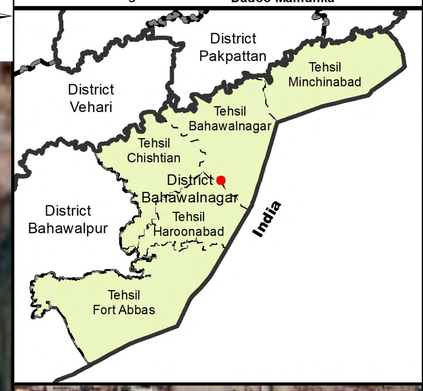

ND-1
GL=567.44
IL=566.6

626'

ND-3
GL=566.48
IL=565.65

397'

Daduwala

ND-2
GL=568.52
IL=567.22

ND-5
GL=567.13
IL=564.59

280'

ND-4
GL=567.65
IL=566.81

ND-6
GL=566.04
IL=564.21

105'

ND-7
GL=566.64
IL=563.79

GL=567.15
IL=563.78

104'
1.5'x1.5'

SEPTIC TANK-T1
Plot Size=1.59 Marla

327'

3" HDPE PIPE ULTIMATE DISPOSAL TO WATER COURSE

Title:
Proposed Drainage Network Plan

Legend:

- SETTLEMENT
- NODE
- 3" HDPE PIPE
- DRAIN TYPE-1
- SULLAGE CARRIER
- SEPTIC TANK
- SETTLEMENT BOUNDARY

Drain Type 1=1963 Rft
Sullage Carrier=104 Rft

Scale: 1:840
1 inch = 70 feet
Paper Size: A3

0 40 80 160
Kilometers

Project:
Engineering Design & Construction Supervision, Punjab Rural Sustainable Water Supply & Sanitation Project, Cluster South III

PRWSC
ENVIRONMENTAL TECHNOLOGIES
ASIAN CONSULTING ENGINEERS
www.asiancon.com

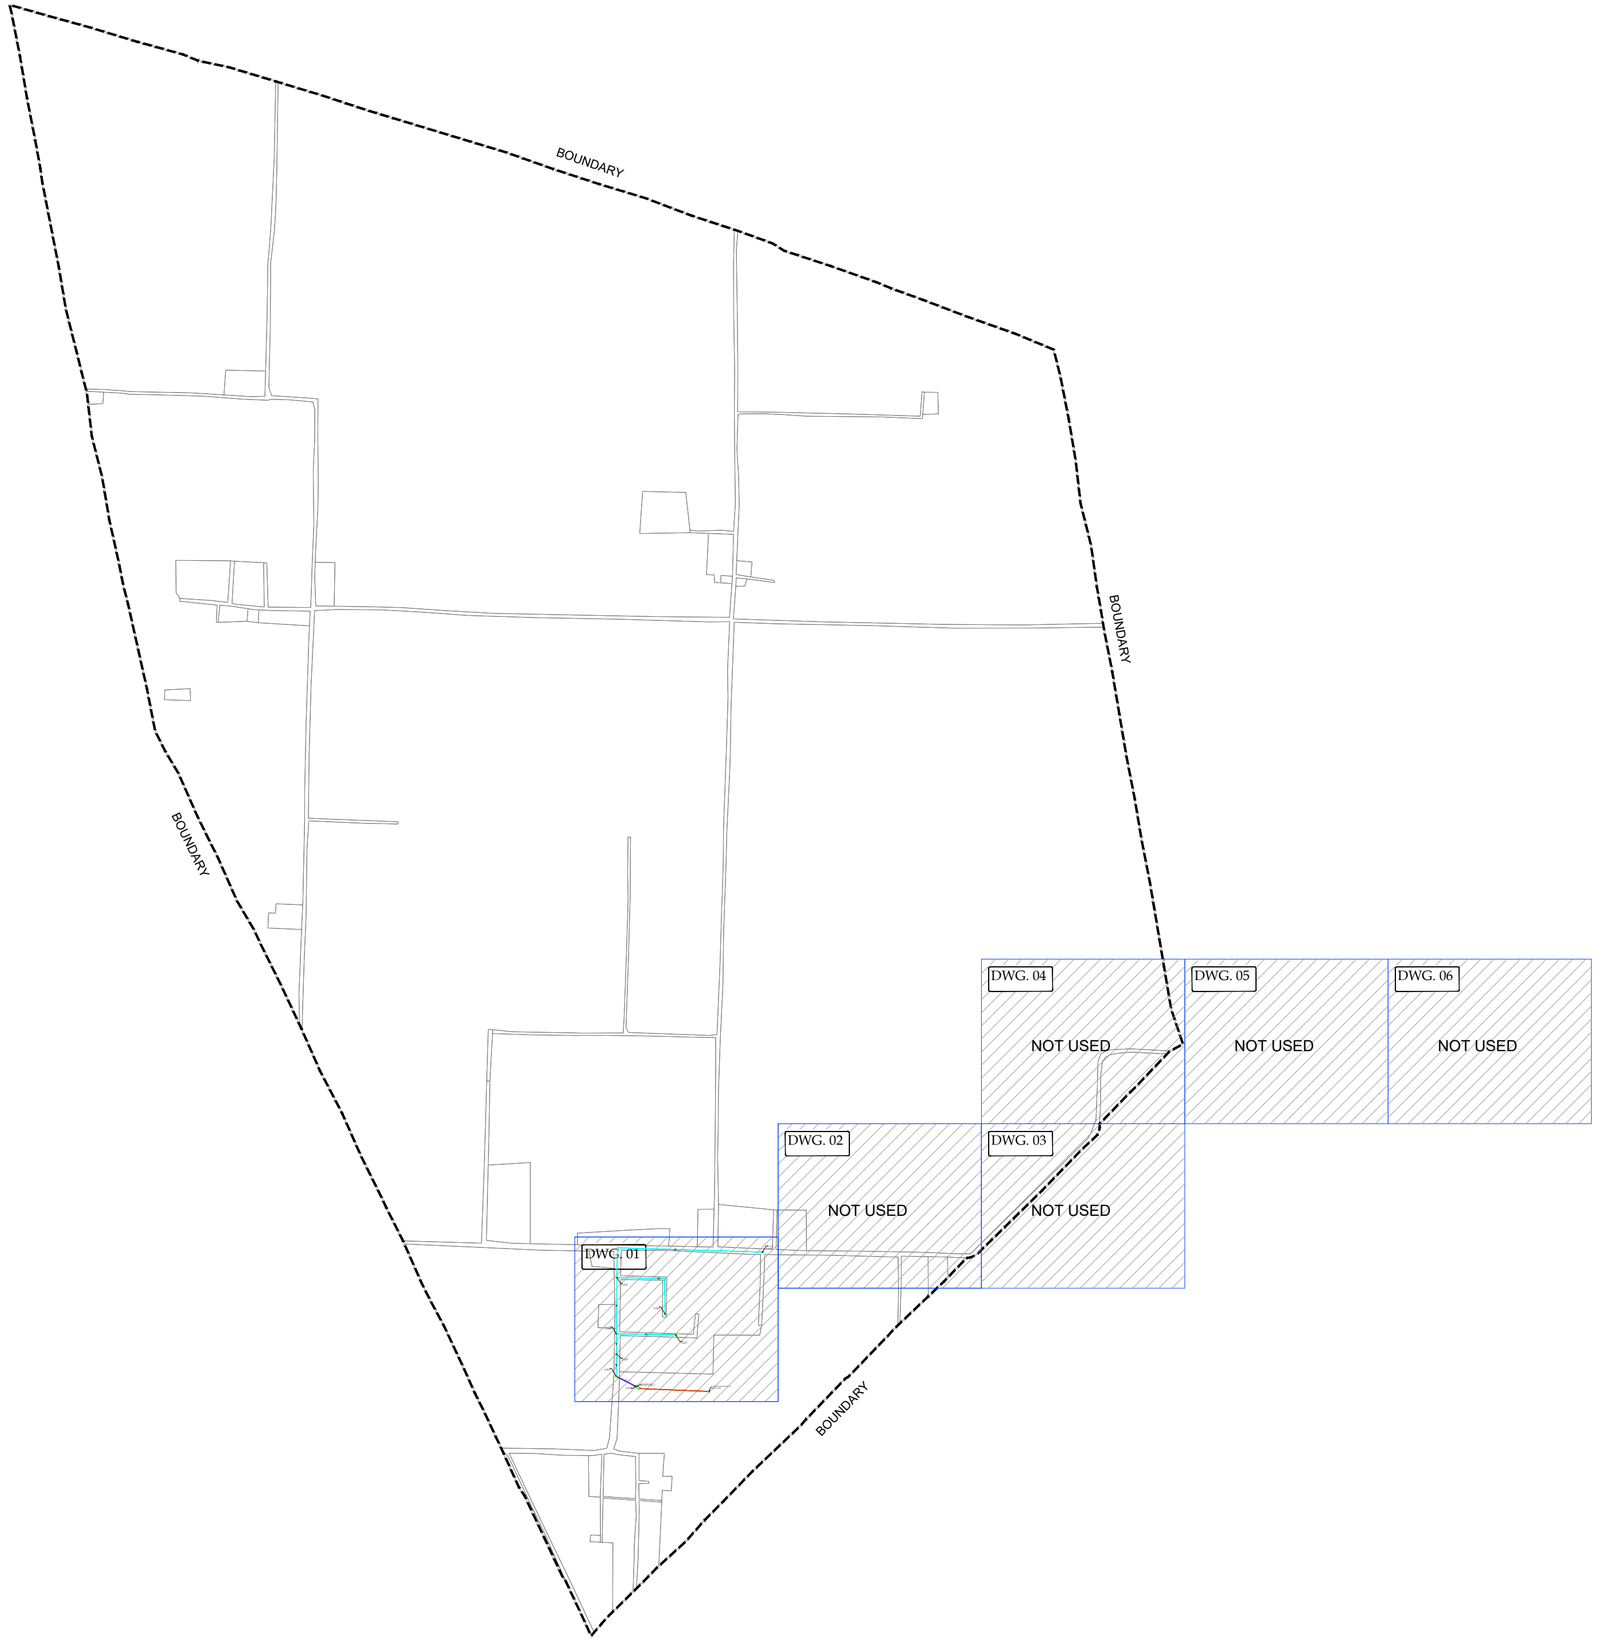

LEGEND:

- DRAIN TYPE-I
- SULLAGE CARRIER
- Ø3" HDPE PIPE
- BOUNDARY

VILLAGE: DADOO MAMMUNKA (BWN)

TITLE.

DRAINAGE SYSTEM KEY PLAN

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 520'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	28-04-2026	DETAILED DESIGN	M.ASIF	ENGR. FAIEZ	ENGR. HSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING N°: PRMSC-BWN-DM-WS-KP-00

SHEET 00 OF 00

REV 00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT
ASIAN CONSULTING ENGINEERS (PVT) www.asiancon.com

PRMSC-BWN-DM-SEW-KP-00

LAYOUT PLAN

1
GL=567.44
IL=566.6

826'

3
GL=566.48
IL=565.65

392'

265'

2
GL=568.52
IL=567.22

5
GL=567.13
IL=564.59

280'

4
GL=567.65
IL=566.81

95'

6
GL=566.04
IL=564.21

105'

7
GL=566.64
IL=563.79

1.5' x 1.5'

104'

SEPTIC TANK TYPE -I
REF:PRMSC-SEW-ST-C-01

GL=567.15
IL=563.78

Ø3" HDPE ULTIMATE DISPOSAL TO
WATER COURSE

327'

N
W
E
S

KEY PLAN

LEGEND:

DRAIN TYPE-I

SULLAGE CARRIER

Ø3" HDPE PIPE

BOUNDARY

PRMSC-BWN-DM-SEW-LP-01

VILLAGE: DADOO MAMMUNKA (BWN)

TITLE.

DRAINAGE SYSTEM LAYOUT PLAN-01

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	D E S C R I P T I O N	DRAWN	DESIGNED	APPROVED
01	28-04-2026	DETAILED DESIGN	M.ASIF	ENGR FAIEZ	ENGR IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-DM-WS-LP-01	01 OF 06	00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

HYDRAULIC STATEMENT

Node		Length	Slope	Elevation Ground	Elevation Ground	Invert	Invert	Depth
FROM	TO	ft	ft/ft	U/S	D/S	U/S	D/S	ft
1	3	826	0.004	567.44	566.48	566.6	565.65	0.83
2	3	392	0.004	568.52	566.48	567.22	565.65	1.3
3	5	265	0.004	566.48	567.13	565.65	564.59	0.83
4	5	280	0.004	567.65	567.13	566.81	565.69	0.83
5	6	95	0.004	567.13	566.04	564.59	564.21	2.54
6	7	105	0.004	566.04	566.64	564.21	563.79	1.83
7	ST- Type- I	104	0.004	566.64	567.15	563.79	563.78	2.85

VILLAGE: DADOO MAMMUNKA (BWN)

TITLE.

HYDRAULIC STATEMENT

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	28-04-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. HSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº: PRMSC-BWN-DM-SEW-HS-00

SHEET 01 OF 01

REV 00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH-III

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS www.asiancon.com

PRMSC-KPT-DM-SEW-HS-01

DARA SANATTEKA

KEY PLAN

Revenue Village: Dara Sanatteka Sheet-1

SEPTIC TANK-T4
Plot Size
=3.04 Marla

District:	Bahawlanagar
Tehsil:	Bahawlanagar
Revenue Village:	Dara Sanatteka

Title:
Proposed Drainage Network Plan

Legend:

- NODE
- 3" HDPE PIPE
- DRAIN TYPE-1
- SULLAGE CARRIER
- SEPTIC TANK
- SETTLEMENT BOUNDARY

Drain Type-1=3837 Rft
Sullage Carrier=1307 Rft

Scale: 1:1,500
1 inch = 125 feet
Paper Size: A3

0 40 80 160
Kilometers

Project:
Engineering Design & Construction Supervision, Punjab Rural Sustainable Water Supply & Sanitation Project, Cluster South III

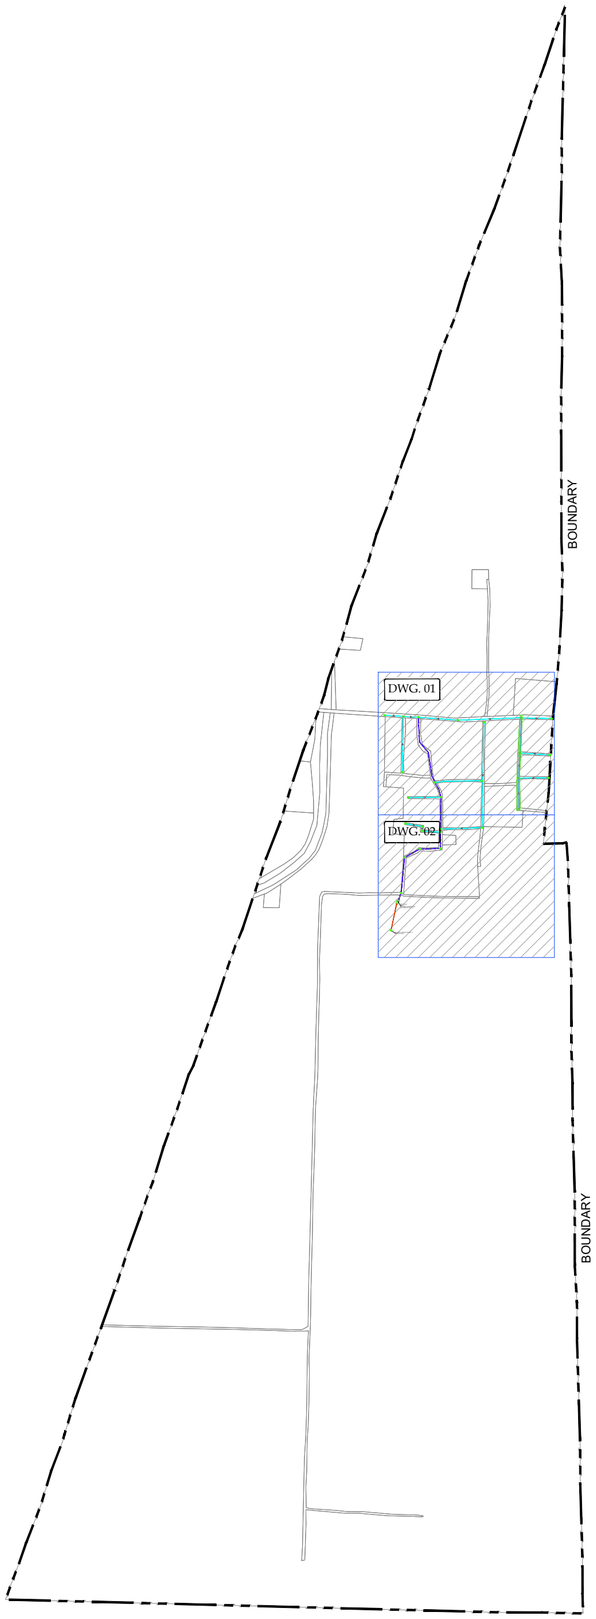

N
W
E
S

LEGEND:

- DRAIN TYPE - I
- SULLAGE CARRIER
- Ø3" HDPE PIPE
- EXISTING SOLING
- BOUNDARY

VILLAGE: DARA SANETTEKA (BWN)

TITLE:

DRAINAGE SYSTEM KEY PLAN

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 600'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	02-02-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02	16-02-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-DST-SEW-KP-00	00 OF 00	01

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT
ASIAN CONSULTING ENGINEERS
www.asiancon.com

PRMSC-BWN-DST-SEW-KP-00

LAYOUT PLAN

KEY PLAN

LEGEND:

- DRAIN TYPE - I
- SULLAGE CARRIER
- Ø3" HDPE PIPE
- EXISTING SOLING
- BOUNDARY

VILLAGE: DARA SANETTEKA (BWN)

TITLE:

DRAINAGE SYSTEM LAYOUT PLAN-01

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	02-02-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02	16-02-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
03					
04					
05					
06					
07					

DRAWING Nº: PRMSC-BWN-DST-SEW-LP-01

SHEET 01 OF 02

REV 01

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS
www.asianconsultingengineers.com

PRMSC-BWN-DST-SEW-LP-01

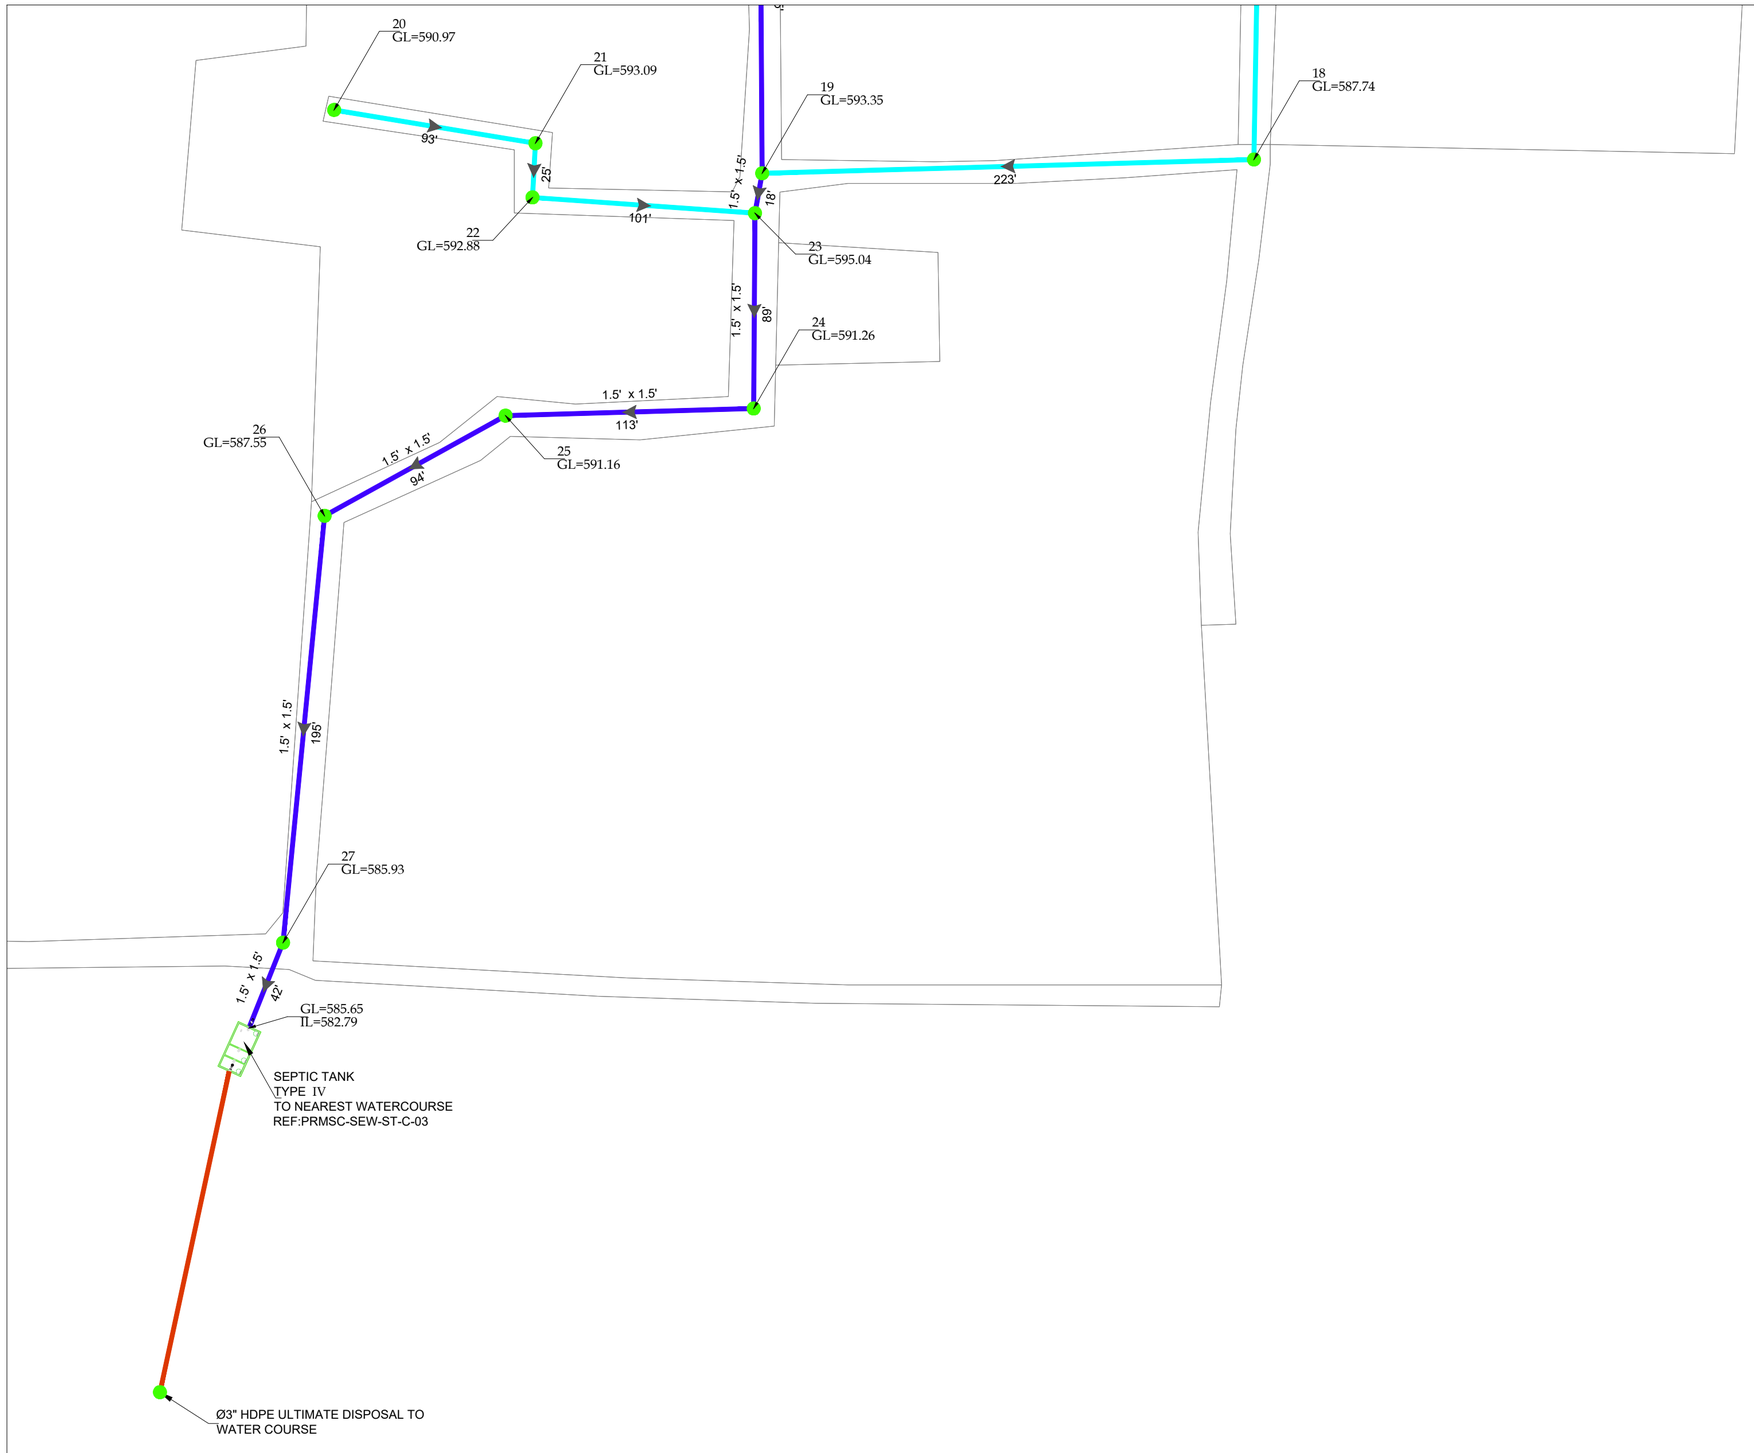



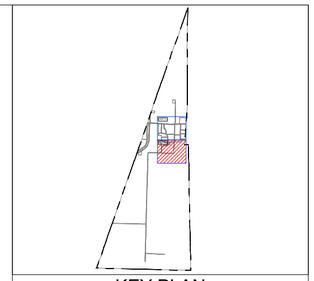

KEY PLAN

LEGEND:

- DRAIN TYPE - I
- SULLAGE CARRIER
- Ø3" HDPE PIPE
- EXISTING SOLING
- BOUNDARY

VILLAGE: DARA SANETTEKA (BWN)

TITLE.

DRAINAGE SYSTEM LAYOUT PLAN-02

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	02-02-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02	16-02-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-DST-SEW-LP-02	02 OF 02	01

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

PRMSC-BWN-DST-SEW-LP-02

HYDRAULIC STATEMENT

Node		Length	Slope	Elevation Ground	Elevation Ground	Invert	Invert
FROM	TO	ft	ft/ft	U/S	D/S	U/S	D/S
START NODE	STOP NODE	LENGTH	SLOPE	G.L U/S	G.L D/S	I.L U/S	I.L D/S
1	3	167	0.001	587.98	588.23	586.98	587.14
2	3	165	0.001	588.3	588.23	587.46	587.3
3	5	138	0.001	588.23	588.58	586.84	586.98
4	5	163	0.001	588.45	588.58	587.62	587.46
5	7	192	0.001	588.58	589.26	586.65	586.84
6	7	164	0.001	590.02	589.26	588.42	588.59
7	8	346	0.001	589.26	591.35	586.3	586.65
8	12	217	0.001	591.35	589.46	586.08	586.3
9	11	304	0.001	589.95	589.04	588.21	588.51
10	11	103	0.001	588.21	589.04	587.38	587.28
11	12	82	0.001	589.04	589.46	587.28	587.2
12	14	378	0.002	589.46	594.91	585.17	584.41
13	14	255	0.001	591.59	594.91	590.5	590.76
14	16	88	0.002	594.91	594.86	584.41	584.24
15	16	177	0.001	593.76	594.86	592.93	592.75
16	19	173	0.002	594.86	593.35	584.24	583.89
17	18	573	0.001	590.7	587.74	587.48	586.91
18	19	223	0.001	587.74	593.35	586.68	586.91
19	23	18	0.002	593.35	595.04	583.85	583.89
20	21	93	0.001	590.97	593.09	590.13	590.04
21	22	25	0.001	593.09	592.88	590.04	590.02
22	23	101	0.001	592.88	595.04	590.02	589.92
23	24	89	0.002	595.04	591.26	583.85	583.68
24	25	113	0.002	591.26	591.16	583.68	583.45
25	26	94	0.002	591.16	587.55	583.26	583.45
26	27	195	0.002	587.55	585.93	582.87	583.26
SP TYPE -IV	27	42	0.002	585.65	585.93	582.79	582.87

VILLAGE: DARA SANETTEKA (BWN)

TITLE.

HYDRAULIC STATEMENT

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	18-09-2025	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº: PRMSC-BWN-DST-SEW-HS-00

SHEET 00 OF 00

REV 00

PROJECT: ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER CENTRAL

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS www.asianeco.com

DHANRAJ PURA

KEY PLAN

Revenue Village: Dhanraj Pura Main Sheet

District:	Bahawalnagar
Tehsil:	Bahawalnagar
Revenue Village:	Dhanraj Pura

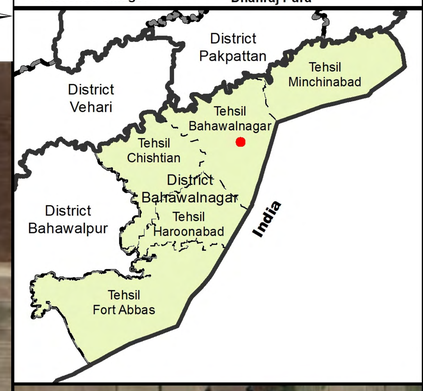

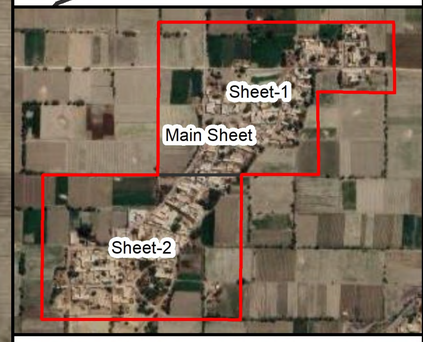

Title:
Proposed Drainage Network Plan

Legend:

- SETTLEMENT
- NODE
- 3" HDPE PIPE
- DRAIN TYPE-1
- SULLAGE CARRIER
- SEPTIC TANK
- SETTLEMENT BOUNDARY

Drain Type 1=5055 Rft

Sullage Carrier= 2080 Rft

Scale: 1:1,800

1 inch = 150 feet

Paper Size: A3

0 40 80 160

Kilometers

Project:

Engineering Design & Construction Supervision, Punjab Rural Sustainable Water Supply & Sanitation Project, Cluster South III

PRSMC ENVIRONMENTAL TECHNOLOGIES ASIAN CONSULTING ENGINEERS www.asiancon.com

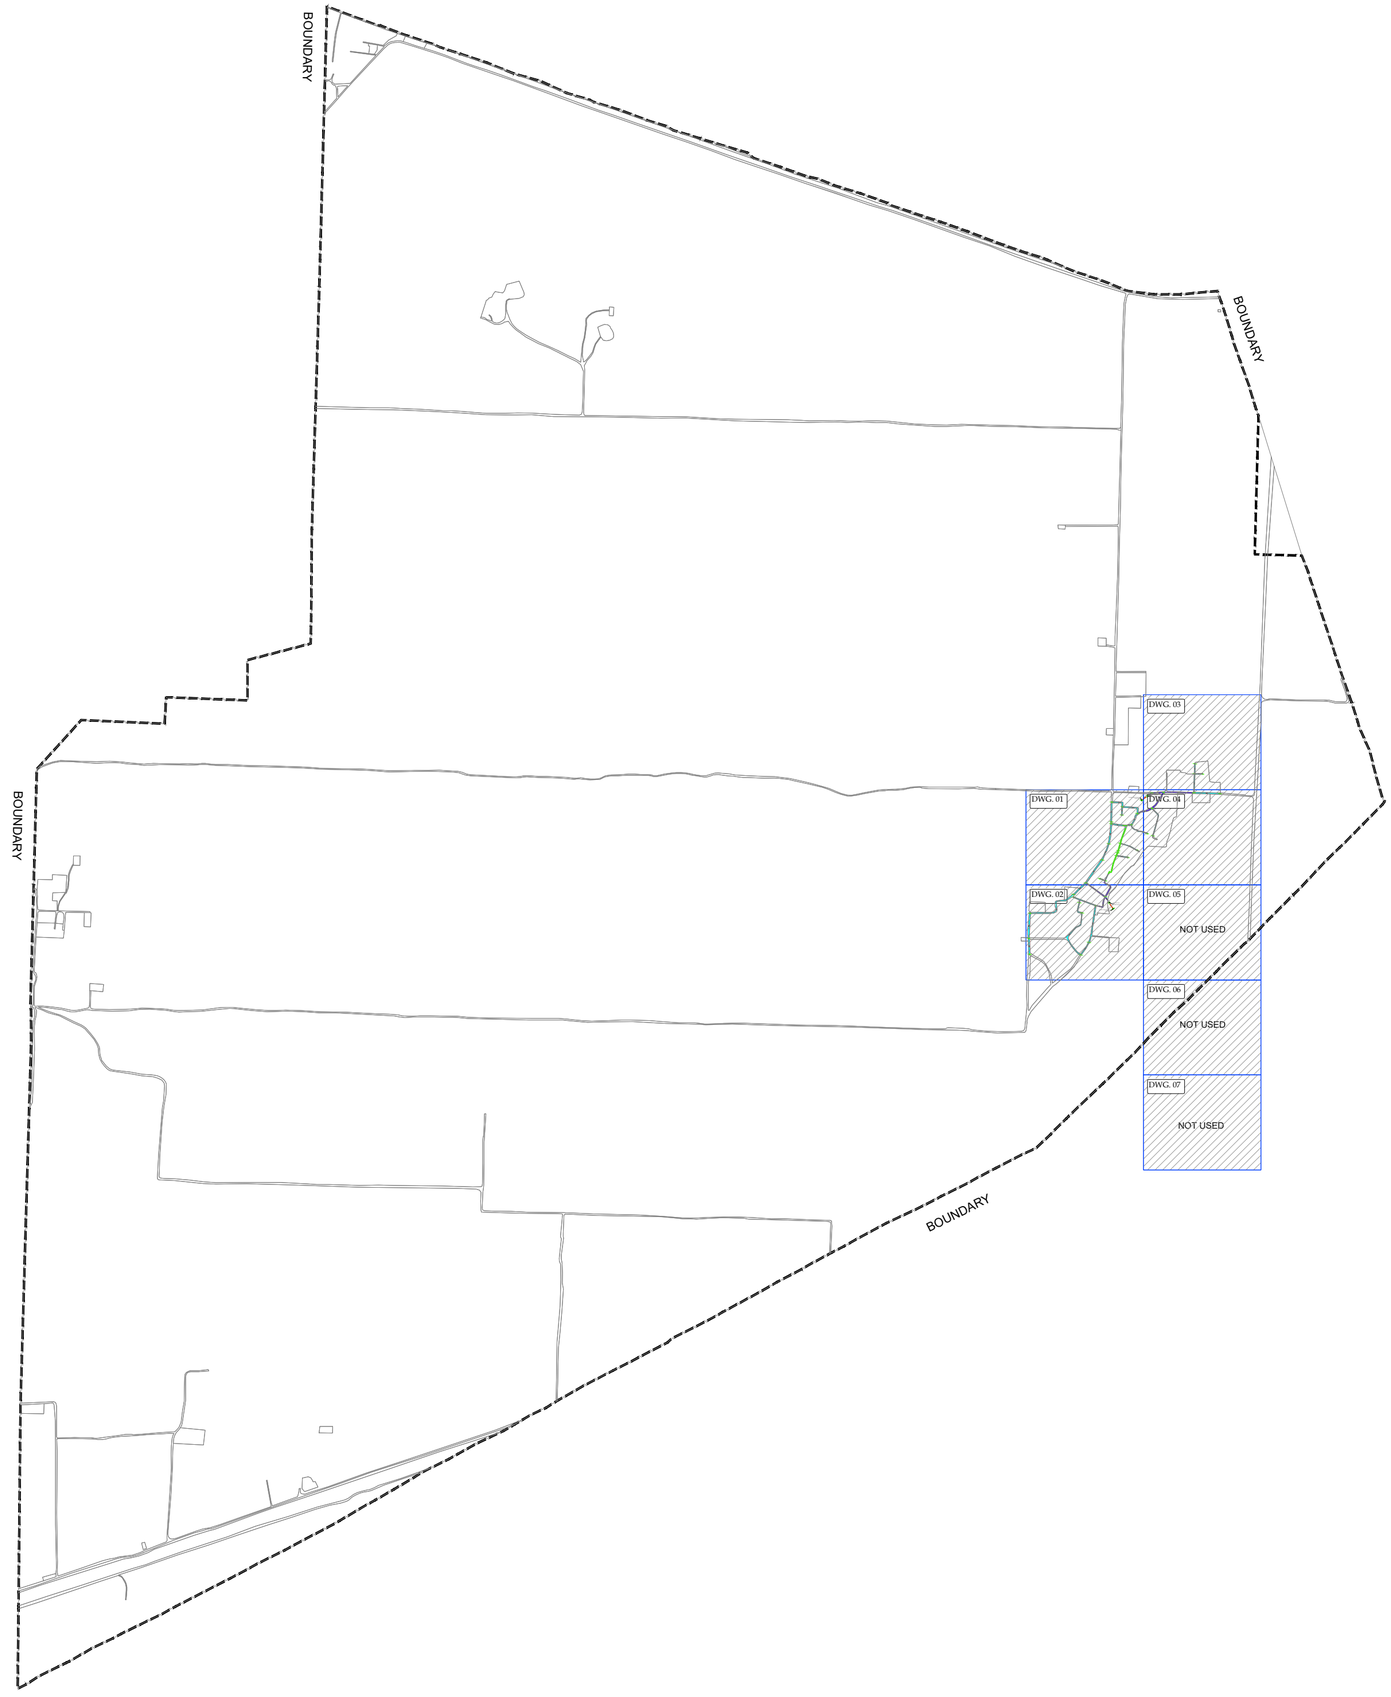

LEGEND:

- DRAIN TYPE - I
- SULLAGE CARRIER
- Ø3" HDPE PIPE
- EXISTING SOLING
- BOUNDARY

VILLAGE: DHANRAJPURA (BWN)

TITLE.

DRAINAGE SYSTEM KEY PLAN

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 900'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	16-12-2025	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02	19-04-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-DHP-SEW-KP-00	00 OF 00	01

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT
ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

PRMSC-BWN-DHP-SEW-KP-00

LAYOUT PLAN

Revenue Village: Dhanraj Pura Sheet-1

District:	Bahawalnagar
Tehsil:	Bahawalnagar
Revenue Village:	Dhanraj Pura

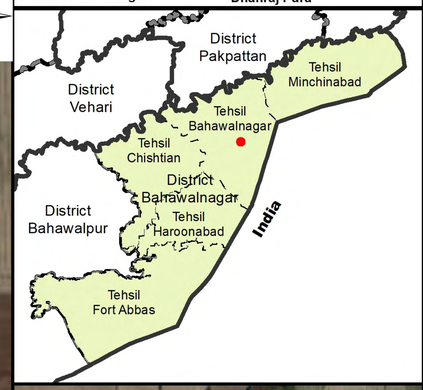

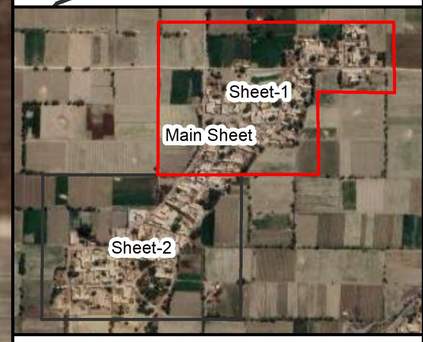

SEPTIC TANK-T1
Plot Size=1.59 Marla
GL=542.19
IL=539.76

ND-14 GL=542.61 IL=541.78
ND-16 GL=544.27 IL=541.61
ND-15 GL=543.5 IL=542.47
ND-18 GL=542.94 IL=541.3
ND-17 GL=543.36 IL=542.52
ND-19 GL=543.94 IL=540.23
ND-40 GL=540.69 IL=539.86
ND-8 GL=543.41 IL=542.58
ND-10 GL=543.86 IL=542.34
ND-9 GL=545.19 IL=543.29
ND-11 GL=544.56 IL=542
ND-13 GL=545.2 IL=541.75
ND-7 GL=544.49 IL=543.22
ND-30 GL=545.2 IL=544.33
ND-4 GL=545.75 IL=544.92
ND-29 GL=545.63 IL=544.79
ND-6 GL=545.84 IL=544.15
ND-5 GL=546.4 IL=545.57
ND-12 GL=545.78 IL=544.95
ND-31 GL=544.51 IL=543.68
ND-3 GL=547.21 IL=545.53
ND-1 GL=547 IL=545.17
ND-35 GL=550.77 IL=549.94
ND-2 GL=552.21 IL=551.38
ND-34 GL=547.57 IL=546.74
ND-32 GL=544.67 IL=543.39
ND-38 GL=548.49 IL=548.35
ND-37 GL=546.66 IL=545.57
ND-33 GL=545.93 IL=541.78
ND-36 GL=546.22 IL=543.63

Title:
Proposed Drainage Network Plan

Legend:

- NODE
- 3" HDPE PIPE
- DRAIN TYPE-1
- SULLAGE CARRIER
- SEPTIC TANK
- SETTLEMENT BOUNDARY

Drain Type 1=5055 Rft
Sullage Carrier= 2080 Rft

Scale: 1:1,200
1 inch = 100 feet
Paper Size: A3

0 40 80 160
Kilometers

Project:
Engineering Design & Construction Supervision, Punjab Rural Sustainable Water Supply & Sanitation Project, Cluster South III

ENVIRONMENTAL TECHNOLOGIES
ASIAN CONSULTING ENGINEERS www.asiancon.com

Revenue Village: Dhanraj Pura Sheet-2

District:	Bahawalnagar
Tehsil:	Bahawalnagar
Revenue Village:	Dhanraj Pura

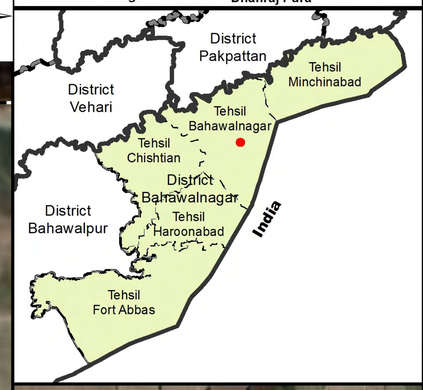

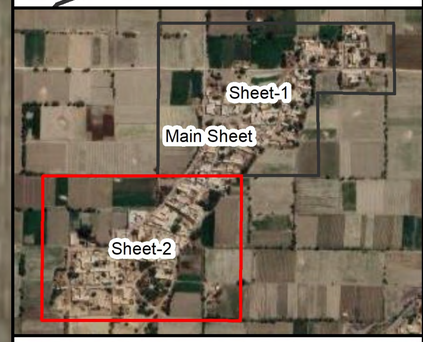

ND-36 GL=548.49 IL=546.39
ND-32 GL=544.67 IL=543.39
ND-37 GL=548.66 IL=545.57
ND-38 GL=546.22 IL=543.63
ND-33 GL=543.93 IL=541.78
ND-28 GL=545.99 IL=542.05
ND-23 GL=546.96 IL=545.84
Dhani Molapurwali
ND-39 GL=543.8 IL=541.4
GL=544.08 IL=541.30
SEPTIC TANK-T2 Plot Size=2 Marla
ND-41 GL=550.41 IL=549.58
ND-24 GL=545.9 IL=543.55
ND-20 GL=550.43 IL=549.36
ND-27 GL=543.79 IL=542.96
ND-26 GL=546.61 IL=543.78
ND-25 GL=549.8 IL=548.3
ND-22 GL=546.35 IL=545.52
ND-21 GL=548 IL=546.02
3" HDPE ULTIMATE DISPOSAL TO WATER COURSE

Title:
Proposed Drainage Network Plan

Legend:

- SETTLEMENT
- NODE
- 3"HDPE PIPE
- DRAIN TYPE-1
- SULLAGE CARRIER
- SEPTIC TANK
- SETTLEMENT BOUNDARY

Drain Type 1=5055 Rft
Sullage Carrier= 2080 Rft

Scale: 1:1,000
1 inch = 83 feet
Paper Size: A3

0 40 80 160
Kilometers

Project:
Engineering Design & Construction Supervision, Punjab Rural Sustainable Water Supply & Sanitation Project, Cluster South III

PRWSC
ENVIRONMENTAL TECHNOLOGIES
ASIAN CONSULTING ENGINEERS www.asiancon.com

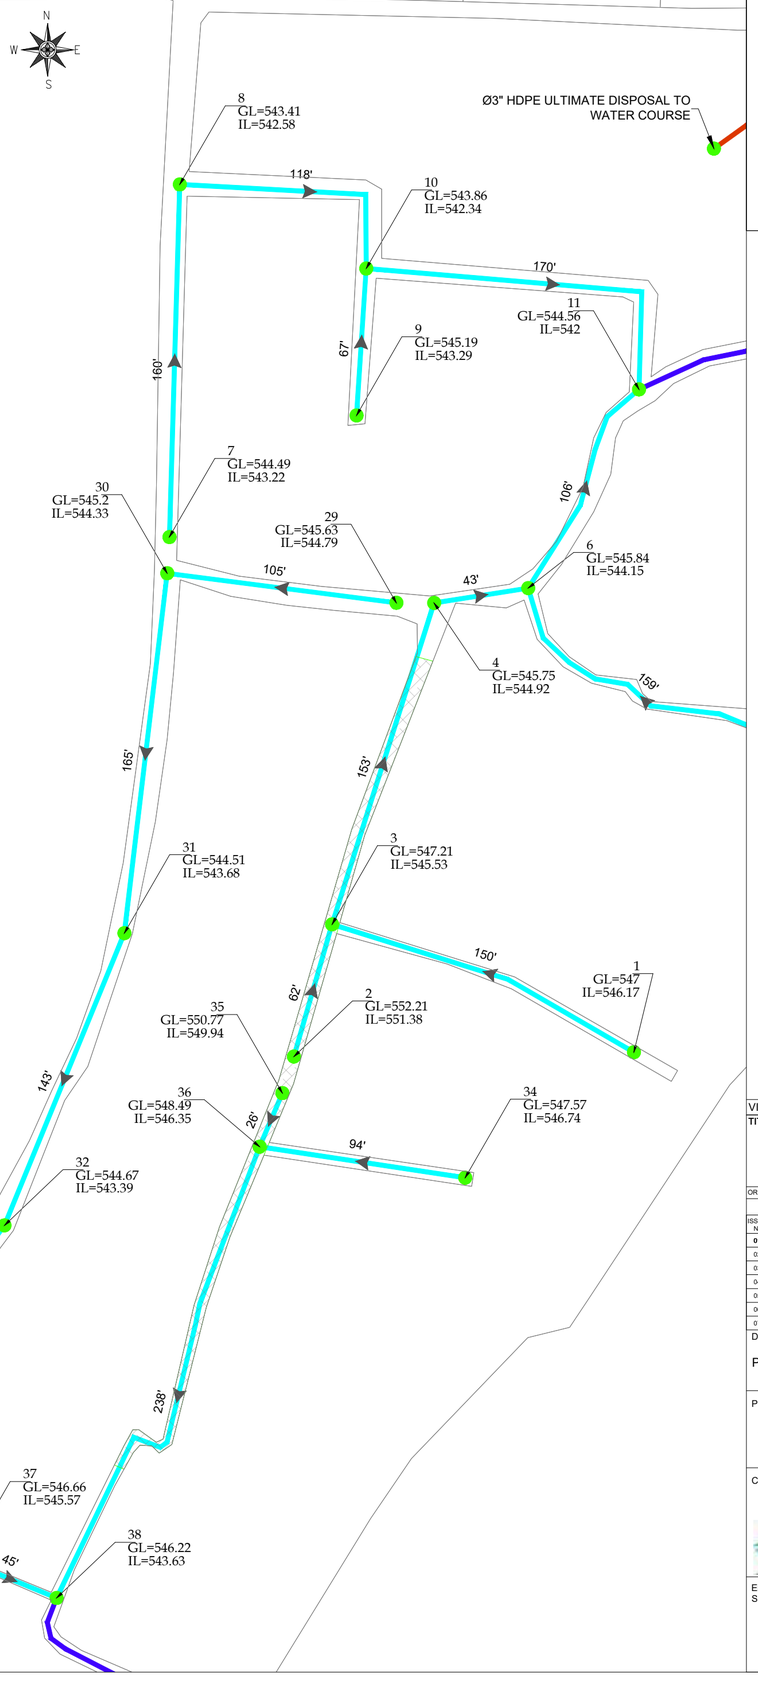

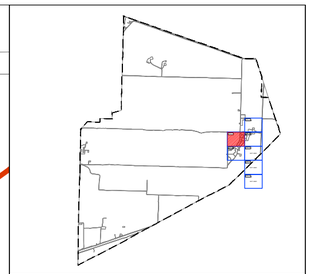

KEY PLAN

LEGEND:

- DRAIN TYPE - I
- SULLAGE CARRIER
- Ø3" HDPE PIPE
- EXISTING SOLING
- BOUNDARY

VILLAGE: DHANRAJPURA (BWN)

TITLE.

DRAINAGE SYSTEM LAYOUT PLAN-01

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	16-12-2025	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02	19-04-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-DHP-SEW-LP-01	01 OF 07	01

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

PRMSC-BWN-DHP-SEW-LP-01

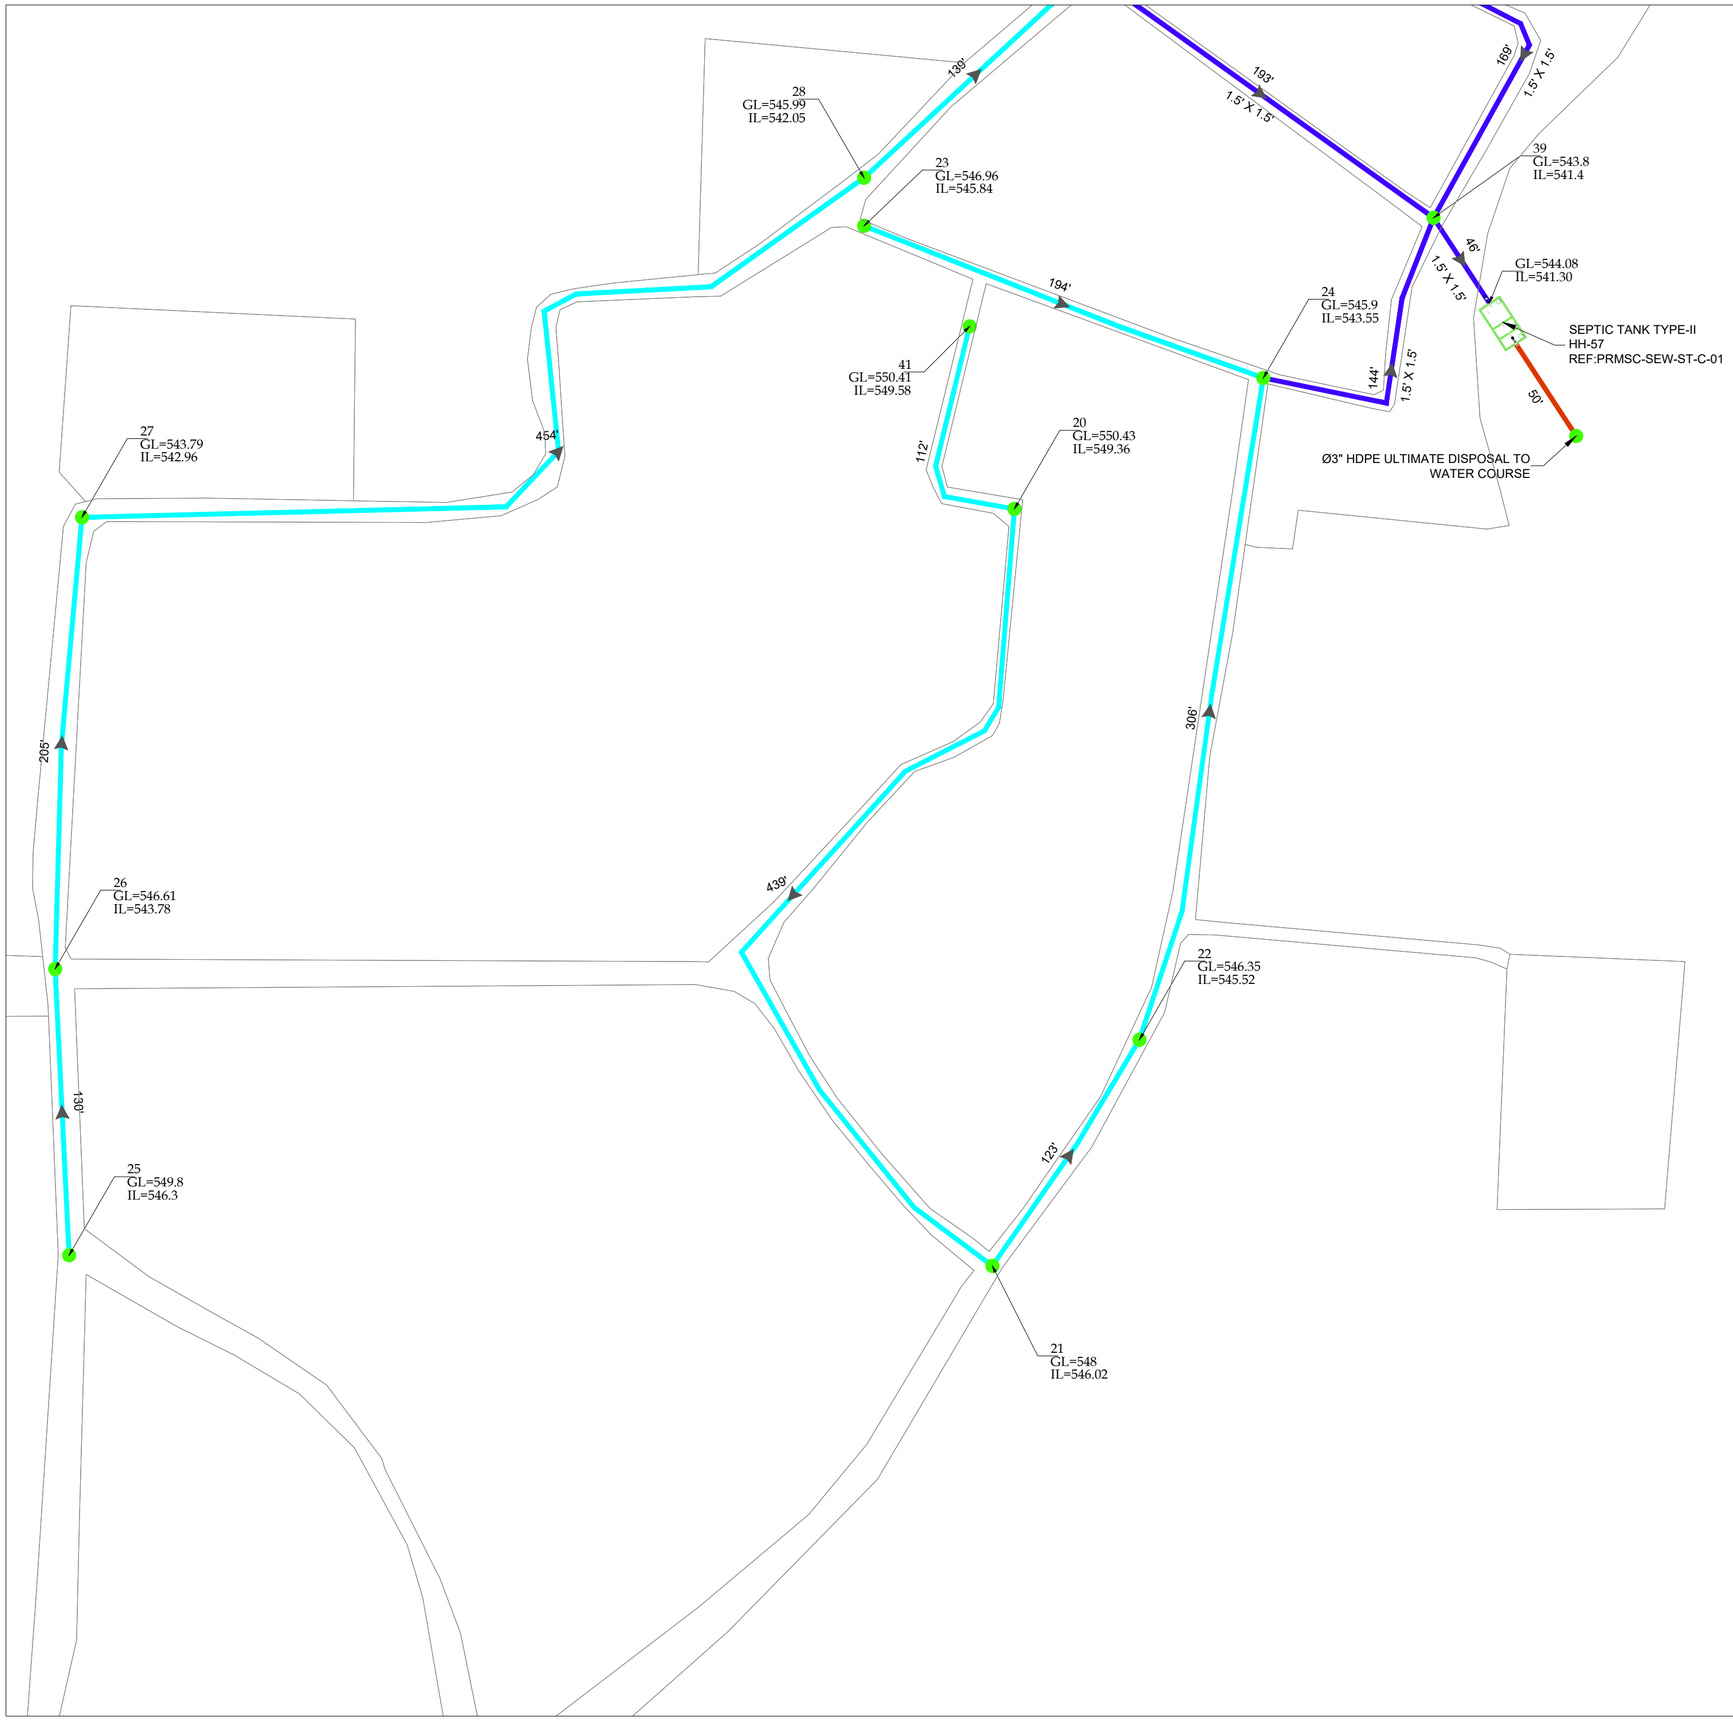

PRMSC-BWN-DHP-SEW-LP-02

KEY PLAN

LEGEND:

- DRAIN TYPE - I
- SULLAGE CARRIER
- Ø3" HDPE PIPE
- EXISTING SOLING
- BOUNDARY

VILLAGE: DHANRAJPURA (BWN)

TITLE.

DRAINAGE SYSTEM LAYOUT PLAN-02

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	16-12-2025	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02	19-04-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
03					
04					
05					
06					
07					

DRAWING N°:	SHEET	REV
PRMSC-BWN-DHP-SEW-LP-02	02 OF 07	01

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS JV
www.asianconjv.com

KEY PLAN

LEGEND:

DRAIN TYPE - I

SULLAGE CARRIER

Ø3" HDPE PIPE

EXISTING SOLING

BOUNDARY

VILLAGE: DHANRAJPURA (BWN)

TITLE.

DRAINAGE SYSTEM LAYOUT PLAN-03

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	16-12-2025	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02	19-04-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-DHP-SEW-LP-03	03 OF 07	01

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

PRMSC-BWN-DHP-SEW-LP-03

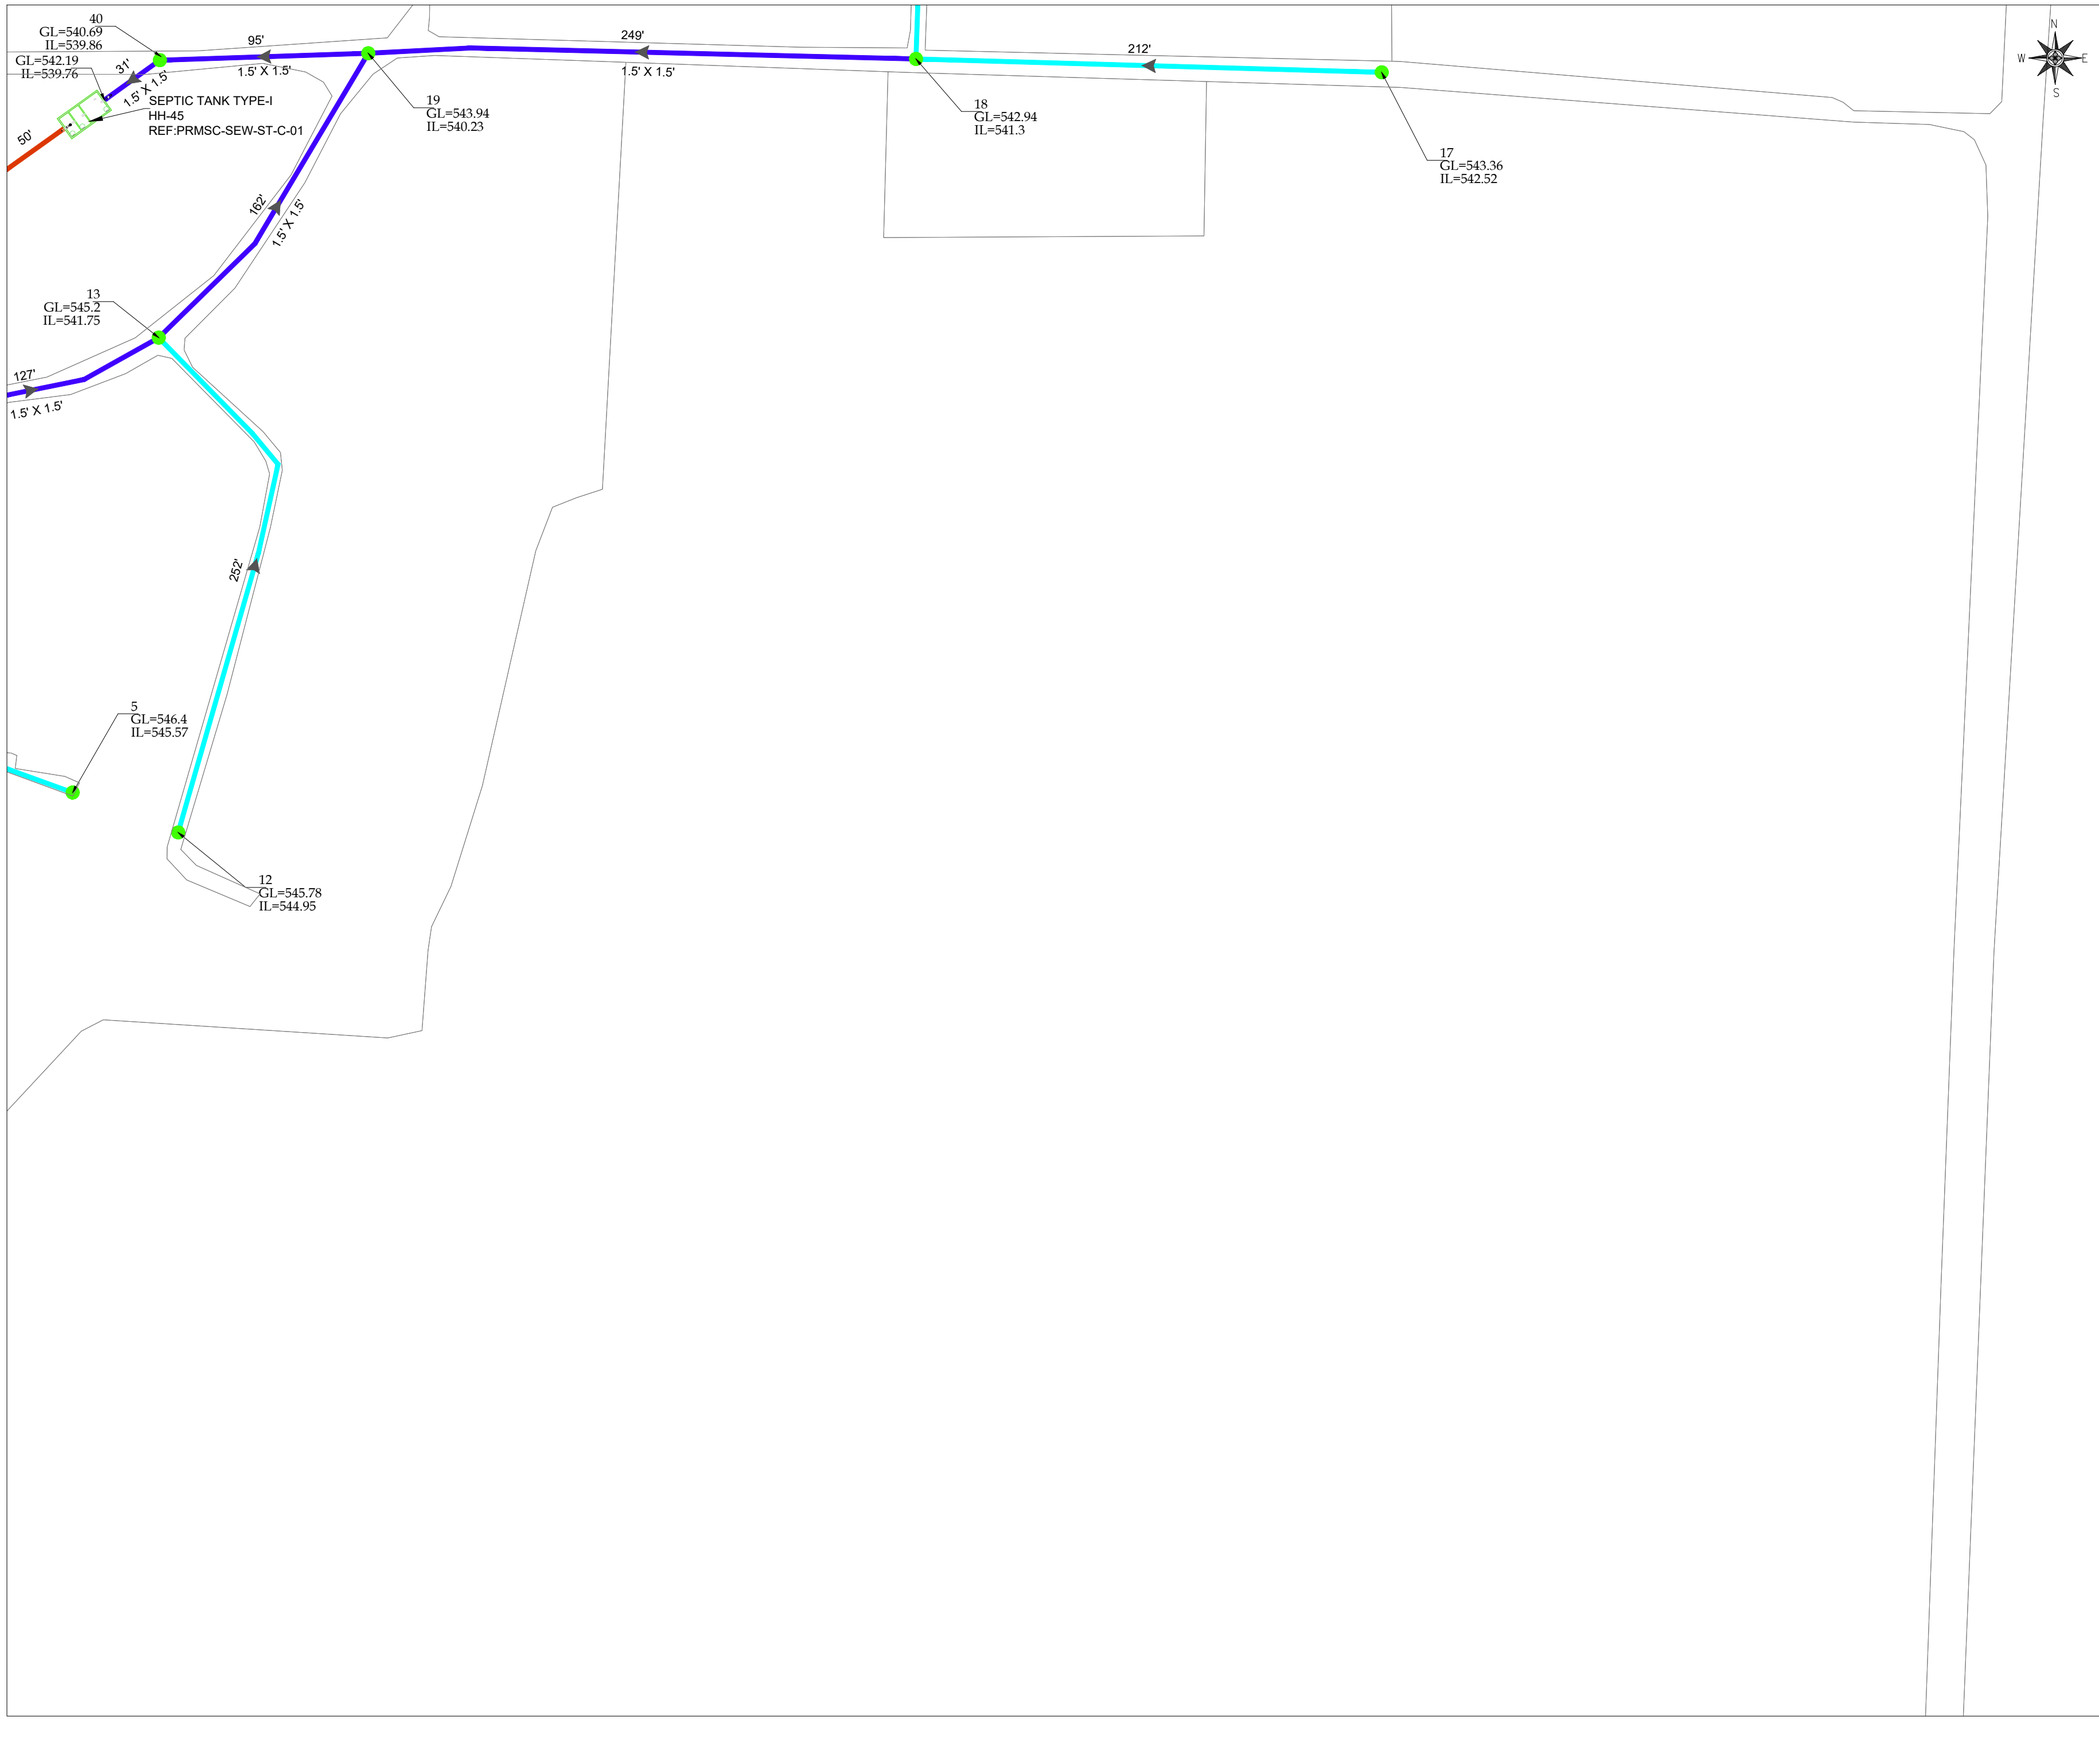

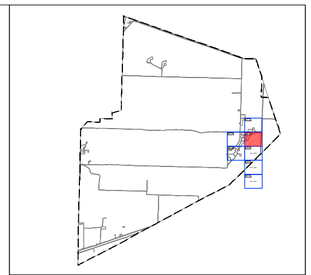

KEY PLAN

LEGEND:

- DRAIN TYPE - I
- SULLAGE CARRIER
- Ø3" HDPE PIPE
- EXISTING SOLING
- BOUNDARY

VILLAGE: DHANRAJPURA (BWN)

TITLE.

DRAINAGE SYSTEM LAYOUT PLAN-04

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	16-12-2025	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02	19-04-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-DHP-SEW-LP-04	04 OF 07	01

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS
www.asiacon.com.pk

PRMSC-BWN-DHP-SEW-LP-04

HYDRAULIC STATEMENT

Node		Length	Slope	Elevation Ground	Elevation Ground	Elevation Invert	Elevation Invert	Depth
FROM	TO	ft	ft/ft	U/S	D/S	U/S	D/S	ft
1	3	150	0.002	547	547.21	546.17	545.87	0.83
2	3	62	0.094	552.21	547.21	551.38	545.53	0.83
3	4	153	0.004	547.21	545.75	545.53	544.92	1.67
4	6	43	0.002	545.75	545.84	544.92	544.83	0.83
5	6	159	0.004	546.4	545.84	545.57	545.01	0.83
6	11	106	0.004	545.84	544.56	544.15	543.72	1.7
7	8	160	0.004	544.49	543.41	543.22	542.58	1.27
8	10	118	0.002	543.41	543.86	542.58	542.34	0.83
9	10	67	0.004	545.19	543.86	543.29	543.03	1.9
10	11	170	0.002	543.86	544.56	542.34	542	1.52
11	13	127	0.002	544.56	545.2	542	541.75	2.56
12	13	252	0.002	545.78	545.2	544.95	544.36	0.83
13	19	162	0.002	545.2	543.94	541.75	541.42	3.45
14	16	83	0.002	542.61	544.27	541.78	541.61	0.83
15	16	63	0.002	543.3	544.27	542.47	542.34	0.83
16	18	155	0.002	544.27	542.94	541.61	541.3	2.66
17	18	212	0.002	543.36	542.94	542.52	542.1	0.83
18	19	249	0.002	542.94	543.94	541.3	540.81	1.64
19	40	94	0.004	543.94	540.69	540.23	539.86	3.7
40	ST-TYPE-I-NO SP	49	0.002	540.69	542.19	539.76	539.86	1.08
41	20	112	0.002	550.41	550.43	549.36	549.58	1.98
20	21	439	0.008	550.43	548	546.02	549.36	0.83
21	22	123	0.004	548	546.35	546.02	545.52	1.12
22	24	306	0.002	546.35	545.9	545.52	544.91	2.35
23	24	194	0.004	546.96	545.9	545.84	545.06	3.5
24	39	144	0.004	545.9	543.8	543.55	542.97	2.83
25	26	130	0.004	549.8	546.61	546.3	545.78	0.83
26	27	205	0.004	546.61	543.79	543.78	542.96	3.94
27	28	454	0.002	543.79	545.99	542.96	542.05	0.84
28	33	139	0.002	545.99	543.93	542.05	541.78	0.87
29	30	105	0.004	545.63	545.2	544.79	544.37	0.83
30	31	165	0.004	545.2	544.51	544.33	543.68	1.28
31	32	143	0.002	544.51	544.67	543.68	543.39	2.15
32	33	229	0.002	544.67	543.93	543.39	542.93	0.83
33	39	193	0.002	543.93	543.8	541.78	541.4	0.83
34	36	94	0.002	547.57	548.49	546.74	546.55	2.14
35	36	26	0.086	550.77	548.49	549.94	547.66	1.09
36	38	238	0.004	548.49	546.22	546.35	545.39	2.59
37	38	45	0.004	546.66	546.22	545.57	545.39	2.4
38	39	169	0.004	546.22	543.8	543.63	542.97	0.83
39	ST-TYPE-II-NO SP	46	0.002	543.8	544.08	541.4	541.3	0.83

VILLAGE: DHANRAJPURA (BWN)

TITLE:

HYDRAULIC STATEMENT

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	16-12-2025	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. HSAN-UL-HAQ
02	19-04-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. HSAN-UL-HAQ
03					
04					
05					
06					
07					

DRAWING Nº: PRMSC-KPT-GA-SEW-HS-01

SHEET 01 OF 01

REV 01

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER CENTRAL

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS www.asiancon.com.pk

PRMSC-KPT-HS-SEW-HS-01

HASAN RAIKA

KEY PLAN

Revenue Village: Hasan Raika Main Sheet

N

District:	Bahawalnagar
Tehsil:	Bahawalnagar
Revenue Village:	Hasan Raika

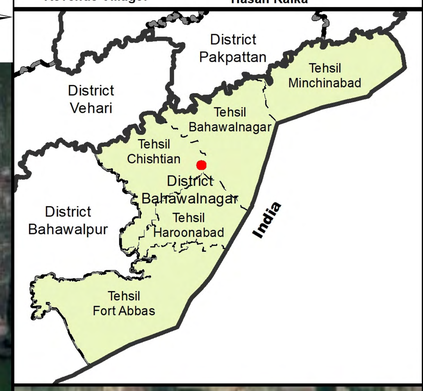

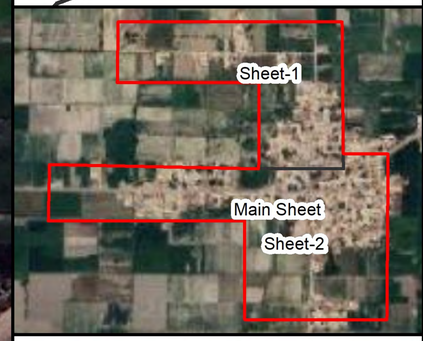

Title:
Proposed Drainage Network Plan

Legend:

- SETTLEMENT
- NODE
- 3" HDPE PIPE
- DRAIN TYPE-1
- SULLAGE CARRIER
- SEPTIC TANK
- SETTLEMENT BOUNDARY

Drain Type 1=6443 Rft

Sullage Carrier= 4423 Rft

Scale: 1:2,300

1 inch = 192 feet

Paper Size: A3

0 40 80 160

Kilometers

Project:

Engineering Design & Construction Supervision, Punjab Rural Sustainable Water Supply & Sanitation Project, Cluster South III

PRWSC

ENVIRONMENTAL TECHNOLOGIES

ASIAN CONSULTING ENGINEERS www.asiancon.com

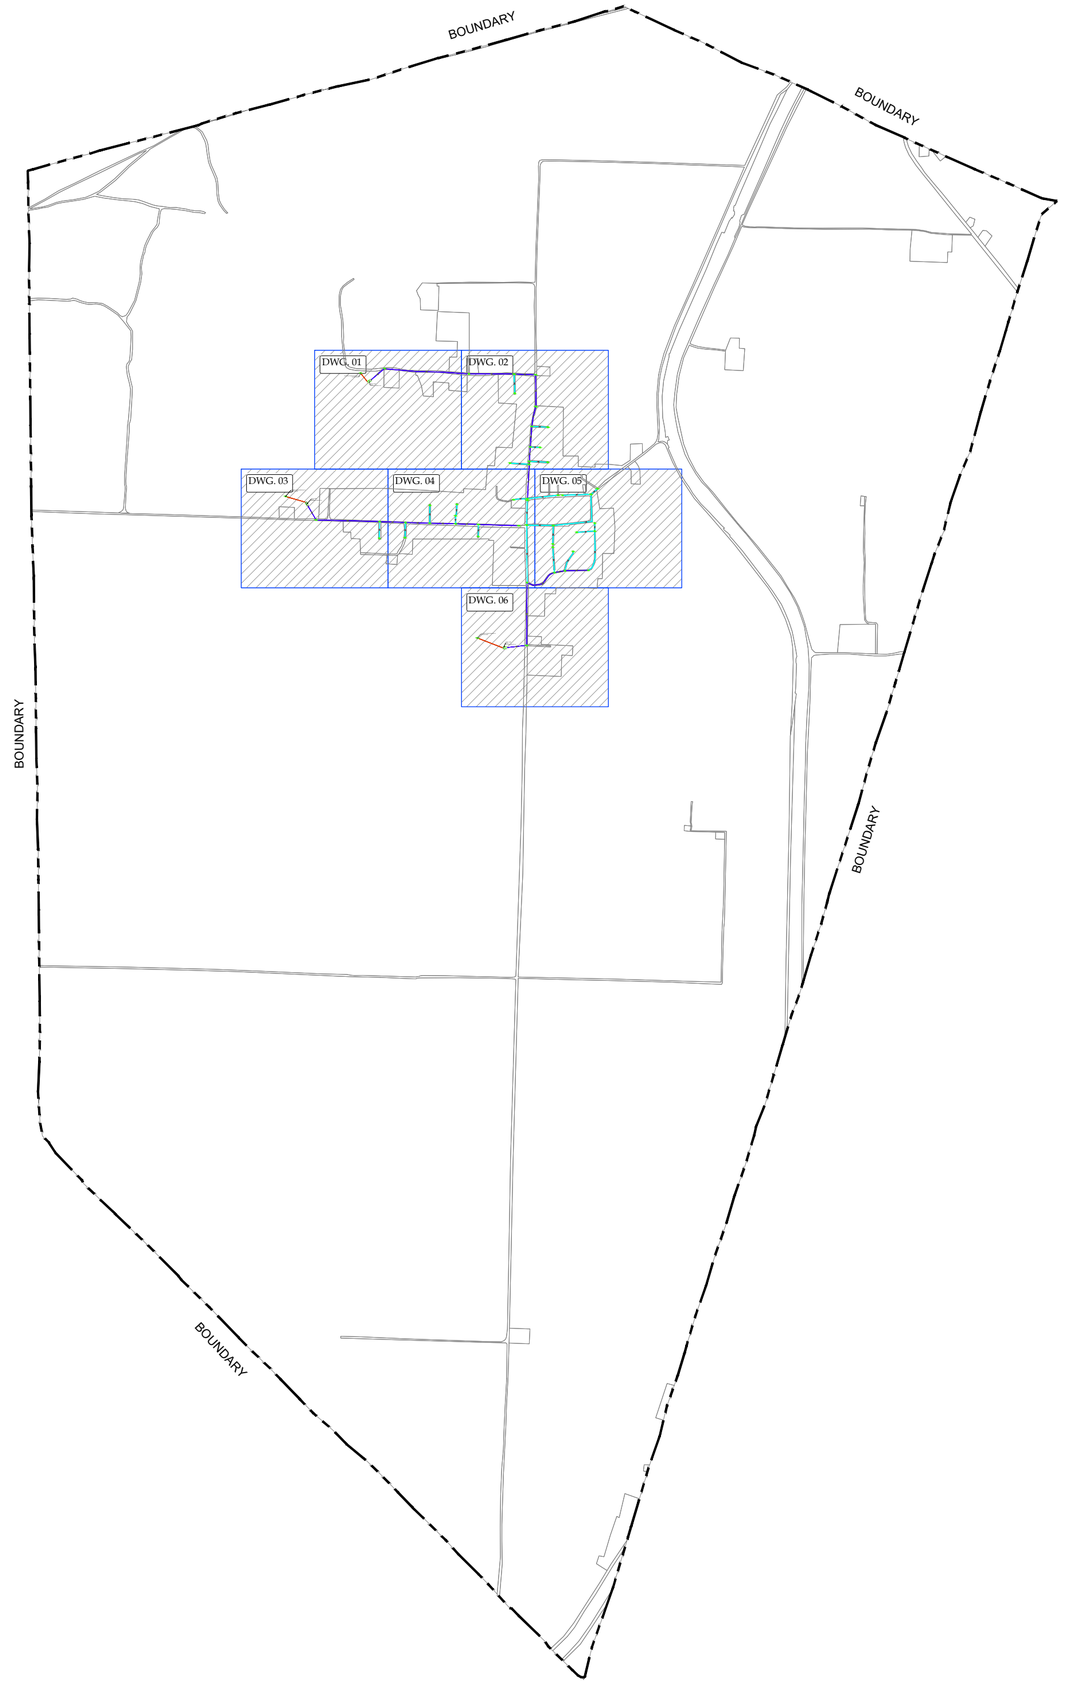

N
W
E
S

LEGEND:

- DRAIN TYPE - I
- SULLAGE CARRIER
- Ø3" HDPE PIPE
- BOUNDARY

VILLAGE: HASAN RAEKA (BWN)

TITLE.

DRAINAGE SYSTEM KEY PLAN

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 720'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	16-12-2025	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02	20-04-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
03					
04					
05					
06					
07					

DRAWING Nº: PRMSC-BWN-HRK-SEW-KP-00

SHEET 00 OF 00

REV 01

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT
ASIAN CONSULTING ENGINEERS
www.asiancon.com

PRMSC-BWN-HRK-SEW-KP-00

LAYOUT PLAN

Revenue Village: Hasan Raika Sheet-1

District:	Bahawalnagar
Tehsil:	Bahawalnagar
Revenue Village:	Hasan Raika



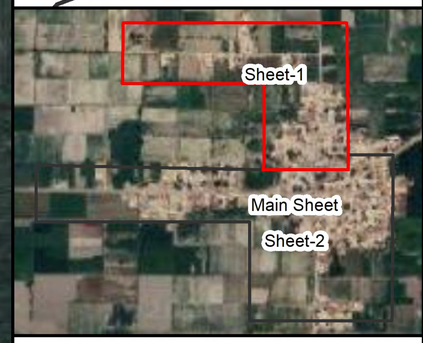

Title:
Proposed Drainage Network Plan

Legend:

- SETTLEMENT
- NODE
- 3" HDPE PIPE
- DRAIN TYPE-1
- SULLAGE CARRIER
- SEPTIC TANK
- SETTLEMENT BOUNDARY

Drain Type 1=6443 Rft

Sullage Carrier= 4423 Rft

Scale: 1:1,500
1 inch = 125 feet
Paper Size: A3

0 40 80 160
Kilometers

Project:

Engineering Design & Construction Supervision, Punjab Rural Sustainable Water Supply & Sanitation Project, Cluster South III

PRMSC

ENVIRONMENTAL TECHNOLOGIES

ASIAN CONSULTING ENGINEERS www.asiancon.com

Revenue Village: Hasan Raika Sheet-2

District:	Bahawalnagar
Tehsil:	Bahawalnagar
Revenue Village:	Hasan Raika

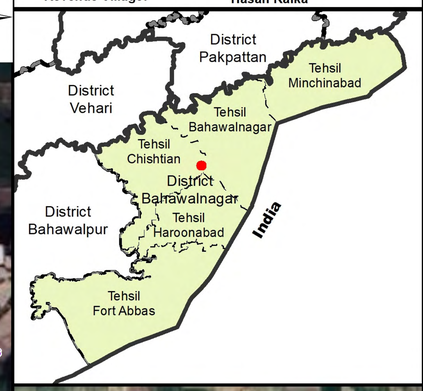

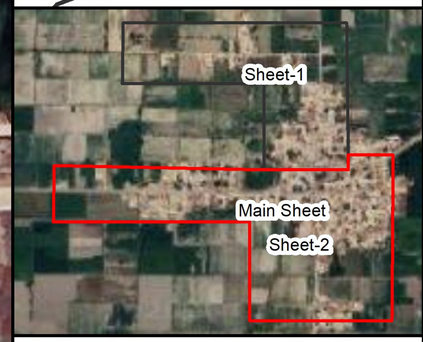

GL=507.07
IL=504.92

SEPTIC TANK-T2
Plot Size=2 Marla

FIRM RR ULTIMATE DISPOSAL TO WATER COURSE

ND-9 GL=507.21 IL=505.03
ND-8 GL=511.4 IL=508.7
ND-7 GL=509.64 IL=508.81
ND-6 GL=512.89 IL=509.35
ND-44 GL=510.29 IL=509.45
ND-30 GL=512.38 IL=511.4
ND-5 GL=512.11 IL=510.99
ND-31 GL=512.16 IL=511.29
ND-4 GL=512.05 IL=511.21
ND-3 GL=512.14 IL=511.16
ND-2 GL=512.38 IL=511.55
ND-46 GL=512.93 IL=511.45
ND-1 GL=514.79 IL=512.36
ND-35 GL=518.48 IL=515.64
ND-39 GL=513.47 IL=512.64
ND-25 GL=513.85 IL=512.09
ND-38 GL=514.89 IL=513.8
ND-24 GL=514.37 IL=513.15
ND-36 GL=513.39 IL=514.56
ND-23 GL=516.35 IL=513.63
ND-37 GL=518.75 IL=515.92
ND-22 GL=516.52 IL=513.93
ND-21 GL=517.92 IL=515.35
ND-20 GL=517 IL=516.16
ND-11 GL=515.23 IL=514.4
ND-10 GL=515.37 IL=514.12
ND-43 GL=516.81 IL=515.98
ND-47 GL=517.82 IL=516.99
Gadoki
ND-34 GL=515.84 IL=515.01
ND-42 GL=517.25 IL=513.69
ND-41 GL=516.57 IL=515.74
ND-15 GL=515.18 IL=514.11
ND-13 GL=515.83 IL=512.19
ND-45 GL=517.46 IL=516.54
ND-18 GL=517.37 IL=516.54
ND-42 GL=515.71 IL=514.87
ND-16 GL=514.87 IL=513.84
ND-33 GL=514.15 IL=512.03
ND-47 GL=514.73 IL=513.89
ND-14 GL=512.65 IL=510.32

GL=509.35
IL=508.52

ND-19 GL=510.74 IL=508.65

SEPTIC TANK-T2
Plot Size=2 Marla

Title:
Proposed Drainage Network Plan

Legend:

- SETTLEMENT
- NODE
- 3" HDPE PIPE
- DRAIN TYPE-1
- SULLAGE CARRIER
- SEPTIC TANK
- SETTLEMENT BOUNDARY

Drain Type 1=6443 Rft
Sullage Carrier= 4423 Rft

Scale: 1:2,200
1 inch = 183 feet
Paper Size: A3

0 40 80 160
Kilometers

Project:
Engineering Design & Construction Supervision, Punjab Rural Sustainable Water Supply & Sanitation Project, Cluster South III

PRWSC
ENVIRONMENTAL TECHNOLOGIES
ASIAN CONSULTING ENGINEERS
www.asiancon.com

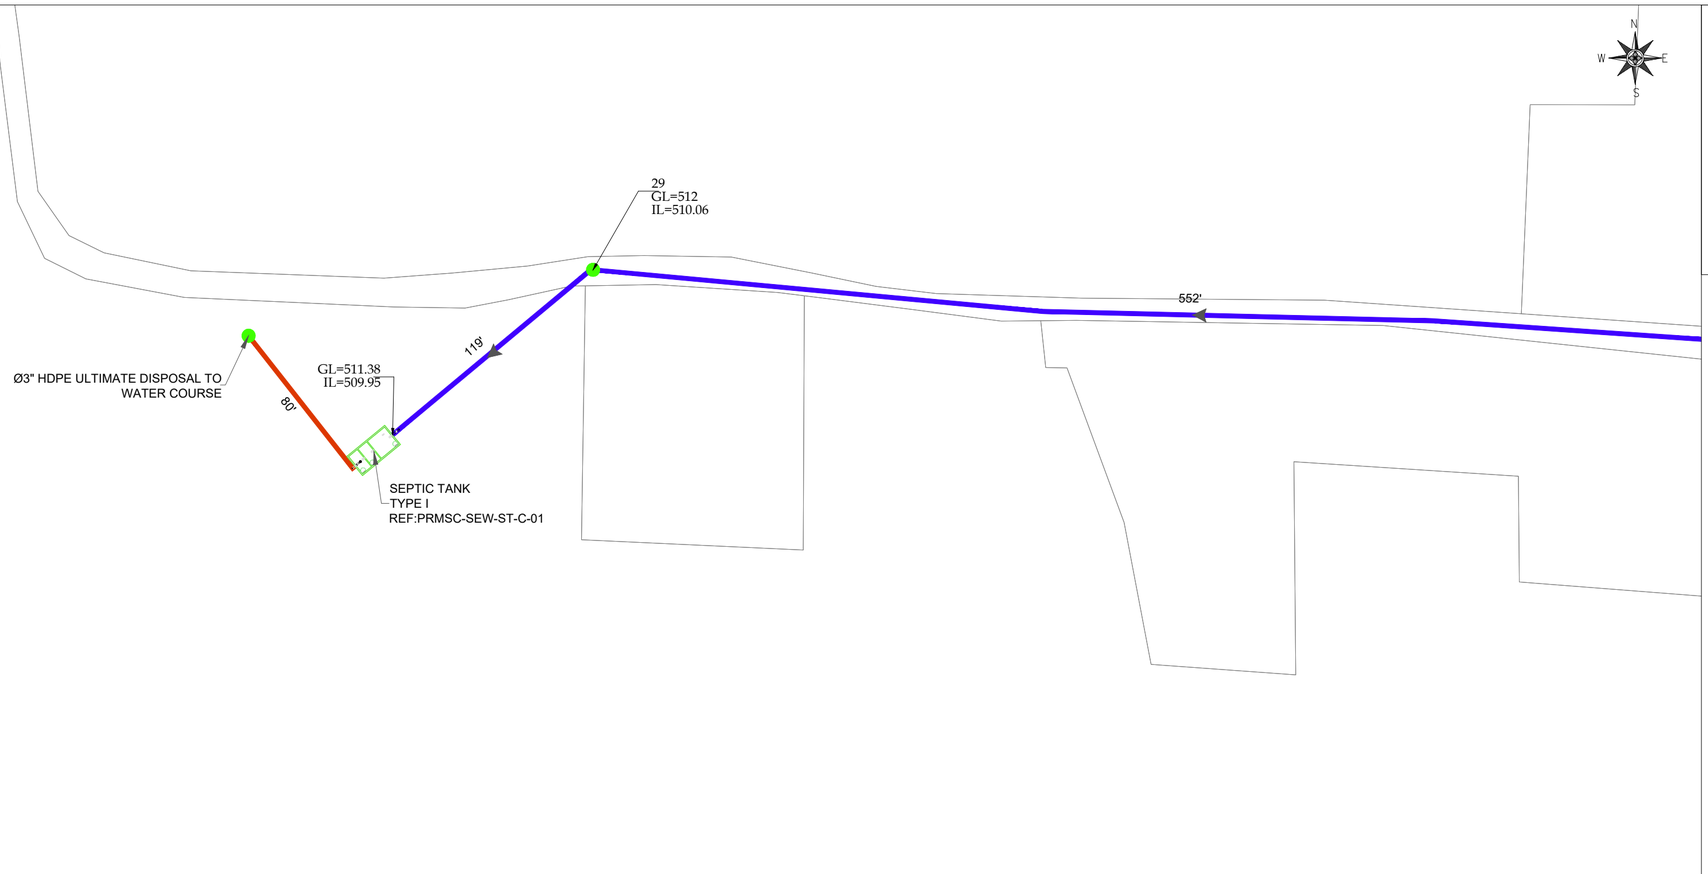



KEY PLAN

LEGEND:

- DRAIN TYPE - I
- SULLAGE CARRIER
- Ø3" HDPE PIPE
- BOUNDARY

VILLAGE: HASAN RAEKA (BWN)

TITLE.

DRAINAGE SYSTEM LAYOUT PLAN-01

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	16-12-2025	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. HSAN-UL-HAQ
02	20-04-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. HSAN-UL-HAQ
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-HRK-SEW-LP-01	01 OF 06	01

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:
ASIAN CONSULTING ENGINEERS
www.asiacon.com.pk

PRMSC-BWN-HRK-SEW-LP-01

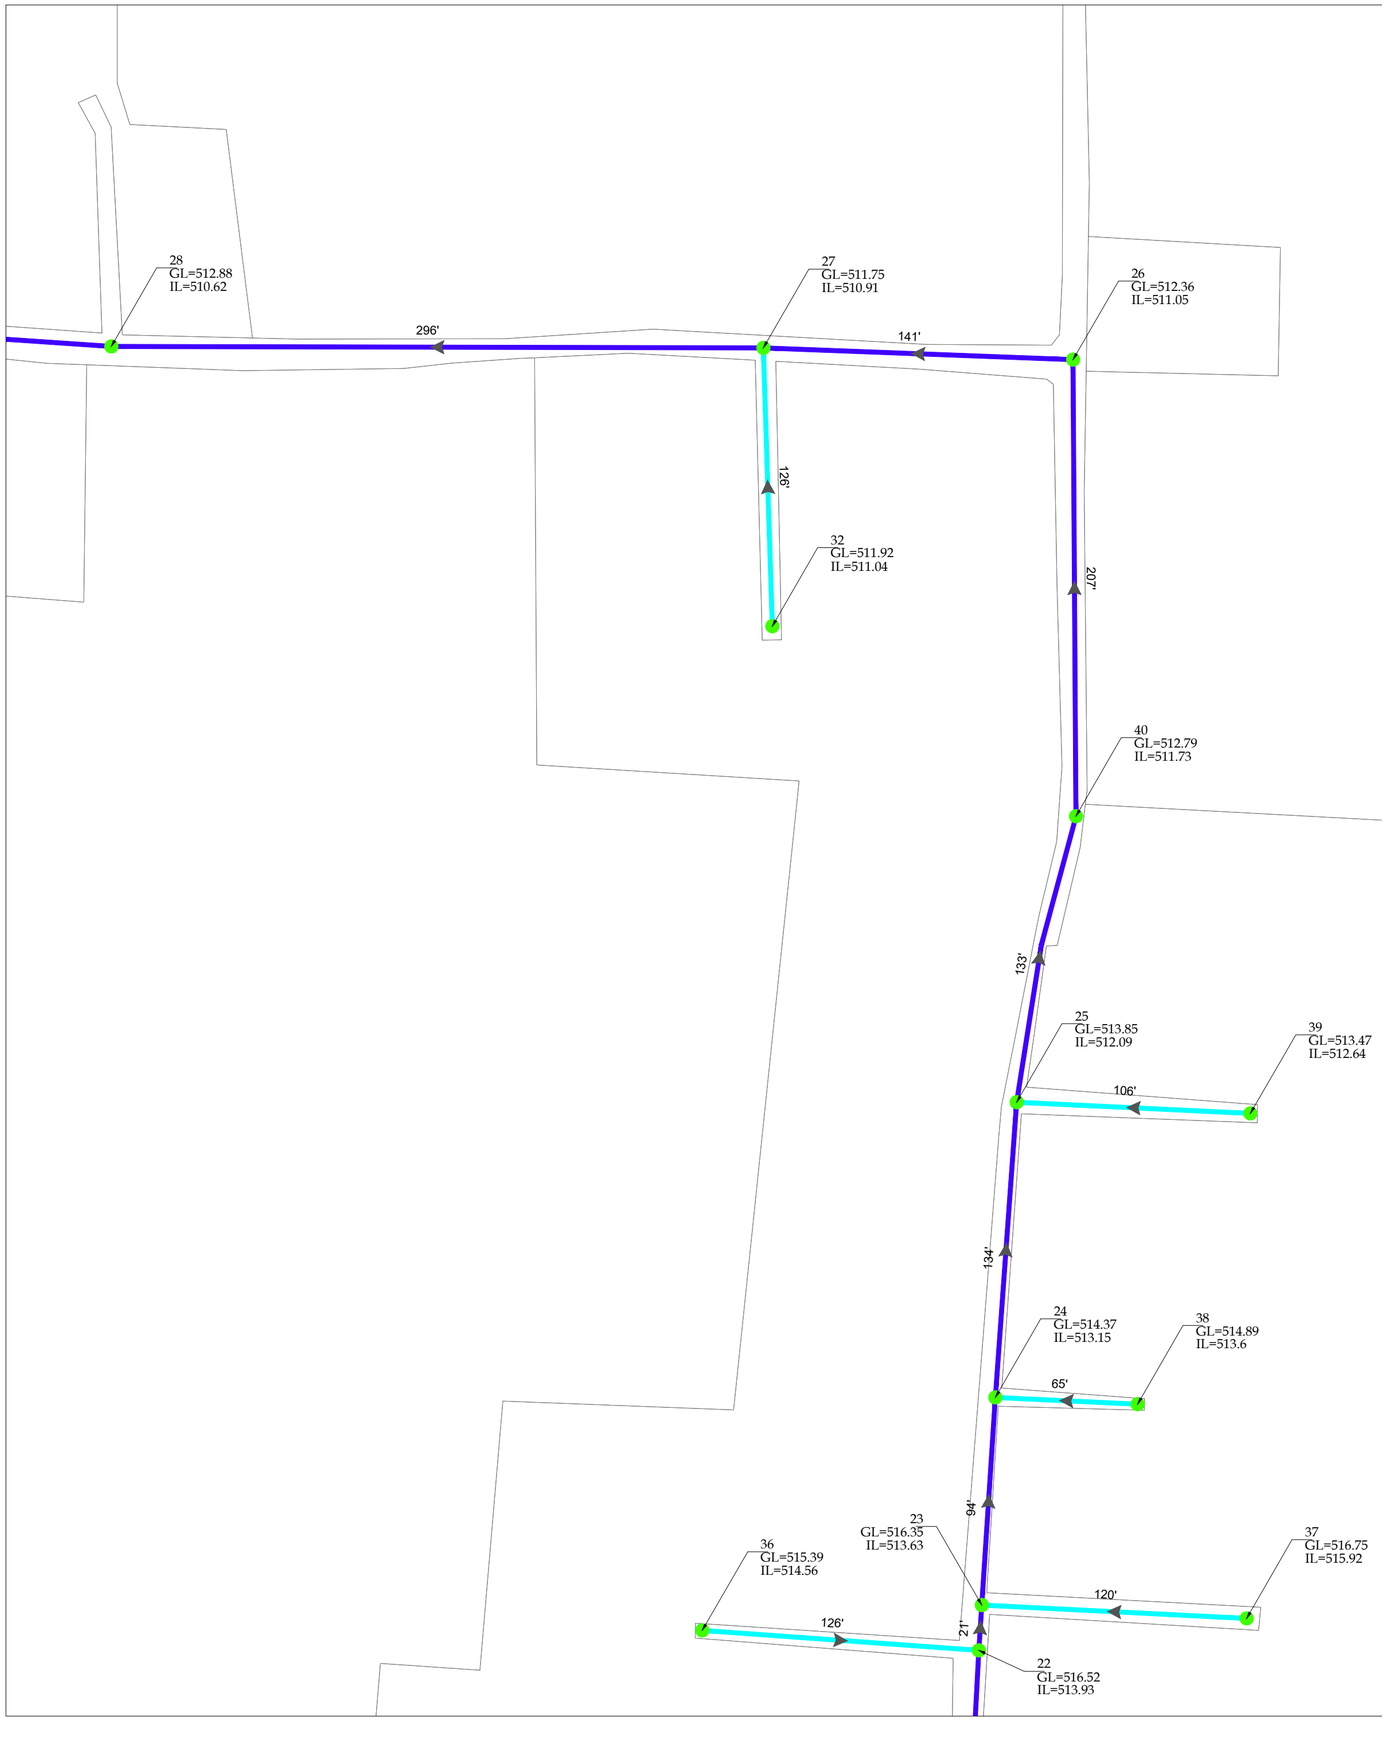

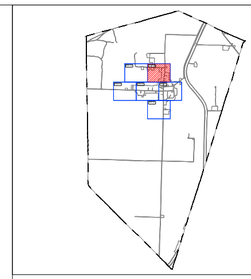

KEY PLAN

LEGEND:

- DRAIN TYPE - I
- SULLAGE CARRIER
- Ø3" HDPE PIPE
- BOUNDARY

VILLAGE: HASAN RAEKA (BWN)

TITLE.

DRAINAGE SYSTEM LAYOUT PLAN-02

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°.	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	16-12-2025	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02	20-04-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-HRK-SEW-LP-02	02 OF 06	01

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS www.asiaconsultants.com JV

PRMSC-BWN-HRK-SEW-LP-02

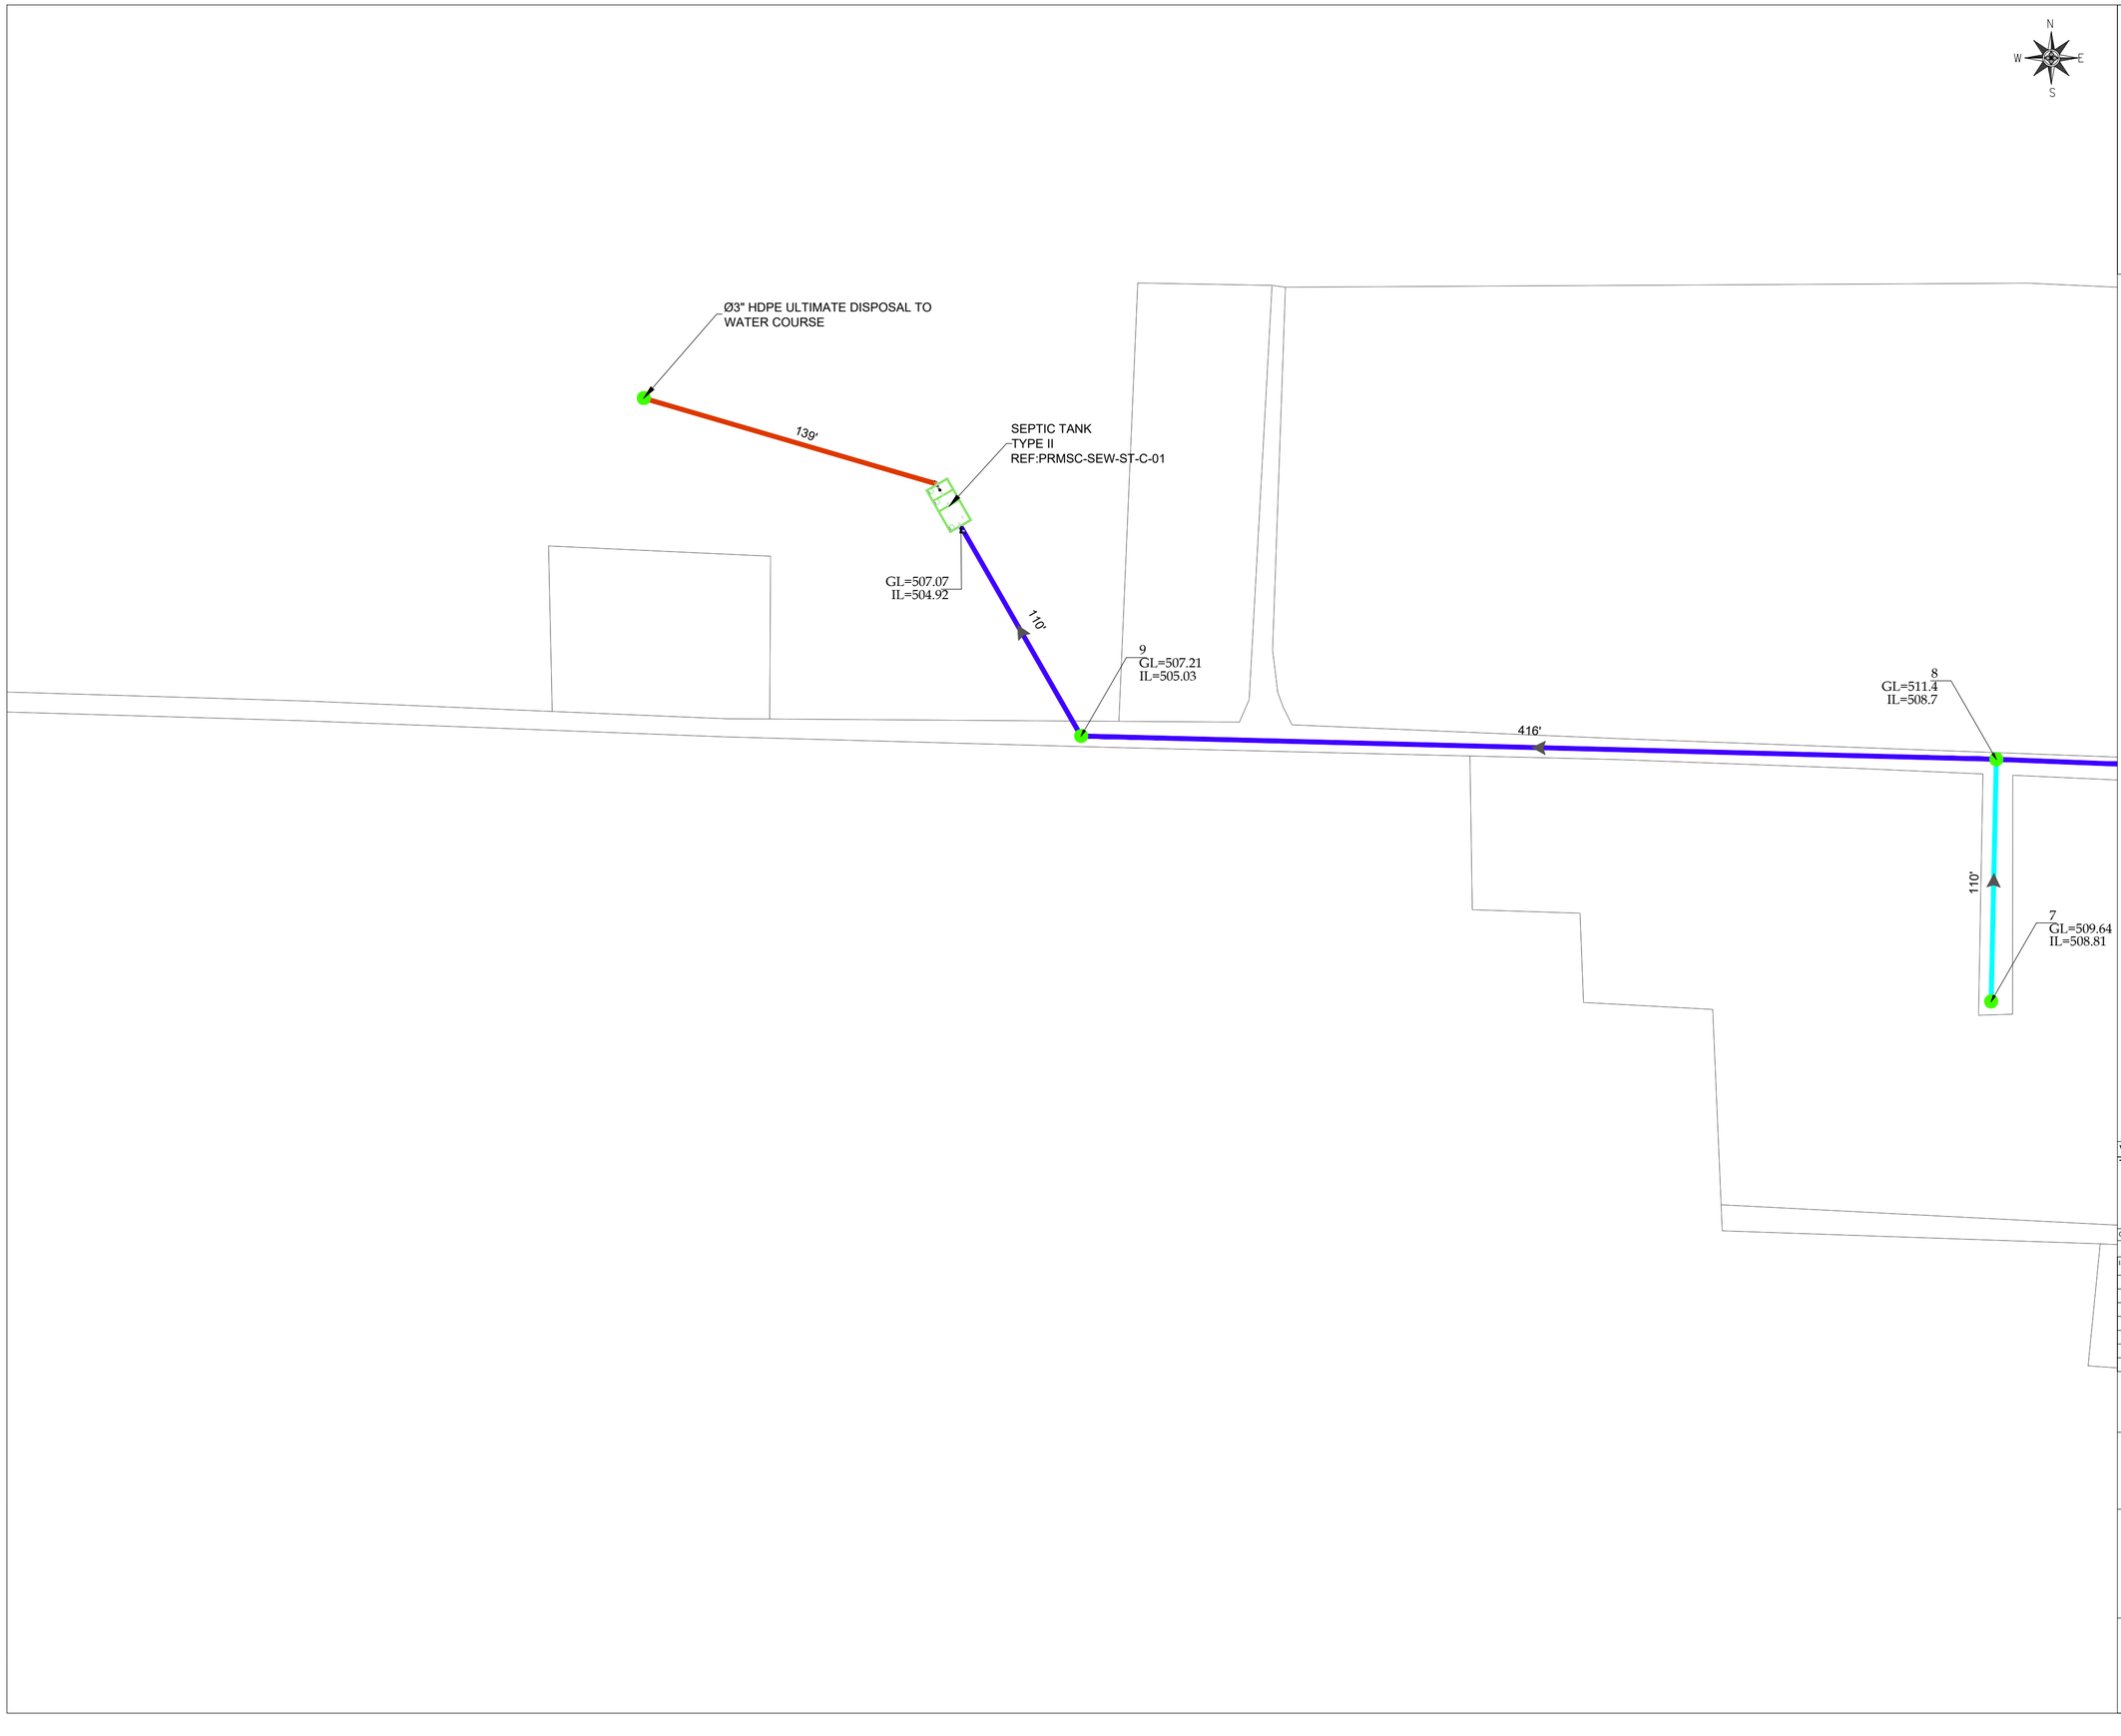



KEY PLAN

LEGEND:

- DRAIN TYPE - I
- SULLAGE CARRIER
- Ø3" HDPE PIPE
- BOUNDARY

VILLAGE: HASAN RAEKA (BWN)

TITLE.

DRAINAGE SYSTEM LAYOUT PLAN-03

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	16-12-2025	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. HSAN-UL-HAQ
02	20-04-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. HSAN-UL-HAQ
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-HRK-SEW-LP-03	03 OF 06	01

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:
ASIAN CONSULTING ENGINEERS
www.asiacon.com.pk

PRMSC-BWN-HRK-SEW-LP-03

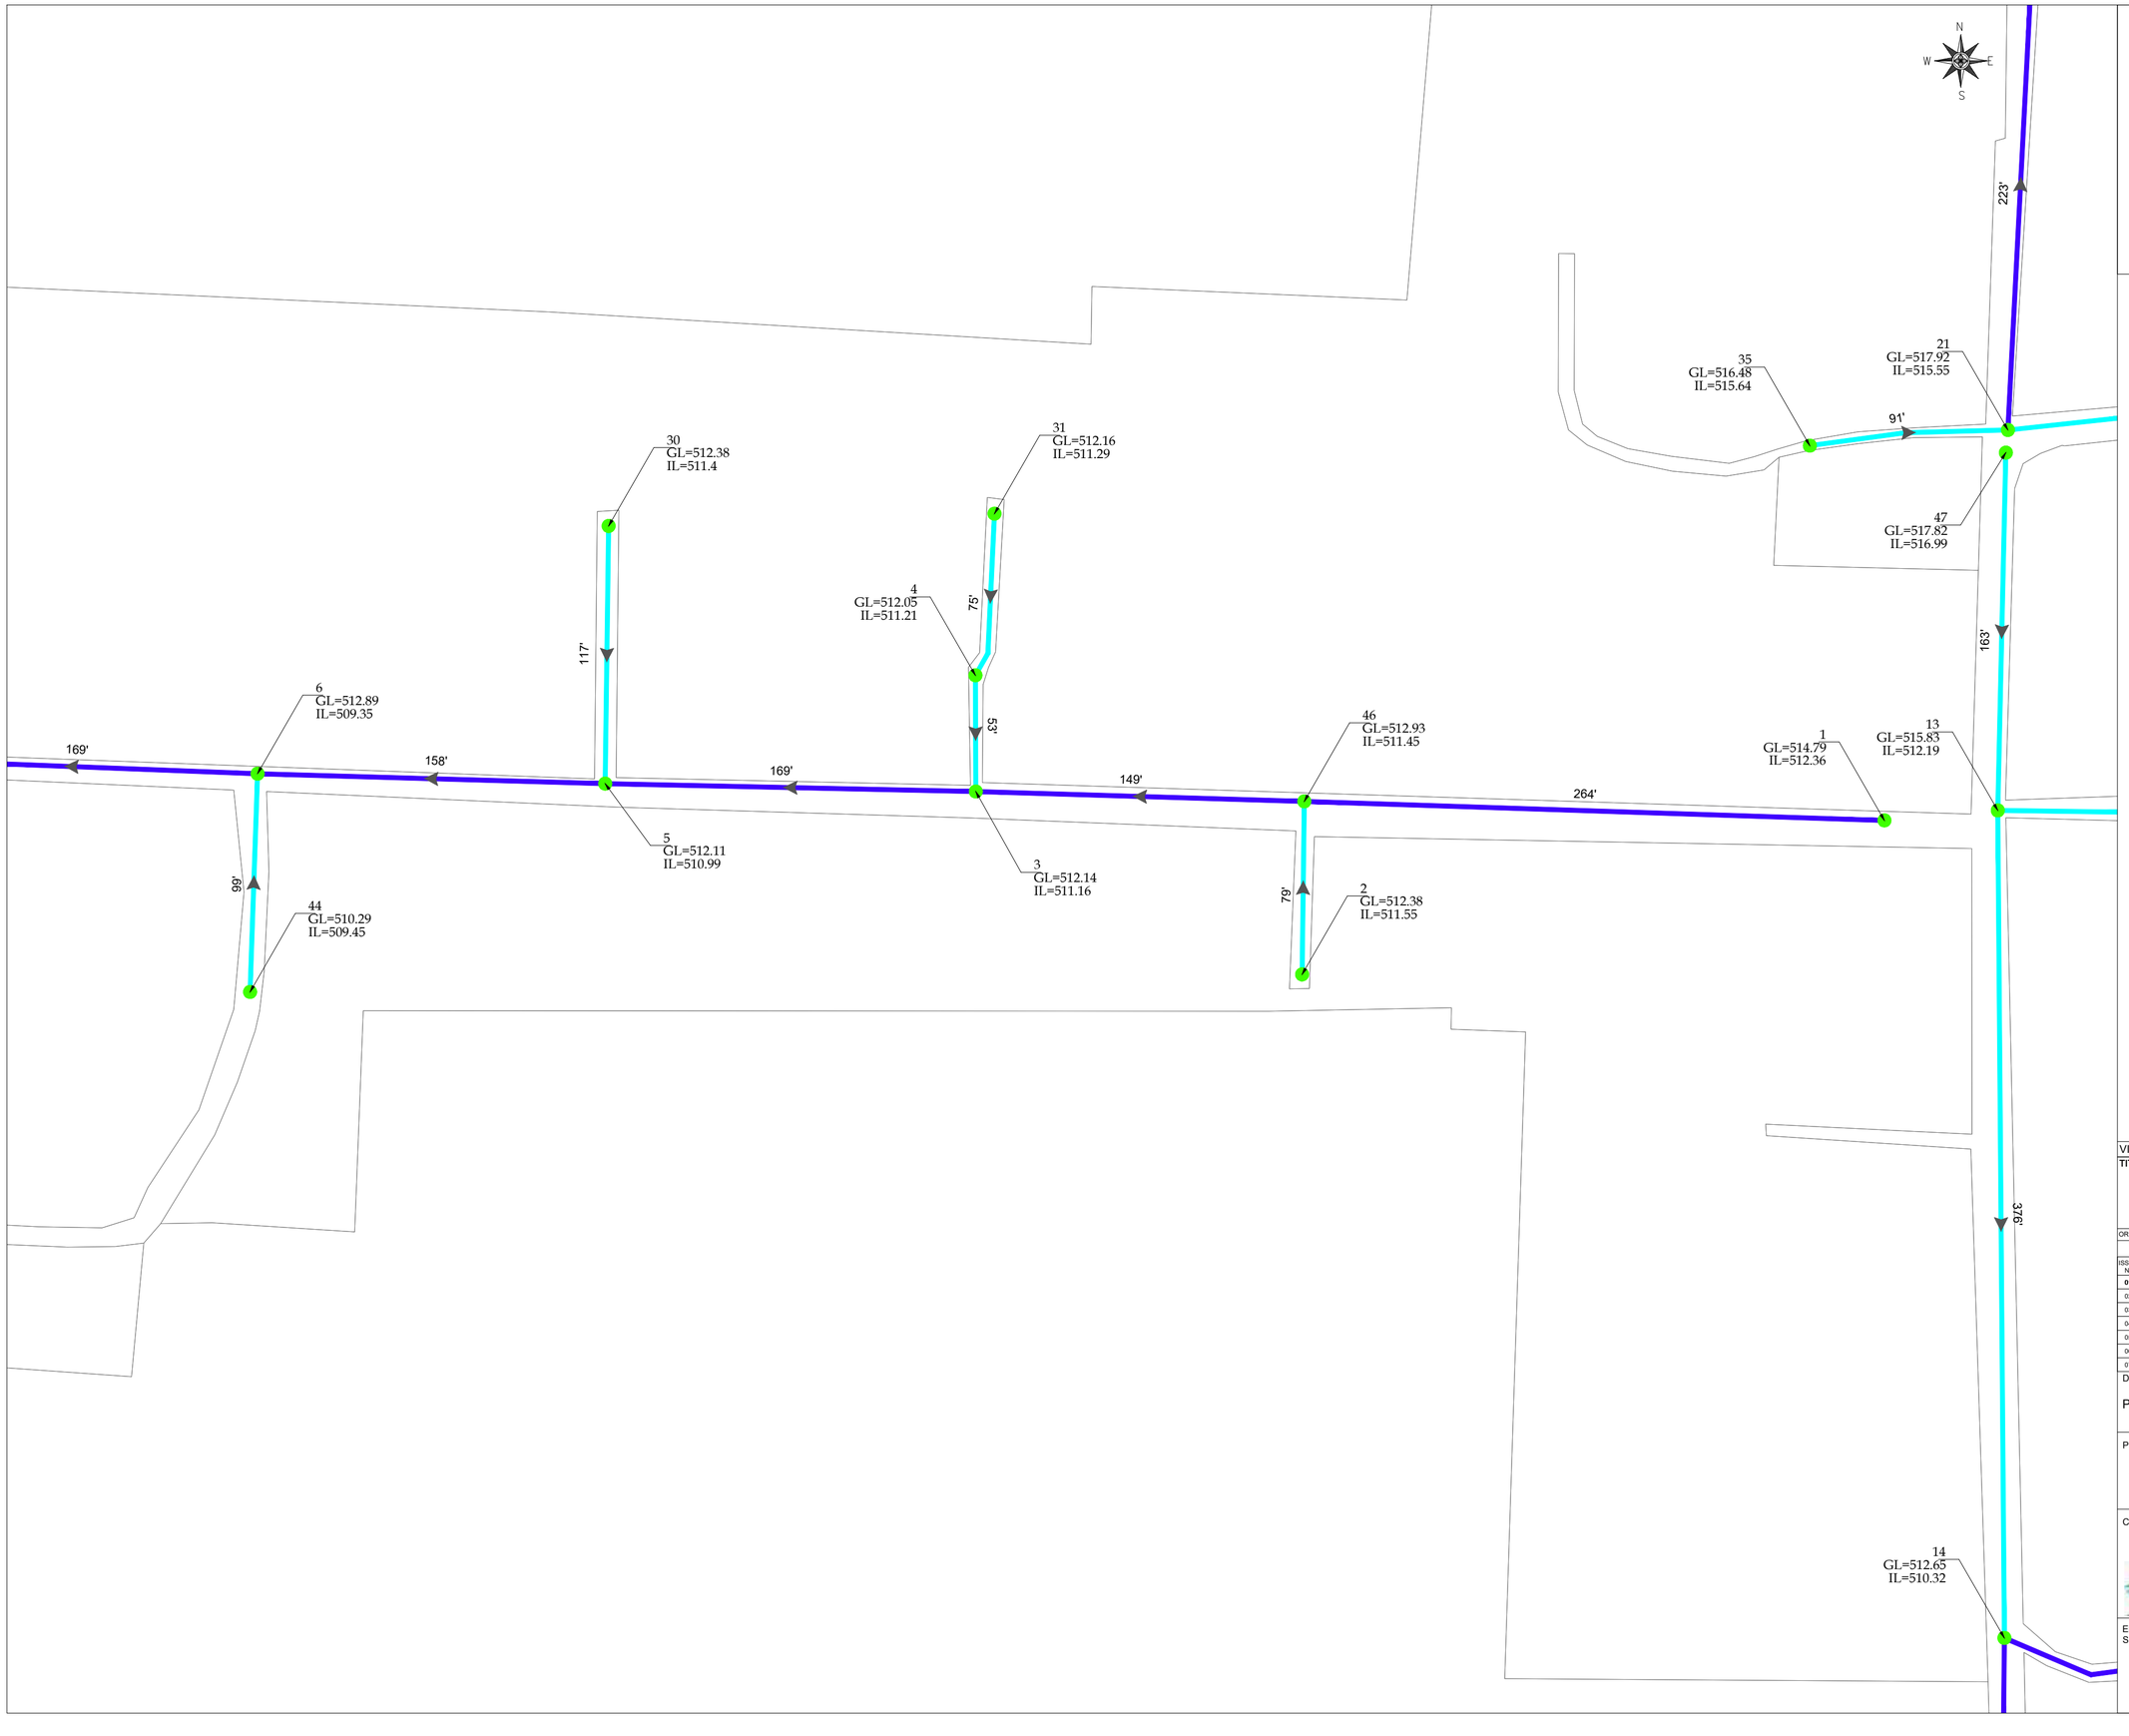

KEY PLAN

LEGEND:

- DRAIN TYPE - I
- SULLAGE CARRIER
- Ø3" HDPE PIPE
- BOUNDARY

VILLAGE: HASAN RAEKA (BWN)

TITLE.

DRAINAGE SYSTEM LAYOUT PLAN-04

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	16-12-2025	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02	20-04-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-HRK-SEW-LP-04	04 OF 06	01

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:
ASIAN CONSULTING ENGINEERS
www.asiacon.com.pv

PRMSC-BWN-HRK-SEW-LP-04

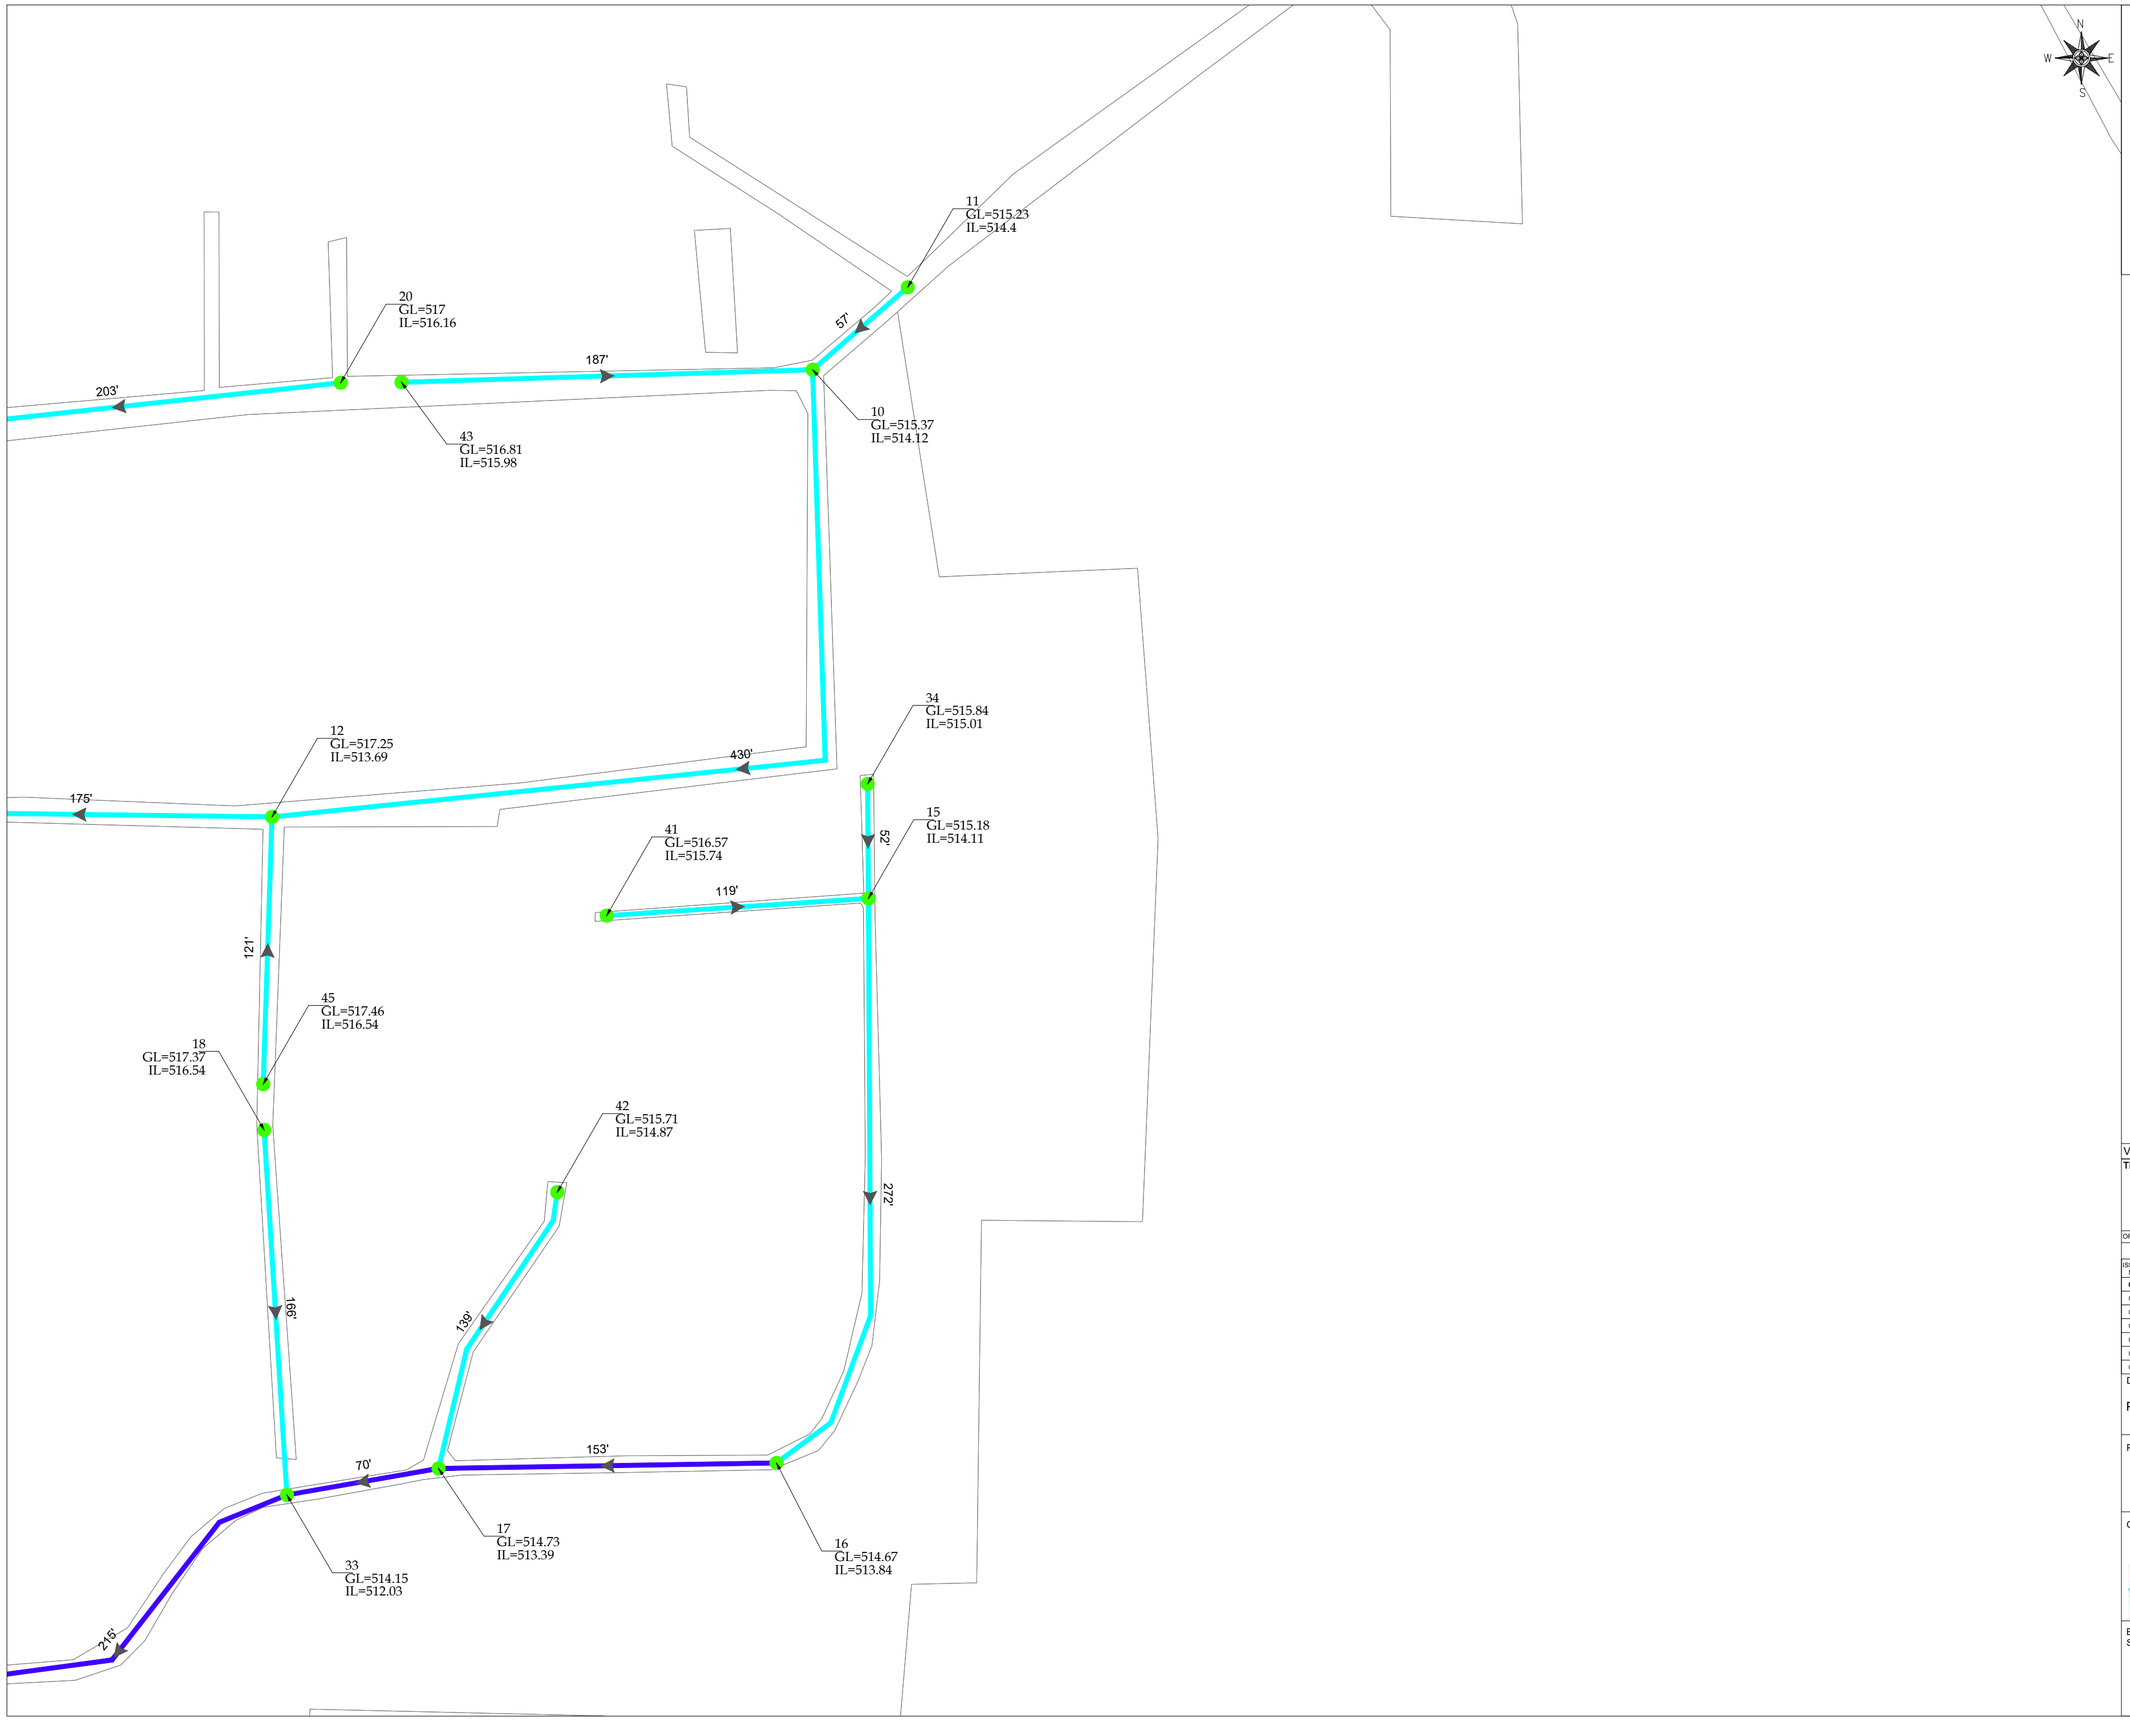

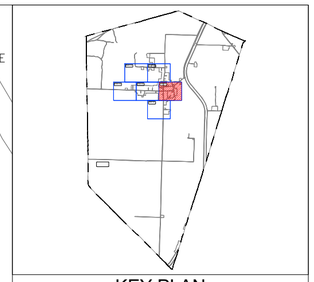

KEY PLAN

LEGEND:

- DRAIN TYPE - I
- SULLAGE CARRIER
- Ø3" HDPE PIPE
- BOUNDARY

VILLAGE: HASAN RAEKA (BWN)

TITLE.

DRAINAGE SYSTEM LAYOUT PLAN-05

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	16-12-2025	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02	20-04-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
03					
04					
05					
06					
07					

DRAWING N°:	SHEET	REV
PRMSC-BWN-HRK-SEW-LP-05	05 OF 06	01

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

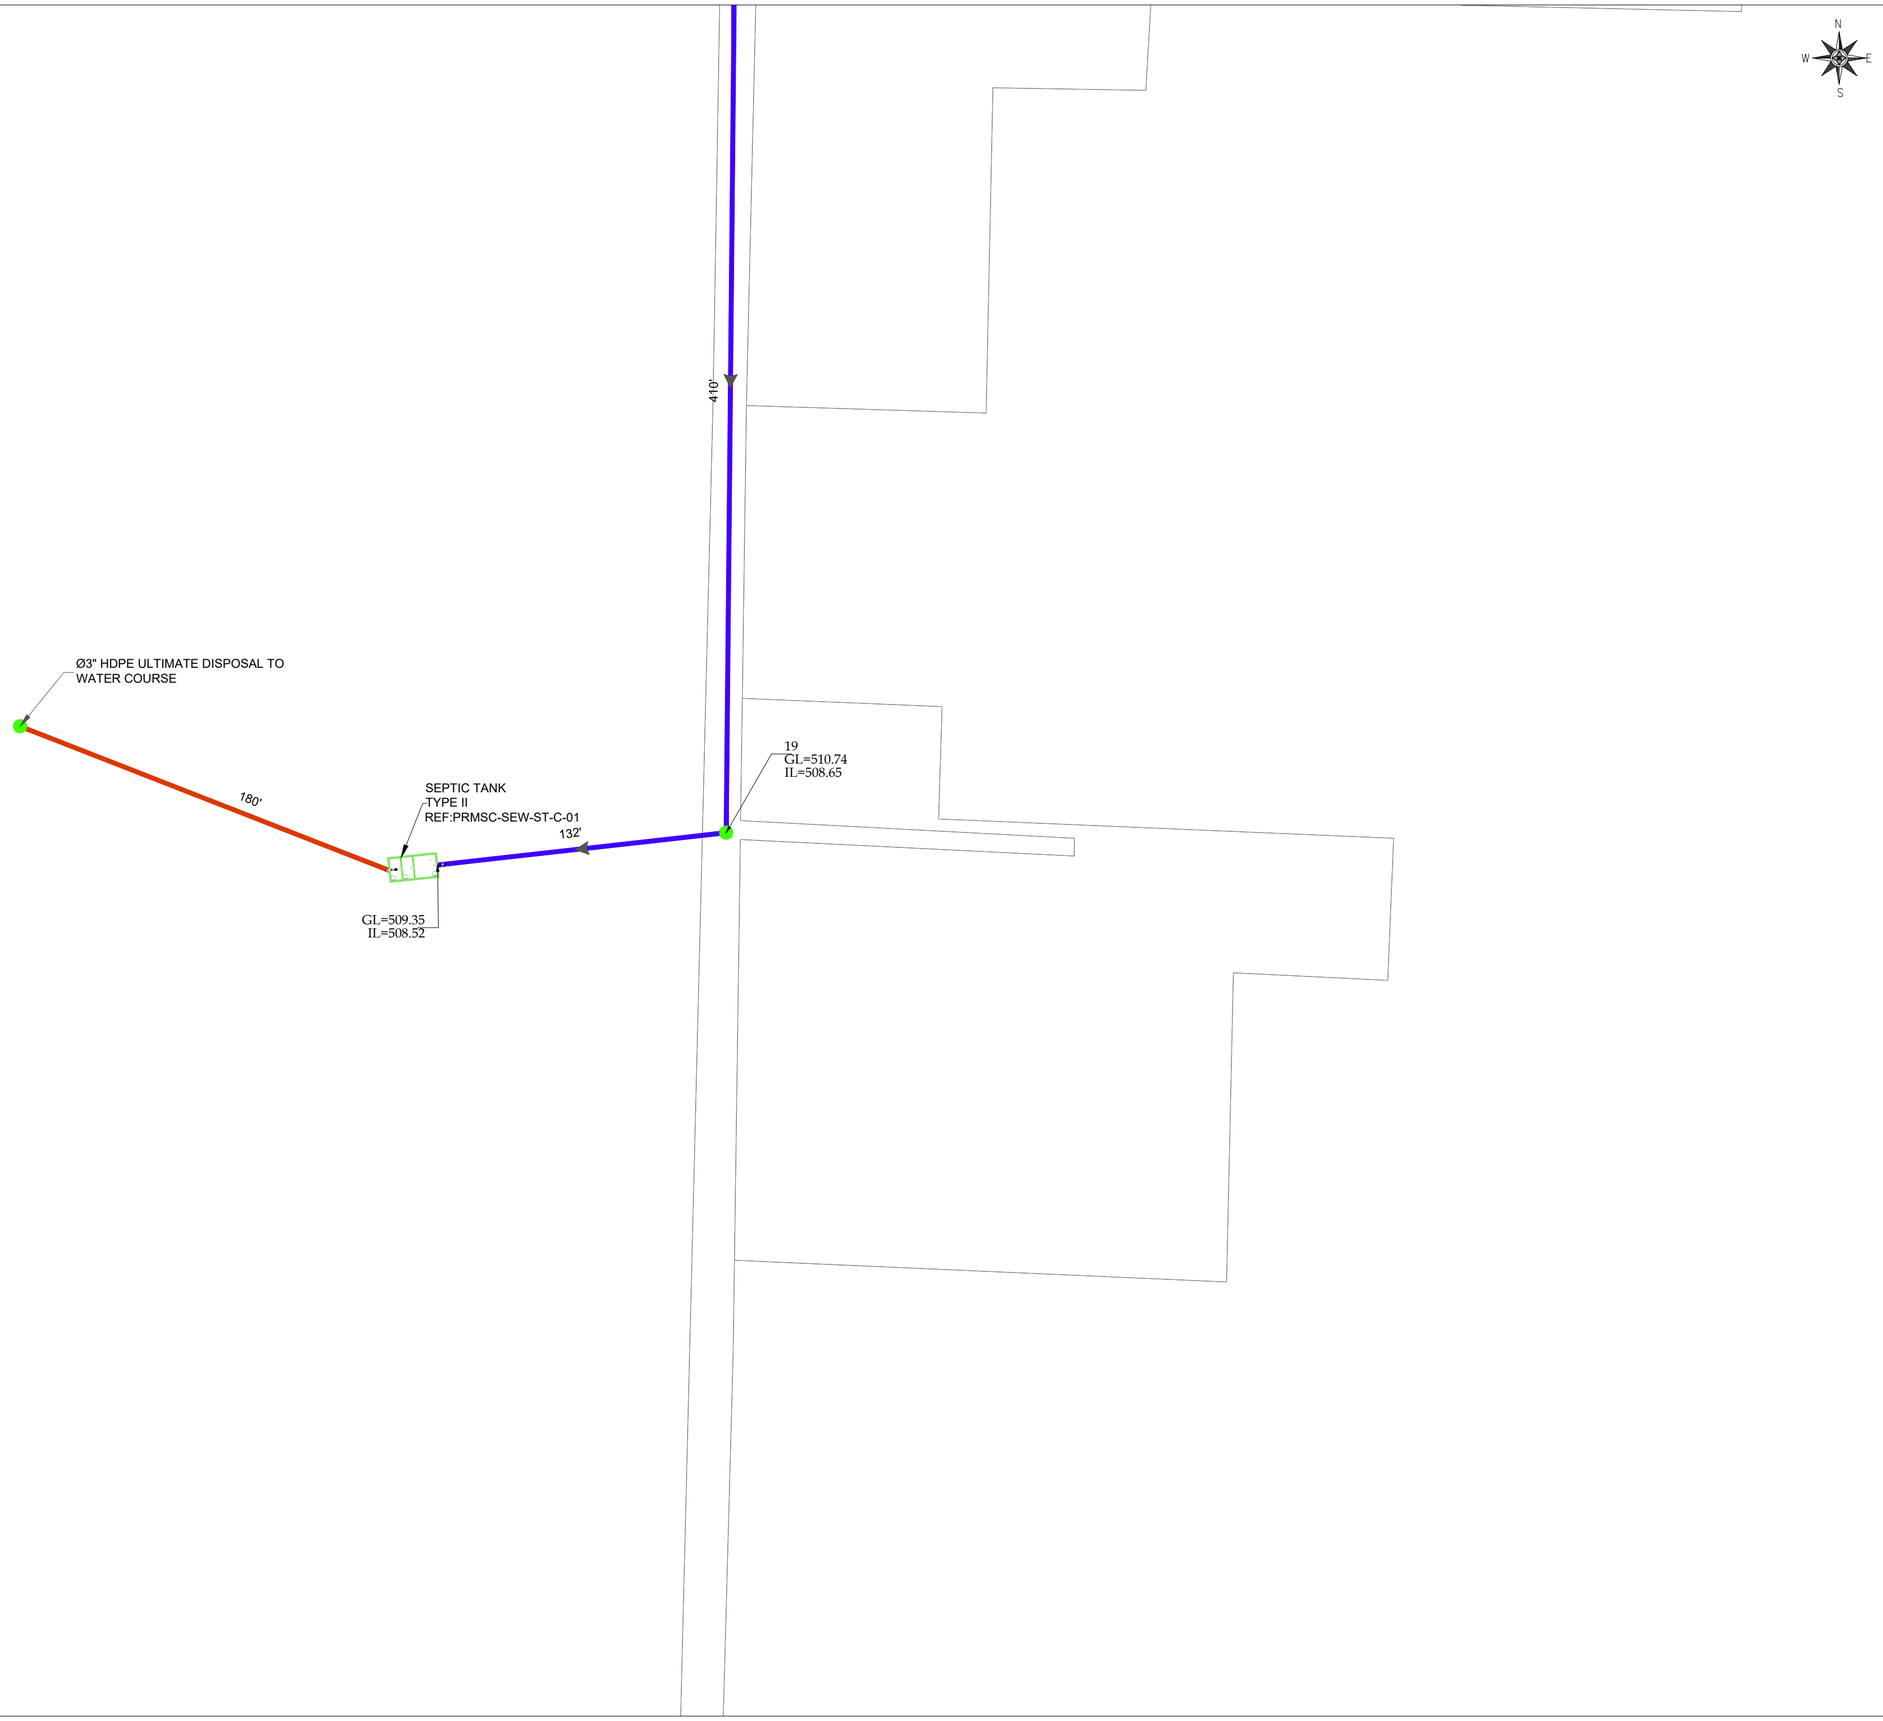

N
W
E
S



KEY PLAN

LEGEND:

- DRAIN TYPE - I
- SULLAGE CARRIER
- Ø3" HDPE PIPE
- BOUNDARY

VILLAGE: HASAN RAEKA (BWN)

TITLE.

DRAINAGE SYSTEM LAYOUT PLAN-06

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	16-12-2025	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02	20-04-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-HRK-SEW-LP-06	06 OF 06	01

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:
ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

PRMSC-BWN-HRK-SEW-LP-06

HYDRAULIC STATEMENT

Node		Length	Slope	Elevation Ground	Elevation Ground	Elevation Invert	Elevation Invert	Depth
FROM	TO	ft	ft/ft	U/S	D/S	U/S	D/S	ft
1	46	264	0.001	514.79	512.93	512.36	512.1	2.43
2	46	79	0.001	512.38	512.93	511.55	511.47	0.83
46	3	149	0.001	512.93	512.14	511.3	511.45	0.98
31	4	75	0.001	512.16	512.05	511.21	511.29	0.83
4	3	53	0.001	512.05	512.14	511.16	511.21	1.12
3	5	169	0.001	512.14	512.11	511.16	510.99	3.54
30	5	117	0.001	512.38	512.11	511.28	511.4	0.83
5	6	158	0.001	512.11	512.89	510.83	510.99	2.71
44	6	99	0.001	510.29	512.89	509.35	509.45	2.17
6	8	169	0.001	512.89	511.4	509.35	509.18	1.26
7	8	110	0.001	509.64	511.4	508.81	508.7	0.83
8	9	416	0.009	511.4	507.21	508.7	505.03	3.57
9	ST-2-TYPE-I-NO SP	110	0.001	507.21	507.07	505.03	504.92	3.64
43	10	187	0.01	516.81	515.37	514.12	515.98	2.33
11	10	57	0.005	515.23	515.37	514.4	514.12	1.06
10	12	430	0.001	515.37	517.25	513.69	514.12	0.83
45	12	121	0.001	517.46	517.25	516.42	516.54	1.34
12	13	175	0.001	517.25	515.83	513.69	513.51	0.83
47	13	163	0.029	517.82	515.83	512.19	516.99	2.09
13	14	376	0.001	515.83	512.65	511.81	512.19	0.83
41	15	119	0.014	516.57	515.18	514.11	515.74	2.37
34	15	52	0.017	515.84	515.18	514.11	515.01	2.59
15	16	272	0.001	515.18	514.67	513.84	514.11	2.72
16	17	153	0.001	514.67	514.73	513.69	513.84	1.23
42	17	139	0.011	515.71	514.73	513.39	514.87	1.75
33	17	70	0.001	514.15	514.73	513.32	513.39	1.31
18	33	166	0.027	517.37	514.15	516.54	512.03	0.83
33	14	215	0.001	514.15	512.65	511.81	512.03	2.26
14	19	410	0.001	512.65	510.74	510.32	509.91	1.94
19	ST-3-TYPE-II-NO SP	132	0.001	510.74	509.35	508.65	508.52	0.99
20	21	203	0.001	517	517.92	516.16	515.96	0.87
35	21	91	0.001	516.48	517.92	515.55	515.64	0.88
21	22	223	0.001	517.92	516.52	515.55	515.33	2.12
36	22	126	0.005	515.39	516.52	513.93	514.56	0.83
22	23	21	0.006	516.52	516.35	513.8	513.93	0.83
37	23	120	0.019	516.75	516.35	513.63	515.92	0.83
23	24	94	0.001	516.35	514.37	513.63	513.54	0.83
38	24	65	0.001	514.89	514.37	513.54	513.6	1.29
24	25	134	0.001	514.37	513.85	513.01	513.15	0.83
39	25	106	0.001	513.47	513.85	512.53	512.64	1.06
25	40	133	0.001	513.85	512.79	512.09	511.96	0.83
40	26	207	0.001	512.79	512.36	511.53	511.73	0.83
26	27	141	0.001	512.36	511.75	511.05	510.91	0.83
32	27	126	0.001	511.92	511.75	510.91	511.04	0.83
27	28	296	0.001	511.75	512.88	510.91	510.62	0.92
28	29	552	0.001	512.88	512	510.62	510.06	1.48
29	ST-1-TYPE-II-NO SP	119	0.001	512	511.38	510.06	509.95	0.83

VILLAGE: HASAN RAEKA (BWN)

TITLE.

HYDRAULIC STATEMENT

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	16-12-2025	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. HSAN-UL-HAQ
02	20-04-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. HSAN-UL-HAQ
03					
04					
05					
06					
07					

DRAWING N°: PRMSC-KPT-HRK-SEW-HS-01

SHEET 01 OF 01

REV 01

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER CENTRAL

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

PRMSC-HRK-HS-SEW-HS-01

JAGGA SANATTEKA

KEY PLAN

Revenue Village: Jagga Sanatteka Main Sheet

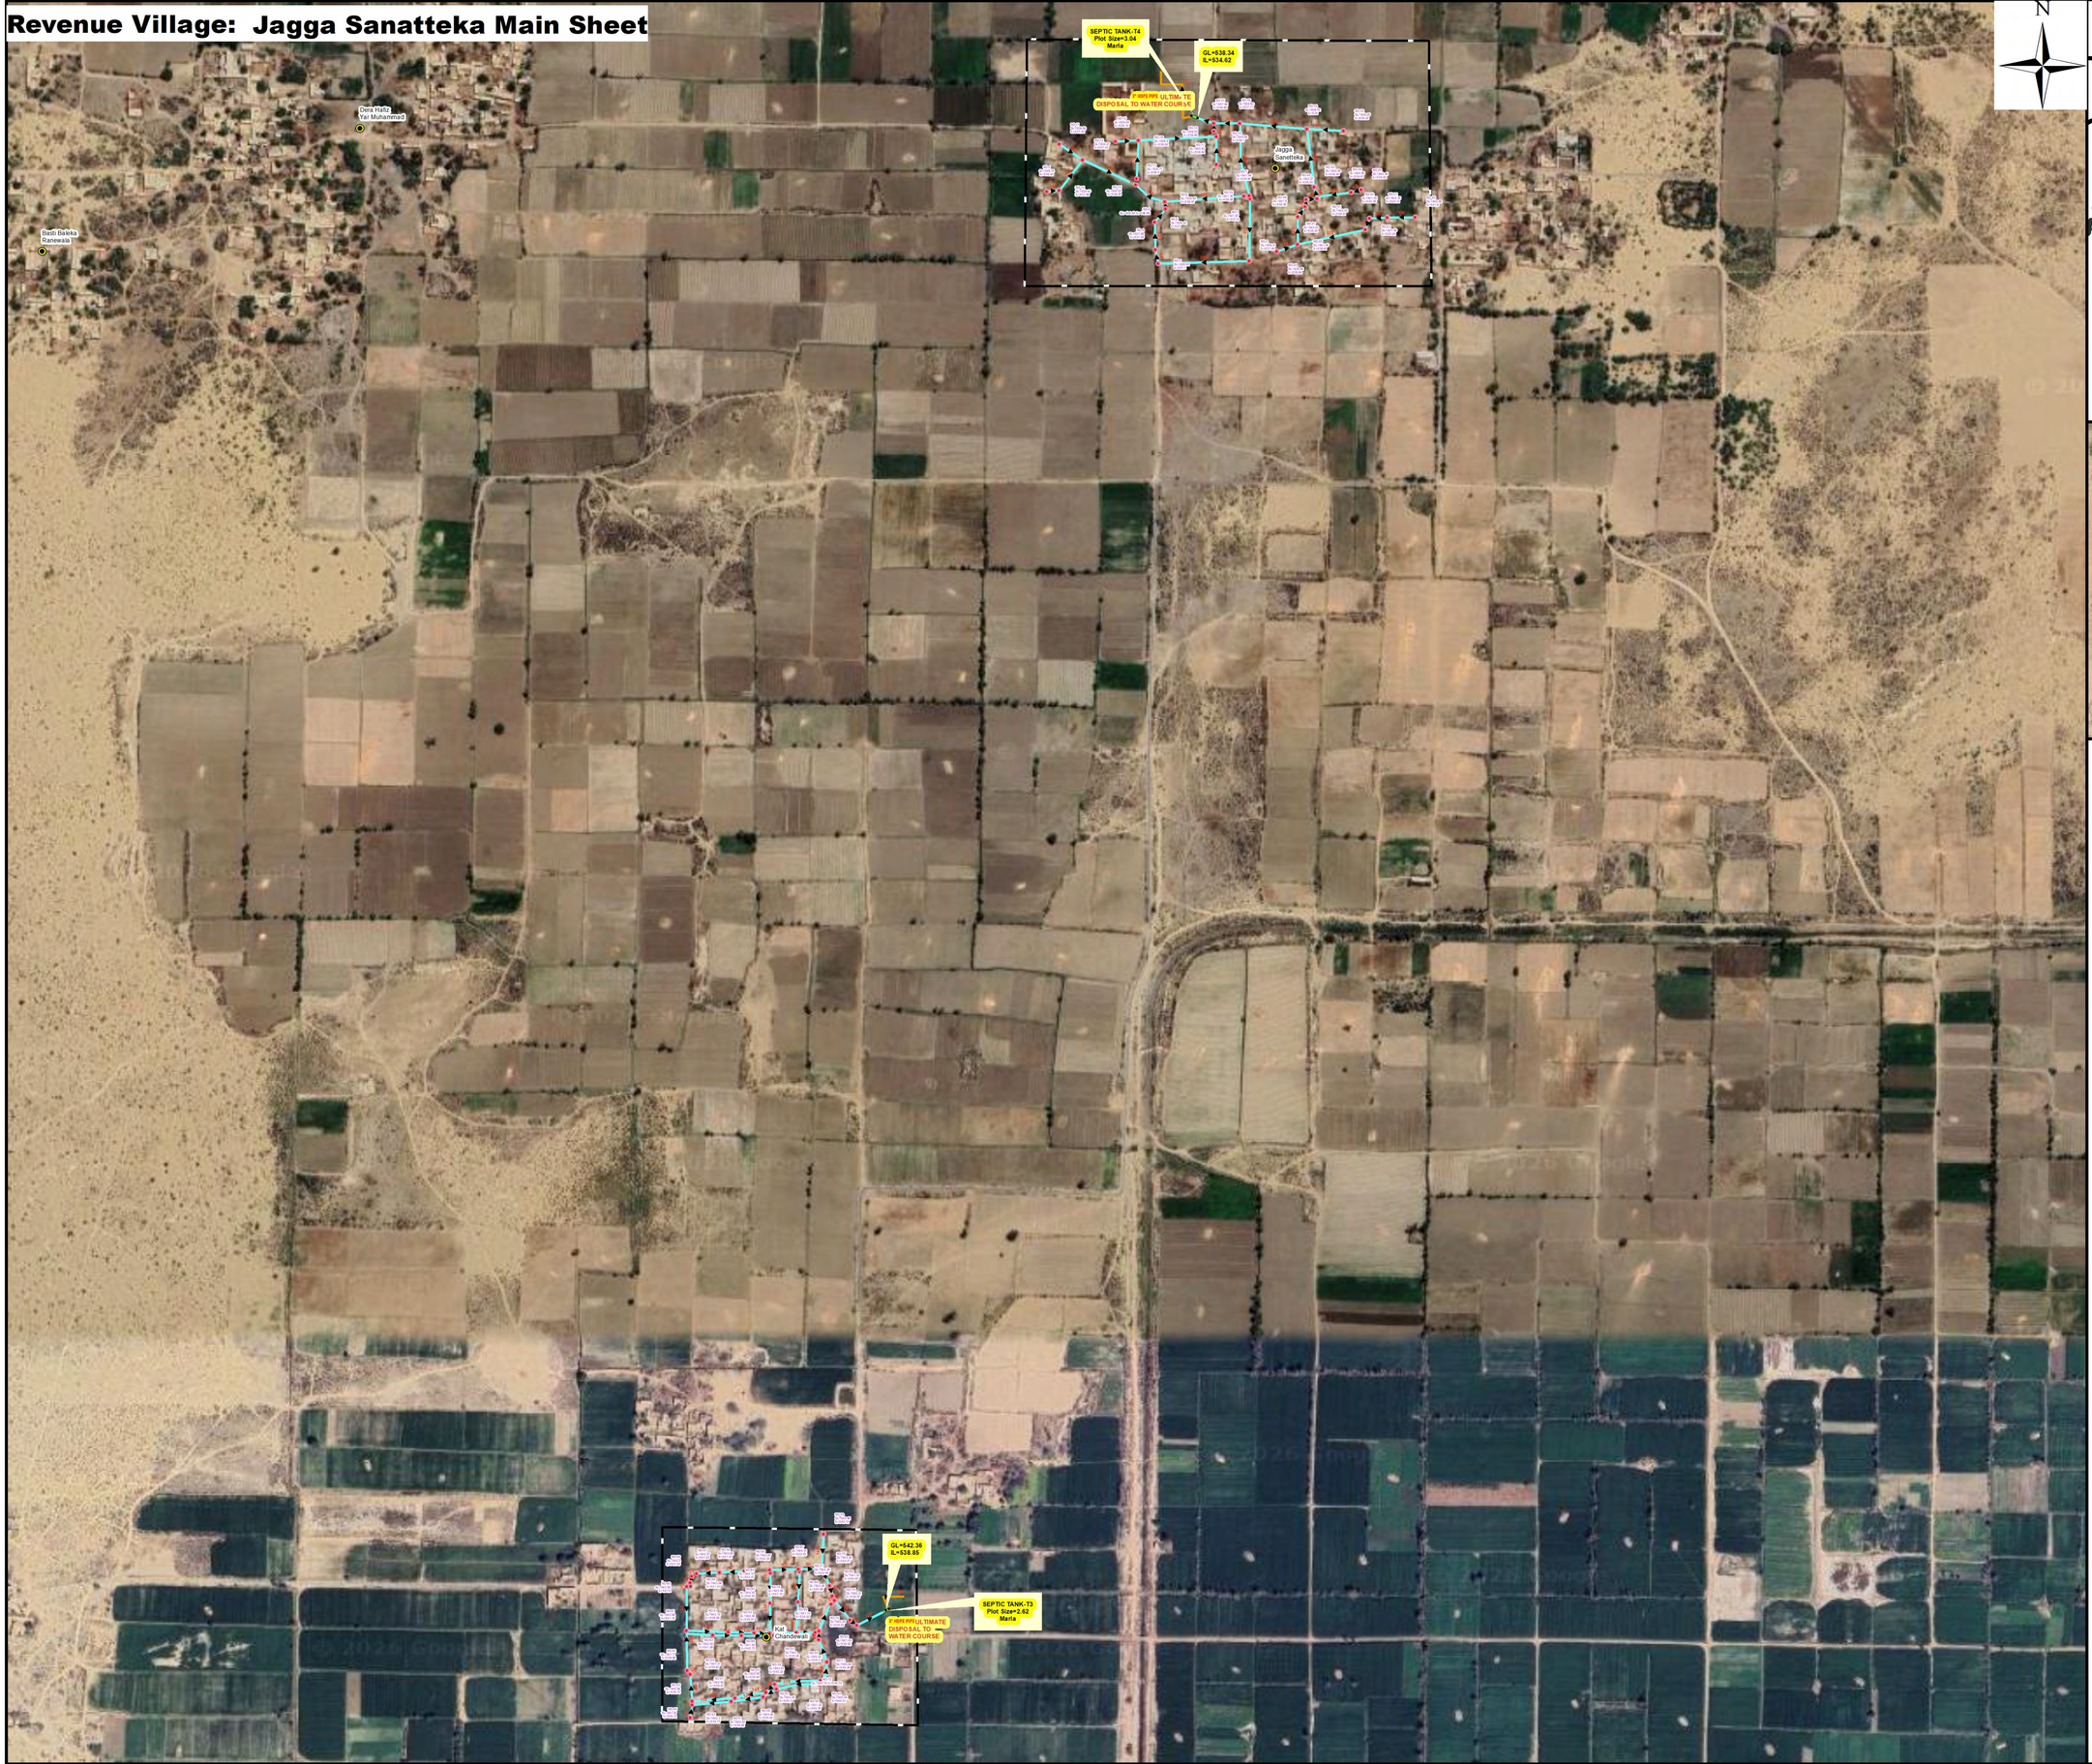

N

District:	Bahawalnagar
Tehsil:	Bahawalnagar
Revenue Village:	Jagga Sanatteka

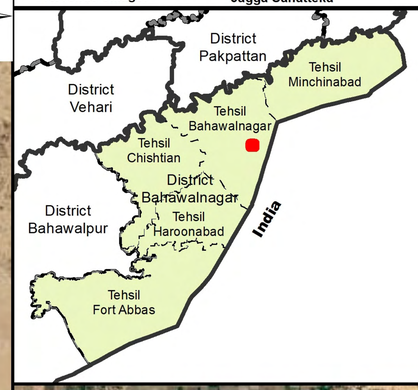

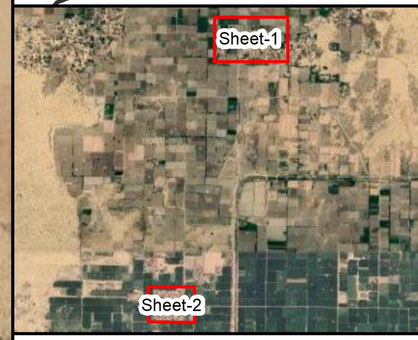

Title:
Proposed Drainage Network Plan

Legend:

- SETTLEMENT
- NODE
- 3" HDPE PIPE
- DRAIN TYPE-1
- SEPTIC TANK
- SETTLEMENT BOUNDARY

Drain Type 1=9133 Rft

Sullage Carrier= 1377 Rft

Scale: 1:8,100

1 inch = 675 feet

Paper Size: A3

0 40 80 160

Kilometers

Project:

Engineering Design & Construction Supervision, Punjab Rural Sustainable Water Supply & Sanitation Project, Cluster South III

PRSSC

ENVIRONMENTAL TECHNOLOGIES

ASIAN CONSULTING ENGINEERS www.asiancon.com

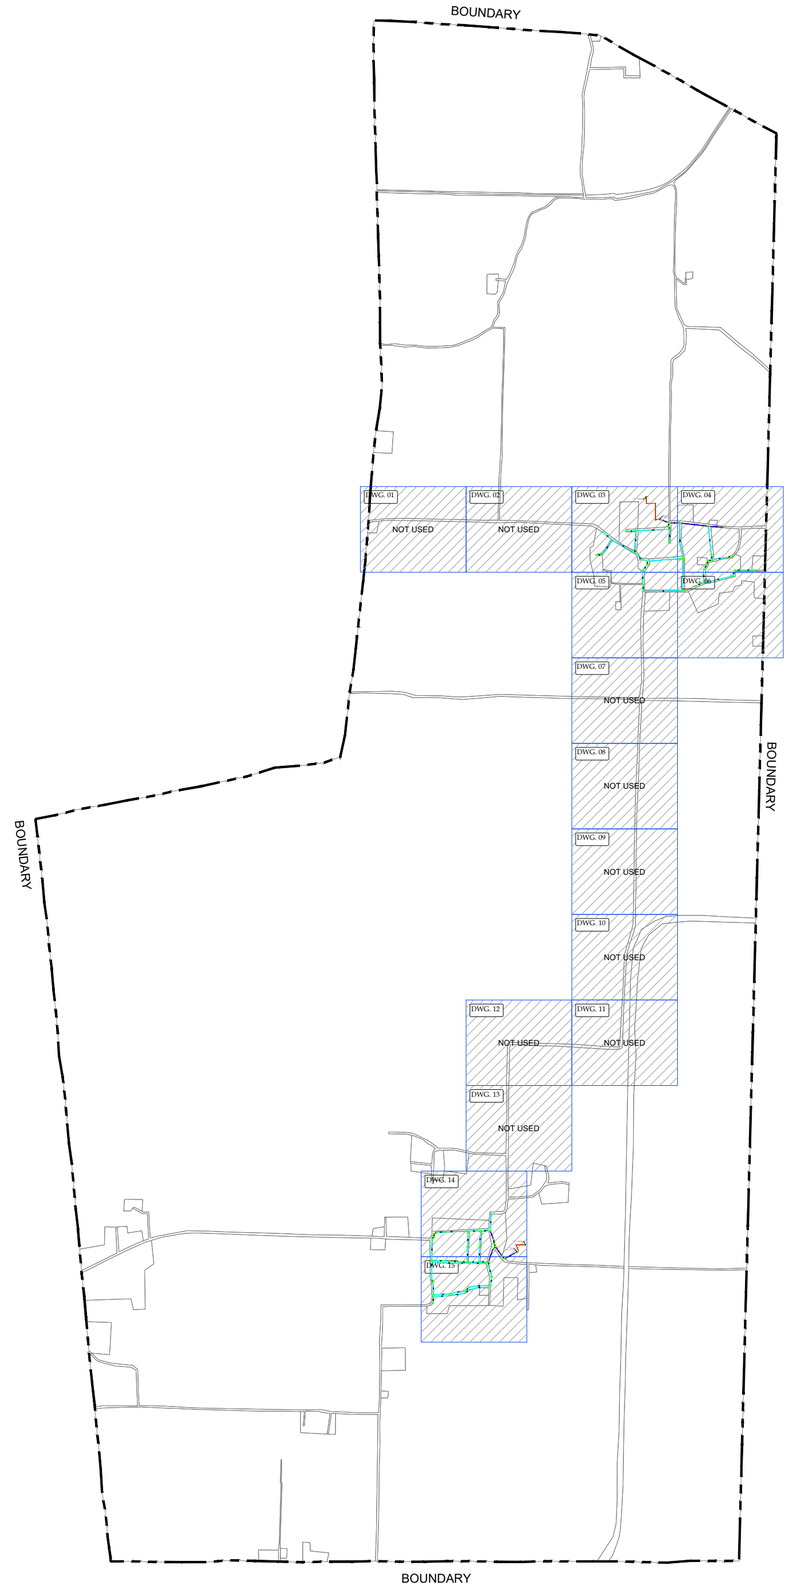

N
W
E
S

LEGEND:

- DRAIN TYPE - I
- SULLAGE CARRIER
- Ø3" HDPE PIPE
- BOUNDARY

VILLAGE: JAGGA SANETTEKA (BWN)

TITLE:

DRAINAGE SYSTEM KEY PLAN

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 1000'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	16-12-2025	DETAILED DESIGN	ASAD	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02	21-04-2026	DETAILED DESIGN	ASAD	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
03					
04					
05					
06					
07					

DRAWING Nº: PRMSC-BWN-JST-SEW-KP-00

SHEET 00 OF 00

REV 01

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT
ASIAN CONSULTING ENGINEERS
www.asiancon.com

PRMSC-BWN-JST-SEW-KP-00

LAYOUT PLAN

Revenue Village: Jagga Sanatteka Sheet-1

GL=538.34
IL=534.62

3" HDPE ULTIMATE DISPOSAL TO WATER COURSE

SEPTIC TANK-T4
Plot Size=3.04 Marla

Jagga Sanetteka

ND-1 GL=541.67 IL=537.48
ND-2 GL=539.41 IL=537.48
ND-3 GL=538.03 IL=537.41
ND-4 GL=537.88 IL=537.05
ND-5 GL=539.54 IL=537
ND-6 GL=539.64 IL=536.97
ND-7 GL=541.98 IL=538.84
ND-8 GL=539.62 IL=536.96
ND-9 GL=539.74 IL=538.91
ND-10 GL=539.03 IL=537.59
ND-11 GL=538.89 IL=537.59
ND-12 GL=538.27 IL=537.43
ND-13 GL=538.77 IL=538.0
ND-14 GL=540.03 IL=538.65
ND-15 GL=539.04 IL=538.14
ND-16 GL=53819 IL=536782
ND-17 GL=540.93 IL=538.94
ND-18 GL=539.03 IL=536.69
ND-19 GL=539.88 IL=5367
ND-20 GL=542.88 IL=5416
ND-21 GL=542.55 IL=540.31
ND-22 GL=541.09 IL=540.26
ND-23 GL=541.99 IL=540.24
ND-24 GL=539.48 IL=538.64
ND-25 GL=541.96 IL=538.61
ND-26 GL=541.9 IL=538.56
ND-27 GL=542.43 IL=538.54
ND-28 GL=542.27 IL=538.53
ND-29 GL=540.46 IL=539.63
ND-30 GL=540.12 IL=539.61
ND-31 GL=542.09 IL=538.51
ND-32 GL=542.09 IL=538.49
ND-33 GL=539.05 IL=539.22
ND-34 GL=539.42 IL=538
ND-35 GL=541.58 IL=538.06
ND-36 GL=538.63 IL=537.11



District: Bahawalnagar
Tehsil: Bahawalnagar
Revenue Village: Jagga Sanatteka

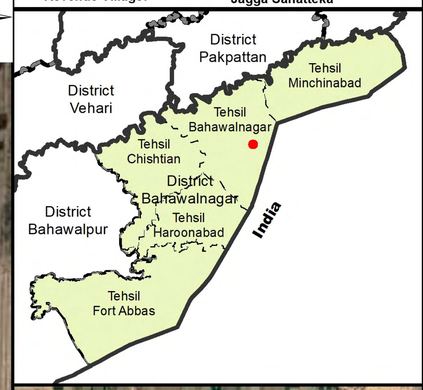

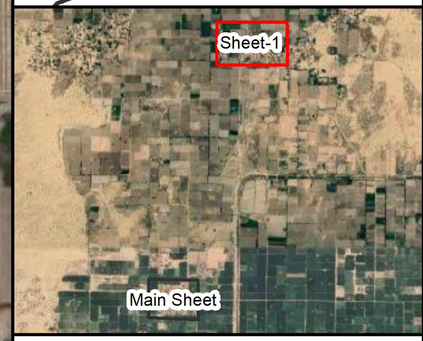

Title:
Proposed Drainage Network Plan

Legend:

- SETTLEMENT
- NODE
- 3" HDPE PIPE
- DRAIN TYPE-1
- SEPTIC TANK
- SETTLEMENT BOUNDARY

Drain Type 1=9133 Rft
Sullage Carrier= 1377 Rft

Scale: 1:1,700
1 inch = 142 feet
Paper Size: A3

0 40 80 160
Kilometers

Project:
Engineering Design & Construction Supervision, Punjab Rural Sustainable Water Supply & Sanitation Project, Cluster South III

PRWSC ENVIRONMENTAL TECHNOLOGIES ASIAN CONSULTING ENGINEERS www.asiancon.com

Revenue Village: Jagga Sanatteka Sheet-2

District:	Bahawalnagar
Tehsil:	Bahawalnagar
Revenue Village:	Jagga Sanatteka



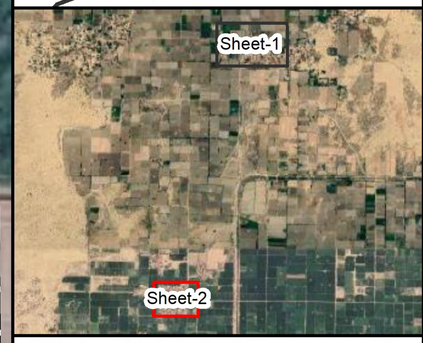

GL=542.36
IL=538.85

SEPTIC TANK-T3
Plot Size=2.62 Marla

Kat Chandewali

Title:
Proposed Drainage Network Plan

Legend:

- SETTLEMENT
- NODE
- 3" HDPE: PIPE
- DRAIN TYPE-1
- SEPTIC TANK
- SETTLEMENT BOUNDARY

Drain Type 1=9133 Rft
Sullage Carrier= 1377 Rft

Scale: 1:1,000
1 inch = 83 feet
Paper Size: A3

0 40 80 160
Kilometers

Project:
Engineering Design & Construction Supervision, Punjab Rural Sustainable Water Supply & Sanitation Project, Cluster South III

PRWSC
ENVIRONMENTAL TECHNOLOGIES
ASIAN CONSULTING ENGINEERS
www.asiancon.com

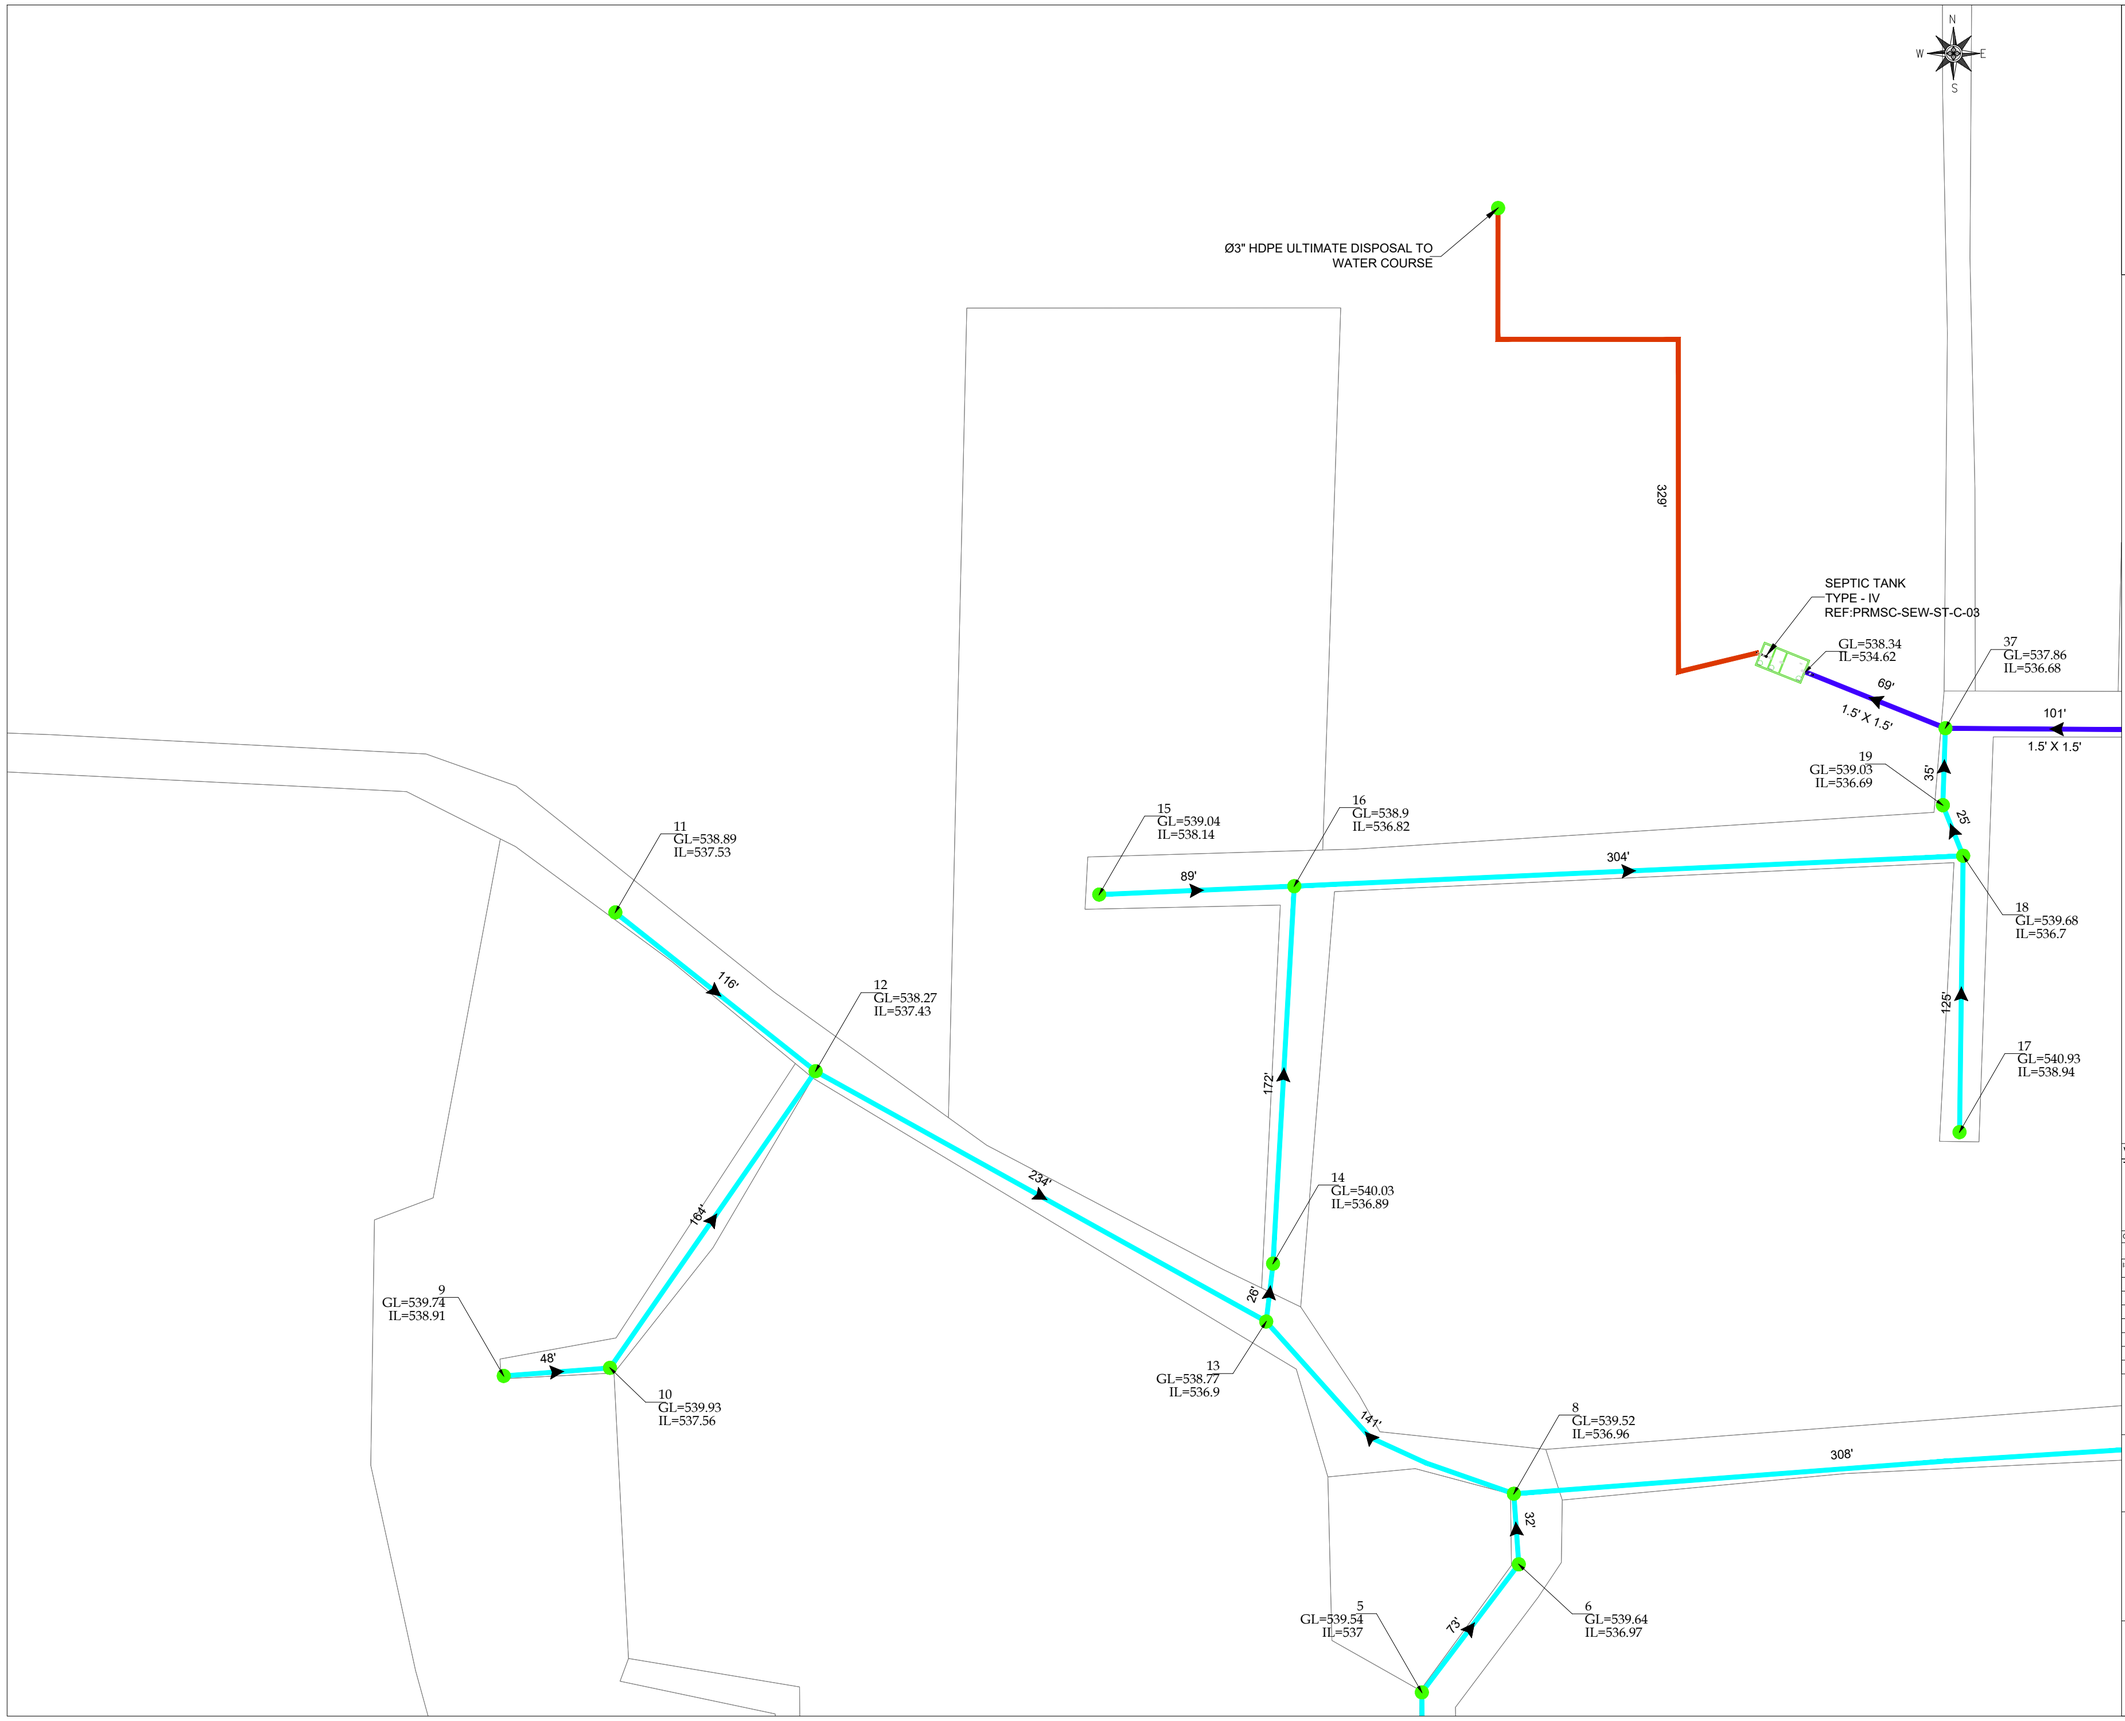

PRMSC-BWN-JST-SEW-LP-03



KEY PLAN

LEGEND:

- DRAIN TYPE - I
- SULLAGE CARRIER
- Ø3" HDPE PIPE
- BOUNDARY

VILLAGE: JAGGA SANETTEKA (BWN)

TITLE.

DRAINAGE SYSTEM LAYOUT PLAN-03

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	16-12-2025	DETAILED DESIGN	ASAD	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02	21-04-2026	DETAILED DESIGN	ASAD	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
03					
04					
05					
06					
07					

DRAWING N°: PRMSC-BWN-JST-SEW-LP-03

SHEET 03 OF 15

REV 01

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS
www.asianceb.com

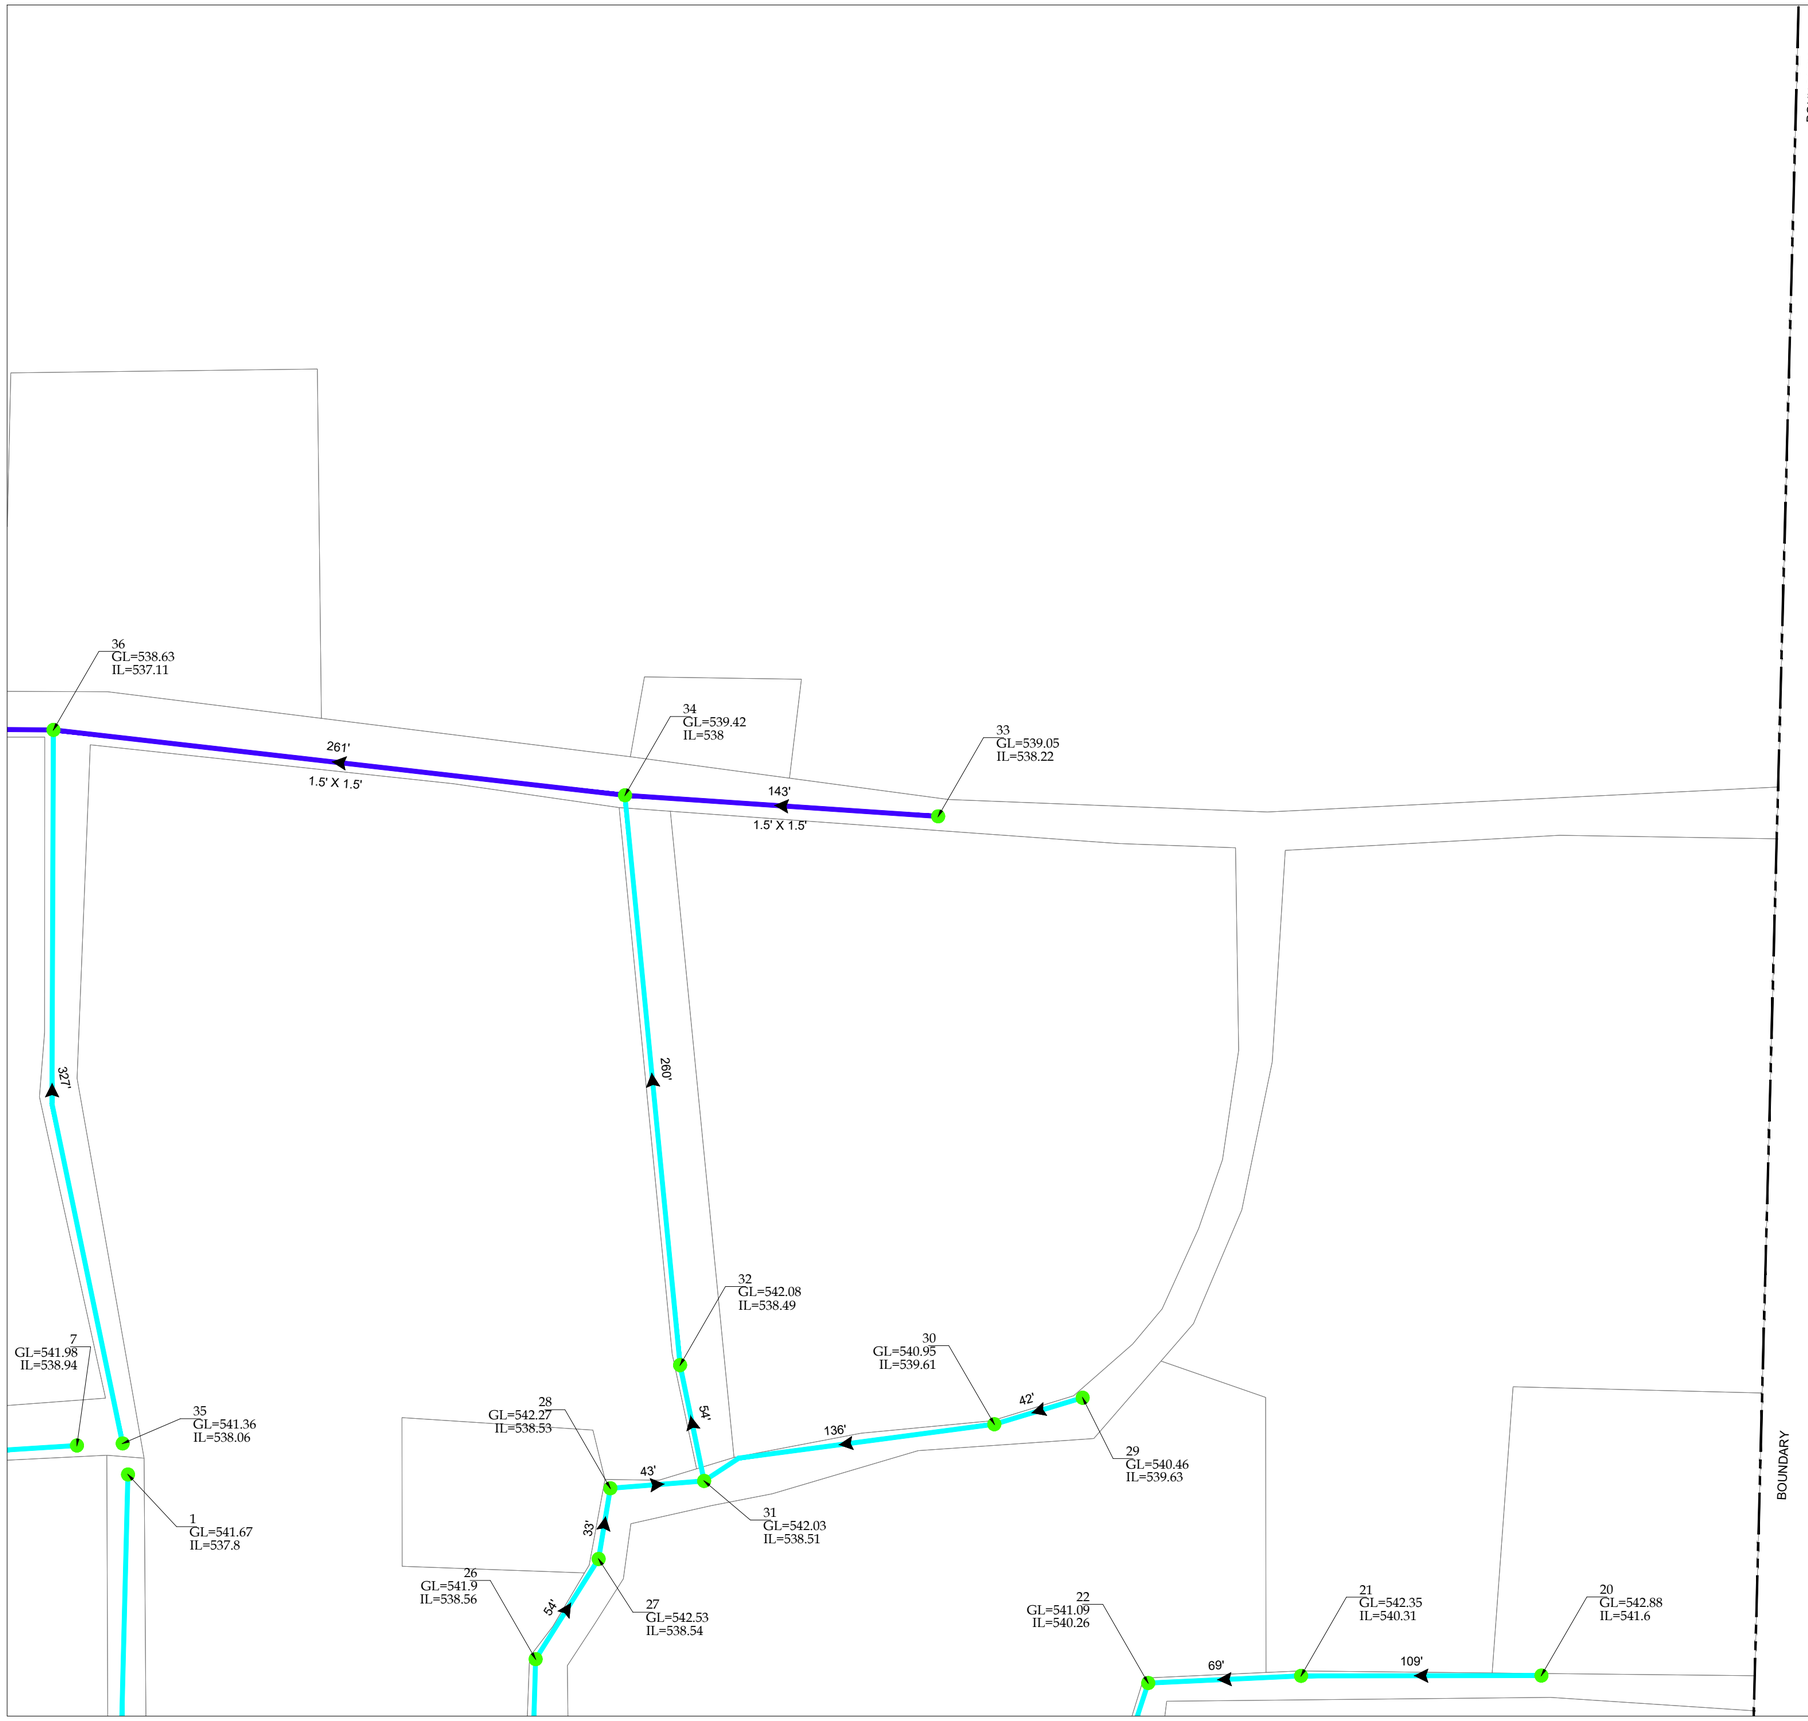

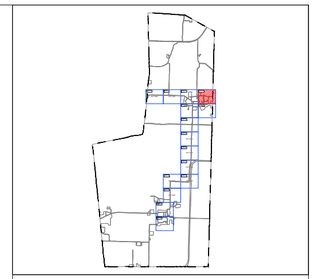

KEY PLAN

LEGEND:

- DRAIN TYPE - I
- SULLAGE CARRIER
- Ø3" HDPE PIPE
- BOUNDARY

VILLAGE: JAGGA SANETTEKA (BWN)

TITLE.

DRAINAGE SYSTEM LAYOUT PLAN-04

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	16-12-2025	DETAILED DESIGN	ASAD	ENGR FAIEZ	ENGR HSAN-UL-HAQ
02	21-04-2026	DETAILED DESIGN	ASAD	ENGR FAIEZ	ENGR HSAN-UL-HAQ
03					
04					
05					
06					
07					

DRAWING Nº: PRMSC-BWN-JST-SEW-LP-04

SHEET 04 OF 15

REV 01

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

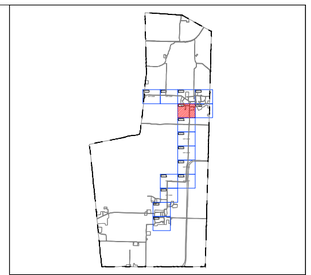

KEY PLAN

LEGEND:

- DRAIN TYPE - I
- SULLAGE CARRIER
- Ø3" HDPE PIPE
- BOUNDARY

VILLAGE: JAGGA SANETTEKA (BWN)

TITLE.

DRAINAGE SYSTEM LAYOUT PLAN-05

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	16-12-2025	DETAILED DESIGN	ASAD	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02	21-04-2026	DETAILED DESIGN	ASAD	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-JST-SEW-LP-05	05 OF 15	01

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

PRMSC-BWN-JST-SEW-LP-05

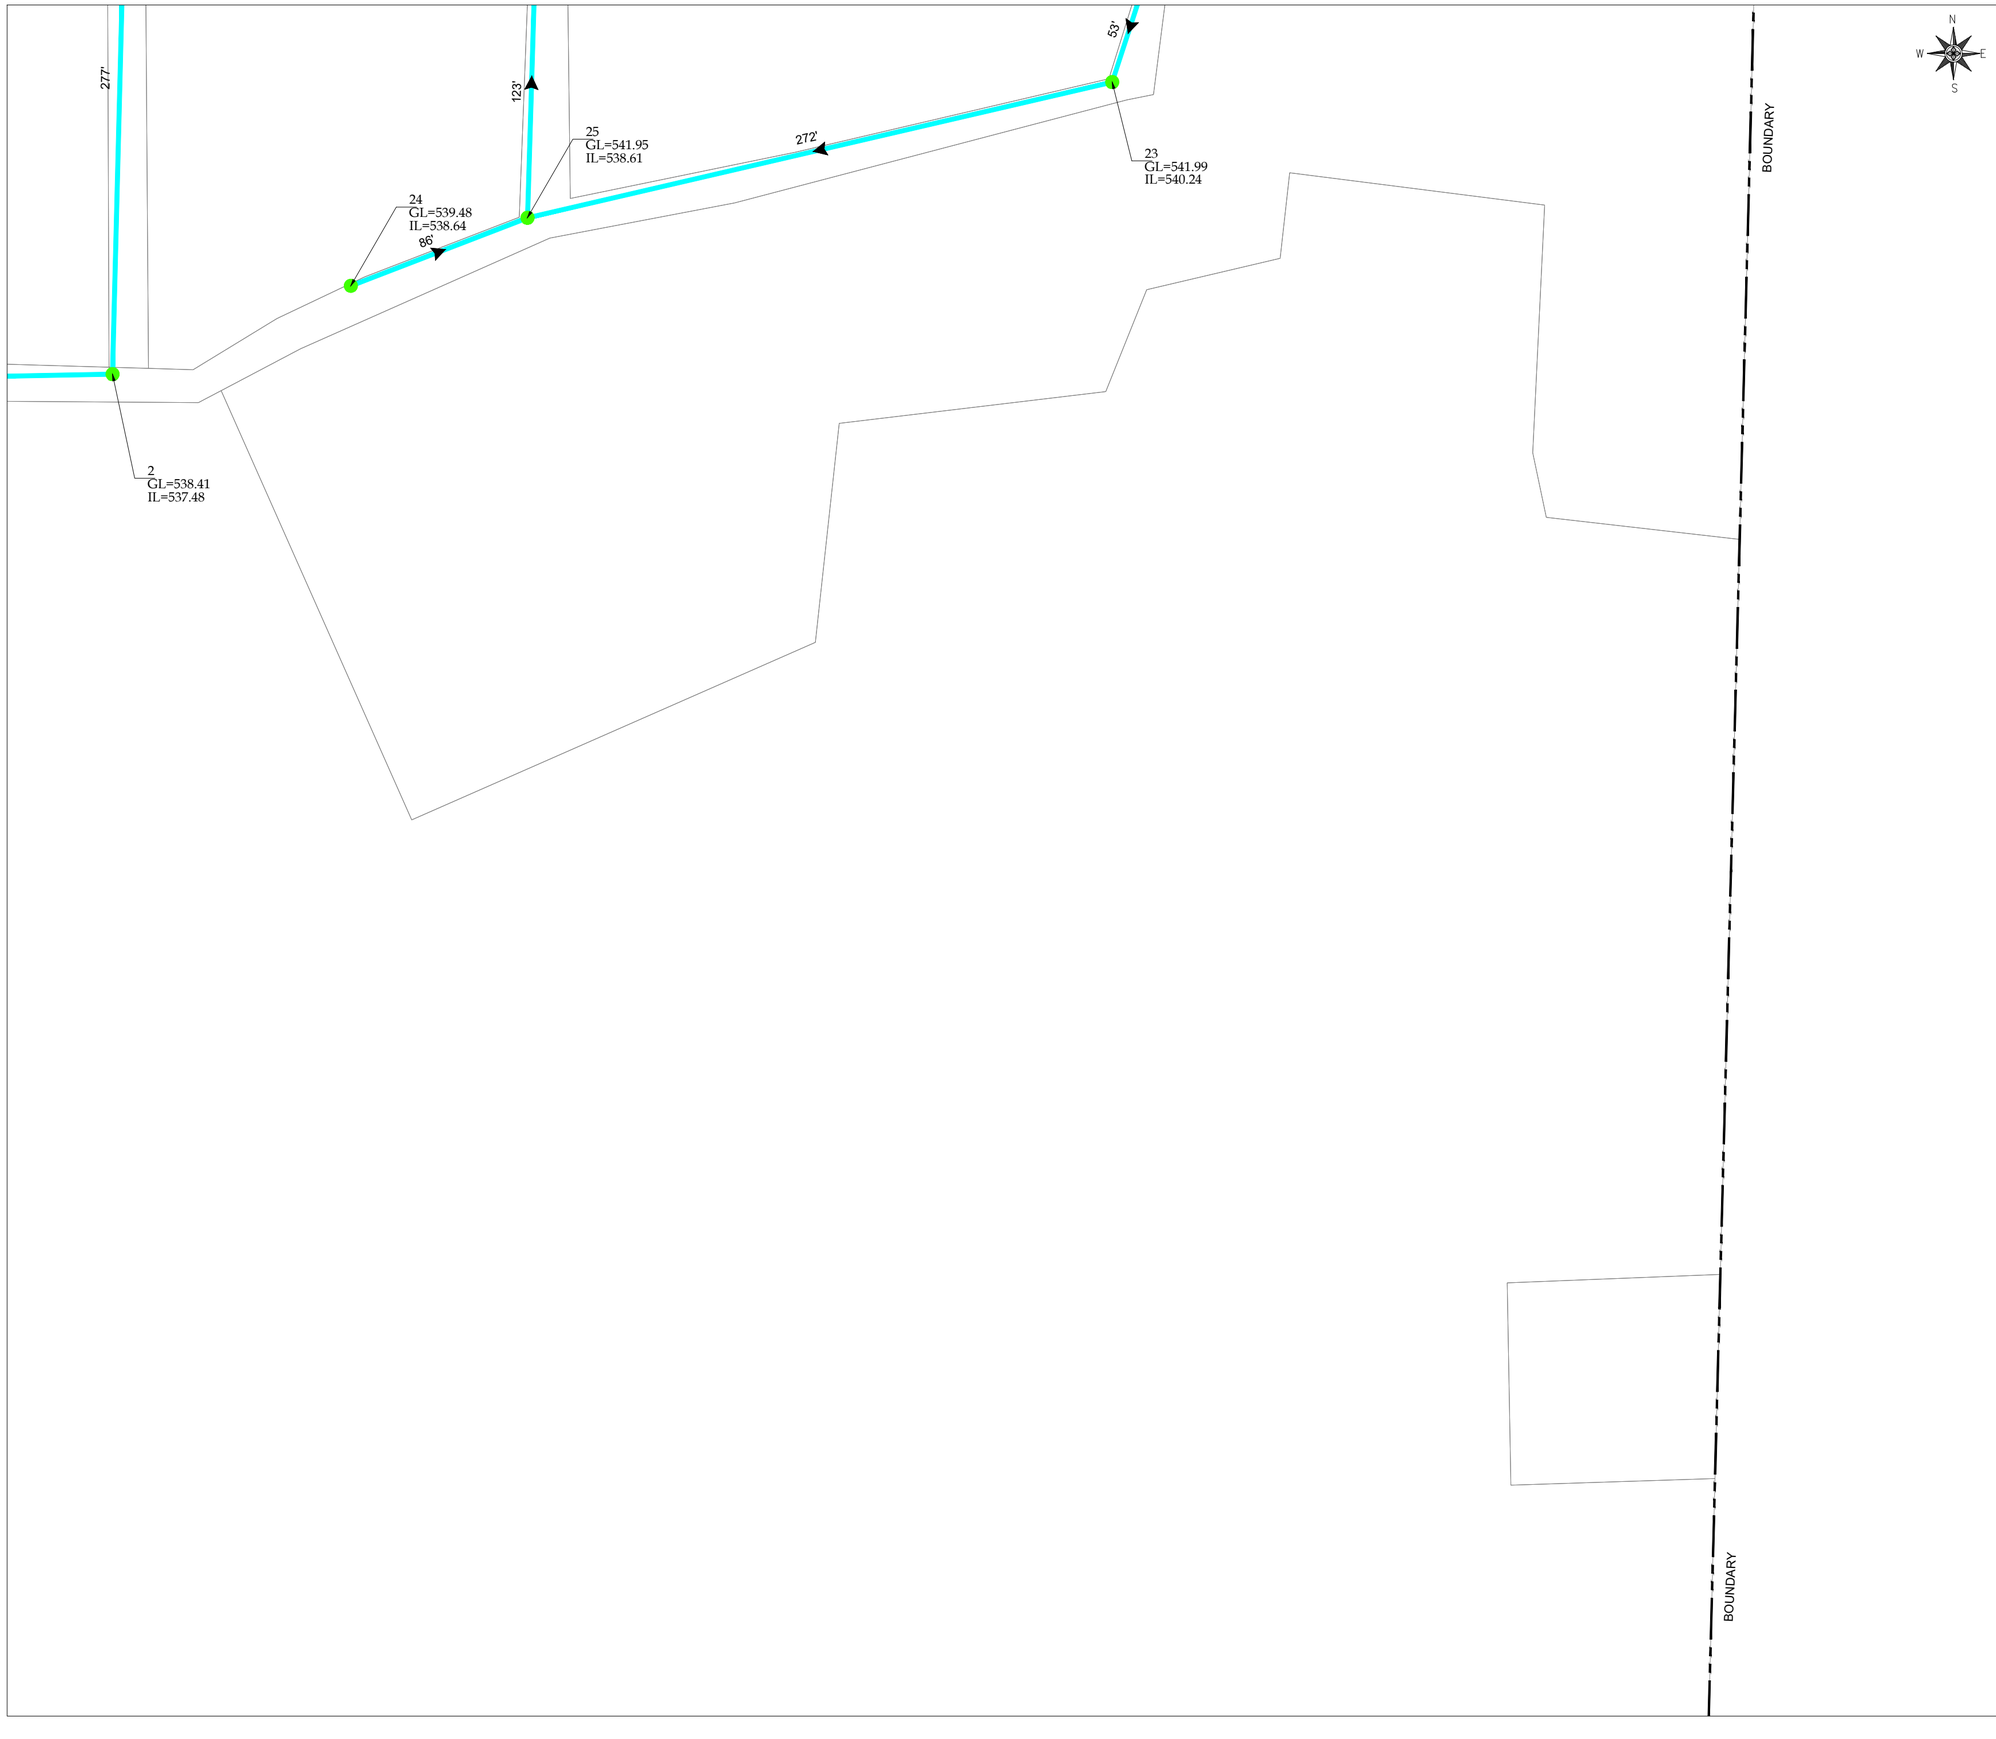

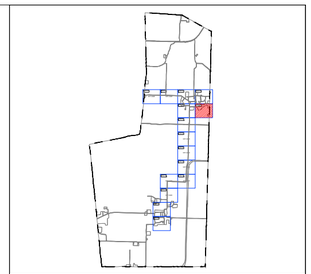

KEY PLAN

LEGEND:

- DRAIN TYPE - I
- SULLAGE CARRIER
- Ø3" HDPE PIPE
- BOUNDARY

VILLAGE: JAGGA SANETTEKA (BWN)

TITLE.

DRAINAGE SYSTEM LAYOUT PLAN-06

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	16-12-2025	DETAILED DESIGN	ASAD	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02	21-04-2026	DETAILED DESIGN	ASAD	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-JST-SEW-LP-06	06 OF 15	01

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

PRMSC-BWN-JST-SEW-LP-06

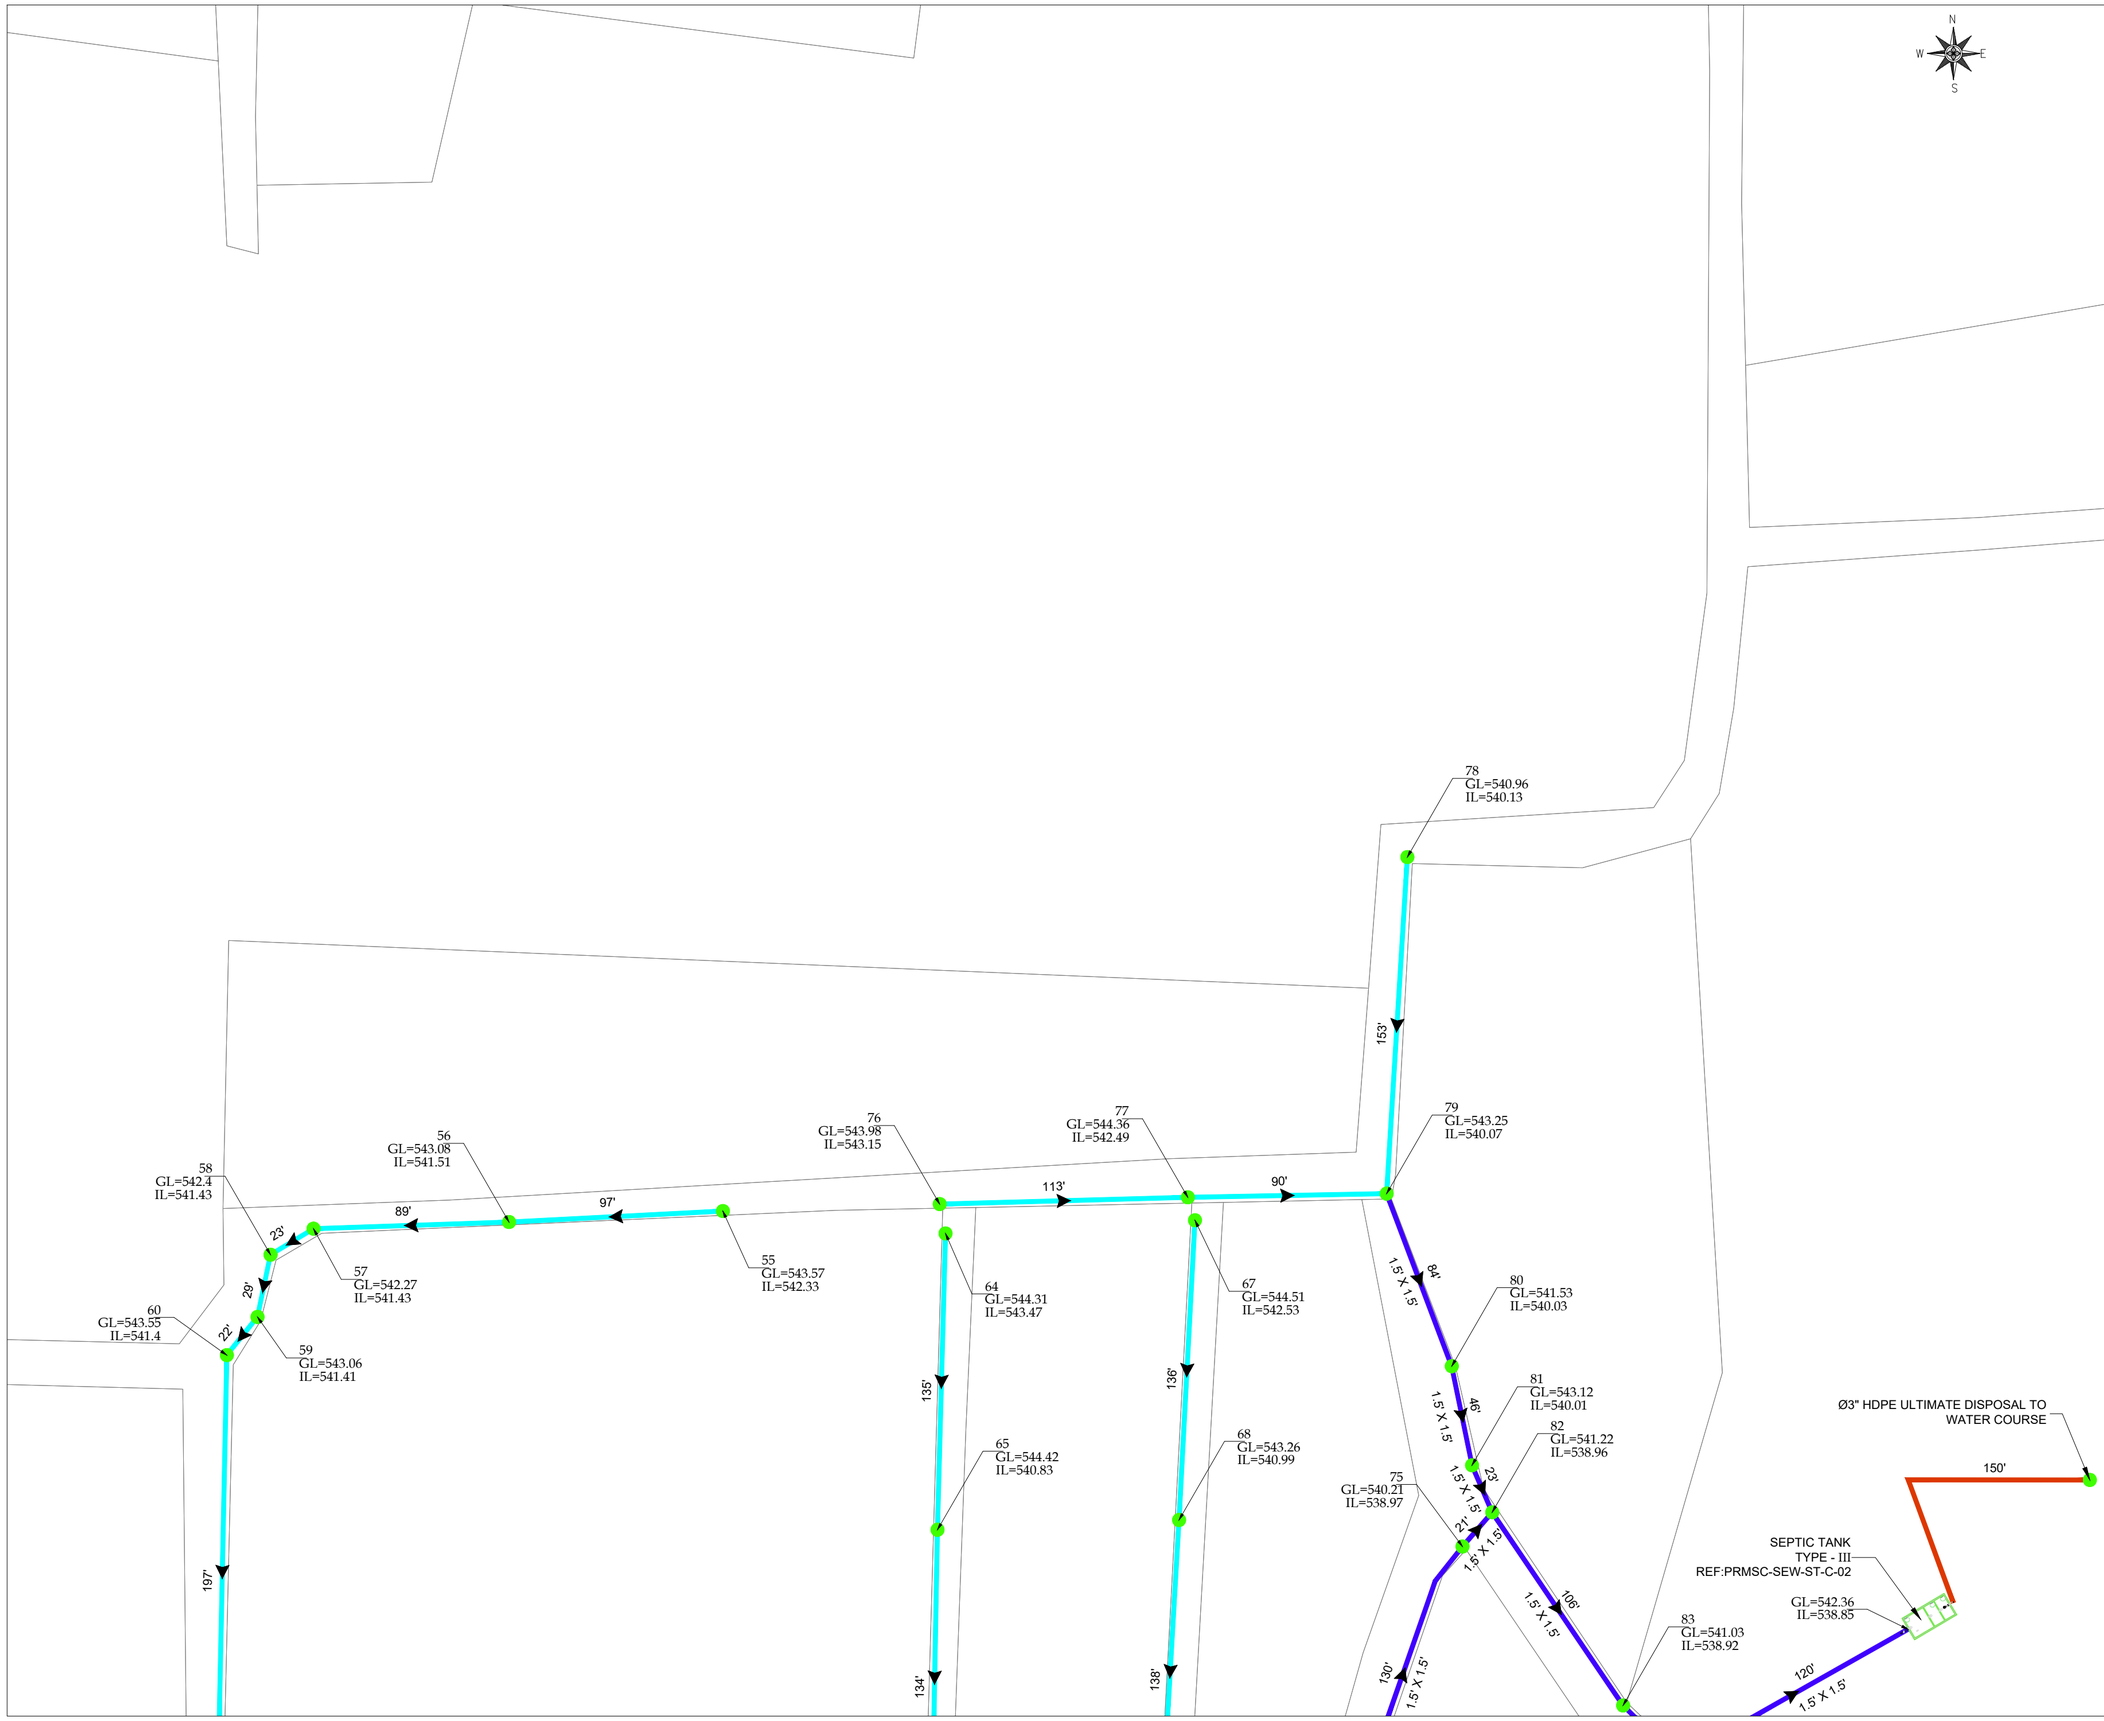

KEY PLAN

LEGEND:

- DRAIN TYPE - I
- SULLAGE CARRIER
- Ø3" HDPE PIPE
- BOUNDARY

VILLAGE: JAGGA SANETTEKA (BWN)

TITLE.

DRAINAGE SYSTEM LAYOUT PLAN-14

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	16-12-2025	DETAILED DESIGN	ASAD	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02	21-04-2026	DETAILED DESIGN	ASAD	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-JST-SEW-LP-14	14 OF 15	01

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS
www.asiancep.com

PRMSC-BWN-JST-SEW-LP-15

KEY PLAN

LEGEND:

- DRAIN TYPE - I
- SULLAGE CARRIER
- Ø3" HDPE PIPE
- BOUNDARY

VILLAGE: JAGGA SANETTEKA (BWN)

TITLE.

DRAINAGE SYSTEM LAYOUT PLAN-15

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	16-12-2025	DETAILED DESIGN	ASAD	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02	21-04-2026	DETAILED DESIGN	ASAD	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-JST-SEW-LP-15	15 OF 15	01

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS
www.asianeon.com

HYDRAULIC STATEMENT

Node		Length	Slope	Elevation Ground	Elevation Ground	Elevation Invert	Elevation Invert	Depth
FROM	TO	ft	ft/ft	U/S	D/S	U/S	D/S	ft
1	2	277	0.003	541.67	538.41	537.8	537.58	3.87
2	3	355	0.003	538.41	538.03	537.48	537.2	0.93
3	4	63	0.003	538.03	537.88	537.1	537.05	0.93
4	5	123	0.003	537.88	539.54	537.05	537	0.83
5	6	73	0.003	539.54	539.64	537	536.97	2.54
6	8	32	0.003	539.64	539.52	536.97	536.96	2.67
7	8	308	0.003	541.98	539.52	538.94	538.69	3.04
8	13	141	0.003	539.52	538.77	536.96	536.9	2.57
9	10	48	0.003	539.74	539.93	538.91	538.89	0.83
10	12	164	0.003	539.93	538.27	537.56	537.43	2.36
11	12	116	0.003	538.89	538.27	537.53	537.43	1.37
12	13	234	0.003	538.27	538.77	537.43	537.34	0.83
13	14	26	0.003	538.77	540.03	536.9	536.89	1.86
14	16	172	0.003	540.03	538.9	536.89	536.82	3.14
15	16	89	0.003	539.04	538.9	538.14	538.07	0.9
16	18	304	0.003	538.9	539.68	536.82	536.7	2.08
17	18	125	0.003	540.93	539.68	538.94	538.84	1.99
18	19	25	0.003	539.68	539.03	536.7	536.69	2.97
19	37	35	0.003	539.03	537.86	536.69	536.68	2.34
20	21	109	0.003	542.88	542.35	541.6	541.51	1.28
21	22	69	0.003	542.35	541.09	540.31	540.26	2.03
22	23	53	0.003	541.09	541.99	540.26	540.24	0.83
23	25	272	0.003	541.99	541.95	540.24	540.13	1.75
24	25	86	0.003	539.48	541.95	538.64	538.61	0.83
25	26	123	0.003	541.95	541.9	538.61	538.56	3.34
26	27	54	0.003	541.9	542.53	538.56	538.54	3.33
27	28	33	0.003	542.53	542.27	538.54	538.53	3.99
28	31	43	0.003	542.27	542.03	538.53	538.51	3.75
29	30	42	0.003	540.46	540.95	539.63	539.61	0.83
30	31	136	0.003	540.95	542.03	539.61	539.56	1.34
31	32	54	0.003	542.03	542.08	538.51	538.49	3.53
32	34	260	0.003	542.08	539.42	538.49	538.38	3.6
33	34	143	0.003	539.05	539.42	538.22	538.16	0.83
34	36	261	0.003	539.42	538.63	538	537.79	1.42
35	36	327	0.003	541.36	538.63	538.06	537.79	3.31
36	37	101	0.003	538.63	537.86	537.11	537.02	1.52
37	ST-TYPE-IV-NO SP	69	0.003	537.86	538.34	536.68	534.62	1.18
38	39	174	0.003	541.22	543.03	540.39	540.32	0.83
39	40	62	0.003	543.03	543.25	540.32	540.3	2.71
40	41	126	0.003	543.25	542.52	540.3	540.25	2.96
41	43	155	0.003	542.52	540.56	539.85	539.73	2.67
42	43	58	0.003	542.3	540.56	539.77	539.73	2.53
43	48	17	0.003	540.56	541.87	539.73	539.72	0.83
44	45	181	0.003	540.84	542.48	540.01	539.94	0.83
45	46	50	0.003	542.48	543.06	539.94	539.92	2.55
46	47	124	0.003	543.06	542.95	539.92	539.87	3.15
47	48	168	0.003	542.95	541.87	539.87	539.8	3.08
48	49	118	0.003	541.87	541.31	539.72	539.67	2.15
49	50	22	0.003	541.31	541.71	539.67	539.66	1.63
50	51	268	0.003	541.71	543.15	539.66	539.56	2.05
51	52	112	0.003	543.15	542.46	539.56	539.51	3.59
52	53	126	0.003	542.46	542	539.51	539.46	2.94

HYDRAULIC STATEMENT

Node		Length	Slope	Elevation Ground	Elevation Ground	Elevation Invert	Elevation Invert	Depth
FROM	TO	ft	ft/ft	U/S	D/S	U/S	D/S	ft
53	54	157	0.003	542	540.52	539.46	539.4	2.53
54	70	12	0.003	540.52	540.29	539.4	539.39	1.12
55	56	97	0.003	543.57	543.08	542.33	542.25	1.24
56	57	89	0.003	543.08	542.27	541.51	541.43	1.58
57	58	23	0.003	542.27	542.4	541.43	541.43	0.83
58	59	29	0.003	542.4	543.06	541.43	541.41	0.97
59	60	22	0.003	543.06	543.55	541.41	541.4	1.65
60	61	197	0.003	543.55	543.96	541.4	541.33	2.15
61	62	163	0.003	543.96	542.93	541.33	541.26	2.63
62	63	102	0.003	542.93	542.01	541.26	541.18	1.67
63	66	60	0.003	542.01	541.55	540.77	540.72	1.24
64	65	135	0.003	544.31	544.42	543.47	543.42	0.83
65	66	134	0.003	544.42	541.55	540.83	540.72	3.59
66	69	104	0.003	541.55	541.72	540.72	540.68	0.83
67	68	136	0.003	544.51	543.26	542.53	542.42	1.98
68	69	138	0.003	543.26	541.72	540.99	540.88	2.27
69	70	73	0.003	541.72	540.29	539.52	539.46	2.2
70	74	16	0.003	540.29	539.85	539.03	539.02	1.26
71	72	82	0.003	540.69	540.15	539.38	539.32	1.31
72	73	104	0.003	540.15	540.21	539.32	539.28	0.83
73	74	39	0.003	540.21	539.85	539.05	539.02	1.16
74	75	130	0.003	539.85	540.21	539.02	538.97	0.83
75	82	21	0.003	540.21	541.22	538.97	538.96	1.25
76	77	113	0.003	543.98	544.36	543.15	543.1	0.83
77	79	90	0.003	544.36	543.25	542.49	542.42	1.87
78	79	153	0.003	540.96	543.25	540.13	540.07	0.83
79	80	84	0.003	543.25	541.53	540.07	540.03	3.19
80	81	46	0.003	541.53	543.12	540.03	540.01	1.5
81	82	23	0.003	543.12	541.22	540.01	540	3.11
82	83	106	0.003	541.22	541.03	538.96	538.92	2.26
83	84	35	0.003	541.03	540.33	538.92	538.9	2.11
84	ST-TYPE-III-NO SP	120	0.003	540.33	542.36	538.9	538.86	1.43

VILLAGE: DHANRAJPURA (BWN)

TITLE.

HYDRAULIC STATEMENT

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	16-12-2025	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02	19-04-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-KPT-JST-SEW-HS-01	01 OF 01	01

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER CENTRAL

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS www.asianeon.com

PRMSC-KPT-HS-SEW-HS-01

JALWALA

KEY PLAN

Revenue Village: Jalwala Sheet-1

N

District:	Bahawalnagar
Tehsil:	Bahawalnagar
Revenue Village:	Jalwala



ND-16 GL=530.56 IL=529.73
ND-17 GL=531.05 IL=529.89
ND-21 GL=530.6 IL=528.73
ND-22 GL=529.49 IL=528.66
ND-23 GL=530.1 IL=527.76
ND-24 GL=528.39 IL=527.3
GL=528.09 IL=527.26
SEPTIC TANK-T1 Plot Size=1.59 Marla
ND-20 GL=532.05 IL=529.86
ND-19 GL=532.56 IL=531.73
ND-12 GL=532.16 IL=531.32
ND-13 GL=531.79 IL=530.96
ND-14 GL=531.38 IL=530.91
ND-15 GL=533.71 IL=530.4
ND-5 GL=533.65 IL=531.88
Jalwala
ND-18 GL=533.79 IL=532.96
ND-7 GL=533.63 IL=532.8
ND-8 GL=531.49 IL=529.33
ND-10 GL=529.98 IL=528.47
ND-11 GL=529.24 IL=527.78
ND-6 GL=532.7 IL=530.86
ND-4 GL=533.14 IL=531.96
ND-3 GL=533.02 IL=532.18
ND-2 GL=532.02 IL=531.19
ND-1 GL=532.55 IL=531.72
ND-9 GL=530.29 IL=529.46
583'
4" HDPE PIPE ULTIMATE DISPOSAL TO WATER COURSE

Title:
Proposed Drainage Network Plan

Legend:

- SETTLEMENT
- NODE
- 3" HDPE PIPE
- DRAIN TYPE-1
- SULLAGE CARRIER
- SEPTIC TANK
- SETTLEMENT BOUNDARY

Drain Type 1=1843 Rft

Sullage Carrier= 981 Rft

Scale: 1:1,100

1 inch = 92 feet

Paper Size: A3

0 40 80 160

Kilometers

Project:

Engineering Design & Construction Supervision, Punjab Rural Sustainable Water Supply & Sanitation Project, Cluster South III

PRMSC

ENVIRONMENTAL TECHNOLOGIES

ASIAN CONSULTING ENGINEERS www.asiancon.com

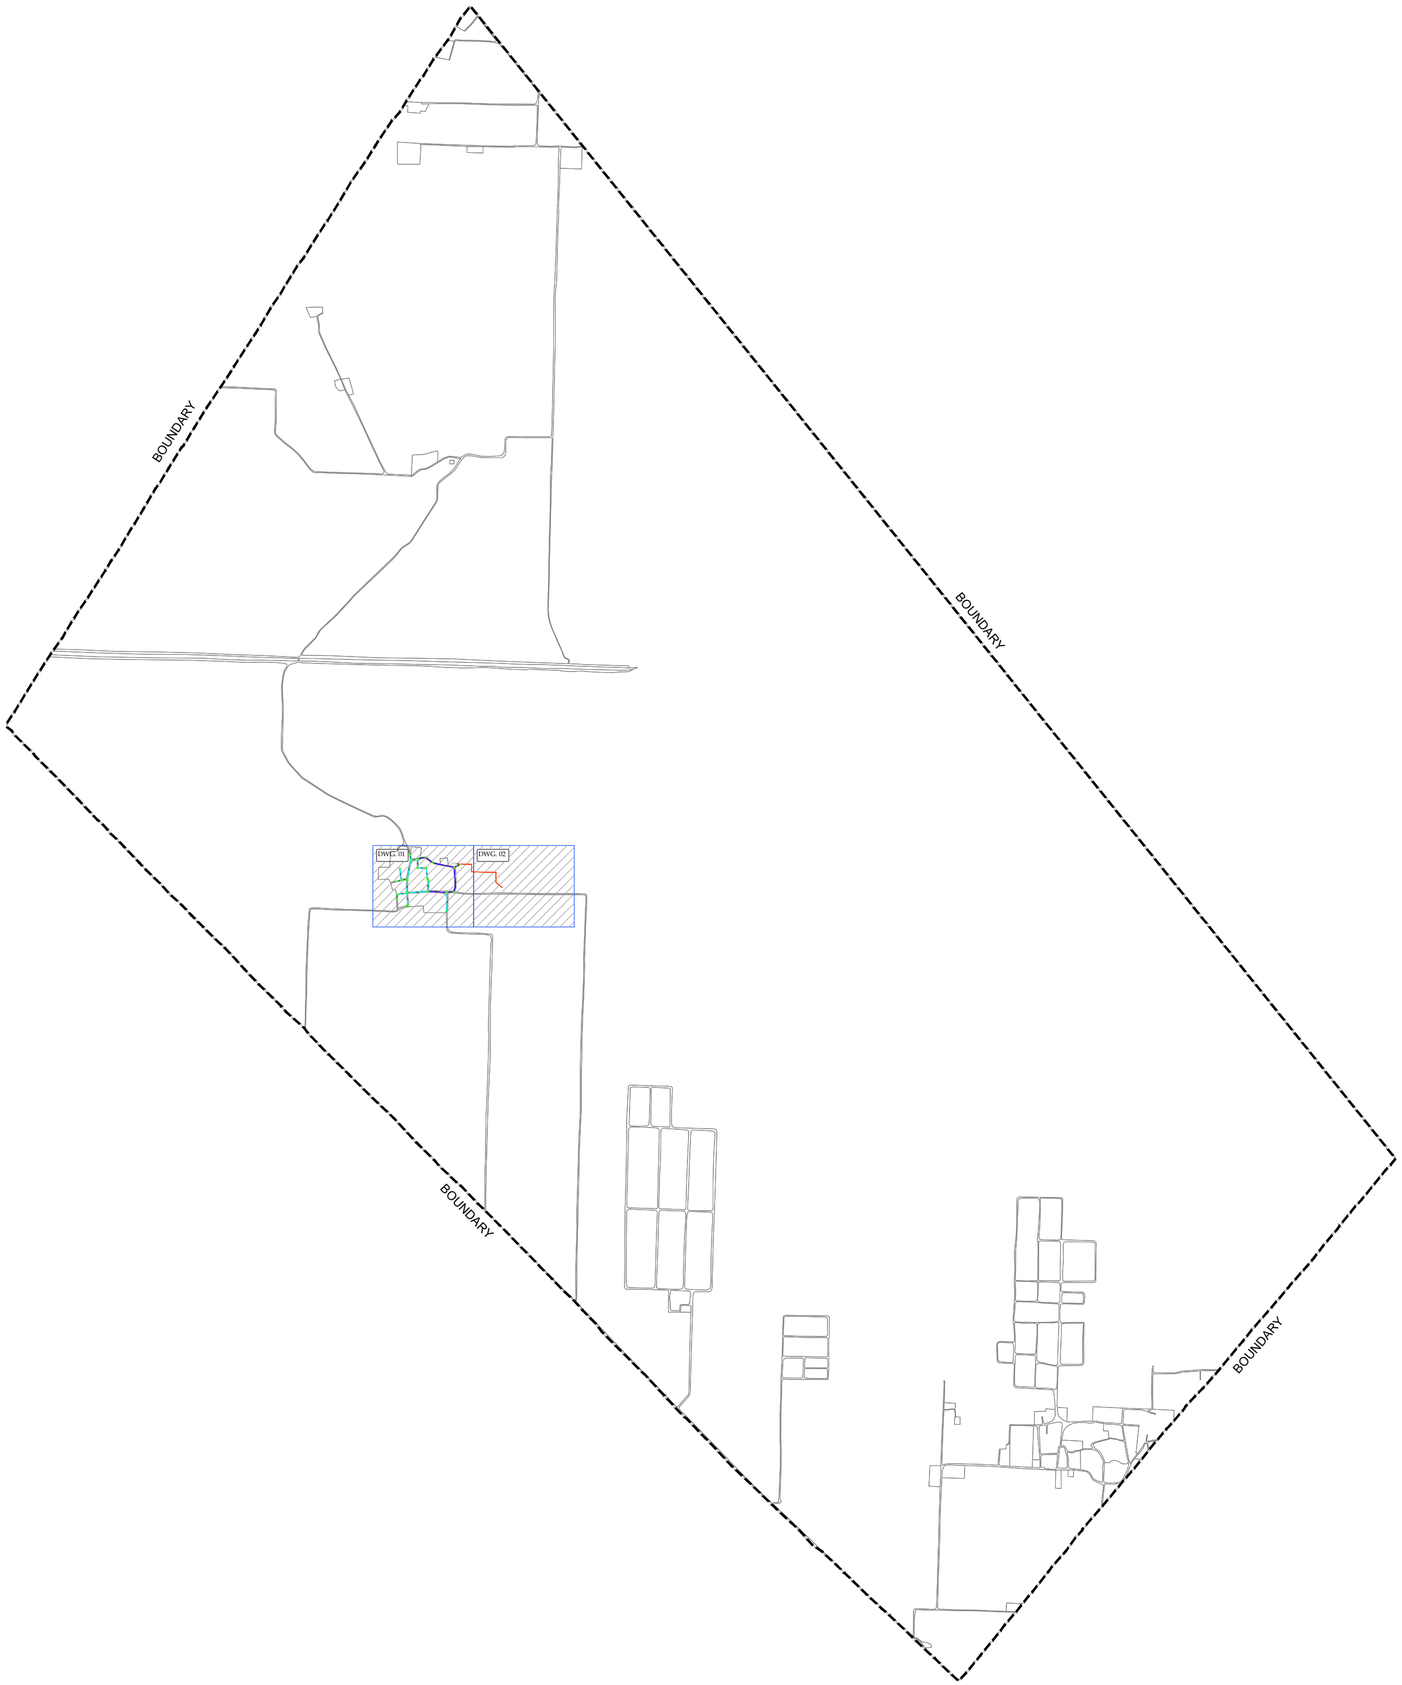

LEGEND:

- DRAIN TYPE - I
- SULLAGE CARRIER
- Ø3" HDPE PIPE
- BOUNDARY

VILLAGE: JAALWALA (BWN)

TITLE.

DRAINAGE SYSTEM KEY PLAN

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 1050'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	20-04-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. HSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº: PRMSC-BWN-JAW-SEW-KP-00

SHEET 00 OF 00

REV 00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT
ASIAN CONSULTING ENGINEERS
www.asianeng.com.pk

PRMSC-BWN-JAW-SEW-KP-00

LAYOUT PLAN

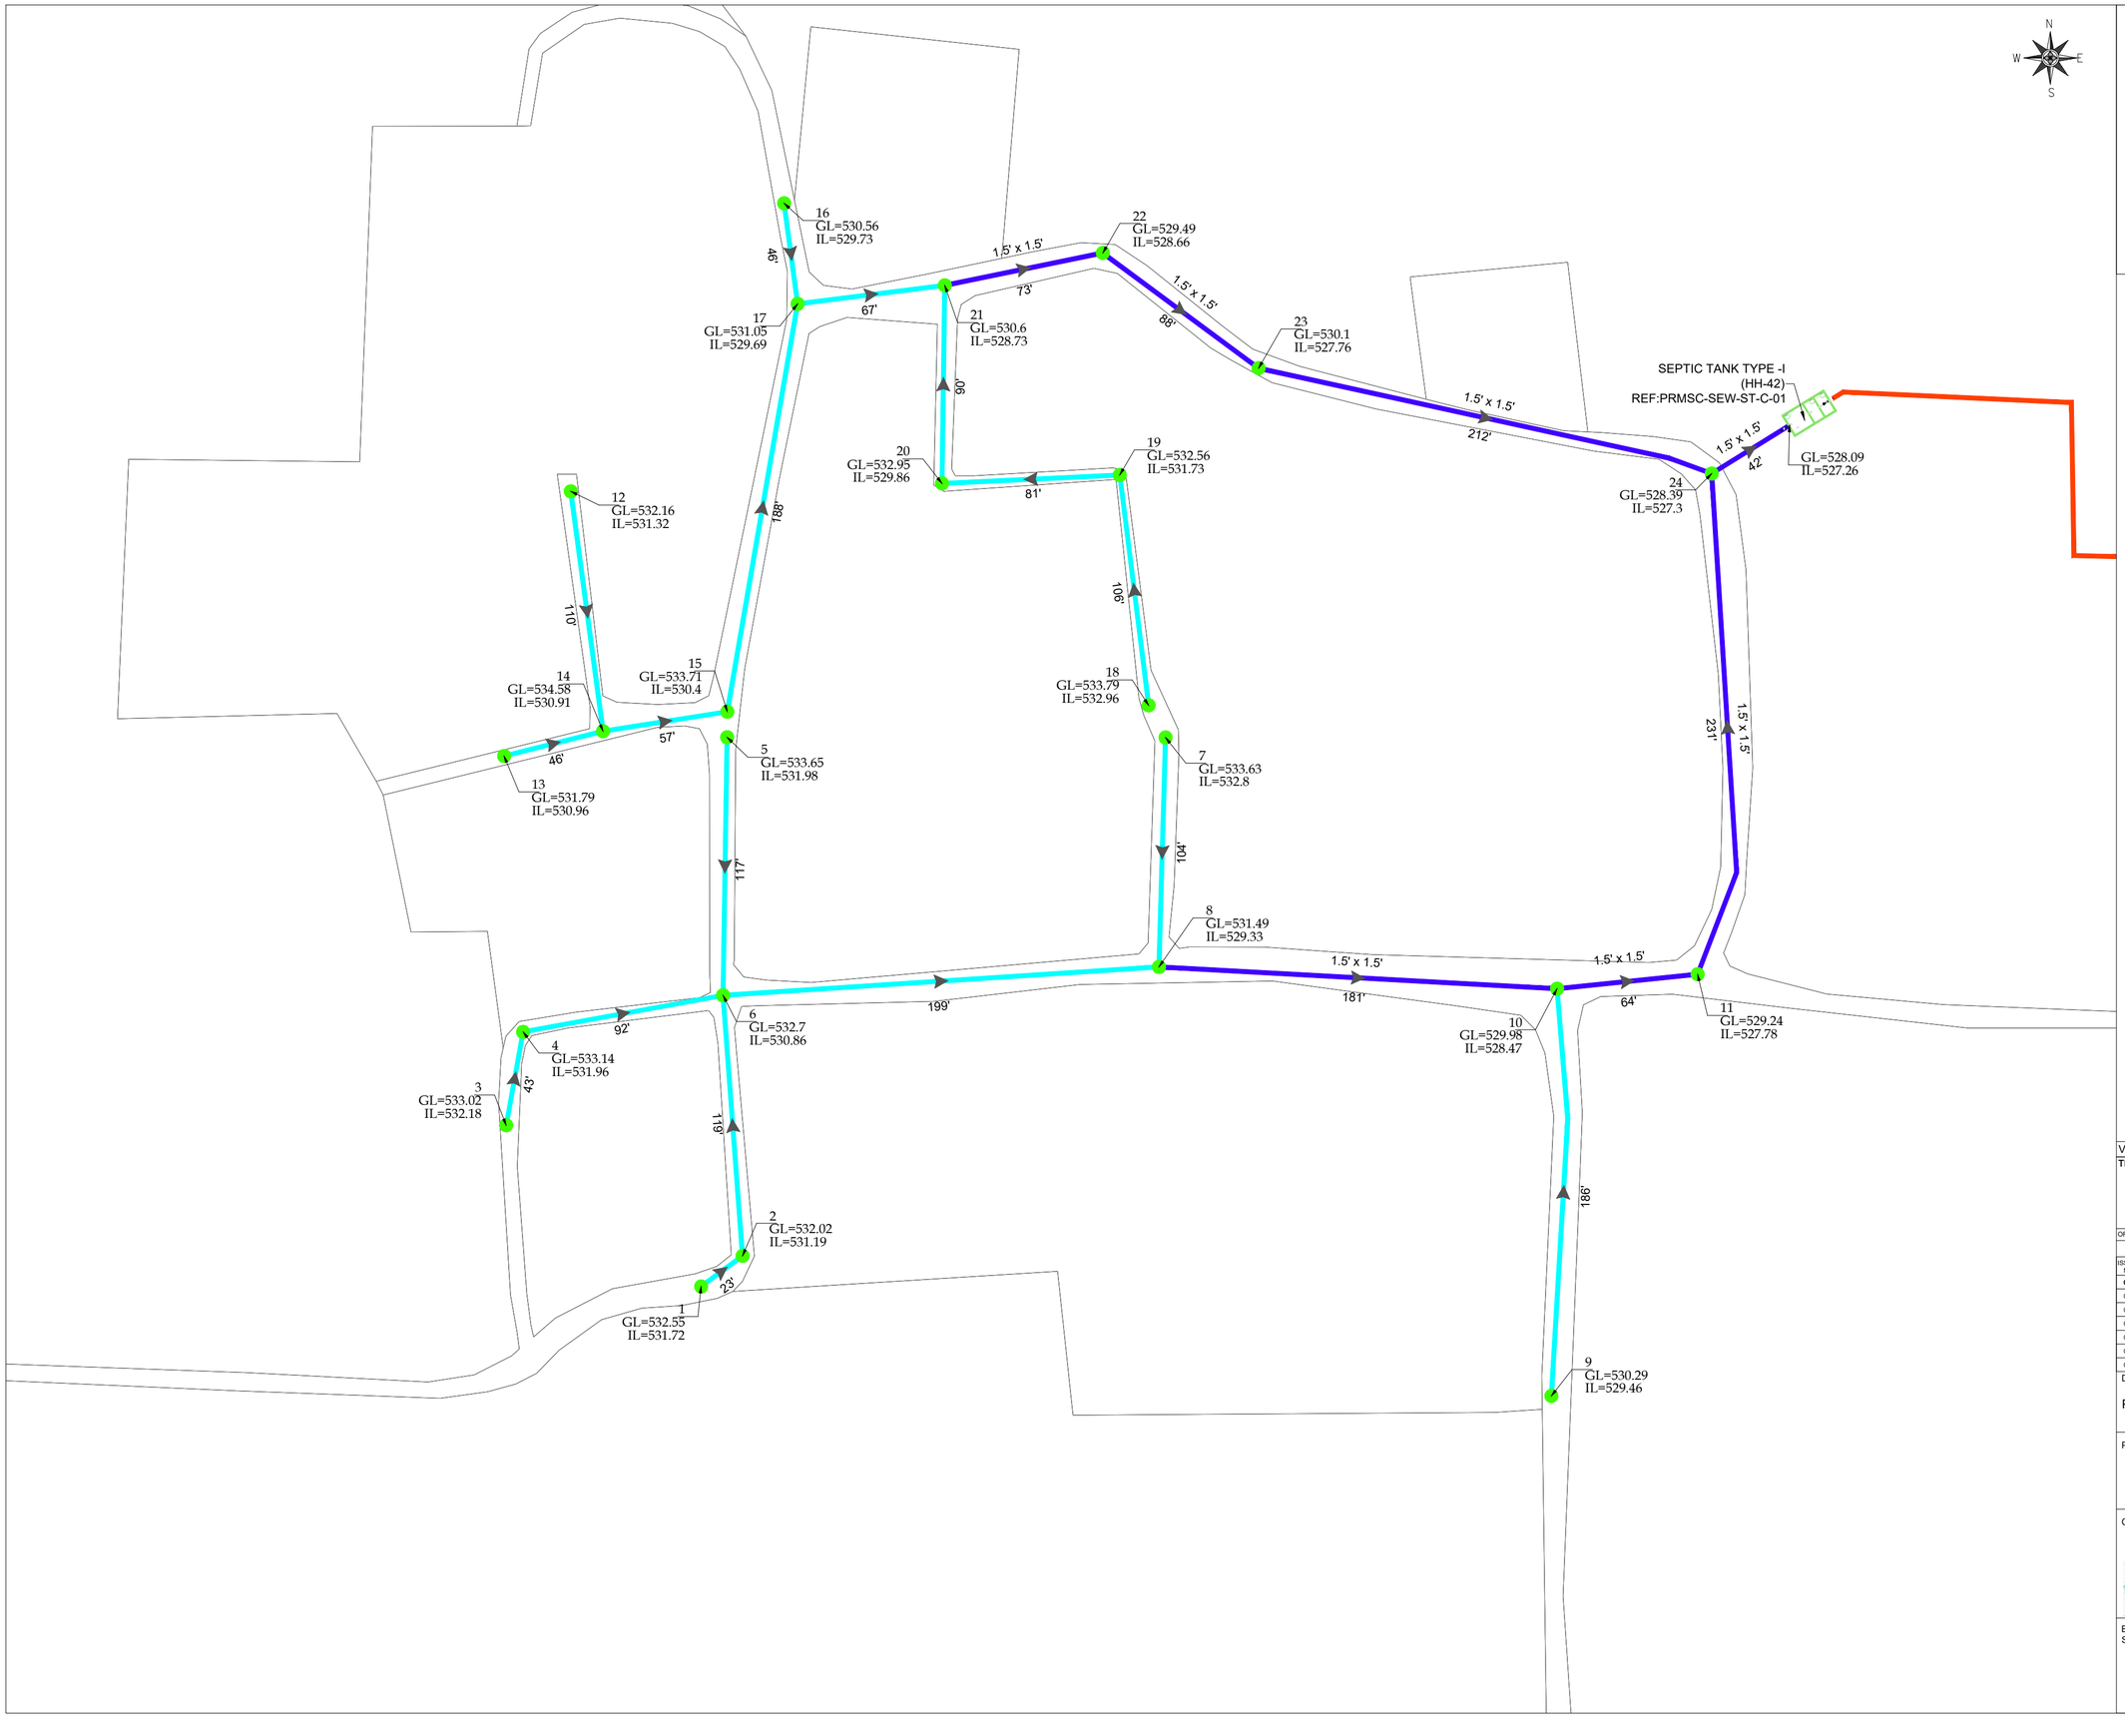

KEY PLAN

LEGEND:

- DRAIN TYPE - I
- SULLAGE CARRIER
- Ø3" HDPE PIPE
- BOUNDARY

VILLAGE: JAALWALA (BWN)

TITLE.

DRAINAGE SYSTEM LAYOUT PLAN-01

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	20-04-2026	DETAILED DESIGN	MUNEEB	ENGR FAIEZ	ENGR IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº: PRMSC-BWN-JAW-SEW-LP-01

SHEET 01 OF 02

REV 00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

PRMSC-BWN-JAW-SEW-LP-01

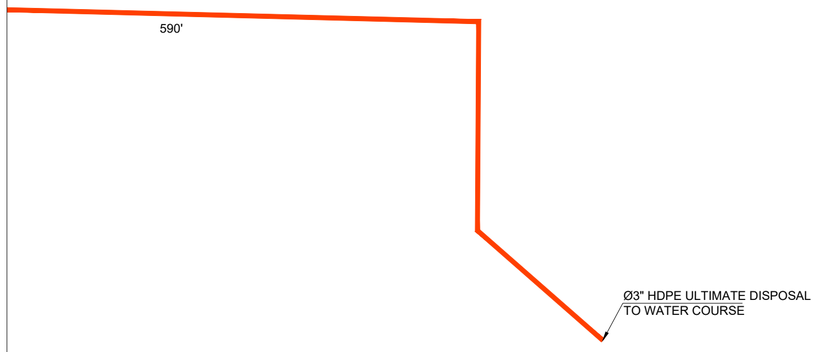

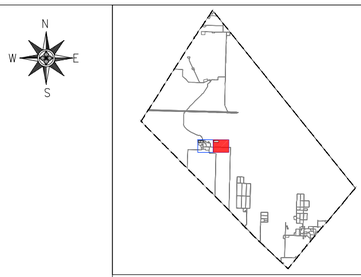

KEY PLAN

LEGEND:

- DRAIN TYPE - I
- SULLAGE CARRIER
- Ø3" HDPE PIPE
- BOUNDARY

VILLAGE: JAALWALA (BWN)

TITLE.

DRAINAGE SYSTEM LAYOUT PLAN-02

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	20-04-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. HSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-JAW-SEW-LP-02	02 OF 02	00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:
ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

PRMSC-BWN-JAW-SEW-LP-02

HYDRAULIC STATEMENT								
Node		Length	Slope	Elevation Ground	Elevation Ground	Invert	Invert	Depth
FROM	TO	ft	ft/ft	U/S	D/S	U/S	D/S	ft
1	2	23	0.022	532.55	532.02	531.72	531.19	0.83
2	6	119	0.001	532.02	532.7	531.19	531.07	0.83
3	4	43	0.001	533.02	533.14	532.18	532.14	0.83
4	6	92	0.001	533.14	532.7	531.96	531.86	1.19
5	6	117	0.001	533.65	532.7	531.98	531.86	1.67
6	8	199	0.001	532.7	531.49	530.86	530.66	1.84
7	8	104	0.033	533.63	531.49	532.8	529.33	0.83
8	10	181	0.001	531.49	529.98	529.33	529.15	2.16
9	10	186	0.005	530.29	529.98	529.46	528.47	0.83
10	11	64	0.001	529.98	529.24	528.47	528.4	1.51
11	24	231	0.001	529.24	528.39	527.78	527.55	1.45
12	14	110	0.001	532.16	534.58	531.32	531.21	0.83
13	14	46	0.001	531.79	534.58	530.96	530.91	0.83
14	15	57	0.001	534.58	533.71	530.91	530.85	3.67
15	17	188	0.001	533.71	531.05	530.4	530.22	3.3
16	17	46	0.001	530.56	531.05	529.73	529.69	0.83
17	21	67	0.001	531.05	530.6	529.69	529.62	1.36
18	19	106	0.012	533.79	532.56	532.96	531.73	0.83
19	20	81	0.001	532.56	532.95	531.73	531.65	0.83
20	21	90	0.001	532.95	530.6	529.86	529.77	3.09
21	22	73	0.001	530.6	529.49	528.73	528.66	1.87
22	23	88	0.001	529.49	530.1	528.66	528.57	0.83
23	24	212	0.001	530.1	528.39	527.76	527.55	2.34
24	ST Type-I (HH=42)	42	0.001	528.39	528.09	527.3	527.26	1.09

VILLAGE: JAALWALA (BWN)

TITLE.

HYDRAULIC STATEMENT

ORIGINAL :		DATE :		SCALE :	
A2		JULY, 2025			
ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	20-04-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº: PRMSC-BWN-JAW-SEW-HS-01 | SHEET 01 OF 01 | REV 00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT
ASIAN CONSULTING ENGINEERS www.asiancon.com

PRMSC-BWN-JAW-SEW-HS-00

JANOOWALA

KEY PLAN

Revenue Village: Janoowala Main Sheet

District:	Bahawalnagar
Tehsil:	Bahawalnagar
Revenue Village:	Janoowala

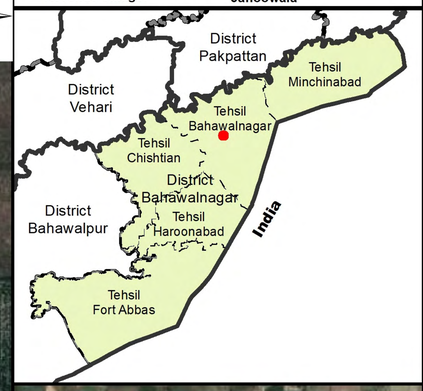

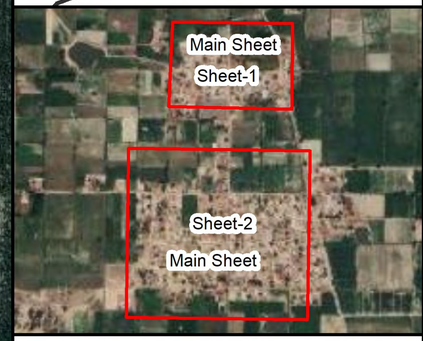

Title:
Proposed Drainage Network Plan

Legend:

- SETTLEMENT
- NODE
- 3" HDPE PIPE
- DRAIN TYPE-1
- SULLAGE CARRIER
- SEPTIC TANK
- SETTLEMENT BOUNDARY

Drain Type 1=9363 Rft

Sullage Carrier=3329 Rft

Scale: 1:2,600

1 inch = 217 feet

Paper Size: A3

0 40 80 160

Kilometers

Project:
Engineering Design & Construction Supervision, Punjab Rural Sustainable Water Supply & Sanitation Project, Cluster South III

PRWSC

ENVIRONMENTAL TECHNOLOGIES

ASIAN CONSULTING ENGINEERS www.asiancon.com

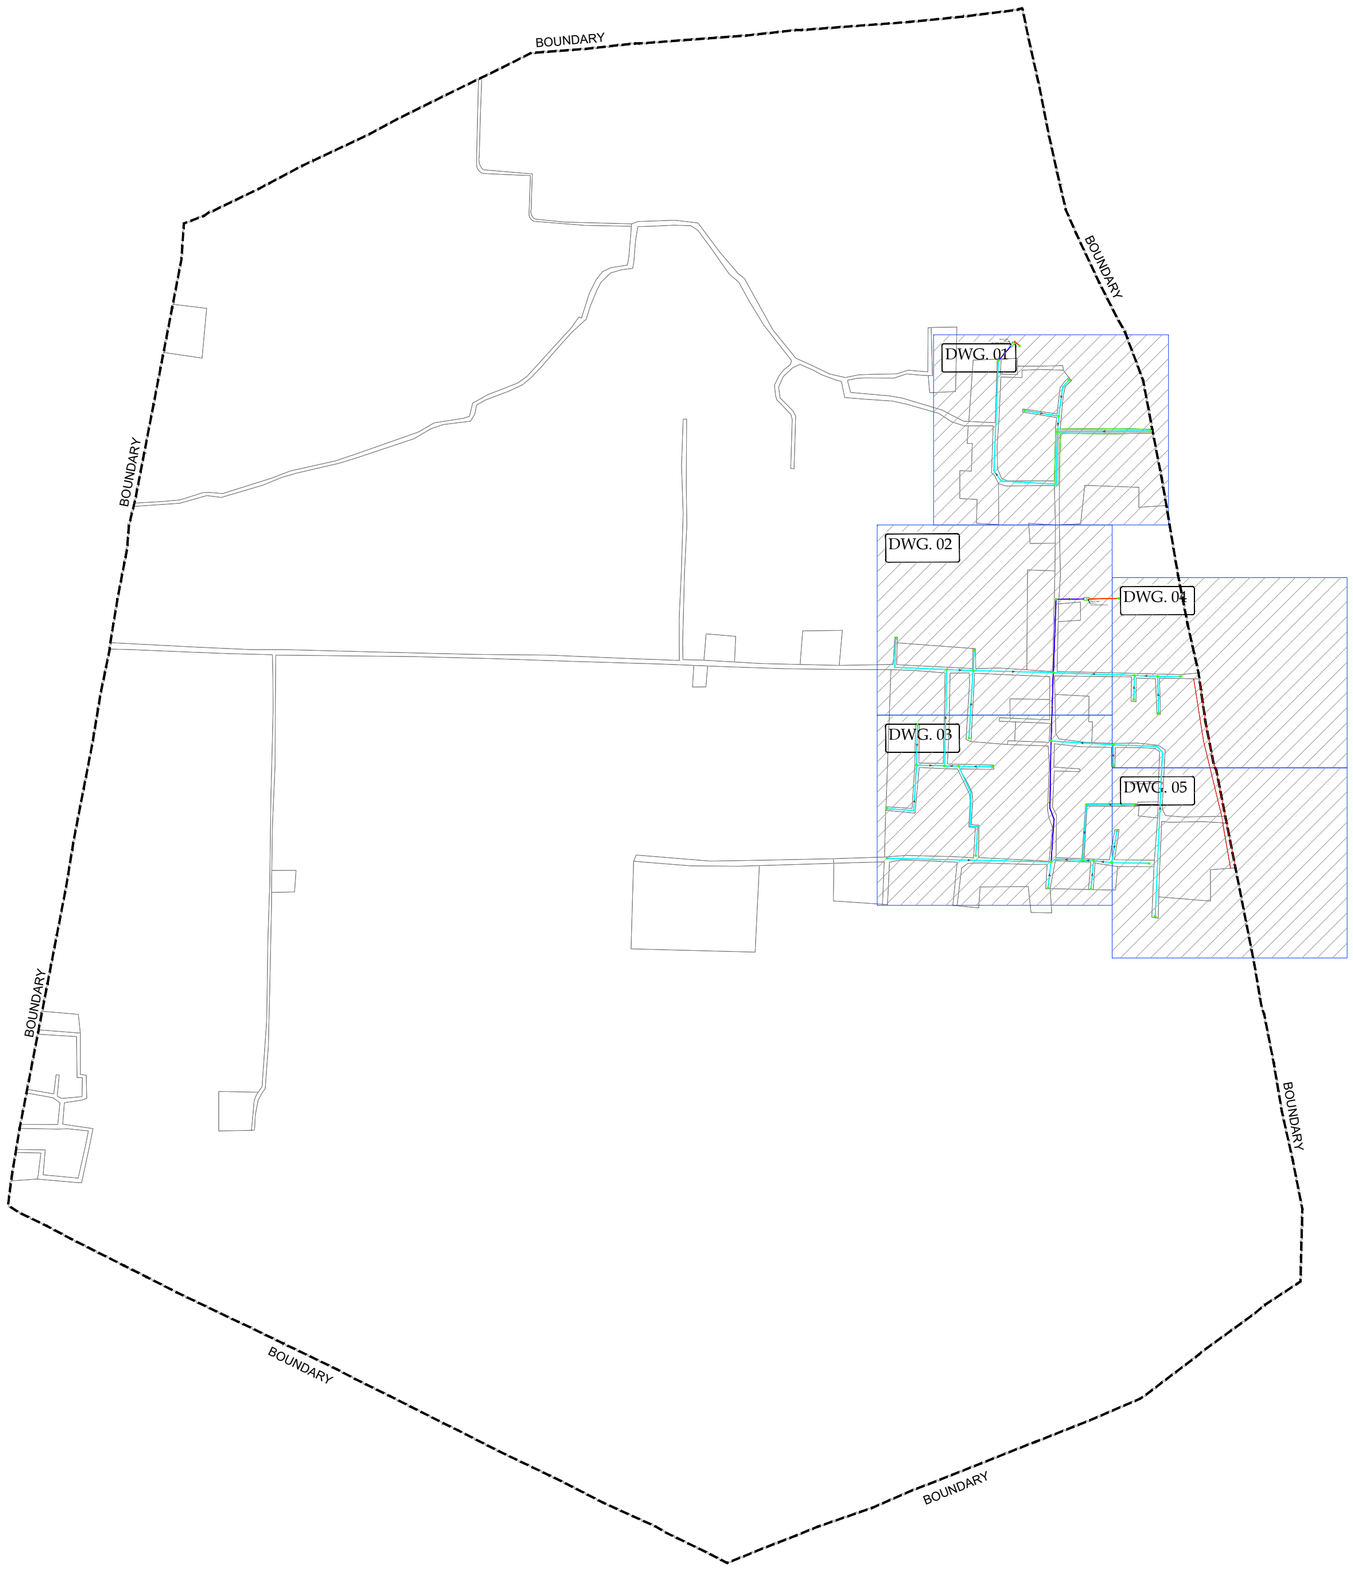

LEGEND:

- DRAIN TYPE - I
- SULLAGE CARRIER
- Ø3" HDPE PIPE
- EXISTING SOLING
- METALLED ROAD
- BOUNDARY

VILLAGE: JANOOWALA (BWN)

TITLE.

DRAINAGE SYSTEM KEY PLAN

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 450'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	02-01-2026	DETAILED DESIGN	HANNAN	ENGR. FAIEZ	ENGR. HSANULHAQ
02	20-04-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. HSANULHAQ
03					
04					
05					
06					
07					

DRAWING N°:	SHEET	REV
PRMSC-BWN-JNW-SEW-KP-00	00 OF 00	01

PROJECT:

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:

PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT

ASIAN CONSULTING ENGINEERS www.asiancon.com.pk

PRMSC-BWN-JNW-SEW-KP-00

LAYOUT PLAN

Revenue Village: Janoowala Sheet-1

District:	Bahawalnagar
Tehsil:	Bahawalnagar
Revenue Village:	Janoowala

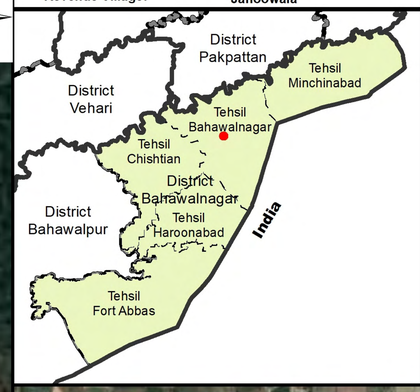

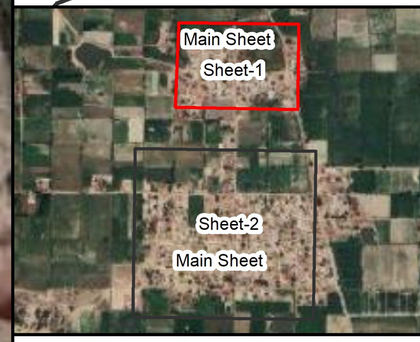

GL=500.26
IL=499.29

SEPTIC TANK-T1
Plot Size=1.59 Marla

1.5"

FINAL ULTIMATE DISPOSAL TO WATER COURSE

75'
1.5" x 1.5"

ND-6
GL=501.25
IL=499.47

ND-2
GL=502.64
IL=501.8

180'

ND-3
GL=504.09
IL=502.73

142'

ND-4
GL=503
IL=501.48

Kapur Janu Khanu

ND-5
GL=503.67
IL=501.36

ND-1
GL=503.45
IL=502.62

Title:
Proposed Drainage Network Plan

Legend:

- SETTLEMENT
- NODE
- 3" HDPE PIPE
- DRAIN TYPE-1
- SULLAGE CARRIER
- SEPTIC TANK
- SETTLEMENT BOUNDARY

Drain Type 1=9363 Rft
Sullage Carrier=3329 Rft

Scale: 1:900
1 inch = 75 feet
Paper Size: A3

0 40 80 160
Kilometers

Project:
Engineering Design & Construction Supervision, Punjab Rural Sustainable Water Supply & Sanitation Project, Cluster South III

PRSSC
ENVIRONMENTAL TECHNOLOGIES
ASIAN CONSULTING ENGINEERS www.asiancon.com

Revenue Village: Janoowala Sheet-2

GL=504.52
IL=500.59

SEPTIC TANK-T5
Plot Size=3.42
Marla

ND-40
GL=503.88
IL=500.8

ND-29
GL=504.86
IL=503.82

ND-32
GL=504.64
IL=503.8

ND-30
GL=506.98
IL=502.58

ND-33
GL=504.54
IL=502.97

ND-39
GL=505.05
IL=501.4

ND-36
GL=504.48
IL=504.45

ND-38
GL=504.98
IL=504.59

ND-35
GL=505.78
IL=504.95

ND-37
GL=505.24
IL=504.04

ND-34
GL=507.56
IL=506.72

ND-26
GL=504.87
IL=504.03

ND-31
GL=504.78
IL=503.92

ND-21
GL=505.85
IL=501.93

ND-20
GL=505.9
IL=503.52

ND-27
GL=504.71
IL=503.6

ND-28
GL=506.12
IL=503.37

ND-24
GL=506.03
IL=504.61

ND-23
GL=507.13
IL=505.75

ND-19
GL=507.01
IL=505.4

Kapur
Muhammad
Amin

ND-25
GL=505.02
IL=504.19

ND-9
GL=508.45
IL=507.01

ND-8
GL=509.37
IL=508.41

ND-11
GL=508.68
IL=507.85

ND-7
GL=505.12
IL=504.29

ND-22
GL=506.25
IL=505.42

ND-17
GL=506.92
IL=502.95

ND-15
GL=506.93
IL=505.95

ND-12
GL=508.5
IL=508.34

ND-40
GL=509.48
IL=508.28

ND-14
GL=506.87
IL=506.04

ND-16
GL=505.74
IL=504.91

ND-13
GL=507.31
IL=506.48

ND-18
GL=508.12
IL=505.28

N

District:	Bahawalnagar
Tehsil:	Bahawalnagar
Revenue Village:	Janoowala

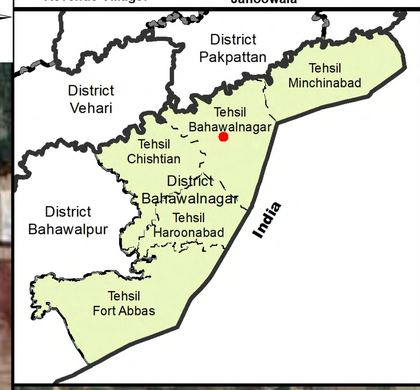

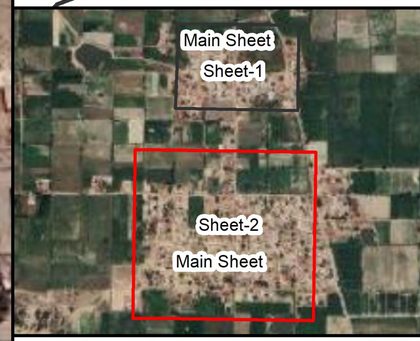

Title:
Proposed Drainage Network Plan

Legend:

- SETTLEMENT
- NODE
- 3" HDPE PIPE
- DRAIN TYPE-1
- SULLAGE CARRIER
- SEPTIC TANK
- SETTLEMENT BOUNDARY

Drain Type 1=9363 Rft
Sullage Carrier=3329 Rft

Scale: 1:1,500
1 inch = 125 feet
Paper Size: A3

0 40 80 160
Kilometers

Project:
Engineering Design & Construction Supervision, Punjab Rural Sustainable Water Supply & Sanitation Project, Cluster South III

PRSSC

ENVIRONMENTAL TECHNOLOGIES

ASIAN CONSULTING ENGINEERS
www.asiancon.com

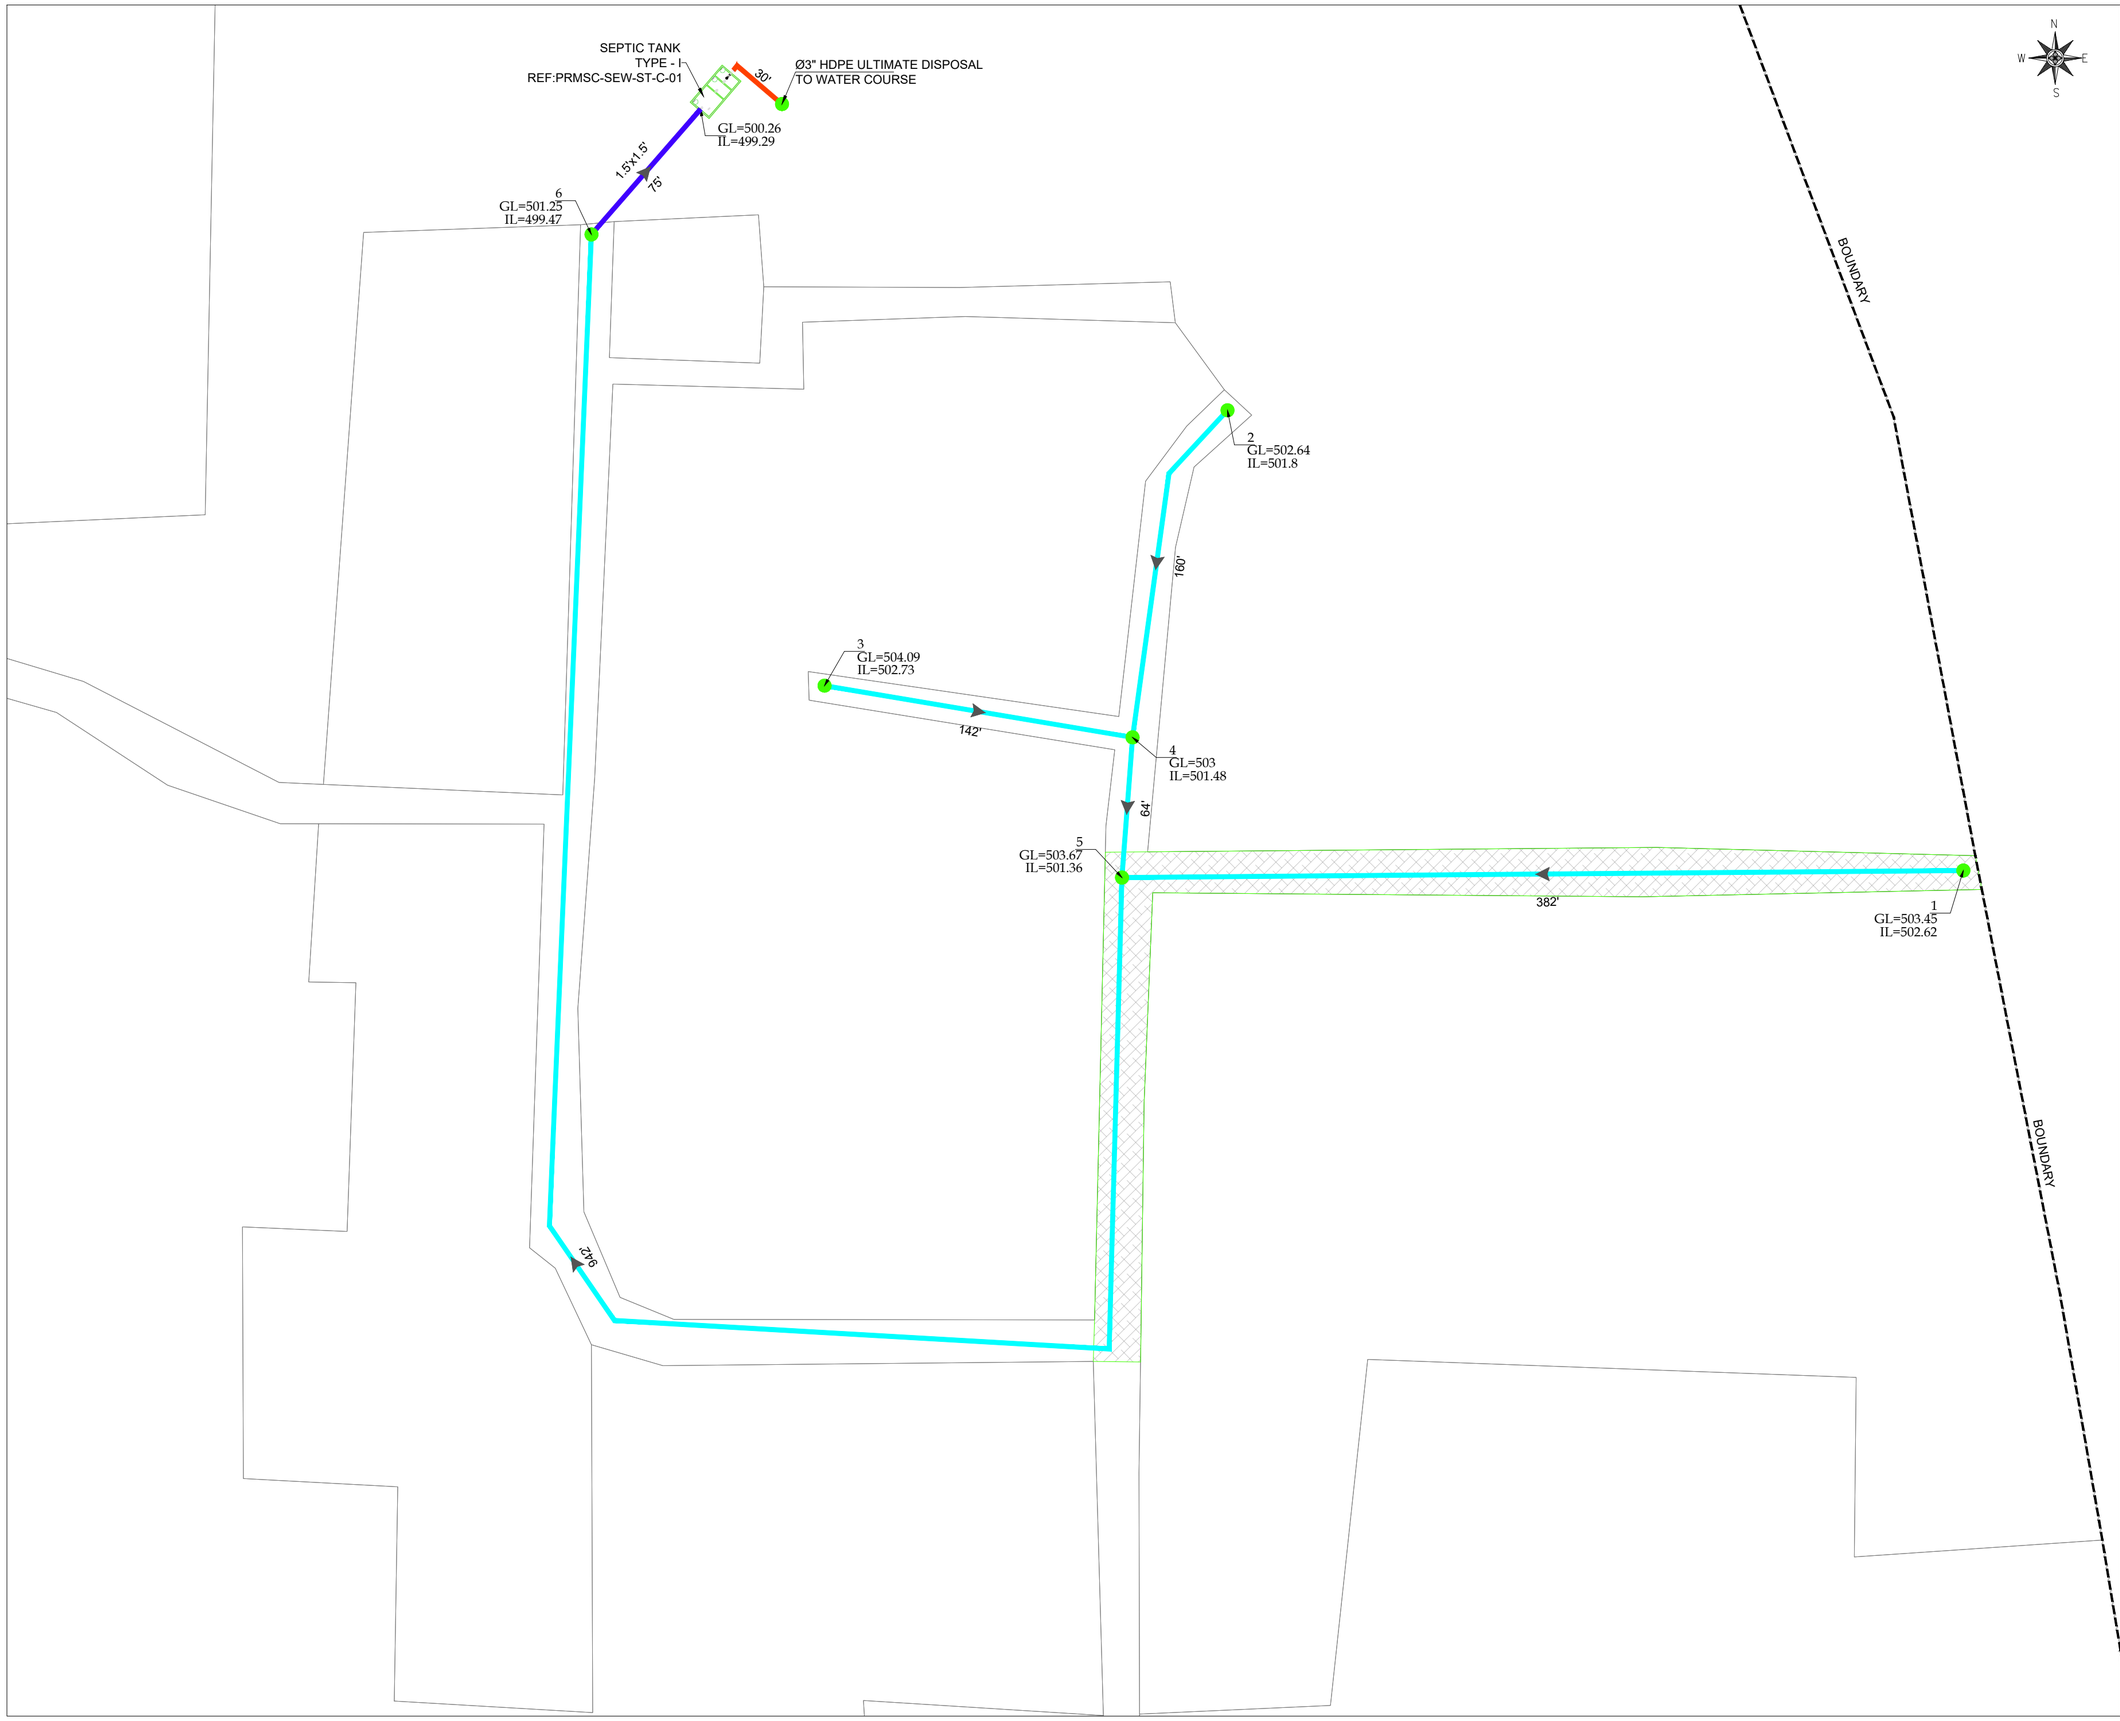

PRMSC-BWN-JNW-SEW-LP-01

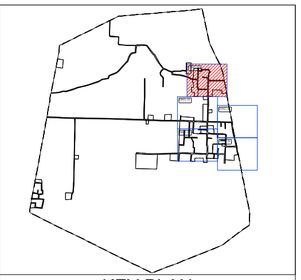

LEGEND: KEY PLAN

- DRAIN TYPE - I
- SULLAGE CARRIER
- Ø3" HDPE PIPE
- EXISTING SOLING
- METALLED ROAD
- BOUNDARY

VILLAGE: JANOOWALA (BWN)

TITLE.

DRAINAGE SYSTEM LAYOUT PLAN-01

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	02-01-2026	DETAILED DESIGN	HANNAN	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02	20-04-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-JNW-SEW-LP-01	01 OF 05	01

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS
www.asianceh.com JV

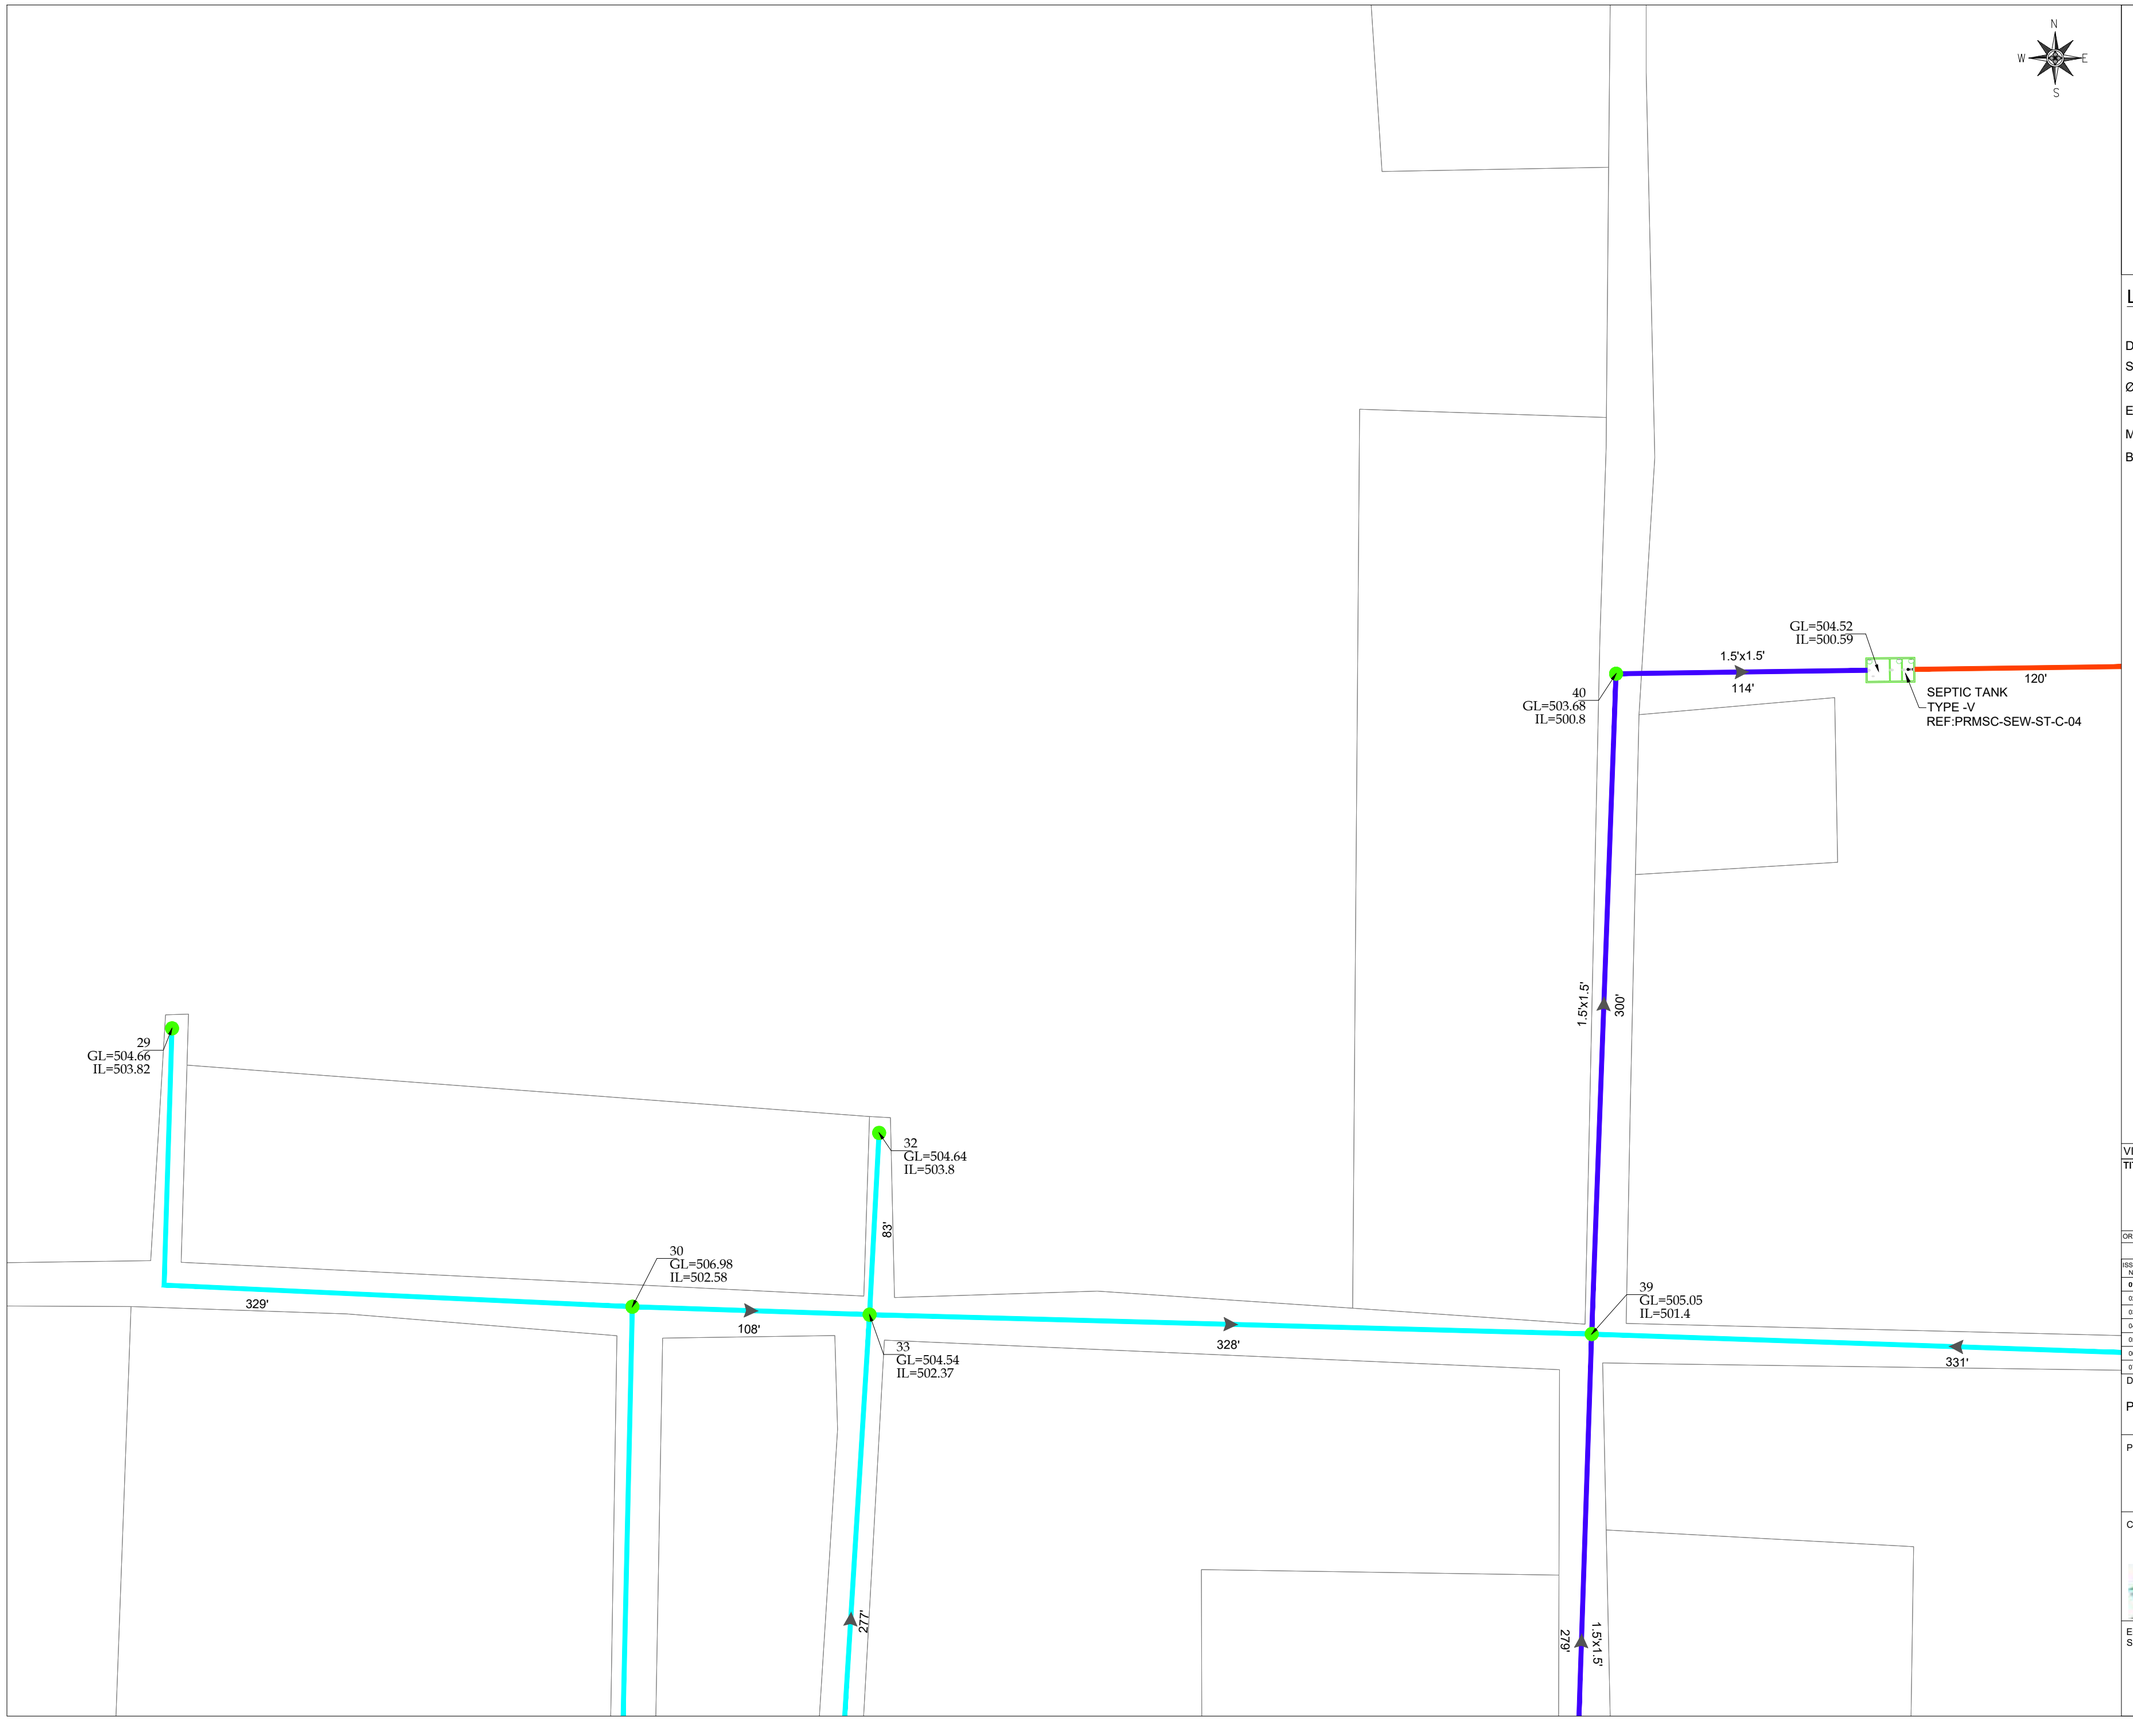

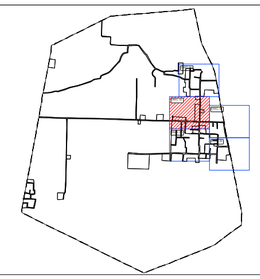

LEGEND: KEY PLAN

- DRAIN TYPE - I
- SULLAGE CARRIER
- Ø3" HDPE PIPE
- EXISTING SOLING
- METALLED ROAD
- BOUNDARY

VILLAGE: JANOOWALA (BWN)

TITLE.

DRAINAGE SYSTEM LAYOUT PLAN-02

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	02-01-2026	DETAILED DESIGN	HANNAN	ENGR FAIEZ	ENGR HSAN-UL-HAQ
02	20-04-2026	DETAILED DESIGN	MUNEEB	ENGR FAIEZ	ENGR HSAN-UL-HAQ
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-JNW-SEW-LP-02	02 OF 05	01

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:
ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

PRMSC-BWN-JNW-SEW-LP-02

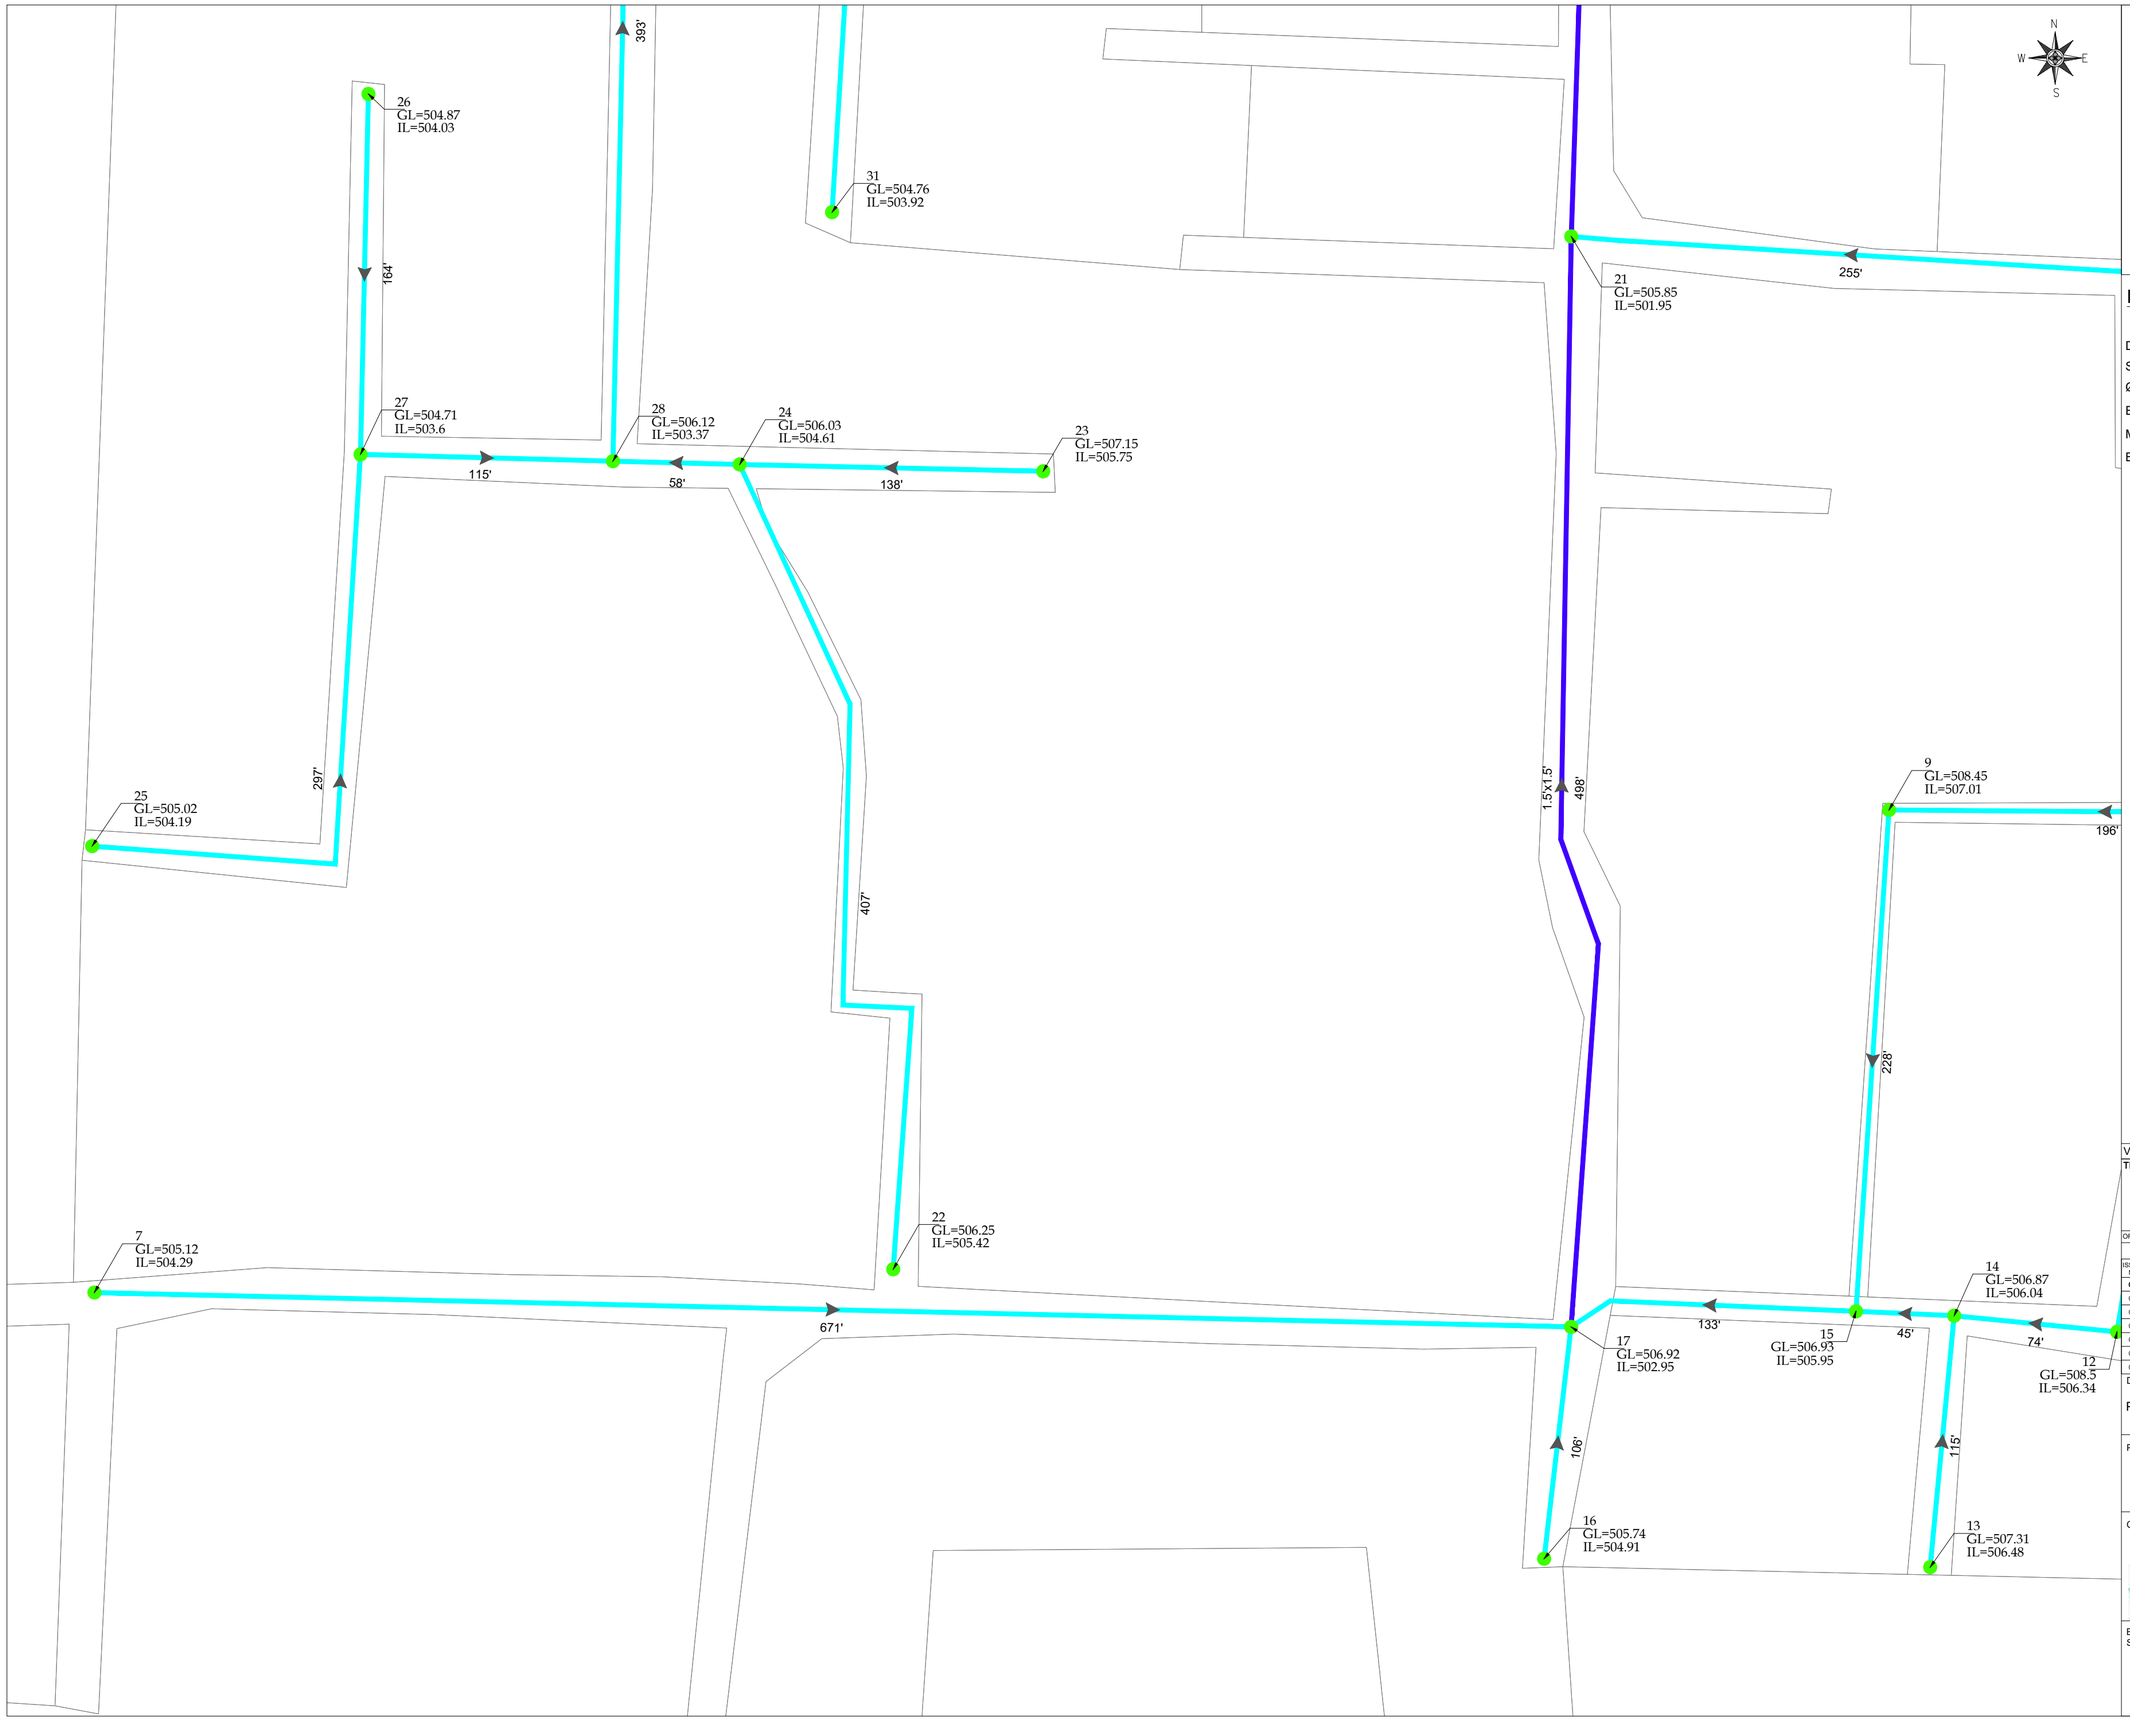

LEGEND: KEY PLAN

- DRAIN TYPE - I
- SULLAGE CARRIER
- Ø3" HDPE PIPE
- EXISTING SOLING
- METALLED ROAD
- BOUNDARY

VILLAGE: JANOOWALA (BWN)

TITLE.

DRAINAGE SYSTEM LAYOUT PLAN-03

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	02-01-2026	DETAILED DESIGN	HANNAN	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02	20-04-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
03					
04					
05					
06					
07					

DRAWING N°:	SHEET	REV
PRMSC-BWN-JNW-SEW-LP-03	03 OF 05	01

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:
ASIAN CONSULTING ENGINEERS
www.asiacon.com.pk

PRMSC-BWN-JNW-SEW-LP-03

Ø3" HDPE ULTIMATE DISPOSAL
TO WATER COURSE

BOUNDARY

36
GL=504.38
IL=503.55

38
GL=504.48
IL=503.45

96'

93'

35
GL=505.78
IL=504.95

99'

37
GL=505.24
IL=504.04

150'

34
GL=507.56
IL=506.72

BOUNDARY

20
GL=505.9
IL=503.52

84'

19
GL=507.01
IL=505.4

PRMSC-BWN-JNW-SEW-LP-04

N
W
E
S

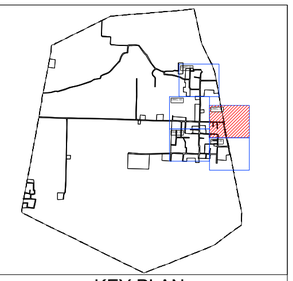

KEY PLAN

LEGEND:

DRAIN TYPE - I
SULLAGE CARRIER
Ø3" HDPE PIPE
EXISTING SOLING
METALLED ROAD
BOUNDARY

VILLAGE: JANOOWALA (BWN)

TITLE.

DRAINAGE SYSTEM LAYOUT PLAN-04

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	02-01-2026	DETAILED DESIGN	HANNAN	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02	20-04-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
03					
04					
05					
06					
07					

DRAWING Nº: PRMSC-BWN-JNW-SEW-LP-04

SHEET 04 OF 05

REV 01

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS
www.asiaecon.com.pv

PRMSC-BWN-JNW-SEW-LP-05

N
W
E
S

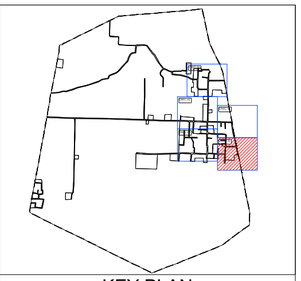

LEGEND: KEY PLAN

- DRAIN TYPE - I
- SULLAGE CARRIER
- Ø3" HDPE PIPE
- EXISTING SOLING
- METALLED ROAD
- BOUNDARY

VILLAGE: JANOOWALA (BWN)

TITLE.

DRAINAGE SYSTEM LAYOUT PLAN-05

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	02-01-2026	DETAILED DESIGN	HANNAN	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02	20-04-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-JNW-SEW-LP-05	05 OF 05	01

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:
ASIAN CONSULTING ENGINEERS
www.asiacon.com.pk

HYDRAULIC STATEMENT

Node		Length	Slope	Elevation Ground	Elevation Ground	Invert	Invert	Depth
FROM	TO	ft	ft/ft	U/S	D/S	U/S	D/S	ft
1	5	382	0.003	503.45	503.67	502.62	501.36	0.83
2	4	160	0.002	502.64	503	501.8	501.48	0.83
3	4	142	0.004	504.09	503	502.73	502.17	1.36
4	5	64	0.002	503	503.67	501.48	501.36	1.52
5	6	941	0.002	503.67	501.25	501.36	499.47	2.32
6	Septic Tank Type I	75	0.002	501.25	500.26	499.47	499.32	1.77
7	17	671	0.002	505.12	506.92	504.29	502.95	0.83
8	9	196	0.004	509.37	508.45	508.41	507.62	0.96
9	15	228	0.004	508.45	506.93	507.01	506.09	1.45
10	12	153	0.004	509.48	508.5	508.28	507.66	1.2
11	12	130	0.002	508.68	508.5	507.85	507.59	0.83
12	14	74	0.004	508.5	506.87	506.34	506.04	2.16
13	14	115	0.004	507.31	506.87	506.48	506.04	0.83
14	15	45	0.002	506.87	506.93	506.04	505.95	0.83
17	15	133	0.002	506.92	506.93	505.69	505.95	0.97
16	17	106	0.002	505.74	506.92	504.91	504.69	0.83
17	21	498	0.002	506.92	505.85	502.95	501.95	3.97
18	20	883	0.002	506.12	505.9	505.28	503.52	0.83
19	20	84	0.004	507.01	505.9	505.4	505.07	1.6
20	21	255	0.002	505.9	505.85	503.52	503.01	2.38
21	39	279	0.002	505.85	505.05	501.95	501.4	3.89
22	24	407	0.002	506.25	506.03	505.42	504.61	0.83
23	24	138	0.004	507.15	506.03	505.75	505.2	1.4
28	24	58	0.002	506.12	506.03	504.49	504.61	1.42
25	27	297	0.002	505.02	504.71	504.19	503.6	0.83
26	27	164	0.003	504.87	504.71	504.03	503.6	0.83
27	28	115	0.002	504.71	506.12	503.6	503.37	1.12
28	30	393	0.002	506.12	506.98	503.37	502.58	2.75
29	30	329	0.004	504.66	506.98	503.82	502.58	0.83
30	33	108	0.002	506.98	504.54	502.58	502.37	4.4
31	33	277	0.002	504.76	504.54	503.92	503.37	0.83
32	33	83	0.002	504.64	504.54	503.8	503.64	0.83
33	39	328	0.003	504.54	505.05	502.37	501.4	2.17
34	36	150	0.021	507.56	504.38	506.72	503.55	0.83
35	36	93	0.015	505.78	504.38	504.95	503.55	0.83
36	38	96	0.001	504.38	504.48	503.55	503.45	0.83
37	38	99	0.004	505.24	504.48	504.04	503.65	1.2
38	39	331	0.002	504.48	505.05	503.45	502.79	1.03
39	40	300	0.002	505.05	503.68	501.4	500.8	3.65
40	Septic Tank Type V	114	0.002	503.68	504.52	500.8	500.57	2.89

VILLAGE: JANOOWALA (BWN)

TITLE.

HYDRAULIC STATEMENT

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	02-01-2026	DETAILED DESIGN	HANNAN	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02	20-04-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
03					
04					
05					
06					
07					

DRAWING Nº: PRMSC-BWN-JNW-SEW-HS-00

SHEET 01 OF 01

REV 01

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT
ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

PRMSC-BWN-BIB-SEW-HS-00

KHAWAJA BUX BODLA

KEY PLAN

Revenue Village: Khawaja Bux Bodla Sheet-1

GL=562.23
IL=561.40

SEPTIC TANK-T1
Plot Size=1.59
Marla

District:	Bahawalnagar
Tehsil:	Bahawalnagar
Revenue Village:	Khawaja Bux Bodla

Title:
Proposed Drainage Network Plan

Legend:

- NODE
- 3" HDPE PIPE
- DRAIN TYPE-1
- SULLAGE CARRIER
- SEPTIC TANK
- SETTLEMENT BOUNDARY

Drain Type 1=1155 Rft
Sullage Carrier=924 Rft

Scale: 1:1,000
1 inch = 83 feet
Paper Size: A3

0 40 80 160
Kilometers

Project:
Engineering Design & Construction Supervision, Punjab Rural Sustainable Water Supply & Sanitation Project, Cluster South III

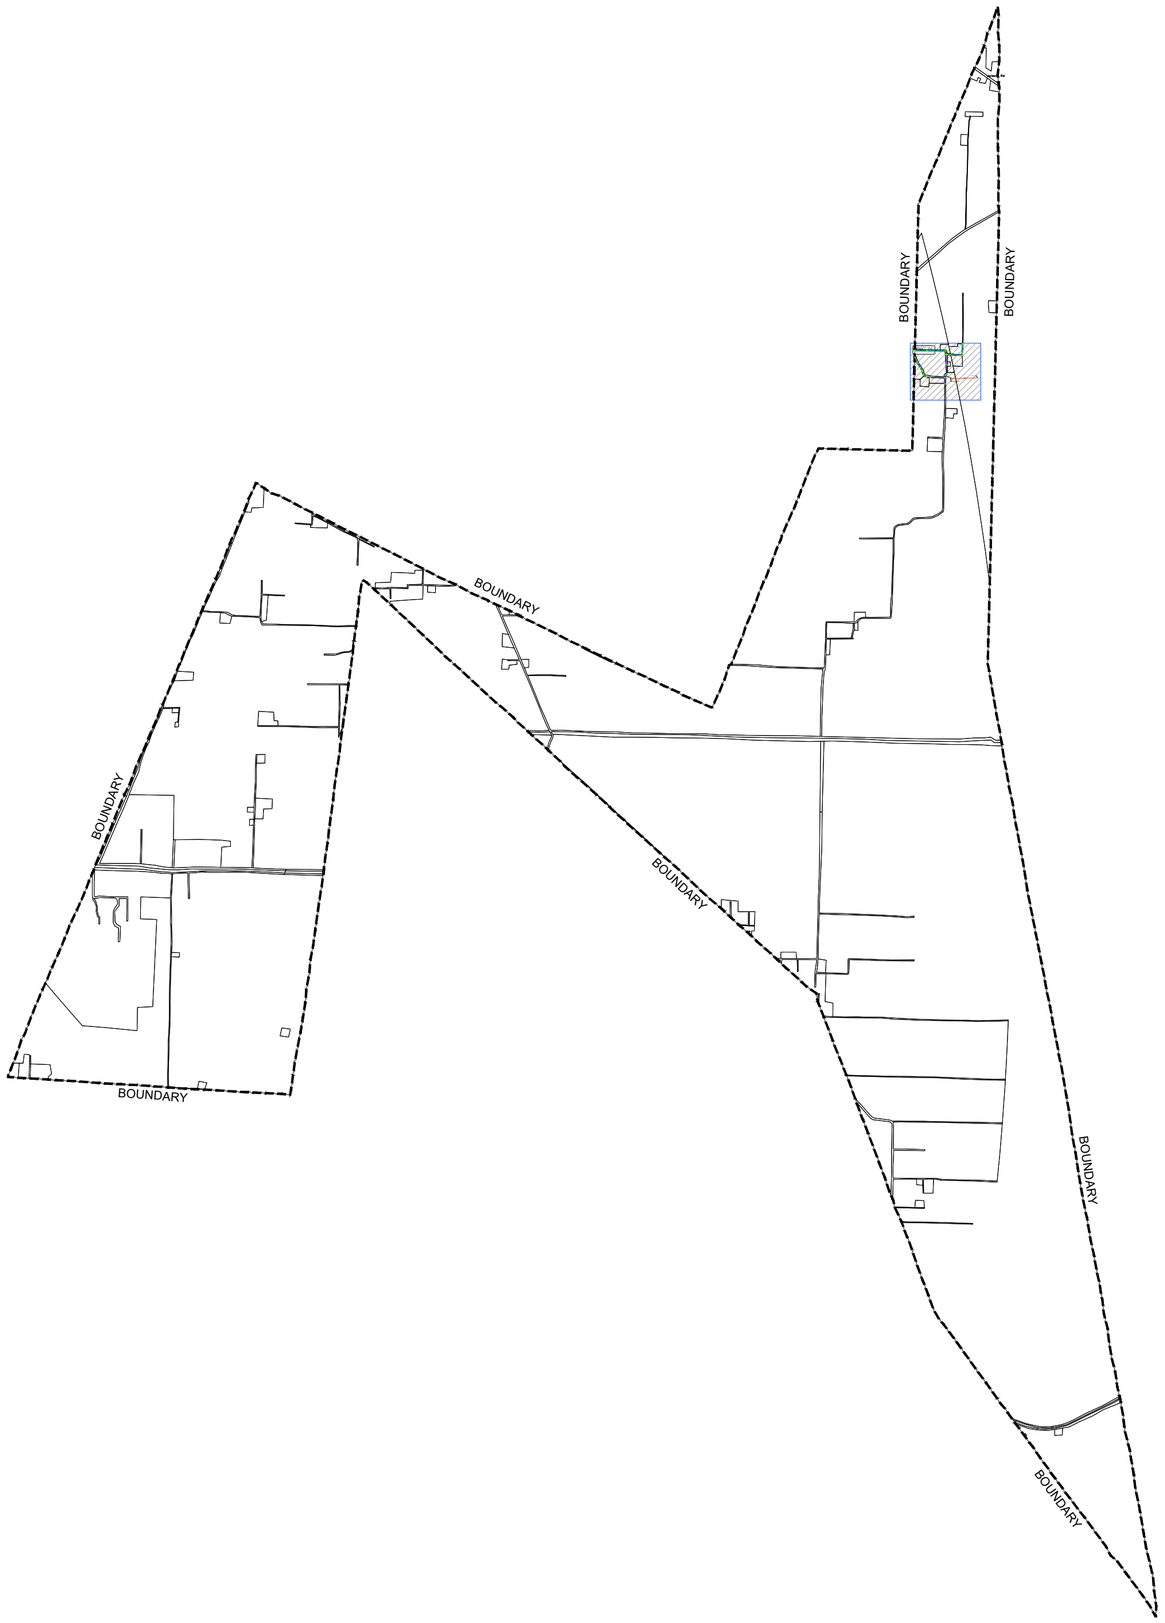

LEGEND:

- DRAIN TYPE - I
- SULLAGE CARRIER
- Ø3" HDPE PIPE
- BOUNDARY

VILLAGE: KHAWAJA BAKHSH BODLA (BWN)

TITLE.

DRAINAGE SYSTEM KEY PLAN

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 1500'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	20-04-2026	DETAILED DESIGN	ASAD	ENGR. FAIEZ	ENGR. IHSAN UL HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº: PRMSC-BWN-KBB-SEW-KP-00

SHEET 00 OF 00

REV 00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT
ASIAN CONSULTING ENGINEERS
www.asiancon.com

PRMSC-BWN-KBB-SEW-KP-00

LAYOUT PLAN

BOUNDARY

1
GL=565.01
IL=564.18

158'

2
GL=565.73
IL=564.02

257'

3
GL=565.87
IL=563.77

1.5' x 1.5'

53'

4
GL=566.23
IL=563.71

13'

1.5' x 1.5'

53'

8
GL=565.85
IL=562.87

132'

21
GL=564.4
IL=563.5

132'

5
GL=564.2
IL=563.35

24'

25'

6
GL=564.16
IL=563.03

7
GL=563.83
IL=563

9
GL=565.67
IL=562.82

1.5' x 1.5'

140'

13
GL=565.46
IL=564.62

79'

14
GL=566.59
IL=564.54

85'

15
GL=568.02
IL=564.46

47'

16
GL=567.38
IL=564.42

65'

17
GL=565.34
IL=563.93

43'

1.5' x 1.5'

55'

1.5' x 1.5'

200'

1.5' x 1.5'

18
GL=564.72
IL=563.89

19
GL=565.14
IL=561.98

10
GL=565.35
IL=562.31

1.5' x 1.5'

119'

12
GL=562.55
IL=561.47

29'

1.5' x 1.5'

11
GL=563.03
IL=561.75

36'

1.5' x 1.5'

71'

1.5' x 1.5'

GL=562.23
IL=561.40

20
GL=562.61
IL=561.75

1.5' x 1.5'

28'

22
GL=562.93
IL=561.86

Ø3" HDPE ULTIMATE DISPOSAL
TO WATER COURSE

375'

SEPTIC TANK TYPE I
TO NEAREST WATER BODY
REF:PRMSC-SEW-ST-C-01

BOUNDARY

PRMSC-BWN-KBB-WS-LP-01

N
W
E
S

KEY PLAN

LEGEND:

- DRAIN TYPE - I
- SULLAGE CARRIER
- Ø3" HDPE PIPE
- BOUNDARY

VILLAGE: KHAWAJA BAKHSH BODLA (BWN)

TITLE.

DRAINAGE SYSTEM LAYOUT PLAN-01

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	20-04-2026	DETAILED DESIGN	ASAD	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-KBB-SEW-LP-01	01 OF 01	00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS
www.asiancep.com

HYDRAULIC STATEMENT

Node		Length	Slope	Elevation Ground	Elevation Ground	Elevation Invert	Elevation Invert	Depth
FROM	TO	ft	ft/ft	U/S	D/S	U/S	D/S	ft
1	2	158	0.001	565.01	565.73	564.18	564.02	0.83
2	3	257	0.001	565.73	565.87	564.02	563.77	1.7
3	4	53	0.001	565.87	566.23	563.77	563.71	2.11
4	9	13	0.001	566.23	565.67	563.71	563.7	2.51
21	5	132	0.001	564.4	564.2	563.37	563.5	0.85
5	6	24	0.001	564.2	564.16	563.33	563.35	1.13
6	7	25	0.001	564.16	563.83	563	563.03	0.83
7	8	132	0.001	563.83	565.85	562.87	563	2.98
8	9	53	0.001	565.85	565.67	562.82	562.87	2.85
9	10	140	0.001	565.67	565.35	562.68	562.82	3.03
10	11	119	0.001	565.35	563.03	562.19	562.31	1.28
11	12	29	0.001	563.03	562.55	561.72	561.75	1.08
13	14	79	0.001	565.46	566.59	564.62	564.54	0.83
14	15	85	0.001	566.59	568.02	564.54	564.46	2.04
15	16	41	0.001	568.02	567.38	564.46	564.42	3.56
16	17	65	0.001	567.38	565.34	564.42	564.35	2.97
17	18	43	0.001	565.34	564.72	563.93	563.89	1.41
18	19	55	0.001	564.72	565.14	563.89	563.83	0.83
19	20	200	0.001	565.14	562.61	561.98	561.78	3.16
22	20	82	0.001	562.93	562.61	561.78	561.86	0.86
20	12	36	0.001	562.61	562.55	561.75	561.72	0.9
12	ST-TYPE-I	70	0.001	562.55	562.23	561.47	561.4	1.07

VILLAGE: KHAWAJA BAKHSH BODLA (BWN)

TITLE.

HYDRAULIC STATEMENT

ORIGINAL :		DATE :		SCALE :	
A2		JULY, 2025			
ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	18-09-2025	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº: PRMSC-BWN-KBB-SEW-HS-00

SHEET 01 OF 01

REV 00

PROJECT: ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER CENTRAL

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS www.asiancon.com

PRMSC-BWN-KBB-SEW-HS-00

MAHNI BEGKA

KEY PLAN

Revenue Village: Mahni Begka Sheet-1

SEPTIC TANK-1A
Plot Size=1.15 Marla

Said Sir Baig

District:	Bahawalnagar
Tehsil:	Bahawalnagar
Revenue Village:	Mahni Begka

Title:
Proposed Drainage Network Plan

Legend:

- SETTLEMENT
- NODE
- 6" uPVC PIPE
- DRAIN TYPE-1
- SEPTIC TANK
- SETTLEMENT BOUNDARY

Drain Type 1=882 Rft
Sullage Carrier=55 Rft

Scale: 1:700
1 inch = 58 feet
Paper Size: A3

0 40 80 160
Kilometers

Project:
Engineering Design & Construction Supervision, Punjab Rural Sustainable Water Supply & Sanitation Project, Cluster South III

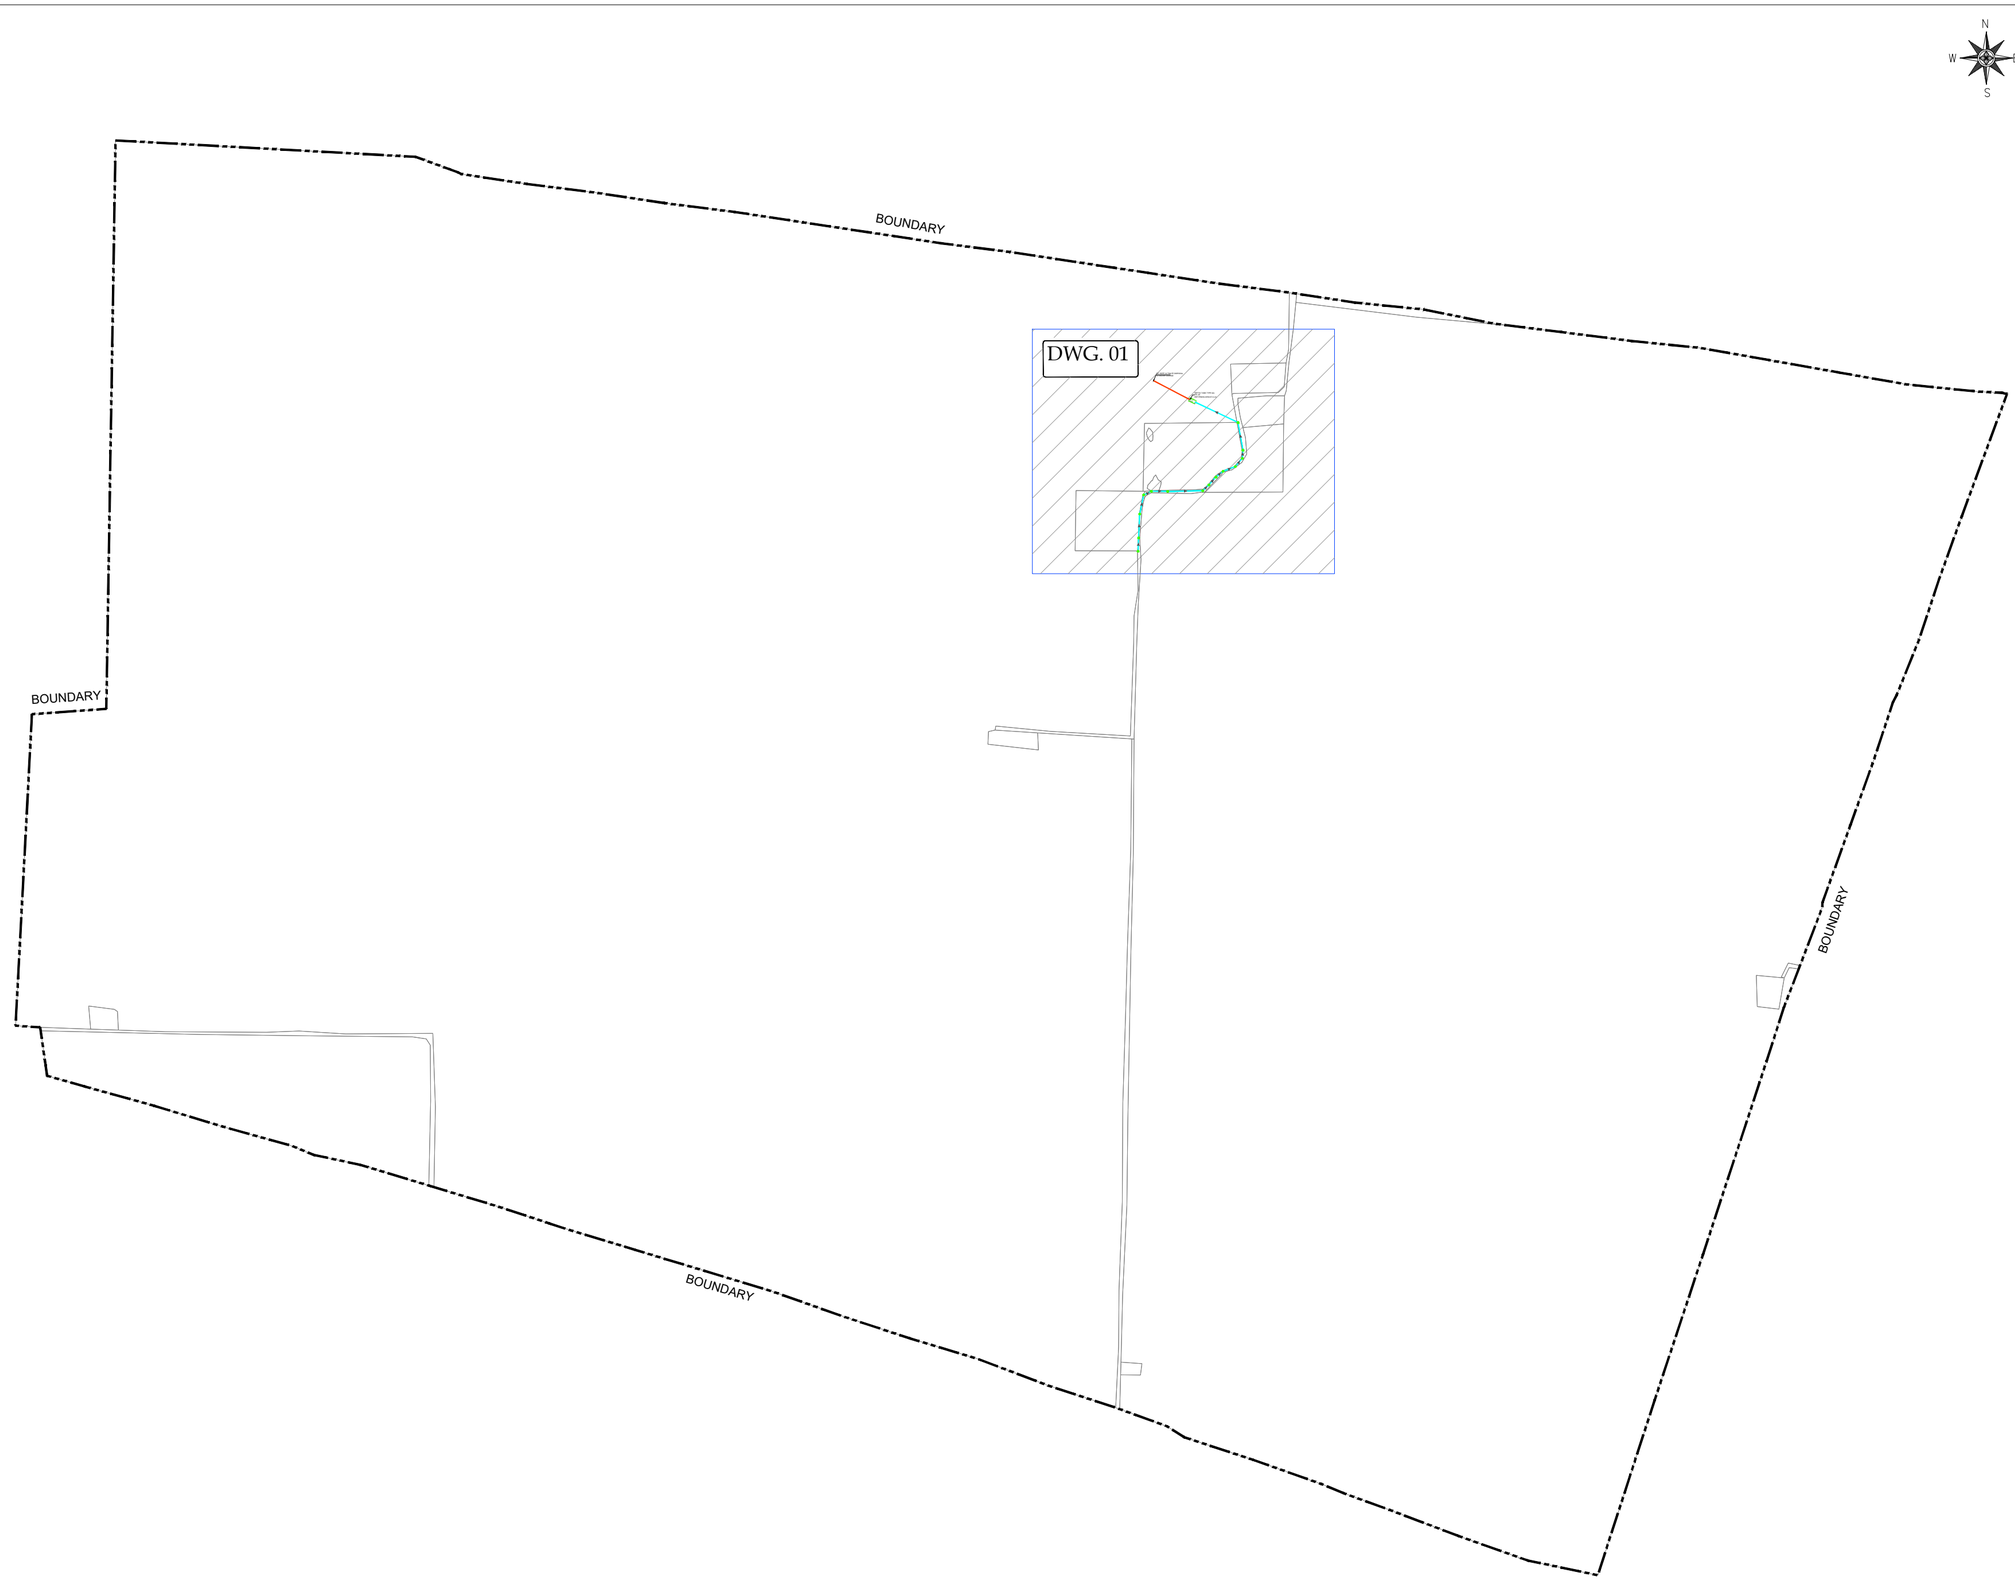

LEGEND:

DRAIN TYPE - I

Ø3" HDPE PIPE

BOUNDARY

VILLAGE: MAHNI BEGKA (BWN)

TITLE.

DRAINAGE SYSTEM KEY PLAN

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 350'

ISSUE N°	DATE	D E S C R I P T I O N	DRAWN	DESIGNED	APPROVED
01	20-04-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-MBK-SEW-KP-00	00 OF 00	00

PROJECT:

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:

PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT

ASIAN CONSULTING ENGINEERS
www.asianeen.com.pk

PRMSC-BWN-MBK-SEW-KP-00

LAYOUT PLAN

KEY PLAN

LEGEND:

DRAIN TYPE - I

Ø3" HDPE PIPE

BOUNDARY

VILLAGE: MAHNI BEGKA (BWN)

TITLE.

DRAINAGE SYSTEM LAYOUT PLAN-01

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	20-04-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº: PRMSC-BWN-MBK-SEW-LP-01

SHEET 01 OF 01

REV 00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

PRMSC-BWN-MBK-SEW-LP-01

HYDRAULIC STATEMENT

Node		Length	Slope	Elevation Ground	Elevation Ground	Elevation Invert	Elevation Invert	Depth
FROM	TO	ft	ft/ft	U/S	D/S	U/S	D/S	ft
1	2	42	0.001	512.67	511.27	510.44	510.48	2.19
2	3	76	0.001	511.27	510.39	509.56	509.63	1.64
3	4	62	0.001	510.39	509.12	508.29	508.35	2.04
4	5	27	0.001	509.12	508.42	507.59	507.61	1.51
5	6	52	0.001	508.42	507.86	507.03	507.08	1.34
6	7	111	0.001	507.86	507.48	506.65	506.76	1.1
7	8	27	0.001	507.48	506.75	505.92	505.94	1.54
8	9	33	0.001	506.75	506.57	505.74	505.77	0.98
9	10	29	0.001	506.57	505	504.17	504.2	2.37
10	11	42	0.001	505	502.89	502.06	502.1	2.9
11	12	34	0.001	502.89	500.32	499.49	499.52	3.37
12	13	26	0.001	500.32	499.76	498.93	498.95	1.37
13	14	89	0.001	499.76	497.89	497.06	497.15	2.61
14	ST-TYPE-IA-NO SP	150	0.001	497.89	497.48	496.65	496.8	1.09

VILLAGE: MAHNI BEGKA (BWN)

TITLE.

HYDRAULIC STATEMENT

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	20-04-2026	DETAILED DESIGN	MUNEEB	ENGR FAIEZ	ENGR HSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº: PRMSC-BWN-MBK-SEW-HS-00

SHEET 01 OF 01

REV 00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT
ASIAN CONSULTING ENGINEERS
www.asianeca.com

PRMSC-BWN-MBK-SEW-HS-00

MALAK PURA

KEY PLAN

Revenue Village: Malak Pura Sheet-1

District:	Bahawalnagar
Tehsil:	Bahawalnagar
Revenue Village:	Malak Pura

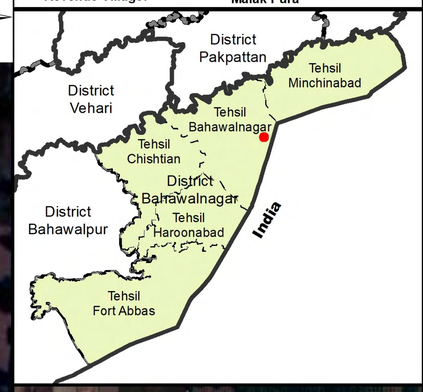

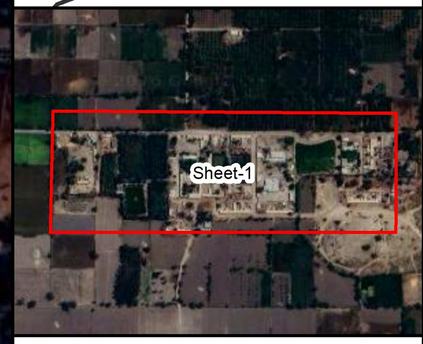

ND-10 GL=569.91 IL=567.84
ND-9 GL=571.13 IL=568.5
ND-8 GL=571.85 IL=568.92
ND-5 GL=572.27 IL=569.17
ND-4 GL=571.91 IL=569.56
ND-3 GL=572.41 IL=569.61
ND-2 GL=573.07 IL=570.03
ND-12 GL=573.68 IL=571.43
ND-11 GL=573.52 IL=571.27
ND-15 GL=573.77 IL=571.52
Malikpura
ND-16 GL=569.45 IL=565.04
GL=570.23 IL=565.79
PROPOSED ULTIMATE DISPOSAL TO WATER COURSE
SEPTIC TANK-T1 Plot Size=1.59 Marla
ND-17 GL=573.89 IL=571.84
ND-6 GL=573.84 IL=569.8
ND-14 GL=572.56 IL=570.31
ND-7 GL=572.23 IL=569.98
ND-1 GL=575.48 IL=571.74
ND-13 GL=576.21 IL=573.96

Title:
Proposed Drainage Network Plan

Legend:

- SETTLEMENT
- NODE
- **3" HDPE**: PIPE
- DRAIN TYPE-1
- SULLAGE CARRIER
- SEPTIC TANK
- SETTLEMENT BOUNDARY

Drain Type 1=2510 Rft

Sullage Carrier=2533 Rft

Scale: 1:1,800

1 inch = 150 feet

Paper Size: A3

0 40 80 160

Kilometers

Project:
Engineering Design & Construction Supervision, Punjab Rural Sustainable Water Supply & Sanitation Project, Cluster South III

PRMSC

ENVIRONMENTAL TECHNOLOGIES

ASIAN CONSULTING ENGINEERS www.asiancon.com

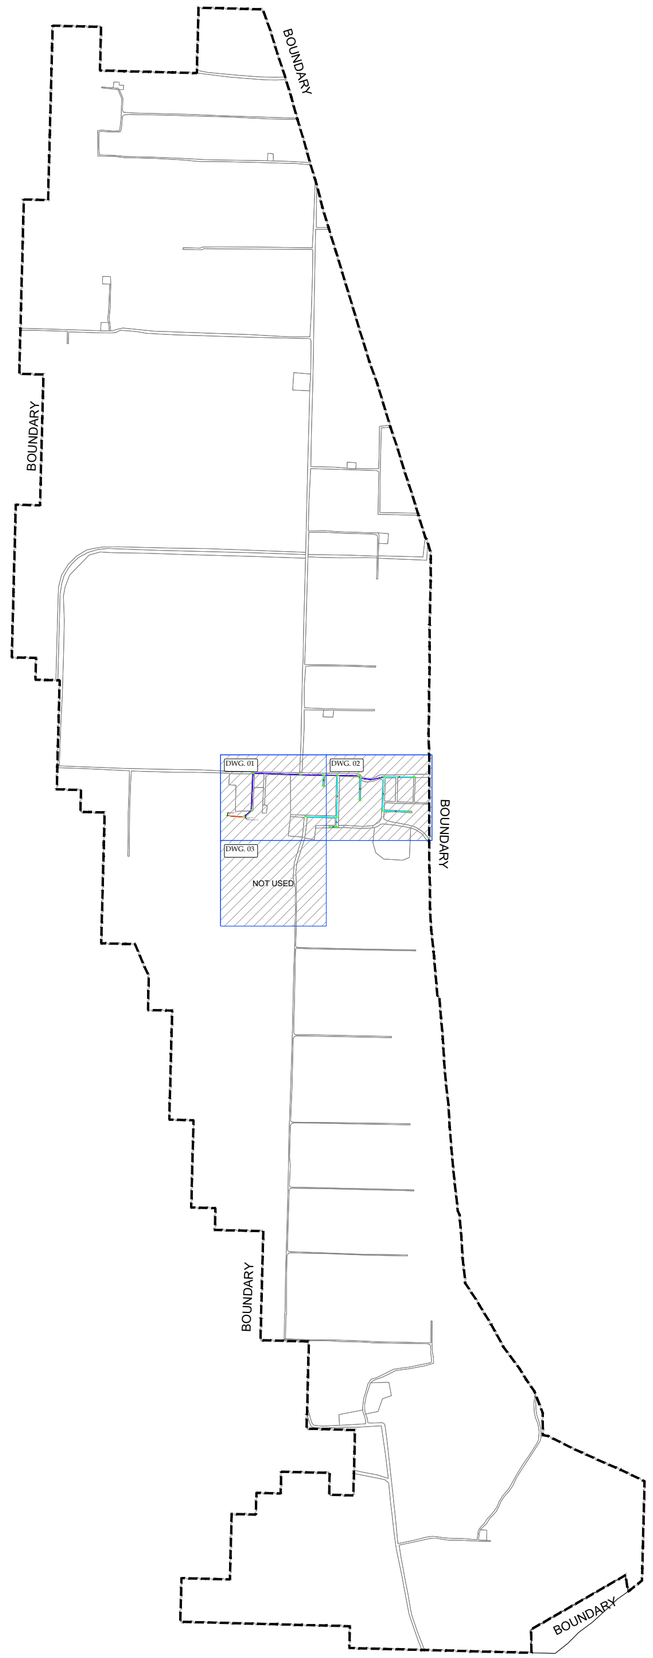

LEGEND:

- DRAIN TYPE - I
- SULLAGE CARRIER
- Ø3" HDPE PIPE
- BOUNDARY

VILLAGE: MALAK PURA (BWN)

TITLE.

DRAINAGE SYSTEM KEY PLAN

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 1000'

ISSUE N°	DATE	D E S C R I P T I O N	DRAWN	DESIGNED	APPROVED
01	20-04-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº: PRMSC-BWN-MLP-SEW-KP-00

SHEET 00 OF 00

REV 00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT
ENVIROLEVEL TECHNOLOGIES
ASIAN CONSULTING ENGINEERS
www.asianceb.com

PRMSC-BWN-MLP-SEW-KP-00

LAYOUT PLAN

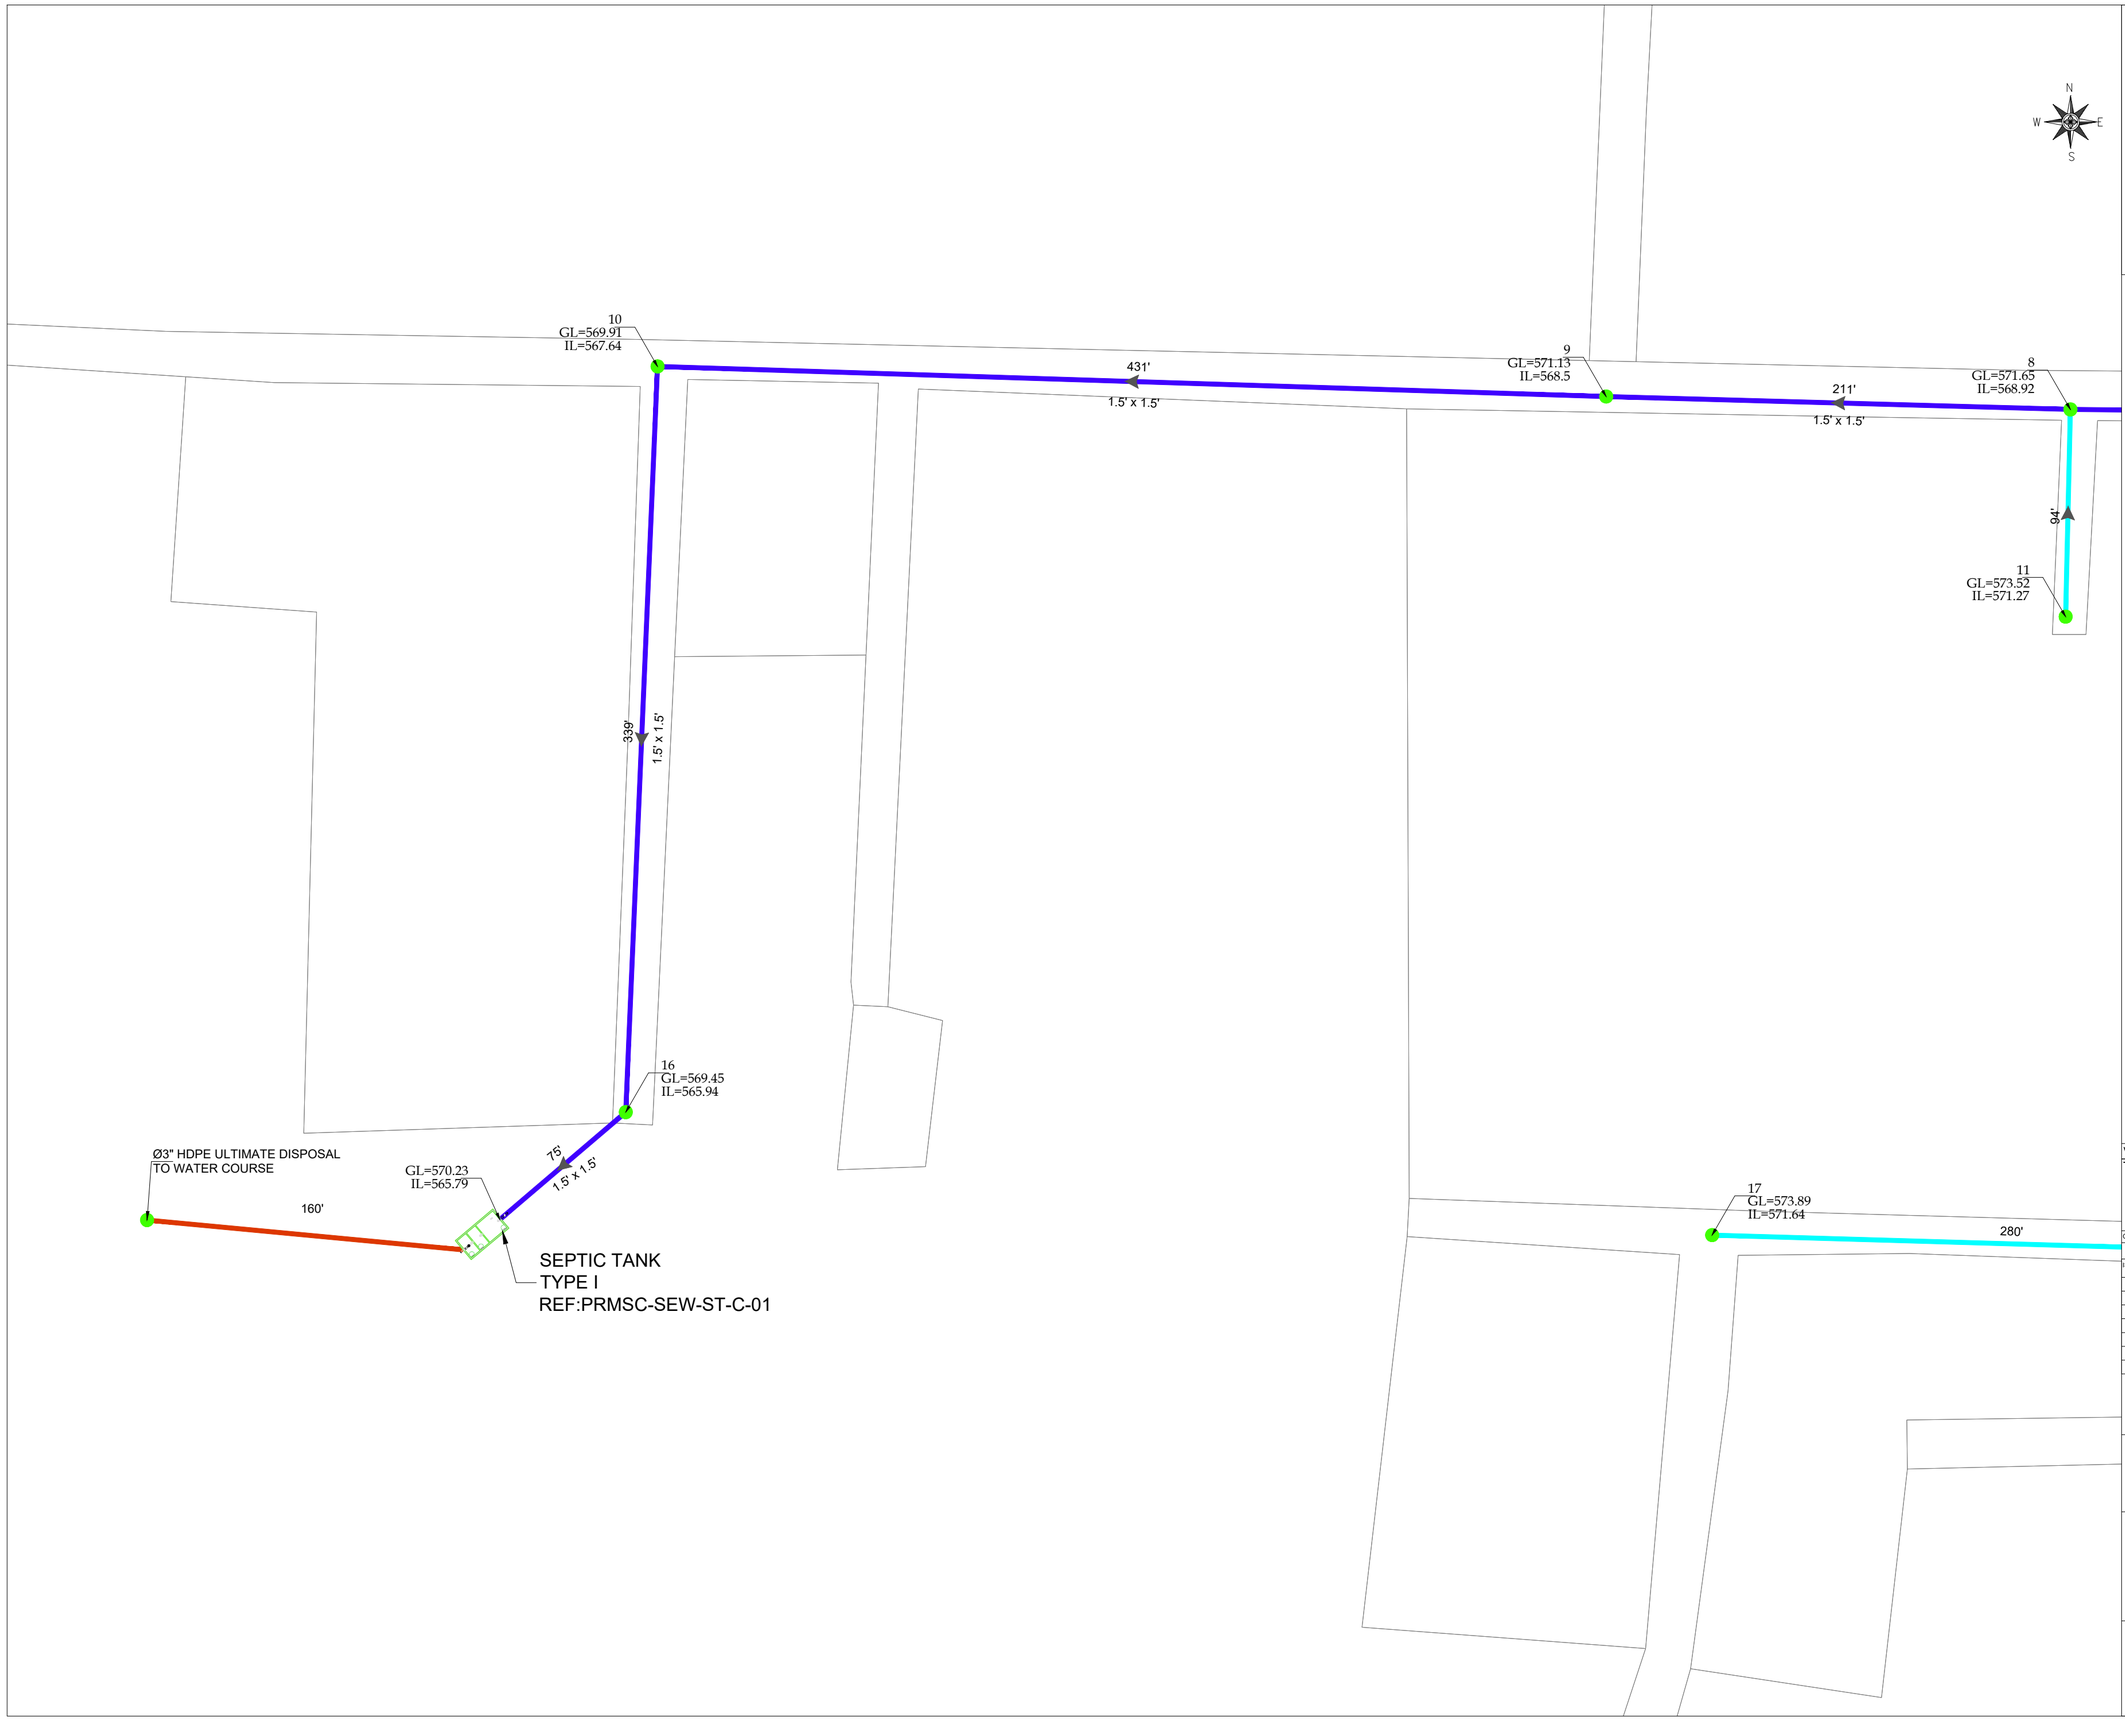

KEY PLAN

LEGEND:

- DRAIN TYPE - I
- SULLAGE CARRIER
- Ø3" HDPE PIPE
- BOUNDARY

VILLAGE: MALAK PURA (BWN)

TITLE.

DRAINAGE SYSTEM LAYOUT PLAN-01

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	20-04-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº: PRMSC-BWN-MLP-SEW-LP-01

SHEET 01 OF 03

REV 00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:
ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

PRMSC-BWN-MLP-SEW-LP-01

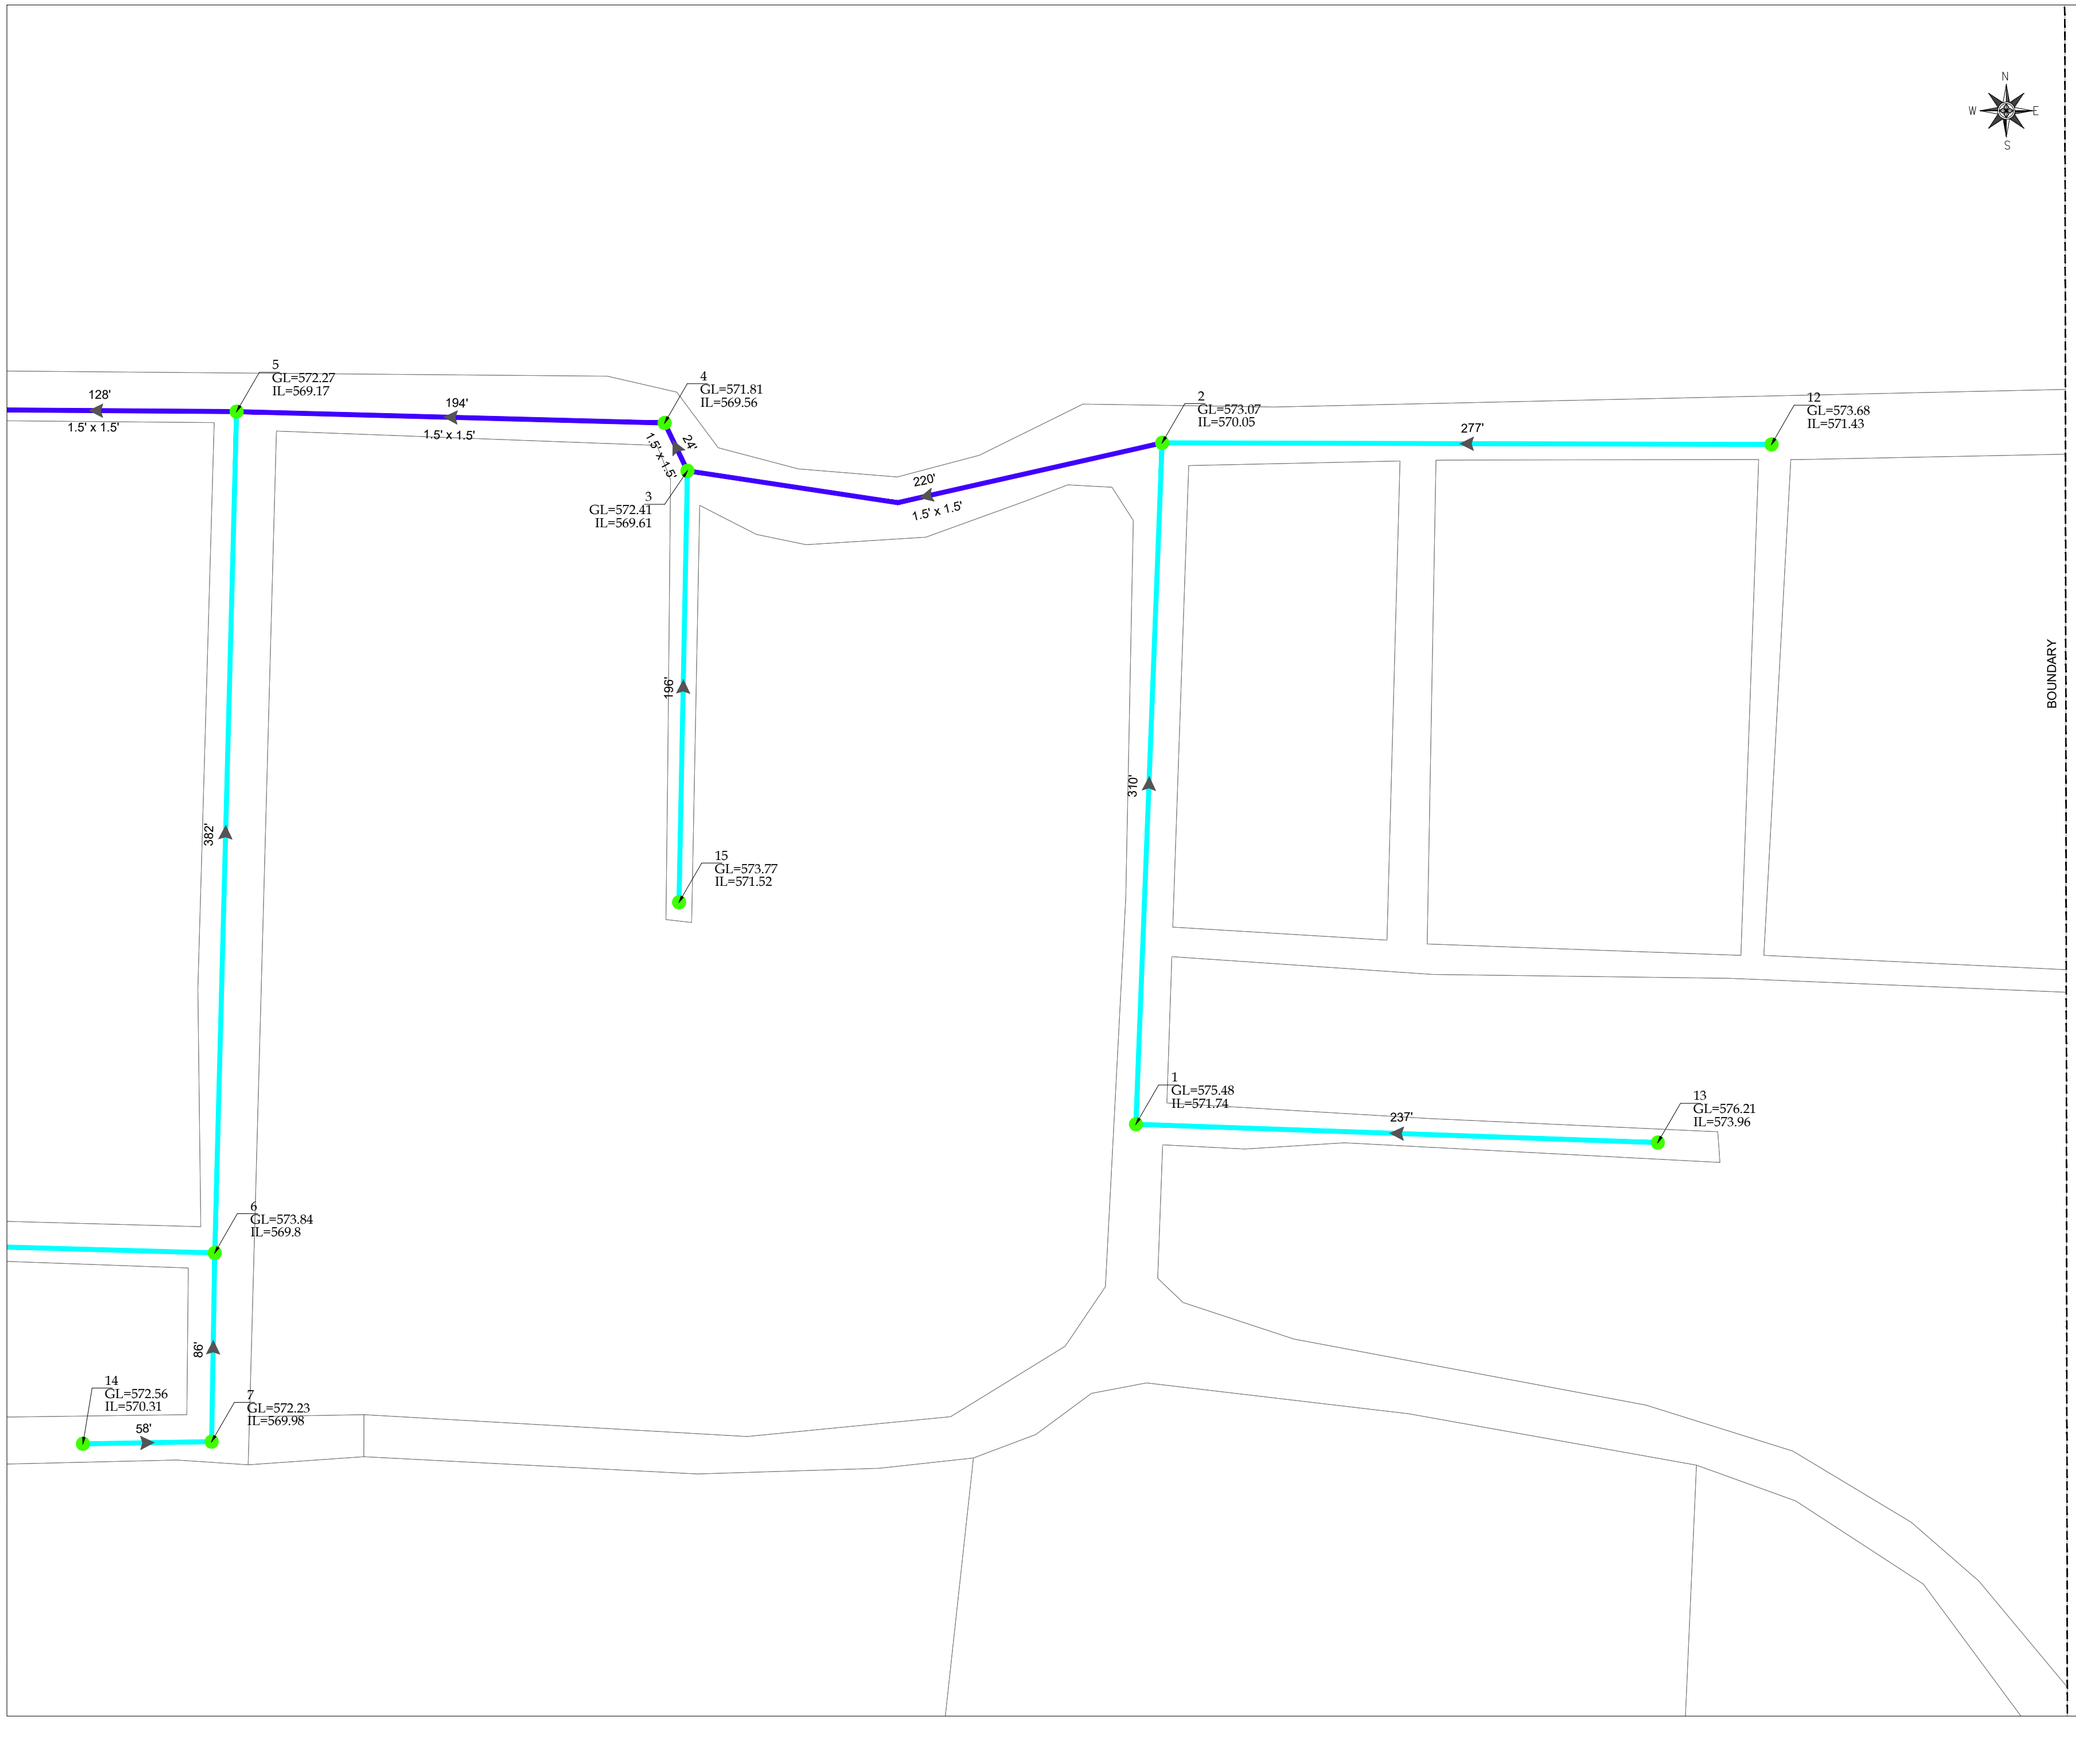



KEY PLAN

LEGEND:

- DRAIN TYPE - I
- SULLAGE CARRIER
- Ø3" HDPE PIPE
- BOUNDARY

VILLAGE: MALAK PURA (BWN)

TITLE.

DRAINAGE SYSTEM LAYOUT PLAN-02

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	20-04-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING N°:	SHEET	REV
PRMSC-BWN-MLP-SEW-LP-02	02 OF 03	00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

HYDRAULIC STATEMENT								
Node		Length	Slope	Elevation Ground	Elevation Ground	Elevation Invert	Elevation Invert	Depth
FROM	TO	ft	ft/ft	U/S	D/S	U/S	D/S	ft
13	1	237	0.009	576.21	575.48	571.74	573.96	3.74
1	2	310	0.003	575.48	573.07	570.82	571.74	3.01
12	2	277	0.005	573.68	573.07	570.05	571.43	2.8
2	3	220	0.002	573.07	572.41	569.61	570.05	2.25
15	3	196	0.01	573.77	572.41	569.61	571.52	3.09
3	4	24	0.002	572.41	571.81	569.56	569.61	4.03
4	5	194	0.002	571.81	572.27	569.17	569.56	2.25
17	6	280	0.007	573.89	573.84	569.8	571.64	2.73
14	7	58	0.006	572.56	572.23	569.98	570.31	2.63
7	6	86	0.002	572.23	573.84	569.8	569.98	2.27
6	5	382	0	573.84	572.27	569.8	569.79	2.25
5	8	128	0.002	572.27	571.65	569.17	568.92	2.25
11	8	94	0.025	573.52	571.65	568.92	571.27	2.25
8	9	211	0.002	571.65	571.13	568.5	568.92	2.25
9	10	431	0.002	571.13	569.91	567.64	568.5	2.25
10	16	339	0.005	569.91	569.45	567.64	565.94	3.51
16	ST-TYPE-I	75	0.002	569.45	570.23	565.79	565.94	2.25

VILLAGE: MALAK PURA (BWN)

TITLE.

HYDRAULIC STATEMENT

ORIGINAL :		DATE :		SCALE :	
A2		JULY, 2025			
ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	20-04-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING N°: PRMSC-BWN-MLP-SEW-HS-00 | SHEET 00 OF 00 | REV 00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT
ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

MINA SANATTEKA

KEY PLAN

Revenue Village: Mina Sanatteka Sheet-1

GL=536.32
IL=532.98

SOAKAGE PIT

SEPTIC TANK-T1
Plot Size=1.59
Marla

N

District: Bahawalnagar
Tehsil: Bahawalnagar
Revenue Village: Mina Sanatteka

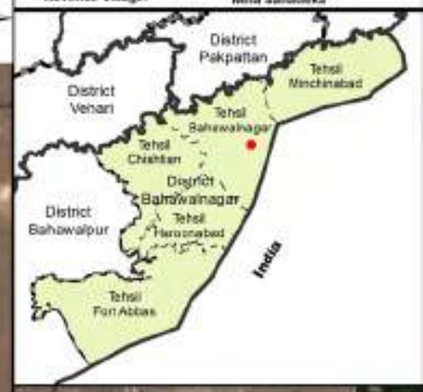

Title:
Proposed Drainage Network Plan

Legend:

- SOAKAGE PIT
- NODE
- DRAIN TYPE-1
- SULLAGE CARRIER
- SEPTIC TANK
- SETTLEMENT BOUNDARY

Drain Type 1=2669 Rft
Sullage Carrier=624 Rft

Scale: 1:1,200
1 inch = 100 feet
Paper Size: A3

0 40 80 160
Kilometers

Project:
Engineering Design & Construction Supervision, Punjab Rural Sustainable Water Supply & Sanitation Project, Cluster South III

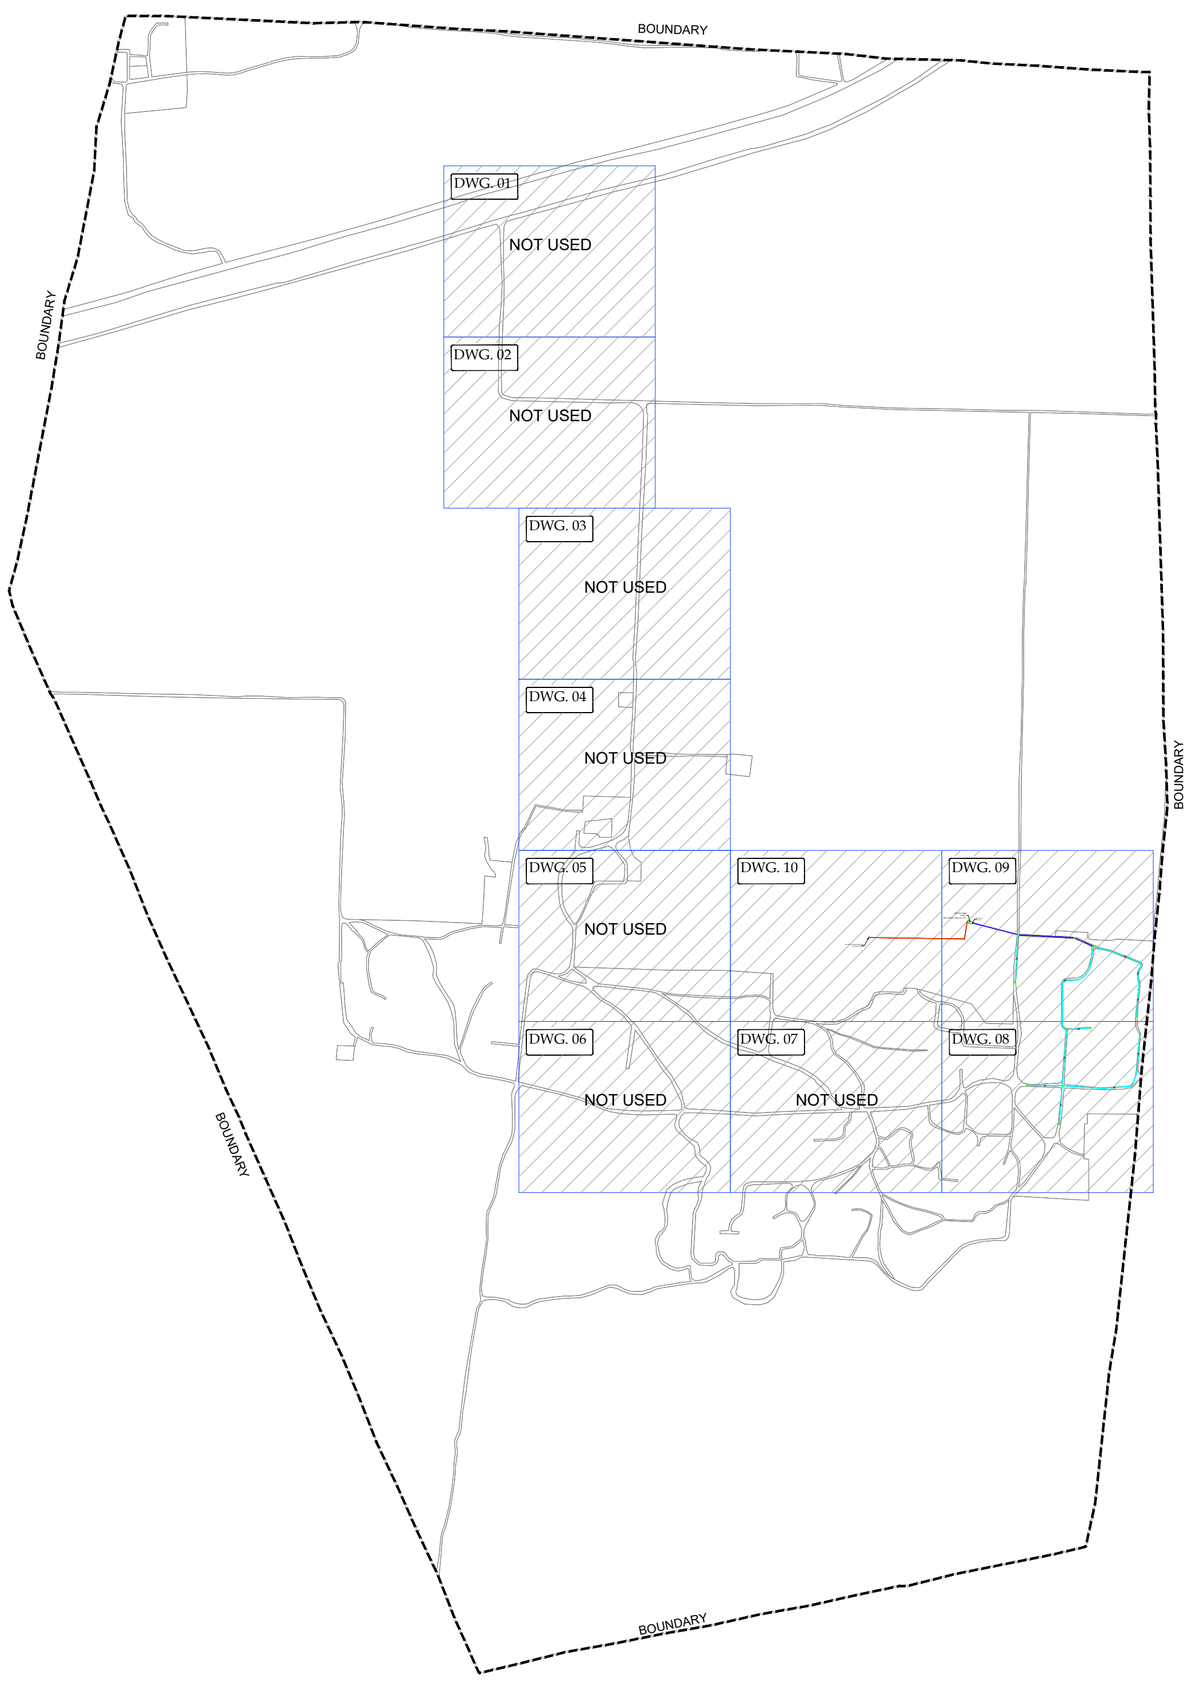

LEGEND:

- DRAIN TYPE - I
- SULLAGE CARRIER
- Ø3" HDPE PIPE
- BOUNDARY

VILLAGE: MINA_SANATIKA (BWN)

TITLE.

DRAINAGE SYSTEM KEY PLAN

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 1000'

ISSUE N°	DATE	D E S C R I P T I O N	DRAWN	DESIGNED	APPROVED
01	23-05-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSANUL HAQ
02					
03					
04					
05					
06					
07					

DRAWING N°:	SHEET	REV
PRMSC-BWN-MS-SEW-KP-00	00 OF 00	00

PROJECT:

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:

PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT

ASIAN CONSULTING ENGINEERS www.asiancon.com.pk

PRMSC-BWN-MS-SEW-KP-00

LAYOUT PLAN

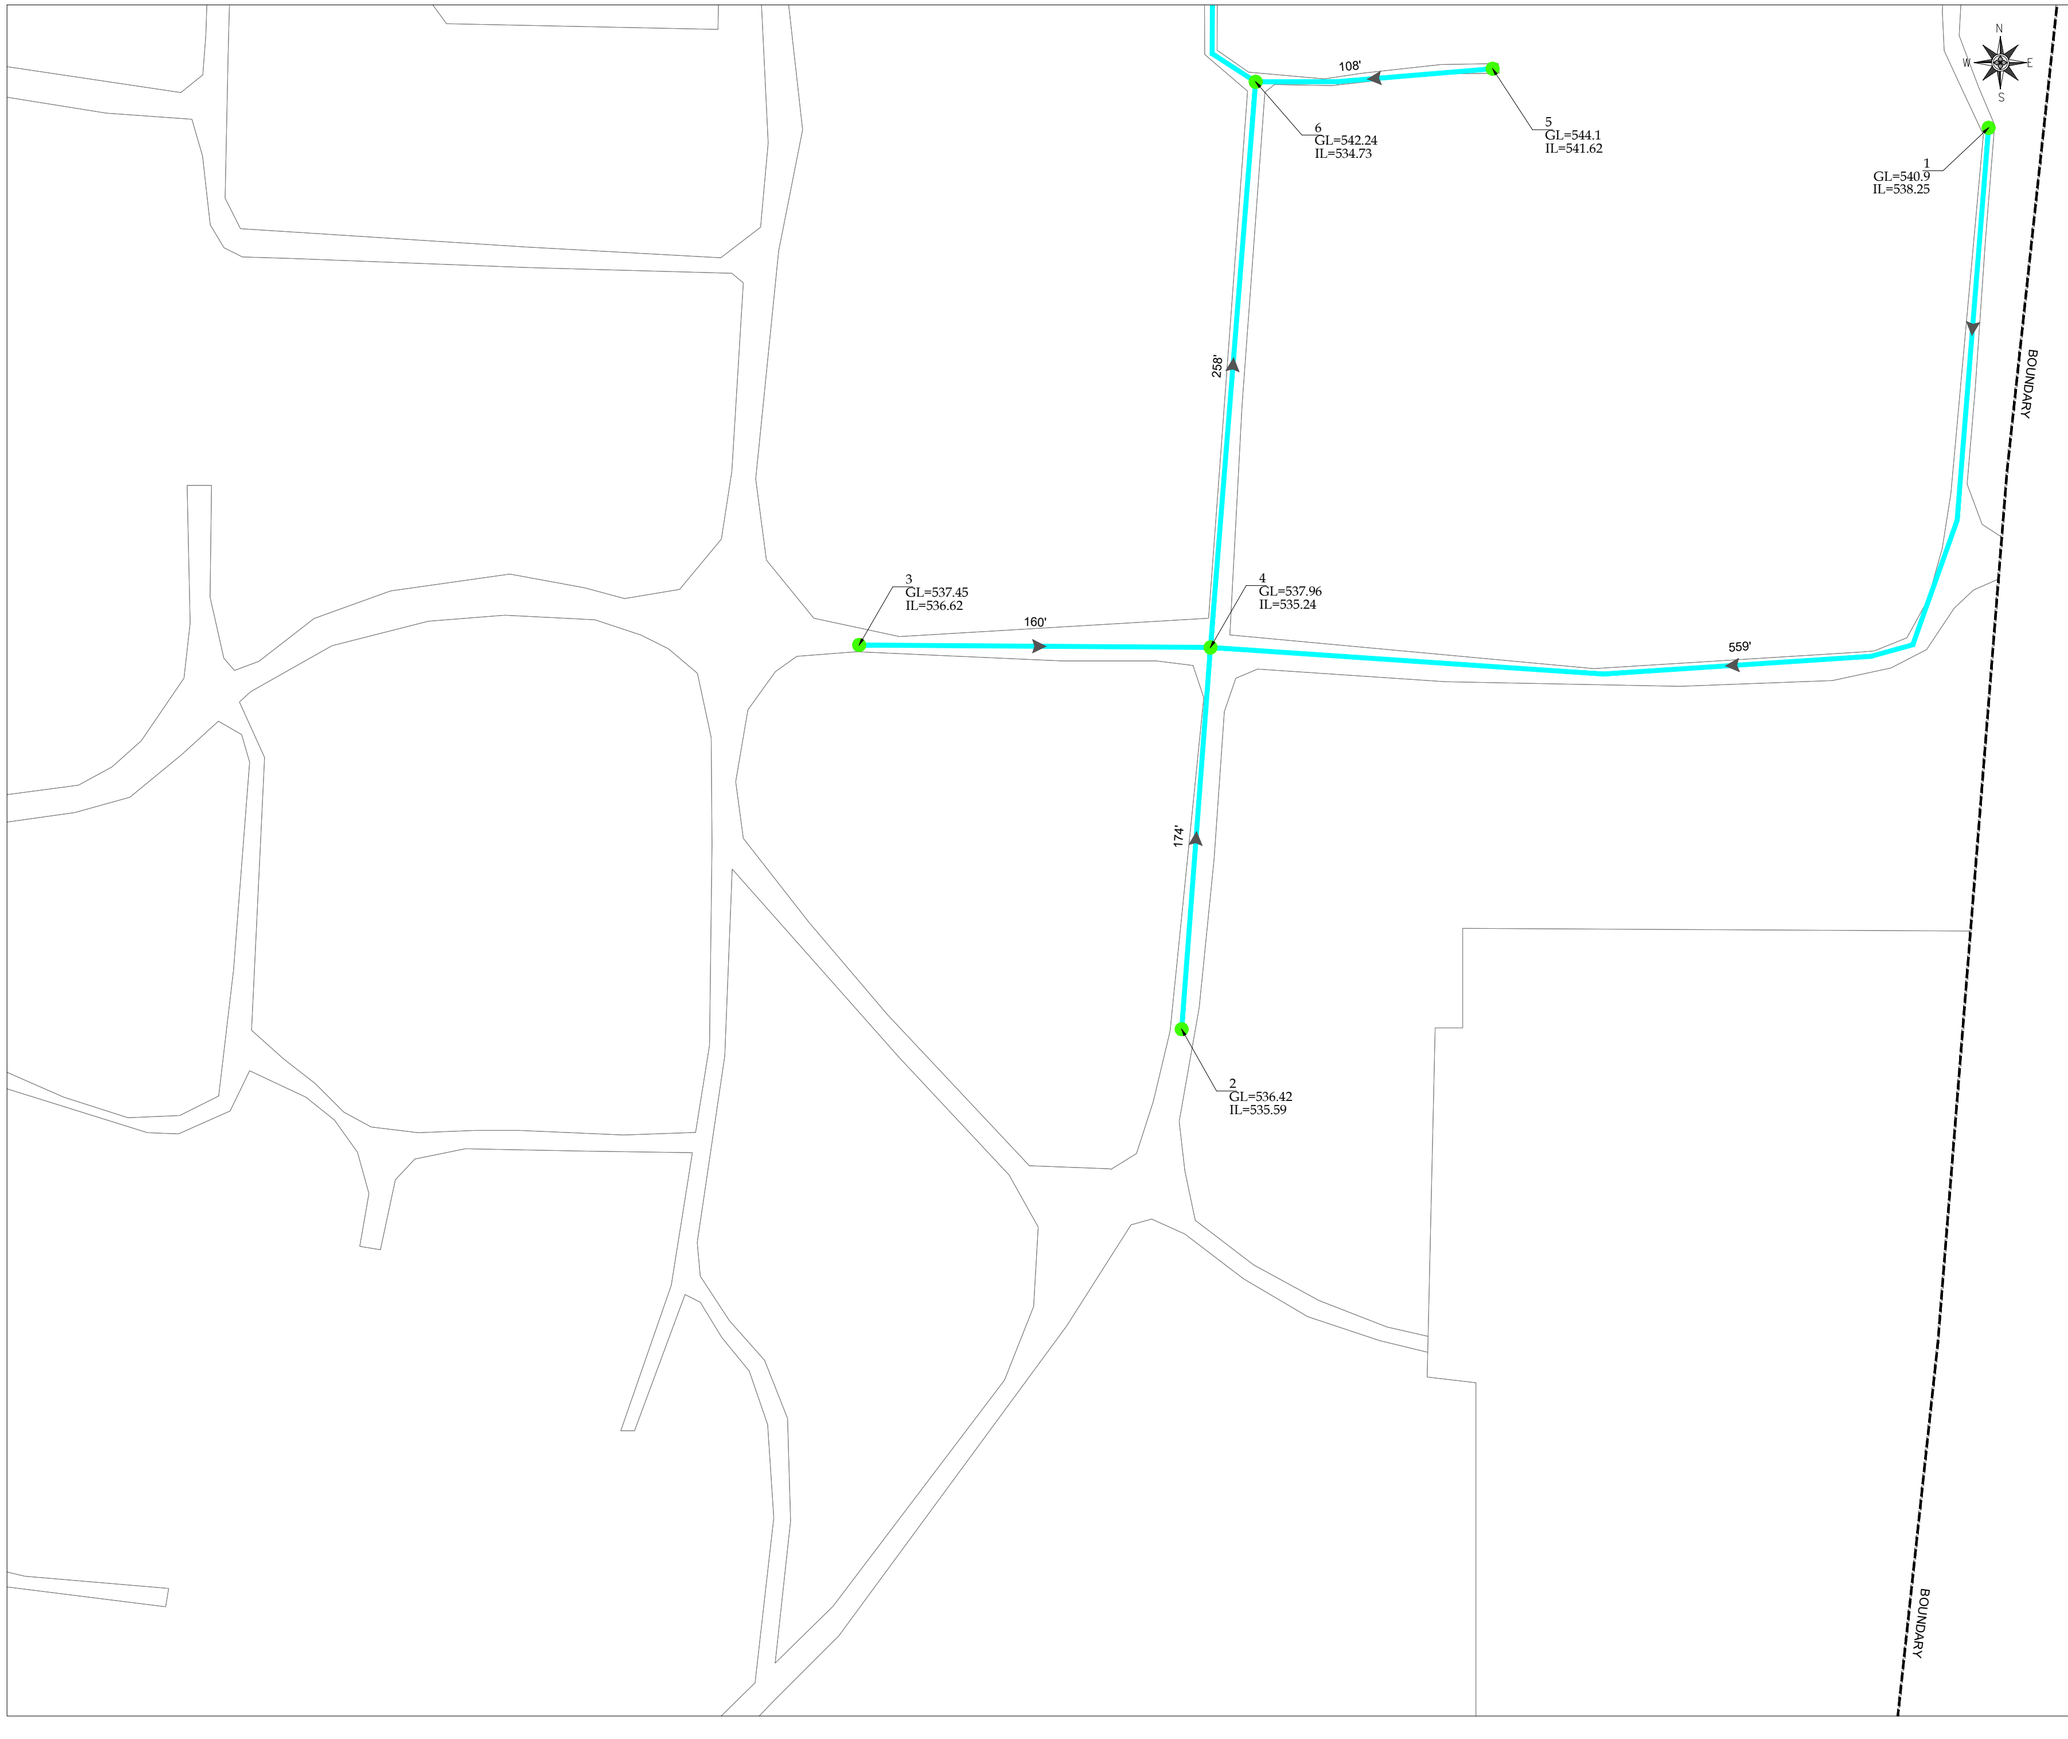

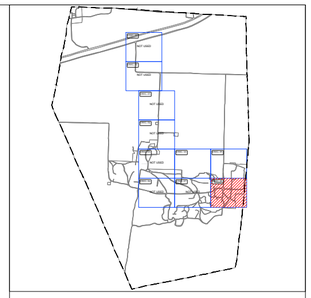

LEGEND:

- DRAIN TYPE - I
- SULLAGE CARRIER
- Ø3" HDPE PIPE
- BOUNDARY

VILLAGE: MINA SANATIKA (BWN)

TITLE.

DRAINAGE SYSTEM LAYOUT PLAN-08

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	23-05-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-MS-SEW-LP-08	08 OF 10	00

PROJECT:

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:

PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT

ASIAN CONSULTING ENGINEERS (PVT) LTD. www.asiancon.com.pk

PRMSC-BWN-MS-SEW-LP-08

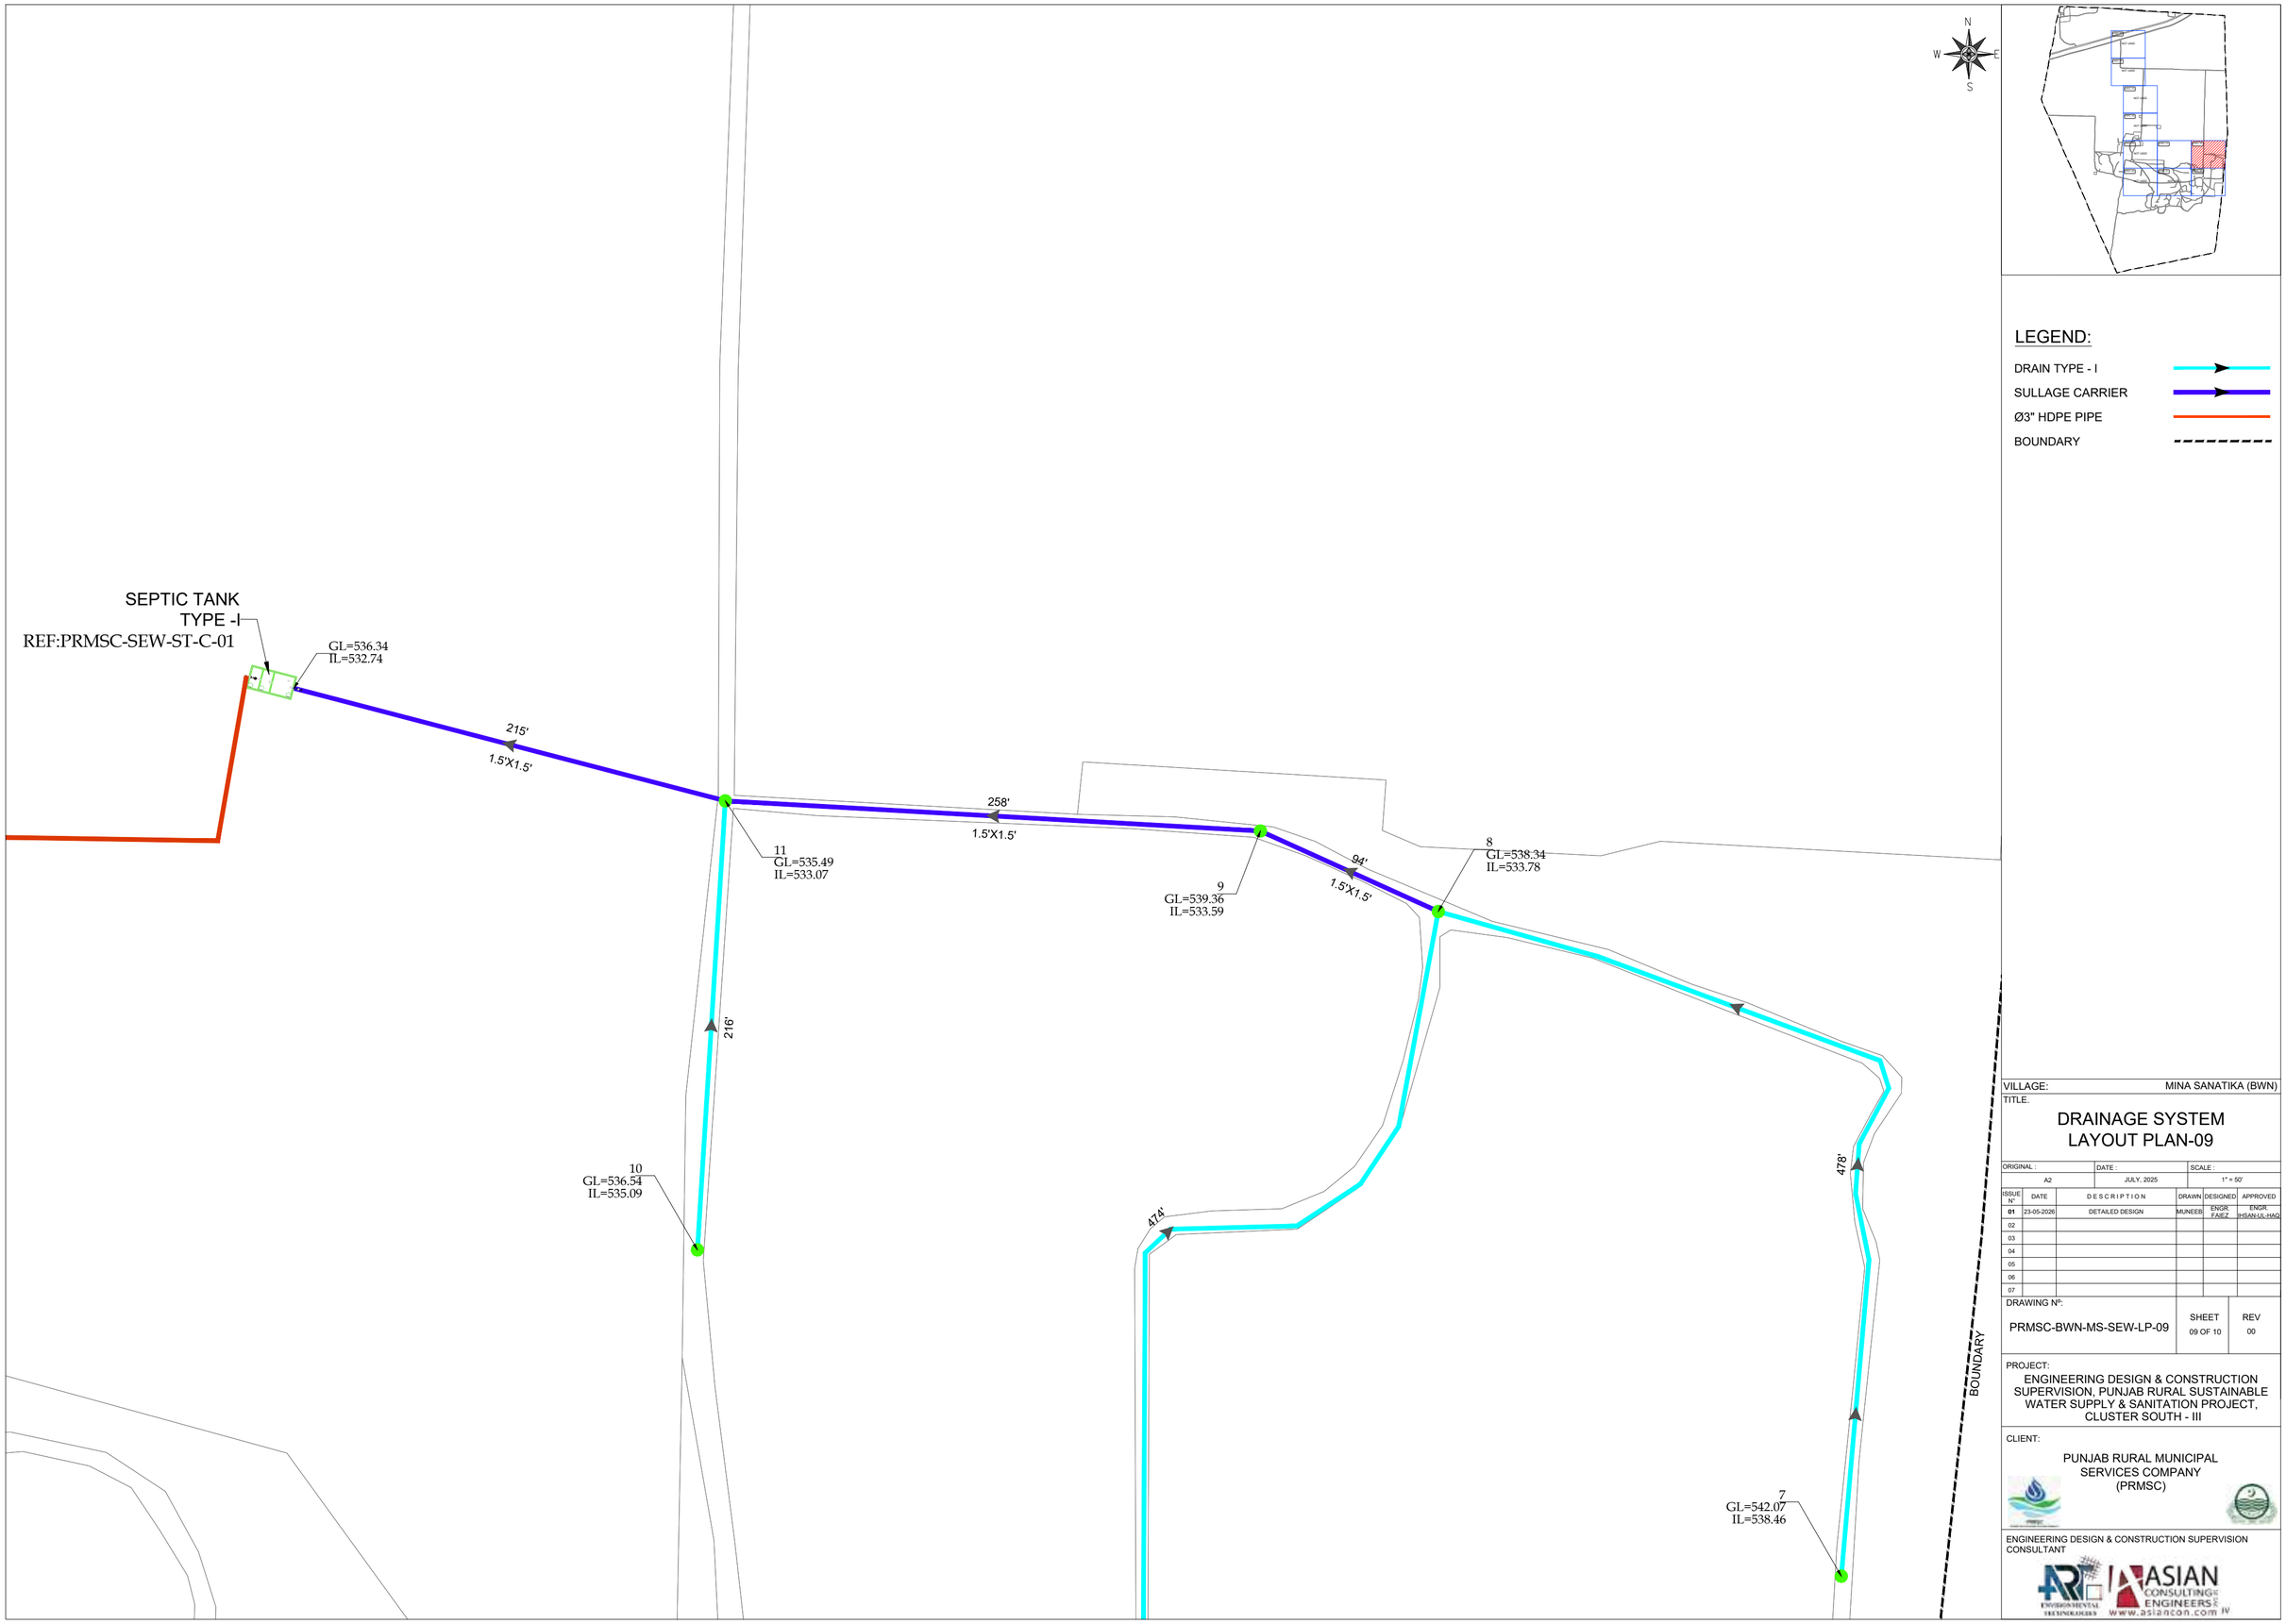

VILLAGE: MINA SANATIKA (BWN)

TITLE.

DRAINAGE SYSTEM LAYOUT PLAN-09

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	23-05-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:

PRMSC-BWN-MS-SEW-LP-09

SHEET 09 OF 10

REV 00

PROJECT:

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:

PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT

ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

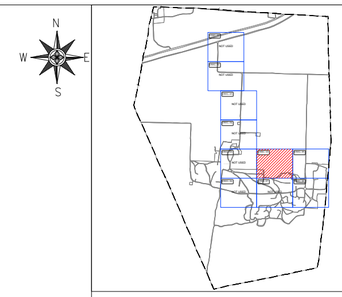

LEGEND:

- DRAIN TYPE - I
- SULLAGE CARRIER
- Ø3" HDPE PIPE
- BOUNDARY

514'

Ø3" HDPE ULTIMATE DISPOSAL
TO WATER COURSE

PRMSC-BWN-MS-SEW-LP-10

VILLAGE: MINA SANATIKA (BWN)

TITLE.

DRAINAGE SYSTEM LAYOUT PLAN-10

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	23-05-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. HSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-MS-SEW-LP-10	10 OF 10	00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT
ASIAN CONSULTING ENGINEERS
www.asianconsultingengineers.com

HYDRAULIC STATEMENT

Node		Length	Slope	Elevation Ground	Elevation Ground	Invert	Invert	Depth
FROM	TO	ft	ft/ft	U/S	D/S	U/S	D/S	ft
1	4	559	0.002	540.9	537.96	538.25	537.13	2.65
2	4	174	0.002	536.42	537.96	535.59	535.24	0.83
3	4	160	0.002	537.45	537.96	536.62	536.3	0.83
4	6	258	0.002	537.96	542.24	535.24	534.73	2.72
5	6	108	0.002	544.1	542.24	541.62	541.41	2.48
6	8	474	0.002	542.24	538.34	534.73	533.78	2.51
7	8	478	0.002	542.07	538.34	538.46	537.51	3.6
8	9	94	0.002	538.34	539.36	533.78	533.59	3.57
9	11	258	0.002	539.36	535.49	533.59	533.07	5.77
10	11	216	0.002	536.54	535.49	535.09	534.66	1.45
11	ST Type I	164	0.002	535.49	536.34	533.07	532.74	2.42

VILLAGE: MINA_SANATIKA (BWN)

TITLE.

HYDRAULIC STATEMENT

ORIGINAL :		DATE :		SCALE :	
A2		JULY, 2025			
ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	16-12-2025	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING N°: PRMSC-BWN-MS-SEW-HS-00 | SHEET 00 OF 00 | REV 00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT
ASIAN CONSULTING ENGINEERS
www.asiancon.com

MUHAMMAD ASAD KHAN

KEY PLAN

Revenue Village: Muhammad Asad Khan Sheet-1

N

District:	Bahawalnagar
Tehsil:	Bahawalnagar
Revenue Village:	Muhammad Asad Khan

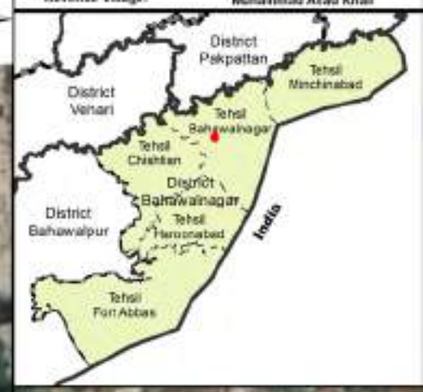

Title:
Proposed Drainage Network Plan

Legend:

- NODE
- DRAIN TYPE-1
- SULLAGE CARRIER
- SEPTIC TANK
- SETTLEMENT BOUNDARY

Drain Type 1=7882 Rft
Sullage Carrier= 4980 Rft

Scale: 1:1,300
1 inch = 108 feet
Paper Size: A3

0 40 80 160
Kilometers

Project:
Engineering Design & Construction Supervision, Punjab Rural Sustainable Water Supply & Sanitation Project, Cluster South III

SEPTIC TANK-T2
Plot Size=2 Marla

Revenue Village: Muhammad Asad Khan Sheet-2

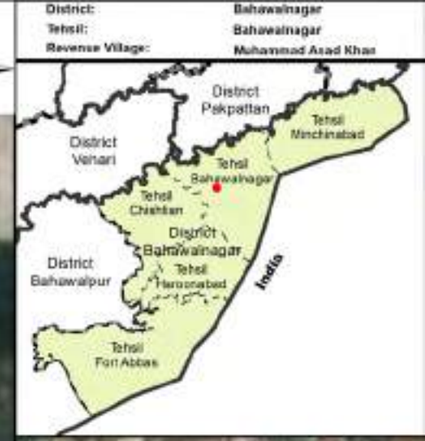

Title:
Proposed Drainage Network Plan

Legend:

- SETTLEMENT
- NODE
- DRAIN TYPE-1
- SULLAGE CARRIER
- SEPTIC TANK
- SETTLEMENT BOUNDARY

Drain Type 1=7882 Rft
Sullage Carrier= 4980 Rft

Scale: 1:900
1 inch = 75 feet
Paper Size: A3

0 40 80 160
Kilometers

Project:
Engineering Design & Construction Supervision, Punjab Rural Sustainable Water Supply & Sanitation Project, Cluster South III

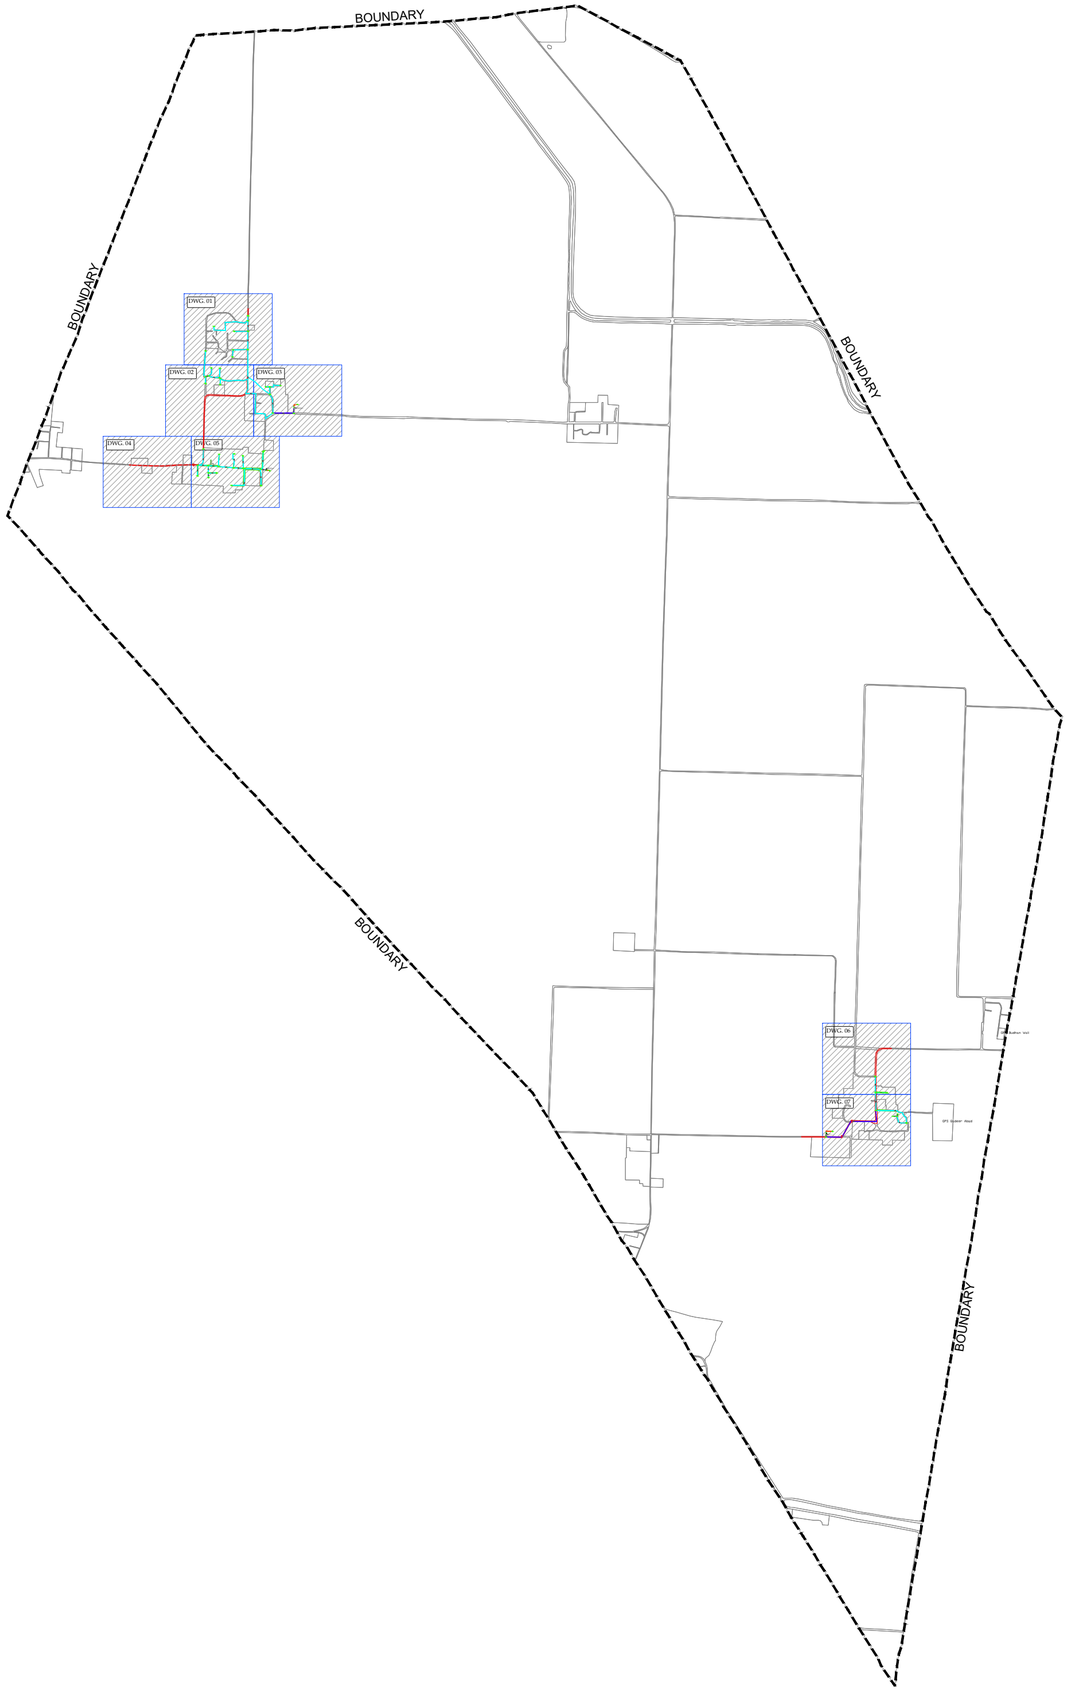

LEGEND:

- DRAIN TYPE - I
- SULLAGE CARRIER
- Ø3" HDPE PIPE
- EXISTING SOLING
- METALLED ROAD
- PROPOSED CULVERT
- BOUNDARY

VILLAGE: MUHAMMAD ASAD KHAN (BWN)

TITLE.

DRAINAGE SYSTEM KEY PLAN

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 1200'

ISSUE N°	DATE	D E S C R I P T I O N	DRAWN	DESIGNED	APPROVED
01	02-01-2026	DETAILED DESIGN	HANNAN	ENGR. FAIEZ	ENGR. HSAN-UL-HAQ
02	21-04-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. HSAN-UL-HAQ
03					
04					
05					
06					
07					

DRAWING N°: PRMSC-BWN-MAK-SEW-KP-00

SHEET 00 OF 00

REV 01

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT
ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

PRMSC-BWN-MAK-SEW-KP-00

LAYOUT PLAN

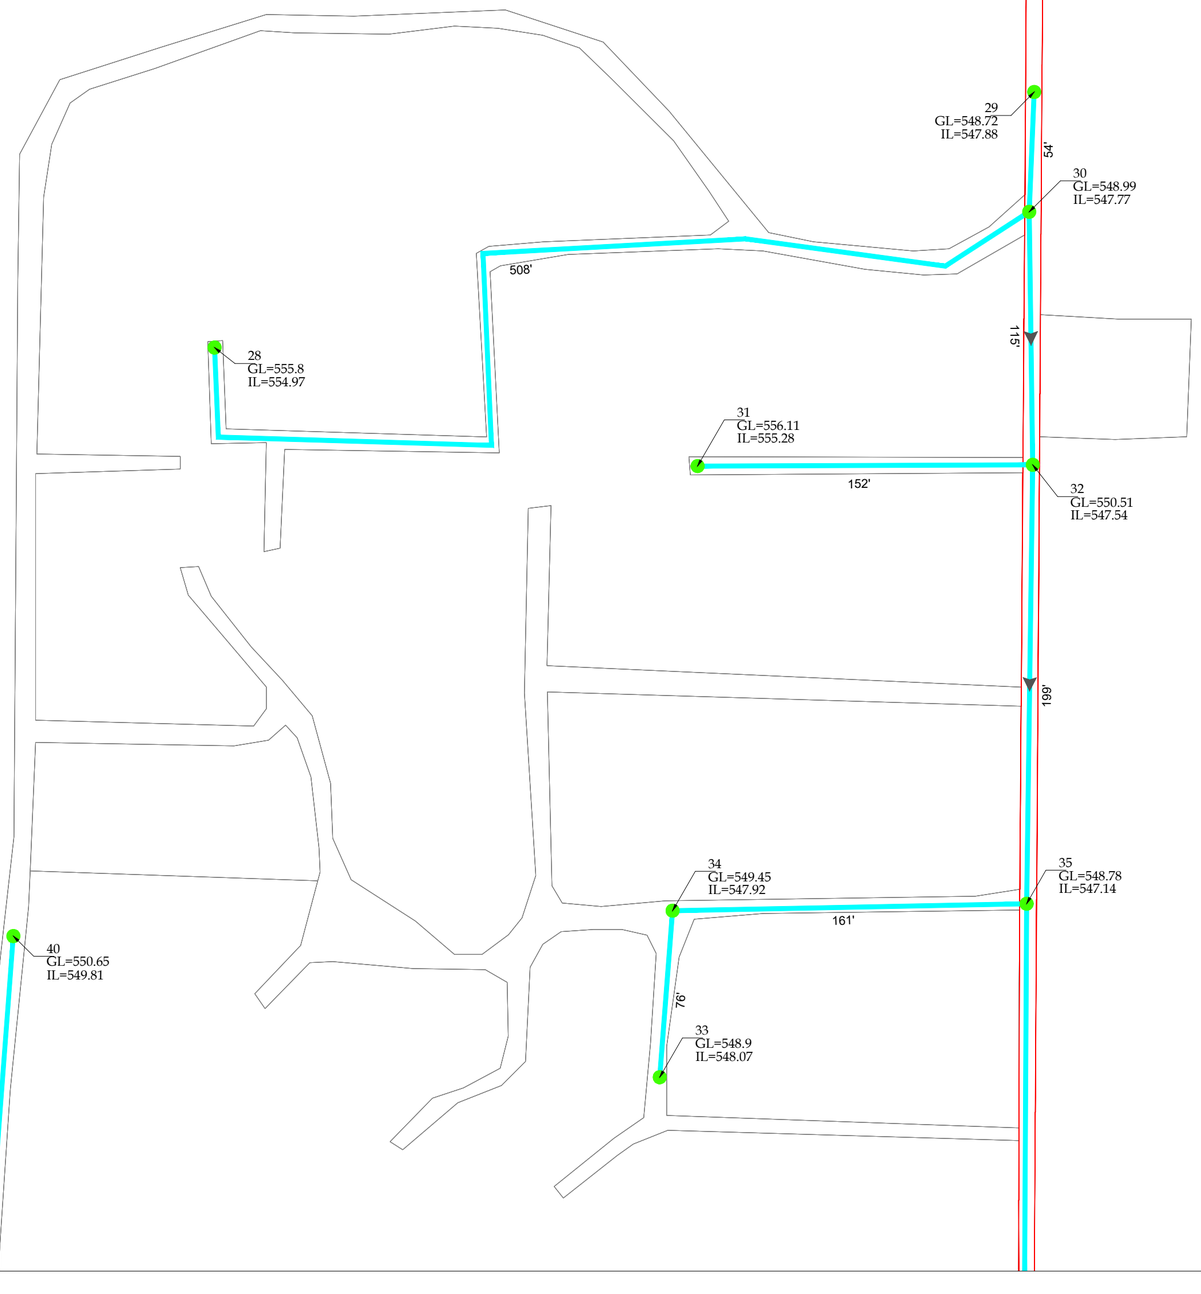

N
W
E
S



KEY PLAN

LEGEND:

- DRAIN TYPE - I
- SULLAGE CARRIER
- Ø3" HDPE PIPE
- EXISTING SOLING
- METALLED ROAD
- PROPOSED CULVERT
- BOUNDARY

VILLAGE: MUHAMMAD ASAD KHAN (BWN)

TITLE.

DRAINAGE SYSTEM LAYOUT PLAN-01

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	02-01-2026	DETAILED DESIGN	HANNAN	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02	21-04-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-MAK-SEW-LP-01	01 OF 07	01

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:
ASIAN CONSULTING ENGINEERS
www.asiancon.com

PRMSC-BWN-MAK-SEW-LP-01

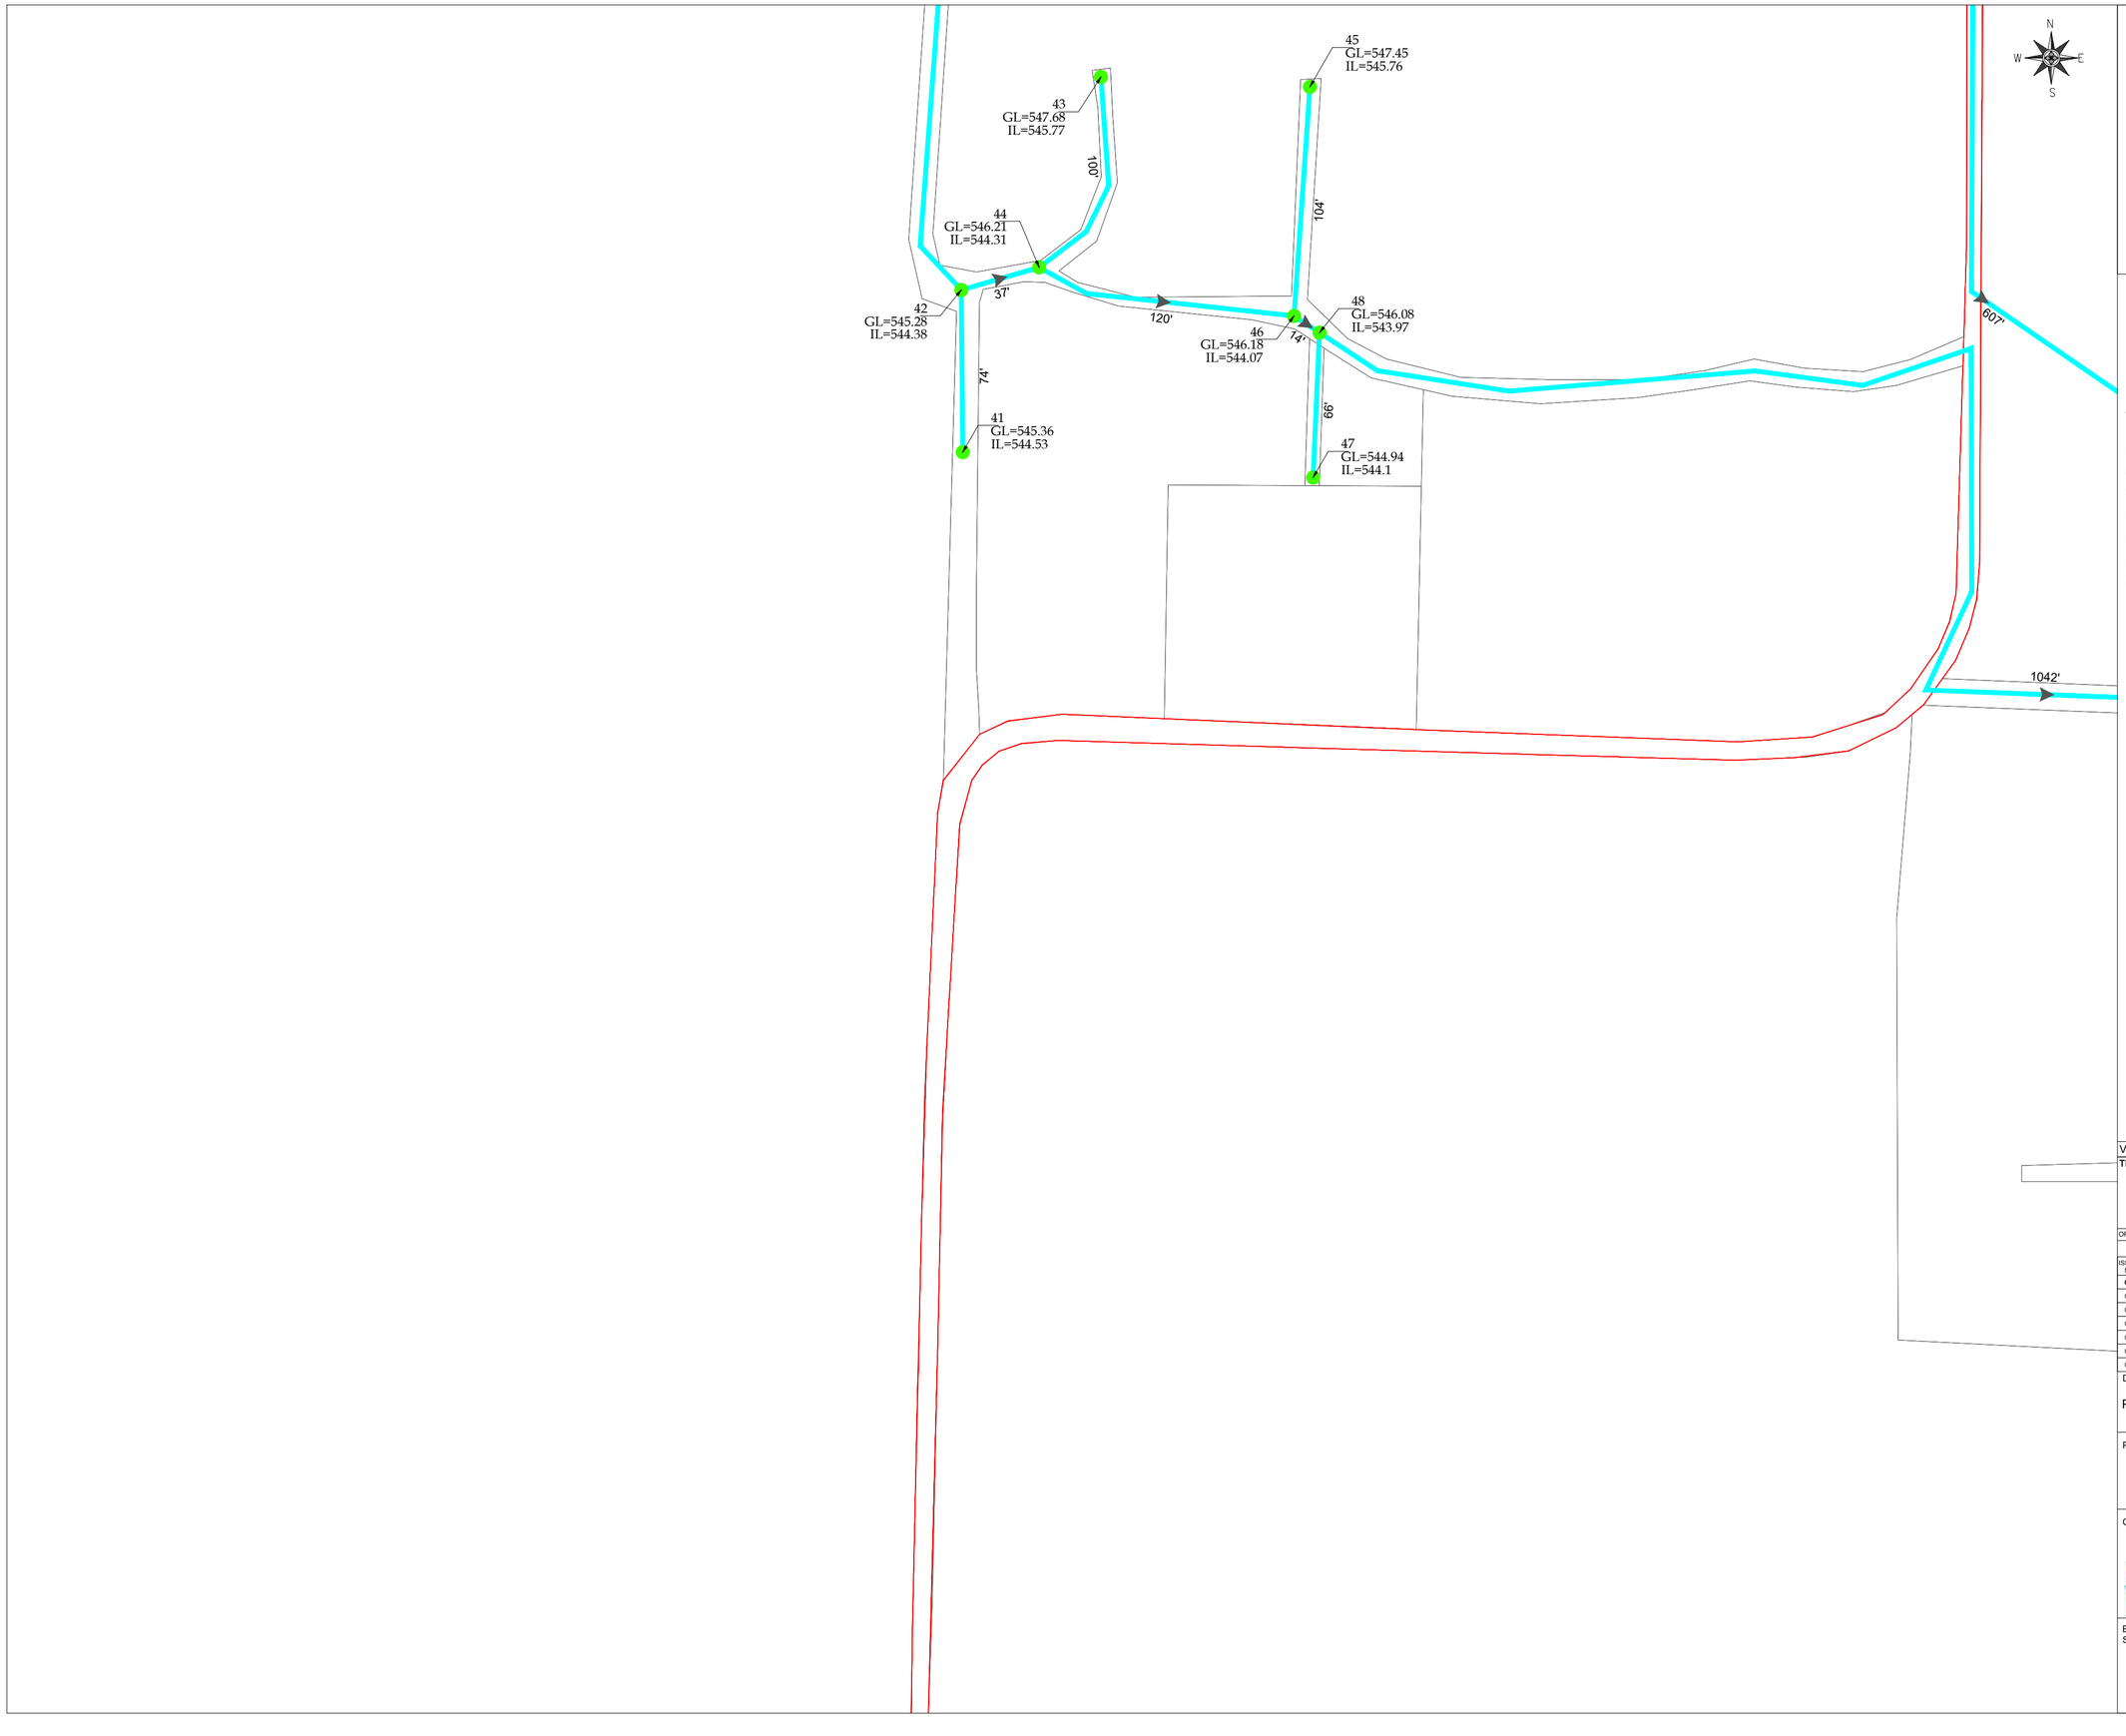



KEY PLAN

LEGEND:

- DRAIN TYPE - I
- SULLAGE CARRIER
- Ø3" HDPE PIPE
- EXISTING SOLING
- METALLED ROAD
- PROPOSED CULVERT
- BOUNDARY

VILLAGE: MUHAMMAD ASAD KHAN (BWN)

TITLE.

DRAINAGE SYSTEM LAYOUT PLAN-02

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	02-01-2026	DETAILED DESIGN	HANNAN	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02	21-04-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-MAK-SEW-LP-02	02 OF 07	01

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS
www.asiaecon.com.pv

PRMSC-BWN-MAK-SEW-LP-02

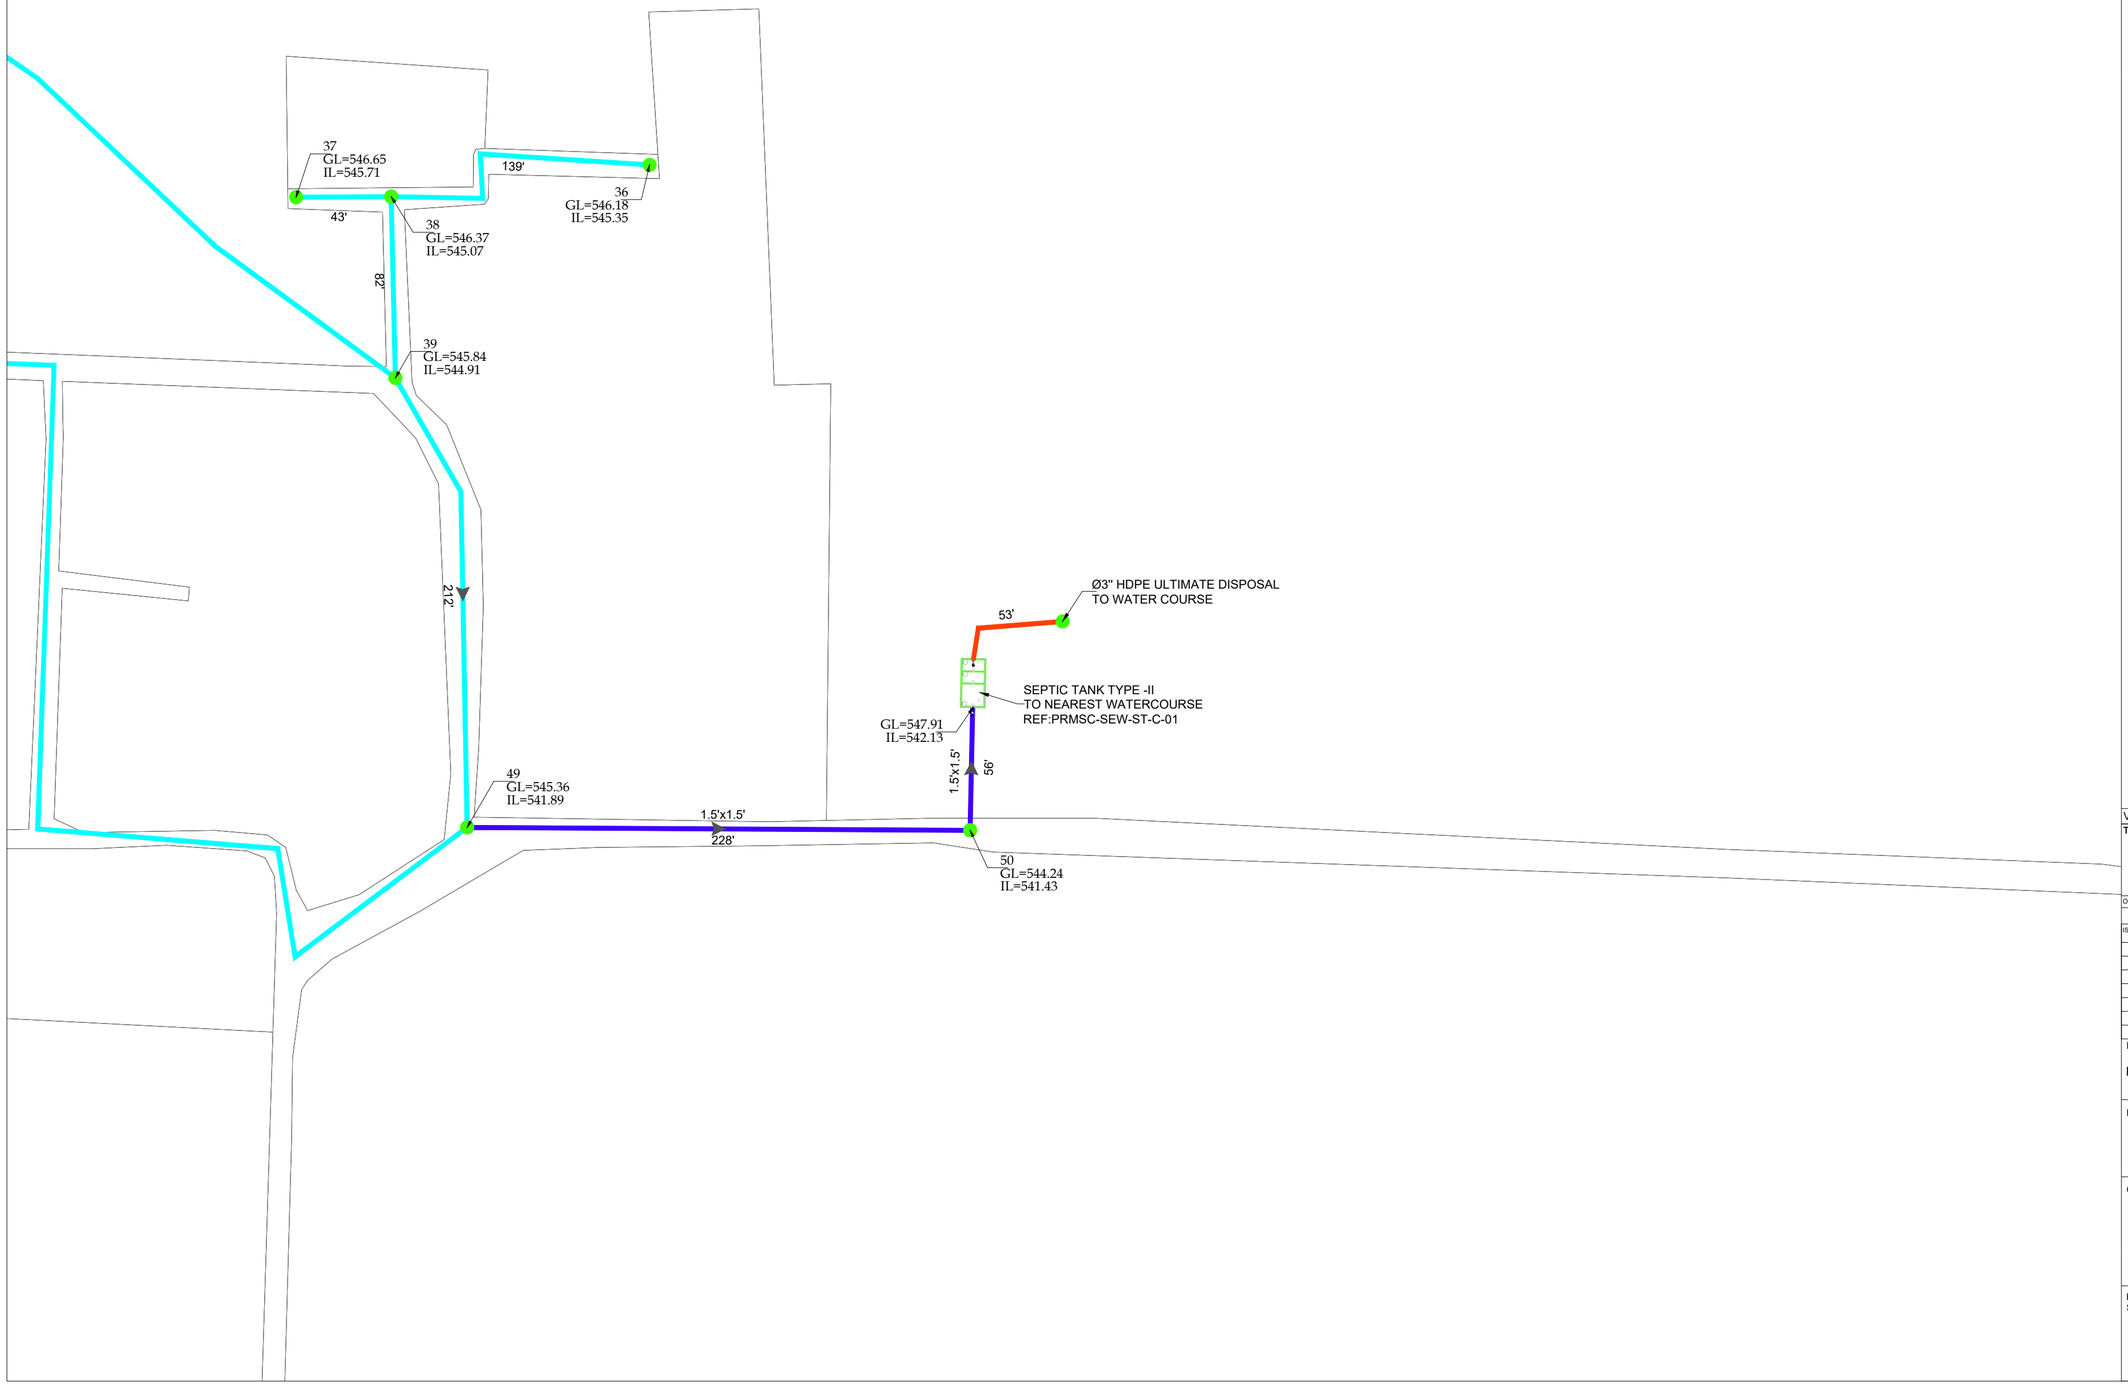

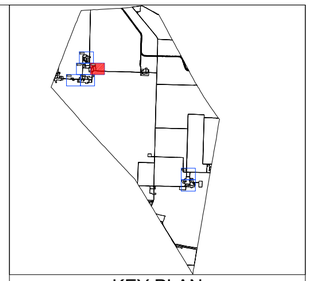

KEY PLAN

LEGEND:

- DRAIN TYPE - I
- SULLAGE CARRIER
- Ø3" HDPE PIPE
- EXISTING SOLING
- METALLED ROAD
- PROPOSED CULVERT
- BOUNDARY

VILLAGE: MUHAMMAD ASAD KHAN (BWN)

TITLE.

DRAINAGE SYSTEM LAYOUT PLAN-03

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	02-01-2026	DETAILED DESIGN	HANNAN	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02	21-04-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
03					
04					
05					
06					
07					

DRAWING Nº: PRMSC-BWN-MAK-SEW-LP-03

SHEET 03 OF 07

REV 01

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:
ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

PRMSC-BWN-MAK-SEW-LP-03

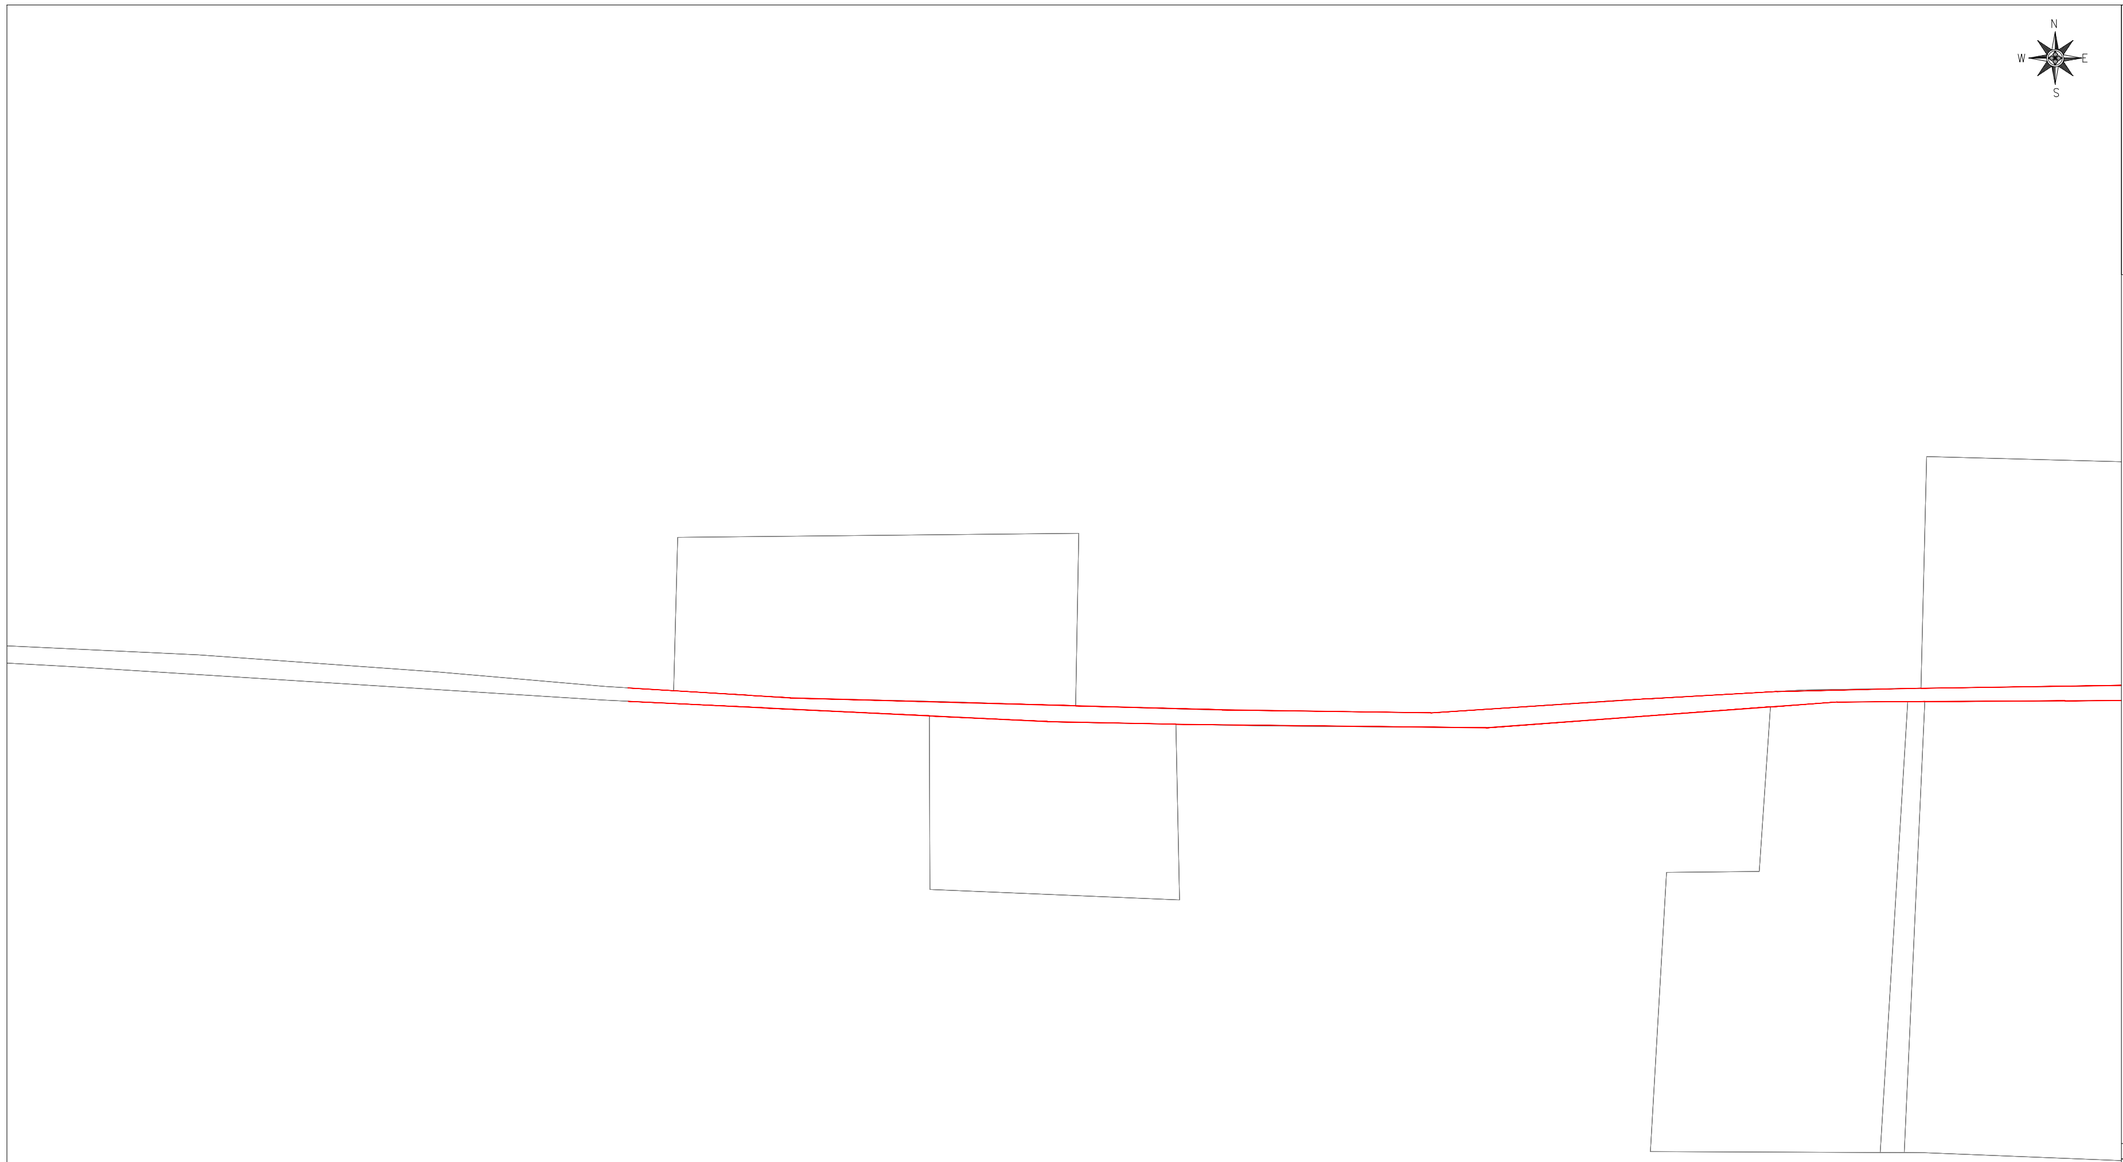

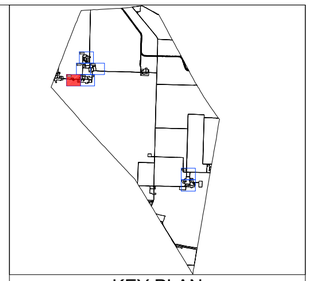

KEY PLAN

LEGEND:

- DRAIN TYPE - I
- SULLAGE CARRIER
- Ø3" HDPE PIPE
- EXISTING SOLING
- METALLED ROAD
- PROPOSED CULVERT
- BOUNDARY

VILLAGE: MUHAMMAD ASAD KHAN (BWN)

TITLE.

DRAINAGE SYSTEM LAYOUT PLAN-04

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	02-01-2026	DETAILED DESIGN	HANNAN	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02	21-04-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-MAK-SEW-LP-04	04 OF 07	01

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

PRMSC-BWN-MAK-SEW-LP-04

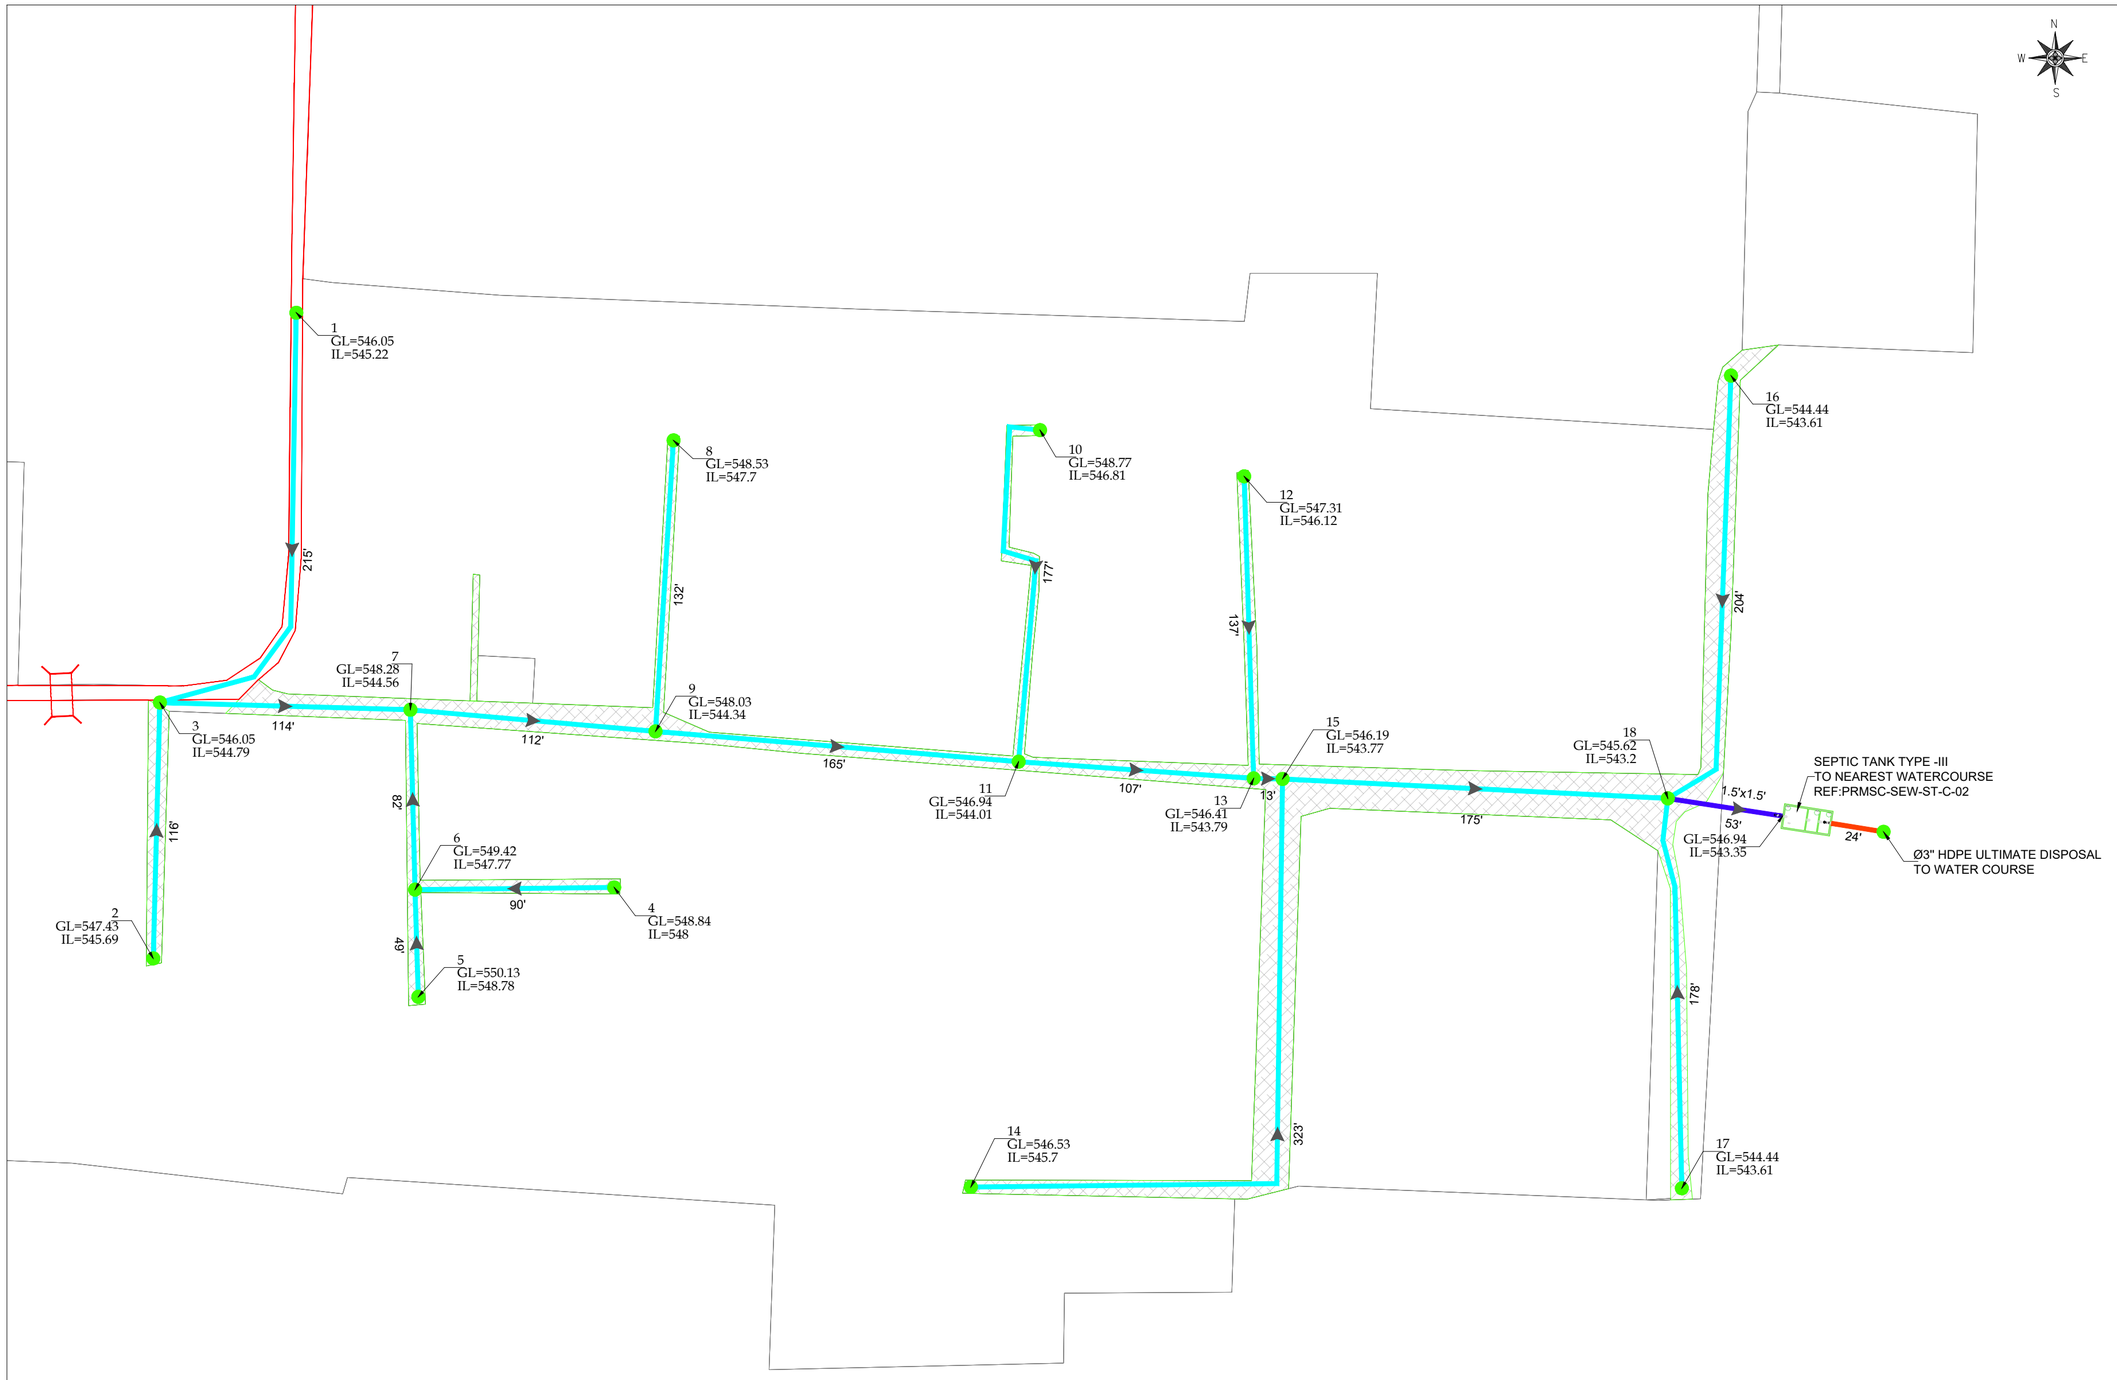

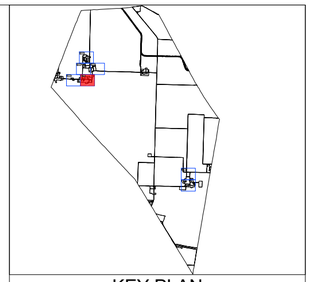

KEY PLAN

LEGEND:

- DRAIN TYPE - I
- SULLAGE CARRIER
- Ø3" HDPE PIPE
- EXISTING SOLING
- METALLED ROAD
- PROPOSED CULVERT
- BOUNDARY

VILLAGE: MUHAMMAD ASAD KHAN (BWN)

TITLE.

DRAINAGE SYSTEM LAYOUT PLAN-05

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	02-01-2026	DETAILED DESIGN	HANNAN	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02	21-04-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
03					
04					
05					
06					
07					

DRAWING N°: PRMSC-BWN-MAK-SEW-LP-05

SHEET 05 OF 07

REV 01

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

PRMSC-BWN-MAK-SEW-LP-05

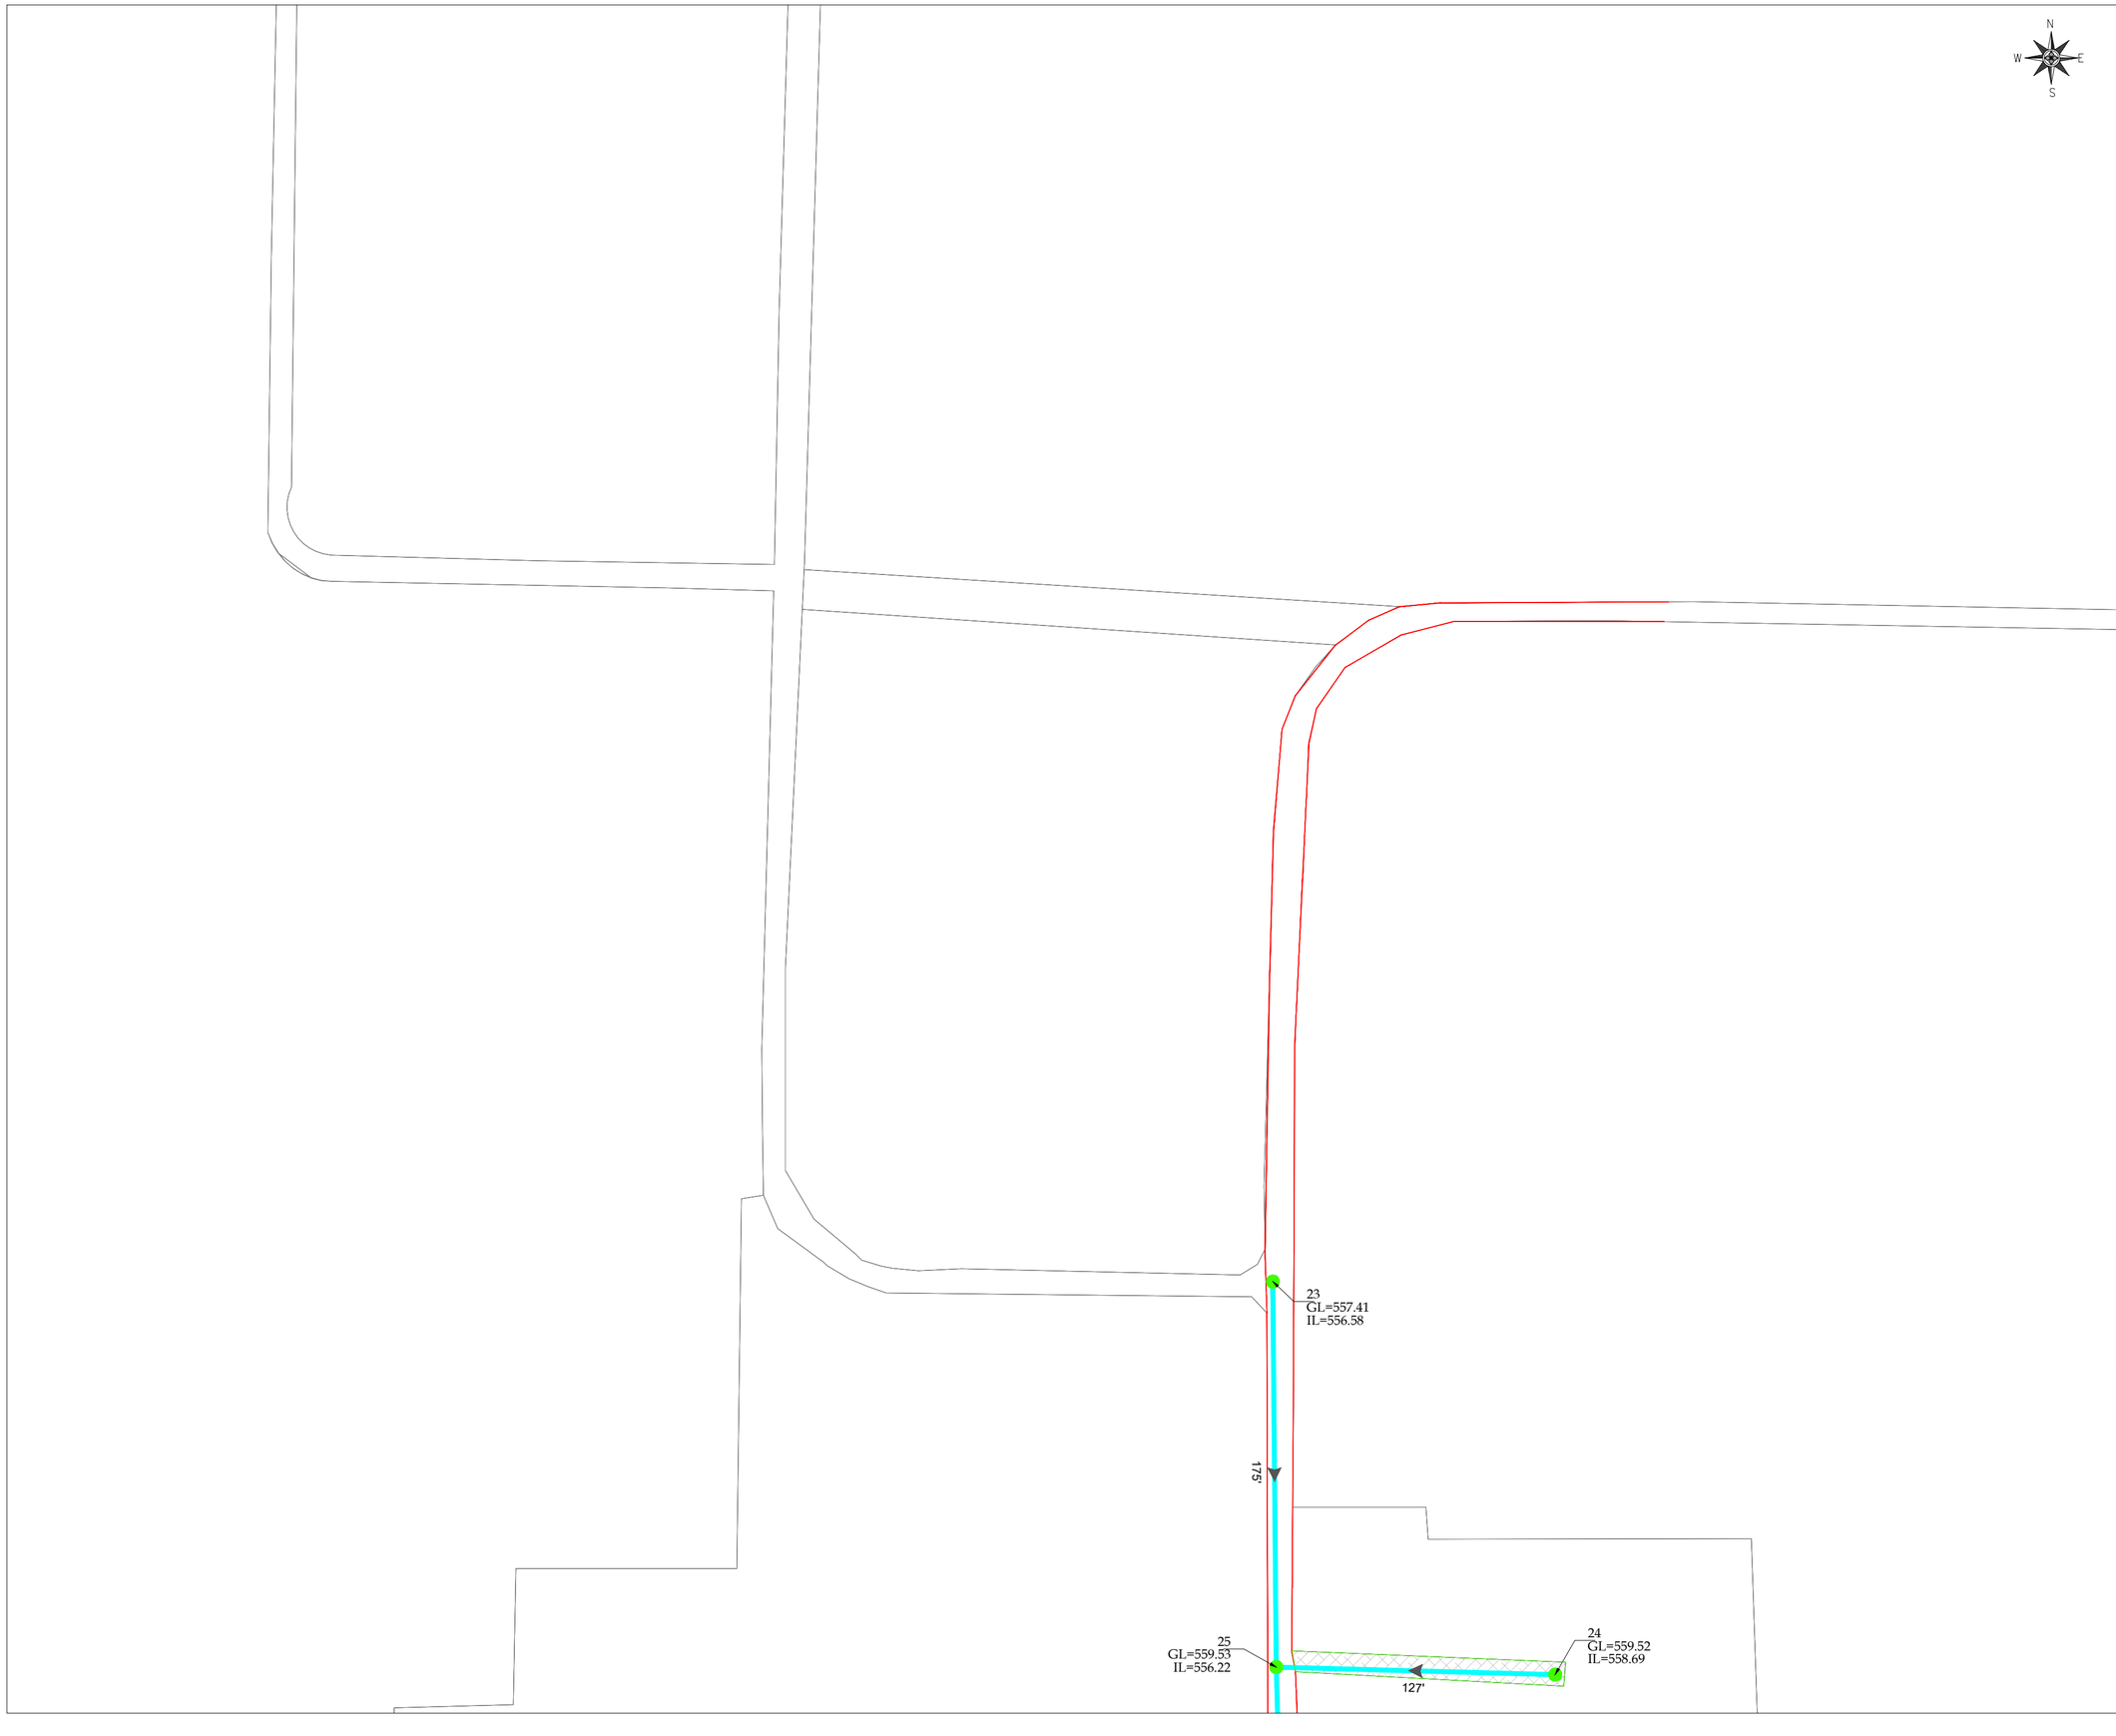

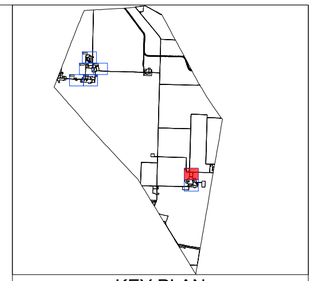

KEY PLAN

LEGEND:

- DRAIN TYPE - I
- SULLAGE CARRIER
- Ø3" HDPE PIPE
- EXISTING SOLING
- METALLED ROAD
- PROPOSED CULVERT
- BOUNDARY

VILLAGE: MUHAMMAD ASAD KHAN (BWN)

TITLE.

DRAINAGE SYSTEM LAYOUT PLAN-06

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	02-01-2026	DETAILED DESIGN	HANNAN	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02	21-04-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
03					
04					
05					
06					
07					

DRAWING Nº: PRMSC-BWN-MAK-SEW-LP-06

SHEET 06 OF 07

REV 01

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

PRMSC-BWN-MAK-SEW-LP-06

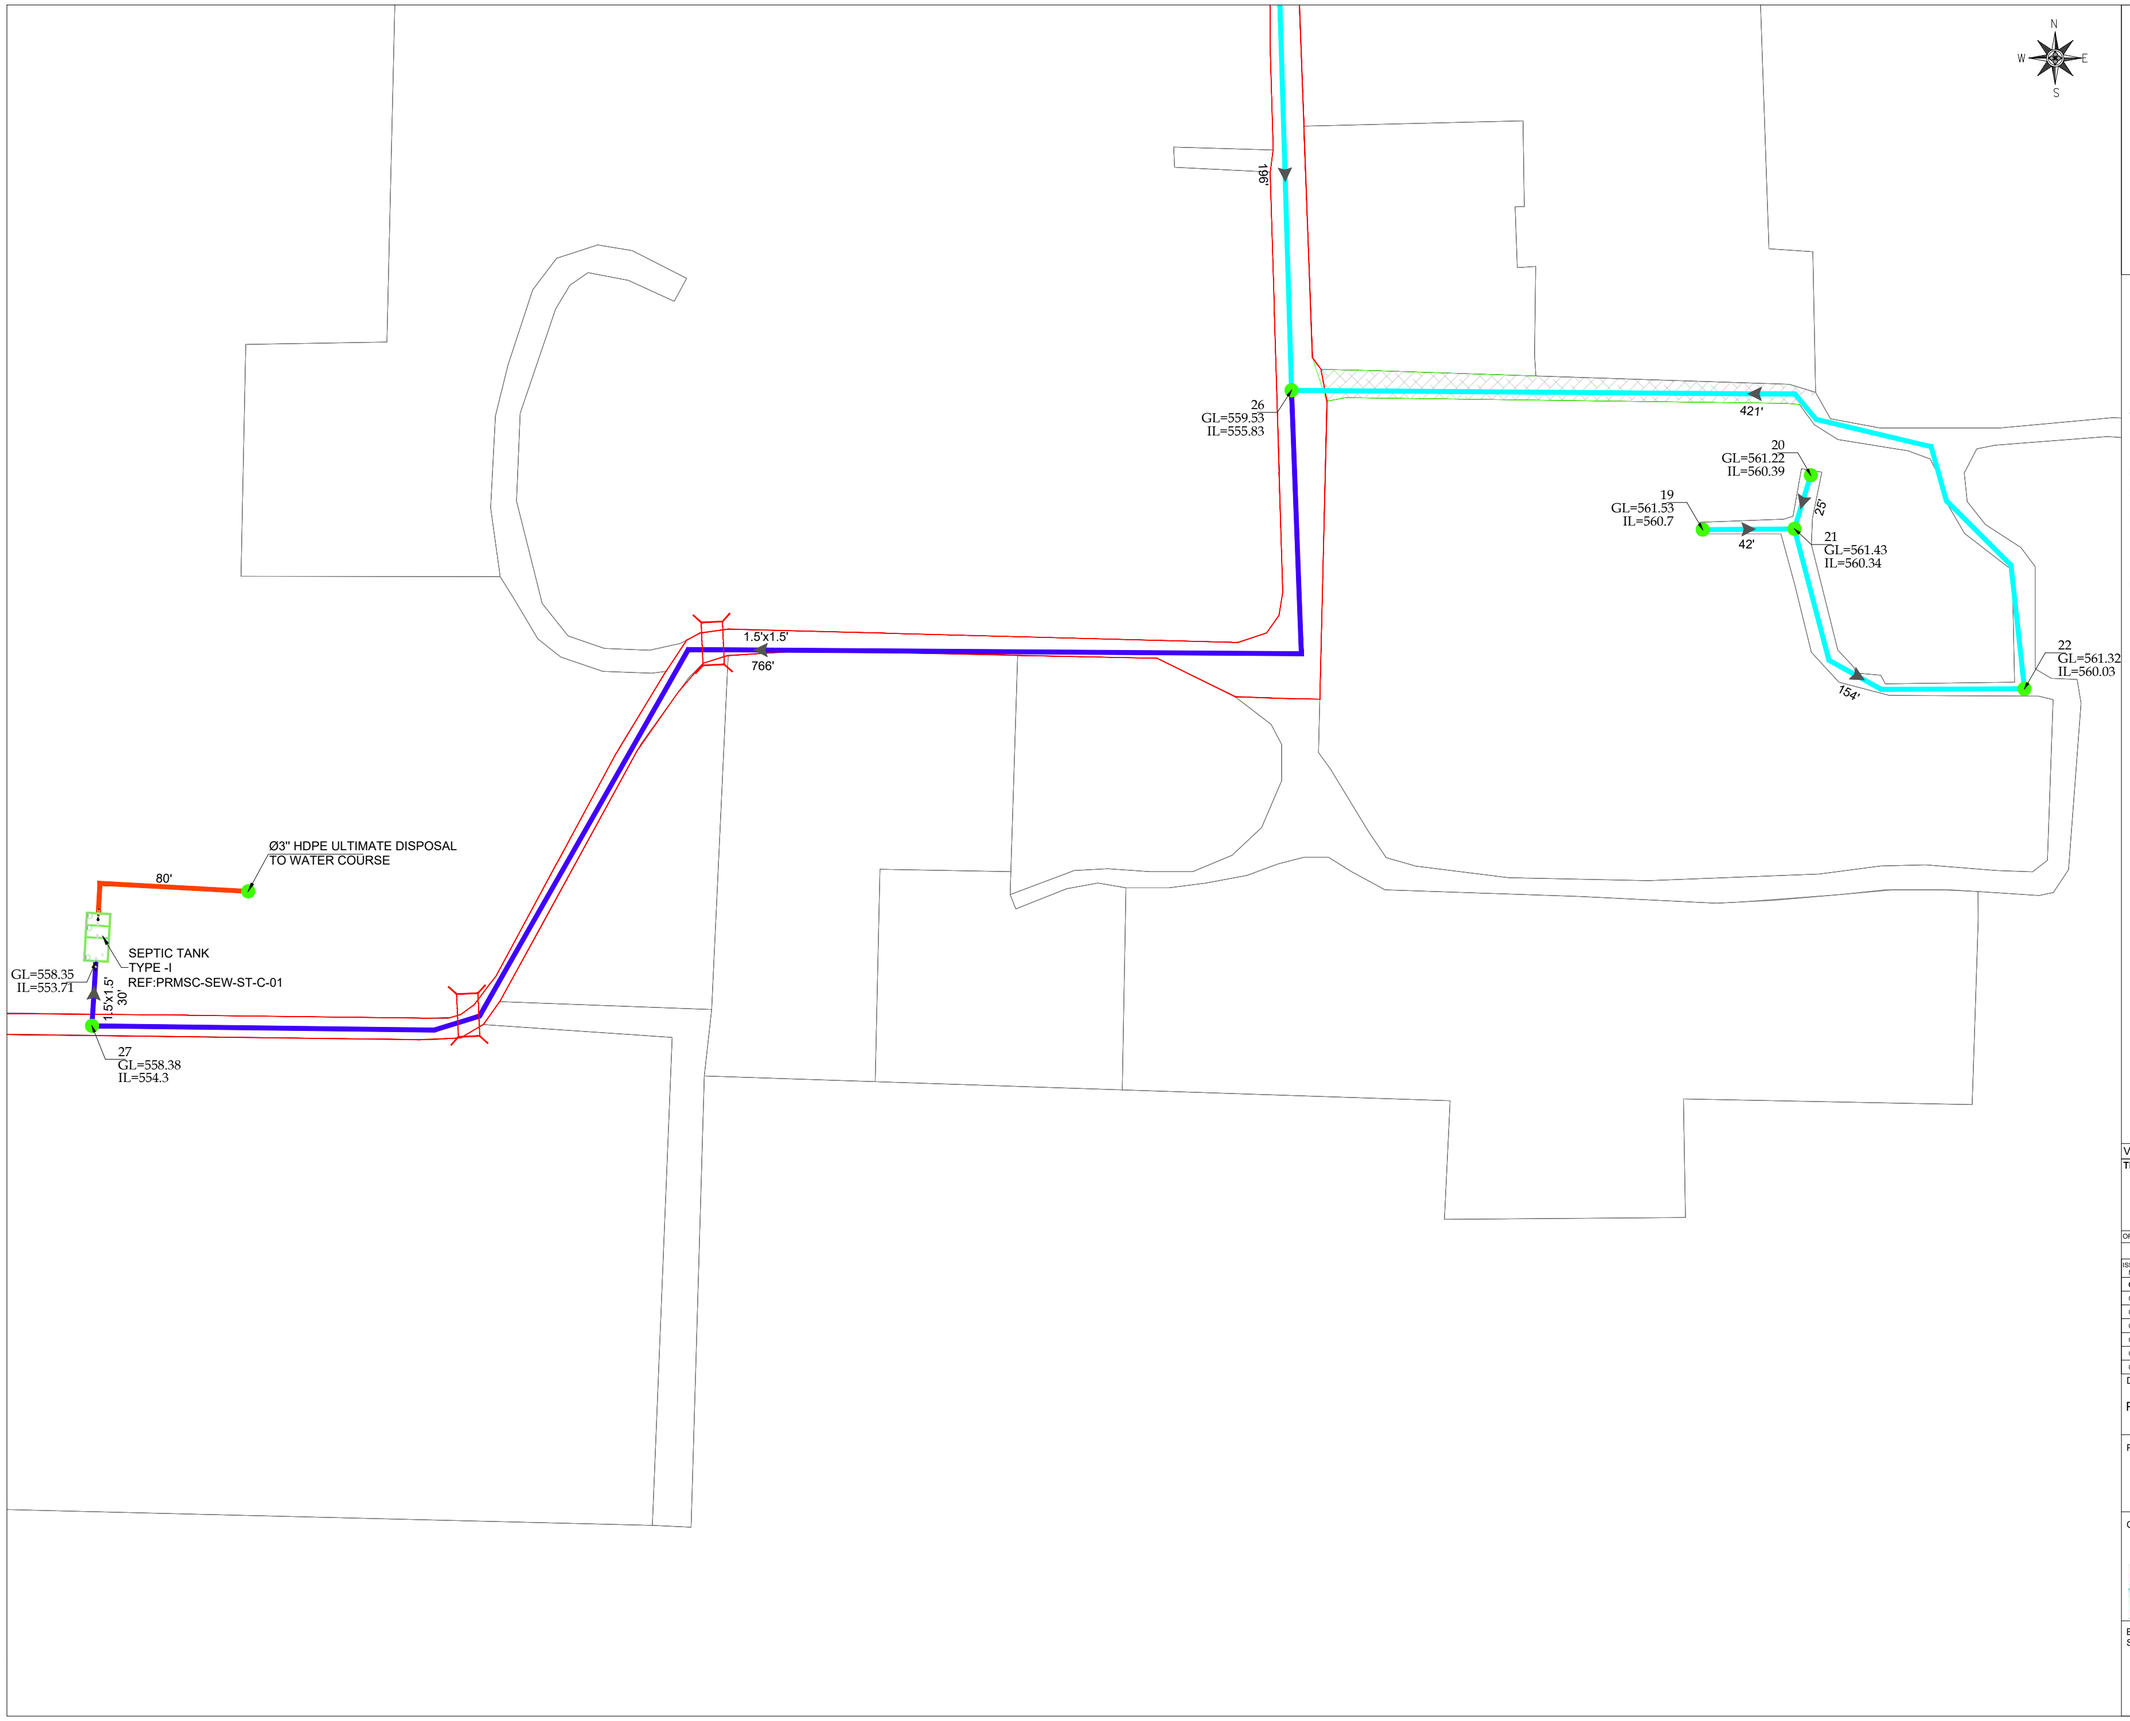

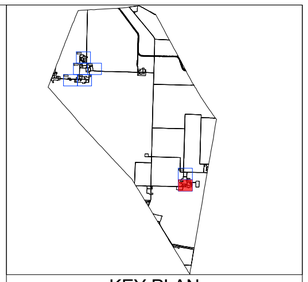

KEY PLAN

LEGEND:

- DRAIN TYPE - I
- SULLAGE CARRIER
- Ø3" HDPE PIPE
- EXISTING SOLING
- METALLED ROAD
- PROPOSED CULVERT
- BOUNDARY

VILLAGE: MUHAMMAD ASAD KHAN (BWN)

TITLE.

DRAINAGE SYSTEM LAYOUT PLAN-07

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	02-01-2026	DETAILED DESIGN	HANNAN	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02	21-04-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
03					
04					
05					
06					
07					

DRAWING Nº: PRMSC-BWN-MAK-SEW-LP-07

SHEET 07 OF 07

REV 01

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS
www.asianconsultants.com JV

PRMSC-BWN-MAK-SEW-LP-07

HYDRAULIC STATEMENT								
Node		Length	Slope	Elevation Ground	Elevation Ground	Elevation Invert	Elevation Invert	Depth
FROM	TO	ft	ft/ft	U/S	D/S	U/S	D/S	ft
1	3	215	0.002	546.05	546.05	545.22	544.79	0.83
2	3	116	0.004	547.43	546.05	545.69	545.22	1.74
3	7	114	0.002	546.05	548.28	544.79	544.56	1.26
4	6	90	0.003	548.84	549.42	548	547.77	0.83
5	6	49	0.004	550.13	549.42	548.78	548.59	1.35
6	7	82	0.004	549.42	548.28	547.77	547.44	1.65
7	9	112	0.002	548.28	548.03	544.56	544.34	3.71
8	9	132	0.004	548.53	548.03	547.7	547.19	0.83
9	11	165	0.002	548.03	546.94	544.34	544.01	3.69
10	11	177	0.004	548.77	546.94	546.81	546.1	1.96
11	13	107	0.002	546.94	546.41	544.01	543.79	2.93
12	13	137	0.004	547.31	546.41	546.12	545.57	1.19
13	15	13	0.002	546.41	546.19	543.79	543.77	2.61
14	15	323	0.002	546.53	546.19	545.7	545.06	0.83
15	18	175	0.003	546.19	545.62	543.77	543.2	2.42
16	18	204	0.002	544.44	545.62	543.61	543.2	0.83
17	18	178	0.002	544.44	545.62	543.61	543.2	0.83
18	Septic Tank Type III	91	0.002	545.62	547.07	543.2	543.01	2.42
21	19	42	0.002	561.43	561.53	560.6	560.7	0.83
21	20	25	0.002	561.43	561.22	560.34	560.39	0.83
22	21	154	0.002	561.32	561.43	560.03	560.34	1.09
26	22	421	0.003	559.53	561.32	558.7	560.03	1.29
23	25	175	0.002	557.41	559.53	556.58	556.22	0.83
25	24	127	0.002	559.53	559.52	558.43	558.69	0.83
25	26	196	0.002	559.53	559.53	556.22	555.83	3.3
26	27	766	0.002	559.53	558.38	555.83	554.3	3.7
27	Septic Tank Type I	30	0.002	558.38	557.66	554.3	554.24	4.08
28	30	508	0.014	555.8	548.99	554.97	547.77	0.83
29	30	54	0.002	548.72	548.99	547.88	547.77	0.83
30	32	115	0.002	548.99	550.51	547.77	547.54	1.21
31	32	152	0.051	556.11	550.51	555.28	547.54	0.83
32	35	199	0.002	550.51	548.78	547.54	547.14	2.97
33	34	76	0.002	548.9	549.45	548.07	547.92	0.83
34	35	161	0.002	549.45	548.78	547.92	547.59	1.53
35	39	607	0.004	548.78	545.84	547.14	544.91	1.64
36	38	139	0.002	546.18	546.37	545.35	545.07	0.83
37	38	43	0.004	546.65	546.37	545.71	545.54	0.93
38	39	82	0.002	546.37	545.84	545.07	544.91	1.3
39	49	212	0.002	545.84	545.36	544.91	544.48	0.94
40	42	290	0.019	550.65	545.28	549.81	544.38	0.83
41	42	74	0.002	545.36	545.28	544.53	544.38	0.83
42	44	37	0.002	545.28	546.21	544.38	544.31	0.9
43	44	100	0.004	547.68	546.21	545.77	545.37	1.91
44	46	120	0.002	546.21	546.18	544.31	544.07	1.9
45	46	104	0.004	547.45	546.18	545.76	545.34	1.69

HYDRAULIC STATEMENT								
Node		Length	Slope	Elevation Ground	Elevation Ground	Elevation Invert	Elevation Invert	Depth
FROM	TO	ft	ft/ft	U/S	D/S	U/S	D/S	ft
46	48	14	0.002	546.18	546.08	544.07	544.04	2.11
47	48	66	0.002	544.94	546.08	544.1	543.97	0.83
48	49	1042	0.002	546.08	545.36	543.97	541.89	2.11
49	50	228	0.002	545.36	544.24	541.89	541.43	3.47
50	Septic Tank Type II	56	0.002	544.24	547.91	541.43	541.32	2.81

VILLAGE: MUHAMMAD ASAD KHAN (BWN)

TITLE.

HYDRAULIC STATEMENT

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	02-01-2026	DETAILED DESIGN	HANNAN	ENGR FAIEZ	ENGR HSAN-UL-HAQ
02	21-04-2026	DETAILED DESIGN	MUNEEB	ENGR FAIEZ	ENGR HSAN-UL-HAQ
03					
04					
05					
06					
07					

DRAWING Nº: PRMSC-BWN-MAK-SEW-HS-01

SHEET 01 OF 01

REV 01

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT

ASIAN CONSULTING ENGINEERS www.asiancon.com

PRMSC-BWN-MAK-SEW-HS-00

MUHSAN PURA

KEY PLAN

Revenue Village: Muhsan Pura Sheet-1

District:	Bahawalnagar
Tehsil:	Bahawalnagar
Revenue Village:	Muhsan Pura

Ahmad Kot

SEPTIC TANK-T3
Plot Size=2.82 Marla

Title:
Proposed Drainage Network Plan

Legend:

- SETTLEMENT
- NODE
- 6" uPVC PIPE
- DRAIN TYPE-1
- SULLAGE CARRIER
- SEPTIC TANK
- SETTLEMENT BOUNDARY

Drain Type 1=4235 Rft
Sullage Carrier= 1874 Rft

Scale: 1:1,900
1 inch = 158 feet
Paper Size: A3

0 40 80 160
Kilometers

Project:
Engineering Design & Construction Supervision, Punjab Rural Sustainable Water Supply & Sanitation Project, Cluster South III

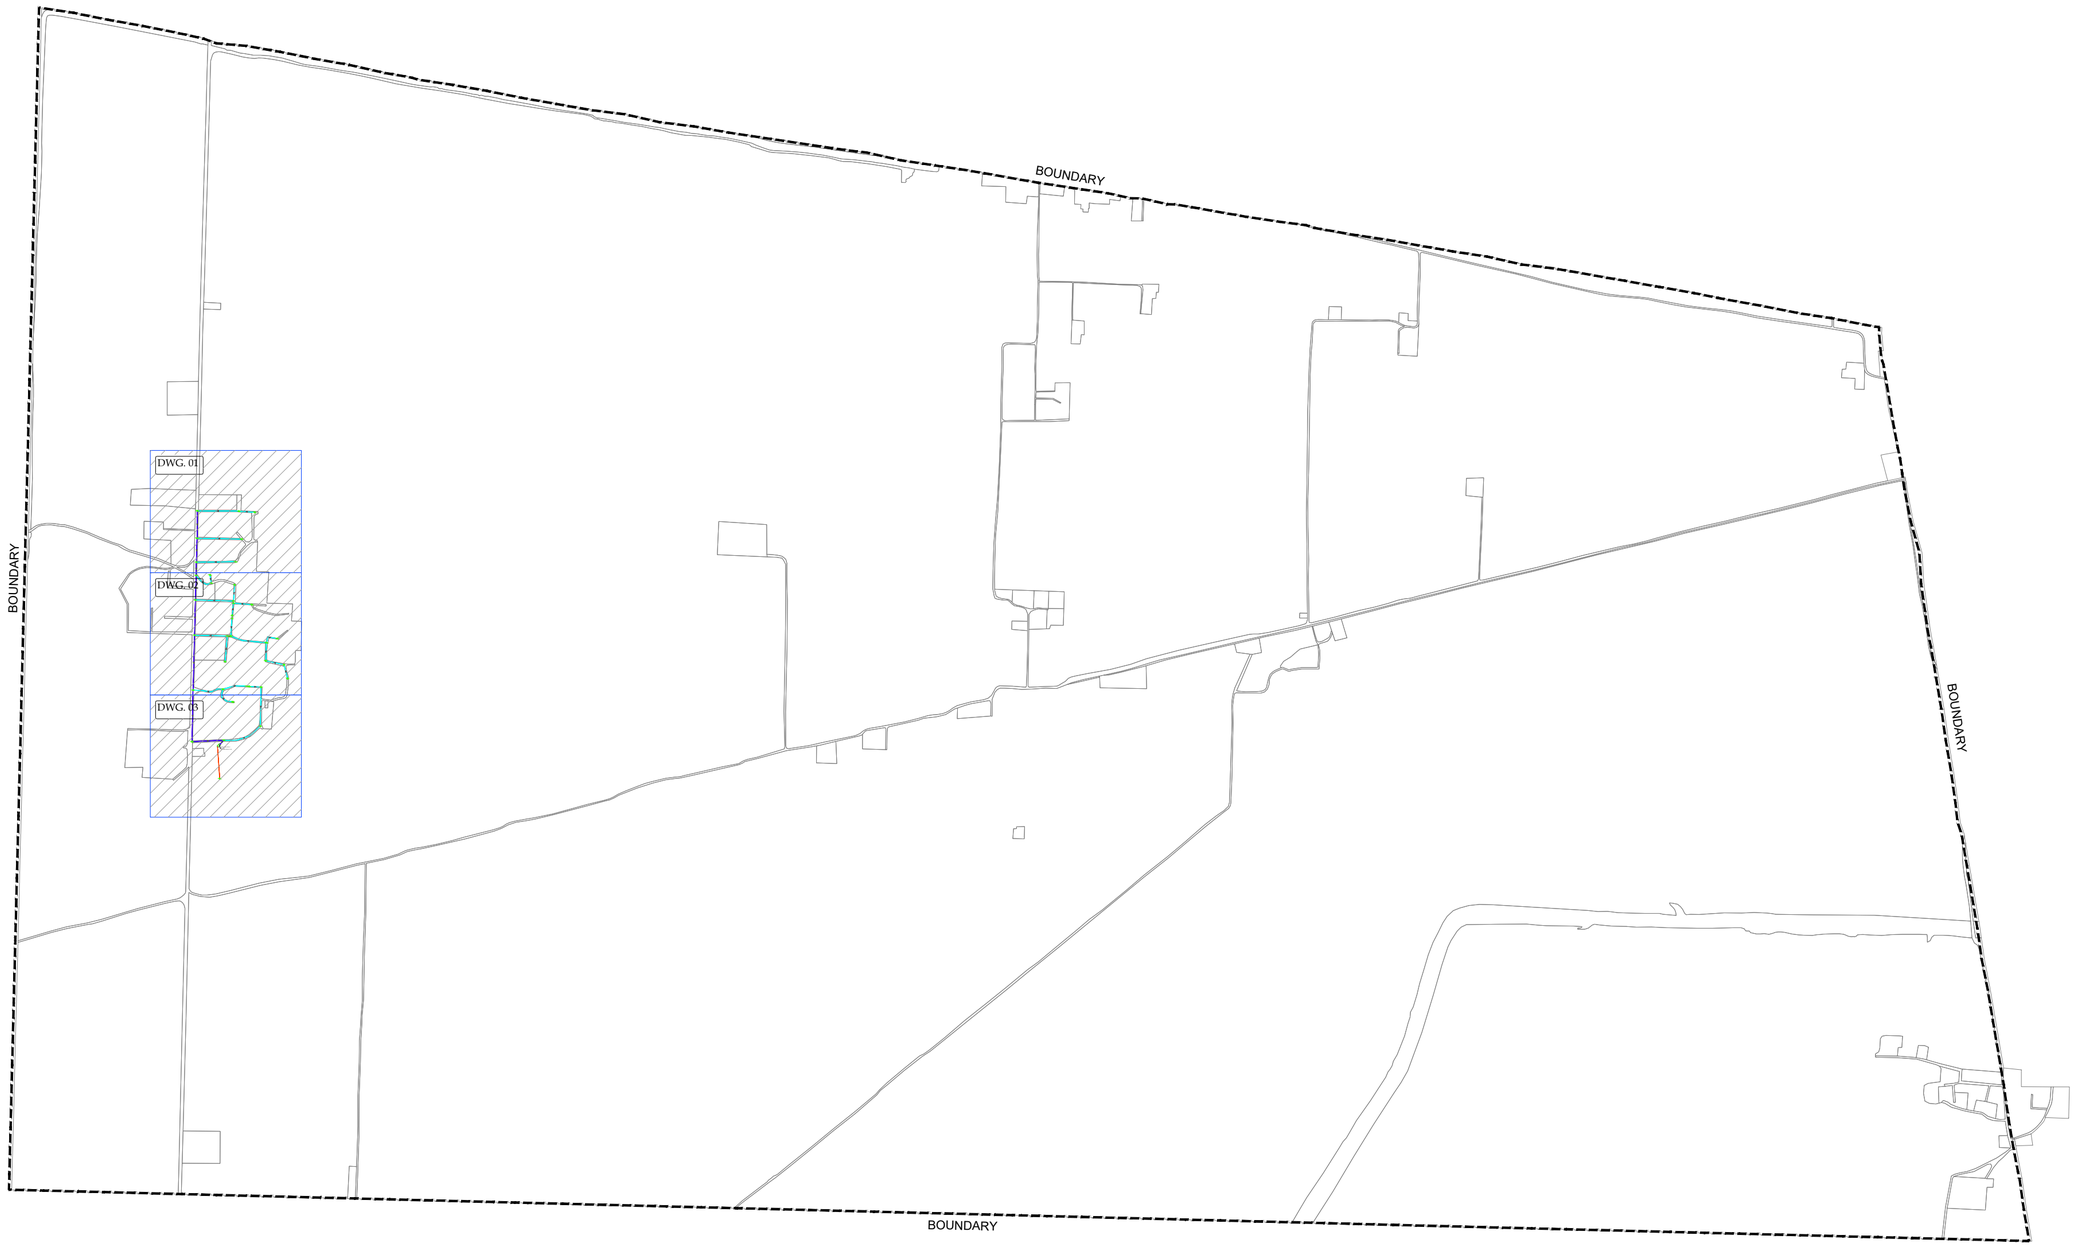

LEGEND:

- DRAIN TYPE - I
- SULLAGE CARRIER
- Ø3" HDPE PIPE
- BOUNDARY

VILLAGE: MOHSIN PUR (BWN)

TITLE.

DRAINAGE SYSTEM KEY PLAN

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 700'

ISSUE N°	DATE	D E S C R I P T I O N	DRAWN	DESIGNED	APPROVED
01	07-01-2026	DETAILED DESIGN	HANNAN	ENGR. FAIEZ	ENGR. HSAN-UL-HAQ
02	20-04-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. HSAN-UL-HAQ
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-MHP-SEW-KP-00	00 OF 00	01

PROJECT:

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:

PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT

ASIAN CONSULTING ENGINEERS www.asianeng.com.pk

PRMSC-BWN-MHP-SEW-KP-00

LAYOUT PLAN

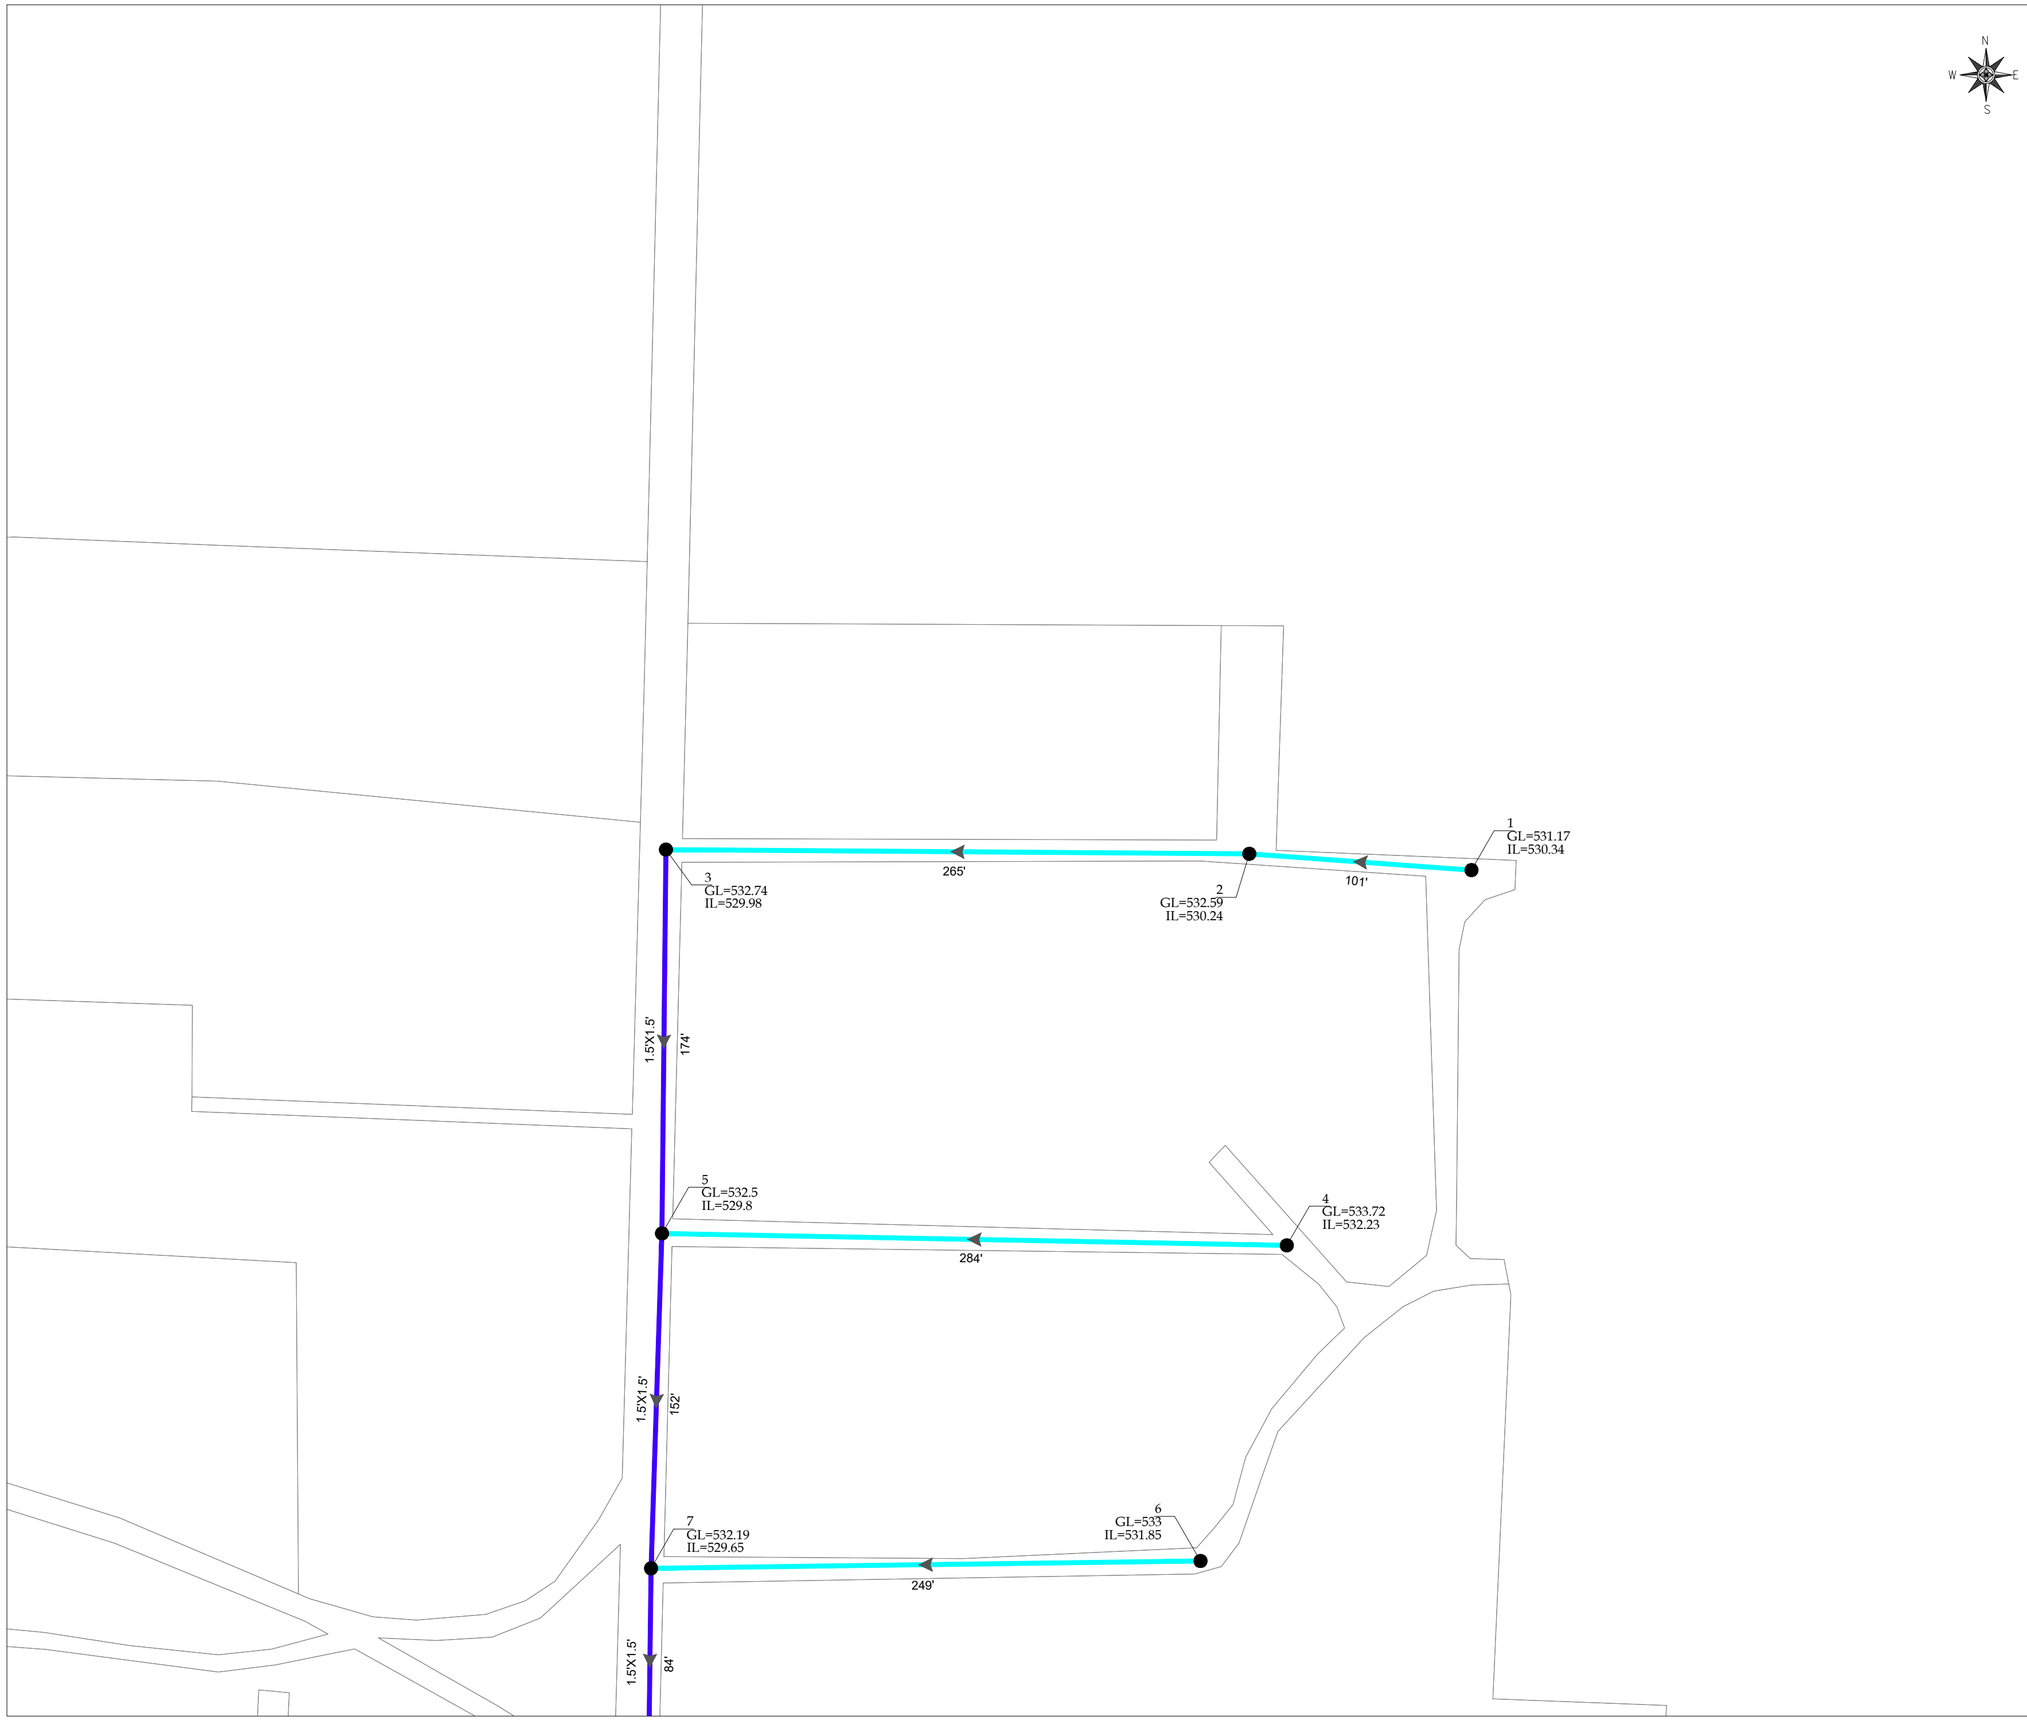

PRMSC-BWN-MHP-SEW-LP-01



KEY PLAN

LEGEND:

- DRAIN TYPE - I
- SULLAGE CARRIER
- Ø3" HDPE PIPE
- BOUNDARY

VILLAGE: MOHSIN PUR (BWN)

TITLE.

DRAINAGE SYSTEM LAYOUT PLAN-01

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	07-01-2026	DETAILED DESIGN	HANNAN	ENGR. FAIEZ	ENGR. HSAN-UL-HAQ
02	20-04-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. HSAN-UL-HAQ
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-MHP-SEW-LP-01	01 OF 03	01

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

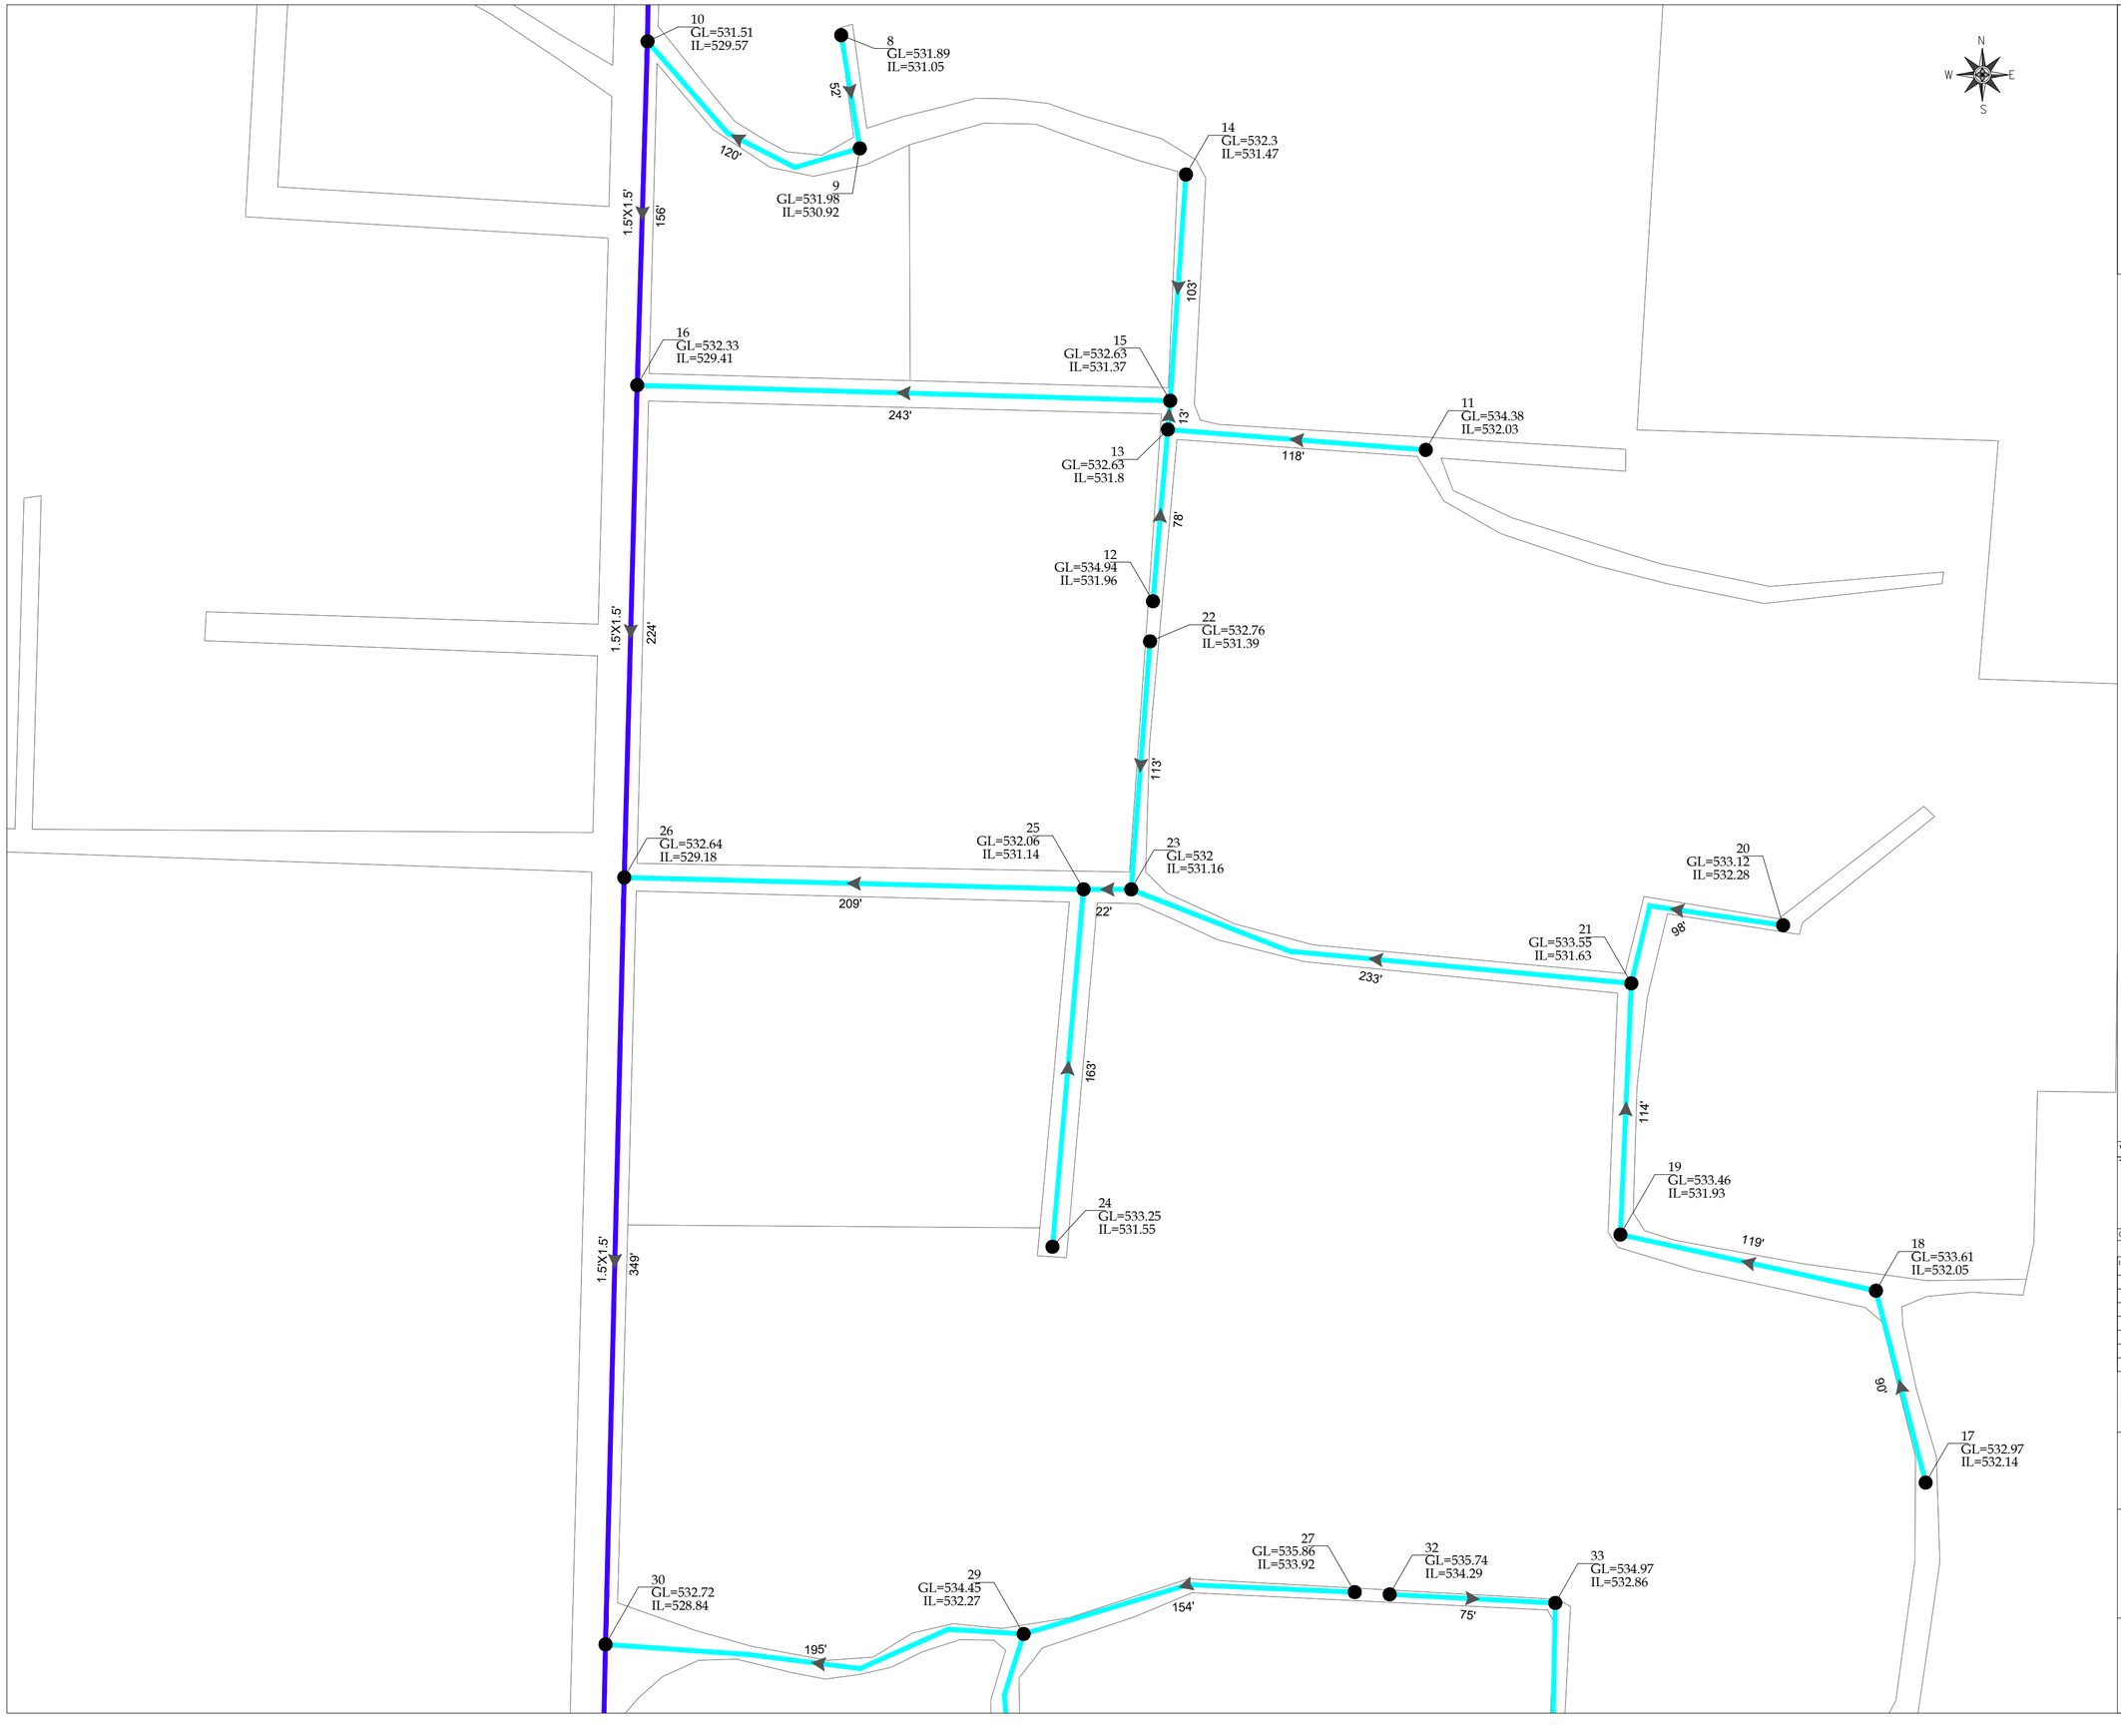

KEY PLAN

LEGEND:

- DRAIN TYPE - I
- SULLAGE CARRIER
- Ø3" HDPE PIPE
- BOUNDARY

VILLAGE: MOHSIN PUR (BWN)

TITLE.

DRAINAGE SYSTEM LAYOUT PLAN-02

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	07-01-2026	DETAILED DESIGN	HANNAN	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02	20-04-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
03					
04					
05					
06					
07					

DRAWING N°:	SHEET	REV
PRMSC-BWN-MHP-SEW-LP-02	02 OF 03	01

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

PRMSC-BWN-MHP-SEW-LP-02

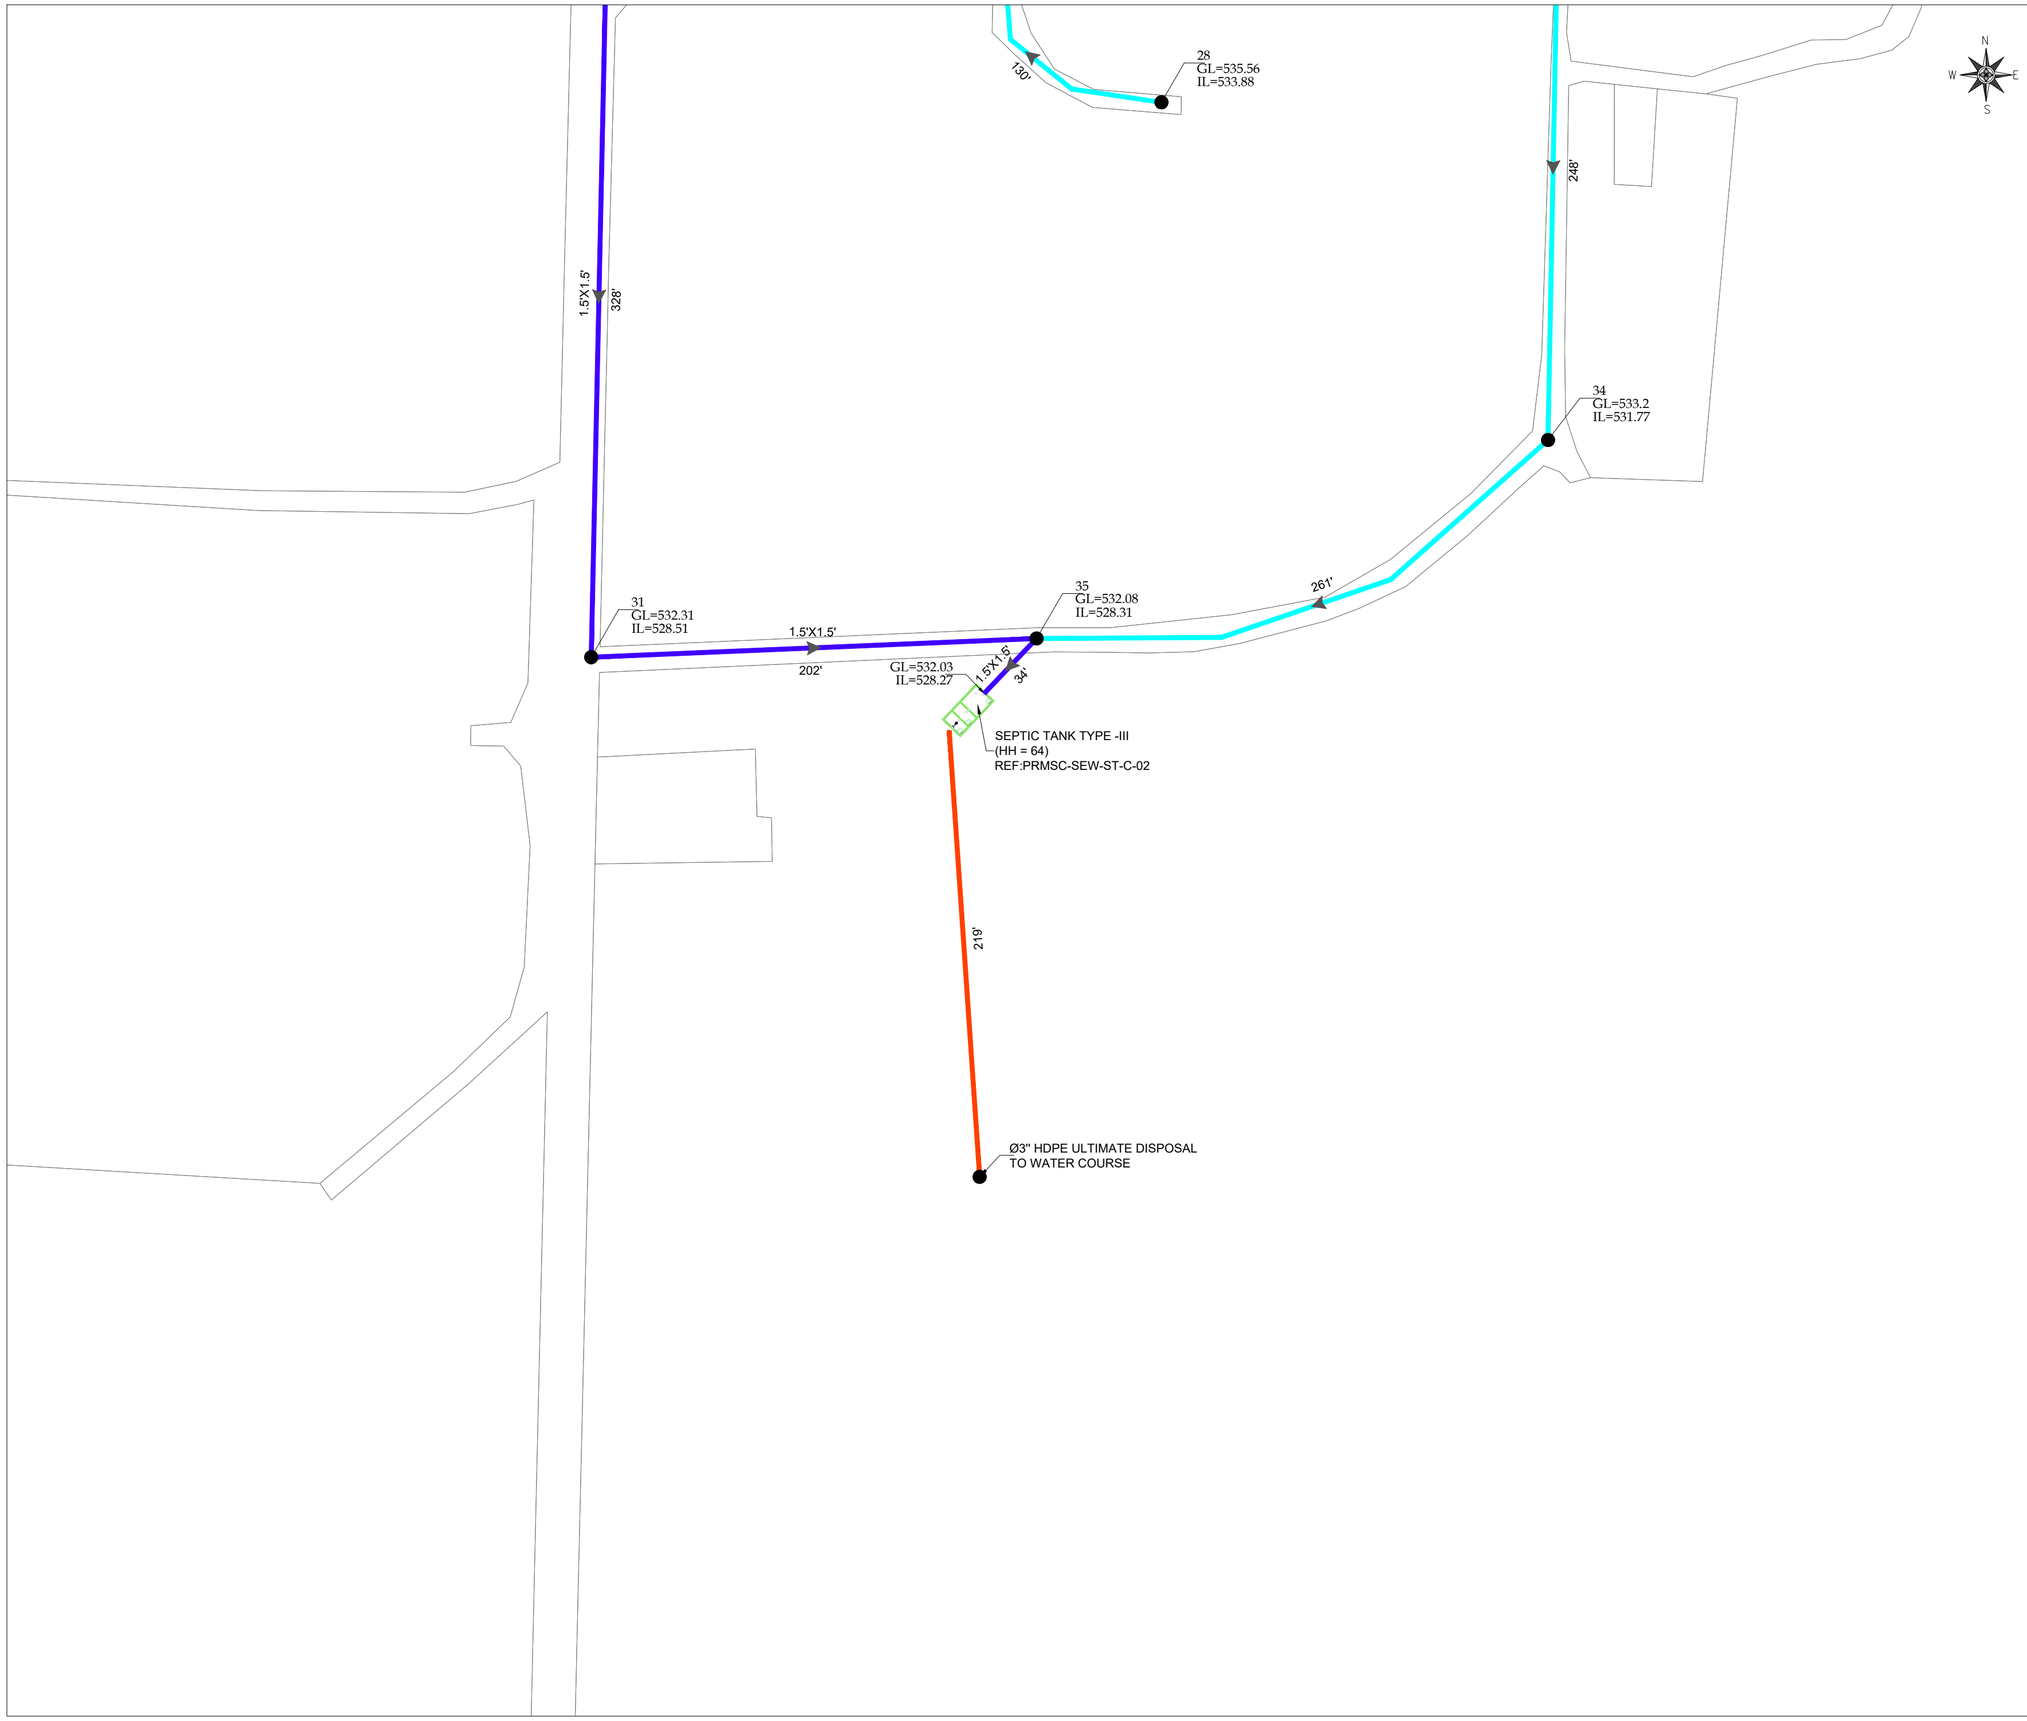



KEY PLAN

LEGEND:

- DRAIN TYPE - I
- SULLAGE CARRIER
- Ø3" HDPE PIPE
- BOUNDARY

VILLAGE: MOHSIN PUR (BWN)

TITLE.

DRAINAGE SYSTEM LAYOUT PLAN-03

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	07-01-2026	DETAILED DESIGN	HANNAN	ENGR FAIEZ	ENGR HSAN-UL-HAQ
02	20-04-2026	DETAILED DESIGN	MUNEEB	ENGR FAIEZ	ENGR HSAN-UL-HAQ
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-MHP-SEW-LP-03	03 OF 03	01

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:
ASIAN CONSULTING ENGINEERS
www.asianeon.com

PRMSC-BWN-MHP-SEW-LP-03

HYDRAULIC STATEMENT								
Node		Length	Slope	Elevation Ground	Elevation Ground	Elevation Invert	Elevation Invert	Depth
FROM	TO	ft	ft/ft	U/S	D/S	U/S	D/S	ft
1	2	101	0.001	531.17	532.59	530.34	530.24	0.83
2	3	265	0.001	532.59	532.74	530.24	529.98	2.35
3	5	174	0.001	532.74	532.5	529.98	529.8	2.76
4	5	284	0.002	533.72	532.5	532.23	531.66	1.49
5	7	152	0.001	532.5	532.19	529.8	529.65	2.7
6	7	249	0.002	533	532.19	531.85	531.35	1.15
7	10	84	0.001	532.19	531.51	529.65	529.57	2.54
8	9	52	0.001	531.89	531.98	531.05	531	0.84
9	10	120	0.002	531.98	531.51	530.92	530.68	1.06
10	16	156	0.001	531.51	532.33	529.57	529.41	1.94
11	13	118	0.002	534.38	532.63	532.03	531.8	2.35
12	13	78	0.002	534.94	532.63	531.96	531.8	2.98
13	15	13	0.001	532.63	532.63	531.8	531.79	0.83
14	15	103	0.001	532.3	532.63	531.47	531.37	0.83
15	16	243	0.001	532.63	532.33	531.37	531.13	1.26
16	26	224	0.001	532.33	532.64	529.41	529.18	2.92
17	18	90	0.001	532.97	533.61	532.14	532.05	0.83
18	19	119	0.001	533.61	533.46	532.05	531.93	1.56
19	21	114	0.001	533.46	533.55	531.93	531.81	1.53
20	21	98	0.001	533.12	533.55	532.28	532.18	0.84
21	23	233	0.002	533.55	532	531.63	531.16	1.92
22	23	113	0.002	532.76	532	531.39	531.16	1.37
23	25	22	0.001	532	532.06	531.16	531.14	0.84
24	25	163	0.002	533.25	532.06	531.55	531.22	1.7
25	26	209	0.001	532.06	532.64	531.14	530.93	0.92
26	30	349	0.001	532.64	532.72	529.18	528.84	3.46
27	29	154	0.002	535.86	534.45	533.92	533.62	1.94
28	29	130	0.002	535.56	534.45	533.88	533.62	1.68
29	30	195	0.002	534.45	532.72	532.27	531.88	2.18
30	31	328	0.001	532.72	532.31	528.84	528.51	3.88
31	35	202	0.001	532.31	532.08	528.51	528.31	3.8
32	33	75	0.002	535.74	534.97	534.29	534.14	1.45
33	34	248	0.002	534.97	533.2	532.86	532.37	2.11
34	35	261	0.002	533.2	532.08	531.77	531.25	1.43
35	ST Type-3 (HH = 64)	34	0.001	532.08	532.03	528.31	528.27	3.77

VILLAGE: MOHSIN PUR (BWN)

TITLE:

HYDRAULIC STATEMENT

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	07-01-2026	DETAILED DESIGN	HANNAN	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02	20-04-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
03					
04					
05					
06					
07					

DRAWING Nº: PRMSC-BWN-MHP-SEW-HS-01

SHEET 01 OF 01

REV 01

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT
ASIAN CONSULTING ENGINEERS
www.asiancon.com

PRMSC-BWN-MHP-SEW-HS-01

NOOR JAHANIAN

KEY PLAN

Revenue Village: Noor Jahanian Sheet-1

SEPTIC TANK-T1
Plot Size=1.59 Marla

GL= 535.01
IL=533.18

ND-8
GL=535.43
IL=533.36

41'
1.5'X1.5'

107'

3" HDPE PIPE ULTIMATE DISPOSAL TO WATER COURSE

15'

ND-7
GL=535.52
IL=533.67

274'

ND-6
GL=535.7
IL=534.21

228'

ND-5
GL=535.84
IL=534.66

264'

ND-1
GL=540.4
IL=539.57

134'

ND-2
GL=539.05
IL=538.22

195'

ND-3
GL=537.77
IL=536.93

253'

ND-4
GL=538
IL=535.17

N

District:	Bahawalnagar
Tehsil:	Bahawalnagar
Revenue Village:	Noor Jahanian

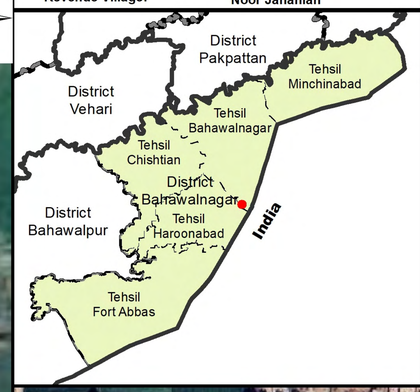

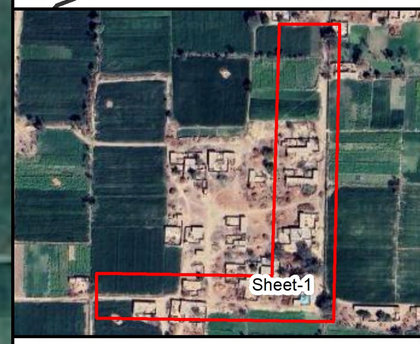

Title:
Proposed Drainage Network Plan

Legend:

- NODE
- 3" HDPE PIPE
- DRAIN TYPE-1
- SULLAGE CARRIER
- SEPTIC TANK
- SETTLEMENT BOUNDARY

Drain Type 1=1521 Rft
Sullage Carrier=41 Rft

Scale: 1:1,100
1 inch = 92 feet
Paper Size: A3

0 40 80 160
Kilometers

Project:
Engineering Design & Construction Supervision, Punjab Rural Sustainable Water Supply & Sanitation Project, Cluster South III

PRWSC
ENVIRONMENTAL TECHNOLOGIES
ASIAN CONSULTING ENGINEERS
www.asianconi.com

LEGEND:

- DRAIN TYPE-I
- SULLAGE CARRIER
- Ø3" HDPE PIPE
- BOUNDARY

VILLAGE: NOOR JAHANIAN (BWN)

TITLE.

DRAINAGE SYSTEM KEY PLAN

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 950'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	28-04-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. HSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING N°: PRMSC-BWN-NJH-SEW-KP-00

SHEET 00 OF 00

REV 00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT
ASIAN CONSULTING ENGINEERS
www.asiancon.com

PRMSC-BWN-NJH-SEW-KP-00

LAYOUT PLAN

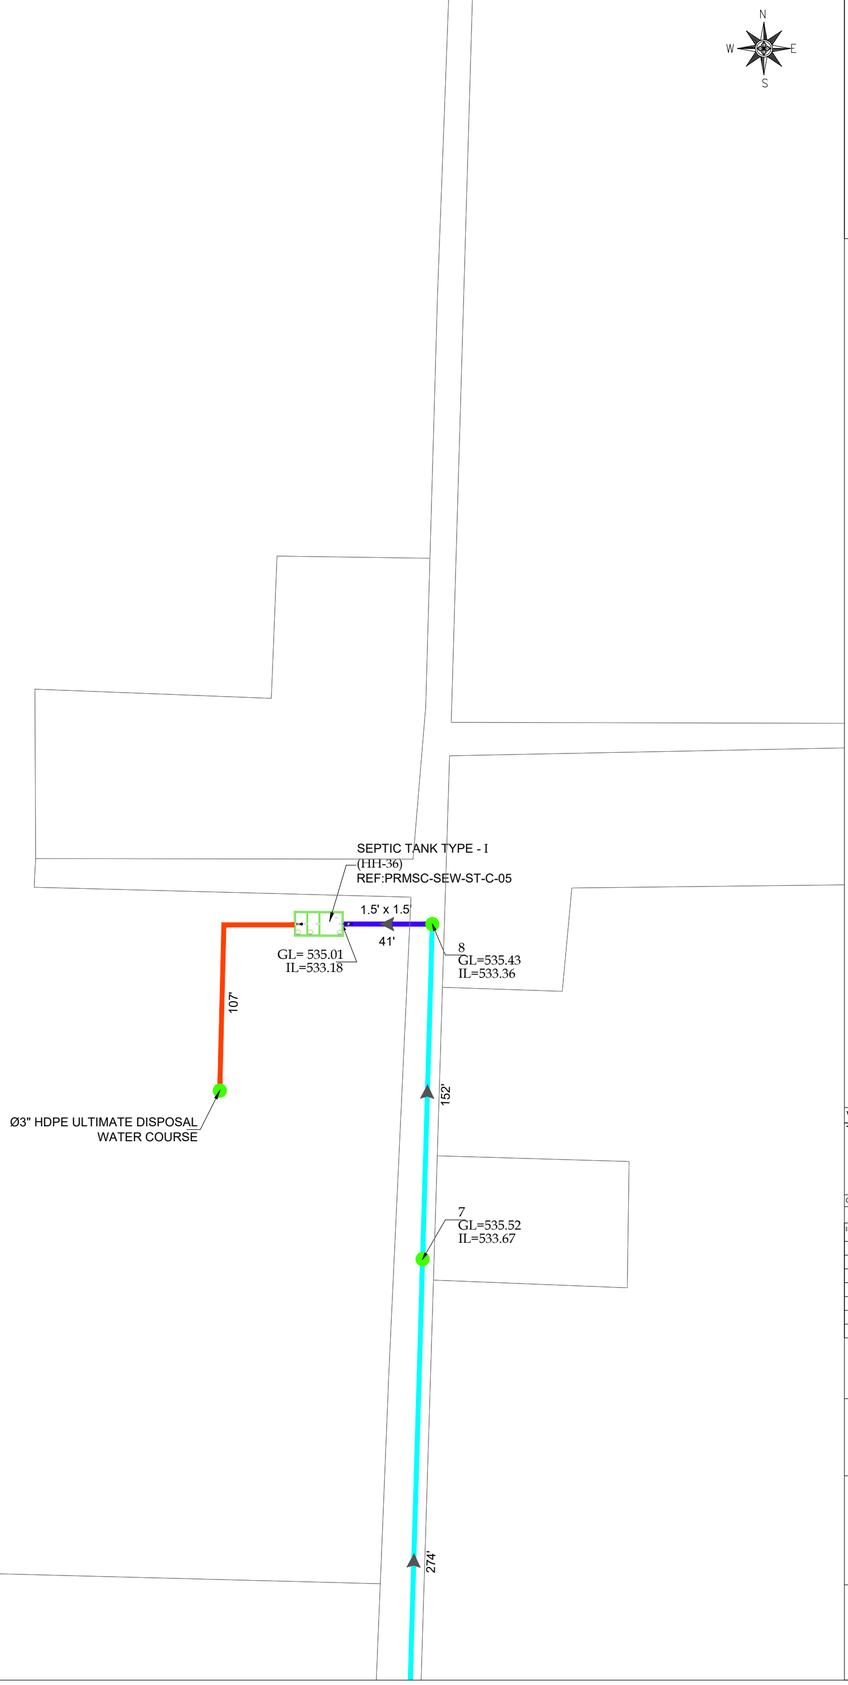

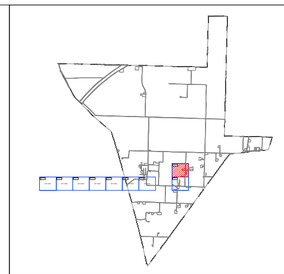

KEY PLAN

LEGEND:

- DRAIN TYPE-I
- SULLAGE CARRIER
- Ø3" HDPE PIPE
- BOUNDARY

VILLAGE: NOOR JAHANIAN(BWN)

TITLE.

DRAINAGE SYSTEM LAYOUT PLAN-08

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	28-04-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-NJH-SEW-LP-08	08 OF 09	01

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:
ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

PRMSC-BWN-NJH-SEW-LP-08

KEY PLAN

LEGEND:

- DRAIN TYPE-I
- SULLAGE CARRIER
- Ø3" HDPE PIPE
- BOUNDARY

VILLAGE: NOOR JAHANIAN(BWN)

TITLE.

DRAINAGE SYSTEM LAYOUT PLAN-09

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	28-04-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-NJH-SEW-LP-09	09 OF 09	01

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:
ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

PRMSC-BWN-NJH-SEW-LP-09

HYDRAULIC STATEMENT

Node		Length	Slope	Elevation Ground	Elevation Ground	Invert	Invert	Depth
FROM	TO	ft	ft/ft	U/S	D/S	U/S	D/S	ft
1	2	171	0.004	540.4	539.05	539.57	538.22	0.83
2	3	195	0.004	539.05	537.77	538.22	536.93	0.83
3	4	253	0.004	537.77	536	536.93	535.17	0.83
4	5	254	0.004	536	535.84	535.17	534.66	0.83
5	6	222	0.004	535.84	535.7	534.66	534.21	1.18
6	7	274	0.004	535.7	535.52	534.21	533.67	1.48
7	8	152	0.004	535.52	535.43	533.67	533.36	1.86
8	Septic Tank Type I	41	0.004	535.43	535.01	533.36	533.2	2.06

VILLAGE: NOOR JAHANIAN (BWN)

TITLE.

HYDRAULIC STATEMENT

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	28-04-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº: PRMSC-BWN-NJH-SEW-HS-01

SHEET 01 OF 01

REV 00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT
ASIAN CONSULTING ENGINEERS
www.asiancon.com

PRMSC-BWN-NJH-SEW-HS-00

PARAN WALA

KEY PLAN

Revenue Village: Paran Wala Sheet1

GL=478.00
IL=476.25

SEPTIC TANK-T2
Plot Size=2 Marla

N

District: Bahawalnagar
Tehsil: Bahawalnagar
Revenue Village: Paran Wala

Title:
Proposed Drainage Network Plan

Legend:

- NODE
- 3" HDPE PIPE
- DRAIN TYPE-1
- SULLAGE CARRIER
- SEPTIC TANK
- SETTLEMENT BOUNDARY

Drain Type 1=4235 Rft
Sullage Carrier=1874 Rft

Scale: 1:1,400
1 inch = 117 feet
Paper Size: A3

0 40 80 160
Kilometers

Project:
Engineering Design & Construction Supervision, Punjab Rural Sustainable Water Supply & Sanitation Project, Cluster South III

GL=480.80
IL=478.69
SEPTIC TANK-T2
Plot Size=2 Marla

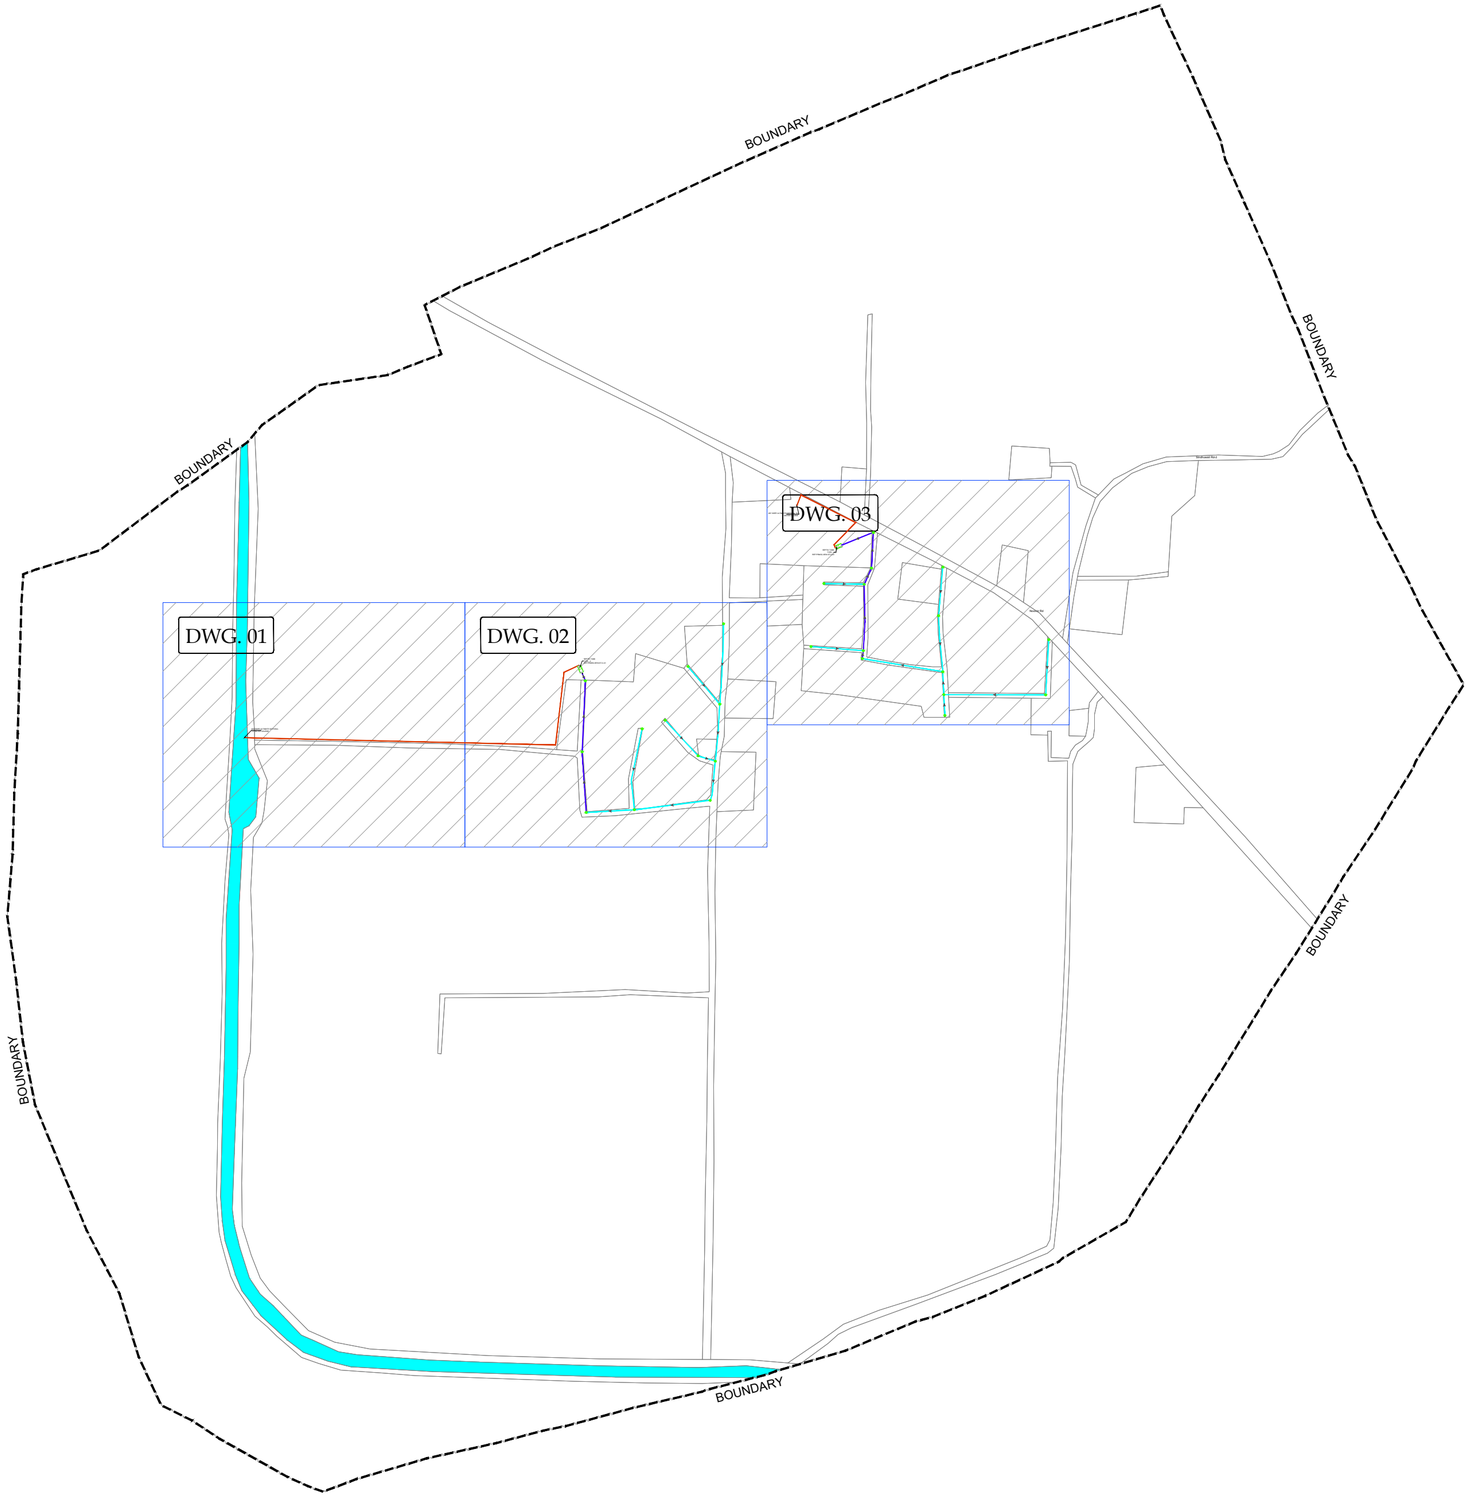

LEGEND:

- DRAIN TYPE - I
- SLUDGE CARRIER
- Ø3" HDPE PIPE
- BOUNDARY

VILLAGE: PARAN WALA (BWN)

TITLE.

DRAINAGE SYSTEM KEY PLAN

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 350'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	16-12-2025	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. HSANUL-HAQ
02	07-05-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. HSANUL-HAQ
03					
04					
05					
06					
07					

DRAWING Nº: PRMSC-BWN-PW-SEW-KP-00

SHEET 00 OF 00

REV 01

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT
ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

PRMSC-BWN-PW-SEW-KP-00

LAYOUT PLAN

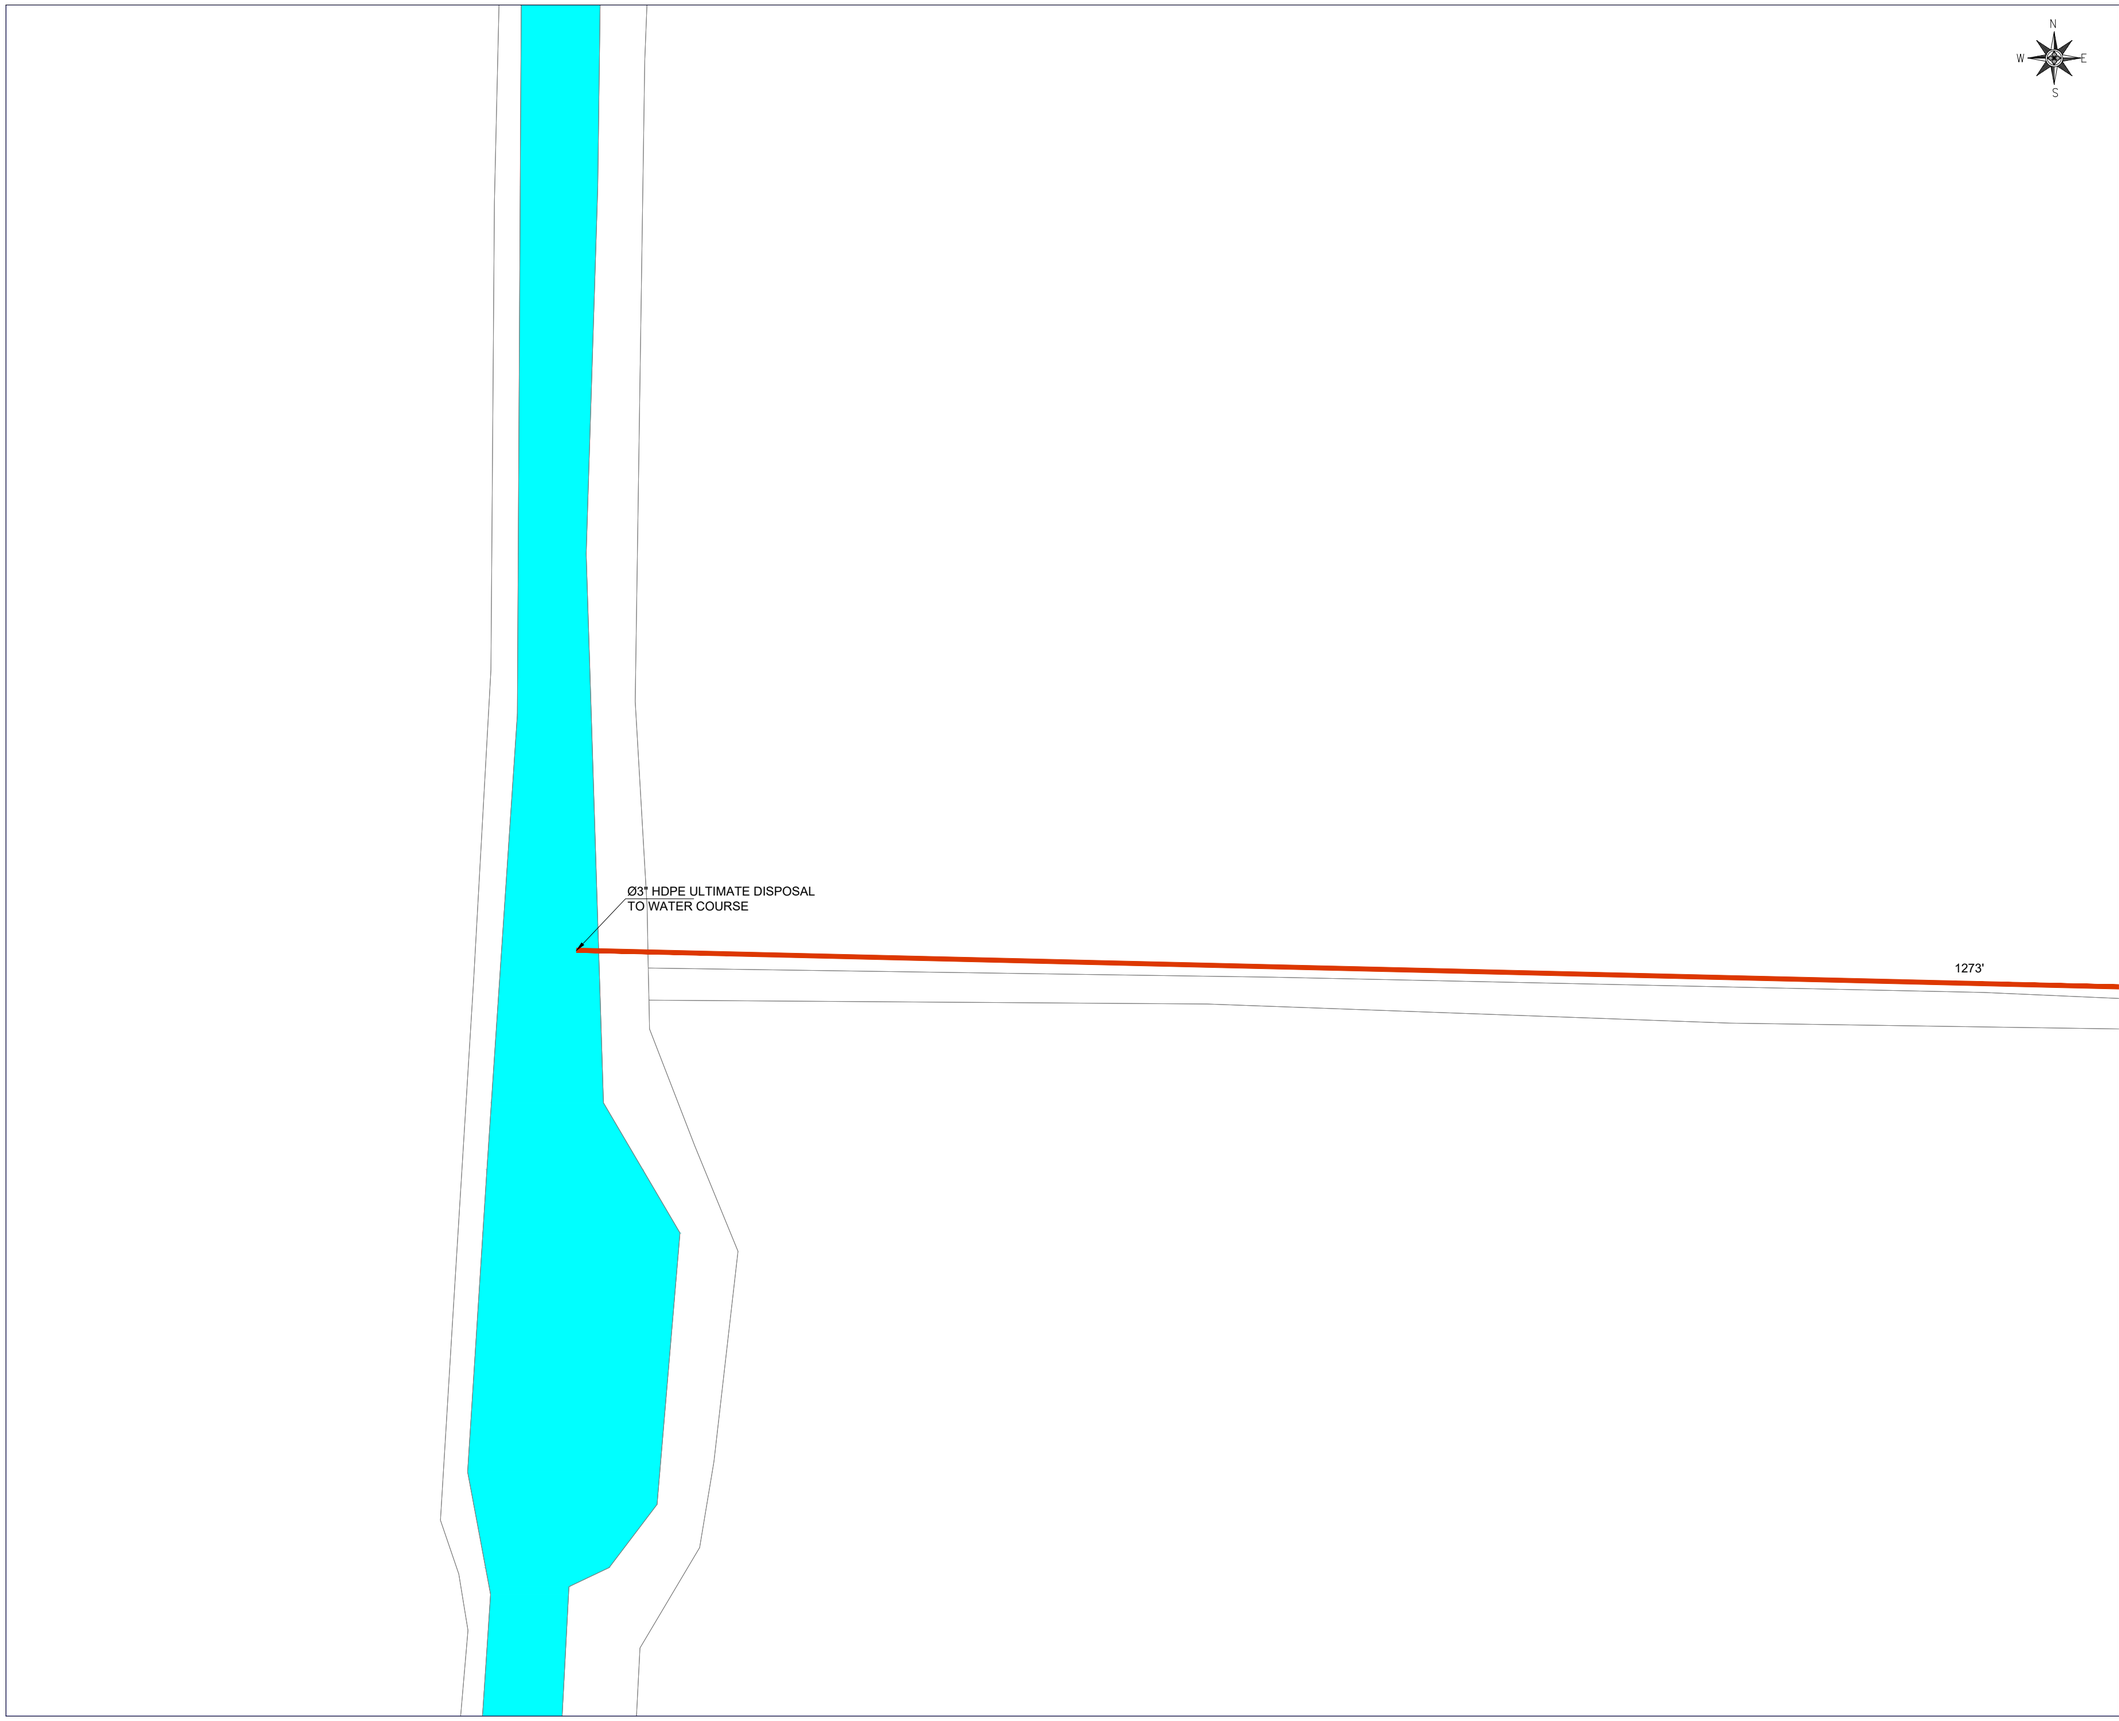

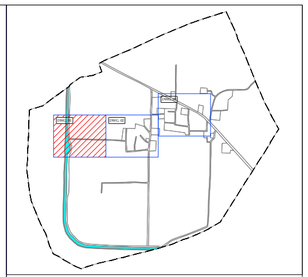

KEY PLAN

LEGEND:

- DRAIN TYPE - I
- SLUDGE CARRIER
- Ø3" HDPE PIPE
- BOUNDARY

VILLAGE: PARAN WALA (BWN)

TITLE.

DRAINAGE SYSTEM LAYOUT PLAN-01

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	D E S C R I P T I O N	DRAWN	DESIGNED	APPROVED
01	16-12-2025	DETAILED DESIGN	MUNEEB	ENGR FAIEZ	ENGR HSAN-UL-HAQ
02	07-05-2026	DETAILED DESIGN	MUNEEB	ENGR FAIEZ	ENGR HSAN-UL-HAQ
03					
04					
05					
06					
07					

DRAWING Nº: PRMSC-BWN-PW-SEW-LP-01

SHEET 01 OF 03

REV 00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:
ASIAN CONSULTING ENGINEERS
www.asianeon.com.pk

PRMSC-BWN-PW-SEW-LP-01

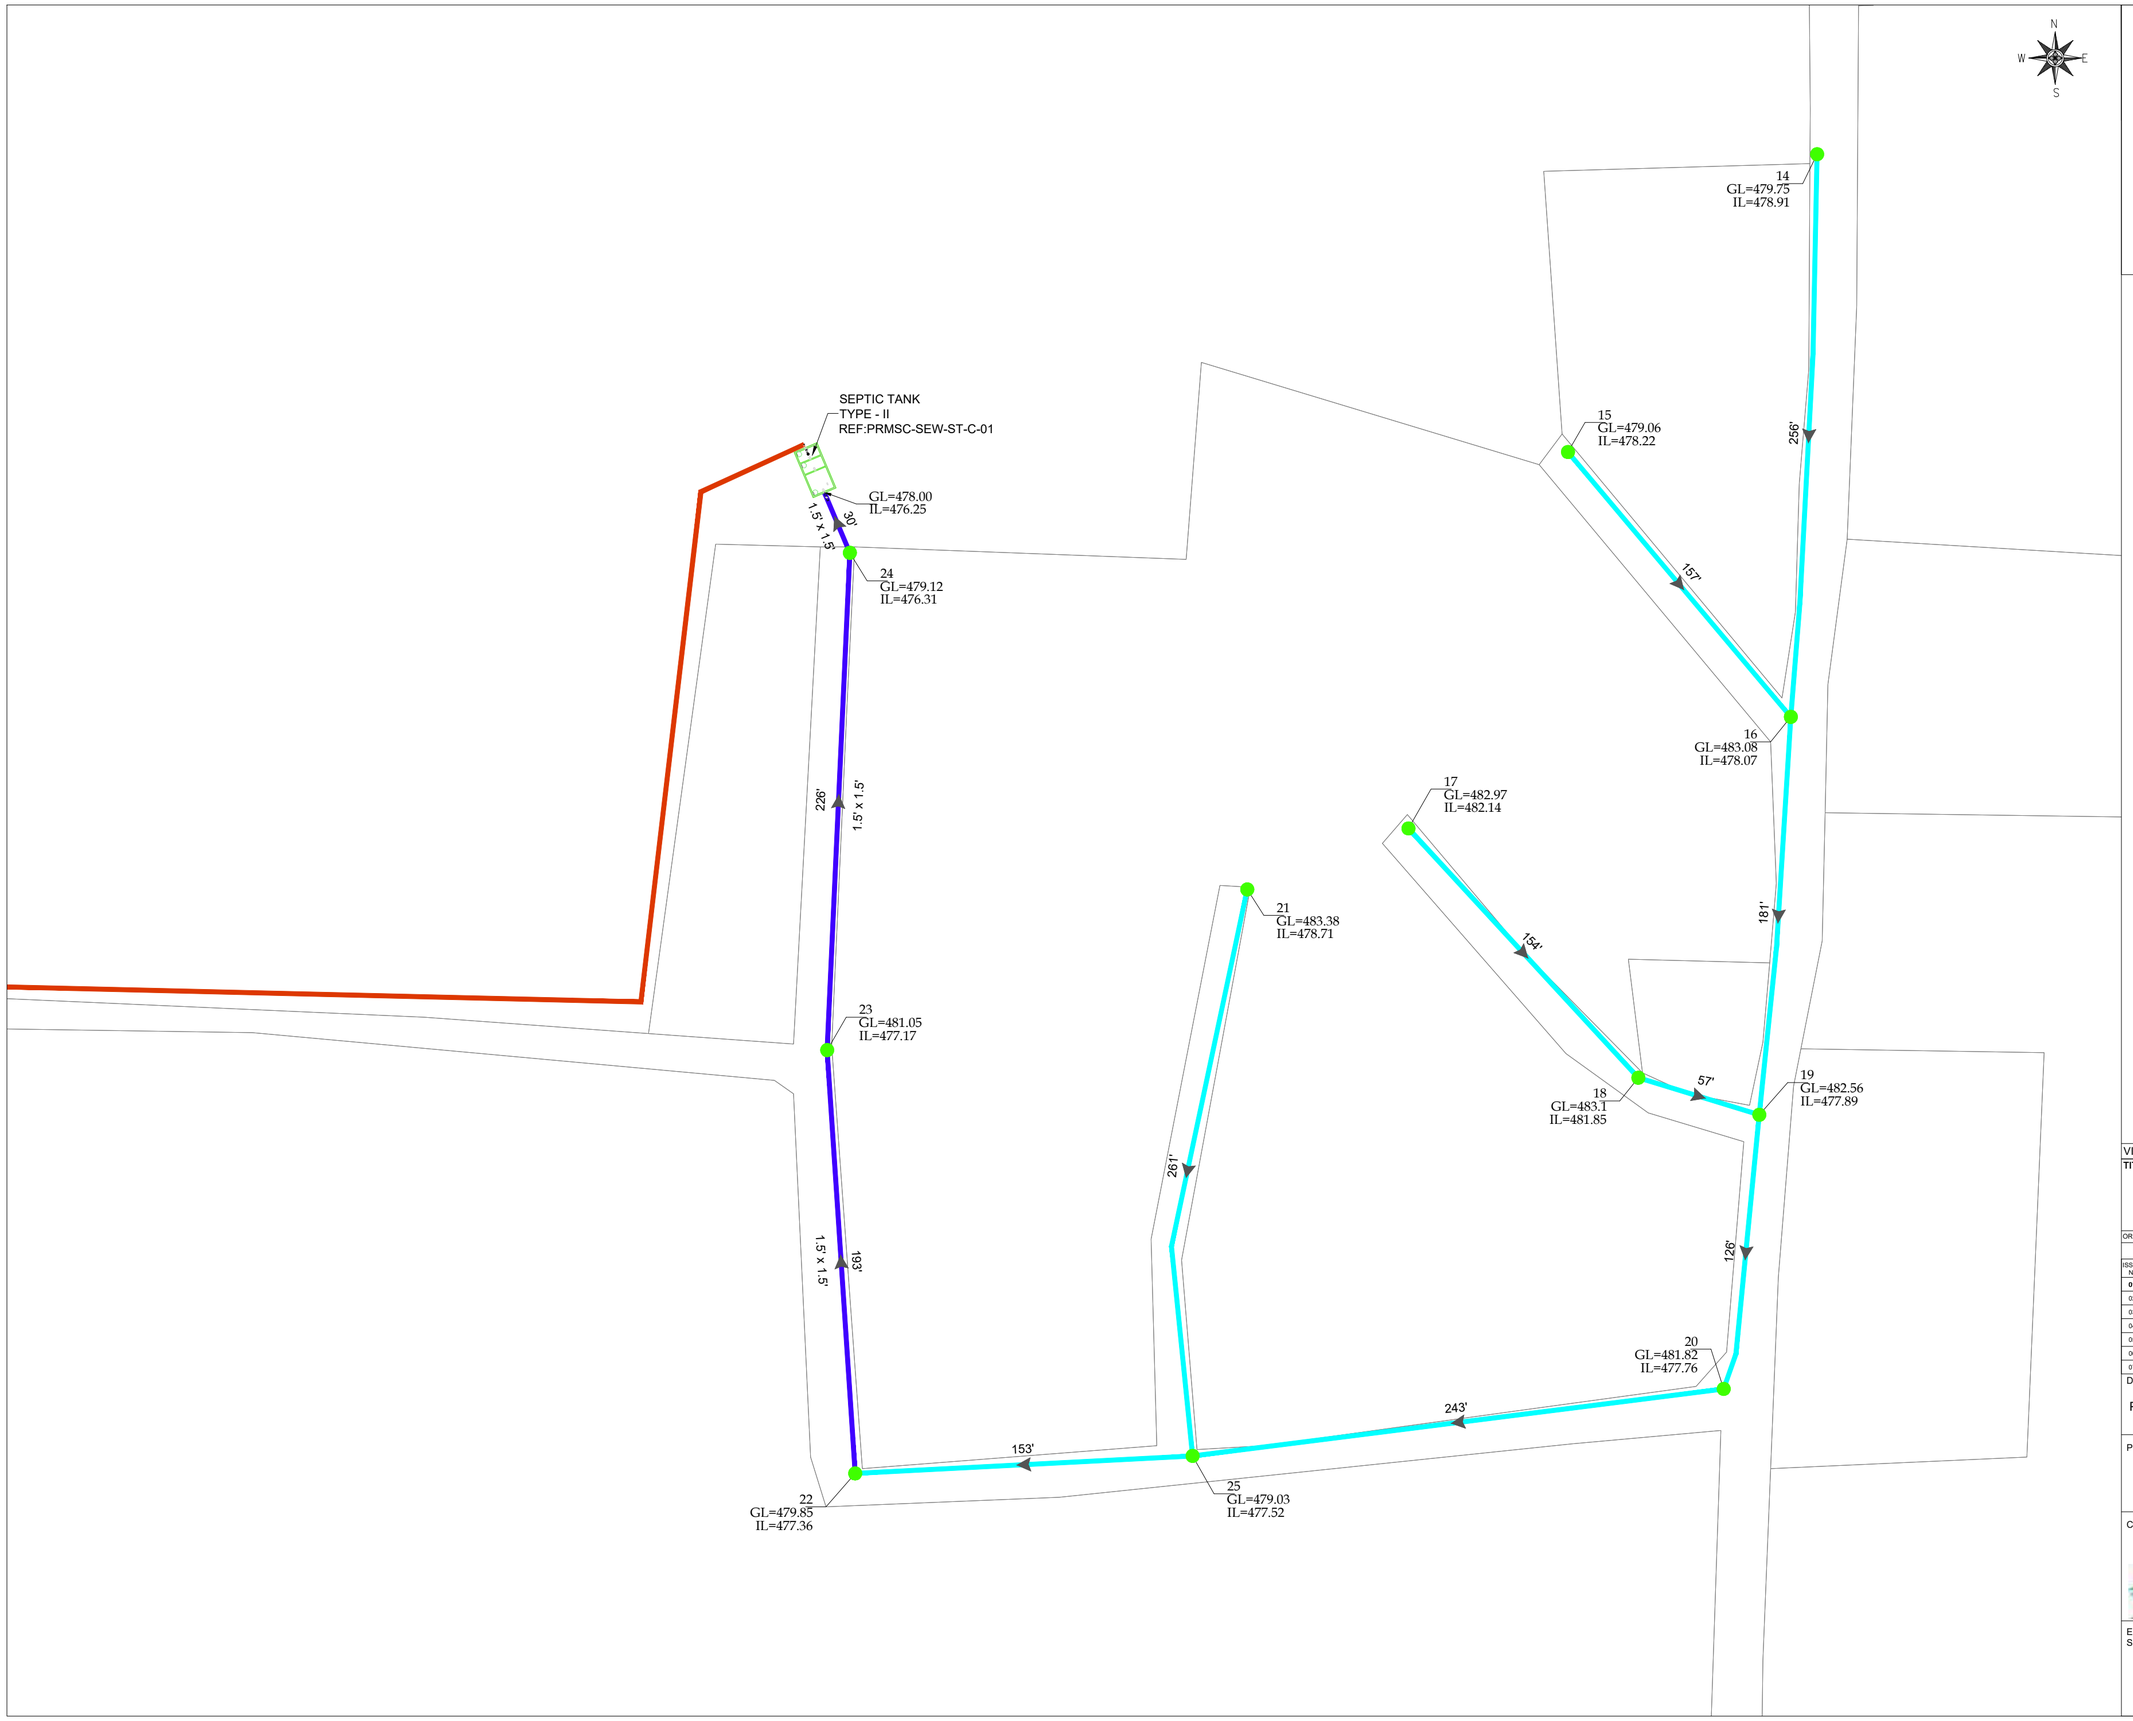

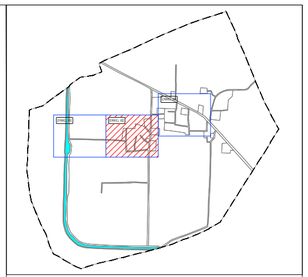

KEY PLAN

LEGEND:

- DRAIN TYPE - I
- SLUDGE CARRIER
- Ø3" HDPE PIPE
- BOUNDARY

VILLAGE: PARAN WALA (BWN)

TITLE.

DRAINAGE SYSTEM LAYOUT PLAN-02

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	16-12-2025	DETAILED DESIGN	MUNEEB	ENGR FAIEZ	ENGR IHSAN-UL-HAQ
02	07-05-2026	DETAILED DESIGN	MUNEEB	ENGR FAIEZ	ENGR IHSAN-UL-HAQ
03					
04					
05					
06					
07					

DRAWING Nº: PRMSC-BWN-PW-SEW-LP-02

SHEET 02 OF 03

REV 00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS
www.asianeng.com.pk

PRMSC-BWN-PW-SEW-LP-02

Ø3" HDPE ULTIMATE DISPOSAL TO WATER COURSE

341'

SEPTIC TANK
TYPE - II
REF:PRMSC-SEW-ST-C-01

GL=480.80
IL=478.69

108'
1.5' x 1.5'

13
GL=480.55
IL=478.8

114'
1.5' x 1.5'

12
GL=482.23
IL=479.03

57'
1.5' x 1.5'

11
GL=482.42
IL=481.59

128'

10
GL=482.61
IL=480.6

211'
1.5' x 1.5'

9
GL=482.05
IL=481.22

167'

8
GL=483.56
IL=481.05

25'
1.5' x 1.5'

7
GL=483.32
IL=481.27

259'

4
GL=482.89
IL=481.53

73'

3
GL=483.06
IL=481.87

66'

26
GL=482.77
IL=481.94

5
GL=485.54
IL=482.02

155'

6
GL=482.55
IL=481.71

179'

1
GL=483.8
IL=482.97

176'

2
GL=484.07
IL=482.79

323'

Noorsir Rd

N
W
E
S

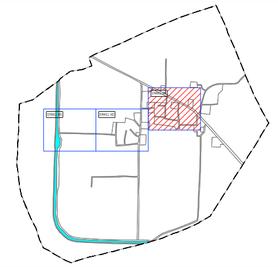

KEY PLAN

LEGEND:

- DRAIN TYPE - I
- SLUDGE CARRIER
- Ø3" HDPE PIPE
- BOUNDARY

VILLAGE: PARAN WALA (BWN)

TITLE.

DRAINAGE SYSTEM LAYOUT PLAN-03

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	16-12-2025	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02	07-05-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
03					
04					
05					
06					
07					

DRAWING Nº:

PRMSC-BWN-PW-SEW-LP-03

SHEET 03 OF 03

REV 00

PROJECT:

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:

PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

PRMSC-BWN-PW-SEW-LP-03

HYDRAULIC STATEMENT							
Node		Length	Slope	Elevation Ground	Elevation Ground	Elevation Invert	Elevation Invert
FROM	TO	ft	ft/ft	U/S	D/S	U/S	D/S
1	2	176	0.001	483.8	484.07	482.97	482.79
2	3	323	0.00175	484.07	483.06	482.79	482.23
26	3	66	0.001	482.77	483.06	481.87	481.94
3	4	73	0.001	483.06	482.89	481.8	481.87
5	6	155	0.002	485.54	482.55	482.02	481.71
6	4	179	0.001	482.55	482.89	481.71	481.53
4	7	259	0.001	482.89	483.32	481.27	481.53
7	8	25	0.001	483.32	483.56	481.25	481.27
9	8	167	0.001	482.05	483.56	481.22	481.05
8	10	211	0.001	483.56	482.61	480.84	481.05
11	10	128	0.001	482.42	482.61	481.59	481.46
10	12	57	0.002	482.61	482.23	480.48	480.6
12	13	114	0.002	482.23	480.55	478.8	479.03
13	ST 1-TYPE-II-NO SP	108	0.001	480.55	480.8	478.69	478.8
14	16	256	0.001	479.75	483.08	478.91	478.66
15	16	157	0.001	479.06	483.08	478.22	478.07
16	19	181	0.001	483.08	482.56	478.07	477.89
17	18	154	0.00192	482.97	483.1	482.14	481.85
18	19	57	0.002	483.1	482.56	481.85	481.73
19	20	126	0.001	482.56	481.82	477.89	477.76
20	25	243	0.001	481.82	479.03	477.76	477.52
21	25	261	0.002	483.38	479.03	478.71	478.19
25	22	153	0.001	479.03	479.85	477.36	477.52
22	23	193	0.001	479.85	481.05	477.17	477.36
23	24	226	0.001	481.05	479.12	476.94	477.17
24	ST 2-TYPE-II-NO SP	30	0.002	479.12	478	476.31	476.25

VILLAGE: PARAN WALA (BWN)

TITLE.

HYDRAULIC STATEMENT

ORIGINAL :		DATE :		SCALE :	
A2		JULY, 2025			
ISSUE N°	DATE	D E S C R I P T I O N	DRAWN	DESIGNED	APPROVED
01	16-12-2025	DETAILED DESIGN	MUNEEB	ENGR FAIEZ	ENGR HSAN-UL-HAQ
02	07-05-2026	DETAILED DESIGN	MUNEEB	ENGR FAIEZ	ENGR HSAN-UL-HAQ
03					
04					
05					
06					
07					

DRAWING Nº: PRMSC-BWN-PW-SEW-HS-01

SHEET 01 OF 01

REV 01

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT
ASIAN CONSULTING ENGINEERS
www.asianeng.com.pk

PRMSC-BWN-PW-SEW-HS-00

RAMNAGAR

KEY PLAN

Revenue Village: Ram Nagar Main Sheet

GL=578.12
IL=574.63

F.WRM PRE ULTIMATE DISPOSAL TO WATER COURSE

GL=576.20
IL=574.29

SEPTIC TANK-T1A
Plot Size=1.15 Marla

SEPTIC TANK-T1A
Plot Size=1.15 Marla

F.WRM PRE ULTIMATE DISPOSAL TO WATER COURSE

GL=577.24
IL=574.10

F.WRM PRE ULTIMATE DISPOSAL TO WATER COURSE

SEPTIC TANK-T1A
Plot Size=1.15 Marla

GL=573.66
IL=571.30

3" HDPE PIPE TIMATE DISPOSAL TO WATER COURSE

Chak Ramnagar

SEPTIC TANK-T3
Plot Size=2.62 Marla

Basti Hamdra

District:	Bahawalnagar
Tehsil:	Bahawalnagar
Revenue Village:	Ram Nagar

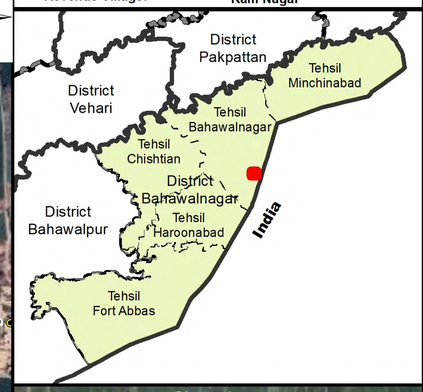

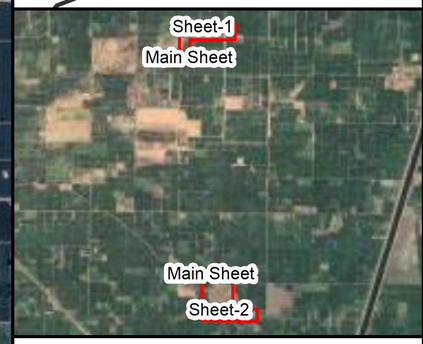

Title:
Proposed Drainage Network Plan

Legend:

- SETTLEMENT
- NODE
- 3" HDPE PIPE
- DRAIN TYPE-1
- SULLAGE CARRIER
- SEPTIC TANK
- SETTLEMENT BOUNDARY

Drain Type 1=8726 Rft
Sullage Carrier=1874 Rft

Scale: 1:9,100
1 inch = 758 feet
Paper Size: A3

0 40 80 160
Kilometers

Project:
Engineering Design & Construction Supervision, Punjab Rural Sustainable Water Supply & Sanitation Project, Cluster South III

PRMSC
ENVIRONMENTAL TECHNOLOGIES
ASIAN CONSULTING ENGINEERS www.asiancon.com

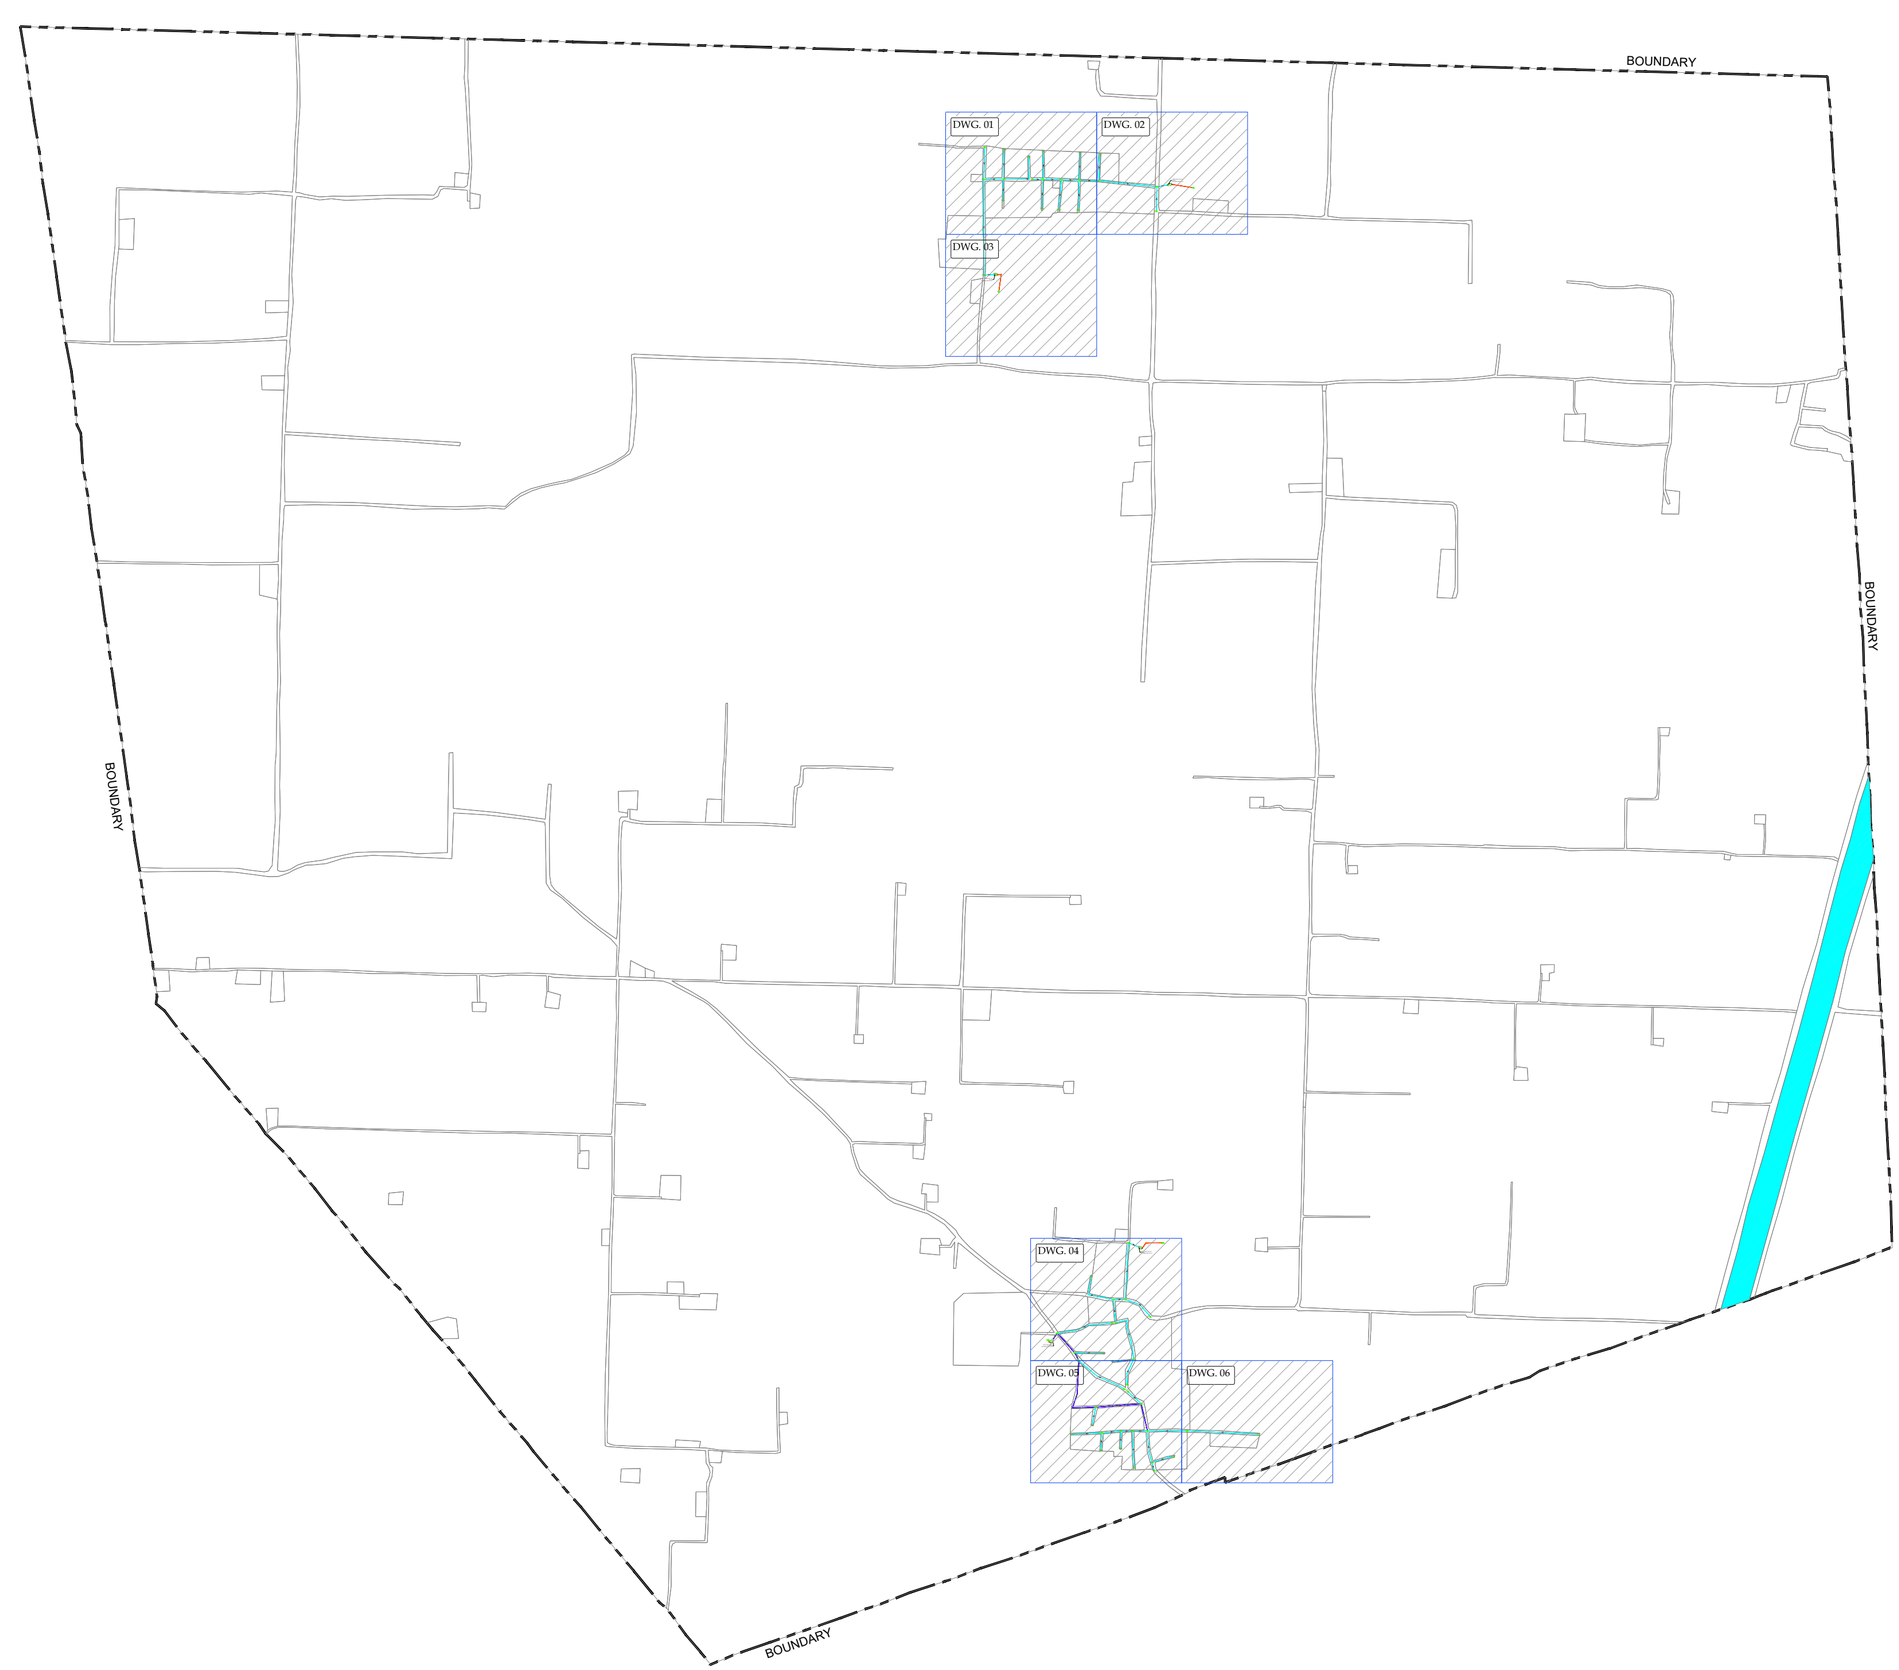

LEGEND:

- DRAIN TYPE - I
- SULLAGE CARRIER
- Ø3" HDPE PIPE
- BOUNDARY

VILLAGE: RAM NAGAR (BWN)

TITLE.

DRAINAGE SYSTEM KEY PLAN

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 700'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	24-12-2025	DETAILED DESIGN	HANNAN	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02	22-04-2026	DETAILED DESIGN	HANNAN	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-RMG-SEW-KP-00	00 OF 00	01

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT
ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

PRMSC-BWN-RMG-SEW-KP-00

LAYOUT PLAN

Revenue Village: Ram Nagar Sheet-1

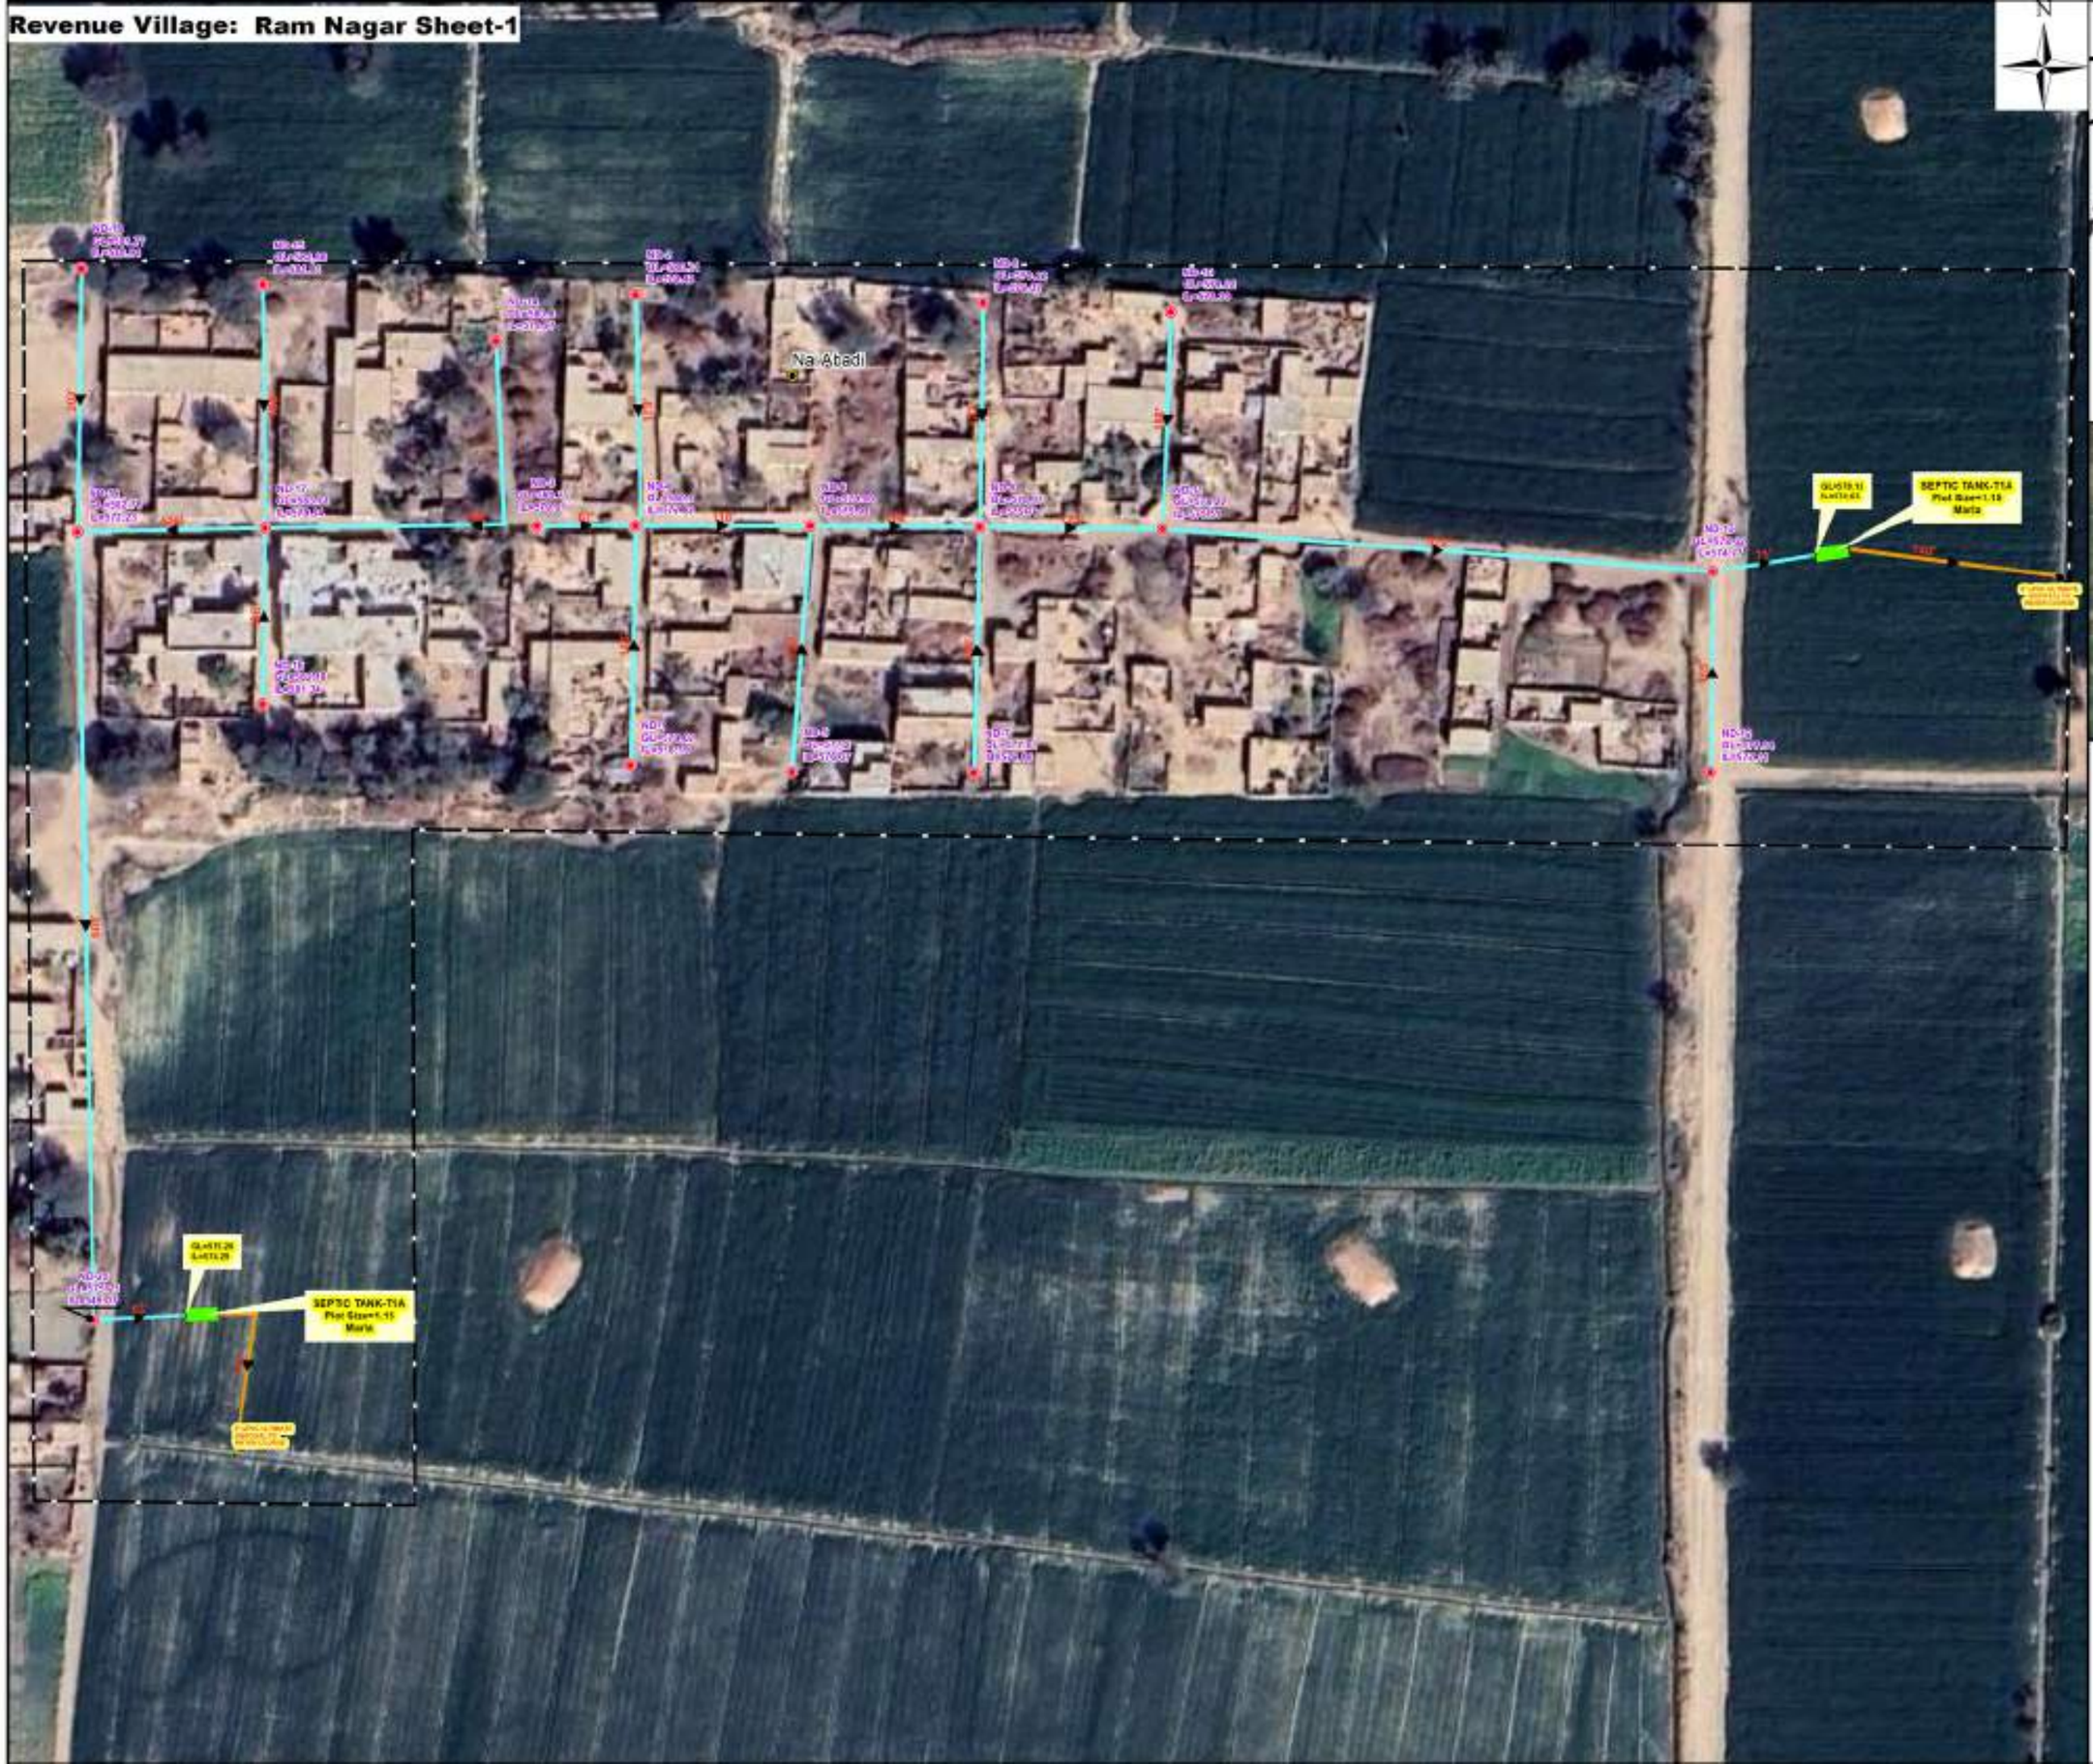

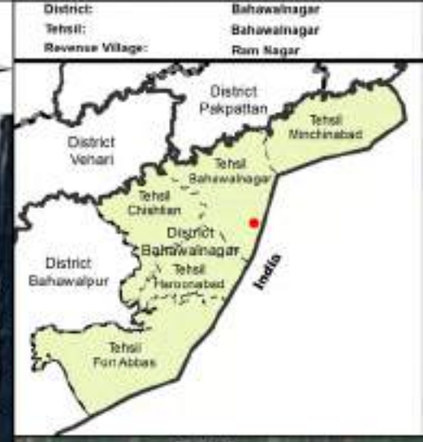

Title:
Proposed Drainage Network Plan

Legend:

- SETTLEMENT
- NODE
- 6" uPVC PIPE
- DRAIN TYPE-1
- SEPTIC TANK
- SETTLEMENT BOUNDARY

Drain Type 1=8726 Rft
Sullage Carrier=1874 Rft

Scale: 1:1,400
1 inch = 117 feet
Paper Size: A3

0 40 80 160
Kilometers

Project:
Engineering Design & Construction Supervision, Punjab Rural Sustainable Water Supply & Sanitation Project, Cluster South III

Revenue Village: Ram Nagar Sheet-2

District:	Bahawalnagar
Tehsil:	Bahawalnagar
Revenue Village:	Ram Nagar

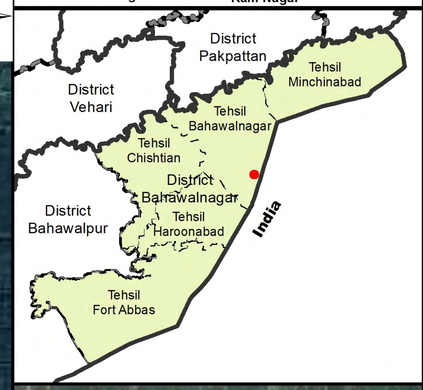

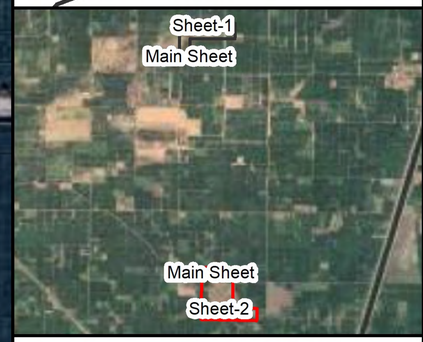

Title:
Proposed Drainage Network Plan

Legend:

- SETTLEMENT
- NODE
- 3" HDPE PIPE
- DRAIN TYPE-1
- SULLAGE CARRIER
- SEPTIC TANK
- SETTLEMENT BOUNDARY

Drain Type 1=8726 Rft
Sullage Carrier=1874 Rft

Scale: 1:1,600
1 inch = 133 feet
Paper Size: A3

0 40 80 160
Kilometers

Project:
Engineering Design & Construction Supervision, Punjab Rural Sustainable Water Supply & Sanitation Project, Cluster South III

PRWSC

ENVIRONMENTAL TECHNOLOGIES

ASIAN CONSULTING ENGINEERS www.asiancon.com

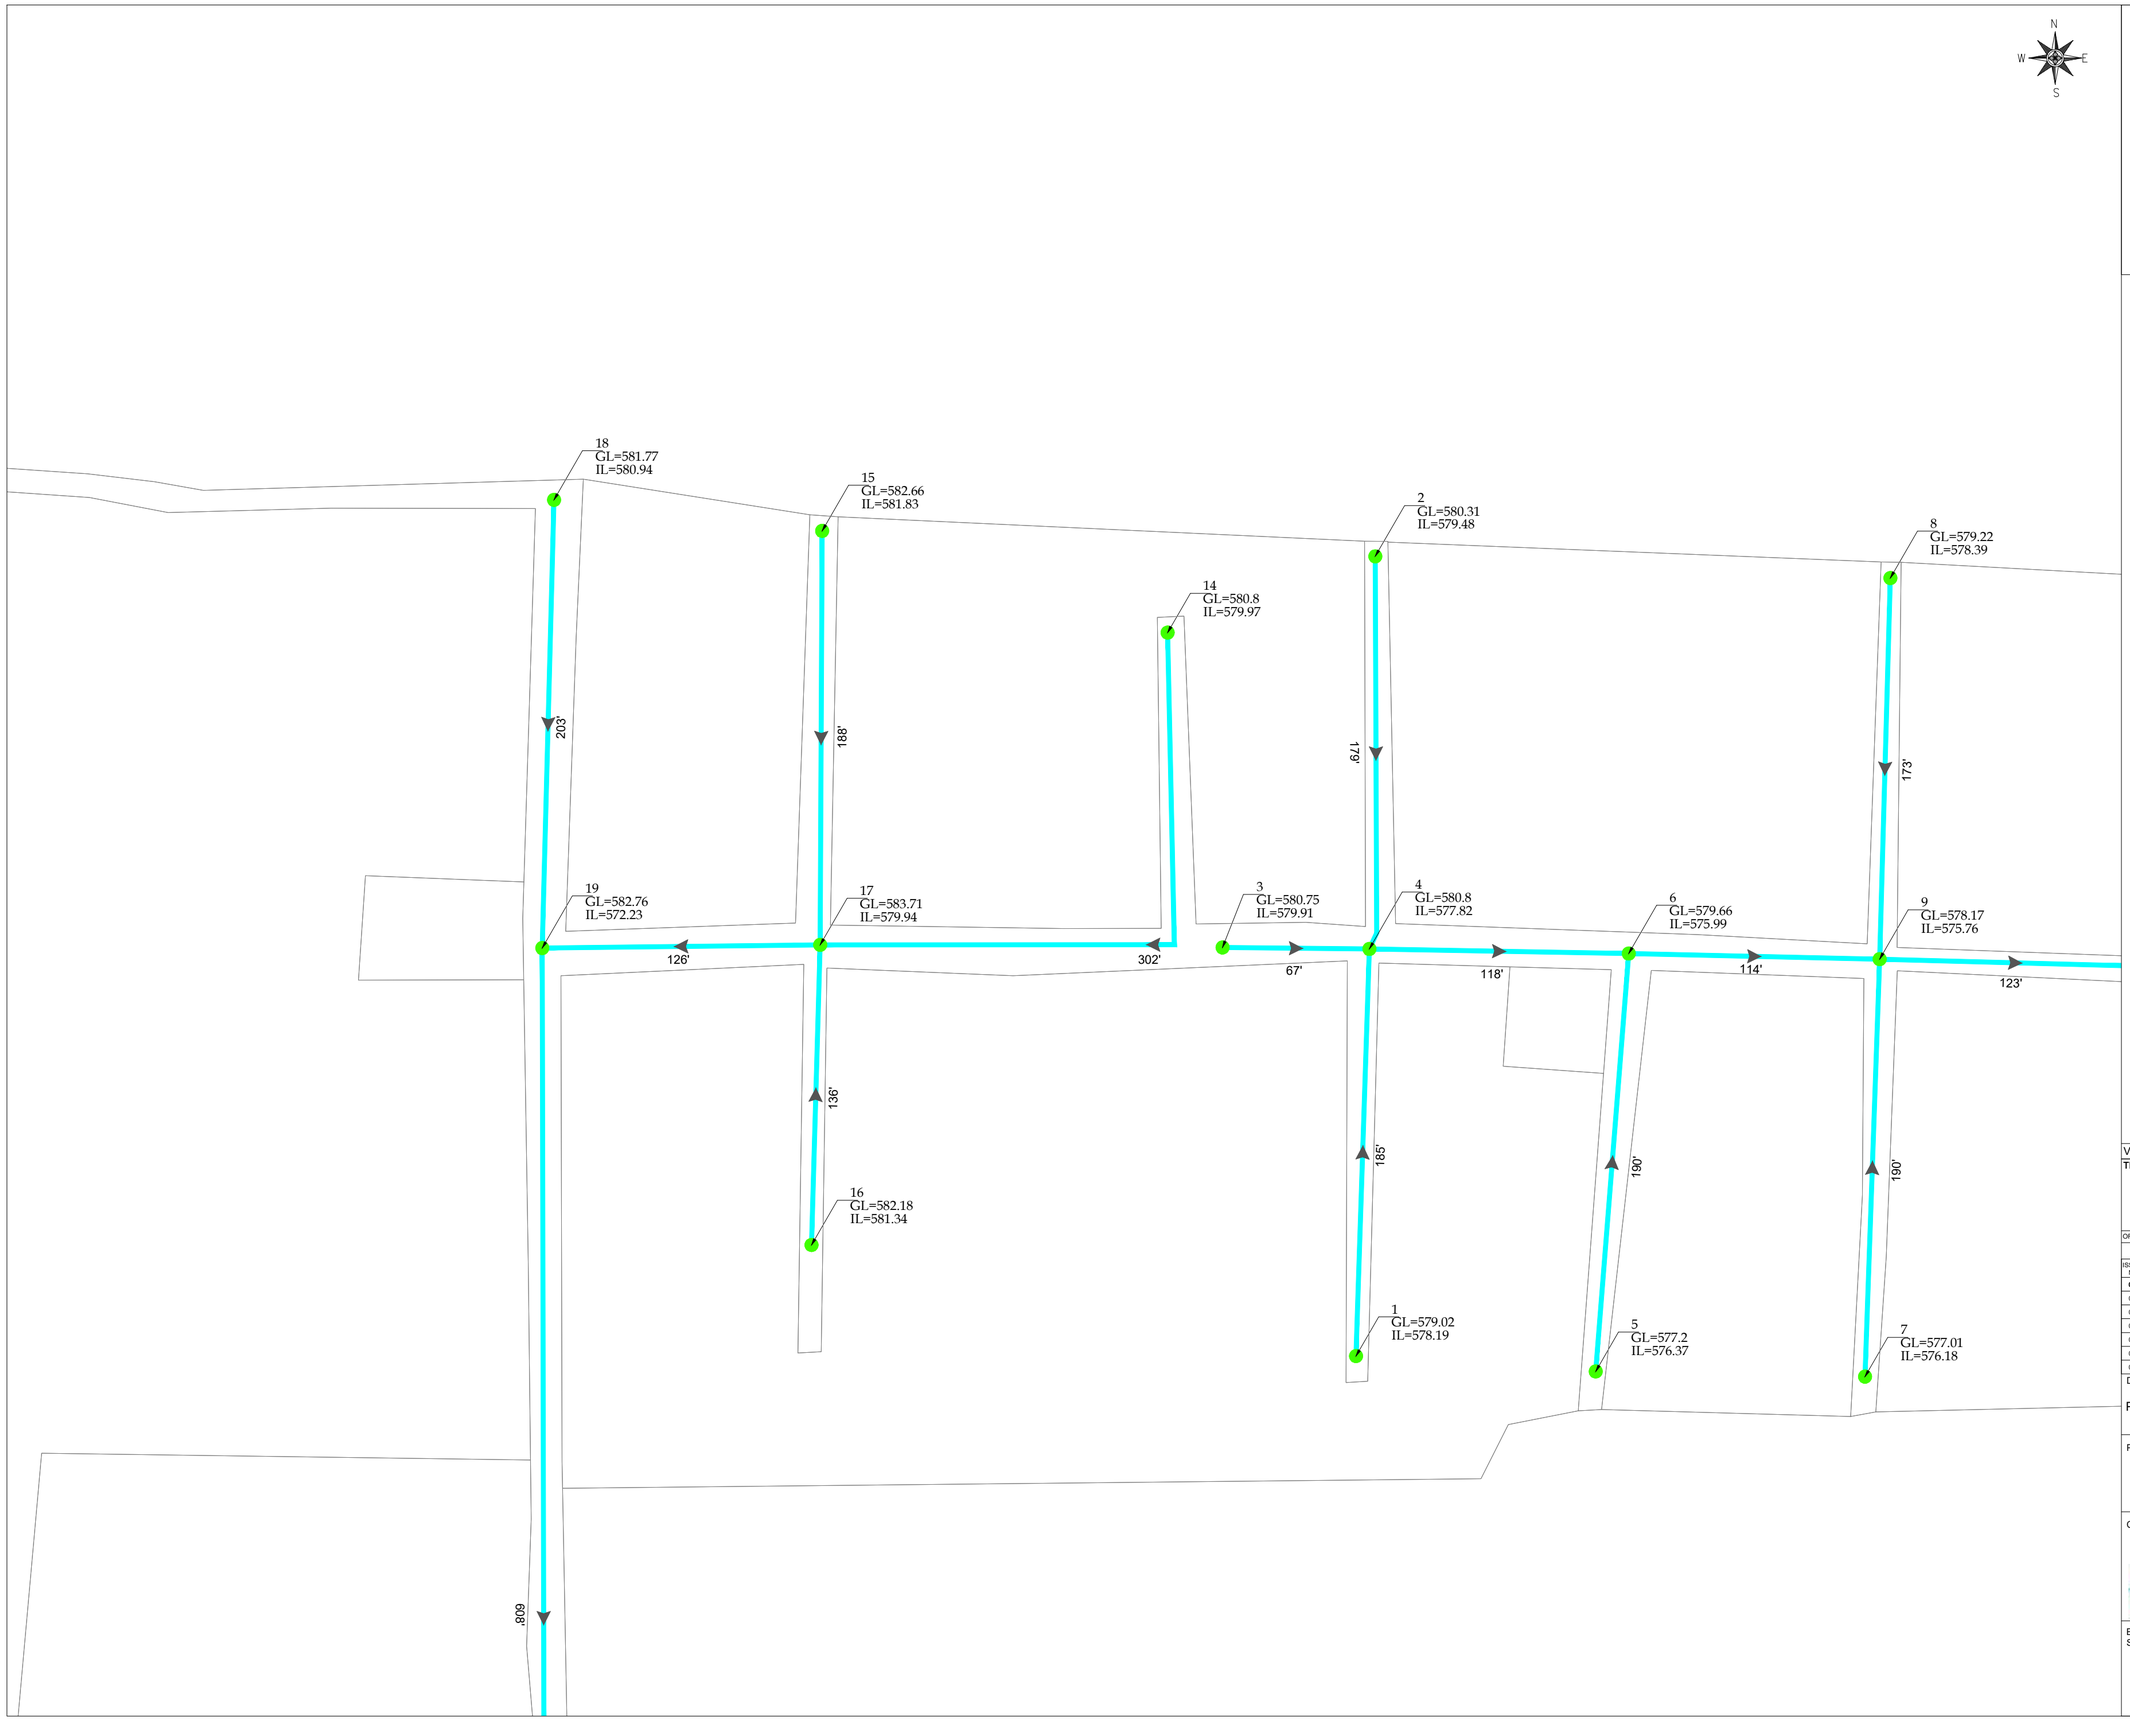

PRMSC-BWN-RMG-SEW-LP-01



KEY PLAN

LEGEND:

- DRAIN TYPE - I
- SULLAGE CARRIER
- Ø3" HDPE PIPE
- BOUNDARY

VILLAGE: RAM NAGAR (BWN)

TITLE.

DRAINAGE SYSTEM LAYOUT PLAN-01

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	24-12-2025	DETAILED DESIGN	HANNAN	ENGR FAIEZ	ENGR IHSAN-UL-HAQ
02	22-04-2026	DETAILED DESIGN	HANNAN	ENGR FAIEZ	ENGR IHSAN-UL-HAQ
03					
04					
05					
06					
07					

DRAWING N°: PRMSC-BWN-RMG-SEW-LP-01

SHEET 01 OF 06

REV 01

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

N
W
E
S



KEY PLAN

LEGEND:

- DRAIN TYPE - I
- SULLAGE CARRIER
- Ø3" HDPE PIPE
- BOUNDARY

VILLAGE: RAM NAGAR (BWN)

TITLE.

DRAINAGE SYSTEM LAYOUT PLAN-02

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	24-12-2025	DETAILED DESIGN	HANNAN	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02	22-04-2026	DETAILED DESIGN	HANNAN	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-RMG-SEW-LP-02	02 OF 06	01

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:
ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

PRMSC-BWN-RMG-SEW-LP-02

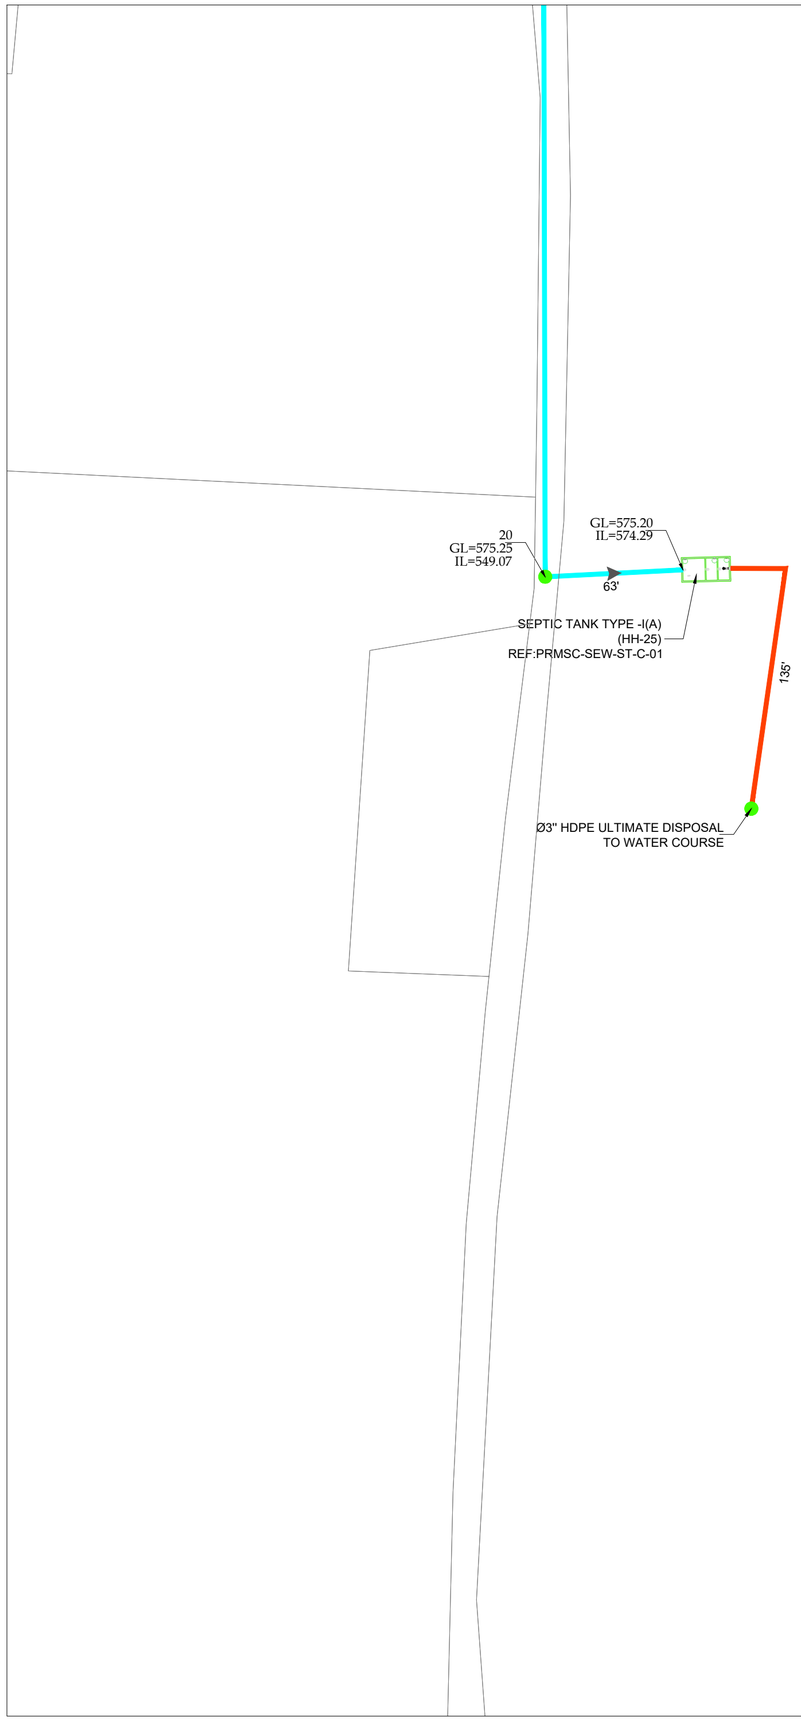



KEY PLAN

LEGEND:

- DRAIN TYPE - I
- SULLAGE CARRIER
- Ø3" HDPE PIPE
- BOUNDARY

VILLAGE: RAM NAGAR (BWN)

TITLE.

DRAINAGE SYSTEM LAYOUT PLAN-03

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	24-12-2025	DETAILED DESIGN	HANNAN	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02	22-04-2026	DETAILED DESIGN	HANNAN	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-RMG-SEW-LP-03	03 OF 06	01

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:
ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

PRMSC-BWN-RMG-SEW-LP-03

N
W E
S

29
GL=575.35
IL=565.35

GL=577.24
IL=574.10

71'

150'

Ø3" HDPE ULTIMATE DISPOSAL
TO WATER COURSE

SEPTIC TANK TYPE -I(A)
(HH-25)
REF:PRMSC-SEW-ST-C-01

361'

25
GL=576.1
IL=575.26

281'

26
GL=578.64
IL=566.23

28
GL=578.45
IL=566.07

76'

200'

148'

27
GL=576.2
IL=575.36

51
GL=580.71
IL=579.88

24
GL=579.37
IL=575.26

357'

52
GL=574.15
IL=571.35

324'

GL=573.65
IL=571.30

1.5X1.5'

50'

Ø3" HDPE ULTIMATE DISPOSAL
TO WATER COURSE

22'

SEPTIC TANK TYPE -III
(HH-72)
REF:PRMSC-SEW-ST-C-02

1.5X1.5'

164'

50
GL=575.18
IL=571.94

49
GL=577.79
IL=576.95

183'

1.5X1.5'

57'

23
GL=576.74
IL=575.91

PRMSC-BWN-RMG-SEW-LP-04



KEY PLAN

LEGEND:

- DRAIN TYPE - I
- SULLAGE CARRIER
- Ø3" HDPE PIPE
- BOUNDARY

VILLAGE: RAM NAGAR (BWN)

TITLE.

DRAINAGE SYSTEM LAYOUT PLAN-04

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	24-12-2025	DETAILED DESIGN	HANNAN	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02	22-04-2026	DETAILED DESIGN	HANNAN	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-RMG-SEW-LP-04	04 OF 06	01

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

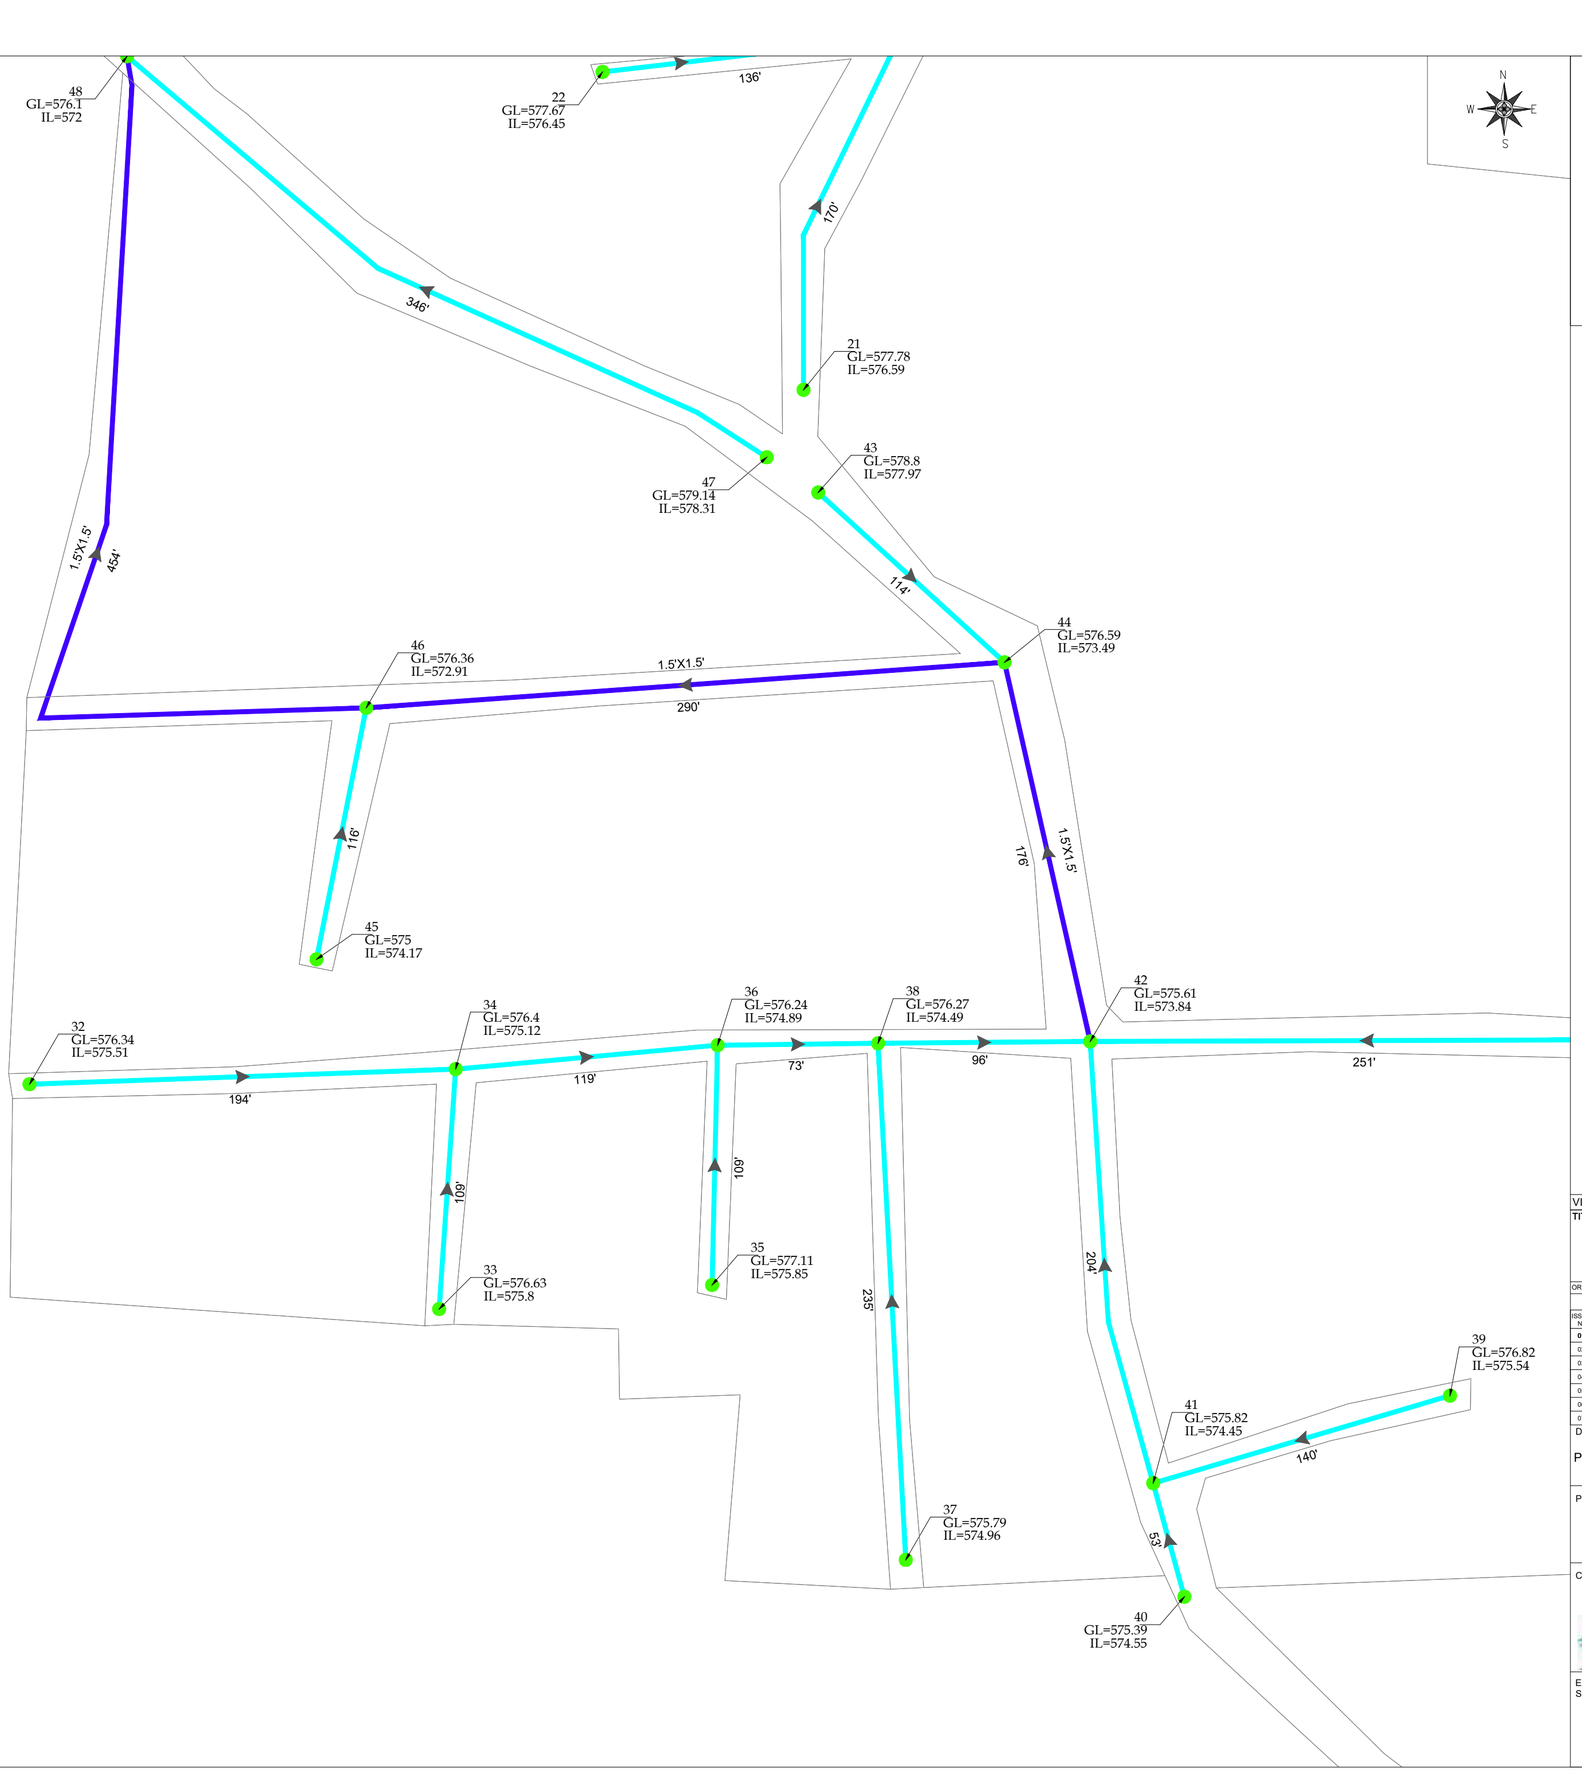

N
W
E
S

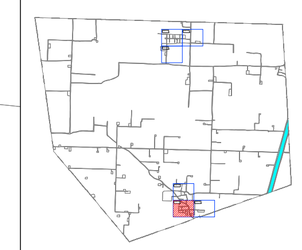

KEY PLAN

LEGEND:

- DRAIN TYPE - I
- SULLAGE CARRIER
- Ø3" HDPE PIPE
- BOUNDARY

VILLAGE: RAM NAGAR (BWN)

TITLE.

DRAINAGE SYSTEM LAYOUT PLAN-05

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	24-12-2025	DETAILED DESIGN	HANNAN	ENGR FAIEZ	ENGR IHSAN-UL-HAQ
02	22-04-2026	DETAILED DESIGN	HANNAN	ENGR FAIEZ	ENGR IHSAN-UL-HAQ
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-RMG-SEW-LP-05	05 OF 06	01

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:
ASIAN CONSULTING ENGINEERS
www.asiancon.com

PRMSC-BWN-RMG-SEW-LP-05

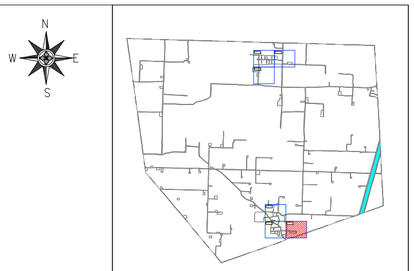

KEY PLAN

LEGEND:

DRAIN TYPE - I

SULLAGE CARRIER

Ø3" HDPE PIPE

BOUNDARY

30
GL=576.12
IL=575.29

452'

31
GL=575.18
IL=574.35

BOUNDARY

BOUNDARY

PRMSC-BWN-RMG-SEW-LP-06

VILLAGE: RAM NAGAR (BWN)

TITLE.

DRAINAGE SYSTEM LAYOUT PLAN-06

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	24-12-2025	DETAILED DESIGN	HANNAN	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02	22-04-2026	DETAILED DESIGN	HANNAN	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-RMG-SEW-LP-06	06 OF 06	01

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS
www.asiacon.com.pk

HYDRAULIC STATEMENT

Node		Length	Slope	Elevation Ground	Elevation Ground	Invert	Invert	Depth
FROM	TO	ft	ft/ft	U/S	D/S	U/S	D/S	ft
1	4	185	0.002	579.02	580.8	578.19	577.82	0.83
2	4	179	0.002	580.31	580.8	579.48	579.12	0.83
4	3	67	0.002	580.8	580.75	579.78	579.91	0.83
6	4	118	0.002	579.66	580.8	577.58	577.82	2.98
5	6	190	0.002	577.2	579.66	576.37	575.99	0.83
9	6	114	0.002	578.17	579.66	575.76	575.99	3.68
7	9	190	0.002	577.01	578.17	576.18	575.76	0.83
8	9	173	0.015	579.22	578.17	578.39	575.76	0.83
11	9	123	0.002	578.22	578.17	575.51	575.76	2.41
10	11	168	0.017	579.22	578.22	578.39	575.51	0.83
13	11	372	0.002	578.32	578.22	574.77	575.51	2.71
12	13	155	0.002	577.94	578.32	577.11	576.8	0.83
13	ST Type-1A (HH=25)	71	0.002	578.32	578.12	574.77	574.63	3.55
14	17	302	0.000	580.8	583.71	579.97	579.94	0.83
15	17	188	0.002	582.66	583.71	581.83	581.45	0.83
16	17	136	0.002	582.18	583.71	581.34	581.07	0.83
17	19	126	0.06112	583.71	582.76	579.94	572.23	3.77
18	19	203	0.002	581.77	582.76	580.94	580.53	0.83
19	20	608	0.03808	582.76	575.25	572.23	549.07	10.53
20	ST Typpe-1A (HH=25)	63	0.002	575.25	575.2	549.07	548.94	26.18
21	23	170	0.004	577.78	576.74	576.59	575.91	1.19
22	23	136	0.004	577.67	576.74	576.45	575.91	1.22
23	24	324	0.002	576.74	579.37	575.91	575.26	0.83
24	26	148	0.06112	579.37	578.64	575.26	566.23	4.11
25	26	281	0.03216	576.1	578.64	575.26	566.23	0.83
26	28	76	0.002	578.64	578.45	566.23	566.07	12.41
27	28	200	0.002	576.2	578.45	575.36	574.96	0.83
28	29	361	0.002	578.45	575.35	566.07	565.35	12.38
29	ST Typpe-1A (HH=25)	71	0.002	575.35	577.24	565.35	565.21	10
30	31	452	0.00208	576.12	575.18	575.29	574.35	0.83
31	42	251	0.002	575.18	575.61	574.35	573.84	0.83
32	34	194	0.002	576.34	576.4	575.51	575.12	0.83
33	34	109	0.00216	576.63	576.4	575.8	575.56	0.83
34	36	119	0.002	576.4	576.24	575.12	574.89	1.27
35	36	109	0.004	577.11	576.24	575.85	575.41	1.26
36	38	73	0.002	576.24	576.27	574.89	574.74	1.36
37	38	235	0.002	575.79	576.27	574.96	574.49	0.83
38	42	96	0.002	576.27	575.61	574.49	574.3	1.78
39	41	140	0.004	576.82	575.82	575.54	574.98	1.27
40	41	53	0.002	575.39	575.82	574.55	574.45	0.83
41	42	204	0.00297	575.82	575.61	574.45	573.84	1.37
42	44	176	0.002	575.61	576.59	573.84	573.49	1.76
43	44	114	0.03912	578.8	576.59	577.97	573.49	0.83
44	46	290	0.002	576.59	576.36	573.49	572.91	3.1
45	46	116	0.002	575	576.36	574.17	573.94	0.83
46	48	454	0.002	576.36	576.1	572.91	572	3.45
47	48	346	0.01825	579.14	576.1	578.31	572	0.83
48	50	57	0.00109	576.1	575.18	572	571.94	4.1
49	50	183	0.02734	577.79	575.18	576.95	571.94	0.83
50	52	164	0.00358	575.18	574.15	571.94	571.35	3.24
51	52	357	0.02389	580.71	574.15	579.88	571.35	0.83
52	ST Typpe-3 (HH=72)	50	0.00328	574.15	573.65	571.35	571.19	2.8

VILLAGE: RAM NAGAR (BWN)

TITLE.

HYDRAULIC STATEMENT

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	24-12-2025	DETAILED DESIGN	HANNAN	ENGR FAIEZ	ENGR IHSAN-UL-HAQ
02	22-04-2026	DETAILED DESIGN	HANNAN	ENGR FAIEZ	ENGR IHSAN-UL-HAQ
03					
04					
05					
06					
07					

DRAWING Nº: PRMSC-BWN-RMG-SEW-HS-01

SHEET 01 OF 01

REV 01

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT
ASIAN CONSULTING ENGINEERS
www.asiancon.com

PRMSC-BWN-RMG-SEW-HS-01

SANDAR BASHNOI

KEY PLAN

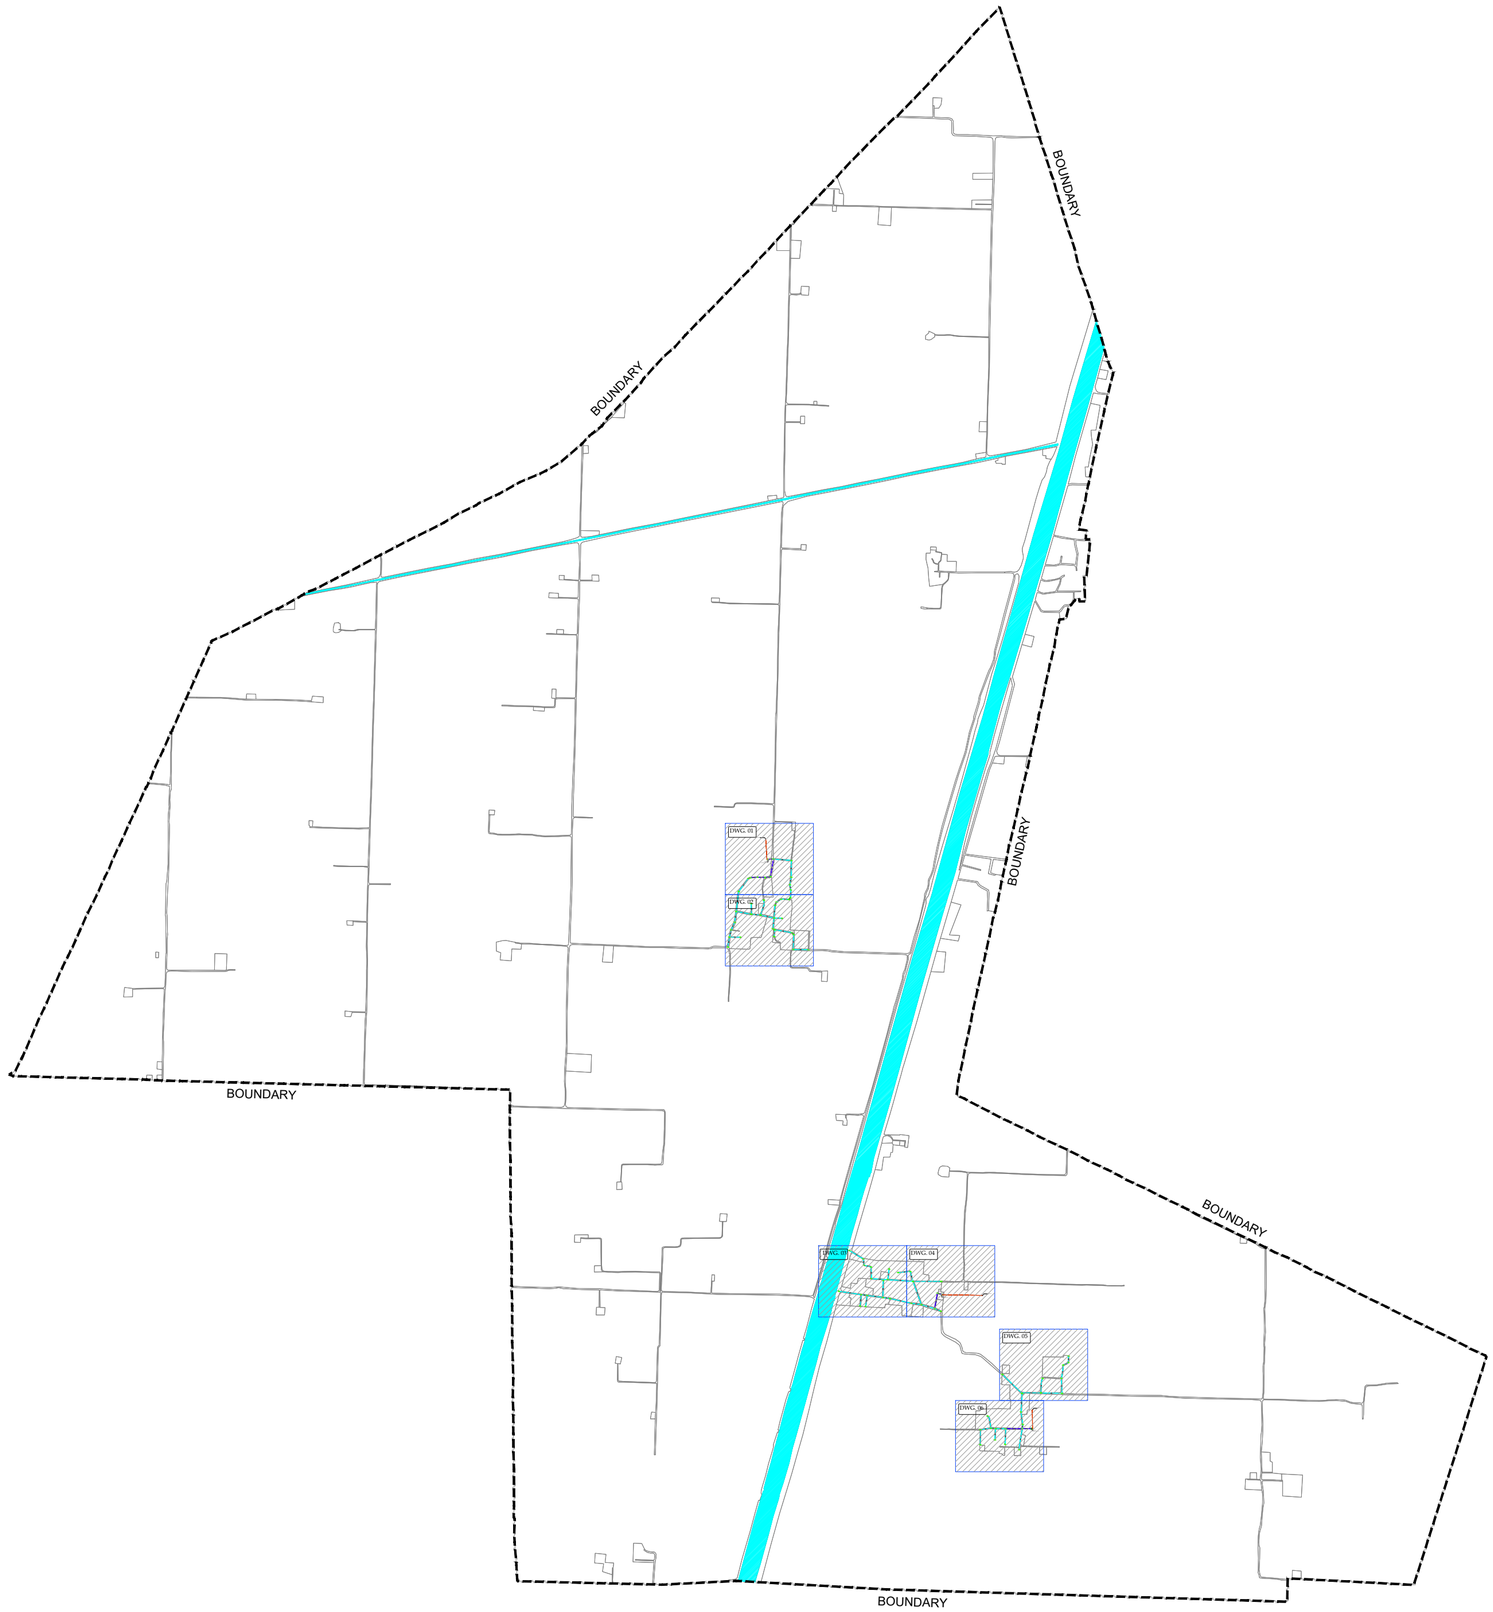

LEGEND:

- DRAIN TYPE - I
- SULLAGE CARRIER
- Ø3" HDPE PIPE
- BOUNDARY

VILLAGE: SUNDAR BASHNOAI (BWN)

TITLE.

DRAINAGE SYSTEM KEY PLAN

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 1200'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	02-01-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. HSANUL-HAQ
02	11-02-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. HSANUL-HAQ
03					
04					
05					
06					
07					

DRAWING N°:	SHEET	REV
PRMSC-BWN-SBN-SEW-KP-00	00 OF 00	01

PROJECT:

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:

PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT

ASIAN CONSULTING ENGINEERS
www.asianeon.com

PRMSC-BWN-SBN-SEW-KP-00

LAYOUT PLAN

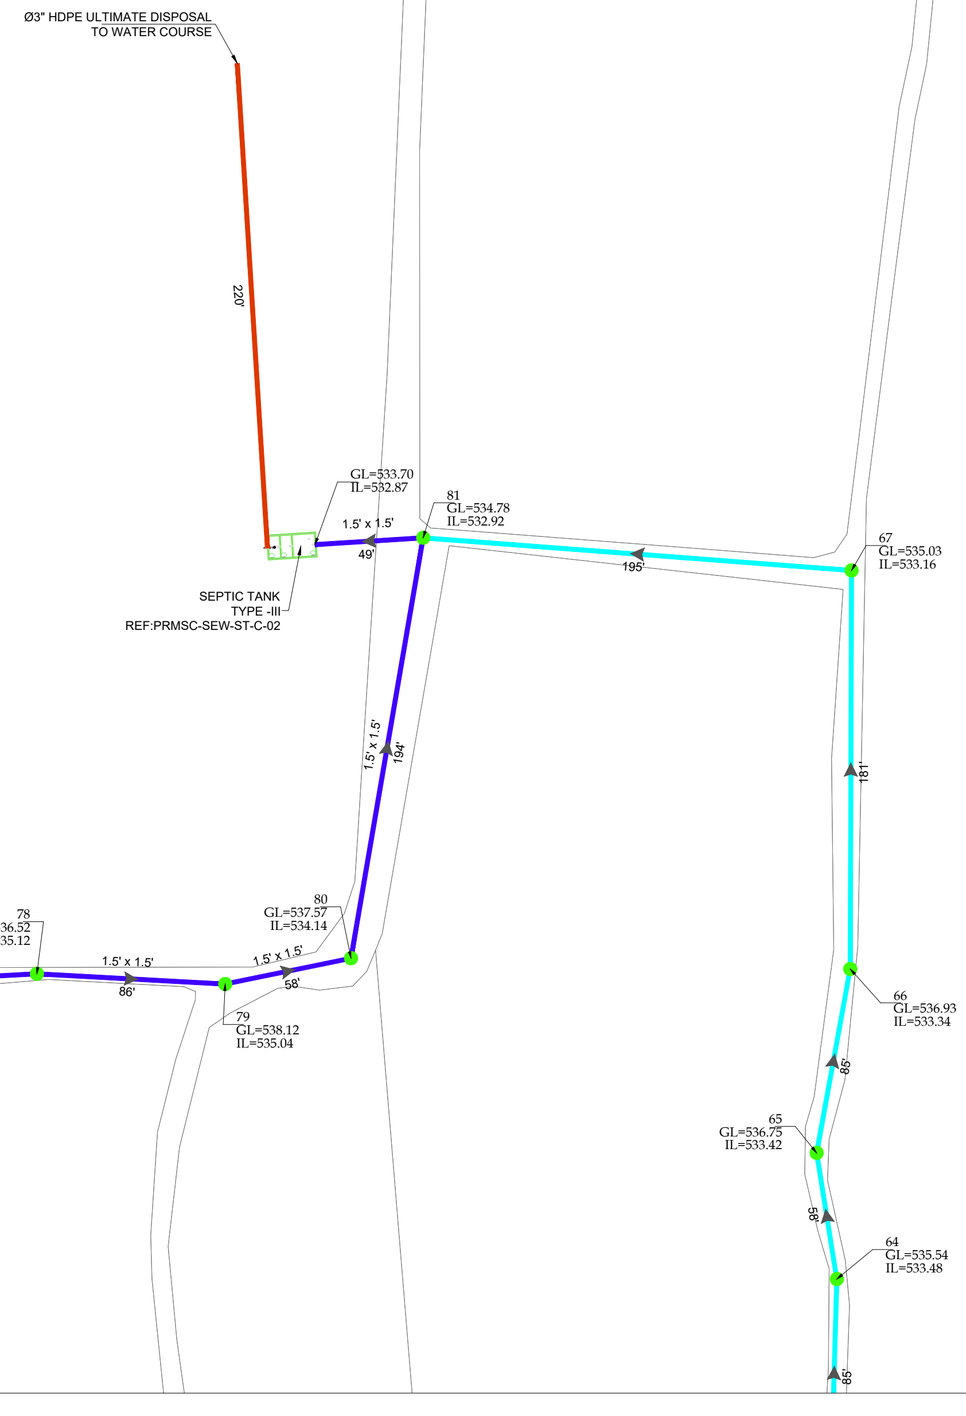

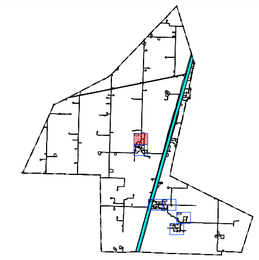

KEY PLAN

LEGEND:

- DRAIN TYPE - I
- SULLAGE CARRIER
- Ø3" HDPE PIPE
- BOUNDARY

VILLAGE: SUNDAR BASHNOAI (BWN)

TITLE:

DRAINAGE SYSTEM LAYOUT PLAN-01

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	02-01-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02	11-02-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
03					
04					
05					
06					
07					

DRAWING Nº: PRMSC-BWN-SBN-SEW-LP-01

SHEET 01 OF 06

REV 01

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

PRMSC-BWN-SBN-SEW-LP-01

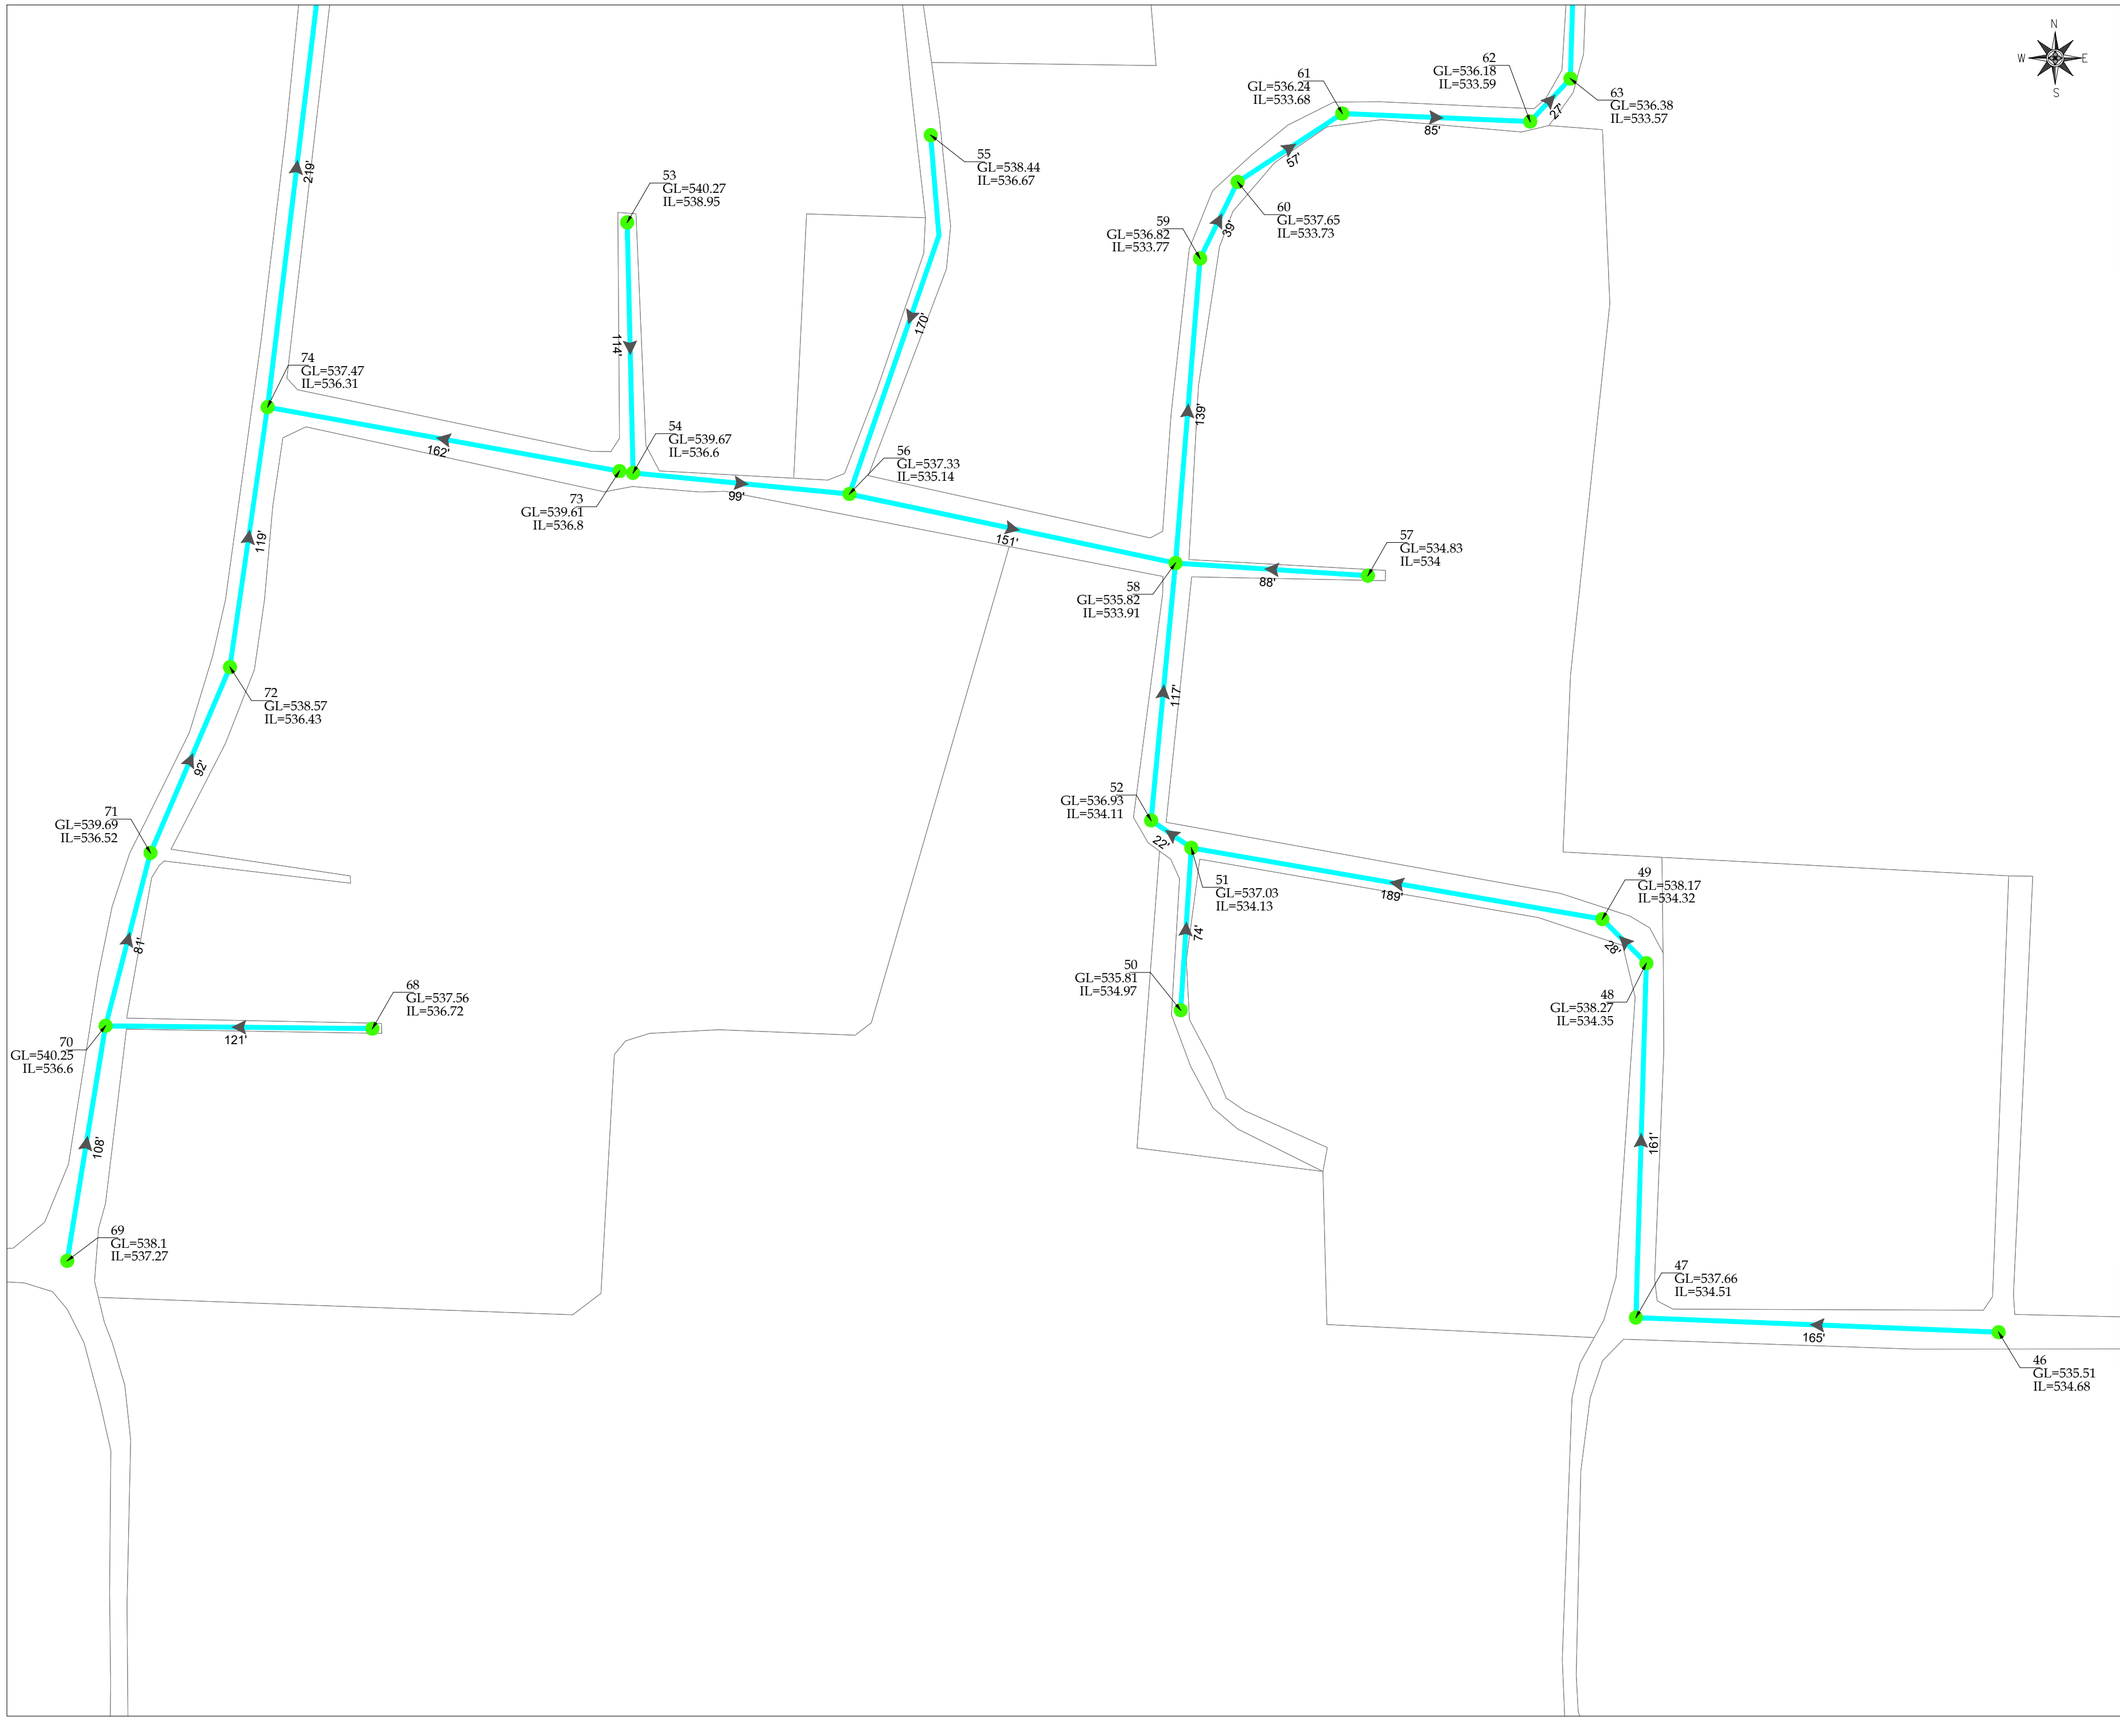

KEY PLAN

LEGEND:

- DRAIN TYPE - I
- SULLAGE CARRIER
- Ø3" HDPE PIPE
- BOUNDARY

VILLAGE: SUNDAR BASHNOAI (BWN)

TITLE.

DRAINAGE SYSTEM LAYOUT PLAN-02

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	02-01-2026	DETAILED DESIGN	MUNEEB	ENGR FAIEZ	ENGR IHSAN-UL-HAQ
02	11-02-2026	DETAILED DESIGN	MUNEEB	ENGR FAIEZ	ENGR IHSAN-UL-HAQ
03					
04					
05					
06					
07					

DRAWING Nº: PRMSC-BWN-SBN-SEW-LP-02

SHEET 02 OF 06

REV 01

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:
ASIAN CONSULTING ENGINEERS
www.asianeon.com.pv

PRMSC-BWN-SBN-SEW-LP-02

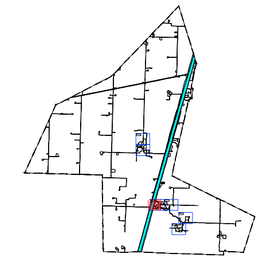

KEY PLAN

LEGEND:

- DRAIN TYPE - I
- SULLAGE CARRIER
- Ø3" HDPE PIPE
- BOUNDARY

VILLAGE: SUNDAR BASHNOAI (BWN)

TITLE.

DRAINAGE SYSTEM LAYOUT PLAN-03

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	02-01-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02	11-02-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
03					
04					
05					
06					
07					

DRAWING N°: PRMSC-BWN-SBN-SEW-LP-03

SHEET 03 OF 06

REV 01

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

PRMSC-BWN-SBN-SEW-LP-03

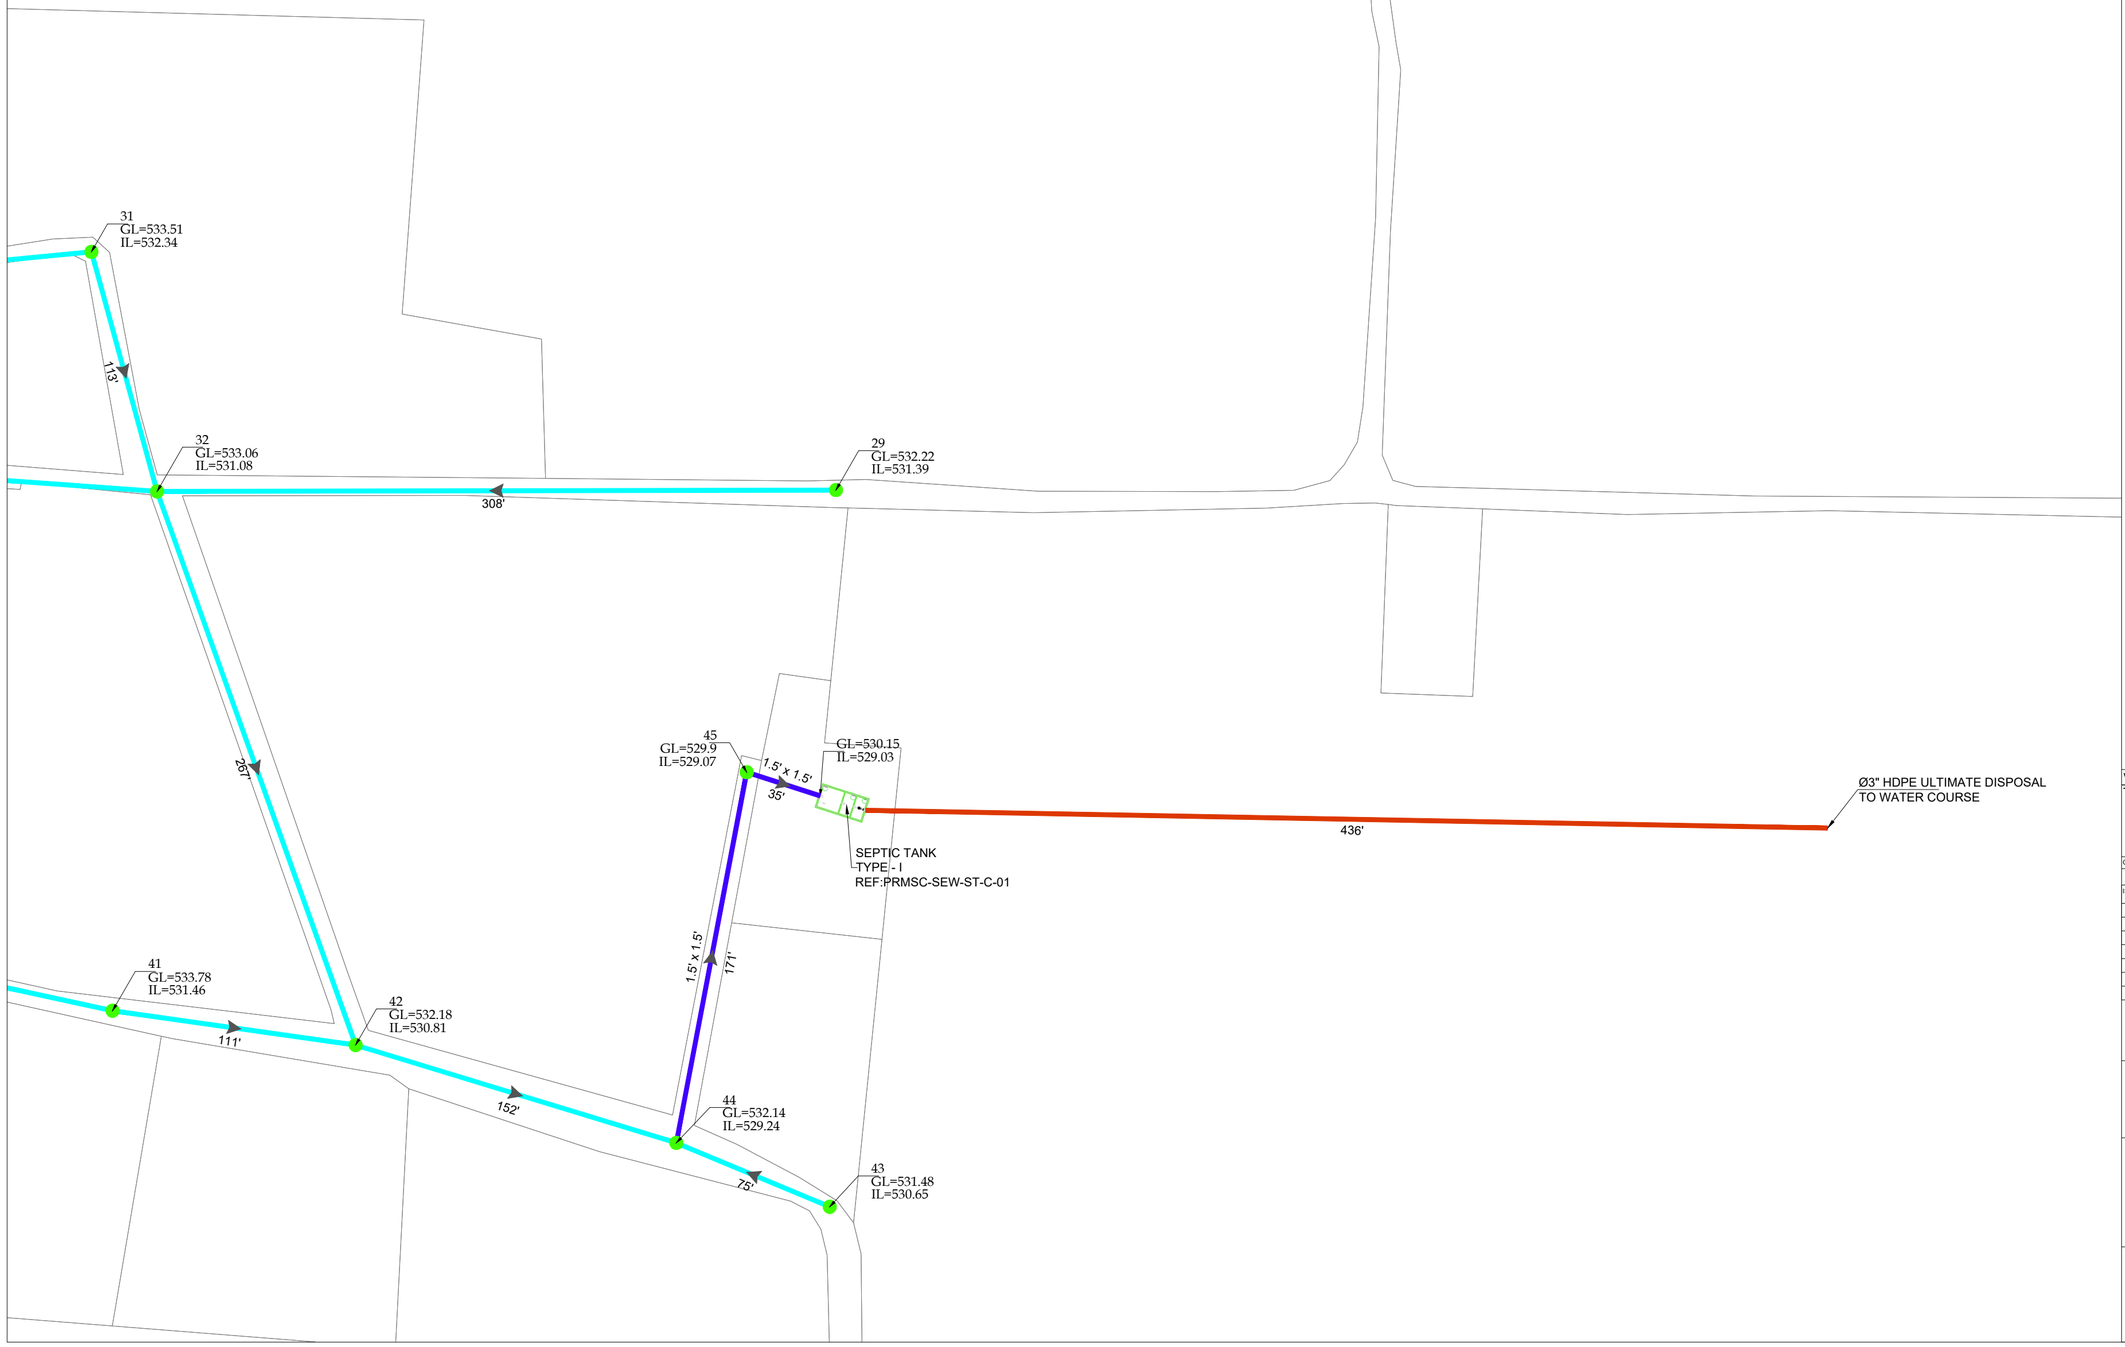

PRMSC-BWN-SBN-SEW-LP-04

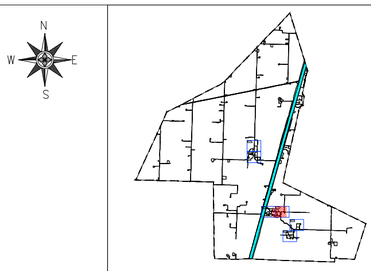

KEY PLAN

LEGEND:

- DRAIN TYPE - I
- SULLAGE CARRIER
- Ø3" HDPE PIPE
- BOUNDARY

VILLAGE: SUNDAR BASHNOAI (BWN)

TITLE:

DRAINAGE SYSTEM LAYOUT PLAN-04

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	02-01-2026	DETAILED DESIGN	MUNEEB	ENGR FAIEZ	ENGR HSAN-UL-HAQ
02	11-02-2026	DETAILED DESIGN	MUNEEB	ENGR FAIEZ	ENGR HSAN-UL-HAQ
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-SBN-SEW-LP-04	04 OF 06	01

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

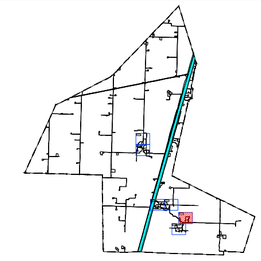

KEY PLAN

LEGEND:

- DRAIN TYPE - I
- SULLAGE CARRIER
- Ø3" HDPE PIPE
- BOUNDARY

VILLAGE: SUNDAR BASHNOAI (BWN)

TITLE.

DRAINAGE SYSTEM LAYOUT PLAN-05

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	02-01-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02	11-02-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-SBN-SEW-LP-05	05 OF 06	01

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:
ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

PRMSC-BWN-SBN-SEW-LP-05

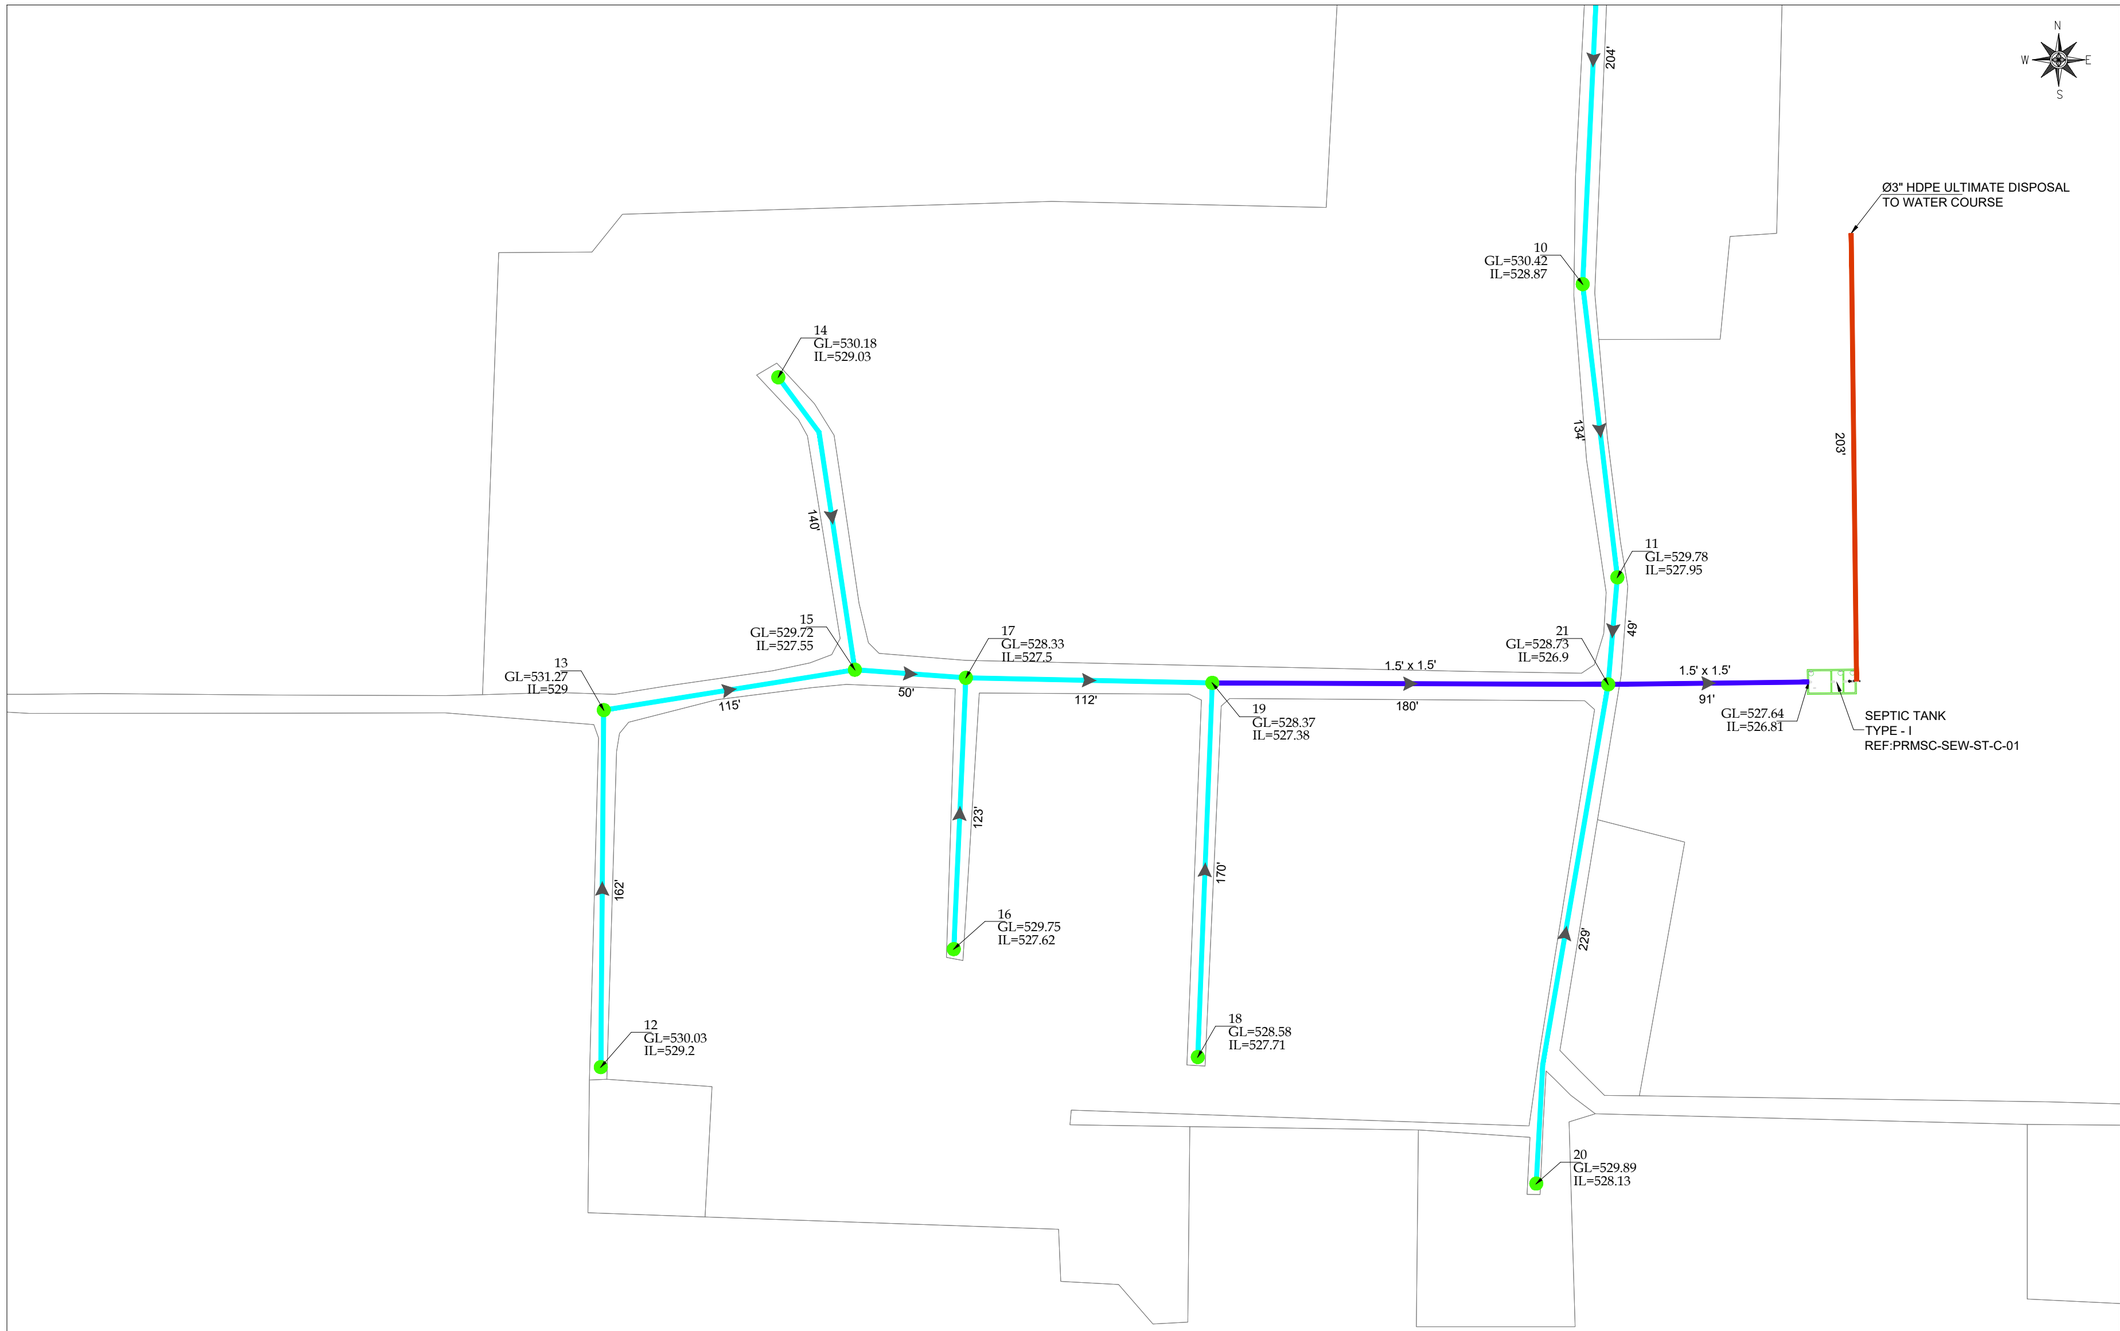

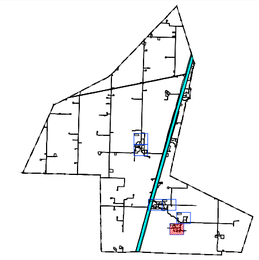

KEY PLAN

LEGEND:

- DRAIN TYPE - I
- SULLAGE CARRIER
- Ø3" HDPE PIPE
- BOUNDARY

VILLAGE: SUNDAR BASHNOAI (BWN)

TITLE.

DRAINAGE SYSTEM LAYOUT PLAN-06

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	02-01-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. HSAN-UL-HAQ
02	11-02-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. HSAN-UL-HAQ
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-SBN-SEW-LP-06	06 OF 06	01

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:
ASIAN CONSULTING ENGINEERS
www.asiaecon.com.pk

PRMSC-BWN-SBN-SEW-LP-06

HYDRAULIC STATEMENT

Node		Length	Slope	Elevation Ground	Elevation Ground	Invert	Invert	Depth
FROM	TO	ft	ft/ft	U/S	D/S	U/S	D/S	ft
1	2	71	0.002	532.17	531.54	530.85	530.71	1.32
2	3	62	0.002	531.54	530.91	530.2	530.08	1.34
3	4	145	0.002	530.91	530.51	529.97	529.68	0.94
4	5	165	0.001	530.51	531.07	529.68	529.51	0.83
5	7	228	0.001	531.07	530.53	529.51	529.28	1.56
6	7	161	0.002	531.21	530.53	530.02	529.7	1.19
7	9	207	0.001	530.53	530.32	529.28	529.08	1.25
8	9	296	0.001	530.59	530.32	529.76	529.46	0.83
9	10	204	0.001	530.32	530.42	529.08	528.87	1.24
10	11	134	0.001	530.42	529.78	528.87	528.74	1.55
11	21	49	0.002	529.78	528.73	527.99	527.9	1.79
12	13	162	0.001	530.03	531.27	529.2	529.03	0.83
13	15	115	0.001	531.27	529.72	529.03	528.89	2.24
14	15	140	0.002	530.18	529.72	529.17	528.89	1.01
15	17	50	0.002	529.72	528.33	527.6	527.5	2.12
16	17	123	0.002	529.75	528.33	527.74	527.5	2.01
17	19	112	0.001	528.33	528.37	527.5	527.38	0.83
18	19	170	0.001	528.58	528.37	527.75	527.54	0.83
19	21	180	0.001	528.37	528.73	527.38	527.21	0.99
20	21	229	0.002	529.89	528.73	528.36	527.9	1.53
21	ST-TYPE-I (HH=40)	91	0.002	528.73	527.64	526.99	526.81	1.74
22	23	176	0.002	535.6	535.27	534.77	534.44	0.83
23	24	69	0.002	535.27	534.65	533.95	533.82	1.32
24	25	79	0.002	534.65	534.49	533.81	533.66	0.84
25	26	128	0.002	534.49	533.21	532.63	532.38	1.86
26	28	179	0.001	533.21	533.41	532.38	532.2	0.83
27	28	117	0.002	535.23	533.41	532.81	532.58	2.42
28	32	274	0.001	533.41	533.06	532.2	531.92	1.21
29	32	308	0.001	532.22	533.06	531.39	531.08	0.83
30	31	133	0.002	534.67	533.51	532.94	532.68	1.73
31	32	113	0.002	533.51	533.06	532.45	532.23	1.06
32	42	267	0.001	533.06	532.18	531.08	530.81	1.98
33	35	246	0.002	535.16	534.49	534.15	533.66	1.01
34	35	123	0.001	534.32	534.49	533.49	533.36	0.83
35	37	66	0.001	534.49	534.26	533.36	533.3	1.13
36	37	120	0.001	534.15	534.26	533.32	533.2	0.83
37	39	171	0.002	534.26	533.51	533.02	532.68	1.24
38	39	184	0.002	534.51	533.51	533.05	532.68	1.46
39	40	79	0.002	533.51	532.71	532.03	531.88	1.48
40	41	235	0.001	532.71	533.78	531.88	531.57	0.83
41	42	111	0.002	533.78	532.18	531.57	531.35	2.21

HYDRAULIC STATEMENT

Node		Length	Slope	Elevation Ground	Elevation Ground	Invert	Invert	Depth
FROM	TO	ft	ft/ft	U/S	D/S	U/S	D/S	ft
42	44	152	0.001	532.18	532.14	530.81	530.66	1.37
43	44	75	0.001	531.48	532.14	530.65	530.57	0.83
44	45	171	0.002	532.14	529.9	529.41	529.07	2.73
45	ST-TYPE-I (HH=40)	35	0.001	529.9	530.15	529.07	529.03	0.83
46	47	165	0.001	535.51	537.66	534.68	534.51	0.83
47	48	161	0.001	537.66	538.27	534.51	534.35	3.15
48	49	28	0.001	538.27	538.17	534.35	534.32	3.92
49	51	189	0.001	538.17	537.03	534.32	534.13	3.85
50	51	74	0.001	535.81	537.03	534.97	534.9	0.84
51	52	22	0.001	537.03	536.93	534.13	534.11	2.9
52	58	117	0.002	536.93	535.82	534.11	533.91	2.82
53	54	114	0.002	540.27	539.67	539.06	538.83	1.21
54	56	99	0.002	539.67	537.33	536.7	536.5	2.97
55	56	170	0.002	538.44	537.33	536.84	536.5	1.6
56	58	151	0.002	537.33	535.82	535.29	534.99	2.04
57	58	88	0.001	534.83	535.82	534	533.91	0.83
58	59	139	0.001	535.82	536.82	533.91	533.77	1.91
59	60	39	0.001	536.82	537.65	533.77	533.73	3.05
60	61	57	0.001	537.65	536.24	533.73	533.68	3.92
61	62	85	0.001	536.24	536.18	533.68	533.59	2.56
62	63	27	0.001	536.18	536.38	533.59	533.57	2.59
63	64	85	0.001	536.38	535.54	533.57	533.48	2.81
64	65	58	0.001	535.54	536.75	533.48	533.42	2.06
65	66	85	0.001	536.75	536.93	533.42	533.34	3.33
66	67	181	0.001	536.93	535.03	533.34	533.16	3.59
67	81	195	0.001	535.03	534.78	533.16	532.96	1.87
68	70	121	0.001	537.56	540.25	536.72	536.6	0.84
69	70	108	0.001	538.1	540.25	537.27	537.16	0.83
70	71	81	0.001	540.25	539.69	536.6	536.52	3.65
71	72	92	0.001	539.69	538.57	536.52	536.43	3.17
72	74	119	0.001	538.57	537.47	536.43	536.31	2.14
73	74	162	0.002	539.61	537.47	536.97	536.64	2.64
74	75	219	0.001	537.47	537.11	536.31	536.09	1.16
75	76	178	0.002	537.11	536.05	535.58	535.22	1.53
76	77	25	0.001	536.05	536.1	535.22	535.2	0.83
77	78	73	0.001	536.1	536.52	535.2	535.12	0.9
78	79	86	0.001	536.52	538.12	535.12	535.04	1.4
79	80	58	0.001	538.12	537.57	535.04	534.98	3.08
80	81	194	0.002	537.57	534.78	534.33	533.95	3.24
81	ST-TYPE-III (HH=80)	49	0.002	534.78	533.7	532.96	532.87	1.82

VILLAGE: SUNDAR BASHNOAI (BWN)

TITLE.

HYDRAULIC STATEMENT

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	02-01-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02	11-02-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
03					
04					
05					
06					
07					

DRAWING Nº: PRMSC-BWN-SBN-SEW-HS-01

SHEET 01 OF 01

REV 01

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT
ASIAN CONSULTING ENGINEERS
www.asiancon.com

PRMSC-BWN-SBN-SEW-HS-00

SHER SINGH WALA

KEY PLAN

Revenue Village: Sher Singh Wala Main Sheet

Title:
Proposed Drainage Network Plan

Legend:

- SETTLEMENT
- NODE
- 6" uPVC PIPE
- DRAIN TYPE-1
- SULLAGE CARRIER
- SEPTIC TANK
- SETTLEMENT BOUNDARY

Drain Type 1=5649 Rft
Sullage Carrier= 2929 Rft

Scale: 1:6,200
1 inch = 517 feet
Paper Size: A3

0 40 80 160
Kilometers

Project:
Engineering Design & Construction Supervision, Punjab Rural Sustainable Water Supply & Sanitation Project, Cluster South III

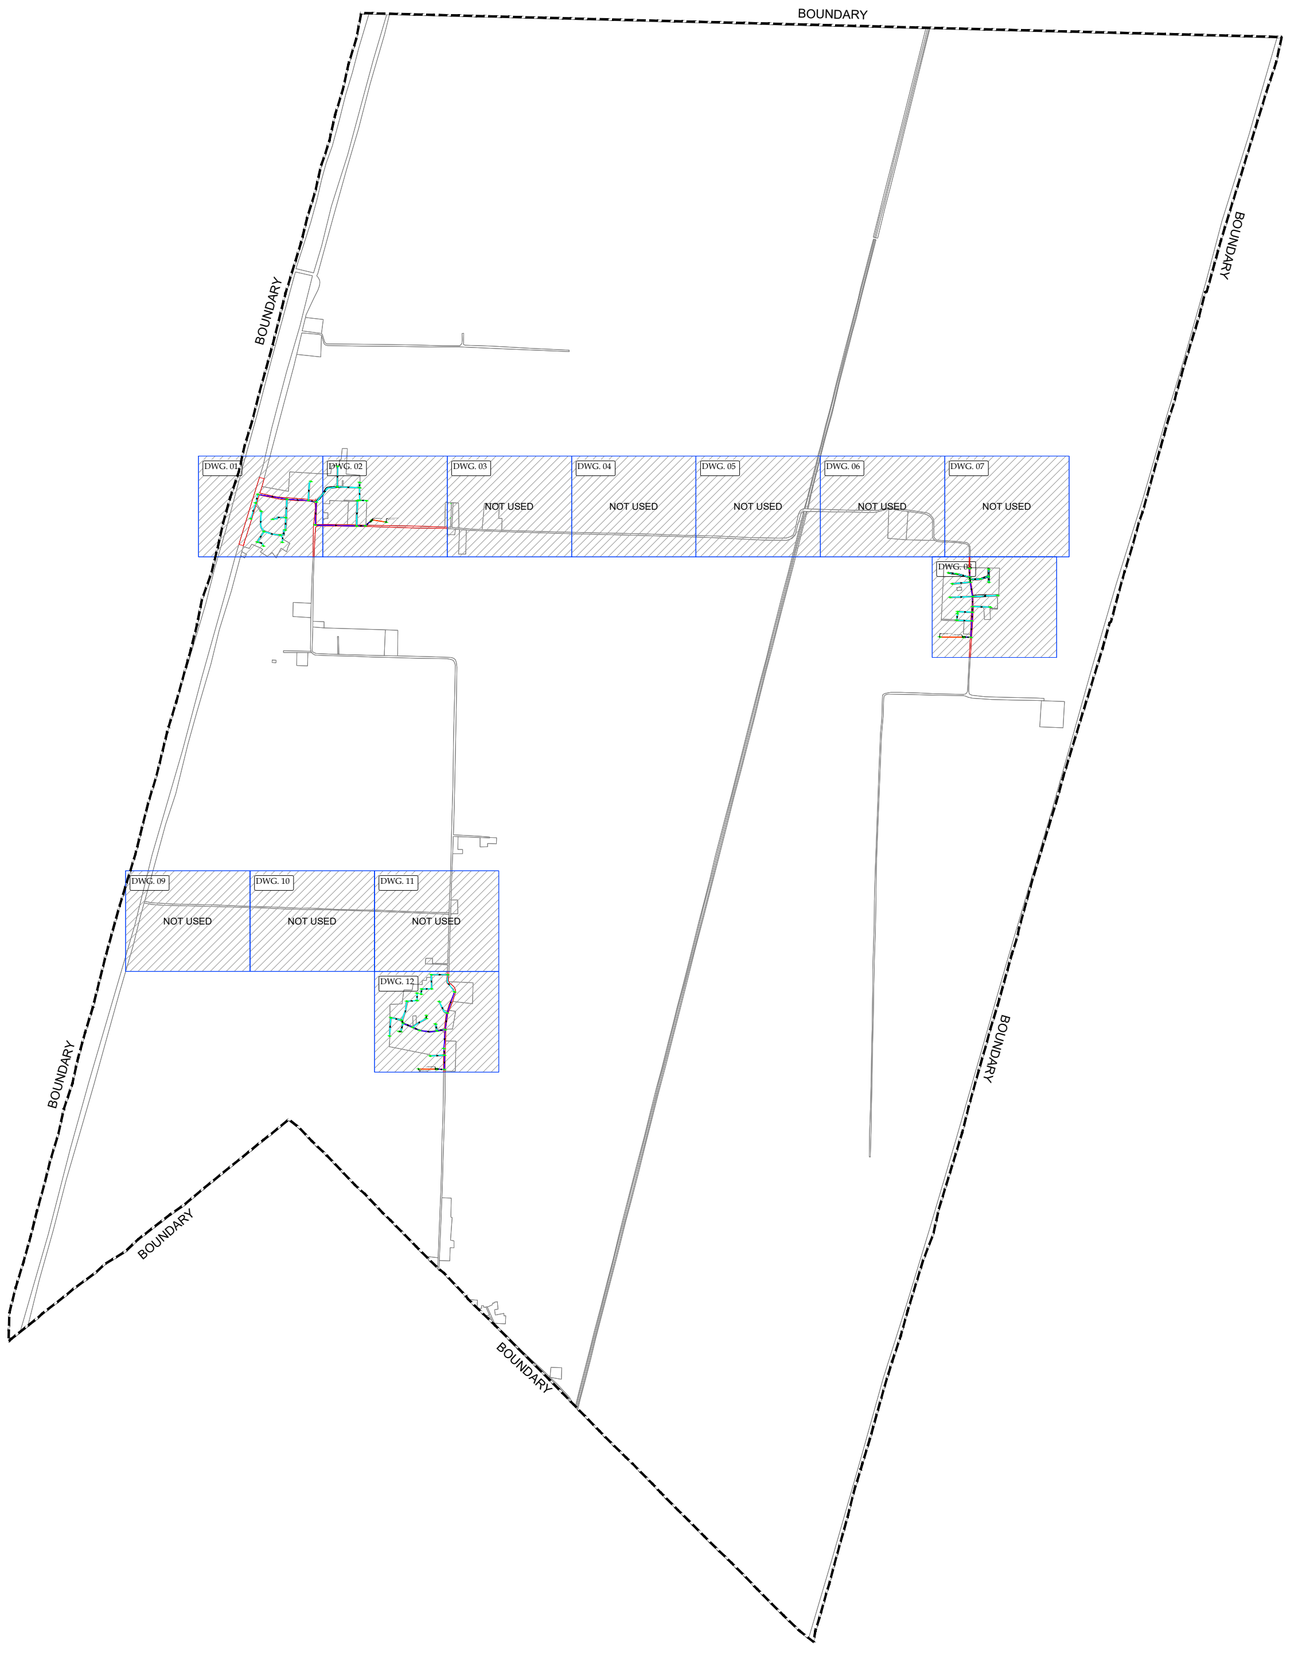

N
W
E
S

LEGEND:

- DRAIN TYPE - I
- SULLAGE CARRIER
- Ø3" HDPE PIPE
- EXISTING SOLING
- METALLED ROAD
- BOUNDARY

VILLAGE: SHER SINGH WALA (BWN)

TITLE.

DRAINAGE SYSTEM KEY PLAN

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 850'

ISSUE N°	DATE	D E S C R I P T I O N	DRAWN	DESIGNED	APPROVED
01	23-05-2026	DETAILED DESIGN	MUNEEB	ENGR FAIEZ	ENGR IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-SSW-SEW-KP-00	00 OF 00	00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT
ASIAN CONSULTING ENGINEERS
www.asiancon.com

PRMSC-BWN-SSW-SEW-KP-00

LAYOUT PLAN

Revenue Village: Sher Singh Wala Sheet-1

District:	Bahawalnagar
Tehsil:	Bahawalnagar
Revenue Village:	Sher Singh Wala

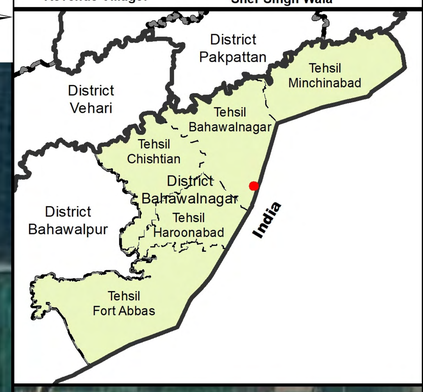

Title:
Proposed Drainage Network Plan

Legend:

- SETTLEMENT
- NODE
- 3" HDPE PIPE
- DRAIN TYPE-1
- SULLAGE CARRIER
- SEPTIC TANK
- SETTLEMENT BOUNDARY

Drain Type 1=5649 Rft

Sullage Carrier= 2929 Rft

Scale: 1:1,300

1 inch = 108 feet

Paper Size: A3

0 40 80 160

Kilometers

Project:

Engineering Design & Construction Supervision, Punjab Rural Sustainable Water Supply & Sanitation Project, Cluster South III

PRWSC

ENVIRONMENTAL TECHNOLOGIES

ASIAN CONSULTING ENGINEERS www.asiancon.com

Kallaliwali Dhani

GL=548.81
IL=547.21

SEPTIC TANK-T4
Plot Size=3.04 Marla

4" HDPE PIPE ULTIMATE DISPOSAL TO WATER COURSE

Revenue Village: Sher Singh Wala Sheet-2

Chak Sher Singh

SEPTIC TANK-T2
Plot Size=2 Marla

GL=548.18
IL=546.93

District:	Bahawalnagar
Tehsil:	Bahawalnagar
Revenue Village:	Sher Singh Wala

Title:
Proposed Drainage Network Plan

Legend:

- SETTLEMENT
- NODE
- 6" uPVC PIPE
- DRAIN TYPE-1
- SULLAGE CARRIER
- SEPTIC TANK
- SETTLEMENT BOUNDARY

Drain Type 1=5649 Rft
Sullage Carrier= 2929 Rft

Scale: 1:700
1 inch = 58 feet
Paper Size: A3

0 40 80 160
Kilometers

Project:
Engineering Design & Construction Supervision, Punjab Rural Sustainable Water Supply & Sanitation Project, Cluster South III

Revenue Village: Sher Singh Wala Sheet-3

District:	Bahawalnagar
Tehsil:	Bahawalnagar
Revenue Village:	Sher Singh Wala

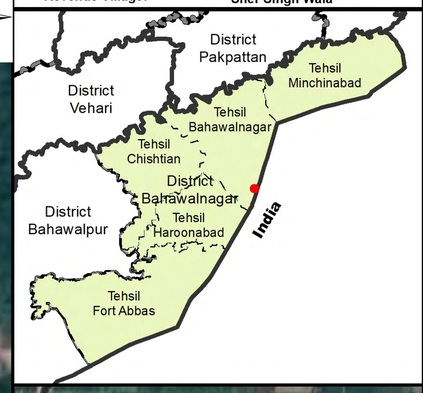

ND-26 GL=546.95 IL=543.12
ND-27 GL=547.99 IL=543.99
ND-25 GL=548.44 IL=546.34
ND-24 GL=548.23 IL=547.29
ND-23 GL=548.13 IL=547.3
ND-31 GL=549.24 IL=548.4
ND-28 GL=548.39 IL=545.84
ND-33 GL=549.44 IL=548.24
ND-32 GL=550.17 IL=548.35
ND-29 GL=549.99 IL=547.69
ND-30 GL=548.3 IL=545.67
Chak Ratni Khera
ND-40 GL=550.77 IL=549.84
ND-35 GL=549.26 IL=548.1
ND-38 GL=548.77 IL=547.93
ND-41 GL=550.81 IL=549.92
ND-39 GL=549.62 IL=547.91
ND-44 GL=548.85 IL=548.01
ND-42 GL=550.67 IL=547.83
ND-43 GL=550.01 IL=547.77
ND-45 GL=549.27 IL=546.75
ND-46 GL=547.45 IL=545.54
ND-37 GL=550.2 IL=549.37
ND-36 GL=551.37 IL=548.92
ND-34 GL=549.52 IL=548.69
1.5' x 1.5'
ND-47 GL=548.36 IL=545.39
ND-48 GL=547.46 IL=546.62
ND-49 GL=547.55 IL=545.34
SEPTIC TANK-T2
Plot Size=2 Marla
GL=545.25
IL=544.42
ND-50 GL=546.75 IL=544.52

Title:
Proposed Drainage Network Plan

Legend:

- SETTLEMENT
- NODE
- **3" HDPE**: PIPE
- DRAIN TYPE-1
- SULLAGE CARRIER
- SEPTIC TANK
- SETTLEMENT BOUNDARY

Drain Type 1=5649 Rft

Sullage Carrier= 2929 Rft

Scale: 1:900

1 inch = 75 feet

Paper Size: A3

0 40 80 160

Kilometers

Project:

Engineering Design & Construction Supervision, Punjab Rural Sustainable Water Supply & Sanitation Project, Cluster South III

PRWSC

ENVIRONMENTAL TECHNOLOGIES

ASIAN CONSULTING ENGINEERS www.asiancon.com

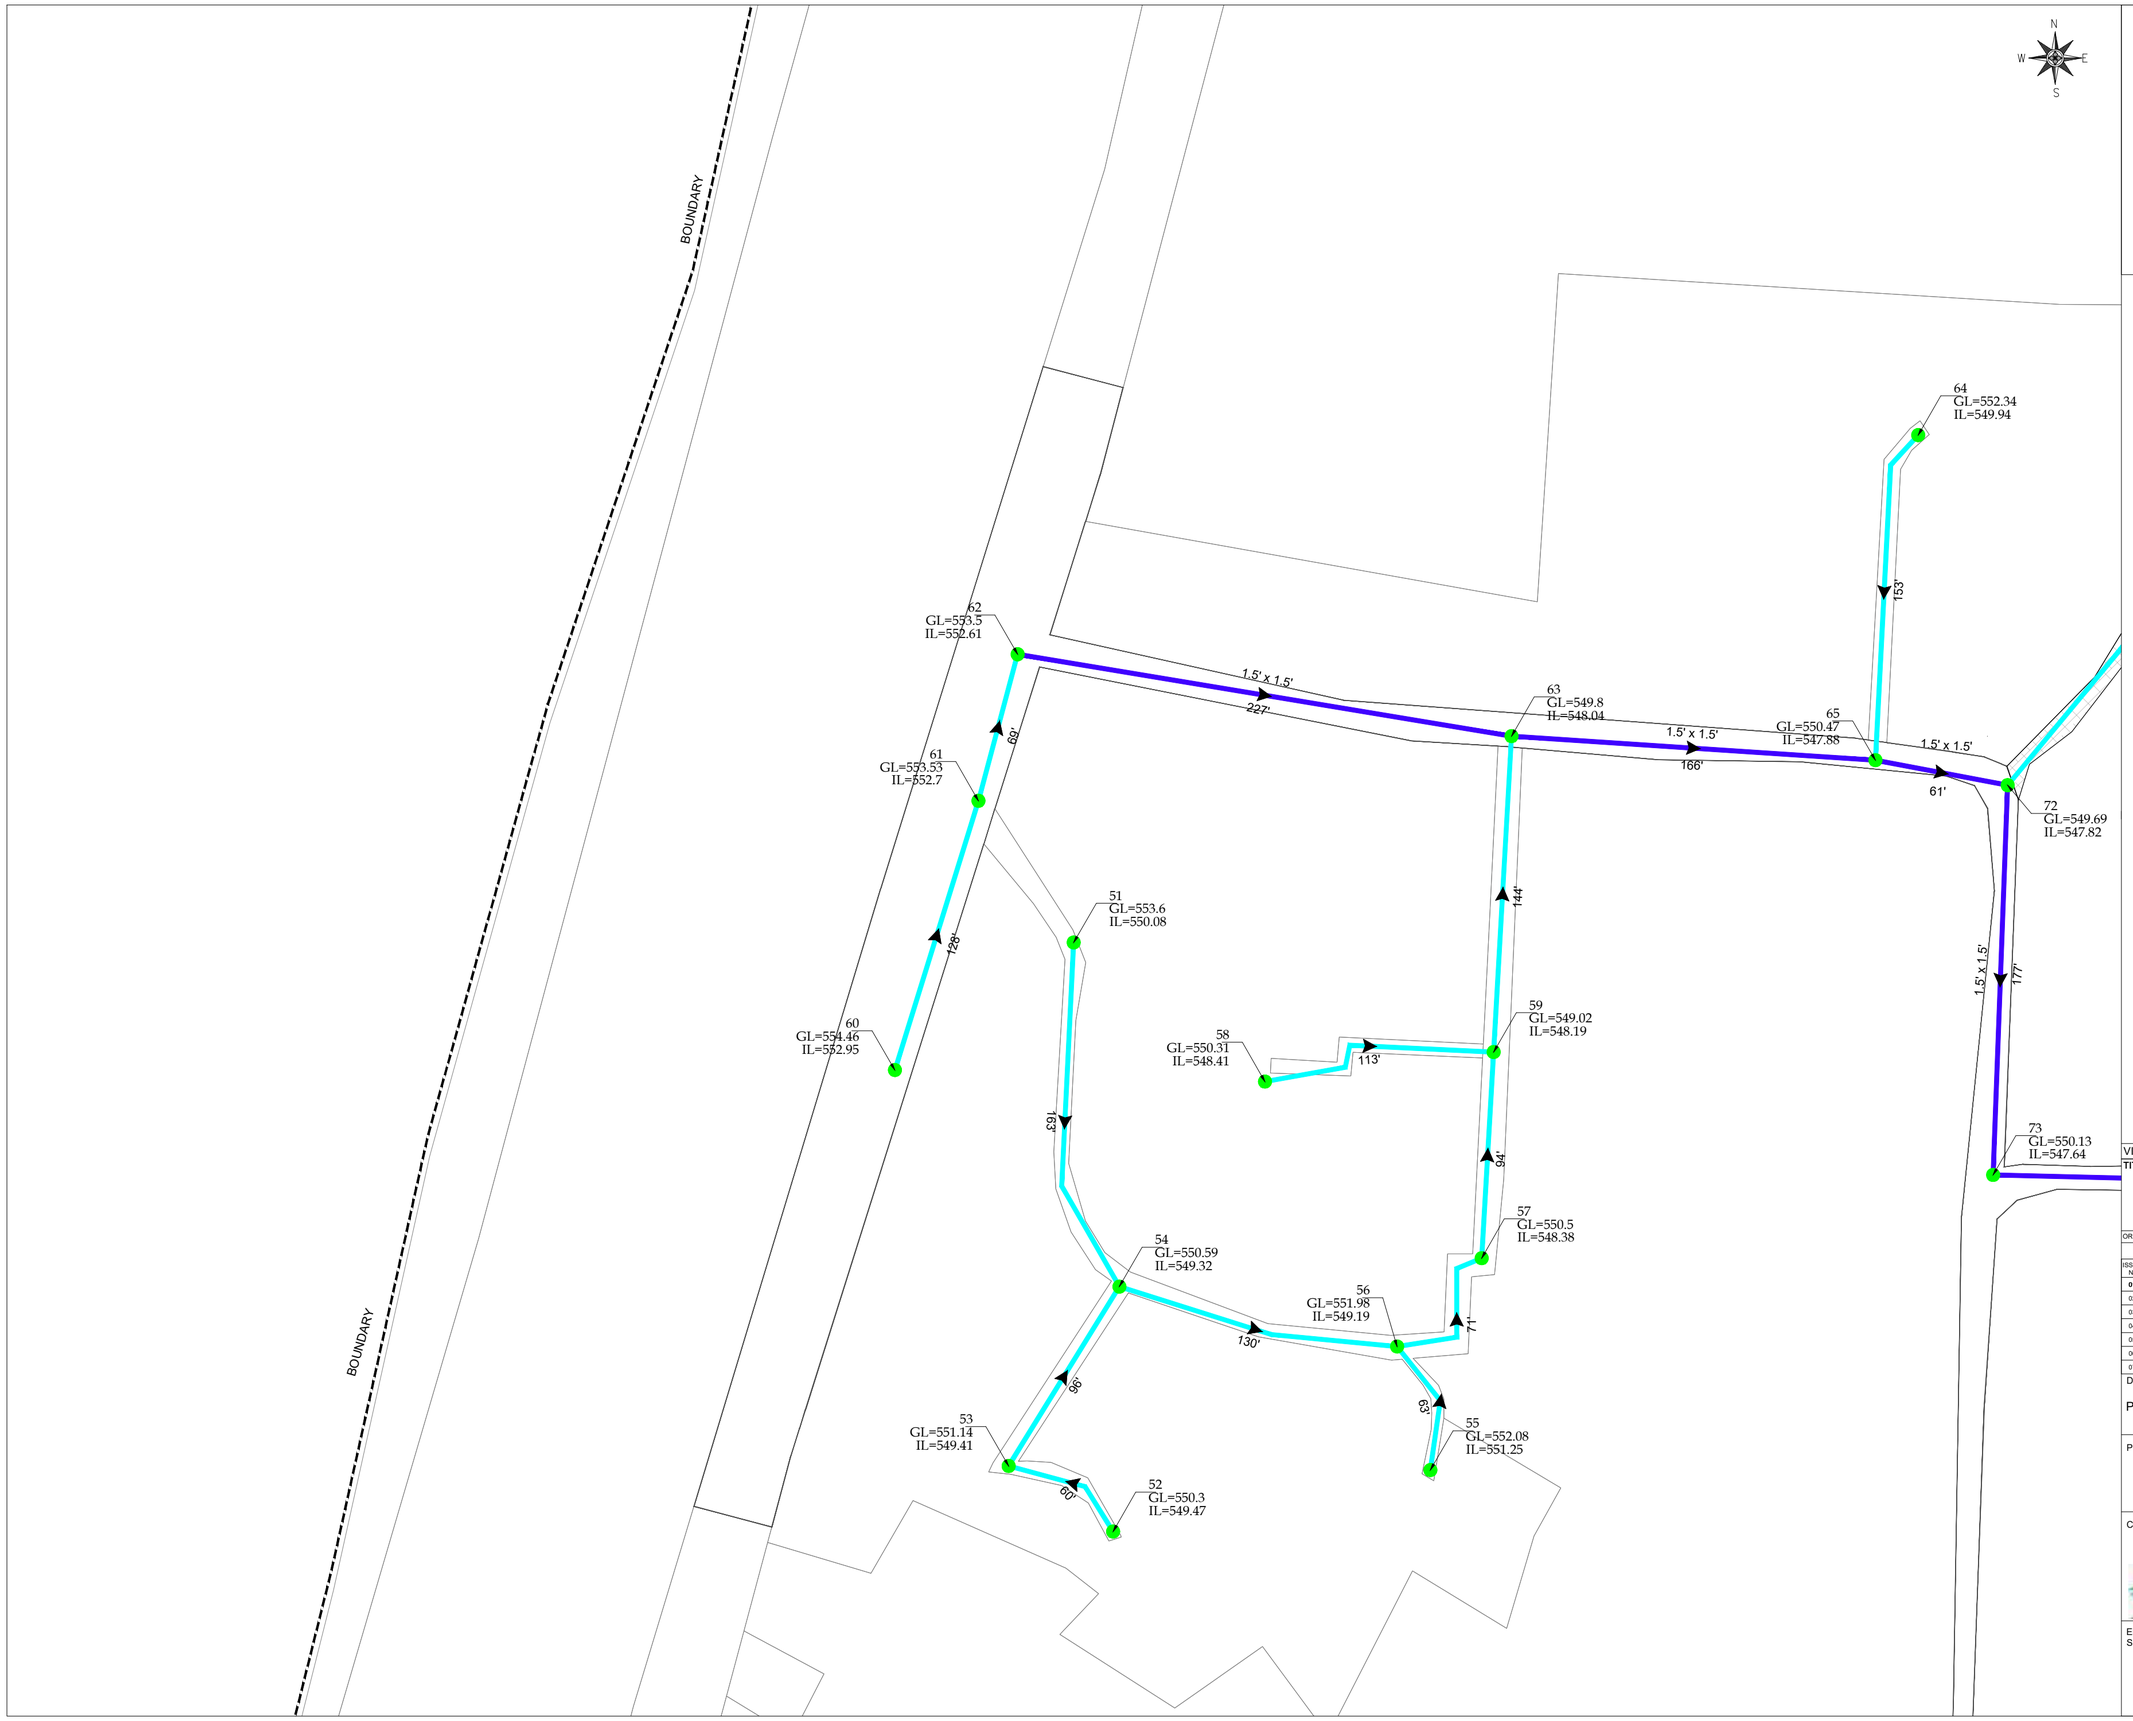

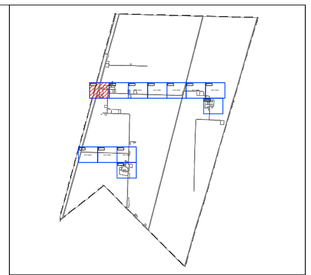

KEY PLAN

LEGEND:

- DRAIN TYPE - I
- SULLAGE CARRIER
- Ø3" HDPE PIPE
- EXISTING SOLING
- METALLED ROAD
- BOUNDARY

VILLAGE: SHER SINGH WALA (BWN)

TITLE.

DRAINAGE SYSTEM LAYOUT PLAN-01

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	23-05-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:

PRMSC-BWN-SSW-SEW-LP-01

SHEET 01 OF 12

REV 01

PROJECT:

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS
www.asiacon.com.pv

PRMSC-BWN-SSW-SEW-LP-01

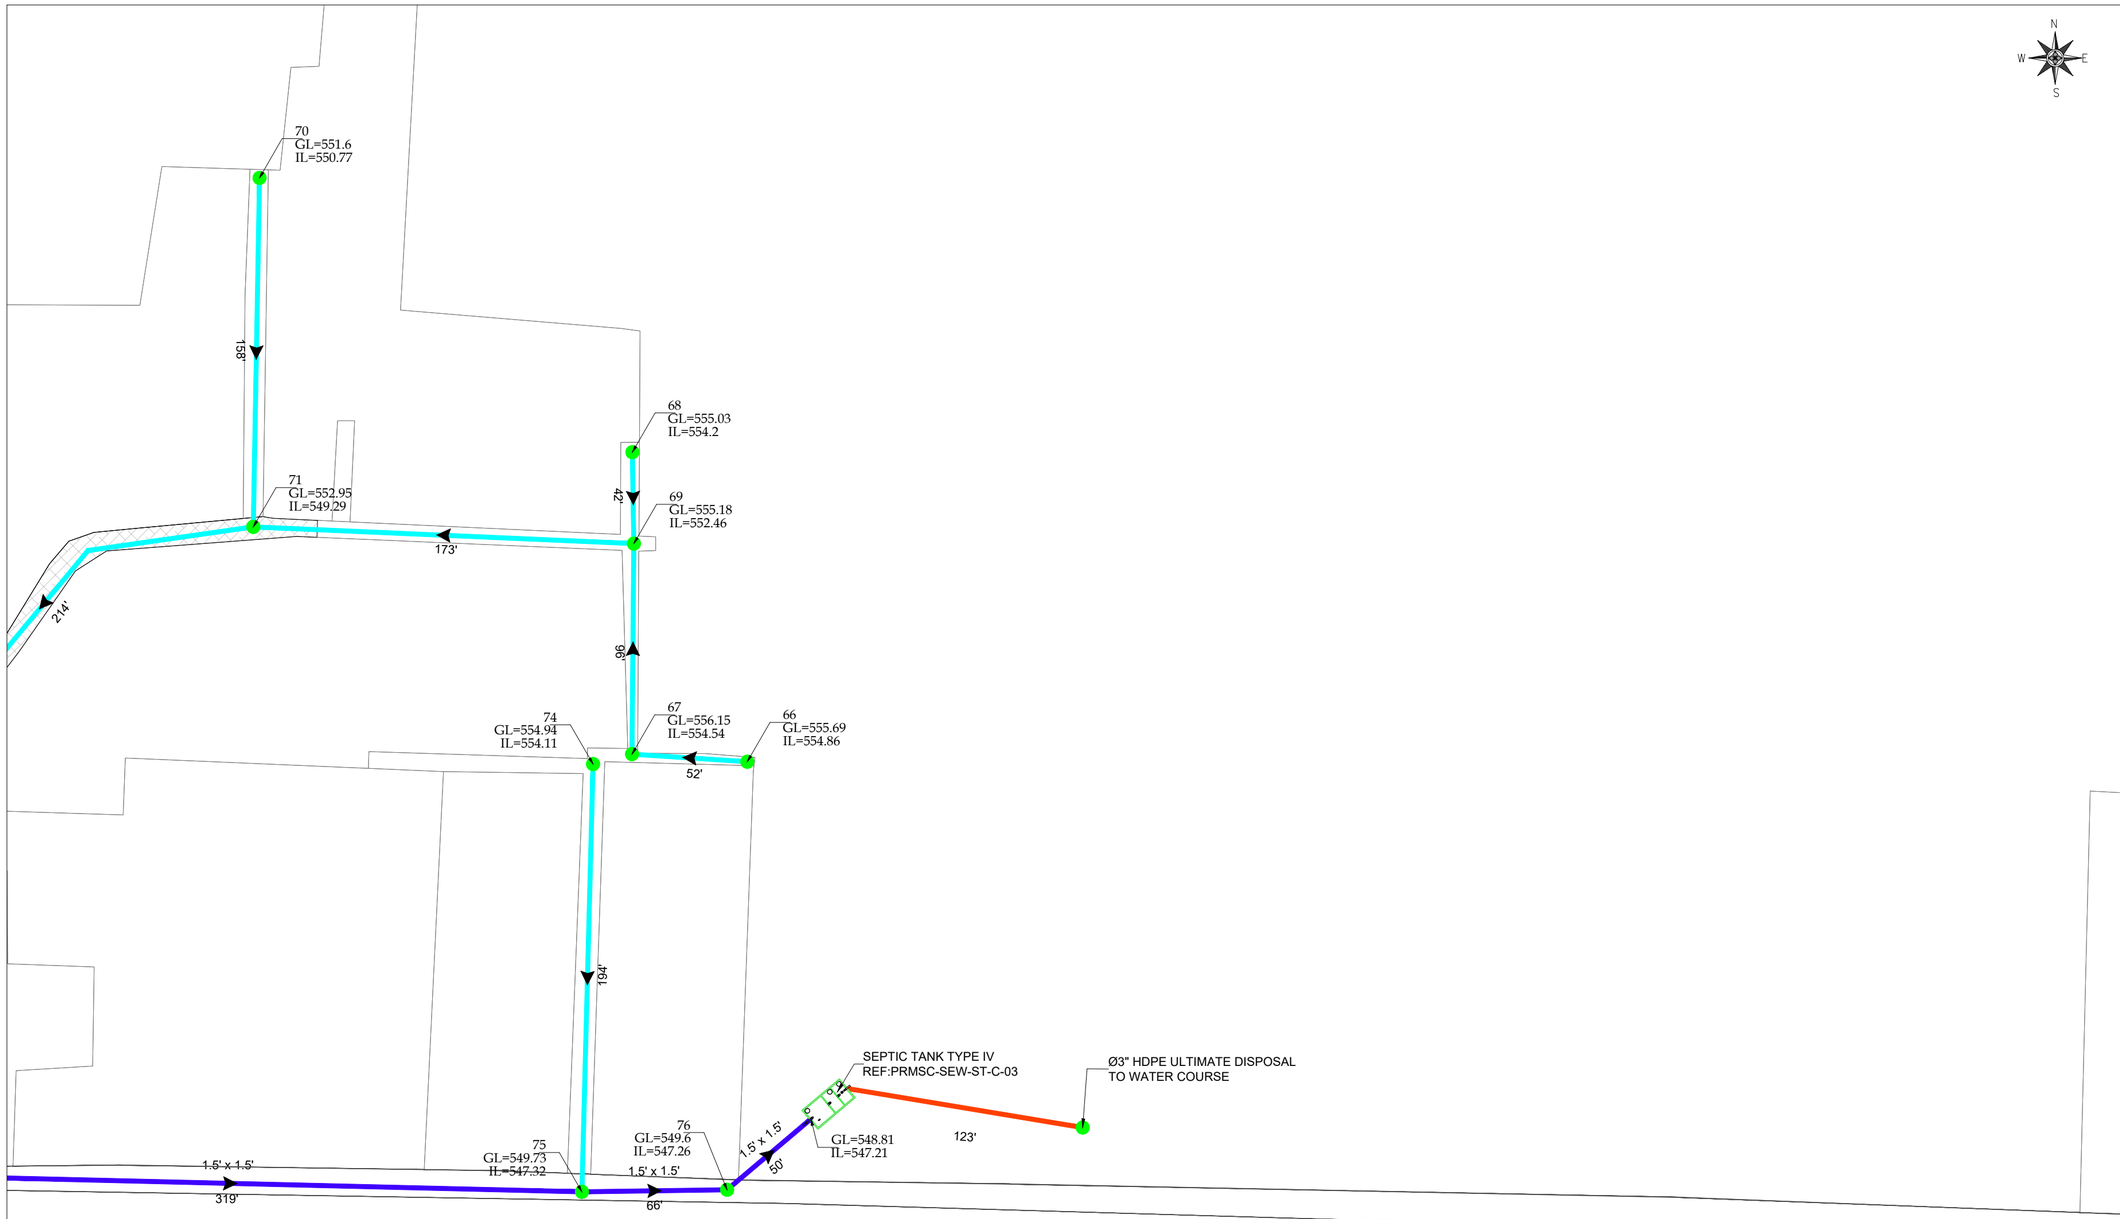

KEY PLAN

LEGEND:

- DRAIN TYPE - I
- SULLAGE CARRIER
- Ø3" HDPE PIPE
- EXISTING SOLING
- METALLED ROAD
- BOUNDARY

VILLAGE: SHER SINGH WALA (BWN)

TITLE.

DRAINAGE SYSTEM LAYOUT PLAN-02

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	23-05-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING N°: PRMSC-BWN-SSW-SEW-LP-02

SHEET 02 OF 12

REV 01

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:
ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

PRMSC-BWN-SSW-SEW-LP-02

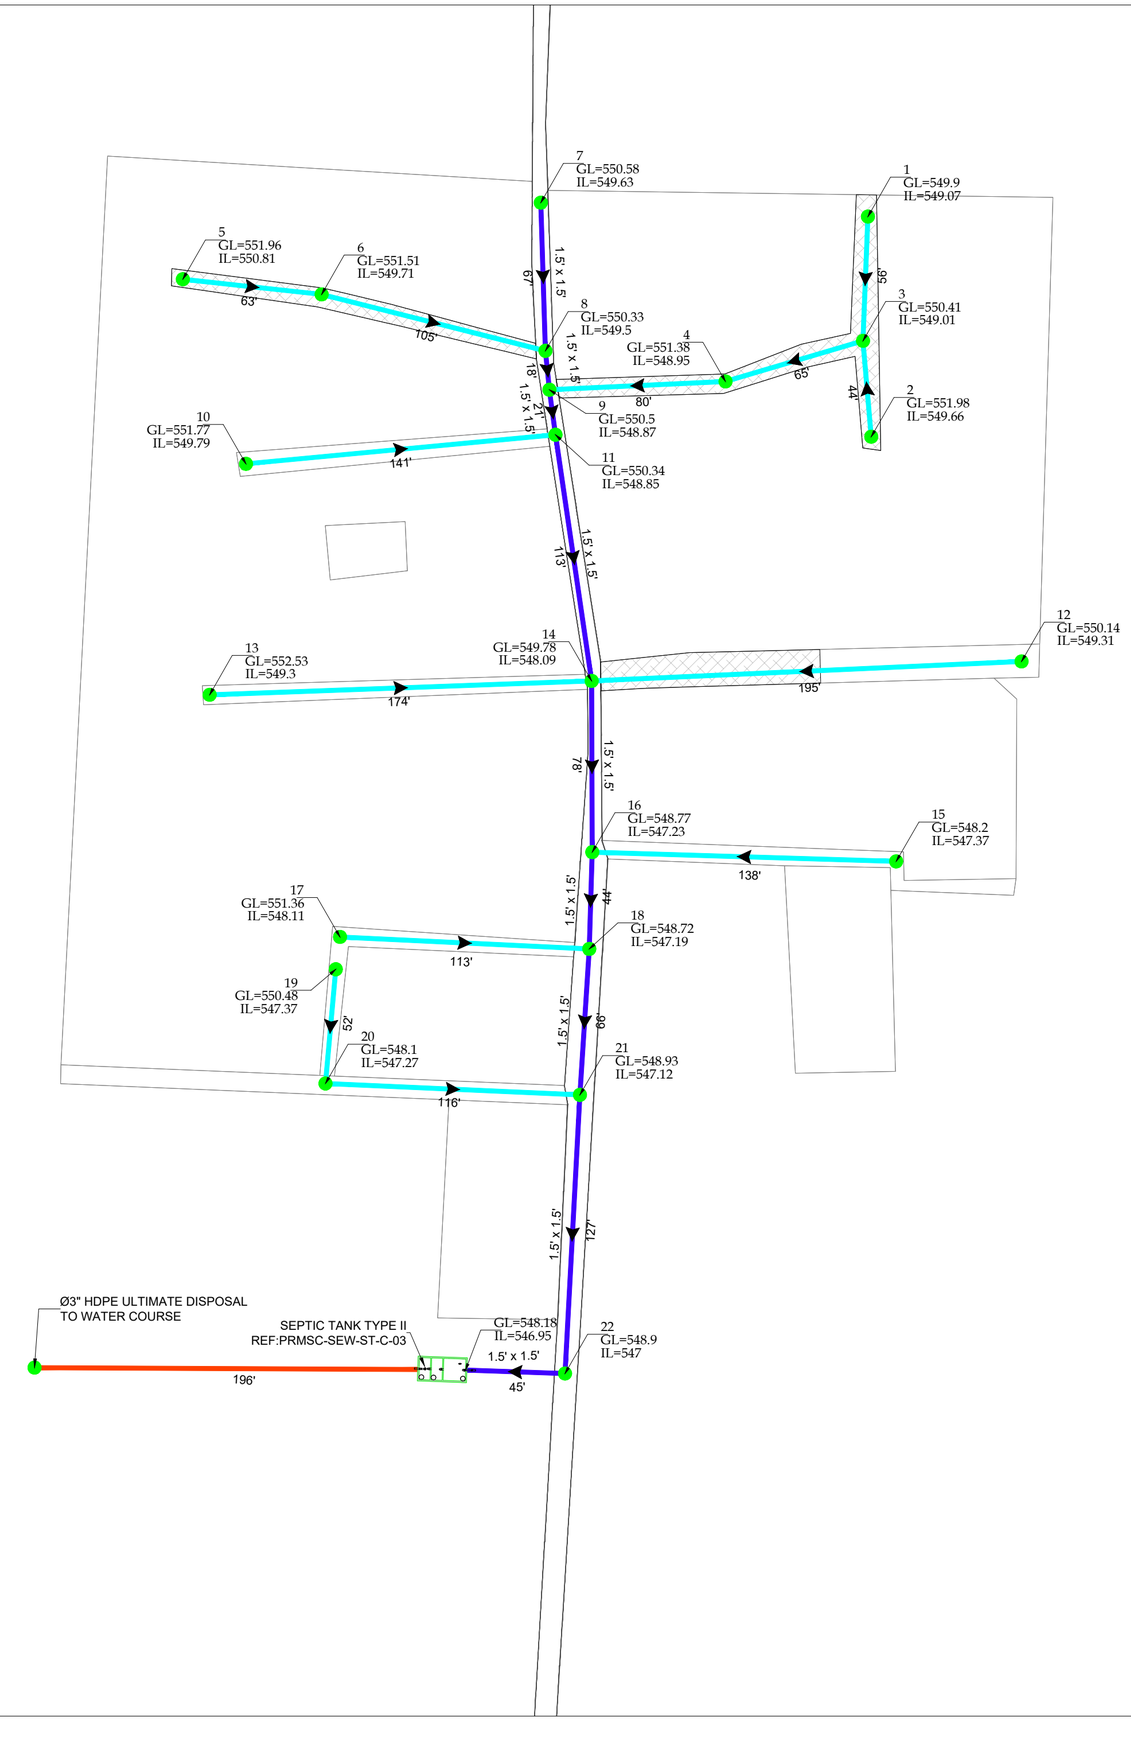

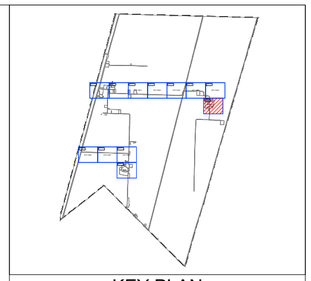

KEY PLAN

LEGEND:

- DRAIN TYPE - I
- SULLAGE CARRIER
- Ø3" HDPE PIPE
- EXISTING SOLING
- METALLED ROAD
- BOUNDARY

VILLAGE: SHER SINGH WALA (BWN)

TITLE.

DRAINAGE SYSTEM LAYOUT PLAN-08

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	23-05-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING N°: PRMSC-BWN-SSW-SEW-LP-08

SHEET 08 OF 12

REV 01

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

PRMSC-BWN-SSW-SEW-LP-08

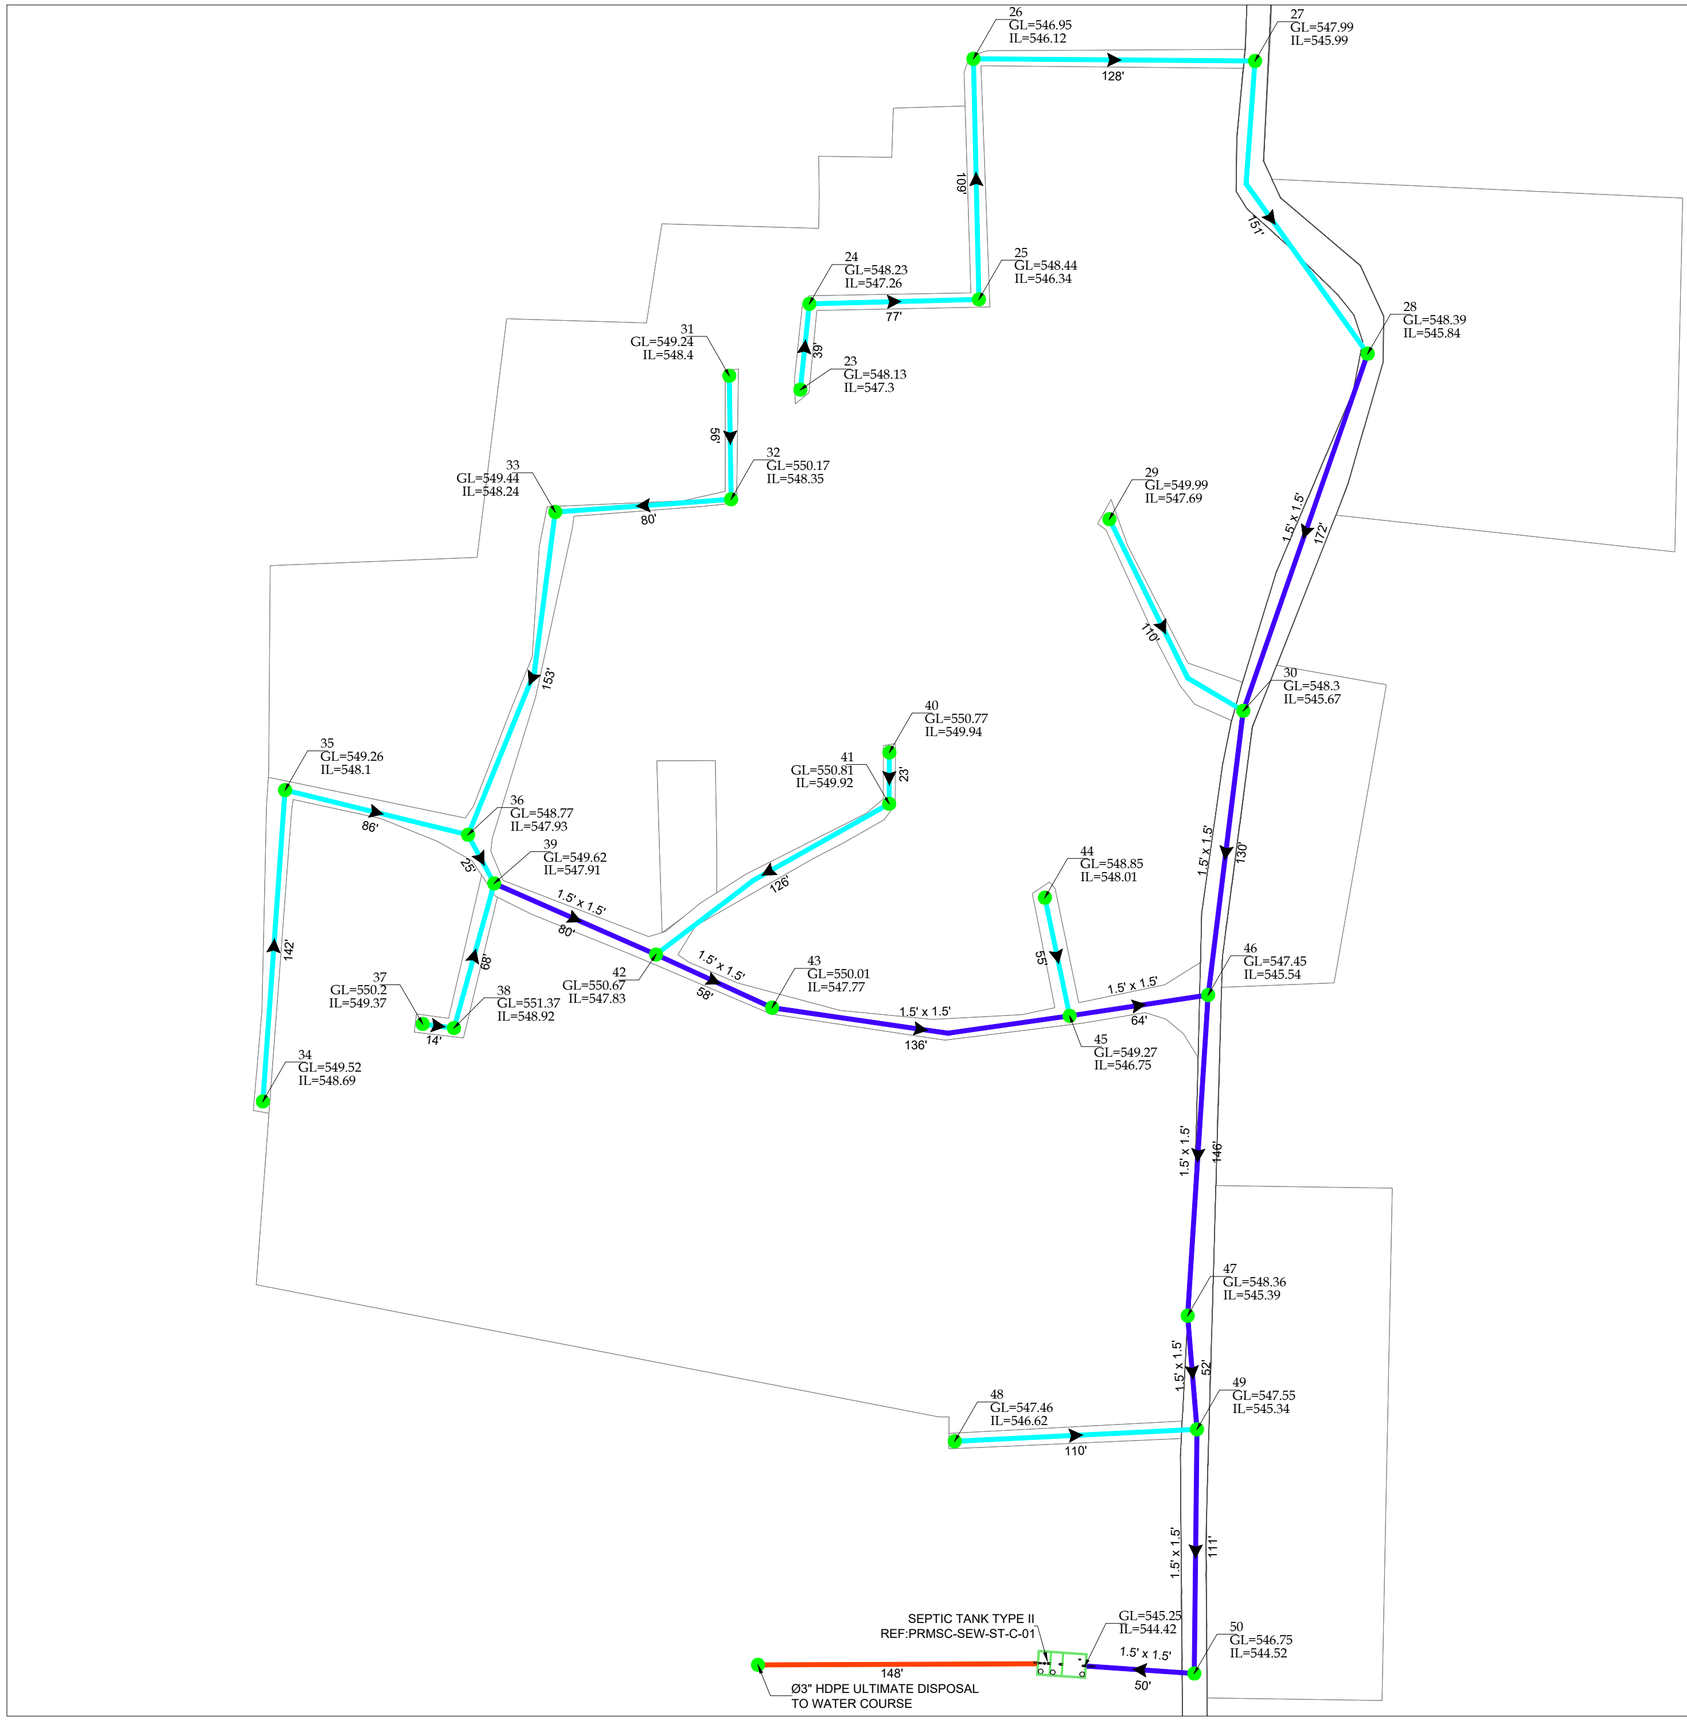

N
W
E
S



KEY PLAN

LEGEND:

- DRAIN TYPE - I
- SULLAGE CARRIER
- Ø3" HDPE PIPE
- EXISTING SOLING
- METALLED ROAD
- BOUNDARY

VILLAGE: SHER SINGH WALA (BWN)

TITLE.

DRAINAGE SYSTEM LAYOUT PLAN-12

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	23-05-2026	DETAILED DESIGN	MUNEEB	ENGR FAIEZ	ENGR IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING N°:

PRMSC-BWN-SSW-SEW-LP-12

SHEET 12 OF 12

REV 01

PROJECT:

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:

PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

PRMSC-BWN-SSW-SEW-LP-12

HYDRAULIC STATEMENT

Node		Length	Slope	Elevation Ground	Elevation Ground	Elevation Invert	Elevation Invert	Depth
FROM	TO	ft	ft/ft	U/S	D/S	U/S	D/S	ft
1	3	56	0.001	549.9	550.41	549.07	549.01	0.83
2	3	44	0.002	551.98	550.41	549.66	549.57	2.32
3	4	65	0.001	550.41	551.38	549.01	548.95	1.4
4	9	80	0.001	551.38	550.5	548.95	548.87	2.43
5	6	63	0.002	551.96	551.51	550.81	550.68	1.15
6	8	105	0.002	551.51	550.33	549.71	549.5	1.8
7	8	67	0.002	550.58	550.33	549.63	549.5	0.95
8	9	18	0.001	550.33	550.5	549.5	549.48	0.83
9	11	21	0.001	550.5	550.34	548.87	548.85	1.63
10	11	141	0.002	551.77	550.34	549.79	549.51	1.98
11	14	113	0.001	550.34	549.78	548.85	548.73	1.49
12	14	195	0.00183	550.14	549.78	549.31	548.95	0.83
13	14	174	0.002	552.53	549.78	549.3	548.95	3.23
14	16	78	0.002	549.78	548.77	548.09	547.93	1.69
15	16	138	0.001	548.2	548.77	547.37	547.23	0.83
16	18	44	0.001	548.77	548.72	547.23	547.19	1.54
17	18	113	0.002	551.36	548.72	548.11	547.89	3.25
18	21	66	0.001	548.72	548.93	547.19	547.12	1.53
19	20	52	0.002	550.48	548.1	547.37	547.27	3.11
20	21	116	0.00128	548.1	548.93	547.27	547.12	0.83
21	22	127	0.001	548.93	548.9	547.12	547	1.81
22	ST Type - II	45	0.001	548.9	548.18	547	546.95	1.9
23	24	39	0.001	548.13	548.23	547.3	547.26	0.83
24	25	77	0.001	548.23	548.44	547.26	547.18	0.97
25	26	109	0.002	548.44	546.95	546.34	546.12	2.1
26	27	128	0.001	546.95	547.99	546.12	545.99	0.83
27	28	151	0.001	547.99	548.39	545.99	545.84	2
28	30	172	0.001	548.39	548.3	545.84	545.67	2.55
29	30	110	0.002	549.99	548.3	547.69	547.47	2.3
30	46	130	0.001	548.3	547.45	545.67	545.54	2.63
31	32	56	0.001	549.24	550.17	548.4	548.35	0.84
32	33	80	0.00135	550.17	549.44	548.35	548.24	1.82
33	36	153	0.002	549.44	548.77	548.24	547.93	1.2
34	35	142	0.00184	549.52	549.26	548.69	548.43	0.83
35	36	86	0.002	549.26	548.77	548.1	547.93	1.16
36	39	25	0.001	548.77	549.62	547.93	547.91	0.84
37	38	14	0.001	550.2	551.37	549.37	549.35	0.83
38	39	68	0.002	551.37	549.62	548.92	548.79	2.45

HYDRAULIC STATEMENT

Node		Length	Slope	Elevation Ground	Elevation Ground	Elevation Invert	Elevation Invert	Depth
FROM	TO	ft	ft/ft	U/S	D/S	U/S	D/S	ft
39	42	80	0.001	549.62	550.67	547.91	547.83	1.71
40	41	23	0.001	550.77	550.81	549.94	549.92	0.83
41	42	126	0.001	550.81	550.67	549.92	549.79	0.89
42	43	58	0.001	550.67	550.01	547.83	547.77	2.84
43	45	136	0.001	550.01	549.27	547.77	547.63	2.24
44	45	55	0.001	548.85	549.27	548.01	547.96	0.84
45	46	64	0.002	549.27	547.45	546.75	546.62	2.52
46	47	146	0.001	547.45	548.36	545.54	545.39	1.91
47	49	52	0.001	548.36	547.55	545.39	545.34	2.97
48	49	110	0.001	547.46	547.55	546.62	546.51	0.84
49	50	111	0.001	547.55	546.75	545.34	545.23	2.21
50	ST Type - II	50	0.002	546.75	545.25	544.52	544.42	2.23
51	54	163	0.002	553.6	550.59	550.08	549.75	3.52
52	53	60	0.001	550.3	551.14	549.47	549.41	0.83
53	54	96	0.001	551.14	550.59	549.41	549.32	1.73
54	56	130	0.001	550.59	551.98	549.32	549.19	1.27
55	56	63	0.00163	552.08	551.98	551.25	551.15	0.83
56	57	71	0.001	551.98	550.5	549.19	549.11	2.79
57	59	94	0.002	550.5	549.02	548.38	548.19	2.12
58	59	113	0.002	550.31	549.02	548.41	548.19	1.9
59	63	144	0.001	549.02	549.8	548.19	548.04	0.83
60	61	128	0.002	554.46	553.53	552.95	552.7	1.51
61	62	69	0.0013	553.53	553.5	552.7	552.61	0.83
62	63	227	0.016	553.5	549.8	552.61	548.97	0.89
63	65	166	0.001	549.8	550.47	548.04	547.88	1.76
64	65	153	0.002	552.34	550.47	549.94	549.64	2.4
65	72	61	0.001	550.47	549.69	547.88	547.82	2.59
66	67	52	0.001	555.69	556.15	554.86	554.81	0.83
67	69	96	0.002	556.15	555.18	554.54	554.35	1.61
68	69	42	0.001	555.03	555.18	554.2	554.16	0.83
69	71	173	0.002	555.18	552.95	552.46	552.12	2.72
70	71	158	0.001	551.6	552.95	550.77	550.61	0.83
71	72	214	0.002	552.95	549.69	549.29	548.86	3.66
72	73	177	0.001	549.69	550.13	547.82	547.64	1.87
73	75	319	0.001	550.13	549.73	547.64	547.32	2.49
74	75	194	0.03494	554.94	549.73	554.11	547.32	0.83
75	76	66	0.001	549.73	549.6	547.32	547.26	2.41
76	ST-Type IV	50	0.001	549.6	548.81	547.26	547.21	2.34

VILLAGE: SHER SINGH WALA (BWN)

TITLE.

HYDRAULIC STATEMENT

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	20-04-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. HSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº: PRMSC-BWN-SSW-SEW-HS-00 | SHEET 00 OF 00 | REV 00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT
ASIAN CONSULTING ENGINEERS www.asiancon.com

TOBI QAMAR-UD-DIN

KEY PLAN

Revenue Village: Tobi Qamar-Ud-Din-Main Sheet

Tibba Qamar Din

Mistrian di Bhaini

COMMUNAL SEPTIC TANK Plot Size=0.38 Marla

COMMUNAL SEPTIC TANK Plot Size=0.38 Marla

COMMUNAL SEPTIC TANK Plot Size=0.38 Marla

COMMUNAL SEPTIC TANK Plot Size=0.38 Marla

GL=526.35
IL=524.12

3" HDPE PIPE ULTIMATE DISPOSAL TO WATER COURSE

SEPTIC TANK-T1A Plot Size=1.15 Marla

COMMUNAL SEPTIC TANK Plot Size=0.38 Marla

COMMUNAL SEPTIC TANK Plot Size=0.38 Marla

COMMUNAL SEPTIC TANK Plot Size=0.38 Marla

COMMUNAL SEPTIC TANK Plot Size=0.38 Marla

N

District:	Bahawalnagar
Tehsil:	Bahawalnagar
Revenue Village:	Tobi Qamar-Ud-Din

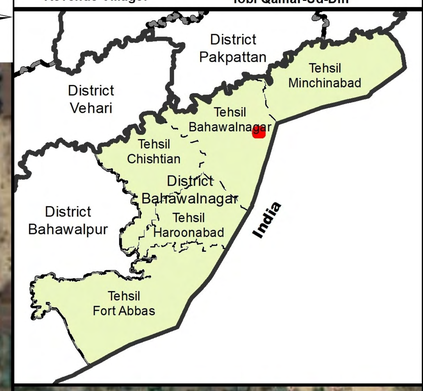

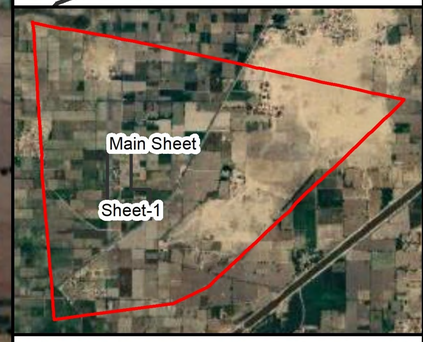

Title:
Proposed Drainage Network Plan

Legend:

- SETTLEMENT
- NODE
- 3" HDPE PIPE
- DRAIN TYPE-1
- SEPTIC TANK
- SETTLEMENT BOUNDARY

Drain Type 1=4876 Rft

Scale: 1:6,900
1 inch = 575 feet
Paper Size: A3

0 40 80 160
Kilometers

Project:
Engineering Design & Construction Supervision, Punjab Rural Sustainable Water Supply & Sanitation Project, Cluster South III

PRWSC
ENVIRONMENTAL TECHNOLOGIES
ASIAN CONSULTING ENGINEERS www.asiancon.com

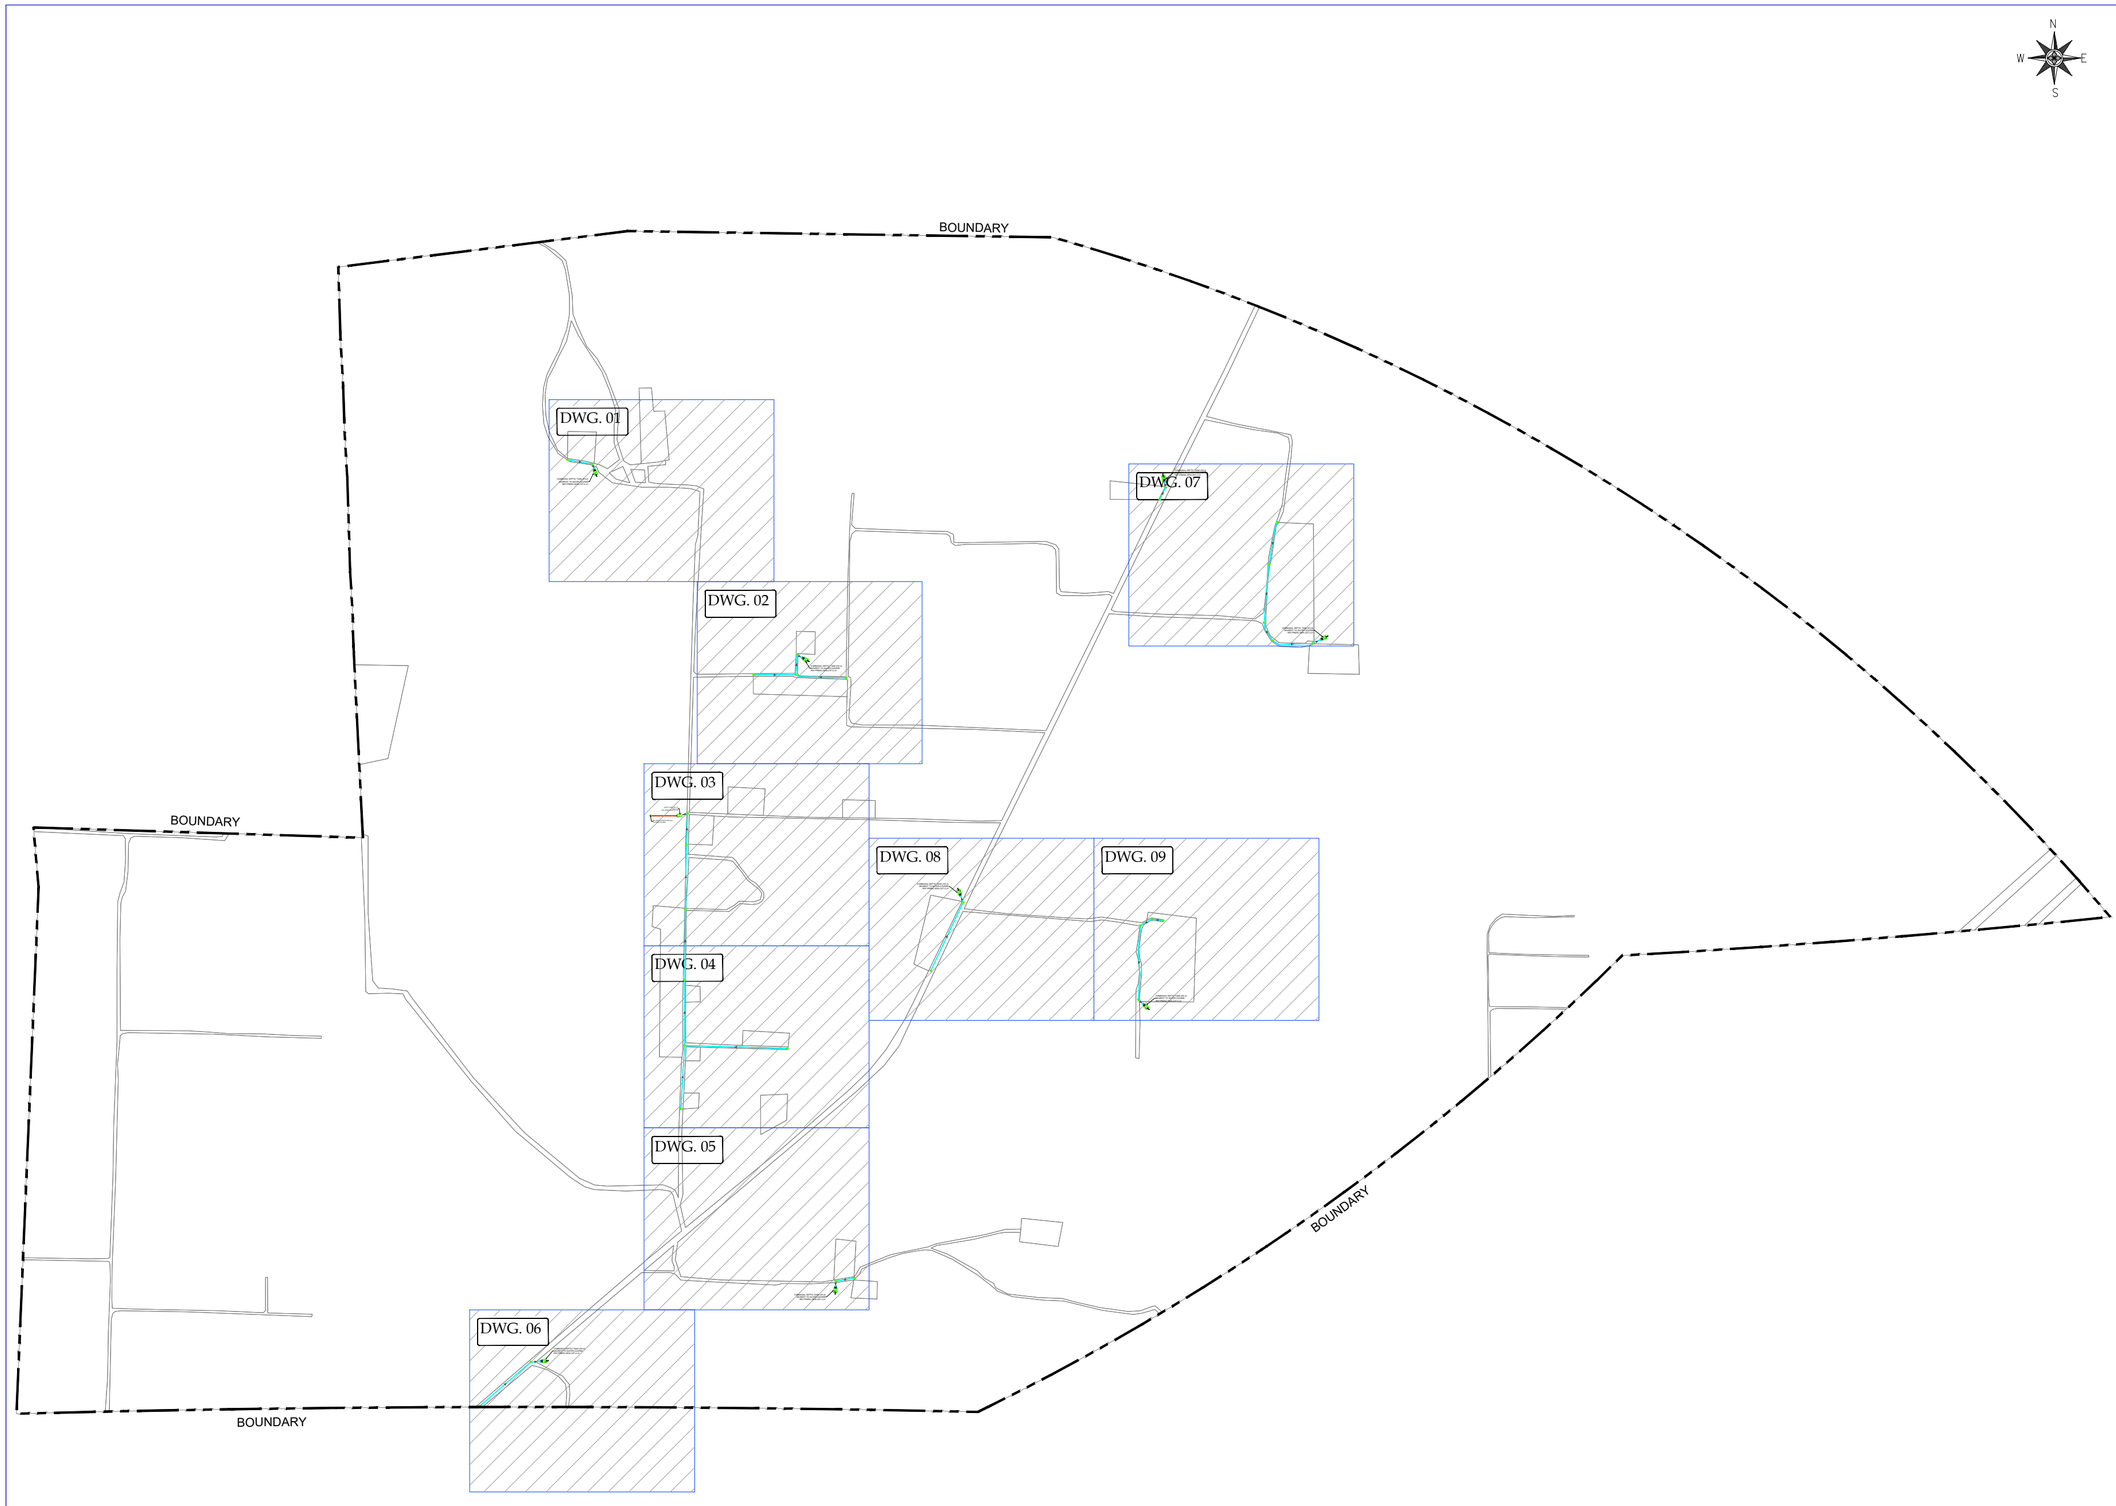

LEGEND:

- DRAIN TYPE - I
- Ø3" HDPE PIPE
- BOUNDARY

VILLAGE: TOBI QAMAR UD DIN (BWN)

TITLE:

DRAINAGE SYSTEM KEY PLAN

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 850'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	20-04-2026	DETAILED DESIGN	MUNEEB	ENGR FAIEZ	ENGR IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº: PRMSC-BWN-TQB-SEW-KP-00

SHEET 00 OF 00

REV 00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT
ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

PRMSC-BWN-TQD-SEW-KP-00

LAYOUT PLAN

Revenue Village: Tobi Qamar-Ud-Din Sheet-1

GL=526.35
IL=524.12

6" HDPE PIPE ULTIMATE DISPOSAL TO WATER COURSE

112'

SEPTIC TANK-T1A
Plot Size=1.15 Marla

ND-30
GL=527.93
IL=524.15

133'

ND-29
GL=525.11
IL=524.29

275'

ND-28
GL=528.69
IL=524.83

ND-27
GL=530.07
IL=528.46

260'

ND-26
GL=530.7
IL=529.55

460'

ND-24
GL=530.82
IL=529.99

457'

ND-25
GL=531.39
IL=530.41

N

District: Bahawalnagar
Tehsil: Bahawalnagar
Revenue Village: Tobi Qamar-Ud-Din

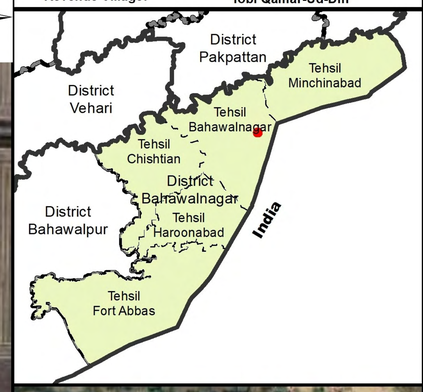

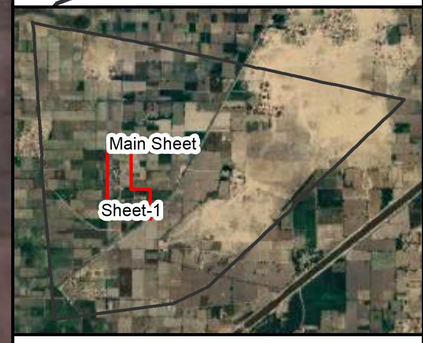

Title:
Proposed Drainage Network Plan

Legend:

- NODE
- 6" uPVC PIPE
- DRAIN TYPE-1
- SEPTIC TANK
- SETTLEMENT BOUNDARY

Drain Type 1=4876 Rft

Scale: 1:1,600
1 inch = 133 feet
Paper Size: A3

0 40 80 160
Kilometers

Project:
Engineering Design & Construction Supervision, Punjab Rural Sustainable Water Supply & Sanitation Project, Cluster South III

PRWSC
ENVIRONMENTAL TECHNOLOGIES
ASIAN CONSULTING ENGINEERS www.asiancon.com

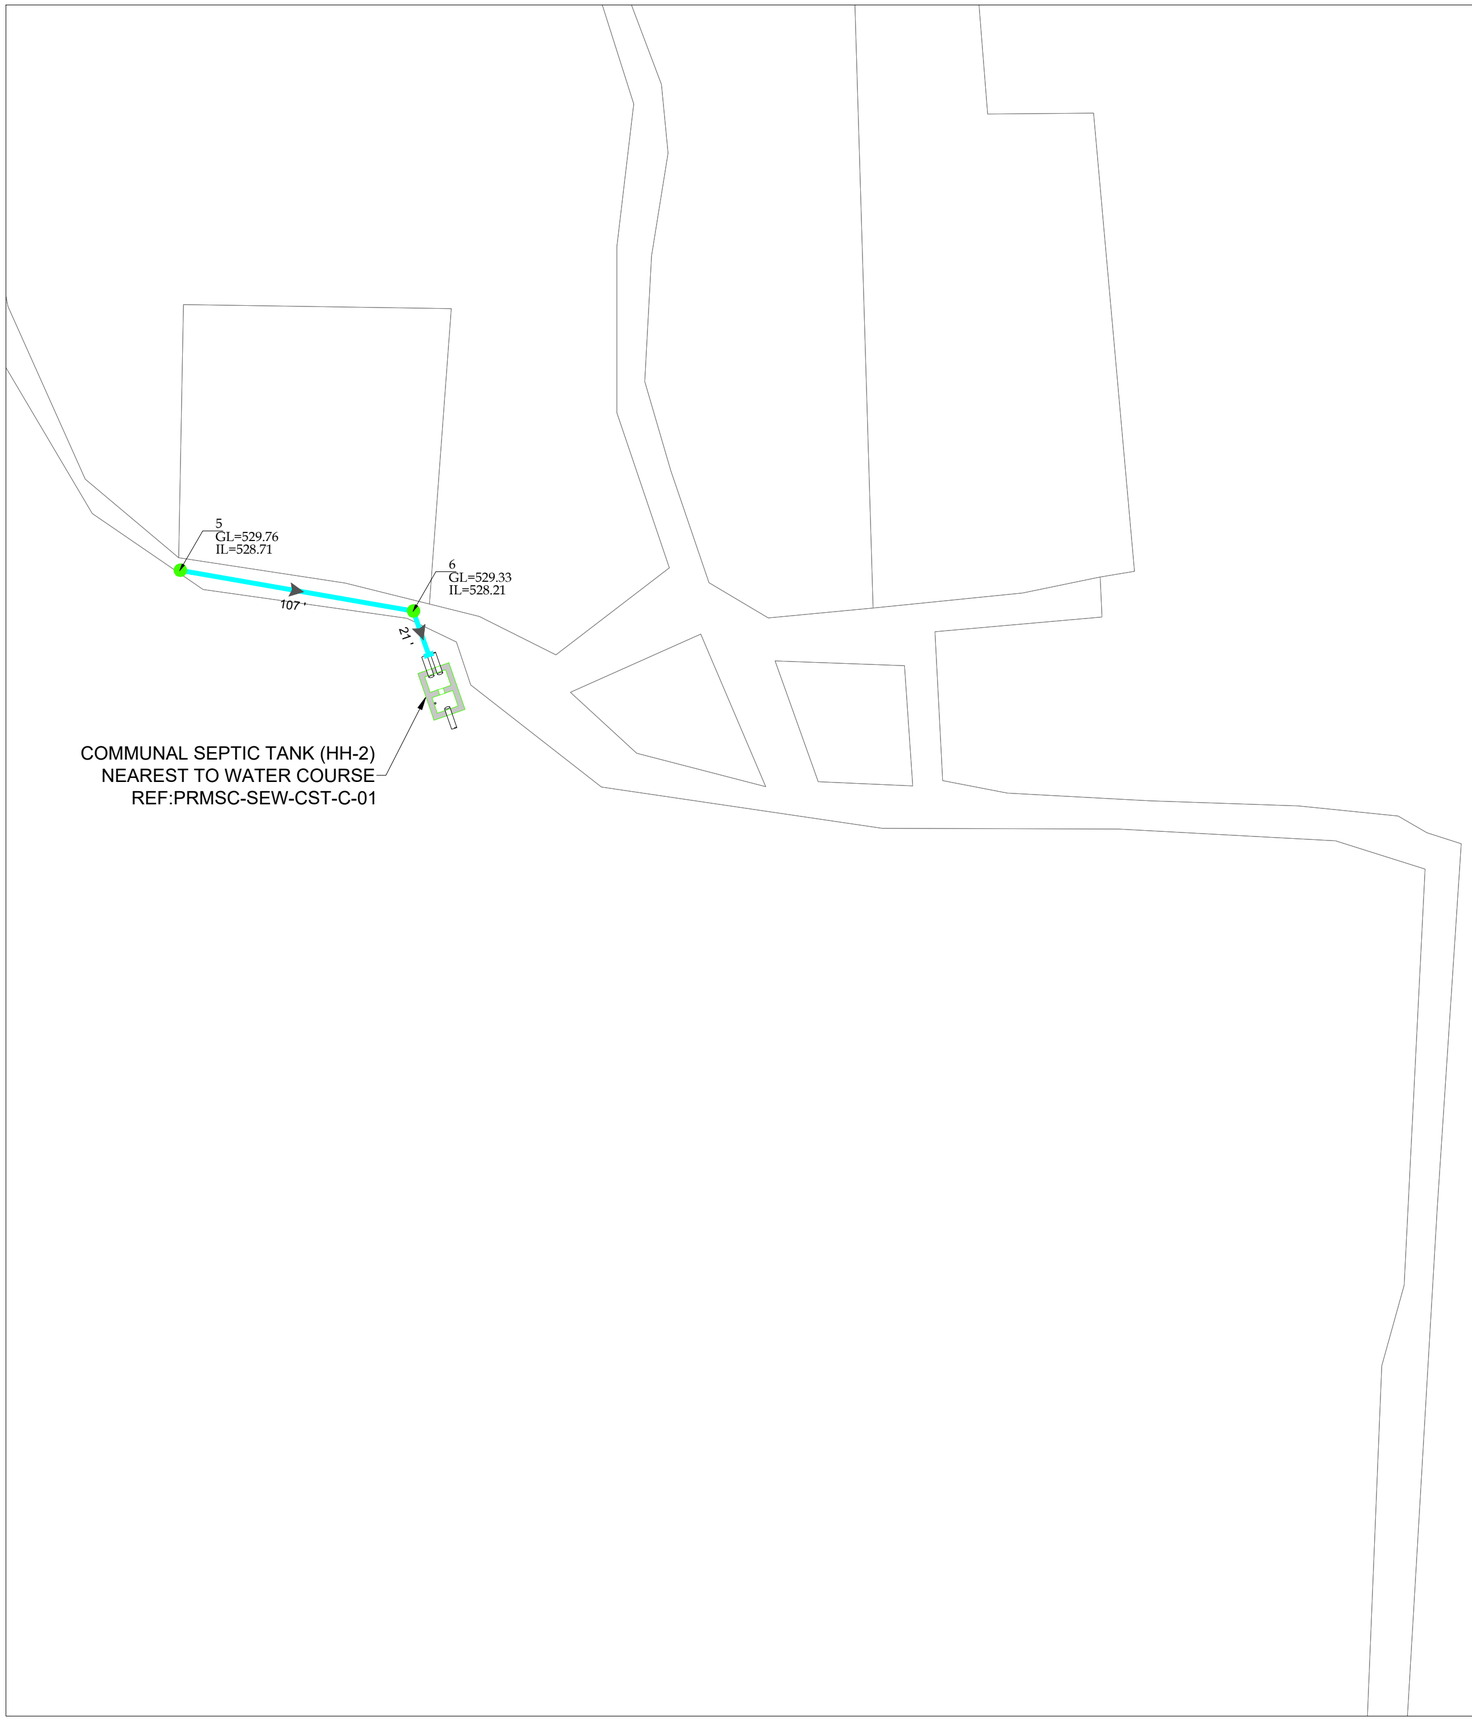

N
W
E
S



KEY PLAN

LEGEND:

DRAIN TYPE - I

Ø3" HDPE PIPE

BOUNDARY

VILLAGE: TOBI QAMAR UD DIN (BWN)

TITLE.

DRAINAGE SYSTEM LAYOUT PLAN-01

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	20-04-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº: PRMSC-BWN-TQD-SEW-LP-01

SHEET 01 OF 09

REV 00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:
ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

PRMSC-BWN-TQD-SEW-LP-01

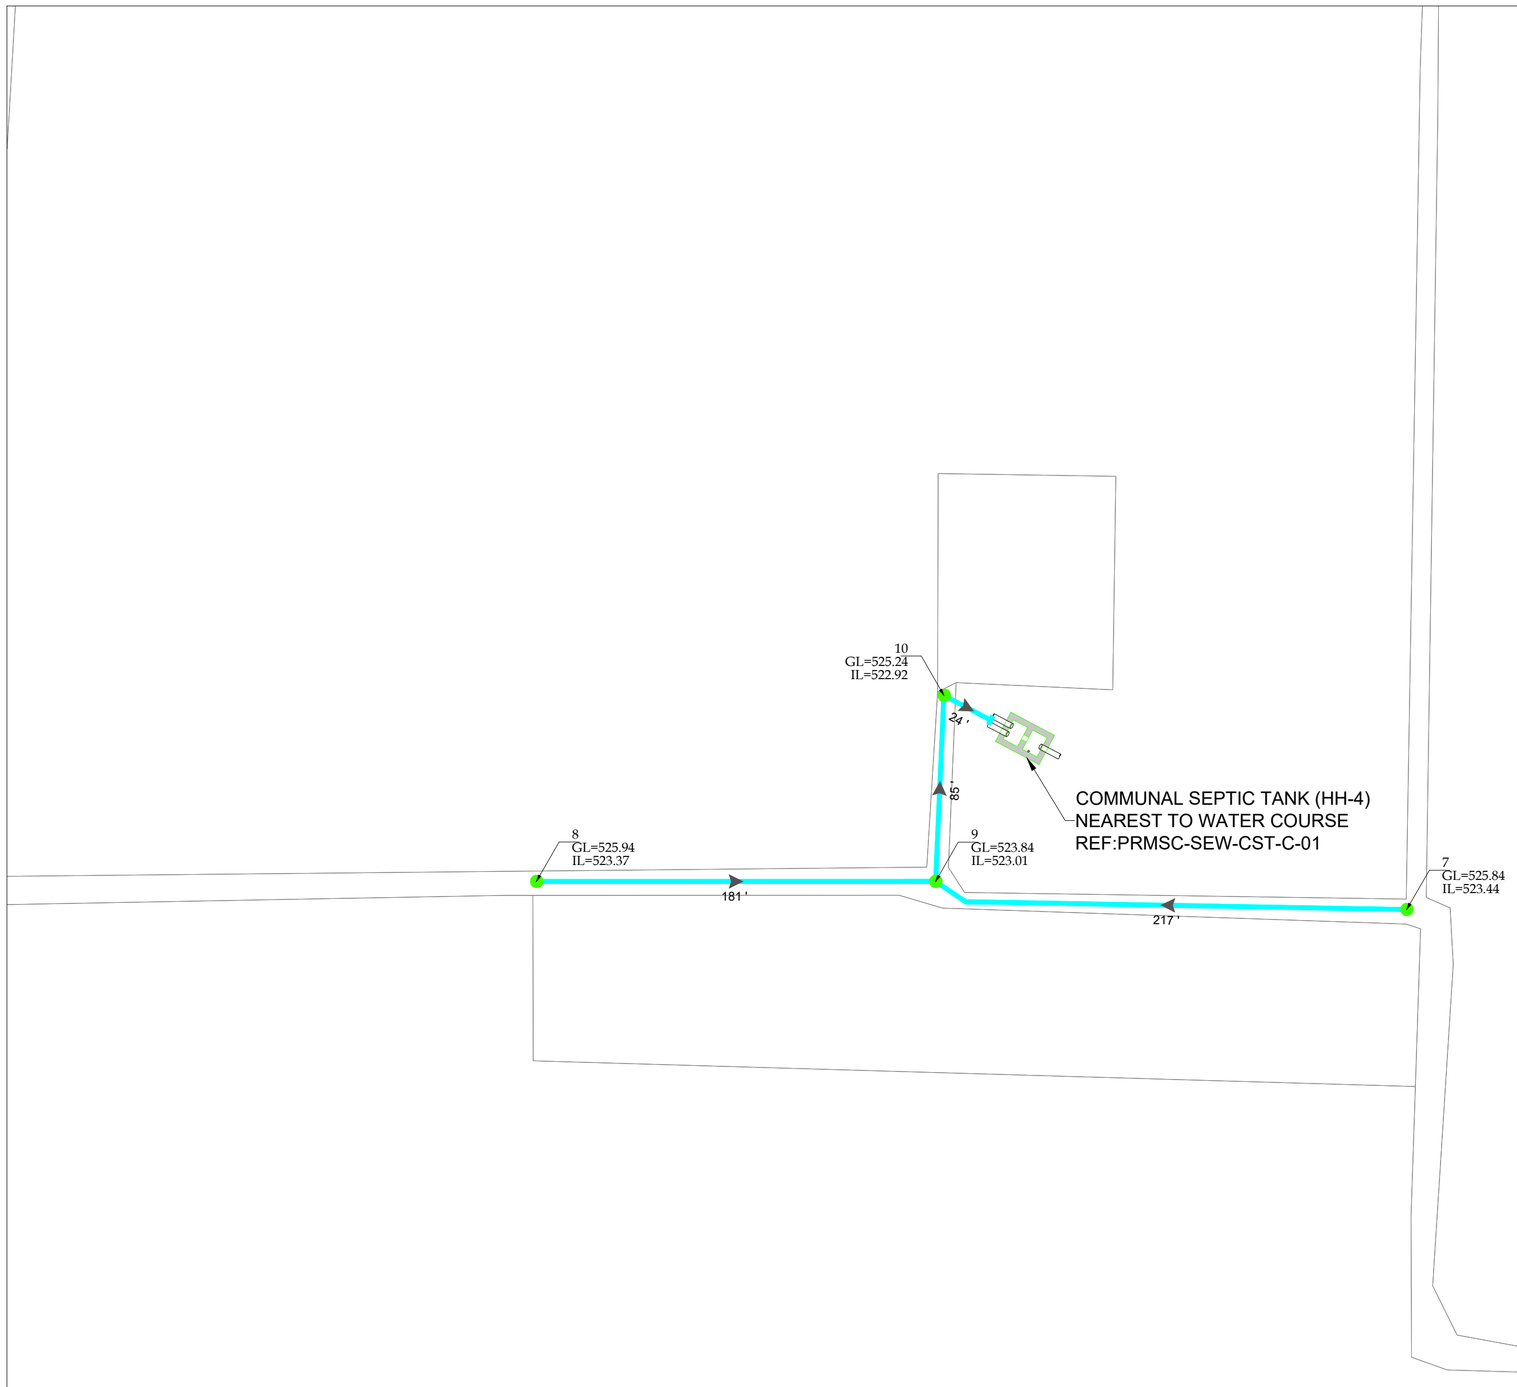

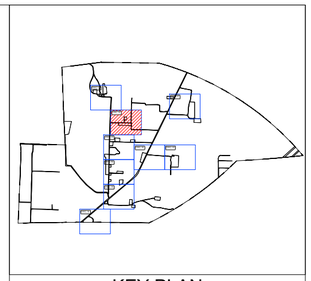

KEY PLAN

LEGEND:

DRAIN TYPE - I

Ø3" HDPE PIPE

BOUNDARY

VILLAGE: TOBI QAMAR UD DIN (BWN)

TITLE.

DRAINAGE SYSTEM LAYOUT PLAN-02

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	20-04-2026	DETAILED DESIGN	MUNEEB	ENGR FAIEZ	ENGR IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº: PRMSC-BWN-TQD-SEW-LP-02

SHEET 02 OF 09

REV 00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:
ASIAN CONSULTING ENGINEERS
www.asiaecon.com.jv

PRMSC-BWN-TQD-SEW-LP-02



KEY PLAN

LEGEND:

DRAIN TYPE - I

Ø3" HDPE PIPE

BOUNDARY

VILLAGE: TOBI QAMAR UD DIN (BWN)

TITLE.

DRAINAGE SYSTEM LAYOUT PLAN-03

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	20-04-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-TQD-SEW-LP-03	03 OF 09	00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

PRMSC-BWN-TQD-SEW-LP-03

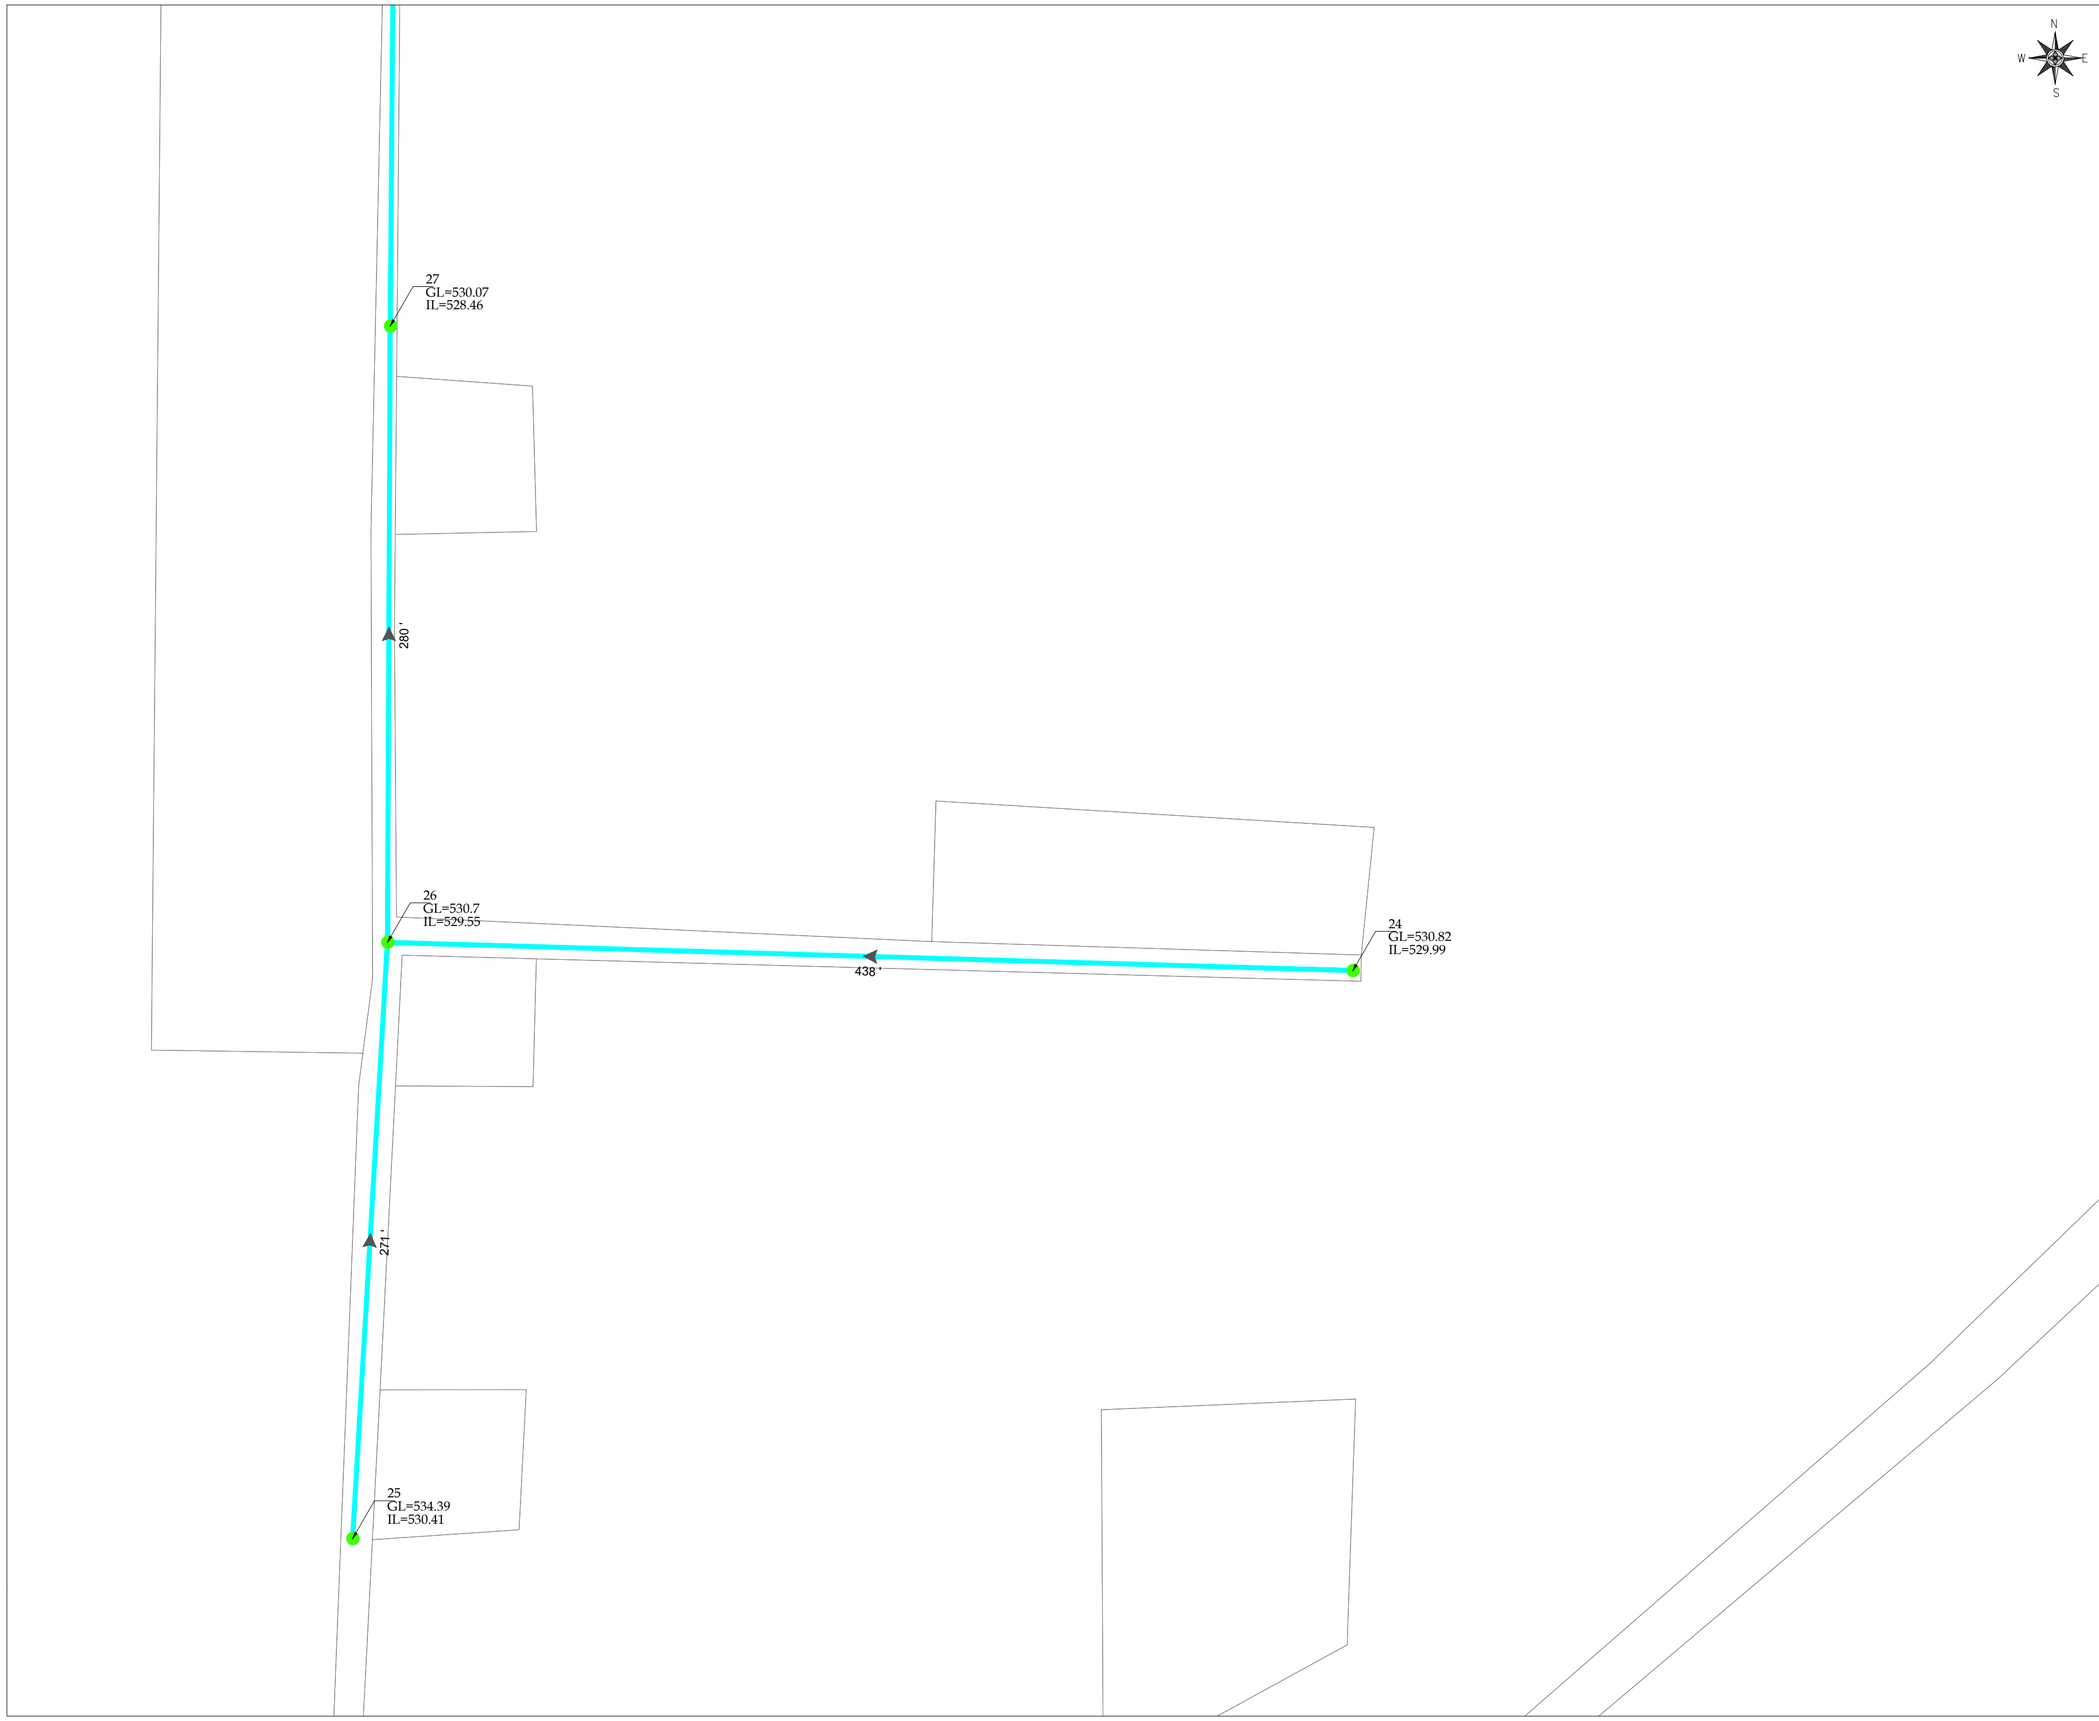



KEY PLAN

LEGEND:

DRAIN TYPE - I

Ø3" HDPE PIPE

BOUNDARY

VILLAGE: TOBI QAMAR UD DIN (BWN)

TITLE.

DRAINAGE SYSTEM LAYOUT PLAN-04

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	D E S C R I P T I O N	DRAWN	DESIGNED	APPROVED
01	20-04-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº: PRMSC-BWN-TQD-SEW-LP-04

SHEET 04 OF 09

REV 00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:
ASIAN CONSULTING ENGINEERS JV
www.asiancon.com.pk

PRMSC-BWN-TQD-SEW-LP-04



KEY PLAN

LEGEND:

DRAIN TYPE - I

Ø3" HDPE PIPE

BOUNDARY

4
GL=528.23
IL=525.54

80 '

21 '

3
GL=529.86
IL=527.55

COMMUNAL SEPTIC TANK (HH-3)
NEAREST TO WATER COURSE
REF:PRMSC-SEW-CST-C-01

VILLAGE: TOBI QAMAR UD DIN (BWN)

TITLE.

DRAINAGE SYSTEM LAYOUT PLAN-05

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	20-04-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:

PRMSC-BWN-TQD-SEW-LP-05

SHEET 05 OF 09

REV 00

PROJECT:

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:

PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS

www.asiancon.com.pk

PRMSC-BWN-TQD-SEW-LP-05

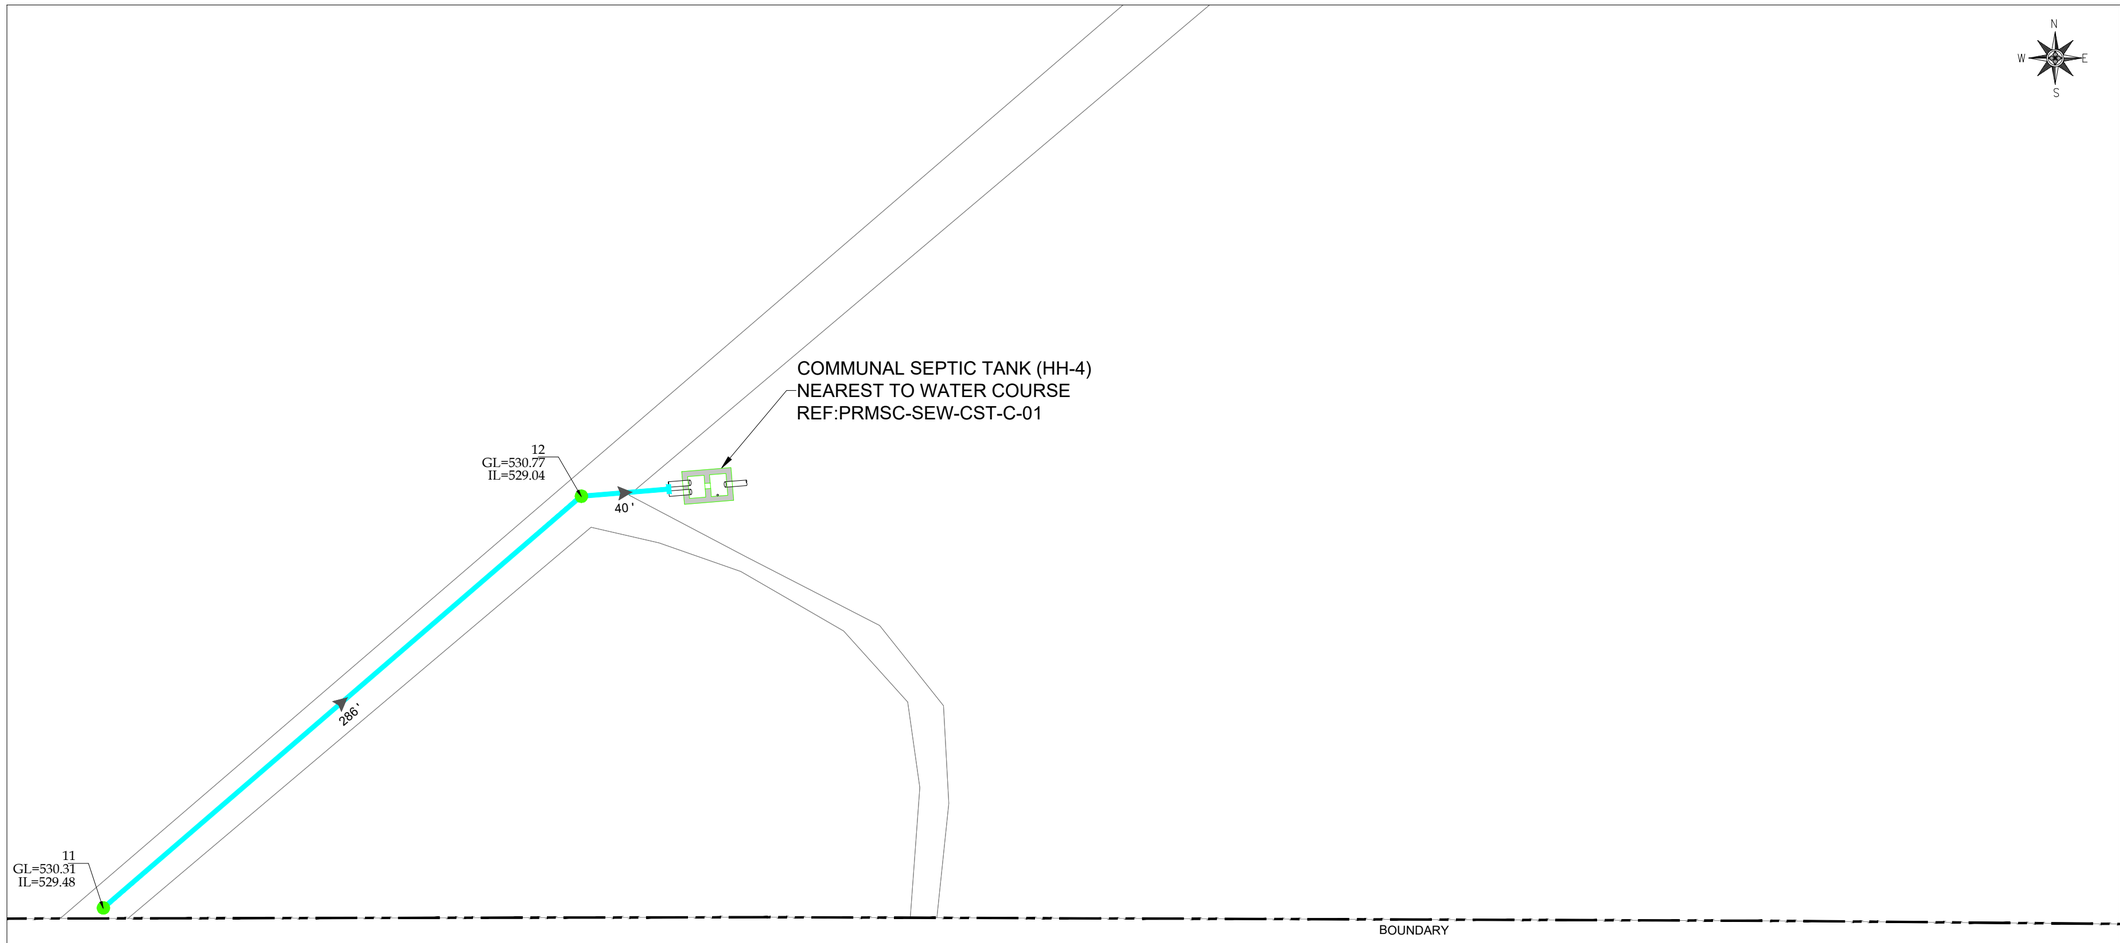



KEY PLAN

LEGEND:

DRAIN TYPE - I

Ø3" HDPE PIPE

BOUNDARY

VILLAGE: TOBI QAMAR UD DIN (BWN)

TITLE.

DRAINAGE SYSTEM LAYOUT PLAN-06

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	20-04-2026	DETAILED DESIGN	MUNEEB	ENGR FAIEZ	ENGR IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-BWN-TQD-SEW-LP-06	06 OF 09	00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS
www.asiacon.com.pk JV

PRMSC-BWN-TQD-SEW-LP-06

COMMUNAL SEPTIC TANK (HH-3)
NEAREST TO WATER COURSE
REF:PRMSC-SEW-CST-C-01

1
GL=523.27
IL=522.09

58 '

2
GL=522.81
IL=521.58

23 '

19
GL=528.68
IL=527.85

187 '

20
GL=528.67
IL=527.66

248 '

21
GL=528.44
IL=527.41

89 '

22
GL=528.47
IL=526.01

177 '

23
GL=526.49
IL=523.11

36 '

COMMUNAL SEPTIC TANK (HH-8)
NEAREST TO WATER COURSE
REF:PRMSC-SEW-CST-C-01

N
W
E
S



KEY PLAN

LEGEND:

DRAIN TYPE - I
Ø3" HDPE PIPE
BOUNDARY

VILLAGE: TOBI QAMAR UD DIN (BWN)

TITLE.

DRAINAGE SYSTEM LAYOUT PLAN-07

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	20-04-2026	DETAILED DESIGN	MUNEEB	ENGR FAIEZ	ENGR IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº: PRMSC-BWN-TQD-SEW-LP-07

SHEET 07 OF 09

REV 00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

PRMSC-BWN-TQD-SEW-LP-07

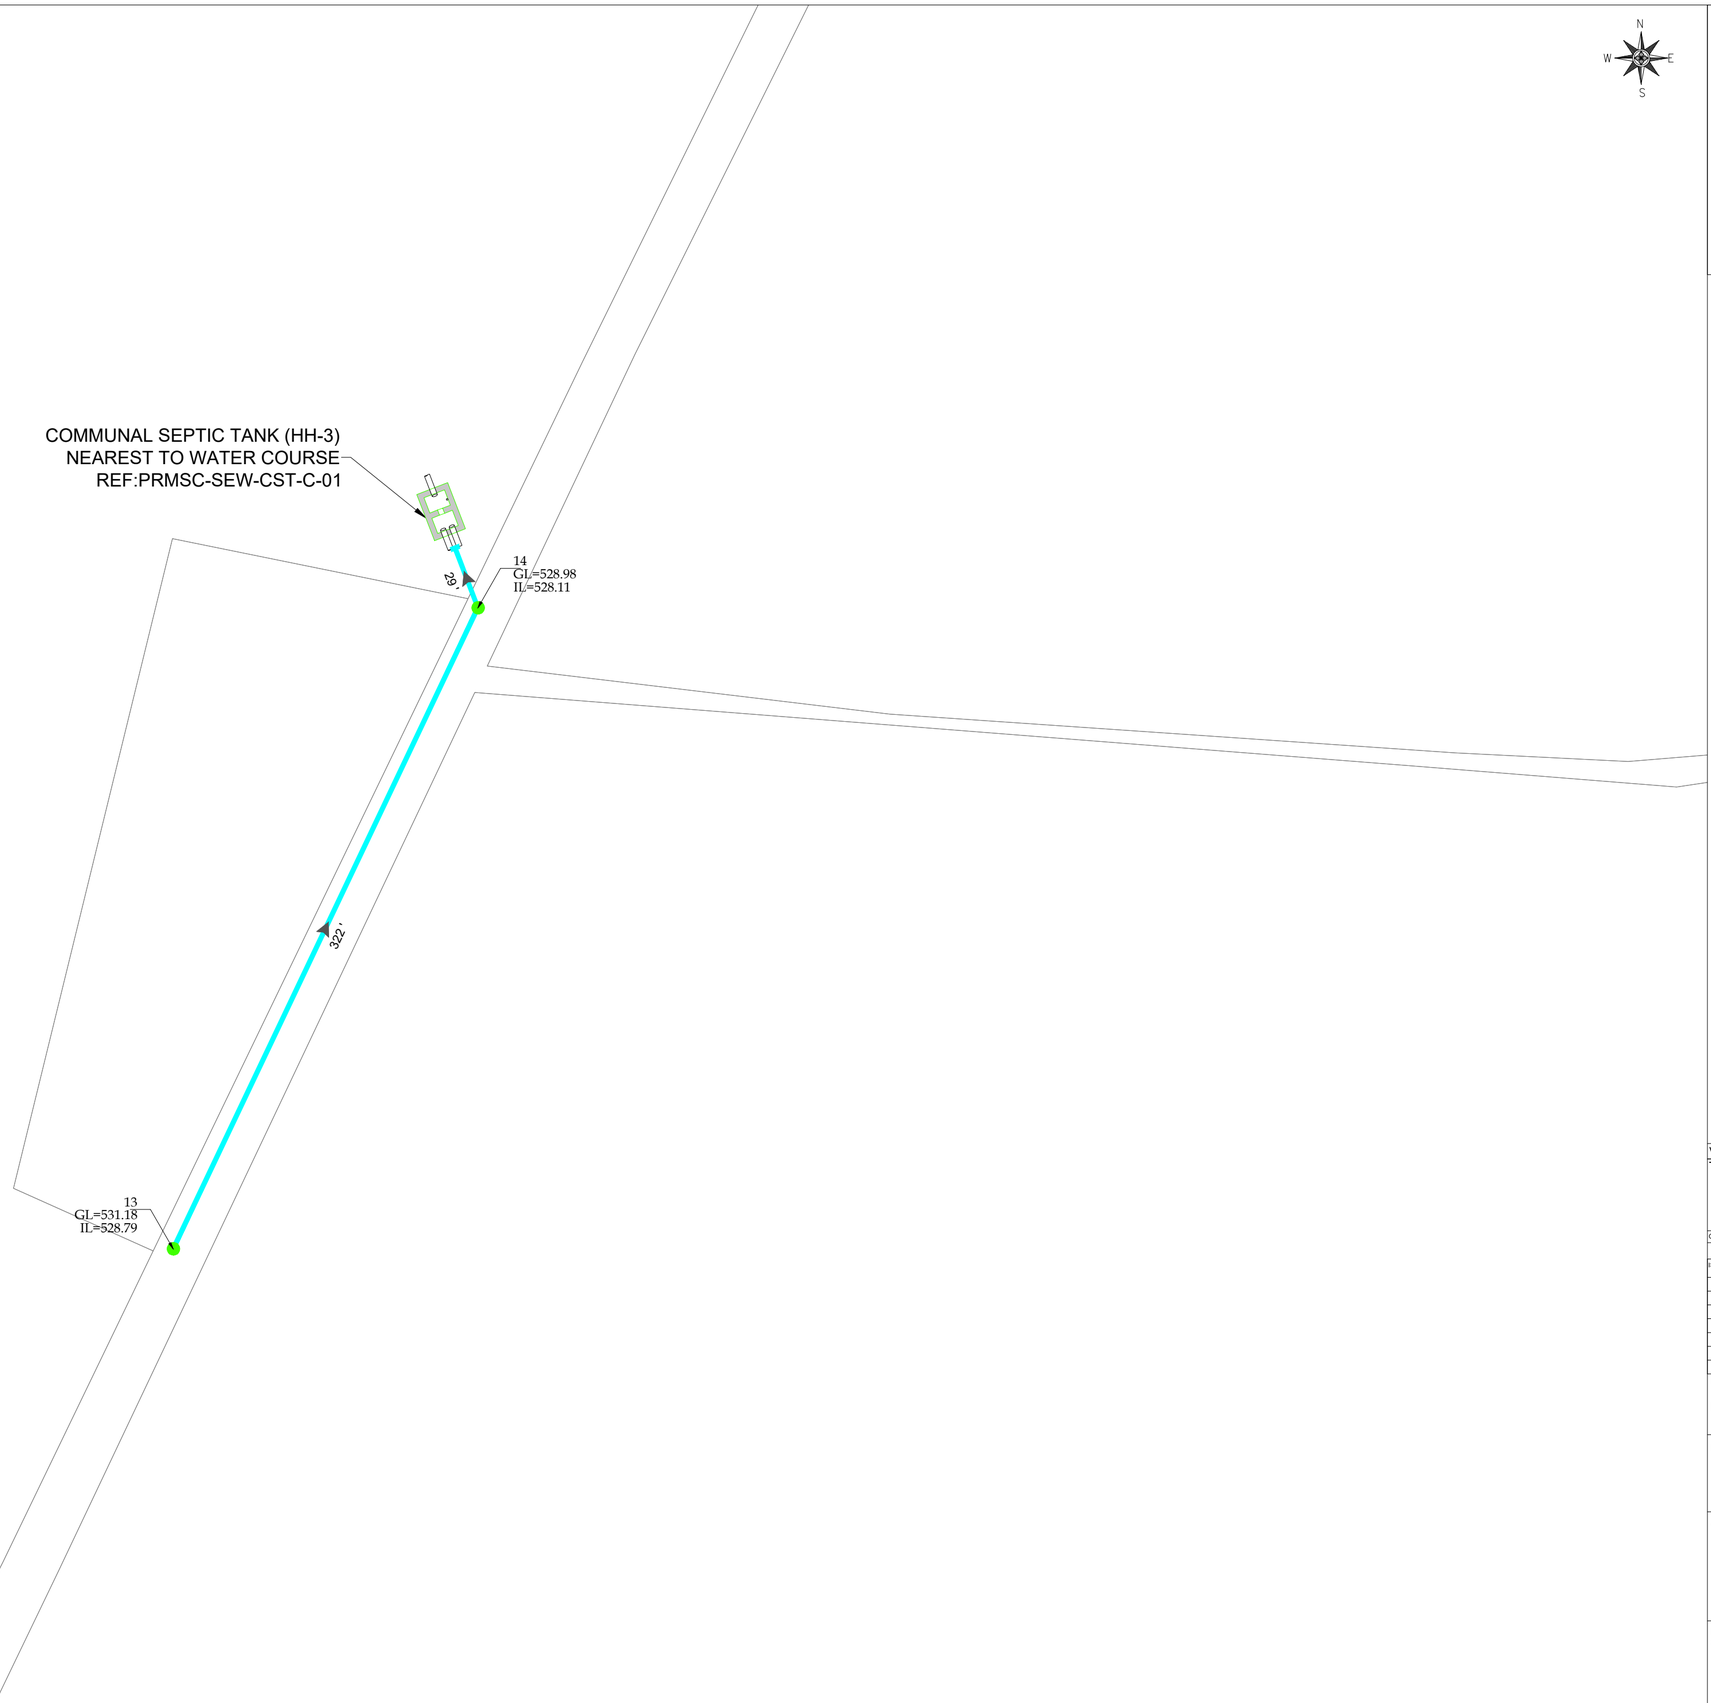



KEY PLAN

LEGEND:

DRAIN TYPE - I

Ø3" HDPE PIPE

BOUNDARY

VILLAGE: TOBI QAMAR UD DIN (BWN)

TITLE.

DRAINAGE SYSTEM LAYOUT PLAN-08

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	20-04-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº: PRMSC-BWN-TQD-SEW-LP-08

SHEET 08 OF 09

REV 00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS
www.asiacon.com.pv

PRMSC-BWN-TQD-SEW-LP-08

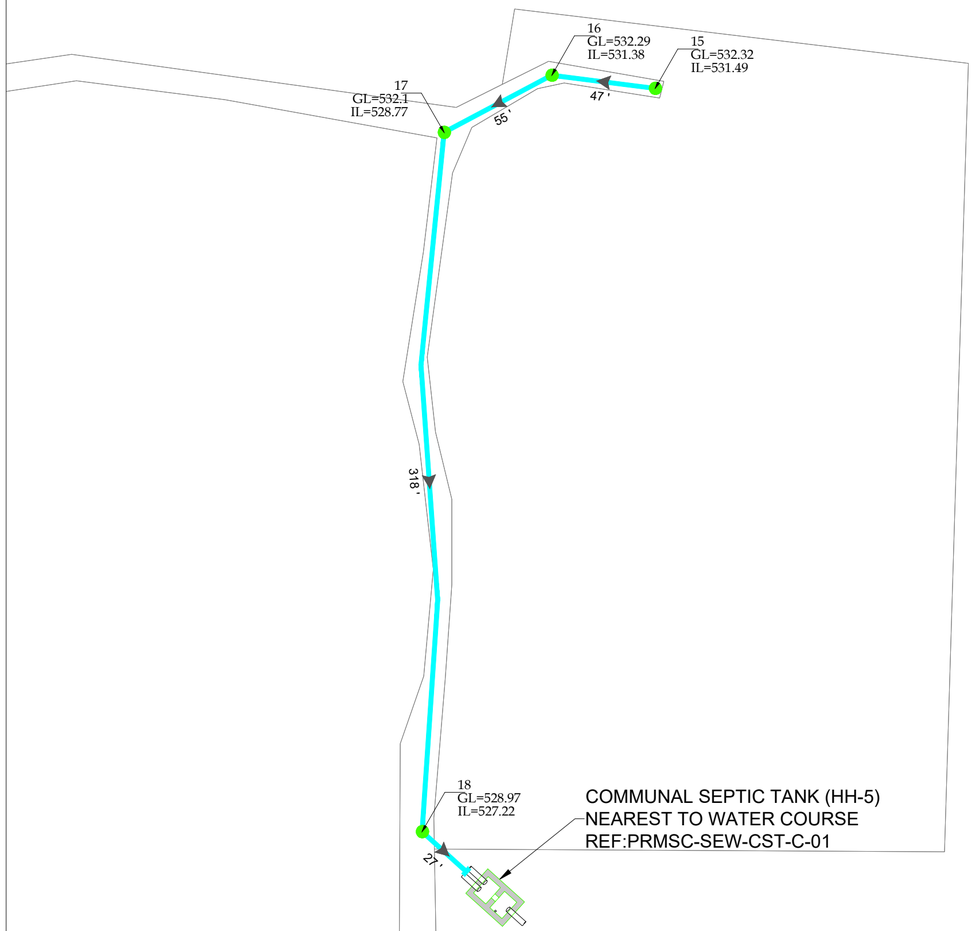

N
W
E
S



KEY PLAN

LEGEND:

DRAIN TYPE - I

Ø3" HDPE PIPE

BOUNDARY

VILLAGE: TOBI QAMAR UD DIN (BWN)

TITLE.

DRAINAGE SYSTEM LAYOUT PLAN-09

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 50'

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	20-04-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº: PRMSC-BWN-TQD-SEW-LP-09

SHEET 09 OF 09

REV 00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

PRMSC-BWN-TQD-SEW-LP-09

HYDRAULIC STATEMENT								
Node		Length	Slope	Elevation Ground	Elevation Ground	Elevation Invert	Elevation Invert	Depth
FROM	TO	ft	ft/ft	U/S	D/S	U/S	D/S	ft
1	2	58	0.002	523.27	522.81	522.09	521.97	1.18
2	Communal Septic Tank (For 3 HH)	23	0.002	522.81	522.36	521.58	521.53	1.23
3	4	80	0.002	529.86	528.23	527.55	527.39	2.31
4	Communal Septic Tank (For 3 HH)	21	0.002	528.23	526.33	525.54	525.5	2.69
5	6	107	0.002	529.76	529.33	528.71	528.5	1.05
6	Communal Septic Tank (For 2 HH)	21	0.002	529.33	529	528.21	528.17	1.12
7	9	217	0.002	525.84	523.84	523.44	523.01	2.4
8	9	181	0.002	525.94	523.84	523.37	523.01	2.57
9	10	85	0.001	523.84	525.24	523.01	522.92	0.83
10	Communal Septic Tank (For 4 HH)	24	0.001	525.24	524.93	522.92	522.9	2.32
11	12	286	0.002	530.31	530.77	529.48	529.04	0.83
12	Communal Septic Tank (For 4 HH)	40	0.002	530.77	529.79	529.04	528.96	1.73
13	14	322	0.002	531.18	528.98	528.79	528.15	2.39
14	Communal Septic Tank (For 3 HH)	29	0.002	528.98	528.89	528.11	528.05	0.87
15	16	47	0.001	532.32	532.29	531.49	531.44	0.83
16	17	55	0.002	532.29	532.1	531.38	531.27	0.91
17	18	318	0.002	532.1	528.97	528.77	528.13	3.33
18	Communal Septic Tank (For 5 HH)	27	0.002	528.97	528	527.22	527.17	1.75
19	20	187	0.001	528.68	528.67	527.85	527.66	0.83
20	21	248	0.001	528.67	528.44	527.66	527.41	1.01
21	22	86	0.001	528.44	528.47	527.41	527.33	1.03
22	23	177	0.002	528.47	526.49	526.01	525.66	2.46
23	Communal Septic Tank (For 8 HH)	36	0.002	526.49	523.87	523.11	523.04	3.38
24	26	438	0.001	530.82	530.7	529.99	529.55	0.83
25	26	271	0.002	534.39	530.7	530.41	529.87	3.98
26	27	280	0.001	530.7	530.07	529.55	529.24	1.15
27	28	301	0.002	530.07	528.69	528.46	527.86	1.61
28	29	275	0.002	528.69	525.11	524.83	524.28	3.86
29	30	133	0.001	525.11	527.93	524.28	524.15	0.83
30	Septic Tank Type (1A)	26	0.001	527.93	526.35	524.15	524.12	3.78

VILLAGE: TOBI QAMAR UD DIN (BWN)

TITLE.

HYDRAULIC STATEMENT

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	20-04-2026	DETAILED DESIGN	MUNEEB	ENGR. FAIEZ	ENGR. HSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº: PRMSC-BWN-TQD-SEW-HS-01

SHEET 01 OF 01

REV 00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS
www.asianceb.com

PRMSC-BWN-TQD-SEW-HS-01

TYPICAL DETAILS

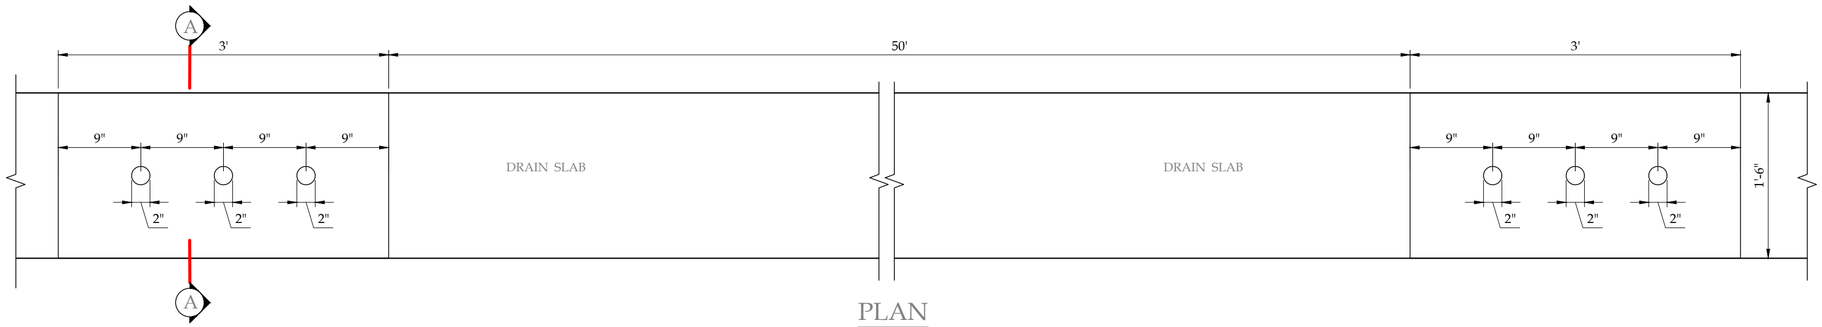

PLAN

SCALE:- 1" = 1'-0"

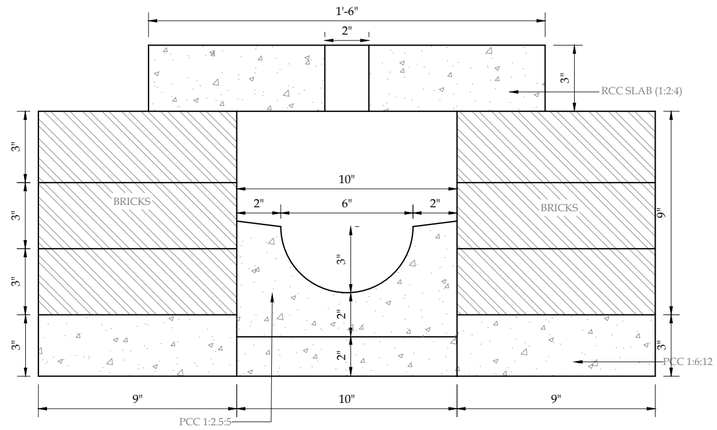

DRAIN TYPE - I
SECTION AT A-A
Scale :- 1:4

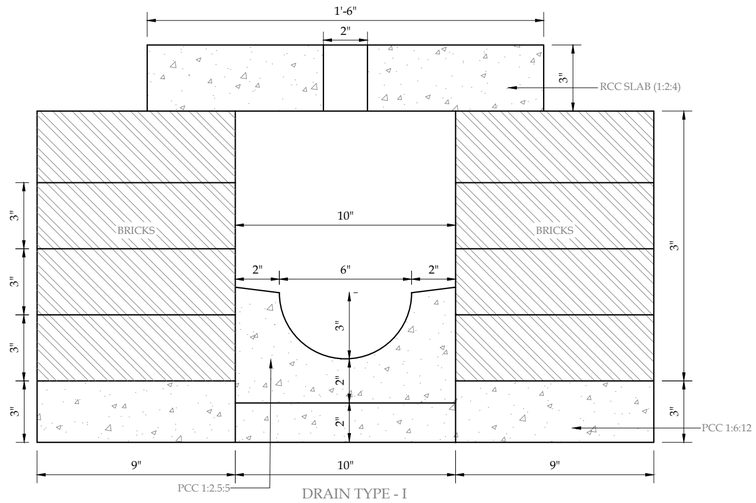

DRAIN TYPE - I
SECTION AT A-A
Scale :- 1:4



DRAIN TYPE - I
RPC SLAB
Scale :- 1:4

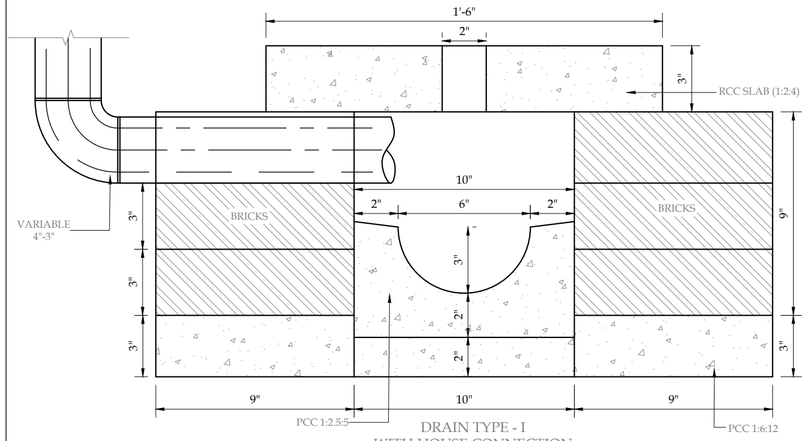

DRAIN TYPE - I
WITH HOUSE CONNECTION
SECTION AT A-A
Scale :- 1:4

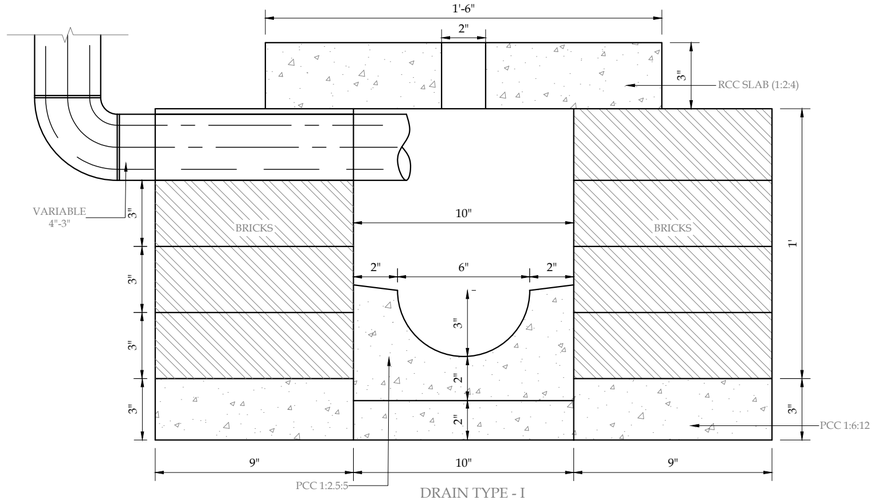

DRAIN TYPE - I
WITH HOUSE CONNECTION
SECTION AT A-A
Scale :- 1:4

SPECIAL NOTES:-

1. USE CONCRETE HAVING 3000 Psi CYLINDER STRENGTH FOR ALL STRUCTURAL MEMBERS.
2. USE DEFORMED STEEL HAVING MINIMUM YIELD STRENGTH OF 60,000 PSI AS PER ASTM 615

TITLE.

TYPICAL DETAILS DRAIN TYPE - I

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 1'-0"

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	29-08-2025	DETAILED DESIGN	ASAD	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING N°: PRMSC-SW-TD-04

SHEET

REV 00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:
ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

PRMSC-SW-TD-04

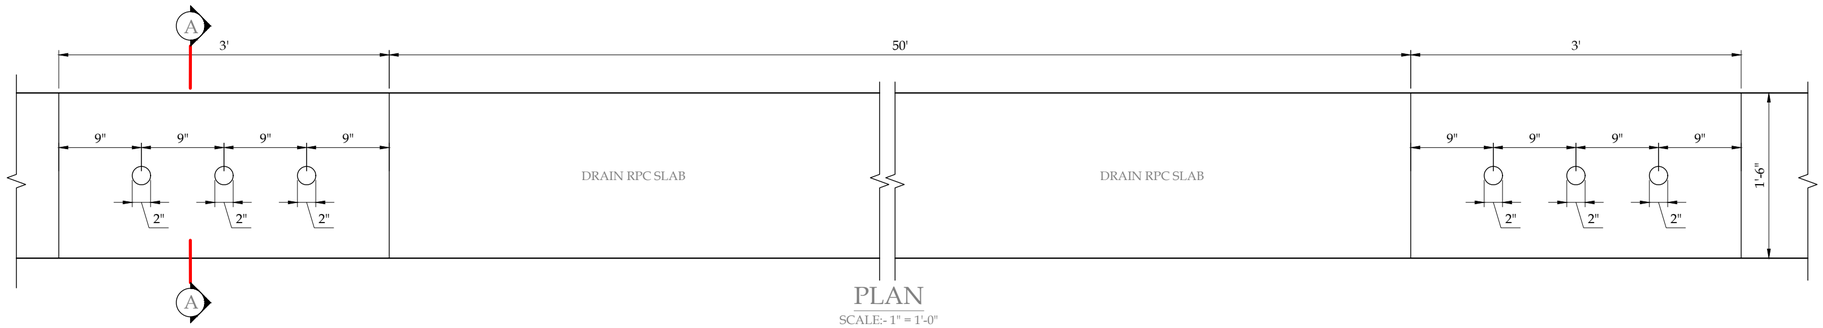

PLAN

SCALE:- 1" = 1'-0"

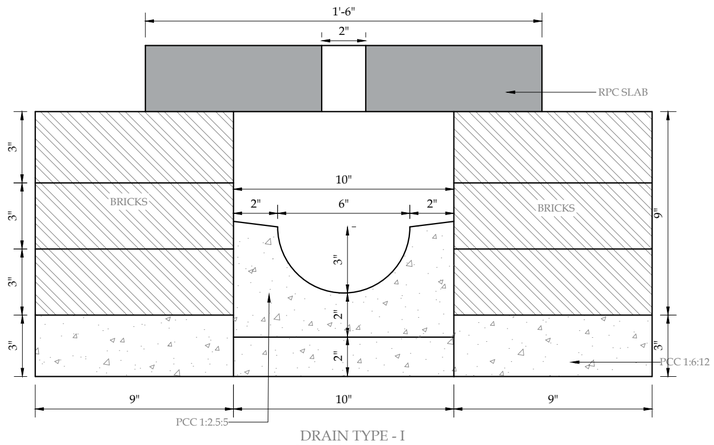

DRAIN TYPE - I
SECTION AT A-A
Scale :- 1:4

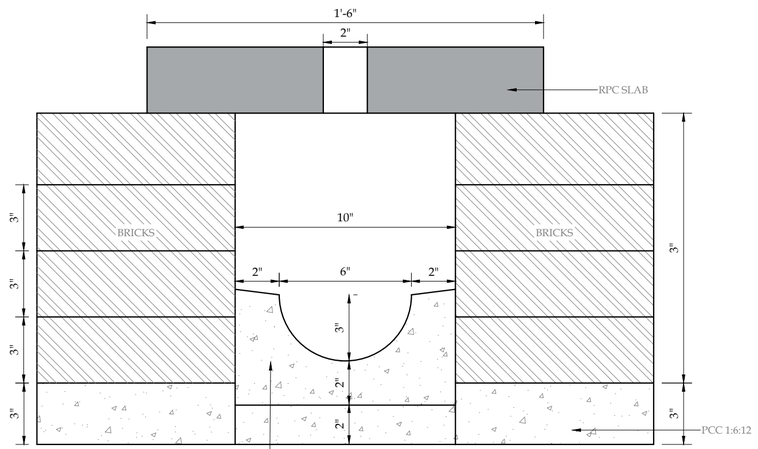

DRAIN TYPE - I
SECTION AT A-A
Scale :- 1:4

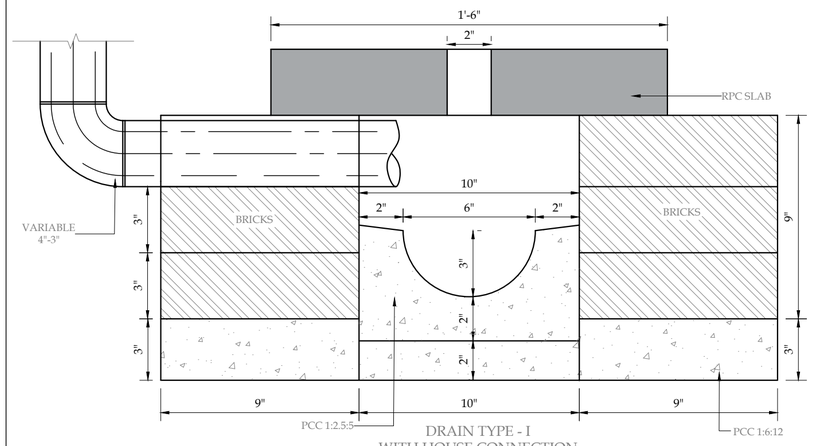

DRAIN TYPE - I
WITH HOUSE CONNECTION
SECTION AT A-A
Scale :- 1:4

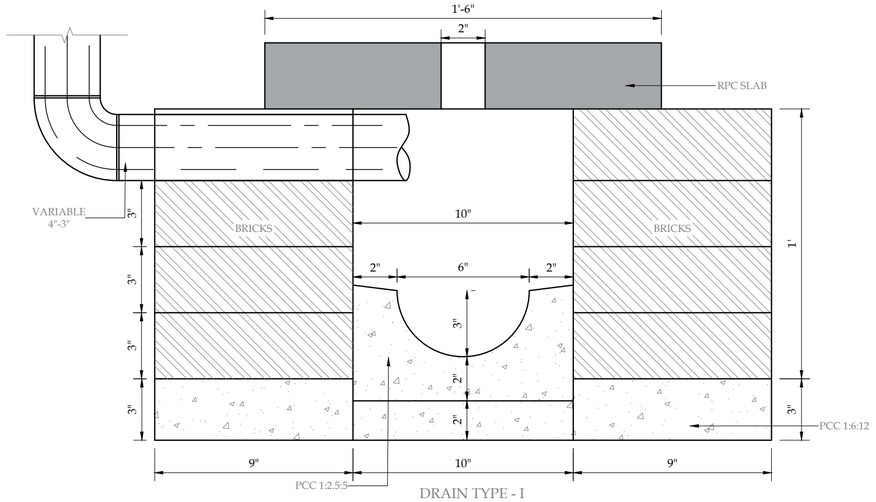

DRAIN TYPE - I
WITH HOUSE CONNECTION
SECTION AT A-A
Scale :- 1:4

NOTES:-

1.

TITLE.

TYPICAL DETAILS DRAIN TYPE - I
WITH HOUSE CONNECTION

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 1'-0"

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	29-08-2025	DETAILED DESIGN	ASAD	ENGR FAIEZ	ENGR IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:

PRMSC-SW-TD-04A

SHEET

REV 00

PROJECT:

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:

PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

PRMSC-SW-TD-04A

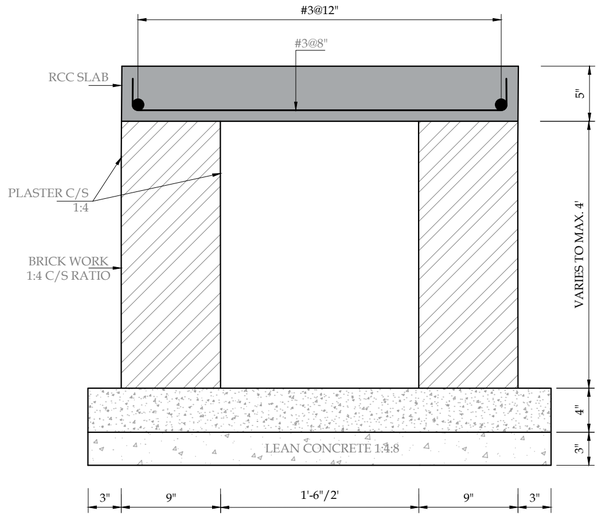

(TYPICAL) DRAIN SECTION FOR 1'-6" & 2' WIDE DRAIN UNDER WALKWAY & GREEN AREAS

SCALE:- 1" = 10"

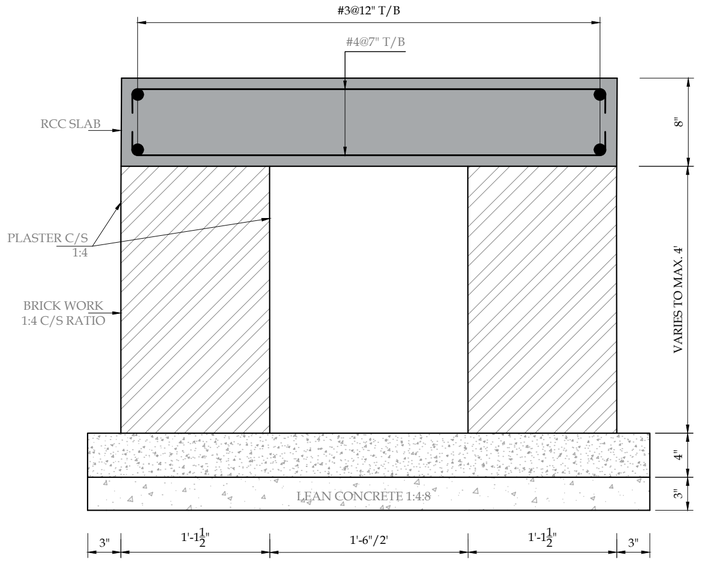

(TYPICAL) DRAIN SECTION FOR 1'-6" & 2' WIDE DRAIN UNDER ROAD SECTION

SCALE:- 1" = 10"

NOTES:-

1.

TITLE.

TYPICAL DETAILS DRAIN

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1" = 1'-0"

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	29-08-2025	DETAILED DESIGN	ASAD	ENGR. FAIEZ	ENGR. HSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-SW-TD-04B		00

PROJECT:

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:

PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS www.asianeon.com

PRMSC-SW-TD-04B

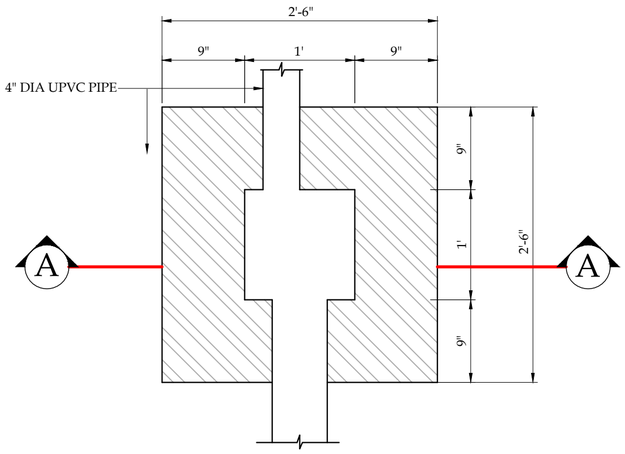

DRAIN HOUSE CONNECTION
CHAMBER 1'x1'x2'
SCALE:- 1" = 1'-0"

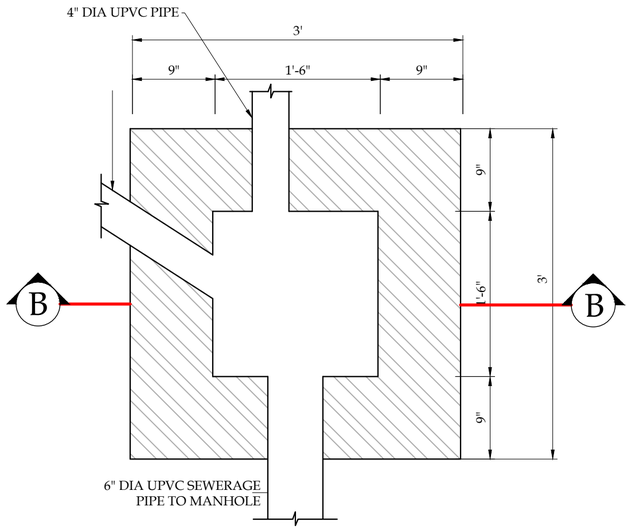

DRAIN HOUSE CONNECTION
CHAMBER 1.5'x1.5'x2'
SCALE:- 1" = 1'-0"

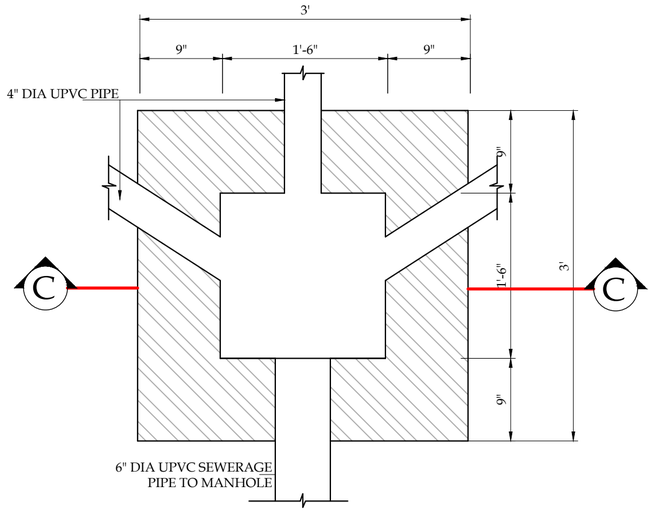

DRAIN HOUSE CONNECTION
CHAMBER 1.5'x1.5'x1.5'
SCALE:- 1" = 1'-0"

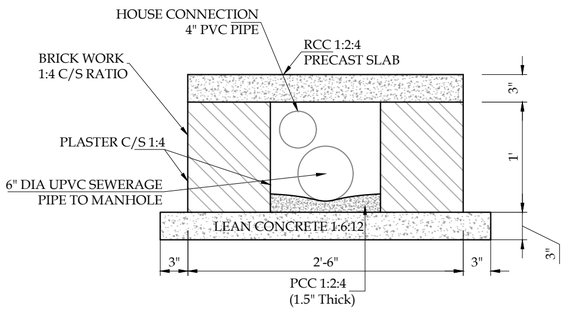

SECTION A-A
SCALE:- 1" = 1'-0"

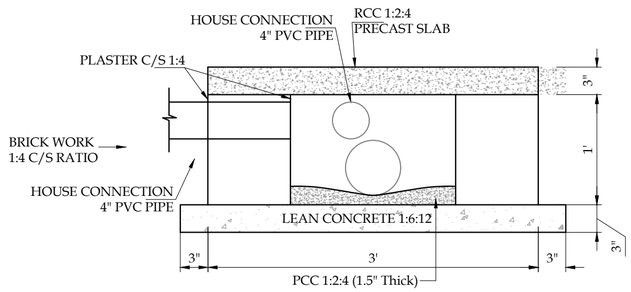

SECTION B-B
SCALE:- 1" = 1'-0"

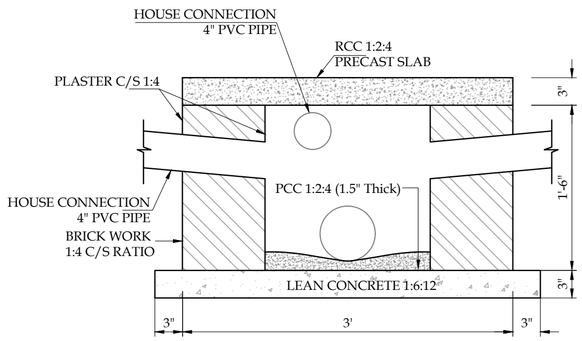

SECTION C-C
SCALE:- 1" = 1'-0"

TITLE.
DRAINAGE
HOUSE CONNECTION CHAMBER

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	AS SHOWN

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	29-08-2025	DETAILED DESIGN	ASAD	ENGR. FAIEZ	ENGR. HSANULHAQ
02					
03					
04					
05					
06					
07					

DRAWING N°:
PRMSC-SW-TD-06

SHEET

REV
00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:
ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

PRMSC-SW-TD-06

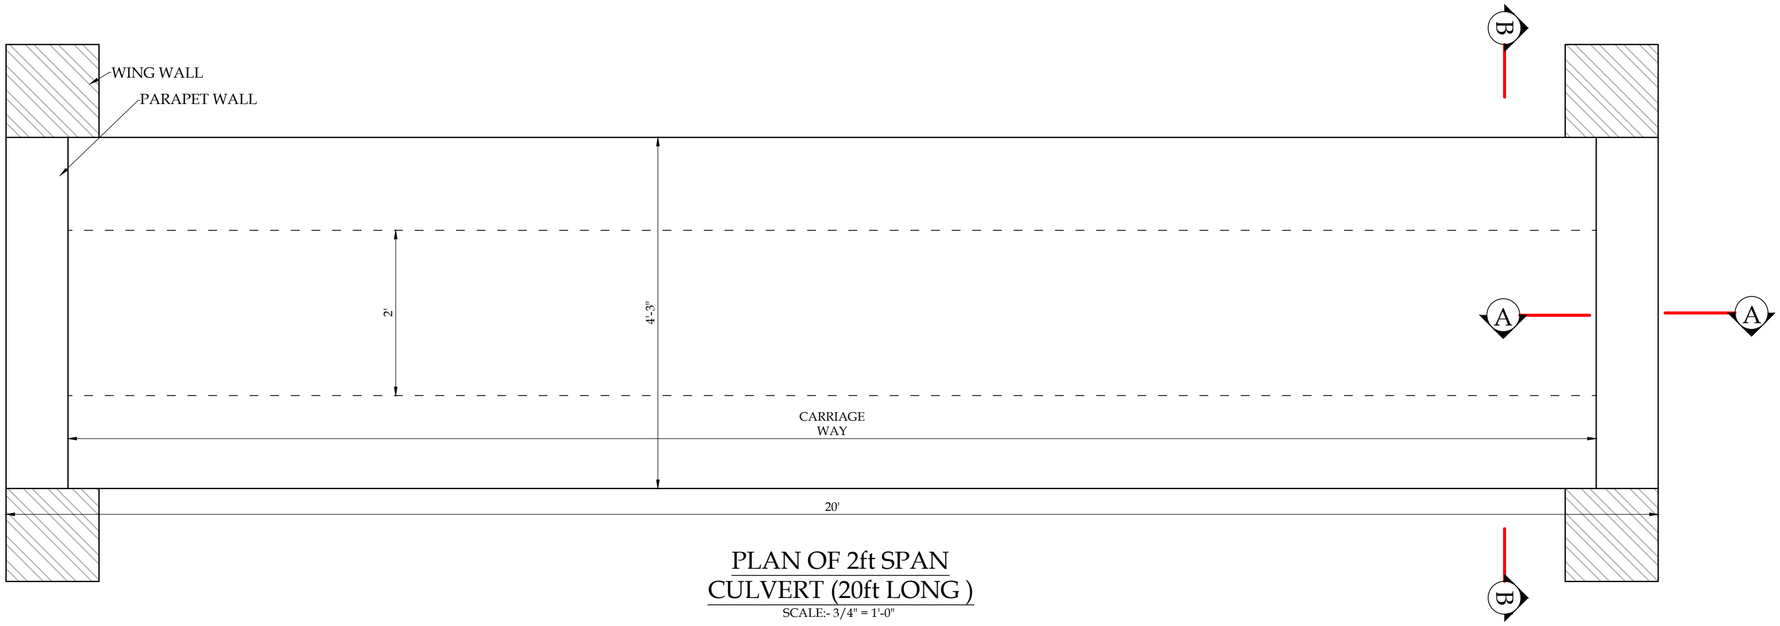

PLAN OF 2ft SPAN
CULVERT (20ft LONG)
SCALE:- 3/4" = 1'-0"

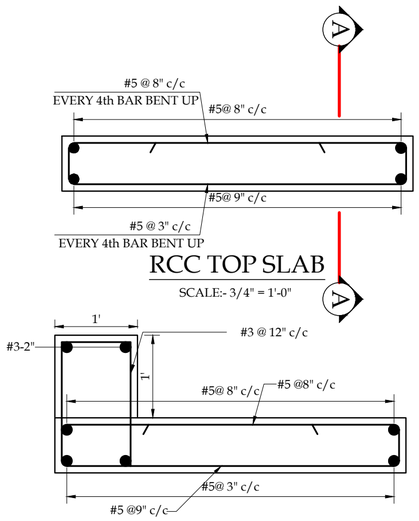

RCC TOP SLAB
SCALE:- 3/4" = 1'-0"

SECTION A-A
SCALE:- 3/4" = 1'-0"



WING WALL SECTION
SCALE:- 3/4" = 1'-0"

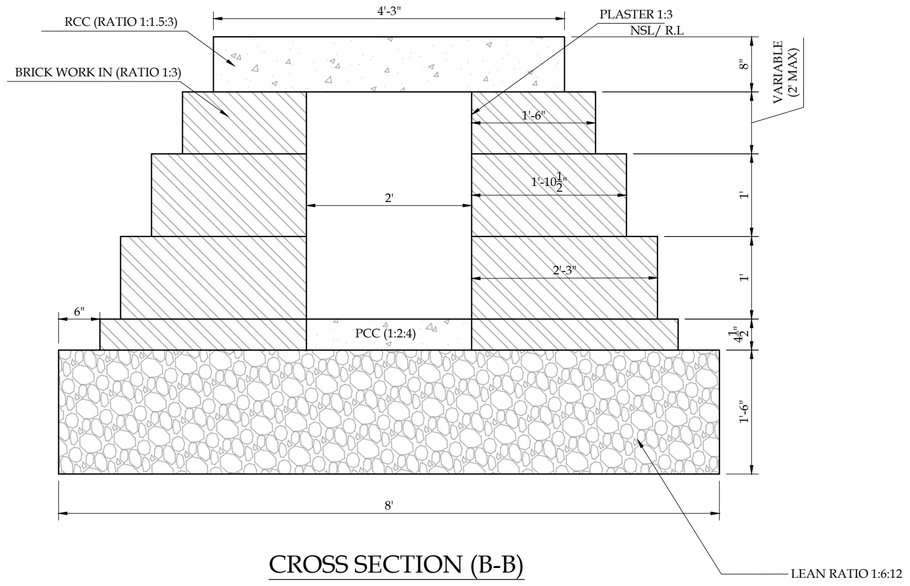

CROSS SECTION (B-B)
SCALE:- 3/4" = 1'-0"

NOTES

THIS TYPICAL CULVERT DETAIL
TO BE USED AS PER SITE REQUIREMENT.

TITLE.

TYPICAL CULVERT DETAIL

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	AS SHOWN

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	29-08-2025	DETAILED DESIGN	ASAD	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº: PRMSC-SW-TD-07 | SHEET | REV 00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:
ASIAN CONSULTING ENGINEERS
www.asianeon.com.pk

COMMUNAL SEPTIC TANK

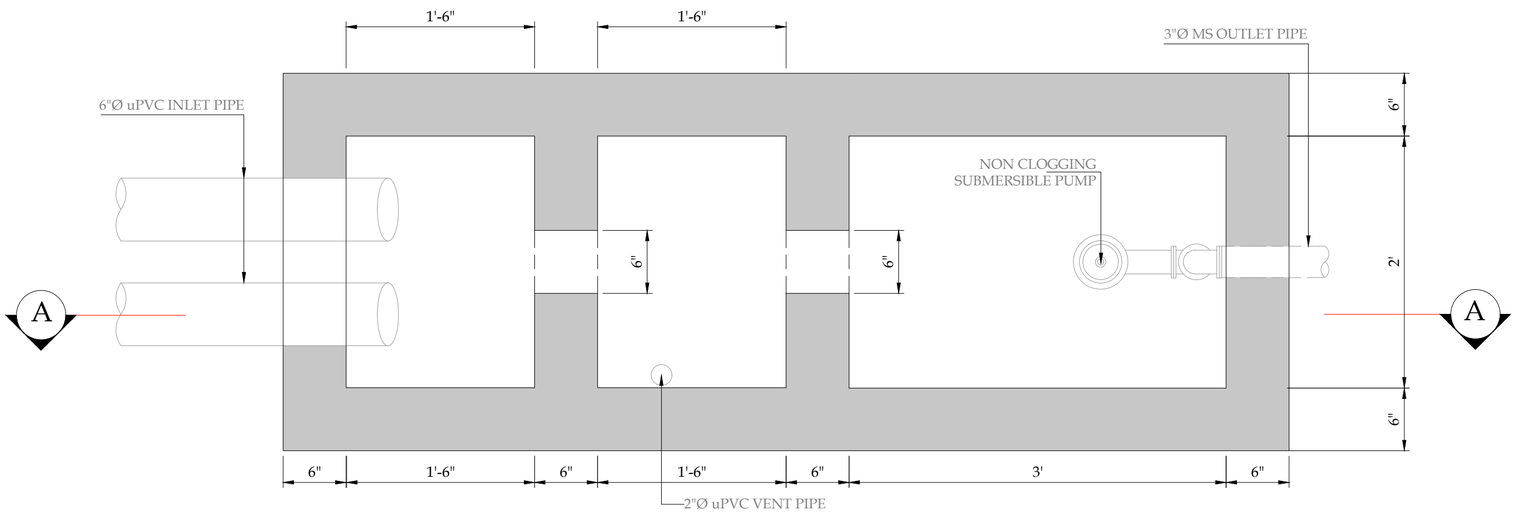

PLAN

SCALE:- 1" = 1'-0"

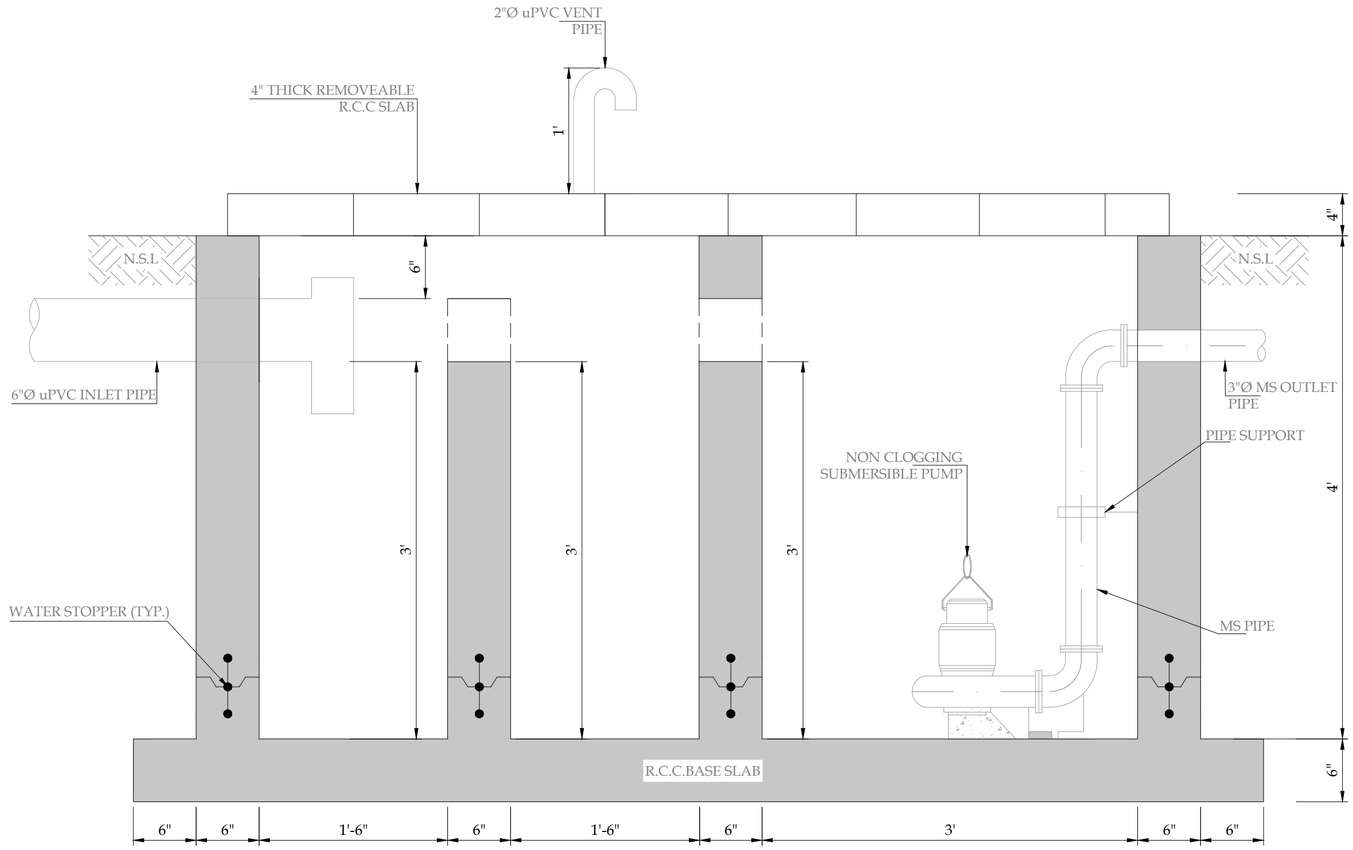

SECTION A-A

SCALE:- 1" = 1'-0"

NOTE

THE BOTTTOM OF THE CURB SHALL BE SUNK AT LEAST 4 FT. BELOW THE TOP OF FIRST LAYER OF SUITABLE SOIL STRATA ENCOUNTERED ALL GRANULAR SOILS, MEDIUM TO COARSE SAND OR GRAVEL SHALL BE CONSIDERED SUITABLE FOR THIS PURPUSE AND AS PER INSTRUCTION OF THE ENGINEER INCHARGE.

TITLE.

LAYOUT PLAN & SECTION OF
COMMUNAL SEPTIC TANK TYPE-I

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1/4" = 1'-0"

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	21-11-2025	DETAILED DESIGN	ASAD	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING N°: PRMSC-SEW-ST-C-01

SHEET 1 OF 1

REV 00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:
ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

PRMSC-SEW-ST-C-01

SEPTIC TANK TYPE I(A)

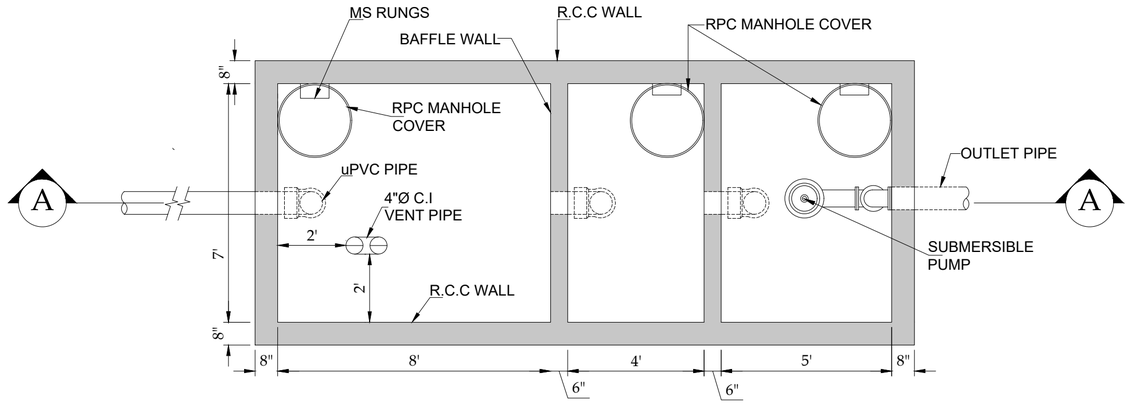

SEPTIC TANK SECTIONAL PLAN

SCALE:- 1/4" = 1'-0"

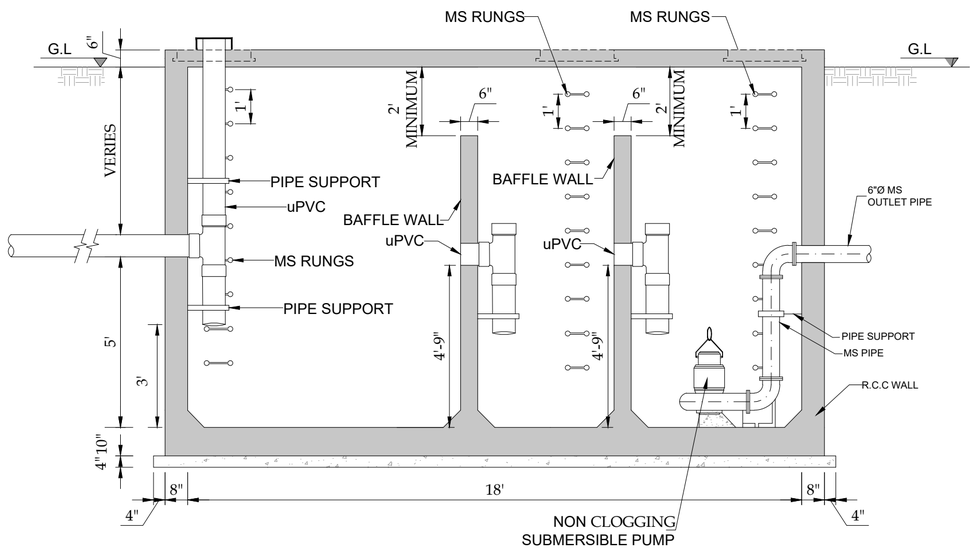

SECTION A-A

SCALE:- 1/4" = 1'-0"

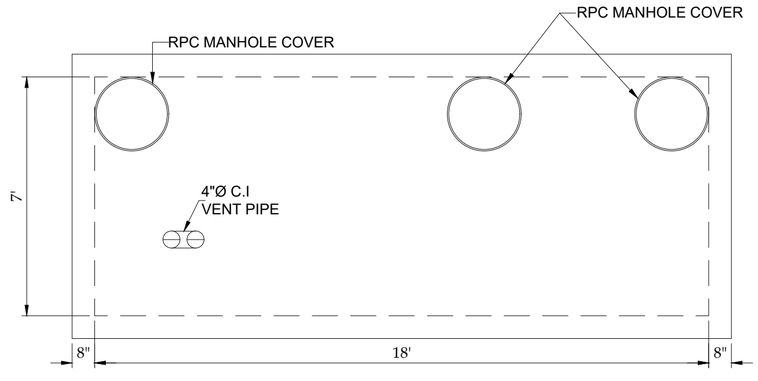

SEWER BEFELL ROOF PLAN

SCALE:- 1/4" = 1'-0"

PUMPS ID	TYPE	FLOW	HEAD	STATUS
P1	NON CLOGGING SUBMERSIBLE PUMP	VARIABLE	VARIABLE	ON DUTY

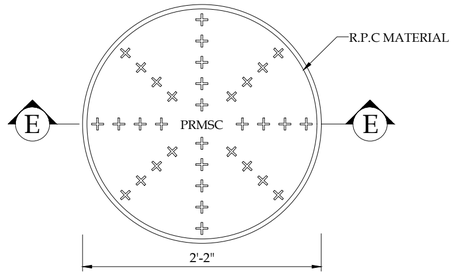

RPC MANHOLE COVER PLAN

SCALE:- 1" = 1'-0"



SECTION AT E-E

SCALE:- 1" = 1'-0"



M.S IRON STEP

SCALE:- 1" = 1'-0"

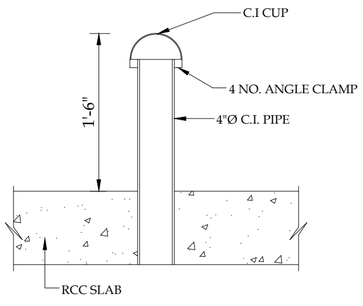

ELEVATION

SCALE:- 1" = 1'-0"

NOTE

THE BOTTTOM OF THE CURB SHALL BE SUNK AT LEAST 4 FT. BELOW THE TOP OF FIRST LAYER OF SUITABLE SOIL STRATA ENCOUNTERED ALL GRANULAR SOILS, MEDIUM TO COARSE SAND OR GRAVEL SHALL BE CONSIDERED SUITABLE FOR THIS PURPUSE AND AS PER INSTRUCTION OF THE ENGINEER INCHARGE.

TITLE.

LAYOUT PLAN & SECTION OF SEPTIC TANK TYPE-I(A)

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1/4" = 1'-0"

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	21-11-2025	DETAILED DESIGN	ASAD	ENGR. FAIEZ	ENGR HSANUL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING N°:	SHEET	REV
PRMSC-SEW-ST-C-01	1 OF 1	00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:
ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

PRMSC-SEW-ST-C-01

SEPTIC TANK TYPE I

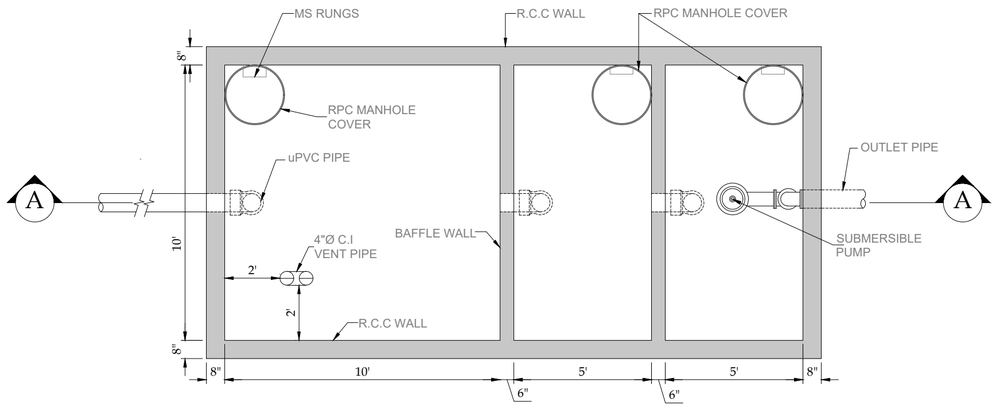

SEPTIC TANK SECTIONAL PLAN

SCALE:- 1/4" = 1'-0"

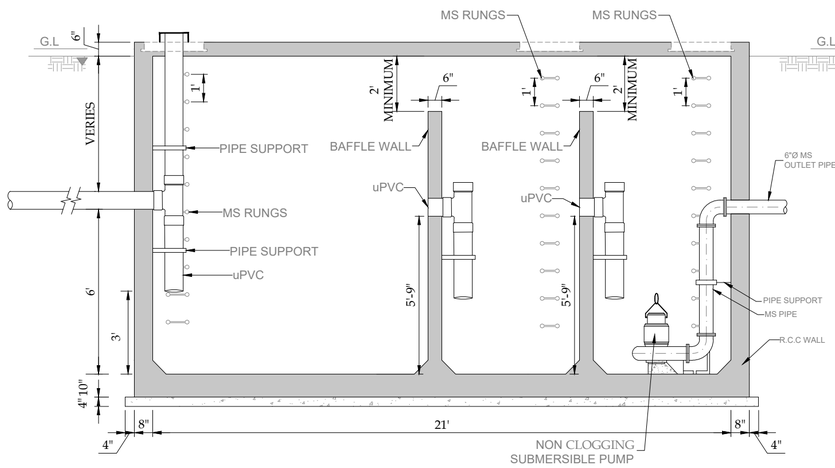

SECTION A-A

SCALE:- 1/4" = 1'-0"

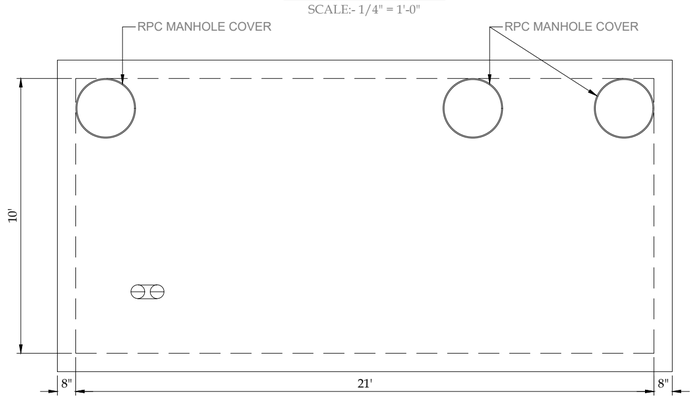

SEWER BEFELL ROOF PLAN

SCALE:- 1/4" = 1'-0"

PUMPS ID	TYPE	FLOW	HEAD	STATUS
P1	NON CLOGGING SUBMERSIBLE PUMP	VARIABLE	VARIABLE	ON DUTY

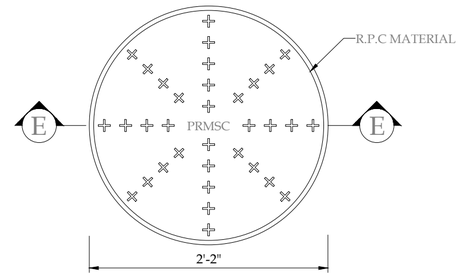

RPC MANHOLE COVER PLAN

SCALE:- 1" = 1'-0"



SECTION AT E-E

SCALE:- 1" = 1'-0"



M.S IRON STEP

SCALE:- 1" = 1'-0"

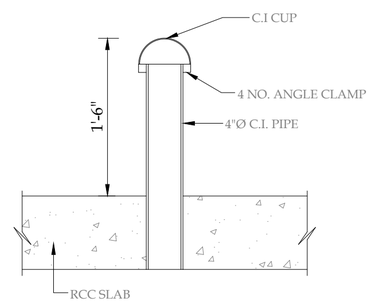

ELEVATION

SCALE:- 1" = 1'-0"

NOTE

THE BOTTTOM OF THE CURB SHALL BE SUNK AT LEAST 4 FT. BELOW THE TOP OF FIRST LAYER OF SUITABLE SOIL STRATA ENCOUNTERED ALL GRANULAR SOILS, MEDIUM TO COARSE SAND OR GRAVEL SHALL BE CONSIDERED SUITABLE FOR THIS PURPUSE AND AS PER INSTRUCTION OF THE ENGINEER INCHARGE.

TITLE.

LAYOUT PLAN & SECTION OF SEPTIC TANK TYPE-I

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1/4" = 1'-0"

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	21-11-2025	DETAILED DESIGN	ASAD	ENGR FAIZ	ENGR HSANULLHAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº: PRMSC-SEW-ST-C-01

SHEET 1 OF 1

REV 00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS www.asiancon.com

PRMSC-SEW-ST-C-01

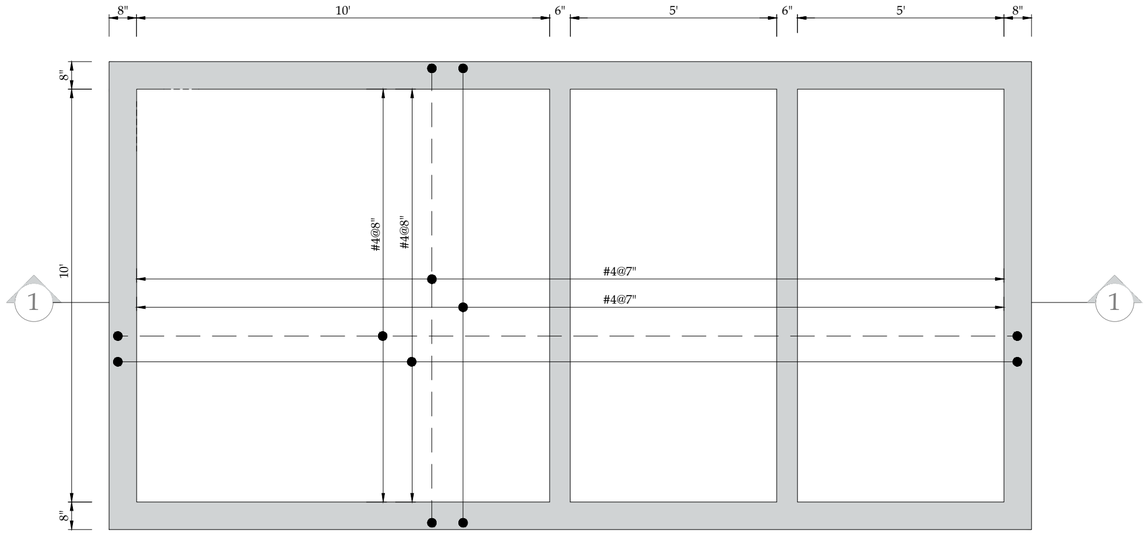

FOUNDATION LAYOUT PLAN

SCALE:- 3/8" = 1'-0"

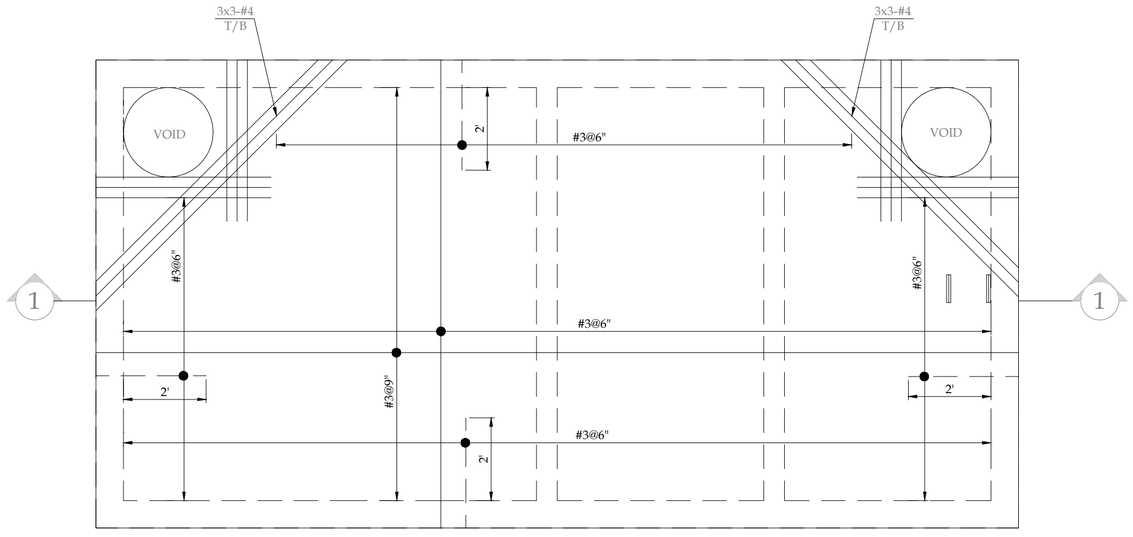

TOP SLAB=6" THICK

SCALE:- 3/8" = 1'-0"

NOTE:

1. DISTRIBUTION TOP BARS #3@12"c/c.

NOTES:

1. APPLY TWO COATS OF ConGuard CTE (COAL TAR EPOXY RESIGN INTERNAL SURFACE COATING 0.5 KG PER SQ.M) BY RADIANT CONSTRUCTION TECHNOLOGIES ON INNER SURFACES WHICH ARE IN DIRECT CONTACT WITH WATER

SPECIAL NOTES

1. THE FOUNDATION IS DESIGN USING ASSUMED BEARING CAPACITY OF 0.70 TSF. CONTRACTOR/CLIENT REQUIRED TO CONFIRM BEFORE EXECUTION OF WORK.
2. THE STRUCTURE IS DESIGNED ASSUMING THAT WATER TABLE IS AT 50'-0" FROM EXISTING GROUND LEVEL.
3. THE FOUNDATION DESIGN IS SUBJECT TO SOIL CONDITION, FINALIZED AS PER GEO-TECHNICAL SOIL INVESTIGATION REPORT.
4. THE BACK FILLING BEHIND WALL OF TANK SHALL NOT BE DONE BEFORE COSTING OF ROOF SLAB.

TITLE.

SEPTIC TANK STRUCTURAL DETAIL-1 TYPE-I

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	--

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	21-11-2025	DETAILED DESIGN	ASAD	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-SEW-ST-S-01A	1 OF 1	00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:
ASIAN CONSULTING ENGINEERS www.asiancon.com.pk

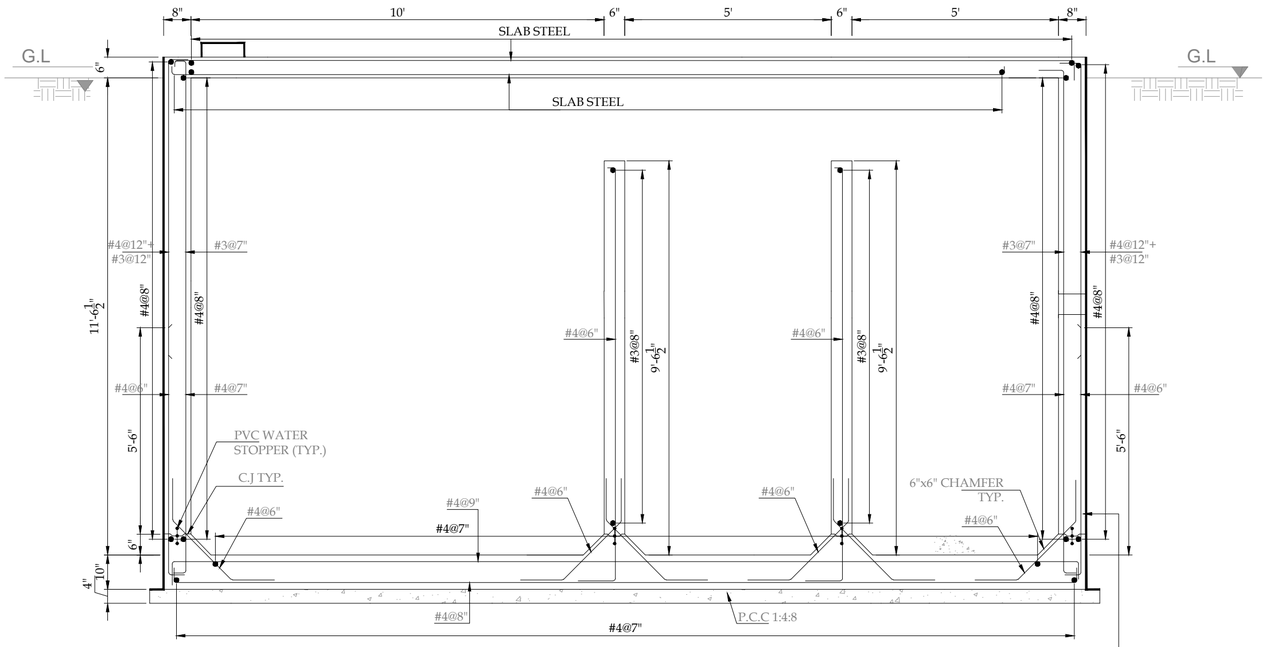

SECTION 1-1

SCALE:- 3/8" = 1'-0"

PROVIDING AND LAYING OF BITUMINOUS WATER PROOFING MEMBRANE 4MM THICK REINFORCED WITH ROT-PROOF, NON-WOVEN POLYESTER CARRIER OVER ONE COAT OF PRIMER GRIP CONFIRMS TO ATSM D41

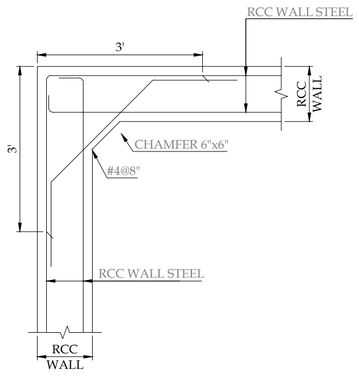

TYP. RCC WALL CORNER REINFORCEMENT DETAIL

SCALE:- 1/2" = 1'-0"

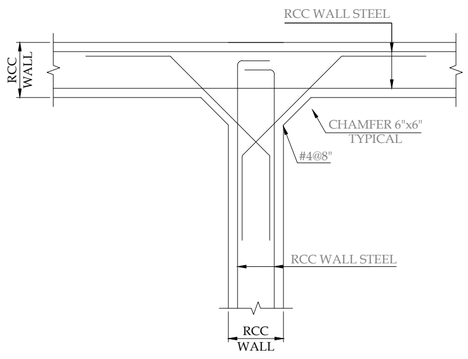

TYP. RCC WALL T-SHAPED REINFORCEMENT DETAIL

SCALE:- 1/2" = 1'-0"

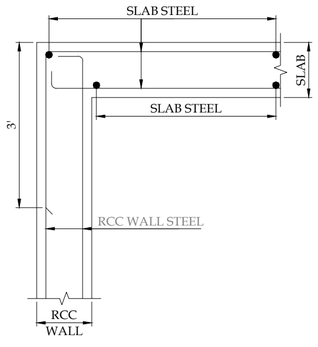

TYP. RCC WALL RCC SLAB CONNECTION DETAIL

SCALE:- 1/2" = 1'-0"

NOTES:

1. APPLY TWO COATS OF ConGuard CTE (COAL TAR EPOXY RESIGN INTERNAL SURFACE COATING 0.5 KG PER SQ.M) BY RADIANT CONSTRUCTION TECHNOLOGIES ON INNER SURFACES WHICH ARE IN DIRECT CONTACT WITH WATER

SPECIAL NOTES

1. THE FOUNDATION IS DESIGN USING ASSUMED BEARING CAPACITY OF 0.70 TSF. CONTRACTOR/CLIENT REQUIRED TO CONFIRM BEFORE EXECUTION OF WORK.
2. THE STRUCTURE IS DESIGNED ASSUMING THAT WATER TABLE IS AT 50'-0" FROM EXISTING GROUND LEVEL.
3. THE FOUNDATION DESIGN IS SUBJECT TO SOIL CONDITION, FINALIZED AS PER GEO-TECHNICAL SOIL INVESTIGATION REPORT.
4. THE BACK FILLING BEHIND WALL OF TANK SHALL NOT BE DONE BEFORE COSTING OF ROOF SLAB.

TITLE.

SEPTIC TANK
STRUCTURAL DETAIL-2 TYPE-I

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	-

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	21-11-2025	DETAILED DESIGN	ASAD	ENGR FAIEZ	ENGR HSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-SEW-ST-S-01B	1 OF 1	00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:
ASIAN CONSULTING ENGINEERS
www.asiancon.com

PRMSC-SEW-ST-S-01 (2)

SEPTIC TANK TYPE II

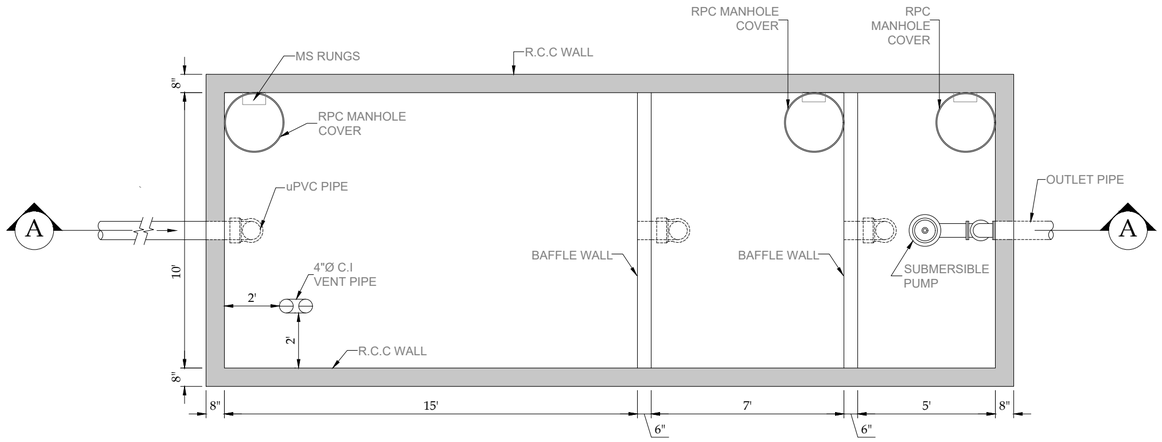

SEPTIC TANK SECTIONAL PLAN

SCALE:- 1/4" = 1'-0"

PUMPS ID	TYPE	FLOW	HEAD	STATUS
P1	NON CLOGGING SUBMERSIBLE PUMP	VARIABLE	VARIABLE	ON DUTY

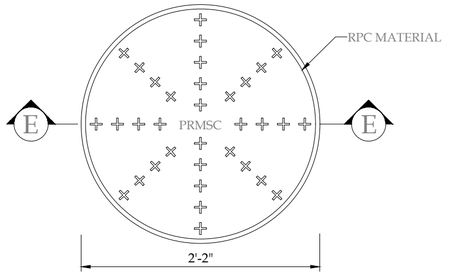

RPC MANHOLE COVER PLAN

SCALE:- 1" = 1'-0"

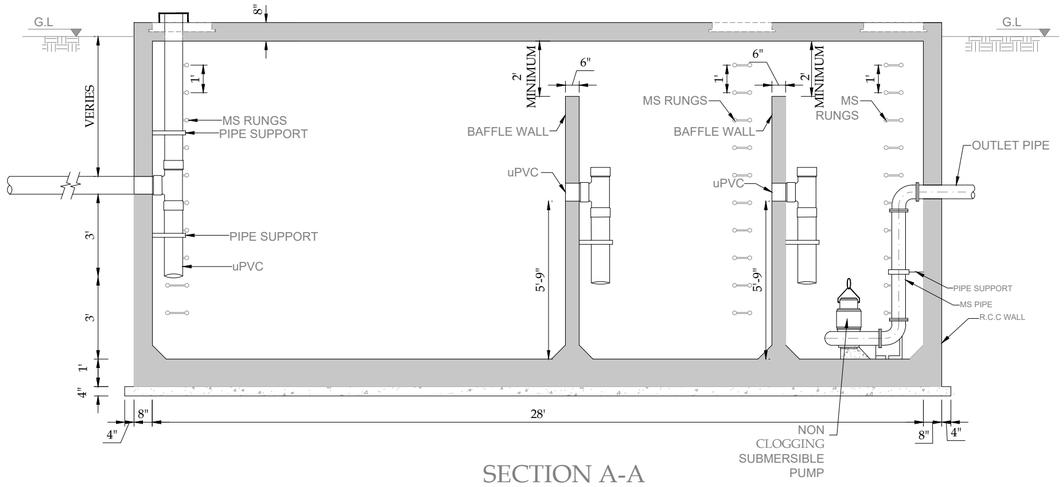

SECTION A-A

SCALE:- 1/4" = 1'-0"

SEWER BEFELL ROOF PLAN

SCALE:- 1/4" = 1'-0"



SECTION AT E-E

SCALE:- 1" = 1'-0"



M.S IRON STEP

SCALE:- 1" = 1'-0"

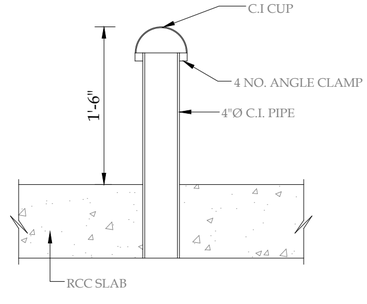

ELEVATION

SCALE:- 1" = 1'-0"

NOTE

THE BOTTTOM OF THE CURB SHALL BE SUNK AT LEAST 4 FT. BELOW THE TOP OF FIRST LAYER OF SUITABLE SOIL STRATA ENCOUNTERED ALL GRANULAR SOILS, MEDIUM TO COARSE SAND OR GRAVEL SHALL BE CONSIDERED SUITABLE FOR THIS PURPUSE AND AS PER INSTRUCTION OF THE ENGINEER INCHARGE.

TITLE.

LAYOUT PLAN & SECTION OF SEPTIC TANK TYPE-II

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1/4" = 1'-0"

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	21-11-2025	DETAILED DESIGN	ASAD	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:

PRMSC-SEW-ST-C-01

SHEET 1 OF 1

REV 00

PROJECT:

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:

PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS www.asianconsultingengineers.com

PRMSC-SEW-ST-C-02

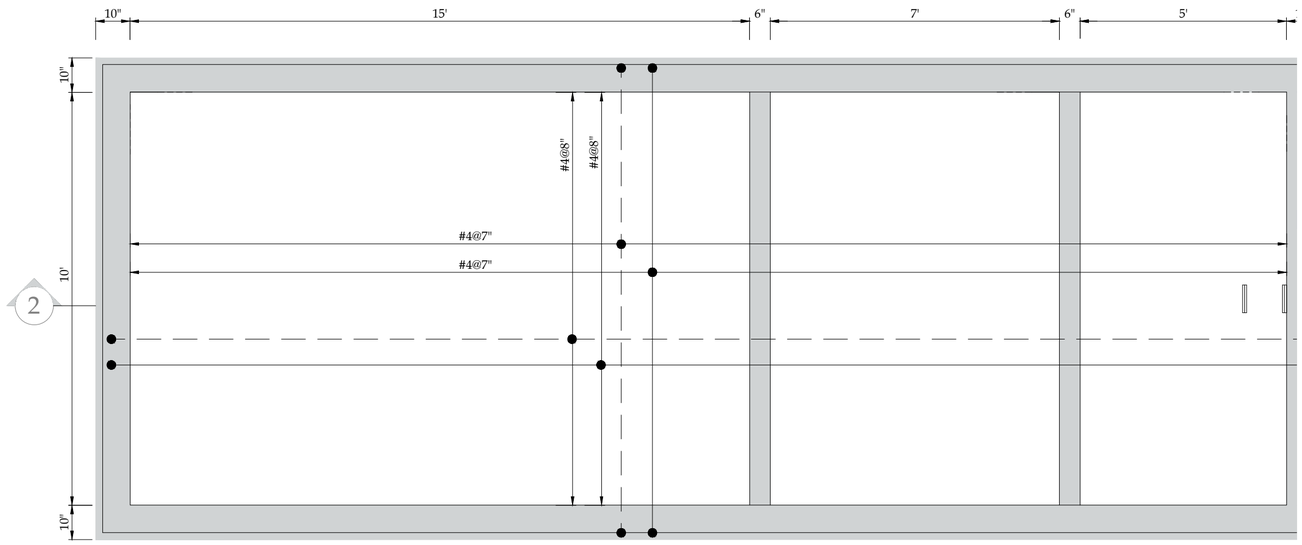

FOUNDATION LAYOUT PLAN

SCALE:- 3/8" = 1'-0"

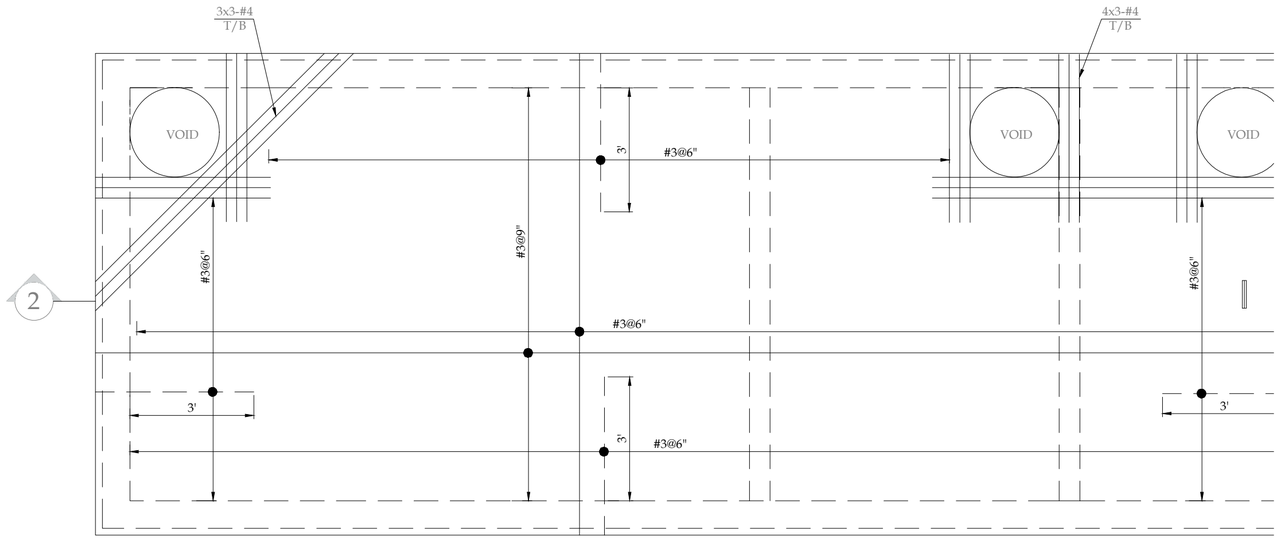

TOP SLAB=6" THICK

SCALE:- 3/8" = 1'-0"

NOTE:

1. DISTRIBUTION TOP BARS #3@12"c/c.

NOTES:

1. APPLY TWO COATS OF ConGuard CTE (COAL TAR EPOXY RESIGN INTERNAL SURFACE COATING 0.5 KG PER SQ.M) BY RADIANT CONSTRUCTION TECHNOLOGIES ON INNER SURFACES WHICH ARE IN DIRECT CONTACT WITH WATER

SPECIAL NOTES

1. THE FOUNDATION IS DESIGN USING ASSUMED BEARING CAPACITY OF 0.70 TSF. CONTRACTOR/CLIENT REQUIRED TO CONFIRM BEFORE EXECUTION OF WORK.
2. THE STRUCTURE IS DESIGNED ASSUMING THAT WATER TABLE IS AT 50'-0" FROM EXISTING GROUND LEVEL.
3. THE FOUNDATION DESIGN IS SUBJECT TO SOIL CONDITION, FINALIZED AS PER GEO-TECHNICAL SOIL INVESTIGATION REPORT.
4. THE BACK FILLING BEHIND WALL OF TANK SHALL NOT BE DONE BEFORE COSTING OF ROOF SLAB.

TITLE.

SEPTIC TANK
STRUCTURAL DETAIL-1
TYPE-II

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	--

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	21-11-2025	DETAILED DESIGN	ASAD	ENGR. FAIEZ	ENGR. HSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-SEW-ST-S-01	1 OF 1	00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:
ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

PRMSC-SEW-ST-S-01 (2)

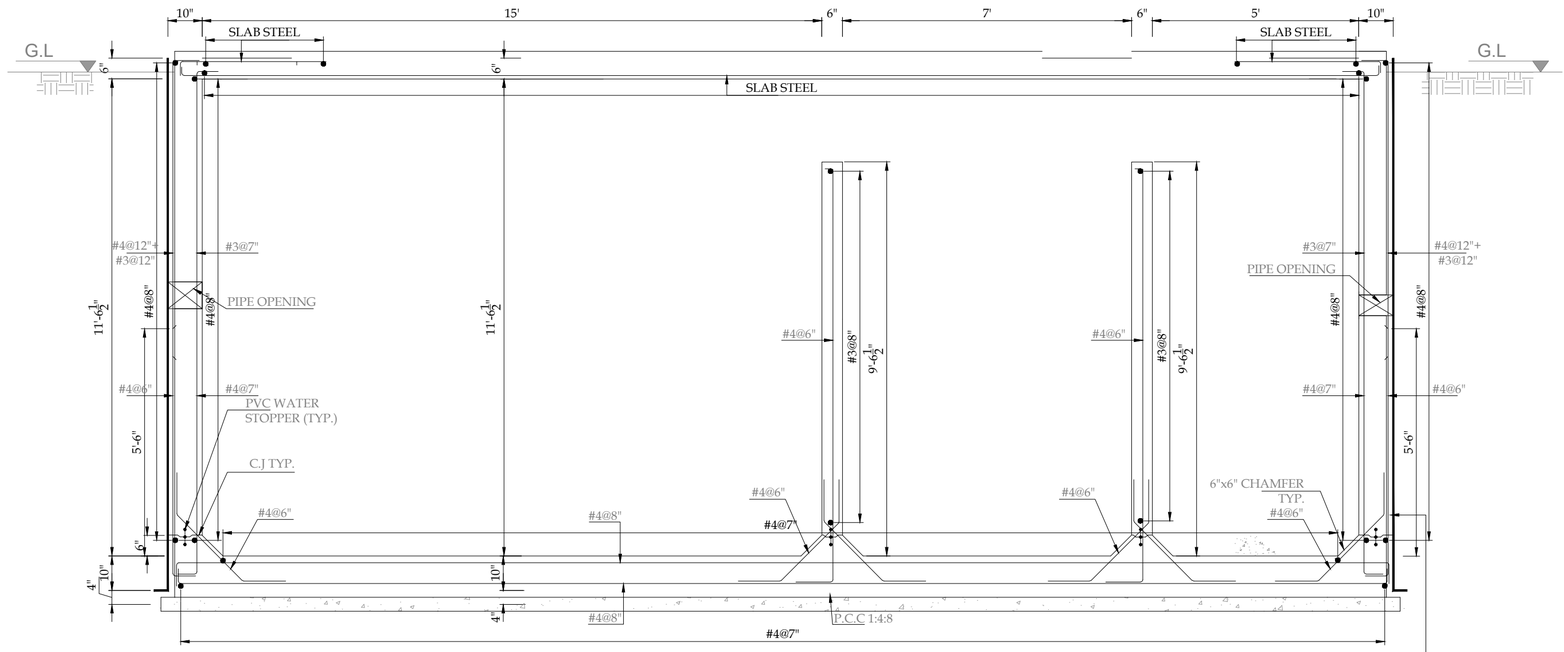

SECTION 2-2

SCALE:- 3/8" = 1'-0"

PROVIDING AND LAYING OF BITUMINOUS WATER PROOFING MEMBRANE 4MM THICK REINFORCED WITH ROT-PROOF, NON-WOVEN POLYESTER CARRIER OVER ONE COAT OF PRIMER GRIP CONFIRMS TO ATSM D41

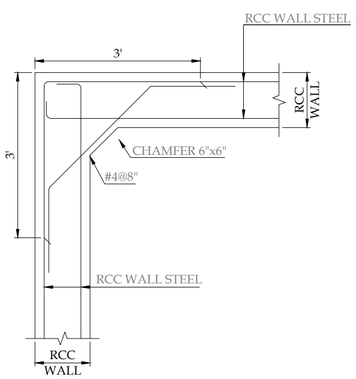

TYP. RCC WALL CORNER REINFORCEMENT DETAIL

SCALE:- 1/2" = 1'-0"

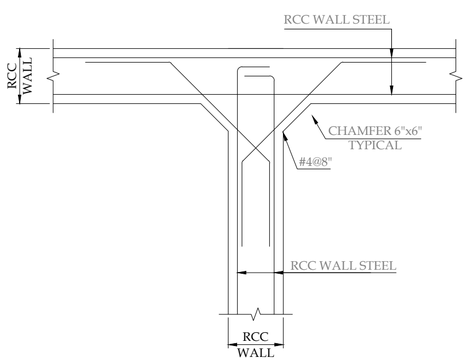

TYP. RCC WALL T-SHAPED REINFORCEMENT DETAIL

SCALE:- 1/2" = 1'-0"

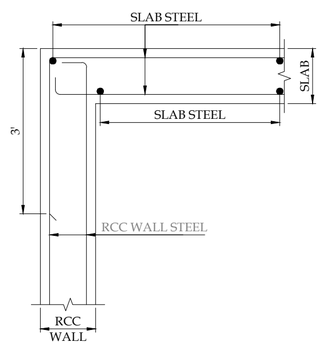

TYP. RCC WALL RCC SLAB CONNECTION DETAIL

SCALE:- 1/2" = 1'-0"

NOTES:

1. APPLY TWO COATS OF ConGuard CTE (COAL TAR EPOXY RESIGN INTERNAL SURFACE COATING 0.5 KG PER SQ.M) BY RADIANT CONSTRUCTION TECHNOLOGIES ON INNER SURFACES WHICH ARE IN DIRECT CONTACT WITH WATER

SPECIAL NOTES

1. THE FOUNDATION IS DESIGN USING ASSUMED BEARING CAPACITY OF 0.70 TSF. CONTRACTOR/CLIENT REQUIRED TO CONFIRM BEFORE EXECUTION OF WORK.
2. THE STRUCTURE IS DESIGNED ASSUMING THAT WATER TABLE IS AT 50'-0" FROM EXISTING GROUND LEVEL.
3. THE FOUNDATION DESIGN IS SUBJECT TO SOIL CONDITION, FINALIZED AS PER GEO-TECHNICAL SOIL INVESTIGATION REPORT.
4. THE BACK FILLING BEHIND WALL OF TANK SHALL NOT BE DONE BEFORE COSTING OF ROOF SLAB.

TITLE.

SEPTIC TANK
STRUCTURAL DETAILS-2
TYPE-II

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	-

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	21-11-2025	DETAILED DESIGN	ASAD	ENGR FAIEZ	ENGR HSANULHAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº: PRMSC-SEW-ST-S-02

SHEET 1 OF 1

REV 00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:
ASIAN CONSULTING ENGINEERS
www.asiancon.com

PRMSC-SEW-ST-S-01

SEPTIC TANK TYPE III

PUMPS ID	TYPE	FLOW	HEAD	STATUS
P1	NON CLOGGING SUBMERSIBLE PUMP	VARIABLE	VARIABLE	ON DUTY

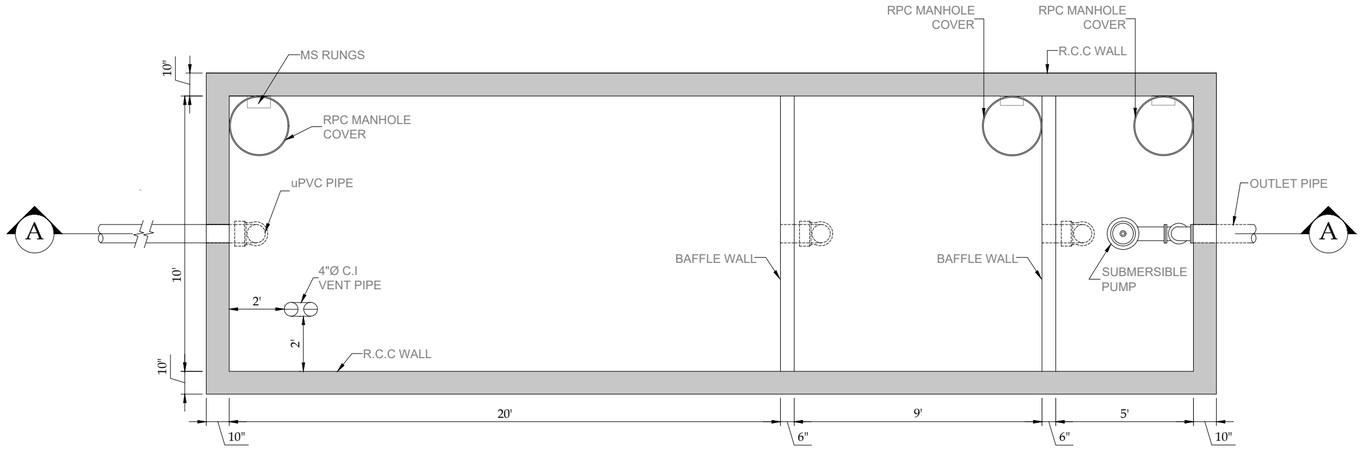

SEPTIC TANK SECTIONAL PLAN

SCALE:- 1/4" = 1'-0"

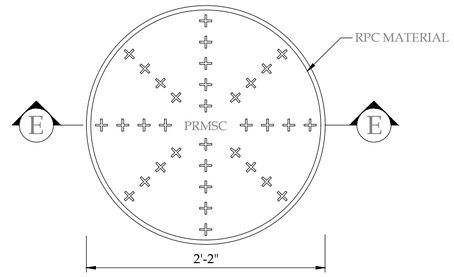

RPC MANHOLE COVER PLAN

SCALE:- 1" = 1'-0"



SECTION AT E-E

SCALE:- 1" = 1'-0"

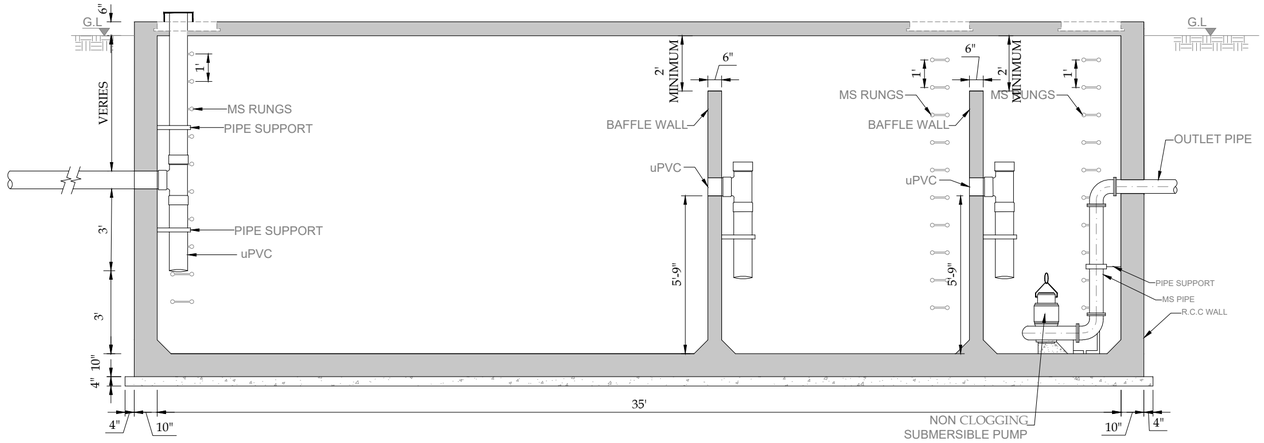

SECTION A-A

SCALE:- 1/4" = 1'-0"



M.S IRON STEP

SCALE:- 1" = 1'-0"

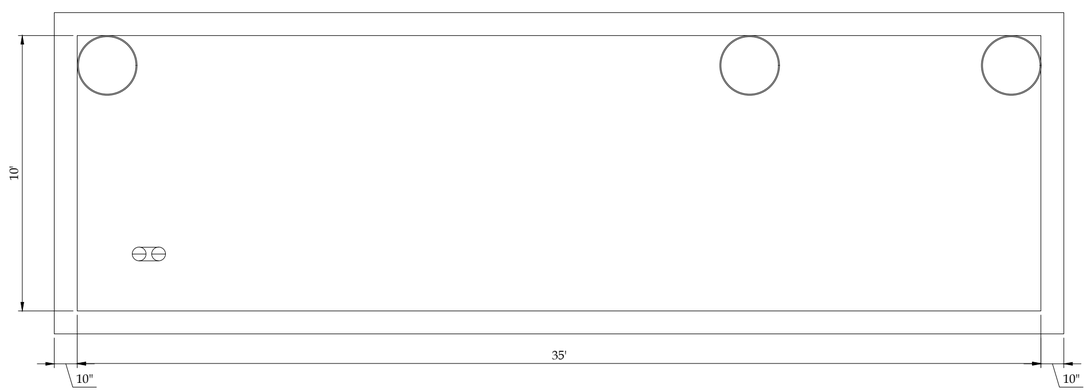

SEWER BEFELL ROOF PLAN

SCALE:- 1/4" = 1'-0"

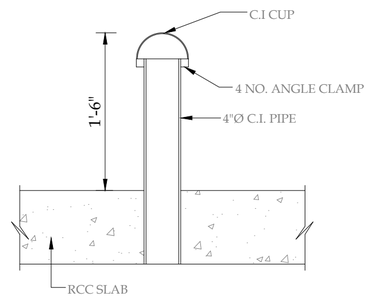

ELEVATION

SCALE:- 1" = 1'-0"

NOTE

THE BOTTTOM OF THE CURB SHALL BE SUNK AT LEAST 4 FT. BELOW THE TOP OF FIRST LAYER OF SUITABLE SOIL STRATA ENCOUNTERED ALL GRANULAR SOILS, MEDIUM TO COARSE SAND OR GRAVEL SHALL BE CONSIDERED SUITABLE FOR THIS PURPUSE AND AS PER INSTRUCTION OF THE ENGINEER INCHARGE.

TITLE.

LAYOUT PLAN & SECTION OF SEPTIC TANK TYPE-III

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1/4" = 1'-0"

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	21-11-2025	DETAILED DESIGN	ASAD	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº: PRMSC-SEW-ST-C-02

SHEET 1 OF 1

REV 00

PROJECT: ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT: ASIAN CONSULTING ENGINEERS www.asiancon.com.pk

PRMSC-SEW-ST-C-03

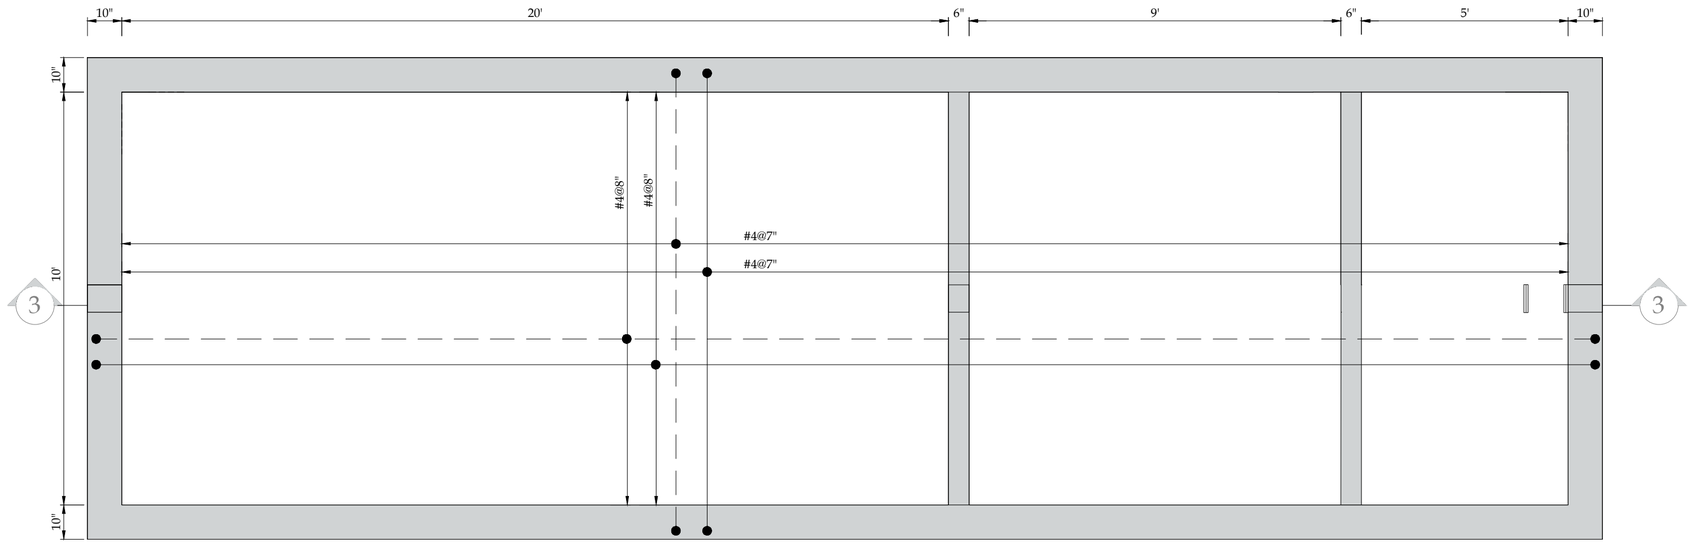

FOUNDATION LAYOUT PLAN

SCALE:- 3/8" = 1'-0"

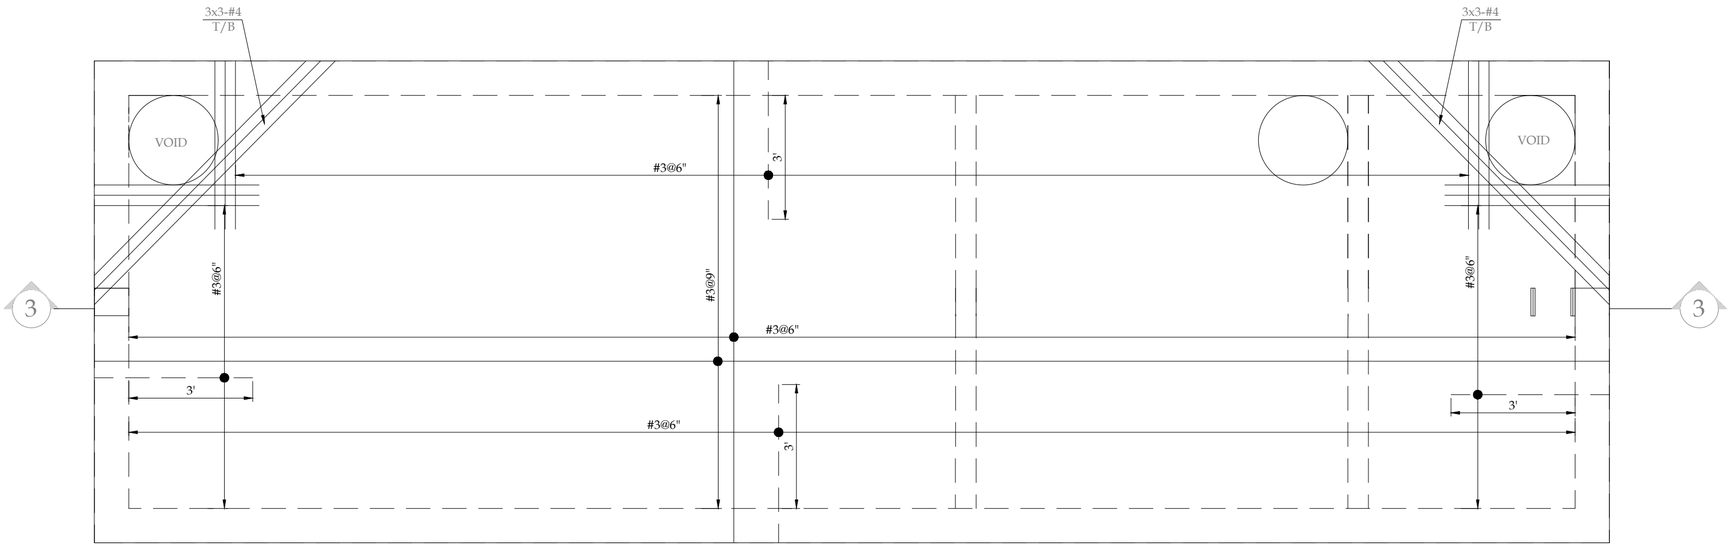

TOP SLAB=6" THICK

SCALE:- 3/8" = 1'-0"

NOTE:

1. DISTRIBUTION TOP BARS #3@12"c/c.

NOTES:

1. APPLY TWO COATS OF ConGuard CTE (COAL TAR EPOXY RESIGN INTERNAL SURFACE COATING 0.5 KG PER SQ.M) BY RADIANT CONSTRUCTION TECHNOLOGIES ON INNER SURFACES WHICH ARE IN DIRECT CONTACT WITH WATER

SPECIAL NOTES

1. THE FOUNDATION IS DESIGN USING ASSUMED BEARING CAPACITY OF 0.70 TSF. CONTRACTOR/CLIENT REQUIRED TO CONFIRM BEFORE EXECUTION OF WORK.
2. THE STRUCTURE IS DESIGNED ASSUMING THAT WATER TABLE IS AT 50'-0" FROM EXISTING GROUND LEVEL.
3. THE FOUNDATION DESIGN IS SUBJECT TO SOIL CONDITION, FINALIZED AS PER GEO-TECHNICAL SOIL INVESTIGATION REPORT.
4. THE BACK FILLING BEHIND WALL OF TANK SHALL NOT BE DONE BEFORE COSTING OF ROOF SLAB.

TITLE.

SEPTIC TANK
STRUCTURAL DETAIL-1
TYPE-III

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	--

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	21-11-2025	DETAILED DESIGN	ASAD	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:

PRMSC-SEW-ST-S-03

SHEET 1 OF 1

REV 00

PROJECT:

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS www.asiancon.com.pk

PRMSC-SEW-ST-S-01 (2)

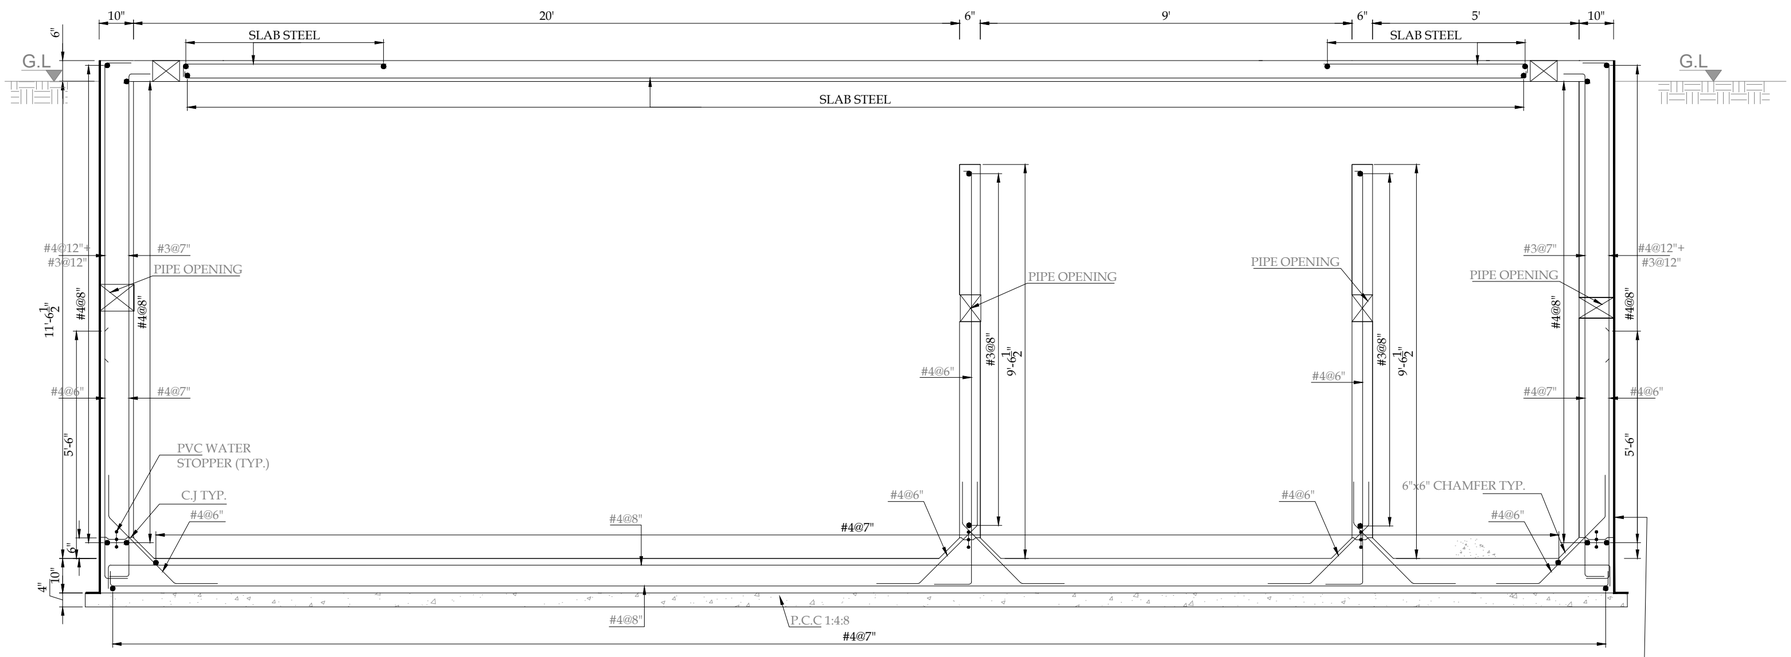

SECTION 3-3

SCALE:- 3/8" = 1'-0"

PROVIDING AND LAYING OF BITUMINOUS WATER PROOFING MEMBRANE 4MM THICK REINFORCED WITH ROT-PROOF, NON-WOVEN POLYESTER CARRIER OVER ONE COAT OF PRIMER GRIP CONFIRMS TO ATSM D41

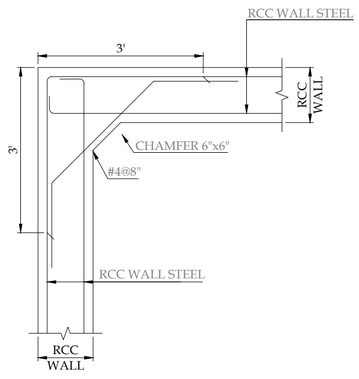

TYP. RCC WALL CORNER REINFORCEMENT DETAIL

SCALE:- 1/2" = 1'-0"

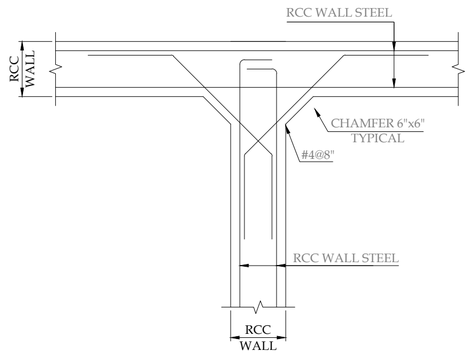

TYP. RCC WALL T-SHAPED REINFORCEMENT DETAIL

SCALE:- 1/2" = 1'-0"

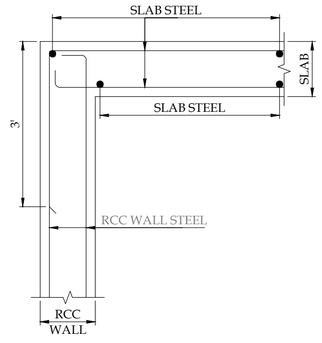

TYP. RCC WALL RCC SLAB CONNECTION DETAIL

SCALE:- 1/2" = 1'-0"

NOTES:

1. APPLY TWO COATS OF ConGuard CTE (COAL TAR EPOXY RESIGN INTERNAL SURFACE COATING 0.5 KG PER SQ.M) BY RADIANT CONSTRUCTION TECHNOLOGIES ON INNER SURFACES WHICH ARE IN DIRECT CONTACT WITH WATER

SPECIAL NOTES

1. THE FOUNDATION IS DESIGN USING ASSUMED BEARING CAPACITY OF 0.70 TSF. CONTRACTOR/CLIENT REQUIRED TO CONFIRM BEFORE EXECUTION OF WORK.
2. THE STRUCTURE IS DESIGNED ASSUMING THAT WATER TABLE IS AT 50'-0" FROM EXISTING GROUND LEVEL.
3. THE FOUNDATION DESIGN IS SUBJECT TO SOIL CONDITION, FINALIZED AS PER GEO-TECHNICAL SOIL INVESTIGATION REPORT.

TITLE.

SEPTIC TANK STRUCTURAL DETAILS-2 TYPE-III

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	--

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	21-11-2025	DETAILED DESIGN	ASAD	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING N°: PRMSC-SEW-ST-S-04

SHEET 1 OF 1

REV 00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:
ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

PRMSC-SEW-ST-S-01

SEPTIC TANK TYPE IV

PUMPS ID	TYPE	FLOW	HEAD	STATUS
P1	NON CLOGGING SUBMERSIBLE PUMP	VARIABLE	VARIABLE	ON DUTY

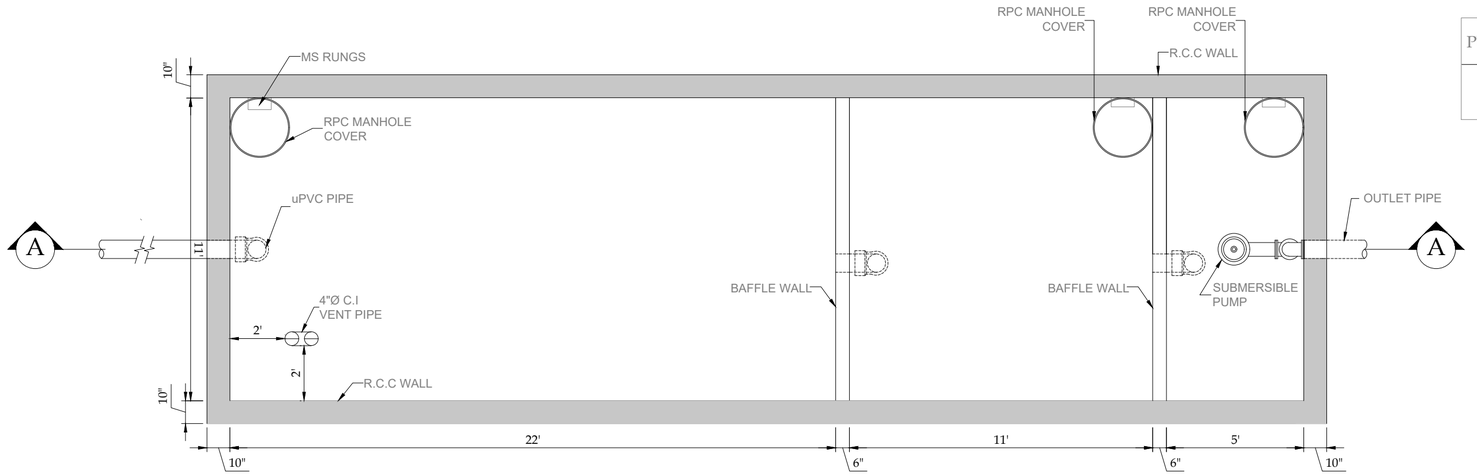

SEPTIC TANK SECTIONAL PLAN

SCALE:- 1/4" = 1'-0"

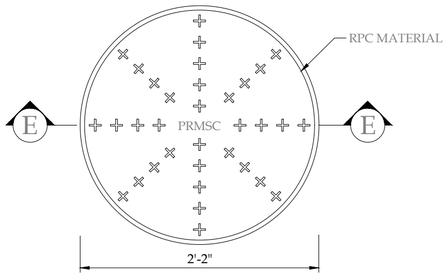

RPC MANHOLE COVER PLAN

SCALE:- 1" = 1'-0"

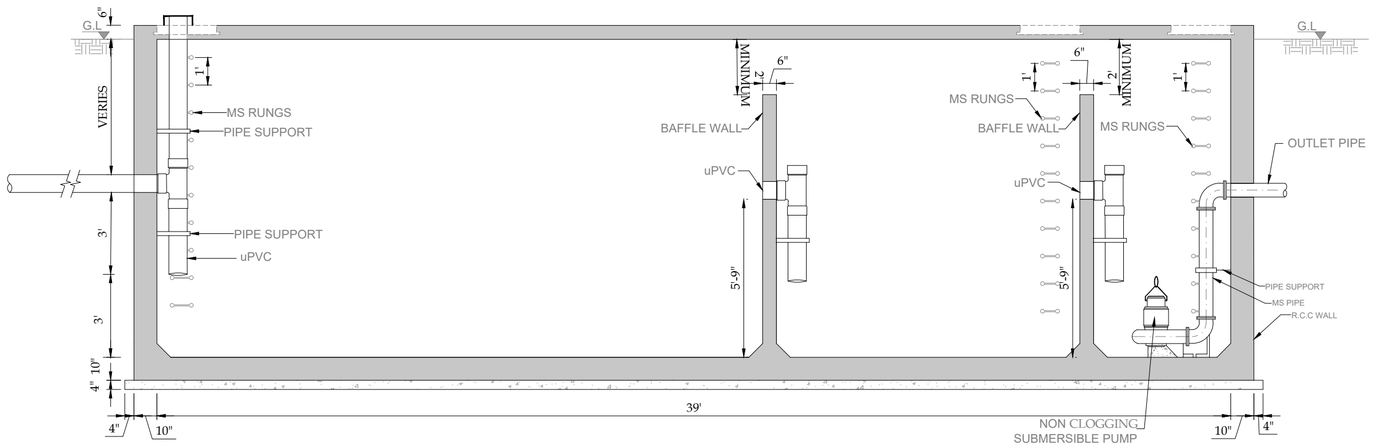

SECTION A-A

SCALE:- 1/4" = 1'-0"



SECTION AT E-E

SCALE:- 1" = 1'-0"

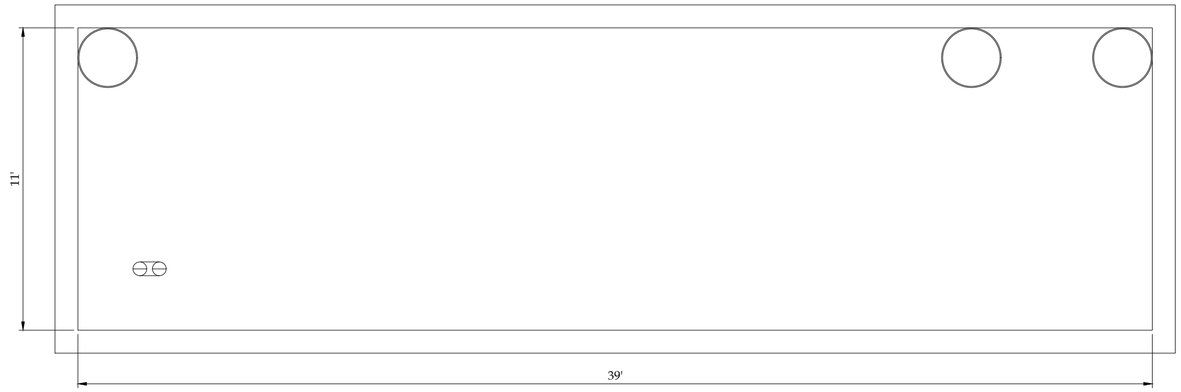

SEWER BEFELL ROOF PLAN

SCALE:- 1/4" = 1'-0"



M.S IRON STEP

SCALE:- 1" = 1'-0"

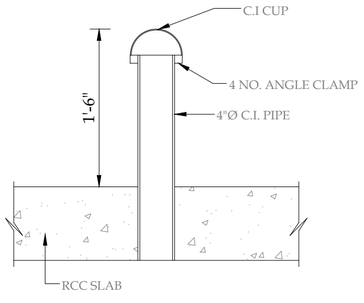

ELEVATION

SCALE:- 1" = 1'-0"

NOTE

THE BOTTTOM OF THE CURB SHALL BE SUNK AT LEAST 4 FT. BELOW THE TOP OF FIRST LAYER OF SUITABLE SOIL STRATA ENCOUNTERED ALL GRANULAR SOILS, MEDIUM TO COARSE SAND OR GRAVEL SHALL BE CONSIDERED SUITABLE FOR THIS PURPUSE AND AS PER INSTRUCTION OF THE ENGINEER INCHARGE.

TITLE.

LAYOUT PLAN & SECTION OF SEPTIC TANK TYPE-IV

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1/4" = 1'-0"

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	21-11-2025	DETAILED DESIGN	ASAD	ENGR FAIEZ	ENGR IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING N°: PRMSC-SEW-ST-C-03

SHEET 1 OF 1

REV 00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:
ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

PRMSC-SEW-ST-C-03

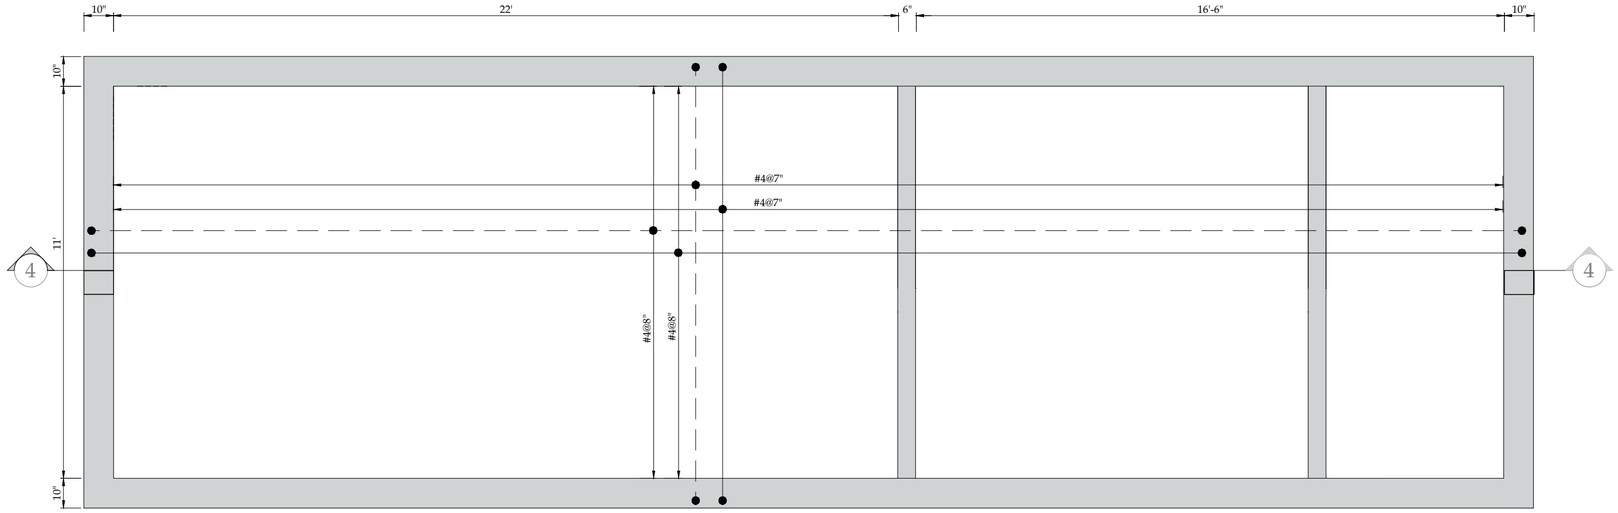

FOUNDATION LAYOUT PLAN

SCALE:- 3/8" = 1'-0"

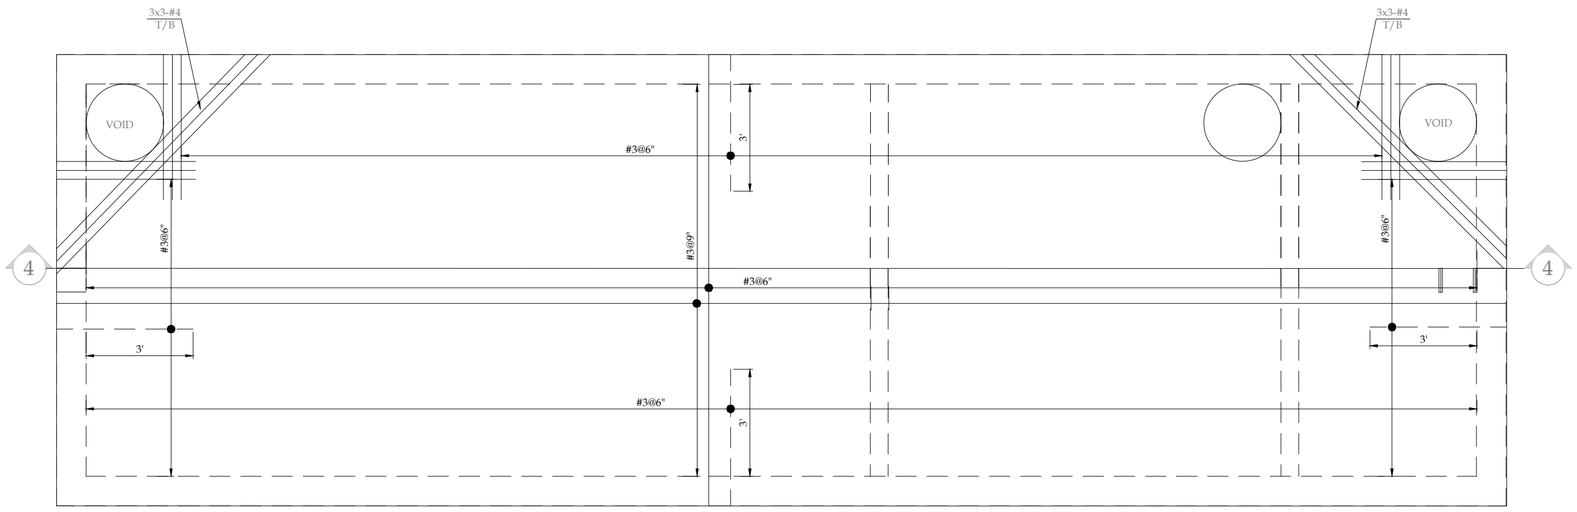

TOP SLAB=6" THICK

SCALE:- 3/8" = 1'-0"

NOTE:

1. DISTRIBUTION TOP BARS #3@12"c/c.

NOTES:

1. APPLY TWO COATS OF ConGuard CTE (COAL TAR EPOXY RESIGN INTERNAL SURFACE COATING 0.5 KG PER SQ.M) BY RADIANT CONSTRUCTION TECHNOLOGIES ON INNER SURFACES WHICH ARE IN DIRECT CONTACT WITH WATER

SPECIAL NOTES

1. THE FOUNDATION IS DESIGN USING ASSUMED BEARING CAPACITY OF 0.70 TSF. CONTRACTOR/CLIENT REQUIRED TO CONFIRM BEFORE EXECUTION OF WORK.
2. THE STRUCTURE IS DESIGNED ASSUMING THAT WATER TABLE IS AT 50'-0" FROM EXISTING GROUND LEVEL.
3. THE FOUNDATION DESIGN IS SUBJECT TO SOIL CONDITION, FINALIZED AS PER GEO-TECHNICAL SOIL INVESTIGATION REPORT.
4. THE BACK FILLING BEHIND WALL OF TANK SHALL NOT BE DONE BEFORE COSTING OF ROOF SLAB.

TITLE.

SEPTIC TANK STRUCTURAL
DETAIL-1
TYPE-IV

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	--

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	21-11-2025	DETAILED DESIGN	ASAD	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº: PRMSC-SEW-ST-S-05

SHEET 1 OF 1

REV 00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

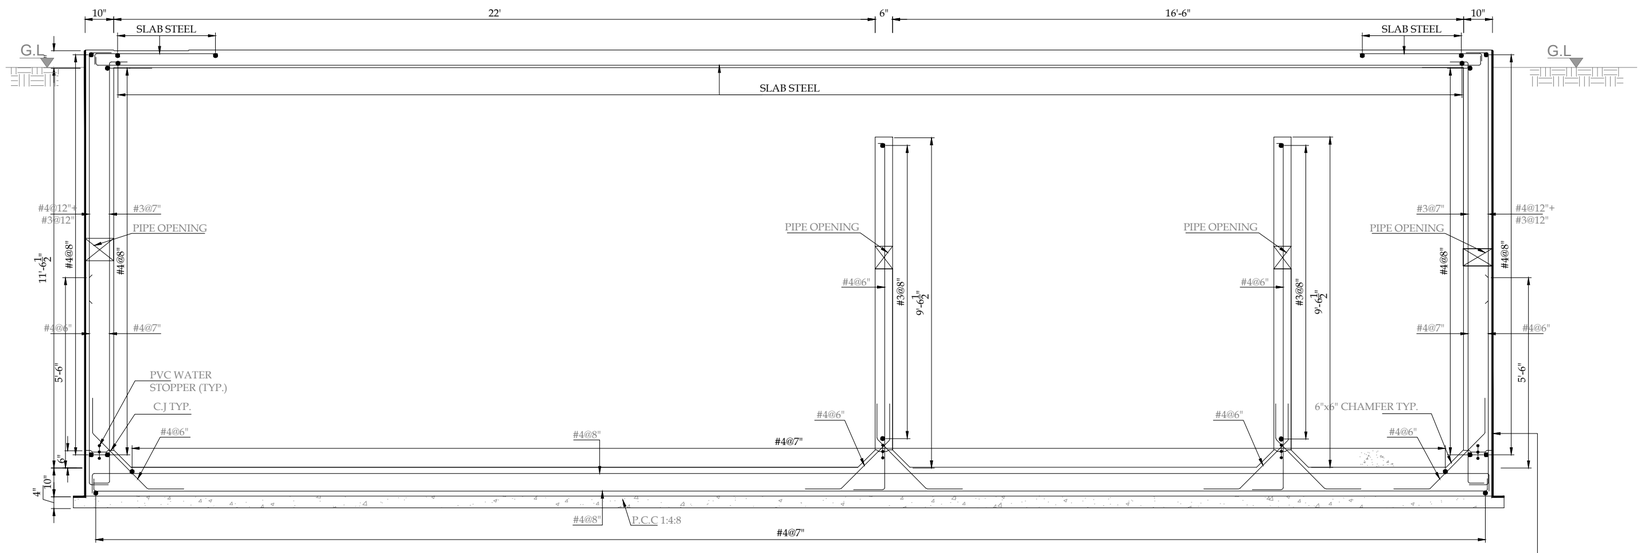

SECTION 4-4

SCALE:- 3/8" = 1'-0"

PROVIDING AND LAYING OF BITUMINOUS WATER PROOFING MEMBRANE 4MM THICK REINFORCED WITH ROT-PROOF, NON-WOVEN POLYESTER CARRIER OVER ONE COAT OF PRIMER GRIP CONFIRMS TO ATSM D41

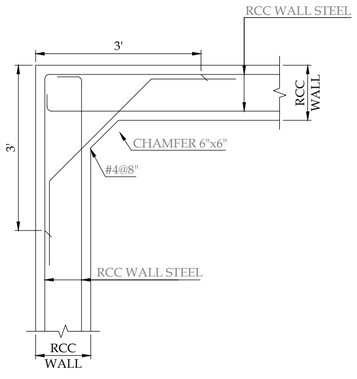

TYP. RCC WALL CORNER REINFORCEMENT DETAIL

SCALE:- 1/2" = 1'-0"

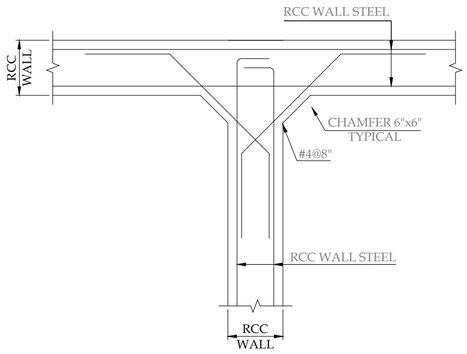

TYP. RCC WALL T-SHAPED REINFORCEMENT DETAIL

SCALE:- 1/2" = 1'-0"

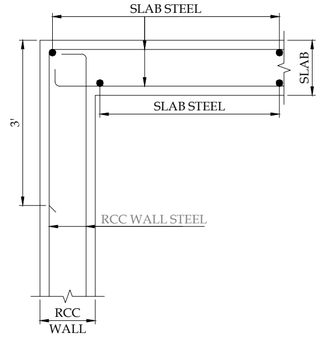

TYP. RCC WALL RCC SLAB CONNECTION DETAIL

SCALE:- 1/2" = 1'-0"

NOTES:

1. APPLY TWO COATS OF ConGuard CTE (COAL TAR EPOXY RESIGN INTERNAL SURFACE COATING 0.5 KG PER SQ.M) BY RADIANT CONSTRUCTION TECHNOLOGIES ON INNER SURFACES WHICH ARE IN DIRECT CONTACT WITH WATER

SPECIAL NOTES

1. THE FOUNDATION IS DESIGN USING ASSUMED BEARING CAPACITY OF 0.70 TSF. CONTRACTOR/CLIENT REQUIRED TO CONFIRM BEFORE EXECUTION OF WORK.
2. THE STRUCTURE IS DESIGNED ASSUMING THAT WATER TABLE IS AT 50'-0" FROM EXISTING GROUND LEVEL.
3. THE FOUNDATION DESIGN IS SUBJECT TO SOIL CONDITION, FINALIZED AS PER GEO-TECHNICAL SOIL INVESTIGATION REPORT.
4. THE BACK FILLING BEHIND WALL OF TANK SHALL NOT BE DONE BEFORE COSTING OF ROOF SLAB.

TITLE.

SEPTIC TANK STRUCTURAL DETAILS-2 TYPE-IV

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	--

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	21-11-2025	DETAILED DESIGN	ASAD	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-SEW-ST-S-06	1 OF 1	00

PROJECT:

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS www.asianco.com.pk

PRMSC-SEW-ST-S-01

SEPTIC TANK TYPE V

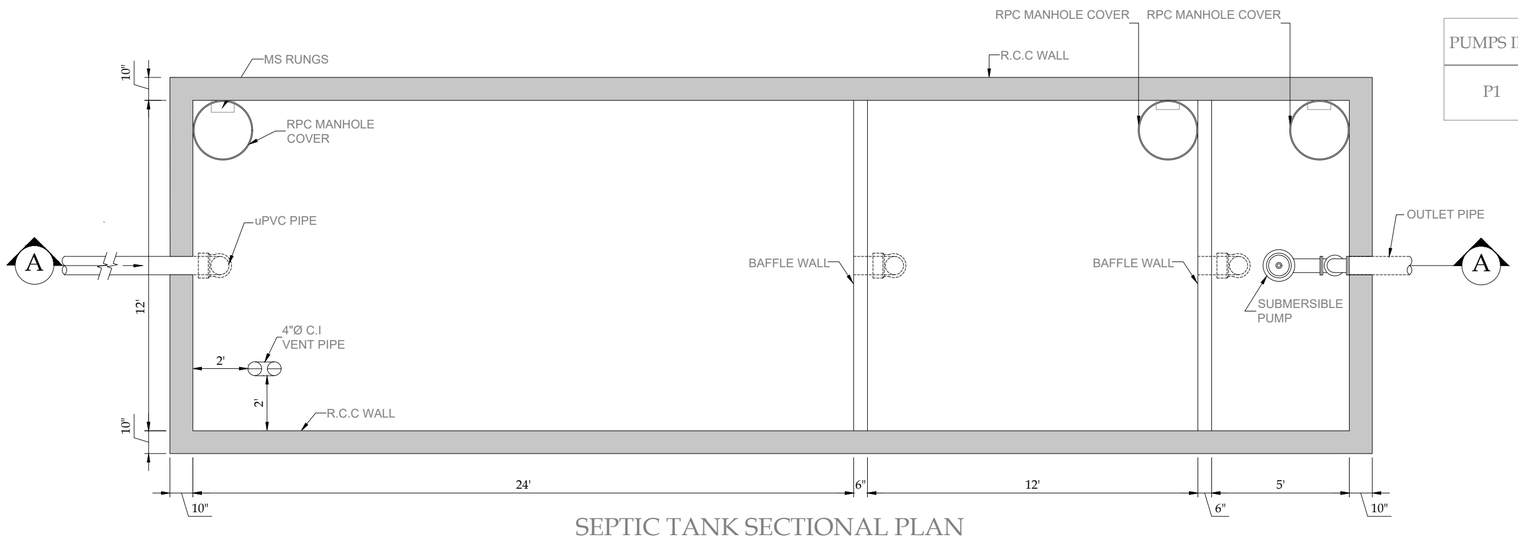

SEPTIC TANK SECTIONAL PLAN

SCALE:- 1/4" = 1'-0"

PUMPS ID	TYPE	FLOW	HEAD	STATUS
P1	NON CLOGGING SUBMERSIBLE PUMP	VARIABLE	VARIABLE	ON DUTY

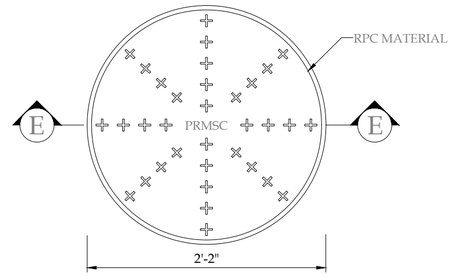

RPC MANHOLE COVER PLAN

SCALE:- 1" = 1'-0"

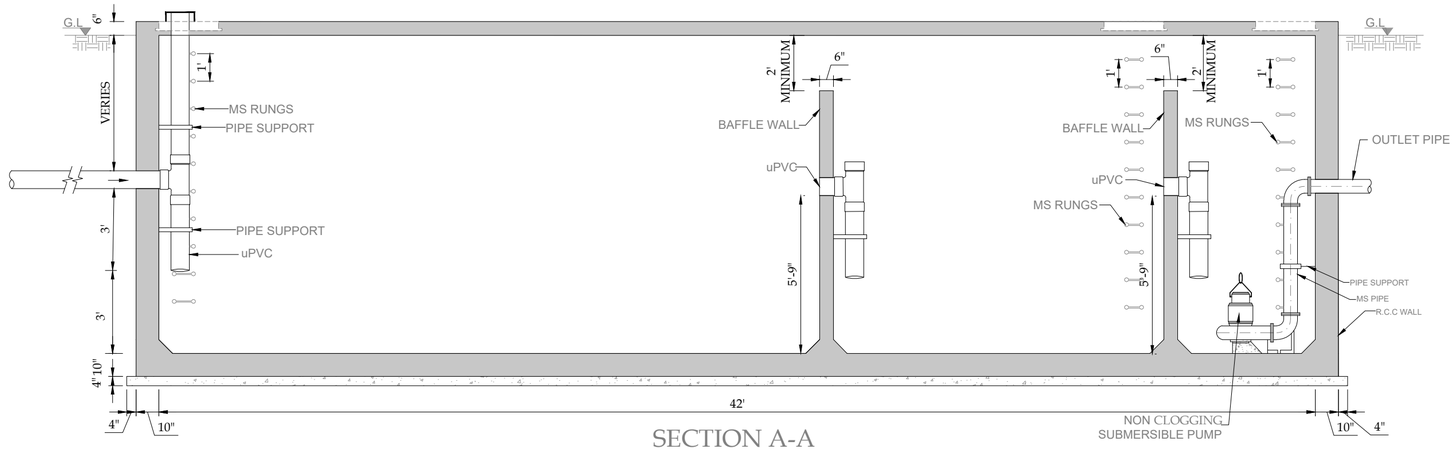

SECTION A-A

SCALE:- 1/4" = 1'-0"



SECTION AT E-E

SCALE:- 1" = 1'-0"



M.S IRON STEP

SCALE:- 1" = 1'-0"

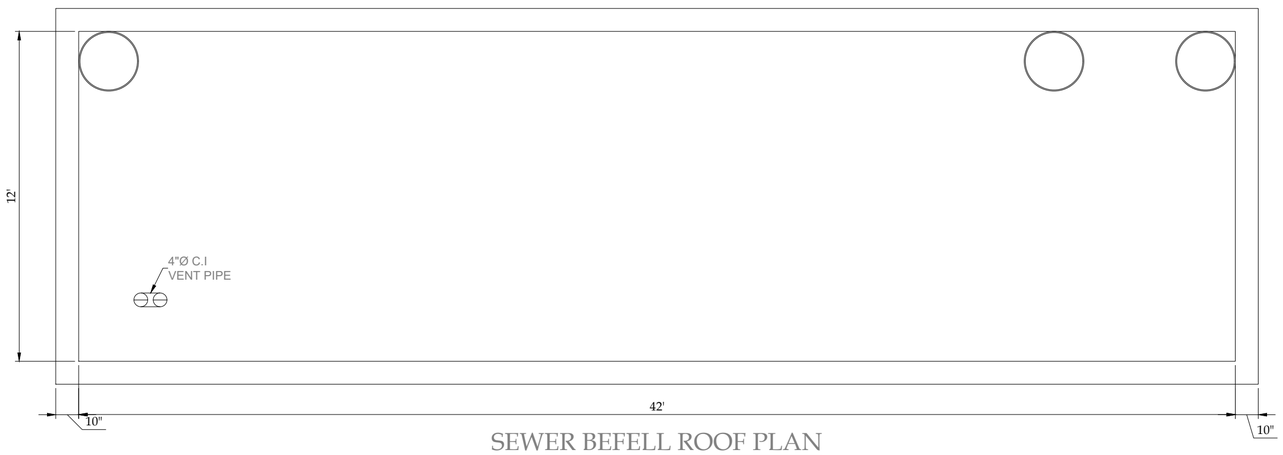

SEWER BEFELL ROOF PLAN

SCALE:- 1/4" = 1'-0"



ELEVATION

SCALE:- 1" = 1'-0"

NOTE

THE BOTTTOM OF THE CURB SHALL BE SUNK AT LEAST 4 FT. BELOW THE TOP OF FIRST LAYER OF SUITABLE SOIL STRATA ENCOUNTERED ALL GRANULAR SOILS, MEDIUM TO COARSE SAND OR GRAVEL SHALL BE CONSIDERED SUITABLE FOR THIS PURPUSE AND AS PER INSTRUCTION OF THE ENGINEER INCHARGE.

TITLE.

LAYOUT PLAN & SECTION OF SEPTIC TANK TYPE-V

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1/4" = 1'-0"

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	21-11-2025	DETAILED DESIGN	ASAD	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:

PRMSC-SEW-ST-C-04

SHEET 1 OF 1

REV 00

PROJECT:

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:

PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS www.asiancon.com.pk

PRMSC-SEW-ST-C-05

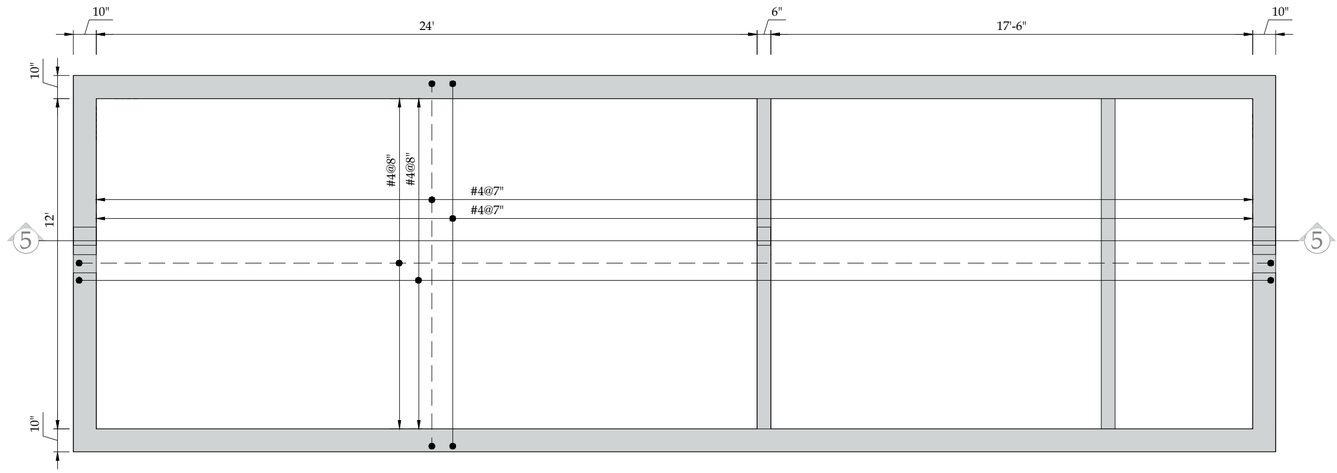

FOUNDATION LAYOUT PLAN

SCALE:- 1/4" = 1'-0"

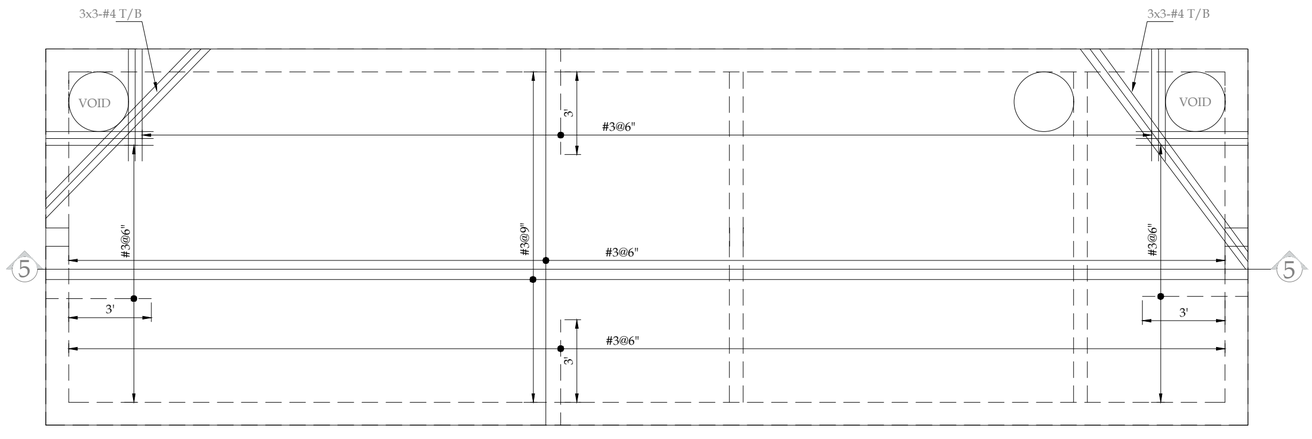

TOP SLAB=6" THICK

SCALE:- 1/4" = 1'-0"

NOTE:

1. DISTRIBUTION TOP BARS #3@12"c/c.

NOTES:

1. APPLY TWO COATS OF ConGuard CTE (COAL TAR EPOXY RESIGN INTERNAL SURFACE COATING 0.5 KG PER SQ.M) BY RADIANT CONSTRUCTION TECHNOLOGIES ON INNER SURFACES WHICH ARE IN DIRECT CONTACT WITH WATER

SPECIAL NOTES

1. THE FOUNDATION IS DESIGN USING ASSUMED BEARING CAPACITY OF 0.70 TSF. CONTRACTOR/CLIENT REQUIRED TO CONFIRM BEFORE EXECUTION OF WORK.
2. THE STRUCTURE IS DESIGNED ASSUMING THAT WATER TABLE IS AT 50'-0" FROM EXISTING GROUND LEVEL.
3. THE FOUNDATION DESIGN IS SUBJECT TO SOIL CONDITION, FINALIZED AS PER GEO-TECHNICAL SOIL INVESTIGATION REPORT.
4. THE BACK FILLING BEHIND WALL OF TANK SHALL NOT BE DONE BEFORE COSTING OF ROOF SLAB.

TITLE.

SEPTIC TANK
STRUCTURAL DETAIL-1
TYPE-V

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	--

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	21-11-2025	DETAILED DESIGN	ASAD	ENGR. FAIEZ	ENGR. HSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:	SHEET	REV
PRMSC-SEW-ST-S-07	1 OF 1	00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS www.asianconsultingengineers.com

PRMSC-SEW-ST-S-01 (2)

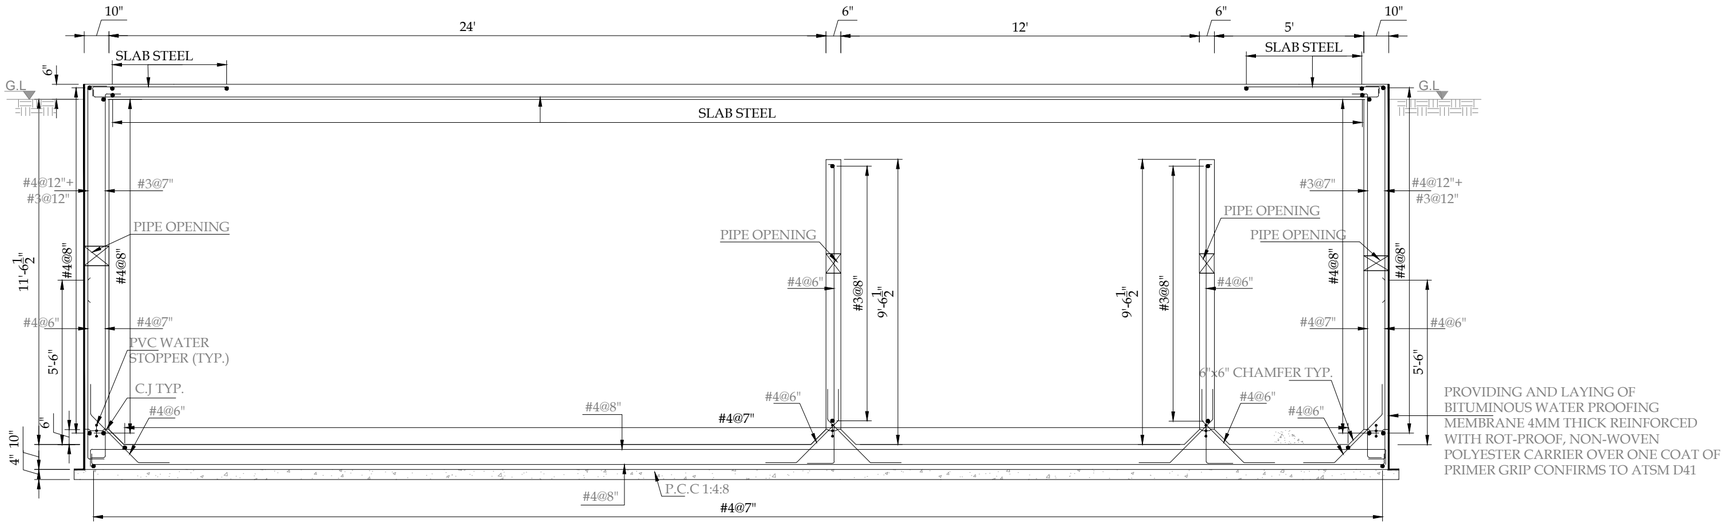

SECTION 5-5

SCALE:- 1/4" = 1'-0"

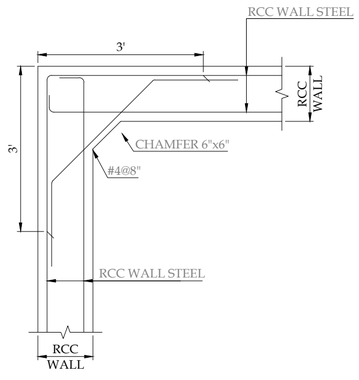

TYP. RCC WALL CORNER REINFORCEMENT DETAIL

SCALE:- 1/2" = 1'-0"

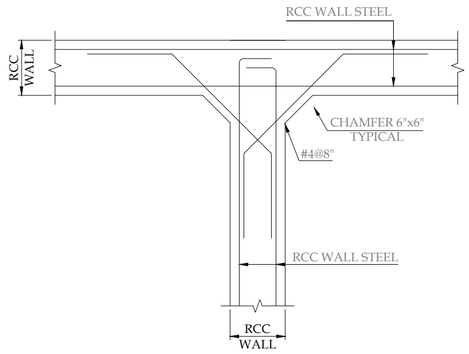

TYP. RCC WALL T-SHAPED REINFORCEMENT DETAIL

SCALE:- 1/2" = 1'-0"

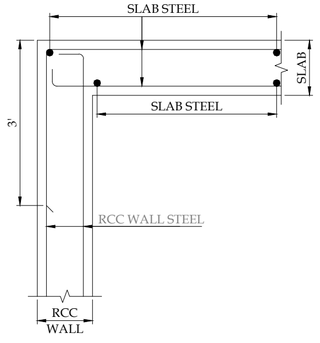

TYP. RCC WALL RCC SLAB CONNECTION DETAIL

SCALE:- 1/2" = 1'-0"

NOTES:

1. APPLY TWO COATS OF ConGuard CTE (COAL TAR EPOXY RESIGN INTERNAL SURFACE COATING 0.5 KG PER SQ.M) BY RADIANT CONSTRUCTION TECHNOLOGIES ON INNER SURFACES WHICH ARE IN DIRECT CONTACT WITH WATER

SPECIAL NOTES

1. THE FOUNDATION IS DESIGN USING ASSUMED BEARING CAPACITY OF 0.70 TSF. CONTRACTOR/CLIENT REQUIRED TO CONFIRM BEFORE EXECUTION OF WORK.
2. THE STRUCTURE IS DESIGNED ASSUMING THAT WATER TABLE IS AT 50'-0" FROM EXISTING GROUND LEVEL.
3. THE FOUNDATION DESIGN IS SUBJECT TO SOIL CONDITION, FINALIZED AS PER GEO-TECHNICAL SOIL INVESTIGATION REPORT.

TITLE.

SEPTIC TANK
STRUCTURAL DETAILS-2
TYPE-V

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	--

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	21-11-2025	DETAILED DESIGN	ASAD	ENGR. FAIEZ	ENGR. HSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº: PRMSC-SEW-ST-S-08

SHEET 1 OF 1

REV 00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS www.asiancon.com

PRMSC-SEW-ST-S-01

SEPTIC TANK TYPE VI

PUMPS ID	TYPE	FLOW	HEAD	STATUS
P1	NON CLOGGING SUBMERSIBLE PUMP	VARIABLE	VARIABLE	ON DUTY

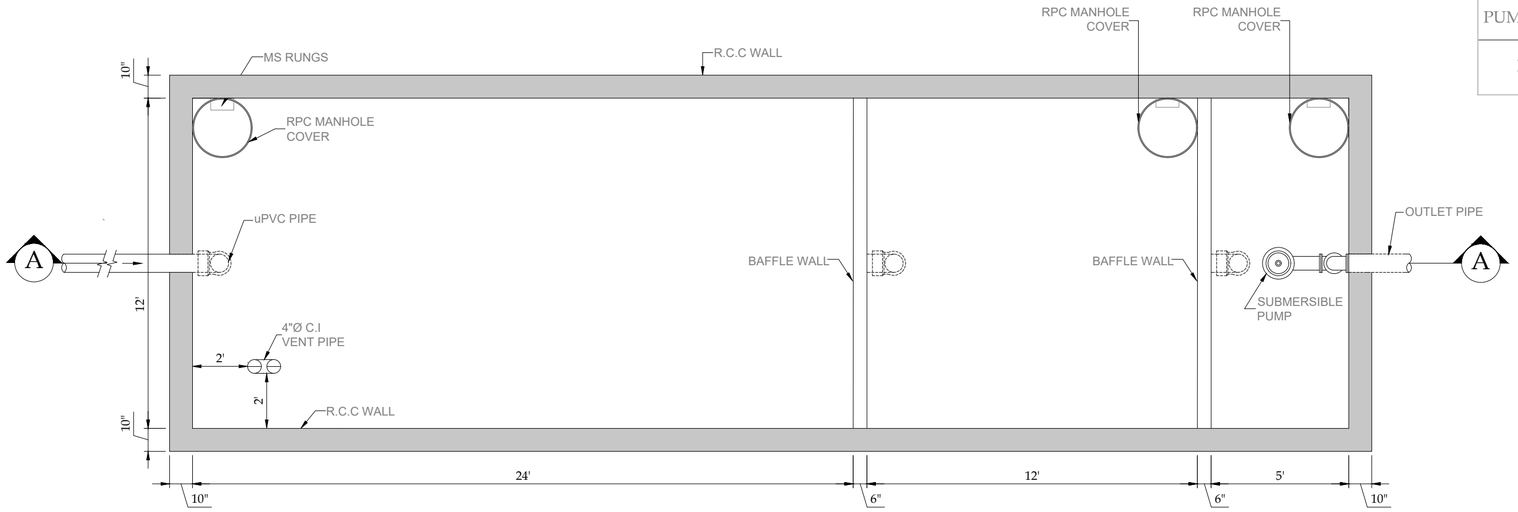

SEPTIC TANK SECTIONAL PLAN

SCALE:- 1/4" = 1'-0"

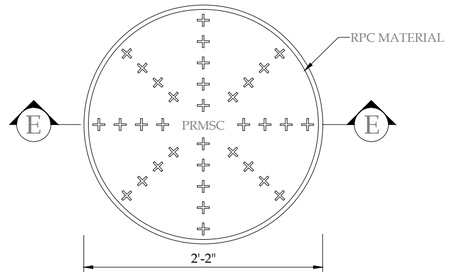

RPC MANHOLE COVER PLAN

SCALE:- 1" = 1'-0"

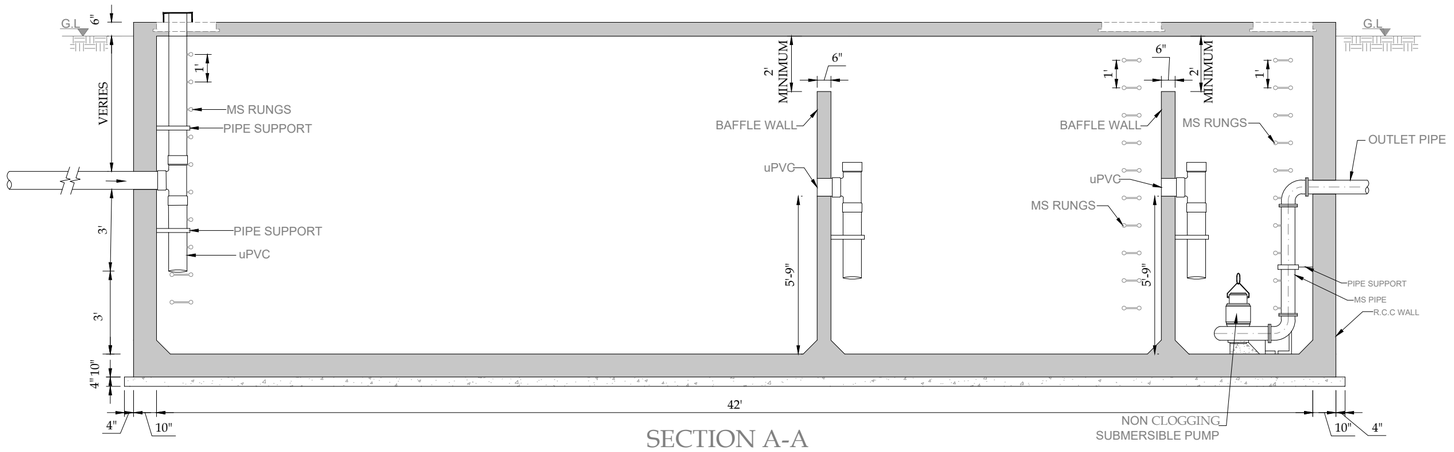

SECTION A-A

SCALE:- 1/4" = 1'-0"



SECTION AT E-E

SCALE:- 1" = 1'-0"

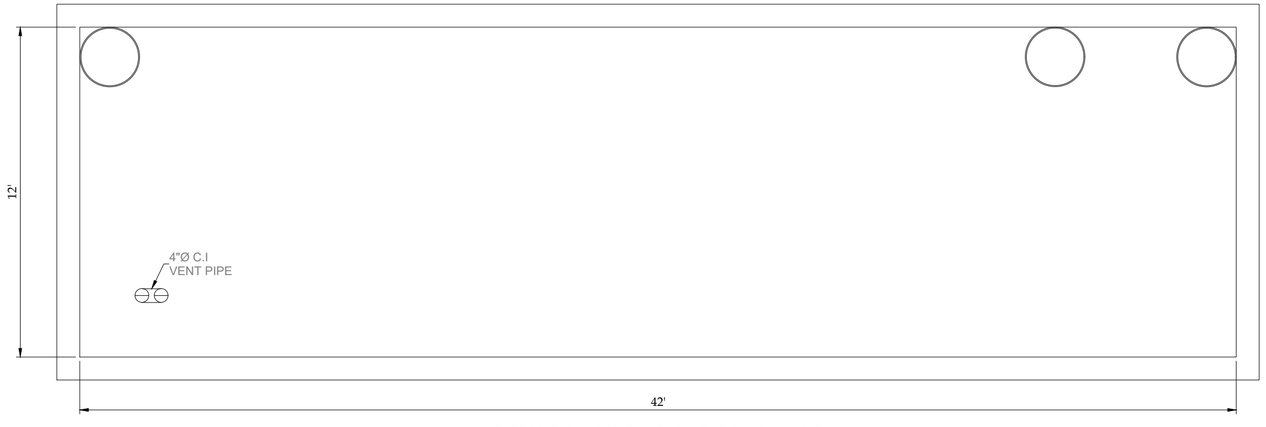

SEWER BEFELL ROOF PLAN

SCALE:- 1/4" = 1'-0"



M.S IRON STEP

SCALE:- 1" = 1'-0"



ELEVATION

SCALE:- 1" = 1'-0"

NOTE

THE BOTTTOM OF THE CURB SHALL BE SUNK AT LEAST 4 FT. BELOW THE TOP OF FIRST LAYER OF SUITABLE SOIL STRATA ENCOUNTERED ALL GRANULAR SOILS, MEDIUM TO COARSE SAND OR GRAVEL SHALL BE CONSIDERED SUITABLE FOR THIS PURPUSE AND AS PER INSTRUCTION OF THE ENGINEER INCHARGE.

TITLE.

LAYOUT PLAN & SECTION OF SEPTIC TANK TYPE-VI

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	1/4" = 1'-0"

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	21-11-2025	DETAILED DESIGN	ASAD	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº:

PRMSC-SEW-ST-C-05

SHEET 1 OF 1

REV 00

PROJECT:

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:

PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS www.asiancon.com

PRMSC-SEW-ST-C-05

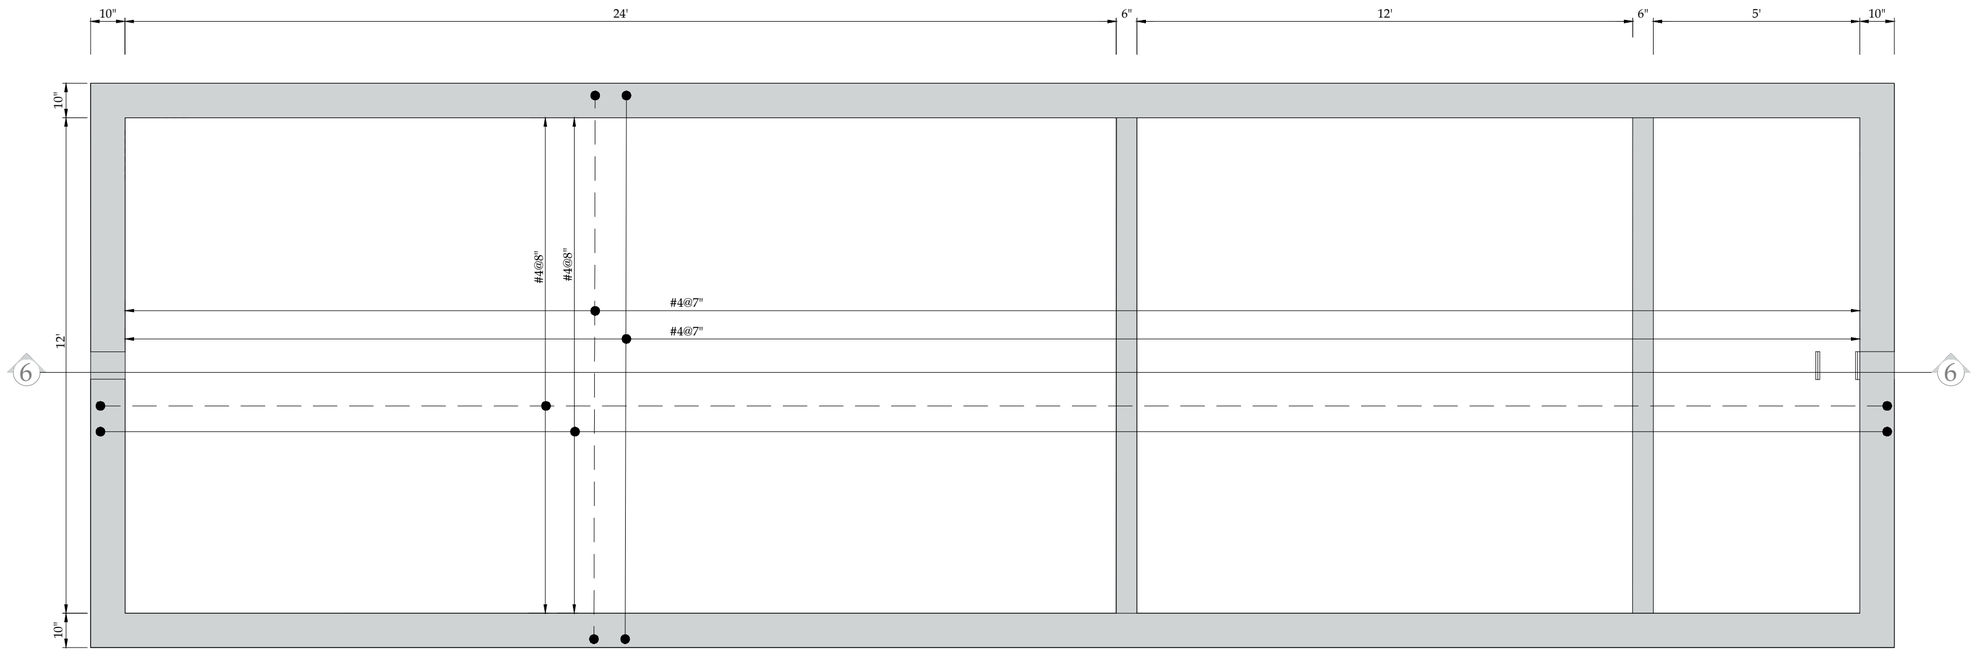

FOUNDATION LAYOUT PLAN

SCALE:- 3/8" = 1'-0"

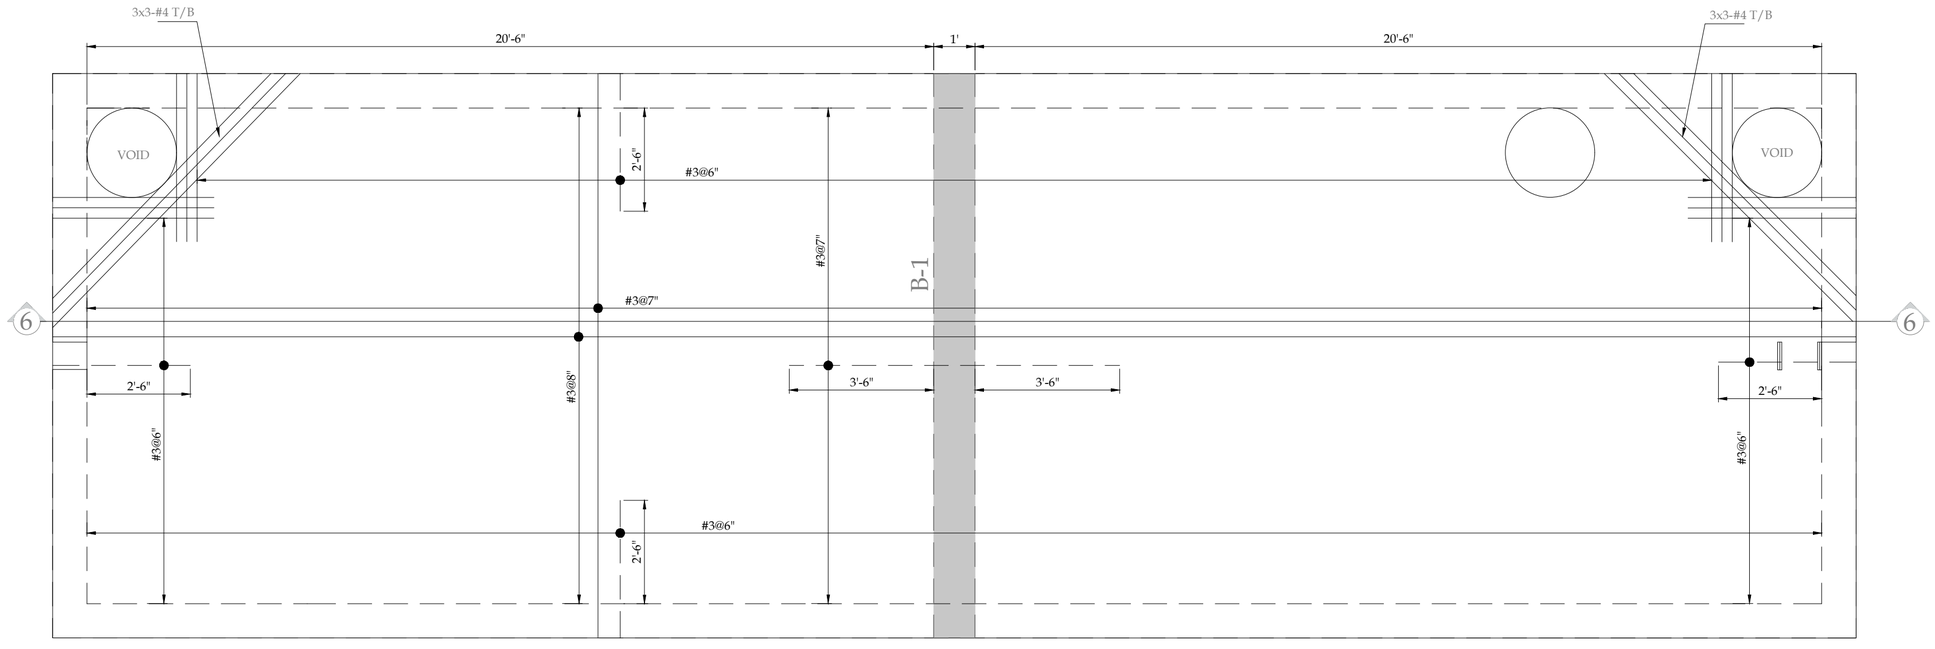

TOP SLAB=6" THICK

SCALE:- 3/8" = 1'-0"

NOTE:

1. DISTRIBUTION TOP BARS #3@12"c/c.

NOTES:

1. APPLY TWO COATS OF ConGuard CTE (COAL TAR EPOXY RESIGN INTERNAL SURFACE COATING 0.5 KG PER SQ.M) BY RADIANT CONSTRUCTION TECHNOLOGIES ON INNER SURFACES WHICH ARE IN DIRECT CONTACT WITH WATER

SPECIAL NOTES

1. THE FOUNDATION IS DESIGN USING ASSUMED BEARING CAPACITY OF 0.70 TSF. CONTRACTOR/CLIENT REQUIRED TO CONFIRM BEFORE EXECUTION OF WORK.
2. THE STRUCTURE IS DESIGNED ASSUMING THAT WATER TABLE IS AT 50'-0" FROM EXISTING GROUND LEVEL.
3. THE FOUNDATION DESIGN IS SUBJECT TO SOIL CONDITION, FINALIZED AS PER GEO-TECHNICAL SOIL INVESTIGATION REPORT.
4. THE BACK FILLING BEHIND WALL OF TANK SHALL NOT BE DONE BEFORE COSTING OF ROOF SLAB.

TITLE.

SEPTIC TANK
STRUCTURAL DETAIL-1
TYPE-VI

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	--

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	21-11-2025	DETAILED DESIGN	ASAD	ENGR. FAIEZ	ENGR. HSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº: PRMSC-SEW-ST-S-09

SHEET 1 OF 1

REV 00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:
ASIAN CONSULTING ENGINEERS
www.asianconsulting.com.pk

PRMSC-SEW-ST-S-01 (2)

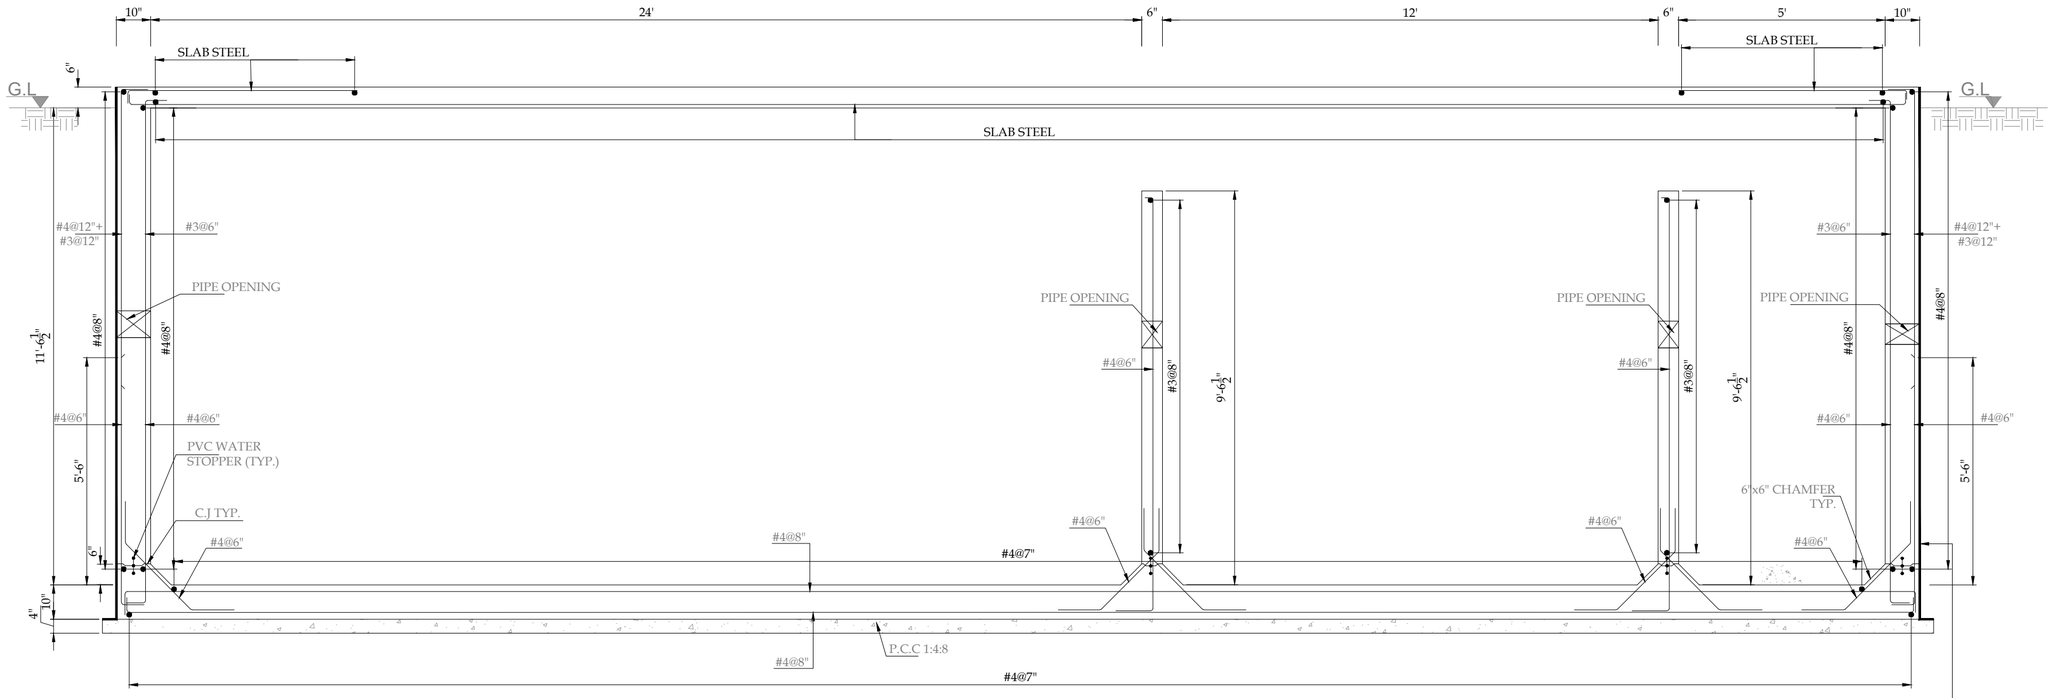

SECTION 6-6

SCALE:- 3/8" = 1'-0"

PROVIDING AND LAYING OF BITUMINOUS WATER PROOFING MEMBRANE 4MM THICK REINFORCED WITH ROT-PROOF, NON-WOVEN POLYESTER CARRIER OVER ONE COAT OF PRIMER GRIP CONFIRMS TO ATSM D41

NOTES:

1. APPLY TWO COATS OF ConGuard CTE (COAL TAR EPOXY RESIGN INTERNAL SURFACE COATING 0.5 KG PER SQ.M) BY RADIANT CONSTRUCTION TECHNOLOGIES ON INNER SURFACES WHICH ARE IN DIRECT CONTACT WITH WATER

SPECIAL NOTES

1. THE FOUNDATION IS DESIGN USING ASSUMED BEARING CAPACITY OF 0.70 TSF. CONTRACTOR/CLIENT REQUIRED TO CONFIRM BEFORE EXECUTION OF WORK.
2. THE STRUCTURE IS DESIGNED ASSUMING THAT WATER TABLE IS AT 50'-0" FROM EXISTING GROUND LEVEL.
3. THE FOUNDATION DESIGN IS SUBJECT TO SOIL CONDITION, FINALIZED AS PER GEO-TECHNICAL SOIL INVESTIGATION REPORT.
4. THE BACK FILLING BEHIND WALL OF TANK SHALL NOT BE DONE BEFORE COSTING OF ROOF SLAB.

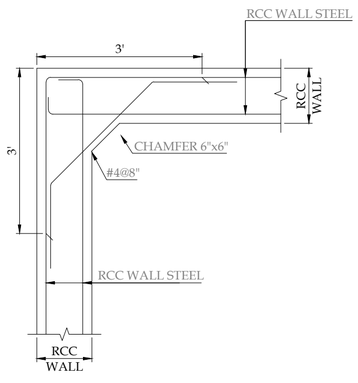

TYP. RCC WALL CORNER REINFORCEMENT DETAIL

SCALE:- 1/2" = 1'-0"

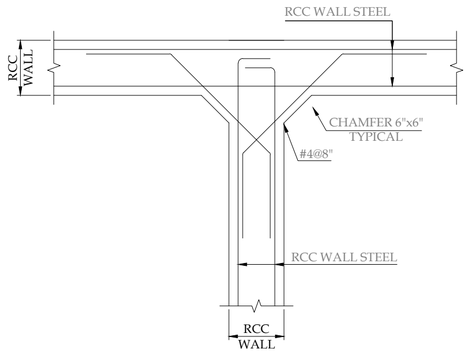

TYP. RCC WALL T-SHAPED REINFORCEMENT DETAIL

SCALE:- 1/2" = 1'-0"

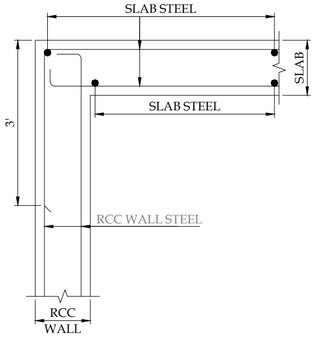

TYP. RCC WALL RCC SLAB CONNECTION DETAIL

SCALE:- 1/2" = 1'-0"



BEAM B-1

SCALE:- 1" = 1'-0"

TITLE.

SEPTIC TANK
STRUCTURAL DETAILS-2
TYPE-VI

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	--

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	21-11-2025	DETAILED DESIGN	ASAD	ENGR. FAIEZ	ENGR. IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº: PRMSC-SEW-ST-S-10

SHEET 1 OF 1

REV 00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS www.asiancon.com

PRMSC-SEW-ST-S-01

A. GENERAL

1- READ ALL DRAWINGS IN CONJUNCTION WITH ARCHITECTURAL, CIVIL, MECHANICAL, ELECTRICAL & ANY OTHER RELEVANT DRAWING.

2- NOTES, GIVEN IN THIS DRAWING, ARE APPLICABLE TO ALL DRAWINGS UNLESS MENTIONED OTHERWISE. NOTES WRITTEN ON A DRAWING, SHALL BE APPLICABLE TO THAT PARTICULAR DRAWING ONLY UNLESS OTHERWISE CROSS-REFERRED.

3- ALL MATERIAL AND WORKMANSHIP SHALL CONFORM TO CONTRACT SPECIFICATIONS. IN THE ABSENCE OF ANY SPECIFICATIONS , ALL MATERIALS & WORKMANSHIP SHALL CONFORM TO RELEVANT BRITISH/ACI CODES AND SHALL SUBJECT TO APPROVAL OF THE ENGINEER.

4- THE CONTRACTOR SHALL BE RESPONSIBLE FOR THE SAFETY OF THE STRUCTURES DURING CONSTRUCTION. HE SHALL ALSO VERIFY ALL DIMENSIONS AND LEVELS BEFORE EXECUTION OF WORK. ANY DISCREPANCY, ERROR OR OMISSION, IF FOUND SHALL BE BROUGHT TO THE NOTICE OF THE ENGINEER FOR CORRECTION AND APPROVAL.

5- THE CONTRACTOR SHALL CO-ORDINATE WITH ARCHITECTURAL AND VARIOUS SERVICES DRAWINGS FOR SIZES & LOCATION OF ALL STRUCTURAL MEMBERS, FLOORS, WALLS, OPENINGS, FLOOR FINISHES, PIPES ETC.

6- THE CONTRACTOR SHALL BE RESPONSIBLE FOR THE EXECUTION OF DEWATERING SYSTEM WHERE SO REQUIRED DURING CONSTRUCTION.COST DEEMED TO BE INCLUDED IN OTHER COST DEEMED ITEMS.

7- TERMITE CONTROL TREATMENT SHALL BE CARRIED OUT IN ALL BUILDINGS/ STRUCTURES

8- ALL LEVELS AND DIMENSIONS ARE IN FEET & INCHES UNLESS OTHERWISE NOTED.

9- DO NOT SCALE THE DRAWINGS. DIMENSIONS, GIVEN ON THE DRAWING, SHALL GOVERN.

10- ALL FABRICATION, PAINTING, ERECTION AND QUALITY CONTROL IS TO BE DONE IN ACCORDANCE WITH THE LATEST APPLICABLE SPECIFICATIONS/ BRITISH STANDARDS.

11- APPLY TWO COATS OF ConGuard CTE (COAL TAR EPOXY RESIGN INTERNAL SURFACE COATING 0.5 KG PER SQ.M) BY RADIANT CONSTRUCTION TECHNOLOGIES ON INNER SURFACES WHICH ARE IN DIRECT CONTACT WITH WATER.

B. FOUNDATION

1- THE DESIGN OF FOUNDATION IS BASED ON ASSUMED BEARING CAPACITY 0.7 TSF. CONTRACTOR/CLIENT REQUIRED TO CONFIRM BEFORE EXECUTION OF WORK.

2- BEFORE LAYING OF FOUNDATION ALL EXCAVATED AREA SHOULD BE INSPECTED BY THE ENGINEER FOR COMMENCEMENT OF WORKS.

3- COMPACTED SAND FILL (THE ENGINEER FILL MATERIAL OF A-3 TYPE AS PER AASHTO SOIL CLASSIFICATION) UP TO 95% MODIFIED PROCTOR DENSITY

4- PROVIDING AND LAYING OF DAMP PROOF COURSE OF CEMENT CONCRETE (1:2:4) INCLUDING 2 COATS OF HOT BITUMEN

5- THE STRUCTURE IS DESIGNED ASSUMING THAT WATER TABLE IS AT 50'-0" FROM EXISTING GROUND LEVEL.

C. DESIGN & LOADS

1- STRUCTURAL DESIGN IS BASED ON THE BUILDING CODE OF PAKISTAN & AMERICAN CONCRETE INSTITUTE CODE OF REINFORCED CONCRETE (ACI 318-08) AND APPROVED DESIGN CRITERIA

D. REINF. CONCRETE WORKS

1- ALL STRUCTURAL CONCRETE SHALL CONFORM TO AMERICAN STANDARD.

2- USE CONCRETE HAVING 4000 Psi CYLINDER STRENGTH FOR ALL STRUCTURAL MEMBERS

4- WATER CEMENT RATIO SHALL NOT EXCEED 0.50 OR AS INCLUDED IN CONTRACT SPECIFICATIONS.

5- NO CONCRETING SHALL BE CARRIED OUT UNTIL PERMISSION IS GIVEN IN WRITING TO DO SO BY THE ENGINEER.

6- ALL REINFORCEMENT FOR FOUNDATION, COLUMNS, WALLS, BEAMS & SLABS SHALL BE HIGH STRENGTH DEFORMED STEEL GRADE 60 WITH A MINIMUM YIELD STRENGTH OF 60,000 psi, UNLESS OTHERWISE MENTIONED

7- ALL REINFORCEMENT SHOULD BE BENT COLD

E. MISCELLANEOUS WORKS

1- THE CONTRACTOR SHALL SUBMIT CONCRETE POURING SCHEDULE FOR ENGINEER'S APPROVAL. NO CONCRETE SHALL BE PLACED UNTIL WRITTEN PERMISSION IS GIVEN BY THE ENGINEER.

2- DURING CONSTRUCTION, STACKING OF CONSTRUCTION MATERIALS, BLOCKS, etc. SHOULD BE AVOIDED ON SLAB PANELS.

3- BEFORE CASTING OF ANY STRUCTURAL MEMBER, THE CONTRACTOR SHALL ENSURE THAT ALL EMBEDDED ITEMS FOR ELECTRICAL, MECHANICAL, HVAC, PLUMBING, STRUCTURAL STEEL AND OTHER WORKS ARE PROPERLY LOCATED IN PLACE.

4- THE CONNECTION OF COLUMN & MASONRY SHALL BE BY G.I. SHEET 4" WIDE, GAUGE 22 EXTENDING 3 FEET FROM FACE OF COLUMN, IN TWO LAYERS, 6 SHEETS ON EACH COLUMN (PER STOREY), 3 ON EITHER SIDE

5- IN 4" THICK WALLS, A REINFORCEMENT OF 1" WIDE 18 GAUGE HOOP IRON SHALL BE PLACED IN COURSES NOT MORE THAN 12" APART AND CONTINUED FOR 9" INTO THE MAIN WALL ON WHICH THE PARTITION WALL ABUTS. IF THE PARTITION WALL EXCEEDS 20' IN LENGTH OR 15' HEIGHT, THE HOOP IRON SHALL BE INTRODUCED AT COURSES NOT MORE THAN 6" APART.

9- CLEAR COVER TO REINFORCEMENT SHALL BE: (inches)

STRUCTURAL ELEMENT	COVER (INCHES)
BASE SLAB / RAFT: a) BOTTOM SIDE b) TOP SIDE c) SIDES	 2 2 3
BEAMS	1½
COLUMNS	1½
12" THICK FLOOR SLABS, POTABLE WATER TANK BASE & ROOF SLABS: a) BOTTOM SIDE b) TOP SIDE	 3/4 3/4
ROOF SLAB: a) BOTTOM SIDE b) TOP SIDE	 3/4 1
EXTERNAL WALLS: a) OUTER FACE b) INNER FACE NOTE: CLEAR COVER IN PORTION OF EXTERNAL WALLS FORMING INTERNAL PART OF DUCTS WILL REMAIN SAME AS FOR EXTERNAL WALL.	 2 1
ALL INTERNAL WALLS: (3'-0" THICK, 18"-THICK,12"-THICK, 6"-THICK): a) OUTER FACE b) INNER FACE	 3/4 3/4

10- ALL REINF. STEEL SHALL BE ACCURATELY LOCATED IN THE FORMS AND HELD FIRMLY IN PLACE BEFORE & DURING THE PLACING OF CONCRETE, BY MEANS OF WIRE AND SUPPORTS ADEQUATE TO PREVENT DISPLACEMENT DURING THE COURSE OF CONSTRUCTION.

F. CONSTRUCTION JOINTS

1- JOINTS, NOT SHOWN ON THE DRAWING, SHALL BE SO MADE AND LOCATED AS TO LEAST IMPAIR THE STRENGTH OF THE STRUCTURE AND SHALL NEED PRIOR APPROVAL OF THE ENGINEER. THEY SHALL BE LOCATED NEAR THE MIDDLE OF THE SPANS OF SLAB & BEAMS. JOINT IN WALLS & COLUMNS SHALL BE AT THE UNDER-SIDE OF FLOORS, SLABS OR BEAMS AND AT THE TOP OF FOOTINGS OR FLOOR SLABS

2- JOINTS SHALL BE PERPENDICULAR TO MAIN REINFORCEMENT. ALL REINFORCING STEEL SHALL BE CONTINUED ACROSS JOINTS.

3- JOINTS IN THE BASE SLAB & WALLS AND ROOF SLAB, IN ADDITION TO THOSE SHOWN ON THE DRAWINGS SHALL BE BORNE BY THE CONTRACTOR. BEAMS & BRACKETS SHALL BE PLACED AT THE SAME TIME AS SLABS.

G. ELECTRICAL & COMMUNICATION SYSTEMS

1- CONDUITS, FOR ELECTRICAL WORKS, SHALL BE PLACED WITHIN THE REINFORCED CONCRETE. THEY SHALL BE PLACED WITHIN THE MIDDLE THIRD OF THE SECTION IN BEAMS & SLABS AND WITHIN THE MIDDLE HALF OF THE THICKNESS. SPACING BETWEEN PARALLEL CONDUITS SHALL NOT BE LESS THAN 6 INCHES.

2- THE CONTRACTOR WILL PREPARE SHOP DRAWINGS FOR ALL THE ELECTRICAL & COMMUNICATION SYSTEMS FOR THE PROJECT MANAGER APPROVED BEFORE EXECUTION OF WORK.

3- SAMPLES / TECHNICAL DATA FOR ALL THE ITEMS WILL BE SUBMITTED & APPROVED BY THE PROJECT ENGINEER BEFORE PROCUREMENT.

4- THE WORK WILL BE CARRIED OUT THROUGH APPROVED ELECTRICAL CONTRACTOR HAVING A VALID ELECTRICAL LICENCE OF THE AREA.

5- CONTRACTOR WILL PROVIDE TEST REPORT DULY VERIFIED FROM THE ELECTRICAL INSPECTOR OF THE AREA.

6- THE CONTRACTOR WILL USE MATERIALS OF APPROVED MAKE & VENDORS / MANUFACTURERS.

H. SHORING & BRACING

1- SHORE & BRACE ALL PARTS OF THE BUILDING DURING CONSTRUCTION, TO THE EXTENT NECESSARY TO ENSURE COMPLETE SAFETY, STRENGTH & SERVICEABILITY OF ALL STRUCTURAL ELEMENTS UNDER ALL CONDITIONS OF LOADS WHICH MAY OCCUR DURING CONSTRUCTION. SUCH SHORING & BRACING IS THE CONTRACTOR'S SOLE RESPONSIBILITY AND IS NOT SHOWN ON STRUCTURAL DRAWINGS OR SPECIFIED IN THE PROJECT.

I. WATER RETAINING STRUCTURES

1- WATER PROOFING ADMIXTURE OF APPROVED BRAND/TYPE WILL BE ADDED TO CEMENT CONCRETE OF WATER TANK, THE COST DEEMED TO BE INCLUDED IN THE RESPECTIVE ITEM OF CEMENT CONCRETE. THE PERFORMANCE OF TANK WITH RESPECT TO LEAKAGE WILL BE THE RESPONSIBILITY OF THE CONTRACTOR; ADDITIONAL PROTECTION IF SO REQUIRED TO MAKE IT WATER PROOF WILL BE APPLIED SUBJECTED TO ENGINEER APPROVAL. NO ADDITIONAL COST OF THIS TREATMENT IF SO REQUIRED WILL BE PAYABLE.

VERTICAL BAR SPACING



BAR SPACING IN BEAM



REINFORCEMENT AROUND SLEEVE IN SLAB & WALLS (TYP)

(NOTE: FOLLOW ABOVE REINFORCEMENT PATTERN ONLY IF NOT SPECIFICALLY SHOWN ON RESPECTIVE DESIGN / REINF. DETAIL DRAWINGS)



REINFORCEMENT DETAIL AT OPENING IN SLAB & WALLS (TYP)

(NOTE: FOLLOW ABOVE REINFORCEMENT PATTERN ONLY IF NOT SPECIFICALLY SHOWN ON RESPECTIVE DESIGN / REINF. DETAIL DRAWINGS)

NOTES

- FOR OPENING WITH MAXIMUM DIMENSION OVER 5'-0" REFER TO OTHER DETAILS.
- USE THIS DETAILS IF NOT SHOWN IN DESIGN DRAWINGS



SECTION A-A

WJT-WS-OHR-GN-01

TITLE.

GENERAL NOTES-I

ORIGINAL :		DATE :		SCALE :	
A2		JULY, 2025		-	
ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	21-11-2025	DETAILED DESIGN	ASAD	ENGR FAIEZ	ENGR IHSAN-UL-HAQ
02					
03					
04					
05					
06					
07					

DRAWING N°:	SHEET	REV
PRMSC-SEW-STP-GN-01	01 OF 02	00

PROJECT:
ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT:
PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:
ASIAN CONSULTING ENGINEERS
www.asiancon.com.pk

LAP LENGTH (INCHES)FOR GRADE 60, UNCOATED,OTHER THAN TOP BARS

BAR NO.	F'C (NORMAL WEIGHT CONCRETE) , PSI	
	3000	4000
3	21	18
4	27	24
5	36	30
6	42	36
7	63	54
8	72	63

LAP LENGTH INCHES)FOR GRADE 60, UNCOATED TOP BARS

BAR NO.	F'C (NORMAL WEIGHT CONCRETE) , PSI	
	3000	4000
3	27	24
4	39	33
5	48	42
6	54	48
7	81	72
8	93	81

DEVELOPMENT LENGTH (INCHES) IN TENSION OF TOP BARS

BAR NO.	F'C (NORMAL WEIGHT CONCRETE) , PSI	
	3000	4000
3	21	18
4	30	24
5	36	33
6	42	36
7	63	54
8	72	63

DEVELOPMENT LENGTH (INCHES) IN TENSION OF BOTTOM BARS

BAR NO.	F'C (NORMAL WEIGHT CONCRETE) , PSI	
	3000	4000
3	18	15
4	21	18
5	27	24
6	33	30
7	48	42
8	54	48

DEVELOPMENT LENGTH ldh (INCHES) OF STANDARD HOOKS FOR UNCOATED GRADE 60 BARS*

BAR NO.	F'C (NORMAL WEIGHT CONCRETE) , PSI					
	3000	4000	5000	6000	8000	10,000
3	8.2	7.1	6.4	5.8	5.0	4.5
4	11.0	9.5	8.5	7.7	6.7	6.0
5	13.7	11.9	10.6	9.7	8.4	7.5
6	16.4	14.2	12.7	11.6	10.1	9.0
7	19.2	16.6	14.8	13.6	11.7	10.5
8	21.9	19.0	17.0	15.5	13.4	12.0
9	24.7	21.4	19.1	17.5	15.1	13.5
10	27.8	24.1	21.6	19.7	17.0	15.2
11	30.9	26.8	23.9	21.8	18.9	16.9
14	37.1	32.1	28.7	26.2	22.7	20.3
18	49.5	42.8	38.3	35.0	30.3	27.1

EQUIVALENT DIAMETERS OF BUNDLED BARS, IN.

BAR NO	BAR DIAMETER	2-BAR BUNDLE	3-BAR BUNDLE	4-BAR BUNDLE
6	0.750	1.06	1.30	1.50
7	0.875	1.24	1.51	1.75
8	1.000	1.42	1.74	2.01
9	1.128	1.60	1.95	2.26
10	1.270	1.80	2.20	2.54
11	1.410	1.99	2.44	2.82
14	1.693	2.39	2.93	3.39

POSSIBLE REINFORCING BAR BUNDLING SCHEMES

SCHEDULE OF LINTEL BEAMS

SPAN	W	D	MK-1	MK-2	MK-3
UP TO 3'-0"	WIDTH OF WALL	6"	2-#4	2-#4	3#8" c/c
3'-6" TO 5'-0"	WIDTH OF WALL	9"	2-#4	2-#6	3#7" c/c
5'-6" TO 7'-0"	WIDTH OF WALL	12"	2-#4	2-#6	3#6" c/c
7'-6" TO 9'-0"	WIDTH OF WALL	12"	2-#4	2-#6 + 1-#4	3#6" c/c
9'-6" TO 12'-0"	WIDTH OF WALL	15"	2-#4	3-#6	3#5" c/c



NOTE:-

WHEN SPAN DIFFERENCE TO LOWER SIDE IS EXCESSIVE INTERPOLATE DEPTH USING SAME STEEL

STANDARD HOOKS FOR PRIMARY REINFORCEMENT

BAR SIZE, NO.	MIN.FINISHED BEND DIA. (a)
3 THROUGH 8	$6D_B$
9, 10, 11	$8D_B$
14 and 18	$10D_B$



(a) MEASURED ON INSIDE OF BAR



CURTAILMENT DETAIL FOR BEAM AND SLAB



(TYP.) R.C.C COLUMN & BRICK WALL 9" THICK CONNECTION DETAIL

SCALE:- 3/4" = 1'-0"



(TYP.) R.C.C COLUMN & BLOCK WALL 4" THICK CONNECTION DETAIL

SCALE:- 3/4" = 1'-0"

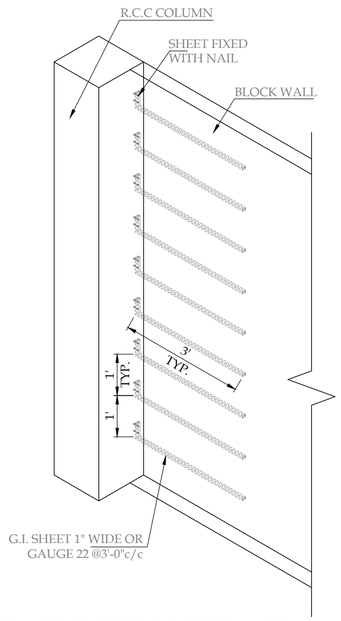

(TYP.) ISOMETRIC VIEW OF R.C.C COLUMN & 4" BLOCK WALL CONNECTION DETAIL

SCALE:- 3/8" = 1'-0"

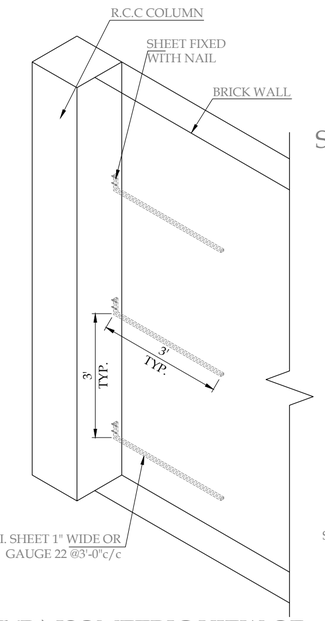

(TYP.) ISOMETRIC VIEW OF R.C.C COLUMN & 9" BRICK WALL CONNECTION DETAIL

SCALE:- 3/8" = 1'-0"

STANDARD HOOKS FOR STIRRUPS AND TIE REINFORCEMENT

BAR SIZE, NO.	MIN. FINISHED BEND DIA. (B)
3 THROUGH 5	$4D_B$
6 THROUGH 8	$6D_B$



(b) MEASURED ON INSIDE OF BAR

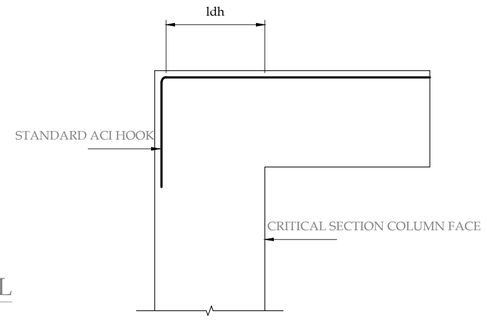

TOP BAR DEVELOPMENT SECTION

TITLE.

GENERAL NOTES-II

ORIGINAL :	DATE :	SCALE :
A2	JULY, 2025	-

ISSUE N°	DATE	DESCRIPTION	DRAWN	DESIGNED	APPROVED
01	21-11-2025	DETAILED DESIGN	ASAD	ENGR. FAIEZ	ENGR. IHSAN UL HAQ
02					
03					
04					
05					
06					
07					

DRAWING Nº: PRMSC-SEW-STP-GN-02

SHEET 02 OF 02

REV 00

PROJECT: ENGINEERING DESIGN & CONSTRUCTION SUPERVISION, PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT, CLUSTER SOUTH - III

CLIENT: PUNJAB RURAL MUNICIPAL SERVICES COMPANY (PRMSC)

ENGINEERING DESIGN & CONSTRUCTION SUPERVISION CONSULTANT:

ASIAN CONSULTING ENGINEERS www.asiancon.com

WJT-WS-OHR-GN-02

PRMSC

Punjab Rural Municipal Services Company

"Tender Package for Civil Infrastructure Works

TECHNICAL SPECIFICATIONS

APRIL-2023

TABLE OF CONTENTS

PART-A, GENERAL 1

SECTION-1 GENERAL 2

1.1 SITE INFORMATION 2
1.2 LAYOUT 2
1.3 SURVEY EQUIPMENT 2
1.4 PLANT, EQUIPMENT AND TOOLS 3
1.5 STORAGE & HANDLING FACILITIES 3
1.6 TEST LABORATORY TESTING AND TESTING REPORT 3
1.7 PROTECTION OF THE WORKS 4
1.8 RESTORATION AND CLEANING 4
1.9 COORDINATION WITH OTHER WORKS 4
1.10 DEFINITIONS 4
1.11 ABBREVIATIONS 4

PART-B, WATER DISTRIBUTION NETWORK 6

SECTION-2 EARTH WORK FOR WATER LINES 7

2.1 SCOPE OF WORK 7
2.2 CLEARING AND GRUBBING 7
2.3 EXCAVATION 7
2.4 BACKFILLING 9
2.5 BORROW 10
2.6 GRADING 10
2.7 Testing Density of Soil In Place 10
2.8 MEASUREMENT AND PAYMENT 11

SECTION-3 HDPE PIPES & FITTINGS 12

3.1 SCOPE OF WORK 12
3.2 DEFINITIONS 12
3.3 APPLICABLE STANDARDS AND CODES 12
3.4 TECHNICAL REQUIREMENTS 13
3.5 TOOLS 19
3.6 CONTROL OF WATER 19
3.7 INSPECTION AND TESTING 20
3.8 PIPELINE TESTING 21
3.9 PIPELINE DISINFECTION 25
3.10 PACKING, MARKING AND VENDOR DOCUMENTATION 27

3.11 STORAGE OF PIPES AND APPURTENANCES 29
3.12 MEASUREMENT AND PAYMENT 30
SECTION-4 PIPELINE APPURTENANCES 31
4.1 SCOPE OF WORK 31
4.2 GATE VALVE 31
4.3 CHECK VALVE 32
4.4 AIR-RELEASE VALVE 33
4.5 VALVE CHAMBERS 33
4.6 VALVE BOX 33
4.7 THRUST BLOCKS 34
4.8 APPROVAL OF MATERIALS AND EQUIPMENT 34
4.9 TESTS AND ACCEPTANCE 35
4.10 MEASUREMENT AND PAYMENT 35
SECTION-5 PIPE BEDDING 36
5.1 SCOPE OF WORK 36
5.2 PURITY AND STACKING 36
5.3 PLACING OF BEDDING MATERIAL 36
5.4 MEASUREMENT AND PAYMENT 36
SECTION-6 WATER SUPPLY SERVICE CONNECTIONS 37
6.1 SCOPE OF WORK 37
6.2 MATERIAL REQUIREMENTS 37
6.3 CONSTRUCTION REQUIREMENTS 37
6.4 MEASUREMENT AND PAYMENT 37
PART-C, TUBE WELL 38
SECTION-7 GENERAL 39
7.1 DESCRIPTION 39
7.2 CONTRACT DRAWINGS 39
7.3 SIZE OF TUBEWELL 39
7.4 Bill of Quantities 40
7.5 STANDARDS 40
7.6 CONSTRUCTION EQUIPMENT AND MATERIAL 40
7.7 CLEAN UP 41
SECTION-8 DRLLING OF BOREHOLE 42
8.1 SCOPE OF WORK 42
8.2 DRILLING OPERATION 42

8.3 DRILLING 42
8.4 DATA AND RECORDS 43
8.5 MEASUREMENT AND PAYMENT 44

SECTION-9 TUBEWELL CONSTRUCTION 45

9.1 SCOPE OF WORK 45
9.2 CASINGS 45
9.3 GROUTING 47
9.4 GRAVEL SHROUDING 47
9.5 DEVELOPMENT AND TESTING 48
9.6 Sealing 52
9.7 MEASUREMENT AND PAYMENT 53

SECTION-10 WATER TESTING 54

10.1 SCOPE OF WORK 54
10.2 COLLECTION OF WATER SAMPLES 54
10.3 TRANSPORTATION AND STORAGE OF SAMPLES 54
10.4 LABORATORY EXAMINATION 55
10.5 RECORD & DATA 55
10.6 MEASUREMENT AND PAYMENT 55

SECTION-11 CONSTRUCTION OF PUMP HOUSE 57

11.1 SCOPE OF WORK 57
11.2 MATERIALS AND CONSTRUCTION REQUIREMENTS 57
11.3 MEASUREMENT AND PAYMENT 57

SECTION-12 ELECTRICAL & MISC. WORKS 58

12.1 SCOPE OF WORK 58
12.2 ELECTRICAL WORKS 58
12.3 POWER TRANSFORMER 63
12.4 MEASUREMENT AND PAYMENT 65

PART-D, SEWERAGE SYSTEM 66

SECTION-13 EARTH WORK FOR SEWERS 67

13.1 SCOPE OF WORK 67
13.2 CLEANING AND GRUBBING 67
13.3 EXCAVATION 67
13.4 ALIGNMENT AND GRADE 68
13.5 SETTING OUT SIGHT RAILS 68
13.6 SHEETING AND BRACING 69

13.7 DEWATERING OF TRENCHES....70
13.8 MAINTENANCE OF EXCAVATIONS....70
13.9 PROTECTION OF EXISTING FACILITIES....70
13.10 DISPOSAL OF SURPLUS EXCAVATED MATERIAL....70
13.11 BACKFILLING....70
13.12 MAXIMUM DENSITY DETERMINATION FOR COMPACTED SOIL....71
13.13 TESTING DENSITY OF SOIL....71
13.14 TOP SOIL....71
13.15 PROXIMITY TO BUILDINGS....71
13.16 LENGTH OF TRENCHES IN ADVANCE OF CONSTRUCTION....72
13.17 DISPOSAL OF FILTH AND GARBAGE....72
13.18 DISPOSAL OF SURPLUS EARTH....72
13.19 TUNNELING....72
13.20 MEASUREMENT AND PAYMENT....73

SECTION-14 REINFORCED CEMENT CONCRETE PIPE SEWERS....74

14.1 SCOPE OF WORK....74
14.2 REINFORCED CEMENT CONCRETE PIPES....74
14.3 CERTIFIED PLANS AND DATA SHEETS....77
14.4 JOINTS FOR CONCRETE PIPE SEWERS....77
14.5 INSTALLATION OF CONCRETE PIPE SEWERS....78
14.6 TESTS FOR INFILTRATION OR EXFILTRATION....79
14.7 MEASUREMENT AND PAYMENT....80

SECTION-15 CONSTRUCTION OF MANHOLES....82

15.1 SCOPE OF WORK....82
15.2 MATERIALS....82
15.3 CONSTRUCTION REQUIREMENTS....82
15.4 MEASUREMENT AND PAYMENT....82

SECTION-16 PIPE BEDDING....84

16.1 SCOPE OF WORK....84
16.2 SOURCE OF BEDDING MATERIAL....84
16.3 PURITY AND STACKING....84
16.4 PLACING OF BEDDING MATERIAL....84
16.5 MEASUREMENT AND PAYMENT....84

PART-E, CIVIL WORKS....85

SECTION-17 EXCAVATION, BACKFILLING & DISPOSAL....86

17.1 SCOPE OF WORK 86
17.2 AUTHORIZED OUTLINES 86
17.3 CONSTRUCTION REQUIREMENTS 86
17.4 MEASUREMENT AND PAYMENT 91

SECTION-18 TERMITE CONTROL 92

18.1 SCOPE OF WORK 92
18.2 APPLICABLE STANDARDS 92
18.3 SUBMITTALS 92
18.4 MATERIAL 92
18.5 QUALITY ASSURANCE 93
18.6 METHOD OF APPLICATION 93
18.7 MEASUREMENT AND PAYMENT 94

SECTION-19 PLAIN & REINFORCED CONCRETE 95

19.1 SCOPE OF WORK 95
19.2 APPLICABLE STANDARDS 95
19.3 SUBMITTALS 97
19.4 MATERIAL REQUIREMENTS 99
19.5 NOMINAL CONCRETE MIXES 102
19.6 DELIVERY, STORAGE AND HANDLING 104
19.7 CAST-IN-SITU CONCRETE 104
19.8 WORKS IN EXTREME WEATHER 112
19.9 PRECAST CONCRETE 113
19.10 CEMENT CONCRETE PAVEMENTS 114
19.11 TEST OF CONCRETE QUALITY 120
19.12 FINISHING OF FORMED SURFACES 121
19.13 TOLERANCEs 126
19.14 ACCEPTANCE OF STRUCTURE 128
19.15 MEASUREMENT AND PAYMENT 130

SECTION-20 REINFORCEMENT 132

20.1 SCOPE OF WORK 132
20.2 APPLICABLE STANDARDS 132
20.3 SUBMITTALS 133
20.4 MATERIAL REQUIREMENTS 133
20.5 DELIVERY & STORAGE 133
20.6 BAR BENDING SCHEDULES 134
20.7 FABRICATING, BENDING & PLACING 134

20.8 MEASUREMENT & PAYMENT 136

SECTION-21 SULPHATE RESISTANT CEMENT CONCRETE 137

21.1 SCOPE OF WORK 137
21.2 MATERIAL REQUIREMENTS 137
21.3 MEASUREMENT AND PAYMENT 137

SECTION-22 CONCRETE FORMWORK & ACCESSORIES 138

22.1 SCOPE OF WORK 138
22.2 APPLICABLE STANDARDS 138
22.3 SUBMITTALS 138
22.4 MATERIAL REQUIREMENTS 138
22.5 DESIGN OF FORMWORK 139
22.6 DELIVERY AND STORAGE 140
22.7 QUALITY ASSURANCE 140
22.8 EXECUTION 140
22.9 MEASUREMENT AND PAYMENT 145

SECTION-23 STRUCTURAL STEEL WORKS 146

23.1 SCOPE OF WORK 146
23.2 SUBMITTALS 146
23.3 MATERIAL REQUIREMENTS 146
23.4 TRANSPORTATION, HANDLING AND STORAGE 147
23.5 FABRICATION 147
23.6 SURFACE PREPARATION & PAINTING 149
23.7 INSPECTION AND TESTS 149
23.8 MEASUREMENT AND PAYMENT 150

SECTION-24 BRICK MASONRY 151

24.1 SCOPE OF WORK 151
24.2 APPLICABLE STANDARDS 151
24.3 SUBMITTALS 151
24.4 MATERIAL REQUIREMENTS 151
24.5 PLACING 153
24.6 CURING 154
24.7 REPAIR 154
24.8 SCAFFOLDING 154
24.9 TOLERANCES 154
24.10 MEASUREMENT AND PAYMENT 155

SECTION-25 DAMP PROOF COURSE 156
25.1 SCOPE OF WORK 156
25.2 MATERIAL REQUIREMENTS 156
25.3 HORIZONTAL DPC 156
25.4 VERTICAL DPC 156
25.5 CONSTRUCTION REQUIREMENTS 156
25.6 MEASUREMENT AND PAYMENT 157
SECTION-26 CEMENT PLASTER 158
26.1 SCOPE OF WORK 158
26.2 APPLICABLE STANDARDS 158
26.3 SUBMITTALS 159
26.4 MATERIAL REQUIREMENTS 159
26.5 PROPORTIONING AND MIXING 159
26.6 PREPARATION OF SURFACE TO BE PLASTERED 160
26.7 APPLICATION OF PLASTER 160
26.8 Metal Lath 161
26.9 BEADS & PROFILES 161
26.10 CLEANING AND PROTECTION 161
26.11 TOLERANCES 162
26.12 POINTING WORK 162
26.13 MEASUREMENT and PAYMENT 162
SECTION-27 POLYVINYLECHLORIDE WATERSTOP 164
27.1 SCOPE OF WORK 164
27.2 MATERIAL REQUIREMENTS 164
27.3 CONSTRUCTION REQUIREMENTS 164
27.4 MEASUREMENT AND PAYMENT 165
SECTION-28 ALUMINIUM WORKS 166
28.1 SCOPE OF WORK 166
28.2 APPLICABLE STANDARDS 166
28.3 GENERAL 166
28.4 MATERIAL requirements 168
28.5 WORKMANSHIP 168
28.6 PRODUCT DELIVERY AND STORAGE 168
28.7 ERECTION 169
28.8 PROTECTION AND CLEANING 169
28.9 DEFECTIVE WORK 169

28.10 GUARANTEE 169
28.11 MEASUREMENT AND PAYMENT 169

SECTION-29 GLAZING 171

29.1 SCOPE OF WORK 171
29.2 APPLICABLE STANDARDS 171
29.3 SUBMITTALS 171
29.4 MATERIAL requirements 171
29.5 DELIVERY, STORAGE AND HANDLING 173
29.6 INSTALLATION OF GLAZING 173
29.7 PROTECTION AND CLEANING OF GLAZING 174
29.8 MEASUREMENT and PAYMENT 174

SECTION-30 PAINTING 175

30.1 SCOPE OF WORK 175
30.2 APPLICABLE STANDARDS 175
30.3 GENERAL 175
30.4 MATERIAL REQUIREMENTS 176
30.5 DELIVERY STORAGE AND CONTAINER SIZES 176
30.6 SURFACE PREPARATION 176
30.7 APPLICATION 177
30.8 FINISHES 177
30.9 JOB CONDITIONS 178
30.10 QUALITY ASSURANCE 178
30.11 MEASUREMENT AND PAYMENT 178

SECTION-31 CERAMIC TILE WORK 179

31.1 SCOPE OF WORK 179
31.2 MATERIAL REQUIREMENTS 179
31.3 WORKING DRAWINGS 179
31.4 CONSTRUCTION REQUIREMENTS 179
31.5 MEASUREMENT AND PAYMENT 181

SECTION-32 TERRAZZO WORK 182

32.1 SCOPE OF WORK 182
32.2 APPLICABLE STANDARDS 182
32.3 SUBMITTALS 182
32.4 MATERIAL REQUIREMENTS 182
32.5 EXECUTION 183
32.6 MEASUREMENTS & PAYMENTS 185

SECTION-33 DETAILED TECHNICAL SPECIFICATIONS (DTS) FOR ELECTRICAL WORKS AND DG SETS....186
33.1 SCOPE OF WORK:....186
33.2 DC System:....189
33.3 Diesel Generators with AMF & Synchronising Panel. 189
33.4 PROJECT INFORMATION:....190
33.5 Design Criteria for Electrical Equipment / System....190
1.1.1 EARTHING & LIGHTNING PROTECTION SYSTEM: 196
1.1.2 Drawings / Documents for Reference....197
SECTION-34 GENERAL TECHNICAL & PARTICULAR REQUIREMENTS FOR ELECTRICAL EQUIPMENT/ SYSTEMS:....199
34.1 415V METAL ENCLOSED SWITCH BOARDS:....199
34.2 LOCAL PUSH BUTTON STATIONS....225
34.3 APFC PANEL WITH CAPACITOR BANKS....226
34.4 CABLES & CABLING SYSTEM....230
34.5 Applicable Standards:....230
34.6 EARTHING & LIGHTNING PROTECTION SYSTEM....239
34.7 LIGHTING & VENTILATION SYSTEM....246
34.8 DC SYSTEM....272
1.1.3 Drawings/ Documents Required:....279
SECTION-35 SAFETY EQUIPMENTS/ REQUIREMENTS AND MISCELLANEOUS ITEMS: 281
35.1 FIRE SAFETY....281
35.2 DEGREE OF PROTECTION....281
35.3 ELECTRICAL EQUIPMENT FOR HAZARDOUS AREAS....281
SECTION-36 INSTALLATION, TESTING & COMMISSIONING – ELECTRICAL EQUIPMENT:....283
36.1 GENERAL:....283
36.2 POWER/ DISTRIBUTION TRANSFORMERS....284
36.3 HV/ LV SWITCHGEAR CONTROL PANELS....284
36.4 EARTHING AND LIGHTNING PROTECTION SYSTEM....285
36.5 INSTALLATION OF CABLE RACKS AND CABLE TRAYS....288
36.6 CABLE INSTALLATION....290
36.7 LIGHTING SYSTEM INSTALLATION....302
SECTION-37 PRE COMMISSONING TESTS ON ELECTRICAL EQUIPMENT/ SYSTEMS TO BE CARRIED OUT AFTER INSTALLATION:....309
37.1 GENERAL:....309

37.2 ELECTRICAL EQUIPMENT: 309
1.1.4 Power/ Distribution Transformer 309
37.3 DIESEL STANDBY GENERATOR: 311

PART-A, GENERAL

SECTION-1 GENERAL

1.1 SITE INFORMATION

The Contractor shall visit the site prior to making his bid and shall ascertain the nature of strata, the earth, its quality/quantity, locations, and suitability to meet the specified requirements, existing situation of working area and he shall base his bid estimates solely on his own studies and tests.

Any information about the properties of the soil that may be shown on the Drawings or obtained by the Contractor as a result of discussion with the Engineer or others shall be prejudice and shall not be considered as a valid basis for the Contractor's bid prices and subsequent execution and completion of works. The bore logs shown on the Drawings, if any, are tentative one and do not mean that the same strata will be involved during boring. The Contractor may carry our boring as per the actual strata at no additional cost to the Works.

1.2 LAYOUT

The layout of works for the purposes of execution of roads, water supply, sewerage, drainage and facilities under the scope of work shall be carried out by the Contractor subject to confirmation / check by the Engineer which must be accurately as per the Drawings and instructions of the Engineer. Before commencement of construction work, the layout shall be checked and certified by the Engineer's Representative or Engineer. The measurement for payment shall not be taken for this item of the work, price shall be deemed to be included in other items of Works.

1.3 SURVEY EQUIPMENT

The Contractor with the approval of the Engineer shall provide survey equipment for the Engineer's Representative and his staff which shall be of the number, type and quality (or equivalent) as listed in Table 1.1.

Table 1.1, List of Survey Equipment

Sr. No.	Equipment	Quantity
1	Total Station complete with Standard Accessories model SOKKIA SET 2010 or Equivalent	1-No.
2	Single Tilting Range Pole Prism Complete Set Model SOKKIA KPS 11 PT or Equivalent	1-Set
3	Single Tilting Prism W / Coaxial Target Complete Model SOKKIA KPS 12 or Equivalent	1-Set
4	Automatic Levels, with Standard Aluminium Tripod	2-Nos.

Sr. No.	Equipment	Quantity
	Model B20	
5	Steel Measuring Tapes 50m and 20m long	2-Each
6	Steel Measuring Tapes 3m long	6-Nos.
7	Levelling Staff (4m)	2-Nos.
8	Ranging Rods	as required
9	All Miscellaneous Tools, Equipment and Materials required in Surveying	as required

The cost of said survey equipment shall be deemed included in other items of works; as such no separate payment shall be made. All surveying equipment shall be new and maintained in perfect working condition throughout the contract period and replaced by the Contractor in case of damage or loss under the terms and condition of the agreement.

1.4 PLANT, EQUIPMENT AND TOOLS

The Contractor shall provide at his cost modern plant, equipment and tools, adequate and befitting to the nature, magnitude and size of this Contract, in strict compliance with the requirements of the Contract.

1.5 STORAGE & HANDLING FACILITIES

The Employer will provide the necessary space if available with him, for constructional activities including batching plant, laboratory, workshop, storage of plant, equipment and materials and for Contractor's temporary office/camp, during the currency of the Contract. If the space is ' not available with the Employer then the contractor shall arrange these facilities without additional cost to the Employer.

1.6 TEST LABORATORY TESTING AND TESTING REPORT

Testing, except as otherwise specified herein, shall be performed by testing agency approved by the Engineer and at no extra cost to the Employer. The Contractor shall bear the Cost of such Testing. The Engineer may require all or part testing to be carried out under his supervision only.

The quality control testing shall be performed by the Contractor's competent personnel in accordance with a site testing and quality control program to be established by the Contractor and approved by the Engineer. The Contractor shall keep a complete record of all quality tests performed on site.

All quality control and tests shall be carried out in accordance with

applicable standards and codes.

1.7 PROTECTION OF THE WORKS

The Contractor shall whenever necessary cover up and protect the works from weather and damage by his own or other workmen performing subsequent operation at no extra cost to the Employer including all necessary dust sheets, barriers and guard rails and clear away the same on completion.

1.8 RESTORATION AND CLEANING

Upon completion of the works the Contractor shall restore all items covered by the Contract to the satisfaction of the Engineer.

The Contractor shall do regular cleaning and clean away all rubbish and excess materials that may accumulate from time to time on completion and before handing over. Upon completion of the Works, he shall obliterate all signs of temporary construction facilities such as work areas, structures, foundations of temporary structures, stock piles of excess or waste materials, as directed by the Engineer. Trash shall be removed daily to the satisfaction of the Engineer.

1.9 COORDINATION WITH OTHER WORKS

The Contractor shall coordinate with other Contractors executing other works in the project area or in the vicinity. The Contractor shall plan and schedule these activities in close liaison with other Contractors. The cost of this coordination will be deemed to be included in other items of works as such no separate payment is admissible for the coordination.

1.10 DEFINITIONS

Capitalized terms used in these specifications shall have the meanings specified in Volume-I, Condition of Contract, unless the context expressly or by necessary implication otherwise requires.

1.11 ABBREVIATIONS

Whenever, in these specifications, the following abbreviations are used, the intent and meaning shall be interpreted as follows:

^{o}C	Degree Centigrade
^{o}F	Degree Fahrenheit
AASHTO	American Association of State Highway and Transportation Officials
ASTM	American Society for Testing and Materials
ACI	American Concrete Institute

ASIC	American Institute of Steel Construction
ASCE	American Society of Civil Engineers
AWWA	American Water Works Association
BS	British Standards
BSI	British Standard Institute
CBR	California Bearing Ratio
cm	Centimetre
DIN	Deutsches Institut für Normung
EN	European Norm
HDPE	High Density Polyethylene Pipe
HP	Horse Power
ISO	International Standards Organization
JMF	Job Mix Formula
kg	Kilogram
km	Kilometre
lb	Pound
m	Metre
mm	Millimetre
PN	Pressure Nominal
WBM	Water Bound Macadam

PART-B, WATER DISTRIBUTION NETWORK

SECTION-2 EARTH WORK FOR WATER LINES

2.1 SCOPE OF WORK

EARTH WORK FOR WATER LINES

The work covered by this section of the specifications consists of furnishing all plant, labour, equipment, appliances, and materials and performing all operations in connection with excavation, trenching and back filling (with compaction) for water lines and appurtenances in strict accordance with this section of the specifications and the applicable Drawings, and subject to the terms and conditions of the Contract.

2.2 CLEARING AND GRUBBING

The sites of all excavations shall be cleared of all shrubs, plants, bushes, large roots, rubbish and other surface materials. All such materials shall be removed and disposed of in a manner satisfactory to the Engineer. All trees and shrubbery that are designated by the Engineer to remain shall be adequately protected and preserved in an approved manner.

2.3 EXCAVATION

2.3.1 General

All excavation of whatever substance encountered shall be performed to the depths indicated or as otherwise specified. During excavation, material suitable for backfilling shall be stockpiled in an orderly manner at a sufficient distance from the banks of the excavation to avoid overloading and to prevent sides from caving. All excavated material unsuitable or not require such a manner that street passage is not blocked by excavated material. Grading shall be done as may be necessary to prevent surface water from flowing into trenches or other excavations, and any water accumulated therein shall be removed by pumping or by other approved methods. Unless otherwise indicated or approved by the Engineer, excavation shall be open cut.

2.3.2 Trench Excavation

Unless otherwise directed or permitted by the Engineer not more than 500 feet of any trench in advance of the end of the pipeline already laid shall be opened at any time, unless otherwise directed permitted by the Engineer not more than 1000 feet of any one trench shall be worked on at a time. The banks of the pipe trench shall be as nearly vertical as practicable. Bell holes and depressions for joints shall be dug after the trench bottom has been prepared. The pipe, except for joints, shall rest on the prepared bottom for its length. Bell holes and depressions shall be only of such length, depth, and width as required for properly making the particular type of joints. Stones shall be removed to avoid point bearing. Whenever wet or otherwise unstable

material that is incapable of properly supporting the pipe as determined by the Engineer is encountered in the bottom of the trench, such material shall be removed to the depth required and the trench backfilled to the proper grade with coarse sand, or other suitable approved granular material. Such replacement of unsuitable material will be paid for at the contract unit price for that item of work. Trenches shall be of a depth to provide a maximum cover, over the top of the pipe, of 30 in. from the existing ground surface or finished grade whichever is closer except that trenches for pipe laid in lanes and alleys of narrow travelled way (average width of 8 feet or less between structures) shall be of a depth to provide a minimum cover, over the top of the pipe, of 18 in from the existing ground surface or finished grade whichever is closer.

2.3.3 Excavation for Appurtenances

Excavation for appurtenances shall be sufficient to leave at least 12-inch but not more than 24 in., between the outer surface and the embankment or timber that may be used to hold and protect the banks. Any over depth excavation below such appurtenances that has not been directed by the Engineer, will be considered unauthorized and shall be refilled with compacted sand, gravel or concrete, as directed by the Engineer and at no additional cost to the Employer.

2.3.4 Maintenance of Excavation

All excavation shall be properly maintained while they are open and exposed. Sufficient suitable barricades, warning lights, flood lights, signs, and similar items shall be provided by the Contractor. The Contractor shall be responsible for any damage due to his negligence.

2.3.5 Removal of Water

The Contractor shall build all drains and do ditching, pumping, well pointing, bailing, and all other work necessary to keep the excavation clear of ground water, sewage and storm water during the progress of the work and until the finished work is safe from injury. All water pumped or drained from the work shall be disposed of in a manner satisfactory to the Engineer and necessary precautions against flooding shall be taken.

2.3.6 Sheeting and Bracing

If ordinary open cut excavation is not possible or advisable, sheeting and bracing shall be furnished to the work and to provide working conditions which are safe. The Contractor shall furnish and place all sheeting, shoring, wall braces, timbers and similar items, necessary for the safety of the work, the general public and adjacent property. Sheeting shoring and bracing shall be removed as the work progresses and in such a manner as to prevent damage to finished work and adjacent structures and property. As soon as withdrawn, all voids left by the sheeting and bracing shall be carefully filled

with sand and compacted. The Contractor shall be fully responsible for the safety of work in progress, for the finished work, the workmen, and the public and adjacent property.

2.3.7 Protection of Facilities

Existing subsurface facilities likely to be encountered during the execution of work require special precaution for the protection, such as sewers, drain pipes, water main, conduits and electric cables and the foundations of adjacent structures. The Contractor shall be responsible for the damage of any such facility and shall repair the same at his expense whether or not this facility has been shown on the Drawings.

2.3.8 Surplus Materials

All surplus materials shall be disposed of at locations approved by the Engineer. The disposal of surplus material shall not interfere with other works and shall not damage or spoil other material. When it is necessary to haul earth or rock material over street or pavement, the Contractor shall prevent such material from falling on the street or pavement.

2.3.9 Cutting Pavement

In cutting or breaking street surfacing, the Contractor shall not use equipment which will damage the adjacent pavement. Existing paved surfaces shall be cut back beyond the edges of the trenches to form neat square cuts. The road ballast, brick pavement, and other materials shall be placed on one side and shall be preserved for re-instatement when the trench is filled. Wherever necessary or required for the convenience of the public or individual residents, at street crossings and at private driveways, the Contractor shall provide suitable temporary bridges over unfilled excavations. All such bridges shall be maintained in service until backfilling has been completed. The Contractor shall keep the road crossings manned 24 hours per day. During night time, enough red lights shall be provided to warn traffic. If detour is necessary, the Contractor shall make proper detour for the traffic and shall install signs 1 metre by 1.2 metre in size indicating the detour.

2.4 BACKFILLING

a. The trenches shall not be completely backfilled until all required pressure tests are performed and until the water lines as installed conform to the requirements of specifications. Where in the opinion of the Engineer, damage is likely to result from withdrawing sheeting, shoring; the same shall be left in place and cut off at a level 12-inch below ground surface. Sheeting left in place at the direction of the Engineer will be paid for at the contract unit price/approved rate for that item of work. Trenches shall be backfilled to the ground surface

with selected excavated material or other material that is suitable for proper compaction. Trenches improperly backfilled shall be reopened to the depth required for proper compaction, then refilled and compacted to the specified density. The surface shall be restored to its original or better condition. Pavement and base course disturbed by trenching operations shall be replaced.

b. Lower Portion of Trench: Backfill material shall be deposited in 6-inch maximum thickness layers and compacted with suitable hand tampers to ninety percent of maximum density until there is a cover of not less than 12-inch over the water lines. The backfill material in this portion of trench shall consist of sandy clay or other approved materials free from stones and humps.

c. Remainder of Trench: The remainder of the trench shall be backfilled with material that is free from stones larger than 6-inch in any dimension. Backfill material shall be compacted to ninety percent of maximum density.

2.5 BORROW

Where suitable material for backfill is not available in sufficient quantity from required excavations, suitable material shall be obtained from approved sources at the contractor's responsibility. The necessary clearing and grubbing or borrow areas, disposal and burning of debris there from, the developing of sources including any access roads for hauling and the necessary right-of-way, and the satisfactory drainage of the borrow shall be considered as incidental items to borrow excavation.

2.6 GRADING

After the completion of all backfilling operations, the contractor shall grade the work areas to the lines, grades and elevation shown on the Drawings. Finished grading shall not be done until the installation of all water lines has been completed and tested. The top surface after completion shall be “in level “to the adjacent existing surface. Prior to final acceptance, all damage due to settlement shall be repaired by and at the expense of the Contractor.

2.7 TESTING DENSITY OF SOIL IN PLACE

The Engineer will make tests using the calibrated sand cone method/core cutter method to determine the density of soil in place. If soil in place fails to meet the specified degree of compaction the areas represented by the failing tests shall be removed, replaced and compacted to the specified density in the manner directed by the Engineer and at no additional cost to the Employer.

2.8 MEASUREMENT AND PAYMENT

2.8.1 Measurement

The measurement shall be made for the actual quantity of the work done in cubic foot or cubic metre (whichever is included in Bill of Quantities). The maximum width of the trenches along with height allowed for payment for various pipe sizes are included in the Drawings.

2.8.2 Payment

The unit rate included in the Bill of Quantities for excavation of trenches for water supply lines shall be considered as full compensation for the work specified in this section and shall include all excavation, backfilling, compacting, constructing and removing all temporary arrangements, pumping and dewatering, disposal of surplus materials, removal of soft soil from bottom of trenches, removing the surface material and all incidentals to complete this work in all respects.

SECTION-3 HDPE PIPES & FITTINGS

3.1 SCOPE OF WORK

This work shall consist of providing, laying, testing and disinfection of High-Density Polyethylene (HDPE) pipes conforming to ISO 4427, DIN 8074/8075 & PS 3580 with PN-8, 10 & 12.5 (PE 100) and in trenches to correct alignment and grade, as indicated in the drawing and specifications including all other accessories and equipment.

3.2 DEFINITIONS

The following terms shall have the meanings hereby assigned to them except where the Contract clearly renders these meanings inapplicable.

"Pipe" means pipe or pipes, bends, fittings and other specials and includes joints, jointing parts and materials.

"Valves" means gate valves, butterfly valves, air valves and the like and includes jointing materials, operating gear and associated fittings.

"Installation" means removing from storage, loading, hauling, handling, placing, fixing, jointing in position and testing whether in trench or elsewhere in the Works.

"Pipeline" means those parts of the works comprising pipe, fittings, valves, valve chambers, other chambers, anchors, thrust blocks and all other appurtenances required for proper functioning, operation and maintenance of the pipeline.

3.3 APPLICABLE STANDARDS AND CODES

The following codes and standards, to the extent specified herein, form a part of this specification. The latest edition of these codes and standards shall govern the work.

ISO 4427	Polyethylene (PE) pipes for water supply - specifications
IS0161-1	Thermoplastic pipes for conveyance of fluids - nominal outside diameter and nominal pressure- part 1: Metric series
ISO 1167-1 to 4	Thermoplastic pipes, fittings and assemblies for the conveyance of fluids
IS0 3126	Plastic pipe - Measurement of dimensions
ISO 4065	Thermoplastic pipes - Universal wall thickness table
ISO 6964	Polyolefin pipes and fittings - Determination of carbon black content by calcination and pyrolysis - Test method and basic specification.
ISO 9080	Thermoplastic pipes for the transport of fluids - Method

	of extrapolation of hydrostatic stress rupture data to determine the long-term hydrostatic strength of thermoplastic pipe materials.
ISO 11922-1	Thermoplastic pipes for the conveyance of fluids - Dimensions and tolerances Part: 1: Metric series.
IS012162	Thermoplastic materials for pipes and fittings for pressure applications - Classification and designation - overall service (design) coefficient.
ISO 13761	Plastic pipes and fittings - pressure reduction factors for polyethylene pipeline systems for use at temperatures above 200 C.
ISO 7005- 3	Metallic flanges - Part 3, Copper alloy and composite flanges
BS EN 12201	Plastic piping systems for water supply · polyethylene
ISO 974	Determination of the brittleness temperature by impact
ISO 2505	Thermoplastics pipes · Longitudinal reversion
ISO 6259	Determination of tensile properties
ISO 1133	Determination of the melt mass-flow rate (MFR) and the melt volume-flow
ISO 877	Methods of exposure to direct weathering

3.4 TECHNICAL REQUIREMENTS

3.4.1 Material

The Contractor shall identify the manufacturer of the resin, the resin type and classification. In addition, the Contractor shall provide evidence that the resin proposed is suitable for use at the design temperature and under the design pressures.

Any change in the material, the material specification, or the manufacturer's location shall be subject to prior approval of the Engineer.

Pipes and fittings shall be homogenous throughout and free from visible cracks, holes, foreign inclusions, blisters, dents or other damaging defects.

Material shall be uniform in opacity, density, interior smoothness, and other physical properties.

It shall have adequate resistance to weathering and other ageing from storage for a minimum of two years after manufacture.

The material of the polyethylene pipes and fittings which is in contact with or likely to come in contact with drinking water shall not constitute a toxic hazard, shall not support microbial growth and shall not give rise to unpleasant taste or odour, cloudiness or discoloration of the water.

The concentration of substances, chemical and biological agents leached from materials in contact with drinking water, and measurement of the relevant organoleptic / physical parameters, shall not exceed the maximum values recommended by the World Health Organisation in its "Guidelines for Drinking Water Quality" or the EEC Council Directive on the "Quality of Water Intended for Human Consumption", whichever is more stringent in each case.

For the manufacturing of pipes & fittings new materials to be used only (Rework material is not acceptable.)

Pipe manufacturer shall confirm that all fittings to be provided for the pipe systems shall meet the same quality requirements as for the pipes to ensure the same performance for design life cycle.

The pipes and fittings shall be manufactured from polyethylene containing only those antioxidants, UV stabilizers and pigments necessary for the manufacturing process to fulfil the requirements of the specification.

All pipes and fittings shall be suitable for butt fusion or electro fusion techniques.

Contractor shall provide HDPE manufacturers guideline for the applicability of the material used. If required HDPE manufacturers shall provide assistance and training.

3.4.2 Physical Properties

Pipes and fittings shall be made of HDPE and shall comply with the requirements of ISO 4427 PE 100. The material shall be produced by a member of the PE 100 + Association.

The material used for the manufacturer of pipes and fittings shall be in accordance with Table-1 and Table-2 of clause 4.4 of ISO 4427-1. The minimum required strength (MRS) of the material compound shall be 10 MPa at 20^{o}C. The design stress shall be 8 MPa.

Lifecycle durability of 80 years is to be confirmed.

Pressure reducing coefficients, as included in Annexure-A of ISO 4427-1, are also applicable. The thermal stability of polyethylene material shall meet the requirements of ISO 4427.

3.4.3 Pipe Dimensions

The pipe dimensions for water systems shall be based on standard dimensions according to ISO 4427 and measured in accordance with ISO 3126.

Straight pipe shall be supplied in standard lengths measured at 239^{o}C ± 29^{o}C, unless otherwise specified; coil lengths shall not exceed 100 m (328 ft).

Coiled pipes shall be coiled such that localized deformation is voided and diameter of the coil shall not be less than 18 dn.

3.4.4 Pipe Appearance

When viewed without magnification the internal and external surfaces of pipes shall be smooth, clean and free from scoring, cavities and other surface defects. The pipe ends shall be cut cleanly and square to the axis of the pipe.

All polyethylene pipes to be used for the transmission and distribution of potable water shall be black and have blue stripes.

The carbon black content in the compound shall be 2.25% ± 0.25% by mass when measured in accordance with ISO 6964. The dispersion of carbon black when determined in accordance with ISO 11420 shall be equal to or less than grade 3.

3.4.5 Fittings

The fittings shall be injection moulded and formed from material that is compatible to that of the pipe and shall be as resistant to the external and internal environments as the other demands of the pipe system.

At locations where HDPE pipe to metal connections is specified, Nylon-11 based polyamide coating system complying with the requirement of AWWA C224 or epoxy coated backing rings shall be used, or special restrained transition fittings subject to approval by the Engineer. The flanges shall be drilled to ISO 7005-2, as per the design requirements.

3.4.6 Fittings Appearance

When viewed without magnification the internal and external surfaces of pipes shall be smooth, clean and free from scoring, cavities and other surface defects. The fitting shall be blue or black.

3.4.7 Fittings Dimensions

The dimensions shall be measured in accordance with EN/ISO 3126.

3.4.8 Wall Thickness of Fittings

The wall thickness of the body of the fitting at any point shall be equal to or greater than the minimum wall thickness of the corresponding pipe.

3.4.9 Pipe Installation

a. Trench excavation shall be carried out in accordance with Section Excavation of the specifications.

b. Install pipe, fittings, and accessories in accordance with manufacturer's instructions:

- Provide qualification details of the manufacturer's technical expert to be assigned to the Contract. The technical expert shall have expertise, experience and skills necessary for advising and monitoring all aspects of transport, storage, handling, installation and testing of pipes as appropriate.

- The technical expert shall provide comprehensive technical assistance to the Contractor throughout Contract and regularly monitor the Contractor's activities and report on shortcomings.

c. The pipeline shall be within 1-inch of the specified line and the invert level shall be within 6mm of the specified value and shall be such that there is no back fall at any point on a gravity pipeline.

d. Install bedding, surround and backfill in accordance with the pipe manufacturer's requirements.

e. Install appurtenant facilities on the pipeline such as manholes, valve chambers as specified of the specification.

f. Lay pipes from downstream to upstream unless agreed otherwise with the Engineer.

g. HDPE pipelines can accommodate gradual changes of direction in the vertical and horizontal plane. However, the pipe should not normally be bent to a radius less than 25 times the outside diameter of the pipe.

h. When cut pipe is required, ensure that the cutting is done by a machine, leaving a smooth cut at right angles to the axis of the pipe.

i. Ensure that all pipes and fittings are sound and clean before laying. When pipe lying is not in progress, ensure that the pipe ends are at all times fitted with watertight plugs or caps. The plugs or caps shall only be removed for the purposes of making a connection of the pipe end or testing the pipeline. The plugs or cap shall be replaced immediately on completion of the test.

3.4.10 Backfilling

The selected fill material as shown on the Drawings shall be hand-compacted in layers not exceeding 150mm to complete the pipeline surround. Compaction shall be carried out equally on either side of the pipeline to prevent displacement. The backfill shall be hand-compacted up to 300 mm above the crown of the pipe. Any temporary support shall be gradually withdrawn during placing of the bedding and backfill materials to ensure that materials are placed against the trench side. The remaining portion of the trench shall be compacted in layers not exceeding 200 mm using approved mechanical rammers.

Where filter fabric is used to enclose granular pipe surrounds, the fabric will be placed on the prepared trench formation and carefully supported during pipe laying operations. When the pipe has been laid complete with granular surround to the correct level the filter fabric will be closed by forming a lap equal to trench width. Care shall be taken that the membrane is not punctured or damaged in any way during these operations and backfilling

the trench.

Where concrete bedding or surround is specified, concreting shall be carried out as specified in SECTION-20 PLAIN & REINFORCED CONCRETE. The backfill other than first 150 mm of cover shall not be placed before the compressive strength of the concrete has reached 15 MPa. The remaining portion of the trench shall be backfilled as specified.

3.4.11 Cutting Pipes

The Contractor shall be responsible for taking the measurements required to determine the lengths of cut portions of pipes for insertion as closing lengths in pipelines. The pipe and methods of jointing shall be such that the locations of fittings and lengths of pipe can be adjusted in the field to suit field conditions and variations in stationing. No extra payment will be made for such adjustments or for any welding, couplings, fittings, or special lengths required to meet this requirement.

The cutting of ductile iron and HDPE pressure pipes for inserting specials, fittings or closure pieces shall be performed by the Contractor. Cutting shall be carried out in a neat and workman like manner with an approved cutting machine without damage to the pipe and so as to leave a smooth end at right angles to the axis of the pipe. The cut ends of pipes shall be chamfered. The Contractor shall take every precaution to ensure that both the measurements and the cutting of pipes are to the accuracy required and should any errors occur the Contractor shall remedy same at his own expense and as the Engineer directs.

3.4.12 Butt Fusion Jointing

Butt fusion jointing shall only be used to join pipes of the same PE material with compatible MFR and with the same nominal wall thickness and outside diameter. The following procedures shall serve as a general guide only. The Contractor shall obtain detailed jointing instructions from the manufacturer who shall have a technical representative available at the Engineer's request during the jointing process.

- The butt fusion machine should be sited within a shelter and the ends of the pipe being joined should be covered or plugged to prevent through drafts.
- Each component that is to be fused should be held in position in the purpose-built clamping. The lengths of pipe hanging outside the jig should be supported by means of roller cradles.
- The pipe ends should be faced so that the finished surfaces are perfectly smooth free of visible ridges, valleys or other surface imperfections.
- The outside diameters of the pipe ends should match closely without the offset exceeding 10%.

- The pipe ends should be heated to the pipe manufacturer's recommended temperature and interfacial pressure. The Contractor should use a pyrometer or other surface temperature measuring device to confirm and record the actual surface temperature for each weld. Temperature indicating crayons should not come into contact with the surface to be welded.
- After the pipe ends have been properly melted, the heater tool should be removed within the specified time. The molten pipe ends should be brought together and allowed to cool without disturbance to form the permanent weld. The proper bead size and geometry specified for the pipe being welded should be formed.

3.4.13 Saddles/Sidewall Jointing

Saddle /sidewall fusion jointing shall be accomplished by using a mechanical saddle fusion machine that has been designed for this purpose to ensure proper alignment, temperature and force control. The following procedures shall serve as a general guide only. The Contractor shall obtain detailed jointing instructions from the manufacturer who shall have a technical representative available at the Engineer's request during the jointing process.

- Any dirt or coating that might interfere with the proper operation of the saddle fusion machine should be removed from the pipe and the surfaces of the pipe and saddle roughened to expose fresh material and any reside brushed away.
- Test fit the saddle fusion machine to ensure that alignment and contact are as they should be.
- Commence the fusion process and periodically verify the surface temperature using a pyrometer or other surface temperature measuring device. If temperature indicating crayons are used, they should not be used on a surface which comes into contact with the surfaces to be welded.
- After the heating period, remove the heater plate and check for the correct melt pattern on both the fitting and the pipe. Join the fitting to the pipe with the prescribed fusion force.
- Cool the joint without disturbance until the melt has formed a permanent weld. The joint should. not be subjected to any external stresses until the fusion joint has cooled.

3.4.14 Electro Fusion Jointing

Electro fusion jointing involves heating the electro fusion joint internally, either by a wire coil at the interface of the joint or by a conductive polymer. Heat is created by an electric current passed to the conductive material in the fitting.

- Ensure that the fitting is dimensionally appropriate for welding to the

Pipe. Clean the pipe surface in the joint area. Cut the end of the pipe square. Mark on the pipe surface the proper position of the fitting to be installed. Scrape the surface of pipe area to be joined, removing all surface degradation and contamination. Avoid contamination of the scraped pipe surfaces.

- Place the pipe and fitting in the clamping fixture to prevent movement of the pipe or fitting.
- Connect the electro fusion control box to the fitting and to the power source. Apply electric current to the fitting as specified in the manufacturer's instructions. Turn off the current when the proper time has elapsed to heat the joint properly.
- Allow the joint to cool for the recommended time and remove the clamping fixtures. Do not remove prematurely from the clamps as any strain on a joint that has not fully cooled can be detrimental to joint performance.

3.4.15 Mechanical Joints and Fittings

Many types of mechanical connection styles and methods exist. The Contractor shall submit suitable mechanical joints. All such joints shall be recommended and acceptance tested by the manufacturer of the pipe. Where marked on the Drawings end-load resistant fittings of an approved type shall be used.

When tightening polyethylene flanges care shall be taken to produce an equal torque load to the limits given by the manufacturer. A torque wrench shall be used. Since polyethylene creeps under load, it is essential that the bolts are re-tightened several times prior to commissioning to minimize the risk of leakage.

All joint materials and gaskets shall be suitable for use in the prevailing climate, soil, ground water, and potable water and irrigation water conditions.

3.5 TOOLS

The Contractor shall supply all necessary tools for cutting, chamfering, jointing, and testing and for any other requirement for satisfactorily installing the HDPE pipelines.

3.6 CONTROL OF WATER

The Contractor shall furnish, install and operate all necessary machinery, appliances, and equipment to keep the excavation sufficiently free from water during construction of the work to permit proper laying and jointing.

3.7 INSPECTION AND TESTING

3.7.1 Certification and Documentation

Contractor shall supply the Engineer with copies of certificate and test documents. Such documentation shall be subject to the Engineers' approval prior to shipping.

3.7.2 Test Results and Frequencies

The Manufacturer shall establish and maintain a current record of test results according to the requirements of the applicable standards and this specification. The Manufacturer shall perform all the tests required by ISO 4427 to demonstrate the characteristics and quality of the resin material and the dimensional tolerances of the pipe. The Manufacturer shall document all the tests, with frequencies and results as indicated in ISO 4427. The records shall be kept for 10 years as a minimum.

3.7.3 Inspection and Audit Requirements

Pipe shall comply fully with ISO 4427, the requirements of the PE 100 + Association and all the additional requirements of this specification.

To verify compliance with this specification, the Engineer shall reserve the right to appoint an independent third-party inspector to witness the applicable qualification tests, review production records, and inspect general handling and shipping procedures. The third-party inspector shall have full access to the testing and production facilities and will be a fully authorized representative of the Engineer.

3.7.4 Acceptance Criteria

The order shall meet the following criteria:

a. A copy of the raw material Manufacturer's "Certificate of Quality Control Testing" covering each batch of raw material used for pipes purchased under this specification, shall be available for inspection by the Engineer on request.

b. Pipe wall thickness shall be controlled by continuous scanning using ultra-sound or other qualified devices. These devices shall be regularly calibrated for accuracy by certificated agency.

c. Successful test performance and acceptable results for the testing program outlined in this specification.

d. Acceptable results, when tested by the Engineer from samples collected from storage of pipes at the site of works, for tests included in ISO 4427 and summarised in Table 3.1.

Table 3.1, Testing Requirements of HDPE Pipe

Sr. No.	Parameter to be Tested	Test Method
1	Mean Outside Diameter (Min. & Max.)	ISO 3126
2	Out-of-Roundness (Ovality)	ISO 3126
3	Wall Thickness (Min. & Max.)	ISO 3126
4	Minimum Required Strength	ISO 12162
5	Density	ISO 1183
6	Hydrostatic Strength at 20oC	ISO 1167
7	Elongation at Break	ISO 6259
8	Tensile Strength at Yield	ISO 6259
9	Longitudinal Reversion	ISO 2505
10	Carbon Black Content	ISO 6964
11	Melt Mass Flow Rate	ISO 1133

3.7.5 Defects

When the rejected item is a length or coil of pipe, the lengths or coils manufactured immediately before and after the defective lengths or coils shall be carefully examined. If further defects are found, this is sufficient cause for rejecting the entire batch. This will not apply to local damage that did not occur during manufacture, such as gouges or cuts during handling or transit.

3.7.6 Quality Assurance/Quality Control

A copy of the Manufacturer's QA/QC plan shall be submitted to the Engineer with its quotation for review and concurrence prior to award. If Manufacturer's facility is ISO certified, QA audit requirements shall be waived in favour of ISO 9000 registrar audits, unless the Engineer's trend analysis program indicates areas of concern.

3.8 PIPELINE TESTING

3.8.1 General

The Contractor shall submit for the Engineer's approval details of his proposed methods and programme for testing (including details of test equipment) and shall arrange for all tests to be witnessed by the Engineer. Unless otherwise directed by the Engineer, the Contractor shall ensure that no section of pipeline remains untested with pipe trenches and joints left exposed for more than 7 days after laying each pipeline section. The method of achieving this shall be entirely the Contractor's responsibility and no time extension or additional payments whatsoever shall be entertained on account of Contractor's failure to achieve this condition.

The Contractor shall provide all things necessary for carrying out testing and cleaning including potable water, pumps, gauges, pipes, connections, stop-ends and all other temporary works.

Pipelines shall be properly completed and supported before being put under test except as hereinafter detailed.

The Contractor shall provide for transmitting the unsupported end thrusts to solid ground at the ends or into the sides of the trenches.

Before testing any pipeline, the Contractor shall ensure that the anchorage of bends is complete and thrusts from all branch outlets are properly stayed.

No testing will be permitted until seven days after thrust blocks and other holding down works have been completed.

Open ends shall be stopped with plugs, caps, or blank flanges properly jointed and restrained from movement.

No claims whatsoever will be entertained on account of leaking valves, or any other difficulties in closing of lengths of pipe work for testing, which shall be entirely at the Contractor's expense.

All water required for testing and cleaning the pipelines shall be potable water drawn off at locations approved by the Employer and shall be provided by the Contractor at his cost.

In addition to any tests of individual joints or other interim tests which may be specified elsewhere, the Contractor shall submit all parts of the pipelines to a final acceptance test. Notwithstanding the foregoing the Contractor may at any stage of construction, carry out such other tests as he considers desirable to check materials and workmanship on the pipeline but this shall not relieve the Contractor of his obligations to achieve successful tests under the Contract.

The Engineer shall have power to require the Contractor to vary any test procedure or pressure as he (the Engineer) thinks fit at no extra cost to the Employer.

The Contractor should note that neither the satisfactory testing of pipeline, section of a pipeline or any other pipe work, nor the acceptance of such testing by the Engineer or his representative shall in any way relieve the Contractor of any of his responsibilities and obligations under the Contract.

The Contractor shall notify the Engineer at least 24 hours before hand of his intention to test a section of pipeline having satisfied him in the first instance that the section of pipeline to be tested in the presence of the Engineer is satisfactory in all aspects.

Test gauges used for testing pressure pipelines shall be of conventional circular type of approved manufacturer, not less than 8-inch diameter, calibrated in bars or psi. Before any gauge is used, the Contractor shall arrange for it to be calibrated independently and a dated certificate of its accuracy shall be provided to the Engineer.

One additional gauge as above shall be handed over to the Engineer for purposes of verification during testing.

Calibration of pressure gauges shall be carried out by the Contractor at regular intervals as required by the Engineer.

The Contractor shall remain responsible for the care of the works during testing of the pipe work.

3.8.2 Interim Pipeline Testing

The interim test shall be carried out after the pipeline section to be tested has been laid, jointed and backfilled to a depth of at least 12-inch above the crown of the pipe but leaving the joints exposed. The sections to be tested shall be approved by the Engineer. The joints between each tested section shall then be left exposed until the pipeline has passed the Final Test on Completion

For purposes of interim testing, the pipeline shall be divided into sections and each section shall be separately tested to the Engineer's satisfaction for deflection and pressure when each section is completed and before the joints are covered in the case of buried pipes.

The Contractor shall submit to the Engineer detailed procedures for performing hydrostatic pressure tests of installed piping, fittings, valves, meters and appurtenances for approval. Procedures for performing hydrostatic pressure tests for each section of pipeline shall indicate the location and capacity of the test pump, test pressure at the pump as well as that at the highest and lowest points procedures for venting the air from the pipeline and disposing the water after satisfactory testing.

Each pipeline or section thereof shall be filled with water and all air removed as far as possible. If permanent air vents are not located at all high points, the Contractor shall install suitable cocks at such points so that the air can be expelled as the line is filled with water. After all the air has been expelled all cocks shall be closed and the test pressure applied. The line shall be filled slowly to prevent possible water hammer. The test pump and gauge shall be connected to the pipeline at a location other than the highest point in the line to facilitate the release of air from the highest point.

The pressure in the pipeline shall then be raised steadily up to and maintained at rated pressure of the pipe (10-bars for PN10 HDPE pipe) for a period of not less than 12 hours to allow for absorption and achieve conditions as stable as possible for testing. The standing period will commence from the time at which the rated pressure (10-bars for PN10 HDPE pipe) was reached successfully, after which all exposed joints shall be carefully inspected for evidence of leakage.

If neither appreciable movement of the pipeline nor any leakage has been observed during the visual inspection the section shall be subjected to the proper pressure test.

Pumping shall then be resumed and the pressure slowly raised to the specified test pressure i.e., 15-bars for PN10 HDPE pipe (1.5-times rated pressure of pipe). The test pressure shall be continuously maintained by the use of the pump for a period of at least 3 hours and the amount of makeup water required to maintain the pressure shall be accurately measured (to the nearest 1/8 litre) regularly every 30 minutes throughout the test.

The pipeline shall be deemed to have passed the test if:

a. No water is visible coming out of the pipe or joints at any point

b. Leakage is equal to or less than the number of imperial gallons per hour as determined by the following formula:

$$Q = \frac{n \, x \, d \, x \sqrt{p}}{1850}$$

where,

Q = Leakage in imperial gallons per hour

n = Number of joints in test section

d = Nominal diameter of pipe in inches

P = Average test pressure during the test in psi

During all testing, the trench generally and the joint pockets in particular shall be kept clear of water and should the trench become unstable due to work or leaking on testing or re-testing it shall be excavated to solid ground and made up with lean mix concrete or such other material as the Engineer may direct, all at the Contractor's expense. Should a test fail, the Contractor shall at his own expense replace defective pipes or fittings or make good leaking joints or otherwise rectify defective work. Cleaning, inspection and testing shall then be repeated until the work is to the Engineer's satisfaction and at no extra cost to the Employer.

The length of the section of pipeline to be tested shall not normally exceed 1,500 feet or as directed by the Engineer.

A simple stop end consists of a section of steel pipe about 1.5-3.0 feet long onto which a closing plate has been welded, containing the necessary opening for accommodating ingoing water and out-coming air. The stop end may also include an opening through which the test water may be pumped from the line, if necessary. The stop end may be jointed to the pipe to be tested by means of a standard coupling or other method approved by the Engineer. Thrust blocks or temporary anchorages shall be provided to

hold the stop end in place against the test pressure. The Contractor may also use propriety restrained joints in lieu of thrust blocks.

3.8.3 Final Acceptance Testing

The final acceptance test shall be carried out after all lengths have been joined together on completion of construction and interim tests have been carried out satisfactorily on the entire length of the pipeline.

Final pipeline acceptance procedures shall be as prescribed above for interim pipeline testing. The Contractor shall repair the pipeline if it fails to pass this test. The test shall be repeated and repairs affected until the pipe line passes the test.

3.8.4 Valves

Valves and all pipeline appurtenances shall be hydraulically tested together with the pipeline in which they are installed. Valves shall be tested for operation under working pressure and shall be adjusted so that they operate smoothly, seat properly and are installed to tolerances recommended by the manufacturer.

Before pressure testing is started the Contractor shall re-check pipes and valves for cleanliness and shall re-check the operation of all valves. The "open" ends of the pipeline (or sections thereof) shall normally be stopped off by blank flanges or cap ends additionally secured where necessary by temporary struts and wedges all anchor and thrust blocks shall have been completed and all pipe straps and other devices intended to prevent the movement of pipes shall have been securely fastened.

3.9 PIPELINE DISINFECTION

3.9.1 General

Pipelines shall be disinfected after they have been thoroughly cleaned and at the time the pipeline final acceptance testing is satisfactorily completed.

3.9.2 Disinfection of Pipelines

All potable water pipe, fittings, valves, meters and appurtenances shall be disinfected by the Contractor as specified herein.

All water and chlorine required for disinfection of pipelines shall be provided by the Contractor at his own expense. Bacteriological testing will be performed at a laboratory approved by the Employer the cost of which shall be borne by the Contractor.

The attention of the Contractor is directed to the requirements of these Specifications whereby he is responsible for preventing the entry of foreign material of any kind into the pipe work. The Contractor shall take extreme care to keep the interior of the pipe work free of dirt and other foreign material. If in the opinion of the Engineer, direct or other foreign material

enters the pipe work, which will not be removed by flushing, then the Contractor shall clean and swab the interior of the pipe work with a five percent hypochlorite disinfecting solution to the satisfaction of the Engineer.

After testing and immediately before commissioning, all pipelines shall be washed out and disinfected as follows:

- All mains shall be flushed out with clean water until there is no evidence of foreign matter or colour in the waste flushing water.
- A stock disinfecting solution shall be prepared by mixing for not less than 5 minutes, in a clean container, Sodium Hypochlorite solution (15 percent available chlorine) and distilled water in the proportion of 0.8 litres to 1000 litres of water by volume. After mixing, the solution shall stand for a further 5 minutes after which the clear supernatant liquid shall be decanted into another clean container. Stock solutions shall be made up fresh daily.
- The main to be disinfected shall be filled with potable water at the same time as the stock solution is added through a convenient air valve in such quantities (to be determined by the Contractor and approved by the Engineer) as will result in a final solution containing 50-70 mg/l free chlorine. Care shall be taken to ensure that the stock solution is added at a constant rate, commencing when water is fed into the main and ending as soon as the main is full.
- Every main charged with disinfection solution shall stand for 24 hours. A sample shall then be taken at a washout valve by the Contractor in the presence of the Engineer, from whom the sampling bottle shall be obtained. If the sample does not show at least 2 mg/l free chlorine, disinfection shall be repeated. If the sample is satisfactory the main shall be emptied, flushed out and filled with potable water and allowed to stand for 1 hour.
- Two further samples shall then be taken as before, one for a further determination of free chlorine and the other, in a sterilized bottle, for bacteriological analysis. If the free chlorine determination shows more than 4 mg/l free chlorine the main shall be flushed out again. If the bacteriological analysis is unsatisfactory, disinfection and sampling shall be repeated until satisfactory results are obtained before the main is commissioned.
- The Contractor shall provide all equipment, materials and testing apparatus, etc., as may be necessary for the effective disinfection of all pipelines.

3.9.3 Cleaning of Pipe work

All pipe work shall be cleaned by the Contractor after all pressure tests and disinfection operations have been performed and accepted by the

Engineer. However, it is the responsibility of the Contractor to prevent all dirt and foreign mater from entering the pipe work and for cleaning each length of pipe and all fittings, valves, meters and appurtenances, of sand, dirt and foreign matter during the installation. Cleaning of chlorinated lines shall conform to the recommendations of the Chlorine Institute.

All potable water required for testing, flushing and disinfection of pipelines shall be provided by the Contractor at his own expense.

3.9.4 Disposal of Water Used for Testing, Disinfection and Cleaning

The Contractor shall provide suitable means for disposal of water used for testing, disinfection and flushing such that no damage results to facilities, structures or property. These means shall be subject to the approval of the Engineer and local authorities. Details shall be submitted to the Engineer upon request. The Contractor shall be responsible for any damage caused by his filling, testing, disinfection, flushing and wastewater disposal operations.

3.10 PACKING, MARKING AND VENDOR DOCUMENTATION

3.10.1 Pipe Identification and Packing

The marking information and sequence shall comply with ISO 4427. All pipes and fittings, including test samples shall be clearly and permanently marked using indent printing in a colour that contrasts with the pipe.

All pipes shall be indelibly marked at maximum intervals of 1m indicating at least the following information:

- The manufacturer's name and/or trademark;
- The dimensions (nominal outside diameter x nominal wall thickness);
- Material and designation;
- The nominal pressure (PN) in bar;
- The pipe series (S or SDR) (optional);
- The production period (date or code); and
- The number of this International Standard.

The word "water" shall also be included if the pipe is intended for potable water. The maximum quantity of pipe to have the same coil/length number is one silo (coiled pipe) or one bundle (straight lengths). The maximum combined length of pipe in the silo or bundle with the same coil/length number shall not exceed the maximum allowable coil length as specified,

When pipe material is boxed, me coil number shall be clearly marked on the outside edge of the box or silo. Invoices and packing lists shall include the date of manufacture and coil/length numbers for all material in the shipment.

The fittings shall be packaged in bulk or individually protected were necessary in order to prevent deterioration and contamination. The package

shall have at least one label with manufacturer name, type and dimension of the fittings and number of units.

3.10.2 Packaging and Transportation

The Contractor/Manufacturer shall provide packing and transportation procedures for approval by the Engineer and shall comply with the following requirements.

a. Delivery

Delivery of the plastic pipes and fittings to site, shall be no later than six months after the stamped manufacture date.

b. Weathering

A certificate from the pipe/fitting manufacturers shall be provided, confirming that the products may be stored in the open for minimum of 2 years without any adverse effect.

c. Tie-downs

Tie-downs shall be at least 100 mm (4.0 inch) wide and be clean and free from sand, gravel and other such materials. For straight length pipe (up to 12 m (39 ft), a minimum of 6 tie-downs are required.

d. Pallets

The pallets shall be suitable for transporting the material from the place of manufacture to the designated receiving location without causing any damage to the pipe. The pallets shall not contain any broken planks or extremities that may damage the coiled pipe or straight lengths. They shall be durable enough to prevent loose pallet nails from gouging the bottom coil/straight length.

e. Overhang

Pipe shall not overhang at either end of the trailer.

f. Stacking

The Contractor/Manufacturer shall not ship small coils stacked inside silos of larger coils. Frames manufactured for the containment of straight lengths of polyethylene pipe during transport and storage shall not contain nails or other fastening devices that may damage the pipe.

g. Trucking

Where pipes are transported by vehicles, the vehicles should have a flat bed and be free from sharp edges or projections. During transport, polyethylene pipes shall be protected from diesel fumes and be continuously supported to prevent movement between the material and its support.

h. Silos

Silo packs of coiled pipes shall be squarely stacked and well supported on pallets. Coils shall not overhang the pallets and, shall not be stacked higher than 2.3 m (8.0 ft)

3.11 STORAGE OF PIPES AND APPURTENANCES

All pipes and materials shall be stored in accordance with the manufacturer's recommendations and the following:

- Jointing materials and operational gear shall be stored under cover. Pipes may be stored in the open, but shall be placed on adequate timber bearers to prevent damage to sheathing or sockets. Pipes not delivered on manufacturers' pallets may be stacked one above the other up to three pipes high provided suitable protective packing is placed between them. If any pipes or fittings show signs of corrosions or deterioration during storage either they shall immediately be treated at no extra charge by the Contractor to arrest and prevent the corrosion or removed from site as the Engineer directs.
- The Contractor shall properly stack the pipes in his storage area and the stacks shall be laid out in a regular pattern and the limits of each stack marked so that the movement of cranes and vehicles is restricted to access tracks between stacks and the control of delivery and removal of pipes is facilitated.
- The number of tiers of HDPE pressure pipe stacks shall be as per the Manufacturer's instructions and approval of the Engineer. Each pipe, including those in the bottom course, shall bear evenly upon not less than three timbers with an aggregate width not less than 300mm. The pipes shall be stacked parallel to each other.
- The timbers supporting each course of pipes in a stack shall be of uniform thickness and stiff enough for the pipes to be rolled across the stack and shall be supplied by the Contractor at his own expense.
- The outermost pipes in each course shall be secured against rolling by sandbags or by wedges.
- Where the pipes are to be delivered and stacked by the Contractor on sites along the pipeline route, the areas where the pipes are to

be stacked shall, if required, be graded flat by the Contractor at his own expense to provide a firm and even surface and shall be kept free from loose stones, rubble or waste liable to damage the pipes.

- Jointing materials, valves, fittings and specials, meters, gauges and polyethylene sheeting shall be stored in covered storage areas until required for installation.
- Pipe shall be removed from storage and directly distributed to their point of installation only in such quantities as can be installed in one week.

3.12 MEASUREMENT AND PAYMENT

3.12.1 Measurement

Measurement for HDPE pipes for water supply shall be made for the actual quantity of the work done in linear metre or linear feet (whichever is included in Bill of Quantities) on the axis of the piping including all fittings, bends, crosses, tees etc. No deduction will be made for the laying lengths of valves, fire hydrants, specials, etc. installed in the lines

3.12.2 Payment

The unit rate quoted in the Bill of Quantities for supplying and laying HDPE pipe for water supply shall be the full compensation for all cost of completing the item of work as per provision of this section and shall include cost of pipe, its carriage to the site, laying, cutting, joining, testing and disinfecting, etc. and all incidentals to complete the item except valves assembly and backing blocks, which shall be paid separately.

SECTION-4 PIPELINE APPURTENANCES

4.1 SCOPE OF WORK

The work included in this section consists of providing, laying, jointing, cleaning, disinfection, testing and commissioning of pipelines appurtenances for water supply. The Contractor shall provide all labour, materials and equipment necessary including removing from storage, transporting to sites, excavation, backfilling and compaction, laying, jointing and testing, disposal of excess excavated materials and removal of surplus pipes, fittings, valves and jointing materials. The responsibility for the safety and soundness of all material shall rest with the Contractor.

The Contractor is advised to carry out any tests at his cost needed to satisfy himself regarding the soundness of the valves, appurtenances and jointing materials including the pipeline installation before acceptance for testing by the Engineer.

4.2 GATE VALVE

Gate valves shall be of cast iron body conforming to BS 5150 with bolted bonnet, solid wedge, inside screw, non-rising stem, flange connection and fitted with cast iron hand wheel.

Specific clauses of BS 5150 are amplified as follows:

Sr. No.	Parameter	Details
1	Clause 3: Types of Valves	Solid wedge with non-rising stem
2	Clause 4: Nominal Sizes	All valves shall be of flanged end with sizes as specified on the Drawings
3	Clause 5: Nominal Pressure	PN 16 unless otherwise specified on the Drawings
4	Clause 9: Body Tapping	As specified to BS 21 (1S0 /R7) fitted with bronze or gunmetal plug
5	Clause14: Operation	Gate valves shall be provided with cast iron hand wheels or square heads for tee key operation as required. The direction of operation shall be clockwise to close the valve. Hand wheels shall require a force not greater than 20 kg on the outer rim to operate with a balanced pressure across the valve. Tee keys shall require a force not greater than 12 kg applied at the opposite ends of a standard key from the closed position.
6	Clause 19: Test Certificates	The Contractor shall provide a test certificate confirming that the valves have been tested in accordance with BS 5150

Sr. No.	Parameter	Details
		and stating the actual pressure and medium used in the test. In addition, the Contractor shall ensure that the Engineer has access to the manufacturer's works at all reasonable times for the purposes of inspecting the assembled valves and witnessing testing.

The material of construction of gate valves shall be as under:

Sr. No.	Part	Material
1	Body	Grey cast iron
2	Bonnet	Grey cast iron
3	Wedge	Grey cast iron
4	Gland	Grey cast iron
5	Stem	Stainless steel 304
6	Seat Ring, Wedge Ring	Stainless steel 304
7	Back Seat Bush	Stainless steel 304
8	Nuts & Bolts	Stainless steel 304
9	Painting	Wet blue epoxy paint, corrosion resistant

4.3 CHECK VALVE

Check valve shall comply with the requirements of BSS 5153. The valve shall be of swing type with quick acting single door and pressure rating of PN 16 unless otherwise specified on the Drawings. The valve design shall ensure closure in the shortest possible lime following deceleration of the water column, ideally reaching its seat without slamming at the instant forward motion of the column cases.

The material of construction of check valves shall be as under:

Sr. No.	Part	Material
1	Body	Grey cast iron
2	Bonnet (Top Plate)	Grey cast iron
3	Disc	Grey cast iron
4	Seat Rings	Stainless steel 304
5	Hinge Pin	Stainless steel 304
6	Disc Hanger	Grey cast iron
7	Gasket	Flexible graphite
8	Nuts & Bolts	Stainless steel 304
9	Painting	Wet blue epoxy paint, corrosion resistant

Swing Check Closure is affected by gravity (Weight of disc) and reverse flow. The pivot point of the swing check is outside the periphery of the disc and the greater the head, the greater the possibility that the fluid will flow back through the valve before the disc can be shut off. To effect complete shut off, the disc of a swing check valve must travel through a 700 to 900 arc to the valve seat. Without resistance to slow the disc's downward thrust and

reverse flow, the shut off can result in slamming and damaging water hammer.

4.4 AIR-RELEASE VALVE

Automatic air relief valve shall be designed to meet the following conditions:

a. Discharge air during charging of the pipeline.

b. Admit air during emptying of the pipeline or when the pipe in pressure falls below atmospheric pressure during a surge event.

c. Discharge air accumulated at local peaks along operating conditions the pipeline under normal

Conditions 'a' and 'b' shall be met by the employment of a large orifice capable of handling large volumes of air at a high flow rate and condition 'c' by a small orifice capable of discharging small quantities of air as it accumulates. Valves with air intakes or exhaust facilities shall have approved screening arrangements to prevent the ingress of air borne sand.

The valve shall conform to AWWA C512 pressure rating of PN 16 unless otherwise specified on the Drawings. Valve Body ends shall be flanged with raised faces and drilled to EN 1092-1.

The material of construction of air release valves shall be as under:

Sr. No.	Part	Material
1	Body	Grey cast iron
2	Bonnet (Top Plate)	Grey cast iron
3	Float Ball	Stainless steel 304
4	Gasket	EPDM - Asbestos Free
5	Nuts & Bolts	Stainless steel 304
6	Painting	Wet blue epoxy paint, corrosion resistant

Each valve shall be provided with isolating valves as detailed in the Drawings.

4.5 VALVE CHAMBERS

Chambers for gate valves, air valves, washouts, etc. shall be constructed in accordance with the details shown on the Drawings, or as directed by the Engineer.

Brick masonry, Portland cement concrete, and other materials shall meet the specified requirements of the relevant sections of these specifications.

4.6 VALVE BOX

Valve boxes shall be provided for all valves which are installed below ground level in conformance with the details shown in the Drawings. Valve boxes shall be of the heavy-duty type capable of withstanding a ten-ton load when located within carriageways. Ordinary valve boxes shall be used in other locations. All valve boxes shall be of the lockable type. They shall be installed

on concrete bases as shown in the Drawings.

4.7 THRUST BLOCKS

The Contractor shall construct all thrust blocks as shown on the Drawings. Thrust blocks shall be constructed to the dimensions shown on the Drawings. The thrust blocks are designed for soil parameters as shown on the Drawings. Where considerably better ground conditions, such as rock, are encountered, the dimensions of the particular thrust blocks may be reduced. Supporting calculations for any reduced size thrust blocks must be submitted to the Engineer at least 48 hours before construction of that particular thrust block commences.

Unless otherwise specified or directed, thrust blocks shall be provided on pipelines laid to gradients steeper than 1:20; up to 1:15 every third pipe shall be anchored, up to 1:10 every second pipe and at 1:5 every pipe should be anchored.

Concrete shall extend to undisturbed ground on thrust faces or thrust blocks and on both faces of anchor blocks.

Each thrust block shall be designed to have a sufficient bearing area and shall be placed to safely transmit to the surrounding point. Thrust devices shall be cast-in-place concrete. Thrust blocks shall be constructed of Class-C concrete as included in SECTION-20.5.2 and shall be placed between fitting and trench wall or trench bottom, as the case may be. The bearing faces of the block shall be placed against freshly cut and undisturbed trench wall or bottom of sound material. If the thrust exceeds the bearing value of the surrounding soil, the soil shall be pre-compacted before placing concrete. All concrete shall be kept behind the sockets and flanges of fittings. Formwork shall be constructed wherever necessary to confine the concrete to the prescribed dimensions for the block. All form lumber shall be removed before testing.

The blocks shall, unless otherwise shown or directed by the Engineer, be so placed that the pipe and fittings joints will be accessible for repair. Before internal pressure is applied to a pipeline, all concrete thrust blocks shall have been constructed and cured for a minimum of 7 days.

4.8 APPROVAL OF MATERIALS AND EQUIPMENT

As soon as practicable but within thirty-days after the receipt of notice to proceed and before any material or equipment is purchased, the Contractor shall submit for approval by the Engineer a complete schedule of materials and equipment to be incorporated in the work, together with the names and addresses of the manufacturers and their catalogue, item numbers and trade names. The schedule shall include catalogue cuts, diagrams, drawings, and such other descriptive data and as may be required by the Engineer. Samples of materials shall be provided as required. No consideration will be given to partial lists submitted from time to time. Approval of materials and

equipment under this provision shall not be construed as authorization of any deviations from the specifications unless the attention of the Engineer has been directed to the specific deviations. Laboratory results and certifications, specified or otherwise required, shall be submitted prior to delivery of the material or equipment to the site.

4.9 TESTS AND ACCEPTANCE

All valves, fittings and accessories delivered to the job site shall be accompanied by test reports certifying that the valves, couplings and/or fittings and accessories conform to the relevant specifications.

The Contractor shall take the necessary measures to allow the Engineer to be present during the tests at the factory, if the Engineer finds it necessary to do so. Failure to present the aforementioned certificate, or to inform of the date and time of the factory tests, shall constitute grounds for rejection of the valves, fittings or couplings that do not comply with these conditions.

Acceptance of such material shall only be possible if the rejected batch of valves, fittings and joints is tested under the Engineer's supervision, at the Contractor's expense, and only those passing the tests shall be accepted.

In addition, the right shall be reserved for the Engineer to subject any consignment of valves, fittings and couplings to any or all of the tests, over and above the tests conducted by the manufacturer. The Contractor shall furnish all labour, material and equipment necessary to assist in performing the tests and inspecting the valves, fittings and couplings.

4.10 MEASUREMENT AND PAYMENT

4.10.1 Measurement

Measurement for fire hydrants, valves air release valves, washout valves etc. shall be made in number and shall include the chamber and all other materials to complete the work as per Drawings including connection with pipeline. Backing blocks for bends, tees etc. shall be measured in cubic foot or cubic metre (whichever is included in Bill of Quantities).

4.10.2 Payment

The unit rates quoted in the Bill of Quantities for the supply and installation of fire hydrants, air release valves, sluice/gate valves, washout valves including chambers and other specials and shall be full compensation for supply, installation, testing, commissioning, disinfecting and all incidentals to complete the items of the work as per Drawings. The thrust blocks provided will be measured separately for payment.

SECTION-5 PIPE BEDDING

5.1 SCOPE OF WORK

Wherever specifically called for by means of notes on the contract Drawings or by written order of the Engineer, the Contractor shall furnish and place sand bedding under water lines, drain pipes and other structures as a separate item of payment.

5.2 PURITY AND STACKING

Sand bedding shall be from a source and of specifications approved by the Engineer.

The sand stone shall be free from clay, salt, alkali, organic matter, shale, loam, soft flaky particles and other deleterious substances. It shall be stacked at the place designated by the Engineer and kept free from the admixture of deleterious materials mentioned herein. The sand shall not contain clay/silt more than 5%. Laboratory testing prior to its use under bedding will be arranged.

5.3 PLACING OF BEDDING MATERIAL

The material for bedding shall be placed to the specified thickness and compacted by rammers of approved weight. The compaction level shall not be less than 95% of modified dry density as determined by AASHTO T-180.

5.4 MEASUREMENT AND PAYMENT

5.4.1 Measurement

The measurement shall be made by volume for the actual quantity of the work done and the unit of measurement shall be cubic foot or cubic metre (whichever is included in Bill of Quantities).

5.4.2 Payment

Payment for this item of work shall be made for the actual quantity of work done as specified in this section, at the unit rate quoted in the Bill of Quantities.

SECTION-6 WATER SUPPLY SERVICE CONNECTIONS

6.1 SCOPE OF WORK

Work under this section consists of furnishing all material, plant, machinery, labour and performing all functions and operations in connection with the execution of service connections for water supply, in strict accordance with the Drawings and applicable specifications and as directed by the Engineer.

6.2 MATERIAL REQUIREMENTS

SECTION-7 THE EARTH WORK SHALL BE PERFORMED AS PER REQUIREMENTS OF SECTION-2 EARTH WORK FOR WATER LINES

.

Service connection pipe shall be of HDPE of diameter as shown on the Drawings. Whereas, Clamp Saddle shall of Polypropylene with built-in rubber washer. Fittings and specials shall be as recommended by the manufacturer of the pipe and as approved by the Engineer. The plugging of the end will be part of the item.

7.1 CONSTRUCTION REQUIREMENTS

Service connection shall be executed as per Drawings or as indicated by the Engineer.

Connection arrangement shall be as per requirements/recommendations of the manufacturer of the pipe and as directed by the Engineer. Service pipe shall be connected with the pipe running either in front of the individual plot or from other side of the road. Service end of the pipe shall be duly plugged.

7.2 MEASUREMENT AND PAYMENT

7.2.1 Measurement

Measurement for service connection shall be number of service connections installed, tested and commissioned including all fittings, saddle arrangement, etc. but excluding cost of pipe as per specifications and accepted by the Engineer for payment.

Measurement for HDPE pipe of specified diameter is in linear metre or linear feet (whichever is included in Bill of Quantities) on the axis of the pipe.

7.2.2 Payment

Measurement as carried above shall be paid for at the unit rate quoted in the Bill of Quantities and shall be full compensation for furnishing all materials, tools, plants, labour and incidentals to complete the work.

PART-C, TUBE WELL

SECTION-8 GENERAL

8.1 DESCRIPTION

The tube well of indicated capacity is to be drilled by direct rotary or reverse rotary method. Total depth of borehole shall vary depending upon the material encountered. An accurate drilling log of the tube well is to be made, and samples of the materials encountered through which the tube well is drilled are to be preserved and handed over to the Engineer.

Upon completion of drilling, blind and slotted tube well casing sections, of specified material, diameter and length are to be placed in the tube well, mild steel pump housing casing of required diameter and length is then to be connected to the tube well casing by means of a tapered reducer and installed in the tube well.

After installation of the pump housing and tube well casing, the tube well is to be shrouded (packed and grouted) with selected gravel of specified quality, sizes and gradation and specified cement grout after which it is to be developed and tested until it will efficiently produce clear water at a pumping rate of 50% higher than the designed capacity. After the tube well has been satisfactorily developed and tested, pump house of the specified design is to be constructed. The tube well is to be equipped with a vertical turbine pump connected to a vertical hollow shaft, electric motor. All motor control and necessary electrical equipment are to be installed, placed in operating condition and tested to demonstrate that the entire installation meets the requirements of the contract documents. A chlorinator and other equipment are to be installed with the tube well as specified.

The connection of electrical equipment to the power main shall be by others, testing of the installed equipment is however, part of this contract. Construction of facilities to convey water from the discharge pipe flange point to water main is part of this Contract.

8.2 CONTRACT DRAWINGS

The Drawings covering tube well and appurtenant works show the scope of work to be performed by the Contract. The tender drawings shall not be used as a basis for placing preliminary orders for materials. The drawings issued for construction will be drawings from which shop erection, concrete placing, formwork or other construction details shall be prepared by the Contractor. The works shall be executed in conformity with the Drawings issued.

8.3 SIZE OF TUBEWELL

The tube well may vary in depth, therefore, minimum and maximum depth for the tube well shall not be guaranteed. The pump head, pump setting and length of housing of tube well shown on the Drawings are indicative only. The

horsepower, rating of the pump motor and the motor controls are specified under applicable sections of specifications.

8.4 BILL OF QUANTITIES

The bill of quantities set forth is the approximate quantities of the works. The amount of bid for each item of bill of quantities shall be full payment for completion and maintenance of the works specified herein and elsewhere in the document and Drawings.

8.5 STANDARDS

Except as otherwise provided by this specification or the Drawings and in case no specification and standards are indicated in the document, all materials, equipment fabrication and testing thereof shall conform to the latest applicable standards and specifications in accordance with the specification epilogue.

If the Contractor, at any time and for any reason wishes to deviate from the above standards, or desires to use material or equipment not covered by the said standards, he shall state the exact nature of the change, the reasons for making the change and shall submit the complete specifications of the materials and equipment for approval of the Engineer, whose decision shall be conclusive and binding on the Contract.

8.6 CONSTRUCTION EQUIPMENT AND MATERIAL

Unless otherwise specifically stated in the document, the Contractor shall furnish all necessary construction equipment and material for the construction and installation of the tube well and appurtenances. The construction equipment shall include but not be limited to drilling equipment of the Rotary or percussion type, together with all supporting and additional equipment and accessories necessary for taking samples for installing the tube well casing and pumping-housing casings, for placing gravel shrouding and cement grouting, for developing and testing the tube well, for determining the straightness and verticality for pump housing casing; for constructing the cement concrete pump pedestal and floor slab for installing the pump motor, motor controls and necessary electrical equipment, chlorinator, valves and discharge pipes, for constructing the pump house and for the performance of development tests.

All construction equipment shall be in good, serviceable condition and shall be capable of doing the work.

The Contractor shall also furnish all testing instruments, equipment and materials required by the Contractor for his use in ascertaining that construction materials, permanently installed equipment and the finished work conforms to the requirements of specifications and for carrying out all

tests required by the specifications to be performed by the Contractor.

Materials to be furnished by the Contractor shall include all materials necessary for the operation and maintenance of the Contractor's equipment and all the materials for installation in the tube well including casing, gravel shrouding, Portland cement, brick, reinforcement, aggregates, electrical conductance, wiring and fittings and all other equipment and materials necessary to perform the work in complete and satisfactory manner.

8.7 CLEAN UP

Upon completion of construction, equipment installation and operation, test of tube well, the Contractor shall tear down and remove all temporary structures provided and occupied by him, shall remove all plant and refuse, all waste materials; shall remove from the site of the work, or satisfactorily cover with earth.

SECTION-9 DRLLING OF BOREHOLE

9.1 SCOPE OF WORK

The work covered under the specifications is furnishing all plant, labour, equipment, appliances, and materials, and in performing all operations in connection with the drilling of borehole(s) in strict accordance with this section of specifications in reasonably close conformity with the lines and dimensions shown on the Drawings or established by the Engineer.

9.2 DRILLING OPERATION

Drilling of tube well shall include, but not be limited to moving in, setting up, preparing the site, drilling the borehole, collecting data and removing temporary casing, dismantling, moving out and cleaning up. Measurement for tube well drilling will be made of the actual depth of each borehole drilled, measuring from the original ground surface. No measurement will be made over-drilling required because of the sloughing, caving ground or for the Contractor's use in setting casing; for tube well abandoned due to jammed tools, caving ground, or negligence on the part of the Contractor; or for tube well not constructed in accordance with all the requirements of these specifications.

9.3 DRILLING

The Contractor shall drill each borehole of the diameter indicated on the Drawings and at the locations shown on the Drawings. The Contractor shall prepare the site for the construction of the tube well and shall provide for the disposal of water, cuttings, and refuse from his operation away from the site and to the satisfaction of the Engineer.

The borehole shall be drilled by the reverse circulation rotary method. Each borehole shall be drilled to the depth specified by the Engineer. It is anticipated that the depth of tube well (s) will vary; however, no minimum depth of any individual tube well or average depth for all tube wells is guaranteed. The borehole shall be drilled sufficiently straight and plumb so that the pump and the tube well casing may be installed concentric with the hole and within the tolerance specified for the plumbness of the casing. Waste materials from the drilling operation shall be disposed of in a manner approved by the Engineer.

The Contractor shall be responsible for protecting the tube well from contamination by foreign materials until the completed tube well and appurtenant facilities are accepted by the Engineer. The Contractor shall bear any expense that may result from damage to any tube well, tools or equipment that may be caused by caving, washing or other disturbance within the tube well.

If unstable material is encountered in drilling, the Contractor shall stabilize the material in a manner approved by the Engineer. The use of drilling fluid additives or other suitable materials may be employed for stabilizing the borehole when such use is specifically approved by the Engineer. If necessary, temporary casing shall be furnished and installed by the Contractor to hold walls of the hole during drilling operations and until the gravel shrouding has been placed. All temporary casing shall be removed by the Contractor in stages as gravel shrouding is placed. The temporary casing may be new or used and will remain the property of the Contractor.

If, in the opinion of the Engineer, it is necessary to discontinue work on any borehole because it is out of line more than the amount specified or on account of jammed tools, caving ground or because of negligence on the part of the Contractor, he will not be entitled to payment for any work done or materials furnished for borehole abandoned as a result of his operations or negligence.

9.4 DATA AND RECORDS

The Contractor shall keep an accurate drilling logs of borehole drilled including description of all materials encountered and their location in the borehole. The fact that the Engineer or his representative may be present and keep a separate record, shall not release the Contractor from this responsibility. In the case of defective or incomplete records, the Contractor shall complete the records at his own expense. All records and data shall be kept by the Contractor on forms approved by the Engineer. The Contractor shall deliver to the Engineer, the original of all records and all such records shall become the property of the Owner.

Representative ditch samples or cuttings of the materials penetrated shall be taken of each lithology encountered and from each ten feet of the depth for non-water bearing depth and each four feet for water bearing depth of the borehole. Special care shall be exercised to determine the thickness and location of each change in material encountered and to obtain satisfactory samples. Immediately upon taking samples, the samples shall be placed in cloth bag, partitioned wooded box, or other approved container, properly marked for identification, and plainly labelled with the depth of the top and bottom of the section of the borehole represented. The containers shall be furnished by the Contractor, the method of obtaining, processing and storing the samples shall be subject to approval by the Engineer. The Contractor shall deliver all samples to the Engineer at the site of the tube well or to the filed headquarters of the Engineer as directed.

9.5 MEASUREMENT AND PAYMENT

9.5.1 Measurement

The quantity of drilling to be paid for shall be measured by linear metre or linear foot, whichever is included in Bill of Quantities, and drilled as mentioned above.

9.5.2 Payment

The accepted quantity measured as provided above shall be paid for at the contract unit price per linear metre or linear foot of drilling (whichever is included in Bill of Quantities) of specified diameter of borehole for the pay items included in the Bill of Quantities, which price and payment shall constitute full compensation for furnishing all materials, various drilling operations, labour, equipment, tools and incidentals necessary to complete the item.

Backfilling of the borehole, if a particular borehole is not developed, shall be done as per instructions of the Engineer, payment for which shall be made separately.

SECTION-10 TUBEWELL CONSTRUCTION

10.1 SCOPE OF WORK

The work shall consist of furnishing all plant, labour, equipment, appliances, and materials and performing all operations in connection with tube well construction except drilling, in accordance with these specifications and in close conformity with the dimensions shown in the Drawings or as established by the Engineer.

10.2 CASINGS

Casing shall consist of all work required in connection with furnishing and installing casing pipe, comprising of steel conductor pipe and steel pump housing pipe and fibre glass / brass or any other specified material, tube well casing (both plain and slotted), required for the tube well and shall include, but not be limited, providing storing, fabricating and installing including concentric reducers and equalizers.

10.2.1 Fibre Glass Strainer & Blind Pipe

Glass Fibre shall conform to the following specifications:

- ASTM-2996 for Filament-Wound Fibreglass
- ASTM 2997 for Centrifugally Cast Fibreglass

The fibre glass strainer will be from the approved source. The Contractor to this effect will submit for approval of the Engineer, a sample with complete specifications. Prior approval of the material is obligatory and without this approval, the procurement and installation of material will not be accepted for measurement and payment.

10.2.2 Fabrication

The depth of conductor pipe and pump house casing will be established by the Engineer for the tube well depending upon local sanitary conditions of shallow ground waters. Lengths of specified diameter of steel casing shall be provided to extend the pump housing casing from the elevation of the top of the pump housing casing to the depth established by the Engineer.

Adjoining sections of conductor pipe and pump housing casing shall be assembled by field welding. Butt welding straps shall be provided. All field welding shall be performed by the electric arc method, using heavily coated welding rods suitable for all position welding. After being deposited welds shall be cleaned of slag and shall show uniform sections, smoothness of weld metal, feather edges without overlap, and freedom from porosity and clinkers. The pump housing casing shall be connected to tube well casing with a concentric tapered reducer.

The length and sizes of tube well casing to be installed will be specified for the tube well by the Engineer, and will be sufficient to extend from the bottom of the pump housing casing to the bottom of the tube well. The bottom of the tube well casing shall be fitted with a bail plug. The tube well casing shall consist of slotted sections for installation in the water yielding formation and plain pipe sections in the lowest one metre of the tube well and opposite non-water yielding formations as directed by the Engineer.

10.2.3 Installation

The Contractor shall install the entire pump housing and tube well casing assembly straight, plumb, and concentric in the drilled hole to permit the installation of the pump in such a manner that it will operate satisfactorily and without damage. The methods employed by the Contractor in the installation of the casing and in obtaining or correcting the verticality and straightness of the pump housing casing shall be subject to the approval of the Engineer.

Centralizer shall be attached to the pump housing casing so that it will be centred in the drilled hole throughout its entire length and held in such position while gravel shrouding is being placed. Centralizers will be placed at 25-feet intervals throughout the length of the tube well or as directed by the Engineer.

The Contractor shall install the pump housing casing, so that the deviation of its axis from the vertical shall not exceed 35 mm at the bottom of the pump housing casing. Measurements for determination of verticality and straightness of the pump housing casing shall be made by the Contractor in the presence of the Engineer, upon completion of gravel shrouding. Plumbs, pipes and dummies used in these tests shall be approved by the Engineer.

Measurements for determining the deviation of the pump housing casing from the vertical shall be made by the use of a circular plumb having a minimum outside diameter of 15 mm less than the inside diameter of the pump housing casing. The plumb shall hang vertically and shall be suspended in the centre of the casing. When the plumb is lowered to the bottom of the pump housing casing, the line from which the plumb is suspended shall not deviate from the centre of the pump housing casing at the top by more than that corresponding to a deviation of the plumb of 35 mm at the bottom of the pump housing casing. All deviations shall refer to a vertical line passing through the centre of the pump housing casing at the top.

Straightness shall be determined by lowering a section of pipe 40 feet long or a dummy of the same length to the bottom of the pump housing casing. The minimum outer diameter of the pipe or dummy shall be 15 mm less than inside diameter of the pump housing casing. If a dummy is used, it shall consist of a rigid spindle with three cylindrical rings, each ring having a height of at least 300 mm. The rings shall be true cylinders and shall be located at each end

and in the centre of the dummy. The central shaft of the dummy shall be rigid so that it will maintain the alignment of the axis of the cylindrical rings. The pump housing casing shall be sufficiently straight so that the pipe or dummy can be passed freely throughout the entire length of the pump housing casing.

The tube well failing to meet the specified requirements for straightness, verticality and concentricity shall be abandoned, and the Contractor shall construct a new well at his own expense at an alternative site designated by the Engineer.

10.3 GROUTING

The annular space outside of the conductor pipe shall be sealed with cement grout. The grout shall consist of one part of cement and one part of sand by volume and not more than 5 gallons of water per cubic foot of cement. Grout materials shall be ordinary Portland cement conforming to BS 12, clean sand and clean portable water. The annular space shall be flushed with water prior to grouting to ensure that the space is open and to remove foreign material. The grout shall be applied from the bottom up and in one continuous operation. The grout shall be placed through a minimum 1-inch diameter grout pipe extending to the bottom of the annular space initially and shall remain submerged in the grout during the entire time the grout is being placed to ensure complete filling of the annular space. The grout shall be pumped into the pipe or applied continuously by gravity.

The pipe may be left in place or it shall be gradually removed. In the event of interruption in the grouting operations, the bottom of the pipe shall be raised until all air and water have been displaced from the grout pipe. The grout shall be allowed to set a minimum of 7 days after placement prior to resuming work on the well.

10.4 GRAVEL SHROUDING

Gravel shrouding shall consist of all work required in connection with furnishing and installing gravel shrouding in the annular space between the conductor pipe and the pump housing pipe, the walls of the borehole and the outside of the casing assembly and in any uncased length of borehole including but not limited to, developing the gravel source, excavating, stockpiling, grading, washing, storing, shipping, and installing gravel shrouding in the tube well.

10.4.1 Material

All gravel used for shrouding shall be clean, hard, well-rounded, washed, carbonate free and water-worn, without thin, flat particles and with the gradation as included in Table 10.1.

Table 10.1, Gradation Requirements for Shrouding Material

Sr. No.	Sieve	Percentage Passing
1	3/8 inch	100
2	No.4	60-80
3	No.7	20-40
4	No.14	0.50

10.4.2 Installation

The specified spaces shall be gravel shrouded by the Contractor from the bottom to the top of the tube well in such a manner that there will be no voids other than the annular space between the gravel particles. The method of placing the gravel, and the equipment used, shall be subject to approval by the Engineer. Water shall be circulated in the tube well, as the gravel is being laced, by lowering the drill pipe inside the casing and operating the circulation pump. The gravel shall be placed to the top of the tube well and shall be finally settled by bailing after all gravel has been placed. The top of the gravel shrouding shall be maintained at the ground level at all times during development, testing and pumping. Gravel and gravel placement not meeting these requirements will be subject to rejection by the Engineer, and all gravel so rejected shall be replaced by the Contractor at his own expense. Temporary casing, if used, shall be carefully withdrawn in 1-3 meters stages during placement of gravel shrouding and gravel shall be introduced so that each stage of the hole above the bottom of the casing is completely filled before the casing is withdrawn to the next stage. The process of withdrawing the temporary casing is at least 3 meters above the top of tube well casing. Above this point, the temporary casing may be removed or left in place, at the option of the Contractor; however, no payment will be made to the Contractor for temporary casing left in place.

10.5 DEVELOPMENT AND TESTING

Development and testing shall consist of all work required in connection with the development of the tube-well to produce the design capacity of water. It is carried out by breaking the layer of bentonite or sealing clay or compounds in the borehole, and taking out mud, chemical used and fine particles of sand from the shrouding and the aquifer near to shrouding throughout the depth of the tube-well strainer. The development of the well shall be so effective that after its completion the turbidity of water and sand content shall be reduced to minimum permissible limit as recommended by WHO standards. After completion of development of tube-well, the water shall be tested to determine the chemical and bacteriological quality of water, draw down at designed discharge and the specific capacity of tube-well. Any tube-well not developed properly and not meeting above standards shall be rejected and re-drilled. The recovery of tube-well during

the test shall also be observed.

10.5.1 Method

The tube-well shall be developed with vertical turbine pumping unit preferably closely coupled with a diesel engine through universal cross shaft which facilitates in pump speed adjustment to draw required discharge from the tube-well. Electric prime mover may also be used but with such arrangement which give variable speeds to the pumping units. The pumping unit shall allow the measurement of water level at any time during operation of the pump; and should be able to reverse its direction of rotation.

10.5.2 Equipment Required

The Contractor shall furnish all the equipment required for the development and testing of the tube-well as indicated below:

a. Vertical turbine pump with variable speed and reversal in direction of rotation. Capable of discharge twice the rated capacity for the design discharge of the tube-we/l.

b. Prime Mover (Electric or diesel) closely coupled with V.T.P. and capable to give a variable/ adjustable speed to the pumping unit.

c. Discharge Measuring Device, Electronic flow metre, sluice valve for regulation of discharge.

d. Electronic measuring device to measure water level in tube-well during operation of pumping unit.

e. Imhoff Cone (Sand Cone)

10.5.3 Back Wash

Back washing is done by reversing the direction of the pumping unit for a small time depending upon the condition of the water pumped. The water is pushed back into the aquifer thus stirring the locked sand particles and loosening them for pumping out. Back washing of tube-well shall be done during development at suitable intervals, to pump all fines from the tube-well shrouding. It shall be single backwash if the well is not pumping greater quantity of sand and shall be doubled if it is sandy. The development and backwashing shall be continued till the sand contents are reduced to permissible limit, which shall be checked continuously by Imhoff Cone graduated in PPM (parts per million).

10.5.4 Duration

Static water level or sub soil water level shall be measured before start of development.

a. Development (1st Stage)

Initial development shall be done step wise as included in Table 10.2.

Table 10.2, Duration of Development for Tube Well

Sr. No.	Discharge	Period of Development
1	0.75 times the designed discharge of tube well	1 hour
2	1.00 times the designed discharge of tube well	1 hour
3	1.25 times the designed discharge of tube well	1 hour
4	1.50 times the designed discharge of tube well	3 hours
5	2.00 times the designed discharge of tube well	3 hours
	Total	9 hours

Backwash shall be done every 5-minutes depending upon the sand contents pumped.

b. Recovery (1st Stage)

Pump shall be stopped after 1st stage of development and well shall be allowed to recover its water table. Reading/measurement of water table shall be taken as provided in the under-mentioned intervals.

Table 10.3, Frequency of Measurement during Recovery Period for Tube Well

Sr. No.	Period (from pump closure)	Measurement Frequency
1	1st 5 minutes	Every minute
2	Up to15 minutes	Every 2-minutes
3	Up to 30 minutes	Every 5-minutes
4	Up to 1 hour	Every 10-minutes
5	Up to 3 hours	Every 20-minutes
	Total	3-hours

c. Testing for Development (2nd Stage)

The well shall be pumped in steps as included in Table 10.2.

Sand contents shall be measured every 5-minutes during each pumping, however during 1st five minutes sand content shall be taken every minute. The water level shall be measured in the same way as explained in Recovery period, for each pumping stage and draw down (the difference between the static water level and that during pumping) shall be worked out for each measurement

d. Recovery (2nd Stage)

The well shall again be allowed to recover and the measurements of water table shall be carried out in the same way as in the first stage of recovery; Table 10.3.

The difference shall be noted between 1st stage and 2nd stage of recovery.

e. Testing for Re-Development (3rd Stage)

The tube-well shall be re-developed for another 9 hours in steps as included in Table 10.2.

Sand contents shall be measured every 5-minutes during each pumping, however during 1st five minutes sand content shall be taken every minute. The water level shall be measured in the same way as explained in Recovery period, for each pumping stage and draw down (the difference between the static water level and that during pumping) shall be worked out for each measurement.

f. Recovery (3rd Stage)

Well shall again be allowed to recover for 3 hours and measurements of water table shall be done as in 1st and 2nd stage; Table 10.3. There shall be no difference at the recovery of water table between 2nd stage and 3rd stage. If it is observed that there is an appreciable difference of recovery, well shall he redeveloped for 6 hours with back wash and recovery should again be allowed for 3 hours to match it with 3rd stage recovery. The process shall be repeated till the preceding recovery is matched.

g. Stop Pumping

The pump shall be stopped for next 4 hours before start of final pumping test for approval of the well.

h. Final Pump Test

The tube-well shall be pumped finally for 4 hours at the rated discharge and final draw down shall be noted to find out the specific capacity of the tube-well.

Hence the summary of development and testing of tube-well is included in Table 10.4.

Table 10.4, Summary of Tube Well Development Procedure

Sr. No.	Development Step	Time Period

1	Development	
	Development, 1st Stage	9 hours
	Recovery, 1st Stage	3 hours
2	Testing	
	Development, 2nd Stage	9 hours
	Recovery, 2nd Stage	3 hours
	Development, 3rd Stage	9 hours
	Recovery, 3rd Stage	3 hours
	Step Pumping	4 hours
	Final Pump Test	4 hours
	Total	44 hours

The duration of development and testing given above is minimum, and may be increased to total duration of 72 hours as per the direction of Engineer.

10.5.5 Performa for Records

Proper Performa shall be developed for development, recovery and testing of the tube-well giving discharge pumped, water level in tube-well, sand contents and timings of the measurements and shall be filled in accurately and precisely. If it seems that there is a mistake in measurement, the process shall be repeated. Proper records shall be kept for each tube-well for subsequent and future references

10.5.6 Operation of Pump & Motor

Power needs to be continuously available to pump during the tests. If power is interrupted, it shall be necessary to terminate the test, allow the well to recover up to initial water level and run a new test. Required pumping rate is to be maintained during the development of the tube-well has been satisfactorily completed and approved by the Engineer. The contractor shall disinfect the tube-well by chlorine solution throughout the entire depth of the well to obtain a minimum chlorine content of 50 parts per million. The procedure and equipment used to introduce and disperse the chlorine in the tube-well shall be approved by the Engineer

10.5.7 Disinfection

After development and testing of the tube well has been satisfactorily completed, and when approved by the Engineer, the Contractor shall disinfect the tube well by dispersing chlorine solution throughout the entire depth of the well to obtain a minimum chlorine content of 50 mg/l. The procedure and equipment used to introduce and disperse the chlorine in the tube well shall be subject to approval of the Engineer.

10.6 SEALING

Upon completion of disinfections of the tube-well, the contractor shall seal the tube-well by welding the 6mm (1/4") steel plate cap to the pump housing casing around its circumference. Compliance with these requirements will

not relieve contractor of his responsibility for safeguarding any complete part of the tube-well until the certificate of acceptance is issued for the entire tube-well installation

10.7 MEASUREMENT AND PAYMENT

10.7.1 Measurement

The quantity of MS housing pipe, blind pipe and screen of specified material and diameter shall be measured in linear metre or linear foot (whichever is included in Bill of Quantities) of actually installed at site on the basis of tentative quantities included in the Drawings.

The bail plugs, well caps and concentric reducers of specified diameter shall be measured in numbers, actually installed as per Drawings.

Grouting of space between inside of well drilled and outside of housing pipe shall be measured in linear metre or linear foot (whichever is included in Bill of Quantities) of actual executed quantity as per site.

The quantity of gravel shrouding shall be measured in cubic foot or cubic metre (whichever is included in Bill of Quantities) of actual executed quantity as per site.

The measurement for development and testing of tube well shall be measured in hours of testing and development to the satisfaction of the Engineer.

10.7.2 Payment

The accepted quantity MS housing pipe, blind pipe and screen of specified material and diameter, as above, shall be paid for at the contract unit rate which price and payment shall constitute full compensation for furnishing all materials, labour, equipment, tools and incidentals to complete these items including cost of centralizers (not payable separately).

The bail plug, well cap, concentric reducer of specified diameter/size, gravel shrouding and cement sand grouting, etc shall be paid at the contract unit rate and this price shall constitute full compensation for furnishing all materials, labour, equipment, etc. to complete this item to the satisfaction of the Engineer.

The payment for development and testing of tube well will be made at the contract unit rate which price and payment will be full compensation for all materials, labour, equipment, development, testing, disinfection, etc. as per the specifications and to the satisfaction of the Engineer.

SECTION-11 WATER TESTING

11.1 SCOPE OF WORK

The work covered under these specifications shall consist of collection, transportation, storage, and laboratory examination of water samples for the tube well that has been developed and tested. The water shall be tested for complete chemical and bacteriological examination in accordance with WHO (World Health Organisation) Guidelines 1985 or latest edition with the procedures established in the latest version of "standard Methods for Examination of Water and Wastewater" published by American Public Health Association. The examination of water samples shall be carried out in a laboratory approved by the Engineer.

11.2 COLLECTION OF WATER SAMPLES

The water samples shall be collected in separate sterilized containers for bacteriological (i.e., Total Coliform, and Faecal Coliform) and Physio-chemical examination. The samples shall be collected from a tap fitted on the discharge pipe of the pump. The tube well shall be operated at its design capacity for a minimum period of 15 minutes, before collecting the first sample.

11.2.1 Collection for Bacteriological examination

The volume of each sample intended for bacteriological examination shall not be less than 100 ml. Sterilized glass bottle provided with ground-glass stoppers shall be used for collecting samples. The sample bottle shall not be kept unopened until the moment, it is required for filling. During sampling, the stopper and neck of the bottle shall be handled to protect from hand contamination. The bottle shall be filled without rinsing and the stopper shall be replaced immediately after the bottle is filled.

11.2.2 Collection for Physio-Chemical Examination

The volume of each sample shall be at least 2 litres. The samples shall be collected in a chemically clean bottle, made of practically colourless glass and fitted with a ground-glass stopper. The bottle shall be rinsed at least three times with the water that is to be sampled before bottle is filled. While sampling, the bottle shall be held near its base.

11.3 TRANSPORTATION AND STORAGE OF SAMPLES

With the water samples intended for bacteriological examination, the laboratory procedures shall be started as soon as possible, preferably within one hour of collection. However, the time elapsing between collection and examination of samples shall in no case exceed 24 hours. During the elapsing between collection and examination, the temperature of samples shall be maintained as close as the time of sampling.

Water samples intended for physio-chemical examination, the samples shall be kept cool during transport and storage. The time elapsing between collection and examination shall in no case exceed 48 hours.

11.4 LABORATORY EXAMINATION

Following methods shall be used for determination of turbidity, colour, total dissolved solids, chlorides, total coliform and faecal coliform, in the water samples:

11.4.1 Turbidity

The turbidity shall be determined by Nephelometric method as described in the "Standard Methods". The turbidity of samples shall be measured and reported in Nephelometric Turbidity Unit (NTU).

11.4.2 Colour

The true colour of sample shall be determined by comparing it with Nesseler colour comparison tubes. The colour shall be determined and reported in colour units based on Platinum-Cobalt scale.

11.4.3 Total Dissolved Solids

The total dissolved solids shall be determined by Filtration-Evaporation method and expressed in mg/l.

11.4.4 Chlorides

Chlorides shall be determined by employing Mohr method, which uses silver nitrate as titrant and Potassium Chromate as the indicator. Chlorides shall be expressed and reported in units of mg/l.

11.4.5 Total Coliform and Faecal Coliform

Total coliform and faecal coliform concentrations shall be determined by employing Standard Methods. Dilution-Tube Technique shall be used. The results shall be reported in units of MPN/100 ml.

11.5 RECORD & DATA

A record shall be made of each sample by the Contractor and each bottle shall be identified including the information sufficient to identify the sample at some later date i.e. name of sample collector; date, hour, and location of sampling and water temperature. All records and data shall be kept by the Contractor on forms approved by the Engineer.

11.6 MEASUREMENT AND PAYMENT

11.6.1 Measurement

The measurement shall be made for each sample, tested in accordance the provisions of this section of the document and accepted by the Engineer.

11.6.2 Payment

Payment shall be made for each set of samples tested and measured as above, at the unit rate appearing in the Bill of Quantities. This price and payment will be full compensation for all steps required to complete the work.

SECTION-12 CONSTRUCTION OF PUMP HOUSE

12.1 SCOPE OF WORK

The work shall consist of construction of pump house complete as per Drawings and in accordance with these specifications and in close conformity with the lines, grades and dimensions shown on the Drawings or as established by the Engineer.

12.2 MATERIALS AND CONSTRUCTION REQUIREMENTS

Materials and construction requirements shall conform to the respective items included in the document.

12.3 MEASUREMENT AND PAYMENT

12.3.1 Measurement

Lump sum or item rate, whichever is included in Bill of Quantities, will be the basis for measurement for the item of various works involved for the completion of this item.

12.3.2 Payment

When the bill of quantities calls for a lump sum price, construction of pump house will be paid for at the contract unit rate which price and payment will be full compensation for all miscellaneous operations for all civil, electrification, lights, fans, complete as shown on the Drawings or established by the Engineer.

SECTION-13 ELECTRICAL & MISC. WORKS

13.1 SCOPE OF WORK

The work shall consist of furnishing all plant, labour, equipment, appliances, and materials and of performing all operations in connection with the electrical work and other works in strict accordance with this section of the specifications and the applicable Drawings, and subject to the terms and conditions of the contract.

13.2 ELECTRICAL WORKS

13.2.1 Regulation

All electrical installation work shall conform to the Electricity Act, 1910 and the Electricity Rules 1937, as adopted and modified by the Government of Pakistan from time to time and WAPDA Specifications; and the requirements specified herein. Except where otherwise shown or specified all electrical equipment shall be suitable for operation 230 volts, 50 cycles, alternating current power supply. All electrical materials shall be new. Defective equipment or equipment damaged during installing or testing shall be replaced or repaired by the Contractor at his own expense.

13.2.2 Coordination

The Drawings indicate the extent and the general location and arrangement of equipment, conduit and wiring. The Contractor shall study building plans and details so that the outlets and equipment will be properly located and readily accessible. Lighting fixture equipment and outlets shall be located to avoid interference with mechanical or structural features; otherwise, lighting fixtures shall be symmetrically located according to building arrangement. If any conflict occurs necessitating departure from the Drawings, details of departure and reasons therefore shall be submitted as soon as practicable for written approval of the Engineer.

13.2.3 Standard Products

Material and equipment used for this work shall be standard products from manufacturers regularly engaged in producing such equipment and shall be the manufacturer's latest standard design complying with specification requirements.

13.2.4 Material and Equipment Schedules

As soon as practicable and before starting installation of any material or equipment, the Contractor shall submit 6 copies of a complete list of materials and equipment proposed for installation to the Engineer for his approval. The list shall include manufacturer's names and materials or equipment identification such as styles, types, or catalogue numbers, to permit ready and complete identification.

13.2.5 Workmanship

All materials and equipment shall be installed in accordance with recommendations of the manufacturer subject to approval by the Engineer and in such a manner as to conform to the contract documents.

13.2.6 Grounding

All electrical equipment, including motors, meters, lighting and distribution panels, switchgear and similar items shall be grounded. All exposed non-current carrying metallic parts of electrical equipment, raceway systems and neutral conductor of the wiring system shall be grounded. Earth plates for the grounding system shall consist of copper plates of the minimum size of 609.6mm square and 3.175mm thick. The top earth plate shall be 2.44m below the ground level with critical watering arrangement or at the natural water level whichever is easy to install. A minimum 152.4mm layer of charcoal and rock salt shall be provided underneath each earth plate and a minimum 457.2mm layer of charcoal and rock salt shall be provided above each earth plate. The ground connection from the earth plate shall be securely bolted by a copper nut and bolt and additionally soldered to the plate. The ground connection including earth plate shall be kept clear of the structure foundation. The earth plate shall be located not nearer than 1.83m from the outer face of the building wall. Ground connections indicated as 3.18x25.4mm copper tape may be made with number 4/0 AWG or SWG cable. Ground connections indicated as 3.18mm by 12.7mm copper tape may be made with number 2/0 AWG or SWG cable. All ground connections shall run vertically and horizontally exposed on the surface of the wall and shall run concealed in the floor. Connections and splices shall be of the brazed, welded, bolted, or pressure connector type, except that pressure connectors or bolted connections shall be used for connections to removable equipment. Ground connection from the building to the earth plate shall be run at a depth not less two feet below ground level.

13.2.7 Conduit

Unless otherwise indicated, electrical wiring shall be run in galvanized steel (G.I.) conduit or PVC Pipe according to the specification PVC pipe shall not be used as conduit for buried or embedded run. Minimum size of raceways for branch circuit wiring shall be 19.1mm. Conduit pipes shall be exposed on walls and ceilings but shall run concealed in floors. Conduit shall be continuous when passing through wall or floor. Conduits installed on the surface of walls shall be supported and secured at intervals of not more than 0.91m and shall be installed parallel or perpendicular to walls, structural members or inter sections of vertical planes and ceilings. Field made bends and offsets shall in general be avoided, but if so required these shall be made with an approved method or by conduit bending machine. Changes in direction of runs shall be made with symmetrical bends or cast-iron fittings. Crushed or deformed raceways shall not be installed. Trapped raceways in damp and wet locations shall be avoided where possible. Care shall be

taken to prevent the lodgement of plaster, dirt or trash in raceways boxes, fittings, and equipment during the course of construction. Clogged raceways shall be entirely free of obstructions or shall be replaced. Raceways crossing expansion joints in concrete slabs shall be provided with suitable expansion fittings or other suitable means to compensate for expansion contraction. Raceways installed underground or under slabs shall be coated with an approved type of protective coating.

a. Galvanized Iron (GI) Conduits

The galvanized iron (GI) conduits shall have minimum wall thickness of 1.65mm (i.e., 16 SWG) and shall have the diameter indicated on the Drawings. Damaged portions of galvanizing at joints shall be cleaned and painted with a silver-coloured rust inhibitive paint. Conduit shall be cut and threaded in such a manner that there are no sharp edges. Conduit bends shall be uniform and shall have minimum radius of 5 times the diameter of the conduit or shall be made through pull or junction boxes.

b. PVC Pipe

PVC pipe and specials shall conform to British Standard Specification BS 3505:1962 "Unplasticized PVC pipe (Type 1420) for Cold Water Supply" and shall be class B. The entire conduit system shall be completed by cutting the PVC pipes and jointing and sealing to respective specials with P.V.C. solution as recommended by the PVC pipe manufacturers.

c. Additional Requirements for Exterior Conduit

All joints between sections of conduit, conduit and specials, and conduit and switches or lights shall be made water proof in an approved manner. Except where otherwise indicated, conduit shall be supported at least every 0.914m. Drainage fittings or seep holes shall be provided at unavoidable low points where moisture can collect. A maximum of two 90-degree bends will be allowed between boxes. Conduits shall be buried underground at minimum of 457.2m below finish grade. Bearing of conduit shall be uniform throughout its length in bottom of trench. Backfilling shall be in 101.6x152.4mm layers, compacted to 95 percent of maximum density.

13.2.8 Conductors

a. General

Conductors shall be new and shall be of polyvinyl chloride (PVC) insulated copper unless otherwise specified. Wire connector of insulating material or solderless pressure connectors properly taped shall be utilized for all splices where possible soldered mechanical joints insulated with tape shall be kept to a minimum. Vinyl plastic tape of suitable quality is acceptable in lieu of rubber and friction tapes. The entire conduit system shall be completed and

anchored prior to installing the wiring.

b. Conductor Sizes

Conductor sizes for tube-well motor main cables shall be as indicated in the Drawings. Control circuit conductors shall not be smaller than number 12 AWG except that for circuits of more than 30.48m from panel to load centre number 10 AWG shall be used.

c. Conductor Insulation

In normally dry locations, conductor number 8 AWG or larger shall have rubber or thermoplastic insulation of a heat resistant grade RH, RW, RHH or THW. Conductors smaller than number 8 AWG shall have a heat resistant rubber insulation type RH or RH RW or thermoplastic insulation, type T or TW.

13.2.9 Boxes and Supports

Boxes shall be provided wherever required for pulling of wires, making connections, and mounting devices or fixtures. Boxes for metallic raceways shall be of the cast iron hub type when located in normally wet locations. Boxes in other locations shall be sheet steel except that non-metallic boxes may be used with non-metallic conduit system. Steel boxes shall be fabricated of structural quality flat rolled minimum 18-gauge sheet of steel free from irregularities, mill scale and surface corrosion shall be neatly and accurately formed with corners squared and sides jointed by welding. Each box shall have the volume required for the number of conductors enclosed in the box. Boxes for mounting lighting fixtures shall be not less than 4 inches. Cast iron boxes installed in wet locations and boxes installed flush with the outside of exterior surfaces shall be gasketed. Boxes for use with raceway systems shall not be less than 38.1mm deep. Exterior pull boxes, junction boxes, boxes for exterior electrical supply points, switch boxes and all other boxes required for exterior electrical work shall be weather proof, heavy duty, galvanized steel.

13.2.10 Lamp Fixture and Accessories

All incandescent lighting fixtures shall be suitable for bayonet base lamps. All accessories such as straps, mounting plates, nipples or brackets shall be provided as required for proper installation. The exterior light points shall be provided with all fittings, accessories, metal clad switches, weatherproof light fixtures, holders, bulbs and covers.

13.2.11 Electrical Supply Points (Outlet Connections)

Electrical supply points shall be provided where indicated on the Drawings. Electrical supply points shall have the types of receptacles suitable for the plugs of the equipment to be connected to these points. Where receptacles are not available to match the plugs of equipment, standard receptacles

shall be used and plugs on equipment supply leads shall be replaced by the contractor with plugs to match standard receptacles. Each electrical supply point shall be complete with a switch. Exterior electrical supply points shall be provided where indicated. Exterior electrical supply points shall be weather proof, complete with switch and of the type suitable for the plugs of the equipment to be connected to these points.

13.2.12 Flexible Connections

Flexible connections of short lengths shall be provided for all motors and equipment. The flexible connections shall be water tight.

13.2.13 Fuse Circuits and Fuse Boxes

The Contractor shall provide proper fuse boxes for each circuit. The fuse boxes and the switches shall be metal clad and suitable for the load for which the circuit is designed. All fuse boxes shall be complete with proper size fuse strips fitted to fuse bridges.

13.2.14 Power Switchgear Assemblies

Power switchgear assemblies shall be metal enclosed and air circuit breaker type. The type and make of the circuit breaker shall be subject to approval of the Engineer.

13.2.15 Exterior Switches

Except where otherwise indicated exterior switches shall be of the push button weatherproof type.

13.2.16 Testing

Before any electrical system is put into service, the entire system installation shall satisfactorily pass the tests prescribed by the Electricity Department and the following tests. The Contractor shall furnish all instruments and personnel required for the tests, and the Employer will furnish the necessary electric power.

a. Insulation Resistance

The insulation resistance shall be measured by applying voltage between earth and the entire system of conductor or any section thereof, with all fuses in place and all switches on. A direct current voltage of not less than twice the working voltage shall be applied. The insulation resistance of the installation measured as above shall not be less than 25 megaohms divided by the number of points in the circuit. The metal conduit shall be tested for electrical resistance. The electrical resistance of such conduits measured between the main switch and each point shall not exceed 2 ohms.

b. Operating Test

After the wiring system has successfully passed by the insulation resistance test, and at such time as the Engineer may direct, the Contractor shall conduct an operating test for approval. The equipment shall be demonstrated to operate in accordance with the requirements of this specification. The test shall be performed in the presence of the Engineer.

c. Earth Plate Resistance

Resistance to each earth plate shall be tested by a standard earth tester, not sooner than 72 hours after a rain and without prewetting ground. The resistance of each earth plate shall not be more than 10 ohms. The test shall be performed by the contractor in the presence of the Engineer. Earth plates having a resistance of more than 10 ohms shall be replaced and retested. The Contractor shall submit in writing to the Engineer upon completion of the project, the measured ground resistance of each earth plate, indicating the location of the earth plate and the resistance and the soil conditions at the time, the measurements were made.

13.2.17 Repair

The work shall be carefully laid out in advance. Cutting, channelling, chasing or drilling of floors, walls, partitions, ceilings or other surfaces as necessary for the proper installation, support or anchorage of the conduit, raceways or other electrical work shall be carefully done. Damage to building surfaces, piping and equipment (including pointing work) shall be repaired to its original condition by skilled mechanics of the trades involved at no additional cost to the Employer.

13.3 POWER TRANSFORMER

13.3.1 General

The power transformer shall be indoor type, oil immersed, self-cooled, designed and built to give efficient and reliable service at their full rated capacity on the climatic conditions given in the general information of these specification. Transformer s built to the following standard will be acceptable.

- BS 171-1970 or any other relevant latest British Standard
- VDE 0532

13.3.2 Construction

The transformer tank shall be constructed of welded sheet steel plates and provided with external radiating tubes.

The transformer shall be fully tropicalized for temperature rise, humidity, altitude etc. The local conditions shall be taken into account while following the above standards. The transformer shall be complete with oil filling, all

accessories and attachments detailed in these specifications or otherwise required and the contractor shall provide all details, drawings, data and complete test results for final approval before installation. The tank and radiating tubes shall be designed to withstand, without developing any deformation, pressure at least 25% greater than the maximum operating pressure. The steel plate cover shall be bolted to the tank, using gasket for perfect oil seal. Two earth terminals shall be provided at the base of the tank.

The oil preservation system shall utilize on expansion the conservative tank fitted with silica gel breather and oil level indicator.

The transformer core shall be built of high-grade electrical steel laminations, each lamination insulated to reduce eddy current losses. The core laminations shall be clamped and bolted effectively to reduce 'humming'.

The winding core shall be of high-grade electrolytic copper conductor, flat or round paper insulated, thoroughly dried and impregnated as desired.

The high voltage leads shall be brought out and terminated to glazed porcelain insulator bushings for external connection.

The low voltage three lines and neutral leads shall be brought out and terminated to glazed porcelain insulator bushings for connection to L.V. side by copper bus bars or cables. The transformer neutral shall be earthed.

Off-load operated tap changer shall be provided on the tank cover. The tapping shall be -7.5%, ±5%, ±2.5%. A clear marking illustrated by diagram shall be provided to indicate the tap positions.

The transformer shall be provided with the following accessories.

- Oil filling valve for vacuum filling of oil;
- Oil drain plug;
- Bi-directional rollers fixed to the base steel channel, for rolling in the directions of both centre lines of the transformer;
- Lifting lugs, for handling and un-tanking the transformer; and
- Dial type thermometer for indicating oil temperature and having two hands, one showing existing oil temperature and other showing maximum oil temperature reached since the hand was last reset.

13.3.3 Drawings and Data

The manufacturer shall supply complete structural Drawings showing plan and elevations with complete dimensions and all relevant details of technical data of the offered transformer.

13.3.4 Transformer Technical Data

The technical data for Power Transformer shall be as included in Table 13.1.

Table 13.1, Technical Data for Power Transformer

Sr. No.	Parameter	Data
1	KVA rating	As shown on Drawings
2	No load ratio	11kv/415 V
3	H.V. Winding	
	Line to line volts	11000
	Connections	Delta
4	L.V. Winding	
	Line to line volts	415
	Connections	Star
5	Vector Group	DY 11
6	Tapping on H.V side	-7.5%, ±5%, ±2.5%
7	H.V Termination	Bushing
8	L.V cable size	7x300 mm2
9	L.V Termination	Bushing
10	Impedance voltage	4.5% to 6%
11	Losses in watts	
	Iron at no load	to be furnished by Bidder
	Copper at full load	to be furnished by Bidder
12	Cooling	On
13	Temperature rise over 50°C ambient	
	Oil	40°C
	Winding	50°C

13.4 MEASUREMENT AND PAYMENT

13.4.1 Measurement

The measurement of each item shall be as per provisions of the bill of quantities.

13.4.2 Payment

The items will be paid for at the contract unit price which price and payment shall be full compensation for furnishing, installing and commissioning all machinery and equipment for electrical works, chlorination equipment etc. complete in all respects as shown in the Drawings including all labour, tools, equipment and incidental to complete the work.

PART-D, SEWERAGE SYSTEM

SECTION-14 EARTH WORK FOR SEWERS

14.1 SCOPE OF WORK

The work shall consist of furnishing all materials, equipment and labour for excavation, trenching and backfilling for sewers, drainage facilities, structures and all other appurtenances of sewage collection system, in accordance with Drawings to proper line and grade and refilling the trenches and dressing them to proper surface.

14.2 CLEANING AND GRUBBING

The sites of all excavations shall be cleared of all shrubs, plants, bushes, large roots, rubbish and other surface materials. All such materials shall be removed and disposed of in a manner, satisfactory to the Engineer. All trees and shrubbery, that are designated by the Engineer, or his representative shall be adequately protected and preserved in an approved manner.

14.3 EXCAVATION

14.3.1 General

The Contractor shall do all excavation of whatever substance encountered to the depth shown on the Drawings or as otherwise specified. Excavation shall include without classification the removal and disposal of all materials of whatever nature that would interfere with the proper construction and completion of the work and shall include the furnishing, placing and maintenance of supports for the sides of the excavations. The work shall also include all pumping, ditching, dewatering and other measures required for the removal and exclusion of water. During excavation, material suitable for backfilling shall be stock-piled in an orderly manner at a sufficient distance from the bank of the excavation to avoid over-loading and to prevent sides from caving. Top soil should be stock-piled separately for subsequent reuse as necessary. All excavated material unsuitable or not required for backfilling shall be removed and disposed of at a location approved by the Engineer.

For contract purposes hereunder, the earth excavation work has been classified into two categories, earth excavation in trenches, and earth excavation for structures.

14.3.2 Earth Excavation in Trenches

Except as otherwise provided herein, excavation for a sewer line shall be open cut trenches with vertical side and not more than 200 feet of any trench in advance of the end of the built sewer shall be opened at any time and unless written permission to the Contractor is given by the Engineer. The trench shall be excavated to its full depth for a distance permitted for the sewer to be laid. Trenches for sewer-lines and appurtenances shall be to the lines and grades shown on the drawing or as ordered in writing by the

Engineer as necessary for the proper completion of the work. Bell holes and depressions for joints shall be dug after the trench bottom has been graded. The pipe except for joints shall rest on the prepared bottom for its full length. Bell holes and depressions shall be only of such length, depth and width as required for properly making the particular type of joint. Stones shall be removed to avoid point bearing.

Where the bottom of the excavation is in material which, in the judgment of the Engineer by reason of its hardness cannot be excavated to provide a uniform bearing for the pipe, said material shall be removed to minimum of 6" below the grade of the bottom of the pipe, and the trench backfilled to the required pipe sub grade with sand or other material acceptable to the required depth or with concrete Class-E, if so ordered. In no case material removed from such excavations shall be used as backfill material unless approved by the Engineer. All instructions shall be in writing by the Engineer.

14.3.3 Earth Excavation for Structures

All earth excavation under this Contract, which is not included under the classification of “Earth Excavation in Trenches " shall be classified and paid for as earth excavation for structures.

The Contractor shall provide adequate timbering or shoring for excavations. Should the sides and ends of any excavations give way the contractor shall, at no extra cost, remove all disturbed ground. Any excavation carried outside the limits shown on Drawings and specified herein as the payment limits, shall not be treated as excavation and shall not be paid for.

When foundation level is reached, the Engineer's Representative will inspect the exposed ground and give directions as to what further excavation, if any, he considers necessary. The excavation should be done in such a manner, as to ensure that the work rests on a solid and perfectly clean foundation. If the Contractor allows any portion of such foundations to deteriorate due to exposure, he shall make good the foundation to the satisfaction of the Engineer without extra cost.

14.4 ALIGNMENT AND GRADE

The sewers are to be laid to the alignment and gradient shown on the Drawings, but subject to such modifications as shall be ordered by the Engineer from time to time to meet the requirements of the work. No deviations from the lines, depths of cutting or gradients of the sewers shown on the Drawings and sections shall be permitted except by express directions in writing of the Engineer.

14.5 SETTING OUT SIGHT RAILS

The sewer shall be constructed and laid to a true grade and in straight lines between curves as shown on the plan. The sewer shall be laid and

constructed to their proper levels with the aid of suitable boning rods and sight rails which shall be fixed according to the requirements of the Engineer at intervals not exceeding 40 feet, and also by levelling along the invert with levelling instrument. The sight rails and boning rods shall be provided, fixed and maintained by the Contractor who shall also provide and maintain suitable levelling instruments and equipment and shall set the positions and levels of the sewers and other work according to the Drawings and any instructions which he may receive from the Engineer. All sight rails and posts shall be well seasoned deodar timber of ample size and strength. The rails and boning rods shall be suitably and accurately planned and no warped or otherwise defective or damaged sight rails or boning rods shall be used. Sight rails shall be secured to the posts by strong steel clamps to the approval of the Engineer and in such a manner that they shall be fixed as immovable, in relation to the correct lines and levels. All boning rods and sight rails shall have the centre line accurately marked thereon, by a fine saw cut and shall be painted black and white to the requirements of the Engineer. All boning rods shall suitably be shooed with iron. At least four separate sight rails shall always be maintained in correct level and alignment along the line of sewer at every place where construction work is proceeding and the alignment and level of the sight rails shall be checked by the level and line at least twice every day to ensure that no disturbance or interference of the alignment and level have taken place. Whenever required the Contractor shall erect and maintain such additional sight rails as the Engineer shall direct. The Contractor shall, at all times, see that his workmen or other unauthorized persons are not allowed, accidentally or otherwise, to tamper or interfere with sight rails or other alignment or level marks.

All bends and curves shall be set out mathematically in a manner to be approved by the Engineer and the Contractor shall provide and maintain for the purpose such additional sight rail posts and other wrought and rough timber work, steel wire and other articles as the Engineer shall require from time to time.

14.6 SHEETING AND BRACING

If ordinary open-cut excavation is not possible or advisable, sheeting and bracing shall be furnished and installed in excavations to prevent damage and delay to the work and to provide working conditions, which are safe. The Contractor shall furnish and place all shoring, sheeting, wall braces, timbers and similar items necessary for the safety of work, the general public and adjacent property. Sheeting, shoring and wall bracing shall be removed as the work progresses and, in such manner, as to prevent damage to the finished work and adjacent structures and property. As soon as it is withdrawn all voids left by the sheeting and bracing shall be carefully filled with selected material and compacted. The Contractor shall be fully responsible for the safety of the work in progress, for the finished work, the workmen, the public expenses, as part of the work under the excavation items and at no extra

cost.

14.7 DEWATERING OF TRENCHES

As part of the work under the excavation items and at no extra cost, the Contractor shall build all drains and do ditching, pumping, well-pointing, bailing and all other work necessary to keep the excavation clear of ground water, sewage and storm water during the progress of the work and until the finished work is safe from injury, the Contractor shall provide all necessary pumping equipment for the dewatering work, as well as operating personnel, maintenance, power etc. all at no extra cost. All water pumped or drained from the work shall be disposed of in a manner satisfactory to the Engineer. Necessary precautions against water flooding shall be taken.

14.8 MAINTENANCE OF EXCAVATIONS

All excavation made hereunder shall be properly maintained while these are open and exposed. The Contractor shall provide warning lights, signs and similar items sufficient suitable barricades. The Contractor shall be responsible for any personal injury or property damage due to his negligence.

14.9 PROTECTION OF EXISTING FACILITIES

The Contractor shall take special care of existing sub-surface facilities likely to be encountered during the excavation for their protection, such as sewers, drain pipes, water mains electric cables, communication cables and the foundations of adjacent structures. The Contractor shall be responsible for any damage to any such facility and shall repair the same at his expense whether or not the facility has been shown on the drawing.

14.10 DISPOSAL OF SURPLUS EXCAVATED MATERIAL

All surplus material excavated by the Contractor shall be disposed of at locations approved by the Engineer. The disposal of surplus material shall not interfere with other works and shall not damage or spoil other materials. When it is necessary to haul earth material over street or pavements, the Contractor shall prevent such material from falling on the streets or pavements.

14.11 BACKFILLING

14.11.1 General

After the completion of sewer line, drainage facilities foundations, walls and other structures below the elevation of the final grade all voids shall be backfilled with suitable materials specified below.

14.11.2 Backfilling for Structures

Backfilling operations for structures shall be performed as part of the Contractor's work under the payment items for earth excavation and at no extra cost. Backfill material for foundations, walls and other structures shall

consist of excavated soil, which is free from stones and hard clods not larger than 3 inch in any dimension, and also free from trash, lumber and other debris. Backfill material shall have enough moisture for proper compaction and shall be compacted in an approved manner to 90 percent of maximum density for cohesive soils and 95 percent of maximum density for cohesion less soils. Backfill shall not be placed against foundation walls earlier than 4 days after placing of concrete or brick masonry.

14.11.3 Backfilling for Trenches

After the sewers have been constructed and tested as specified and to the satisfaction of the Engineer, the trench shall be backfilled. Utmost care shall be taken in doing this so that no damage shall be caused to the sewer and other underground utilities. After this has been laid the trench and other excavation shall be backfilled carefully in 150mm layers with earth as approved by the Engineer, each layer being watered to assist in the compaction unless the Engineer shall otherwise direct.

14.12 MAXIMUM DENSITY DETERMINATION FOR COMPACTED SOIL

The maximum density of the soil shall be determined in accordance with the latest revision of "American Society for Testing Materials (ASTM) Standard D 1557 Density Relations of Soils, using 6.8 kg Rammer and 450mm Drop".

14.13 TESTING DENSITY OF SOIL

The Engineer will make tests using the calibrated sand cone method/core cutter method to determine the density of soil in place in accordance with ASTM Designation D 2558, latest revision. If soil in place fails to meet the specified degree of compaction the areas represented by the failing tests shall be re-excavated and compacted to the specified density in the manner directed by the Engineer at no extra cost.

14.14 TOP SOIL

Top soil, which has been stock-piled during excavation, shall be used for the top 150mm of backfill, in locations as ordered by the Engineer. Top soil shall be saturated with water and after it has dried, shall be spread to the required final grade and of required density. The work shall be performed at no extra cost.

14.15 PROXIMITY TO BUILDINGS

Where buildings in the opinion of the Engineer near excavation are likely to be affected, the Contractor shall provide shoring to protect such buildings in addition to timbering of trenches. The Contractor shall be required to leave timbering inside trenches if so required by the Engineer for protection of these buildings at no extra cost.

14.16 LENGTH OF TRENCHES IN ADVANCE OF CONSTRUCTION

Unless otherwise directed in writing by the Engineer of the work not more than 200 ft in advance of constructed or laid sewer shall be left open at any time.

14.17 DISPOSAL OF FILTH AND GARBAGE

No night-soil, filth and garbage met with during the excavation shall be allowed to be deposited on side of road/street so as to cause nuisance or obstruction to traffic. The same shall be disposed of by the Contractor to a place to the satisfaction of the Engineer.

14.18 DISPOSAL OF SURPLUS EARTH

The Contractor shall dispose of all surplus excavated materials not required to be used on the work. This shall include surplus earth after refilling and compaction.

14.19 TUNNELING

14.19.1 Formation of Soil

Tunnelling shall only be permitted in strong hard and homogenous, clay formations, which are not likely to collapse under normal working conditions. The work shall not be permitted in running sand. In weaker formations such as mixture of clay and sand, which are liable to collapse when exposed to atmosphere, the roof shall be protected by adequate timbering and shoring. If the tunnel is subject to any sort of traffic, it shall be provided with adequate timbering and shoring for its roof and walls.

14.19.2 Length of Tunnel

Normally the length of tunnel without adequate support shall not exceed 3 feet. This length shall, however, be exceeded under the directions of the Engineer, where depth of tunnel below ground level is considerable to avoid any danger of collapse. The tunnel, however, shall be driven in longer length up to 150 feet, if drive casing is provided as the tunnel is being excavated.

14.19.3 Horizontal Boring Machines

When considered necessary by the Engineer, horizontal boring machines shall be employed for crossing sewers underneath highways and canals. Whenever such machinery is used, drive casing of steel pipes shall be driven to avoid any collapse of the tunnel.

14.19.4 Backfilling of Tunnels

Backfilling of tunnels shall be done with clean river sand through bore holes duly lined with casing pipes, to be provided in the roof of the tunnel at suitable locations as per directions of the Engineer. The backfilling shall be made after the construction inside has been duly completed as per directions of Engineer.

14.20 MEASUREMENT AND PAYMENT

14.20.1 Measurement

The measurement shall be made for the actual quantity of the work done in cubic foot or cubic metre (whichever is included in Bill of Quantities). The maximum width of the trenches allowed for payment for various pipe sizes are included in the Drawings.

14.20.2 Payment

The unit rate tendered in the Bill of Quantities for excavation of trenches for sewer lines shall be considered as full compensation for the work specified in this section and shall include all excavation, backfilling, compacting, constructing and removing all temporary arrangements, pumping and dewatering disposal of surplus materials, removal of soft soil from bottom of trenches, removing the surface material and all incidentals to complete this work in all respects.

SECTION-15 REINFORCED CEMENT CONCRETE PIPE SEWERS

15.1 SCOPE OF WORK

The work shall consist of furnishing all pipes, plant, labour, equipment, appliances and materials and in performing all operations required for installing and testing the sewer pipes of reinforced cement concrete in strict accordance with the specifications of this section and the applicable drawing and subject to the terms and conditions of the contract.

15.2 REINFORCED CEMENT CONCRETE PIPES

15.2.1 General

All reinforced concrete pipes furnished and installed under this contract shall conform to ASTM C76 "Reinforced Concrete Culvert, Storm Drain and Sewer Pipe" and as per provisions of these technical specifications, using structural steel reinforcement. Sulphate Resistance Cement shall be used for sewers.

15.2.2 Classes of Pipe

The reinforced cement concrete pipes to be furnished and installed under this contract shall be of the strength classes shown on the Drawings and designated in Bill of Quantities of the Bidding Documents.

The strength classes shall be identified as one or more of the following:

- Class-I
- Class-II
- Class-III
- Class-IV
- Class-V

The design requirements for these five classes of reinforced cement concrete pipe shall be as described in ASTM C76-2003, or its latest version, Tables I through V for the respective strength classes. Unless otherwise called for in other parts of these Bidding Documents or applicable variation order, all reinforced cement concrete pipes under this contract shall comply with the Wall B design requirements as set forth in said Tables I through V of ASTM Designation ASTM C76-2003, or its latest version.

15.2.3 Basis of Acceptance

RCC pipes shall be used conforming to ASTM C76-2003, or its latest version, Class III, Wall "B" and acceptance of same shall be determined on the basis of following test results:

a. Concrete Compressive strength

i Compressive strength of concrete used for the fabrication of the RCC pipe shall be minimum 4000 psi;

ii Compression test determining concrete compression strength may be made on concrete cylinder compacted and cured as pipe; and

iii All type pertaining information for conducting the compressive test is given in the specification ASTM C76-2003, or its latest version, which should be followed.

b. Inspection

i Whether the required quantity or steel reinforcement is provided and placed for the fabrication of RCC pipe as required by the Specification; and

ii Manufactured pipe for visual defects and imperfection such as diameter, wall thickness, length of pipe and smoothness of the inner/outer surface of the pipe.

c. Three Edge Bearing Test

i The three-edge bearing test shall be conducted as required by ASTM C76-2003, or its latest version; and

ii Test load expressed in pounds-force per linear foot per foot of diameter to produce a 0.01-inch crack. The dead load to produce 0.01-inch crack as desired by the ASTM C76-2003, or its latest version shall be 1000 lbs force per linear foot per foot of diameter.

d. Crushing Load Test

i The crushing load test on the manufactured pipe shall be conducted in compliance with ASTM C76-2003, or its latest version; and

ii Test load as desired by the specification shall ne 1,500 lbs force per linear foot per foot of diameter.

e. Marking

The following information shall be marked on each pipe:

i Pipe class and specification designation;

ii Name or trade mark of the manufacturer; and

iii Identification of plants.

The Contractor shall bear the cost of such tests and pay fees etc., and also pay for the carriage of such samples and all other expenses contingent to tests. The manufacture of the pipes at the factory shall be watched and tested by the authorized representative of the Engineer.

15.2.4 Materials

All materials used in the manufacture of reinforced cement concrete pipes for use under this contract shall conform to ASTM C76-2003, or its latest version, and also with the following specifications:

a. Cement

The Portland cement which is required to be used in the manufacture of reinforced concrete pipes to be furnished and installed under this contract shall conform to the requirements of ASTM Designation C-150 latest revision.

b. Aggregate

The course/fine aggregate to be used in the manufacture of concrete pipes to be furnished and installed under this contract shall be generally in accordance with the provisions of section of these specifications.

c. Steel Reinforcement

The material will conform to the specifications contained in relevant Section of these specifications.

15.2.5 Mixing of Concrete

The proper types and amounts of Portland cement, mineral aggregates and water shall be thoroughly mixed in an approved type of mechanical batch mixer which shall be kept in first class condition. Admixtures in the concrete will not be permitted.

15.2.6 Pipe Dimensions

The internal diameters and wall thickness of reinforced concrete pipes under this contract shall be as set forth in ASTM C76-2003, or its latest version, in Tables I through V for “Wall B" pipe as required and shown on the Drawings.

The lengths of reinforced concrete pipes under this contract shall be as required to provide the designated laying length shall be in full, and shall not be less than 6 feet, nor more than 8 feet, unless otherwise approved in writing by the Engineer. Only one laying length shall be permitted for each size of reinforced concrete pipe under this contract and pipes not of the approved uniform laying length shall not be used in the work.

15.2.7 Lift Holes not permitted

Lift holes in the walls of reinforced cement concrete pipes will not be permitted under this contract for the purpose of handling and laying. Other approved lifting methods shall be employed.

15.3 CERTIFIED PLANS AND DATA SHEETS

The Contractor shall submit in triplicate, for approval by the Engineer, certified plans and data sheets as required to provide complete information on all concrete sewer pipes, dimensions, type and dimensions of pipe ends, joint details, proposed concrete design mix for each different strength class of reinforced or non-reinforced concrete pipe and any other information needed to demonstrate full compliance with these specifications.

No concrete sewer pipe shall be delivered to the work site until the Engineer has formally approved the plans and data sheets and until all test requirements called for in the respective ASTM Standard Specifications ASTM C76-2003, or its latest version, and C-14 have been met.

15.4 JOINTS FOR CONCRETE PIPE SEWERS

15.4.1 General

Joints for concrete sewer pipes of more than 150mm diameter shall be Rubber Gasket joints as provided in the Drawings. No other types of joints will be permitted under this contract. For pipes of 150mm internal diameters collar joints will be used.

15.4.2 Rubber Gasket Joints

Rubber gasket joints shall be used for either tongue and groove or bell & spigot pipes.

Rubber gasket joints shall be made using specially designed rubber gaskets, made to fit the applicable tongue and groove or bell and spigot pipes and adequately tested under operating conditions. Special care must be taken in the selection and handling of the concrete pipes for use with rubber gasket joints, to ensure that pipe ends shall be smooth and concentric with tolerance which closely conforms to the requirements of the manufacturer of the rubber gaskets. The tongue or spigot end of each pipe shall be specially designed to perform groove or offsets to fit the manufacturer's rubber gasket design.

The rubber gasket joints shall conform to all applicable requirements of the latest revision of ASTM Designation C-443, entitled "Joints for Circular Concrete Sewer and Culvert Pipe, using Flexible Watertight Rubber Type Gaskets", except that the test pressure need not exceed 10 feet of head at which the completed sewers shall meet the infiltration or exfiltration limits set forth hereinafter.

The groove end of tongue and groove pipes of either the reinforced or non-reinforced concrete type, shall have at least one line of wire reinforcing of 8-gauge size placed in the centre of the groove.

The rubber gasket shall be installed on the pipe in accordance with the instructions of the gasket manufacturer. In general, the gaskets shall be pre-assembled to the pipe at the pipe manufacturing plant. The pipes shall be handled with special care at all times to prevent damage to the pipe ends. A lubricant shall be used for jointing the pipes as recommended by the rubber gasket manufacturer. Care shall be taken to avoid contamination of the gasket and lubricated surfaces with earth or other undesirable material during installation.

For either tongue and groove or bell and spigot pipes, mechanical means shall be used to pull the pipe home for all sizes of 12-inch or larger diameter in accordance with the recommendations of the rubber gasket manufacture. Pipes of 9 inch or smaller diameter may be coupled manually using a cross member and bar. Under no circumstances will bars alone be used nor shall any motor driven equipment be used to force the pipe home.

15.5 INSTALLATION OF CONCRETE PIPE SEWERS

15.5.1 Handling of Pipes

Concrete sewer pipes shall be handled with special care at all times during the manufacture, while transporting to the site of work, and while installing. Each pipe shall be carefully inspected before being laid and no cracked, broken or defective pipe shall be used in the work. Chipping of the tongue and groove or bell and spigot pipe ends, which in the Engineer's opinion may cause defective joints, shall be sufficient cause for the rejection of any concrete pipe.

15.5.2 Excavation and Backfill

The excavation and backfill for sewer installations shall be as specified in applicable provisions of these technical specifications and will be paid for under separate contract items as classified.

15.5.3 Trench Bedding

Wherever called for on the Drawings or where ordered in writing by the Engineer, the Contractor shall furnish and place bedding, and/or concrete encasement for the concrete pipe sewers under this contract. The bedding shall be as specified in applicable provisions of these technical specifications and will be paid for under separate contract item as classified, described and listed in the Bill of Quantities or and as called for in applicable variation order.

The concrete encasement shall be placed in accordance with the details and notations on the Drawings or as ordered in writing. Concrete work shall be as specified in applicable provisions of Item of these technical specifications and will be paid for under separate contract items as classified, described and listed in the Bill of Quantities or as called for in applicable variation orders.

15.5.4 Laying of Sewers

Neither any sewer pipe nor the bedding shall be laid or placed till the alignment of the sewer and its levels nor have gradients been carefully checked and tested with the trench excavation and found correct.

Each length of sewer pipe shall be checked for cracks and defects before placing in the line. Defects which in the opinion of the Engineer indicate imperfect placing, shall make the pipe liable to rejection. Each pipe shall be placed carefully to line and grade and in close contact with adjoining pipe. These specifications require rejection of the work if the sewer invert varies as much as 12mm from the proper elevation. As shown on Drawings, the bottom of the trench must be shaped to fit the pipe barrel, with holes left for the bells. If excavation has been carried below the correct grade, refilling must be done with satisfactory materials as approved by the Engineer at no extra cost.

The concrete pipe joints shall be of the types designated above and shall be made in accordance with the aforesaid specifications.

When laying is not in progress, the open pipe shall be closed with a tapered wooden plug to keep out foreign matter.

15.5.5 Pavement Restoration

The contractor shall restore paved surfaces which have been cut under this contract, as part of the work under the excavation items and at no extra cost to the Owner.

15.6 TESTS FOR INFILTRATION OR EXFILTRATION

15.6.1 General

All pipes built under this contract shall be tested for infiltration or exfiltration as specified below. The Contractor shall furnish labour, materials and equipment required for making the tests with no extra compensation over and above the agreed contract price for the sewers. The tests shall be made at times selected or approved by the Engineer. Sections of the completed sewer shall be isolated and measurements of the infiltration or exfiltration shall be made by approved methods.

15.6.2 Infiltration Tests

The sewers which are constructed with the ground water level above the crown of the pipe shall be tested for infiltration after the sewers have been installed and backfilling has been substantially completed. The tests and measurement shall be performed by the Contractor in the presence of and in a manner approved by the Engineer. The duration of the tests shall be only long enough to establish the true rate of infiltration. The amount of leakage over a 24 hours period will then be calculated from the result of the measured true rate of infiltration.

15.6.3 Exfiltration Tests

The sewers which are constructed with the ground water level below the crown of the pipe shall be tested for exfiltration by isolating a section of sewers between manholes by means of approved temporary type of water tight bulk heads. The method of testing for exfiltration shall be generally as follows:

a. After isolation of sewer section, it shall be filled with water to a level which is 1m above the crown of the sewer at the higher end of the isolated section under test. The level will not be more than 6 feet above the crown of the sewer pipe at its lower end.

b. The duration of the exfiltration test shall be one hour after the filling with water has been completed.

c. Determination of the amount of exfiltration shall be made by measuring the total loss of volume of water in the manholes.

d. The amount of exfiltration over a 24 hours period will then be calculated from the measured loss of volume during the test observation period.

15.6.4 Allowable Infiltration or Exfiltration

The calculated amount of infiltration or exfiltration over a 24 hours period shall not exceed 75 litre per mm of pipe diameter per km of sewer, which rate shall be applied to the actual sewer size and length tested to determine the allowable infiltration or exfiltration over the 24 hours period.

If the measured infiltration or exfiltration exceeds the specified allowable limit, then the Contractor shall locate the points of leakage and make necessary repairs so as to reduce the leakage to less than permissible maximum stated above.

15.7 MEASUREMENT AND PAYMENT

15.7.1 Measurement

Measurement for reinforced cement concrete pipes shall be made for the actual quantity of the work done in linear metre or linear feet (whichever is included in Bill of Quantities) of different sizes and strength installed tested and approved as authorized for payment under the Contract. The measurement will be made along the centre line of the pipe and between the inside walls of manholes or junction chambers.

15.7.2 Payment

The unit rate quoted in the Bill of Quantities for supplying, laying and jointing cement concrete sewer pipes, will be considered full compensation for the cost of pipes, charges for their carriage to site and testing before and after laying, labour charges for laying, jointing, etc. and cost of all incidentals for

completion of this item of work as per specifications laid down in this section. Payment for this item of work shall be made at the unit rate(s) quoted in the Bill of Quantities for various internal diameters of pipes.

SECTION-16 CONSTRUCTION OF MANHOLES

16.1 SCOPE OF WORK

The work consists of constructing manholes (including connection chamber) for sewerage at positions shown on the Drawings or where otherwise directed by the Engineer, and in accordance with the detailed Drawings supplied from time to time, complete in all respects.

16.2 MATERIALS

Brick masonry, Portland cement concrete, and other materials shall meet the specified requirements of the relevant sections of the specifications.

Manhole steps shall be of malleable iron conforming to BS 1247.

16.3 CONSTRUCTION REQUIREMENTS

Manholes shall be constructed with brick masonry of specified wall thickness laid in specified cement sand mortar, built on concrete slab. The cover shall be 1:2:4 reinforced cement concrete, fitted with Mild Steel angle frame which shall have reinforced cement concrete cover as shown in the Drawings. The outside of the walls shall be plastered with specified cement sand mortar, painted with two coats of bitumen. At the bottom of manholes for sewers, a proper channel as per Drawings, shall be constructed in the whole length of the manhole along with centre line of the sewers, to lead the sewage from one sewer to the other.

Malleable iron steps shall be installed inside the manhole, during the construction of the manhole walls. Cutting holes into the wall for the steps after construction will not be permitted. Top rung shall be 18" below the manhole cover and the lowest not more than 12" above the benching (floor).

16.4 MEASUREMENT AND PAYMENT

16.4.1 Measurement

Measurement shall be made for the actual number of manholes of the appropriate type constructed at site as per Drawings and specifications laid down in this section and to the approval of the Engineer. The depth / height of manhole for the purposes of measurement and payment shall be difference of level between the top of manhole (top of cover) and invert level of manhole.

16.4.2 Payment

The unit rate quoted in the Bill of Quantities for the construction of manhole shall be considered full compensation to cover the cost of all materials including form work for concrete, excavations, brick masonry, steps, frame and concrete cover, and connecting pipe with the manhole, and all labour

including curing, plastering, benching and bitumen painting etc. and all incidentals to completely construct them at site as per Drawings and specifications laid down in this section.

Payment shall be made for the actual number of manholes constructed and counted as above, at the appropriate rate quoted in the Bill of Quantities.

SECTION-17 PIPE BEDDING

17.1 SCOPE OF WORK

Wherever specifically called for by means of notes on the contract Drawings or by written order of the Engineer, the Contractor shall furnish and place sand or gravel/crushed stone bedding under sewer lines, drain pipes and other structures as a separate item of payment.

17.2 SOURCE OF BEDDING MATERIAL

Sand and gravel/crushed stone bedding material shall be from a source and of specifications approved by the Engineer.

17.3 PURITY AND STACKING

The sand and gravel/crushed stone shall be free from clay, salt, alkali, organic matter, shale, loam, soft flaky particles and other deleterious substances. It shall be stacked at the place designated by the Engineer and kept free from the admixture of deleterious materials mentioned herein. The sand shall have clay/silt contents not more than 5%.

17.4 PLACING OF BEDDING MATERIAL

The material for bedding shall be placed to the specified thickness and compacted by rammers of approved weight.

17.5 MEASUREMENT AND PAYMENT

17.5.1 Measurement

The measurement shall be made by volume for the actual quantity of the work done and the unit of measurement shall be cubic foot or cubic metre (whichever is included in Bill of Quantities).

17.5.2 Payment

Payment for this item of work shall be made for the actual quantity of work done as specified in this section, at the unit rate quoted in the Bill of Quantities.

PART-E, CIVIL WORKS

SECTION-18 EXCAVATION, BACKFILLING & DISPOSAL

18.1 SCOPE OF WORK

The work under this section consists of excavating, in all types of soil, lifting, transportation and disposal of the excavated material, back-fill and fill for building foundations, and under floors including all incidental work necessary for excavation to the required depth and dimensions and in accordance with the Drawings or as directed. The work shall be carried out in complete conformity with the specifications set-forth hereunder.

18.2 AUTHORIZED OUTLINES

Unless otherwise specified or directed in writing, all earthwork, i.e., excavation of trenches, pits, etc. for foundations, filling under floors, etc. shall be executed to the widths, depths, lengths, alignments grades and levels shown on the Drawings. If they are not indicated on the Drawings then the Contractor shall prepare the drawing showing the existing ground levels and the actual grades and levels of excavation for obtaining necessary approval from Engineer before excavating the ground.

Similarly, for all backfill and fill works the Contractor shall prepare drawings showing the existing ground levels and the actual finished level to ascertain the volume of fill for obtaining approval before the commencement of work.

18.3 CONSTRUCTION REQUIREMENTS

18.3.1 Excavation

a. General

All excavation, in any kind of soil encountered, shall be performed to the depths and widths indicated or as otherwise specified by the Engineer. During excavation, material suitable for backfilling shall be stockpiled in an orderly manner at a sufficient distance from the banks of the excavation to avoid overloading and to prevent sides from caving. Topsoil shall be stockpiled separately, for subsequent re-use as necessary. All excavated material unsuitable or not required for backfilling shall be removed and collected at a location approved by the Engineer.

It is anticipated that all excavation work under this Contract, will be earth excavation. The term “earth” as used herein shall include all materials which do not in the opinion of the Engineer, require blasting, barring or wedging of material for removal from its original bed.

Unless otherwise indicated or approved by the Engineer, excavation shall be open cut.

b. Timbering or Sheeting

The Contractor shall provide adequate timbering or sheeting for excavation where necessary, as part of the excavation work, to hold up the sides and ends of all excavations. Should the sides and ends of any excavation give away, the Contractor shall, at no extra cost to the Employer reinstate all disturbed ground.

If ordinary open-cut excavation is not possible or advisable, sheeting and bracing shall be furnished and installed in excavations generally in accordance with the details shown on Drawings to provide safe working conditions. The Contractor shall furnish and place all sheeting walls, braces, timbers, and similar items, necessary for the safety of the work, the general public and adjacent property. Sheeting and bracing shall be removed, as the work progresses in such manner as to prevent damage to finished work and adjacent structures and property. As soon as it is withdrawn, all voids left by the sheeting and bracing shall be carefully filled with selected material and compacted. The Contractor shall be fully responsible for the safety of work in progress, for the finished work, the workmen, the public and adjacent property. All sheeting and bracing shall be at the Contractor's expense, as part of the work under the excavation items and at no extra cost to the Employer.

The Engineer may order, in writing, any or all shoring, sheeting and piling to be left in place for safety reasons, whether such sheeting is shown on Drawings or not. If left in place, such sheeting shall be cut of at the elevation approved by the Engineer, and shall be paid separately.

c. Inspection of Foundations

When excavation up to foundation level is reached, as per Drawings, it is inspected by the Engineer and approved before start of any permanent construction. If safe foundation could not be obtained at the depth shown on the Drawings or at maximum depth of five feet below the ground level, the work shall be carried out as directed by the Engineer. Additional cost, if any approved by the Engineer, shall be paid in accordance with the provisions of the Conditions of Contract.

d. Disposal of Unsuitable/Surplus Materials

The unsuitable /surplus earth shall not be heaped within 5-feet of the top edge of any foundation. All surplus material excavated by the Contractor shall be disposed of at locations approved by the Engineer. The method of disposal shall not interfere with other works and shall not damage or spoil other materials. When it is necessary to haul earth material over streets or pavements, the Contractor shall prevent such material from falling on the

streets or pavements. The surplus material shall be disposed-of within the site without any additional cost.

e. Excavation to be kept Free of Water

All excavations shall be kept free from water from whatever source it may come, at all times, except where otherwise specified or permitted in writing by the Engineer.

As part of the works, under the excavation items, and at no extra cost to the Employer, the Contractor shall build all drains and do ditching, pumping, well pointing, bailing and other work necessary to keep the excavation clear of ground, sewage or storm water during the progress of the work and until the finished work is safe from injury. The Contractor shall provide all necessary pumping equipment for the dewatering works as well as operating personnel, maintenance, power etc. all at no extra cost to the Employer. All water pumped or drained from the work shall be disposed of in a manner satisfactory to the Engineer. Necessary precautions against flooding shall be taken.

f. Safety Measures

All excavations shall be properly maintained while they are open and exposed. Sufficient suitable barricades, warning lights, signs and similar items shall be provided by the Contractor. The Contractor shall be responsible for any personnel injury or property damage due to his negligence.

The Contractor shall take special precautionary and protective measures with existing subsurface facilities likely to be encountered during the execution of works such as sewers, drain pipes, water mains, conduits, electric cables, communication cables, foundations of adjacent structures etc. As part of the works, the Contractor shall shore up all buildings, walls, poles and other structures, the stability of which is liable to be endangered by the execution of the works. The Contractor shall be responsible for damage to any such facility and shall repair the same at his expense whether or not this facility has been shown on the Drawings.

g. Excess Excavation

In the event of any excavation being carried out wider or deeper than shown on the Drawings, it shall be filled in by the Contractor at his own expense to meet the required dimension and levels with concrete or any other material approved for such purpose.

The bottom and side slopes of excavation upon or against which structures or other required constructions are to be placed shall be finished accurately to the required grades and dimensions and, if required, shall be moistened

with water and tamped or rolled with suitable tools or equipment for the purpose of forming firm foundation. Whenever the natural foundation material is disturbed or loosened or excavated beyond the approved lines and grades the loose material shall be removed and the extra excavation made good at Contractor's expense with selected materials which shall be thoroughly compacted by tamping rolling in layers not exceeding 6-inch.

h. Classification of Material

No classification will be made for payment purposes of any material excavated as to its class, nature, origin or condition, unless an unusual obstruction or embedded matter or substance is encountered. If this occurs, it shall be submitted by the Contractor for evaluation of design and working out of a necessary treatment. New items shall be mutually agreed.

i. Transportation of Materials

All carts, trucks or other vehicles used by the Contractor for transportation of the material shall be suitably constructed or lined out to permit any leakage of soil while the vehicles are on the move. These would be so loaded and arranged as not to spill on the site and public roads. Whenever any vehicle so used is found leaking and unsuitable it shall be immediately withdrawn from the work.

j. Termite Control

The approved foundation trenches shall be treated with the termite control solution as provided in SECTION-19.

18.3.2 Compacted Backfill

a. Excavated Earth for Backfilling

All fill or refill around structures, i.e., within the slopes and limits of the established lines for excavation for the structures and below the natural surface level, shall be defined as "Back Filling".

Backfilling operations for structure shall be performed as part of Contractor's work under the payment items for earth excavation, and at no extra cost to the Employer. It comprises returning, transportation and filling the selected excavated material around foundations, and at back of walls etc., up to finished levels shown on the Drawings or as required in layers not exceeding 6 inches carefully rammed and consolidated (with addition of water if required) so as to achieve a maximum density of 90%. The backfilling earth shall be free from stones and hard clods, larger than 3 inches in any dimension and also free from trash, lumber and other debris.

No backfilling shall be made until the concrete foundations and footings etc.

have been inspected and approved. Earth to be used for filling must be free of all the organic impurities, debris or any other foreign matter. Earth which contains more than 1% of salts, particularly sulphates, will not be used in filling.

Testing shall be performed using the calibrated sand cone method to determine the density of soil in place. If soil in place fails to meet the specified degree of compaction it shall be removed, replaced with approved material and compacted to the specified density in the manner directed by the Engineer, in the areas represented by the failing tests at no additional cost to the Employer.

b. Borrow Earth for Backfilling

In case of non-sufficiency of excavated material and unsuitability of earth for back-filling, appropriate material conforming to these specifications shall be brought by the Contractor.

Where satisfactory materials for backfill are not available in sufficient quantity from required excavation, "Earth Borrow" shall be obtained from suitable sources at the Contractor's responsibility as a separate payment item. The necessary clearing and grubbing of borrow areas, disposal and burning of debris there from the developing of sources including any access roads for hauling and the necessary right-of-way, and the satisfactory drainage of the borrow areas, shall be considered as incidental items to borrow excavation. "Earth Borrow" under this separate payment item shall be furnished and placed by the Contractor only where specifically called for by the Engineer.

Filling shall be approved selected material from excavated or other predominantly granular material, free from slurry and organic or other unsuitable matter and capable of compaction by ordinary means

c. Sand Backfill

Special sand backfill is to be provided when specifically required by the Drawings or when ordered in writing by the Engineer. This work shall consist of removal of the excavated material to waste and provision in lieu of graded clean and fill, free of all foreign matter, such that 100% passes a ¾" screen with not more than 5% passing a No.4 sieve. This shall be compacted to 95% of the maximum density as determined by AASHTO T 180, Method D.

18.3.3 Filling Under Floors

18.3.4 Earth Filling

All fill or refill (from the excavated earth at site) about structures, i.e., above the natural surface level shall be defined as "filling under floors or embankment from excavated earth".

After the masonry has been laid up to the plinth level and the Damp

Concrete Proof Course, if required is laid the space between the walls shall be cleared of debris and loose earth shall be laid in layers of 6-innch and each layer watered and compacted until the filling is completed up to the base level of the floor as shown on the Drawings. Only sandy soil free from salt peter either from the materials excavated from the foundations if such materials is suitable and sufficient or suitable material brought from outside shall be used.

18.3.5 Sand Filling

All fill or refill, from the material provided and brought from outside the site (any lead), about structures, i.e., above the natural surface level shall be defined as "filling under floors with earth provided and brought from outside".

Unless otherwise specified the base of all ground floors shall be constructed through sand filling, done in layers not more than 4-inch thick and shall be rammed after saturation to such an extent that 4-inch layer is reduced to about 2.7" after compaction.

The required in situ density with respect to maximum density to optimum moisture content shall be in compliance with test 12 of B.S. 1377-1967.

Sand shall conform in all respect to the specifications for fine aggregate except for its grading, i.e., it shall pass through a sieve No. 16 and not more than 30% shall pass through a sieve No. 100.

18.4 MEASUREMENT AND PAYMENT

18.4.1 Measurement

The measurement shall be made in cubic feet or cubic metre (whichever is included in Bill of Quantities) of earth acceptably excavated and backfilled for trenches and structures within the lines and grades shown on the drawing or as directed by the Engineer duly compacted as required. The measurement of dewatering in trenches or structures shall be not be made and cost of this item shall be deemed included in the cost of excavation, backfilling and compaction.

Any excavation carried beyond the limits shown on the Drawings and specified herein as the payment limits, shall be treated as excess excavation and shall not be measured for payment.

18.4.2 Payment

Payment for this item of work shall be made for the actual quantity of work done as specified in this section, at the unit rate quoted in the Bill of Quantities.

Filling under floors from excavated earth or borrowed sand shall be measured and paid separates as per respected items included in the Bill of Quantities

SECTION-19 TERMITE CONTROL

19.1 SCOPE OF WORK

The work for anti-termite treatment includes injection of insecticide in sides and bottom of foundations or elsewhere as directed by the Engineer. The scope also covers treatment of all woodworks if any, with insecticides before installation in position. The contractor shall furnish all materials, labour and equipment to carry-out the termite treatment complete in all respects.

19.2 APPLICABLE STANDARDS

All methods of termite protection used herein shall be in accordance with the standard practice of National Pest Control Association, USA and the British Wood Preserving Association.

19.3 SUBMITTALS

Contractor shall prepare and submit, for the approval of Engineer, the following:

a. Qualification data of manufacturer;

b. Product data for termiticide to be used;

c. Detailed method statement describing the methodology maintained in applying termite control treatment;

d. After application of termiticide is completed, submit report for Employer's record and information, with minimum following information:

- Date and time of application.
- Moisture content of soil before application.
- Brand name and manufacturer of termiticide.
- Quantity of undiluted termiticide used.
- Dilutions, methods, volumes, and rates of application used.
- Areas of application.
- Water source for application.

6. Special warranty specified in this Section that will be submitted by manufacturer at date of Substantial Completion.

19.4 MATERIAL

An emulsible concentrate insecticide specially formulated to prevent infestation by termites shall be used. Fuel oil will be permitted as a diluent. A working solution of one of the following chemicals with clean potable water with ratio specified by the manufacturer shall be used.

- Imidacloprid 5.0%, Chloronicotinyl, Formulation SL/SC with clean water in maximum ratio of 1:120.

- Fipronil 2.5%, Formulation EC (Emulsified Concentrate) with clean water in maximum ratio of 1:250.

Insecticide shall be obtained from the Sole distributor, in sealed drums in quantity necessary for the requirement of works.

All mixing shall be done at site and mixing proportion of insecticide with water shall be verified by the Engineer.

Pure turpentine shall be used for dilution of insecticide, in approved proportion for application to woodwork where such application is required

19.5 QUALITY ASSURANCE

19.5.1 Manufacturer's Instructions

In addition to the requirements of these specifications, the manufacturer's instructions and recommendations for the work, including preparation of sub-strata and application shall be complied with.

19.5.2 Application

A professional operator shall be engaged who shall have license in accordance with regulation of governing authority for application of soil treatment solution.

19.5.3 Guarantee

The Contractor is to guarantee that the building shall be free from termites (white ants), wood bores and other pests, which cause damage to wood or other organic material for 10 years from the date of Substantial Completion.

In the event of any damage caused within the guaranteed period, the Contractor shall replace at his own cost such damaged material, finishes affected and suitably preserve and treat the entire premises with the best method known to the trade to prevent the spreading of termites.

19.6 METHOD OF APPLICATION

a. All mixing will be done at site and mixing proportion of insecticide with water shall be verified by the Engineer.

a. Insecticide solution shall be applied with approved spraying equipment maintaining a pressure of 150 psi to all applications to, on or in earth.

b. Soil treatment shall begin after all work of preparation of earth prior to laying of concrete. After application, no additional earth moving or work upon subgrade shall be done. No covering of earth of concrete shall be applied over soil treatment until at least 24 hours after treatment.

c. Insecticide solution shall not be applied during wet weather, or when the earth surface is excessively wet. Application shall be made to all areas/beneath concrete slab-on-grade, including sidewalks and

paving abutting building for the distance of at least 6.5 ft beyond building line. Solution shall be applied on amounts of not less than 0.5 litres per sq.ft. of area. If applied over gravel or sand fill, application shall not less than 0.7 litre per sq.ft. of areas. Insecticide shall penetrate to a depth of 1-inch minimum in porous earth at bottom and 2 inches to 3 inches at side of excavations.

d. Sides of foundation excavations and similar areas shall be treated with solution at a minimum rate of 0.5 litres per sq.ft. upon inner sides of such excavation and at all locations where concrete slabs for platforms and similar work about the building.

e. In the area of application sign shall be fixed to show that soil treatment has been applied. Such sign shall be removed when area is covered by other construction.

f. Care shall be exercised to ensure that no marks or damage occurs to the finished structure as a result of the work under this section.

g. All woodwork for the entire project is to be insecticide treated (before application of solignum) in the case of material to receive before treatments, insecticide shall be sprayed on all surfaces of all the wooden work viz, door frames, blocking, furring, planks, boards etc. before installation. Spraying shall be necessary after field sawing, jointing or installation of such material.

19.7 MEASUREMENT AND PAYMENT

19.7.1 Measurement

Measurement of acceptably completed works of termite control treatment will be made on basis of number of square feet or square metre (whichever is included in Bill of Quantities) area to be termite proofed as per instructions of the Engineer.

19.7.2 Payment

The payment will be made on the basis of measurement made as above and at the unit rate quoted in the Bill of Quantities and shall constitute full compensation for all the works related to the item.

No separate measurement and payment shall be made for termite control treatment on wood works and turpentine/water required for mixing insecticide solution.

SECTION-20 PLAIN & REINFORCED CONCRETE

20.1 SCOPE OF WORK

The work under this section of the specification consists of furnishing all plant, labour, equipment, appliances and materials and in performing all operations in connection with the supply, manufacturers, transporting, placing, consolidating and curing of plain & reinforced concrete and its constituents. Reinforcing steel does not form part of this section and is described in SECTION-21.

20.2 APPLICABLE STANDARDS

The work shall conform to requirements of latest editions of following standards, wherever applicable, unless otherwise specified.

20.2.1 Pakistan Standards

- PS 232, Portland cement (ordinary & rapid hardening)
- PS 243, Natural aggregates for concrete
- PS 279, Abrasion of coarse aggregates by the use of Los Angeles machine
- PS 280, Determination of aggregates crushing value
- PS 281, Organic impurities in sand for concrete aggregate
- PS 282, Material finer than No. 200 PS test sieve in aggregates
- PS 283, Soundness test for aggregates by the use of sodium sulphate or magnesium sulphate
- PS 284, Sampling aggregates for concrete
- PS 285, Sieve or screen analysis of fine and coarse
- PS 286, Description and classification of mineral aggregates
- PS 421, Sampling fresh concrete
- PS 422, Slump test for concrete
- PS 560, Making and curing concrete compression test specimen in the field
- PS 612, Sulphate-resistant Portland cement type 'A' and sampling fresh concrete in the laboratory
- PS 716, Mixing
- PS 717, Compacting factor test for concrete
- PS 746, Definitions and terminology of cements
- PS 849, Making and curing concrete compression test cubes

20.2.2 ASTM (American Society for Testing and Materials)

- ASTM C 33, Concrete Aggregates
- ASTM C 39, Test Method for Compressive Strength of Cylindrical Concrete Specimens

- ASTM C 40, Organic impurities in sand for concrete
- ASTM C 87, Effect of organic impurities in fine aggregates on strength of mortar
- ASTM C 88, Soundness of aggregates
- ASTM C 94, Ready mixed Concrete
- ASTM C 109, Compressive strength of hydraulic cement mortars
- ASTM C 117, Material finer than No. 200 (0.075mm) sieve
- ASTM C 123, Light weight pieces in aggregates
- ASTM C125, Concrete and concrete aggregates
- ASTM C 127, Specific gravity and absorption of coarse aggregate
- ASTM C 128, Specific gravity and absorption of fine aggregate
- ASTM C 13, Resistance to abrasion of small size coarse aggregate
- ASTM C 136, Sieve or screen analysis of fine and coarse aggregate
- ASTM C 142, Clay lumps and friable particles in aggregates
- ASTM C 143, Slump of Portland Cement Concrete
- ASTM C 150, Portland cement
- ASTM C 156, Water retention by concrete curing material
- ASTM C 171, Sheet material for curing concrete
- ASTM C 185, Air content or hydraulic cement mortar
- ASTM C 188, Density of hydraulic cement
- ASTM C 191, Time of setting of hydraulic cement by vicat needle
- ASTM C 260, Air entraining admixture for concrete
- ASTM C 289, Potential reactivity of aggregate
- ASTM C 309, Liquid membrane forming compounds for curing concrete
- ASTM C 494, Chemical admixtures for concrete
- ASTM C 535, Resistance to abrasion of large size coarse aggregates
- ASTM C 75, Aggregate sampling
- ASTM C 994, Preformed expansion joint filler for concrete
- ASTM C 1190, Concrete joint sealer (hot poured elastic type)
- ASTM C 1715, Preformed expansion joint filler for concrete paving and structural concrete
- ASTM D 1850, Concrete joint sealer (cold application type)
- ASTM E11, Wire cloth sleeves for testing purposes
- ASTM E 96, Water vapour transmission of materials in sheet form
- ASTM E 154, Materials for use as vapour barrier under concrete slabs
- ASTM E 337, Relative humidity by wet and dry bulk psychrometer

20.2.3 ACI (American Concrete Institute)

- ACI 211, Recommended practice for selecting proportions for normal and heavy weight concrete
- ACI 214, Quality control charts
- ACI 301, Specifications for structural concrete for building
- ACI 304, Recommended practice for measuring, mixing, transporting and placing concrete
- ACI 305, Hot weather concreting
- ACI 308, Recommended practice for curing concrete
- ACI 309, Recommended practice for consolidation of concrete
- ACI 315, Manual of standard practice of detailing reinforcement concrete structure
- ACI 318, Building code requirement of reinforced concrete
- ACI 347, Recommended practice for concrete formwork

20.2.4 British Standards

- BS 12, Portland cement, ordinary and rapid hardening
- BS 410, Test Sieves
- BS 812, Methods for the sampling and testing of mineral aggregates, sand fillers
- BS 822, Concrete aggregates from natural sources
- BS 1881, Methods of testing concrete
- BS 3148, Tests for water for making concrete
- BS 3837, Expanded polystyrene boards
- BS 3869, Rigid expanded polyvinyl chloride for thermal insulation.
- BS 4027, Sulphate – resisting Portland cement
- CP 8110, Structural use of concrete
- OP 114, Structural use of reinforced concrete in buildings

In addition, the latest editions of other Pakistan and British Standards, American Concrete Institute Standards, American Society for Testing and Materials Standards and other Standards as may be specified by the Engineer for special Materials and Construction are also relevant.

20.3 SUBMITTALS

a. Suitable templates or instructions or both shall be provided for setting out of items not placed in the forms. Embedded items and other materials for mechanical and electrical operations shall have been completed, inspected, tested and approved before concrete is placed.

b. For special concrete finish and for special methods of construction, formwork shop drawings shall be designed and prepared by the Contractor, at his own cost. Approval of shop drawings as well as that of actual samples of concrete finish shall be obtained before work is commenced.

c. The Contractor shall supply to the Engineer at fortnightly intervals, test certificates with the appropriate standard in respect of the samples of cement from the work-site. These tests shall be carried out in a laboratory approved by the Engineer.

d. The grading of the coarse and fine aggregates shall be tested at least once for every 100 tons supplied, to ensure that the grading is uniform and same as that of the samples used in the preliminary tests.

e. Where doubt exists as to the suitability of the water, it shall be tested in accordance with BS 3148.

f. The Contractor shall provide Mix design by weight for each class of concrete. Manufacture 12 test cylinder for each 3 mix design batches (6 Dia. x 12 high) inches in accordance with the Mix design batching by weight and test 3 cylinders each at 3, 7, 14 & 28 days intervals in the presence of Engineers Representative and submit all relevant data and results of tests for approval of the Engineer. The Contractor shall obtain approval from the Engineer in writing for each Mix design before producing the actual concrete for the Works.

g. 'Workability' of Concrete shall be determined by either the slump or compaction factor tests as directed by the Engineer and these shall be performed in accordance with the methods given ASTM C 143.

h. The slump or compaction factor for each class of concrete shall be determined during the preliminary Test mixes and the value obtained shall not be modified without the written consent of the Engineer.

i. Manufacturer's recommendations and instructions along with the sample of material shall be submitted to the Engineer for his approval.

j. The Contractor shall, at his own cost, make optimum mix design and testing for approval of the composition of non-shrinking grout and non-shrink second stage Concrete Grout, prior to Commencement of the work.

k. The Contractor shall be required to submit a sample of pre-cast unit for the approval of the Engineer: all pre-cast units shall strictly conform to the approved sample. The proposal for transporting and erecting pre-cast units in position shall also be submitted by the Contractor for the approval of the Engineer.

l. All submittals shall be made as per the requirements of relevant

section.

20.4 MATERIAL REQUIREMENTS

20.4.1 Aggregates

a. The sources of supply of all fine and coarse aggregates shall be as specified or approved by the Engineer.

b. All fine and coarse aggregates shall be clean and free from clay, loam, silt and other deleterious matter. If required, the Engineer reserves the right to have them washed by the Contractor at no additional expense. Coarse and fine aggregates shall be delivered and stored separately at site. Aggregates shall not be stored on muddy ground or where they are likely be become dirty or contaminated. They shall be placed on sloped hard strata to ensure well drained at all times.

c. Fine aggregate shall be hard coarse sand, crushed stone or gravel screenings and shall conform to requirements of PS 243 and/or BS 882 and or ASTM C-33. Only fine aggregate of grading zones 1 to 3 (BS 882) shall be used.

d. Coarse aggregate shall be crush stone of hard, durable material free from laminated structure and conforming to PS 243 and/or BS 882 and/or ASTM C-33, graded as included in Table 20.1, for use in mass concrete as in foundations.

Table 20.1, Gradation Requirements for Coarse Aggregate in Mass Concrete

Sr. No.	BS Sieve	Percent Passing by Weight
1	3-inch (76.20mm)	100
2	1.5-inch (38.10mm)	95-100
3	0.75-inch (19.05mm)	30-70
4	0.37-inch (9.52mm)	10-35
5	0.19-inch (4.76mm)	0-5

e. Coarse aggregate for all cast-in-place concrete other than mass concrete, as for foundations, shall be graded with the limits as included in Table 20.2.

Table 20.2, Gradation Requirements for Coarse Aggregate in other than Mass Concrete

Sr. No.	BS Sieve	Percent Passing by Weight
1	1.5-inch (38.10mm)	100
2	0.75-inch (19.05mm)	95-100
3	0.37-inch (9.52mm)	25-55
4	0.19-inch (4.76mm)	0-10

f. Wherever feasible, the nominal maximum size of aggregate for cast-

in place reinforced concrete slabs and other members shall be 3/4-inch. If there are difficulties in placing such a concrete the maximum size may be restricted to 1/2-inch. Provided the requirements for strength are satisfied, as approved by the Engineer.

g. Except where it can be shown to the satisfaction of the Engineer that a supply of properly graded aggregate of uniform quality can be maintained over the period of the work, the grading of the aggregates shall be controlled by obtaining the 3/4-inch maximum nominal size, the different sizes being stocked in separate stock piles and recombined in the correct proportion for each batch at the batching plant. The materials shall be stockpiled for a period before use so as to drain nearly to constant moisture content (as long as site and other conditions permit, preferably for at least a day). The grading of the coarse and fine aggregates shall be tested at least once for every 100 tons supplied, to ensure that the grading is uniform and same as that of the samples used in the preliminary tests.

20.4.2 Cement

a. The cement shall be fresh and of approved origin and manufacture. It shall be one of the following as may be specified by the Engineer.

b. Ordinary or Rapid Hardening Portland cement complying with the requirements of PS 232 or BS 12 or ASTM C-150.

c. Sulphate Resisting Portland/Cement complying with the requirements of P.S.612 or BS 4027 or ASTM C-150.

d. Unless otherwise specified. Ordinary Portland cement complying with the requirements of BS 12 shall be used.

e. For all fair faced concrete, it will be necessary to use approved cement with a view to obtain a light shade concrete as approved by the Engineer.

f. The Contractor shall supply to the Engineer at fortnightly intervals, test certificates with the appropriate standard in respect of the samples of cement from the work site. These tests shall be carried out in a laboratory approved by the Engineer.

g. Only one brand of each type of cement shall be used for concrete in any individual member of the structure. Cement shall be used in the sequence of receipt of shipment, unless otherwise directed.

h. There shall be sufficient cement at site to ensure that each section of work is completed without interruption. If the cement is supplied by the Employer, the Contractor should inform the Employer, of his requirements sufficiently in advance of its use in construction.

i. Cement reclaimed from cleaning of bags or from leaky containers shall not be used.

j. The contractor shall provide and erect (at his cost) a suitable plain, dry, well ventilated, weather proof and water proof shed of sufficient capacity to store the cement.

k. The cement shall be used as soon as possible after delivery and cement which the Engineer considers has become stale or unsuitable through absorption of moisture from the atmosphere or otherwise "shall be rejected and removed immediately from the site at the Contractor's expense. Any cement in containers damaged so as to allow the contents to spill or permitting access of the atmosphere prior to opening of the container at the time of concrete mixing shall be rejected and removed immediately from the site at the Contractor's expense.

l. The mixing together of different types of cement will not be permitted.

20.4.3 Water

Water shall be tested in accordance with PS 3148 and shall be used only from an approved source.

The Contractor shall supply sufficient water for all purposes, including mixing the concrete, curing and cleaning plant and tools. Where water can be shown to contain any sugar or an excess of acid, alkali or salt, the Engineer may refuse to permit its use.

20.4.4 Additive

All additives such as foaming and water proofing agents shall be from a manufacturer approved by the Engineer.

Air Entraining Admixtures conforming to ASTM C-260, and other Admixtures conforming to ASTM C-494 shall be used subject to approval of the Engineer.

20.4.5 PVC Water Stop

PVC Water Stop shall follow the requirements as included in SECTION-28.

20.4.6 Non-Shrink Grout

Grout for placement under base and bearing plates of machinery and equipment, for grouting anchor bars and dowels and for similar uses shall be as follows:

- Non-shrink grout of less than 1-inch thickness shall consist of one-part Portland cement and one part of clean sharp sand conforming to the requirements of these specifications and 1:22,000 to 1:15000 part of grained aluminium powder containing non-polishing agent.
- Non-shrink grout of 1-inch or more in thickness shall be proportioned as above except that 1-1/2 parts of 3/8-inch to ¼--inch pea gravel shall be added.

- The above-specified composition may be varied if required by the Engineer.
- Proportioning shall be done by weight.
- Mixing water shall be proportioned so as to provide a flow able mixture without segregation or bleeding. Dry packing will not be permitted.

20.4.7 Non-Shrink Second Stage Concrete Grout

Non-shrink second stage concrete grout shall be provided and placed in position where shown on the Drawings or as directed by the Engineer. Non-shrink concrete mix proportion shall be one-part cement two parts coarse clean sand and four parts of coarse aggregates meeting the requirements of these specifications and 1:22,000 to 1:15000 part of grained aluminium powder containing non-polishing agent. Proportioning shall be done by weight.

The above-specified composition may be varied if required by the Engineer.

20.4.8 Non-Shrink Concrete Grout for Stair Railing Column Post

Grout for placement in pockets for stair columns shall be non-shrink and shall be of strength 10,000 psi.

20.5 NOMINAL CONCRETE MIXES

20.5.1 Proportions of Mix

a. Cement and aggregates

The cement, fine aggregate and the coarse aggregate shall be weighed separately. The proportions of cement to fine aggregate and coarse aggregate shall be adjusted so as to provide the concrete of the required crushing strength when tested as set out in Table 20.3.

b. The Contractor shall prepare mix design of various grades of concrete for the approval or Engineer prior to starting concrete works. He shall regulate and arrange mixing of the ingredients of the concrete by weigh batching. The cost of designing the mix shall be borne by the Contractor.

c. Water Cement Ratio

The quantity of water used shall be just sufficient to produce a dense concrete of adequate strength and workability for its purpose. For all external work and foundations, the water/cement ratio should not exceed 0.55.

d. Workability

The workability shall be controlled by direct measurement of the water content, allowance being made for any water in the fine and coarse aggregates. The concrete shall be sufficiently workable to be placed and compacted, without difficulty, by the available means.

Workability shall be determined by either the slump or compaction factor tests as directed by the Engineer and these shall be performed in accordance with the methods given in PS 422 and PS 177 or ASTM C-143. The slump or compaction factor for each class of concrete shall be determined during the preliminary test mixes and the value obtained shall not be modified without the written consent of the Engineer. Unless otherwise permitted or specified, the concrete shall be proportioned and produced to have a slump of 3-inch or less if consolidation is to be by vibration. A tolerance of up to 1-inch above the indicated maximum shall be allowed for individual batches provided the average for all batches or the most recent 10 batches tested, whichever is fewer, does not exceed the maximum limit. Concrete of lower than usual slump may be used provided it is properly placed and consolidated.

20.5.2 Strength requirements for concrete

a. Concrete made with Portland cement shall comply with the strength requirements as included in Table 20.3.

Table 20.3, Strength Requirements for Portland Cement Concrete

Sr. No.	Concrete Class	Nominal Ratio*	Concrete Strength**
1	A	1:1:2	4500
2	B (or A3)	1:1.5:3	4000
3	C (or A1)	1:2:4	3000
4	D	1:3:6	2200
5	E (Lean Concrete)	1:4:8	1400

* Nominal Ratio is indicative only, Contractor to prepare mix design to achieve the cylinder strength for the corresponding class of concrete.

** Cylinder strength at 28-days after mixing and pouring in psi.

b. The strengths given in Table 20.3 are based on the assumption that average temperature is 20 degree C. Where accurate records of temperature are kept, allowance may be made for change of temperature or the cylinders may be tested at the equivalent maturity.

c. All structural concrete shall conform to BS 5328.

d. Unless otherwise stated, the types of concrete shall be classified on the basis of compressive strength requirements. The Contractor shall provide Mix Design by weight for each class of concrete.

Manufacture 12 test cylinders (6-inch diameter x 12-inch height) in accordance with the mix design, batching by weight, and test 3 cubes each at 3, 7, 14 & 28 days intervals in the presence of Engineer's Representative and submit all relevant data and results of tests for approval of the Engineer. The Contractor shall obtain approval from the Engineer in writing for each Mix design before producing the actual concrete for the works.

No payments for producing the mix design, manufacture of test cubes and testing shall be made. The Contractor shall include this cost in the relevant item of concrete.

20.6 DELIVERY, STORAGE AND HANDLING

Except where it can be shown to the satisfaction of the Engineer that a supply of properly graded aggregate of uniform quality can be maintained over the period of the work, the grading of the aggregates shall be controlled by obtaining the 3/4" maximum nominal size, the different sizes being stocked in separate stock piles and recombined in the correct proportion for each batch at the batching plant. The materials shall be stockpiled for a period before use so as to drain nearly to constant moisture content (as long as site and other conditions permit, preferably for at least a day).

The Contractor shall provide and erect (at his cost) a suitable plain, dry, well ventilated, weatherproof and water proof shed of sufficient capacity to store the cement.

20.7 CAST-IN-SITU CONCRETE

20.7.1 Batching

a. All cement, including cement supplied in bulk, shall be batched by weight. A bag of cement may be taken as 110 lbs. with the prior approval of the Engineer.

b. Aggregates shall be batched by weight, due allowance being made for moisture content. The apparatus for weigh-batching may be an integral part of the mixer or a separate unit of a type approved by the Engineer. It shall be accurate within 2% and shall be checked for accuracy at least once a month.

c. The quantity of additives i.e. foaming and water proofing agents etc. shall be as prescribed by the manufacturer or as directed by the Engineer.

d. Where the batching plant is of the type in which cement and aggregates are weighed in the same compartment, the cement shall be introduced into the compartment between two sizes of aggregates.

e. Each batch shall be so charged into the mixer that some water will enter in advance of the cement and aggregates. Water shall

continue to flow for a period which may extend to the end of the first 25 percent of the specified mixing time. Controls shah, be provided to prevent batched ingredients from entering the mixer before the previous batch has been completely discharged.

20.7.2 Mixing

a. The concrete shall be mixed in an approved batch mixer conforming to the requirements of BS 305. It shall be fitted with the manufacturer's plate stating the rates, capacity and the recommended number of revolutions per minute and shall be operated in accordance therewith. It shall be equipped with a suitable charging mechanism and an accurate water measuring device.

b. Mixing shall continue for the period recommended by the mixer manufacturer or until there is apparently a uniform distribution of the materials and the mass is uniform in colour, whichever period is longer. If it is desired to use a mixing period of less than 1½ minute, the Engineer's approval shall be obtained in writing.

c. Controls shall be provided to ensure that the batch cannot be discharged until the required mixing time has elapsed. At least three quarters of the required mixing time shall take place after the last of the mixing water has been added.

d. The interior of the mixer shall be free of accumulations that will interfere with mixing action. Mixing blades shall be replaced when they have lost 10 percent of their original height.

e. Concrete shall be mixed only in quantities for immediate use. Concrete which has set shall not be re-tempered, but shall be discarded.

20.7.3 Transporting

a. The concrete shall be transported from the place of mixing to the place of final deposit as rapidly as practicable by means which will prevent segregation or loss of or addition to ingredients it shall be deposited as nearly as practicable in its final position so as to avoid re-handling or flowing. All skips vehicles, or containers used for transporting the concrete shall be thoroughly clean.

b. During hot or cold weather, concrete shall he transported in deep containers, on account of their lower ratios of surface area to mass, which reduces the rate of loss of water by evaporation during hot weather and loss of heat during cold weather.

20.7.4 Placing

a. Before placing of concrete, formwork shall have been completed, water shall have been removed reinforcement shall have been

secured in place; expansion joint material, and other embedded items shall have been kept in position; and the entire preparation shall have been approved.

b. No concrete is to be placed into the foundation trenches until the ground to receive the same has been examined and approved by the Engineer for this purpose.

c. Concrete shall be deposited continuously, or in layer of such thickness that no concrete will be deposited on concrete which has hardened sufficiently to cause the formation of seams or planes of weakness within the section. If a section cannot be placed continuously, construction joints shall be located as shown in the Contract Documents or as approved by the Engineer. Placing shall be carried out at such a rate that the concrete which is being integrated with fresh concrete is still plastic. Concrete which has partially hardened shall not be deposited Temporary spreaders in forms shall be removed when the concrete placing has reached an elevation rendering their services unnecessary. They may remain embedded in the concrete only if made of metal or concrete and if prior approval has been obtained.

d. The actual sequence of construction proposed by the Contractor shall he subject to the Engineer's approval before construction starts on any part of the structure, and this sequence shall not be varied without the Engineer's approval.

e. The concrete shall be placed as soon after it has been mixed as is practicable. Once the concrete has left the mixer, no more water shall be added, although the concrete may be mixed or agitated to help maintain workability. The concrete shall not be used if, through any cause, the workability of the mix at the time of placing too low for it to be compacted fully and to an acceptable finish by whatever means available.

f. The time between mixing and placing should be reduced if the mix is richer or the initial workability of the mix is lower than normal; if a rapid hardening cement or an accelerator is used, or if the work is carried out at a high temperature or exposed to a crying atmosphere.

g. The Contractor shall ensure that the delay between mixing and placing does not exceed 45 minutes under any circumstances. Any concrete which does not satisfy this requirement shall not be used.

h. The concrete shall be deposited as nearly as possible in its final position to avoid re-handling. In no circumstances may concrete be railed or made to flow along the forms by the use of vibrators. Concreting shall be carried on as a continuous operation using methods which shall prevent segregation or loss of ingredients.

i. The free fall of concrete shall not be allowed to exceed 5 ft. (1.5 m) and where it is necessary for the concrete to be lowered more than this depth, it is not to be dropped into its final position, but shall be placed through pipes fed by a hopper. When a pipe is used for placing concrete the lower end shall be kept inside, or close to the freshly deposited concrete. The size of the pipe shall be not less than 9-inch (225mm) diameter.

j. The workmen carrying concrete to the site, and all other workmen moving about on the reinforcement before the concrete is placed, shall move only along runways or planks placed for the purpose and no person shall be allowed to walk on the reinforcement itself.

k. Prior to the laying of concrete on load bearing masonry walls, bearing plates and at other points, as may be directed by the Engineer, the surface will be brought to a true, hard, smooth, level surface using cement sand mortar in the ratio of 1-part of cement to 3-parts of sand. Two layers of building paper will then be laid flat to separate the concrete from the surface on which it is to be laid.

20.7.5 Construction Joints

a. Concreting shall be carried out continuously up to construction joints, the arrangement of which shall be predetermined by the Engineer.

b. Joints not shown on the Drawings shall be so made and located as to least impair the strength of the structure and shall need prior approval of the Engineer. In general, they shall be located near the middle of the spans of slabs and beams unless a secondary beam intersects a main beam at this point, in which case the joint in the main beam shall be offset a distance equal to twice the width of the secondary beam. Joints in walls and columns shall not be at the underside of floor slabs or beams, and at the top of footings or floor slabs. Beams, brackets, columns, capital haunches and drop panels shall be placed at the same time as slabs. Joints shall be perpendicular to the main reinforcement.

c. All reinforcing steel shall be continued across joints. Key and inclined dowels shall be provided as directed by the Engineer. Longitudinal keys at least 1½-inch (40 mm) deep shall be provided in all joints in walls and between walls and slabs or footings.

d. When the work has to be resumed on a surface which has hardened, such surface shall be roughened in an approved manner which will expose the aggregate uniformly and will not leave laitance, loosened particles of aggregate or damaged concrete at the surface. Feather edges will be avoided.

e. The hardened concrete of construction joints and of joints between

footings and walls or columns, between walls or columns and beams or floors they support, joints in unexposed walls and all others not mentioned herein shall be dampened (but not saturated) immediately prior to placing of fresh concrete.

f. The hardened concrete of joints in exposed work, joints in the middle of beams and slabs; and joints in work designed to contain liquids shall be dampened (but not saturated) and then thoroughly covered with a coat of cement grout similar in proportions to the mortar in the concrete. The grout shall be as thick as possible on vertical surfaces and at least 150 mm thick on horizontal surfaces. The fresh concrete shall be placed before the grout has attained initial set.

g. Where the concrete has not fully hardened, all laitance shall be removed by scrubbing the wet surface with wire or bristles and brushed, care being taken to avoid dislodgment of particles of aggregate. The surface shall then be coated with neat cement grout. The first layer of concrete to be placed on this surface shall not exceed 6-inch (150 mm) in thickness, and shall be well rammed against old work, particular attention being paid to corners and closed spots.

20.7.6 Expansion Joints

Expansion joints shall be provided wherever indicated on the Drawings. In no case shall the reinforcement, corner protection angles, or other embedded items be run continuous or through an expansion joint. All expansion joints shall be carefully placed so as not to be displaced during concreting. The method of placing the expansion joints shall be strictly in accordance with the Drawings and as approved by the Engineer. All materials for use in the expansion joints shall have, prior approval of the Engineer before placing order for supply.

20.7.7 Embedded Items

a. The material, design and location of water stops in joints shall be as indicated in the Contract Documents. Each piece of re-moulded water stop shall be of maximum practicable length in order that the number of end joints will be held to a minimum

b. Joints at intersections and at ends of pieces shall be made in the manner most appropriate to the material being used. Joints shall develop effective water-tightness fully equal to that of the continuous water stop material, shall permanently develop not less than 50 percent of the mechanical strength of the parent section, and shall permanently retain their flexibility

c. Electric conduits and other pipes which are planned to be embedded shall not, with their fittings, displace more than four

percent of the area of the cross section of a column on which stress is calculated or which is required for fire protection. Sleeves, conduits, or other pipes passing through floors, walls, or beams shall be of such size or in such location as not to impair unduly the strength of the construction; such sleeves, conduits, or pipes may be considered as replacing structurally in compression the displaced concrete, provided that they are not exposed to rusting or other deterioration, are of uncoated or galvanized iron or steel not thinner than standard steel pipe, have a nominal inside diameter not over 50 mm and are spaced not less than three diameters on centres except when Drawings of conduits and pipes are approved by the Engineer embedded pipes and conduits other than those merely passing through, shall not be larger in outside diameter than one third the thickness of the slab, wall, or beams in which they are embedded nor so located as to impair unduly the strength of the construction. Sleeve pipes, or conduits of any material not harmful to concrete and within the limitations of this section may be embedded in concrete with the approval of the Engineer provided they are not considered to replace the displaced concrete.

d. All sleeves, inserts, anchors, and embedded items required for adjoining work or for its support shall be placed prior to concreting.

e. All Contractors whose work is related to the concrete or must be supported by it shall be given ample notice and opportunity to introduce and/or furnish embedded items before the concrete is placed.

f. Expansion joint material, water stops and other embedded items shall be positioned accurately and supported against displacement. Voids in sleeves, inserts, and anchor slots shall be filled temporarily with readily removable material to prevent the entry of concrete into the voids.

20.7.8 Mass Concrete

Mass-concrete shall be placed in layers approximately 18-inch thick. Vibrator heads shall extend into the previously placed layer.

20.7.9 Consolidation

a. All concrete shall be consolidated by vibration, spading, Roding or forking so that the concrete is thoroughly worked around the reinforcement, around embedded items and into comers of forms, eliminating all air or stone pockets which may cause honeycombing, pitting, or planes of weakness. Internal vibrators shall have a minimum frequency of 8000 vibrations per minute and sufficient amplitude to consolidate the concrete effectively. They shall be operated by competent workmen. Use of vibrators to transport

within forms shall not be allowed. Vibrators shall be inserted and withdrawn at points approximately 18-inch apart. At each insertion, the duration shall be sufficient to consolidate the concrete but not excessive so as to cause segregation, generally from 5 to 15 sec. A spare Vibrator shall be kept on the job site during all concrete placing operations.

Where the concrete is to have an as-cast finish, a full surface of mortar shall be brought against the form by the vibration process, supplemented, if necessary, by spading to work the coarse aggregate back from the formed surface.

b. If there is any tendency for the mix to segregate during consolidation, particularly if this produces excessive laitance, the mix proportions shall be modified to effect an improvement in the quality of the concrete to the satisfaction of the Engineer and in conformity with the provisions of SECTION-20.5.

c. Vibrator shall not be allowed to contact the formwork for exposed concrete surfaces.

d. Mechanical vibrators shall be of a type suited in the opinion of the Engineer to the particular conditions.

e. Over-vibration or vibration of very wet mixes is harmful and should be avoided.

20.7.10 Curing and Protection

a. Beginning immediately after placement, concrete shall be protected from premature drying, excessively hot or cold temperatures and mechanical, injury and shall be maintained with minimum moisture loss at a relative constant temperature for the period necessary for hydration of the cement and hardening of the concrete. The materials and methods of curing snail be subject to approval of the Engineer.

b. For concrete surfaces not in contact with forms, one of the following procedures shall be applied immediately after completion of placement and finishing:

- Ponding or continuous sprinkling;
- Application of absorptive mats or fabric kept continuously wet;
- Application of waterproof sheet materials approved by the Engineer;
- Application of other moisture-retaining covering as approved; and
- Application of a curing compound conforming to ASTM C 309.

The compound shall be applied in accordance with the recommendations of the manufacturer immediately after- any water sheen, which may develop after finishing has disappeared from the concrete surface. It shall

not be used on any surface against which additional concrete or other material is to be bonded unless it is proved that the curing compound will not prevent bond, or unless positive measures are taken to remove it completely from areas to receive bonded applications.

c. Moisture loss from surfaces placed against wooden forms or metal forms exposed to heating by the sun shall be minimized by keeping the forms wet until they can be safely removed. After form removal the concrete shall be cured until the end of the time prescribed for curing.

d. Curing in accordance. with sub-clause 'a' & 'b' above shall be continued for at least 10 days in the case of all concrete except concrete with rapid-hardening Portland Cement for which the period shall be at least 3 days. Alternatively, if tests are made of cylinders kept adjacent to the structure and cured by the same methods, moisture retention measures may be terminated when the average compressive strength has reached 70 percent of the minimum specified works cylinder strength.

   If one of the first four curing procedures of sub-clause 'b' is used initially, it may be replaced by one of the other procedures of that sub-clause any time after the concrete is one day old provided the concrete is not permitted to become surface dry during the transition.

e. When the mean daily outdoor temperature is less than 5 degree C (41 deg. F) temperature of the concrete shall be maintained between 14 and 20 degrees C (50 to 68 deg. F) for the required curing period of sub-clause 'd'.

   When necessary, arrangements for heating, covering insulation or housing the concrete work shall be made in advance of placement and shall be adequate to maintain the required temperature without injury due to concentration of heat. Combustion heaters shall not be used during the first 24 hours unless precautions are taken to prevent exposure of the concrete to exhaust gasses, which contain carbon dioxide.

f. During hot weather when necessary, provision for wind-brakes, shading for spraying, sprinkling, ponding or wet covering with a light-coloured material shall be made, in advance of placement. Such protective measures shall be taken as quickly as concrete hardening and finishing operation will allow.

g. Changes in temperature of the air immediately adjacent to the concrete during and immediately following the curing period shall be kept as uniform as possible and shall not exceed 3 deg. C (37 deg. F) in any one hour or 14 degree C (50 deg. F) in any 24-hour period.

h. During the curing period, the concrete shall be protected from damaging mechanical disturbances, such as load stresses, heavy shock and excessive vibrations. All finished concrete surfaces shall be protected from damage by construction equipment, materials or methods by application of curing procedures, and by rain or running water. Self-supporting structures shall not be loaded in such a way as to over stress the concrete.

20.7.11 Application of Non-Shrink Grout

Concrete surfaces to receive non-shrinking grout shall be roughened, cleaned and dampened.

Form shall be provided to retain the grout until sufficiently hard to support itself.

Grout shall he poured in place and thoroughly rodded or washed to prevent the formation of voids.

After non-shrink grout has received its initial set, it shall be kept damp for 24 hours.

20.7.12 Placing of Vapour Barrier

Vapour barrier shall be laid in position wherever shown on the Drawings.

The material shall be supplied in rolls and laid by rolling over the prepared surface at the levels and position in the areas shown on the Drawings. Where joint is necessary at the side or end of a sheet, this shall be a double weld folded joint made by placing the edges together and folding over twice continuously taking the top edge prior to concreting. The Contractor shall protect the film sheets from damages during laying and subsequent operations and shall replace at his own cost all damaged film sheets to the satisfaction of the Engineer.

20.8 WORKS IN EXTREME WEATHER

a. Unless adequate protection is provided and approval is obtained from the Engineer, concrete shall not be placed during rain.

Rainwater shall not be allowed to increase the mixing water nor to damage the surface finish.

b. When the temperature of the surrounding air is expected to be below 5^{o}C during placing or within 24 hours thereafter, the temperature of the plastic concrete, as placed, shall be no lower than 13^{o}C for sections less than 12-inch in any dimension nor 10^{o}C for any other sections.

When necessary concrete material should be heated before mixing and carefully protected after placing, in general, heating or mixing

water alone to about 60°C may be sufficient for this purpose. Dependence should not be placed on salt or other chemicals for the prevention of freezing. No frozen material or materials, containing ice shall be used. All concrete damaged by frost shall be removed. It is recommended that concrete exposed to the action of freezing weather should have entrained air and the water content, of the mix should not exceed 5.5 gallon/bag of cement.

If water or aggregate is heated above 38°C the water shall be combined with the aggregate in the mixer before cement is added. Cement shall not be mixed with water or with mixtures of water & aggregate having a temperature greater than 38°C.

c. During hot weather, the temperature of the concrete as placed shall not be so high as to cause difficulty from loss of slump, flash set, or cold joints and should not exceed 32°C. For massive concrete, this temperature should not exceed 21°C. When the temperature of the concrete exceeds 32°C, precautionary measures approved by the Engineer shall be put into effect. When the temperature of the steel is greater than 50°C, steel forms and reinforcement shall be sprayed with water just prior to placing the concrete. The ingredients shall be cooled before mixing, or flaked ice or well crushed ice of a size that will melt completely during mixing may be substituted for all part of the mixing water if, due to high temperature, low slump, flash set or cold joints are encountered.

Other precautions recommended by ACI Standard 305 shall also be adopted.

20.9 PRECAST CONCRETE

Precast concrete units shall be fair faced, cast to the sizes and dimensions as indicated on the Drawings. The concrete used for precast units shall conform to the specifications laid down for cast in situ reinforced cement concrete unless otherwise required and directed by the Engineer.

The Contractor shall be required to submit a sample of precast unit for the approval of the Engineer all pre-cast units shall strictly conform to the approved sample.

Pre-casting platform of the size and at the location approved by the Engineer shall be constructed. The concrete in one pre-cast unit shall be placed in one operation, in accordance with the details shown on the Drawings.

The material and design of formwork and the method of pre- casting the units shall be approved by the Engineer. The erection/installation and removal of the precast units from the pre-casting platform shall not be permitted until and unless they are properly cured to the satisfaction of the Engineer.

All precast units shall be smoothly finished to the required lines, grades, angles etc. Holes, grooves, pockets, hooks shall be provided as shown and/or as directed by the Engineer. The units shall be properly stacked on a platform without causing any cracks and damages. Curing of all the precast units shall be done in accordance with the relevant BS/approval of the Engineer.

20.9.1 Erecting Precast Units

All the precast units shall be transported and erected into position in a manner as approved by the Engineer.

The Contractor shall submit his proposal in this regard and obtain approval from the Engineer in advance.

The units shall be embedded or otherwise installed in their permanent positions as shown on the Drawings or as directed by the Engineer.

20.9.2 Lifting Beams

The Contractor shall use lifting beams at his own cost, for erecting pre-cast members where the Engineer so directs. Lifting beams shall be supplied and erected by the Contractor, at his own cost, at all points where lifting is necessary for maintaining the plant but is inaccessible to mobile cranes or alternatively, covered by overhead traveling cranes. The Contractor, however, is to supply the trolleys and erect them on the lifting beams, and to test operation of installed equipment.

20.10 CEMENT CONCRETE PAVEMENTS

For all concrete work relevant specifications of this section shall apply.

20.10.1 Side Forms and Construction

Side forms shall be of steel or any other suitable material and of a design as approved by the Engineer.

In general, only materials and methods that have proved their acceptability by past performance will be considered. All form shall be constructed so that they can be removed without hammering or prying against the concrete.

Horizontal joints in the forms will not be permitted. Forms shall be thoroughly cleaned and oiled with linseed/mineral oil or shall be given two coats of nitro-cellulose lacquer each time they are used.

The forms shall be set on a thoroughly compacted base true to line and level and firmly secured in position by appropriate methods. Conformity with the alignment and levels shown on the Drawings shall be checked as and when required by the Engineer. Where necessary corrections shall be made immediately before placing the concrete; where any form has been disturbed it shall be reset and rechecked.

Pavements shall be constructed in panels of sizes as shown on the Drawings.

The panels shall be laid alternately, the adjoining panels being concreted when the side forms are struck and the jointing materials placed, inspected and approved by the Engineer. Each panel is to be concreted in one operation and no interruptions shall be permitted during the operation. The concrete shall be tipped from the trolley slightly in advance of the working place and then shovelled into position. The spreading shall be carried out very carefully. Compaction shall be done by means of vibro-compactors or approved surface vibrators. If a vibro-compactor is used. it shall be operated on the concrete and will not be allowed to strike or displace the forms. The spreading and compacting of the successive layers shall proceed without interruptions and as quickly as practicable so as to ensure that the slab is monolithic throughout its depth.

The wearing surface shall be laid while the base concrete is still wet and screeded to line and level. When the initial set takes place the surface shall be trowelled smooth with a steel trowel to provide a dense closed surface.

All the joints shall be carefully formed as shown on the Drawings or as directed by the Engineer. The joint filler together with preformed groove shall provide complete separation of adjacent slabs. The joints shall all be sealed with bitumen as shown on the Drawings or/and as directed by the Engineer.

20.10.2 Protection and Curing

a. General Requirements

Concrete shall be protected adequately from injurious action sun, rain, flowing water and mechanical injury, and shall not be allowed to dry from the time it is placed until the expiry of the minimum curing periods specified hereinafter. Water curing shall be accomplished by keeping the surface of the concrete continuously wet by covering with water or with approved water saturated covering, where wood forms are left in place for curing.

They shall be kept sufficiently damp at all times to prevent openings at the joints and drying out of the concrete. All portions of the structure shall be kept moist for the full curing periods, specified hereinafter.

When liquid membrane curing compound is used the surface of the concrete shall be protected from traffic or other abrasive action that may break the membrane, for the full period of curing. The membrane curing compound shall be white coloured and shall be approved by the Engineer and shall comply with ASTM C 309, type 2.

b. Curing Periods

The curing period shall be at least 10 days, or as directed by the Engineer

c. Removal of Forms

The Contractor shall exercise great care in avoiding damage to joints, arises, dowel bars etc. while removing the forms. Under no circumstances will the use of pry bars between the forms and pavement be permitted. Side forms shall not be removed until at least 40 hours have elapsed from the time of completing the concreting of the slab which they contain. In no case shall forms be removed until the concrete has hardened sufficiently to permit removal without damage to the concrete. Concrete work shall be protected from damage during the removal of formwork and from injury resulting from the storage or movement of material during construction.

20.10.3 Finishing

All unformed surfaces shall be finished with a wood float except as otherwise specified. Visible vertical surfaces shall have all projections and irregularities removed. The entire surface shall be rubbed if required by the Engineer, with a No. 16 carborundum brick, or other abrasive until even, smooth and of uniform appearance, and shall be washed clean. Plastering of surface, application of cement or other coating will not be permitted.

All exposed corners shall be chamfered, 1-inch x 1-inch (25x25mm) unless otherwise mentioned or shown in the Drawings or directed by the Engineer. Concrete surface which will be covered with other materials shall be screeded without floating.

20.10.4 Spreading, Finishing and floating of concrete in pavements

a. General Requirements

The striking off, compacting and floating of concrete shall be done by mechanical methods, if approved by the Engineer. Where the Engineer determines that it is impracticable to use mechanical methods, manual methods of spreading, finishing and floating may be used on pavement lines as indicated on the Drawings.

b. Mechanical Methods

The concrete shall be spread uniformly between the forms, immediately after it is placed, by means of an approved spreading machine. The spreader shall be followed by an approved finishing machine equipped with two oscillating or reciprocating screeds. The spreading machine or the finishing machine shall be equipped with vibrating equipment that will vibrate the concrete for the full paving width. Internal vibrators shall be used adjacent to the longitudinal edge of the pavement. These vibrators shall be attached to the rear of the spreading machine onto the finishing machine. Vibrators shall not rest on new pavements or side forms or in contact with any dowel bars, and the arrangement of power supply to the vibrators shall be such that when the

motion of machine is stopped, vibration shall cease. The rate of vibration shall be not less than 8000 vibrations per minute. The concrete shall be spread to full width before being struck off and compacted so that the surface will conform to the finished grade and cross-section as shown on the Drawings and at the same time leave sufficient material for the floating operation. The spreading & finishing machine shall move over the pavement as many times and at such intervals as may be required by the Engineer to ensure thorough compaction.

Except as otherwise specified, after the pavement has been struck off and compacted, it shall be finished with an approved longitudinal float. The Contractor may use a longitudinal float composed of one or more cutting and smoothing Floats, suspended from and guided by rigid frame. The frame shall be carried by four or more visible wheels riding on and constantly in contact with the forms.

The Contractor may use a longitudinal float which works with a sawing motion, while held in a floating position parallel to the road centre line and passing gradually from one side of the pavement to the other. Movements ahead, along the centre line of the road, shall be in successive advances of not more than half the length of the float.

Instead of using other type of longitudinal float a single machine which will affect satisfactory compaction, finishing and floating may be used. This machine may be towed by a spreading machine: This combination, finishing floating machine shall be equipped with screeds and vibrators as hereinafter specified for spreading and finishing machine Floating shall be accomplished by means of a non-oscillating float held in a suspended position from the frame.

If any spreading, finishing and floating equipment is not maintained in full working order or if the equipment as used by the Contractor proves inadequate to obtain the results prescribed, such equipment shall be improved or satisfactory equipment substituted or added at the direction of the Engineer.

c. Manual Methods

When striking-off and compacting by manual methods is permitted, the concrete shall be levelled and then struck-off to such an elevation that, when properly compacted, the surface will conform to the required grade and cross-section. The strike board shall be moved forward with a combined longitudinal and transverse motion, the manipulation being such that neither ends is raised from the side forms during the process. While striking off, a slight excess of concrete shall be kept in front of the cutting edge at all times. Prior to tamping, the concrete along the forms shall be thoroughly spaded or vibrated. The entire area of pavement shall be tamped or vibrated a manner

that will ensure maximum compaction. The concrete shall be brought to the required grade and shape by the use of a tamper consisting of a heavy plank whose length exceeds the width of the pavement by 1 foot or by the use of a mechanical vibrating unit spanning the full width of the spread. The tamper shall be constructed with properly trussed roads to stiffen it and prevent sag and shall be shod with a heavy strip or metal for a tamping surface. The tamper shall be moved with a combined tamping and longitudinal motion, raising it form side form and dropping it so that the concrete will be thoroughly compacted and rammed into place. A small surplus material l is com acted and rammed into front of the tamper or vibrating unit and taming or vibrating shall continue until the true cross-section is obtained reed and the mortar flushes slightly to the surface. .

On grades in e. excess of 5 percent where hand methods are permitted, a little strike board shall follow at a speed of 25 ft to 50 ft per hour back of the heavy strike board, and shall be used in the same way, so as to remove waves caused by flow of concrete.

Where hand tamping is permitted, not less than two strike boards or tampers shall be used for production in excess of 350 cubic feet. After the concrete has been compacted, it shall be smoothed with a wooden float where necessary, as directed by the Engineer.

d. Longitudinal Floating

Manual floats shall be at least 12 ft. in length not less than 6 inches in width and shall be properly stiffened to prevent bending or warping. In using the float, it shall be held parallel to centre line of the pavement at all time and shall be moved laterally across the pavement from one side or edge to the other until all high areas are cut down and floated into depressions, leaving a surface that is smooth and true to grade. Batch transverse passage of the longitudinal manual float shall lap the proceeding passage by half.

e. First Straight Edge Testing

Immediately following final floating, the entire area of the pavement shall be tested with a 10-ft. (approx. 3-meters) straight edge. Any depressions found shall be immediately filled with fresh concrete which shall be struck off compacted and finished. High areas shall be worked down and refinished. The straight edge testing and re-floating shall continue until the pavement has the required surface contour.

f. Burlap, (Coarse Canvas) Dragging

After the first straight edge testing and when most of the water sheet has disappeared from the surface and just before the concrete becomes non-plastic, the surface shall be dragged with a strip of burlap (coarse canvas) 3

ft. to 10 ft. wide and having a length 4 ft. more than the width of the slab. The burl of shall be dragged along the surface of the pavement in a longitudinal direction. Burlap shall be clean and kept free from coatings of hardened concrete. It shall be moist at the time of use.

g. Second Straight Edge Testing

After the concrete has hardened sufficiently to permit walking on it, the surface of the pavement shall again be tested with a 10-ft. straight edge. Any portion of the pavement which shows a variation from the testing edge of more than 1/8 inch shall be corrected by cutting, or shall be removed and replaced at the expense of the Contractor.

20.10.5 Expansion and Contraction Joints

a. All the expansion and contraction joints shall be carefully formed as shown on the Drawings or as directed by the Engineer. As regards dowel bars and joint assemblies, such stakes, brackets or other devices shall be used, as necessary to keep the entire joint assembly in true vertical and horizontal position. The joint filler together with the preformed groove shall provide complete separation of adjacent slabs. The joints shall be sealed with the specified non-extruding sealing compound set in a 3/4-inch wide preformed chase as shown on the Drawings. The lie preformed chase shall be thoroughly cleaned of all dust, debris, stone or other hard material prior to its sealing. The riser of all joints shall be rounded to a radius as shown on the Drawings before the concrete hardens.

b. The joints sealing compound shall be hot poured bitumen or approved sealing compound for concrete pavements complying with BS-2499 for hot tropical climates and heavy-duty industrial site subject to severe exposure. All joints are to be filled with flexell expansion joint filler, or an approved elastic, compressible, durable and rot-proof equivalent of sufficient rigidity to enable it to be satisfactorily installed in the joint and resist deformation during the passage of the concreting equipment. The filler is to be of the same thickness as the joint width. Holes to accommodate the dowel bars shall accurately be drilled or punched out. Where shown on the Drawings, dowel bars of required diameter shall be placed at the specified spacing. The bars shall be lubricated with an approved lubricant. One' end of the dowel bar at expansion joints shall be provided with a closely fitting sleeve 3-inch long, consisting of bitumen coated plastic or other approved material to permit expansion. A loose plug 1 inch deep of approved compressible filling material shall be inserted into the sleeve as shown on the Drawings at the end of the bar. All the dowel bars shall be mild steel bars of

the size shown on the Drawings and shall conform to the requirements as specified in the SECTION-21, REINFORCEMENT.

c. Contraction joints shall be provided as shown on the Drawings.

d. The assembly and method of constructing the expansion joints/contraction joints shall be subject to the approval of the Engineer.

e. In general, all PVC water stops/hydrofoil shall be placed in the centre of the structural member. Each piece of the water stop-hydrofoil shall be of maximum practicable length. An ordinary sharp knife saw or any other sharp tool can be used to cut the water stop. Joints at inter sections and at ends of pieces shall be made in the manner most appropriate to the material being used. Joints shall develop effective water tightness fully equal to that of the continuous water stop material and shall permanently retain their flexibility. For straight line connection melting method of connection can be used by passing two water stops intended for connection against a heated iron or copper sheet. When they are melted, the two are combined.

f. After joining, the water stop should be allowed to cool.

g. For all other connections such as T-type or L-type, the welding method of joining should be used. Welding rod of same material as the water stop shall be used. The welding rod & the water stop shall be heated & melt at the same time, by means of heated air jetting from the hot jet gun.

20.11 TEST OF CONCRETE QUALITY

The Contractor shall provide samples of concrete for testing at the Engineer's direction. Proper facilities shall be provided for making and curing the test specimens. A competent person shall be employed by the Contractor whose first duty shall be to supervise all stages in the preparation and placing of the concrete. All test specimens shall be made at site and tests carried out under his direct supervision.

Cylinder test shall be performed in accordance with the discretion of the Engineer. The standard of acceptance for preliminary and works tests shall be as given below,

The usual test for concrete with maximum size of aggregate up to 1-112 inch is the 6-inch cylinder tested in compression. Details of the testing are given in ASTM C 39.

For all grades of concrete; preliminary cylinder strength test with the mixes and materials to be used shall be performed in accordance with ASTM C 31 before the work is begun and subsequently whenever any change is to be

made in the materials or in the proportions of materials to be used, or as required by the Engineer. The strengths shall comply with the standard of quality specified in accordance with Table 20.3 in accordance with ASTM C 39. The cost of such testing shall be borne by the Contractor.

Test sample shall be taken at the mixer or as directed by the Engineer. The test specimens shall be cured in accordance with ASTM C 31.

Records shall be kept of all test cylinders identifying the mix used the section of work for which the concrete was used and the date poured.

Five test cylinders are to be tested for compressive strength as specified in ASTM C 39. These tests shall be carried out at site or in a laboratory, approved by the Engineer. Two cylinders shall be tested at the age of seven days and three at 28 days and the strengths determined are to comply with the standard of quality specified. The laboratory tests shall be carried out by an independent organization, such as Government Testing' Laboratory or such other undertakings approved by the Engineer. The original test reports received from the 'above authorities should be submitted to the Engineer.

For all grades of concrete, the appropriate strength requirement shall be considered to be satisfied if none of the strengths of the cylinders is below the specified cylinder strength or if the average strength of the three cylinders is not less than the specified cylinder strength and the difference between the greatest and the least strength is not more than 20% of the average.

When the results of works cylinder tests show that the strength of any concrete is below the minimum specified* the Engineer may give instructions for the whole or part of the work concerned to be removed and replaced at the expense of the Contractor. The Contractor shall bear the cost of any other part of his, or any other contractor's worst, which has to be removed and replaced as a result of the defective concrete. If any concrete is held to have failed, the Engineer may order the proportions of that class of concrete to be changed in order to provide the specified strength.

20.12 FINISHING OF FORMED SURFACES

20.12.1 General

a. After removal of forms, the surfaces of concrete shall be given one or more of the finishes specified below in locations designated by the Contract Documents.

b. When finishing is required to match a small sample furnished to the Contractor, the sample finish shall be reproduced on an area at least 100 sq.ft. in an inconspicuous location designated by the Engineer before proceeding with the finish in the specified location.

c. Allowable deviations from plumb or level and from the alignment, profile grades, and dimensions are specified in clause 9. Tolerances

for concrete construction are defined as tolerances to be distinguished from irregularities in finish as described herein. The finish requirements for concrete surfaces shall be as generally specified in this clause and as indicated on the Drawings. Finishing of concrete surfaces shall be performed only by workmen who are skilled in concrete finishes. The Contractor shall keep the Engineer advised as to when finishing of concrete will be performed. Unless inspection is waived in each specific case, finishing of concrete shall be performed only in the presence of the Engineer. Concrete surfaces will be tested by the Engineer where necessary to determine whether surface irregularities are within the limits herein after specified, surface irregularities are classified as abrupt or gradual. Offsets caused by displaced or misplaced form sheeting or lining or section, or otherwise defective form lumber will be considered as abrupt irregularities, and will be tested by direct measurements. All other irregularities will be considered as gradual irregularities, and will be tested by use of a template, consisting of a straight edge or the equivalent thereof for curved surfaces. The length of the template 2 metre for testing of formed surfaces and 3 metre for testing of unformed surfaces.

20.12.2 As-cast Finishes

Unless otherwise specified or indicated on the Drawings the classes of finish shall apply as follows:

a. Rough form finish

No selected form facing materials shall be specified for rough form finish surfaces. The holes and defects shall be patched. Otherwise, surfaces shall be left with the texture imparted by the forms.

b. Fair face finish

Fair face finish applies to concrete formed surfaces, the appearance of which is considered by the Engineer to be of special importance, such as surfaces of structures prominently exposed to public inspection. Surfaces of concrete structures requiring fair face finish as shown in the Drawings. Surface irregularities, measured as described in sub-clause 7.2.1, 'Rough form finish', shall not exceed 4 mm for gradual irregularities and 6mm for abrupt irregularities, except that abrupt irregularities will not be permitted at construction joints. Abrupt irregularities at construction joints and elsewhere in excess of 6 mm and gradual irregularities in excess of 1/8 inch. (3mm) shall be reduced by grinding so as to conform to the specified limits. Abrupt irregularities at construction joints shall be ground on level of 1 to 20 ratio of height to length.

Unless otherwise approved, repair of imperfections in formed concrete shall be completed within 24 hours after removal of forms. The form facing material shall produce a smooth, hard, uniform texture on the concrete. It may be plywood, temperated concrete form grade hardboard metal, plastic paper, or other approved material capable of producing the desired fair face finish. The arrangement of the facing material shall be orderly and symmetrical, with the number of seams kept to the practical minimum. It shall be supported by studs or other backing capable of preventing excessive deflection. Material with raised grain, torn surfaces, worn edge, patches, dents, or other defects which will impair the texture of the concrete surface shall not be used. The holes and defects shall be patched. All fins shall be completely removed

c. Architectural Finish Concrete

Architectural finish to concrete formed surfaces as shown on the Drawings is required by the Engineer where the architectural appearance of surfaces of structures exposed to public view is of special consideration and importance. The Contractor shall use approved special material for formwork and design the forms in conformity with the specified architectural patterns, textures and finishes in order to obtain first class architectural finish on formed concrete surface without any defect, irregularities, blemishes, imperfections and encrustations.

i Sample approvals of precast & in-situ concrete

These samples will be reviewed and approved on the basis of colour, dimensional accuracy, and finish of surfaces and general appearance. The same requirements for sample approval will be required for both precast and in-situ concrete exposed surfaces.

ii Forms

The contractor must maintain the forms unusually tight and braces to prevent movement, mal-alignment and bleeding that will result in sand streaks, honeycomb, fins, stain or unsightly appearance.

It wood forms are chosen to be used by the Contractor they shall .be constructed of 3/4 inch. (20mm) minimum thickness plywood constructed in a fashion to allow many re-uses with all surfaces sealed with a polyurethane varnish.

Edges, surfaces and corners of forms shall be sealed to prevent loss of any matrix or unequal absorption of water. Corners of wood forms shall be filled with suitable compound and all contact surfaces sealed with a polyurethane varnish.

Re-use of forms shall be subject to approval of the Engineer.

iii Curing

Curing shall be done in shade (out of direct sunlight) and shall be for a minimum period of 4 days.

iv Finishing procedures:

Finishing procedures for filling air void in smooth finished concrete developed by a formed surface.

While the concrete surface is still damp (not more than three days after removal of forms), apply a thin coat of medium consistency neat cement slurry by means of bristle brushes to provide a bonding coat within any pit or blemishes in the parent concrete; avoid coating large areas of the finished surface. Before slurry has dried or changed colour, apply a dry (almost crumbly) grout comprised of one-part cement, of the type and brand of cement used in the original concrete, to one and one-half parts clean masonry sand with a fineness modulus of approximately 2.25 and complying with the gradation requirements of the ASTM Specifications C144. Mix proper amounts of white cement and colouring with the parent mortar to produce a satisfactory colour match with the parent concrete after hardening. Use samples previously prepared.

Apply the finishing grout uniformly with damp (neither dripping wet nor dry) pads of coarse burlap approximately 6-inch square used as a float. Scrub the grout well into the pits to provide a dense mortar in all the imperfections to be filled. Allow the mortar to partially harden, from one to two hours, depending upon the weather. Avoid direct hot sunlight. If the air is hot and dry, keep the concrete surface damp during this period using a fine fog spray. When the grout has hardened sufficiently so it can be scraped from the surface with the edge of a steel trowel without damaging the grout from the small pits of holes, cut off all that can be removed with a trowel without delay; next allow the surface to dry thoroughly and rub it vigorously with clean, dry burlap to completely remove any dried grout. No visible film of grout shall remain after this rubbing. Complete the entire cleaning and grouting operation for the grout to dry after it has been cut with the trowel, so it can be wiped off clean with the burlap.

On the day after the repair work, the concrete surfaces should again be wiped off clean with dry burlap to remove any inadvertent dust leave no built-up surfaces on the parent surfaces. Employ, if possible, a used piece of burlap containing old hardened mortar to act as a mild abrasive. Use of find abrasive stone if needed to remove any remaining built-up film without breaking through the surface film of the original concrete. Such scrubbing should be light and sufficient only to remove excess material without working up a lather of mortar or changing the texture of concrete. Following the final bagging or stoning operation, provide a thorough wash down with stiff bristle brushes to remove all extraneous materials and spray the concrete surface

with a fine fog spray periodically to maintain a continually damp condition for at least three days after application of the pit repair grout.

v Rust Stains

All rust stains are to be removed employing the following procedure:

The rust stain shall be soaked for 10 minutes with a solution of (0.055 lb.) 25gm of sodium citrate in (0.33lb) 150 gms water (brushing the solution at short intervals is satisfactory). Then the surface is sprinkled with crystals of sodium hydrosulfite and covered with a paste of Fuller's Earth and water. On a vertical surface, the paste is applied with a trowel, with the crystals first sprinkled on the paste so they will be in direct contact with the stain. The paste is allowed to dry for 10 minutes then scraped off and the treatment repeated if necessary.

vi Repairing of Formed Surfaces:

It is the intention of Specification to require, forms, mixture of concrete and workmanship so that concrete surfaces, when exposed, will require no patching. Any concrete which is not formed as required and conforming to approve samples or for any reason is out of alignment or level or shows a defective surface, shall be removed from the job by the Contractor at his expense unless the Engineer grants permission to repair the defective area. Permission to patch any such area shall not be considered as waiver of the Engineer's right to require a complete removal of defective work if the repair does not, in his opinion, satisfactorily restore the quality and appearance of the surface. The Engineer shall be the sole judge of acceptability of appearance.

vii Finishes of Unformed Surfaces

Where monolithic concrete floor finish is shown on the Drawings, placing shall proceed continu6usly for the full thickness of the course or RCC slab without change in concrete mix. Mixing water shall be the minimum required for proper area shall be kept damp for 7 days. Metal tools shall not be used in finishing a patch in a formed wail, which will be exposed.

Where as-cast finishes are specified, the quantity of patched area shall be strictly limited. The combined total of patched areas in as-cast surfaces shall not exceed 2 sq ft. in each 1000 sq.ft. of as-cast surface. This is in addition to form tie patches, if the project design permits ties to fall within as-cast areas.

Any patches in as-cast architectural concrete shall be indistinguishable from surrounding surfaces. The mix formula for patching mortar shall be determined by trial to obtain a good colour match with the concrete when both patch and concrete are cured and dry. After initial set, surfaces of patches shall be dressed manually to obtain the same texture as surrounding surfaces.

Patches in architectural concrete surfaces shall be cured for 7 days. Patches shall be protected from premature drying to the same extent as the body of the concrete.

viii Tie and Bolt Holes

After being cleaned and thoroughly dampened, the tie and bolt holes shall be filled solid with patching mortar.

ix Proprietary Materials

If permitted or required by the Engineer, proprietary compounds for adhesion or as patching ingredients may be used in lieu of or in addition to the foregoing patching procedures. Such compounds shall be used in accordance with the manufacturer's recommendations with prior approval of the Engineer.

20.13 TOLERANCES

Where tolerances are not stated in the Drawings for any Individual structure or feature thereof maximum permissible deviations from established lines, grades and dimensions shall conform to the following. The Contractor is expected to set and maintain concrete limits. These allowable tolerances shall not relieve the Contractor of the responsibility for correct fitting of indicated materials. Those tolerances are not cumulative.

a. Variation from the plumb (or the specified better for inclined walls)

i In the lines and surfaces of columns, piers, and walls and in arises.

In any 10 ft. (3 metre) of length or height:	1/4" (6 mm)
In any storey or 20 ft. (6 metre) maximum:	3/8" (10 mm)
Maximum for the entire length or height:	1" (25 mm)

ii For exposed corner columns, control joint grooves and other conspicuous lines.

In any bay or 20 ft. (6 metre) maximum	1/4" (6 mm)
Maximum for the entire length or height	1/2" (13 mm)

b. Variation from the level or from the grades indicated on the Drawings.

i In floors, ceilings, beams soffits and in arises.

In any 10 ft. (3 metre) of length	1/4" (6 mm)
In any bay or 20 ft. (6 metre) maximum	3/8" (10 mm)
Maximum for the entire length	3/4" (20 mm)

ii For exposed lintels, sills, parapets, horizontal grooves and other

conspicuous lines.

In any bay or 20 ft. (6 metre) maximum	1/4" (6 mm)
Maximum for the entire length	3/8" (10 mm)

c. Variation of the linear building lines from established position in plan and related position of columns, walls and partitions.

In any bay or 10 ft. (3 metre) maximum	1/2" (13 mm)
Maximum for the entire length	1" (25 mm)

d. Variation in the sizes and locations of sleeves, Floor openings and wall openings. ± 1/4" (± 6mm)

e. Variation in cross-sectional dimensions of columns and beams and in the thickness of slabs and walls.

Minus	1/4" (6mm)
Plus	1/2" (13mm)

f. Footings

i Variation in dimensions in plan Minus

Minus	1/2" (13 mm)

Plus (plus variation applied to concrete only, not to reinforcing bars or dowels). 2" (50mm)

ii Misplacement or eccentricity

2 percent of the footing width in the direction of misplacement but not more than (applies to Concrete only, not to reinforcing bars or dowels). 2" (15 mm)

iii Thickness

Decrease in specified thickness	5%
Increase in specified thickness	No limit

g. Variation in Steps

i In a flight of stairs

Rise	1/8" (3 mm)
Tread	1/4" (6 mm)

ii In consecutive steps:

Rise	1/16" (1.5 mm)

Tread	1/8” (3 mm)

h. Tolerances for Pre-Cast Concrete Constructions

Forms must be true to size and dimensions of concrete members shown on the Drawings and be so constructed that the dimensions of the finished products will be within the following limits at the time of placement of these units in the structure, unless otherwise noted on structural-architectural Drawings:

i	Overall dimensions of members	1/16” per 10 feet
ii	Cross-sectional dimensions	
Sections less than 3-inch		1/16” (1.5 mm)
Sections over 3-inch and less than 18-inch		1/8” (3 mm)
Sections over 18-inch		1/4” (6 mm)
iii	Deviations from straight line in long sections	
Not more than		1/8” per 10 feet
iv	Deviation from specified camber	1/16” per 10 feet
v	Maximum differential between adjacent units in erected position	1/4” (6 mm)

20.14 ACCEPTANCE OF STRUCTURE

20.14.1 General

a. Completed concrete work which meets all applicable requirements will be accepted subject to the other terms of the Contract Documents.

b. Completed concrete work which fails to meet one or more of the requirements and which has been repaired to bring it into compliance will be accepted subject to the other terms of the Contract Documents.

c. Completed concrete work which fails to meet one or more of the requirements and which cannot be brought into compliance may be accepted or rejected as provided in these Specifications or in the Contract Documents. In this event, modifications may be required to assure that remaining work complies with the requirements.

20.14.2 Dimensional Tolerances

a. Formed surfaces resulting in concrete outlines smaller than permitted by the tolerances of SECTION-20.13 shall be considered potentially deficient in strength and subject to the provisions of SECTION-20.14.4.

b. Formed surfaces resulting in concrete outlines larger than permitted

by the tolerance of SECTION-20.13 may be rejected and the excess material shall be subject to removal. If removal of the excess material is permitted, it shall be accomplished in such a manner as to maintain the strength of the section and to meet all other applicable requirements of function and appearance. Permission is required if excess material is to be removed in accordance with this clause.

c. Concrete members cast in the wrong location may be rejected if the strength, appearance or function of the structure is adversely affected or if misplaced items interfere with other construction.

d. Inaccurately formed concrete surfaces exceeding the limits of SECTION-20.13 or SECTION-23 CONCRETE FORMWORK & ACCESSORIES and which are exposed to view, may be rejected and shall be repaired or removed and replaced if required.

20.14.3 Appearance

a. Architectural concrete with surface defects exceeding the limitations of SECTION-23 CONCRETE FORMWORK & ACCESSORIES shall be removed and replaced.

b. Other concrete exposed to view with defects which adversely affect the appearance of the specified finish may be repaired only be approved methods.

c. Concrete not exposed to view is not subject to rejection for defective appearance.

20.14.4 Strength of Structure

a. The strength of the structure in place will be considered potentially deficient if it fails to comply with any requirements which control the strength of the structure, including but not necessarily limited to the following conditions:

- Concrete strength requirements not considered to be satisfied in accordance with SECTION-20.5.2.
- Reinforcing steel size, quantity, strength, position or arrangement at variance with the requirements as listed under specification of 'Reinforcement' or in the contract documents.
- Concrete which differs, from the required dimensions or location in such a manner as to reduce the strength.
- Curing less than that specified.
- Inadequate protection of concrete from extremes of temperature during early stages of hardening and strength development.
- Mechanical injury, construction fires, accidents of premature removal of formwork likely to result in deficient strength.
- Poor workmanship likely to result in deficient strength.

b. Structural analysis and/or additional testing may be required when the strength of the structure is considered potentially deficient.

c. Core tests may be required when the strength of the concrete in place is considered potentially deficient.

d. If core tests are inconclusive or impractical to obtain or if structural analysis does not confirm the safety of the structure, load tests may be required and their result evaluated in accordance with British Standard, CP 110 or ACI 318.

e. Concrete work judged inadequate by structural analysis or by results of a load test shall be reinforced with additional construction if so directed by the Engineer or shall be replaced, at the Contractor's expense.

f. The Contractor shall pay all costs incurred in providing the additional testing and/or analysis required by this section.

g. All costs of additional testing and/or analysis which is made at the Employer request and which is not required by these Specifications, or by the Contract Documents shall also be borne by the Contractor.

20.15 MEASUREMENT AND PAYMENT

20.15.1 Measurement

Concrete will be measured for the number of cubic foot or cubic metre (whichever is included in Bill of Quantities) acceptably placed complete in all respects as per Drawings and in strict accordance with this section of specification.

Except otherwise specified herein or elsewhere in the Contract Documents, no measurement and payment will be made for the under mentioned specified works related to the relevant items of the Bills of Quantities. The cost thereof shall be deemed to have been included in the quoted unit rate of the respective items of the Bills of Quantities.

The rates quoted by the Contractor in the Bill of Quantities shall include work to be executed under this specification in any floor and at any height except where otherwise specifically stated in the relevant item of Bill of Quantities and the Contractor shall not be entitled to any claim or claim any compensation on this account:

- Providing, fixing, striking, etc. of formwork.
- Providing, placing and fixing of anchor bolts or any other embedded parts.
- Providing and installing all type of joints in concrete structure, including expansion joints.
- Providing and fixing water stoppers.

20.15.2 Payment

Payment will be made in accordance with the unit prices in the Bill of Quantities for the various items in accordance with the specifications and shall constitute full compensation for furnishing all materials, shuttering, equipment and labour and for performing all operation necessary to complete the work.

Concrete shall be measured as executed but no deductions shall be made for the following:

- Volume of any steel embedded in the concrete;
- Volume occupied by water pipes, conduits etc. not exceeding 10 square inches each in cross-sectional area; and
- Voids not exceeding 4 square inch in work given in square feet. If any void exceeds 4 square inch, total void shall be deducted.

Voids, which are not to be deducted as specified above refer only to openings or vents which are wholly within the boundaries of measured areas.

Openings or vents which are at the boundaries of measured areas shall always be subject to deductions irrespective of size.

Concrete work shall be classified and measured separately as listed under items of Bills of Quantities.

Junction between straight and curved works shall in all cases be deemed to be included with the work in which they occur.

SECTION-21 REINFORCEMENT

21.1 SCOPE OF WORK

The work under this section of specifications consists of furnishing, cutting, fabricating, bending and placing steel reinforcement as shown on the Drawings or as directed by the Engineer. The scope of this section of specification is covered with detailed specifications as laid down herein.

21.2 APPLICABLE STANDARDS

The work shall conform to requirements of latest editions of following standards, wherever applicable, unless otherwise specified.

21.2.1 Pakistan Standard

- PS 241, Tensile testing of steel
- PS 244, Bend test for steel
- PS 580, Rolled deformed steel bars (intermediate grade) for concrete reinforcement
- PS 605, Rolled deformed steel bars (hard grade) for concrete reinforcement
- PS 606, Rolled deformed steel bars (structural grade) for concrete reinforcement
- PS 607, General technical delivery requirement for steel

21.2.2 British Standard

- BS 693, General requirements for oxy-acetylene welding of mild steel
- BS 785, Hot rolled bars and hard drawn wire for the reinforcement of concrete
- BS 1856, General requirement for the metal arc welding of mild steel
- BS 4449, hot rolled steel bars for reinforcement of concrete
- BS 4461, Cold worked steel bars for reinforcement of concrete
- BS 4466, Bending dimensions and scheduling of bars for the reinforcement of concrete

21.2.3 ASTM Standard

- ASTM A 305, Minimum requirement for the deformations of deformed steel bars for concrete reinforcement
- ASTM A 615, Deformed billet steel bars for concrete reinforcement

21.2.4 ACI Standard

- ACI 315, Manual of standard practice for detailing reinforced concrete structure
- ACI 318, Building code requirements for reinforced concrete

In addition to the above, the latest editions of other Pakistan Standards, British standards, American Concrete Institute Standards, American Society for Testing and Materials Standards and other standard as may be specified by the Engineer for Special Material and construction are also relevant.

21.3 SUBMITTALS

The Contractor shall submit the following to the Engineer for approval before commencement of work:

- Bar bending schedule prepared by Contractor on the basis of approved Drawings for the approval of the Engineer.
- Results of all tests performed upon steel reinforcement bars obtained from the site of work as per directions of the Engineer.

21.4 MATERIAL REQUIREMENTS

Reinforcement for concrete shall conform to the respective Pakistan, British, ASTM, or other Standards as specified in the Drawings and in the Contract Documents or as may be specified by the Engineer.

Unless otherwise specified, all plain reinforcing bars shall comply with the requirements of BS 4449 for plain mild steel bars and shall have a minimum characteristic strength of 40,000 psi.

Unless otherwise specified, all deformed reinforcing bars shall comply with the requirements of BS 4461 for deformed cold worked new stock billet steel bars and shall have a minimum characteristic strength of 60,000 psi.

Steel wire mesh reinforcement shall conform to requirements of ASTM Designation A-185-64 or BS 4483. Standard Specifications for Welded Steel Wire Fabric for concrete reinforcement. It shall be used where shown on the Drawings.

Reinforcement shall be free from all loose or flaky rust and mill scale, or coating, including ice, and any other substance that would reduce or destroy the bond. Reduced section steel reinforcement shall not be used.

21.5 DELIVERY & STORAGE

21.5.1 Delivery

Steel reinforcement bars shall be kept in bundles firmly secured and tagged.

21.5.2 Storage

The method of storage shall be approved by the Engineer. Reinforcing bars shall be stored in racks or platforms above the surface of ground and shall be protected free from scaling, rusting, oiling, coatings, damage, contamination and structural defects prior to placement in works. Bars of different diameters and grades of steel reinforcement shall be kept separately.

21.6 BAR BENDING SCHEDULES

The Contractor shall prepare bar bending schedules of all the reinforcing steel bars and these bar bending schedules shall be submitted to the Engineer for approval. The Contractor shall obtain approval of the bar bending schedules before starting actual bar bending works.

21.7 FABRICATING, BENDING & PLACING

All metal for reinforcement shall be free from loose mill scale, loose rust, mud, oil, grease, or other harmful matter immediately before the concrete is placed.

Reinforcement is to be accurately placed as shown in the Drawings, and secured against displacement by using 16-gauge G.I wire ties or suitable slips at intersections and supported from the formwork by using concrete, metal or plastic chairs and spacers or hangers of an approved pattern. Where concrete blocks are used for ensuring the cover, they shall be made of mortar not leaner than 1 part of cement to 2 parts of sand.

Where the concrete surface will be exposed to the weather in the finished structure, the portions of all accessories in contact with the form work shall be galvanized or shall be made of plastic.

Bars used for concrete reinforcement shall be fabricated in accordance with the dimensions shown in the bar bending schedule approved by the Engineer. The cutting tolerance for all bars shall be ± 1 inch. (± 25 mm).

Where an overall or an internal dimension of a bent bar is specified in the schedule, the bending tolerance, unless otherwise stated, shall be as included in Table 21.1.

Table 21.1, Bending Tolerances for Reinforcement Bars

Sr. No.	Dimension of Bent Bars		Tolerance	
	Over Feet	Up to & Including Feet	Plus Inch	Minus Inch
1	-	3	1/5	1/5
2	3	6	1/5	1/5
3	6	-	1/5	1

Bars shall be placed to the tolerances as included in Table 21.2.

Table 21.2, Placement Tolerances for Reinforcement Bars

Sr. No.	Location of Bars	Tolerance
1	Concrete cover to formed surfaces	± 1/4" (± 6mm)
2	Minimum spacing between bars	± 1/4" (± 6mm)
3	Top bars in slabs and beams	
	Members 8 inch deep or less	± 1/4" (± 6mm)

Sr. No.	Location of Bars	Tolerance
	Members more than 8 inch but not over 24 inch deep	± 3/8" (± 10mm)
	Members more than 24 inch deep	± 1" (± 25mm)
4	Crosswise members spaced evenly within	± 2" (± 50mm)
5	Lengthwise members	± 2" (± 50mm)

Bars may be moved as necessary to avoid interference with other reinforcing steel, conduits, or embedded items. If bars are moved more than one bar diameter or enough to exceed the above tolerances, the resulting arrangement of bars shall be subject to approval of Engineer.

Vertical bars in columns shall be offset at least one bar diameter at lapped splices. To ensure proper placement, templates shall be furnished for all column dowels.

Reinforcement shall not be bent or straightened in a manner that will injure the material.

No bars shall be bent twice in the same place, nor shall they be straightened after bending.

Unless permitted, by Engineer reinforcement shall not be bent after being partially embedded in hardened concrete.

No splice of reinforcement shall be made except as shown on the working Drawings.

Welding shall be permitted for, bars only under suitable conditions and with suitable safeguards in accordance with BS 693, PS 1856, or AWS D12.1, provided the type of reinforcement bar has the required welding properties. Tack welding may be used to fix in position bars that cross each other, only with prior approval of the Engineer.

Exposed reinforcement intended for bonding with future extensions is to be effectively protected from corrosion Protection is also to be provided to reinforcement partly built into concrete where the exposed part is to be built into later concrete.

No concreting is to be carried out until the reinforcement has been checked and approved by the Engineer.

Welding shall be done as in section 'Structural Steel Works'. All detailing shall be done as per ACI standards ACI-315 and AC1-318.

Concrete clear cover for reinforcing steel shall be as provided in Drawings. All reinforcing steel shall be held firmly in place before and during the placing of concrete by means of wires and supports adequate to prevent displacement during the course of construction.

21.8 MEASUREMENT & PAYMENT

21.8.1 Measurement

The measurement for acceptably completed works of reinforcement according to bar bending schedules approved by the Engineer shall be made by weight computed on the bases of Table 21.3.

The Contractor shall not claim for the difference in the actual weights of bars and their standard weights given in Table 21.3.

Table 21.3, Standards Weights of Reinforcement Bars

Sr. No.	Nominal Bar Diameter, Inch	Bar No.	Weight, lb/ft
1	3/8	#3	0.376
2	1/2	#4	0.668
3	5/8	#5	1.043
4	3/4	#6	1.502
5	7/8	#7	2.044
6	1	#8	2.670
7	1-1/8	#9	3.400
8	1-1/4	#10	4.303

The rates quoted by the Contractor in the Bill of Quantities shall include work to be executed under these specifications in any floor and at any height except where otherwise specifically stated in the relevant item of Bill of Quantities and the Contractor shall not be entitled to any claim or claim any compensation on this account.

Providing and installing cover blocks, chairs, supports, hooks, spacers, binding wires, and laps not shown on Drawings including wastage and rolling margin and as such are not payable. Laps shown on Drawings shall be payable.

21.8.2 Payment

Payment will be made for acceptable measured quantity of reinforcement on the basis of unit rate per metric ton or kg (whichever is included in Bill of Quantities and shall constitute full compensation for all the works related to the item.

The rate quoted include all lead/lift required for steel fabrication & placement at/in any floor or at any height as per Drawings.

SECTION-22 SULPHATE RESISTANT CEMENT CONCRETE

22.1 SCOPE OF WORK

This work shall consist of providing sulphate resistant cement in place of Portland cement to all classes of concrete subject to the contact with soil having sulphate content more than 0.1% and with ground water having sulphate content more than 1500 ppm or as mentioned in the drawing or directed by the Engineer. Maximum Chloride Ion Concentration (as a percentage of weight of cement) arising from all sources including aggregates should not exceed 0.1 for pre-stressed concrete, 0.2 for any concrete using sulphate resistance cement and 0.35 for all other cement containing matter. All requirements of concrete with sulphate resistant cement are same as mentioned in SECTION-20, PLAIN & REINFORCED CONCRETE except amended in this section

22.2 MATERIAL REQUIREMENTS

Sulphate resistant cement where required shall be sulphate resistant cement type 'A' fully conforming to Pakistan standard specification PS 612:1967 and satisfying to requirements for fineness, chemical composition, strength, setting time and soundness etc. The average compressive strength of three mortar cubes prepared with 1:3 cement and standard silica sand mortar shall not be less than 20.0 N/mm sq. at seven days. The initial setting time shall not be less than 45 minutes and final setting time not more than 10 hours.

22.3 MEASUREMENT AND PAYMENT

22.3.1 Measurement

The quantity of concrete with sulphate resistant cement shall be measured exactly in same way as mentioned in SECTION-20 PLAIN & REINFORCED CONCRETE and subsequently paid as elaborated below.

22.3.2 Payment

The accepted quantity measured as provided above shall be paid only for the difference of cost for providing sulphate resistant cement in place of ordinary Portland cement at the contract unit price for particular pay item(s) as provided in the Bill of Quantities, which price and payment shall be full compensation for all the costs involved in the proper completion of the works.

SECTION-23 CONCRETE FORMWORK & ACCESSORIES

23.1 SCOPE OF WORK

The work under this section of the specifications consists of furnishing all plant, labour, equipment, appliances and materials and in performing all operations in any floor and at any height in connection with the supply and installation of formwork for the purpose of shuttering in concreting work, complete in strict accordance with this section of the specifications and the applicable Drawings and subject to the terms and conditions of the Contract.

23.2 APPLICABLE STANDARDS

The work shall conform to requirements of latest editions of following standards, wherever applicable, unless otherwise specified.

23.2.1 American Concrete Institute

- ACI 301, Specifications for Structural Concrete for Buildings
- ACI 318, Building Code Requirements for Reinforced Concrete
- ACI 347, Recommended Practice for Concrete Formwork

23.2.2 American Plywood Association:

- APA, High Density Overlaid Concrete Form, Class 1
- APA, Structural 1, Exterior Quality, Class 1
- APA, Plastic Overlaid Plywood Forms

23.2.3 American National Standard Institute

- A199.1, Construction and Industrial Plywood.

23.3 SUBMITTALS

a. Product's Data: Submit manufacturer's specifications and installation instructions for proprietary materials and items as required, including form coatings, manufactured form systems, ties and accessories.

b. Detail Shop Drawings: Submit data on sequence of the concrete placement, location of construction joints, camber details, bearing values of the soils supporting false-work under wet and dry conditions, the anticipated settlements as well as false-work release sequence.

23.4 MATERIAL REQUIREMENTS

23.4.1 Concrete Formwork

Unless otherwise specified construct formwork of plywood, metal, metal framed plywood faced or other panel type materials acceptable to

Engineer to provide continuous, straight, smooth surfaces. Provide formwork in the largest practice sizes to minimize number of joints and to conform to joint system indicated on Drawings. Provide form material with sufficient thickness to withstand pressure of newly placed concrete without bow or deflection. Provide wood forms of minimum thickness of 16 mm.

23.4.2 Forms of Unexposed Finish Concrete

Provide forms of plywood, lumber, metal or glass fibre reinforced plastic or other acceptable material.

23.4.3 Form Ties

Provide factory fabricated, adjustable length, removable or snap off metal form ties, designed to prevent form deflection and to prevent spalling concrete surfaces upon removal. Use Plastic cone type, with threaded steel rod. For water tanks or other water retaining structures use watertight form ties as recommended by the manufacturer.

Unless otherwise indicated, provide ties so that portion remaining within concrete after removal of exterior parts is at least 38 mm from the outer concrete surface. Provide form ties which will not leave a hole larger than 25 mm diameter in the concrete surface.

Form ties fabricated on Project Site and wire ties are not acceptable.

23.4.4 Form Release

Non staining, non-reactive, rust preventive guaranteed not to affect bond of subsequent surface applications to concrete.

23.5 DESIGN OF FORMWORK

Design, erect, support, brace and maintain formwork to safely support vertical and lateral loads applied, until such loads can be supported by the concrete structure. Carry vertical and lateral loads to ground by formwork system and in-place construction that has attained adequate strength for the purpose. Design and construct formwork of concrete members and structures to correct size, shape, alignment, elevation and position.

Design form and false-work to include assumed value of live load, dead load, weight of moving equipment operated on formwork, concrete mix, height of concrete drop, vibrator frequency, ambient temperature, foundation pressures, stresses, lateral stability and other factors pertinent to safety of structure during construction.

Design formwork to be readily removable without impact, shock or damage to cast in place concrete surfaces and adjacent materials.

Provide formwork sufficiently tight to prevent leakage of cement paste during concrete placement. Solidly butt joints and provide back-up material at joints as required to prevent leakage and fins.

Design forms according to ACI 318, Parts 1, 2, and 3 requirements as well as ACI 347 requirements for loads, lateral pressure, and allowable stresses; in addition to other design parameters.

23.6 DELIVERY AND STORAGE

23.6.1 Delivery

The delivery of formwork materials shall be done in such a manner that damage can be prevented.

23.6.2 Storage

Formwork should be stored, after cleaning and preparing for re-use if used before, in such a manner that access to all different materials is available.

Material which can be affected by weathering shall be stored in appropriate building or under covers and shade.

23.7 QUALITY ASSURANCE

Design, construct, erect, support, brace, maintain and remove forms according to ACI 318, Parts 1, 2, and 3 requirements as well as ACI 347 requirements for loads, lateral pressure and allowable stresses; in addition to other design parameters such as wind loads.

Construct formwork so that cast concrete surfaces will conform to the requirements of ACI 301, Chapter 4, Paragraph 4.3 Tolerances.

Maximum allowable deflection of forming surfaces from concrete pressure will be length/360 between supports.

Provide surveys as required to check the lines and levels of the completed formwork for exposed concrete before concrete is placed. Make the required corrections or adjustments to formwork to correct deviations which exceed the specified tolerances.

Check formwork during concrete placement to ensure forms, shores, false-work, ties and other features have not been unduly disturbed by concrete placement methods or equipment. Report in writing to the Engineer deviations from the allowable tolerances

23.8 EXECUTION

23.8.1 Inspection

Examine substrate and conditions under which concrete formwork is to be performed. Correct any unsatisfactory conditions. Proceed with the work after unsatisfactory conditions have been corrected in a manner acceptable to the Engineer.

23.8.2 Form Construction

a. General

Construct forms complying with ACI 347, to sizes, shapes, lines and dimensions indicated and required to obtain accurate alignment, location, grades, level and plumb work in the finished structures. Provide for openings, offsets, sinkages, keyways, recesses, mouldings, rustication, reglets, chamfers, blocking, screed, bulkheads, anchorages, inserts, and other features required. Use selected materials to obtain the required finishes.

Fabricate forms for easy removal without hammering or prying against concrete surfaces. Provide crush plates or wrecking plates where stripping may damage cast concrete surfaces. Provide top forms for inclined surfaces where the slope is too steep to place concrete with bottom forms only. Kerf wood inserts for forming keyways, reglets, recesses, and the like, to prevent swelling and assure ease of removal.

Provide temporary openings where interior area of formwork is inaccessible for cleanout, inspection before concrete placement and placement of concrete. Securely brace temporary closures and set tightly to forms to prevent loss of concrete mortar. Locate temporary openings in forms at inconspicuous locations.

Form intersecting planes to provide true, clean out corners, with edge grain of plywood not exposed as form for concrete.

b. False-work

Erect false-work and support, brace and maintain it to safely support vertical, lateral and asymmetrical loads applied until such loads can be supported by in-place concrete structures. Construct false-work so that adjustments can be made for take up and settlement.

Provide wedges, jacks or camber strips to facilitate vertical adjustment. Inspect false-work and formwork during and after concrete placement operations to determine abnormal deflection or signs of failure and make necessary adjustments to produce work of required dimensions.

Provide shores and struts with positive means of adjustment capable of taking up formwork settlement during concrete placing operations, using wedges or jacks or a combination thereof. Provide trussed supports when adequate foundations for shores cannot be secured.

Support form facing materials by structural members spaced sufficiently close to prevent deflection. Fit forms placed in successive units for continuous surfaces to an accurate alignment, free from irregularities and within allowable tolerances. Provide camber in formwork as required for anticipated deflections due to weight and pressures of fresh concrete and construction loads for long span members without intermediate supports.

Provide temporary openings in wall forms and at other locations necessary to permit inspection and clean out.

c. Forms for Exposed Concrete

Drill forms to suit ties used and to prevent leakage of concrete mortar around tie holes. Do not splinter forms by driving ties through improperly prepared holes.

Do not use metal cover plates for patching holes or defect in forms.

Provide sharp, clean corners at intersecting planes, without visible edges or offsets. Back joints with extra studs or girts to maintain true, square intersections.

Use extra studs and bracing as required to prevent bowing of forms between studs and to avoid bowed appearance in concrete. Do not use narrow strips of form material which will produce bow.

Assemble forms in a way to be readily removed without damage to exposed concrete surfaces.

Form mouldings shapes, recesses and projections with smooth finish materials and install in forms with sealed joints to prevent displacement.

d. Corner Treatment

Form exposed corners to produce square, smooth, solid, unbroken lines, except as otherwise indicated.

Provide chambers for surfaces where indicated on Drawings.

Unless otherwise indicated, form chamfers using wood strips 19 x 19 mm; accurately formed and surfaced to produce uniformly straight lines and tight edge joints. Extend terminal edges to required limit and miter chamfer strips at changes in direction.

e. Provisions for other Trades

Provide openings in concrete formwork to accommodate work of other trades. Determine size and location of openings, recesses and chases required for such work. Accurately place and securely support built-in items into forms.

f. Cleaning and Tightening

Thoroughly clean forms and adjacent surfaces to receive concrete. Remove chips, wood, sawdust, dirt or other debris just before concrete placement. Re-tighten forms immediately after concrete placement as required to eliminate mortar leaks.

23.8.3 Form Coatings

Coat form contact surfaces with form coating compound before placing the reinforcement. Provide form coating compounds that will not bond with, stain, nor adversely affect concrete surfaces and will not impair subsequent treatment of concrete surfaces requiring bond or adhesion nor impede the wetting of surfaces to be cured with water or curing compounds. Do not allow excess form coating material to accumulate in the forms or to come into contact with surfaces against which fresh concrete will be placed. Apply in compliance with manufacturer's instructions.

Coat steel forms with a non-staining, rust preventive form oil or otherwise protect against rusting. Rust stained steel formwork is not acceptable.

23.8.4 Installation of Embedded Items

a. General

Set and build into the work anchorage devices and other embedded items required for other work that is attached to, or supported by, cast in place concrete. Use setting drawings, diagrams, instructions and directions provided by the suppliers of these items to be attached thereto.

b. Edge Forms and Screed Strips for Slabs

Set edge forms or bulkheads and intermediate screed strips for slabs to obtain required elevations and contours in the finished slab surface. Provide and secure units to support types of screed required.

c. Metal Inserts

Provide metal inserts for anchorage of materials or equipment to concrete construction, as required for the work.

Provide adjustable wedge inserts of malleable cast iron, complete with bolts, nuts and washers; 19 mm bolt size unless otherwise indicated.

Provide threaded inserts of malleable cast iron, furnish complete with full depth bolts; 19 mm bolt size, unless otherwise indicated.

Provide box out sections in concrete work as required for installation of equipment or other work.

Coordinate location of all required embedded weld plates and other items for attachment of precast concrete to cast in place concrete.

23.8.5 Shores and Supports

Shore floor directly under slab being placed so that loads from construction above will safely transfer directly to these shores. Space out shoring below this level in such a manner that no member will be excessively loaded or will

induce tensile stress in concrete members where no reinforcing steel is provided. Extend shores beyond minimum if required to ensure the proper distribution of loads and the safety of all concrete members.

Remove shores and reshore in a planned sequence to avoid damage to partially cured concrete, and to assure that the structure supported is not subjected to impact or loading eccentricities. Locate and provide adequate reshoring to safely support the work.

23.8.6 Removal of Forms

Formwork not supporting concrete, such as sides of beams, columns, walls, and similar parts of the work (vertical faces) may be removed not less than 24 hours after placing concrete provided that concrete is sufficiently hard and will not be damaged by form removal operations, and provided that curing and protection operations are maintained.

Formwork supporting weight of concrete, such as slabs and other structural elements must remain in place for the time period shown in ACI 347 (assuming design live load is less than dead load) and until concrete has attained design minimum 28-day compressive strength determined by field-cured specimens as defined below. Do not remove forms until the approval has been obtained from the Engineer.

Form facing material may be removed not less than 4 days after placement, provided shores and other vertical supports have been arranged to permit removal of form facing material without loosening or disturbing shores and supports and provided that concrete has achieved adequate compressive strength to safely support the load.

Use necessary means and precautions to protect workmen, passer-by, the installed work and material of other trades and complete safety of structure.

Cut nails as well as form ties off flush leaving surfaces smooth and clean.

Remove metal spreader ties on exposed concrete by removing or snapping off inside the wall surfaces and pointing up and rubbing the resulting pockets to match surrounding surfaces.

Flush holes resulting from spreader rods and sleeve nuts, using water, and solidly pack throughout the wall thickness with cement grout applied under pressure by means of grouting gun; grout shall be one part cement to 2-1/2 parts sand; apply grout immediately after removing forms.

23.8.7 Re Use of Forms

Clean and repair surfaces of forms to be reused in the work. Split, frayed, delaminated or otherwise damage form facing material will not be acceptable. Apply new form coating compound material to concrete contact surfaces as specified for new formwork.

When forms are extended for successive concrete placement thoroughly clean surfaces, remove fins and laitance, and tighten forms to close all joints. Align and secure joints to avoid offsets. Do not use patched forms for exposed concrete surfaces

23.9 MEASUREMENT AND PAYMENT

23.9.1 Measurement

No separate measurement shall be made for the works involved within the scope of this section of the specifications unless otherwise specifically stated in the Bills of Quantities.

23.9.2 Payment

No separate payment, unless otherwise included in the Bills of Quantities, shall be made. The cost thereof shall be deemed to have been included in quoted unit rates of relevant items of the Bills of Quantities.

SECTION-24 STRUCTURAL STEEL WORKS

24.1 SCOPE OF WORK

The work covered by this section, consists of supply of all material, labour, plant, equipment and appliances including welding, bolts, nuts, washers, anchor bolts, embedded parts etc., fabrication, erection and painting in accordance with the specifications, as per Drawings and as directed by the Engineer.

24.2 SUBMITTALS

a. Product Data: Submit manufacturer's product information, specifications and installation instructions for all structural steel components and accessories.

b. Shop Drawings: Submit complete shop drawings, including details and schedules for fabrication, assembly and erection of structural steel members, procedures, and diagrams. Include details of cuts, connections, camber, holes, and other pertinent data. Indicate welds by standard AWS symbols and show size, length, and type of each weld. Provide setting drawings showing all anchor bolt locations on plan with column grids. Show projection of each bolt above foundation concrete, length of threaded portion of each bolt and orientation of shear lugs.

c. Design Analysis and Calculations: Provide design analysis and calculations for structural steel members of which sizes are not shown, and connections for beams, girders and other steel member intersections.

d. Test Reports: Provide reports for tests conducted on shop- and field-bolted and welded connections. Include data on type(s) of tests conducted and test results.

24.3 MATERIAL REQUIREMENTS

Except otherwise stated in the Drawings, the material specifications shall conform to the following:

a. Structural steel shapes, plates and bars shall conform to the requirements of ASTM A36.

b. Cold-Formed Steel Tubing: Comply with requirements of ASTM A500, Grade B.

c. Hot-Formed Steel Tubing: Comply with requirements of ASTM A501.

d. Steel Pipe: Comply with requirements of ASTM A53, Type E or S, Grade B; or ASTM A501.

e. Build-up Members Fabricated from Plate or Bar stock: Comply with requirements of ASTM A529, A570 or A572; minimum 50,000 psi yield

strength.

f. Members Fabricated by Cold Forming: Comply with requirements of ASTM A607, Grade 50.

g. Galvanized Cold-Formed Members: Comply with requirements of ASTM A446, Grade D, galvanized to ASTM A525, Class G90.

h. Steel forging shall conform to the requirements of ASTM A235.

i. Steel casting shall conform to the requirements of ASTM A27, Grade 65-35, medium-strength carbon steel.

j. Galvanized Steel Sheet: Comply with requirements of ASTM A446, Grade C, galvanized to ASTM A525, Class G90.

k. Welding Electrodes for manual shielded metal arc welding shall conform to AWS A 5.1 latest edition or the A 5.5 latest edition. Equivalent locally manufactured electrodes may be used subject to the approval of the Engineer.

l. Common Bolts, Anchor Bolts, Nuts and Washers Bolts and Nuts shall conform to the requirements of ASTM A307.

m. High strength carbon steel bolts including nuts and washers shall conform to the requirements of ASTM A325 latest editions and of AISI B18.2

n. Cut Washers shall be of structural grade steel and shall conform to the dimension of the manufacturer's regular standard for plain washers for the size of bolts used.

o. Cast iron Shall conform to the requirements of latest edition of ASTM A 48.

p. Structural Steel Primer Paint: SSPC - Paint 2, red lead-iron oxide, oil alkyd.

24.4 TRANSPORTATION, HANDLING AND STORAGE

Stack materials out of mud and dirt and provide for proper drainage. Exercise care to avoid abrasions and other damage to shop primer paint. Protect from damage or soiling by adjacent construction operations. Keep steel members off ground by using pallets, platforms, or other supports. Protect material against corrosion and deterioration.

24.5 FABRICATION

24.5.1 Straightening of Material

Rolled material, before being worked upon must be straightened within tolerances, by ASTM specifications A6 Straightening, necessarily shall be done by mechanical means or by the application of a limited amount of localized heat. The temperature of heated areas, as measured by approved methods, shall not exceed 1100^{o}F for A514 steel or 1200^{o}F for other steels.

24.5.2 Cutting

As far as possible cutting must be done by shearing. Oxygen cutting shall be done where shear cutting is not possible and shall preferably be done by Machine. All edges shall be free from gauges, notches or burs. If necessary, the same shall be removed by grinding.

24.5.3 Holes Punching Drilling

Holes shall be punched where thickness of the material is not greater than the diameter of bolt +3 mm. Where the thickness of the material is greater the holes shall either be drilled or sub-punched and reamed to size. The die for all sub-punched holes and the drill to all sub-drilled holes shall be at least 1.58 mm smaller than the nominal diameter of the rivet or bolt. Holes for A514 steel plates over 13 mm thick shall be drilled.

24.5.4 Welding

a. General

The execution and inspection of welding will be done in accordance with the provisions of the American welding society code for welding in Building construction, D1.0. No welding for piping/electrical supports shall be made transversely to any tension flanges of trusses, beams or columns.

b. Automatic submerged Arc Welding

For all built-up members, i.e., sections fabricated from plates and flat bars or compound rolled sections, plate and box girders, where long continuous, welding is to be done, should be executed by Automatic submerged Arc Welding process in accordance with relevant AWS specifications.

Maximum and minimum size and lengths of fillet welds shall be in accordance with AISC specifications.

Surface to be welded shall be free from loose scale, slag, rust, grease, paint or any other foreign matter except mill scale which withstands vigorous wire brushing.

24.5.5 Tolerances

A variation of I mm is permissible in the overall length of members with both ends finished for Contact bearing. The bearing surfaces prepared to a common plane by mining.

Members without end finished for contact bearing which are to be framed to other steel parts of the structure shall have a variation from detailed length not greater than 3 mm.

24.6 SURFACE PREPARATION & PAINTING

24.6.1 Surface Preparation

All structural steel material i.e., rolled steel sections, plates, pipes, flat bars, chequered plates shall be cleaned free from loose scale, rust, burrs slag, etc. by means of sand blasting.

24.6.2 Painting

a. Immediately after surface preparation all material shall be given one prime coat of rust preventive paint.

b. After fabrication one shop coat of prime paint and then one coat of enamel paint shall be applied.

c. One final coat of enamel paint shall be applied after erection of all components.

d. The type of primer and enamel paints to be applied shall be as specified on the Drawings.

e. All other requirements for the specified paint system shall be in accordance with the paint manufacturer's specification recommendations.

f. The Contractor shall use the best quality of the type of paint specified and shall get the same approved by the Engineer.

g. Steel work/Surfaces not to be painted

- Steel work to be encased/embedded in concrete or surface in coated with contact with concrete or grout shall not be painted, but shall be given a cement wash after sand blasting.
- Machined finished surfaces shall not be painted but shall be coated with rust preventive compound, (approved by the Engineer) immediately after finishing. Such surfaces shall also be protected with wooden pads or other suitable means for transportation. Unassembled pins, keys, and bolt thread shall be greased and wrapped with moisture resistant paper.

24.7 INSPECTION AND TESTS

Manufacturer's Work Test Certificate for all material used shall be furnished by the contractor for Engineer's scrutiny and approval.

Rolling tolerance of all shapes and profile according to AISC shall be in accordance with the provisions of the American Society for Testing and Materials Designation A.6. These shall be checked by the Contractor before being worked upon and shall be rejected if found not within limits.

The Contractor shall arrange for analysis and test of all material rolled locally at a testing laboratory selected by the Engineer.

a. Inspection of Welding

The inspection of welding shall be performed in accordance with the American Welding Society specifications, as directed by the Engineer.

b. Rejection

Materials or workmanship not in reasonable conformance with the provisions of these specifications shall be rejected at any time during the progress of the work or the completion and erection at site.

24.8 MEASUREMENT AND PAYMENT

24.8.1 Measurement

Measurement for miscellaneous items shall be made as per the units included in the Bill of Quantities.

24.8.2 Payment

Payment shall be made for the number of units of items as provided the Bill of Quantities, measured as above, and at the Contract unit price to furnish, construct and shaping the item and shall constitute full compensation for all work related to that item.

SECTION-25 BRICK MASONRY

25.1 SCOPE OF WORK

The work under this section of the specifications consists of furnishing all plant, labour, equipment, appliances, scaffoldings and materials and performing all operations in connection with furnishing and installing brick masonry in position including Portland cement and sand for mortar & masonry, complete in strict accordance with this section of the specifications and applicable Drawings and subject to the terms and conditions of the Contract.

25.2 APPLICABLE STANDARDS

The work shall conform to requirements of latest editions of following standards, wherever applicable, unless otherwise specified:

- ACI 530, Building code requirements for masonry structures
- ACI 530.1, Specifications for masonry structures
- PS 208, Classification, strength and properties of bricks
- ASTM C67, Standard method for sampling and testing brick and structural clay tile
- ASTM C144, Standard specifications of aggregates for masonry mortar
- ASTM C150, Specifications for Portland cement

25.3 SUBMITTALS

The Contractor shall submit the following to the Engineer for approval before commencement of work:

- Methodology and sequence of work
- Specimen samples of bricks, aggregates for mortar or grout and Portland cement.
- Results of all tests performed upon the materials and masonry units obtained from the site of work as per directions of the Engineer.

25.4 MATERIAL REQUIREMENTS

25.4.1 Cement

Portland cement for mortar shall conform to the applicable requirements specified in the SECTION-20, PLAIN & REINFORCED CONCRETE.

25.4.2 Sand

Sand for mortar used in brickwork shall be furnished by the Contractor, and shall meet the requirements set forth in ASTM C144. The Fineness Modules of the sand shall range between 1.9 & 2.8 and the grading shall be within the limits

Sand shall be stored at the site in such a manner that it is not mixed with foreign matter. Methods employed by the Contractor for unloading, loading, handling and storage shall be subject to the approval of the Engineer. Sufficient quantity shall be maintained at the Site at all times to assure continuous work

25.4.3 Water

Water used in the manufacture of bricks and in the preparation of mortar shall be free from objectionable quantities of silt, organic matter, alkali, salts and other impurities, and shall conform to the applicable requirements as specified in the SECTION-20, PLAIN & REINFORCED CONCRETE.

25.4.4 Mortar

Mortar for all brickwork shall, except as otherwise specified in Drawings or directed by the Engineer, shall consist of one part Portland Cement to four parts of sand by volume for 4-1/2-inch thick walls, one part of cement to six parts of sand for 9-inch and over thick walls for building works and one part of cement to 5 parts of sand for other works. Where directed by the Engineer for increased workability, hydrated lime putty, approved by the Engineer, shall be added to the mortar but shall not exceed 25 percent, by volume of the dry cement.

Methods and equipment used for mixing mortar be such as will accurately determine and control the amount of each separate ingredient entering into the mortar and shall be subject to the approval of the Engineer. Mortar shall be mixed only in sufficient quantities for immediate use and all mortar not used within 30 minutes after addition of water to the mix shall be rejected. Re-tempering of mortar shall not be allowed. The mixers shall be thoroughly cleaned and washed at the end of each day's work.

25.4.5 Bricks

All bricks, except otherwise specified, shall be of first-class quality made from good brick earth, free from saline deposit and shall be hand moulded. They shall be thoroughly burnt without being vitrified, shall be regular, uniform in shape and size with sharp and square edges, parallel faces and of deep red or copper colour. First class bricks shall be homogeneous in texture and shall emit a clear ringing sound when struck, and shall be free from flaws, cracks, chips, stones and modules of lime. First class brick in an oven dried condition shall not absorb more than 1/5 of its weight of water when immersed one hour in water at 21 to 27 degrees centigrade and shall show no signs of efflorescence on subsequent drying. The average compressive strength of five representative first class bricks shall be not less than 2000 psi and not less than 1500 psi for any individual brick.

All bricks shall be manufactured by the Trench Kiln Method or other standard methods approved by the Engineer. The earth used in manufacturing bricks

shall be carefully selected and shall be free from objectionable quantities of lime, gravel coarse sand, roots, or other organic matter. Salts shall not exceed 0.3 percent and calcium carbonate shall not exceed 2.0 percent.

The moulds used in the manufacture of bricks shall be thoroughly sanded before each use and shall be sufficiently larger than the size of the bricks being manufactured to allow for shrinkage in drying and burning. Over-size, irregular and worn moulds shall be destroyed. Each finished brick for brick masonry shall be 9 inch by 4-1/2 inch by 3 inch in size and shall weigh between 3.2 to 4.2 kilograms. All bricks shall have a "frog" 1/4-inch-deep on one face.

Bricks of approved samples shall only be used in the works. If at any time during the progress of the work, use of sub-standard material is found by the Engineer, such work shall be rejected and the Contractor shall replace the rejected work at his cost

25.5 PLACING

The methods and equipment used for transporting the brick and mortar shall be such as will not damage the brick not delay the use of mixed mortar Brick shall not be placed during rains sufficiently heavy or prolonged to wash the mortar from the brick. Mortar already spread which becomes diluted by rain shall be removed and replaced before continuing with the work. All brick to be used in brick masonry shall be moistened with water for three to four hours before they are used by a method which will ensure that each brick is thoroughly and uniformly wetted. All bricks shall be free from water adhering to their surface when they are placed in the brick masonry.

Bricks shall be laid "frog" upward with mortar joints and in English and Flemish bond as shown on the Drawings or as directed by the Engineer. Both bed and vertical joints shall be 1/4 inch in thickness completely filled with cement mortar as specified herein, and each brick shall be bedded by firmly tapping with the handle of the trowel. All horizontal joints shall be parallel and all vertical joints in alternate courses shall be directly over one another. Excess mortar at the outer edges shall be removed and joints drawn straight with the edge of a trowel and a straight edge. All anchors and similar work required to be embedded in the brick masonry shall be installed as the work progresses. At the completion of the work all holes or defective mortar joints shall be cut out and repointed.

Where shown on the drawing the exterior faces of the walls shall be finished by striking the joints as the work proceeds. The joints shall be struck by raking the green mortar after the brick work has been laid and finishing the joint with a pointing tool. Horizontal joints shall be struck to form a weathered joint and vertical joint shall be struck with a V notch. Care shall be taken that the striking tools do not develop a cutting edge as the object of striking the joint is to

compress the mortar into the joints.

The exposed faces of all brick masonry shall be thoroughly cleaned and left bear with struck joints as specified above.

25.6 CURING

All brick masonry shall be water cured and shall be kept wet for at least seven days by an approved method which will keep all surfaces to be cured continuously wet. Method to be utilised by the Contractor for curing of brick masonry shall be subject to the approval of the Engineer. Water used for curing shall meet the requirements of the Specifications for water used in the manufacture of bricks.

25.7 REPAIR

If, after the completion of any brick masonry work, the brick is not in alignment or level, or does not conform to the lines and levels shown on the Drawings, or shows a defective surface, it shall be moved and replaced by the Contractor at his expense unless the Engineer grants permission, in writing, to patch or replace the defective area.

At the completion of the work, all holes and defective mortar joints shall be cut and repointed. Exposed masonry shall be protected against staining or other damages and excess mortar shall be cleared off the surfaces as the work progresses. All exposed masonry shall be clean, smooth, plumb and shall be of acceptable finish. In the event ordinary cleaning is not adequate, special methods such as sand blasting or otherwise as approved by the Engineer, shall be used to clean the surfaces

25.8 SCAFFOLDING

Contractor shall provide safe scaffolding of adequate strength for use of workmen at all levels and heights at his own expense. Scaffolding which is unsafe in the opinion of the Engineer shall not be used until it has been strengthened and made safe for use of workmen. Cost of scaffolding etc., shall be included by the Contractor in the unit rate for masonry items.

Damage to masonry from scaffolding or from any other cause shall be repaired by the Contractor at his own cost.

25.9 TOLERANCES

The nominal/standard dimensions of brick are 9-inch (length) x 4-1/2-inch (width) x 3-inch (thickness). No dimension of brick (width, height and length) shall differ from the specified standard dimension by more than 1/8 inch.

Moreover, all brick work shall be erected plumb and true to line and level having maximum variation in plumb in height up to 1/16 inch for 3-feet height and limited to 1 inch for the entire height.

25.10 MEASUREMENT AND PAYMENT

25.10.1 Measurement

The measurement for brick work shall be made in cubic feet or cubic metre (whichever is included in Bill of Quantities) of brick work provided within the limits as shown on the Drawings or as directed by the Engineer.

25.10.2 Payment

Payment for brickwork shall be made at the contract unit price per cubic feet or cubic metre (whichever is included in Bill of Quantities). Payment shall constitute full compensation for furnishing all materials, equipment and labour including all incidentals necessary to complete the work.

SECTION-26 DAMP PROOF COURSE

26.1 SCOPE OF WORK

The work under this section of the specifications consists of furnishing all plant, labour, equipment and materials and performing all operations in connection with furnishing damp proof course (DPC) in position complete in strict accordance with this section of the specifications, applicable Drawings and as specified in the Bill of Quantities.

26.2 MATERIAL REQUIREMENTS

All materials i.e., cement, sand, aggregate, water polythene sheet and bitumen shall conform to the specifications given in respective sections.

26.3 HORIZONTAL DPC

26.3.1 In Walls

Unless specified in the Drawings, the horizontal DPC. shall consist of 2-inch thick, Class-C cement concrete mixed with 2.5 kg of pudlo per bag of cement or other approved quality water proofing compound as per manufacturer's specifications two floats of hot bitumen 10/20 penetration grade and intervening layer of polythene sheet.

26.3.2 Under Floors

Same as in walls except bitumen layers to be laid on 1/2" - 3/4" blinding screed (1:6) to even out surface of Class-E hard core.

26.4 VERTICAL DPC

Unless specified in the Drawings, the vertical DPC shall consists of ½" thick cement sand plaster in 1:3, mixed with 2.5 kg of pudlo per bag of cement or other approved quality water proofing compound as per manufacturer's specifications and shall be applied at required levels as per Drawings and instructions by the Engineer, including two float of hot bitumen 10/20 penetration grade.

26.5 CONSTRUCTION REQUIREMENTS

The Contractor shall lay the DPC only when the level, quality of masonry work, etc. is approved.

The concrete work of DPC shall conform to the applicable requirements specified in SECTION-20, PLAIN & REINFORCED CONCRETE.

Horizontal DPC shall extend to the full width of the wall i.e., up to the external faces. No portion of doors opening, etc. shall be left while laying DPC. The period of curing of concrete shall be not less than 72 hours. Every care should be taken that concrete is not left dry during this period. The work of laying

DPC shall be carried out as follows unless otherwise described in Bill of Quantities:

- Placing 2-inch thick layer of Class-C cement concrete.
- Laying 2 coats of hot bitumen 10/20 penetration grade @ 20 lbs. per sq.ft. (each coat) over entire width and lengths of concrete after the concrete has been properly cured for at least 72 hours, and sand blinding where specified.
- Laying of polythene sheet 500 gauge over entire width and length of concrete after the concrete has been treated with 2 coats of hot bitumen.

The application of bitumen coating in case of vertical DPC shall be same as mentioned above.

26.6 MEASUREMENT AND PAYMENT

26.6.1 Measurement

Measurement shall be made in square feet or square metre (whichever is included in Bill of Quantities) of superficial area or surface damp proofed as per this section of specification and accepted by the Engineer.

26.6.2 Payment

Payment will be made for the number of square feet or square metre (whichever is included in Bill of Quantities) of superficial area damp proofed at the contract unit price and will include full compensation for furnishing and placing all materials and for all labour, equipment, tools and incidentals necessary to complete the work prescribed in the Bill of Quantities.

SECTION-27 CEMENT PLASTER

27.1 SCOPE OF WORK

The work under this section of the specifications consists of furnishing all plant, labour, equipment, appliances, and materials and in performing all operations in connection with providing and installation of cement plaster, and specified external rendering complete in strict accordance with this section of the specifications and the applicable Drawings and subject to the terms and conditions of the Contract.

27.2 APPLICABLE STANDARDS

The work shall conform to requirements of latest editions of following standards, wherever applicable, unless otherwise specified.

27.2.1 Pakistan Standard

- PS 232, Ordinary Portland Cement

27.2.2 ISO (International Organization for Standardization)

- R 597 Definitions and terminology of cement.
- R 679 Method of testing strength of cements, compressive and flexural strength of plastic mortar (Rilem - (embureau method).
- P 680 Chemical analysis of cement & main constituents of Portland Cement.
- R 681 Chemical analysis of cements-mixer Constituents of Portland cement.
- R 682 Chemical analysis of cements - determination of sulphur as sulphide.

27.2.3 ASTM (American Society for Testing and Material)

- ASTM C144, Aggregate for Masonry mortar
- ASTM C631, Bonding Compounds for interior plastering

27.2.4 BSI (British Standards Institution)

- BS 812, Methods for sampling and testing of mineral aggregates, sands and fillers.
- BS 1199, Sands for external renderings Internal plastering with lime and Portland cement and floor screeds.
- BS 1369, Metal lathing (steel) for plastering.
- BS 5262, External rendered finishes.
- BS 5492, Internal plastering.

27.3 SUBMITTALS

Sample of materials shall be submitted to the Engineer for his approval prior to use in the works.

27.4 MATERIAL REQUIREMENTS

Portland cement for mortar shall conform to the applicable requirements specified in the SECTION-20, PLAIN & REINFORCED CONCRETE.

Sand for plaster shall comply with the requirements of BS 1199, BS 1200 or the Pakistan Standard "Sand for Plaster" as directed by the Engineer.

Water for plaster shall conform to the applicable requirements specified in the SECTION-20, PLAIN & REINFORCED CONCRETE.

All materials and workmanship for plaster not explained in these specifications, shall comply with the requirements of relevant BS CP 211 and CP 221 or as directed by the Engineer.

27.5 PROPORTIONING AND MIXING

Except as may be otherwise shown on surfaces specified, all plaster work, both internal and external shall be Ordinary Portland Cement plaster of the required thickness and cement/sand ratio as shown on the Drawings.

Measurement of materials by volume shall be by containers of known capacity to maintain consistent proportions. No lumpy or caked material shall be used. Mixing equipment boxes and tools shall be clean. Materials shall be proportioned as specified on the Drawings or as directed by the Engineer. Mixing shall be continuous until all ingredients are evenly distributed and thoroughly mixed.

Only limited water shall be added for proper workability and such quantity of mortar shall be prepared which can be consumed in thirty minutes after preparation. Preparation of mortar in bulk quantity for use during the entire day or for any other time more than that stipulated above is expressly prohibited. Re-tempering shall not be permitted and all mortar which has begun to stiffen shall be discarded.

Plaster ingredients shall be thoroughly mixed either by hand on a clean cement concrete platform or by a mechanical mixer, as directed by the Engineer.

Additives for controlling the setting and working characteristics of plaster or for imparting anticorrosion, fungicidal or water proofing properties, shall be added to the plaster strictly in accordance with the particular manufacturer's written instructions. Good quality hair or manila fiber in reasonably well distributed proportion may be to the plaster to assist application and reduce droppings. No additives shall be used except as specified in the Contract Documents

27.6 PREPARATION OF SURFACE TO BE PLASTERED

Plastering shall not commence until all electric conduits, drainage and sanitary pipes, inlets to tanks, brackets, clamps, doors and window frames and all sorts of inserts and embedded items are fixed in position. It shall be the responsibility of the Contractor to make sure that all such work is carried out by other contractors before starting of plaster work. Chiselling and repairing of cement plaster shall not be permitted without the approval of the Engineer.

Concrete surface to be plastered shall be cleaned to remove all grease, form oil and other surface impurities which will otherwise adversely affect the adhesion of plaster to the surface concerned. The surface of all concrete ceilings, beams and columns shall be lightly hacked by approved means to give the required key for plastering.

All masonry surface to be plastered shall be cleaned to remove all matter which will otherwise adversely affect the adhesion of plaster to the surface concerned. The surface shall be washed with clean water and kept damp for 24 hours before further treatment, the surface thus prepared shall be treated uniformly with cement and sand slurry. The slurry to be used shall be one-part cement to one-part sand by volume with water added to make a stiff. Spatter dash of slurry shall be applied on surface to receive plaster and be left to cure for three days.

27.7 APPLICATION OF PLASTER

The plaster of a thickness less than the specified thickness shall be rejected. If the plaster is to be more than ½-inch thick, it shall be done in two coats. The surface of first coat shall be made rough before the second coat is applied. Plaster shall not have wavy surface and shall be perfectly in plumb. The edges and corners shall represent a straight line. The plaster shall be kept wet continuously for at least ten days. No extra payment shall be allowed for jambs, junctions, corners, edges, round surfaces or plaster required due to any unevenness in the work done by the Contractor. The plaster work is to cover all conduits, pipes etc. fixed in the walls and ceiling. Wherever specified, metal lath shall be nailed firmly before plastering is commenced. The plaster surface shall be tested frequently with a 10-feet straight edge and plumb bob.

Plaster containing cracks, blisters, pits, discolouration or any defects shall not be acceptable. Any plaster giving hollow sound or loose plaster shall be removed and replaced with plaster in conformity with these specifications and as additionally directed by the Engineer. Contractor shall cut out and patch all defective work at his own cost. All damaged plaster shall be patched as directed by the Engineer. Patching plaster shall match appearance of and shall be finished level with adjoining plaster.

27.8 METAL LATH

Before plastering, wherever brick masonry meets with reinforced concrete members, 6-inch wide continuous strip of expanded metal lath shall be nailed to the masonry and the reinforced concrete member covering the point completely to prevent cracking of the joint

Metal lathing shall be fabricated from sheet steel, and shall be of uniform quality and tree from flaws broken strands, cracks and corrosive pitting, shall he rectangular and true to shape and shall comply with BS-1369.

All lathing shall be galvanized. Where plastering material depends entirely on the lathing for its key, these shall be not less than two complete mesh openings per 1.12-inch in one direction and the width of the aperture shall not be less than 0.2-inch.

Sheet shall be not less than 1.60 kg/m^2 when fabricated, using 0.7mm thick steel sheet. Where used on smooth surfaces to form a key, it shall be not less than 1.20 kg/m^2 when fabricated, using 0.5mm thick steel sheet. Typing wire shall be 1.2mm diameter galvanized annealed iron wire.

27.9 BEADS & PROFILES

Angle beads, corner beads, stop beads, architrave beads, depth gauge beads, edging profiles, plaster dividing profiles, interior angle profiles, plaster borders and the like shall all be manufactured from sheet steel and galvanized after fabrication, all beads & profiles shall be perforated at edges to ensure good adhesion of the plaster work. Thickness and dimensions shall suit particular locations and plaster work thickness.

Nails for fixing lathing shall be galvanized and have either clout heads or small flat heads to suit particular locations.

All angle beads, stop beads, architrave beads, depth gauge beads, and the like are to be fixed in accordance with the manufacturer's instructions.

27.10 CLEANING AND PROTECTION

Rubbish and debris shall be removed as necessary to make way for work of other trades and as directed by the Engineer. As each room or space is completed all rubbish, debris, scaffolding and tools should be removed to leave the room clean.

Prior to plastering, all doors/windows, finished metals etc. should be covered by sheet of plastic or tarpaulin to protect them from damage.

Protect finished, plaster from injury by any source. Contractor shall also protect walls, floors and work of other trades from plaster materials.

27.11 TOLERANCES

Surfaces of plaster work shall be finished with a true plane to correct line and level unless otherwise specified and with walls reveals plumb and square.

Maximum permitted tolerances shall not exceed 1/8-inch in 6-feet variation from plumb or level in any exposed line or surface and 1/16-inch variation between planes of abutting edges or ends.

27.12 POINTING WORK

Joints of masonry work to be pointed shall be properly raked to 1/2-inch depth, cleaned and wetted.

For struck pointing the mortar shall be filled in the joints flush with masonry with a pointing trowel and then pressed with proper pointing tools to form weathered and struck horizontal and triangular or V-notched vertical joints.

For flush pointing after pressing mortar in the joints these shall be tilled up with mortar and finished level with edges.

After pointing the face of the work shall be cleared of all surplus mortar. No washing shall be done till the pointing has set. All defects shall he treated at Contractor's expense. All work shall be kept wet for 10 days and protected from extreme temperatures and weather.

27.13 MEASUREMENT AND PAYMENT

27.13.1 Measurement

Except otherwise specified herein or elsewhere in the Contract Documents, no measurement and payment will be made for the under mentioned specified works related to the relevant items of the Bill of Quantities. The cost thereof shall be deemed to have been included in the quoted unit rate of the respective items of the Bill of Quantities.

- Metal lath over reinforced concrete and masonry joint.
- Joints, junctions, corners, drip course, edges and rounding.
- More than one layer due to any unevenness in the finished works.
- Cutting & patching of all defective works.
- Surface preparation, cleaning and protection as specified.
- Water proofing agent for water proof plaster.
- Angles beads, corner beads, stop beads, architrave beads, depth gauge edging profiles, plaster dividing profiles, interior angle profiles and plaster borders used in. plaster works as shown on Drawings.

Measurement shall be made of cement plastering for the actual area in square feet or square metre (whichever is included in Bill of Quantities) in accordance with this section of specification or as directed by the Engineer.

27.13.2 Payment

Payment shall be made for the number of square feet or square metre (whichever is included in Bill of Quantities) of surface area cement plastered at the contract unit price and shall constitute full compensation for furnishing all materials, equipment and labour including all incidentals necessary to complete the work in strict accordance with this section of specification.

SECTION-28 POLYVINYLECHLORIDE WATERSTOP

28.1 SCOPE OF WORK

The work comprises of providing all labour, tools, equipment, to install, place and fabricate in position and locations rubber water stops together with all jointing and sealing materials as per recommendations, specifications of the Manufacturer and instructions. All embodiment in concrete, lapping, turning, sealing shall ensure absolute water tightness subjected to any pressures. The workmanship and operation shall be perfect and guarantee leak proof at places wherever used in the structure.

28.2 MATERIAL REQUIREMENTS

Polyvinyl chloride water-stop shall be extruded from an elastomeric plastic compound, the basic resin of which shall be polyvinyl chloride (PVC). The compound shall contain such additional resins, plasticizers, stabilizers or other materials needed to ensure that when the material is compounded and extruded to the shapes and dimensions shown, it will have physical characteristics as included in Table 28.1.

Table 28.1, Material Requirements for PVC Water Stopper

Sr. No.	Parameter	Test Method	Criteria
1	Tensile Strength	ASTM C 638	Min. 1750 psi
2	Ultimate Elongation	ASTM C 638	Min. 350%
3	Low Temperature Brittleness	ASTM D 746	No Failure @ -37°C
4	Stiffness in Flexure	ASTM D 747	Min. 400 psi
5	Specific Gravity	ASTM D 792	Max. 1.37
6	Hardness, Shore A	ASTM D 2240	70-80

28.3 CONSTRUCTION REQUIREMENTS

Splices in the continuity or at the intersections of runs of PVC waters-stops shall be performed by heat sealing the adjacent surfaces in accordance with the manufacturer's recommendations or as directed. A thermostatically controlled electric source of heat shall be used to make all splices. The correct temperature at which splices should be made will differ with the material used but should be sufficient to melt but not char the plastic. After splicing, a remoulding iron with ribs and corrugations to match the pattern of the water-stop shall be used to reform the ribs at the splice. The continuity of the characteristic components of the cross-section of the water-stop design (ribs, tabular centre axis, protrusions, and the like) shall be maintained across the splice.

The expansion joints wherever indicated on Drawings shall have centre bulb rubber water stops or its equivalent as indicated on Drawings to be cast

integrally with the in-situ-concrete of retaining walls, beams, columns, slabs or at any locations marked on the Drawings incorporating junction places or as straight lengths with separate intersection pieces to be jointed at Site as per Manufacturer's recommendations and Specifications. The water stops shall be installed so as to hold them securely in their correct position during the placement of concrete. The concrete shall be fully and properly compacted around the water stops to ensure that no voids or porous areas remain. Where reinforcement is present adequate clearance shall be left between water stops and the reinforcement to permit proper compaction of concrete. No holes shall be made through any water stops. Hot or cold vulcanizing for jointing places of water-stops at site shall be done with the prior Approval in accordance with the Manufacturer's recommendations and specifications.

28.4 MEASUREMENT AND PAYMENT

28.4.1 Measurement

Polyvinylchloride water stop of the size and gauge as shown on the Drawings will be measured for the number of linear feet or linear metre (whichever is included in Bill of Quantities) acceptably placed in the work. In computing the quantities, no allowance will be made for laps.

28.4.2 Payment

Payment will be made in accordance with the unit prices in the Bill of Quantities for the item as measured above in accordance with the specifications and shall constitute full compensation for furnishing all materials, shuttering, equipment and labour and for performing all operation necessary to complete the work.

SECTION-29 ALUMINIUM WORKS

29.1 SCOPE OF WORK

The work under this section of specification includes furnishing all labour, equipment, appliances and materials and performing all operations in carrying out the work of anodized aluminium doors, windows (other than curtain wall type doors and windows) ventilators, louver and fly screen. All related items such as sealants, rubber gasket for glazing, netting, rollers, latches, fastenings, glazing, anchor bolts and all items supplied by other trades and customarily built in and/or installed in strict accordance with this section of the specifications and the applicable Drawings and subject to the terms and conditions of the Contract.

29.2 APPLICABLE STANDARDS

The work shall conform to requirements of latest editions of following standards, wherever applicable, unless otherwise specified.

29.2.1 ISO (International Organization for Standardization)

- ISO 1804, Doors Terminology
- ISO 6442, Door leaves, Measurement of defects of general flatness.
- ISO 6443, Door leaves, Measurement of dimensions and defects of squareness.
- ISO 6444, Door Leaves, Test of behaviour under humidity variations (successive uniform climates)
- ISO 6612, Windows & Doors, Wind resistance tests.
- ISO 6613, Windows & Doors, Air permeability test.

29.2.2 BSI (British Standard Institution)

- BS 1227, Hinges
- BS 4873, Aluminium alloy windows.

29.3 GENERAL

Aluminium doors and windows shall be of profile, pattern and design shown on Drawings and manufactured by reputable manufacturer approved by the Engineer. The contractor shall provide manufacture literature completely describing the product, instructions for installation and maintenance.

All the sections used for doors, windows, ventilators & fly screens shall be of best quality aluminium products such as equal and unequal angles, channels, tubes, corrugated strips, mouldings etc., in accordance with International standards conforming to ASTM B 308 & B 221.

All doors, windows & ventilators shall be of type and size indicated on Drawings and shall conform to the requirements shown and specified herein.

Contractor shall arrange tests and analysis if directed by the Engineer of scaled models of each window type at the maker's works or any laboratory specified by the Engineer for the material supplied by him to be tested in the presence of the Engineer's Inspector, to whom test certificates, proof sheets, etc. shall be furnished. The models shall be submitted to the Engineer for approval prior to testing. Nevertheless, neither the fact that the materials have been tested in the presence of the inspector nor that the Engineer may have been furnished with test certificates in lieu of sending an inspector to the works shall affect the liberty of the Engineer to reject, after delivery of materials found not in accordance with these specifications.

The contractor shall submit shop drawings which shall show full construction details, quantities. and locations, fastenings and attachment to adjacent construction and materials. Shop drawings shall be submitted at the proper time to allow for checking, revisions, agreement and permit manufacturer's product delivery and start of site work to suit the building programme. The Contractor shall submit representative samples of finished windows, anchoring mechanism, embedded parts, fastenings, glass panes, accessories and other materials for the Engineering approval.

After approval of shop drawings and tests etc., the contractor shall submit at his own cost one mock-up sample of each type of aluminium works complete with glazing, all components assembly method and required fittings and accessories prior to be actual fabrication of the bulk. The samples shall be returned to the contractor for incorporation in the works after installation of at least 80% of the works.

Fabricate and assemble all work in the shop of the approved manufacturer to reduce field fabrication to a minimum unless otherwise directed by the Engineer.

The glass shall conform to specification laid down under section 'Glazing' and shall be free from all blemishes, bubbles, distortions and other flaws of any kind and shall be properly cut to size as shown on Drawings, so as to fit the grooves in door and window members. All the glass shall be best quality of approved manufacture.

The structural shape of the Aluminium members shall be of uniform quality, colour and temper, clean, round, commercially straight and free from injurious defects.

All doors, windows and ventilators shall be fabricated as a complete unit, fully airtight and watertight, including rubber gasket for glazing, rollers, latch, anodized in specified colour, inclusive of glass sheet, necessary holes for fixing, door locks, door closures and window locking requirements, all as

approved by the Engineer.

Contractor shall, on request, get certificate signed by the manufacturer stating that each lot has been sampled, tested and inspected and has met the requirements in accordance with these specifications, and the same shall be furnished to the Engineer.

29.4 MATERIAL REQUIREMENTS

The frames/shutters of anodized aluminium doors, windows, ventilator and louvers shall be formed from rolled, strip or extruded aluminium and be as per Drawings. Fastenings bolts and screws shall be made from hardened aluminium.

Fasteners shall be stainless steel of a type selected to prevent galvanic action with the components fastened.

Gaskets shall be vinyl glazing channel gasket to commercial standard CS-230-60.

Hardware shall be manufacturer's standard hardware flush to match door and windows finish Joint sealant shall be approved elastomer.

The finish shall be in approved colour in accordance with the standards of Aluminium Association.

Minimum coating should not be less than 23-25 micron.

29.5 WORKMANSHIP

The Contractor shall be responsible for the protection and installation of all items furnished. All items shall be installed plumb and square and shall be solidly anchored in a good workman like manner in accordance with the manufacturer's instruction and as specified herein. The Contractor shall be responsible for the protection of installed items from damage by other trades. All items shall be left in operating, neat and clean condition, free from dirt, finger marks, etc. The Contractor shall be responsible for final cleaning before the final acceptance.

The glass panes shall firmly be secured in the rebates with the rubber gasket. Ensure that the beads and grooves are clean, dry and unobstructed at the time of glazing. The complete unit shall be airtight and watertight on completion. No doors windows ventilator louvers shall be considered complete until and unless the finger prints and other stains and marks have been removed from the surface of glass and aluminium.

29.6 PRODUCT DELIVERY AND STORAGE

Deliver doors, windows, ventilator and louvers in a manner preventing damage to units. Store materials off the ground under cover in a manner preventing deterioration or damage.

All embedded parts and anchor bolts shall be delivered to the site carefully and keeping the fabricated shape and configuration. All these parts shall be suitably marked for identification.

29.7 ERECTION

Rawl plugs and anchoring bolts shall he embedded into the concrete or block masonry for holding the doors, windows, ventilators and louvers in their correct positions.

Care shall be taken to install the doors and windows, ventilators and louvers in line and plumb & solidly anchored in a workman like manner in accordance with the Drawings. Should any scale or scratch appear on the surface of doors, windows, ventilators and louvers the contractor shall at his own expense and at the Engineer's direction have all exposed surfaces cleaned to bare bright specified

All works shall be installed in strict accordance with the manufacturer's instructions.

29.8 PROTECTION AND CLEANING

Temporary protection shall be achieved by applying water soluble protective coating capable of withstanding the action of lime mortar.

Apply coating in the manufacturer's plant to the exposed surfaces of all components.

Before application of coating, remove all fabrication compounds, moisture and dirt accumulations.

29.9 DEFECTIVE WORK

In the event of non-conformance to specifications and Drawings the aluminium work shall be rejected by the Engineer and the Contractor shall remove and replace the rejected works by new work of same specifications.

29.10 GUARANTEE

The manufacturer shall furnish his standard written guarantee against leakage of rain, excessive infiltration of dust and air and all defects in materials and workmanship covering all work under this section.

Such guarantee shall be in addition to and not in lieu of all other liabilities which manufacturers and the Contractor may have by law or by other provisions of the Contract Documents.

29.11 MEASUREMENT AND PAYMENT

29.11.1 Measurement

Measurement and payment for doors, windows, and ventilators shall be in

square feet or square metre (whichever is included in Bill of Quantities) of net openings in the walls where aluminium doors, windows and ventilators have been acceptably fixed complete including glazing, in all respects as per relevant Drawings or as directed by the Engineer.

29.11.2 Payment

Payment shall be made on the basis of measurement as measured above at the contract unit price for all supply of items and means of fixing, cutting, shaping, glazing, and all other operations required for the complete erection and commissioning to the full satisfaction of the Engineer.

SECTION-30 GLAZING

30.1 SCOPE OF WORK

The work under this section of the specifications consists of furnishing all labour, equipment, tools, appliances, scaffoldings and providing glass gaskets, sealants, compound and other materials required for performing all operations in connection with the installation and setting of all types of glass, glazing and glass blocks complete in every respect in accordance with the Drawings or as directed by the Engineer.

30.2 APPLICABLE STANDARDS

The work shall conform to requirements of latest editions of following standards, wherever applicable, unless otherwise specified:

- BS-952, Glass for glazing
- BS-5051, Security glazing Part I & II
- CP-152, Glazing

30.3 SUBMITTALS

Contractor shall submit samples for each type of glass, minimum 12-inch x 12-inch in size with protective edges. Samples of glazing sealant minimum 0.1 litre specified types shall be submitted. Samples of minimum of three glass blocks shall also be submitted.

Contractor shall submit 12-inch long sample each type of glazing gasket.

Contractor shall also submit printed materials manufacturers installation instructions for specified glazing gaskets, compounds sealants and accessories including description of required equipment and procedures and precautions to be observed.

30.4 MATERIAL REQUIREMENTS

30.4.1 General

Glass shall be free from all blemishes, bubbles, distortions and other flaws of any kind and shall be properly cut to fit the rebates so as to have a uniform clearance of 1.6 mm round the panes between the edges of glass and the rebates. All glass shall be of best quality manufacture as approved by the Engineer.

Each type of glass shall have the manufacturer's label on each pane, and the labels shall remain on the glass until final cleaning.

Spacer shims (distance pieces) shall he plasticized polyvinyl chloride (PVC). Thickness shall be equal to space shown on Drawings between glass and rebates, bead or cleat. Depth shall give not less than ¼ inch cover of glazing sealant.

30.4.2 Glass

Glass for windows and ventilators and louvers shall be of thickness and size as shown on the Drawings of approved quality.

a. Plain / Tinted Glass.

Glass for doors and windows shall be Local Float Glass where the sheet glass is to be used and for double glazing imported order made double layer vacuum glass of appropriate thickness tinted as selected and as approved by the Project Manager.

b. PSG Heat-strengthened glass or PSG Tempered glass

It is manufactured by heating up flat glass to a temperature of around 700°C and then blowing air on to its surface, quenching it down swiftly and uniformly. It can be divided into two types depending on the degree of heat treatment, heat-strengthened glass or tempered glass. PSG heat-strengthened glass in manufactured by controlling the tensile stress caused by heat treatment process with in a certain range of temperature. PSG tempered glass has an impact strength which is 5 times higher than that of the annealed flat glass of the same thickness, as well as 3 to 4 times higher resistance to weight.

30.4.3 Rubber Acrylic Glazing Sealant

Contractor shall provide material coloured to match frame in which glass is installed. Provide only compounds known to be fully compatible with surfaces which they will contact as follows:

- Two component polysulfide glazing sealant.
- One component acrylic glazing sealant.
- Acrylic-latex glazing sealant consisting of modified latex rubber and acrylic emulsion, non-hardening, non-staining and non-bleeding.
- Cleaners, Primers and sealer as recommended by the sealant manufacturer.

30.4.4 Accessories

a. Vinyl Glazing Bead

It shall be for external windows and entry doors and shall be in accordance with glass manufacturer's recommendation.

b. Glazing Sealant

It shall be tape or ribbon of polymerized butyl or mixture of butyl and polyisobutylene compounded with inert fillers and pigments, solvent based, 95 percent solids thread or fabric reinforced, paintable, non-staining.

c. Setting Blocks

It shall be chloroprene (Neoprene) 70 to 90 durometer hardness, compatible with sealant used, channel shaped and of the necessary height for proper perimeter clearance.

d. Channels. Gaskets and Spacer's

It shall be chloroprene (Neoprene), 40 to 50 durometer hardness compatible with sealant used.

30.5 DELIVERY, STORAGE AND HANDLING

Contractor shall deliver materials in manufacturers original, unopened containers clearly labelled with manufacturer's name and address, material, brand, type, class and rating as applicable. Contractor shall store the materials in original unopened containers with labels intact/protected from ground contact and from elements which may damage glass. Contractor shall handle the materials in a manner to prevent breakage of glass and damage to surfaces.

30.6 INSTALLATION OF GLAZING

Glazing shall comply with the recommendations of glass and glazing materials manufacturers.

Examine each piece of glass and discard and replace glass with edge damage or face imperfection. All glazing shall be wind tight and fully water tight on completion.

Clean glazing channels and other framing members indicated to receive glass. Remove coatings which are not firmly bonded to the substrate. Remove lacquer from metal surfaces wherever electrometric sealants are to be used. Apply primer and sealer to joint surfaces wherever recommended by the sealant manufacturer and as shown on the Drawings.

Trim and clean excess glazing materials from surrounding surfaces immediately after installation and eliminate stains and discolorations.

Cure glazing sealants and compounds in compliance with manufacturer's instructions to obtain high early bond strength internal cohesive strength and surface durability.

While glazing operation is in progress care shall be taken to avoid breakage or damage to the glass and adjoining glazing. The Contractor shall make good at his own cost, all glass broken by his workmen while cleaning or carrying out other operations. On the completion of the glazing work, all glass that has been set by the Contractor shall, if it becomes loose, within the maintenance period, be re-fixed at Contractor's expense.

No glazing shall be considered complete until and unless paint and other stains have been removed from the surface of the glass and checked by the Engineer for water tightness.

30.7 PROTECTION AND CLEANING OF GLAZING

Remove all smears, labels and excess glazing sealant, leave clean inside and outside tree from scratches. The Contractor shall be responsible for the protection of installed glass. Before final acceptance, damaged or broken glass shall be removed and replaced with new glass at no additional expense to the Employer. All glass surfaces shall be washed clean both inside and outside within two weeks prior to final acceptance by the Employer.

30.8 MEASUREMENT AND PAYMENT

30.8.1 Measurement

No separate measurement shall be made of glazing of doors/windows, ventilators.

30.8.2 Payment

No separate payment, unless otherwise included in the bill of quantities, shall be made for doors, windows, and ventilators.

SECTION-31 PAINTING

31.1 SCOPE OF WORK

The work under this section of the specifications consists of furnishing all materials, plant, labour, equipment, appliances and performing all operations in connection with surface preparation, mixing, painting concrete works, plaster works, gates, frames, walls, ceilings and all such surfaces as shown on the Drawings and/or as directed by the Engineer.

31.2 APPLICABLE STANDARDS

Latest editions of following British Standards are relevant to these specifications, wherever applicable:

- BS 245, Specification for mineral solvents (white spirits and related hydrocarbon solvents) for paints and other purposes
- BS 2521, Lead-based priming paint for woodwork
- BS 2523, Lead based priming paint for iron and steel
- BS 2569, Sprayed metal coatings
- BS 4800, Paint colours for building purposes
- CP 231, Painting of building
- CP 3012, Cleaning and preparation of metal surfaces

31.3 GENERAL

Except as otherwise specified, all painting shall be applied in conformity with BS CP 231 "Painting of Building" as applicable to the work.

The Contractor shall repair at his own expense all damaged or defective areas of shop-painted metal works and structural steelwork. Metal surfaces against which concrete to be placed will be furnished shop-painted and shall cleaned prior to being embedded in concrete.

Except as otherwise specified, all concrete and plastered surfaces are to be painted.

The Engineer will furnish a schedule of colours for each area and surface. All colours shall be mixed in accordance with the manufacturer's instructions.

Colours of priming coat and body coat where specified, shall be lighter than those of finish coat. The Engineer shall have unlimited choice of colours.

Samples of all colours, and finishes shall be prepared in advance of requirement so as not to delay work and shall be submitted to the Engineer for approval before any work is commenced. Any work done without such approval shall be redone to the Engineer's satisfaction, without additional expense to the Employer. Samples of each type of paint shall be on separate 1-ft. x 1-ft. x 1/8-inch tempered hard board panels. Manufacturer's colour

chart shall be submitted for colour specifications and selection.

31.4 MATERIAL REQUIREMENTS

All materials shall be acceptable, proven, first grade products and shall meet or exceed the minimum standards of approved manufacturers.

Colours shall be pure, non-fading pigments, mildew-proof sun-proof, finely ground in approved medium. Colours used on plaster and concrete surfaces shall be lime-proof. All materials shall be subject to the Engineer's approval.

The plastic emulsion/weather shield paint or similar as approved by the Engineer shall be used where specified on the drawing as directed by the Engineer.

The synthetic enamel paints and primers for structural steel or metal works shall be the best available for its type and shall be approved by the Engineer prior to its procurement.

All material shall be delivered to site in their original unbroken containers or packages and beef the manufacturer's name, label, brand and formula and will be mixed and applied in accordance with his directions.

31.5 DELIVERY STORAGE AND CONTAINER SIZES

Paints shall be delivered to the site in sealed containers which plainly show the type of paint, colour (formula or specifications number) batch number, quantity, and date of manufacture, name of manufacturer and instructions for use. Pigmented paints shall be supplied in containers not larger than 20 litres. All materials shall be stored under cover in a clean storage space which should be accessible at all times to the Engineer. If storage is allowed inside the building, floors shall be kept clean and free from paint spillage.

31.6 SURFACE PREPARATION

All oil, grease, dirt, dust, loose mill scale and any other foreign substance shall be removed from the surface to be painted, polished and white washed by the use of a solvent and clean wiping material. Following the solvent cleaning, the surfaces shall be cleaned by scrapping, chipping. blasting, wire brushing or other effective means as approved by the Engineer.

In the event the surfaces become otherwise contaminated in the interval between cleaning and painting, recleaning will be done by the Contractor at no additional cost.

All the surfaces to be painted shall be free from dust, dirt, fungus, lichen, algae etc. Oil paint, varnish and lime wash should always be removed by scraping and washing.

No work in this section shall be allowed until all surfaces or conditions have been inspected and approved by the Engineer.

31.7 APPLICATION

All paint and coating materials shall be in a thoroughly mixed condition at the time of application. All work shall be done in a workman like manner, leaving the finished surface free from drips, ridges, waves, laps, and brush marks. All paints shall be applied under dry and dust free condition unless approved by the Engineer. Paint shall not be applied when the temperature of the metal or of the surrounding air is below 7 degrees centigrade. Surfaces shall be free from moisture at the time of painting.

All primary paint shall be applied by brushing. The first coat of paint shall be applied immediately after cleaning. When paint is applied by spraying, suitable measures shall be taken to prevent segregation of the paint in the container during painting operation.

Effective means shall be adopted for removing all free oil and moisture from the air supply lines of the spraying equipment.

Each coat of paint shall be allowed to dry or harden thoroughly before the succeeding coat is applied. Surfaces to be painted that will be inaccessible after installation shall be completely painted prior to installation.

Only as much material should be mixed as can be used up in one hour. Over-thinning will not be permitted. After the first coat the surfaces will be soaked evenly four or five times and the second coat shall be applied after leaving for at least overnight.

Where shown on Drawings all exterior finishes shall be painted with weather resistant paint in approved colours as per manufacturer's specifications.

Plastic emulsion paint of the approved make and shade shall be applied to surfaces as shown on Drawings or as specified by the Engineer.

Polyvinyl Distemper of the approved make and shade shall be applied to surfaces as specified.

31.8 FINISHES

The finished coating film shall show uniform coverage throughout and shall be reasonably free from brush marks, runs, sags or noticeable colour variations. Edges, where coating ends, change colour or change thickness shall be clean and straight.

The completed coating shall be compared with sample areas. The completed coating shall be at least as smooth (free from orange feel effect, overspray, embedded or partially embedded particles, craters, pinholes, holes etc.) as the approved sample areas.

The thickness of the coating shall be checked by the Engineer at random locations by cutting out sections on concrete or plaster surfaces. The cut-out sections shall be patched by the contractor, using the same material and

thickness used originally. Porosities shall be marked and patched with the basic primer material or with a mixture of basic primer material and finely divided filler or with a proprietary patching compound compatible with coating. Any moisture on the surface of the coating shall be allowed to dry thoroughly before patching. In addition, all porosities and imperfections which become evident after applying subsequent coats shall be repaired. This repairing shall be done with basic coating material or with a proprietary patching compound compatible with specific coating, except for the top coat, where only basic coating material shall be used. The completed coating shall be free of porosity visible to the naked eye.

31.9 JOB CONDITIONS

Observe manufacturer's recommended minimum and maximum temperature but do not apply paint or finish to any surface unless ambient temperature is 10°C or above and less than 43°C. Non painting shall be done above 90% relative humidity.

Adequately protect all finished work.

Remove and replace all items of finish hardware, device plates, accessories, lighting fixtures or other removable items.

In no case shall any finish hardware or other finished item that is already fitted into place be painted, unless otherwise specified.

31.10 QUALITY ASSURANCE

All paint for any one surface shall be top quality, of one manufacturer of the specified. Deep tone accent colours shall be used and the unavailability of final coat colours may be the basis for rejecting materials for any one surface.

31.11 MEASUREMENT AND PAYMENT

31.11.1 Measurement

Measurement for painting shall be made in square feet or square metre (whichever is included in Bill of Quantities) of painted area acceptably completed in all respects as per Drawings and in strict accordance with this section of specification or as directed by the Engineer.

31.11.2 Payment

Payment will be made for the number of square feet or square metre (whichever is included in Bill of Quantities) of painted area measured as above at the Contract unit price and shall constitute full compensation for all work and all other incidentals to complete the work.

SECTION-32 CERAMIC TILE WORK

32.1 SCOPE OF WORK

The work covered under this section comprises of providing and laying best quality local made glazed/matt ceramic tiles of approved size and pattern wherever required or shown on the Drawings or mentioned in the Bill of Quantities.

32.2 MATERIAL REQUIREMENTS

32.2.1 General

The work shall conform to requirements of latest editions of following standards, wherever applicable, unless otherwise specified:

- BS 1281, Glazed ceramic tiles and tile fittings for internal wall
- BS CP 212, Fixing methods and workmanship.

32.2.2 Joint Filling

Joint Filler shall be white Portland cement grout which shall bond to dry tile, shall be non-shrinking, stain resistant, permanent in colour, and shall not inhabit fungus and bacterial growth. It shall be odourless and non-toxic, of smooth consistency for easy preparation and neat, rapid installation, and shall contain non-metallic material. Grout shall be water resistant and shall not wash out under water.

32.2.3 Adhesives

Adhesives for ceramic tiling as specified in the British Code of Practice CP 212 or Dry Bond Floor and wall thin set mortar as manufactured by Shabbir Tile and Ceramics Limited or equivalent approved.

32.2.4 Samples and Tests

The samples shall be furnished in sizes and colours and adequate in number for testing in an approved laboratory.

32.3 WORKING DRAWINGS

The Contractor shall prepare working Drawings on the basis of working Drawings for all the ceramic tile work to be carried out. These Drawings will show clearly the sizes, method of fixing, jointing and the anchorage to be used in the process and the Contractor shall get approval in writing well in time before the actual start of the work.

32.4 CONSTRUCTION REQUIREMENTS

32.4.1 In Cement Sand Mortar

Surfaces to receive the ceramic tiling shall be clean and free of dirt, dust, oil, grease or other objectionable matter. Setting beds and tile shall be installed

with their respective surfaces to true planes, level or pitched to off-sets as required by the Drawings, so that the surface of the completed tiling work will be at the elevations and grades shown. Re-tempering of mortar will not be permitted. Tiles shall be laid out from the centre lines of each space outward and adjustments made along walls, partitions and borders, if any, so as to symmetries the pattern with a minimum of cut tiles.

Joint between tiles shall be of uniform width and the same as the tile installed. Fractional changes in dimensions without varying the uniformity of joint widths shall be permitted. Tile shall be cut with a suitable cutting tool and rough edges shall be rubbed smooth. Cut-tile misfits shall be laid to the straight edges. Straight edges shall be accurately set to the lines established and reset at suitable intervals to keep the joints parallel over the entire area.

Over the existing bed a topping of 1-1/2" thick PCC 1:2:4 shall be laid. Scratch coats for application as foundation coats shall be not less than 5/8" thick and shall be composed by volume of 1-part Grey Portland Cement to 3 parts dry sand, mixed with the minimum amount of water necessary to produce a workable mass. Mortar for scratch coats shall be used within one hour after mixing and re-tempering will not be permitted. Scratch coats shall be applied in sufficient quantity and with sufficient pressure to cover the entire area and to form good keys, shall be deeply scoured or scratched and cross-scratched, shall be protected and kept moist during the curing period. Scratch coats shall be thoroughly damp-cured, and an interval of not less than 24 nor more than 48 hours shall be permitted between application of scratch coats and application of float coats.

Float coats shall be composed by volume of 1-part Grey Portland cement to 2 parts dry sand, mixed with a minimum amount of water necessary to produce a workable mass. Float coats shall be applied in sufficient quantity to entire area and to form a good key, shall be brought out flush with the temporary screeds or guide strips so placed as to give a true even surface at the proper distance from the finish suitable for reception of tiles.

Joints shall be straight, level perpendicular and of even width throughout. Vertical joints shall be maintained plumb for the entire height of the tile work. Each tile shall be brought to true level and plane by uniformly applied pressure under a straight edge or rubber faced block. Tiles that are out of true plane or misplaced shall be removed and reset. Damaged or defective tile shall be replaced. The tile shall be installed as follows:

- Wall tile shall be set by trowelling a skim coat of neat Portland cement on the float coat or by applying a skim coat to the back of each tile unit and immediately floating the tile into place. After tile has set remove mortar using a minimum of water. Replace damage tiles.
- After the tiles have been thoroughly set, joints shall be grouted full

with a plastic mix of neat, white cement immediately after a suitable area of tile has been set. The joints shall be struck flush and excess mortar shall be cut off and wiped from the mortar joints after grout has been cleaned from the surface shall be roughened at once and filled flush with the tile edge, before the mortar begins to harden. Tile skirting and coves shall be solidly backed with mortar.

32.4.2 In Thin Set Mortar

Tiles laid in Thin Set Mortar shall be applied as per details shown on Drawings and shall consist of a P.C.C. base of specified thickness. Tiles shall be set by trowelling a skin coat of Dry Bond Mortar on the base coat and combed with a notched edge of trowel. Back butter each tile unit to ensure 100% mortar coverage and float the tile into place, tapping the tile to ensure maximum bond strength. All other installation requirements shall be as per specifications mentioned above.

32.5 MEASUREMENT AND PAYMENT

32.5.1 Measurement

Measurement shall be made in square feet or square metre (whichever is included in Bill of Quantities) of ceramic tile work acceptably placed complete in all respects as per Drawings and in strict accordance with this section of specification or as directed by the Engineer.

32.5.2 Payment

Payment will be made for the number of square feet or square metre (whichever is included in Bill of Quantities) of ceramic tile work as above at the contract unit price and shall constitute full compensation for all work including material, labour, plant, equipment, and all other incidentals to complete the work.

SECTION-33 TERRAZZO WORK

33.1 SCOPE OF WORK

The work covered by this section of the specifications, consist of furnishing all plant, labour, equipment, appliances and materials and in performing all operations complete in strict accordance with this section of the specifications and the applicable drawings and subject to the terms and conditions of the contract. The work under the section include precast terrazzo tiles flooring and in situ terrazzo flooring, dada or skiting.

33.2 APPLICABLE STANDARDS

Unless otherwise specified, terrazzo work shall be in conformity with British standard Code of Practice C.P. 204 In Situ Flooring Part 1, 'General' and Part 3 "Terrazzo Flooring" as applicable to the work shown on the Drawings and specified in the Bill of Quantifies.

33.3 SUBMITTALS

All materials used for terrazzo work shall be submitted to the Engineer for obtained approval. Same materials should also be tested and this shall be got done by the Contractor at its own expense from a laboratory approved by the Engineer.

33.4 MATERIAL REQUIREMENTS

Cement, Sand, Aggregate and Water for Concrete shall conform to specification as included in SECTION-20 PLAIN & REINFORCED CONCRETE.

Marble Chips shall be crushed marble and shall be best quality white or coloured sound and hard local marble chips approved by the Engineer and of the as mentioned in the Bill of Quantities or as required by the Engineer.

Dividing Strips shall be glass, brass or marble strips 4-5 mm thick and 1-1/2" wide or as specified in the Bill of Quantities.

Angle Clips for precast toilet partitions shall be chromium plated steel or stainless steel clips as shown on drawings.

Bolts of precast toilet partitions shall be 5/16" inch bars bolts chrome-plated, with acorn heads, fitted to wall anchors.

Terrazzo Tiles Terrazzo tiles shall be first grade, mechanically compressed type conforming to PS-531. Tiles shall be 12"x12"x0.88" / 30.0x30.0x2.2cm with a toping of 0.4" or 10.00mm thickness composed of 1:2 cement & marble chips. The base being 1:3 cement mortar. The colour, quality and size of chips shall be as per Project Manager's approval.

The Compound used for all cleaning of terrazzo shall be an approved neutral chemical cleaner free from acid and alkali or any other material that will

affect the colour or otherwise damage the terrazzo and shall not affect the conductivity of terrazzo floors.

33.5 EXECUTION

33.5.1 In Situ Terrazzo Flooring

The floor shall consist of a wearing surface to consistency and net thickness as specified in Bill of Quantities, laid over 1:2:4 under bedding concrete of the specified thickness. The net uniform thickness specified for wearing surface shall be that obtained after grinding and polishing. The 1:2:4 concrete shall be mixed and laid in the manner specified for cement concrete floor using a minimum quantity of water.

The concrete shall be levelled with a trowel and straight edge consolidated and finished with steel trowels to an even but rough surfaces. The top layer of cement and marble chips mixed in the proportion of 1:2 (1 cement and 2 marble chips) shall be laid over it within 12 hours. The cement and marble chips must be mixed dry in such quantities that are sufficient for a unit area of one specified shade. Water shall be added to only such quantities that can be mixed thoroughly and consumed in less than 30 minutes, the quantity of water being the minimum for workability.

Mixing must to be done on water tight platform and any mix not used within 30 minutes shall be discarded and removed from the Site. A layer of cement and marble chipping mixture should be well trowelled into the surface of the base concrete before filling to the top level of the screeds. The layer should be well compacted and all voids shall be filled in. A layer of neat cement, of the specified colour shall then be well-trowelled into a plain smooth surface. Floors shall be laid in panels of sizes as shown on drawings and in Bill of Quantities or as directed by the Project Manager. Dividing strips, as specified shall be provided and fixed to exact levels making an allowance for grinding.

Three days after laying, the top layer must be evenly and smoothly machine ground with Carborundum blocks of coarse, medium and fine grades so as to ensure that all marble chipping are evenly exposed all over the surface.

If marble chips are not evenly exposed the Contractor shall pull down the sin face and relay it at his own cost. The surface after grinding shall be left undisturbed and cured for 2 to 3 weeks after which it shall be cleaned of dirt and dust gently by rubbing with pumise stone or washing soda in sufficient water. Three days after the surface has been cleaned, it shall be rubbed hard with 1:10 solution of oxalic acid using fell. The surface shall then be cleaned and washed with plenty of water. After the surface has dried a final gloss shall be given by polishing surface to the satisfaction of the Project Manager.

33.5.2 Terrazzo Dado & Skirting

marble chips and cement shall conform to specifications for floor. Mixing shall

be done in the same manner and proportion. The plastered surface over which the dado/skirting is to be applied shall be well roughened and watered, cement mortal of specified ratio shall then be plastered over this well roughened surface to indicated thickness. Before the base course had set, the layer of terrazzo mixture of the specifications for flooring shall be well trowelled into the surface of the base to a thickness which after, grinding shall result in the finished thickness as per Bill of Quantities. A layer of neat cement of the specified colour shall then he well trowelled into the surface leaving a plain smooth surface. After 24 hours the Contractor shall start finishing as for floors specified above, Terrazzo skirting shall be provided around all terrazzo floors unless otherwise shown. Skirting and dado shall be straight, level and in plumb. Intersections at floors shall be straight and flush. They shall be with 1/4 radius coved at floor unless otherwise shown.

33.5.3 Terrazzo on Stairs

The stair risers and treads shall be finished according to exact sizes including the terrazzo making allowance for grinding of terrazzo.

33.5.4 Terrazzo Finished Precast Partitions of Urinals

Partitions walls of urinals shall be precast R.C.C. slabs finished will) l/'l" thick polished terrazzo on both faces. The finished thickness of these walls shall be 3" or as shown on drawings and BOQ R.C.C. slab shall conform to the specification for "Concrete" and terrazzo as per this section. Fixing of these partitions of floor walls. etc. shall be as directed by the Project Manager and as shown on Drawings.

33.5.5 Terrazzo Tile Works

The terrazzo tiles will be laid to the required levels and grades over a bedding of cement mortar comprising of 1 part of cement and 3 parts of sand by volume. I thickness of cement sand bedding screed shall be as per Bill of Quantities.

The curing period of the bedding shall be as directed by the Project Manager. As large an area of bedding shall be spread at one time as can be covered with tiles before the mortar has set. Surplus mortar shall be removed. The thickness of bedding in any space shall not be less than 1/2" / 12.5mm.

Floor and wall surfaces to receive the tiles shall be thoroughly cleaned of all dirt, dust, oil and other objectionable matters. Tiles shall be laid out from the Centre line of each space in an outward direction and the pattern should be made symmetrical with a minimum number of cut tiles. Joints between the tiles shall be of uniform width. Tiles shall be cut with a suitable cutting tool and rough edges shall be nibbed smooth. Tiles shall be laid to the straight edges.

After seven days the terrazzo tile floors shall be machine ground to a true

even surface using various grades of abrasive stones as required and directed by the Project Manager. After the first grinding the floor shall be grouted with the same colour composition as used for its manufacture. The grout shall be of the consistency of thick cream and shall be brushed over the floor to fill in the joints and after 72 hours the grouting coat shall be removed by grinding till a smooth and even surface is obtained. Area and portion of the floor inaccessible for the grinding machine shall be ground and rubbed by hand. The final gloss shall be given by polishing the surface to the satisfaction of the Project Manager.

The tiled floor shall be kept wet for at least 72 hours and no one should be allowed to walk on the tiles during that period.

33.6 MEASUREMENTS & PAYMENTS

33.6.1 Measurement

Except otherwise specified herein or elsewhere in the Contract Documents, no measurement and payment will be made for the under mentioned specified works related to the relevant items of the Bill of Quantities. The cost thereof shall be deemed to have been included in the quoted unit rate of the respective items of the Bill of Quantities.

- Grinding, washing polishing and finishing of Terrazzo work.
- Under bedding and screening.
- Preparation of concrete surface for Terrazzo works.
- Cement concrete base.

Measurement shall be made of cement plastering for the actual area in square feet or square metre (whichever is included in Bill of Quantities) in accordance with this section of specification or as directed by the Engineer.

33.6.2 Payment

Payment shall be made for the number of square feet or square metre (whichever is included in Bill of Quantities) of acceptable measured quantify of Terrazzo Work at the contract unit price quoted in the Bill of Quantities and shall constitute full compensation for furnishing all materials, equipment and labour including all incidentals necessary to complete the work in strict accordance with this section of specification.

SECTION-34 DETAILED TECHNICAL SPECIFICATIONS (DTS) FOR ELECTRICAL WORKS AND DG SETS

34.1 SCOPE OF WORK:

1.1. The scope of services covers the design, detailed engineering, preparation of construction drawing, manufacture, acceptance testing at manufacturer's works or at any accredited agency, supply, packing, forwarding and delivery from manufacturer's works/ place of storage to erection site including transit insurance, unloading, storage at site, moving from place of storage to place of installation, assembly, erection, testing, commissioning & performance demonstration and handing over along with all necessary spares of original ratings & specifications on Design, Build & Operate basis. Inland and overseas transit insurance, transport, testing at site shall be Contractor scope. Tender Bill of Quantities (BOQ) and Drawings are for reference purpose only which is the minimum requirements for the water supply system including raw water Intake, various Headwork/ Sub-Headwork with/ without water treatment facility as applicable; Contractor to ensure that design & equipments are as per specification requirements.

1.2. The Contractor shall prepare design calculations based on parameters/ design criteria indicated in the specifications. The Contractor shall prepare detailed engineering and construction purpose drawings to make his/ her own estimate of ratings & quantities (minimum requirements as per price schedule, technical data sheets, reference drawings & other relevant details) for entire electrical systems including all items, systems such as equipments, cables/ cabling system, lighting, ventilation, earthing, lightning protection, main & auxiliary power distribution, instruments, civil works required for completion of Works.

1.3. Contractor shall take due care of the site Seismic conditions while design of all equipments/ components used in entire electrical systems covered in this specification. Contractor shall furnish list of additional design parameters considered in design to fulfill above requirement.

1.4. Design and detailed engineering of the materials procured by Contractor is included in scope.

Contractor shall submit design drawings/ calculations of each system which is included in scope to Purchaser/ Purchaser's representative for final review/ approval. All design documents/ calculations prepared by Contractor shall be as per ISO documentation i.e., with duly singed by qualified authorities and

stamped. Design documents/ calculations prepared by Sub-Contractors shall be approved by Contractor and stamped copy of approval along with no-deviation sheet from Sub-Contractor shall be submitted by the Contractor to Purchaser/ Purchaser's representative for final review/ approval.

1.5. Expert or manufacturer supervision for SUB-Contractor supplied material shall be provided by Contractor and included in offer.

1.6. Contractor shall be solely responsible for any shortages or damages in transit for his supply scope, handling and/ or in storage of any materials and erection of the equipment, supply of erection tools at site. Contractor shall ensure that it will not affect any activity or project schedule. Any demurrage, other such charges claimed by the transporters, railways etc. shall be to the account of the Contractor.

1.7. Contractor shall identify activities and mile stones of the work forecasted for next month with optimistic and pessimistic dates of work completion. Contractor shall prepare program evaluation and review techniques to identify critical path of project and activity sequences. The project schedule shall be prepared and updated fortnightly in MS Project.

1.8. Nothing in this specification shall be constructed to relieve the Contractor of his/ her responsibilities towards following best engineering practices established in the country.

1.9. Obtaining approval including load sanction/ release LESCO (Lahore Electric Supply Company), No Objection Certificates from LESCO relevant government agencies, statutory authority, as applicable is included in Contractor's scope.

1.10. All necessary legal fees required for various applications to LESCO, relevant government agencies, statutory authorities shall be paid by the Purchaser. The LESCO deposit required to be paid for load sanction/ release shall also be borne by the Purchaser.

1.11. The Contractor's scope shall include measurement of soil resistivity at site by Wenner's four electrode method as per ISO: 3043-1987 (Reaffirmed in 2006) at minimum four locations at site. The earthing shall be designed for the actual mean soil resistivity value obtained.

1.12. Even if all components of a system included in this specification are not explicitly identified and/ or listed herein, these shall be supplied under this contract to ensure completeness of the system and facilitate proper operation and easy maintenance of the plant. Any and all other works not indicated above but necessary/ required to complete the system in all aspects, are included in the

Contractor's scope.

1.13. The Contractor shall include start up spares, essential spares, recommended spares and a set of special tools necessary for operation, routine maintenance of equipment supplied for a period as specified in this contract.

1.14. Whether specifically called for or not, all accessories required for normal and satisfactory operation (as deemed by the Purchaser) of the equipment shall be considered to be a part of the Contractor's basic scope of supply and/ or work and no claims whatsoever, for extra payment on these grounds, will be accepted.

1.15. Contractor should visit site and get him/ her ascertained regarding the scope of work for the complete Electrical works before submission of quote/ offer for the pumping stations for 24 x 7 Water Supply.

1.16. Contractor's scope shall include design, engineering, manufacture, supply, testing, commissioning and handover of following electrical equipment/ systems as per tender specifications, BOQ, reference drawings and other relevant details for the following pumping stations for 24 x 7 Water Supply for WASA.

1.16.1. Tariff metering equipment as applicable (as per LESCO) & electric supply connection including necessary liaison works (Tariff metering equipment & electric supply connection shall be provided by LESCO for which necessary liaison shall be done by the Contractor).

1.16.2. 415 V Metal Enclosed Switchgears including Power & Motor Control Centre (PMCC) including Starter Panels, PDBs, Sub DBs, Lighting DBs, Receptacles for utilities. Local Start/ Stop Push Button Stations shall be provided near those motors which are not controlled from a Local Console/ Panel.

1.16.3. LV Capacitor Banks with control panel consisting of automatic power factor correction (APFC) relay to improve the plant power factor up to 0.99. APFC panels shall be provided on both bus sections of the PCC/ MCC.

1.16.4. Cabling system shall consists of various HV/ LV grade, XLPE/ PVC insulated, multi-stranded Al/ Cu, GI round wire/ flat strip armoured power, control cables, GI ladder/ perforated type Cable Trays & associated accessories including support structures.

1.16.5. Provision for continuous monitoring of electrical Power & Energy parameters like Voltage, Current, Power Factor, Frequency, Kilo Watts, Kilowatt-Hours etc.

1.16.6. Earthing for HV/ LV equipments and lightning protection system for

all buildings in the plant premises. The general design shall be on the basis of following codes and standards (their latest amendments) in line with design criteria & specification requirements.

a) ISO 3043 Code of practice for Safety Earthing

b) ISO/ IEC 62305 Code of Practice for the protection of buildings and allied structures against lightning.

c) CEA guidelines 2010 Measures related to safety & electric supply.

1.16.7. Lighting system for all indoor & outdoor areas of plant(s). The lighting system will be controlled by lighting panels installed in respective plant/ station areas, which will be fed from the main lighting DB.

34.2 DC SYSTEM:

a) 24/ 30V or 110V DC in built DC power pack unit shall be provided wherever applicable.

b) 24/ 30V or 110V DC Battery & Battery Charger (with inbuilt DCDB) shall also be provided wherever applicable.

34.3 DIESEL GENERATORS WITH AMF & SYNCHRONISING PANEL.

All necessary and supplementary items & equipment required for completeness, safe & efficient operation of the system, even though these may not have been mentioned in this specification. Spares & consumables for successful commissioning, establishment of performance guarantee and five years of trouble-free & safe operation of the plant.

1.17 Submission of drawings & documentation as specified under ''General Technical & Particular Requirement'' section for Electrical equipment/ systems.

1.18. Contractor's scope shall also include all civil works required for electrical equipment/ structure such as equipment foundations, indoor & outdoor trenches, equipment support structures, two pole structures, flow meter chamber, control rooms, all excavation works including those for earthing, cabling etc, de-tanking area, soak pits, burnt oil pits, chamber etc.

1.19. It is not the intent to completely specify all details of design and construction herein.

Nevertheless, the Electrical system shall conform to high standard of engineering, design and workmanship in all respects and shall be capable of performing satisfactorily in continuous commercial operation under the specified environmental conditions.

1.20. Purchaser reserves the right to issue addendum to the technical specification to indicate modification/ changes in the requirements, if so

required at a later date.

34.4 PROJECT INFORMATION:

34.4.1 Site / Environmental Conditions

- Ambient temperature : 45ºC (site specific)
- Relative Humidity : 5 - 95%
- Area Classification : Non Hazardous / Hazardous
- Seismic Data : As per ISO 1893 (latest Issue)

34.4.2 Nominal System Voltage

Incoming AC power supply voltage to the plant premises is derived based on Load Demand as per GERC norms as follows:

Contract Demand	Supply Voltage
Not exceeding 100 KVA up to 1 MVA	415V
Exceeding 1 MVA KVA & up to 4 MVA	415V and 11 KV,
Exceeding 4 MVA	11 KV & above

34.4.3 Plant Power/ Control Supply Distribution Voltage:

Plant Power Distribution Voltage:	415V, 3 Phase, 4 Wire, 50 Hz, AC
General Lighting & Space Heating:	240V, 1 Ph, 2 Wire, 50Hz, AC
Control, Protection & Emergency Lighting:	24/ 30 or 110V, 2 Wire DC (as applicable)
Voltage Transformer Secondary:	110 V, 3 Ph, 50 Hz, AC
Voltage Variation:	10%,
Frequency Variation:	5% and
Combined Voltage & Frequency Variation:	10%

34.4.4 System Earthing

132 kV, 3 Ph AC system:	Neutral Grounding Resister
11 kV, 3 Ph AC system:	Neutral Solidly Earthed
415 V, 3 ph, AC system:	Neutral Solidly Earthed
240 V, 1 ph, AC system:	Neutral Solidly Earthed

34.5 DESIGN CRITERIA FOR ELECTRICAL EQUIPMENT / SYSTEM

34.5.1 General

The design criteria, given below has to be followed by the Contractor for designing/ sizing of electrical equipments covered under Contractor's battery limits; However it is to be noted by the Contractor that, following this design criteria does not relieve the Contractor from adherence to the standards, regulatory requirements & best engineering practices.

ESTIMATION OF LOAD/ MAX DEMAND: The following considerations are to be

followed to arrive at the maximum electrical demand.

a. Load Factor

a)	Main motors	0.9
b)	Auxiliary load (valve actuators, Crane/ Hoist, etc.)	0.4
c)	Lighting load	1.0

b. Diversity Factor

a)	Main motors	1.0
b)	Auxiliary load (valve actuators, Crane/ Hoist, etc.)	1.1
c)	Lighting load	1.1

Power factor of Motors : As per the Manufacture's Data sheets

Efficiency of Motors : As per the Manufacturer's Data sheets

34.5.2 INCOMER SIZING/ SELECTION:

The capacity of the incomer(s) will be calculated based on the total simultaneous maximum demand (calculated based on the load factors and diversity given above, PF, efficiency).

Additional 20% contingency shall be considered for deriving incomer sizing.

% voltage dip at motor terminal shall not exceed 15% i.e. with the use of appropriate starter & considering largest motor starting & base load (all other loads except the highest rating motor are running); the % voltage dip during starting at motor terminal shall not exceed 15%.

a) The Voltage dip and fault level calculations needs to be calculated based on following actual data collected from nearest Substation and Grid.

   i. The fault level of HV bus from which power supply will be taken to the plant.

   ii. Impedance of HV Overhead Line Conductor/ HV Cable interconnecting the HV bus of Substation and HV switchboards of the Plant

b) For the per unit calculation purpose, minimum starting current for various types of starter applications shall be considered as following:

   i. DOL Starter – 6 times the rated current.

   ii. Star- Delta Starter – 3 times the rated current.

   iii. Auto Transformer Starter (ATS) – 3 times the rated current.

   iv. Soft Starter – 3 times the rated current.

34.5.3 SWITCHGEAR SIZING/ SELECTION:

Switchgear shall be sized/ selected considering the following:

a) Rating suitable for carrying full load current of the equipment.

b) Suitability for Short Circuit Rating for 1 sec duration.

c) Switchgear for motors shall be suitable for motor duty application.

Switchgear for all the motor feeders shall be as per Type-2 co-ordination.

Motor starter selection shall be done as follows:

a) Direct On Line (DOL) Starter – For motors rated up to 5.5 kW

b) Star- Delta Starter - For motors rated above 5.5 kW to 15 kW

c) Auto Transformer Starter (ATS) - For motors rated above 15 kW to 75 kW

d) Soft Starter – For all low/ medium voltage motors above 75 kW rating.

e) In-panel de-ration of minimum 20% or as provided in Manufacturer's catalogue, whichever is higher shall be considered.

a. Bus Bar Sizing:

a) The Contractor shall furnish calculations after award of contract, establishing the adequacy of the bus bar sizes to meet the continuous and short time current ratings as calculated.

b) The bus-bars shall be sized considering the following criteria:

i. Sleeving made of insulating material on all bus bars.

ii. Design ambient temperature 50ºC.

iii. Final temperature of the bus-bars complying with requirements of ISO 8623 & IEC 60947. Reduced temperature rise limit by 5K (for indoor panels) & 10K (for outdoor panels) to that of mentioned in ISO 8623 & IEC 60947 shall be considered to satisfy the final temperature.

iv. Bus bars being inside the panel; De- ration for enclosure and ventilation.

v. Bus bar suitability for carrying rated current continuously.

vi. Configuration of bus bars and Proximity effect

vii. Bus bars shall withstand the short time rating of the panel for 1 sec duration.

34.5.4 POWER FACTOR IMPROVEMENT:

APFC Panel shall be sized considering following design criteria:

Minimum 8 steps in an APFC relay shall be considered.

Capacitor shall be All Poly Propylene (APP), double layer type.

Fixed type capacitor bank, with manual & auto switching and components as indicated in reference electrical Single Line Diagram(s) shall be provided in each mains incomer (LV) panel for transformer no load compensation.

For each bus section of the Main LV PCC/ MCC panel, separate APFC panel-based on above design criteria to be provided. Other requirements of APFC panel & its components shall be as per requirement provided in this specification.

Total capacity & capacitor bank sizes shall be as given in Table below:

Capacity	5 kVAr	10 kVAr	15 kVAr	25 kVAr	50 kVAr	100 kVAr
* kVAr	# Nos.	# Nos.	# Nos.	# Nos.	# Nos.	# Nos.

(*) = Contractor has to calculate the capacitor rating based on the system power factor (0.85 or actual, whichever is lesser - to be corrected for 0.99. Rating of APFC panel shall be based on 50% of running load on each bus section & not on the connected load basis. Number of stages/ steps in a particular APFC panel shall be decided by the Contractor such that minimum 8 steps & maximum 16 steps shall be provided in a particular panel. CT changeover scheme when only one transformer is running to be considered.

CABLE SIZING: The Contractor shall ensure that cable and wires associated with the power distribution and control systems, plant wiring and all other installations throughout the Works are adequately rated for their use.

The following main aspects shall also be considered while deciding the final size of the cables-

a) Supply voltage and frequency

b) All cables shall be selected to carry the corresponding full load current under site conditions.

c) Route length and disposition of cables

d) Maximum allowable temperature rise under normal full load condition based on the material of cable insulation (XLPE/ PVC).

e) Maximum short circuit current duration (fault clearing time) and final temperature of cable during short circuit current flowing through the cable.

f) For Cables emerging from ACB outgoing, fault clearing time shall be considered as 0.16 second (for Tie feeders if any it shall be 0.5 second)

g) For Cables emerging from MCCB outgoing, fault clearing time shall be considered as 0.01 second

h) Cable from metering kiosk to PCC incomer, fault clearing time shall be 1sec

i) Contractor to note that, the above fault clearing times are minimum to be considered & fault clearing time shall be considered as per actual relay co-ordination study.

j) Appropriate de-rating factors as per cable manufacturer's catalogue and enlisted below shall be considered for sizing the cable:

   i. Ambient Air Temperature (minimum 50ºC).

   ii. Ambient ground temperature (minimum 40ºC to be considered)

   iii. Laid in Air/ ducts/ directly in ground etc.

   iv. Depth of cable burial (minimum 750 mm for LT and 900 mm 11kV HV)

   v. Thermal Resistivity of Soil (minimum 150ºC Cm/ W to be considered)

   vi. No. of cables in a group-touching each other or separated by a distance vii. No. of cable trays in tier

   viii. Any other de-ration factors as applicable & as per Manufacturer's catalog.

k) % voltage dip at motor terminal shall not exceed 15% i.e. with the use of appropriate starter & considering largest motor starting & base load (all other loads except the highest rating motor are running) The Voltage dip calculations, minimum starting current for various types of starter applications shall be considered as following:

   i. DOL Starter – 6 times the rated current.

   ii. Star- Delta Starter – 3 times the rated current.

   iii. Auto Transformer Starter (ATS) – 3 times the rated current.

   iv. Soft Starter – 3 times the rated current.

l) In running condition, cumulative voltage drop (at 100% rated load) shall not exceed 5% (measured at load end) for the LV loads.

m) LV cables shall be 1.1 kV grade, multi-stranded Copper/ Al conductor, XLPE insulated, colour coded, inner and outer extruded PVC sheathed, galvanized steel round wire/ flat strip armoured cables.

n) Cables up to & including 4.0 sq.mm shall be Cu multi-stranded conductor with galvanized steel round wire armoured & balance cables shall be Al multi-stranded conductor with galvanized steel round wire/ flat strip armoured.

o) Single core cable shall have non magnetic material armouring.

p) Control cables shall be Cu multi-stranded conductor with galvanized steel round wire/ flat strip armoured. For cables above 7 cores, minimum two spare cores shall be considered.

34.5.5 ILLUMINATION SYSTEM:

Illumination for various indoor & outdoor areas shall be conforming to the requirements mentioned below:

All lighting fixtures for indoor and outdoor shall be of LED only.

The illumination levels to be considered for the design of lighting system for various areas shall be as following. These are the illumination levels achieved at Work plane. Work plane height shall be considered as 0.76 m from FGL.

Area	Illumination Level (Lux) - Average values
Office rooms	300
Switchgear rooms	250
Control rooms	300
Chemical and general stores	150
All other indoor areas	150
Outdoor platforms and walk ways	50
Outdoor plant areas	20
Switchyard & Transformer Area - General - On Equipment	 10 30
Roads	15

Critical lighting shall be designed such that at all junctions, exit passages & strategic locations the Lux level shall be maintained above 10 Lux. Installite fixtures with built in battery backup shall be considered.

Lighting design shall be performed using DiaLux Software Version 4.5 or its latest version/ Original Equipment Manufacturer (OEM) validated software. The Validation Report along with software and data files shall be acceptable to Purchaser/ Purchaser's representative.

Various design factors shall be considered as following:

a) Maintenance Factor:

i) Outdoor area: 0.6 (0.7 for LED)

ii) Indoor areas: 0.7 (0.8 for LED)

b) Reflectance Factors:

i) Wall 30%

ii) Ceiling 10%

iv) Floor 30%

c) Uniformity (Min. / Avg.)

50% Minimum for indoor and 30% for outdoor

1.1.1 EARTHING & LIGHTNING PROTECTION SYSTEM:

The safety earthing and lightning protection system will be generally on the basis of following codes and standards (including their latest editions).

a) ISO 3043 -1987 (Reaffirmed in 2006): Code of practice for Safety Earthing.

b) IEEE 80 - 2000.

c) ISO/ IEC 62305 - 2013: Code of Practice for the protection of buildings and allied structures against lightning.

d) CEA guidelines - 2010: Measures related to safety & electric supply.

The fault levels considered shall be as follows:

System Voltage	Fault level in kA (*)
11 kV	18.4 kA for 1 sec
415 V	50 kA for 1 sec

(*) Contractor to design on the basis of actual impedance and adequacy calculations for sufficiency of earth conductor size shall be provided.

Following factors shall be considered for sizing the earthing conductor:

a) Design Ambient Temperature 50C

b) Allowable temperature rise for steel welded joints 500C

c) Fault clearing time 1 Second

d) Overall earthing resistance to be achieved as per ≤ 1 Ohm for transmission

IEEE std 80 – 2000 substation.

≤ 5 Ohm for distribution substation.

Measurement of soil resistivity shall be done using Wenner's four (4) electrode method as described in ISO 3043 -1987(Reaffirmed in 2006) including its latest amendment.

The soil resistivity of the plant area has not yet been measured; the same should be carried out during detailed engineering by successful Contractor.

After soil resistivity measurement; length of conductor, number of earth electrodes and no. of test pits shall be finalized based on these design criteria & the requirements specified in earthing requirements.

1.1.2 DRAWINGS / DOCUMENTS FOR REFERENCE

The electrical Single Line Diagram(s)/ PLC system architecture for water supply project including raw water intake & various headwork/ sub-headwork with/ or without water treatment facility (as applicable) form part of this specification and should be used for reference purpose only.

The equipment/ switchgear component ratings & requirements shown in the reference electrical Single Line Diagram(s) are minimum requirements & after award of contract, Contractor has to get approval for the equipment selection with the approval for sufficiency calculations.

1.1.2.1 The fault levels considered shall be as follows:

System Voltage	Fault level in kA (*)
11 kV	18.4 kA for 1 sec
415 V	50 kA for 1 sec

(*) Contractor to design on the basis of actual impedance and adequacy calculations for sufficiency of earth conductor size shall be provided.

1.1.2.2 Following factors shall be considered for sizing the earthing conductor:

a)	Design Ambient Temperature	50C
b)	Allowable temperature rise for steel welded joints	500 C
c)	Fault clearing time	1 Second
d)	Overall earthing resistance to be achieved as per IEEE std 80 – 2000	≤ 1 Ohm for transmission substation.
		≤ 5 Ohm for distribution substation.

Measurement of soil resistivity shall be done using Wenner's four (4) electrode method as described in ISO 3043 -1987(Reaffirmed in 2006) including its latest amendment.

The soil resistivity of the plant area has not yet been measured; the same should be carried out during detailed engineering by successful Contractor.

After soil resistivity measurement; length of conductor, number of earth electrodes and no. of test pits shall be finalized based on these design criteria & the requirements specified in earthing requirements.

34.5.6 Drawings/Document for Reference

The electrical Single Line Diagram(s)/ PLC system architecture for water supply project including raw water intake & various headwork/ sub-headwork with/ or without water treatment facility (as applicable) form part of this specification and should be used for reference purpose only.

The equipment/ switchgear component ratings & requirements shown in the reference electrical Single Line Diagram(s) are minimum requirements & after award of contract, Contractor has to get approval for the equipment

selection with the approval for sufficiency calculations.

SECTION-35 GENERAL TECHNICAL & PARTICULAR REQUIREMENTS FOR ELECTRICAL EQUIPMENT/ SYSTEMS:

35.1 415V METAL ENCLOSED SWITCH BOARDS:

35.1.1 Applicable Standards

The design, manufacture and performance of equipment shall conform to the latest standards specified below. In case of conflict between standards and this specification, this specification shall govern.

Metal enclosed switchgear- General requirements

Factory Built Assemblies of SWGR and control gear for Voltages up to and including 1000V AC & 1200VAC ISO: 3427

ISO: 8623 / BS: 5486 / IEC: 439

Air Break Switches ISO: 13947-P3 / BSEN6049 / IEC: 947-3

Miniature Circuit BreakersISO: 8828 / BSEN: 60898

Low Voltage FusesISO: 13703 / BS: 1362 / IEC: 269-1

Contactors ISO: 13947/ BSEN: 60947 4 / IEC: 947-1

Starters ISO: 13947/ BSEN60947-4/ IEC: 292-1 to 4

Control Switches & Push buttonsISO: 6857 / BSEN: 60947

Current Transformer ISO: 2705 / BS: 7626

Voltage Transformer ISO: 3156 / BS: 7625 / IEC: 44, 186

Indicating instruments ISO: 1248 / BS: 89 / IEC: 51

Marking and Identification of Conductors and Apparatus Terminals

ISO: 11353 / BS: 159

A.C. Electricity Meters ISO: 722, 8530 / BS: 5685 / IEC 145,211

Degree of Protection ISO: 13947 / IEC: 947-P1

Selection installation and maintenance of switchgear and control gear

Code of practice for phosphating iron and steel

Specification for copper rods and bars for electrical purposes

Control transformers for switchgear and control gear voltage not exceeding

1000V AC

ISO: 10118

ISO: 6005 / BS: 3189

ISO: 613

ISO: 12021

35.1.2 Constructional Features:

The switchgear shall be metal enclosed, modular type suitable for indoor/ outdoor installation, dust & burning proof, self standing floor/ plinth mounting with a height not exceeding 2300 mm and shall have following features:

a) Panels shall be complying to Form-4 as per ISO 8623: 1993, Part I/ IEC 439-1

b) Breaker up to 1250A shall be installed in two tiers and above 1250A, it shall be mounted in single tier.

c) Minimum clearance between live parts shall be phase to phase 25.4 mm & phase to neutral 20 mm at any location & shall be complying with the BIL for the panel.

d) Switchgear shall be divided into distinct vertical sections each comprising :

   i. A completely enclosed bus bar compartment running horizontally.

   ii. Enclosed vertical bus bars serving all modules in vertical section.

   iii. A separate horizontal enclosure for all auxiliary power and control buses.

   iv. Vertical cable alley of minimum 250 mm wide covering entire height e) Operating devices shall be incorporated only in the front of switchgear.

f) Each shipping section shall have metal sheets at both ends

g) Cable alley shall be provided with suitable hinged doors

h) All doors shall be with concealed type hinges and captive screws

i) Each vertical section shall be equipped with a space heater controlled by thermostat

j) Each switchgear cubicle shall be provided with interior lighting with 11W CFL luminaries inclusive of lamp with door limit - on/ off switch.

k) A power socket (240 V AC, 5/ 15 A) shall be provided in the interior of each cubicle with On-Off switch.

l) All identical equipment and corresponding parts be fully interchangeable without any modifications

m) Main and Auxiliary Buses:

   i. Switchgear bus bars shall be of uniform cross section throughout the length and made of Electric grade Aluminium (91 E- 63401)

ii. All bus bars shall be covered with heat shrinkable black PVC sleeves. Coloured polyester tapes for phase identification shall be provided at suitable locations.

iii. Bus bar shall be adequately supported to withstand stresses developed due to short circuits.

iv. Bus bar joints shall be provided with contact grease at the joints and shall be complete with tensile steel bolts, washers and nuts

v. The exposed bus live parts in the cable alley shall be totally covered against accidental contact by a shroud (and not by sleeve) to protect the workmen working on the switchgear.

vi. Vertical bus bars shall have Short Circuit rating same as main bus bar and shall be suitable for all connected load of vertical section.

vii. Neutral bus bar size shall be 50% of phase bus bar.

viii. Termination on bus bars at ACB, MCCBs shall be as per IEC60947-2. For terminations on MCCBs, where phase-phase and phase to earth clearance are not possible, Cu spreaders of suitable size shall be used along with the use of separators.

ix. Bus bar supports shall only be WASA irrespective of bus bar size. The span between the two insulators shall be adequate. Joint positions and insulators shall be properly adjusted so that they don't interfere.

x. For the Main PMCC, Contractor shall ensure that incoming feeders from transformer shall be suitably designed for terminating bus duct. Contractor shall consider the necessary arrangement (dummy panel, adapter panel, rear extension etc.) if required, for terminating the bus-duct. Phase transposition, if required, will be done in the Main PMCC.

xi. Wherever Cu bus bars are provided, it shall be tinned copper & not bare Cu.

n) All mounting accessories like base channels, cross angles if required, nuts, bolts etc. shall be supplied by the Contractor.

o) All the indoor switchgear panels shall be suitable for IP-54 degree of ingress protection for the enclosure. Outdoor panels shall be with minimum IP-55, degree of protection

p) All panels shall be made up of CRCA sheet steel of following thickness

i. Load bearing members: 2.5 mm.

ii. Doors and partitions: Doors - 2.0 mm, Partition - 1.5 mm.

iii. Mounting plate: 2.0 mm.

iv. Gland plate: 3.0 mm for both incomer and outgoing. For single core cable these plates shall be non magnetic.

q) All the panel wiring shall be done with PVC FRLS, multi-stranded copper wires

r) Feeder shall have hinged open-able (more than 105˚) type door with panel locks. All bus-bar covers and other panel covers shall be screw fixed.

s) Suitable barriers of FRP material shall be provided between two terminals connected to different voltage supplies.

t) All doors and detachable components shall be earthed with flexible green coloured (with Yellow coloured band) PVC sheathed 2.5/ 4.0 sqmm. multi-stranded Copper cable.

u) The equipment shall be given tropical and fungicidal treatment.

v) Each compartment & component shall be provided with name plates (with white letters on Black background) at front, inside & rear side.

w) Equipment nameplates shall be fixed by screws/ rivets and shall not be pasted.

x) Metallic Shrouding shall be provided for the isolation of main and vertical bus; as well as to avoid accidental contacts with live parts.

y) Drawing pocket shall be provided on the inside of incomer feeder door.

z) Provision for Top/ Bottom cable entry shall be made to suit the site condition.

aa) Lifting hooks/ eyes shall be provided in each shipping section of the equipment and shall be removable type.

bb) All the panels shall be provided with 20% extra power & control terminals.

cc) All unused contacts of the circuit breaker, protection, auxiliary, control relays shall be wired up to the terminal block.

dd) All terminals of different control voltages shall be separate from each other.

ee) Stud type terminals and ring type lugs shall be used for control cables.

ff) All the control/ power wiring shall be dressed neatly & the wire running through troughs shall be provided with covers

gg) Switchgear shall be easily extensible on both sides by the addition of vertical sections after removing the end covers. It shall be provided with a metal sill frame made of structural steel channel section properly drilled for mounting the switchgear along with necessary mounting hardware. Hardware shall be zinc plated or passivated. It shall be provided with labels on the front and rear indicating the switchgear designation.

hh) Any operating handle of switchgear shall not be more than 1800 mm and not lower than 300 mm from base of the panel.

i) For individual feeder modules arranged in multi tier formation, it is essential that the modules are integral multiples of the unit size to provide for flexibility in changes if any at site. For safety isolation of the vertical bus bars, insulating barrier with cut outs shall be provided to allow the power slab contacts to engage with vertical Bus bars. A vertical cable alley shall be sufficiently wide for motor control modules and for circuit breaker control modules.

jj) A horizontal separate enclosure for all auxiliary power and control buses, as required shall be located so as to enable easy identification, maintenance and segregation from the main power buses. Tap off connections from these buses shall be arranged separately for each vertical section.

kk) All equipment associated with a single circuit shall be housed in a separate module compartment of the vertical section.

ll) For draw out type modules, only the handles of control and selector switches, push buttons, knobs & cut outs for lamps and meters shall be arranged on the front doors of the respective compartments to permit operation without opening the door.

mm) On circuit breaker controlled circuits, protective relays shall be mounted on the front door of the compartment. All other equipment pertaining to a circuit shall be mounted on the withdrawal chassis. All cut outs shall be provided with gaskets for the purpose of dust proofing.

nn) Current transformers shall not be directly mounted on the buses. Current transformer on circuit breaker controlled circuits shall be mounted on the fixed portion of the compartment.

oo) In breaker compartments, external cable connections shall be carried out in separate cable compartments for power and control

cables.

pp) After isolation of the power and control connections of a circuit, it shall be possible to safely carry out maintenance in a compartment with the Bus bars and adjacent circuit live.

qq) The withdrawals chassis shall move on suitable guides and on suitably plated steel or stainless steel rollers or balls to facilitate easy withdrawal.

rr) Cable alleys shall be provided with suitable hinged doors. It shall be possible to safely carryout maintenance work on cable connections to any one circuit with the Bus bars and adjustment circuits live. Adequate number of slotted cable support arms shall be provided for cleating the cables.

ss) Rear of single front switchgear shall be provided with removable panels. It shall be possible for one person to remove and fix the removable panel.

tt) All doors shall be provided with concealed type hinges and captive screws.

uu) The draw out contacts shall be only between copper/copper alloy/ aluminum fuses, which are silver or tinplated. The contact design shall be such that there should be no arcing/ deformation under the associated peak short circuit current.

vv) Switchgear shall be designed in such a way that all components equipment and Bus bars operate satisfactorily without exceeding their respective maximum permissible rise in temperature under ambient temperature conditions prevailing within the switchgear cubical, with reference to ambient temperature outside the switchgear cubical.

ww) Provision of ventilating louvers shall be provided with fine-screened brass or GI meshes to prevent entry of vermin and dust.

xx) The various types of modules indicating the control requirements of each type together with the list of component equipment required for each type shall be as follows:

i. Incoming circuit - Draw Out type air circuit breaker for above 630A/ Fixed type MCCB for 630A & below

ii. Outgoing feeder - ACB/ MCCB/ MPCB

iii. Auxiliary services - Starters, capacitors, Distribution Boards and other auxiliary load

yy) Physical size of compartment for each type of control and current rating shall be so chosen that all the basic and additional equipment

can be housed in the compartment. No equipment associated with any particular circuit shall be permitted to be mounted in any other circuit module.

4.1.3. Power Distribution Board (PDB) configuration shall be two no. *A TPN MCCB I/Cs and six no.

*A TPN MCCB O/G feeders. The O/G feeders shall be supplying to Sub DBs. The configuration of Sub Distribution Board (SDB) shall be *A FP MCCB I/C and 2 nos. 63A TPN

MCB & 12 nos. 20A SP MCBs as outgoing feeders. (*A) shall be decided during detailed engineering.

4.1.4. Separate instrument's compartment for indicators of flow meter (s), energy meter, level & pressure controller (if any) shall be provided as per actual requirement of suitable size.

35.1.3 Control Voltages:

Following control voltages shall be used in LV panels

a) All ACBs tripping/ Closing shall be suitable for 110/ 240V AC (24/ 110VDC) as applicable. The trip coil and closing coils of ACBs shall operate satisfactorily under the following conditions of supply voltage:

   i. Closing coils- 85 % to 110 % of rated voltage

   ii. Trip coils- 70 % to 110 % of rated voltage.

b) Indications/ Annunciator for LV Main PCC/ MCC- 110/ 240V AC (24/ 110VDC)

c) Indications for auxiliary DBs - 240V AC

d) Space heater, 5/ 15A socket, panel illumination lamp etc- 240V AC derived from AC bus e) 240V AC, 110V AC and other voltages shall be segregated to avoid mix-up of voltages.

f) Control transformers suitably rated of voltage ratio 415/ 240/ 110 V on the Incomer/ Bus shall be provided. For the control transformers, fuses shall be provided on the 415 V side and MCBs on the 240/ 110V side. The control transformer shall be cast resin type only.

35.1.4 Painting:

a) All sheet steel work shall be paint through 7 tank electrostatic powder coating process in accordance with the required procedure and with the applicable standards. The switchgear enclosure shall be powder coated with shade as per RAL-7032.

b) The final finished thickness of paint film on sheet steel enclosure shall not be less than

80 microns. Finished painted appearance of equipment shall present an aesthetically pleasing appearance, free from dents and uneven surfaces.

35.1.5 Interchangeability:

All identical equipment and corresponding parts including chassis of draw out modules of the same size shall be fully interchangeable without having to carryout modifications. For trouble free interchangeability, the draw out arrangements shall be designed such that normal dimensional variations are taken care of by self-aligning feature of the modules.

35.1.6 Drawings & Documents:

Prior to fabrication of the switchgear, the Contractor shall submit following for Purchaser Representative's approval - the dimensional drawing and design calculations indicating bus bar size, short circuit rating of all the electrical component used, internal wiring, components mounting details etc. The Contractor shall submit manufacturers catalogues of the electrical components installed in the switchgear.

35.1.7 Inspection:

At all reasonable times during production and prior to dispatch of the switchgear to site, the Contractor shall arrange and provide all the facilities at their plant for inspection & testing of switchgear.

35.1.8 Earthing:

a) Al/ GI earth bus bars of adequate size shall be provided for the entire length of the panel.

The framework of the enclosure shall be connected to this earth bus. Provisions shall be made for connection form this earth bus to the main earthing bus bar coming from the earth pit on both side of the switchgear.

b) The earth continuity conductor of each incoming and outgoing feeder shall be connected to this earth bus bar. The armour of cables shall be properly connected with earthing clamp and the clamp shall be ultimately bonded with the earth bus bar.

35.1.9 Labels & Name Plate:

a) Engraved PVC labels shall be provided on all incoming and outgoing feeders. Single line circuit diagram showing the arrangements of circuit inside shall be pasted on inside of the panel door and covered with transparent laminated plastic sheet.

b) A nameplate with the switchgear designation in bold letters shall be fixed at top of the central panel. A separate nameplate giving feeder details shall be provided for each feeder module door.

c) Inside the feeder compartments the electrical components, equipments, accessories like switchgear shall be provided with stickers shall suitably identify control gear, lamps, relays etc.

d) Engraved nameplates shall preferably be of 3-ply (Red-White-Red or Black-White-Black) lamicoid sheet however black engraved perplex sheet nameplates shall also be acceptable. Engraving shall be done with square grove cutters.

e) Nameplate shall be fastened by counter sunk screws and not by adhesives.

35.1.10 Danger Notice Plates:

a) The danger notice plate shall be affixed in a permanent manner on operating side of the switchgear.

b) The danger notice plate shall indicate danger notice in Gujarati, Hindi and English.

c) The danger notice plate, in general shall meet to requirements of local inspecting authorities.

d) Caution name plate, "Caution Live Terminal" shall be provided at all the points where the terminals are likely to remain live and isolation is possible only at remote end i.e. incomer to the switchboard.

e) The danger notice plate shall be made from minimum 1.6 mm thick steel sheet and after due pretreatment to the plate, the same shall be painted white with vitreous enamel paint on both front and rear surface of the plate.

f) The letters, figures, the conventional skull and bones shall be positioned on the plate as per recommendations of latest edition of ISO 2551-1982.

g) The said letters, the figures and the sign skull and bonds shall be painted in signal Red color as per latest edition of ISO 5 - 1978.

h) The danger plate shall have rounded corners. Locations of fixing holes for the plate shall be decided to suit the design of the switchgear enclosure.

35.1.11 Cable Entry:

a) The panel shall have provisions of cable entry from top/ bottom. The removable cable gland plate shall be provided to make entry dust and vermin proof.

b) The panel shall have provisions for fixing the multi-core cable glands.

c) The cable glands support plates shall be 3 mm thick.

d) Cable entries to the panel shall be from the bottom unless otherwise specified. Cable gland shall be double compression screwed type and made of brass.

35.1.12 Mountings:

a) All equipments in front of panel shall be of flush mounting type.

b) All equipment shall be so mounted that the removal and replacement may be accomplished individually without interruption of services of others.

c) All equipment inside the panel shall be so located that their terminals and adjustments are readily accessible for inspection or maintenance.

d) The centerline of switches, push buttons and indicating lamps shall be matched to give a neat and uniform appearance. Likewise the top lines of all meters, relays and recorders etc. shall be matched.

It is important to note that when pumping station is idle and transformer is required to be kept energized under no load/ part (miniscule) load condition, the necessary LV fixed capacitor bank (approx. 5% of transformer rating) shall be provided in PMCC (transformer LV incomer) panel and shall be manually/ automatically switched on to maintain power factor more than 0.95 but less than 0.99 (near unity). All the components for fixed type Capacitor bank (to be mounted in Main LV PMCC) panel shall be as indicated in typical electrical Single Line Diagram attached with the specifications. This is a complete responsibility of the Contractor to maintain the power factor under idle condition of pumping station. Any power factor adjustment charges levied by power utility shall be recovered from the Contractor along with 5 % lump sum administrative charge by the Owner.

35.1.13 Air Circuit Breaker (ACB):

a) All the incomers & bus coupler ACBs shall be 4P EDO type. All other ACBs shall be TPN EDO type.

b) All the ACBs shall have Ics=Icu=Icw=100%

c) Up to and including 630 A, Fixed Type FP/ TPN MCCB shall be considered, while above 630A FP/ TPN, fully draw out type ACB shall be considered in line with the electrical Single Line Diagram requirements.

d) All ACBs shall be provided with additional 6 NO + 6 NC contacts, exclusively for Purchaser's use.

e) All the ACBs (except for APFC panel) shall be provided with microprocessor based O/L+ S/C + inbuilt E/F protections.

f) ACBs/ MCCBs for APFC panel shall be provided with thermal

magnetic based O/L+ S/C + E/F protections.

g) Each ACB shall be provided with – On, Off, Trip, Spring Charged, Trip Coil Healthy, Service & Test Position indication lamps.

h) For incomer feeders R, Y & B Phase indication lamps shall be provided.

i) All ACBs shall be Schneider make 'Masterpact NW'/ Siemens '3WL'/ L&T 'C Power' OR Equivalent from the approved make list.

j) Circuit breaker shall be horizontal withdrawal type, comprising three/ four identical poles operated through a common shaft.

k) It shall be suitable for switching duty of transformer and motors and other devices.

l) It shall be possible to push in and withdraw the breaker easily and without much effort.

Insulating plugs and sockets for power as well as for control circuits shall be of robust design and fully self-aligning. Plugs and sockets for power circuits shall be silver faced, insulated with PVC or other insulating material.

m) The breaker shall have three distinct positions namely services, test and fully withdrawn positions. In test position, it shall be possible to operate the circuit breaker without energizing the power circuits. Separate limit switches each having a minimum of four (4) contacts shall be provided for both service and test position of the circuit breaker. These contactors shall be rated for 10 Amp, 240 volts AC.

35.1.14 Operating Mechanism:

a) The EDO type ACB shall be power operated by a motor charged spring operated mechanism & MDO type shall be manual type spring operated mechanism.

b) The operating mechanism shall have anti-pumping features under every method of closing. The operating mechanism shall normally be operated by Local/ Remote electrical control, when the breaker is in service position. Shunt trip coils shall perform electrical tripping.

c) The main poles of the breaker shall operate simultaneously. Also there shall not be any objectionable rebound of the moving contact in the fixed contacts.

d) The mechanism shall be such that any failure of auxiliary spring shall not prevent tripping. When the breaker is in closed position, failure of any auxiliary spring shall not cause damage to the CB or danger the operation.

e) A mechanical indicator shall be provided on the breaker operating

mechanism to indicate open and closed position of the breaker. This shall be visible to a man standing in front of the cubical with the door closed.

f) It shall be possible to operate the breaker mechanically. This shall be possible only after opening the cubical door. Provision shall be made for local electrical control also when the breaker is in the test position by a control switch on the cubical doors.

g) All working parts of the mechanism shall be of corrosion resistance material. All split pins; bolts, nuts and other parts shall be properly pinned and locked to prevent loosening with repeated operation of the breakers.

h) Auxiliary switch containing 6 NO +6 NC potential free contacts rated for 10 Amp 240 V AC (Inductive breaking).

35.1.15 Spring Charged Mechanism:

a) Spring operated mechanism shall be complete with motor, opening spring, closing spring with limit switch for automatic charging and all necessary accessories to make the mechanism a complete operating unit.

b) The breaker operation shall be independent of the motor, which shall be used only for tensioning/ compressing of the spring.

c) The closing operation shall automatically charge the tripping spring. The closing, opening shall get charged immediately after a closing operation is performed.

d) Motor used shall be preferably universal type operated on AC supply. The Motor shall operate satisfactory at all values "between" 85% to 110% of rated voltage.

35.1.16 Mechanical/ Electrical Interlocking:

a) Mechanical interlock arrangement shall be provided between two incomer breakers.

Interlocking arrangement shall be robust, heavy-duty type and sturdy in construction.

b) Interlocking between two-incomer breakers shall be provided in such a way that in normal condition bus coupler shall be in " OFF " position so that both the transformer can be kept charged and the total load can be divided equally between two circuits.

c) During fault, maintenance or any other abnormal condition while one of the transformer is not in working mode, the bus coupler shall be in " ON "position so that total load can be supplied by the remaining transformer circuit.

d) Interlock shall be Mechanical and Electrical type. In case if one of the interlock fails the other way can be used for interlocking purpose.

35.1.17 Moulded Case Circuit Breakers (MCCB)

a) The MCCBs shall conform to IEC 947 & the latest applicable standards.

b) All MCCBs shall be of fixed type unless otherwise specified in the specifications elsewhere.

c) MCCBs shall be of four pole/ triple pole with neutral construction arranged for simultaneous four/ three-pole manual closing and opening and for automatic instantaneous tripping on short circuit.

d) All the incomer & bus coupler MCCBs for Main LT PMCC panels shall be FP type with microprocessor based O/L+S/C+inbuilt E/F release & all outgoings MCCBs shall be TPN with thermal magnetic based O/L+S/C+ E/F releases.

e) All MCCB's shall be Schneider make Compact NSX/ Siemens- Sentron 3VL OR equivalent from the approved make list.

f) For achieving the Earth Fault protection in thermal magnetic (TM) based MCCBs, external CBCT, Earth Fault relay & shunt trip provision shall be considered as part of complete TM based MCCB.

g) The ON, OFF and TRIP positions of the MCCB shall be clearly indicated by using LED indications.

h) MCCBs shall be with Ics = Icu = 100%

i) MCCB shall be capable of withstanding the thermal stresses caused by overloads and locked rotor currents of values associated with protective relay settings of the motor starting equipment and the mechanical stresses caused by the peak short circuit current of value associated with the switch gear rating.

j) All the MCCBs shall be of current limiting type and shall provide a cut off in 4-8 milli seconds for prospective currents during faults.

k) All the MCCBs shall be provided with rotary operating handle with door interlock.

l) MCCB terminals shall be shrouded and designed to receive cable lugs for cable sizes relevant to circuit ratings.

m) All MCCBs shall be provided with additional 2 NO + 2 NC contacts, exclusively for Purchaser's use.

n) All the switchgear selection for motor feeders shall be Type-2 co-ordinated.

Entire LV system shall be fuse less type & fuses shall be used only for VT/ Control

Transformer primary side. MCBs shall be provided on secondary of PT/ Control transformer

35.1.18 Miniature Circuit Breaker (MCB):

a) MCB shall be hand operated, air break, quick make, quick break type.

b) Operating mechanisms shall be mechanically trip-free from the operating knob to prevent the contacts being held closed under overload or short-circuit conditions.

c) Each pole shall be fitted with a bi-metallic element for overload protection and a magnetic element for short-circuit protection. Multiple pole MCBs shall be mechanically linked such that tripping of one pole simultaneously trips all the other poles. The magnetic element tripping current classification shall be of the type suitable for the characteristics of the connected load. Where this is not specified, it shall be Type C.

d) The short circuit rating shall be not less than that of the system to which they are connected.

35.1.19 Direct-On-Line Starters:

Direct on line motor starter shall have following components/ features:

a) Direct-on-line starters shall be suitable for Class AC-3 utilization category as per ISO:

13947 (Part 4), unless otherwise mentioned in tender.

b) DOL starter shall have MCCB/ MPCB, Overload Relay with SPP, Contactor etc.

c) Type 2 Co-ordination shall be ensured.

35.1.20 Automatic Star-Delta Starters:

Automatic star-delta motor starters shall have following components/ features:

a) Three sets of contactors one for the line, one for the star point and one for the delta, and a timer to automatically change the connections from star to delta.

b) Star Delta Starters shall consist of MCCB/ MPCB, Overload Relay with SPP, Contactors, electronic timer etc.

c) Star-delta contactors shall be electrically interlocked to permit starting of the motor in the proper sequence, namely star contactor closing, line contactor closing, timer energized after time delay, timer contact de-energizing the star contactor, and delta contactor closing.

d) Star-delta starters shall be suitable for AC-3 utilization category as per ISO: 13947 (Part unless otherwise mentioned in tender.

e) Type Coordination shall be ensured.

35.1.21 Reversing Starters:

Motor Reversing starter shall have following components/ features:

a) Forward and reverse contactors, electrically interlocked with each other.

b) Reversing starters shall be suitable for Class AC-4 duty as specified in applicable standards, unless otherwise mentioned in tender.

35.1.22 Auto Transformer Starter (ATS):

Auto Transformer starter shall have following components/features:

a) Auto transformer shall be air cooled type having three (3) tappings of 50%, 65% and 80%. The same should be wound with Copper wire. The size of the wire should be determined to suit the associated motor rating. The tapping requirement indicated is minimum required & Contractor to ensure proper tapping selection based on motor starting requirement.

b) Stamping of reputed make and winding wire with 'B' class insulation should be used.

This should also be suitable for minimum 6 starts per hour. Core shall be of CRGO material.

c) Maximum temperature rise should not be more than 115°C. Kordnoffer circuit (Closed Transition type) should be adopted in ATS panel. There shall be an acrylic/ Hylam sheet over & below the transformer. Also to absorb humming rubber sheet shall be provided below auto transformer.

d) Auto transformer shall be vacuum impregnated.

e) Testing of transformers should withstand full load starting current for six starts per hour, each kick of 15 seconds duration as per relevant ISO.

f) ATS shall be provided with thermal overheat protector in each coil of transformer from overheating. Thermal overheat protector rating shall be 900ºC with 10% tolerance.

g) ATS shall consist of MCCB/ MPCB, Overload Relay, and Contactors etc.

35.1.23 Soft Starters

Fully automatic microprocessor based soft starters with built-in bypass terminals for pump control application shall be considered for the motors

above 75 kW. The features/ requirements of the starters shall be as per following but not limited to:

a) The soft starter shall be designed, built and tested according to the latest editions of applicable IEC standards/ IEC 947-4-UL, CE.

b) Input Voltage – 3Ph, 415V, ±10%

c) Input Frequency – 50 Hz, ±5%

d) Control Voltage – 100 - 240 V AC

e) Ambient Conditions:

   i. Temperature- 50 Deg C. (Operating range -5 to 70ºC)

   ii. Relative Humidity of 5 to 95%

   f) Control Method - Torque Control/ Reduced Voltage/ Ramp

g) Motor Protection - Thermal overload protection

h) Starter Protection - S/C, Phase imbalance, Phase failure, Phase reversal, O/ V, U/ V, Locked rotor, excessive starts per hour for application, Phase loss input/ output, Motor output loss.

i) EMC standard – IEC 61000-4-2 level-3, IEC 61000-4-3 level-3

j) Built-in communication port for RS 485.

k) Type 2 Co-ordination shall be ensured.

l) The soft starter shall be complete with the following acceleration and deceleration settings & display requirements as a minimum-

   i. Starting Torque: Initial torque shall be adjustable from 0-100% of maximum locked rotor torque.

   ii. Ramp Time: The time between starting torque and maximum torque shall be adjustable between 1 to 60 seconds. The time between maximum torque & stop shall be adjustable between 2 to 120 seconds

   iii. The current limit feature shall have the following characteristics:

   The maximum allowed current during start shall be adjustable from 150% to 500% of soft-starter maximum current rating.

   Starting torque shall be fixed at 40% when utilizing the current limit function.

   iv. Voltage Ramp start & Full voltage DOL start shall be possible.

   v. For stop function – Linear torque control, Quadratic Torque

Control, Voltage ramp control, soft break etc. functions shall be provided.

vi. The soft-starter shall be provided with a functional ground to remove and/ or minimize electrical noise injected on the soft starter control board.

vii. Normally open output relays shall be provided for faults and status indications.

viii. Normally closed contacts for fault relays shall be provided as an option.

ix. The soft-starter shall be provided with a 2-position dip switch to select between the normal in-line connection (3-lead motor) and inside the delta (6-lead or 12-lead delta wound motors).

x. The soft-starter shall be controlled completely through solid state design algorithms. No moving electromechanical contacts shall be allowed.

xi. All adjustments shall be made from the front of the soft starter through keyboard (soft keys)

xii. The Soft starter shall have in-built/ remote display parameters. With following display

- Three Phase Currents
- Three Phase Voltages
- Shaft Power in kW / HP (selectable)
- Motor thermal capacity
- Motor Energy consumption (kWh)
- Power factor
- Run time in hours

The Soft starter shall have following fault indications

- Line failure
- Phase imbalance
- Over temperature – Motor
- Over temperature – Soft Starter
- Shorted Thyristor
- Open Thyristior
- Locked Rotor
- Motor output loss
- Overload - Shaft Torque
- Underload - Shaft Torque

- Over voltage
- Under voltage
- Excessive Starts
- Phase reversal

xiv. Shaft Power measurement without the use of external electro mechanical sensors.

xv. Shaft overload and under load protection shall be available through the controller, even in a by-pass configuration.

xvi. When fault conditions are detected, the controller shall inhibit starting or shut down SCR pulse firing.

xvii. The standard feature pump control shall be implemented to provide closed loop control of a motor to match the specific torque requirements of centrifugal pumps for both starting and stopping. This shall aid in eliminating the phenomenon commonly referred to as "water hammer".

xviii. The soft-starter shall be designed for three-phase control with two anti parallel SCRs in each phase. SCR-Diode combination shall not be acceptable.

- The PCB shall provide digital microprocessor control and supervision of all controller operation, including SCR pulse firing control.
- The PCB power supply shall be self-tuning to accept control power input from 100 to 240 or 380 to 500 V AC, 50/ 60 Hz.
- The SCR firing circuitry shall incorporate an RC snubber network to prevent false SCR firing.
- When fault conditions are detected, the controller shall inhibit starting or shut down SCR pulse firing.

xix. SCRs shall have the following minimum repetitive peak inverse voltage ratings:

- 200 to 525V: 1600 V
- 200 to 690V: 1800V

m) Soft Starter shall be ABB make PSTB 840-600-70/ Schneider make Alistart-48 or better from the approved make list.

35.1.24 Contactors:

The power contactors used in switchboard shall have following features:

a) The contactors shall confirm to ISO 13947 & the latest applicable standards

b) The power contactors shall be of, air break, single throw, triple pole, electromagnetic type.

c) The insulation class of contactor's coil should be B or higher.

d) Operating coils of all contactors shall be suitable for operation on 110/ 240 V, single phase, 50 Hz, AC supply.

e) Contactors shall be provided with at least two pairs of NO and NC auxiliary contacts.

f) Contactors shall not drop out at voltages down to 70 % of coil rated voltage.

g) All the switchgear selection for motor feeders shall be Type- 2 coordinated.

h) Motor starters shall be complete with auxiliary relays, timers and necessary indications.

35.1.25 Relays:

a) Main protective relays shall be Numerical type. They shall be suitable for semi-flush mounting with only flanges projecting on the front with connections from the rear.

b) All relays shall be enclosed in rectangular shaped, dustproof cases and shall be suitable for flush mounting.

c) All protective relays shall be in draw out cases with built in test facilities.

d) Auxiliary relays and timers shall be rated to operate satisfactorily between 70 % and 110 % of the rated voltage

e) Test block and switches shall be located just below each relay for testing unless otherwise specified. All auxiliary relay and timers shall be supplied in non-draw out cases.

f) All protective relays shall be provided with at least two pair of potential free output contacts, exclusively for Purchaser's use.

g) Relay cases shall have adequate number of terminals for making potential free connections, to the relay coils and spare contacts. Paralleling of contacts if any shall be done at the terminals on the casing of the relay.

h) Each relay shall have provision for easy isolation of trip circuit for the purpose of testing and maintenance.

i) All relays shall with stand out a test voltage of 2 KV, 50 Hz RMS voltages for one minute.

j) Auxiliary seal in units provided on the protective relay shall be shunt reinforcement type.

k) 250 kW & above rated motors shall be breaker controlled with motor protection relay Siemens '7SK 80' OR equivalent from approved make list.

35.1.26 Thermal Overload Relays

a) Starters shall be complete with a three element, positive acting, ambient temperature compensated, time lagged thermal overload relay with adjustable settings. The setting range shall be properly selected in accordance with the rating of the motor.

b) Thermal overload relays shall be hand reset type

c) 'Stop' push button of the starter and hand-reset device shall be separate from each other.

d) Overload relay hand reset push button shall be brought out on the front of the compartment door. Overload relay shall be provided with at least 1 'NO' and 1 'NC' or one changeover contact.

35.1.27 Timers

Thermal/ Electronics timer for change over in star-delta and ATS panel should be provided.

35.1.28 Switch And Contactor Ratings:

Switch and contactor rating for various motor starter modules shall be selected by the Contractor, based on the specifications. Contractor shall also select appropriate ratings & ranges for thermal overload relays. These details shall be subject to the Purchaser's approval.

35.1.29 Single Phasing Preventers:

a) Single phasing preventer relay shall be provided to protect motors against single phasing.

b) It should operate satisfactory from 320/ 480V. Timing range of delay start 0 - 45 seconds.

c) Toggle switch for Auto SPP by pass should be provided on front of unit.

d) The relay shall not operate for supply voltage unbalance of ± 5%. After sensing single phasing, the relay shall operate with a time delay of 2 to 3 secs.

e) The relay shall not operate for a 3- phase power supply failure. The relay shall be of the hand-reset type with a hand-reset push button. Resetting shall be instantaneous and independent of the adjusted time delay in the tripping of the unit. Visual indication for the operation of the relay shall be provided.

f) The relay shall be suitable for application to protect reversible and non reversible motors.

g) The relay operation shall be independent of the motor KW rating, the loading conditions prior to the occurrence of the single phasing

and RPM of the motor.

h) The relay shall be of the fail-safe type and shall operate to trip the motor when the relay internal wiring is accidentally open circuited.

35.1.30 Power & Control Wiring Connections:

a) Terminals for both incoming and outgoing cable connections shall be suitable for 1.1kV grade Al/ Cu conductor XLPE armoured cable and shall be suitable for connections of solder less sockets for the cable size.

b) Main PMCC incomer feeder shall be suitable for bus duct connections using Aluminum Bus bars

c) Both control and power wiring shall be suitable for Bus Duct/ Cable termination as per guidelines mentioned in transformer specifications.

d) Both control and power terminals shall be properly shrouded. Power terminals shall be of stud type.

e) 20% spare terminals shall be provided on each terminal block. Sufficient terminals shall be provided on each terminal block so that not more than one out going wire is connected to per terminal.

f) Suitable barriers of enclosures shall preferably separate terminals strips for power and control from each other.

g) Wiring inside the modules for power, control, protection and instruments etc shall be done with use of 1.1 kV grades, multistranded Cu, PVC FRLS wiring.

h) Power wiring inside the starter module shall be rated for full current rating of respective contactor but not less than 4.0 Sq. mm. 2.5 Sq. mm copper wire shall be used for current transformer circuits.

i) Other control wiring shall be done with 1.5 Sq. mm copper conductor wires.

j) Wires for connection to the door shall be flexible. All conductors shall be crimped with solder less sockets at the ends before connections are made to the terminals.

k) There shall be control transformer for control power supply (110/ 240V AC) and separate control bus.

l) Particular care shall be taken to ensure that the layout of wirings is neat and orderly.

Identification ferrules shall be filled to all the wirings terminations for ease of identification and to facilitate checking and testing.

m) Washers shall be used for all Copper and Aluminum connections.

n) Final wiring diagram of power and control circuit with ferrules nos. shall be submitted along with the panel as one of the documents against the contract.

35.1.31 Terminals

a) The outgoing terminals and neutral shall be brought to a cable alley suitably located and accessible from the panel front.

b) The current transformer for instruments metering shall be mounted on the disconnecting type terminal blocks. No direct connection of incoming or outgoing cables to internal components of the distribution board is permitted; only one conductor may be connected in one terminal.

35.1.32 Wire Ways:

a) The horizontal PVC wire way with screwed covers shall be provided at the top to take interconnecting control wiring between different vertical sections.

35.1.33 Indicating Instruments:

a) All analogue indicating meters shall be 144 x 144 mm size taut band with 240º Scale. All indicating meters shall be provided as per enclosed electrical Single Line Diagram.

b) Ammeters for motor feeders shall have suppressed scale up to 6 times beyond full load.

c) Dials shall be parallax free and white with black numbers and letterings & pointer shall be of knife-edge type. Such instruments shall be provided with zero adjustor accessible from the front.

d) Instruments shall have an accuracy class 1.0 or better.

e) Instrument dials shall be white with black numbers and lettering.

f) Ammeter and current coils of wattmeter's and ammeters shall continuously withstand 120 % of rated current and 10 times the rated current for 0.5 second without loss of accuracy.

g) Voltmeters and potential coils of voltmeters shall withstand 120% rated voltage continuously and twice the rated voltage for 0.5 seconds without loss of accuracy.

35.1.34 Metering Instruments:

a) Multifunction meters shall be provided for incomers, main pump motor feeders and outgoing feeders of 250A & above. Size of the MFM shall be 96 x 96 sq. mm & provided with following metering features:

i. Current, Voltage, Energy (kWh), MD (kW, kVA), PF & Hz etc.

ii. MFM shall be L&T make 'Quasar'/ Siemens OR equivalent.

iii. MFM shall be with accuracy class 1.0 or better & having RS 485 communication port.

b) Multifunction meters shall be suitable for operation from the secondary of CTs and VTs.

They shall be provided with a separate 3 phases, 4 wires type test terminal blocks for testing of meters without disturbing CT and VT secondary connections.

c) Current coils of meters shall have a continuous overload capacity of 120 % for both accuracy as well as thermal limits. Also the coil shall withstand at least 10 times rated current for 0.5 second without loss of accuracy.

35.1.35 Current Transformers:

a) Current transformers shall be of cast resin type. Insulation Class shall be Class 'E' or better.

b) Current transformer shall have a short time withstand rating equal to the short time withstand rating of the associated switchgear for one second for breaker feeders.

c) Unless otherwise specified, the minimum performance requirement of current transformers is as follows:

i. Measuring CTs -15 VA, accuracy class 1.0 or better.

ii. Protective CTs - 15 VA, accuracy class 5P20.

d) The above mentioned burdens are minimum required & it will be Contractor's responsibility to coordinate the current transformer burden with the requirements of relays, instruments and leads associated with that particular current transformer. Contractor has to provide sufficiency calculations for the same.

e) Current transformer (CT) shall have polarity markings indelibly marked on each transformer and at the lead terminations at the associated terminal block

f) CT shall be able to withstand the thermal and mechanical stresses resulting from the maximum short circuit current

g) Test links shall be provided in both secondary leads of the CTs to easily carry out current and phase angle measurement tests.

h) Identification labels giving type, ratio, output and serial numbers shall be provided.

35.1.36 Voltage Transformers:

a) Voltage transformers shall be of cast resin type. Insulation Class shall

be Class 'E' or better.

b) Unless otherwise specified, the minimum performance requirements of Voltage transformers are as follows:

i. Measuring VTs - 50 VA per phase and accuracy class 1.0

ii. Protective VTs - 50 VA per phase and accuracy class 3P.

iii. Dual purpose VTs - 100 VA and dual accuracy class 1.0/ 3P for metering and protection respectively. VA is per phase.

iv. The above mentioned burdens are minimum required & Contractor has to provide sufficiency calculations for the same.

c) All secondary windings of voltage transformers including open delta windings shall be rated for 110 V /√3, 110V/ 3 per phase.

d) Voltage transformer shall have a continuous over voltage factor of 1.2 and short time over voltage factor as follows:

i. 1.5 for 30 seconds in case of effectively earthed system.

ii. 1.9 for 8 hours in case of non-effectively earthed system.

e) Voltage transformers shall be complete with suitable rated primary, fuses. Primary fuses shall have a rupturing capacity equal to the rupturing capacity rating of the associated switchgear. All the secondary circuits of the VT shall be protected by MCBs.

f) It shall be possible to replace voltage transformers without having to de-energize the main bus bars.

g) The terminals of VT secondary and tertiary windings, which are required to be connected to earth, shall be earthed by an isolating link without a fuse.

h) Identification labels giving type, ratio, output and serial numbers shall be provided.

35.1.37 Push Buttons:

a) Push buttons shall have two normally open and two normally closed contacts unless otherwise specified. The contacts shall be able to make and carry 5A at 110V DC and shall be capable of breaking 1A inductive load at 110V DC. They shall be provided with inscription plates engraved with their functions.

b) Emergency stop' push buttons shall be of Mushroom type, lockable in the pushed position and shall be shrouded to prevent accidental operation. Key shall not be required for the operation of the push button.

c) The Internal wiring and terminal blocks shall meet the relevant requirements.

35.1.38 Auxiliary Transformers:

Any auxiliary voltage required for any of the component inside the switchgear shall be derived from the main supply by providing adequately rated auxiliary transformer mounted inside.

35.1.39 Indicating Lamps: Indicating lamps shall be:

a) Clustered LED type and of low watt consumption.

b) Provided with series resistors.

c) Provided with translucent lamp covers of colors 'Red', 'Green' and Amber' etc. as required.

d) Indicating lamp shall be of the double contact, bayonet cap type rated for operation at either 110 V AC or at the specified AC/ DC system voltage as applicable.

35.1.40 Control & Selector Switches: Control and selector switches shall be:

a) Rotary type with enclosed contacts.

b) Adequately rated for the purpose intended (Minimum acceptable rating is 10A continuous at 230V AC and 1A (inductive break) 220V DC.

c) Provided with escutcheon plates clearly marked to show the positions.

d) Control switches shall be spring return to normal type & provided with pistol grip type handles.

e) Selector switches shall be maintained contact stay put type. Switches in ammeter circuits shall be of break type contact. Selector switches shall be provided with oval handles.

35.1.41 Space Heaters:

a) Adequately rated anti-condensation space heaters shall be provided, one for each control panel, for each switchboard and for each marshalling kiosk.

b) Space heater shall be of the industrial strip continuous duty type, rated for operation on a 240 V, 1 phase, 50 Hz, AC system.

c) Each space heater shall be provided with a single pole MCB with overload and short circuit release, a neutral link and a control thermostat to cut off the heaters at 350 C.

d) Space heater indicated in the breaker modules represents the space heater for each vertical section of the switchboard. Where breakers are mounted in two-tier formation, then only one space

heater with associated MCB and thermostat is adequate for the vertical section

35.1.42 Cubicle Lighting/ Receptacle:

a) Each control cabinet, marshalling box, etc. shall be provided with interior lighting by means of 11 W CFL luminaries with door operated On/ Off switch.

b) A 240 V, 1 phase, AC receptacle (socket) plug point shall be provided in the interior of each panel with a MCB.

Routine and Acceptance Tests to be conducted by the manufacturer at their own risk and cost in presence of Purchaser/ Purchaser's representative during inspection & testing at manufacturer's works:

a) Following Routine tests as per ISO: 13947 and IEC: 60947 standards & other specified relevant ISO standards shall be performed by the manufacturer and witnessed by Purchaser/ Purchaser's representative on LV Switchgear panel complete with the accessories.

i. Dielectric test on main circuit.

ii. Test on auxiliary and control circuit.

iii. Measurement of insulation resistance of the main circuit.

iv. Tightness of main circuit.

v. Design and visual check.

vi. Dimensional check and BOM verification.

vii. High Voltage test on power & control circuit.

viii. Functional & mechanical operation test of all components.

ix. Measurement of thickness of sheet steel & paint.

x. Verification of wiring as per approved schematic.

b) Following Type Tests reports as per ISO: 13947 and IEC: 60947 to be submitted for the same rating & type of LV Switchgear panel conducted in past for review of Purchaser at the time of inspection & testing of equipment. Type test reports should be valid and not be older than the 5 years.

i. Dielectric test on main and auxiliary circuit.

ii. Temperature rise test.

iii. Making and Breaking test of switching elements.

iv. Degree of protection test.

v. Short circuit withstand test.

vi. Electromagnetic compatibility test.

c) Certified copies of all type and routine test certificates and Calibration Certificates of measurement instruments which are used during inspection shall be submitted for the Purchaser's review/ approval before dispatch of the switchgear.

35.1.43 Test Certificates:

a) Testing of switchgear shall be carried out at factory or at site as per standard in presence of Purchaser/ Purchaser's representative.

b) The test results shall be recorded on prescribed forms. The certificates for the test carried out at factory or at site shall be submitted in duplicate to the Purchaser/ Purchaser's Representative for approval. Components and equipment that are not fully interchangeable are liable for rejection. Contractor shall replace all such non interchangeable equipment at his cost.

35.1.44 Drawings/ Documents:

After award of contract, Contactor has to submit drawings/ documents for Purchaser's approval as mentioned below but not limited to:

a) General arrangement diagram showing dimensions of enclosure, length, widths and depth of enclosure and bill of quantity indicating the rating, make of each components and quantity.

b)

b) Complete assembly drawings of the switchboard/ distribution board/ MCC showing plan, elevation and typical sectional views and location of cable boxes and control cable terminal blocks for external wiring connections, etc.

c) Foundation plan showing the location of channel sills, foundation, anchor bolts and anchors, floor plans and openings.

d) Schematic power and control wiring diagrams with bus bar rating with material, instrument & control transformers, switchgear rating, control interlocks, relays, instruments, space heaters details etc.

35.2 LOCAL PUSH BUTTON STATIONS

35.2.1 Constructional Features

The constructional features of the local push button stations shall be as follows:

a) Metal enclosed, weatherproof, suitable for mounting on wall or steel structures. The enclosure shall be die cast aluminum or sheet metal of 2 mm thickness.

b) Dust and vermin proof.

c) Provide a degree of protection of not less than IP55.

d) Metal parts shall be given tropicalising treatment as per standards and painted with one coat of epoxy primer and two coats of light gray epoxy paint.

e) Provided with inscription plates of rear engraved Perspex with white letters on black background. The letter size shall be 6 mm.

f) Provided with two earthing terminals suitable for earthing wire /strip.

g) Provided with removable undrilled gland plate and cable glands for two nos. 5C x 2.5 mm² Copper conductor, XLPE insulated, armoured cable. The cable entry shall be from the bottom.

h) Earthing shall be provided by 8 SWG GI wire and connected to earthing system.

35.3 APFC PANEL WITH CAPACITOR BANKS

Scope of this specification covers design, manufacture, testing at manufacturer's works, supply, packing, forwarding and delivery from place of storage/ manufacturer's works to erection site including transit insurance, unloading, storage at site, assembly, erection, testing, installation, commissioning and performance demonstration of the following equipment with associated accessories.

35.3.1 Capacitor Banks:

a) The type of capacitors shall be All Polypropylene type double layer conforming to ISO 13585 - 1994 & having following specifications:

Supply	3 phase, 3 wire
Rated voltage	415 V
Rated frequency	50 Hz.
Permissible over voltage	1.1 Vn
Permissible over current:	1.5 In
Temperature category:	50º C

b) The capacitor shall be vacuum impregnated with liquid dielectric having high thermal stability.

c) The capacitors shall have Low Dielectric Loss of 0.5 W / kVAr. d) Each capacitor bank shall be provided with the 7% detuned filter.

e) * kVAr is net reactive compensation required to maintain 0.99 PF at 415 V Bus, i.e. excluding compensation required for detuned filters.

f) Bushing should have high mechanical strength & method of fixing should be proper so that no leakage occurs.

g) Auto/ Manual switch shall be provided in the APFC panel. For manual switching, every capacitor bank feeder shall be provided with ON & OFF push buttons along with the ON & OFF indications.

h) Minimum current rating under site conditions, of circuit breakers, contactors and cables shall be at least 150% of rated capacitor current, to take care of harmonics.

i) Contactor for switching of capacitor banks shall have AC-6b utilization category according to IEC 60947-4-1 & sized accordingly.

j) All the components shall be suitable for capacitor duty application.

k) The capacitor banks shall be complete with all parts that are necessary or essential for efficient operation. Such parts shall be deemed to be within the scope of supply whether specifically mentioned or not. Capacitor shall be designed to improve the power factor to 0.99 lagging

l) It shall be complete with the required capacitors along with the supporting post insulators, steel rack assembly, Al/ Cu bus bars, Al/ Cu connecting strips, foundation channels, fuses, fuse clips, etc. The steel rack assembly shall be hot dip galvanized.

f) Capacitor switching and automatic power factor correction panel shall be designed in such a way that power factor of 0.99 lagging shall always be maintained. Timings to cut in capacitors shall be provided in such a manner to facilitate capacitor discharging before next switching and shall also avoid hunting due to temporary fluctuations of load. The timer shall be provided in both auto and manual mode.

g) The Automatic power factor correction panel and capacitor panel are integral type, prewired including power connections. Due consideration shall be given for adding/removal of capacitor or other components and maintenance considerations. Contractor shall submit General Arrangement drawings of capacitor and capacitor control panel, with description of power factor control panel with its components.

h) For control circuit 415/ 240/ 110V AC control transformer shall be considered. VA burden to be decided by the Contractor.

i) Minimum clearance between live parts shall be phase to phase 25.4 mm & phase to neutral 20 mm.

j) Bus bars shall be sleeved with coloured heat shrinkable sleeves. All

the Bus bar supports shall be WASA type only.

k) Degree of protection shall be IP-42 for the enclosure, epoxy painted, powder coated with colour shade RAL-7032 for exterior & interior with minimum thickness 80 micron.

l) All necessary auxiliary contactors are included in scope.

m) Contractor shall note that verification of double layer construction shall be done on any one of the capacitor bank during inspection by opening the capacitor bank at no extra cost.

n) The cubicle shall be fabricated out of 2.0 mm thick cold rolled sheet steel & shall comprise of :

i. Isolating ACB/ MCCB

ii. Contactors with overload element

iii. Sequencing devices, timers and auxiliary relays for automatic sequential switching of capacitor units in and out of circuit.

iv. Auto-manual selector switch

v. Microprocessor based Automatic Power Factor Correction (APFC) Relay minimum 10 stage relays.

vi. Push button for opening and closing the power circuit

vii. Red and Green lamps for capacitors ON/ OFF indication

viii. Protective relays to protect the healthy capacitor units when one unit fails in a series connection

ix. Space heater and cubicle lighting & receptacles.

35.3.2 Principle of Operation:

On deviations from set power factor, the power factor controller shall release command signals to switch on/ switch off capacitor bank stages and maintain the set power factor.

35.3.3 APFC Relay:

APFC relay shall have following standard features:

a) The Automatic Power Factor Correction relay shall be of microprocessor based type and shall automatically switch ON/ OFF the capacitor banks to attain the value of "pf" close to the set value.

b) Switching shall follow first in first out (FIFO) method to ensure uniform use of all capacitor banks. At least eight steps shall be provided for switching.

c) To measure/ monitor power factor and VAR continuously. Status of

switching step shall be displayed through LED.

d) Following adjustment shall be available in APFC Relay.

i. Power factor

ii. Dead band capacitive region with respect to set power factor (PF).

iii. Inductive region with respect to set PF

iv. Operating time for programmable switching steps.

v. Auto/ manual selector switch.

vi. Manual step control.

e) All control knobs, LEDs for display and selector switches shall be mounted on the front face of relay casing/ panel.

f) It should be fully programmable. There should be a choice for customer to select operating sequence up to 4 to 5 which will have maximum number of steps of capacitors equal to fourteen (14). The sequence shall be arithmetic 1, 2, 3.....13, 14.

g) Operating time selection of time interval designation between switching stages shall be possible using time selector switches. The device shall take care that any stage which has just been switched out will only be reconnected by the pulse counter, after 60 sec. has elapsed so that it has safely discharged. This is a requirement for 415 V capacitors

h) Loss of voltage element- This would prevent abnormal switching surges on loss of supply. Also it would control the switching On/ Off surges.

i) Dead band features- Relay response sensitivity adjustable using dead band so that hunting is prevented.

j) Auto/ Manual control- This would help testing and commissioning at site as well as ease in operation when either mode fails during service time.

35.3.4 Performance Tests:

a) Contractor shall carry out all routine tests as specified in relevant ISO/ IEC standards on all major components and furnish copies of test reports for Purchaser's approval.

Wherever required, Contractor shall conduct the necessary type tests in the presence of Purchaser/ Purchaser's representative.

b) Contractor shall also carry out all routine and functional tests as specified in the relevant ISO on the assembled switchgear panels

in the presence of the Purchaser's representative at works before dispatch and furnish copies of test reports for approval. If required stage inspection will be carried out by the Purchaser.

c) During inspection, Contractor shall furnish copies of routine test report for all bought out items for Purchaser's approval.

d) Primary Injection Test for various currents & time settings shall be provided in routine test.

e) All the components shall be tested for their entire operating range & certification for the same shall be provided at the time of inspection.

35.3.5 Maintenance Requirements:

a) As far as possible the switchgear shall be so designed that no special tools are necessary for installation and maintenance. However, if special tools are required, the Contractor shall supply one complete set of such tools along-with the equipment.

b) Contractor shall furnish detailed inter panel wiring diagrams, internal wiring diagrams, detailed component layout drawings to carry out maintenance work.

35.3.6 Drawings/ Documents Required:

a) Dimensioned general arrangement drawings of capacitor and capacitor control panel.

b) Justification for number of steps for switching.

c) Fully dimensioned general arrangement drawings of capacitor and capacitor control panel with elevation side view, sectional view and foundation details.

d) Complete schematic and wiring diagrams for capacitor control panel.

35.4 CABLES & CABLING SYSTEM

The scope shall be inclusive of supply, installation, testing & commissioning of power, control cables, cable terminations, cable accessories, stripping of cable insulation, supplying and fixing of Aluminium lugs for aluminium cables & tinned plated copper lugs for copper cables and crimping the same to the conductor, supply and fixing of double compression cable glands including all labour supply and consumable material required for jointing/ termination. The rate shall also include the laying of cable in ground/ in cable trays / cleating to structure etc.

35.5 APPLICABLE STANDARDS:

The cables shall confirm to the latest applicable standards specified below.

In case of conflict between standards and this specification, this specification shall govern.

PVC insulated cables (for voltage up to 1100 V)	ISO/BS: 694
HRPVC & PVC insulated cables heavy duty	ISO/BS: 1554
Cross linked polyethylene insulated PVC sheathed cables	ISO/BS: 7098
Low frequency cables and wires with PVC insulation and sheath	IEC: 189-1 & IEC-189-2
PVC insulation and sheath of electric cables	ISO/BS: 5831
Polyethylene insulation and sheath for electric cables	ISO/BS: 6474
Conductors for insulated electric cables	ISO/BS: 8130
Methods of test for cables	ISO/BS: 10810
Specification for drums of electric cables	ISO/BS: 10418
Specification for PVC insulated cables for electricity supply	BS: 6346
Specification for PVC insulation and sheath of electric cables	BS: 6746

35.5.1 Constructional Features

a) HV power cables shall conform to 11kV Earthed grade (E), three core, stranded, Aluminium conductor, screened by extruded semi-conducting compound, cross-linked poly ethylene (XLPE) insulated, cores screened with non-magnetic metallic tape laid up with inner and outer extruded PVC sheath compound Type-ST2 and galvanized steel strip armouring. The cables shall generally conform to ISO/BS 7098-1985 with relevant parts thereof.

b) Armouring shall confirm to latest version of ISO/BS: 3975.

c) LV Power cables shall be 1.1kV grade, 4/ 3.5/ 3 Core, multi-stranded, Al/ Cu conductor, XLPE insulated, extruded inner & outer PVC sheath compound type ST2 and galvanized wire (up to 6 sq mm)/ steel strip (>6 sq mm) armoured cables. All single phase, Lighting cables, UPS cables shall have 100% Neutral.

d) All the control cables shall be 1.1kV grade, no. of cores (as per requirement/ application with minimum 2 spare cores for 7C & above) multi-stranded, Copper conductor, XLPE insulated, extruded inner PVC & outer PVC FRLS sheath compound type ST2 and galvanized steel round wire armoured.

e) All control cables shall be with following specific requirements:

   i. Copper conductor stranded class 2.

   ii. XLPE Insulated

   iii. Provided with inner extruded PVC and outer PVC FRLS sheath of extruded black PVC compound.

   iv. Galvanized steel armouring in the form of GI round wire.

v. Core identification shall be by printed numerals.

vi. The insulation over the individual conductor core will be colour coded.

vii. Minimum 2 spare cores for above 7C.

f) The DC power supply cable shall be two core, multistranded copper conductor, armoured cables with inner extruded PVC & outer PVC FRLS sheath. All control wiring shall be PVC FRLS insulated.

g) All the power, control cables used in the Hazardous area shall be flame proof type suitable for the intended application.

h) Earthing Cable shall be Single core multi-stranded Cu, 1.1 kV grade, XLPE insulated, un-armoured green coloured outer sheath with yellow strips/ band cable to be laid in trays, underground, trenches etc. as applicable.

i) Submersible Cables: Multi core flexible Cu conductor XLPE insulated & PVC sheathed heavy duty cable suitable for submersible application (in case of submerged pumps) shall be manufactured as per governing standards. High purity electrolytic grade, annealed Cu conductor shall be used. Cables shall be extruded inner & outer PVC sheathed. PVC compound shall be dielectric grade & shall be impervious to water, oils & grease etc. Similarly double PVC sheathing shall also be done as per ISO/BS: 5831/ 1984. Flexible inner sheath & high abrasion resistant flexible outer sheath is required for these cables. Double PVC sheathing shall be done so as to withstand abrasion & prevent ingress of water along the interstices of the cable. Core identification shall be by printed numerals. Conductors shall be as per ISO/BS 8130. Cable shall be constructed as per relevant ISO/BS/ IEC standards.

35.5.2 Cable Colours:

a) All cable cores shall be colour coded throughout their length and shall be so connected between switchboard, distribution board, plant and accessories, that the correct sequence or phase colours are preserved throughout the system.

b) The colour coding should be as follows:

i. 3 phase Red, Yellow and Blue

ii. single phase or dc supply Red and Black

iii. earth Green/Green with Yellow coloured band

iv. control Gray (DC)

35.5.3 Cable Conductors;

a) Cables up to 4.0 sq.mm shall be Cu multi-stranded conductor with galvanized steel round wire armoured & balance cables shall

be Al multistranded conductor with galvanized steel round wire/ flat strip armoured.

b) Single core cable shall have non magnetic material armouring.

c) Lighting final distribution circuits shall be of a minimum cross-section of 1.5 mm2.

d) Small control cables shall be of a minimum cross-section of 1.5 mm2.

e) Internal wiring of control panels shall be of a minimum cross-section of 1.5 mm2 flexible and multistranded.

f) Control cabling shall be of a minimum cross-section 1.5 mm2 for external use and 1.0 mm2 for internal use.

g) Cable Sizing shall be done as per design criteria specified in specifications.

35.5.4 Cable Numbering

All cables shall be allocated a unique number which shall be fixed to each end of the cable using a corrosion resistant label. Necessary loop at both ends shall be provided for future use and cables of different categories shall be tagged with the following subscripts and three digit number.

HV power	HV-P_ _ _
LV power	P_ _ _
Control	C_ _ _
Instrumentation	I_ _ _
Protection	PR_ _ _
Telecommunication	T_ _ _

35.5.5 Cable Terminations

a) Cable Lugs

i. Cable lugs shall be of tinned copper, solder less crimping type for Cu cables & AL lugs for the AL cables.

ii. The current rating of the lugs shall be same as that of the respective cable conductors.

iii. Bi-metal strip/ Bi-metallic lug shall be used whenever two different metals are to be connected together.

iv. Double holes extended neck (long barrel neck) type lugs shall be used in case of cables above 185 sq. mm.

v. Anticorrosion/ anti-oxidation compounds shall be used for crimping lugs. This shall especially be ensured for Al cable terminations & bimetallic terminations shall be used wherever required.

vi. If termination is done with crimping tool employing crimping die then forming dies shall be used to make the sector shaped conductor into a round conductor before crimping the lugs on the conductor. The lug must not be crimped directly on the sector conductor. Before crimping the lug, the conductor shall be thoroughly cleaned and special jelly applied over it to prevent further oxidation.

b) Cable Glands

i. Glands shall generally be of the double compression hexagonal type brass glands. Earth continuity of brass glands shall be assured.

ii. Double compression type cable glands shall be used. Cable glands shall be brass casting, machine finished and Nickel-plated to avoid corrosion and oxidation. Rubber components used in cable gland shall be of neoprene.

iii. For single core cables, gland shall be with brass ring.

iv. Glands for single core cables shall be constructed from non-magnetic materials.

v. Cable glands shall be with metric threads.

vi. Where holes for cable entries are not provided it shall be the responsibility of the Contractor to mark out and drill such holes. Burrs and swarf shall be removed, care being taken to ensure that swarf and filings, etc do not enter the equipment.

vii. For non-hazardous areas cable glands in situations where moisture may be present shall be double seal weatherproof type, gland shrouds shall be used and entry shall be sealed.

viii. For dry indoor situations, standard industrial glands with shrouds are acceptable.

ix. For hazardous areas, glands conforming to IEEE standard shall be used with double seal and shroud.

c) Trefoil Clamps for Single Core Cables:

i. All the single core cables shall be laid in trefoil formation only.

ii. The grouping & sequencing of three single core cables arranged in trefoil formation shall be done in such a way to ensure balanced current distribution.

iii. Trefoil clamp of suitable size & having non magnetic material shall be used.

iv. The Trefoil groups shall be held in trefoil clamps at an interval not exceeding 3.0 meters.

v. In addition to trefoil clamps as mentioned above, the trefoil groups of cables shall be additionally tied by means of 3.0 mm dia. nylon cord clamp at an interval not exceeding 750 mm.

d) Wherever applicable, supply & installation provision of bimetallic strip for connection between Al to Cu strip & GI to Cu strip shall be provided.

35.5.6 Cable Drums:

a) Cables shall be supplied in non-returnable wooden drums. The wood used for construction of the drum shall be properly seasoned and free from defects and wood preservative shall be applied to the entire drum. All ferrous parts shall be treated with a suitable rust preventive coating to avoid rusting during transit or storage.

b) Before winding the cables on drums, Contractor shall obtain Purchaser's approval for the drum lengths. Cable ends shall be sealed by non-hygroscopic sealing caps.

c) Contractor has to ensure reference of an arrow and suitable accompanying wording which shall be stenciled on the sides of the drums indicating which way it should be rolled. The number on each drum shall be either branded at the end of the drum or stamped on the metal attached to an end of the drum. The cable shall be placed on the drum in such a manner that it will be protected from injury during transit. Each end of the cable shall be firmly and properly secured to the drum. The drum shall be securely blocked in position so that the cable will not be displaced during transit. Cable ends shall be sealed by non-hygroscopic sealing caps.

d) It shall be the Contractor's responsibility to prepare the drum cutting schedule so that cable wastage is minimum while cutting.

e) Contractor shall obtain Purchaser's approval for the drum lengths.

f) The following information shall be given on the drums as a minimum:

i. Drum identification number

ii. Voltage grade

iii. Type of cable.

iv. Number of cores and cross-sectional area

v. Cable quantity

vi. Purchaser's order number and item number

vii. Total weight of cable and drum

35.5.7 Tests Before and After Laying of Cables at Site

Following Routine & acceptance tests on each drums as per ISO/BS 10810, ISO/BS 7098 standard & other specified relevant standards shall be performed by the manufacturer and witnessed by Purchaser/ Purchaser's Representative.

a) For 1.1 kV Power & Control cables:

i. Dimensional & visual check

ii. Conductor resistance test

iii. Insulation Resistance Test

iv. High voltage test

b) For 11 kV power cables:

i. Design and visual check

ii. Conductor resistance test

iii. Very low frequency AC HV test (instead of DC test)

iv. Insulation resistance including P.I. at rated voltage

v. Capacitance and tan delta

vi. AC leakage current

vii. Partial discharge measurement

c) All HV cables shall be subjected to DC or AC (preferably DC) high voltage test after terminating but before commissioning as per Table 6.0 in ISO/BS: 1255 (Code of practice for Installation & Maintenance of Power Cables up to and including 33kV).

d) Cables shall be checked for insulation resistance before and after jointing. The voltage rating of the Megger for cables of different voltage grades shall be as indicated below.

Voltage Grade	Megger rating
1.1kV	500V
11kV	1000V

e) Following tests in the presence of Purchaser/ Purchaser's representative shall be carried out at site before commissioning of cables.

i. Insulation Resistance test between phases and phase to Neutral and phase to earth.

ii. Continuity test of all the phases, neutral and earth continuity conductor.

iii. Sheathing continuity test.

iv. Earth resistance test of all the phases and neutral.

f) Cable Gland:

i. Cable glands required for glanding all cables at both ends shall be supplied by Contractor.

ii. A minimum of 20% of cable glands shall be supplied as spare.

iii. Cable glands shall be of SS 316 and double compression type suitable for armoured cables.

iv. All cable glands shall be weatherproof to IP-66. Flameproof glands wherever required shall be supplied with Ex (d) certification suitable for Gas Groups IIA / IIB / IIC.

v. All cable glands shall be with LSF shrouds.

vi. For all field items and junction box end, NPT threaded cable glands shall be used and for control room / control panel end, cable glands shall be ET threaded types.

g) Junction Boxes:

i. In order to make the most economic use of cable tray and trench capacity, multicore / multipair cabling shall be utilised in order to connect instrumentation groups by using suitably located junction boxes.

ii. The junction boxes shall have weather protection suitable for the area in which they are to be installed and for the type of circuit.

iii. They shall be readily accessible for maintenance and clearly labeled.

iv. Junction box shall be constructed of die cast aluminium and provide degree of protection IP 65.

v. Wires and terminals for the digital and analog signals shall be segregated within junction boxes.

35.5.8 Drawings/ Documents Required

a) As a part of the Bid, Contractor shall furnish the following :

i. General information

ii. Principal technical data

b) After award of contract it shall be the responsibility of Contractor to work out a detailed layout for the complete plant cabling system. The layout drawing shall be furnished for the approval of Purchase/ Purchaser's representative before commencement of installation including cable trays, cable racks/ trenches, accessories, tray supports, conduits etc.

c) Contractor to submit following drawings/ details after award of contract

i. Cable Sizing calculations

ii. Details of Installation of cables in trenches, on cable trays, directly buried etc at all locations inside the plant.

iii. Cable routing lay out inside and outside the plant with route marker provided at 30 meter interval.

iv. Bill of quantities of cables, lugs and glands.

v. HV Cable termination and mounting Kit Layout drawing.

d) Following Type Tests reports as per relevant standard to be submitted for the same rating & type of Cables conducted in past for review of Purchaser/ Purchaser's Representative by the Contractor at the time of inspection & testing of equipment. Type test reports should be valid and not be older than the 5 years.

i. Annealing test

ii. Tensile test

iii. Wrapping test

iv. Test for thickness of insulation & sheath

v. Physical test for insulation & sheath

vi. Tensile strength and elongation at break of insulation and sheath

vii. Loss of mass test

viii. Ageing in air oven

ix. Shrinkage test

x. Heat shock test

xi. Insulation resistance test

xii. High voltage test

xiii. Flammability test

35.5.9 Cable Tray & Accessories:

a) Cable trays shall be of Galvanised Steel/ Fiber Reinforced Plastic and of ladder/ perforated/ solid type, complete with all necessary coupler plates, elbows, tees, bends, reducers, stiffeners and other accessories and hardware as detailed in the relevant drawings. All hardware (i.e. bolts, nuts, screws, washers, etc) shall be hot dip galvanized.

b) Cable trays of ladder and perforated types and the associated accessories such as coupler plates, tees, elbows etc., shall be fabricated from 14 gauge (2.0 mm thick) mild steel sheets. Cable tray covers shall be fabricated from 16 gauge perforated (1.60 mm thick) M.S. sheets.

c) The cable trays shall be supplied in standard lengths of 2500 mm and clear inside widths of trays shall be as follows:

i. Perforated type trays: 150, 300, 450 and 600 mm.

ii. Ladder type trays: 300, 450, 600 and 750 mm

d) Cable trays, accessories and covers shall be painted with one shop coat of red oxide zinc chromate primer and two site coats of aluminium alkyd paint for indoor use.

e) For outdoor use, cable trays, accessories and covers shall be either galvanized or made of aluminium as specifically mentioned in the layout drawings.

f) For use in corrosive atmospheres both indoors and outdoors, the cable trays, accessories and covers shall be as per serial no. (e) above.

g) The spacing of rungs for ladder type of trays shall be 250 mm unless otherwise noted.

h) All finished cable trays and accessories shall be free from sharp edges, corners, burrs and unevenness.

35.6 EARTHING & LIGHTNING PROTECTION SYSTEM

35.6.1 Scope

a) The scope includes collection of data, design of the system as per relevant National/International Standards preparation of layout drawing supply of earthing conductors, earth electrode, earthing strips installation and approval to the satisfaction of electrical inspector under this tender specification.

b) Earthing system shall be provided to ensure equipment safety, personnel safety and facilitate designed operation of protective switching during earth fault conditions in the associated system.

35.6.2 Applicable Standards

The earthing and lightning protection system shall conform to the CEA guidelines and the latest applicable standards indicated below:

a) Code of Practice for Earthing : ISO/BS: 3043

b) Code of Practice for the Protection of : ISO/BS: 2309

c) Building and allied structure against

35.6.3 Earthing & Lightning system:

a) The design basis for designing earthing conductor is indicated under design criteria for electrical system. Earthing system shall be provided for complete plant i.e. pumping stations, switchyard and all electrical equipments as per the latest edition including all official amendments and revisions of ISO/BS-3043 and CEA guidelines.

b) All materials and fittings used in the earthing installation shall conform to the relevant Pakistan Standards or shall be approved by the Engineer's representative.

c) Contractor has to carry out soil resistivity test at, at least 4 locations for which locations shall be provided by Purchaser's representative. Testing to be done at each site.

d) Soil resistivity shall be carried out by Wenner four electrode method as described in ISO/BS 3043. Contractor has to carry out the test in presence of Purchaser's representative & test shall be carried out keeping electrode spacing as 1, 2, 4, 6, 8, 10, 15, 25 M (each, along all 8 directions) as per normal practice and report has to be submitted. Polar curves shall be used for measurement of mean soil resistivity, which shall be used in finding earthing resistance at a particular location. Mean soil resistivity values shall be approved by Purchaser's representative.

e) The Contractor shall base his earthing calculations on actual measurement carried out by him in the presence of Purchaser/ Purchaser's Representative.

f) Galvanized Iron flat / wire shall be used as earthing conductor.

g) The conductor sizes & types shall be as per specified in the Technical schedules in Volume- II, Section A3. Contractor to note that, the sizes indicated are minimum required & earthing conductor sizes shall be approved by the Purchaser/ Purchaser's representative on the basis of adequacy calculations submitted by Contractor.

h) The underground joints in the system shall be properly welded or brazed and the bolted type connection shall be made with structures/ equipments. Petroleum jelly shall be applied to contact surface of the bolted joints, which will be covered with bituminous compounded and tapes.

i) Earthing conductor shall be protected against mechanical damages considering the installation conditions.

j) The earthing system shall comprise one or more earth electrodes, earthing grid or a combination of these in order to obtain the required earth electrode resistance of less than one (1) Ohms/ or as per IEEE Std 80 -2000.

k) For equipment earthing, two earthing leads will be used if rated voltage of the equipment is 250 volts & above and one earthing lead will be provided for equipment rated below 250 volts.

l) The earthing conductors in outdoor areas shall be installed at a minimum depth of 600 mm below FGL.

m) For each 11 KV DP/ FP Structure, minimum 2 nos. of CI plate type earthing electrodes shall be provided. The earth plate shall be buried in specifically prepared earth pit- 3 mtr. below ground with alternate layers of charcoal and salt, 40 NB GI pipe with funnel with a wire mesh for watering and bricks masonry block and CI Cover complete as per ISO/BS 3043 with necessary length of double GI earth flat 25x6 mm bolted with lug to the plate complete connected to the required point of DP with end socket as per direction and duly tested by earth tester conforming to ISO/BS as per drawing and specifications complete with 600 x 600 x 6.0 mm CI earth plate.

n) For each transformer neutral, minimum 2 nos. of Cu plate type earthing electrodes shall be provided. The earth plate shall be buried in specifically prepared earth pit 3 mtr. below ground with alternate layers of charcoal and salt, 40 NB GI pipe with funnel with a wire mesh for watering and bricks masonry block CI Cover complete as per ISO/BS/IEEE 3043 with necessary length of double Copper earth flat 25x6 mm bolted with lug to the plate complete connected to the transformer neutral with end socket as per direction and duly tested by earth tester conforming to ISO/BS/IEEE as per drawing and specifications complete with 600 x 600 x 3.15 mm Copper earth plate.

o) For other equipment & area, Earth electrodes shall be of heavy duty galvanized mild steel of not less than 40 mm NB and minimum 3000 mm long. Where multiple rods are used they shall be separated

by a distance of not less than the driven length.

p) Each earth electrode pipe shall be welded at the top to a mild steel plate to which the earthing strips shall be connected. These connections shall each be housed in individual inspection chamber set which shall project 100 mm above the finished ground level and shall allow disconnection for testing of individual electrodes. The chamber shall be permanently marked `Electrical Earth'.

q) All materials used for the earth electrode installation shall be purpose made for the application and site conditions and shall be approved by the Purchaser's Representative.

r) All civil works, such as excavation, boring, provision of charcoal & salt in adequate quantity, backfilling for the installation of the earth electrodes and the earth pit/ inspection pit shall be in the scope of Contractor.

s) After the earth installation has been completed the Contractor shall demonstrate to the Purchaser/ Purchaser's Representative that the resistance of the electrodes to earth and the continuity of the earth network are within the limits specified. Any additional earth electrodes and test instruments required for the tests shall be provided by the Contractor.

t) Main Equi-potential Bonding Conductor: Main equi-potential bonding conductors shall be provided to connect the earth electrode system to conductive parts forming the Works.

u) Circuit Protective Conductors: An independent circuit protective conductor shall be provided for each circuit and may comprise one or any of the following as appropriate:

i. a separate core within a multicore cable

ii. a separate conductor installed within a conduit or trunking. Steel conduit or trunking shall not be used as a circuit protective conductor.

iii. The metal sheath of an armoured cable. The sheath shall be bonded to the metal work of the apparatus and to the apparatus earth bar, if any.

iv. the copper sheath of a mineral insulated copper sheathed cable

v. An independent earthing conductor MS or GS run adjacent to the circuit it protects.

vi. The size of the circuit protective conductor shall be

calculated in such a manner as not to take into consideration the contribution of any other parallel or fortuitous earth paths.

vii. The armoring of the supply cable shall not form the sole means of earthing a switchboard or large electrical load.

35.6.4 Important Instructions for Earthing:

a) Each pole of lightning arrestors shall be earthed with separate earth pit.

b) Two-earth conductor shall connect outdoor CT secondary winding to earth grid.

c) The switchyard fencing shall be earthed at every alternate block and the switchyard gate shall be earthed with flexible GI wire.

d) All the earthing material with laying etc. shall be included in the scope.

e) The entire plant will have an earth grid laid in trenches/ trays/ buried in the ground outside. The main earthing grid shall be embedded at a minimum depth of 600 mm below FGL which shall be connected to earth electrodes.

f) All interconnections of the earthing grid conductors will have welded type joints except at electrodes with disconnecting facility and at equipment with bolted connections. All indoor earthing grids will be suitably interconnected to the external earthing grid.

g) Each steel/ RCC column of the building will be interconnected to the floor-earthing grid.

Steel columns, steel strips / conduits, cable trays etc. will not be used as earth continuity conductors.

h) Disconnecting type facility shall be provided between Earthing grid & each earth electrode.

i) All connection between the conductors shall be welded/ brazed type. Metallic pipe, conduit, structures shall be bonded to lightning protection conductors to prevent the side flashover. But no metallic pipe, conduit, structure shall be used as air termination conductor or down conductor.

j) The down conductors shall be fixed with embedded brass posts (on concrete columns) with nuts & bolts used for fixing the saddle/ clamp (direct drilling of down comer and fixing with screw shall not be acceptable).

k) Cleats for 'earthing and lightning protection systems' shall be of GI.

l) The lightning protective conductor shall not be connected with the earthing above ground however both the systems shall be interconnected below ground.

m) The earth pits may require boring & drilling in the soil & the same shall be considered in Contractor's scope.

n) Earth electrode with disconnecting facility shall be provided so that the resistance of the independent earth electrode may be measured.

o) Internal earth Bus of each panel shall be connected to both ends to the earthing system by means of earthing conductor.

p) Metallic frames of all current carrying equipment, structures supporting and adjacent to current carrying conductors, lightning protection system conductors, metallic structures, metallic stairs, hand rails, fences shall be connected to a single earthing system. Neutral points of various systems shall be connected to the dedicated treated earth pits and these earth pits shall be interconnected to each other below ground.

q) All connections in the equipment earth conductors buried in ground (or otherwise) shall be cad welded/ brazed, whereas connection at equipment end shall be of bolted type. All connections shall be of low resistance. All bimetallic connection shall be treated with suitable compound to prevent moisture ingression. For Bimetallic bolted connection, bimetallic washers shall be used. All bolted joints shall have minimum two bolts to ensure proper surface contact. Termination of stranded conductors at earth inserts shall be with ring type/ lugs.

r) Galvanized conductors shall be touched up with zinc-rich paint where holes are drilled at site for bolting to equipment/structure.

s) Suitable earth risers approved by the Engineer shall be provided above finished floor/ ground level, if the equipment is not available at the time of laying of the main earth conductor. The minimum length of such risers inside the building shall be 200 mm and outdoor shall be 500 mm above ground level.

t) Metallic conduits and pipes shall be connected to the earthing system unless specified otherwise.

u) All cable trays will be earthed at minimum two places by suitable sized GI flats to main earthing system earth conductor. The cable trays shall also be earthed at a regular interval of not more than 10 meters by 25 x 3 mm GS flat.

v) Earthing Pits:

i. Adequate number of earthing pits shall be provided in conjunction with earthing grid for the earthing system. The minimum spacing between two adjacent earthing pits shall not be less than length of the electrode (minimum 3 m) and shall be kept 1500 mm away from footings of the structure.

ii. Earthing pits shall be located in ground, which has a reasonable chance of remaining moist. Arrangement comprising of GI pipe with top funnel with wire mesh shall be made to facilitate pouring of water to keep earthing pit wet.

iii. A galvanized iron strip of adequate size (as per calculations) shall be provided from plate electrode to about ground level to facilitate jointing with earth conductors. Each earth electrode ending at the pit shall be connected to suitable linking strips to connect and disconnect the earthing suitably.

iv. Earthing chamber shall be of RCC/ brick chamber of 600 mm x 600 mm, with removable 6 mm thick MS chequered plates. The covers shall have holes for handling. Earthing pits (chambers) shall be painted Green and the earth-pit number shall be marked on it.

v. Earthing cables crossing other metallic structures such as conduits pipelines etc shall be minimum 300 mm away from such structures.

vi. Earthing conductors shall be protected against mechanical damage.

vii. All earth lead connections shall be as short and direct as possible and shall be without kink.

viii. The main earth loop in plant area shall be generally routed along cables. When equipments are located away from main earth loops, suitable sub-loops shall be run up to them for deriving connections for individual equipment. The entire earthing system shall fully comply with the CEA guidelines and requirements.

ix. The Contractor shall have to carry out any changes as desired by the Electrical inspector or the Engineer in charge, in order to make installation conforming to the CEA guidelines 2010.

35.6.5 Lightning Protection

a) The lightning protection system need will be established by calculating the risk factor value of each building, structure etc. as per procedure given in ISO/BS/IEEE 2309-1989 and if found necessary the same shall be provided by the Contractor.

b) For Lightning protection of Civil Structures including RCC Buildings, fixing of 25x6 mm GI earth strip to roof as per ISO/BS/IEEE/ IEC std, saddle clamp, down comer connector etc. as required with all hardware shall be in Contractor's scope. Structural Columns (which are used as down comers for lightning protection system) bottom shall be connected to the earth pit with 25x6 mm bare GI strip.

35.6.6 Galvanizing

a) Wherever galvanizing has been specified, the hot dip process shall be used. The galvanized coating shall be of uniform thickness. Weight of Zinc coatings for various applications shall not be less than those indicated below

Fabricated Steel

i.	Thickness less than 2 mm, but not less than 1.2 mm	340 gms/ sq.m
ii.	Thickness less than 5 mm, but not less than 2 mm	460 gms/ sq.m
iii.	Thickness 5 mm and over	610 gm/ sq.m

b) Burrs shall be removed before galvanizing. Any site modification of galvanized parts should be covered well by zinc rich primer and aluminium paint.

c) Contractor shall ensure to use calibrated test equipment having valid calibration test certificates from standard laboratories traceable to National Standards.

35.6.7 Drawings/ Documents Required

The Contractor should prepare Layout drawings, after award of contract and before commencement of work for Purchaser's approval, showing the location of earthing grid, electrodes, interconnection grids and earthing leads to various equipment, down comers, isolating links etc. should be accompanied by design calculations.

35.7 LIGHTING & VENTILATION SYSTEM

35.7.1 Scope

a) The scope of the Contractor shall include design, supply and installation of all equipment necessary for a complete lighting and

receptacle system. The lighting system includes Lighting fixtures (indoor/ outdoor), lamps, lighting panels (LP), switchboards, Receptacles, JBs, cables/ wires for lighting/ receptacles, conduits etc. The supply of street light/ flood light poles as per ISO/BS/IEEE 2713 or ISO/BS/IEEE 3713 is also included in the Contractor's scope.

b) The various types of lighting fixtures with lamps shall be installed based on the mounting arrangement shown in the typical drawings enclosed with the specification. Installation scope shall include all material to mount the fixtures in proposed manner.

c) The various types of lighting fixtures as per specified in this specifications shall be assembled, installed, tested & commissioned by the Contractor.

d) The type of lighting fixtures and receptacles, illumination level and approximate quantity required shall be generally as per design criteria.

e) Lighting system installation shall be as per the tender specifications

f) It shall be the responsibility of the Contractor to work out complete detailed requirement of lighting and receptacle system for the whole plant and staff quarters including area lighting as per specification and accordingly procure and install them.

35.7.2 General Requirements

The Lighting system includes following items.

a) Lighting fixtures complete with Lamps and accessories. Only LED fixtures shall be used for both indoor & outdoor applications (Except for High mast lighting).

b) Lighting system equipment

c) Light control switches, receptacle units with control switch units, lighting wires, conduits, earth wires and other similar items necessary to complete lighting system.

d) Lighting fixture supports, street lighting poles and flood light towers/ poles.

e) Lighting main distribution board, lighting panels

f) Multi core cables for street, boundary and flood lighting

35.7.3 Lighting Layout

a) It shall be the responsibility of the Contractor to work out a detailed layout for the complete plant in order to provide the levels of illumination as indicated in the relevant standards

b) The types of fixtures to be used in various areas are also indicated in the above mentioned drawing. The Contractor shall be responsible for measuring the levels of illumination and uniformity after installation and establish compliance with the specification.

c) The lighting system will comprise the following:

i. Normal A.C Lighting: Normal lighting in all indoor and outdoor areas will be operated on 230V, 1Phase, 50 HZ A.C supply

ii. Emergency Lighting: Emergency Lighting shall be designed such that at all junctions, exit passages & strategic locations, Lux level shall be maintained above 10 Lux. Emergency light fitting shall be 240 V self contained 2 x 10 W LED fixtue with built in Ni-Cd battery having charging facility and six hours back-up time. The emergency light fittings shall be provided at strategic locations of each house/area. Emergency fixtures shall come in service when AC supply fails. Pump room and Electrical room shall be considered for Emergency lighting.

35.7.4 Applicable Standards:

The design, manufacture and performance of equipment shall conform to the latest standards specified below. In case of conflict between the standards and this specification, this specification shall govern.

a) Lighting Fixtures & Accessories for General & High mast

Electrical lighting fittings general and : ISO/BS/IEEE: 1913/ BS: 4533 safety requirements

Code of practice for industrial lighting : ISO/BS/IEEE: 6665

Code of Practice for Interior Illumination : ISO/BS/IEEE 3646

Code of Practice for Lighting of Public : ISO/BS/IEEE 1944

Thoroughfares

Calculation of co-efficient of utilization : ISO/BS/IEEE: 3646 (Part - III)

Testing procedure of photometric testing for LED luminaires LM 79

Testing procedure on the lifespan of LEDs LM 80

National Lighting Code SP72

Method of Measurement of Lumen Maintenance of Solid State Light (LED) Sources ISO/BS/IEEE:16105

Method of Electrical and Photometric Measurements of Solid-State Lighting (LED) Products

ISO/BS/IEEE:16106

Limits of Harmonic Current Emissions ISO/BS/IEEE 14700-3-2

DC or AC supplied electronic control gear for LED modules performance requirements IEC 62384

Lamp control gear: particular requirements for DC or AC supplied electronic control gear for LED modules

Environmental Testing: Test Z- AD: composite IEC 61347-2-13

temperature/ humidity cyclic test

Electro Magnetic compatibility (EMC)- Limits for	IEC 60068-2-38
Harmonic current emission-– (equipment input current ≤ 16 A per phase)	IEC 61000-3-2
EMC Immunity requirement	IEC 61547
LED modules for general Lighting-Safety requirements	IEC 62031
Classification of degree of protections provided by enclosures (IP Codes)	IEC 60529
Fixed general purpose luminaries	IEC 60598-2-1
General Lighting - LEDs and LED modules – Terms and Definitions	ISO/BS/IEEE:16101 / IEC TS 62504
LED Modules for General Lighting Part 1 Safety Requirements	ISO/BS/IEEE:16103(Part1)
LED Modules for General Lighting Part 2 Performance Requirements	ISO/BS/IEEE:16103(Part2)
Safety of Lamp Control Gear, Part 2 Particular Requirements Section 13 D.C. or A.C. Supplied Electronic Control gear for Led Modules	ISO/BS/IEEE:15885(Part2/Sec13)
Industrial lighting fittings with metal Reflectors :	ISO/BS/IEEE: 1777
Decorative lighting fittings :	ISO/BS/IEEE: 5077
Dust proof electric lighting fittings :	ISO/BS/IEEE: 4012
Dust tight electric lighting fittings :	ISO/BS/IEEE: 4013
Flood lights :	ISO/BS/IEEE: 10322/BS: 4533
Luminaries for street lighting :	ISO/BS/IEEE: 10322 Part 5
Water tight electric lighting fittings :	ISO/BS/IEEE: 3553/ BS: 4533, 5225(I)
High pressure mercury vapour lamps :	ISO/BS/IEEE: 9900/BS: 3677/ IEC: 188
Screw less terminal and electrical connections for lighting fittings :	ISO/BS/IEEE: 10322
High pressure sodium vapour lamps :	ISO/BS/IEEE: 9974
Emergency lighting units :	ISO/BS/IEEE: 9583
Ignition proof enclosures, dust-tight for elect. equipment :	ISO/BS/IEEE: 11005
Luminaries :	ISO/BS/IEEE: 10322(Part I to V)

Lighting System Equipment:

Arrangement for busbars, main connections and auxiliary wiring and marking :	ISO/BS/IEEE: 5578/ 11353/ BS: 159
Enclosed distribution fuse boards and cutouts for voltages not exceeding 1000V :	ISO/BS/IEEE: 2675/BSEN 60439
General requirements for switchgear and control gear for voltages not exceeding 1000 V :	ISO/BS/IEEE: 13947

Code of practice - installation and : ISO/BS/IEEE: 10118/BS: 6423

Maintenance of switchgear BS 6626, BS 6867

Factory built assemblies of switchgear : ISO/BS/IEEE: 8623/BS-5486/ IEC: 439 and control gear for voltages up to and including 1000 V AC and 1200 V DC

Miniature air break circuit breakers for : ISO/BS/IEEE: 8828/BSEN 60898

AC circuits

HRC cartridge fuse links up to 650 V : ISO/BS/IEEE: 9224/BS: 88/ IEC: 269

'D' Type fuses : ISO/BS/IEEE: 8187

Current transformers : ISO/BS/IEEE: 2705/BS: 7626/ IEC: 185

Voltage transformers : ISO/BS/IEEE: 3156/BS: 7625/

IEC: 186

Direct acting electrical indicating : ISO/BS/IEEE: 1248/BS: 89/IEC: 51

Instruments

A.C. electricity meters : ISO/BS/IEEE: 722/BS 5685

Electrical relays for power system : ISO/BS/IEEE: 3231/BS: 142/

protection IEC: 255

Switches for domestic and similar : ISO/BS/IEEE: 3854/BS: 3676

Purposes

Three pin plugs and socket outlets : ISO/BS/IEEE: 1293/BS: 546

Boxes for enclosure of electrical : ISO/BS/IEEE: 5133(1) Accessories

Rigid steel conduits for electrical wiring : ISO/BS/IEEE: 9537/BS: 31

Accessories for rigid steel conduits for : ISO/BS/IEEE: 3837/BS-31 electrical wiring

Flexible steel conduits for electrical : ISO/BS/IEEE: 3480

Wiring

Rigid non-metallic conduits for electrical : ISO/BS/IEEE: 9537/BS: 4607(2)

installations

Fittings for rigid non-metallic conduits : ISO/BS/IEEE: 3419/BS: 4607(2) PVC insulated cables for working : ISO/BS/IEEE: 694

voltages up to and including 1100 V

Tubular steel poles : ISO/BS/IEEE: 2713

Specification for copper rods and bars : ISO/BS/IEEE: 613 for electrical

purposes

Code of practice for phosphate iron : ISO/BS/IEEE: 6005/ BS: 3189

and steel

Fittings for rigid steel conduits for : ISO/BS/IEEE: 2667 electrical wiring

National Building Code of Pakistan (NBC) : NBC 2005

35.7.5 Other Design considerations for Lighting

a) Lighting panels shall be provided in various areas and circuit wiring to the lighting fixtures shall be made from lighting panels. Lighting panel shall comprise of Four pole MCB + RCCB (100 mA) for incomer and SP MCB's for each outgoing single phase circuits.

b) The wiring for lighting circuits in indoor areas will be done by wires run in GI conduits.

For outdoor lighting, wiring will be done by using armoured cables.

c) Lighting cable from Main lighting DB (MLDB) to Lighting panels shall be Al conductor, XLPE insulated, 1.1KV grade, laid in cable trays otherwise cleated along the wall/ column/ beam.

d) For lighting fixtures (Pump room) 1100V grade, 4C x 2.5 sq. mm. PVC insulated, multi stranded copper conductor armoured/ unarmoured cables shall be used.

e) For lighting fixtures (For Office, electrical room, toilets etc. areas) 1100V grade, FRLS PVC, multi-stranded Copper conductor wires of area not less than 1.5 sq mm laid in min. 20 mm dia GI conduit (above false ceiling) shall be used.

f) For 5/15A decorative sockets (For Office, toilets etc. areas) 1100V grade, FRLS PVC, multi-stranded copper conductor wires of area not less than 2.5/ 4.0 sq. mm. Cu laid in minimum 20 mm dia. GI conduit shall be used.

g) Wiring shall be concealed in wall below false ceiling with concealed switch board. Minor civil work like chasing wall, cut outs for conduit, switch board, Lighting Panel in wall, entries for tray, conduits etc. is in scope.

h) Lighting cable from MLDB to Lighting Panels and Lighting Panels to street light fixtures, shall be Al conductor, XLPE insulated, armoured, 1.1 KV grade, laid in cable trays otherwise cleated along the wall/ column/ beam and buried in the ground.

i) The point wiring for lighting/ receptacle/ exhaust fan/ wall mounted fan/ ceiling fan shall include conduits, conduit accessories, FRLS PVC insulated multistranded Copper conductor wires and earthing wires,

pull boxes, ceiling rose, clamps, cleats, hardware, accessories, anchor fasteners etc. It shall include wiring from lighting panel to switchboard and receptacles & switchboard to lighting fixtures. Sheet metal switchboard embedded in wall shall be considered for receptacles and lighting switchboards on wall shall be considered for lighting.

j) For power sockets in wall/ furniture, PVC switch box of approved make with switch plate & accessories and 16 Amp piano modular switches and 5/15A sockets etc. as applicable shall be considered. For all types of point wiring the receptacles with switches shall be included in the point wiring rate.

k) Lighting switchboard consisting of (*) no. of 6A piano switch without indicator, 1 no. 6A piano switch with indicator, 1 no. white coloured cover plate for (*) module (4/ 6/ 8/ 12 module), 1no. 2/ 3 pin shuttered socket of 5/ 15A and metal flush box.

l) Decorative socket switchboard consisting of (*) no. of 16A piano switch with indicator, (*) no. 2/ 3 pin shuttered socket of 5/ 15A and metal flush box, 1 no. white coloured cover plate for (*) module (4/ 6/ 8/ 12 module).

m) Lighting fixtures and fans will be grouped on the circuit wherever required. However, separate circuits shall be used for receptacles wiring.

n) Lighting Control Philosophy as per mentioned below shall be observed. From each switch –

   i. Max. 2 (3 in case unavoidable) normal LED light fixture.

   ii. Max. 4 (5 in case unavoidable) for LED down lighters

o) All indoor, outdoor & street light fixtures shall be controlled directly from respective Lighting Panels, through MCB.

p) Each lighting panel/ Receptacle DB shall have minimum 2 spare circuits of 10/ 16A SPN outgoing feeders. A circuit consists of R, Y, and B Phase each.

q) Lighting for staircase shall be controlled with flushed modular switch. The conduit for main staircase shall be concealed. Lighting for all staircases shall be with 2 way switch

r) Contractor shall note that any chasing in walls or cutouts or openings such as fixing of LPs, DBs, switchboards, concealing conduit in wall etc. in walls required shall be made before plastering of brickwork wherever applicable and installation rates quoted shall be inclusive of chasing, cutting & making the plaster as per standard practice.

s) Lighting for street light fixtures/ flood light fixtures shall be carried out with cables. The supply of cables, junction boxes, street light poles & structural steel required for mounting fixtures/ LPs etc. are in the scope of Contractor. The cable wiring shall include supply & installation of cable required from LP to the junction box mounted on street lighting pole / near indoor fixture and also between junction box mounted inside pole/near indoor fixture to control gear box and same for flood lighting, supply and installation of all termination accessories such as lugs, cable glands etc. DBO Contractor's scope shall also include excavation, preparation of soil bedding, supply and installation of protection cover, back-filling, supply and installation of cable route markers etc.

t) Point Wiring for lighting/ raw power receptacle/ emergency lighting:

i. Point wiring covers the wiring between a circuit of the lighting panel to switchboard and then from switchboard to lighting fixtures connected to that circuit of the lighting panel.

ii. For receptacle circuits point wiring shall cover wiring between circuit of the lighting panel to receptacles connected to that circuit of the lighting panel.

iii. The scope of the Contractor shall include the supply, erection, testing and commissioning of the above LPs/ DB boards for supply of power to the various sockets required for computers, raw power points etc. The point wiring rate from these DBs shall include supply of wires, conduits, cleats/ clamps etc. as may be required and shall be in the scope of electrical Contractor.

iv. The conduit point wiring rate for exhaust fan shall include conduits/ casing capping, conduit/ casing capping accessories, Switch boards, PVC insulated wires and earthing wires, pull boxes, ceiling rose, clamps, cleats, hardware, sheet metal switchboards fabricated out of 16 SWG. sheet steel housing 5 Amp piano switches. It shall include wiring from EXHAUST FAN DB/ RDB to switchboard & switchboard to exhaust fan as applicable. Neutral for individual circuit shall be run separate from DB to individual receptacles.

v. All mounting accessories like base channels, cross angles if required, nuts, bolts etc. shall be supplied by the Contractor under the scope of this contract.

vi. Required no. of 1-Ph & 3-Ph, industrial receptacles with respective 2P/ 4P ELCB (30mA) & 3/ 5 pin plug shall be provided for maintenance purpose.

vii. Receptacle & its ELCB shall be mounted in prefabricated CRCA box of 16 SWG, epoxy painted with shade 631of ISO/BS/IEEE-5. Earthing studs shall be provided for connecting external earthing with receptacle box.

viii. The Configuration of Industrial receptacle units shall be as per following – Combination 240V, 1-Ph, 50Hz, 3 pin, 15A Industrial receptacles with RCBO (30 mA). 415V, 3-Ph, 50Hz, 32/63A Industrial receptacles with respective RCBO (30 mA).

u) Lighting Fixtures and Accessories:

i. General

Normal supply voltage, phase and frequency	240 V, 1 ph, 2 wire, 50 Hz,
Variation in supply	
Voltage (AC & DC)	±10 %
Frequency	±5 %
Combined voltage & frequency	±10 %
Design ambient air temperature	50^0C

ii. The Luminaires shall be designed so as to facilitate easy maintenance, including cleaning, replacement of lamps/starters etc.

iii. Connections between different components shall be made in such a way that they will not work loose by small vibration.

iv. For each type of Luminaires the Contractor shall furnish the utilization factor tables to indicate the proportion of the light emitted by the bare lamps which falls on the working plane.

v. All Luminaires shall be supplied complete with lamps suitable for operation on a supply voltage and the variation in supply voltage, frequency and combined voltage and frequency of 10%, 5% and 10% respectively.

vi. The Luminaires and accessories shall be designed to have low temperature rise.

The temperature rise above the ambient temperature shall be as indicated in the relevant Standards.

vii. The Luminaires shall have a sturdy and corrosion resistant high pressure Die cast Aluminium housing with weatherproof gasket for lamp and control gear accessories. The Housing shall be Epoxy coated, without any cracks or thorough holes, made in a single piece of die-cast LM6 aluminium alloy. The luminaires shall be totally enclosed, dust tight and water proof.

viii. Heat sink used should be aluminium extrusion having high conductivity. The dimensions of luminaires shall be optimum and adequate to permit sufficient heat dissipation, through the body itself, so as to prevent abnormal temperature rise inside the lantern and consequential damage to the cover and gasket materials, LEDs, lenses and electronic drivers. Heat sink must be thermally connected to MCPCB/ LED light source.

ix. The Luminaire Housing shall be suitable for termination of Cable with Double Compression Cable Glands

x. The optical system shall consists of individual PC lenses on high power LEDs designed & tested to achieve typical street lighting distribution from the LED lantern. These lenses provided for individual LEDs are to be fixed on lens plate in order to have consistent light distribution from luminaires. Luminaires should conform to the photometric Distribution / requirements of Cut-Off / Semi Cut – off light distribution and optics as classified in ISO/BS/IEEE 1944.

xi. Suitable number of LED lamps shall be used in the luminaires. The manufacturer shall submit the proof of procurement of LEDs from OEMs at the time of testing

xii. The Luminaires shall be provided with high tensile heat resistant toughened glass of minimum 0.8mm thickness or UV resistant polycarbonate cover fixed with stainless Steel screws.

xiii. An extruded silicon loop gasket shall be provided in the lantern body to ensure a weather proof seal between the cover and the metal housing to exclude the entry of dust, water, insects, etc. Luminaire should conform to degree of protection of IP 65 or above. Felt gasket will not be accepted.

xiv. Year of Manufacture, Batch No., Serial Number or Identification No. Luminaire Manufacturer's Name / Logo, Wattage and Frequency should be embossed on the housing.

xv. LED luminaires, should conform to the various National / International standards for safety & performance. Manufacturer should provide test reports as per LM 79 & LM80. Lumen maintenance report as per LM 80 guidelines shall be submitted for the LEDs used along with the BID.

xvi. Luminaires should conform to the ISO/BS/IEEE standards for Safety & Performance and test certificates as per ISO/BS/IEEE 16107 should be provided by the manufacturer. In case of luminaires are imported, the CONTRACTOR shall conform to test parameters as per UL or equivalent standards.

xvii. The electrical component of the LED and LED driver must be suitably enclosed in sealed unit to function in environment conditions mentioned earlier.

xviii. All the connecting wires inside the Luminaire shall be low smoke halogen free, fire retardant cable.

xix. Adequate protection against Overloading, Short Circuit, Over Voltage, over temperature, Under Voltage, String Open shall be provided within the Luminaires

xx. Design of the thermal management shall be done in such a way that it shall not affect the properties of the diffuser.

xxi. The equipment should be compliant to IEC 60598-1, IEC 62031 and IEC/ PAS 62612 depending on the type of luminaire.

xxii. All the material used in the luminaires shall not contain any toxic material/ metal like mercury; shall be halogen free and fire retardant confirming to relevant standards.

xxiii. The Manufacturer shall have all the relevant testing facilities certified by an accredited laboratory and shall be offered for inspection to the Employer for verification of the required parameters and tests. CONTRACTOR shall confirm the same in the BID.

xxiv. The control gear shall comply with the provisions of IEC 61347-2-13, IEC 62031 and IEC 62384 as appropriate.

xxv. The LED lighting fixtures offered shall comply with the following requirements;

Sr. No.	Parameter	Design Requirement / Value
1.	Type	Dimmable LED Luminaires complete with all accessories for Street Lighting
2.	Rated Voltage	230 V
3.	Expected Frequency	50 Hz +/- 3%
4.	Operating Voltage Range	150 V to 270 V
5.	Power Factor	> 0.90
6.	Operating Temperature Range	0 Deg C to 50 Deg C
7.	Working Humidity	10% - 90% RH
8.	Driver Type	Constant Current based Electronic Driver
9.	Driver Efficiency	> 92%
10.	Driver Life	>20000 hrs.
11.	Protection required in Driver module	
a.	Short Circuit	To be provided by the contractor
b.	Over Voltage	To be provided by the contractor
c.	Over Temperature	To be provided by the contractor
d.	Under Voltage	To be provided by the contractor
e.	String Open Protection	To be provided by the contractor
12.	Luminaires IP Protection	Minimum IP 65 for Outdoor Fixtures
13.	Minimum Surge Protection	>4 KV
14.	THD	≤ 15%
15.	Power Factor	≥ 0.9
16.	Rated Minimum LED Life (L70)	50000 Burning Hours
17.	Rated Minimum Driver Life	20000 Burning Hours
18.	CRI	>70
19.	Junction temperature rise	< 85 Deg C
20.	Solder point temperature	< 70 Deg C
21.	Maximum temperature rise for Driver	<30 Deg C at 45 Deg C ambient
22.	Make of LED	Cree / Nichia/ Philips / Osram
23.	Make of Driver	Cree / Nichia/ Philips / Osram
24.	Operating Hours	Dusk to Dawn (max 12 Hrs.)
25.	Efficacy of Luminaires	>92lm/W
26.	Colour Temperature	5000K – 6000K
27.	Illumination Regulation	<5%
28.	Material used for following	
a.	Housing	Die cast aluminium/ extruded Aluminium body

Sr. No.	Parameter	Design Requirement / Value
		with powder coated finish
b.	Heat Sink	Aluminium extrusion
c.	Clip / Fasteners	Stainless steel.
d.	Diffuser	Toughened glass (0.8mm thick)/ UV stabilized Poly carbonate material
29.	Maximum temperature of Heat sink	<70 Deg C
30.	IK protection of Optic Cover	>IK05
31.	Wires used Inside Luminaires	Cu conductor, low smoke halogen free, fire retardant e-beam cable
32.	Cable gland IP protection	IP 65

xxvi. Each luminaires shall have a terminal block suitable for loop-in, loop-out and T-off connection by 230/ 415 V, 1 core, FRLS PVC insulated Copper conductor wires up to 4 sq. mm in size. In outdoor areas the termination at the luminaires shall be suitable for 1100 V, PVC insulated, Cu/ Al conductor, armoured cables of sizes up to 6/ 16 sq. mm conductor. Terminals shall be of stud or clamp type. The internal wiring should be completed by means of stranded Copper wire of minimum 1 sq. mm size and terminated on the terminal block. Terminal blocks shall be mounted with minimum two fixing screws.

xxvii. Mounting facility and conduit knock-outs for the luminaires shall be provided.

v) Earthing

i. Each luminary shall be provided with an earthing terminal suitable for connection to the earthing conductor of 12 SWG GI wire.

ii. Where separate control gear box is provided for housing the accessories the same shall be provided with an earthing terminal suitable for connecting earthing conductor of 12 SWG GI wire.

iii. All metal or metal enclosed parts of the luminaries/control gear box shall be bonded and connected to the earthing terminal so as to ensure satisfactory earthing continuity.

iv. Earthing of each pole shall be carried out with one dedicated earth electrode. The earth electrode can either be a GI coil type or GI pipe/ rod type electrode. The GI rod/ Pipe electrode shall be 2.5 m deep and can be hammered directly into the ground where ordinary soil is

present. For Hard strata, preparation similar to that mentioned in latest version of ISO/BS/IEEE 3043 or the latest version of Rural Electrification Corporation (REC) manual can be carried out. For GI Coil earthing, preparation as per REC manual shall be followed. The earth electrode shall be connected with two 25X6 sq.mm GI strips to the two distinct earth boss on the pole.

w) Painting/ Finish:

i. All surfaces of the Luminaries/Control gear box housing accessories shall be thoroughly cleaned and degreased. It shall be free from scale, rust, sharp edges and burrs.

ii. When enamel finish is specified, it shall have a minimum thickness of 2 mils for outside surface and 1.5 mils for inside surface. The finish shall be non-porous and free from blemishes, blisters and fading.

iii. The luminaire housing shall be stove-enamelled/epoxy stove-enamelled-vitreous enamelled or anodised as indicated under various types of fittings.

iv. The surface shall be scratch resistant and shall show no sign of cracking or flaking when bent through 90 deg. over 1/2" dia. mandrel.

v. The finish of the luminaries shall be such that no brigHV spots are produced either by direct light source or by reflection.

vi. External control gear box provided for housing accessories shall be painted or galvanised.

35.7.6 Outdoor/ Street Lighting Luminaries:

a) LED luminaires:

i. Street light LED luminaires shall be outdoor weather proof type for illumination of main roads, traffic islands etc.

ii. The luminaires shall be of semi-cut off with cast aluminium housing, acrylic or prismatic cover, polished aluminium reflectors, complete with integral mounted control gear, neoprene gaskets and with rear pipe entry.

iii. The luminaires shall be suitable up to 70/150/ 250 watts LED lamps and for mounting heights from 4 metres to 12 metres.

b) Metal Halide luminaires (For High Mast Only As Applicable):

i. Street light MH luminaries shall be outdoor weather proof type for illumination of main roads, traffic islands etc.

ii. The luminaries shall be of semi-cut off with cast aluminium housing, acrylic or prismatic cover, polished aluminium reflectors, complete with integral mounted control gear, neoprene gaskets and with rear pipe entry.

iii. The luminaries shall be suitable up to 150/ 250 watts MH lamps and for mounting heights from 4 metres to 12 metres.

c) Post Top Lantern:

i. Post top lantern luminaries shall be generally outdoor weather proof type for illumination of walkways, gate posts, gardens etc.

ii. The luminaries shall have cast aluminium spigot finished with corrosion proof paint for mounting, opal acrylic or high density polyethylene (HDP) diffuser bowl, complete with integral mounted control gear, neoprene gaskets, earthing terminal etc.

35.7.7 External Light Poles-Street Light/ High Mast Flood Light (where applicable)

a) All the Poles shall be designed to withstand the maximum wind speed as per ISO/BS/IEEE 875.

The top loading i.e., area and the weight of fixtures are to be considered to calculate maximum deflection of the pole and the same shall meet the requirement of BSEN 40-3:2000, pr EN-40-3-3.

b) These poles shall be coated with bituminous preservative paint on the inside as well as embedded outside surface. Exposed outside surface shall be painted with one coat of red lead oxide primer. After completion of installation two coats of aluminium paint shall be applied. One steel ladder shall be provided separately. The length of each step of the ladder shall be at least 300 mm and spacing between two adjacent steps not more than 300 mm.

c) The supply of poles shall be complete with fixing bracket/ necessary pipe reducer for fixing the fitting and also include the necessary associated pole mounted junction boxes. The required sizes of poles and the junction box shall be as indicated in the attached drawings.

b) The pole shaft may have Octagonal or Conical cross section and shall be continuously tapered with single longitudinal welding as applicable. There shall not be any circumferential welding.

c) All Octagonal or Conical pole shafts shall be provided with the

rigid flange plate of suitable thickness with provision for fixing foundation bolts. This base plate shall be fillet welded to the pole shaft at two locations .i.e. from inside and outside.

d) The welding of Octagonal or Conical pole shaft shall be done by Submerged Arc Welding (SAW) or using high end MIG/ TIG Welding process. The welding shall be carried out conforming to approved procedures. The welding shall be done as per qualified MMAW process approved by Third Party Inspection agency.

e) The Octagonal or Conical poles shall have integrated Junction box with open able door of adequate size (approximate 600mm length) at the elevation of 750 mm from the base plate.

f) The door shall be hinged type with mechanical interlock, dust proof, weather proof and vandal resistance and shall ensure safety of inside connections and components. The door shall be flushed with the exterior surface and shall have suitable locking arrangement. There shall also be suitable arrangement for the purpose of earthing.

g) The door of the integral Junction Box shall permit clear access to the components inside viz., termination strips, connectors, MCBs, cables etc.

h) The Octagonal or Conical pole shall be adequately strengthened at the location of the door to compensate for the loss in section.

i) Material for Octagonal or Conical Poles shall be HT Steel Conforming to grade S355JO; Base plate shall be FE 410 conforming to ISO/BS/IEEE 226/ ISO/BS/IEEE 2062; and Foundation Bolts shall be of EN.8 grade.

j) Aesthetic appearance - All the grooves and carvings of the pole unit shall be free from any kind of distortion for a pleasing aesthetic appearance.

k) The Octagonal or Conical poles shall be hot dip galvanized as per is 2629/ ISO/BS/IEEE 2633/ ISO/BS/IEEE 4759 standard with average coating thickness of 70 micron. The galvanizing shall be done in single dipping.

l) The Octagonal Poles shall be bolted on a pre-cast foundation with a set of foundation bolts for greater rigidity.

m) Top Mountings -The galvanized mounting bracket shall be supplied along with the Poles for Installation of the luminaires.

n) The Octagonal or Conical pole manufacturing & galvanizing unit shall be ISO/BS/IEEEO 9001: 2000 & ISO/BS/IEEEO 14001 certified to ensure consistent quality & environmental protection.

o) Electrical connections - Four way connectors shall be provided along with Slide lock suitable for connecting 1.1 kV grade, 4 C x 16 sq.mm Al cable. It shall also in-house 1 no. 6 amps DP MCB, 2.5 sq.mm connectors for looping with 2.5 Sq.mm Copper wires for connecting to the luminaire through 1.1 kV grade, 3 core X 2.5 mm^2 PVC insulated copper conductor flexible un-armoured Cable from the terminal block to the fixture within the pole. All the cables laid through the pipe shall be without any joint.

p) Two nos. Earth Boss shall be provided at the bottom of the pole (diagonally opposite) suitable for connecting 25X6 mm GI/ CU earth strip for earthing of the poles. Similar Earth Boss suitable for connecting 4 sq.mm copper wires shall be provided on the control plate inside the Junction Box for earthing of the electrical components.

q) Two nos. 50 mm NB HDPE sleeves of suitable length shall be provided through the foundation up to the Junction Box for entry of power cable.

r) The Contractor shall carry out all the relevant tests and inspection in the presence of the Employer or Third Party Agency, as may be selected by the Employer, before the dispatch of the poles at no extra cost to the Employer.

s) The CONTRACTOR shall inform the EMPLOYER at least Fifteen (15) days in advance, about the manufacturing schedule so that arrangement can be made for inspection. EMPLOYER reserves the right to waive the inspection at any stage.

t) All the material/ equipment/ accessories shall be supplied with manufacturer's test certificates.

u) CONTRACTOR shall submit the Proposed Product Catalogue, Detail Data sheet, spare parts list and drawing of Pole & Bracket along with the BID for each product quoted.

v) High mast shall be outdoor weather proof type for illumination of main roads and area lighting, wherever found necessary.

w) The high mast shall be continually tapered, polygon cross section, telescopically jointed steel fabricated construction. The mast shall be hot dip galvanised internally and externally. Weather proof door shall be provided near the base to permit access to winch, cables, plug, socket etc. The mast shall be designed for wind speeds depending upon wind pressure and direction as per relevant Pakistann Standards. Foundation bolts shall be included in the scope of supply.

x) The moving platform shall be of steel construction hot dip galvanised

and designed to hold the number of flood light luminaires specified. The control gear boxes shall be cast aluminium weather proof type mounted on the moving platform. The moving platform shall be raised or lowered with the help of winch, pulley system and stainless steel wire ropes. The winch shall be suitable for hand operation or alternate by electric power.

y) The mast shall be suitable for mounting numbers of luminaires as required. The standard mast heights are generally from 16 to 30 meters.

z) CONTRACTOR shall arrange for all the tools and equipments including M20 concrete foundations shall be provided for all the poles. Approx dimension of the foundation for evaluation purpose is 600X600X1700 mm. However, CONTRACTORs shall design as per the stability requirement and Soil bearing Capacity of each location. The Poles shall be bolted on a pre-cast foundation with minimum four foundation bolts for greater rigidity.

35.7.8 Emergency Light Luminaries

a) Emergency light fitting shall be 240 V self contained 2 x 11 W fixture with built in Ni-Cd battery having charging facility and six hours back-up time. The emergency light fittings shall be provided at strategic locations of each house / area.

b) Emergency fixtures shall come in service when AC supply fails.

c) Pump room and Electrical room shall be considered for Emergency lighting.

d) In addition to above emergency fixtures, every pump station shall be provided with two nos. of portable emergency luminary, which shall be with CRCA sheet steel enclosure, complete with metalized mirror reflector, leak proof re-chargeable battery rated for two hour discharge, battery charger, charger-on lamp, push button switches, automatic changeover switch/relay, two metre length cord with plug, mounting pads and other accessories required for satisfactory operation of the luminaries.

e) The luminaries shall be suitable for connection to 240 V, 50 Hz single phase supply. On failure of normal AC supply the luminary shall start automatically and on restoration of AC supply the luminary shall switch off automatically.

35.7.9 Accessories for Luminaries:

a) The Routine test on each of the offered Luminaire shall be carried out by the CONTRACTOR before dispatch. Following tests shall be carried out as Routine tests by the CONTRACTOR for the offered

Luminaires;

(i) Visual and Dimensional check

(ii) Checking of documents of purchase of LED

(iii) Insulation resistance test

(iv) HV test

(v) The Reverse polarity

b) Acceptance test shall be carried out by EMPLOYER or EMPLOYER's Representative on a sample of the lot offered for Acceptance. The Lot shall be different from the lot from which the Type test samples have been drawn. The cost of the testing shall be borne by the CONTRACTOR. Following tests shall be carried out as Acceptance tests by the CONTRACTOR for the offered Luminaires;

(i) Visual and Dimensional check

(ii) Checking of documents of purchase of LED

(iii) Insulation resistance test

(iv) HV test

(v) Over voltage protection

(vi) Surge protection

(vii) Reverse polarity

(viii) Lux measurement

(ix) Test for IP 65 protection

c) Following Type tests reports shall be provided by the CONTRACTOR for the offered Luminaires along with the BID;

(i) Resistance to humidity

(ii) Insulation resistance test

(iii) HV test

(iv) Over voltage protection

(v) Surge protection

(vi) Reverse polarity

(vii) Temperature rise Test

(viii) Ra (Colour Rendering Index) measurement test

(ix) Lux measurement

(x) Fire retardant Test

(xi) Test for IP 65 protection

(xii) Endurance Test,

(xiii) Life Test

(xiv) Photometric Measurements Test Report (IES LM 79)

(xv) LED Lumen Maintenance Test Report (IES LM 80)

(xvi) Vibration test as per ANSI

35.7.10 Lighting System Equipment:

a) Main Distribution Boards and Lighting Panels:

i. Main Lighting distribution board (MLDB) shall have MCCB as incomer & outgoing feeder with thermal magnetic release for O/L+S/C+E/F protections.

ii. This MLDB shall feed to different Lighting Panels/ Lighting DBs for further distribution.

iii. Where ever MLDB is not applicable, lighting feeder of appropriate rating shall be derived from the local distribution board. This feeder will feed to local LP catering to lighting requirements of that particular area.

b) Constructional Features:

i. Boards and panels shall be sheet steel enclosed and shall be fully dust and vermin proof, providing a degree of protection of IP-54 for indoor. Outdoor panels shall in addition be completely weather-proof with a sloping canopy for protection against rain and providing a degree of protection of IP-55. The sheet steel used for frame, frame enclosures, doors, covers and partitions shall be cold rolled 2.0 mm thick.

ii. The lighting panel for outdoor lighting shall have a programmable timer for automatic control of lighting along-with contactor, MCB, auto/ manual selector switch.

iii. All boards and panels shall be provided with hinged doors for access to equipment. Doors shall be gasketed all round with neoprene gaskets.

iv. A slotted metallic sheet shall be provided inside. Only the MCBs operating knobs shall project out of the metallic sheet slots for safe operation and neat appearance. Incomer to lighting panels shall be provided with Four pole MCB + RCCB

v. All accessible live connections/metals shall be shrouded and it shall be possible to change individual MCBs from the front of the boards/ panels without danger of contact with live metal.

vi. For floor mounting type distribution boards, adequately sized mounting channels shall be supplied and for wall/column/structure mounting type panels suitable mounting straps shall be provided.

vii. Adequate interior cabling space and suitable removable cable entry plates shall be provided for top/ bottom entry of cables through glands and or conduits as required. Necessary number of glands to suit the specified cable sizes shall be provided. Cable glands shall be screwed on type and made of brass.

viii. Two earthing terminals shall be provided to suit the earthing conductor.

ix. All sheet steel parts shall undergo rust-proofing process which should include 7 tank processing. The steel works shall then be painted with two coats of Zinc - chromate primer and two coats of final epoxy based finish paint of colour 631 as per ISO/BS/IEEE 5.

c) Busbars:

i. Busbars shall be of copper conductor of hard drawn (HD) and high conductivity.

ii. Busbars shall be provided with at least the minimum clearances in air as per applicable standards.

iii. Busbars shall be adequately sized for the continuous current rating such that the maximum temperature of the bus bars, bus bar risers/droppers and contacts does not exceed 85 C under site reference temperature.

iv. The bus bars, bus bar connections and bus bar supports shall have sufficient strength to withstand thermal and electro-mechanical stresses of the MCB's let through/cut-off current associated with the specified short-circuit level of the system.

v. Busbar supports shall be WASA type. Separate supports shall be provided for each phase of the bus bars.

vi. The neutral bus of the main 3 phase, 4 wire distribution board shall be 100% of the phase busbars.

d) Panels/ Boards' Component & Lighting Accessories:

i. MCB/ ELCB :

MCBs shall be C curve type for lighting panels.

For all the lighting panels RCCBs shall be with 100 mA sensitivity & for all receptacles RCBO sensitivity shall be 30 mA.

ii. MCCB :

MCCB requirements shall be as per specified in the LV switchgear requirements & as specified above.

iii. Indicating Instruments and Meters:

Whenever required, instruments and meters shall be of the flush mounting type. They shall be suitably mounted so as to provide for easy access to CTs and small wiring.

Instruments shall be of minimum 96 mm square size, shall have provision for zero adjustment outside the cover and black numerals on white dial.

Ammeter/Voltmeter selector switches having 3 positions and off, with stay-put contacts rated 10A shall be provided when specified.

Potential fuses shall be provided at the tap-off point from the bus bars for the voltmeters.

iv. Instrument Transformers:

Current and voltage transformers shall be of cast resin type, with insulation class B, & accuracy class 1.0 unless otherwise specified, it shall be the responsibility of the Contractor to ensure that the VA burden of the instrument transformer is adequate for the meters connected to it.

Test links shall be provided in both secondary leads of the CTs to easily carry out current and phase angle measurement tests. Facilities shall be provided for short-circuiting and grounding the CTs at the terminal blocks.

Voltage transformers shall be provided with suitably rated primary and secondary fuses.

v. Indicating Lamps:

Indicating lamps shall be of the clustered LED type, low watt consumption.

vi. Internal Wiring

Panels/ boards shall be supplied completely wired, ready for the external connections at the terminal blocks. Wiring shall be carried out with 1.1 kV grade, FRLS PVC insulated, multistranded Copper conductors. Conductors of adequate sizes shall be used to suit the rated circuit current.

Cross Ferruling i.e., engraved identification ferrules, marked to correspond with the wiring diagram shall be fitted at both ends of each wire.

All wiring shall be terminated on terminal blocks. Terminal blocks shall be one piece moulded rated 500 V, of reputed make of approved list, preferably stud type for higher current ratings such that wires are connected by cable-lugs and complete with nuts and washers. Terminals shall be adequately rated for the circuit current, the minimum rating shall be 20 A.

Terminals for circuits with voltage exceeding 125 V shall be shrouded.

Terminals shall be numbered and provided with identification strip for identification of the circuit.

Terminal blocks for CT secondary lead wires shall be provided with shorting and disconnecting/earthing facilities.

vii. Labels & Diagram Plate:

All door mounted equipment as well as equipment mounted inside the switchboard/panels shall be provided with individual labels with equipment designation/rating. Also the boards/panels shall be provided on the front with a label engraved with the designation of the board/ panel.

Labels shall be made of non-rusting metal, 3-ply lamicoid or engraved acrylic

Inside the door of the 1 phase ways lighting panels a circuit diagram/ description shall be fixed for reference and identification.

viii. Conduits:

Rigid steel/ non-metallic conduits and their associated fittings as required shall conform to applicable standards. The minimum size of conduit shall be 20 mm for surface installation and 25 mm for concealed installation.

Steel conduits shall be seamed by welding and hot dip galvanised. They shall be supplied in standard lengths of 5 metre.

Supply of conduits shall include all associated fittings like couplers, bends and tees as required for lighting system installation work.

ix. Junction Boxes:

Junction boxes with terminals shall be supplied for branching and terminating lighting cables when required for outdoor areas, three (3) phase receptacles etc.

The junction boxes shall be dust and vermin proof and shall be fabricated from 14 SWG sheet steel and shall be complete with removable cover plate with gaskets, two earthing terminals each with nut, bolt and washer. Boxes shall be additionally weather proof.

The boxes shall have provision for wall, column, pole or structure mounting and shall be provided with cable/ conduit entry knock outs, terminal blocks, and HRC fuses as required.

The terminal blocks, with specified number of terminals, shall be mounted securely on brackets welded to the back sheet of the box. The terminals shall be 600 V, grade, one piece construction complete with terminals, insulation barriers, galvanised nuts, bolts and washers and provided with identification strips of PVC. The terminals shall be made of Copper alloy and shall be of box clamp type.

The boxes shall be painted with one shop coat of red oxide zinc chromate primer followed by a finishing coat of paint.

x. Lighting Poles and Flood Light Pole Mounting:

Lighting poles for street lights and flood lights shall be of stepped tubular steel poles construction as per applicable standard. These poles shall be coated with bituminous preservative paint on the inside as well as embedded outside surface. Exposed outside surface shall be painted with one coat of red lead oxide primer. After completion of installation two coats of aluminium paint shall be applied.

Poles for mounting flood lights shall be supplied whenever required and as per typical attached drawing. Unless

otherwise specified, poles shall be painted with red lead oxide primer and two coats of aluminium paint. One steel ladder shall be provided separately. The length of each step of the ladder shall be at least 300 mm and spacing between two adjacent steps not more than 300 mm.

The supply of poles shall be complete with fixing bracket/necessary pipe reducer for fixing the fitting and also include the necessary associated pole mounted junction boxes.

The required sizes of poles and the junction box shall be as indicated in the attached drawings.

Outdoor JBs shall be minimum IP 55 protected.

Cable entry for street lighting junction boxes shall be from bottom.

Rain water canopy shall be provided at the top for the outdoor JBs. Terminal strip shall be provided for looping loop out of cables.

Street lighting JB shall consist of terminal strip (3 ways) for looping in & loop out of cables. The JB shall be provided with 6A MCB (C- Curve type) for isolation of lighting fixture, as well as sufficient arrangement (earthing studs) for termination of 2 nos. earthing connections.

xi. Ceiling Fans/ Wall Mounted Fans:

Ceiling/ Wall mounted fans shall be suitable for operation on 240 V, 1 phase,

50 Hz supply and shall be complete with standard mounting accessories such as suspension rods, top and bottom caps etc for ceiling fans and easy accessibility for wall mounted fans. The fans shall be supplied with appropriate speed regulators.

Exhaust fans, where ever required shall also be provided. The exhaust fan with all parts shall be according to ISO/BS/IEEE: 2312- 1967 & its latest amendment with IP-55 specification. The exhaust fan shall have epoxy powder coating with specially pretreated components for better resistance to corrosion and acid alkali flumes. The exhaust fan shall have totally enclosed highly efficient heavy duty motor with pressure die cast aluminum rotor mounted on two ball bearings.

The fans shall generally conform to the applicable

standards indicated in Tender. Details regarding blade sweep and suspension requirements shall be as per Project layout drawing/price schedule.

35.8 DC SYSTEM

35.8.1 Scope:

DC system (as applicable) shall include the following:

a) One set of 24/ 30 or 110 V DC, maintenance free rechargeable sealed lead acid batteries of adequate AH capacity shall be provided for control of electrical switchgears in the Plant.

b) Batteries shall be provided with battery charger cum DC distribution board. Battery charger shall include a float & float cum boost charger, indicating lamps and annunciations.

35.8.2 Sealed Maintenance Free Lead Acid Battery

a) Applicable Standards: The sealed maintenance free lead acid battery shall conform to the latest applicable standards specified below. In case of conflict between standards and this specification this specification shall govern.

Sealed lead acid: ISO/BS/IEEE: 1651, 1652 BS: 6290

b) The sealed batteries shall be a starved electrolyte type with electrolyte immobilized in a micro-porous material to allow recombining of generated oxygen internally. The battery shall be completely explosion resistant, shall tolerate freezing and shall not allow gases to escape during normal charging conditions. The battery shall not require any watering and be maintenance free.

c) Positive Plates: Positive plates shall be either of cast solid in pure lead in one piece with plante formation and shall have adequate mechanical strength or of tubular plate which shall consist of a suitable bar with spines cast of suitably alloyed lead to give adequate mechanical strength or of pasted positive plates consisting of either pure lead, low anti- monial lead alloy or lead calcium positive grids; having double separation with a glass wool retainer mat or any other suitable material placed against the surface of the positive plates for good service life.

d) Negative Plates: The negative plates shall normally be of the box type. End negative plates, if of box type may be of the half pasted type. Pasted plates shall have adequate mechanical strength and shall be so designed that the active material is maintained in intimate contact with the grid under normal working conditions.

e) Containers: The containers shall be made of plastics, or fiber

reinforced plastics (FRP). The container shall be spill proof, leak proof, explosion resistant and increased safety type enclosure.

f) Vent Plug: The vent plug shall be for safety pressure vent and of self resealing type.

g) Separators: The plate separator shall consist of a micro-porous matrix which shall serve as the mobiliser for the electrolyte. The battery separator shall maintain the electrical insulation between the plates and shall allow the electrolyte to permeate freely.

h) Connectors and Terminal Posts: Inter-cell and inter-tier connectors and terminal posts shall be of Copper. Terminal posts shall be designed to accommodate external bolted connection conveniently and positively. Each terminal post shall have two bolt holes of the same diameter, preferably at right angles to each other. The bottom hole shall be used to terminate the inter-cell connection. The top hole shall be left for terminal connections. All the metal parts of the terminals shall be lead coated. The junction between terminal posts and cover and between cover and container shall be so sealed as to prevent any seepage of electrolyte.

i) Electrolyte: The electrolyte shall be battery grade sulphuric acid conforming to latest editions of relevant standards. The sealed battery shall be transported with the electrolyte immobilized, sealed and fully charged.

j) Accessories: The battery shall be complete with accessories and devices, including but not limited to the following:

   i. Battery racks

   ii. Set of inter cell, inter-tier and interbank connectors as required for the complete installation.

   iii. One Voltmeter with suitable range and leads for measuring cell voltage

   iv. Insulated wrencher.

k) One set of terminals and cable boxes with glands for connecting cable as required.

l) Battery Racks: Battery racks shall be constructed from good quality teak wood and painted with two coats of approve alkali resisting paint. The construction of the racks shall be suitable for fixing to a flat concrete floor. The racks shall be rigid, free standing type and free from warp and twist. The completed racks shall be suitable for being bolted end to end to form a continuous row. Insulators shall be provided below the legs of the stands.

m) Capacity: The standard ampere-hour capacity at ten hour rate of discharge of the battery has been based on the requirements of loads as applicable and the minimum ambient temperature specified. Contractor shall guarantee that the capacity of the battery offered by him is adequate for the duty specified (all loads being coincident from the instant of supply failure even at the minimum ambient temperature as specified) assuming that the battery is fully charged to

i. 2.15 V at the start of the cycle

ii. 1.75 V/ cell at the end of the cycle.

n) The Battery sizing basis shall be IEEE 485 & the Contractor to note that the Battery sizing shall be done considering design ambient temperature of 50ºC & following factors.

i. Design Factor- Min. 1.1

ii. Aging Factor- Min. 1.25

iii. Temperature Correction Factor- Min. 1.1

o) Cell Identification: Each cell shall be marked in a permanent manner to indicate the following information:

i. Cell number

ii. Type of positive plate

iii. Ah capacity at 10 hour rate

iv. Type of container

v. Manufacturer's name

vi. Month and year of manufacture.

p) Drawings/ Document: The complete battery layout drawing shall be furnished as part of the tender and also after award of contract for Purchaser's approval.

35.8.3 Battery Chargers:

a) The battery charger and DC Distribution board shall conform to the latest applicable standards specified below. In case of conflict between the standards and this Specification, this Specification shall govern Basic climatic and mechanical durability tests for components for electronic and electrical equipment Environmental tests for electronic and electrical equipment Metal clad base material for printed circuits for use in electronic and telecommunication equipment Transformers and inductors (power, audio, pulse and switching) for electronic equipment ISO/ BS/ IEEE:9000

b) Requirements: The Battery Charger shall be microprocessor based & shall have two chargers mainly- i) Float Charger ii) Float cum Boost Charger.

c) The float & float-cum-boost type battery charger shall comprise silicon controlled rectifiers (SCRs) connected in a full wave bridge circuit. Each battery charger shall be suitable for float charging the battery under normal conditions and boost charging the battery when it has discharged during service conditions. The changeover from float to boost mode and vice versa shall be automatic. Microprocessor shall be MU 1000C or Equivalent makes from the approved makes.

d) The rectifier transformer shall be dry type and double wound with required number of taps. The DC output voltage during float charging shall be stabilized within ±1% of the set DC bus voltage for AC input voltage variation of ±10%, frequency variation of ± 5% and DC load variation from 0 - 100%. The voltage regulation shall be achieved by a constant voltage regulator having fast response SCR control. The ripple content shall be within ±1% of DC output nominal voltage with battery disconnected and shall be designed to have voltage regulation of ±1%. Also in any mode of operation, the maximum harmonics in the charger output shall not exceed 5%.The setting of the output DC bus voltage shall be adjustable between ± 10% of nominal rated voltage. There shall be provision for manual control if auto mode fails. Line surge suppressers shall be provided.

e) If the spare float charger supplying DC load fails, the load shall be fed from the point of connection at the tapping of the battery via adequately rated blocking diodes. Two blocking diodes in series shall be provided to take care of short circuit of any one diode

f) For boost charging the discharged battery after a mains failure, the rectifier shall charge the battery at high rate limited to the maximum boost charging voltage. The boost charging shall come on only when selected for boost mode manually. In auto control, the DC output current shall be stabilized within ±2% for AC input voltage and frequency variation of ±10% and ±5% respectively. There shall be provision for manual control if auto-mode fails. The boost charge voltage and current settings shall be adjustable between 70 to 100% of maximum boost charge voltage and between 30 to 100% of maximum boost charging current.

g) Boost charging time for charging the battery to full capacity from fully discharged condition shall not exceed 8 hours.

h) In the float charging mode, the charger shall be designed for supplying:

i. The DC loads of control, indication and annunciation circuits that remain energized during normal operation and the momentary closing and trip coil loads of circuit breakers, vacuum contactors; and

ii. The float charging current of the battery.

iii. 25% margin over the above load.

i) Battery charging equipment complete with all accessories shall be housed in a free standing sheet steel cubicle having degree of protection of IP 42. Sheet steel used for construction shall be 2 mm thick. The units shall be wired using 1100 V grade, FRLS PVC insulated, multi-stranded Copper conductor cables.

j) During boost charging the DC bus load shall be connected via two diodes in series connected to the tap cell of the battery. This is to take care in case of failure of standby charger supplying DC load.

k) All printed circuit cards shall be plug-in type, interlocked to prevent insertion in a wrong slot. Each card shall have LED indication on its front plate to indicate normal condition and readily marked test pins.

l) All components shall be accessible to the maintenance technician for easy disassembly and replacement. Access to parts of equipment shall be with minimum danger from all hazards.

m) All components and modules shall be clearly and unambiguously marked and all wiring colour coded and tagged

n) Each battery charger shall be provided with accessories that include, but not limited to the following:

i. Electronic controller comprising of power supply card, soft start cum current limit card, auto trickle mode card with facility for setting trickle charge current and monitoring battery current, error amplifier cards and pulse generating cards for achieving the DC output voltage stabilization of ±1% and also for achieving current limiting feature. The electronic controller shall have protection features with indications for under-voltage, over-voltage, earth fault, set output voltage and phase failure or voltage unbalance. The controller shall also be suitable for boost charging the battery in case of float-cum-boost charger.

ii. Boost charge current limiter with potentiometer to adjust the setting

iii. Silicon controlled rectifiers connected in full wave bridge circuit with ripple control devices and transient suppression network.

iv. 240 V AC compact fluorescent lamp fixture for internal lighting with MCB

v. Automatic voltage regulator unit with Manual/ Auto control switch

vi. Double wound, dry type, three phase suitably rated mains transformer with fuse protection and with one set of power factor correction capacitors to maintain a power factor of 0.85 (lag).

vii. Electronic controller comprising of power supply card, soft start cum current limit card, auto trickle mode card with facility for setting trickle charge current and monitoring battery current, error amplifier cards and pulse generating cards for achieving the DC output voltage stabilization of ±1% and also for achieving current limiting feature. The electronic controller shall have protection features with indications for under-voltage, over-voltage, earth fault, set output voltage and phase failure or voltage unbalance.

viii. Adequately sized necessary built-in accessories shall be provided such that on failure of the controller in auto mode the voltage can be effectively controlled manually.

ix. Filter circuit comprising of smoothing choke and condensers complete with HRC fuse with trip indication for filter condenser circuit

x. Coarse and fine control potentiometers for manual control

xi. Selector switch for mode of charging i.e. float charging / boost charging

xii. Off-load tap changing switch for changing the taps of the transformer

xiii. DC voltmeter with fuses and a three position selector switch

xiv. DC ammeter with shunt

xv. AC ammeter with selector switch for incoming AC power

xvi. AC voltmeter with selector switch for incoming AC power

xvii. MCB for incoming AC supply along with surge suppressers

xviii. MCB on DC output side with kick fuses and alarm contacts

xix. Voltage dropping diodes in load circuit during boost charging mode

xx. DC under voltage relay and earth fault relay

xxi. AC/ DC switching relays for alarm and indication circuits including buzzer

xxii. Cubicle space heater suitable for 230 V AC, 1 ph, 50 Hz supply, with MCB and thermostat

xxiii. Each battery charger shall be provided with the following alarms / indications:

AC and DC supply 'ON'

AC and DC supply fail

Modes of charging

Over voltage

Under voltage on DC side

Earth fault on DC side

AC/ DC MCB trip

o) The DC circuit switching shall be through DC MCBs only.

p) Power Electronic Components:

i. Diode and thyristors shall be of mono-crystalline type silicon, capable of providing continuous output at specified voltages. It shall have high power efficiency.

ii. If many diode or thyristor assemblies are connected in parallel, care shall be taken to ensure that each rectifier or thyristor operates within its rating and shares the load uniformly.

iii. Each diode or thyristor built in a multi-built assembly shall be provided with a short circuit protection to avoid complete shut-down of the equipment because of a fault on single unit. Suitable fuses shall be provided for such protection.

iv. Necessary spare capacity shall be built in the equipment to continuously supply full load even with one unit out of circuit.

v. The diodes or thyristors shall be protected against overvoltage due to chopping surges with the aid of snubbers (i.e resistor-capacitor combination and Metal oxide variator

35.8.4 DC Distribution Board:

a) The distribution board shall be of floor mounting design. Entry for

incoming and outgoing cables shall be from the bottom. Bus bars shall be of Copper. Incomers, bus coupler and outgoing circuits shall be controlled by suitably rated double pole MCBs suitable for DC application.

b) Constructional features, pre-treatment, painting and other aspects shall comply with the specifications for LV switchboard.

c) An earth busbar of 25x3 mm copper flat shall be provided along the length of the DB at the bottom. Two nos. earthing terminals shall be provided on the external face of the board for connection to the earthing grid.

35.8.5 Tests

a) The batteries, chargers and distribution boards and their components shall be subjected to routine/ acceptance tests as per the applicable standards. For battery & battery charger, following tests are also to be carried out:

i. Visual checks for dimensions and general arrangement.

ii. Wiring checks.

iii. Functional checks.

iv. IR Test.

v. Capacity test.

vi. Test for voltage charging and discharging.

vii. Ampere-hour and watt-hour efficiency test.

viii. Hipot test, excluding electronic controller, at 2 kV AC for one minute.

b) Certificates of type tests carried out on similar equipment not older than 5 years shall be furnished by Contractor.

1.1.3 DRAWINGS/ DOCUMENTS REQUIRED:

After award of contract Contractor has to submit the below mentioned drawings/ documents for Purchaser's approval :

a) Dimensioned general arrangement drawings

b) Fully dimensioned general arrangement drawings of battery and battery charger with elevation, side view, sectional view and foundation details

c) Complete schematic and wiring diagrams.

d) Detailed BOM for the complete panel, with details of switchgear, controller, components etc.

SECTION-36 SAFETY EQUIPMENTS/ REQUIREMENTS AND MISCELLANEOUS ITEMS:

Following safety procedure and practice should be provided by Contractor in switchgear room/ sub-station as per latest edition of GOP MRS SPECS 1967 VOL-1. 5216.

900 mm wide antiskid insulating mat as per ISO/BS/IEEE 15652 and of reputed make to be spread in front of the 11kV, 415V switch gear panels & power DBs, DCDB etc.

First aid box with all the standard contents.

First aid chart made of cloth for electrical shock treatment printed in English, Hindi and Gujarati duly framed with front glasses.

Charts/ drawings duly framed with front glass.

HV and LV power supply single line diagrams in adequate sizes approved by Purchaser/ Purchaser's representative & in line with the local electrical inspector.

Routine maintenance schedule for High Voltage Switchgear, Distribution Transformers, Low voltage Switchgears, APFC panels, Fire Alarm System, UPS system etc.

Provision of portable type Class A, B, C, and D type fire extinguishers at various locations in line with the statutory requirements.

36.1 FIRE SAFETY

The requirement of hand appliance in switchgear room, electrical equipment room shall be provided as per Clause 4.0 of Fire Protection Manual by Regional Tariff Committee, 10th edition 1988.

Water Sealing & Fire Barriers at appropriate locations as specified in this specifications & good engineering practices.

36.2 DEGREE OF PROTECTION

The enclosures of the control cabinets, junction boxes and Marshalling boxes, panels etc. to be installed shall provide minimum degree of protection as detailed here under

a) Installed outdoor – IP 55

b) Installed indoor – IP 54

The degree of protection shall be in accordance with ISO/BS/IEEE 13947 (Part I)/ IEC 947 (Part I)/ ISO/BS/IEEE 2063/ IEC 529

36.3 ELECTRICAL EQUIPMENT FOR HAZARDOUS AREAS

The electrical equipments for hazardous areas shall be selected as per ISO/BS/IEEE 5572. Following factors shall be considered for proper selection of electrical equipments for use in Hazardous Area.

36.3.1 Area Classification (Zone):

Gas Classification (Group) – The characteristics of the gas or vapour involved in relation to the ignition or energy and safe gap data

Temperature Classification - The ignition temperature of the gas or vapour involved or lowest value of the ignition temperature, if more than one combustible material is present.

Environmental conditions – In which apparatus is to be installed. The selected electrical apparatus shall be adequately protected against corrosive and solvent agencies water ingress, thermal and mechanical stresses as determined by the environmental condition.

SECTION-37 INSTALLATION, TESTING & COMMISSIONING – ELECTRICAL EQUIPMENT:

37.1 GENERAL:

In accordance with the specific installation instructions, as shown in Contractor's drawings or as directed by the Engineer In Charge the Contractor shall unload, erect, install, wire, test and place into commercial use of all electrical equipment included in the contract. Equipment shall be installed in a neat manner so that it is level, plumb, and properly aligned and oriented.

The Contractor shall furnish all supervision, labour, tools, equipment, rigging materials and incidental materials such as bolts, wedges, anchors, concrete inserts etc. required to completely install, test and adjust the equipment.

Drawings, instructions and recommendations shall be correctly followed in handling, settling, testing and commissioning of all equipment and care shall be exercised in handling to avoid distortion to stationary structures, the marring of finish, or damaging of delicate instruments or other electrical parts.

The Contractor shall erect and commission the equipment as per the instructions of the Purchaser/ Engineer In Charge and shall extend all co-operations to him.

In case of any doubt/ misunderstanding as to correct interpretation of drawings or instructions, necessary clarification shall be obtained from the Engineer's Representative. The Contractor shall be held responsible for any damage to the equipment consequent to not following instructions correctly.

The Contractor shall move all equipment into the respective buildings through regular doors or floor openings provided specifically for the equipment. The Contractor shall make his own arrangement for lifting of equipment.

Where assemblies are supplied in more than one section, the Contractor shall make all necessary mechanical and electrical connections between sections including the connections between bus bars/ wires. The Contractor shall also carry out the adjustments/ alignments necessary for proper operation of the circuit breakers. All insulators and bushings shall be protected against damage during installation. Insulators or bushings chipped, cracked or damaged due to negligence or carelessness shall be replaced by the Contractor at his own expenses.

The Contractor shall take utmost care in handling instruments, relays and other delicate mechanisms. Wherever the instruments or relays are supplied separately, they shall be mounted only after the associated control panels have been erected and aligned. The blocking material/ mechanism employed for the safe transit of the instruments and relays shall be removed

after ensuring that the panels have been completely installed and no further movement of the same would be necessary. Any damage to relays and instruments shall be immediately reported to the Engineer In charge.

Equipment furnished with finished coats of paint shall be touched up by the Contractor if their surface is spoiled or marred while handling.

Foundation work and grouting of fixing bolts or channels for all transformers, switchgear, motors, and control panels shall be carried out by the Contractor.

37.2 POWER/ DISTRIBUTION TRANSFORMERS

Inspection, storage, installation, testing and commissioning of transformers shall be in accordance with the latest Pakistann Standards Code of Practice ISO/BS/IEEE: 10028. All commissioning tests as applicable, vide Appendix B of ISO/BS/IEEE: 10028 (Part II) shall be carried out. Fire Wall of 4 Hr fire rating shall be provided between two transformers.

37.3 HV/ LV SWITCHGEAR CONTROL PANELS

Switchgear control panels shall be installed in accordance with the latest Pakistann Standard Code of Practice 10118. The switchgear panels shall be installed on finished surface or concrete or steel sills. The Contractor shall be required to install and align any channel sills which form part of the foundations. Tape or compound shall be applied where called for. The base of outdoor type units shall be sealed in an approved manner to prevent ingress of moisture.

Following minimum clearances shall be observed while finalizing the HV/ LV panel layouts-

a) Minimum clearance of 1.0 meter shall be maintained from the rear of the panel to the nearest wall /structure.

b) Minimum clearance of 2.0 meter between panels facing opposite to each other.

c) Side clearance for LV panels shall be either $\leq$ 200mm or $\geq$ 800 mm.

d) For HV metal enclosed, indoor panels, Minimum 1 meter clearance from all sides & 1.5 meter in the front.

Emergency Exit doors shall be provided for electrical room, complying with the requirements of NBC 2005 latest edition.

After installation of all power and control wiring, the Contractor shall perform operating tests on all switchgear and panels to verify the proper operation of switchgear/ panels and the correctness of the interconnections between various items of equipment. This shall be done by applying normal a-c or d-c voltage to the circuits and operating the equipment. Megger tests for

insulation, polarity checks on the instrument transformers, operation tests on equipment, and installation tests shall be carried out by the Contractor who shall also make all necessary arrangements for proper functioning of the equipment.

37.4 EARTHING AND LIGHTNING PROTECTION SYSTEM

The Contractor shall install copper/ steel conductors, braids, etc., required for the system and individual equipment earthing. All work such as cutting, bending, supporting, painting/ coating, drilling, brazing/ soldering/ welding, clamping, bolting and connecting onto structures, equipment frames, terminals, rails or other devices shall be in the Contractor's scope of work. All incidental hardware and consumables such as fixing cleats/clamps, anchor fasteners, lugs, bolts, nuts, washers, bituminous compound, welding rods, anti-corrosive paint as required for the complete work shall be deemed to be included by the Contractor as part of the installation work.

The quantities, sizes, material of earthing conductors and electrodes to be installed as per requirement. Routes of the conductors and locations of electrodes shall be shown in the earthing layout drawings, which are to be prepared by Contractor & approved by Purchaser's representative.

The work of embedment of earthing conductor in RCC floors/ walls along with provision of earth plate inserts/ pads/ earth risers shall be done by the Contractor when the floors are cast or during construction of walls. Contractor's scope of installation shall also include, laying the conductors in position with 60 mm concrete cover, making welded connections to inserts/pads/risers above the floor near the equipments. The embedded conductors shall be connected to reinforcing rods wherever necessary.

If the tap connections (earthing leads) from the floor embedded main earthing grid to the equipment are more than 500 mm long then the same shall be embedded in floor by the Contractor where required, together with associated civil work such as excavation/chasing, concreting and surfacing. The concrete cover over the conductor shall not be less than 60 mm.

Installation of earth conductors in outdoor areas, buried in ground, shall include excavation of earth up to 600 mm deep 450 mm wide, laying of conductors at 600 mm depth, brazing/ welding as required, of main grid conductor joints as well as risers of length 500 mm above ground at required locations and then backfilling material to be placed over buried conductor shall be free from stones and other harmful mixtures. Backfill shall be placed in layers of 150 mm, uniformly spread along the ditch, and tampered utilizing pneumatic tampers or other approved means. If the excavated soil is found unsuitable for backfilling, the Contractor shall arrange for suitable material from outside.

Installation of earth connection leads to equipment and risers on steel

structures/ walls shall include laying the conductors, welding/ cleating at specified intervals, welding/ brazing to the main earth grids risers, bolting at equipment terminals and coating welded/ brazed joints by bituminous paint. Galvanized conductors shall be touched up with zinc rich paint where holes are drilled at site for bolting to equipment/ structure.

Electrodes shall be installed in constructed earth pits, and connected to main buried earth grid, The scope of work shall include excavation, construction of the earth pits including all materials required for construction of earth pits, placing the rod and fixing test links on those pipe/ rod/ plate electrodes in test pits and connecting to main earth conductors.

Installation of lightning conductors on the roofs of buildings shall include laying, anchoring, fastening and cleating of horizontal conductors, grouting of vertical rods wherever necessary, laying fastening/ cleating/ welding of the down comers on the walls/ columns of the building and connection to the test links to be provided above ground level.

Installation of the test links shall include mounting of the same at specified height on wall/column by suitable brackets and connections of the test link to the earth electrode.

Whenever main earthing conductor crosses cable trenches, they shall be buried below the trench floor.

Suitable earth risers shall be provided above finished floor/ ground level. If the equipment is not available at time of laying of the main earth conductors, the minimum length of such riser inside the building shall be 200 mm and outdoors shall be 500 mm above ground level. The risers to be provided shall be marked in project drawings.

Earth leads and risers between equipment earthing terminals and the earthing grid shall follow as direct and short a path as possible.

An earthing mat shall be provided under each operating handle of the isolator and operating mechanism of HV breakers. Operating handle of the isolator and supporting structure shall be bonded together by a flexible connection and connected to the earthing grid.

A separate earth electrode bed shall be provided adjacent to structure supporting lightning arrestors. Each connection shall be as short and as straight as practicable. For arrestors mounted near transformers, earth conductors shall be located clear off the tank and coolers.

Wherever earthing conductors passes through walls, galvanized iron/PVC sleeves shall be provided for the passage of earthing conductor. The pipe ends shall be sealed by the Contractor by suitable water proof compound.

37.4.1 Earthing Connections:

a) All connections in the main earth conductors buried in earth/

concrete and connection between main earthing conductor and earth leads shall be of welded type.

b) Connection between earth leads and earthing terminal provided on the equipment shall be bolted type.

c) All bimetallic connections shall be treated with suitable compound to prevent moisture ingression.

d) Metallic conduits and pipes shall be connected to the earthing system.

e) Lightning protection system down conductors shall not be connected to other earthing conductors above ground level. Also no intermediate earthing connection shall be made to lightning arrester and transformer earthing leads which shall be directly connected to pipe electrode.

37.4.2 Earth Electrodes:

a) Electrodes shall as far as practicable, be embedded below permanent moisture level.

b) Test pits with concrete covers shall be provided for periodic testing of earth resistance.

Installation of pipe electrodes in test pits shall be suitable for watering. The necessary materials required for installation of test pits shall be supplied and installed by Contractor. The installation work shall also include civil work such as excavation and connection to main earth grid.

c) Earth pits shall be treated with salt and charcoal. In case found necessary, then with the approval of Purchaser's representative, Back fill compound of suitable composition may be used. Back fill material shall not be water soluble & shall retain moisture & enhance conduction around electrode. Back fill compound shall be low resistance & non corrosive earth enhancement compound which shall provide safe discharge path to fault current & lightening current.

d) Ohmic value shall be within safe limits & it shall be stable & not fluctuating.

e) Soil, salt and charcoal placed around the electrode shall be finely graded, free from stones and other harmful mixtures. Backfill shall be placed in layers of 250 mm thick uniformly spread and compacted. If excavated soil is found unsuitable for backfilling, the Contractor shall arrange for a suitable soil from outside.

37.5 INSTALLATION OF CABLE RACKS AND CABLE TRAYS

37.5.1 General

a) Lines and grade for trays may be measured from building steel and finished floor elevations. Change in line or grade, or the addition of offsets by means of cutting standard tray sections and inserting additional tray fittings to match with the existing arrangement shall be considered as a normal part of the work.

b) Where embedded steel inserts in concrete floors/ walls for welding the supports for cable racks/ trays are not available, Contractor shall provide suitable anchor fasteners at no extra cost.

c) Cable shall be clamped to the cable trays at every 750 mm distance.

d) Flexible metallic conduits shall be used for termination of connection to equipment such as motors, limit switches and other apparatus.

37.5.2 Cable Trays

All the cable tray shall be hot dipped galvanized with minimum galvanization thickness as per mentioned in this specifications.

a) Cable tray shall be of perforated sheet steel with formed flanges and of minimum thickness not less than 1.25 mm for trays up to 100 mm width, not less than 1.5 mm for trays from 100 mm to 150 mm width and not less than 2.0 mm for trays from 150 mm to 300 mm width.

b) All the cable trays above 300 mm width shall be of ladder type with minimum thickness of 2.5 mm.

c) Cable tray for use in areas where chlorine gas may be present shall be constructed from U-PVC or GRP. Cable tray supports shall be of a compatible finish with the associated cable tray.

d) All cable trays tees, intersection units, bends, turns and sets shall be prefabricated (made by the manufacturer) and shall be of a matching design to the main section of cable tray.

e) Tray shall only be joined by couplers supplied by the manufacturers. The joint shall be secured in accordance with the manufacturer's instructions.

f) Cable tray supports supplied by a manufacturer or made up on Site shall have adequate strength to maintain rigid support to the fully laden cable tray along its entire length and shall ensure that the deflection of any one section does not exceed 15 mm at mid span.

g) Wherever possible, cable trays shall be installed in full lengths without cutting. Should it be necessary to cut or drill a length of tray, the bared ends or damaged section of the tray shall

immediately be given a coat of zinc rich cold galvanized paint. All site manufactured accessories, supports and metal fittings required to ensure correct installation of the cable trays shall be similarly treated.

h) All cables shall be firmly secured to the tray using purpose made saddles, as approved by the Purchaser's Representative, together with proprietary nylon fasteners and/or cable cleats. Following installation of cables, the tray shall remain rigidly supported and the deflection of any section shall not exceed 15 mm at mid span. All brackets and tray work shall be suitable for withstanding a temporary weigh of 125 kgs.

i) Cable trays shall not be cut to allow the passage of cables through the surfaces of the tray

j) The sizing of the cable tray shall provide a minimum of 20% spare capacity.

k) The tray shall be run at least 300 mm clear of plumbing and mechanical services.

l) Bends in the installation shall take account of the minimum bending radii of cables to be installed.

m) All the cable trays shall be supplied with cable tray supports (of adequate size) at no more than 1.2 meter interval.

n) Other cable tray details & cabling system shall be as per typical drawings attached with the specifications.

37.5.3 Cable Trunking – Metal

a) Cable trunking shall be manufactured from mild steel of not less than 1.25 mm and shall be hot dipped galvanized. The Contractor shall ensure that the size of the trunking is adequate for the number of cables to be installed together with 50% spare capacity and shall in any case be 50 mm x 50 mm minimum size.

b) Segregation of cables shall be carried out if required using continuous sheet steel barriers with the bottom edge welded to the trunking.

c) The trunking shall have two return flanges for rigidity. Where necessary, additional strengthening straps shall be fitted internally. The cover shall overlap the trunking and be made of the same gauge. Fixing screws for covers shall be recessed and be of the self retaining `quick fix' type. All bends, tees and intersections shall be of the gusset type and shall, wherever possible, be purpose made by the manufacturer and of a matching design to the main trunking.

d) Cables shall be retained in the trunking when the cover is removed by means of straps.

Internal connecting sleeves shall be fitted across joints in the trunking and earth continuity ensured by bonding each section of trunking to a continuous earth wire.

e) Non-flammable fire barriers shall be inserted where the trunking passes through walls or floors. Conduit connections to trunking shall be made by flanged couplings and male bushes.

f) Trunking shall be supported at intervals not greater than 2 meter horizontally or 2.5 meter vertically.

g) Crossings over expansion joints shall be made in flexible conduit.

h) Should it be necessary to cut or drill a section of trunking or a trunking fitting the bared ends shall immediately be given a coat of zinc rich cold galvanizing paint.

i) Cable and conduit/ trunking runs shall be determined by the Contractor and agreed by the Purchaser's Representative before any work is started. The run shall be at least 300 mm clear of plumbing and mechanical services.

j) Conduit/trunking systems erected outside a building shall be weatherproof.

37.6 CABLE INSTALLATION

37.6.1 General:

a) Cable installation shall be in accordance with ISO/BS/IEEE 1255: 2001- latest edition

b) Cables shall be installed in such a way that the minimum bending radii are not reduced when installed or during installation. Cables shall not be installed in ambient temperatures below that recommended by the cable manufacturer.

c) Cables grouped together shall have insulation capable of withstanding the highest voltage present in the group.

d) Cables of different categories shall be installed so as to maintain satisfactory clearances for safety and in order to reduce the possibility of electrical interference. The following Table details the distances in mm that shall be maintained between the different categories of cable.

Table of Separation Distances in mm between different Categories of Cable

Cable Category	HV Power	LV Power	C&I/ Protection	Tele-communication

HV Power	N/A	300	600	600
LV Power	300	N/A	300	300
C&I/ Protection	600	300	N/A	200
Tele- communication	600	300	200	N/A

e) These separations are minimum and special circumstances such as the presence of high current flows, or harmonic content may necessitate larger separation distances.

f) A distance of minimum 300mm shall be maintained between the cables to be laid on trays/ conduits carrying low voltage AC and DC signals and a distance of minimum 600 mm shall be maintained between cables carrying HV and LT signals.

g) In order to make economic use of the cable support system, cables shall be arranged in groups of 50 mm maximum overall diameter. These groups shall be securely tied to the cable support system at intervals not exceeding 900 mm for horizontal runs and 300 mm intervals on vertical runs.

h) In order to make the most economic use of cable tray and duct capacity, multicore cabling shall be utilized in order to connect instrumentation groups by using suitably located sub-distribution junction boxes. The junction boxes shall be suitable for the area in which they are to be installed and for the type of circuit. They shall be readily accessible for maintenance and clearly labeled junction boxes shall be constructed of die cast Aluminium and provide degree of protection IP 65.

i) Where practical a separate cable support system shall be provided for power and non- power cables. Where this is not practical a separation as per indicated in above table shall be maintained between power and non-power cables when run on the same support system.

j) Heavy duty galvanized iron cable tray and ladder racking shall be used for cable support systems. FRP/ GRP cable support systems shall be used in areas used for the storage and handling of chlorine. These systems shall be used to route cables around walls and within cable trenches. Cables shall be securely fixed to the support systems. Bundling of cables shall be permitted where allowance for this practice has been made in sizing the cables.

37.6.2 Laying of Cables:

a) Each instrumentation and power supply cable shall be terminated to individual panel/ terminal box.

b) Identification of each cable shall be by proper ferrules at each junction as per cable schedule to be prepared by Contractor.

c) Cables shall be laid in accordance with layout drawings and cable schedule which shall be prepared by Contractor and submitted for approval.

d) All cable routes shall be carefully measured and cables cut to the required lengths, leaving sufficient amount for the final connection of the cable to the terminals on either end.

e) Various cable lengths cut from the cable reels shall be carefully selected to prevent undue wastage of cables.

f) A loop of 1.0 meter shall be left near each field instrument before terminating the cable.

g) Cables shall be complete uncut lengths from one termination to the other.

h) Separate cables shall be used for digital and analog signals.

i) All cables shall be identified close to their termination point by cable numbers as per cable interconnection schedules.

j) Identification tags shall be securely fastened to the cables at both the ends.

k) Cable shall be rigidly supported on structural steel and masonry, using individually cast or malleable iron galvanized clips, multiple cable supports or cable trays.

l) The Contractor shall take the actual measurement of the cables and the associated accessories such as cable trays, conduits etc required at site, prior to the placement of order on the cables.

37.6.3 Cables Laid Direct in Ground

a) Buried cable up to 1.1 kV shall have a laid at a minimum depth of 750 mm measured from FGL to the top of the highest cable. On crossing roadways the cable shall be run through a PVC-U duct of minimum diameter 100 mm with a minimum of 1000 mm cover and encased on all sides by 150 mm of concrete.

b) Cables of greater than 1.1kV shall be buried at a minimum depth of 1 meter.

c) The bottom of the cable trench shall be freed of sharp stones and such like and 75 mm of sieved sand laid below the cable. After cable laying 75 mm of sieved sand shall be laid above the cable. For HV cables sand bedding shall be of 150 mm & cables shall be

covered with half round Hume pipes of twice the diameter of cable.

d) Interlocking cable protective covers, minimum 1 m long x 300 mm wide, marked 'Danger-Electric Cable' in English and the vernacular shall be laid on top of the sieved sand. Covers shall extend the whole length of the cable trench and shall overlap cables by a minimum of 50 mm.

e) Warning tape shall be laid a minimum of 200 mm above the protective covers.

f) Cables are to be installed without tees or through joints unless otherwise approved by the Purchaser's Representative. Single core cables shall be run in trefoil formation.

37.6.4 Cables Laid in Underground Ducts

a) Underground ducts shall be constructed of impact resistant PVC-U and laid at a minimum depth of 750 mm, ducts shall be surrounded by at least 75 mm of sieved sand except at road crossings where it shall be 1.0 meter deep and encased on all sides by 150 mm of concrete.

b) The Contractor shall ensure that sufficient draw-in points have been provided and that adequate room has been allowed for installation of cables. Drawstrings shall be provided in all ducts to enable additional cables to be installed when required.

c) Where cables pass in or out of any duct entries into or within buildings such entries, together with any spare ducts shall be sealed against the ingress of moisture by means of duct stoppers and bituminous compounds or by any other method approved by the Purchaser's Representative. The stopper shall have a fire resistance of at least 30 minutes. Single core cables in trefoil formation shall pass through the same duct and shall not be separated. However, for two different trefoil formations, they shall be laid in separate ducts.

37.6.5 Cables installed in Conduit

a) Conduits shall be galvanized heavy gauge solid drawn or welded screwed steel type and be in accordance with ISO/BS/IEEE 9537, Part 2 or BS 4568. Accessories shall either be malleable cast iron screwed type or pressed steel and galvanized.

b) A space factor of 40% shall not be exceeded, but in any case conduit of less than 20 mm diameter shall not be permitted. The tubing shall be perfectly smooth inside and out and free from flaws and imperfections of any kind. Both ends of every length of tubing

shall be properly reamed with all sharp edges removed before erection.

c) Where a number of conduits converge, malleable cast iron or heavy gauge sheet steel adaptable boxes shall be employed in order to avoid crossings. Conduits shall be connected by means of male brass bushes and couplings.

d) Where conduits are greater than 25 mm, straight through joint boxes shall be of the trough type. Where conduit and/ or fittings are attached to equipment casings, the material or case of the casing shall be tapped for a depth of not less than 10 mm or male bushes and flanged couplings shall be used.

e) Heavy hexagonal lock nuts shall be used at all positions where running joints are required and care shall be taken to ensure that they seat firmly and evenly on to the mating faces of coupling or other adjacent accessories. All junction boxes, draw-in boxes, and inspection fittings, shall be so placed that the cables can be inspected and, if necessary, withdrawn and re-wired throughout the life of the installation.

f) Generally not more than two bends or offsets or one coupling will be permitted without a suitable inspection accessory. Fish wires shall not be left in conduits after erection. The whole of the installation shall be arranged for a loop-in type of system with joints being carried out at switches, isolators, etc. Intermediate joints in the cable will only be allowed by arrangement with the Purchaser/ Purchaser's Representative.

g) Ends of conduits which are liable to be left open for any length of time during building operations shall be plugged to prevent the ingress of dirt, cement, etc. and covers, either temporary or permanent, shall be fitted on all boxes.

h) Generally, conduits shall not cross expansion joints of buildings, but where they cannot be installed in any other manner then a flexible conduit shall be used across the expansion joint. A total 150 mm movement shall be allowed.

37.6.6 Surface Installation

a) Surface conduits shall be secured and fixed by means of distance spacing saddles or approved purpose made clips at every 500mm, which allow the conduits to be taken directly into accessories without sets or bends. Conduits shall be run in a square and symmetrical manner. An efficient means shall be adopted to provide for the drainage of condensation and the runs shall be properly ventilated. All surface conduit runs shall be marked out for approval

by the Purchaser's Representative before the installation is carried out. Where large multiple parallel conduit runs would occur, use may be made of galvanized cable trunking. Conduits installed on structural steelwork shall be secured at spacing not exceeding those for surface conduit by girder clips, otherwise fixing shall be as for surface conduits on walls, drilled and tapped to the metalwork. Power driven fixings shall only be used with the express permission of the Purchaser's Representative. Any drilling or access which is required through any structural member of the building shall be agreed with the Purchaser/ Engineer in Charge before carrying out the work.

b) Exposed threads and places where galvanizing has been damaged shall be cleaned and then painted with two coats of an approved metallic zinc based paint. This treatment shall be applied as the work proceeds.

37.6.7 Concealed Installation

a) Concealed conduits shall be securely fixed to prevent movement before laying of screeds, floating of plaster, casting of columns or other building operations necessary after the conduit installation. Crumpets or similar fixings shall be used for attaching the conduit to blockwork, etc. Building nails will not be accepted.

b) At least 15 mm cover shall be allowed for finishes over the conduit. Where this cover cannot be maintained then expanded metal shall be fitted with the conduit. Conduit cast into reinforced concrete floors shall be fixed to the steel reinforcing with binding wire and the conduit boxes filled with expanded polystyrene or enclosed in a plastic bag to prevent the ingress of concrete when poured. Where possible, the conduit boxes shall be fixed to shuttering to give a flush finish.

c) Conduit installed in voids, false ceilings, and other concealed routes shall be installed as specified for the surface conduits. Wiring shall be carried out after the false ceiling or permanent ducts have been completed. Conduit installed in floors shall be sealed against ingress of moisture.

d) The conduit installation shall be inspected by the Purchaser's Representative before the building operation conceals the work.

37.6.8 Cable Installed in Flexible Conduit

a) Flexible conduit shall be of the waterproof galvanized type or PVC wire-wound type with cadmium plated mild steel couplings. Lengths of flexible conduits shall be sufficient to permit withdrawal, adjustment or movement of the equipment to which it is attached

and shall have a minimum length of 300 mm. Flexible conduit shall not be used as a means of providing earth continuity. A single earth conductor of adequate size shall be installed external to the conduit complete with earth terminations.

b) Where conversion from rigid conduit to flexible metallic conduit is to be made, the rigid conduit shall terminate in a through type box and the flexible conduit shall extend from this box to the equipment, the earth continuity cable shall be secured to the box and to the piece of equipment by properly designed earthing screws. The use of lid facing screws, etc., will not be permitted. Adapters shall incorporate a grub screw or a gland to prevent the flexible conduit becoming loose.

37.6.9 Cable Clipped Direct

a) All cable hangers, clips, cleats and saddles shall be of an approved type and appropriate to the type and size of cable installed. Their spacing shall be such as to ensure a neat appearance and prevent sagging of the cables at all times during their installed life.

37.6.10 Cable Installed in Internal Floor Trench

a) In shallow trenches (maximum depth 500 mm)

b) In shallow trenches used for electrical services only, cables may be laid in a neat and orderly manner on the floor of the trench. One layer only shall be allowed. Additional cables shall be installed on the walls of the trench in an acceptable manner & such a way that, in no case the distance between two different types of cable shall not be less than the separation distance tabulated above.

c) Where the trench is shared by other services, cables shall be installed on the walls of the trench in an acceptable manner & such a way that, minimum separation distance of 300mm shall be maintained.

d) All other trenches including walk through service ducts

e) Cable trenches & cable installation shall be in accordance with the attached typical cabling system drawings.

f) Where other services are present the cables shall be segregated from them by separation distances as mentioned above and wherever possible kept above `cold' wet services. Cables should not be run if at all possible above or in close proximity to `hot' services.

g) The cabling shall be installed in such a manner as to allow access to the other services for normal maintenance without disturbance of the electrical installation

37.6.11 Cable Terminations and Joints

a) Power Cable Terminations

i. Power cables shall be terminated in suitable boxes arranged for bolting to switchgear, motor starters and motors.

ii. Cores shall have either crimped lugs or sleeves to match either post terminals or bolted clamp terminals.

iii. Each cable entry into a terminating box shall be made through a suitable gland, which shall have provision for securing the armour where applicable. Where single core glands are required these shall be of the non-magnetic type and the associated box bottom plate, where the core passes through, shall not have a continuous magnetic path.

iv. Adequate provision shall be made to bond the cable armouring to the box and/or switchgear casing of a suitable size to withstand the prospective short circuit fault current of the system, glands shall be fitted with earth bonding tags where intimate screwed contact between gland and cable box is not possible.

v. Where cable glands are exposed to the weather these shall be protected by heat shrink plastic sleeve or purpose moulded sleeves covering the gland continuously from overall sheath to the gland neck.

vi. Where terminations of multicore type have to be made on to items of Plant which have to be dismantled for maintenance, these shall be made off through glands into an adaptable box containing terminals and flexible single cores taken into the equipment via flexible waterproof plastic covered conduit, and a separate earth core linking the box to the equipment.

vii. Where single core cables are glanded to or pass through cabling plates the gland plate or cabling plate shall be constructed of non-magnetic material.

b) Power Cable Joints:

i. Through joints shall only be allowed with the approval of the Purchaser's Representative. Where such joints are necessary in thermoplastic and elastomeric cables, the cables shall be jointed with epoxy or acrylic resin cold setting compound, which has been premeasured and pre-packed ready for use. The boxes shall preferably be of split, moulded plastic type with filling vents for compound. Bonding straps shall be fitted with armour clamps across the joint and inspected by the Purchaser/ Purchaser's Representative prior to filling the box with

compound. Wrapped pressure type joints will not be accepted.

c) Multi-core or Control Cable Terminations:

i. A sufficient number of terminals shall be provided to terminate all cable cores. For control and auxiliary wiring an additional 20% of this number shall be provided as spares.

ii. Not more than one core of internal or external wiring shall be connected on any one terminal. Where duplication of terminal blocks is necessary, purpose-made solid links shall be incorporated in the design of the terminal blocks.

iii. Terminals which remain energized when the main equipment is isolated shall be suitably screened and labeled.

iv. Terminal blocks for different voltages or circuit type shall be segregated into groups and distinctively labeled.

37.6.12 Cable Fixings

a) Ties and strapping shall be suitable for securing cable and cable groups to cable tray or ladder. They shall be resistant to chemical and marine corrosion. Plastic coated metal ties used in order to obtain corrosion resistance shall not be acceptable. Nylon ties shall be resistant to the effects of ultra-violet light and shall be self-extinguishing.

b) Large single cables shall be secured with cable clamps or cable cleats.

37.6.13 Cable Identification

At each end of each cable, in a uniform and visible position a label shall be fixed on the cable in accordance with the cable schedule. Labels shall be made of PVC and shall be indelibly marked to the approval of the Purchaser's Representative. The label shall be retained using proprietary nylon strips passing through two fixing holes at either end of the label. If the cable gland is not normally visible, then the label shall be fixed inside the panel by means of screws.

37.6.14 Marking Locations of Underground Cables

a) The location of all underground cables shall be engraved on brass or other non- corrodible plates to be fixed to the exterior surface of all walls of buildings 300 mm above ground level and directly above the point where cables pass through the wall.

b) Cable route markers as per the attached drawing shall be

installed at an interval not more than 30 meter & at bending/ road crossings the interval shall be at every 10 meter.

c) The minimum depth for laying of underground cable route markers shall be as per indicated in the typical drawings attached with this tender.

37.6.15 Additional Requirements for Cable Installations

a) The Contractor shall install, test and commission the cables specified in the specification. Cables shall be laid directly buried in earth, on cable racks, in built up trenches, on cable trays and supports, in conduits and ducts or bare on walls, ceiling etc. as per drawings, which are to be prepared by Contractor & approved by Purchaser's representative. Contractor's scope of work includes unloading, laying, fixing, jointing, bending, and termination of the cables & all related accessories. The Contractor shall also supply the necessary materials and equipment required for jointing and termination or the cables.

b) All apparatus, connections and cable work shall be designed and arranged to minimize risk of fire and any damage which might be caused in the event of fire. Wherever cables pass through floor or wall openings or other partitions, suitable bushes of an approved type shall be supplied and put into position by the Contractor.

c) Standard cable grips and reels shall be utilized for cable pulling. If unduly difficult pulling occurs, the Contractor shall check the pull required and suspend pulling until further procedure has been approved by the Engineer's Representative. The maximum pull tension shall not exceed the recommended value for the cable measured by the tension dynamometer. In general, any lubricant that does not injure the overall covering and does not set up undesirable conditions of electrostatic stress or electrostatic charge may be used to assist in the pulling of insulated cables in conduits and ducts.

d) After pulling the cable, the Contractor shall record cable identification with date pulled neatly with waterproof ink in linen tags. Identification tags shall be attached securely to each end of each cable with non-corrosive wire. The said wire must be non-ferrous material on single conductor power cable. Tags shall further be attached at 10 meter intervals on long runs of cables on cable trays and in pull boxes. Cable and joint markers and RCC warning covers shall be provided wherever required.

e) Sharp bending and kinking of cables shall be avoided. The bending radius for various types of cables shall not be less than those

specified below:

i.	11 kV, XLPE insulated, multicore armoured cables	15 times the overall dia of the cable
ii.	1.1 kV, XLPE insulated, multicore armoured cables	12 times the overall dia of the cable
iii.	(If shorter radius appears necessary, no bend shall be made until clearance and instructions have been received from the Purchaser/ Engineer in charge)	

f) Power, control and instrumentation cables shall be laid in separate cable racks/ trays.

g) Where groups of HV, LV and control cables are to be laid along the same route, suitable barriers to segregate them physically shall be provided.

h) Where cables cross roads and water, oil, gas or sewage pipes, the cables shall be laid in reinforced spun concrete or steel pipes. For road crossings the pipe for the cables shall be buried at no less than one meter depth.

i) Cables laid in ground shall be laid on a 75 mm riddled earth bed. The cables shall then be covered on top and at their sides with riddled earth of depth of about 150 mm. This is then gently filled up to a depth of about 100 mm above the top of uppermost cable to provide bedding for the protective cable covers which are placed centrally over the cables. The protective cable covers for LV cables may be of earthenware and for HV cables of reinforced concrete. The RCC covers shall have one hole at each end, to tie them to each other with GI wires to prevent displacement. The trench is then backfilled with the excavated soil and well rammed in successive layer of not more than 300 mm in depth, with the trenches being watered to improve consolidation wherever necessary. To allow for subsidence, it is advisable to allow a crown of earth not less than 75 mm in the centre and tapering towards the sides of the trench.

j) In each cable run some extra length shall be kept at a suitable point to enable one or two straight through joints to be made, should the cable develop a fault at a later date.

k) Cables on cable racks, on cable trays and conduits shall be formed to avoid bearing against edges of trays, racks, conduits or their supports upon entering or leaving trays, racks or conduits. Cables shall be racked or laid directory into cantilevered cable trays where practicable, but in some cases it may be necessary that cables are pulled or threaded into trays. To facilitate visual tracing, cables in trays shall be laid only in single layers and unnecessary crossing of

cables shall be avoided. Cables on trays shall finally be clamped in an approved manner.

l) Cable splices will not be permitted except where permitted by the Purchaser/ Purchaser's Representative. Splices shall be made by Contractor for each type of wire or cable in accordance with the instructions issued by cable manufacturer's and the Engineer's Representative. Before splicing, insulated cables shall have conductor insulation stepped and bound or penciled for recommended distance back from splices to provide a long leakage path. After splicing, insulation equal to that on the spliced conductors shall be applied at each splice.

m) Jointing of cables shall be in accordance with relevant Pakistan Standards Codes of Practice. Materials and tools required for cable jointing work, including cold setting bituminous compound shall be supplied by the Contractor. Cables shall be firmly clamped on either side of a straight through joint at a distance of not more than 300 mm away from the joints. Identification tags shall be provided at each joint at all cable terminations.

n) At cable terminal points where the conductor and cable insulation will be terminated, terminations shall be made in a neat, workmanlike and approved manner by men specialized in this class of work.

o) Control cable termination shall be made in accordance with wiring diagrams, using colour codes established by the Purchaser's Representative for the various control circuit, by code marked wiring diagram.

p) When control cables are to be fanned out and cabled together with cord, the Contractor shall make connections to terminal blocks, and test the equipment for proper operation before cables are corded together. If there is any question as to the proper connection, the Contractor shall make a temporary connection with sufficient length of cable so that the cable can be switched to another terminal without splicing. After correct connections are established through operating the equipment, cables shall be cut to their correct lengths, connected to terminals in the specified manner, and corded together where necessary to hold them in place in a workmanlike manner.

q) Cable seals shall be examined to ascertain if they are intact and that cable ends are not damaged. If the seals are found to be broken the cable ends shall not be jointed until after due examination and testing by the Purchaser/ Purchaser's Representative. Before jointing is commenced, insulation resistance

of both sections of cables to be jointed shall be checked by megger.

r) After installation and alignment of motors, the Contractor shall complete the conduit installation, including a section of flexible conduit between motor terminal box and trench/ tray. The Contractor shall install and connect the power, control and heater supply cables as per equipment manufacturer's drawings.

s) Metal sheath and armour of the cable shall be bonded to the earthing system of the station. The size of conductor for bonding shall be appropriate with the system fault current.

37.7 LIGHTING SYSTEM INSTALLATION

This covers the requirements of installation of the following:

a) Lighting fixtures complete with lamps and accessories

b) Main Lighting distribution board

c) Lighting panels

d) Receptacles and lighting control switches

e) Point wiring

f) Street lighting poles and flood light towers

g) Multi core cables for street and boundary lighting

h) Maintaining equipment/ materials during storage and being responsible for the equipment/ material until they are handed over to Purchaser.

i) Installation, testing and commissioning shall be carried out in accordance with the drawings and as stipulated in this specification.

37.7.1 Applicable Standards for lighting system installation

Electrical wiring installations	ISO/BS/IEEE: 732 (System voltage exceeding 650 V)
Code for practice for interior illumination (Part-1)	ISO/BS/IEEE: 3646/ BS: 8206
Code of practice for street lighting installation	ISO/BS/IEEE: 1944
Code of practice for industrial lighting	ISO/BS/IEEE: 6666
Code of practice for fire safety of building	ISO/BS/IEEE: 1646
Boxes for enclosure of electrical accessories	ISO/BS/IEEE: 5133(Part-1)
Guide for safety procedures and practices in electrical work	ISO/BS/IEEE: 5216
Ceiling roses	ISO/BS/IEEE: 371

37.7.2 Lighting Fixtures

a) The installation of lighting fixtures shall be based on the mounting arrangement shown in the drawings. The rates quoted for installation shall include all materials required to mount the fixtures. Hooks in RC slabs for suspension of high bay fixtures shall be provided wherever not already provided. Cost of supply and installation of such hooks shall be included in the cost of installation of lighting fixtures. Rate for installation of lighting fixtures shall include cost of installation of control gear box wherever applicable.

b) Installation of receptacles and switches shall be carried out suitably. Switch shall be mounted in flush with the front cover plate. Cost of supply and installation of necessary hardware shall be included in the lump sum rates quoted for installation of receptacles/ switches.

c) Lighting distribution boards shall be installed at the suitable location. Installation shall include supply and installation of base channels, foundation bolts, etc.

d) Outdoor lighting distribution boards shall be installed on a concrete plinth. The top of plinth shall be 1000 mm (min.) above the grade level. Cost of construction of concrete plinth shall be included in Contractor's scope. No cement and steel will be supplied by Purchaser. Installation cost of lighting distribution board shall include cost of installation of earthing conductor from LDB to the nearest earthing grid.

37.7.3 Point Wiring:

a) Contractor has to prepare the detailed conduit layout drawing showing primary & secondary point wiring points. Point wiring also covers the wiring of the associated control switches of lighting fixtures/control switches of receptacle units.

i. Primary Point Wiring:

Primary point wiring covers the wiring between a circuit of the lighting panel to the junction box of the first lighting fixture/receptacle unit and between junction boxes of the subsequent lighting fixture connected to that circuit of the lighting panel. In some cases where there are junction boxes, the primary point covers the wiring between junction box and the first lighting fixture/receptacle unit in that circuit.

ii. Secondary Point Wiring:

Secondary point wiring covers the wiring of the remaining

lighting fixtures/receptacle unit other than that covered under primary point of that circuit in the lighting panel. Secondary point wiring also covers the wiring of the associated control switches of lighting fixtures/control switches and control switches of receptacle units.

b) Supply and Installation of Conduit Point Wiring:

i. The point wiring shall include supply of necessary materials for the conduit wiring such as galvanized rigid steel conduit, galvanized M.S. fixing saddles with spacer plates, nylon/fiber fixing plugs, galvanized M.S. fixing screws, 12 SWG galvanized steel earthing wire, FRLS PVC insulated Copper conductor wires, control switches and pulling, termination of the earthing/ FRLS PVC insulated wires as required, installation of control switches, drilling holes in brick walls/ RCC roof slabs for taking the wiring conduits and refinishing and any other works/material necessary for making point wiring complete in all respects.

ii. Wires used for conduit point wiring of lighting fixtures/ceiling fans, 5A receptacles and receptacles above 15A shall be 1.1 kV grade, FRLS PVC insulated, single core, multi stranded Copper conductor wires of sizes not less than 1.5 sq. mm and 2.5 sq. mm respectively. Wires shall conform to ISO/BS/IEEE: 694 and shall bear the ISO/BS/IEEEI mark.

iii. Contractor shall take into consideration necessary galvanized MS fixing clamps when the wiring conduits are to be supported from steel roof truss/structural members.

c) Supply & Installation of cabling for Street and Flood Lighting:

i. Work includes supply and installation of cables required between LDB and junction box mounted on street lighting pole/flood lighting tower and also between junction box mounted on flood light tower to metal enclosed control gear box located near flood light fixture, supply and installation of all the termination accessories such as crimping type cable lugs and double compression cable glands at each junction box and fixture, termination, testing and commissioning of cables. Contractor's scope of work also includes excavation, preparation of riddled soil bedding, supply and installation of protective covers over the cable, backfilling, ramming, supply and installation of route markers, supply and installation of HDPE / Hume pipes for road crossing, etc, supply and

installation of necessary cleating arrangement for cabling on flood light tower, supply of labour, supervision, welding equipment, all tools and tackles and testing equipment as required.

ii. Contractor shall plan and cut the cables in such a way that there is no wastage and no cable jointing is required in any run. However, should any joint become necessary the same shall be provided by the Contractor and a joint marker shall also be provided at no extra cost. Earthing of street light pole/flood light tower, lighting fixtures, etc. are included under Contractor scope.

d) Point wiring shall also include/ hold good for the following:

i. Supply and installation of lighting control switches and switchboxes complete with fixing accessories.

ii. Drilling holes in brick/ RCC wall and roof for taking cable or conduit, sealing and refinishing with cement plaster.

iii. Testing, commissioning and handing over the lighting system in commercial working condition.

iv. Marginal shifting of any fixture/accessory from the location indicated in the lighting layout drawings.

37.7.4 Outdoor Lighting (Street and Flood Lighting)

The following shall be deemed to be included as part of the installation work for outdoor lighting point wiring.

a) Installation of multicore/ single core cables between LDB and junction box mounted on street light pole/flood lighting tower, from junction box to metal enclosed control gear box.

b) Supply and installation of crimping type cable lugs, double compression type cable glands at each junction box and fixture, termination, testing and commissioning of cables.

c) Contractor's scope shall also include excavation and preparation for buried cables.

Supply and installation of route markers, supply and installation of HDPE/ Hume pipes for road crossing shall also be included in the scope of installation of point wiring.

d) Supply and installation of necessary cleating arrangement for cabling on flood light poles.

e) Contractor shall provide necessary foundation for erecting street light pole/ flood light tower and install the same. Contractor shall prepare foundation drawings with necessary details & Purchaser

Representative's approval shall be obtained.

f) Contractor shall plan and cut the cables in such a way that there is no wastage and no cable jointing is required in any run. However, should any joint become necessary, the same shall be provided by the Contractor and joint marker shall also be provided at no extra cost.

g) Earthing of street light pole/flood light tower, lighting fixtures, control gear boxes, junction boxes, etc. are also included in the scope of installation of point wiring. Contractor shall earth street light pole/flood light poles and junction box with 25x3 mm G.S. flat tap off from the 25x3 mm M.S. flat earthing grid along the street lighting included in scope. The Contractor shall interconnect earthing grid to plant main earthing grid at first and last pole of each feeder circuit and at one intermediate pole.

h) Installation of lighting Poles and Towers for Outdoor Lighting (Street and Flood Lighting)

i. Work includes supply and installation of street light poles and flood light towers including associated junction boxes with fuses, links and terminals for junction boxes and junction boxes near each flood light fixtures.

ii. All street light poles and towers shall be painted with one shop coat of red oxide oil primer followed by two coats of aluminium alkyd paint.

Installation of Lighting Distribution Board, Lighting Panels (AC & DC), 230 V, AC 1- Ph Distribution Boards.

Installation of above items shall include necessary foundation channels, bolts/ nuts, etc. for grouting lighting distribution boards, iron brackets/ grouting brackets, bolts/nuts for wall/ column mounted panels and associated civil works.

Details of work requirements are covered in lighting installation notes and details and typical drawings which form the part of specification. Any changes, if necessary due to site conditions/requirements shall be carried out after obtaining approval of Purchaser/ Purchaser's Representative. The changes carried out shall be marked clearly in the layout drawings by Contractor and 'AS BUILT DRAWING' shall be prepared by the 'Contractor' and this shall be forwarded to Purchaser's site / design office.

a) Wiring:

i. Wiring shall be carried out strictly as per project drawings and technical specification. All exposed conduit wiring shall have provision for easy inspection. Where cable wiring is specified cable

shall be cleated on to the wall as close to the ceiling as possible. In all types of wiring due consideration shall be given for neatness and appearance.

ii. Wherever DC emergency lighting is provided, emergency lighting wires shall run in a separate conduit. Colour of the wires used shall be as follows; white for positive, black for negative.

iii. Wherever lighting system has three phase distribution, separate conduits shall be used for different phases. For easy identification of phases and neutral wires the following colour wires shall be used.

R - Phase - Red

Y - Phase - Yellow

B - Phase - Blue

N – Neutral - Black

b) There shall be a circuit breaker on each live conductor of supply mains at the point of entry.

c) Conductors not arranged for connection to the same system or supply different phases of the same supply, shall be kept apart throughout their entire run.

d) Receptacles and lighting fittings in general shall be fed from different Circuits. Five amps receptacles for toilet or small rooms can be fed from the lighting circuit with proper isolating arrangement.

e) Each final sub-circuit from a lighting panel shall be controlled by a single pole switch connected to the live conductor.

f) For long conduit wiring runs, inspection/ pull boxes shall be provided at intervals not exceeding 10 meter. Such facilities shall also be provided at conduit bends.

37.7.5 General Practices for lighting

a) All receptacles and switches to be installed in offices and control rooms shall be flush mounted within the wall and those in other areas shall be wall or column mounted.

b) Ceiling roses shall not embody fuse terminals as an integral part. For voltages exceeding 250 volts, a ceiling rose or any similar attachment shall not be used.

c) All exposed metal parts of the plug, when the plug is in complete engagement with the socket outlet, shall be in effective electrical connection with the earthing pin.

37.7.6 Earthing for lighting

Conduits and fittings shall be earthed by 12 SWG GI wires run along the length of the conduit and secured by means of suitable clamps efficiently fastened to conduit tip. To achieve perfect electrical continuity, the conduits shall be bonded effectively on either end of a coupling and other joints.

a) Conduits shall be earthed at the ends adjacent to switch boards at which they originate or otherwise at the earth clip, clamp or gland, in effective electrical contact with the conduit.

b) For outdoor lighting poles & mast 8 SWG GI earth wire shall be run buried in ground at a depth of 600 mm along-with lighting cables and shall be terminated up to the junction box on the pole and 12 SWG wire shall be taken up to the pole fitting. In case of lighting poles where the main earth grid is far away from the pole, local pits shall be provided for pole earthing.

SECTION-38 PRE COMMISSONING TESTS ON ELECTRICAL EQUIPMENT/ SYSTEMS TO BE CARRIED OUT AFTER INSTALLATION:

38.1 GENERAL:

Pre-commissioning tests in addition to mentioned in the specification requirements for various equipments but not limited to following shall be carried out by Contractor in presence of Purchaser/ Purchaser's representative. Commissioning shall be carried out only after obtaining satisfactory results, acceptable to Purchaser/ Purchaser's representative.

38.2 ELECTRICAL EQUIPMENT:

11 KV Equipment (Lightning Arrestors, AB Switch/ Isolators & Insulators etc):

a) Visual checks for cracks in insulators.

b) Earth secured continuity check

c) IR Test with 5KV Megger

1.1.4 POWER/ DISTRIBUTION TRANSFORMER

a) Insulation resistance test HV side, LV side and HV - LV.

b) Magnetizing current test.

c) Winding resistance test.

d) Voltage Ratio & Tap continuity test at all tap.

e) Vector group test.

f) Magnetic Balance Test.

g) Buchholz Relay Test (if any)

h) Neutral CT Test (if any)

i) Winding Temperature Indicator/ Oil Temperature Indicator Test

j) Polarization Index Test (For LV windings 3.3 KV and above)

k) Local/ Remote operations of OLTC (if any)

l) Operational tests of RTCC panel (if any) as per schematic drawing.

m) No load test and performance observations

38.2.1 HV Metal Enclosed Switchgear:

a) IR values of power and control circuits

b) Local/ Remote operations in test as well as service position including all electrical interlocks

c) Control circuit and operational tests as per schematic drawing.

d) Tripping through relays and trip circuit health.

e) Anti pumping device operation

f) Protection system operation stability and sensitivity by primary injection testing method including testing of metering circuits

g) HV Test on switchboard

h) Panel indication, annunciation, space heater circuits

i) Spare contact for customer use

j) Termination correctness & proper installation.

38.2.2 LT Metal Enclosed Switchgears

a) IR Values of power & control circuits.

b) Mechanical charging - closing - tripping of breaker.

c) Electrical charging - closing - tripping of breaker.

d) Trip circuit healthiness and tripping through relays.

e) Remote closing/ Tripping/ Interlocks circuits

f) Indication/ Annunciation/ Panel space heater circuit/ Spare contacts for customer use

g) Secondary injection testing of protective relays/ releases.

h) CT testing for polarity, ratio, IR values and magnetization for class PS characteristics

i) PT testing for ratio, IR values.

j) IR Values of breaker.

k) Testing of modules for DOL/ Star-Delta/ ATS/ Soft Starter starting or any other starting method as per the schematic drawings applicable.

38.2.3 Power and Control Cables

a) IR Values before Hi-pot

b) Hi-pot Test - Measurement of leakage current

c) IR Values after Hi-pot

38.2.4 Induction Motors:

a) IR Values

b) Polarization Index Test

c) Interlocks and simulation tests local / remote operations

d) No load test

38.2.5 Control Panels for Miscellaneous Equipment:

a) IR Values of all power circuits

b) Operational test and scheme - wiring testing as per control schematics

38.2.6 Lighting System:

a) Visual inspection for operating problems

b) System activation -burning in the lamps for 100 Hrs

c) Measuring light level & reflectance.

38.2.7 Earthing System:

a) Earthing resistance of each electrode.

b) Earthing resistance of grid.

Technical Specification for Diesel Generator

38.3 DIESEL STANDBY GENERATOR:

38.3.1 Applicable Standards

The Diesel Standby Generator and its components shall conform to the latest applicable standards specified below:

Diesel Engines for General Purposes The Electrical Performance of Rotating Electrical Machinery : BS 5514 / ISO 3046 BS 5000

Rotating Electrical : Machines ISO/BS/IEEE 4722

Circuit breakers : ISO/BS/IEEE-13118, BS-5311, IEC-56 & 694, BSEN-60942 (P-2)

Air break switches air break :

disconnectors, air break switch ISO/BS/IEEE-13947 (P-3), BS- EN60947, IEC-60947-3

disconnectors and fuse combination

units for voltage not exceeding

1000 V AC or 1200 V DC

Current transformer : ISO/BS/IEEE-2705/BS-7626, IEC-

60185

Voltage transformer : ISO/BS/IEEE-3156/BS-7625/IEC 60186

Electrical Relays : ISO/BS/IEEE-3231, 3842/BS-142/IEC-

60255

Contactors for voltage not :

exceeding 1000 V ac or

1200 VDC ISO/BS/IEEE-13947 Part-IV/ BSEN-

60947-4-1/ IEC-60947-4-1

Control Switches : ISO/BS/IEEE-6875/BSEN-60947 /

IEC-60947-4-1

High Voltage Fuse ISO/BS/IEEE-9385/BS-2692/ IEC-

60282

Low Voltage Fuse : ISO/BS/IEEE-13703/BS-1362 IEC-269-

1

Electrical direct acting :

indicating instruments ISO/BS/IEEE-1248/BS-89/IEC-6005

A.C. electricity metres of :

induction type voltage greater than1000 volts ISO/BS/IEEE722, 8530/BS-5685 / IEC-

60145, 60211

Resistance wire, tapes and :

stripes for heating elements ISO/BS/IEEE-3725

38.3.2 General Requirements:

The diesel engine and generator shall be skid mounted and shall be located in a room near Treatment plant substation building. The diesel engine shall draw cooling air directly from outside the room through a weatherproof, acoustically treated duct. The exhaust system shall be insulated to minimize the amount of heat entering the room and to prevent injury to personnel. The silencer shall be of the 'residential' type and be located externally.

The generation voltage shall be 415V for DG capacity less than 2MVA and generation voltage shall be 11kV for D.G capacity more than 2MVA. In case more than one D.G set is required for achieving the required capacity they shall be operated in parallel with necessary synchronizing arrangement. At no point DG sets will be operating parallel with grid.

The diesel engine fuel shall be stored in an above ground bulk storage steel tank to be located adjacent to the generator room at a site accessible for filling to local road tankers. The storage tank shall be sized to store fuel for one (1) day running of the engine at full load. The tank shall be provided with fittings to permit the visual observation of fuel level and filling by local tanker operators. A level meter shall also be mounted in the tank so that remaining fuel volume can be monitored at the generator / substation PLC and the operator stations in the SCADA room.

The fuel storage tank shall be located in a bund capable of holding not less than 125 % of the maximum storage tank contents. Fuel transfer pumps shall be provided to automatically transfer fuel from the bulk storage tank to a high level 990 litres day tank located in the generator room or generator skid mounted day fuel tank. A semi-rotary hand pump shall be provided to permit transfer of fuel in the event of a failure of the transfer pump. Any leakage from the pumps shall be routed to the bund.

A system shall be provided within the generator room to detect fire, to raise a local audible alarm (manually silenced locally) and if a high level day tank is used, to automatically dump the day fuel back to the bulk storage tank.

The system shall be constructed such that leakage of water, fuel or oil within the generator room shall be routed to a local sump where a detector shall be provided to raise an alarm.

The system shall be constructed such that the leakage of fuel or the accumulation of water within the fuel storage bund shall be detected and shall raise an alarm.

All alarms shall be conveyed to the central HMI through the PLC.

38.3.3 Diesel Generating Set Automatic Control

AMF Diesel Generator Set capable of automatic starting and picking the load within 30 seconds shall be provided to cater for emergency loads and lighting during mains power failure. Diesel generating set for use in auto mains failure mode shall have a three position automatic / off / manual selection and shall operate as follows:

a. Automatic mode

On occurrence of mains failure the following sequence shall be followed. Mains to Generator changeover

- mains failure detected
- delay of 10 seconds
- generator is started and run up to speed
- time delay of 50 seconds
- mains supply is switched off
- generator supply is switched on

Generator to Mains changeover

- mains healthy detected
- manual changeover signal received,
- generator supply is switched off
- mains supply is switched on

- generator runs for 2 minutes and stops

All timer settings shall be adjustable.

If mains power is restored during the initial one minute delay then the power shall be monitored for a further one minute and if it is still healthy, mains power shall be restored. The generator shall be stopped after a further 2 minutes of running on no load. If the generator fails to start after an initial period of cranking, two further attempts shall be made with an appropriate interval between each attempt. If the engine fails to start after three attempts the system shall shut down and a local and remote alarm shall be annunciated.

b. Manual mode:

The generator shall run to the dictates of manual controls on the generator. No automatic changeover of mains to generator supply or vice versa shall take place. The generator shall be loaded by manual switching if required.

38.3.4 Alternator for Diesel Generating Set:

The generation voltage shall be 415V for capacity less than 2MVA and generation voltage shall be 11kV for capacity more than 2MVA.

Alternator shall be 4 pole, 3 phase ,50 Hz, 0.8 P.F, salient pole, revolving field, brushless type, self-regulating continuously rated and manufactured in accordance with ISO/BS/IEEE 4722, BS 5000 : Part 99 or IEC 60034-1. They shall be totally enclosed, screen protected, fan ventilated and vertical drip-proof conforming to IP 23.The Alternator shall be complete with excitation system, AVR and all necessary auxiliaries. The alternator shall be driven by diesel engine detailed below and shall match the same in all respects. The terminal box shall be dustproof with IP 54 degree of protection. The terminal box shall be suitably sized to terminate the size and number of cables involved. Alternators shall be capable of withstanding a 10% overload for 1 hour in any 12 hour Period under the specified conditions of temperature, humidity and atmospheric pressure.

Alternator windings shall be of Class H insulation with Class F temperature rise and tropicalised. The alternator shall have pre-packed grease lubricated ball or roller bearings and provided with facilities for regreasing whilst in service.

The alternator shall be foot mounted on a common bed frame with the prime mover close coupled to the engine flywheel housing. The direction of alternator rotation when viewed from the driven end shall be clockwise and phase voltage sequence UVW. The alternator vibration level shall not exceed the values defined in ISO/BS/IEEE 12075.

The alternator shall be capable of maintaining a short circuit current of three times full load current for a period of 10 seconds. The alternator shall be fitted with an anti-condensation heater. No individual harmonic shall exceed 1%

and the total harmonic shall not exceed 3%. The alternator, its neutral and control panel shall be earthed as per relevant standards.

The alternator rotor assembly shall comprise exciter rotor, full wave silicon bridge rectifier surge protection device and salient pole rotating field system. The rotor shall be fitted with interconnected pole face damping windings. Voltage regulation shall be maintained to within ±2.5% for a power factor of 0.8 to unity, including hot to cold variations. The steady state frequency droop between no load and full load shall not exceed 5%.Transient voltage deviation following a step load of 60% of rated at a power factor of between 0.4 and zero shall not exceed 15% with a voltage recovery time to 97% rated voltage not exceeding 0.5 second. The set shall be capable of continuous operation with a phase current imbalance of 33% of rated current whilst maintaining the output voltage within ±5% of rated.

38.3.5 Diesel Engine for Generating Set:

Engine shall be four strokes, direct injection, and turbocharged industrial machines. They shall be fitted with renewable wet cylinder liners if water cooled and shall be direct coupled to the alternator and mounted on a common rigid steel bedplate.

Engines shall be rated for continuous duty at site ambient conditions with an inherent O/ L Capacity of 10% for 1 hour in any 12 hours. The engine shall be capable of running at full load for not less than 180 hours without maintenance adjustments and 10000 hours between major overhauls. The maximum operating speed shall be 1 500 rpm. The range of manual adjustment shall not be less than ±5% of rated speed. The performance of engine governors under load conditions shall be to Class A2 in accordance with BS 5514: Part 4.

Engine governors shall be suitable for remote control load sharing between identical engine units. In addition to any electrical over speed trips, there shall be a mechanical device which shall operate at 120% of the rated speed. Re-setting of the over speed trip shall be possible by hand only. The steady state output speed drop between no load and full load shall not exceed 5%. The transient output speed deviation shall not exceed 10% for a step of 60%. Engines shall be designed to run on fuel oil complying with ISO/BS/IEEE 1460 or BS 2869, Class A2.Engines shall be cooled by means of a water jacket, heavy duty air blast radiator with integral radiator header tank, circulating pump and engine driven pusher type fan. The fan shall draw air in from the vicinity of the engine block and discharge it through the radiator core. The radiator shall be mounted on the same bedplate as the engine and alternator on suitable vibration isolators and be arranged so that it is located directly behind automatic louvers set into the external wall of the engine room. A thermostatically operated by-pass valve shall be fitted in the cooling system to maintain an optimum operating temperature during starting and running conditions. Drain cocks shall be provided so that all the water can be drained from the system. A separate oil cooler shall be used for cooling

the engine oil. A thermostatic by- pass valve shall be incorporated. Engine lubrication shall be by a closed circuit wet sump, forced feed system supplied by an engine driven pump fitted with pressure regulating and relief valves, sump suction filter and changeover renewable micro-felt full flow line filters. A hand operated semi-rotary oil pump shall be installed to carry out initial priming or to fill or empty the sump as required. The sump shall be fitted with an easily accessible drain point. The oil shall be of the grade recommended by the engine manufacturer. The starting system shall comprise 12 or 24 V heavy duty lead acid batteries (positioned on a floor mounted stand adjacent to the engine) connected by heavy duty flexible butyl rubber cables. Batteries shall be sized to give six consecutive starts of the engine at 0C. An engine driven alternator and charging system shall be provided. An automatic mains energised battery charger shall be provided, with sufficient capacity to maintain the battery in a condition to fulfill the starting requirements. Barring (hand turning) equipment shall be provided so that the engine can be manually rotated for maintenance purposes. It shall be arranged so that normal starting of the engine is inhibited whilst the hand turning equipment is connected. Twin heavy duty air intake filters in accordance with ISO/BS/IEEE 3169 or BS 7226 suitable for operating in dust laden atmospheres shall be fitted. The filters shall be of the paper element with pre-cleaner type. Turbocharger filters shall be fitted. Breathers shall be fitted with washable filters which are easily accessible for maintenance.

Instrumentation shall be provided to monitor speed, oil pressure, oil temperature (sets larger than 250 kVA), water temperature and battery charge current. The bedplate shall be of heavy gauge steel construction, stress relieved and free from distortion.

Machined surfaces shall be incorporated for mountings and for leveling. Anti-vibration mountings shall be fitted between the bedplate and the floor to prevent vibrations being transmitted to the building. The mountings shall be adjustable for leveling purposes and shall be designed to resist horizontal movement of the diesel set.

The fuel System shall comprise an engine driven feed pump with duplex filters, 990 litres day tank with supporting structure or generator skid mounted day fuel tank, with all interconnecting pipe work, flexible engine connection pipe etc.

38.3.6 Diesel Generator Control Panel:

a. The control panel shall be separately mounted on anti vibration mountings and shall

b. Comprise the following:

c. Breaker incorporating short circuit and overload trip

d. Earth fault protection for the Alternator

e. Alternator Over & Under Voltage Protection

f. Voltage Controlled Over Current Relay

g. voltmeter and seven position selector switch

h. ammeter and 4 Position selector switch

i. frequency meter

j. Power Factor Meter

k. kWh Meter

l. engine temperature and oil pressure gauge

m. service hours run indicator

n. key switch start and stop control

o. operational status indicator

p. anti-condensation heater and thermostat

q. alternator anti-condensation heater controls

r. mains fed battery charger

s. Auto start on mains power supply failure facility

t. Fails to Start (Alarm)

u. Over / Under Voltage Alarm

v. Battery Charger Fault (Alarm)

w. Low fuel Oil Level (Alarm)

x. Over Load (Alarm)

y. Low Lube Oil Pressure (Trip)

z. High Water Temperature(Trip)

aa. High Lube Oil Temperature (Trip)

bb. Electrical Protection Relays (Trip).

A reset button shall be provided to cancel the alarm /shut-down condition prior to re-starting. Simple operating instructions shall be detailed on the fascia of the control panel.

38.3.7 Synchronizing Panel

Whenever two sets are required to operate together, necessary synchronizing panel complete with circuit breaker, synchroscope, relays, meters etc shall be provided. The Panel shall be floor standing, CRCA Sheet steel enclosed.

38.3.8 Acoustic Enclosure

a) The DG Set shall be provided with acoustic enclosure, fully

integrated, weather proof with superior finish for long and durable life.

b) The acoustic enclosure shall be CRCA sheet steel enclosed with necessary panels and doors, inside lining of fire retardant foam /glass wool as acoustic material.

c) The sound level shall be restricted to 75 dB at a distance of 1 meter, under full load, free field conditions as per relevant standards.

d) The acoustic enclosure shall be certified to meet the emission norms.

38.3.9 Bulk Fuel Storage Tanks

Tanks and fittings, etc shall conform to ISO/BS/IEEE 803 or BS 799: Part 5. The tank shall be constructed in mild steel and the fittings in materials other than:

- Yellow brass, including low grade alloys of copper and zinc.
- Lead and zinc.
- Galvanized metals.
- Natural rubber.

An ullage volume above maximum contents level of the tank shall not be less than 5% of the maximum volume of the fuel. The maximum fuel surface level below the point of entry of the vent shall not be less than 100 mm. The internal surface shall be cleaned and treated with temporary preservative, soluble in fuel oil, before shipment. The following fittings shall be included:

(a) 600 mm diameter manhole complete with portable cover situated in the top of the tank complete with ladder to the interior.

(b) Dipstick, calibrated in litres with guide tube and striker plate.

(c) Local indication of fuel level to be given at a position where it can be easily read during fuel delivery.

(d) Filling pipe work and fittings complete with isolation valve and captive end cap. The filling point to be at the top of tank to prevent siphoning.

(e) Outlet pipe situated at the raised end of the tank not less than 150 mm above tank bottom, complete with check valve, isolating valve and end cap.

(f) Drain pipe situated at lowest point in tank complete with isolating valve and captive end cap.

(g) Inlet fittings for overflow pipe from daily service tank or tanks (where specified).

(h) Vent pipe situated at high level in the tank. The pipe shall rise continuously from the tank and terminate with an inverted `U' bend

and vermin screen.

(i) External ladder for horizontal tanks more than 2 m diameter.

38.3.10 Drawings / Documents Required:

All Drawings, data, technical particulars, calculations, detailed literature, catalogues Test certificates etc shall be submitted along with the bid/ after award of contract.

Punjab Rural Municipal Services Company (PRMSC)

PUNJAB RURAL SUSTAINABLE WATER SUPPLY AND SANITATION PROJECT (PRSWSSP), ENGINEERING DESIGN AND CONSTRUCTION SUPERVISION

TECHNICAL SPECIFICATIONS

CONSTRUCTION OF TUBE-WELLS

Punjab Rural Sustainable Water Supply and Sanitation Project
Engineering Design and Construction Supervision

TECHNICAL SPECIFICATIONS

CONTENTS

Page No.

1 TUBE-WELL 1

1.1 CONSTRUCTION OF TUBE-WELLS 1
1.1.1 Scope 1
1.1.2 Drilling 1
1.1.2.1 General 1
1.1.2.2 Drill Conditions 1
1.1.2.3 Drilling Procedure 1
1.1.2.4 Data and Records 2
1.1.2.5 Sampling 2
1.1.3 Installation of Tube-Well Components 2
1.1.3.1 General 2
1.1.3.2 Materials 3
1.1.3.3 Fabrication 5
1.1.3.4 Installation 5
1.1.4 Gravel Shrouding 6
1.1.4.1 General 6
1.1.4.2 Gravel Source 6
1.1.4.3 Specifications 6
1.1.4.4 Placing of Gravel 7
1.1.5 Development and Testing 7
1.1.5.1 General 7
1.1.5.2 Development 8
1.1.5.3 Testing 8
1.1.5.4 Summary 9
1.1.5.5 Equipment 9
1.1.5.6 Measurement and Data 9
1.1.5.7 Disinfection 10
1.1.5.8 Sealing 10
1.1.5.9 Approval of Materials 10

1 TUBE-WELL

1.1 Construction of Tube-Wells

1.1.1 Scope

The work covered shall consist of well drilling, installation of components, shrouding, development and testing including all plant, labour, equipment & other miscellaneous works necessary for the satisfactory completion of the tube-well as specified and approved by The Engineer/ Engineer-in- Charge.

Before proceeding with the work, the Contractor shall submit a complete work plan for performing the work. This will include but not limited to manpower, Plant and equipment and schedule of performance for completion of work.

The Contractor shall employ at site a fulltime competent Supervision staff for overall supervision of the work.

1.1.2 Drilling

1.1.2.1 General

The Contractor shall drill bore hole for the tube-well at the designated location established by the Engineer-in-Charge. The Contractor shall prepare the site for the construction of the tube-well and shall provide for water for construction requirements, the disposal of water, cuttings and refuse from the operations away from the tube-well.

1.1.2.2 Drill Conditions

General overall conditions related to the groundwater at the site of tube-well if available will be made known to the Contractor. The contractor is expected to make his own assessment of the character, quality and the conditions that may be encountered and shall take full responsibility for performance of work as specified.

1.1.2.3 Drilling Procedure

The borehole shall be drilled either by direct or reverse circulation rotary method. The diameter of the drilling bit shall depend on the bore size as specified on drawings or as directed by the Engineer- in-Charge. The bore hole shall be drilled straight and plumb so that the pump and tube- well casing may, be installed concentric with the hole and within the tolerance specified for plumbness of the casing. Waste materials from the drilling operation shall be disposed of in a manner approved by the Engineer-in-Charge.

The Contractor shall be responsible for protecting the tube-wells from contamination with foreign materials until the completion of the tube-well. The Contractor shall bear any expense that may result from any damage to tube-well, tools, or equipment that may be caused by caving, washing, or other disturbances within the tube-wells.

To prevent sloughing and caving of surface material and/or the hole, the Contractor shall furnish and install a boring casing pipe with a minimum diameter 2 inches greater than the bit diameter from not-less than 8 inches above the ground surface to bottom of the hole. The casing pipe shall be new or used pipe of adequate strength for the purpose. After the drilling

is completed, the casing pipe shall be removed by the Contractor and shall remain his property.

The use of drilling fluid additives or other suitable materials specially approved by the Engineer-in- Charge may be applied in stabilizing the bore hole. The casing shall be removed by the Contractor after the installation of pump housing pipe along with the strainer in the bore hole. However, in case of the tube-wells where shrouding material is to be provided around the periphery of the strainer (or around the strainer and the pump housing pipe) and the inner walls of the bore hole the casing shall be removed in 1.5 to 3 meter stages as shrouding is placed.

If in the opinion of the Engineer-in-Charge, it is necessary to discontinue work on any bore hole because it is out of line more than the specified limit or on account of jammed tools, or caving ground, or because of negligence on the part of the Contractor, the Contractor shall drill another bore hole at an alternative location designated' by the Engineer-in-Charge. The Contractor will not be entitled to payment for any work done or materials furnished for bore holes abandoned as a result of his operation or negligence.

1.1.2.4 Data and Records

The Contractor shall keep an accurate drilling log of each borehole including a description of all materials encountered and their location in the bore hole. A Hydrogeologist or geologist as The Engineer's representative shall be present during drilling and shall supervise the borehole logging of the hole preparing descriptive geological log. All documentation shall be countersigned by the Engineer's Representative.

All records and data shall be kept by the Contractor on forms approved by the Engineer-in-Charge. The Contractor shall deliver to the Engineer-in-Charge the original of all records completed in all respects.

1.1.2.5 Sampling

Representative ditch samples or cuttings of the material penetrated shall be taken at every 5 ft. (1.5 m) depth of borehole or at each change in lithology encountered whichever is less, or as directed by the Engineer's Representative at site. Special care shall be exercised to determine the thickness and location of each change in material encountered and to obtain satisfactory samples. Immediately upon taking the sample, each sample shall be placed in a plastic or cloth bag or specified partitioned wooden box, or other approved container, properly marked for identification, and plainly labelled with the depth of the top and bottom of the section of the bore hole represented. The containers shall be furnished by the Contractor. The method of obtaining, processing, and storing the samples will be subject to approval by the Engineer-in-Charge. The Contractor shall deliver all samples to the Engineer-in-Charge at the site of the tube-wells, except that when requested to do so by the Engineer-in-Charge, the Contractor shall deliver specified samples to the Engineer's field headquarters without delay, so as to preserve the moisture contents of the samples retrieved.

1.1.3 Installation of Tube-Well Components

1.1.3.1 General

Installation shall consist of all work required in connection with the erection of pumping housing

pipe, blind pipe, reducer, screen and bail plug/ sand trap required. For each tube-well as specified herein, or on the Drawings or as directed by the Engineer-in-Charge shall include, but not limited to storing, fabricating and installing all the tube-well components including concentric reducers.

1.1.3.2 Materials

(i) Pump Housing Pipe

The housing pipe made of mild steel, PVC or fiberglass may have the same diameter as that of the other components or it may be bigger in which case tapered joint/reducer shall be used for connection of the housing pipe with the lower part of tube-well.

The mild steel pump housing pipes shall be new and shall be either seamless (Type S Grade 8 ASTM A- 53), longitudinal welded (Type E Grade 8 ASTM A-53) or special seam fusion welded (Grade 8 ASTM A-139) mild steel of designated diameters and thickness indicated in the drawings.

PVC housing pipe shall conform to BSS-3505/1968, Fiberglass pipe ASTM D-2992, D-2412, D-2444, D-638, D-2584.

All these pipes shall be free from dents, injuries, scars and oval ties. The pump housing pipe shall be installed to extend above ground level as approved by the Engineer-in-Charge in addition to the housing as specified below ground level.

(ii) Well Blind Pipes

Well blind pipes shall be of designated diameters as indicated in the drawings, which shall be fabricated in conformity with the specifications designated here above for pump housing pipes.

Fibre glass well blind pipes whenever used shall be new and shall consist of glass reinforced plastic pipe and couplings manufactured from thermo setting epoxy resins and glass fibre by either centrifugal casting process or by a filament winding process, both using continuous filaments and without the addition of fillers or pigments of any kind.

Glass fiber used in the manufacture of pipe and couplings shall be continuous filament, electrical glass. The glass shall have a finish suitable for use and compatible hardener Each glass fiber or filament shall be thoroughly coated with epoxy resin.

All fiberglass casing pipe and couplings shall be round and straight of uniform quality and workman- ship, and free from all defects including indentations, delamination, bends, cracks, blisters, porosity, dry spots, resin segregation and resin starved areas which due to their nature, degree or extent, detrimentally affect the strength and serviceability of the pipe and couplings. The impregnation of the glass fiber with resin shall be such that when the pipe is slotted no fraying or looseness of glass fibers shall be evident. All pipe ends shall be cut at right angles to the axis of the pipe and any sharp edges shall be removed. The inside of the pipe and couplings shall be smooth and uniform. Acetone rub tests may be employed to check resin nature and curing.

Pipe sections may be furnished with integrally fabricated couplings as specified herein- after, with plain or tapered ends for connection in the manufacturer's plant to separate coupling halves or with threaded ends for connection by means of threaded couplings. The Contractor shall be responsible for the co-ordination of all casing components to ensure proper connection to adjoining sections of the tube-well casing and the MS Pump housing casing.

Couplings for fiberglass casing pipe may be threaded, mechanical or Key type couplings of a design to be approved by the Engineer-in-Charge. The couplings shall be manufactured of the same materials used in the manufacture of the fiberglass pipe separate components for attachment to the pipe section in the manufacturer plant.

All threaded pipe sections shall be field connected by the use of threaded fiberglass couplings. Thread geometry shall conform to the applicable sections of ASTM Standard: D -1694 or equivalent.

Key-type couplings shall consist of male and female halves designed for joining & locking together by means of key-Strip inserted in grooves in the coupling halves. The wall thickness at the groove on the male or spigot end of the pipe may be up to a minimum of 0.15 inches. Key strip and locking strips shall be fiberglass, plastic or other non-corrosive material capable of withstanding shearing and bearing stresses equivalent to the minimum axial tensile load for the couplings.

(iii) Reducer

In case where the size of the pump housing pipe is larger than the size of the strainer, the Mild steel pump housing pipe is connected with strainer or blind pipe by means of a reducer. The reducer shall be provided and made of the same material and of the same thickness as used for pump housing pipe specified above. The upper end of the reducer shall be suitable for welding to the pump housing pipe and the lower end shall be designed for connection to the specified size and type of the well blind pipe.

(iv) Bail Plug/Sand Trap

Bail plug/Sand trap shall be of the same material and thickness as followed for well casing. Sand trap shall be provided with a base plate, welded at one end of the pipe. A steel hook bent in the form of 'U' shall be bolted to the base plate to sustain suspended length casing including the strainer and blind pipe. Bail plug/Sand trap shall be one to three meters long in size or as indicated in the drawing.

(v) Well Screen

Well screen shall be either brass, PVC or fiberglass suitable for gravel pack tube-well and strong enough for location at a depth as shown' on the drawings, below ground level.

The strainer shall have smooth, sharp-edged slots free of burrs, chipped edges, or broken are as on the interior or exterior surfaces of the pipe. The slots shall be machine cut having not more than 1.6 mm width. The width of the slot shall be dependent on the particle sizes of the sand. The open area of slotted casing shall be as approved by the Engineer-in-Charge. The slots or groups of slots shall be distributed in a uniform pattern around the periphery of the pipe. The openings shall be free from jagged edges irregularities or anything that will

accelerate or contribute to clogging or corrosion.

Factory slotted casing to be delivered to the work site *for joining* and placement in the well.

1.1.3.3 Fabrication

The depth of pump housing pipe will be established by the Engineer-in-Charge depending on the future water levels and draw down anticipated. Length of the specified diameter of steel pipe shall be provided to extend the pump housing/casing from the elevation of the top of the pump housing pipe to the depth established by the Engineer-in-Charge.

Adjoining sections of Mild steel pump housing pipe shall be assembled by field welding. The ends of the casing sections shall be lathe turned or other-wise prepared for joining. All fields welding shall be performed by the electric arc method, using heavily coated welding rods suitable for all position welding. After being welded, the welds shall be cleaned of slag and shall show uniform smooth surface without over-lap, porosity and clinker. The pump housing pipe shall be connected to the tube-well casing (slotted and blind pipe) by means of a concentric tapered reducer.

The length and sizes of tube-well casing (slotted and blind pipe) to be installed shall be specified for the tube-well by the Engineer-in-Charge and shall be sufficient to extend from the bottom of the housing pipe to the top of the bail plug. Bail plug shall be provided at the bottom of the tube-well casing. The tube-well casing shall consist of sections for installation opposite water yielding formations and plain pipe sections or bail plug opposite non-water yielding formations as directed by the Engineer-in-Charge.

1.1.3.4 Installation

The Contractor shall install the entire pump housing and tube-well casing assembly straight, plumb, and concentric in the drilled hole to permit the installation of the pump in such a manner that it will operate adequately and without damage. The methods employed by the Contractor in the installation of the casing and in obtaining or correcting the verticality & straightness of the pump housing/ casing shall be subject to the approval of the Engineer-in-Charge. Centralizers, spacers or other suitable devices shall be attached to the tube-well casing so that it will be cantered in the drill hole throughout its entire length an held in such position while gravel shrouding is being placed. Centralizers shall be attached to the pipe in a manner that ensures that the pipe is accurately cantered in the drill hole. The detailed design of centralizers and the method of attachment to the pipe shall be subject to the approval of the Engineer-in-Charge. Unless otherwise directed by the Engineer, centralizers shall be spaced not more than 60 ft. along the overall length of screen and casing assembly.

The Contractor shall install the pump housing casing so that the deviation of its axis from the vertical shall not exceed 4 inches (100 mm) at the bottom of the pump housing casing. Measurements for determination of verticality and straightness of the pump housing casing shall be made by the Contractor in the presence of the Engineer-in-Charge upon completion of the gravel shrouding.

Straightness shall be determined by lowering a section of pipe 40 ft. long or a dummy of the same length to the bottom of the pump housing casing. The minimum diameter of the pipe or dummy shall be 1 inch less than the inside diameter of the pump housing casing. If a dummy

is used, it shall consist of a rigid spindle with three cylindrical rings, each ring having a height of at least 12 inches. The rings shall be true cylinders and shall be located at each end and in the centre of the dummy. The central shaft of the dummy shall be rigid so that it will maintain the alignment of the axis of the cylindrical rings. The pump housing casing shall be sufficiently straights so the pipe or dummy can be passed freely throughout the entire length of the pump housing casing. Plumbs, pipes and dummies used in these tests shall be approved by the Engineer-in-Charge.

Any tube-well failing to meet the specified requirements for straightness, verticality and concentricity shall be abandoned, and the Contractor shall construct a new well at his own expense at an alternative site designated by the Engineer-in-Charge.

After completion of installation of the pump housing casing and approval of the installation by the Engineer-in-Charge, the Contractor shall paint the letter and number designation of the tube-well on that portion of the pump housing casing which projects above the ground surface. All paint, brushes, stencils and other materials required shall be furnished by the Contractor. The characters shall not be less than 6 inches shall be painted with lines I inch wide, and shall be positioned on the casing in accordance with the Engineer's instructions.

1.1.4 Gravel Shrouding

1.1.4.1 General

Gravel shrouding shall consist of all work required in connection with supply and placing of gravel shrouding in annular space between the walls of the drilled hole and the outside of the pump casing. The work shall include, but not limited to development of source, excavation, stock piling, grading, washing, storing, transporting and placing of' gravel shrouding as specified herein or as directed by the Engineer-in-Charge.

1.1.4.2 Gravel Source

The Contractor may obtain gravel from any source or location subject to the approval of the Engineer- in-Charge provided that the gravel meets the requirements of the specifications. The Department will not be responsible for the amount of work involved or the amount of materials wastage in order to obtain the required amount of gravel of proper gradation.

1.1.4.3 Specifications

The gravel shrouding shall be clean, washed, water worn, hard, well rounded of siliceous material, without flaky particles, free from gypsum and shale, and under no circumstances shall contain > 5% calcareous material. The gravel supplied shall be subject to inspection and screening in the field to ensure proper gradation suitable to the formation. The gravel shall be reasonably graded and shall conform to the following Table 1 requirements or as specified by the Engineer-in-Charge.

Table 1: Gravel Grading Requirements

US Standard Screen Number	Sieve Size (mm)	Percentage Passing
No.4	4.75	100
No. 8	2.36	75-91
No.10	2.00	59-75

US Standard Screen Number	Sieve Size (mm)	Percentage Passing
No.12	1.70	38-54
No. 16	1.18	16-32
No.20	0.85	0

1.1.4.4 Placing of Gravel

Gravel shall be placed at constant rate using tremie pipe, hoppers or other similar devices to provide a continuous and uniform gravel flow so as to minimize segregation of particle sizes. When tremie pipe or hoppers are used, gravel shall be introduced in the annular space between the pump housing and the edge of the hole at two points located 180 degrees apart. The tremie pipe, when used, shall be of suitable size and lowered to the bottom· of the well on two opposite sides of the bore hole and calculated quantity of gravel shall be poured in the pipe through a funnel and the pipe shall be raised by 6 ft. {1.80 meters) interval.

In all cases water shall be circulated steadily during gravel placement by inserting the drilling rod into pump housing and operating the circulation pump on the drilling rig. The water level in the annular space outside the pump housing shall be maintained at or above natural surface level by return flow from the cutting bit. Temporary casing, if used, shall be carefully withdrawn in 6 ft. to 10 ft. {1.5 m to 3.0 m) interval during placement of gravel shrouding and the gravel shall be introduced so that each stage of the hole above bottom of the casing is completely filled before the casing is withdrawn to the next stage.

The process of placement of gravel shrouding and withdrawing the temporary casing shall be continued to the ground level or up to level approved by the Engineer-in-Charge. As guidance the process of shall be continued until the bottom of temporary casing is at least 10 ft. above top of the topmost screen. Above this point temporary casing shall be removed or left at the option of the Contractor provided that no payment shall be made to the Contactor for temporary casing left in place except when it is of new material and is an acceptable substitute for an appropriate length of pump housing casing.

1.1.5 Development and Testing

1.1.5.1 General

Development and testing shall consist of all work including power supply required in connection with the development of the tube-well to produce the design capacity of sand free water with a minimum drawdown, and the testing of the tube-well to determine the effectiveness of the development operations as specified herein. Development and testing shall include, but not be limited to surging, back washing and pumping the tube-well at higher than rated capacity, testing the tube-well for specific capacity, sand content and degree of development, and disinfection and sealing of the tube- well.

The Contractor shall be required to sound the well to determine whether excess material has accumulated at the bottom of the well at the following stages of the work;

a) On completion of the casing and screen installation
b) Before the starting of the development and
c) After completion of development and testing

If it is found at any stage mentioned above that the well contains more than 2 ft. of sand or other material in the bail plug, the Contractor shall clear the well down to a level approximately 2 ft. above the bottom plate of the bail plug. Water obtained in development and testing shall be disposed of by the Contractor in an approved manner.

1.1.5.2 Development

The development procedure and methods used for development of the tube-well shall be established by the Contractor subject to approval by the Engineer-in-Charge and the development operations shall be witnessed by the Engineer-in-Charge from their initiation to their completion. The Contractor shall maintain a complete record of the development operation and shall make regular periodic measurements of discharge rates, sand content and water level measurements.

The procedures used shall include backwashing and pumping at 1.5 times the rated capacity and may include surging or similar procedures determined by the Contractor. The Contractor shall notify the Engineer-in-Charge following the completion of the 6 hours pumping, period that the tube-well is ready for testing. In wells where bentonite or other formation stabilizing agents are used, the Contractor shall undertake a program of cleaning the well with phosphates or other dispersing agents in a manner and with chemical dosages as approved by the Engineer-in-Charge prior to starting normal development work.

1.1.5.3 Testing

The contractor shall test each tube-well under the direction of the Engineer-in-Charge as described herein. Upon completion of the development operations the tube-well shall be permitted to recover for a minimum period of one hour. During this recovery period, the tube-well shall be sounded. If the comparison of the depth by sounding and the length of the casing string indicates that there is more than 6.00 feet of material in the tube-well, it shall be cleaned to within 2.0 feet of the bottom of the casing by bailing.

At the end of the first five minutes of pumping, the sand content of the water shall be determined by using a 40 inches Imhoff cone or other device approved by the Engineer-in-Charge. The sand content of the water at this time shall be less than 100 mg/litre. A second sand content determination shall be made 10 minutes after the start of pumping. The sand content at this time shall be less than 30 mg/l. If the sand content tolerances are exceeded at this time, or at any subsequent time up to the time of final acceptance of the installation, sand content determinations, water level, and discharge measurements during the remainder or the one-hours and test period shall be made as directed by the Engineer-in-Charge.

When the sand test has been satisfactorily completed, the tube-well shall be further developed for 4 hours by surging and backwashing with the test pump at five to ten minute intervals. Following the development period, the tube-well shall again be pumped for a period of one hour during which time the sand test shall be repeated. The specific capacity of the tube-well shall be determined from the water level measurements and flow rates obtained, during the pumping periods. If the specific capacity obtained from the second pump test is found to be more than 10 percent greater than that obtained in the first pump test, the development shall be continued as directed by the Engineer-in- Charge.

Upon satisfactory completion of the above one hour pumping period the tube-well shall

be permitted to recover for a period of one hour. Upon the completion of this recovery period, a four-hour multiple step pump test shall be performed by pumping the tube-well for one hour at each of approximately four equal increments.

1.1.5.4 Summary

The following Table 2 is a short summary of the development and testing procedure:

Table 2: Development and Testing Procedure.

Activity	Duration
Development	4 Hours
Testing	
Recovery	1 hours
Pumping Period (Sand Test)	1 hours
Development	3 hours
Pumping period (Retest)	1 hours
Recovery	2 hours
Step pumping	4 hours (one hour each of the rated capacities 35%, 70%, 105%, & 140%)
Pumping period (Constant discharge test)	4 hours (140 %) of rated capacity measurement of final specific capacity sounding of well depth removal of foreign material above 2 feet by a suitable method approved by the Engineer

1.1.5.5 Equipment

The Contractor shall furnish all necessary equipment for testing the tube-well, including a water lubricated or oil lubricated test pump, a valve for fine adjustment of the discharge, an electric measuring device to determine the drawdown during each stage of the test and Imhoff cones to measure sand content. If oil lubricated test pumps are used, the contractor shall exercise all reasonable precautions to keep the leakage of lubricating oil into the tube-well at a minimum and shall promptly remove all oil which collects on the water surface in the tube-well by the addition of detergents or other suitable chemicals proposed by Contractor and approved by the Engineer-in- Charge and pumping the emulsified oil from the tube-well. In the event the Contractor fails to keep the leakage of oil into the tube-well within acceptable limits or to promptly remove oil accumulations from the tube-well, the Engineer-in-Charge will order the use of oil lubricated test pumps discontinued and the Contractor shall use water lubricated pumps for testing of the tube-wells. The actual depth of setting for the test pump will be determined by the Engineer-in-Charge after the tube-well has been developed. Piping, gauges, orifices, meters, wire boxes or other measuring devices shall be furnished, installed and removed by the Contractor and will remain his property. All measuring devices and testing equipment shall be subject to approval by the Engineer-in-Charge.

1.1.5.6 Measurement and Data

The Contractor shall take drawdown and discharge measurements and other pertinent data during each test at intervals as specified by the Engineer-in-Charge. All such data shall be recorded on forms approved by the Engineer-in-Charge, and the original of such forms shall be delivered to the Engineer- in-Charge at the completion of the development and testing operations.

1.1.5.7 Disinfection

After development and testing of the tube-well has been satisfactorily completed, and when approved by the Engineer-in-Charge, the Contractor shall disinfect the tube-well by dispersing chlorine solution throughout the entire depth of the well to obtain a minimum chlorine content of 50 mg/l. The procedure and equipment used to introduce and disperse the chlorine in the tube-well shall be subject to approval by the Engineer-in-Charge.

1.1.5.8 Sealing

Upon completion of the tube-well the Contractor shall seal the tube-well with a¼ inch thick steel plate cap welded to the pump housing at few points using Arc welding, or by some other method approved by the Engineer-in-Charge. Compliance with this requirement will not relieve the Contractor of his responsibility for the safeguarding of any part of the tube-well completed until the Certificate of Acceptance is issued for the entire tube-well installation.

1.1.5.9 Approval of Materials

As soon as practicable but within 30 days after receipt of notice to proceed and before any materials or equipment are purchased, the Contractor shall submit for approval by the Engineer-in-Charge a complete schedule, in triplicate, of materials and equipment to be incorporated in the work, together with the names and addresses of the manufacturers and their catalogue cuts, diagrams, drawings, and such other descriptive data as may be required by the Engineer-in-Charge. No consideration will be given to partial lists submitted from time to time. Approval of materials and equipment under deviations from the specifications shall not be granted unless the attention of the Engineer-in-Charge has been directed to the specific deviations. Laboratory results and certifications, specified or otherwise required, shall be submitted prior to delivery of the material and equipment to site.

(A) Bulk Flow Meters (Quantity = 184 No) - Analogue Meters					
Sr No	**Bulk Meter Type**	**Specifications**	**Quanitity**	**Unit Price including GST**	**Total Cost**
1	**1 in**	Type: Woltman Type Mechanical Meter Size: 25 mm to 200 mm Compliance: ISO 4064 and OIML R49. Certification: OIML R49 and/or MID 2014/32/EU (MI-001). Accuracy Ratio: R160 or higher. Working Pressure: PN16. Body Material: Epoxy-coated ductile iron or Cast iron Temperature: Up to 50°C. Tamper-resistant dry dial register. Factory calibration certificate		**10,030.00**	-
1	3 in			41,300.00	-
2	4 in			47,200.00	-
3	6 in			82,600.00	-
4	8 in			112,100.00	-
					-
Total Cost including of instllation					-

(B) Water Meters (15 mm Nominal Diameter) - (Adjusting 20% Contractor's Profit and 18% GST)

Sr No	BOQ	Quantity	Unit Rate	Total
1	Providing & installation of GI water supply connection pipe including 15mm inner dia HDPE pipe from distribution line to plinth level, inner dia GI pipe 4ft/height from plinth level of the building, GI saddle clamp, brass with foam & nuts, ferrule double action complete in all respect. It includes saddle clamp 110 mm x brass ferrule HDPE pipe connector for ferrule valve joint, 15 mm x nipple, 15 mm female elbow, 15 mm x GI pipe (4ft & 1 ft.) It includes the supply to respective sites at tehsils and schemes, complete installation and commissioning.		5574	
2	**1. Technology:** Single Jet Dry Type **2. General Features** (a) Visual Meter Reading (b) Tamper proof. (c) Provided with non-return valve (d) Un- affected by grit and particulates (e) Provided with wire and lead seal (f) Not effected by Magnetic field **3. Conforming to:** Compliance Certificate required showing compliance to ISO: 4064 (International Organization Standardization) or BS EN ISO: 4064 Certifications: Certificate issued by any Authorized Body of (a) OIML: R49 (International organization for legal Metrology) (b) MID/2004/22/EEC or AWWA Manual on Water Meters M6 or Japan Water Works Association (JWWA) Equipment Used for Testing (Quality Assurance) Equipment used for testing shall comply with clause 4.6 of BS 5750: Part 1987(5) Detailed Metrological Specifications **4. Size: 15mm** **Accuracy: Class II** Material: Brass/Nonferrous Metal Protection: Class IP-68 Ambient Temperature: +5° to 55° C **5. Liquid Temperature upto 50° C** **6. Maximum Working Pressure 16 bar; Dry Dial** **7. CE marking should not be less than 5mm height as per 93/465/EEC** **8. Installation i. Any Direction ii. Horizontal (Single Jet)** **9. Flow rate: Q3/Q1 =160** **10. Maximum flow rate Q3 (m^3 /h) for 15mm Meter = 2.5**		6372	
	Total (PKR)			**0.00**

Grand Total (A+B) for Both Goods Installation	**-**

ENVIRONMENTAL AND SOCIAL MANAGEMENT PLAN

Phase II – 425 Villages

Punjab Rural Sustainable Water Supply and Sanitation Project (PRSWSSP)

Punjab Rural Municipal Services Company
Local Government and Community Development Department ,
Government of Punjab

THE WORLD BANK

TABLE OF CONTENTS

Page No.

Contents

TABLE OF CONTENTS i

LIST OF FIGURES vi

LIST OF TABLES vii

LIST OF ABBREVIATION viii

1 INTRODUCTION 1-1

1.1 GENERAL 1-1
1.2 PROJECT BACKGROUND 1-2
1.3 OBJECTIVE OF ESMP 1-14
1.4 SCOPE OF ESMP 1-15
1.5 CONTRACTUAL REQUIREMENTS/ OBLIGATIONS OF ESMP 1-15
1.6 APPROACH & METHODOLOGY TO WORK 1-15
1.6.1 Approach 1-15
1.6.2 Methodology 1-16
1.7 STRUCTURE OF ESMP 1-19

2 LEGAL AND ADMINISTRATION FRAMEWORK 2-1

2.1 GENERAL 2-1
2.2 SUMMARY OF KEY NATIONAL STRATEGIES, POLICIES, ACTS AND LEGISLATION 2-2
2.3 KEY PROVINCIAL STRATEGIES / POLICIES, LEGISLATION / ACTS, LAWS AND REGULATIONS 2-5
2.4 APPLICABLE WORLD BANK POLICIES 2-12
2.4.1 World Bank Operational Policies 2-12
2.5 MANAGING THE RISKS OF ADVERSE IMPACTS ON COMMUNITIES FROM TEMPORARY PROJECT INDUCED LABOR INFLUX 2-12
2.6 ENVIRONMENTAL, HEALTH & SAFETY GUIDELINES 2-13
2.7 INTERNATIONAL LABOUR ORGANIZATION (ILO) FUNDAMENTAL CONVENTIONS – RATIFIED BY PAKISTAN 2-13
2.8 INTERNATIONAL PROTOCOL/CONVENTIONS 2-13
2.9 INSTITUTION RESPONSIBLE FOR PLANNING, POLICIES AND REGULATIONS 2-14
2.9.1 Environmental Protection Agency, Punjab 2-14

3 PROJECT DESCRIPTION 3-1

3.1 NEED AND PURPOSE OF PROJECT 3-3
3.2 PROJECT LOCATION 3-4
3.3 OBJECTIVES OF PROJECT 3-5
3.4 PROJECT DESCRIPTION 3-5
Stand Post 3-11
3.5 PROJECT COST 3-15
3.6 LAND ACQUISITION 3-15
3.7 PROJECT ADMINISTRATIVE JURISDICTION 3-27
3.8 PROJECT IMPLEMENTATION SCHEDULE 3-27
3.9 CONSTRUCTION ACTIVITIES AND REQUIRED MACHINERY 3-27

3.10 CONSTRUCTION CAMPS 3-27
3.11 CONSTRUCTION MATERIALS 3-28
3.12 WORKFORCE REQUIREMENT 3-28
3.13 SOLID WASTE GENERATION 3-28
3.14 WATER REQUIREMENT 3-28
3.15 WASTEWATER GENERATION DURING CONSTRUCTION PHASE 3-29

4 BASELINE PROFILE 4-1

4.1 GENERAL 4-1
4.2 DELINEATION OF STUDY AREA/ AREA OF INFLUENCE (AOI) 4-1
4.3 PHYSICAL ENVIRONMENT 4-1
4.3.1 Topography 4-1
4.3.2 Geology 4-2
4.3.3 Climate and Meteorology 4-2
4.3.4 Water Resources 4-1
4.3.5 Environmental Monitoring, Sampling and Testing 4-7
4.3.6 Seismology 4-11
4.4 SENSITIVE RECEPTORS 4-11
4.5 BIOLOGICAL ENVIRONMENT 4-25
4.5.1 Flora 4-25
4.5.2 Fauna 4-26
4.5.3 Endangered Species 4-27
4.5.4 Legally Protected Areas 4-27
Figure 7: Wildlife Sanctuaries and Game Reserves 4-29
4.6 SOCIOECONOMIC PROFILE 4-29
4.6.1 Population Size 4-29
4.6.2 Findings of Socioeconomic Survey 4-54
4.6.3 Results of Gender Situation Survey 4-63

5 PUBLIC CONSULTATION 5-1

5.1 GENERAL 5-1
5.2 OBJECTIVES AND PRINCIPLES OF CONSULTATION 5-1
5.3 CONSULTATION AND PARTICIPATION PROCESS 5-1
5.4 IDENTIFICATION OF STAKEHOLDERS 5-2
5.5 INFORMATION DISSEMINATION 5-2
5.6 METHODS OF PUBLIC CONSULTATION 5-2
5.7 APPROACH ADOPTED FOR THE CONSULTATION 5-3
5.8 STAKEHOLDERS CONCERNS TOWARDS THE PROJECT 5-3
5.8.1 Concerns and Issues 5-3
5.9 CONSULTATIONS WITH FEMALE COMMUNITY MEMBERS 5-4
5.10 CONSULTATION WITH INSTITUTIONAL STAKEHOLDERS 5-5
5.11 CONSULTATION WITH NGO 5-8
5.12 PRESSING NEEDS OF THE CONSULTED VILLAGES SUGGESTED BY LOCAL PEOPLE 5-8
5.13 DISCLOSURE OF ESMP 5-8

6 ANTICIPATED ENVIRONMENTAL IMPACTS & MITIGATION MEASURES 6-1

6.1 GENERAL 6-1
6.2 SCOPING OF IMPACTS 6-1
6.3 METHODOLOGY 6-1
6.3.1 Screening Checklist 6-1
6.3.2 Notion of Significance 6-2
6.3.3 Study Area/ Area of Influence 6-2

6.4 Environmental & Social Considerations (E&S) in Project Design....6-2
6.5 Anticipated Impacts during Pre-Construction/Design Phase....6-3
6.5.1 Layout Planning & Design....6-3
6.5.2 Soil Instability....6-3
6.5.3 Impacts of Drains construction....6-3
6.5.4 Environmentally Responsive Design Considerations....6-4
6.5.5 Groundwater....6-5
6.5.6 Surface Water....6-5
6.5.7 Seismic & Other Hazard....6-6
6.5.8 Damage to Existing Infrastructure....6-7
6.5.10 Fire Fighting System....6-7
6.5.11 Land Acquisition....6-8
6.6 Anticipated Impacts during Construction Phase....6-9
6.6.1 Topography....6-9
6.6.2 Soil Erosion....6-9
6.6.3 Soil Contamination....6-10
6.6.4 Trench Failure....6-10
6.6.5 Construction Camps/Camp Sites....6-10
6.6.6 Water Quality....6-11
6.6.7 Air Quality....6-12
6.6.8 Noise....6-13
6.6.9 Municipal and Construction Waste/ Wastewater....6-13
6.6.10 Chance of Finding Artifacts....6-13
6.6.11 Resource Conservation....6-14
6.6.12 Biodiversity Conservation....6-14
6.6.13 Health and Safety....6-15
6.6.14 Traffic Management....6-17
6.6.15 Nuisance/ Disturbance to Sensitive Receptors (Educational, Health and Religious Places)....6-17
6.6.16 Accessibility....6-18
6.6.17 Gender-Based Violence (GBV)....6-18
6.6.18 Influx of Labor....6-19
6.6.19 Social/ Cultural Conflicts....6-20
6.6.20 Child Labor....6-21
6.6.21 Economic Activity....6-21
6.7 Anticipated Impacts during Operational Phase....6-21
6.7.1 Soil....6-21
6.7.2 Air Quality....6-22
6.7.3 Odour....6-22
6.7.4 Elite Capture....6-22
6.7.5 Social Inclusion....6-23
6.7.6 End Water User of Treated Wastewater....6-24
6.7.7 Solid Waste....6-24
6.7.8 Sludge....6-25
6.8 Positive Impacts....6-26
6.8.1 Improved Water Supply System....6-26
6.8.2 Improved Sewerage System....6-26
6.8.3 Improvement in Public Health, Hygiene and Sanitation....6-26
6.8.4 Landscape....6-26
6.8.5 Commulative Impacts of Water Extraction & Sewerage Treatment....6-26
6.8.6 Other Positive Impacts....6-27
6.9 Operational Sustainability....6-27
6.10 Induced Impacts....6-28

7 ENVIRONMENTAL & SOCIAL MANAGEMENT & MONITORING PLAN 7-1
7.1 GENERAL 7-1
7.2 IMPLEMENTATION OF ENVIRONMENTAL & SOCIAL MANAGEMENT PLAN (ESMP) 7-1
7.2.1 Roles and Responsibilities of the Functionaries involved in ESMP Implementation *7-2*
A. World Bank *7-2*
B. Punjab Environmental Protection Department *7-2*
C. PRMSC *7-2*
D. Environmental and Social Cell (ESC) *7-2*
E. Supervisory Consultant (SC) *7-3*
F. Construction Contractor (CC) *7-3*
7.2.2 Institutional Arrangement for Implementation of ESMP by PRMSC during O&M Phase *7-3*
7.3 REPORTING 7-4
7.4 NON-COMPLIANCE WITH THE ESMP 7-4
7.5 CONTRACTORS ESMP 7-4
7.6 INCLUSION OF ESMP IN BIDDING/ CONTRACT DOCUMENTS 7-5
7.7 ENVIRONMENTAL AND SOCIAL MONITORING PLAN 7-5
Layout Planning & Design *7-6*
Impacts of Drains construction *7-6*
Risk to Structures *7-6*
Groundwater *7-7*
Damage to Existing Infrastructure *7-7*
ANTICIPATED IMPACTS DURING THE CONSTRUCTION PHASE 7-8
Topography *7-8*
Soil Erosion *7-9*
Soil Contamination *7-10*
Trench Failure *7-11*
Construction Camps/Camp Sites *7-11*
Water Quality *7-12*
Air Quality *7-13*
Dust 7-15
Noise 7-15
Municipal and Construction Waste/ Wastewater *7-16*
Resource Conservation *7-16*
Occupational Health and Safety *7-18*
Traffic Management *7-21*
Accessibility *7-22*
Resilience to Climate Change *7-22*
Liquid and Solid Waste from Construction Camps *7-23*
Flammable and Hazardous Materials *7-24*
Gender Based Violence (GBV) *7-25*
Influx of Labor *7-26*
Social/ Cultural Conflicts *7-27*
Child Labor *7-28*
ANTICIPATED IMPACTS DURING OPERATIONAL PHASE 7-28
Soil 7-28
Air Quality *7-29*
Odour 7-30
Solid Waste *7-30*
7.8 GRIEVANCE REDRESSAL MECHANISM (GRM) 7-37
7.8.1 Objectives *7-37*
7.8.2 Disclosure of GRM *7-37*

7.8.3 Records and Monitoring *7-38*
7.8.4 Proposed Institutional Mechanisms *7-38*
7.8.5 GRM Process Implementation *7-39*
7.8.6 Mode of Complaint *7-39*
7.8.7 GRM Procedures and Timelines *7-40*

8 ESMP Budget 8-1

8.1 ESMP Cost 8-1
8.2 Budget Estimate for PPE During the Construction Phases 8-2
8.3 Break Up of Health Safety & Environment 8-3
8.4 Environmental Monitoring Cost 8-5
8.5 Training Program 8-6
8.6 Institutional Capacity & Strengthening 8-8
8.7 ESMP Cost of Village 8-10

LIST OF FIGURES

Page No.

Figure 1:Illustrating project intervention in component 1 sub component 1.2 3-1
Figure 2: Illustrating project inventions in component 1 sub component 1.1 3-1
Figure 3: Location Map of Project Area 3-4
Figure 4: Process Flow Diagram of STP / WWTP / ABR.....3-15
Figure 5: Hydrology Map of Punjab Province 4-2
Figure 6: Seismic Zone Map of Project Area 4-11
Figure 7: Wildlife Sanctuaries and Game Reserves.....4-29
Figure 8: Occupational Status of the Respondents.....4-55
Figure 9: Occupational Status of the Respondents.....4-56
Figure 10: Monthly Income of the Respondents 4-57
Figure 11: Monthly Income of the Respondents 4-57
Figure 12: Satisfaction with household water quality 4-58
Figure 13: Type of Sewerage System 4-59
Figure 14: Type of Sanitation Facility.....4-59
Figure 15: Type of Solid Waste Facility 4-60
Figure 16: Type of Construction of House 4-61
Figure 17: Organizational Setup for implementation of ESMP.....7-1

LIST OF TABLES

Page No.

Table 1 : Summary of ESMP Prepared for 180 villages 1-1
Table 2 : Project Area with Number of Villages 1-2
Table 3: Location and Name of Phase-II Villages in Different Tehsils 1-3
Table 4: Key National Strategies / Policies, Legislation / Acts, Laws and Regulations and Their Relevance to the Project 2-2
Table 5:Key Provincial strategies / policies, legislation / Acts, Laws and Regulations and Their Relevance to the Project 2-6
Table 5:International Agreements/Conventions Relevant to the Project 2-14
Table 7: Summary of Proposed Water Supply and Sewerage Components 3-5
Table 7: Manhole Spacing 3-13
Table 8: Manhole Diameter 3-13
Table 9: Land Requirement Details 3-16
Table 10: List of expected Machinery/Equipment 3-27
Table 11: Topographic Variations 4-2
Table 12: Temperature Variation in Summer and Winter Season 4-1
Table 13: Average Wind Speed and Windiest Month in Tehsils 4-1
Table 14: Surface Water Bodies in Targeted Villages of Relevant Tehsils 4-3
Table 15: Groundwater Analysis 4-5
Table 16: Ambient Air Quality Results 4-7
Table 17: Noise Monitoring Results 4-8
Table 18: Results of Wastewater 4-10
Table 19: Sensitive Receptors 4-11
Table 20: Primary data results of Project Area 4-29
Table 21: Findings of the Consultation Meetings 5-3
Table 22: Findings of the Female Consultation Meetings 5-4
Table 23:Concerns of Relevant Government Departments 5-5
Table 24: Distribution of Periodic Reports 7-4
Table 25: Environmental and Social Management Plan (ESMP) 7-6
Table 26: Village-wise ESMP Cost 8-1
Table 27: Budget Estimate for HSE During the Construction Phase 8-2
Table 28:Break Up of Personal Protective Equipment 8-4
Table 29: Environmental Monitoring Cost 8-5
Table 30: Training for Contractors by PRMSC and EDCS consultants 8-6
Table 31: HSE Supervision 8-9
Table 32: ESMP IMPLEMENTATION COST - Village Wise 8-10

LIST OF ABBREVIATION

ABR	Anaerobic Baffled Reactor
AoI	Area of influence
BDL	Below detection limit
BHU	Basic Health Unit
BMPs	Best Management Practices
BOD	Biochemical Oxygen Demand
BOQs	Bills of Quantities
BPs	Bank Procedures
CBD	Convention on the Biological Diversity
CBO	Community Based Organization
CC	Construction Contractor
CFT	Cubic foot
CO	Carbon Mono Oxide
COD	Chemical Oxygen Demand
DC	Design Consultant
DC	Design Consultant
DG	Directorate General
EA	Environmental Assessment
ECO	Economic Cooperation Organization
ECO	Economic Cooperation Organization
EDCS	Engineering, Design & Supervision Consultancy Services
EE	Environmental Engineer
EHS	Environmental, Health & Safety
EIA	Environmental Impact Assessment
ENE	East-Northeast
EPA	Environmental Protection Agency
EPD	Environmental Protection Department
ERPs	Emergency Response Procedures
ESC	Environmental and Social Cell
ESMF	Environmental Social & Management Framework
ESMP	Environment and Social Management Plan
ESS	Environmental & Social Safeguard
GAP	Gender Action Plan
GBV	Gender Based Violence
GHG	Greenhouse Gas
GIIP	Good International Industry Practice
GPD	Gallons per Day
GRC	Grievance Redressal Committee
GRM	Grievance Redress Mechanisms
HDPE	High Density Polyethylene
HHs	Households
HSE	Health, Safety & Environment

IEE	Initial Environmental Examination
LG	Local Government
LPG	Liquefied Petroleum Gas
MGD	Million Gallon per Day
MS	Medical Superintend
MSDS	Material Safety Data Sheets
NCS	National Conservation Strategy
NE	North East
NESPAK	National Engineering Services Pakistan
NGOs	Non-Governmental Organizations
NNE	North-Northeast
NNW	North-Northwest
NO	Nitrogen Oxide
NO2	Nitrogen Di Oxide
NOC	No Objection Certificate
NTU	Nephelometeric Turbidity Unit
NW	North west
O&M	Operational and Maintenance
O3	Ozone
OHS	Occupational Health & Safety
OHWT	Overhead water Tank
OIC	Organization of the Islamic Conference
OP	Operational Policy
PATs	Pakistan Approaches to Total Sanitation
PCC	Public Complaints Center
PD	Project Director
PDWP	Provincial Development working party
PEPA	Punjab Environmental Protection Agency
PEQS	Punjab Environmental Quality Standards
PGA	Peak Ground Acceleration
PGA	Peak Ground Acceleration
PICs	Public Information Centers
PIMU	Project Implementation and monitoring unit
PIU	Programme implementation unit
PKR	Pakistan Rupees
PLGA	Punjab Local Government (Amendment)
PM	Particulate Matter
PPE	Personal Protective Equipment
PRMSC	Punjab Rural Municipal Services Company
PRSWSSP	Punjab Rural Sustainable Water Supply and Sanitation Project
PWA	Punjab Water Act
RCC	Reinforced Cement Concrete
ROW	Right of Way
SAARC	South Asian Association for Regional Cooperation
SBC	Seismic Building Code
SC	Supervision Consultant
SDS	Social Development Specialist

SDU	Service Delivery Unit
SEA	Sexual Exploitation and abuse
SH	Sexual Harassment
SO2	Sulfur Di Oxide
SOP	Standard Operating Procedures
SPM	Suspended particulate Matter
STDs	Sexually Transmitted Diseases
STI	Sexually Transmitted Infections
STP	Sewage Treatment Plant
SWM	Solid Waste Management
TC	Total Coliforms
TCU	True Color Unit
TDS	Total Dissolve Solids
THQ	Tehsil Head quarter
TOR	Terms of Reference
TPV	Third Party Verification
TSS	Total Suspended Solid
UNCCD	United Nation Convention to Combat Desertification
UNESCO	United Nation Educational Scientific and Cultural Organization
UNFCCC	United Nations Framework Convention on Climate Change
UNO	United Nations Organization
WASH	Water, Sanitation and Hygiene
WB	World Bank
WBG	World Bank Guideline
WHO	World Health Organization
WNW	West-Northwest
WWTP	Wastewater Treatment Plant

Executive Summary

1. Introduction

The Local Government & Community Development Department (LG&CDD), Government of Punjab, through its Punjab Rural Municipal Services Company (PRMSC), a company registered under section 42 of "The Companies Act 2017", is implementing Punjab Rural Sustainable Water Supply and Sanitation Project (PRSWSSP)" in target area of 2000 villages in 16 tehsils of Punjab province; with the financial assistance of the World Bank. The current document is the consolidated "Environmental and Social Management Plan (ESMP)" prepared in line with World Bank Safeguard Policies; and as per guidance provided in the project's Environmental Social & Management Framework (ESMF)".

Pilot Phase:

To implement this project, the Executive Committee of the National Economic Council (ECNEC) considered the summary dated 27th January, 2022 submitted by the Ministry of Planning, Development and Special Initiatives titled "Punjab Rural Sustainable Water Supply and Sanitation Project (PRSWSSP) and approved the proposal with the following directions:

i. A "Pilot Project" should be conducted, based on 10% of the approved project scope.
ii. After one year, lessons learned from the pilot phase should be shared with the Central Development Working Party (CDWP), with a specific focus on the operation and maintenance aspects of the project.
iii. The project timeline should be reduced to five years after gaining insights from the pilot phase.

To initiate the Project, an initial pilot phase was undertaken in 200 villages (Annex-1) to assess its feasibility and long-term sustainability. For this purpose, the 16 tehsils were organized into six geographical clusters, and the feasibility studies, engineering designs, PC-I documents, BOQs, and safeguard instruments for all 200 villages were completed across five implementation packages.

Summary of ESMP Prepared for Pilot Phase

Sr.no.	ESMP Phases	No. of villages of Pilot Phase	Date of Approval
1.	Phase 1 of Pilot Phase	26	18th May, 2023
2.	Phase 2 of Pilot Phase	42	27th July, 2023
3.	Phase 3, 4 and 5 of Pilot Phase	132	29th Nov, 2023

Lessons learnt during Pilot Phase and Recommendations for Next Phase

It was observed that the Environmental, Social and Biological baselines, were not properly established in the EIAs and ESMPs. EIAs and ESMPs where not comprehensive enough and documents were lagging in Traffic Management plan (Mobility Plan), Social Impact Assessment and Mitigation Plan, Stakeholder Engagement plan (SEP), Labor Management Plan, Labor Code of Conduct, GBV Plan and Gender action plans and its linkage with project PDOs, man hours for E&S Safeguards related staff in EDCS consultants TORs were found to

be not sufficient, which resulted in delayed approvals of E&S instruments.

The EDCS consultants were advised during the negotiations and bid meetings to establish the baselines through physical visits, rather than through online data and surveys available. E&S instrument must be comprehensive enough. 5% of E&S payment will be released after the approval of ESMPs from bank and EIAs from EPD. Consultants are responsible for FGDs, Stakeholder engagements and conducting public hearing sessions for the ESMP and EIAs.

It was decided that payment of HSE Expert, Social Expert, Gender Expert and inspector should be linked with HSE/PPE compliance in the field. Consultant should also promote PPE/HSE culture for their staff and enforce the same for contractor staff. The man-hours allocated to Environmental and Social (E&S) safeguards should be increased to ensure effective implementation, monitoring, and compliance with World Bank requirements.

During the implementation phase, it was observed that contractors were reluctant to prepare Contractor's ESMPs (C-ESMPs) and to deploy dedicated Health, Safety, and Environment (HSE) staff at construction sites, primarily due to the associated costs and negligence by EDCS consultants in timely compliance of E&S Safeguards as "the engineers/project managers". These costs were not explicitly included in the ESMP budget of pilot phase. To address these issues, the PRMSC Environmental and Social (E&S) Wing incorporated the cost of preparation of C-ESMPs and the hiring of HSE staff as mandatory and clearly defined line items within the ESMP budget approved for remaining 1800 villages.

Furthermore, the ESMP budget was initially a biddable item, which led contractors to quote the lower amounts to remain competitive to win the bid. As a result, contractors were reluctant to implement ESMP requirements or had to absorb these costs independently. To mitigate this risk, PRMSC, with the approval of the World Bank, revised the approach and made the ESMP budget a fixed, non-competitive item to be made part of the bid as provisional sum.

In addition, certain essential environmental and social mitigation measures such as tree plantation, barricading tapes, and reflective safety jackets were not included in the original budget. These items have now been incorporated into the revised ESMP budget to ensure comprehensive and effective implementation.

Remaining Scope of 1800 villages:

Building on the lessons learned from the pilot phase of 200 villages, the CDWP granted approval on 12 December 2024 for PRMSC to proceed with the remaining scope of 1,800 villages. To initiate the preparation of feasibility studies, detailed engineering designs, PC-I documents, and safeguard instruments, PRMSC has reorganized the 16 tehsils into five geographical clusters and engaged five Engineering Design and Supervision Consultants (EDSCs) under the assignment titled "Consultancy Services for Engineering Design and Construction Supervision of Punjab Rural Sustainable Water Supply & Sanitation Project (PRSWSSP)."

Summary of ESMP Prepared for 1800 villages

Sr.no.	ESMP Phases	No. of villages of Pilot Phase	Date of Approval
1.	Phase 0	77	13th January, 2026
2.	Phase 1	232	23rd Februrary, 2026

Phase-II (425 villages)

The ESMP for Phase-II has been developed in accordance with the template used for ESMP Phase 0. All comments and suggestions from Phases 0 and I have been duly incorporated into this ESMP. Under Phase-II, covering the batch of 425 villages. To expedite implementation, the EDSCs have been instructed to submit feasibility studies, detailed engineering designs, PC-I documents, and environmental and social safeguard instruments on a phased basis.

Background

The Project Development Objective (PDO) of PRSWSSP is to provide equitable and sustainable access to safely managed water and sanitation services and to contribute to the reduction of child stunting. This objective will be achieved through improved sanitation systems, provision of clean drinking water, enhanced solid waste management, behavior change interventions, and capacity-building initiatives across rural settlements of Punjab.

For project implementation, the Punjab Rural Municipal Services Company (PRMSC) has divided the 16 tehsils into five clusters based on geographical proximity and has engaged five Engineering Design and Supervision Consultants (EDSCs), one for each cluster. The consultancy assignment, titled “Consultancy Services for Engineering Design and Construction Supervision of Punjab Rural Sustainable Water Supply & Sanitation Project (PRSWSSP),” requires the consultants to:

(i) prepare design documentation including Sub-scheme/Project Documents (PC-I) and Bills of Quantities for water supply and sanitation schemes to ensure economies of scale and effective outcomes; and

(ii) provide resident supervision during infrastructure development.

This Environmental and Social Management Plan (ESMP) addresses the potential impacts associated with the design, construction, and operation of water supply and sewerage facilities. A consolidated ESMP for Phase-II, covering 425 villages, has been prepared and is currently under review for approval by the Provincial Development Working Party (PDWP).

The anticipated environmental and social impacts for these 425 villages are largely localized, site-specific, and temporary in nature. Few, if any, impacts are irreversible, and all can be effectively mitigated through appropriate measures. Based on the Environmental and Social Screening and in accordance with the Environmental and Social Management Framework (ESMF) and Operational Policies (OPs), the project is classified as Category E2, necessitating the preparation and implementation of an ESMP.

2. Policy, Legal and Administrative Framework

The national and provincial Government has promulgated laws/acts, regulations, and standards for the protection, conservation, rehabilitation, and improvement of the environment. The Punjab Environmental Protection Agency (PEPA) is the regulatory authority, which has provided guidelines for conducting Environmental Impact Assessment (EIA) studies and has the authority to issue regulatory clearance/ No Objection Certificates (NOCs) for various projects.

In addition to the laws of the land (Punjab Environmental Protection Act 1997, Review of IEE/EIA Act 2000), World Bank Operational Policies (OPs) are also applicable to the project including Environmental Assessment (OP 4.01), Natural Habitat (OP 4.04), Physical Cultural Resources (OP 4.11), Resettlement and Projects on International Waterways OP/BP 7.50.

3. Project Description

The villages selected for this subproject will be provided with Water Sanitation and Hygiene (WASH) facilities. The subproject involves provision of water supply, sewerage, overhead tanks & Pumping stations with sewage treatment.

The water supply system is planned based on groundwater quality and village size. In areas with adequate underground sweet water and a relatively large number of houses, a complete water supply scheme will be provided, including a tube well, OHR, and transmission network as per demand. In smaller villages where sweet water pockets are limited, water supply will be provided through stand posts. In areas where groundwater is brackish, RO plants will be installed to ensure safe drinking water.

The sewerage system is planned with multiple service options based on housing density, groundwater table depth, and local topography. In areas with a higher number of houses and where the groundwater table is not shallow, a conventional sewerage system will be provided, along with an ABR for treatment of wastewater prior to discharge. In areas with fewer houses, narrow streets, and shallow groundwater conditions, open drains will be provided to improve sanitation.

A hybrid system is introduced in which sewers are laid along main roads, while secondary drains from narrow streets discharge into these sewers. This approach is based on lessons learned from the pilot phase, where excavation in narrow streets caused damage to adjacent house walls. In low-density areas, communal septic tanks are proposed for wastewater treatment, with final discharge to nearby drains, watercourses, or ponds; where groundwater is deep, communal soakage pits will also be provided.

The estimated total cost of the project for the proposed 425 villages of Phase-II is **28,781 million PKR or 102.79 million US$**[1]. Total man power required on site for proposed Project will be approximately 08-30 workers per day per village in construction phase.

Excavators and road cutters are used for trench excavation and cutting of existing pavements during water supply and sewerage works. Dumpers and concrete mixer machines support material handling and preparation of concrete for manholes and thrust blocks. Plate compactors ensure proper backfilling, while generators provide continuous power for site operations. Details of equipment are provided in Section 03 of consolidated ESMP.

[1] 01 USD = 280.00 PKR

PRMSC has divided the 16 tehsils into 5 zones based on geographical location and accordingly hired the services of 5 Engineering Design and Supervisory Consultants (EDCS) for the proposed project. Under Phase-II, interventions are planned across 12 tehsils, within which 425 villages have been identified for implementation. In order to fast track the project implementation and execution of the civil works, PRMSC with the help of consultants has divided 1800 pilot villages from sixteen different tehsils into 5 packages for designing and provision of Water Sanitation and Hygiene (WASH) facilities. This document pertains to 425 villages selected in phase-II from 12 different tehsils. The subproject involves provision of water supply, sewerage, overhead tanks and Pumping stations with sewage treatment plants in all 425 villages.

Water Supply Issues:

- No water supply network in the villages;
- Most of the household use shallow groundwater;
- Shallow ground water is not fit for drinking;
- Polluted drinking water is causing water borne diseases.

Sewerage Issues:

- Properly designed sewerage system does not exist in most of the villages;
- Existing open drains are damaged and do not cover the entire settlements;
- No proper disposal Point in all the villages;
- Sewage collected in soakage pits and open plots seeps into ground and contaminates groundwater;
- Raw sewage ponds are a breeding ground for disease vectors.

Solid waste Issues:

- There is no proper solid waste management system and designated dumping sites in the project area, locals usually throw their waste into open plots or streets.
- There are heaps of waste which attract rodents, flies and disease vectors.
- Organic waste is usually burnt by the villagers, which causes health issues.
- Open drains are used as a garbage/solid waste disposal point thus resulting in decrease of water carrying capacity of these drains.
- During rain, storm water and sewage overflow from the drains and spread solid waste through the area thus causing nuisance, environmental issues and spread of diseases.

- The laying of piping network for water supply and sewerage system will not require land acquisition, as the pipeline will be buried underground. The network will be designed in a manner that the pipeline is laid along the public roads / streets. However, if pipeline route is required to pass through any private lands, special permission for laying and periodic maintenance shall be sought from the landowners. The land required for the construction of overhead tank, pumping station and STP will consist of state land, acquired through

process of No Objection Certificate (NOC). In cases where private land is needed, it shall be obtained through Voluntarily Land Donation (VLD).

- However, land through VLD is only obtained after satisfying the set criteria: first, that the state land is not available in the proposed village; second, when state land in the village is not technically viable – based on requirements of engineering design for the construction of infrastructure; third, only after meeting the VLD Screening Checklist criteria attached as Annexure-8.

4. Baseline Profile

As per the environmental screening study conducted earlier, the project falls in "Category E2" which means that the impacts of the project activities are limited and within the boundary of project area. Therefore, the whole village has been considered Area of Influence (AoI).

A. Physical Environment

The proposed project sites are rural settlements comprising residential and agriculture areas. The topography of the project area is predominantly flat. The ground elevations vary from 126 to 678 ft in proposed villages.

Punjab's area mostly consists of an alluvial plain formed by the southward-flowing Indus River and its four major tributaries. The general slope of the land is from northeast to southwest, but it rises in the areas between rivers Approximately 70 percent land area of the province comprises flood plans of Indus basin. Geologically, lands in the flood plains are lightly mantled with alluvial deposits transported from the Himalaya foothills. The underlying bedrock is composed of Precambrian metamorphic and tertiary consolidated rocks. The overlying alluvium consists of Pleistocene to recent unconsolidated deposits of sand, clay and silt. The formation age of the alluvium also dates from Pleistocene to recent, the latter being predominant earth river banks and the former around the central part of the plains, no major fault zone traverses the project area.

The project area has hot summer and cold winters. The summer starts from May and lasts till September. June is the hottest month. The mean maximum temperature varies between 39-45 ºC and minimum temperature varies between 23-29 ºC respectively for month of June. The winter seasons lasts from November to February. January is the coldest month. The mean maximum ranges between 18 - 30 ºC and mean minimum temperature ranges between 05 - 14 ºC in January

In project areas, most of the times of the year sunny days dominate. A few days per month are partly cloudy and with seldom overcast days. The maximum precipitation is observed during June to August. In project areas are classified as arid region having average annual rainfall less than 250 mm in a year. Highest intensity of rain is recorded in month of July and August owing to monsoon season.

Groundwater

As per (Electrical Resistivity Survey) ERS studies, shallow groundwater is slightly brackish, whereas deep groundwater is relatively sweet at depths of around 200 ft. Handpumps installed at depths of 50-200 ft yield sweet water and are commonly used by the local community for drinking purposes. In contrast, groundwater near the ground surface remains brackish.

As per ERS studies, groundwater at shallow depths of about 20–30 ft occurs in localized sweet water pockets. These pockets are limited to approximately 20 ft in thickness, below which the groundwater becomes brackish and unfit for drinking purposes.

In Liaqatpur groundwater is the primary source of domestic water supply. The quality of groundwater is generally brackish to moderately saline, with elevated Total Dissolved Solids (TDS) reported in several locations. In some areas, the presence of dissolved salts and occasional microbial contamination limits its direct suitability for drinking without basic treatment; however, it remains commonly used for household purposes and limited irrigation.

Groundwater depth in the tehsils of Alipur & Shujabad in the South-II Cluster ranges from 20 to 60 ft and serves as the primary source of water. The groundwater quality is non-objectionable in terms of taste and color, indicating generally acceptable groundwater conditions.

In Liaqatpur groundwater is the primary source of domestic water supply. The quality of groundwater is generally brackish to moderately saline, with elevated Total Dissolved Solids (TDS) reported in several locations.

In Kahror Pakka, parameters such as TDS and total hardness do not comply with PEQs and WHO standards. In Khairpur Tamewali, TDS, turbidity, and total hardness exceed permissible limits. In Ahmadpur Sial, the prevalence of water-borne diseases has been reported in several villages. In Pakpattan, TDS and total hardness are beyond PEQs and WHO standards, while in Darya Khan, biological parameters exceed PEQs limits in some villages. Similarly, in Bhawana, TDS and total hardness are not in compliance with PEQs and WHO guidelines.

Surface Water

Punjab is land of Indus River and its four major tributaries in Pakistan, the Jhelum, Chenab, Ravi, and Sutlej rivers. Punjab Irrigation system is one of the world's largest irrigation systems with a command area of over 21 million acres. The system consists of 24 main canals and 12 barrages and vast network of canals, distributaries and minors spanning over 40,000 kilometers. Targeted villages in north, south and center of the Punjab are in command area of this irrigation system.

The tehsils of Alipur & Shujabad in the South-II Cluster are served by major surface water resources, including the Indus and Chenab Rivers, as well as an extensive irrigation network comprising canals, distributaries, and minors. These water bodies are primarily used for irrigation and local water needs.

In Liaqatpur, canals associated with the Abbasia Canal system provide water primarily for agricultural activities, Surface water is not a major source of potable water but is widely used for irrigation, livestock, and groundwater recharge.

Surface water resources in Kot Momin are mainly influenced by the River Chenab and its associated irrigation network, including the Khadir Feeder. The feeder serves surrounding villages such as Nasir Pur, Midh, Mumrana, Khadir, Chokera, Chani, and Wan Miana, providing irrigation supplies. Seasonal flows and canal operations govern surface water availability and quality within the command area.

In Bahwalnagar the overall water quality is assessed as moderate to poor. Most physico-chemical parameters comply with acceptable limits; however, elevated TSS and turbidity remain concerns. In Kahror paka he tehsils of Kahror Pacca within the South-III Cluster are served by major surface water resources, including the Sutlej River. However, the river remains largely dry or experiences low environmental flows for most of the year. These surface water bodies are primarily utilized for irrigation purposes and to meet local water requirements.

Tehsil Khairpur Tamewali, within the South-III Cluster, relies on the Sutlej River, which has low or seasonal flows and generally moderate to poor water quality, and is mainly used for irrigation and local needs. Tehsil Ahmadpur Sial, located within the South-III Cluster, is served by the Chenab River and an extensive irrigation network that primarily supports irrigation and local water needs. Tehsil Pakpattan is served by one main canal and three distributaries, which primarily support irrigation and local water requirements, with generally moderate water quality.

Tehsil Darya Khan is served by surface water resources of generally moderate to poor quality, conveyed through the irrigation network. These waters are primarily used for agricultural irrigation and local needs, with quality influenced by seasonal variability, sediment load, and potential contamination. The overall water quality is assessed as moderate to poor. Most physico-chemical parameters comply with acceptable limits; however, elevated TSS and turbidity remain concerns.

B. Biological Environment

Project areas are rich in biodiversity because of its diverse landscape and geographical location. The variety of ecosystem is evident and is home to various species. The following section describes the biological environment of the project area.

Common animals found in the project area include wild cat, dogs, cats, jackals, Weasel, house rats, wild boar, bats, porcupine, bandicoot, soft furred rat and Indian gerbil. Domestic livestock observed during field visits include buffaloes, cattle, goats, sheep, and donkeys that are used by the local residents for their livelihood.

Bullfrog (*Hoplobatrachus tigernius*), Pahari tidda maindak (*Fejervarya limnocharis*), frog (rana tigrine) and Toad (Bufo bufo) are also present in the nearby ponds and canals during rainy season.

House sparrow (*Passer domesticus*), House crow (*Corvus splendens*) and Mynah (*Acredotheres tristis*) are the most common sight in the area. In addition, following birds are also seen in the project area**.**

Common tree lizard (*Calotes versicolor*), Monitor lizard (*Varnus bengalensis*), fat tailed lizard (*Uromastix hardwickii*), fringed toed lizard (*Acanthodactylus cantoris*), Tortoise (Testudinidae), snakes (Serpentes), cobra (Naja) and Scorpions (Scorpiones) are observed in and around the proposed site. Saw-scale viper (Echis carinatus), Indian soft-shell turtle (*Aspideretes gangeticus*), striped keelback (Amphiesma stolatum) and Indian falpshell (*Lisseyms punctate andersoni*) are also reported by the local residents.

The major floral species found in the project area include Jand trees, Karir, Beri, Van, Kikar, Sheeham, Neem, Peepal, Aak, Bair and Kikar.

There are no endangered species of either flora or fauna in the project tehsils. Neither any legally protected areas (wetlands, game reserve, biodiversity parks and forests) in the area or in the influence of the project area.

C. Social Environment

Socioeconomic baseline was established using primary and secondary data. Detailed site visits were conducted by Social Experts of consultants to appraise the prevailing socioeconomic conditions and to assess the socioeconomic impacts of the proposed project. During the field

surveys, interviews and consultation meetings were held with the local representatives i.e., Numberdars, residents (Males & Females), shopkeepers, land owners, agriculturists, and their laborers, etc., in all 425 villages of Phase-II.

Primary data was collected through a socio-economic survey with the help of a structured and un-structured questionnaire. Random sample was conducted in all 425 villages of Phase-II, 12 tehsils of Center, North and South. Secondary data was collected from the Pakistan Bureau of Statistics (Census 2023), established literature, and research.

The analysis of water and sanitation conditions across the study area highlights several key issues. Handpumps are the primary drinking water source in most villages, except in Bhawana and Darya Khan where borehole motors dominate, while piped water supply is limited to Shujabad, Kahror Pacca, Khairpur Tamewali, and Bahawalnagar, and RO filter plants are rare, observed only in Alipur and Shujabad. Satisfaction with household water quality is generally low across all Tehsils, with complete dissatisfaction in Liaqatpur and Rojhan, while Bhawana, Pakpattan, and Shujabad show relatively better yet still concerning levels of satisfaction. Open drains dominate the sewerage system, often clogged and poorly designed, causing sewage overflow, while septic tanks and soakage pits are limited to a few villages. Toilet facilities are available to most households, but open defecation persists in several areas, and solid waste management services are partially functional at all tehsils facing partial or severe deficiencies.

During survey it was revealed that the villages lacked adequate sanitation facilities, resulting the local population to unsafe water and poor hygiene conditions. As a result, locals experienced a prevalence of waterborne and water-related diseases, including diarrhea, dysentery, typhoid, cholera, intestinal infections, skin allergies. The absence of safe drinking water and proper wastewater management also adversely affected overall public health and nutritional status. With the provision of reliable water supply, improved sanitation, and appropriate wastewater management under the project, a significant reduction in waterborne diseases and overall improvement in community health and well-being is expected.

Relevance of Project-Supported WASH Interventions

The existing baseline conditions indicate a strong linkage between WASH deficiencies and adverse health and nutrition in villages. Project-supported WASH interventions such as improved access to safe drinking water, sanitation facilities, hygiene awareness, and safe wastewater management are expected to:

- Reduce the incidence of diarrheal and waterborne diseases, particularly among children under five;
- Improve nutrient absorption and overall health, thereby contributing to better nutrition outcomes;
- Reduce household expenditure on medical treatment and improve productivity; and
- Enhance community awareness regarding safe hygiene and sanitation practices.

Overall, the project interventions are likely to directly and positively impact the baseline situation of public health and nutrition, contributing to improved quality of life in villages.

Household incomes range from below Rs. 20,000 to above Rs. 50,000, with most populations especially in Kot Momin, Ahmadpur Sial, Bhawana, Darya Khan, Pakpattan, and Bahawalnagar falling in low- to middle-income groups barely meeting expenses, relatively better conditions in Liaqatpur and Khairpur Tamewali, lower income levels in Rojhan, Alipur, and Shujabad, and a more balanced distribution in Kahror Pacca, overall reflecting economic constraints and reliance on agriculture and labor-based livelihoods. Housing conditions differ across the project area with the pacca houses with RCC roofs dominate in Kot Momin and Shujabad, while kacha houses

remain prevalent in Ahmadpur Sial, Darya Khan, Pakpattan, and Kahror Pacca, with mixed patterns in Liaqatpur and Rojhan and moderate coverage in Alipur and Bahawalnagar, overall reflecting income-linked variations in housing construction. Basic amenities remain inadequate, with limited public transport, poor water quality, and widespread waterborne diseases impacting community health. Access to medical facilities varies, as some tehsils benefit from DHQs while others rely on under-resourced THQs and BHUs. Education facilities exist at primary to high school levels but are not uniformly distributed. Overall, the project area reflects a mix of agricultural dependency, financial vulnerability, limited infrastructure, and insufficient health and civic services.

5. Public Consultation and Information Disclosure

Engagement with stakeholders and disclosure is an integral part of the project's environmental and social assessment. The methods used for public consultation with project stakeholders in order to ascertain their stakes regarding project implementation were general/public meetings, rapid participatory appraisal, and on site meetings.

Different categories of interested parties including project staff, government officials, and local communities were consulted to predict the nature and scale of risks, challenges, and impacts of the project perceived by them. Concerns raised by the locals are as followed. In **Table ES1**.

Table ES1: Concerns raised by locals and their response

Sr. No	Concerns Raised	Locations	Response
1.	In Bagri, the water is not drinkable and there are several waterborne diseases including intestinal issues	Kot Momin,	Provision of clean water is already part of our project, so waterborne diseases shall be reduced and there will be an improvement in public health.
2.	Will employment opportunities be generated for locals during the construction phase?	All project villages	It will be made sure that 75% of the workforce will be employed from the sub-project area.
3.	Arrangements should be made to suppress dust, curtail high-noise activities, and control the vibrations caused due to machinery, to protect the community's health	Kot Momin	Regular sprinkling of water will be carried out over the loose soil to suppress the dust, the noisy activities will not be planned at night and the community will be informed before the execution of any activity that would generate vibrations
4.	Privacy of people should be upheld during construction phase of the sub-project.	All project villages	Contractor will provide trainings to workers regarding gender and privacy issues.
5.	Construction activities should be minimized during schools' opening and closing times.	All project villages	Contractor will be bound to minimize construction activities during schools' opening and closing times.
6.	Will there be any closure of roads during construction phase?	All project villages	In case of road closures, the nearby community will be informed beforehand and alternative routes will be provided.
7.	Solid waste production during construction time is a major concern and that should not be piled up in the project area.	All project villages	The construction and other waste generated at the site shall be collected, stored and transported to the final disposal site by the contractor on daily basis.
8.	Will there be any tree cutting?	All project villages	No, no trees will be cut during the execution of the project.
9.	The construction activities will cause inconvenience to local residents due to hindrance in routine activities	Alipur, Shujabad,	The contractor will ensure that construction work do not create disturbance for local people's access to the local route and their routine life activities.

Sr. No	Concerns Raised	Locations	Response
10.	Will this project cover all households in the village?	Alipur, Shujabad, Taunsa	Yes, all households located in the deh boundary in the selected villages will be covered.
11.	Who will bear the cost of operation and maintenance (O&M)?	Alipur, Shujabad	The community pay O&M in the form of water charges per month. Government or project may provide initial support.
12.	What about wastewater and drainage system?	Alipur, Shujabad	Proper drainage and wastewater disposal points will be included where technically and socially feasible.
13.	Will there be water meters or fixed charges?	Alipur, Shujabad	There will be fixed water charges. The Client may re-consider it whether meter or fixed charges.
14.	What if the water supply stops or gets damaged?	Alipur, Shujabad	The complaint can be registered in the office.
15.	Local people claim that the construction of the project will lead to noise pollutions and social disturbances during construction of the water supply.	Liaqatpur	Regular maintenance of construction machinery to prevent excessive noise. Provide early and continuous information disclosure.

6. Anticipated Environmental Impacts and Mitigation Measures

The construction activities would cause changes in topography, soil contamination, surface & groundwater pollution, air pollution, noise & vibration, solid waste generation, wastewater generation, hazardous waste, disturbance to flora and fauna, overburdening of resources, construction camps issues, health & safety issues, emergency situations, traffic disruption and social issues.

Anticipated impacts during operational stage will include water pollution, air pollution, soil contamination, ecological disturbance, solid waste generation, occupational health & safety issues and emergency situations.

The positive impacts of the project include, improved water supply system, improved sewerage system, improvement in public health, hygiene and sanitation, landscape, economic development, employment generation, development of deprived villages, formation of model villages, synergetic development with cooperation of NGOs, CBOs and other organizations.

7. Environmental and Social Management and Monitoring Plan

Recommended mitigation measures to control potential adverse impacts are described in this Environmental and Social and Management Plan (ESMP). ESMP shall become the part of construction contract agreement and shall be strictly enforced during the implementation of the proposed project.

The proponent PRMSC will be responsible for compliance of with environmental and social safeguard requirements of the proposed project.

The proposed project activities will be monitored and managed by the PRMSC. The Environmental and Social Cell (ESC) staffed by qualified environmental and social specialists has already been established under PRSWSSP. The ESC will be the custodian of the ESMP. ESC will support ensuring the compliance of ESMP. ESC will submit progress reports for the implementation of the ESMP to WB and PEPA as per environmental approval/ NOC conditions for the PRSWSSP.

8. Grievance Redress Mechanism (GRM)

The Grievance Redressal Mechanism (GRM) will be consistent with the requirements of the World Bank safeguard policies to ensure the mitigation of community concerns, risk management, and maximization of environmental and social benefits. The overall objective of the GRM is therefore to provide a robust system of procedures and processes that provides for transparent and rapid resolution of concerns and complaints identified at the village level.

The PRMSC at the Local Government & Community Development Department (LG&CDD) level will serve as the Secretariat for the Grievance Redressal Committee (GRC Directorate) that will be responsible for providing oversight on the entire GRM process at a strategic level and monitoring complaints management.

The complaints may be lodged through:

- Tracking complainant(s) from subprojects sites (field and community level) to PRMSC;
- Dedicated staff to update the database routinely;
- Promote transparency, publicize how complaints are being handled, and periodically evaluate the overall functioning of the mechanism;
- Processes for informing stakeholders about the status of a case; and
- Procedures to retrieve data for reporting purposes, including the periodic reports, from Village and Tehsil and document them into the monthly progress reports at PRMSC.

GRC Tier-I

GRC (Village level) will be responsible to receive, log, and resolve complaints at the village level. The Grievance Redress Committee at the village Panchayats/Villages Organization (VO) will review and identify actions to be taken to address the complaints at its weekly meeting. If not resolved timely then complaint would be referred to GRC-Tehsil Level (PRMSC-TO) within 3 days after receiving.

GRC Tier-II

GRC-PRMSC-TO will try to resolve the complaints in a satisfactory manner.

GRC Tier-III

If the complaint is not satisfactorily resolved by the village panchayats/councils and Tehsil level, then the grievance will be referred for consideration by GRC at the PRMSC/LG&CDD level within one week.

Every effort will be made to address or resolve grievances within the following fixed timelines, which will be an indicator of the performance of the handling system. Acknowledgment of a written submission will be issued to the complainant within three working days.

If the complainant is not satisfied, the complainant will have the option to seek redress through the relevant court of law.

9. Environmental Budget

The total estimated cost for the implementation of ESMP is worked out to be about **PKR 646.24 million rupees or 2.3 million US$[2].**

[2] 1 US$ = 280.00 PKR

1 INTRODUCTION

1.1 General

The Local Government & Community Development Department (LG&CDD), Government of Punjab, through its Punjab Rural Municipal Services Company (PRMSC), a company registered under section 42 of "The Companies Act 2017", is implementing Punjab Rural Sustainable Water Supply and Sanitation Project (PRSWSSP)" in 2000 villages in 16 tehsils of Punjab with the proposed assistance of the World Bank. To implement this project, Executive Committee of National Economic Council (ECNEC) has authorized Punjab Rural Municipal Services Company (PRMSC) to initially implement this project in 200 villages as pilot phase (Annex-1) to understand feasibility and sustainability of the Project.

Pilot Phase:

To implement this project, the Executive Committee of the National Economic Council (ECNEC) considered the summary dated 27th January, 2022 submitted by the Ministry of Planning, Development and Special Initiatives titled "Punjab Rural Sustainable Water Supply and Sanitation Project (PRSWSSP) and approved the proposal with the following directions:

i. A "Pilot Project" should be conducted, based on 10% of the approved project scope.
ii. After one year, lessons learned from the pilot phase should be shared with the Central Development Working Party (CDWP), with a specific focus on the operation and maintenance aspects of the project.
iii. The project timeline should be reduced to five years after gaining insights from the pilot phase.

To initiate the Project, an initial pilot phase was undertaken in 200 villages (Annex-1) to assess its feasibility and long-term sustainability. For this purpose, the 16 tehsils were organized into six geographical clusters, and the feasibility studies, engineering designs, PC-I documents, BOQs, and safeguard instruments for all 200 villages were completed across five implementation packages.

Summary of ESMP Prepared for 1800 villages

Table 1 : Summary of ESMP Prepared for 180 villages

Sr.no.	ESMP Phases	No. of villages of Pilot Phase	Date of Approval
1.	Phase 0	77	13th January, 2026
2.	Phase 1	232	23rd Februrary, 2026

Remaining Scope of 1800 villages:

Building on the lessons learned from the pilot phase of 200 villages, the CDWP granted approval on 12 December 2024 for PRMSC to proceed with the remaining scope of 1,800 villages. To initiate the preparation of feasibility studies, detailed engineering designs, PC-I documents, and safeguard instruments, PRMSC has reorganized the 16 tehsils into five geographical clusters and engaged five Engineering Design and Supervision Consultants

(EDSCs) under the assignment titled “Consultancy Services for Engineering Design and Construction Supervision of Punjab Rural Sustainable Water Supply & Sanitation Project (PRSWSSP).”

Under this arrangement, Phase-II has commenced, covering the batch of 425 villages. To expedite implementation, the EDSCs have been instructed to submit feasibility studies, detailed engineering designs, PC-I documents, and environmental and social safeguard instruments on a phased basis.

Table 1 indicates number of villages, covered in different selected tehsils:

Table 2 : Project Area with Number of Villages

Cluster	Name of Consultant	Tehsil	Phase-II
North	NESPAK	Kot Momin	10
Central	Asian Consulting Engineers	Ahmadpur Sial	16
		Bhawana	15
		Darya Khan	18
		Pakpattan	53
South-I	Alter	Liaqatpur	85
		Rojhan	21
South-II	Rehman Habib Consultants	Alipur	42
		Shujabad	44
South-III	Asian Consulting Engineers	Kahror Pacca	19
		Khairpur Tamewali	42
		Bahawalnagar	60
Total			**425**

The goal of PRSWSSP is to improve sanitation conditions, provide clean drinking water, improve living conditions through behavior change, and capacity building for the sustainability of the project in rural settlements of Punjab.

This Environmental and Social Management Plan (ESMP) has been prepared for the 425 villages in Phase-II of the proposed project in line with World Bank Operational Policies (OPs) and Environmental Social & Management Framework (ESMF) for PRSWSSP. The current study covers various impacts of the design, construction, and operation of water supply, sewerage.

1.2 Project Background

Punjab is the most populous province of Pakistan with 110 million inhabitants out of which 70 million reside in rural areas[3]. The people living in rural areas of Punjab lack access to improved water and sanitation facilities which contribute to child stunting, malnutrition and water borne diseases. Poor condition of Water, Sanitation and Hygiene (WASH) not only affects the health of masses, but it also adversely affects the economic growth of the region.

[3] https://pwd.punjab.gov.pk/population_profile

Poverty and Shared Prosperity Report, 2020[4] reveals that 4 out of 5 people live below the international poverty line in rural areas. Studies conducted in different periods of time have linked improved water and sanitation facilities with the alleviation of poverty.

Despite making significant efforts by successive governments to improve the prevailing situation, 44% population of Punjab still does not have access to improved water and sanitation facilities as per globally established standards. Rural settlements of Punjab, which hold 73% of the province's population living in 23,000 revenue villages, are in dire need of investments to improve WASH. Reports show that 3 in 5 households in Punjab use E-Coli contaminated water and every 25th household in Punjab lacks access to the improved sources of drinking water. Similarly, the situation of sanitation is also immensely deplorable.

Outcomes of various studies and sector assessments have identified requirements for improving climate resilience and planned economic growth of 2,000 villages that will be part of the project. Poverty, water contamination, stunting, and sanitation condition of the areas have been taken as basic parameters for the selection of project sites/tehsils.

The Government of Punjab, with the assistance of the World Bank, will finance complete detailed engineering designs through Engineering, Design & Supervision Consultancy Services (EDCS) under the pilot phase project in the revenue villages of six (06) Geographical based Clusters of selected districts. The services will assist in; (i) design documentation, including Sub-scheme/Project Document (PC-I), Bill of Quantities, for water supply and sanitation services to achieve economies of scale and desired results, and (ii) resident supervision of infrastructure development.

The PRMSC has adopted a Phase wise approach for designing of villages, to fast track the implementation of the project in each cluster. Names of the 425 villages included in Phase-II is listed in **Table 2.** It is to be noted that the current lot of 425 villages is located in 12 Tehsils (out of the original 16 tehsils covered under the geographical scope of the project).

Table 3: Location and Name of Phase-II Villages in Different Tehsils

Cluster	District	Tehsils	Phase-II Villages	
North	Sargodha	Kot Momin	Chak 08 /SB Kot raja	
			Baraham wala	
			Bahar wala	
			Dhudyan	
			Tridianwala	
			Bhakhi khurd	
			Bakh Daim	Settlement -1
				Settlement -2
			Murad wala	Settlement -1
				Settlement -2
				Settlement -3
				Settlement -4
			Dhingrala	
			Dhingrawali	

[4] https://www.worldbank.org/en/publication/poverty-and-shared-prosperity-2020

Cluster	District	Tehsils	Phase-II Villages
Central	Jhang	Ahmadpur Sial	Chak No.1/2-L
			Chak No.3/2-L
			Jhok Dargahi Shah
			Chak No.4/3-L
			Jhainder Niazi
			Basti Lal
			Chak 13/3-L
			Chak No.2/4-R
			Chak No.3/3-L
			Basti Wali Muhammad Jandir
			Bela Badh
			Bhid Wal
			Chak No.1/3-R
			Laghari
			Wahgah
			Detisial
	Chiniot	Bhawana	Chak 248 Jb
			Kamoke
			Kotla Shahzada
			Maral Wala
			Saghar Wala
			Thatta Kundal
			Thatta Rasalu
			Fateh Kot Taja
			Abhulke
			Malake Rajoke
			Shah Fateh Ali
			Nahre Hrseh
			Kot Sahib
			Mehroke
			Thatta Viroka
	Bhakkar	Darya Khan	Chak No.177/T.D.A
			Chak No.53-M.L
			Chak No.1 Rakh Dala
			Karar Noon
			Bilochan Wali
			Chak No.51/M.L
			Chak No.176/T.D.A
			Chak No.50-M.L
			Chak No.54-M.L
			Surani Nasheb
			Daggar Qureshi Janub Gharbi

Cluster	District	Tehsils	Phase-II Villages
			Chak No.5 Rakh Dallo Wala
			Dulle Wala No.1
			Chak No.2 Rakh Dala
			Chak No.3 Rakh Dala
			Chak No.4 Rakh Dala
			Gadai No.2
			Chak No.12-A/TDA
	Pakpattan	Pakpattan	Chak No.102/D
			Bahwan Shah
			Chak Ilahi Bux
			Chak Murad Khan
			Chak Nazam Din
			Gobind Pur Bahmni
			Jand Wala
			Nahla Abad
			Dhamiana
			Chak No.4 S.P.
			Chak Quder Tullah
			Chilli Mamdana
			Dada Ahluka
			Ghar Taj
			Ghazi Mardan
			Arazi Tek Chand
			Ghuri
			Rakh Ferozpur
			Wara Piran Kalan
			Kala Chishti
			Khamam Doggar
			Chak No.12 K.B.
			Musteqim Mamunka
			Malik Rahmun
			Amira Ahluka
			Alam Mehteka
			Chhinah
			Maneke
			Jalil Mehteka
			Khatwan
			Faiz Pur
			Talibali
			Jamal Pur Tahli
			Chak Wasao
			Chak No.105.D

Cluster	District	Tehsils	Phase-II Villages
			Chak No.104/D
			Chak No.100/D
			Chak No.88/D
			Bablana
			Bahdar Khara
			Bahmani
			Bonga Amam Din
			Bonga Shamis
			Chak No.91/D
			Chak Waso Kamboh
			Kirparam
			Lakh Wira
			Magan Pur
			Nabi Bakish
			Saleem Shah Bodla
			Chak No.106.D
			Wara Peran Khurd
			Chak No.101/D
South-I	Rahimyar Khan	Liaqatpur	Ahmed Ali Lar
			Allah Dita Bhela
			Allah Jiwaya Lar
			Ashraf Shah
			Bahan Wala
			Bahar Khaki
			Chak No. 116 NP
			Chak No. 116-A- NP
			Chak No. 117 NP
			Chak No. 118 NP
			Chak No. 119 NP
			Chak No. 119-A- NP
			Chak No. 120 NP
			Chak No. 121 NP
			Chak No. 122 NP
			Chak No. 123 NP
			Chak No. 124 NP
			Chak No. 125 NP
			Chak No. 126 NP
			Chak No. 127 NP
			Chak No. 128 NP
			Chak No. 129 NP
			Chak No. 130 NP

Cluster	District	Tehsils	Phase-II Villages
			Chak No. 131 NP
			Chak No. 132 NP
			Chak No. 133 NP
			Chak No. 137 NP
			Chak No. 138 NP
			Chak No. 34 Abbasia
			Chak No. 35 Abbasia
			Chanjni
			Chohan
			Choudari
			Chur Wala
			Duda Naich
			Gabrani
			Gharib Shah
			Ghemi
			Ghuka
			Goth Amin
			Goth Hayat
			Goth Mahi
			Gous Abad
			Gul Muhammad Lar
			Gulani
			Haroon Abad
			Hussain Abad
			Jhoung Bilawal
			Juma Muhana
			Kandani
			Kotla Daulat
			Kotla Mubarik
			Kotla Nawab
			Kotla Niazi
			Lakhani
			Lal Shah
			Laoon Wala
			Malhani
			Malikpur
			Malkani
			Metla
			Mir Muhammad Lar
			Muhammad Daha

Cluster	District	Tehsils	Phase-II Villages
			Mujawraan
			Nala Musani
			Pakhi War
			Pararan Sharif
			Qadu Wali
			Rais Pathan
			Rashid Abad
			Rindan
			Sadiqpur
			Saidpur
			Shahbazpur Gharbi
			Shamsabad
			Shidani Sharif
			Talbani
			Tanwari
			Trinda Mir Khan
			Ther Posti
			Tibbi Sayyadan
			Wahid Bux Sial
			Yakhtar Maha
			Zaffar Abad
			Unran
	Rajanpur	Rojhan	Badli
			Badli Chak Ladh
			Basti Nikka
			Chak Dim
			Chak Kariya
			Chak Mut-1
			Chak Mut-2
			Dera Dildar
			Dera Jewan Khas
			Garhi Soori
			Kaheeri
			Kin Khas
			Kotla Gulsher
			Kotla Hasan Jamra
			Rakh Kotla Hasan Jamra
			Lutairi
			Miranpur
			Patti Shah Wali

Cluster	District	Tehsils	Phase-II Villages
			Shah Wali
			Solangi
			Wah Machka
South-II	Multan	Shujabad	Agar Khani
			Amanullah Pur
			Bagrain
			Basti Chhaju Shah
			Bhana
			Chak Jakhar
			Chak No 13/F
			Chak Rs
			Choti
			Dairapur
			Dera Arvi
			Dhondo
			Gunwen
			Jai
			Jhangi
			Kaser Pur
			Khalar
			Khanpur
			Khas Punjani
			Kotli Najabat
			Lasoorhi
			Lutf Pur
			Mahara
			Mochi Pura
			Mohan Pur Gharbi
			Pounta
			Punjani
			Raja Raam
			Rasool Pur Janubi
			Rasool Pur Shumali
			Rukan Hatti
			Sat Burji
			Seri
			Shah Musa
			Sheikhpur Shajra
			Soman
			Tahir Pur

Cluster	District	Tehsils	Phase-II Villages
			Thath Galawan Junabi
			Thatha Makhdoom Pur
			Tudar Pur
			Vainus
			Wahi Bhakar
			Wahi Sawaya
			Taror Jalal Pur
	Muzaffargarh	Alipur	Amir Pur Daha
			Baqar Shah Janubi
			Basti Haji
			Baz Wala
			Bet Channa
			Bet Dewan Shah
			Bet Muiziddin
			Chak Dada
			Chak Daud Wala
			Dahaka
			Damar Wala Janubi 1
			Damar Wala Janubi 2
			Daulut Pur
			Fateh Pur Janubi 1
			Fateh Pur Janubi 2
			Ghalwan 1
			Ghalwan 2
			Ghari
			Kachi Lal
			Khair Pur Para
			Khair Pur Sadat
			Khan Pur Nahrka
			Khanani
			Khangarh Donma
			Kundai
			Kundrala
			Latti
			Madd Sohanyara Shah
			Malik Arain
			Misan Kot Behwa
			Mohib Shah
			Mud Wala
			Mutfarqa

Cluster	District	Tehsils	Phase-II Villages
			Nussrat Pur
			Pakka Naich
			Phullan
			Rakh Khanani
			Shah Wasava
			Sheikhani
			Sultan Pur
			Tibi Arian
			Walwat
South-III	Lodhran	Kahror Pacca	Basti Lal
			Chak Qadirpur
			Dera Dilawar
			Kotkora Jhanda
			Arah
			Chak Allah Rakha Khan
			Dhorah Mahar
			Gopal Pur
			Gul Pur
			Bhinda Gerdan
			Chak Muhammad Murad
			19/M
			21/M
			30/M
			Kand Ahmed Asar
			Murshad Pur
			22M
			Chak Choki Kohna
			Hassa Joya
	Bahawalpur	Khairpur Tamewali	Fazlu Kukara
			Khairi Bhabhi
			Kotla Mahi
			Ladar
			Mamdu Mangero
			Bunga Yarani
			Darud Garan
			Goth Ali
			Gith Kamal
			Kamalia
			Ahmed Milkhi
			Amin Fatani

Cluster	District	Tehsils	Phase-II Villages
			Baghban
			Binda Chadhran
			Kharal Nau Baramad
			Chak No. 26
			Dharala Randu
			Haleem
			Khanan Arain
			Chak No. 24 Sharaf Shah
			Khuda Bux Seyal
			Kotla Qaim Khan
			Lal Sohanra
			Luthran
			Mehti
			Mohammad Sharif
			Muhammad Khan
			Mungrani
			Muradpur
			Muradpur Dhrala
			Nurrey
			Qazi Kalra
			Raja
			Rameli
			Rukrani
			Sardar Pur
			Azimpura
			Noor Mohd Khan
			Gaman Wagi
			Gawains
			Goth Jhumar
			Khairpur
	Bahawalnagar	Bahawalnagar	Bonga Ihsan Bibi
			Hasan Raika
			Abrerah Uttar
			Amin Abad
			Boole Shah Hitthar
			Ramnagar
			Paran Wala
			Hussian Abad Hithar
			Hussian Abad Uttar
			Chak Abdul Haq
			Dhanraj Pura

Cluster	District	Tehsils	Phase-II Villages
			Ali Goher No. 326
			Jagga Sanatteka
			Mina Sanatteka
			Sharaf Din
			Mosla
			Pir Sikandar Otar
			Jhulan Chishtian
			Gauspur
			Gaman Dongi
			Akkanwali Khurd
			Kartar Singh
			Khawaja Bux Bodla
			Faqir Shah
			Khober
			Ramzan Shah
			Allahabad
			Muhammad Asad Khan
			Janoowala
			Tobi Qamar-Ud-Din
			Malak Pura
			Jalwala
			Dara Sanatteka
			Hira Bashnoai
			Sandar Bashnoi
			Sher Singh Wala
			Barasajwar Khan
			Noor Jahanian
			Dadoo Mammunka
			Bhole Shah Utar
			Abrerah Hitthar
			Bilara Nabi Bux
			Bilara Qasim Khan
			Madarsa
			Pir Shah
			Kakku Bodla
			Bhangran
			Khilowala
			Mamunka Hatar
			Muhsan Pura
			Beg Kanoor Pur
			Wara Piran
			Chaweka Hitthar

Cluster	District	Tehsils	Phase-II Villages
			Mamunka Uttar
			Dinpur Sharif
			Mari Mian Sahab Hithar
			Ramzan Langah
			Tughera Sharif
			Wilayat Pur
			Nanak Sar

The anticipated environmental and social impacts of the project in the selected 425 villages are mostly localized, site-specific and temporary; which could be easily mitigated through appropriate mitigation measures. According to the findings of the Environmental and Social Screening study, this project falls in Category E2 and requires an ESMP.

Environmental clearance from the Environmental Protection and Climate Change Department (EP&CCD), Punjab is mandatory according to the Punjab Environmental Protection Act, 2012. Section 12 (1) of the Act states that:

"No proponent of a project shall commence construction or operation unless he has filed with the Provincial Agency an initial environmental examination or, where the project is likely to cause an adverse environmental effect, an environmental impact assessment, and has obtained from the Provincial Agency approval in respect thereof."

As per Punjab Environmental Protection Agency (PEPA) Review of Initial Environmental Examination (IEE) and Environmental Impact Assessment (EIA) Regulations 2022, Schedule-II, EIA is required for 'Water Supply, Sewerage System and Treatment' (Category F).

A combined EIA is preparing Tehsil wise and will be submitted to EP&CCD for Environmental Clearance (NOC).

1.3 Objective of ESMP

The objective of this ESMP is the identification of possible environmental and social impacts of the proposed project on both short and long-term bases. Based on the level and nature of these observations, the ESMP delineates proper mitigation measures. As a planning tool, the ESMP aims to ensure that environmental, socio-economic, and cultural issues throughout the entire project lifecycle are anticipated and considered by the project proponent. It also serves as a framework for establishing project controls to reduce or prevent adverse environmental or socioeconomic impacts.

The specific objectives of this ESMP are:

- To assess the existing environmental and socioeconomic conditions of the project area;
- To identify potential impacts of the proposed interventions on the environmental, ecological, and social aspects of the project area, to predict and evaluate these impacts and determine their significance;
- To propose appropriate mitigation measures that should be incorporated in the design of the project to avoid or minimize (if cannot eliminate) the potentially adverse impacts;

- To assess the compliance status of the proposed activities with respect to the national and provincial environmental legislation and WB's OPs;
- To provide institutional, monitoring, reporting, and documentation measures for environmental safeguards compliance; and estimated costs for implementing these measures; and
- To help decision-makers in taking informed decisions.

1.4 Scope of ESMP

The ESMP identifies the potentially significant impacts of the proposed project and suggests the applicable mitigation measures to avoid, minimize or reduce the magnitude of the impacts. It will also indicate the institutional and training requirements to implement mitigation measures during the construction and operation of the proposed project.

The current ESMP presents a preliminary roadmap for the environment and social management for the construction and operation of the water supply scheme, sewerage network and sewage treatment plant (STP) in all 425 villages of Phase-II of Twelve (12) tehsils.

1.5 Contractual Requirements/ Obligations of ESMP

The impacts and their mitigation measures, summarized in ESMP, will be part of the Bidding Documents to ensure that Contractors implement ESMP recommendations at all project stages. The ESMP requirements will be part of the Contract and the details prescribed in the ESMP will be mandatory. The ESMP will be equally applicable to Subcontractors, including nominated Subcontractors (if any).

At the stage of the bidding process, the Contractor will be instructed to carefully consider the requirements for environmental and social management contained in this ESMP when preparing the bid and pricing the items of Work. The Contractor will need to accept that the prescriptions and clauses detailed in the ESMP are an integral part of the Contract for relevant items of Work; unless separate items are included in the Bill of Quantities (BoQs). The Contractor will need to accept that separate payment will not be made in respect to compliance with the ESMP. The Contractor should, therefore, be aware that in case the Contractor or Subcontractors fail to implement the ESMP recommendations, the Environment and Social team shall take necessary action(s) to ensure that the ESMP is properly implemented and/or to rectify the damages caused by such negligence.

1.6 Approach & Methodology to Work

1.6.1 Approach

The study has been conducted in accordance World Bank Safeguards policies (OP 4.01, OP 4.04, OP 4.11, OP 4.12, OP 4.20 & BP 17.50) applicable to this project. Further, Punjab Environmental Protection Agency (PEPA) guidelines were also considered in preparation of this document. The study is based on both primary and secondary data and information. The primary data includes data collected from field i.e., information about existing conditions; environmental sampling and analyses for air, water and noise; environmental sensitive receptors, ecological survey; social survey including demographic characteristics, income dependency & quality of life, occupation, and social amenities etc. The secondary data includes a review of relevant information from literature and previous reports. Discussions were held with stakeholders including government officials, community representatives and a

wide range of local communities. The main purpose of this approach was to obtain an impartial impression of the people's perceptions of the project and its environmental and social impacts.

The assessment remains subject to change with respect to the finalization of technical specifications and alignment of the proposed sewer, water supply lines & location of overhead tanks, pumping station, and STP.

1.6.2 Methodology

An Environmental and Social Checklist for ESMP data collection was designed on Kobo Toolbox. This checklist ensures that the data provided by the EDCS consultants is consistent in format and covers the required extent, with the objectives of digital data collection and analysis to gain real-time insights on local dynamics of villages that can support in anticipating environmental and social impacts and suggesting proper mitigation measures. The following methodology was adopted to develop the ESMP of the proposed Project:

A. Orientation

Meetings and discussions were held among the members of the ESMP Consulting Team. This activity is aimed at achieving a common ground of understanding various issues of the Study.

B. Data Collection Planning

Subsequent to the concept clarification and understanding obtained in the preceding step, a detailed data acquisition plan was developed for the internal use of the ESMP Consulting Team. The plan included; identification of specific data requirements and their sources; determination of time schedules and responsibilities for their collection and the indication of the logistics and other supporting needs for the execution of the data acquisition plan. Field surveys were then conducted based on the data collection plan.

C. Detailed Field Survey

Detailed site visits and technical visits for environmental monitoring and social assessment for the collection of data were conducted in November, 2025 to February, 2026. The data collected was transferred to Kobo-Tool box following WB-GEMS training in July- 2025, and an orientation session conducted for EDCS consultants. The data collected from the field include:

- Identification of environmentally sensitive receptors including air-sensitive receivers, noise-sensitive receivers, and water bodies expected to receive pollutant load;
- Sampling and analysis for air, noise wastewater, and groundwater;
- Ecological survey;
- Socioeconomic survey including public consultation;
- Stakeholders' consultations;

D. Sampling & Analysis of Physical Environmental Parameters

EPA Certified Laboratories (i.e., Pak Green, WELCOS, SEAL, Green Environmental Monitoring and ASIAN Laboratories) were hired for environmental monitoring. The Laboratories were mobilized from August 2025 to December 2025 for collection of water and wastewater samples as well as air and noise monitoring.

E. Review of Secondary Data

Previous environmental and social soundness assessment for 16 tehsils was collected in order to gain a complete understanding of existing environmental conditions of the area including:

- **Physical environment:** topography, geology, soils, surface and groundwater resources, and climate;
- **Biological environment:** flora and fauna (particularly rare or endangered species), critical habitats/zones, and vegetation communities within the project area;
- **Socio-economic environment:** settlements, socio-economic conditions, infrastructure, and land use.
- **Heritage aspects**: sites of cultural, archaeological, or historical significance.

F. Review of Environmental and Social Laws and Institutional Requirements

The project needs to comply with all the applicable national and provincial environmental and social policies, laws, guidelines, acts, and legislations and World Bank's Operational Policies (OPs) requirements. All these requirements and policies were reviewed.

G. Area of influence (AoI)

Considering the project interventions simultaneously in primary settlement as well as number of secondary settlements of revenue villages, the whole revenue village is considered as area of influence of the sub project.

H. Environmental and Social Baseline Survey of the Project

Environmental and social surveys were carried out within the AoI to establish the baseline of the project area from November, 2025 to February, 2026 and all the data collected from the field was transferred to form generated on Kobo-Tool. Prior to the start of field activities, comprehensive checklists, proformas, and maps were developed to gather the following information:

(i) Physical Environment

The following information was acquired for the establishment of the physical environment baseline:

- Topography;
- Water resources (including available surface and groundwater resources and natural streams, hydrology, water supply, water contamination etc.);
- Climate data (including temperature, precipitation, humidity, wind speed, direction etc.);
- Water, surface water, ambient air quality and noise level monitoring data;
- Existing water supply and sewerage systems;
- Seismology;
- Geology
- Environmental Sensitive Receptors.

(ii) Ecological Environment

- Flora (trees, herbs, shrubs, grasses, and overall vegetation including valuable or rare trees and their loss due to implementation of the Project, etc.);
- Fauna/ Wildlife (Mammals, reptiles, amphibians, and avifauna.);
- Reserved forests, Guzara forests, Community forests/ Private forests, and wildlife sensitive or notified areas in AoI;
- Migratory birds' corridors; and
- Endangered species (both flora and fauna).

(iii) Socio-Economic Environment

Analysis is carried out on the basis of secondary data within the AoI in order to develop the socio-economic baseline information of the general settled population. Data and analyses of pertinent socio-economic parameters were revalidated in the socio-economic baseline survey of the sample population settled within the AoI. These aspects include the following:

- Demographic characteristics;
- Nature of business/occupation;
- Livelihood/income;
- Living standard of the population;
- Community Institution available;
- Gender issues;
- Housing construction patterns;
- Mode of transport;
- Basic amenities of the project area;
- Health facilities/ Educational facilities.

I. Stakeholder Consultations

There are two categories of stakeholders in the project:

- Community stakeholder
- Institutional stakeholder

For the current study, community stakeholder consultations were carried out through following techniques:

- Formal/ informal meetings (through village numberdars, politically influentials community resource persons)
- Individual interviews
- Group Discussions

The institutional stakeholder consultation session was carried out by holding meetings at the offices of relevant government functionaries. The study teams met with the institutional stakeholders, affected persons and local communities in and around the project area. The objective of the consultation was to disseminate information on the project and its expected impact, long-term as well as short-term, among primary and secondary stakeholders and to

gather information on relevant issues so that the feedback received could be used to address these issues at an early stage. Stakeholder consultation is discussed in detail in chapter 5.

J. Impact Assessment and Mitigation Measures

A logical and systematic approach was adopted for impact identification and assessment. The process began during the screening and continued through scoping which identified the key issues and classified them into different categories. The tools were used for impact assessment, through environmental and social screening checklists for impact assessment of construction and operational phase.

Identification of potential environmental and social impacts in terms of their nature, magnitude, extent, location, timing, and duration was carried out. The impacts were correlated to the Project location, design stage, construction as well as operation stage. Based on the impacts prediction methods and as a result of public/stakeholder consultations, ESMP team screened the adverse environmental and social impacts for inclusion in the mitigation measures and environmental and social management plan.

ESMP team proposed practicable, economically feasible and socially acceptable mitigation measures for the significant adverse environmental and social impacts. Details of mitigation measures are provided in chapter 6.

1.7 Structure of ESMP

The structure of this ESMP is listed below:

Section 1: Introduction briefly presents the project background, objectives, methodology and need of the study.

Section 2: Legal and Administrative Framework Lists national as well as provincial laws, regulations and procedures and applicable World Bank Operational Policies (OPs).

Section 3: Project Description provides an overall description of the project including proposed networks, design considerations and concepts, manpower requirement, waste generation, machinery and material requirements.

Section 4: Baseline Profile gives a description of baseline physical, biological and socio-economic conditions of the project area.

Section 5: Public Consultation and Information Disclosure identify the main stakeholders and their concerns raised during scoping sessions and deal with the measures to mitigate the social impacts.

Section 6: Anticipated Environmental and Social Impacts and their Mitigations Measures identify, predict, and evaluate the impacts of the project activities during the construction and operation stages and deal with the measures proposed to mitigate potential environmental impacts of the proposed project.

Section 7: Environmental and Social Management & Monitoring Plan This section outlines the organizational framework, mitigation, and monitoring plans, and training requirements, defines roles and responsibilities and estimates budget requirements for satisfactory implementation.

2 LEGAL AND ADMINISTRATION FRAMEWORK

2.1 General

This section deals with the current environmental policy as well as legal and administrative framework required to develop Environmental & Social Management Plan (ESMP) for the proposed interventions in selected Phase-II villages of 12 tehsils. All relevant provisions of environmental policies laid down by the Government of Pakistan, Government of Punjab along with applicable World Bank Policies have been duly discussed and the project proponent will be required to adhere to these regulations throughout the course of the project. The institutional arrangement for compliance with these laws has been described in ESMP (Section 7).

2.2 Summary of Key National Strategies, Policies, Acts and Legislation

The summary of key national strategies, policies, acts and legislation from environmental perspective are briefly described in **Table 3** below:

Table 4: Key National Strategies / Policies, Legislation / Acts, Laws and Regulations and Their Relevance to the Project

Sr. No.	Policy/Strategy	Brief Coverage	Relevance to project
1	Fatal Accidents Act 1855	An act to provide compensation to family's loss occasioned by the death of a person caused by actionable wrong. It is enacted as follows: • Suit for compensation to the family of a person for loss occasioned to it by his death by actionable wrong • Not more than one suit to be brought • Plaintiff shall deliver particulars etc. • Interpretation clause	The provisions of this act would be applicable if any fatal accident occurs during the execution of construction works for the proposed Project.
2	Pakistan Penal Code 1860	It authorizes fines, imprisonment or both for voluntary corruption or fouling of public springs or reservoirs so as to make them less fit for ordinary use.	The provisions of the Penal Code are applicable to the project in terms of penalties for effecting human lives and public property. It also addresses the control of noise, air emissions, and effluent disposal.
3	Land Acquisition Act, 1894 (Including Later Amendments)	The primary law for acquisition of land for public purposes in Pakistan is the "Land Acquisition Act, 1894". The Land Acquisition Act, 1894, is a "law for the acquisition of land needed for public purposes and for companies and for determining the amount of compensation to be paid on account of such acquisition". The exercise of the power of acquisition has been limited to public purposes.	No land acquisition will be carried out through the provisions of this Act under the project. State owned land will be preferred and used for the construction of overhead tanks, pumping stations & STP. Private land will be obtained through VLD, if required.
4	Protection of Trees and Brushwood Act, 1949	This Act prohibits cutting or lopping of trees and brushwood without permission of the Forest Department.	This act will be applicable to the proposed project in term of Tree Cutting which lies in jurisdiction of Forest Department.
5	Pakistan Antiquities Act 1975	The protection of cultural resources in Pakistan is ensured by the Antiquities Act of 1975, which provides a comprehensive definition of Antiquities. The law prohibits new construction in the proximity of a protected antiquity and empowers the Government to prohibit	The provisions of this act would be applicable if any accidental archaeological discoveries occur during the excavation

Sr. No.	Policy/Strategy	Brief Coverage	Relevance to project
		excavation in any area which may contain articles of archaeological significance.	works for the construction of proposed Project.
6	National Conservation Strategy 1992	Pakistan National Conservation Strategy (NCS) is the principal policy document on environmental issues in the Country. The NCS outlines the Country's primary approach towards encouraging sustainable development, conserving natural resources and improving efficiency in the use and management of resources. The NCS has 68 specific programs in 14 core areas in which policy intervention is considered crucial for the preservation of Pakistan's natural and physical environment.	The core areas that are relevant in the context of the proposed project are pollution prevention during construction, conserving, biodiversity and supporting forestry and plantation.
7	Guidelines for Public Consultation, 1997	The Pakistan Environmental Protection Ordinance 1997 requires public participation during the review of an EIA (Section 12(3)). The "Policy and procedures for the filing, review and approval of environmental assessments" requires proponents to consult with the affected community and relevant NGO's during the preparation of an environmental report.	These guidelines are applicable for the preparation of the EIA / ESMP. During the preparation of the ESMP, public consultations were carried out for: • informing the stakeholders about what is proposed; • providing an opportunity for those otherwise unrepresented to present their views and values, therefore allowing more sensitive consideration of mitigation measures and tradeoffs
8	Guidelines for Review and Preparation of Environmental Reports, 1997	These guidelines describe the format and content of IEE/EIA reports to be submitted to Provincial EPA/EPD for obtaining NOC. The guidelines present: • The environmental assessment report format; • Assessing impacts; • Mitigation and impact management and preparing an environmental management plan; • Reporting; • Review and decision making; • Monitoring and auditing; and Project Management.	These guidelines are applicable for the preparation of the EIA.

Sr. No.	Policy/Strategy	Brief Coverage	Relevance to project
9	National Sanitation Policy, 2006	The National Sanitation Policy of Pakistan, 2006, stresses on the safe disposal of excreta away from the dwellings, creation of an open defecation-free environment and, promotion of health and hygienic practices in the country.	This policy is applicable to the project for the efficient management of solid waste or wastewater during construction or operation phase of the project. This project primarily focused on provision of improve sanitation services in target areas.
10	Protection Against Harassment of Women at the Workplace Act, 2010	The Protection Against Harassment of Women at the Workplace Act refers to sexual harassment at the workplace.	This Act will be applicable to the project if women are employed for the construction of the proposed Project or women living in near vicinity of the project area.
11	Canal and Drainage Act 1873 and Amendment Act, 2016	This Act prohibits corruption or fouling of water in canals (defined to include channels, tube wells, reservoirs and watercourses), or obstruction of drainage.	This act is applicable to the project for the efficient management of wastewater disposal during the construction or operation phase of the project.
12	Punjab Local Government (Amendment) Ordinance 2021	The Ordinance establishes a new tier of local government at the village level called Village Councils, which incorporated the main functions of village panchayats prescribed in the Panchayats and Neighborhoods Councils Act, 2019 (PVPNCA 2019) with regards to water, sanitation, and waste management.	This act is applicable to the proposed project, village councils is informed about the project and will remain in contact during the construction or operation phase of the project.

2.3 Key Provincial Strategies / Policies, Legislation / Acts, Laws and Regulations

The provincial policies, strategies, acts and laws relevant for the environmental safeguard of the project activities are given below in **Table 4.**

After the 18th amendment to the constitution of Pakistan, many subjects, including environmental protection and pollution prevention, have been devolved to the provincial jurisdiction. Therefore, the apex environmental statute governing the proposed project will be the Punjab Environmental Protection Act 1997. However, detailed rules, regulations and guidelines required for the implementation of the policies and enforcement of legislation are still in various stages of formulation and discussion. The following description presents a brief overview of the relevance of various existing provincial policies, legislation and guidelines.

Table 5:Key Provincial strategies / policies, legislation / Acts, Laws and Regulations and Their Relevance to the Project

Sr. No.	Strategies / Policies / Legislations / Acts / Laws & Regulations	Brief Coverage	Relevance to project
1	Punjab Land Revenue Act, 1967	WHEREAS it is expedient to consolidate and amend the law relating to the making and maintenance of records-of-rights, the assessment and collection of land-revenue, the appointment and functions of Revenue Officers and other matters connected with the Land Revenue Administration in the Province of the Punjab, or incidental thereto	All the land required for the project, be it public or private, will be transferred in the name of PRMSC under the provisions of this Act
2	Punjab Plantation and Maintenance of Trees Act, 1974	The Punjab Plantation and Maintenance of Trees Act, (1974) regulates tree plantations and enforces measures for their protection. The requirements of this act are applicable in terms of planting new trees and their maintenance by the owner of the proposed Project land who would have the physical possession.	This act would be implemented if any tree cutting activity involved during construction.
3	The Punjab Wildlife (Protection, reservation, Conservation & Management) Act, 1974	This act provides for the protection, preservation, conservation and management of wildlife in the Province of Punjab. This act defines the wildlife sanctuary, game reserves, protected areas, and national parks. It also defines the rules and responsibilities of the relevant authorities and the relevant personnel to protect ecological resources. It also describes the penalties and punishments on offenses against the sections given in the act.	This policy is to avoid any disturbance to ecological system near project area due to construction activities.
4	Punjab Land Acquisition Rules, 1983	This Law provides for the acquisition of land needed for public purposes and for Companies, and determines the amount of compensation to be made on account of such acquisition. It also establishes the due process for land acquisition.	State land will be preferred and used for the construction of overhead tanks, pumping stations & STP. However, Private land if required will be acquired through VLD in this project.
5	The Motor Vehicles Rules, 2000	Subject to the provisions of this Act, and the rules and regulations, no person shall operate a motor vehicle from which air pollutants or noise are being emitted in an amount, concentration or level which is in excess of the National Environmental Quality Standards, or where applicable the standards customary under clause (g) of sub-section (I) of section 6.	During Construction all these rules will be followed to avoid emission of air pollutant from vehicles.

Sr. No.	Strategies / Policies / Legislations / Acts / Laws & Regulations	Brief Coverage	Relevance to project
6	Guidelines and Checklists adopted by Government of Punjab after 18th Amendment	Post the adoption of the 18th Constitutional Amendment in 2011, the subject of environment was devolved and the provinces have been empowered for environmental protection and conservation. The Punjab Environmental Protection Act, 1997 (as Amended upto 2022) is comprehensive legislation and provides the legislative framework for protection, conservation, rehabilitation and improvement of the environment. The „environment" has been defined in the Act as: (a) air, water and land; (b) all layers of the atmosphere; (c) all organic and inorganic matter and living organisms; (d) the ecosystem and ecological relationships; (e) buildings, structures, roads, facilities and works; (f) all social and economic conditions affecting community life; and (g) the interrelationships between any of the factors specified in sub-clauses „a" to „f".	All projects to be implemented in Punjab must comply with PEQS during all the phases i.e., construction and operation. No Objection Certificate (NOC) shall be required from Punjab Environmental Protection Agency (PEPA) before commencement of construction.
7	Punjab Drinking Water Policy 2011	The overall objective of Punjab's Water Policy is to provide clear policy directions to the Government of Punjab on the sustainable management and development of water from all sources of water (surface water, groundwater and rainwater), for all sub-sectors of water use (domestic, stock water, agriculture, industry).	This policy is applicable and drinking water supply will be designed according to this policy guidelines.
8	Punjab Environmental Tribunal Rules, 2012	According to Section-31 of the Punjab Environmental Protection Act, 1997 (XXXIV of 1997), the Tribunal shall make every effort to dispose of a complaint or an appeal or other proceedings regarding environmental problems associated with the construction and development of any project within sixty days from the date of filing of the complaint, appeal or other proceedings but any decision of the Tribunal shall not be rendered invalid by reason of any delay in the disposal of complaint, appeal or other proceedings.	This is applicable to dispose of a complaint or an appeal or other proceedings regarding environmental problems associated with the construction and development of any project within sixty days from the date of filing of the complaint, appeal or other proceedings.
11	Punjab Antiquities Amendment Act, 2012	The Punjab Antiquities Amendment Act, 2012 is adopted from the Pakistan Antiquities Act of 1975 with a few minor changes.	The law will be applicable to the proposed project mainly due to its provision that „any construction activity within 61 meter or 200 ft. of protected antiquities, are prohibited". The

Sr. No.	Strategies / Policies / Legislations / Acts / Laws & Regulations	Brief Coverage	Relevance to project
			provisions of this act would also be applicable, if any accidental archaeological discoveries may occur during the excavation works for the construction of proposed Project.
12	Punjab Local Government Musalihat Anjuman (Constitution and Functions) Rules, 2016	The dispute may be brought to the Musalihat Anjuman. The Musaliheen shall make every reasonable effort in encouraging and assisting the parties in arriving at an amicable settlement but for this purpose shall not impose, coerce or try to dictate terms for any specific resolution of the dispute.	The provisions of this rule would be applicable, if any dispute occur during the execution of proposed Project. The GRM under the project will also be aligned accordingly.
13	Punjab Environmental Quality Standards (PEQS), 2016	In exercise of the powers conferred under clause (c) of sub-section (1) of section 4 of the Punjab Environmental Protection Act, 1997 (XXXIV of 1997), the Environmental Protection Council has approved the Punjab Environmental Quality Standards (PEQS), 2016. They endow information on the permissible limits for discharges of municipal and industrial effluent parameters and industrial gaseous emissions in order to regulate environmental pollution. Results of environmental monitoring (ambient air, water and noise) conceded out at different locations in study area are compared with PEQS values and are conversed in later chapter of the report.	These standards are applicable in compliance with all the Punjab Environmental Quality standards of different Environmental Parameters during Construction and operational phase.
14	The Punjab Flood Plain Regulation Act, 2016	This act regulates construction in the flood plains in the Punjab. According to this act, no construction can be carried out in flood plains without prior approval in writing from canal officer.	Construction work will be carried out in underground for installing of water supply lines and sewerage lines.
15	Punjab Restriction on Employment of Children Act, 2016	According to the sub-section 11(a) of this act, an occupier who employs or permits a child (person under the age of 15 years) to work in an establishment shall be liable to punishment with imprisonment for a term which may extend to six months, but which shall not be less than seven days, and a mandatory fine between 10,000 and 50,000 rupees.	This act will trigger if any contractor hires skilled and unskilled labor under the age of 15. This would be prohibited in the project

Sr. No.	Strategies / Policies / Legislations / Acts / Laws & Regulations	Brief Coverage	Relevance to project
16	The Punjab Bonded Labour System (Abolition) Act 1992 & The Punjab Bonded Labour System (Abolition) (Amendment) Act 2018	The Act abolishes bonded and forced labour system with a view to preventing the economic and physical exploitation of the labour class.	This act will trigger on the payment of advance/ *peshgi,* whether in cash or kind. It will prevent bonded/ forced labour of any kind.
17	The Punjab Minimum Wages Act 2019	The Act regulates minimum rates of wages for unskilled and different categories of skilled workers employed in an industry, industrial and commercial establishments.	This Act will be applicable to ensure payment of minimum wages to the employees, labour, and all the skilled, semi-skilled, and skilled staff of the contractors and consultants during their engagement with this project.
18	The Workmen's Compensation Act 1923	This Act ensures the payment by certain classes of employers to their workmen of compensation for injury by accident.	This act will be applicable to ensure that the employees/ labour receive due compensation for injury by accident during the course of performance of project activities.
19	Punjab Protection of Women against Violence Act, 2016	This act counters gender-based discrimination, violence against women, and economic and social empowerment of women. This act will entail if gender-based violence observed in the project area during construction phase.	This Act will be applicable to the project if women are employed for the construction of the proposed Project or women living in near vicinity of the project area.
20	Punjab Tehsil / Town municipal Administration (Works) rules, 2003 (amendments, 2016)	According to Chapter VIII-A Occupational Safety &Hazard Clause 50 A Workplace Safety and clause 50 B pertains to responsibilities of the Local Government Engineer related to health and safety.	All the mentioned clauses will be applicable on construction labor/workers/ and sewer men/sanitary workers during execution of subprojects.
21	Punjab Environmental Protection Act 1997 (Amended 2022)	Post the adoption of the 18th Constitutional Amendment in 2011, the subject of environment was devolved and the provinces have been empowered for environmental protection and conservation. The Punjab Environmental Protection Act, 1997 (as Amended up to 2022) is comprehensive legislation and provides the legislative	All projects to be implemented in Punjab must comply with PEQS during all the phases i.e., construction and operation. No Objection Certificate (NOC) shall be required from Punjab Environmental Protection

Sr. No.	Strategies / Policies / Legislations / Acts / Laws & Regulations	Brief Coverage	Relevance to project
		framework for protection, conservation, rehabilitation and improvement of the environment. The „environment" has been defined in the Act as: (a) air, water and land; (b) all layers of the atmosphere; (c) all organic and inorganic matter and living organisms; (d) the ecosystem and ecological relationships; (e) buildings, structures, roads, facilities and works; (f) all social and economic conditions affecting community life; and (g) the interrelationships between any of the factors specified in sub-clauses „a" to „f".	Agency (PEPA) before commencement of construction.
22	Punjab Policy on Controlling Smog, 2025 Smog Prevention and Control Rules 2023	The Punjab Environmental Protection Department issued this policy on controlling smog in 2025 It imposed a complete ban on open burning of rice stubble, solid waste and other hazardous materials. It focuses the reasons behind the formation of dense smog in the Punjab, especially in Lahore and its environs, on the onset of winters each year and provide a short and medium to long term plan, including measure for protection of school going children; minimizing road accidents and creating mass awareness on precautionary measures for citizens at large.	During construction and operational phases all PEQS will be followed in accordance with to compliance and to minimize pollution load to control smog.
23	Punjab Labor Policy, 2018	The Punjab Labor Policy, 2018 intends to guide and support the Government and the stakeholders in developing strategies, plans and programs for the protection and promotion of the rights and benefits of working community without jeopardizing the genuine concerns of the employers.	The labor policy will be relevant as it will deal with the protection of labor. Mitigation and enhancement measures have been proposed in this ESMP to ensure proper working conditions for project labor.
24	Punjab Growth Strategy 2018	The document endorses Punjab's health sector vision and strategy, which emphasizes improvement of water, sanitation and hygiene services to prevent communicable diseases.	This strategy will be adopted in design of proposed project.
25	Punjab Occupational Safety and Health Act, 2019	This law was enacted to ensure occupational safety and health of the persons at workplace. It aims at protection of workers against risks arising out of the occupational hazards and to promote safe and healthy working environment catering to the physiological and psychological needs of the employees at workplace.	This act will be applicable to the proposed project in term of the health and safety during the construction and operational phases of the project.

Sr. No.	Strategies / Policies / Legislations / Acts / Laws & Regulations	Brief Coverage	Relevance to project
26	Punjab Water Act 2019	An Act to comprehensively manage and regulate water resources in the Punjab in the interest of conservation and sustainability. It is expedient to provide for comprehensive management of all water resources in the Punjab and to regulate their use in the interest of conservation and sustainability and matters connected with and ancillary thereto.	This act will be applicable to the proposed project. The drinking water supply will be designed in light of PWA, 2019.

2.4 Applicable World Bank Policies

2.4.1 World Bank Operational Policies

The World Bank operational policies applicable to the project and its compliance mechanism, are summarized in the description below

Safeguard Policies	Triggered	Explanation
Environmental Assessment (OP 4.01)	Yes	Under this OP, the World Bank requires environmental assessment (EA) of projects proposed for Bank's financing to help ensure that they are environmentally sound and sustainable and thus to improve decision making through appropriate analysis of actions and of their likely environmental impacts
Natural Habitats (OP/BP 4.04)	No	This OP is not triggered.
Physical Cultural Resource OP/4.11	No	The sub-project does not lie near any cultural and heritage resource therefore OP 4.11 will not be triggered. The possible discovery of archaeological sites or random findings during the excavation and earthworks may occur. In such case, this OP will be triggered. Furthermore, Annexure 4 for Chance Find Procedures will also be implemented.
Involuntary Resettlement OP/4.12	Yes (Not relevant for Phase -0 villages)	OP 4.12 is not triggered as the sub-project does not require any land acquisition, therefore there will be no involuntary resettlement, livelihood impacts, or restrictions to access. Consequently, there is no need of a Resettlement Action Plan.
Forests (OP/BP 4.36)	No	The sub-project area does not fall under forest area and will not affect any forest. So, this OP is not triggered.
Access to information (BP 17.50)	Yes	The World Bank's Policy on Disclosure of Information is to be open about its activities and to welcome and seek out opportunities to explain its work to the widest possible audience. This policy is triggered for sub-projects categorized as A and B. The developer consults project affected groups and local NGOs: a) during scoping and before TORs are prepared; b) when the draft EA is available; and c) throughout project implementation as necessary. The developer provides relevant information in a timely manner prior to consultation and in a form and language accessible to the groups being consulted.
Projects on International Waterways (OP 7.50)	Yes	This policy will be triggered. The Project has got the PAD cleared from Legal department. An exemption for notification has been approved by the SAR VP.

2.5 Managing the Risks of Adverse Impacts on Communities from Temporary Project Induced Labor Influx

World Bank Management has developed a Guidance Note titled "MANAGING THE RISKS OF ADVERSE IMPACTS ON COMMUNITIES FROM TEMPORARY PROJECT INDUCED LABOR INFLUX" to assist Bank staff in establishing an approach to identifying risks to and impacts on local communities associated with the temporary influx of labor that typically results from construction works, and to advising Borrowers accordingly on how to best manage such risks. This guidance note provides guidance on identifying, assessing and managing the risks of adverse social and environmental impacts that are associated with the temporary influx of labor resulting from Bank supported projects. The guidance note contains guiding principles

and recommendations to be considered as part of the design and implementation of projects with civil works that require labor from outside the project's area of influence. This Note does not introduce new requirements, but rather seeks to provide concrete guidance on how to approach temporary labor influx within the environmental and social assessment process.

2.6 Environmental, Health & Safety Guidelines

In addition to operational policies (OP), the WBG has also established its EHS guidelines for all the interventions that are financed by the group. These EHS Guidelines are technical reference documents with general and sector-specific examples of Good International Industry Practice (GIIP). Following EHS guidelines are relevant to the proposed project during the construction and operation phase:

EHS Guidelines for Water & Sanitation (2007): Issues associated water and sanitation are presented in the EHS Guidelines for Water and Sanitation (2007).

EHS General Guidelines: Generic issues related to Environment, Health and Safety and good practices are discussed in EHS General Guideline

EHS Guidelines for Construction Materials Extraction: Issues associated with sourcing of construction materials are presented in the EHS Guidelines for Construction Materials Extraction.

2.7 International Labour Organization (ILO) Fundamental Conventions – Ratified by Pakistan

The following fundamental conventions of ILO shall be applicable to the project:

- Forced Labour Convention, 1930 (Convention No. 29)
- Freedom of Association and Protection of the Right to Organize Convention, 1948 (Convention No. 87)
- Right to Organize and Collective Bargaining Convention, 1949 (Convention No. 98)
- Equal Remuneration Convention, 1951 (Convention No. 100)
- Abolition of Forced Labour Convention, 1957 (Convention No. 105)
- Discrimination (Employment and Occupation) Convention, 1958 (Convention No. 111)
- Minimum Age Convention, 1973 (Convention No. 138) Minimum age specified: 14 years
- Worst Forms of Child Labour Convention, 1999 (Convention No. 182)

2.8 International Protocol/Conventions

As Pakistan is a member of a number of international organizations such as United Nations Organization (UNO), Organization of the Islamic Conference (OIC), South Asian Association for Regional Cooperation (SAARC), Economic Cooperation Organization (ECO) etc., so it has to follow the international protocols and obligations related to the environment. The major protocols, ratification dates by Pakistan and obligations related to the proposed project are provided in the following table.

Table 6:International Agreements/Conventions Relevant to the Project

Sr. No	Agreement/ Convention	Ratification	Description/Relevance
1.	UNESCO Convention on the Protection of the World's Cultural and Natural Heritage, 1972 Web Link: http://whc.unesco.org/en/%20convention%20text/	Pakistan ratified this convention on 23 July 1976.	This Convention requires parties to adopt a general policy on the protection of the natural and cultural heritage, to set up services for such protection, to develop scientific and technical studies, to take appropriate legal, technical, scientific and administrative measures and to foster training and education for such protection. The proposed project design and ESS team paid due attention to archaeological sites and local norms. Both of these factors will also be considered during project implementation.
2.	Convention on Conservation of Migratory Species of Wild Animals, 1979 https://www.cms.int/	Pakistan signed this convention in 1981 and ratified it in December 1987.	Convention on the Conservation of Migratory Species deals with the conservation and protection of the migratory species. Species covered in the Convention should be given special attention during EA and monitoring and any impacts identified should be mitigated to acceptable levels.
3.	The Rio Declaration, 1992 Web Link: http://www.unesco.org/education/pdf/RIO_E.PDF	Pakistan signed the treaty on 13Jun 1992 and ratified on 1 June 1994	The Rio Declaration comprises 27 principles which address important issues such as; sustainable development to integrate environmental protection into the development process; common but differentiated responsibilities to conserve, protect and restore the earth's ecosystems; public participation and information access at the national level, reduce and eliminate unsustainable patterns of production and consumption.
4.	Convention on Biological Diversity, 1994 Web Link: https://www.cbd.int/	Pakistan signed this treaty in 1992 and it was ratified by cabinet in 1994.	The Convention on the Biological Diversity (CBD) has three main goals: Conservation of biological diversity (or biodiversity); sustainable use of its components; and fair and equitable sharing of benefits arising from genetic resources.

2.9 Institution Responsible for Planning, Policies and Regulations

2.9.1 Environmental Protection Agency, Punjab

Implementation of Punjab Environmental Protection Act 1997 (Amended 2012, 2017 & 2022) is the mandate of the Punjab-EPA. Punjab-EPA is headed by a Director General, and sections are headed by Directors, i.e., Director EIA, Technical, Director Administration and Finance, and Director Laboratory. Punjab-EPA has established District Environment Offices at district level.

As the proposed Project falls in 16 different Tehsil of Punjab, therefore, Punjab-EPA will be responsible for reviewing the reports, issuing environmental approval and overall monitoring of the proposed project activities.

3 PROJECT DESCRIPTION

The Punjab Rural Sustainable Water Supply and Sanitation Project (PRSWSSP) is being implemented across 2,000 villages in 16 tehsils of Punjab with support from the World Bank. ECNEC authorized PRMSC to initially execute the Project in 200 villages as a pilot phase (Annex-1) to assess its feasibility and long-term sustainability. With the pilot phase successfully completed, the Project is now progressing toward the remaining 1,800 villages. This ESMP specifically covers 425 villages located in 12 tehsils under Phase-II.

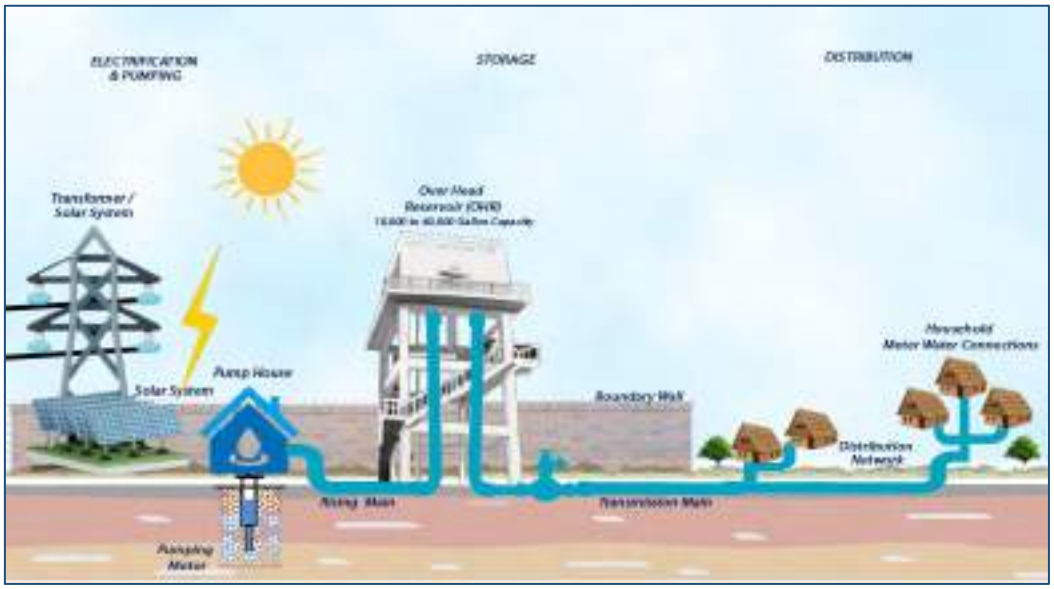

Figure 1:Illustrating project intervention in component 1 sub component 1.2

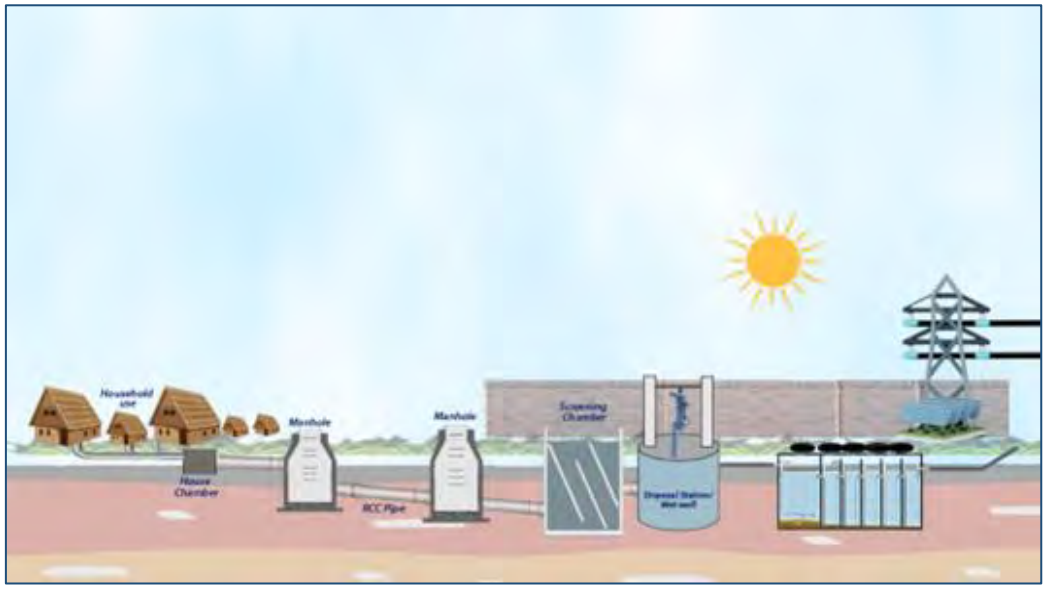

Figure 2: Illustrating project inventions in component 1 sub component 1.1

Project components are briefly described below:

COMPONENT 1: Water Supply and Sanitation Infrastructure Development

Component 1 will fill the infrastructure gap in the existing traditional rural Water Supply and Sanitation (WSS) systems that underlies the low access to safely managed water and sanitation in rural Punjab.

- **Subcomponent 1.1: Sanitation Infrastructure Development.**

  This subcomponent will focus on fecal sludge collection, transference, treatment and disposal.

- **Sub-component 1.2: Water Supply Infrastructure Development**

  The study on technology options and their feasibility informed the choice of technology for water abstraction, treatment, and conveyance.

COMPONENT 2: Behavior Change and Capacity Development

This component will finance activities that facilitate and induce health protective behavior change and build community capacity to support WSS service delivery.

- **Subcomponent 2.1 Awareness raising and behavior change related to safe WASH practices**

  The project will support basic hygiene, small-scale infrastructure to directly promote good hygiene practice and

- **Subcomponent 2.2: Training and Capacity Building of Village-level Institutions**

  Trainings will target village-level institutions that have a defined role in water and sanitation service provision. These will be complemented by household behavior change but are distinct, in that they will build the capacity of informal village level organizations to perform tasks that both complement and the O&M responsibilities assigned to Service Delivery Units (SDU).

COMPONENT 3: Service delivery Improvement

- **Subcomponent 3.1: Establishing institutions and building capacity for service delivery**

  The service delivery model of the project consists of three tiers: (i) a provincial SDU head office that has functions of both, the Project Implementation and Management Unit (PIMU) as the implementing body of the project and a public-owned section 42 company. (ii) Tehsil level units that are on frontlines of service delivery; and (iii) Community Caretakers and Operators (CCO) that may be part of Village Councils, Village Organizations, or just village residents.

- **Subcomponent 3.2: Solid Waste and Animal Waste Management**

  Promoting the safe handling of solid waste is an integral aspect of the design of this project

- **Subcomponent 3.3: Water Quality Monitoring**

The project will support a transition in Punjab towards regular and frequent water quality monitoring in rural areas for both drinking water supply and wastewater.

COMPONENT 4: Project Management and Monitoring

- **Subcomponent 4.1: Project Monitoring through a customized Management Information System**

  The project will develop and use a comprehensive IT based Management Information System (MIS) to track project implementation progress, WSS service delivery performance, the flow of public and donor funds earmarked for WASH and related financial management information, and outcome indicators.

- **Subcomponent 4.2: Strengthening of Project Implementation and Management Unit (PIMU)**

  The key implementation tier will be the Project implementation and management unit (PIMU), which will be associated with the Department of Local Government and Community Development (LG&CD) – the implementing agency - and led by a full-time Project Director.

PRMSC has divided the 16 tehsils into 5 zones based on geographical location and accordingly hired the services of 5 Engineering Design and Supervisory Consultants (EDCS) for the proposed project. Under Phase-II, interventions are planned across 12 tehsils, within which 425 villages have been identified for implementation. In order to fast track the project implementation and execution of the civil works, PRMSC with the help of consultants has divided 1800 pilot villages from sixteen different tehsils into 5 packages for designing and provision of Water Sanitation and Hygiene (WASH) facilities. This document pertains to 425 villages selected in phase-II from 12 different tehsils. The subproject involves provision of water supply, sewerage, overhead tanks and Pumping stations with sewage treatment plants in all 425 villages.

3.1 Need and Purpose of Project

The underlying issues related to water supply and sewerage in the target villages are summarized below:

Water Supply Issues:

- No water supply Network in the villages;
- Most of the household use shallow groundwater;
- Shallow ground water is not fit for drinking;
- Polluted drinking water is causing water borne diseases.

Sewerage Issues:

- Properly designed sewerage system does not exist in most of the villages;
- Existing open drains are damaged and do not cover the entire settlements;
- No proper disposal Point in all the villages;
- Sewage collected in soakage pits and open plots seeps into ground and contaminates groundwater;

- Raw sewage ponds are a breeding ground for disease vectors.

Solid waste Issues:

- There is no proper solid waste management system and designated dumping sites in the project area, locals usually throw their waste into open plots or streets.
- There are heaps of waste which attract rodents, flies and disease vectors.
- Organic waste is usually burnt by the villagers, which causes health issues.
- Open drains are used as a garbage/solid waste disposal point thus resulting in decrease of water carrying capacity of these drains.
- During rain, storm water and sewage overflow from the drains and spread solid waste through the area thus causing nuisance, environmental issues and spread of diseases.

3.2 Project Location

Table 2 in section 01, indicates the Cluster, District and tehsils of Phase-II villages to understand the geographical location of the project. A map of project locations in relevant tehsils is shown in figure 1.

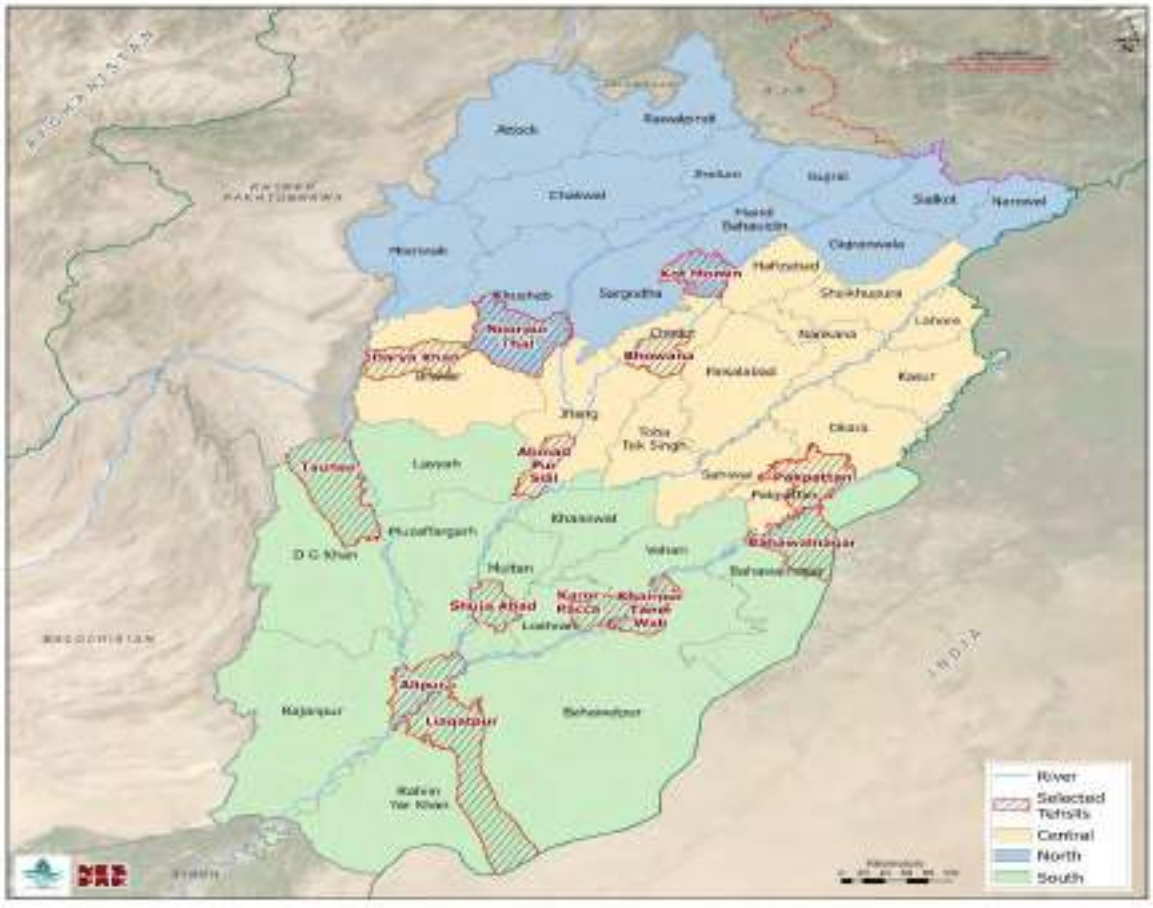

Figure 3: Location Map of Project Area

3.3 Objectives of Project

The project development objective is to provide equitable and sustainable access to safely managed water and sanitation and reduce child stunting.

3.4 Project Description

3.4.1 Existing System

The existing water and sewerage situation of the village is given below.

A. Existing Water Supply System

There is no existing functional water supply system in any of the Phase-II villages hence no water supply network exists here. At present, domestic boreholes are the main water source for the village which is available at a depth of around 50-75 ft. Deeper tube wells at depth of around 150 ft are also bored which are used for irrigation purposes. People bring drinking water from deep boreholes (outside of the village or even from nearby villages) if their village have brackish groundwater (i.e., Shujabad, Bahawalnagar, Kot Momin). Where the sweet water is available people collect water from deep borehole within their villages. Many villagers perceive that this water is unhygienic which results in major waterborne diseases like hepatitis, cholera and diarrhea.

B. Existing Sewerage System

There is no existing sewerage pipe network or disposal station in the villages. The sewerage system is totally based on open drains of varying sizes and capacities. The sewage is first collected in house collection chamber (soakage pits), which is then carried through existing open channels, drains and ultimately dispose of into nearest sewage pond and fields. Some of this sewage is also used to irrigate nearby crops/farmlands through water courses.

A sewage pond exists in each village which is used as a main sewage recipient. Most of the drain's direct sewerage into this pond and rest of the drains after collecting sewage from the adjacent areas disposed of into nearest fields haphazardly.

C. Existing Solid Waste

Solid waste management system and designated dumping sites are not available in the project area. The waste is usually dumped in the streets, agricultural fields or open plots. The heaps of waste cause nuisance and the situation gets worse during rainy season. The organic waste is burnt to meet the fuel demands in the kitchens. Glimpses of existing conditions are shown in **Annex-2.**

3.4.2 Proposed System

Summary of Proposed Water Supply and Sewerage Components are presented tehsil-wise in the table 6.

Table 7: Summary of Proposed Water Supply and Sewerage Components

Tehsil Kot Momin		
Total Length of Forcemain (PN-6)	=	3500 ft
Proposed Drainage Network (10" x 12")	=	3,803 ft

Proposed Drainage Network (12” x s12”)	=	2,354 ft
Proposed Drainage Network (15” x 12”)	=	2,543 ft
Proposed Sewer Network (Ø12”)	=	8,770 ft
Tehsil Ahamdpur Sial		
Stand Post-Type I	No.	1
Stand Post-Type II	No.	16
Drain Rft	Rft	30,481
Sludge Carrier Rft	Rft	12,668
Pipe Netwrok Rft	Rft	9,720
ST+SW Type-I	No.	3
ST+SW Type-II	No.	3
ST+SW Type-III	No.	1
ST+PUMP TYPE-II	No.	1
ST+PUMP TYPE-IV	No.	1
Eject.Pump	No.	13
Tubewell-0.05 cusec	No.	1
Tubewell-0.1 cusec	No.	2
Tehsil Bhawana		
Stand Post-Type I	No.	3
Stand Post-Type II	No.	15
Drain Rft	Rft	40,068
Sludge Carrier Rft	Rft	10,920
Pipe Netwrok Rft	Rft	8,793
ST+SW Type-I	No.	2
ST+SW Type-I(A)	No.	1
ST+SW Type-II	No.	4
ST+SW Type-III	No.	3
ST+SW Type-IV	No.	2
ST+PUMP TYPE-II	No.	1
Tehsil Darya Khan		
Stand Post-Type II	No.	17
Drain Rft	Rft	71,969
Sludge Carrier Rft	Rft	14,294
ST+SW Type-I	No.	1
ST+SW Type-I(A)	No.	6
ST+SW Type-II	No.	2
ST+SW Type-IV	No.	2
ST+SW Type-V	No.	1
ST+PUMP TYPE-III	No.	1
Eject.Pump	No.	13
Tubewell-0.05 cusec	No.	1
Tubewell-0.1 cusec	No.	2
Tehsil Pakpattan		
Stand Post-Type I	No.	9

Stand Post-Type II	No.	52
Drain Rft	Rft	142,649
Sludge Carrier Rft	Rft	54,214
Pipe Netwrok Rft	Rft	51,921
ST+SW Type-I	No.	6
ST+SW Type-II	No.	10
ST+SW Type-III	No.	7
ST+SW Type-IV	No.	2
ST+SW Type-V	No.	2
ST+SW Type-VI	No.	1
ST+PUMP TYPE-I	No.	4
ST+PUMP TYPE-II	No.	5
ST+PUMP TYPE-III	No.	4
ST+PUMP TYPE-IV	No.	4
ST+PUMP TYPE-V	No.	1
ST+PUMP TYPE-VI	No.	2
RO Plant	No.	8
Eject.Pump	No.	23
Tubewell-0.05 cusec	No.	11
Tubewell-0.1 cusec	No.	10
Tubewell-0.2 cusec	No.	2
Tehsil Liaqatpur		
Proposed No. of Tubewells (0.10 Cusecs)	No.	4
Proposed No. of Tubewells (0.15 Cusecs)	No.	3
Proposed No. of Tubewells (0.25 Cusecs)	No.	4
Proposed No. of Tubewells (0.50 Cusecs)	No.	1
Proposed No. of Ejector Pumps (0.01 Cusecs)	No.	99
Proposed No. of Ejector Pumps (0.02 Cusecs)	No.	82
Proposed No. of Ejector Pumps (0.03 Cusecs)	No.	36
Proposed No. of Ejector Pumps (0.04 Cusecs)	No.	15
Proposed No. of Ejector Pumps (0.05 Cusecs)	No.	9
Proposed No. of Ejector Pumps (0.06 Cusecs)	No.	9
Proposed No. of Ejector Pumps (0.07 Cusecs)	No.	6
Proposed No. of Ejector Pumps (0.08 Cusecs)	No.	3
Proposed No. of Ejector Pumps (0.09 Cusecs)	No.	1
Proposed No. of Ejector Pumps (0.10 Cusecs)	No.	3
Proposed No. of Ejector Pumps (0.11 Cusecs)	No.	1
Length of Distribution Network (Ø 6”)	ft	22,950
Length of Distribution Network (Ø 4”)	ft	72,516
Length of Distribution Network (Ø 3.5”)	ft	180,170
Standpost (1000 Gallons)	No.	266
Standpost (2000 Gallons)	No.	14
Drain Type I	ft	1,325,132
Drain Type II	ft	59,446

Length of Drains	Km	422.0
Septic Tank	No.	835
Teshil Rojhan		
Proposed No. of Tubewells (0.10 Cusecs)	No.	2
Proposed No. of Tubewells (0.30 Cusecs)	No.	2
Proposed No. of Tubewells (0.50 Cusecs)	No.	1
Proposed No. of Tubewells (0.80 Cusecs)	No.	2
Length of Distribution Network (Ø 10")	ft	4,129
Length of Distribution Network (Ø 8")	ft	16,650
Length of Distribution Network (Ø 6")	ft	104,556
Length of Distribution Network (Ø 5")	ft	548
Length of Distribution Network (Ø 4")	ft	111,214
Length of Distribution Network (Ø 3.5")	ft	382,468
Proposed No. of OHRs	No.	2
Proposed No. of GSTs	No.	0
Standpost (1000 Gallons)	No.	61
Drain Type I	ft	188,958
Drain Type II	ft	15,413
Septic Tank	No	86
Length of Drains	Km	42.45
Tehsil Alipur		
Stand Posts (Nos.)	=	60
Septic Tanks (Nos.)	=	217
Tehsil Shujabad		
Stand Posts (Nos.)	=	41
Septic Tanks (Nos.)	=	156
Tehsil Kahror Pacca		
Stand Post-Type I	No.	2
Stand Post-Type II	No.	24
Drain Rft	Rft	62,412
Sludge Carrier Rft	Rft	20,002
Pipe Netwrok Rft	Rft	6,015
ST+SW Type-I	No.	1
ST+SW Type-I(A)	No.	10
ST+SW Type-II	No.	3
ST+SW Type-III	No.	2
ST+SW Type-IV	No.	1
ST+SW Type-V	No.	1
ST+PUMP TYPE-II	No.	3
ST+PUMP TYPE-III	No.	1
RO Plant	No.	7
Eject.Pump	No.	2
Tubewell-0.05 cusec	No.	11
Tubewell-0.1 cusec	No.	4

Tehsil Khairpur Tamewali		
Stand Post-Type I	No.	8
Stand Post-Type II	No.	36
Drain Rft	Rft	91,704
Sludge Carrier Rft	Rft	37,186
Pipe Netwrok Rft	Rft	28,365
ST+SW Type-I	No.	2
ST+SW Type-I(A)	No.	7
ST+SW Type-II	No.	3
ST+SW Type-III	No.	1
ST+SW Type-IV	No.	1
ST+SW Type-V	No.	1
ST+SW Type-VI	No.	1
ST+PUMP TYPE-I	No.	4
ST+PUMP TYPE-II	No.	4
ST+PUMP TYPE-III	No.	2
ST+PUMP TYPE-IV	No.	3
Eject.Pump	No.	22
Water Storage Tank (1000L)	No.	1
Tubewell-0.05 cusec	No.	19
Tehsil Bahawalnagar		
Stand Post-Type I	No.	24
Stand Post-Type II	No.	42
Drain Rft	Rft	161,839
Sludge Carrier Rft	Rft	74,709
Pipe Netwrok Rft	100 Cft	82,493
ST+PUMP TYPE-I	No.	16
ST+PUMP TYPE-II	No.	10
ST+PUMP TYPE-III	No.	11
ST+PUMP TYPE-IV	No.	6
ST+PUMP TYPE-V	No.	4
ST+PUMP TYPE-VI	No.	2
RO Plant	No.	14
Eject.Pump	No.	29
Water Storage Tank (2000L)	No.	2
Water Storage Tank (1000L)	No.	2
Tubewell-0.05 cusec	No.	5
Tubewell-0.1 cusec	No.	4
Tubewell-0.2 cusec	No.	13

A. Water Supply System

The project aims to improve the existing drinking water problems through provision of properly treated water as per World Health Organization (WHO) guidelines through metered pipe supply network. The project will help to reduce the water consumption as company plans to charge tariff on the basis of volumetric consumption. This project will also help to discourage

the installation of wells in individual households. A comprehensive behaviour change communication is one of the components of the project in which residents of the villages will be sensitized on the importance of water conservation. Moreover, it is expected the provision of safe drinking water at door step will help to improve the socio-economic conditions of the society by curbing the medical expenses and saving of time required to fetch water. Moreover, the man-hours lost due to illness caused by the water borne diseases can be reduced. PRMSC has hired services of Independent third party (Pakistan Council of Research for Water Resources) to ensure the water quality through frequent testing of the treated water at end of treatment train as well as point of use.

Water supply system can be characterized by following main components:

- Water Source
- Distribution System

Water Source

Number of tube wells for water supply system are proposed after assessment of total water demand of the project areas and where sustainable ground resources are available. The design criteria for tube wells are discussed in the following sections;

Design Criteria for Tube wells

An appropriate well design is a blend of hydraulic and economic efficiencies of the tube well over its life span. It includes the selection of the depth, diameter, construction materials (well casings, screens, filter pack etc.), pump and prime mover in consonance with the local hydro-geological conditions and the design capacity. All these major factors depend upon the "design capacity" which in turn is governed by the aquifer's geometry and parameters.

Capacity of the tube well is based upon the maximum day water requirements, for the served area, with design operational duration (working hours) of 12 hours per day.

In order to design the well, the following major factors are considered:

- Design, construction details, water quality of the existing tube wells;
- Depth to water table under existing and future conditions;
- Groundwater quality;
- Aquifer parameters.

Pumping Facilities

Pumps are devices used to transfer water (or other liquids) from point A to point B with pressure to overcome the resistance along its path. It is important to understand the different types of pumps, their applications, design differences and the procedures used to operate and maintain them.

Water Transmission System

The transmission system's function is to transport water from source to the reservoir, if any, and to the distribution point. Water conduits for the transmission system may be canals, aqueducts or tunnels, free-flow pipelines, or pressure pipelines. The transmission of water is either under gravity or pumping. Pressure pipeline is generally the type of water conduit used for water supply transmission systems.

Water Reservoirs

In distribution systems, whether water is obtained by gravity or by pumping, distribution reservoirs are usually necessary for the following reasons:

- To balance the supply and demand in the system. In small distribution systems, variations in demand may be three or more times the average hourly consumption.
- To maintain adequate and fairly uniform pressure throughout the distribution system.
- To avoid the total interruption of water service when repairing pipes between the source of supply and the reservoir.
- To allow pumps to be operated uniformly throughout the day. Such pumps may be much smaller than would otherwise be required.

Overhead Water Reservoir (OHR)

Overhead Reservoirs (OHRs) are also key component of water distribution system. In water supply system OHRs serve the following functions:

- Store water for use during electric load-shedding and during maintenance works of tube-wells/ pumps.
- Provide balancing of flow and pressure during peak hours.

As per “Technical and Service Delivery Standards for Water Supply and Sanitation Sectors” Storage Capacity of Overhead reservoirs should be based on around 1/6th of average day demand.

Water Distribution System

The purpose of a distribution network is to distribute the potable water from the storage reservoir over the area to be provided, and deliver it to the individual consumer in such a way that at any tap point and at any time sufficient water of good quality can be withdrawn.

Looped System

A distribution network is looped when there are only few or no pipe dead-ends, such that water can move through the system freely. The advantages of a looped system are;

- The lower water velocities in the main reduce head losses, resulting in greater capacity.
- Ma in breaks can be isolated, minimizing serv ice interruptions to consumers.
- Usually, better chlorine residual content is achieved.

Stand Post

The function of the standpost system is to deliver potable water from the distribution network to the public through fixed tapping points. Standposts serve as communal outlets where consumers can conveniently collect water for domestic use. They are typically located at accessible points within residential clusters to minimize walking distance. Each standpost is designed to provide an adequate and controlled flow rate to meet community demand. The system ensures equitable water distribution, promotes hygiene, and supports communities without individual household connections.

B. Sewerage System

The sewerage system of these villages has been designed so that the final disposal of collected sewage should be in the proposed pumping station. This pumping station will pump sewage into Anaerobic Baffled Reactor (ABR). After treatment, treated effluent complying with PEQS, would be discharged into existing nearby sewerage pond or community owned water courses. The sewerage systems have been designed for design year of 2050. Design criteria and consideration are briefly discussed below:

Design Criteria

The design criteria are based on Standards set forth under the Water and Sanitation Agency (WASA), Lahore criteria and past design experiences of similar projects.

The main objectives of the design criteria are as follows:

- To develop a sewerage system, that can be operated with minimum operation and maintenance cost;
- To collect sewage efficiently and safely to prevent diseases and nuisance; and
- To proposed efficient treatment system which will deliver an effluent that will meet the Punjab Environmental Quality Standards (PEQS)

Sewage Flow Estimation

The most fundamental factor for planning and designing sewerage systems is the estimation of the sewage flow. Otherwise, sewers may prove inadequate resulting in overflow or may prove too large in diameter, which may make the system uneconomical and hydraulically inefficient. For the project area, **80%** of the water demand has been taken as sewage generation.

Peak Factor & Flow

The capacities of the sanitary sewer are sufficient to carry peak flows, rather than the average flow because the rates of flows for any design point will vary substantially depending on the local water use customs, climate conditions, the day of the week, the hour of the day etc. So, waste water collection system has been designed to handle peak flows. The peak flow will be calculated by following formula:

Peak flow = Avg. daily flow * Peak factor

Peak Factor depends upon the population; it decreases with an increase in population. Peak Factor shown in the Table below will be taken for the computation of peak flows;

Population	Peak Factor
Up to 5,000	4.50
5,000 to 10,000	4.00
10,000 to 25,000	3.50
25,000 to 50,000	3.00
50,000 to 100,000	2.50
More than 100,000	2.00

Non-Domestic Sewage Flow

The non-domestic sewage flow has been taken as 80% of average non-Domestic water consumption that will cover institutional, commercial and small industrial discharges.

Infiltration Rate

This is additional quantity due to groundwater seepage in to sewers through faulty joints or cracks formed in the pipes. The quantity of the water depends upon the height of the water table above the sewer invert level and permeability of the ground soil. If water table is well below the sewer invert level, the infiltration can occur only after rain when water is moving down through soil.

PHED Criteria has been followed for infiltration rate for the selected localities of the project area.

Storm Water Allowance

Keeping in view the project area, 33% of peak sewage flow has been taken as storm water allowance.

Total Sewage Flow

Total sewage flow is the sum of all the above flow and sewers / conduits has been designed on this total sewage flow.

Total flow = Peak sewerage flow + Infiltration + Storm water Allowance

Manholes

Manholes will be located according to conventional sewer network design i.e., starting point, junctions between sewers and change in direction and grades etc.

Following manhole spacing are adopted for the design of sewerage system;

Table 8: Manhole Spacing

Pipe Size	Interval
9 inches	50 Feet
12 inches	100 Feet
15 inches	150 Feet
18 inches	200 Feet
24 inches	250 Feet
30-42 inches	250 Feet
48-60 inches	250 Feet
Above 60 Inches	250 Feet

Following manholes dimensions are adopted for sewerage systems of project area;

Table 9: Manhole Diameter

Sewer Size	Manhole Internal Diameter
9-18 inches	04 Feet
24-30 inches	05 Feet

Sewer Size	Manhole Internal Diameter
36-42 inches	6.5 Feet
48-54 inches	7.5 Feet
60-66 inches	8 Feet
72 inches	9 Feet

Change in Sewer Diameter in Manhole

To minimize the risk of blockage in sewers, the diameter of the outgoing sewer is not less than the diameter of the largest incoming sewer. The top of smaller sewers entering a manhole will normally be at the same level as that of the outgoing sewer.

Slope of Channel Within Manhole

All manhole invert levels used in the sewer calculations has been the centre of the manhole and all distances and slopes has been calculated between canters of manholes.

Drop Manholes

The drop connections to manholes have been provided if the difference in pipe invert level is greater than 3.0 ft otherwise no drop manholes will be provided.

Manhole Steps

Ductile Iron and Malleable Cast iron steps etc. are usually used in the manholes. Keeping in view the project area and current practices malleable cast iron steps shall be used in the manhole.

Sewage Disposal Stations

Sewage lift / pump station is required to pump sewage collected from various sewage zones to the disposal point. The details of Sewage lift / pump station will be discussed in the following sections.

The pumping station consists of following structures:

i) One screen chamber (Two partitions)

ii) One Wet well (Two partitions)

iii) One Dry well

iv) One valve chamber

Pumps (working + standby) are proposed in dry well having capacity varying from 0.1 to 0.5 cusec depending on the volume of sewerage produce in the village. The sewage will be treated in ABR from where this treated effluent will be disposed into existing water course.

Anaerobic Baffled Reactor (ABR)

Proposed Sewage Treatment plant consists of Screening Chamber, Wet Well, Dry Well with Pumping Machinery and Sewage Force main up to Proposed STP. Anaerobic Baffled Reactor (ABR), which has chambers divided by baffles, provides a mechanism for both primary and secondary sedimentation. The majority of solids are removed by the ABR's first chamber, which also has low sludge formation and high SRT. The bulk of shock loads may be handled by the technology with ease. The system's ease of construction makes it perfect for

wastewater treatment. The anaerobic process reduces the formation of sludge biomass, the particles in the effluent are reduced due to significant sedimentation in the baffled chambers, and most importantly, the ABR has lower capital and operating costs than aerobic processes. Another significant benefit is that this technique works best in semi-arid and tropical environments.

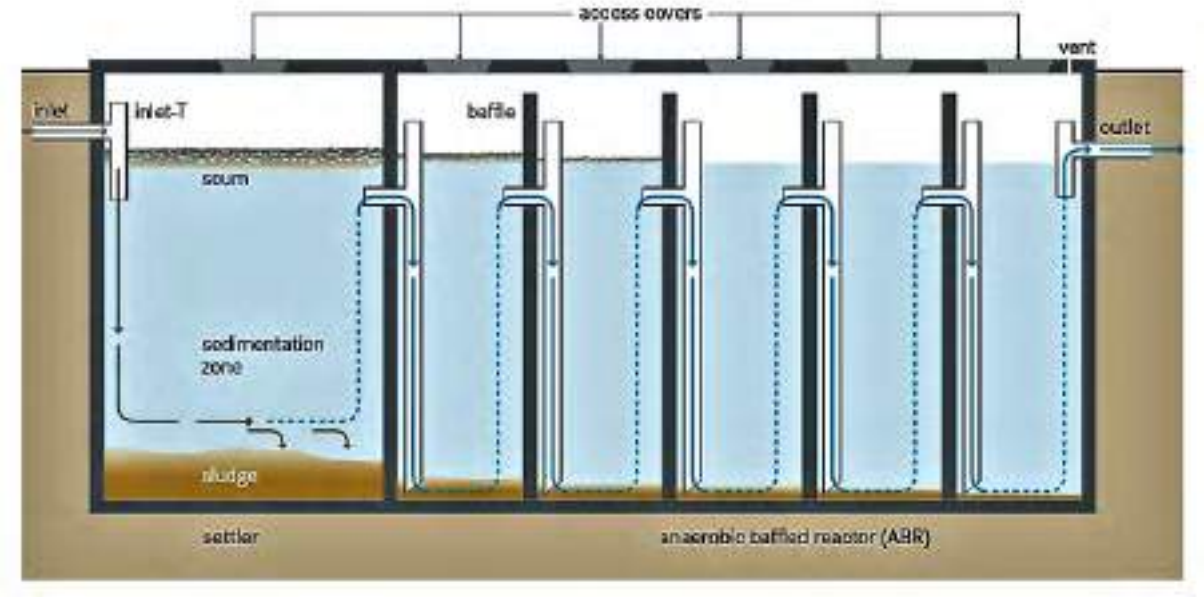

Figure 4: Process Flow Diagram of STP / WWTP / ABR

3.5 Project Cost

The estimated total cost of the project for the proposed 425 villages of Phase-II is 28,781 million PKR or 102.79 million US$[5]

3.6 Land Acquisition

The laying of piping network for water supply and sewerage system will not require land acquisition, as the pipeline will be buried underground. The network will be designed in a manner that the pipeline is laid along the public roads / streets. However, if pipeline route is required to pass through any private lands, special permission for laying and periodic maintenance shall be sought from the landowners.

The land required for the construction of overhead tank, pumping station and STP will consist of state land, acquired through process of No Objection Certificate (NOC). In cases where private land is needed, it shall be obtained through Voluntarily Land Donation (VLD). Village wise breakup of land requirements given in **Table 9.** As is obvious from the table, state land is mostly available in villages called “Chak”. During British Raj, new canals were built to bring the barani areas under cultivation by introducing the irrigated areas around the core of new villages called *Chak*. As sufficient state land is available in these villages (Chaks), therefore NOC process was adopted. Whereas in other villages government land is not available hence private land, donated by community members through VLD procedure, shall be used.

[5] 01 USD = 280.00 PKR

However, land through VLD is only obtained after satisfying the set criteria: first, that the state land is not available in the proposed village; second, when state land in the village is not technically viable – based on requirements of engineering design for the construction of infrastructure; third, only after meeting the VLD Screening Checklist criteria attached as Annexure-8.

Table 10: Land Requirement Details

Sr. No.	Tehsil	Revenue Villages	Private Land required through VLD (in Marla)	State Land required through NOC (in Marla)
1	Kot Momin	Chak No 08/SB (Kot raja)	3	2
2		Baraham Wala	3	2
3		Bahar Wala	0	2
4		Dhudian	3	2
5		Tridianwala	0	2
6		Bukhi Khurd	0	2
7		Bahk Daim	3	2
8		Settment-1	0	2
9		Murad Wala	0	2
10		Dhingrala	2.5	2
11		Dhingra Wali	4	2
12		Haveli Mian Sher	3	2
13	Ahmedpur Sail	Chak No.1/2-L	-	11
14		Chak No.3/2-L	-	11
15		Jhok Dargahi Shah	-	11
16		Chak No.4/3-L	-	14
17		Jhainder Niazi	11	-
18		Basti Lal	11	-
19		Chak 13/3-L	-	8
20		Chak No.2/4-R	8	-
21		Chak No.3/3-L	11	-
22		Basti Wali Muhammad Jandir	8	-
23		Bela Badh	8	-
24		Bhid Wal	11	-
25		Chak No.1/3-R	-	8
26		Laghari	8	-
27		Wahgah	-	11
28		Detisial	-	8
29	Bhawana	Chak 248 Jb	-	11
30		Kamoke	11	-
31		Kotla Shahzada	11	-
32		Maral Wala	6	5
33		Saghar Wala	5	6
34		Thatta Kundal	-	11

Sr. No.	Tehsil	Revenue Villages	Private Land required through VLD (in Marla)	State Land required through NOC (in Marla)
35		Thatta Rasalu	11	-
36		Fateh Kot Taja	11	-
37		Abhulke	-	11
38		Malake Rajoke	-	11
39		Shah Fateh Ali	-	11
40		Nahre Hrseh	-	11
41		Kot Sahib	-	11
42		Mehroke	-	11
43		Thatta Viroka	-	11
44	Darya Khan	Chak No.177/T.D.A	-	11
45		Chak No.53-M.L	-	11
46		Chak No.1 Rakh Dala	-	11
47		Karar Noon	-	11
48		Bilochan Wali	-	11
49		Chak No.51/M.L	-	11
50		Chak No.176/T.D.A	-	11
51		Chak No.50-M.L	-	11
52		Chak No.54-M.L	-	11
53		Surani Nasheb	-	11
54		Daggar Qureshi Janub Gharbi	-	11
55		Chak No.5 Rakh Dallo Wala	5	6
56		Dulle Wala No.1	-	11
57		Chak No.2 Rakh Dala	-	11
58		Chak No.3 Rakh Dala	-	11
59		Chak No.4 Rakh Dala	11	-
60		Gadai No.2	11	11
61		Chak No.12-A/TDA	11	-
62	Pakpattan	Chak No.102/D	20	-
63		Bahwan Shah	-	11
64		Chak Ilahi Bux	-	11
65		Chak Murad Khan	-	17
66		Chak Nazam Din	-	11
67		Gobind Pur Bahmni	6	5
68		Jand Wala	5	6
69		Nahla Abad	-	14
70		Dhamiana	-	11
71		Chak No.4 S.P.	-	11
72		Chak Quder Tullah	4	4
73		Chilli Mamdana	7	7
74		Dada Ahluka	-	30
75		Ghar Taj	-	11

Sr. No.	Tehsil	Revenue Villages	Private Land required through VLD (in Marla)	State Land required through NOC (in Marla)
76		Ghazi Mardan	-	14
77		Arazi Tek Chand	-	14
78		Ghuri	-	20
79		Rakh Ferozpur	-	11
80		Wara Piran Kalan	-	8
81		Kala Chishti	-	8
82		Khamam Doggar	-	11
83		Chak No.12 K.B.	-	8
84		Musteqim Mamunka	-	8
85		Malik Rahmun	-	11
86		Amira Ahluka	-	8
87		Alam Mehteka	-	11
88		Chhinah	-	8
89		Maneke	-	11
90		Jalil Mehteka	-	11
91		Khatwan	-	17
92		Faiz Pur	-	11
93		Talibali	-	11
94		Jamal Pur Tahli	-	11
95		Chak Wasao	-	11
96		Chak No.105.D	-	20
97		Chak No.104/D	-	20
98		Chak No.100/D	-	20
99		Chak No.88/D	18	-
100		Bablana	-	8
101		Bahdar Khara	-	11
102		Bahmani	-	11
103		Bonga Amam Din	-	11
104		Bonga Shamis	-	11
105		Chak No.91/D	8	-
106		Chak Waso Kamboh	-	11
107		Kirparam	-	11
108		Lakh Wira	-	14
109		Magan Pur	-	11
110		Nabi Bakish	-	8
111		Saleem Shah Bodla	4	4
112		Chak No.106.D	-	8
113		Wara Peran Khurd	-	8
114		Chak No.101/D	8	-
115	Liaqatpur	Ahmed Ali Lar	3.3	1.92
116		Allah Dita Bhela	2.3	1.44

Sr. No.	Tehsil	Revenue Villages	Private Land required through VLD (in Marla)	State Land required through NOC (in Marla)
117		Allah Jiwaya Lar	2.9	1.44
118		Ashraf Shah	2.17	1.44
119		Bahan Wala	6.4	3.2
120		Bahar Khaki	24.7	4.8
121		Chak No. 116-A-NP	2.4	0.48
122		Chak No. 116 NP	3.4	0.96
123		Chak No. 117 NP	1.52	1.44
124		Chak No. 118 NP	0.47	0.48
125		Chak No. 119-A- NP	1.2	0.48
126		Chak No. 119 NP	2.4	0.48
127		Chak No. 120 NP	0.12	0.48
128		Chak No. 121 NP	2.96	0.96
129		Chak No. 122 NP	3.9	1.44
130		Chak No. 123 NP	2.2	0.48
131		Chak No. 124 NP	2.7	0.96
132		Chak No. 125 NP	2.7	0.96
133		Chak No. 126 NP	9	0.48
134		Chak No. 127 NP	4.3	2.4
135		Chak No. 128 NP	2	0.48
136		Chak No. 129 NP	2.8	0.96
137		Chak No. 130 NP	0.75	0.48
138		Chak No. 131 NP	0.75	0.48
139		Chak No. 132 NP	1.88	0.48
140		Chak No. 133 NP	1.2	0.48
141		Chak No. 137 NP	0.45	0.48
142		Chak No. 138 NP	1.45	0.48
143		Chak No. 34 Abbasia	1.88	1.48
144		Chak No. 35 Abbasia	3.7	2.88
145		Chanjni	3.7	1.92
146		Chohan	2.75	0.48
147		Choudari	13.6	5.76
148		Chur Wala	1.75	0.48
149		Duda Naich	1.88	1.44
150		Gabrani	17.8	1.44
151		Gharib Shah	4.9	2.88
152		Ghemi	5.87	2.88
153		Ghuka	2.88	0.92
154		Goth Amin	5.51	1.92
155		Goth Hayat	6.3	3.36
156		Goth Mahi	12.8	7.2
157		Gous Abad	6.3	3.36

Sr. No.	Tehsil	Revenue Villages	Private Land required through VLD (in Marla)	State Land required through NOC (in Marla)
158		Gul Muhammad Lar	12.7	1.92
159		Gulani	17.7	7.68
160		Haroon Abad	7.8	2.4
161		Hussain Abad	0.47	0.48
162		Jhoung Bilawal	5.51	1.92
163		Juma Muhana	6.8	3.84
164		Kandani	19.4	2.4
165		Kotla Daulat	14.81	4.8
166		Kotla Mubarik	6.2	1.92
167		Kotla Nawab	6.9	4.8
168		Kotla Niazi	7.8	2.4
169		Lakhani	6.8	3.36
170		Lal Shah	7.8	2.4
171		Laoon Wala	6.8	3.84
172		Malhani	7.5	2.4
173		Malikpur	1.94	2.4
174		Malkani	6.8	3.84
175		Metla	5.9	2.4
176		Mir Muhammad Lar	1.88	1.44
177		Muhammad Daha	6.8	3.36
178		Mujawraan	5.3	2.88
179		Nala Musani	2.76	1.44
180		Pakhi War	5.9	2.4
181		Pararan Sharif	9.7	4.32
182		Qadu Wali	13.2	6.72
183		Rais Pathan	5.52	2.88
184		Rashid Abad	2.76	1.44
185		Rindan	8.1	4.8
186		Sadiqpur	1.9	0.48
187		Saidpur	11.8	4.8
188		Shahbazpur Gharbi	289	0.96
189		Shamsabad	2.2	1.44
190		Shidani Sharif	13.2	2.88
191		Talbani	38.2	9.6
192		Tanwari	6.4	3.36
193		Trinda Mir Khan	11.6	7.2
194		Ther Posti	2.3	1.44
195		Tibbi Sayyadan	6.4	3.36
196		Wahid Bux Sial	6.2	1.92
197		Yakhtar Maha	1.4	1.44
198		Zaffar Abad	17	3.8

Sr. No.	Tehsil	Revenue Villages	Private Land required through VLD (in Marla)	State Land required through NOC (in Marla)
199		Unran	4.9	2.88
200	Rojhan	Badli	2.3	0.48
201		Badli Chak Ladh	1.3	0.96
202		Basti Nikka	0.44	0.48
203		Chak Dim	4.37	0.48
204		Chak Kariya	2.3	0.48
205		Chak Mut-1	0.44	0.48
206		Chak Mut-2	6.88	0.48
207		Dera Dildar	27.3	3.84
208		Dera Jewan Khas	0.47	0.48
209		Garhi Soori	0.11	1.92
210		Kaheeri	1.44	0.98
211		Kin Khas	0.58	1.92
212		Kotla Gulsher	11.9	1.92
213		Kotla Hasan Jamra	0.94	0.48
214		Rakh Kotla Hasan Jamra	1.72	0.48
215		Lutairi	0.23	0.48
216		Miranpur	11.2	3.36
217		Patti Shah Wali	0.3	0.48
218		Shah Wali	17.3	4.8
219		Solangi	0.3	0.48
220		Wah Machka	31.86	3.84
221	Shujabad	Agar Khani	22	-
222		Amanullah Pur	5	-
223		Bagrain	14	-
224		Basti Chhaju Shah	8	-
225		Bhana	5	-
226		Chak Jakhar	6	-
227		Chak No 13/F	6	-
228		Chak Rs	84	-
229		Choti	6	-
230		Dairapur	12	-
231		Dera Arvi	4	-
232		Dhondo	8	-
233		Gunwen	84	-
234		Jai	10	-
235		Jhangi	5	-
236		Kaser Pur	72	-
237		Khalar	7	-
238		Khanpur	48	-
239		Khas Punjani	10	-

Sr. No.	Tehsil	Revenue Villages	Private Land required through VLD (in Marla)	State Land required through NOC (in Marla)
240		Kotli Najabat	216	-
241		Lasoorhi	6	-
242		Lutf Pur	9	-
243		Mahara	4	-
244		Mochi Pura	42	-
245		Mohan Pur Gharbi	11	-
246		Pounta	40	-
247		Punjani	120	-
248		Raja Raam	108	-
249		Rasool Pur Janubi	62	-
250		Rasool Pur Shumali	18	-
251		Rukan Hatti	96	-
252		Sat Burji	12	-
253		Seri	7	-
254		Shah Musa	60	-
255		Sheikhpur Shajra	48	-
256		Soman	44	-
257		Tahir Pur	5	-
258		Thath Galawan Junabi	20	-
259		Thatha Makhdoom Pur	16	-
260		Tudar Pur	60	-
261		Vainus	12	-
262		Wahi Bhakar	13	-
263		Wahi Sawaya	5	-
264		Taror Jalal Pur	21	-
265	Alipur	Amir Pur Daha	10	-
266		Baqar Shah Janubi	5	-
267		Basti Haji	4	-
268		Baz Wala	32	-
269		Bet Channa	4	-
270		Bet Dewan Shah	5	-
271		Bet Muiziddin	14	-
272		Chak Dada	4	-
273		Chak Daud Wala	5	-
274		Dahaka	7	-
275		Damar Wala Janubi 1	14	-
276		Damar Wala Janubi 2	13	-
277		Daulut Pur	6	-
278		Fateh Pur Janubi 1	7	-
279		Fateh Pur Janubi 2	19	-
280		Ghalwan 1	144	-

Sr. No.	Tehsil	Revenue Villages	Private Land required through VLD (in Marla)	State Land required through NOC (in Marla)
281		Ghalwan 2	120	-
282		Ghari	27	-
283		Kachi Lal	6	-
284		Khair Pur Para	3	-
285		Khair Pur Sadat	168	-
286		Khan Pur Nahrka	5	-
287		Khanani	24	-
288		Khangarh Donma	14	-
289		Kundai	9	-
290		Kundrala	7	-
291		Latti	96	-
292		Madd Sohanyara Shah	10	-
293		Malik Arain	48	-
294		Misan Kot Behwa	84	-
295		Mohib Shah	6	-
296		Mud Wala	82	-
297		Mutfarqa	564	-
298		Nussrat Pur	5	-
299		Pakka Naich	21	-
300		Phullan	84	-
301		Rakh Khanani	14	-
302		Shah Wasava	50	-
303		Sheikhani	15	-
304		Sultan Pur	120	-
305		Tibi Arian	48	-
306		Walwat	7	-
307	Kahror Pacca	Basti Lal	10	
308		Chak Qadirpur	11	-
309		Dera Dilawar	-	11
310		Kotkora Jhanda	-	8
311		Arah	-	11
312		Chak Allah Rakha Khan	-	8
313		Dhorah Mahar	-	8
314		Gopal Pur	-	11
315		Gul Pur	-	8
316		Bhinda Gerdan	4	4
317		Chak Muhammad Murad	-	23
318		19/M	-	8
319		21/M	5	6
320		30/M	10	10
321		Kand Ahmed Asar	4	4

Sr. No.	Tehsil	Revenue Villages	Private Land required through VLD (in Marla)	State Land required through NOC (in Marla)
322		Murshad Pur	-	8
323		22M	-	182
324		Chak Choki Kohna	-	17
325		Hassa Joya	26	-
326	Khairpur Tamewali	Fazlu Kukara	-	14
327		Khairi Bhabhi	-	14
328		Kotla Mahi	-	8
329		Ladar	-	8
330		Mamdu Mangero	-	14
331		Bunga Yarani	-	8
332		Darud Garan	10	10
333		Goth Ali	-	17
334		Gith Kamal	-	11
335		Kamalia	-	8
336		Ahmed Milkhi	4	4
337		Amin Fatani	-	8
338		Baghban	-	8
339		Binda Chadhran	-	8
340		Kharal Nau Baramad	-	11
341		Chak No. 26	-	8
342		Dharala Randu	-	8
343		Haleem	-	11
344		Khanan Arain	-	8
345		Chak No. 24 Sharaf Shah	-	11
346		Khuda Bux Seyal	-	29
347		Kotla Qaim Khan	-	8
348		Lal Sohanra	-	11
349		Luthran	-	29
350		Mehti	-	8
351		Mohammad Sharif	-	11
352		Muhammad Khan	-	11
353		Mungrani	-	8
354		Muradpur	-	8
355		Muradpur Dhrala	-	11
356		Nurrey	4	4
357		Qazi Kalra	-	11
358		Raja	-	11
359		Rameli	-	8
360		Rukrani	-	8
361		Sardar Pur	-	44
362		Azimpura	-	44

Sr. No.	Tehsil	Revenue Villages	Private Land required through VLD (in Marla)	State Land required through NOC (in Marla)
363		Noor Mohd Khan	-	35
364		Gaman Wagi	-	41
365		Gawains	-	35
366		Goth Jhumar	-	35
367		Khairpur	-	17
368	Bahawalnagar	Bonga Ihsan Bibi	-	5
369		Hasan Raika	6	5
370		Abrerah Uttar	-	11
371		Amin Abad	-	11
372		Boole Shah Hitthar	17	-
373		Ramnagar	20	-
374		Paran Wala	10	-
375		Hussian Abad Hithar	-	11
376		Hussian Abad Uttar	11	-
377		Chak Abdul Haq	11	-
378		Dhanraj Pura	10	-
379		Ali Goher No. 326	-	11
380		Jagga Sanatteka	8	-
381		Mina Sanatteka	-	80
382		Sharaf Din	11	-
383		Mosla	-	11
384		Pir Sikandar Otar	10	7
385		Jhulan Chishtian	11	-
386		Gauspur	-	11
387		Gaman Dongi	-	14
388		Akkanwali Khurd	23	-
389		Kartar Singh	-	23
390		Khawaja Bux Bodla	-	11
391		Faqir Shah	10	-
392		Khober	-	23
393		Ramzan Shah	10	-
394		Allahabad	-	11
395		Muhammad Asad Khan	-	20
396		Janoowala	11	-
397		Tobi Qamar-Ud-Din	10	-
398		Malak Pura	-	11
399		Jalwala	-	20
400		Dara Sanatteka	10	-
401		Hira Bashnoai	-	11
402		Sandar Bashnoi	10	10
403		Sher Singh Wala	23	-

Sr. No.	Tehsil	Revenue Villages	Private Land required through VLD (in Marla)	State Land required through NOC (in Marla)
404		Barasajwar Khan	-	11
405		Noor Jahanian	-	11
406		Dadoo Mammunka	-	11
407		Bhole Shah Utar	-	17
408		Abrerah Hitthar	-	11
409		Bilara Nabi Bux	-	11
410		Bilara Qasim Khan	11	-
411		Madarsa	10	-
412		Pir Shah	10	-
413		Kakku Bodla	-	11
414		Bhangran	5	6
415		Khilowala	11	-
416		Mamunka Hatar	-	11
417		Muhsan Pura	10	-
418		Beg Kanoor Pur	-	11
419		Wara Piran	5	6
420		Chaweka Hitthar	10	-
421		Mamunka Uttar	-	11
422		Dinpur Sharif	11	-
423		Mari Mian Sahab Hithar	6	5
424		Ramzan Langah	-	11
425		Tughera Sharif	-	11
426		Wilayat Pur	-	11
427		Nanak Sar	10	-
		Total	**4891.17**	**2611.18**
		Grand Total	**7502.35**	

Note: The total 1378 Marla land is required through VLD, whereas 380.43 Marla land is required through NOC. Similar to the trend observed in pilot phase, more area of land is being obtained through VLD because:

1. Suitable state land was not available in most of these villages;

2. In phase-II villages, the requirement of land for the installation of solar panels for reduction of O&M cost for ensuring sustainability has also been foreseen. However, due diligence has also been conducted to ensure that the socio-economic impacts of VLD are negligible.

Furthermore, the size of land required in different villages vary depending upon the population, water requirement, size of OHR, size of ABR, size of solar panel solutions and volume of sewerage generated.

3.7 Project Administrative Jurisdiction

The proposed project falls under the jurisdiction of Deputy Commissioners of relevant tehsils of province.

3.8 Project Implementation Schedule

The project will take 10 months in each village from start to finish. The commencement is scheduled simultaneously in January/February 2026.

3.9 Construction Activities and Required Machinery

Construction activities involve following:

- Earth work
- Structure/ Concrete works
- Pipe laying

Table 10 presents the list of expected machinery required for construction. The number of these machines will be finalized with the detailed design of the proposed road:

Table 11: List of expected Machinery/Equipment

1	Mobile Crane	15	Jack Hammer
2	Dumpers	16	Plate Compactor
3	Road/Power Roller	17	Wood Shuttering
4	Light Weight Compactor	18	Formwork
5	Ramming Machine	19	Steel Cage Shuttering Unit
6	Water Sprinkler and Water Tanker	20	Motor graders
7	Excavator	21	Generators
8	Tractor with Front Blade and Trolley	22	Welding Plant
9	Loader	23	Transit Mixer
10	Road Cutter	24	Vibrators
11	Pneumatic Tyred Roller (PTR	25	Scaffolding
12	Tandem Roller	26	Light Transport
13	Concrete Mixer Machine	27	Mini/ Hand Roller
14	Tower Crane	28	Barricades

3.10 Construction Camps

Camp sites will be selected based on following considerations:

- Number of workforces deployed;
- Type and quantity of machinery mobilized;
- Availability of adequate area for establishing camp sites including parking areas for machinery, stores and workshops;
- Access to communication and local markets;

- Appropriate distance from sensitive areas including settlements and religious and/or cultural facilities.

Final locations will be selected by the contractor with the assistance of Supervision Consultant. A centralized construction camp will be preferred in tehsils where villages are geographically in close proximity; this will result in resource efficiency and better monitoring of construction activities. Care will be taken to safeguard the existing environment of the area and location shall be selected away from settlements. If the campsite is to be established on privately owned land, the contractors will acquire it on rental basis from private landowners. The contractors will return the land on as received basis. All debris, construction materials, left over chemicals and machinery shall be removed before handing back the premises to landowners.

3.11 Construction Materials

The materials used in construction of water supply, sewerage, overhead tanks pumping station & sewage treatment plant (STP) in all villages, would include coarse aggregates (crush), bricks, fine aggregates (sand), soil, water, pipes (RCC & HDPE), cement, reinforcement, asphalt etc. Procurement, safe handling and transportation of these material as per the EHS guidelines and other requisite standards will be responsibility of the Contractors. Local suppliers of construction materials should be preferred if they meet the financial and quality standards criteria.

3.12 Workforce Requirement

Workforce during Construction Phase

Total man power required on site for proposed Project will be approximately 08-30 workers per village per day, depending on the type of construction. Hiring of the local labor will be preferred.

Workforce during Operation Phase

Total man power required during operation phase for proposed Project will be approximately 5 workers per village comprising skilled and unskilled staff.

3.13 Solid Waste Generation

Due to construction activities waste will be generated at construction and contractors camp site. The construction waste will include wastewater, oil spillage from machinery, domestic waste and waste construction materials. Solid waste generated during construction and camp sites will be safely disposed of in demarcated waste disposal sites.

Construction and Operation Phase

The solid waste generation is estimated to be 0.28kg/capita/day during construction phase of the proposed Project.

3.14 Water requirement

Construction Phase

The water consumption is estimated to be 30 liter/day/worker[6] during construction phase of the proposed Project.

[6] The most basic water requirement is stipulated by the World Health Organization (WHO) and varies between 20 and 50 litres per capita per day (LPCD).

Operation Phase

The water consumption is estimated to be 50 liter/capita/day (during operation phase of the proposed project.

3.15 Wastewater Generation during Construction Phase

The wastewater generation is estimated to be 24 liter/capita/day[7] for during construction phase of the proposed Project. Temporary toilets with cesspit will be adequately installed and treated periodically, and after the completion of work, the ground will be restored.

[7] Design Criteria of Public Health Engineering for Water Supply, Sewerage and Storm Water Drain (Domestic sewage generation = 80% of water consumed/day)

4 BASELINE PROFILE

4.1 General

This chapter presents the current environment around the proposed development which has been considered with respect to physical, ecological and socio-economic resources. The ESMP of the proposed project covers a comprehensive description of the project area, including the resources which are expected to be affected by the project, as well as, those which are not expected to be directly affected by the construction and operation of the project.

ESMP teams conducted the reconnaissance and detailed field visits of the project area from November, 2025 to February, 2026. The prime objective of the field visits was to collect the baseline data on physical, eco-biological and environmental & social aspects along with identification, assessment and categorization of the significant environmental and social impacts of the proposed Project. The collected data was later transferred to IT based innovative tool (Kobo-Tool), for prompt retrieval. Further analysis and arriving at the meaningful results. The secondary data was collected from published sources/reports and relevant departments, which were also verified through visual observations during reconnaissance and detailed surveys.

4.2 Delineation of Study Area/ Area of Influence (AoI)

As per the environmental screening study conducted earlier, the project falls in “Category E2”. The impacts of the project activities are limited and within the boundary of each targeted revenue village. The relevant revenue village is considered as project area and boundary of revenue village has been considered Area of Influence (AoI).

To further explain the area of influence on the basis of the project activities, maps explaining the geographical scale and setting of sewerage and water supply network, water and wastewater treatment and disposal of the treated effluent in the pond situated with in the principal settlement of the village are provided at annexure-3. It is to be noted that the outfall of the treated effluent is into the existing wastewater collection pond located within the boundary of the village (within the confines of AoI). As the level of project intervention (water supply and treatment, wastewater collection and treatment system) and on ground conditions (such as sewerage ponds) are similar in all 425 villages therefore, maps of a typical village are shared to develop understanding of the area of influence.

As per the national and provincial regulations along with the requirements of World Bank’s OP’s, impacts and risks have been analyzed within the project AoI. Environmental and social impacts and risks will also be analyzed for all relevant stages of the project cycle, including pre-construction, construction and operation phases of the project.

4.3 Physical Environment

The physical environment includes topography, geology, soil, climate, hydrology, drainage, seismology, surface water, groundwater and ambient air.

4.3.1 Topography

The proposed project sites are rural settlements comprising residential and agriculture areas. The terrain of the project area is mainly characterized by its flat nature. The ground elevations variation is given in **Table 11**:

Table 12: Topographic Variations

Sr. No.	Cluster	Tehsils	Elevation (ft)
1	North	Kot Momin	637.21 to 677.92
2	South-I	Liaqatpur	315
3		Rojhan	223
4	South-III	Bahawalnagar	516 to 535
5		Kahror Pakka	335 to 387
6		Khairpur Tamewali	126 to 137
7	Central	Ahmadpur Sial	455 to 475
8		Pakpattan	527 to 578
9		Darya Khan	553 to 599
10		Bhawana	157 to 177
11	South-II	Alipur	285 to 410
12		Shujabad	350 to 450

4.3.2 Geology

Punjab's area mostly consists of an alluvial plain formed by the southward-flowing Indus River and its four major tributaries. The general slope of the land is from northeast to southwest, but it rises in the areas between rivers Approximately 70 percent land area of the province comprises flood plans of Indus basin. Geologically, lands in the flood plains are lightly mantled with alluvial deposits transported from the Himalaya foothills. The underlying bedrock is composed of Precambrian metamorphic and tertiary consolidated rocks. The overlying alluvium consists of Pleistocene to recent unconsolidated deposits of sand, clay and silt. The formation age of the alluvium also dates from Pleistocene to recent, the latter being predominant earth river banks and the former around the central part of the plains, no major fault zone traverses the project area.

4.3.3 Climate and Meteorology

A. Average Temperatures

The project area has hot summer and cold winters. The summer starts from May and lasts till September. June is the hottest month. The mean maximum temperature varies between 39-45 ºC and minimum temperature varies between 23-29 ºC respectively for month of June. The winter seasons lasts from November to February. January is the coldest month. The mean maximum ranges between 18 - 30 ºC and mean minimum temperature ranges between 05 - 14 ºC in January as shown in the following table:

Table 13: Temperature Variation in Summer and Winter Season

Sr. No.	Cluster	Tehsils	Average Annual Rainfall (mm)	Summer Season		Winter Season	
				Mean Max ºC	Mean Min ºC	Mean Max ºC	Mean Min ºC
1	North	Kot Momin	69	40	27	18	6
2	South-I	Rojhan	147	45	27	25	5
3		Liaqatpur	73	39	28	21	8
4	South-III	Bahawalnagar	45	41	29	20	07
5		Kahror Pakka	71	42	23	31	05
6		Khairpur Tamewali	143	41	28	20	07
7	Central	Ahmadpur Sial	45	45	29	21	05
8		Pakpattan	23	45	24	30	06
9		Darya Khan	45	45	29	21	05
10		Bhawana	46	44	29	19	05
11	South-II	Alipur	253.7	39	28.6	26	12.8
12		Shujabad	60	39.2	28.6	25.8	12.6

In project areas, most of the times of the year sunny days dominate. A few days per month are partly cloudy and with seldom overcast days. The maximum precipitation is observed during June to August. In project areas are classified as arid region having average annual rainfall less than 250 mm in a year. Highest intensity of rain is recorded in month of July and August owing to monsoon season.

B. Wind

In targeted tehsils windier part of the year is April to August. In north, central-I and south-III zones of Punjab, April and July are notably the windiest months. Conversely, in the south-I and central-II zones of Punjab, June experiences higher wind activity. Moreover, from April to July, dust storms are prevalent in the targeted tehsils.

Table 14: Average Wind Speed and Windiest Month in Tehsils

Sr. No.	Cluster	Tehsils	Windiest Month	Avg. Wind Speed
1	North	Kot Momin	May	10-20 km/h
2	South-I	Liaqatpur	June	13 km/h
3		Rojhan	May	14 km/h
4	South-III	Bahawalnagar	June	14 km/h
5		Kahror Pakka	July	11 km/h
6		Khairpur Tamewali	June	16 km/h
7	Central	Ahmadpur Sial	April	28 km/h
8		Pakpattan	June	12 km/h
9		Darya Khan	April	28 km/h
10		Bhawana	May	28 km/h
11	South-II	Alipur	June	15.6 Km/h
12		Shujabad	July	12.4 Km/h

4.3.4 Water Resources

Description of surface water and groundwater of targeted villages in different tehsils is as under. Hydrology map of Punjab Province is shown in **Figure 3.**

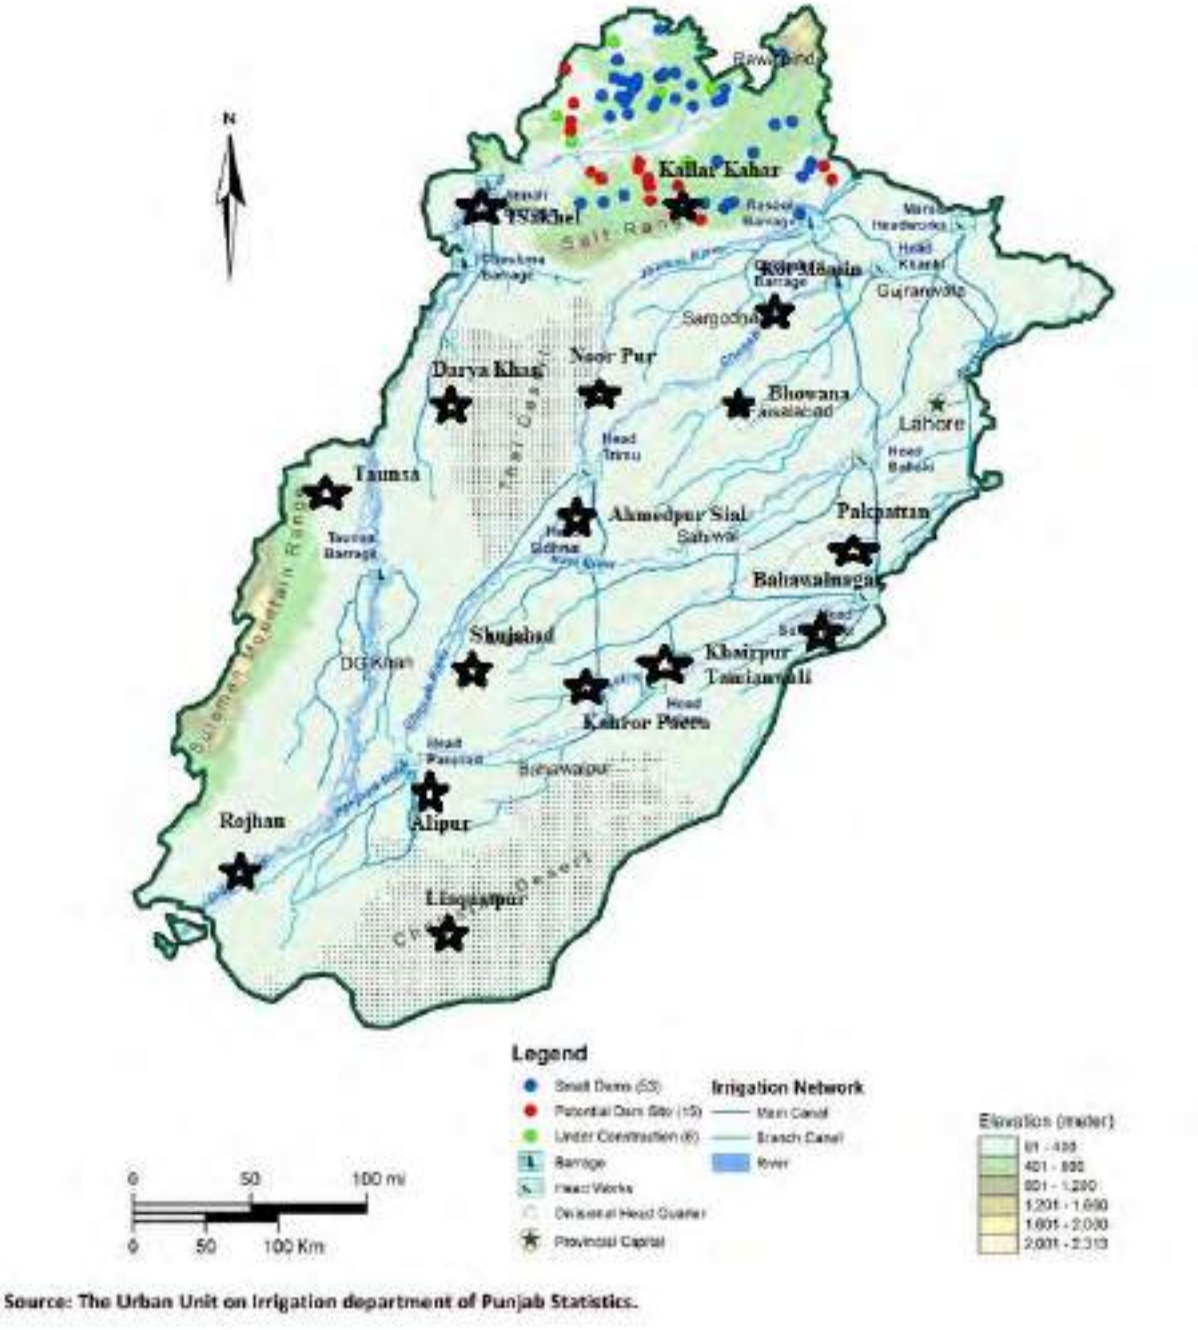

Source: The Urban Unit on Irrigation department of Punjab Statistics.

Figure 5: Hydrology Map of Punjab Province

Surface Water

Punjab is land of Indus River and its four major tributaries in Pakistan, the Jhelum, Chenab, Ravi, and Sutlej rivers. Punjab Irrigation system is one of the world's largest irrigation systems with a command area of over 21 million acres. The system consists of 24 main canals and 12 barrages and vast network of canals, distributaries and minors spanning over 40,000 kilometers. Targeted villages in north, south and center of the Punjab are in command area of this irrigation system. The detail of canal and distributaries passing within or nearby the targeted villages is shared in **table 14:**

The tehsils of Alipur & Shujabadin the South-II Cluster are served by major surface water resources, including the Indus and Chenab Rivers, as well as an extensive irrigation network comprising canals, distributaries, and minors. These water bodies are primarily used for irrigation and local water needs.

In Liaqatpur, canals associated with the Abbasia Canal system provide water primarily for agricultural activities, Surface water is not a major source of potable water but is widely used for irrigation, livestock, and groundwater recharge.

Surface water resources in Kot Momin are mainly influenced by the River Chenab and its associated irrigation network, including the Khadir Feeder. The feeder serves surrounding villages such as Nasir Pur, Midh, Mumrana, Khadir, Chokera, Chani, and Wan Miana, providing irrigation supplies. Seasonal flows and canal operations govern surface water availability and quality within the command area.

In Bahwalnagar the overall water quality is assessed as moderate to poor. Most physico-chemical parameters comply with acceptable limits; however, elevated TSS and turbidity remain concerns. The tehsils of Kahror Pacca within the South-III Cluster are served by major surface water resources, including the Sutlej River. However, the river remains largely dry or experiences low environmental flows for most of the year. These surface water bodies are primarily utilized for irrigation purposes and to meet local water requirements.

Tehsil Khairpur Tamewali, within the South-III Cluster, relies on the Sutlej River, which has low or seasonal flows and generally moderate to poor water quality, and is mainly used for irrigation and local needs. Tehsil Ahmadpur Sial, located within the South-III Cluster, is served by the Chenab River and an extensive irrigation network that primarily supports irrigation and local water needs. Tehsil Pakpattan is served by one main canal and three distributaries, which primarily support irrigation and local water requirements, with generally moderate water quality.

Tehsil Darya Khan is served by surface water resources of generally moderate to poor quality, conveyed through the irrigation network. These waters are primarily used for agricultural irrigation and local needs, with quality influenced by seasonal variability, sediment load, and potential contamination. The overall water quality is assessed as moderate to poor. Most physico-chemical parameters comply with acceptable limits; however, elevated TSS and turbidity remain concerns.

Table 15: Surface Water Bodies in Targeted Villages of Relevant Tehsils

Sr. No.	Cluster	Tehsils	Surface Water Bodies of targeted villages in Tehsils				
			River	Main Canal	Branch Canal	Distributary	Minor Canal
1	North	Kot Momin	Chenab	-	Khadir Feeder	Nasir Pur, Midh, Mumrana, Khadir, Chokera	Chani, Wan Miana
2	South-I	Liaqatpur	Indus	Abbasia Canal, Abbasia Link Canal, Panjnad Main Line	-Minchin Branch	1-L/AC 1-R/AC 3-R/AC 4-R/AC 5-R/AC 6-R/AC 7-R/AC	1-L/1-R/AC Minor 1AL/3-R/AC Minor

Sr. No.	Cluster	Tehsils	Surface Water Bodies of targeted villages in Tehsils				
			River	Main Canal	Branch Canal	Distributary	Minor Canal
3		Rojhan	Indus	Bahawal Canal	-	Qadra Distributary & Umar Kot Distributary	Tariq Minor
4	South-III	Bahawalnagar	-	Forwah Canal	Malik Canal	-	Gujiani Canal
5		Kahror Pakka	Sutlej River	-	-	-	-
6		Khairpur Tamewali	Sutlej River	Bahawal Canal	-	-	-
7	Central	Ahmadpur Sial	Chenab	Rangpur Canal		1L Distributary	1L / 3L Minor
8		Pakpattan	-	100 Wali Canal	-	Malkans Rajwaya Distributary, Malka Hans Ranba	-
9		Darya Khan	-	-	-	Hukam Distributary	Panj Girain Sub Minor, Bahadur Minor, Darya Minor
10		Bhawana	Chenab	LCC	-	-	-
11	South-II	Alipur	Indus River	Rangpur Canal	Muzaffargarh Branch Canal	Distributaries of Muzaffargarh Branch Canal	-
12		Shujabad	Chenab River	Lower Chenab Canal	Shujabad Branch Canal	Faiz Distributary Rana Distributary Panjani Distributary Shujabad Distributary Wali Muhammad Distributary Mahmud Distributary	Sat Burji Minor

A. Groundwater/Drinking Water Quality

The findings of the groundwater investigation indicate that the project area has a plentiful supply of groundwater available at depths ranging from 21 to 50 feet, with the exception of the villages of Pakpattan, Kahror Pakka, and Shujabad. As per ERS (Electrical Resistivity Survey) studies, shallow groundwater is slightly brackish, whereas deep groundwater is relatively sweet at depths of around 350 ft. Handpumps installed at depths of 350-400 ft yield sweet

water and are commonly used by the local community for drinking purposes. In contrast, groundwater near the ground surface remains brackish.

As per ERS studies, groundwater at shallow depths of about 20–30 ft occurs in localized sweet water pockets. These pockets are limited to approximately 20 ft in thickness, below which the groundwater becomes brackish and unfit for drinking purposes.

In Liaqatpur groundwater is the primary source of domestic water supply. The quality of groundwater is generally brackish to moderately saline, with elevated Total Dissolved Solids (TDS) reported in several locations. In some areas, the presence of dissolved salts and occasional microbial contamination limits its direct suitability for drinking without basic treatment; however, it remains commonly used for household purposes and limited irrigation.

Groundwater depth in the tehsils of Alipur & Shujabad in the South-II Cluster ranges from 20 to 60 ft and serves as the primary source of water. The groundwater quality is non-objectionable in terms of taste and color, indicating generally acceptable groundwater conditions.

In Liaqatpur groundwater is the primary source of domestic water supply. The quality of groundwater is generally brackish to moderately saline, with elevated Total Dissolved Solids (TDS) reported in several locations.

In Kahror Pakka, parameters such as TDS and total hardness do not comply with PEQs and WHO standards. In Khairpur Tamewali, TDS, turbidity, and total hardness exceed permissible limits. In Ahmadpur Sial, the prevalence of water-borne diseases has been reported in several villages. In Pakpattan, TDS and total hardness are beyond PEQs and WHO standards, while in Darya Khan, biological parameters exceed PEQs limits in some villages. Similarly, in Bhawana, TDS and total hardness are not in compliance with PEQs and WHO guidelines.

The groundwater analysis of the targeted villages in different tehsils revealed the following facts in **table 15:**

Table 16: Groundwater Analysis

Sr. No.	Cluster	Tehsils	Groundwater Detail of targeted villages in Tehsils				
			Depth	Taste	Color	Source	Remarks
1	North	Kot Momin	40 feet	Slightly Brackish	Slightly Yellowish	Groundwater	Elevated Levels of Zinc, Sodium, And Potassium
2	South-I	Liaqatpur	30 feet	Objectionable	02 (TCU)	Groundwater	Total hardness (as $CaCO_3$) high TDS high
3		Rojhan	21 – 40 feet	Brackish	Slightly Yellow	Groundwater	Waterborne diseases are prevailing in the villages
4	South-III	Bahawalnagar	30 – 40 ft	Brackish	Clear	Seepage of Canal Water	High Floride.
5		Kahror Pakka	>56 ft	Non objectionable	Clear	Ground Water	Some of the parameters

Sr. No.	Cluster	Tehsils	Groundwater Detail of targeted villages in Tehsils				
			Depth	Taste	Color	Source	Remarks
							like TDS, Total hardness, lead and total coli-forms were not in compliance with PEQS and WHO standards.
6		Khairpur Tamewali	25-30 ft	Non-Objectionable	Clear	Ground Water	Water Borne Diseases are prevailing in the Villages
7	Central	Ahmadpur Sial	26 – 50 ft	Non-Objectionable	Yellowish	Ground Water	Water Borne Diseases are prevailing in the Villages
8		Pakpattan	> 56 ft	Non-Objectionable	Clear	Ground water	-
9		Darya Khan	26-40 ft	Non-Objectionable	Clear	Ground Water	Biological parameter is out of PEQs limits in some of the villages
10		Bhawana	40 -60 ft	Non-Objectionable	Clear	Ground Water	Some of the parameters like TDS, total hardness and total coli-forms were not in compliance with PEQS and WHO standards
11	South-II	Alipur	20-60ft	Non-Objectionable	0 TCU	Groundwater	-
12		Shujabad	20-60tf	Non-Objectionable	0 TCU	Groundwater	-

Based on the data in the table 15, where the groundwater is brackish, seepage from the canal water will serve as the primary source of water for the water supply system. Whereas, in areas where the groundwater is deemed acceptable in terms of taste, it will be utilized as a source of water following appropriate treatment measures as indicated below:

- Chlorination for Microbial contamination
- Sand and carbon filters for turbidity
- Adsorption media filter for Arsenic / fluoride

4.3.5 Environmental Monitoring, Sampling and Testing

In order to determine the ambient air, noise levels, groundwater/ drinking water quality, environmental monitoring was carried out through EPA approved environmental labs tin the project area. The sampling locations for the environmental monitoring of ambient air, noise and groundwater/ drinking water and wastewater for the relevant tehsils lies within the boundary of the selected villages. To analyze the quality of groundwater and surface water, monitoring was performed for all the villages.

A. Ambient Air Quality

The ambient air quality monitoring period was 24 hours. The results of ambient air quality monitoring are given in **Table 16.**

Table 17: Ambient Air Quality Results

Sr. No.	Parameters		Carbon monoxide	Sulphur dioxide	Ozone	Nitric oxide	Nitrogen Dioxide	PM (2.5)	PM (10)	Suspended particulate Matter
	Unit		(24 hours) mg/m3	µg/m3	(1 hour) µg/m3	µg/m3	µg/m3	µg/m3	µg/m3	µg/m3
	PEQS		5	120	130	40	80	35	150	500
1	Kot Momin	Chak 08 /SB Kot raja	3.01	46.1	71	6.2	21.41	53	155	444.9
		Baraham wala	2.99	44.2	66	5.2	25.4	56	150	441.2
2	Ahmedpur Sail	Ahmadpur Sial	0.91	27.33	22	7.6	13.1	34	144	305
3	Bhawana	Bhawana	0.76	27.56	19	10	7.82	32	139	321
4	Darya Khan	Darya Khan	0.24	22.56	18	9	9.12	42	161	356
5	Pakpattan	Pakpattan	2.01	32.1	20	8.6	39.69	38	151	324
6	Liaqatpur	Chak 46 Abbasia	1.46	32.65	0	4	2.04	19	78	119
		Chak 09 Abbasia	1.59	75.68	0	3.1	3.2	24	78	112
		Chak 88 Abbasia	1.4	79.23	0	3.8	2.16	20	81	111
7	Rojhan	Bhagsar	1.19	69.22	0	3.9	2.14	23	85	119
8	Alipur	Nawan Dera	0.8	80	66	16	28	37	119	220
		Tibba Burrah	0.7	81	77	19	26	30	129	207
9	Shujabad	Sangri	0.9	69	70	12	27	42	125	235
		Sarai	0.6	88	72	15	25	35	153	201
10	Kahror Pacca	Kahror Pacca	0.35	15.3	21	9.3	13.02	32	118	256

Sr. No.	Parameters		Carbon monoxide	Sulphur dioxide	Ozone	Nitric oxide	Nitrogen Dioxide	PM (2.5)	PM (10)	Suspended particulate Matter
	Unit		(24 hours) mg/m3	µg/m3	(1 hour) µg/m3	µg/m3	µg/m3	µg/m3	µg/m3	µg/m3
	PEQS		5	120	130	40	80	35	150	500
11	Khairpur Tamewali	Khairpur Tamewali	0.68	27.01	18	12	23.41	26	78	118
12	Bahawalnagar	Bahawalnagar	0.82	20.52	24	14	24.25	23	82	136

The ambient air quality monitoring is carried out via mobile air quality laboratories that are stationed at the sides of roads. As a result, areas with heavy traffic may exhibit higher concentrations of particulate matter and gases emanating from vehicular exhausts. The central and northern regions of Punjab are comparatively more industrialized than the southern region, which leads to a greater prevalence of anthropogenic sources of air pollution. The above Table 15 indicates that at most testing location, air quality (majority of the parameters) is within PEQS limits with minor fluctuations. However, some of the parameters surpass the PEQS which are highlighted red in the above table.

B. Noise Level

Noise levels were monitored with the help of a potable digital sound meter at the project area for 24 (twenty-four) hours. The results of noise monitoring are given in **Table 17**.

Table 18: Noise Monitoring Results

Zone	Tehsils	Villages	Equivalent Noise Level (Leq) dB(A)		PEQS Limit dB(A)	
			Day Time	Night Time	Day Time	Night Time
North	Kot Momin	Chak 08 /SB Kot raja	60.2	49.5	55	45
		Baraham wala	60.2	45.5		
Central	Ahmadpur Sial	Chak 4-3L	56	43		
		Chak 12-3L	48	37		
	Bhawana	Chak 156 JB	49	40		
		Chak 203 JB	57	43		
	Darya Khan	Chak 46/ML	50	36		
		Chak 47/ML	52	42		
	Pakpattan	Asadullah Pur	45	31		
		Nizam Adlike	50	39		
South-I	Liaqatpur	Chak 46 Abbasia	47	42		

Zone	Tehsils	Villages	Equivalent Noise Level		PEQS Limit	
			(Leq) dB(A)		dB(A)	
			Day Time	Night Time	Day Time	Night Time
		Chak 09 Abbasia	47	42		
		Chak 88 Abbasia	46	42		
	Rojhan	Bhagsar	46	45		
South-II	Alipur	Nawan Dera	53.6	46.6		
		Tibba Burrah	56.9	45.3		
	Shujabad	Sangri	54.5	45.4		
		Sarai	53.4	46.4		
South-III	Kahror Pacca	Sharak Wah	52	38		
		Humble Wala	49	41		
		Kotla Narangan	53	38		
	Khairpur Tamewali	Piru Joiya	55	40		
		Dhaddi	51	35		
		Thali Talbani	50	36		
		Tibbi Ghafar baksh.	55	33		
		Jhoklal	48	33		
	Bahawalnagar	MP, SW	51	39		
		Shera Chitra	54	37		

The results of the noise monitoring conducted indicate that none of the readings obtained from any of the villages exceeded the prescribed noise limits as set forth by the Punjab Environmental Quality Standards except Chak 08 /SB Kot raja and Baraham wala of Tehsil Kot Momin.

C. Wastewater Quality

Wastewater samples were collected and was analyzed. The analysis results of wastewater samples are compared with PEQS. The detailed monitored results for wastewater quality are given in **Table 18**. Detailed results of wastewater monitoring are provided at Annex-11.

Table 19: Results of Wastewater

Sr. No.	Parameters		pH	COD	BOD	TSS	Oil & Grease
	Unit		-	mg/L	mg/L	mg/L	mg/L
	PEQS		06-Sep	150	80	200	10
1	Kot Momin	Chak 08 /SB Kot raja	7.815 at 24.2	214	112	452	BDL
		Baraham wala	7.79	270	135	355	BDL
2	Ahmadpur Sial	Ahmad Pur Sial	7.6	278	144	566	3.2
3	Bhawana	Bhawana	7.8	148	68	98	2.2
4	Darya Khan	Darya Khan	7.7	410	276	432	4
5	Pakpattan	Pakpattan	7.55	660	288	176	5.5
6	Liaqatpur	Chak 46 Abbasia	7.4	321	170	36	3.5
		Chak 09 Abbasia	7.81	519	278	623	8
		Chak 88 Abbasia	6.57	2010	1075	934	9.5
7	Rojhan	Bhagsar	8.36	216	116	24	5.3
8	Alipur	Baqar Shah Shumali	7.27	480	231	280	3.6
		Bande Shah	6.84	278	130	167	4.8
		Maqwal Hadeir	7.08	422	187	221	9.6
		Nehal Wala	6.68	362	118	340	7.2
		Khayara	6.68	362	118	340	7.2
		Mithan Wali	7.63	910	398	320	2.4
		Ali Wali	6.46	248	109	540	3.6
9	Shujabad	Wahi Riki	7.3	344	154	47	3.6
		Basti Dad	7.17	1122	488	360	2.4
		Chah Miran Khan	7.03	75	40	89	2.4
		Nawan Chak	6.9	1030	460	240	9.6
		Mohan Pur Sharqi	6.95	532	242	147	3.6
		Sangrai	7.44	143	68	79	8.4
		Shahpur Ubha	6.99	94	41	147	6
		Parhar	7.05	244	104	212	6
		Halal Waja	7.16	966	402	108	4.8
		Sarai	6.99	80	29	784	4.8
		Shah Pur Shumali	6.82	401	182	575	4.8
		Nasir Pur	7.04	1017	436	102	7.2
10	Kahror Pacca	Kahror Pakka	7.6	188	88	88	2.5
11	Khairpur Tamewali	Khairpur Tame wali	7.45	178	96	94	1.8
12	Bahawalnagar	Bahawalnagar	7.7	490	248	568	4.8

The collected samples of wastewater are not representative, as they are spot samples taken from open drains and channels. However, the analysis of the wastewater samples indicates that the levels of biological oxygen demand (BOD), chemical oxygen demand (COD), and total suspended solids (TSS) in most of the samples are higher than the limits established in the Punjab Environmental Quality Standards (PEQS). To meet the PEQS requirements, a potential solution is to utilize an Anaerobic Baffled Reactor (ABR) for wastewater treatment, which can readily ensure compliance with these standards.

Environmental Monitoring report can be accessed through the link provided below:

https://drive.google.com/drive/folders/1Xka-OzxfVziSpqu36cMHgvT1L8i0LvLr

4.3.6 Seismology

All tehsils of the project area fall within zone 2A and zone 2B according to the zoning developed by Government of Pakistan. Figure 4 shows the seismic zoning map of Pakistan.

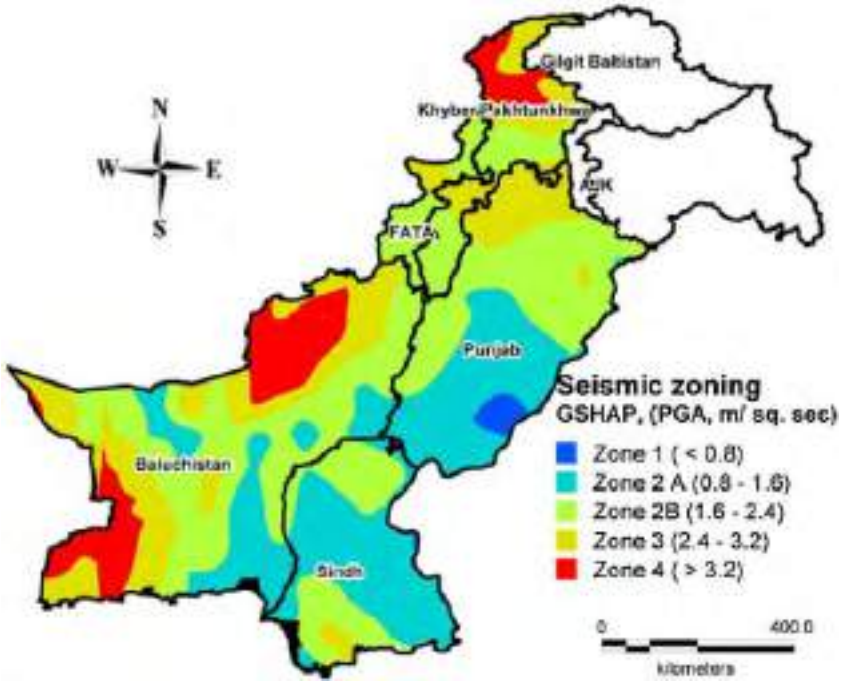

Figure 6: Seismic Zone Map of Project Area

4.4 Sensitive Receptors

Village wise sensitive receptors are identified in the table 19 below:

Table 20: Sensitive Receptors

Phase	Tehsil	Village Name		Schools	Mosques	Hospital / Clinic / BHU	Graveyard	Minority Graveyard	Minority Religious Places	Shrines	Other
Phase -II	Kot Momin	Chak 08 /SB Kot raja		3	2	-	-	-	-	-	-
		Baraham wala		-	1	-	-	-	-	-	-
		Bahar wala		-	1	-		-	-	-	-
		Dhudyan		-	1	-	1	-	-	-	-
		Tridianwala		1	1	-	1	-	-	-	1
		Bhakhi khurd		1	2	-	-	-	-	-	-
		Bakh Daim	Settelment -1	2	4	-	2	-	-	-	1 imam bargah
			Settelment -2								
		Murad wala	Settelment -1	1	3	-	1	-	-	-	1 imam bargah
			Settelment -2								
			Settelment -3								
			Settelment -4								
		Dhingrala		1	1	-	-	-	-	-	1
		Dhingrawali		3	2	-	4	-	-	-	-
	Ahmadpur Sial	Chak No.1/2-L		1	2	-	-	-	-	-	-
		Chak No.3/2-L		1	1	-	-	-	-	-	-
		Jhok Dargahi Shah		2	2	-	-	-	-	-	-
		Chak No.4/3-L		1	1	-	1	-	-	-	-
		Jhainder Niazi		-	3	-	-	-	-	-	-
		Basti Lal		1	-	-	-	-	-	-	-
		Chak 13/3-L		1	1	-	-	-	-	-	-
		Chak No.2/4-R		1	2	-	-	-	-	-	-
		Chak No.3/3-L		2	2	-	-	-	-	-	-
		Basti Wali Muhammad Jandir		2	2	-	-	-	-	-	-
		Bela Badh		1	2	-	-	-	-	-	-
		Bhid Wal		-	1	-	-	-	-	-	-
		Chak No.1/3-R		1	1	-	-	-	-	1	-
		Laghari		1	5	-	-	-	-	-	-
		Wahgah		-	1	-	-	-	-	-	-
		Detisial		-	2	-	-	-	-	-	-
	Bhawana	Chak 248 JB		1	2	-	-	-	-	-	-
		Kamoke		1	2	-	-	-	-	-	-

Phase	Tehsil	Village Name	Schools	Mosques	Hospital / Clinic / BHU	Graveyard	Minority Graveyard	Minority Religious Places	Shrines	Other
		Kotla Shahzada	1	3	-	-	-	-	-	-
		Maral Wala	1	2	-	-	-	-	-	-
		Saghar Wala	4	3	-	-	-	-	-	-
		Thatta Kundal	1	3	-	-	-	-	-	-
		Thatta Rasalu	2	1	-	-	-	-	-	-
		Fateh Kot Taja	1	2	-	-	-	-	-	-
		Saike Saloke	2	3	-	-	-	-	-	-
		Abhulke	-	1	-	-	-	-	-	-
		Malake Rajoke	-	1	-	-	-	-	-	-
		Nahre Hrseh	1	1	-	-	-	-	-	-
		Kot Sahib	-	1	-	-	-	-	-	-
		Mehroke	-	1	-	-	-	-	-	-
		Thatta Viroka	-	1	-	-	-	-	-	-
	Darya Khan	Chak No.177/T.D.A	2	3	-	1	-	-	-	-
		Chak No.53-M.L	2	2	-	-	-	-	-	-
		Chak No.1 Rakh Dala	2	-	-	1	-	-	-	-
		Karar Noon	3	3	-	-	-	-	-	-
		Bilochan Wali	1	3	-	-	-	-	-	-
		Chak No.51/M.L	1	1	-	-	-	-	-	-
		Chak No.176/T.D.A	2	3	-	-	-	-	1	-
		Chak No.50-M.L	1	1	-	-	-	-	-	-
		Chak No.54-M.L	1	2	-	-	-	-	-	-
		Surani Nasheb	1	3	-	-	-	-	-	-
		Daggar Qureshi Janub Gharbi	2	2	-	-	-	-	-	-
		Chak No.5 Rakh Dallo Wala	2	1	-	1	-	-	-	-
		Dulle Wala No.1	2	2	-	-	-	-	-	-
		Chak No.2 Rakh Dala	1	1	-	-	-	-	-	-
		Chak No.3 Rakh Dala	2	1	-	-	-	-	-	-
		Chak No.4 Rakh Dala	3	1	-	-	-	-	-	-
		Gadai No.2	3	1	-	-	-	-	-	-
		Chak No.12-A/TDA	2	2	-	-	-	-	-	-
	Pakpattan	Chak No.102/D	3	1	-	1	-	-	-	-
		Bahwan Shah	1	2	-	-	-	-	-	-
		Chak Ilahi Bux	2	1	-	1	-	-	-	-
		Chak Murad Khan	1	-	-	-	-	-	-	-

Phase	Tehsil	Village Name	Schools	Mosques	Hospital / Clinic / BHU	Graveyard	Minority Graveyard	Minority Religious Places	Shrines	Other
		Chak Nazam Din	1	3	-	1	-	-	-	-
		Gobind Pur Bahmni	-	1	-	1	-	-	-	-
		Jand Wala	2	1	-	1	-	-	-	-
		Nahla Abad	1	3	-	1	-	-	-	-
		Dhamiana	1	2	-	1	-	-	-	-
		Chak No.4 S.P.	2	3	-	-	-	-	-	-
		Chak Quder Tullah	1	1	-	-	-	-	-	-
		Chilli Mamdana	-	2	-	-	-	-	-	-
		Dada Ahluka	1	2	-	1	-	-	-	-
		Ghar Taj	1	-	-	1	-	-	-	-
		Ghazi Mardan	1	3	-	-	-	-	-	-
		Arazi Tek Chand	1	2	-	-	-	-	-	-
		Ghuri	2	1	-	1	-	-	-	-
		Rakh Ferozpur	1	1	-	-	-	-	-	-
		Wara Piran Kalan	-	1	-	-	-	-	-	-
		Kala Chishti	2	3	-	1	-	-	-	-
		Khamam Doggar	-	3	-	1	-	-	2	-
		Chak No.12 K.B.	1	1	-	-	-	-	-	-
		Musteqim Mamunka	1	1	-	1	-	-	1	-
		Malik Rahmun	-	2	-	-	-	-	-	-
		Amira Ahluka	-	1	-	-	-	-	-	-
		Alam Mehteka	2	2	-	-	-	-	1	-
		Chhinah	-	1	-	-	-	-	-	-
		Maneke	-	4	-	-	-	-	-	-
		Jalil Mehteka	1	1	-	-	-	-	-	-
		Khatwan	-	1	-	1	-	-	-	-
		Faiz Pur	1	3	-	1	-	-	1	-
		Talibali	1	1	-	-	-	-	-	-
		Jamal Pur Tahli	1	1	-	1	-	-	-	-
		Chak Wasao	1	1	-	1	-	-	1	-
		Chak No.105.D	1	-	-	-	-	-	-	-
		Chak No.104/D	-	1	-	-	-	-	-	-
		Chak No.100/D	-	2	-	1	-	-	1	-
		Chak No.88/D	1	1	-	1	-	-	1	-
		Bablana	-	3	-	1	-	-	1	-
		Bahdar Khara	1	1	-	-	-	-	-	-

Phase	Tehsil	Village Name	Schools	Mosques	Hospital / Clinic / BHU	Graveyard	Minority Graveyard	Minority Religious Places	Shrines	Other
		Bahmani	2	2	-	-	-	-	-	-
		Bonga Amam Din	-	1	-	1	-	-	-	-
		Bonga Shamis	1	2	-	1	-	-	-	-
		Chak No.91/D	1	1	-	-	-	-	-	-
		Chak Waso Kamboh	-	2	-	-	-	-	-	-
		Kirparam	1	1	-	-	-	-	-	-
		Lakh Wira	2	3	-	1	-	-	1	-
		Magan Pur	1	2	-	1	-	-	1	-
		Nabi Bakish	-	1	-	-	-	-	-	-
		Saleem Shah Bodla	2	2	-	-	-	-	-	-
		Chak No.106.D	2	2	-	-	-	-	-	-
		Wara Peran Khurd	-	1	-	-	-	-	-	-
		Chak No.101/D	-	1	-	-	-	-	-	-
	Liaqatpur	Ahmed Ali Lar	1	5	-	-	-	-	-	-
		Allah Dita Bhela	2	5	-	1	-	-	-	-
		Allah Jiwaya Lar	1	7	-	-	-	-	-	-
		Ashraf Shah	-	5	-	1	-	-	-	-
		Bahan Wala	3	8	-	1	-	-	-	-
		Bahar Khaki	2	9	-	-	-	-	-	-
		Chak No. 116 NP	2	-	-	-	-	-	-	-
		Chak No. 116-A-NP	-	1	-	-	-	-	-	-
		Chak No. 117 NP	-	3	-	-	-	-	-	-
		Chak No. 118 NP	-	2	-	-	-	-	-	-
		Chak No. 119 NP	1	11	-	2	-	-	1	-
		Chak No.119-A- NP	-	1	-	-	-	-	-	-
		Chak No. 120 NP	-	1	-	-	-	-	-	'
		Chak No. 121 NP	-	1	-	-	-	-	-	-
		Chak No. 122 NP	2	1	-	1	-	-	-	-
		Chak No. 123 NP	1	1	-	-	-	-	-	-
		Chak No. 124 NP	1	-	-	-	-	-	-	-
		Chak No. 125 NP	3	2	-	2	-	-	-	-
		Chak No. 126 NP	-	1	-	-	-	-	-	-
		Chak No. 127 NP	1	3	-	-	-	-	-	-
		Chak No. 128 NP	-	1	-	-	-	-	-	-
		Chak No. 129 NP	1	3	-	-	-	-	-	-

Phase	Tehsil	Village Name	Schools	Mosques	Hospital / Clinic / BHU	Graveyard	Minority Graveyard	Minority Religious Places	Shrines	Other
		Chak No. 130 NP	-	1	-	-	-	-	-	-
		Chak No. 131 NP	2	4	-	1	-	-	-	-
		Chak No. 132 NP	1	-	-	-	-	-	-	-
		Chak No. 133 NP	-	1	-	-	-	-	-	-
		Chak No. 137 NP	-	1	-	-	-	-	-	-
		Chak No. 138 NP	1	1	-	-	-	-	-	-
		Chak No. 34 Abbasia	2	3	-	-	-	-	-	-
		Chak No. 35 Abbasia	4	9	-	2	-	-	-	-
		Chanjni	2	8	-	1	-	-	-	Eidgah
		Chohan	2	6	-	1	-	-	-	-
		Choudari	7	21	-	-	-	-	-	-
		Chur Wala	2	1	-	-	-	-	-	-
		Duda Naich	1	3	-	-	-	-	-	-
		Gabrani	3	6	1	-	-	-	-	-
		Gharib Shah	1	11	-	-	-	-	-	-
		Ghemi	4	10	-	2	-	-	1	-
		Ghuka	-	4	-	1	-	-	-	-
		Goth Amin	3	10	-	1	-	-	-	-
		Goth Hayat	7	11	-	2	-	-	-	-
		Goth Mahi	-	2	-	1	-	-	-	-
		Gous Abad	2	6	-	-	-	-	-	-
		Gul Muhammad Lar	3	15	-	-	-	-	-	-
		Gulani	4	14	-	1	-	-	-	-
		Haroon Abad	2	8	-	1	-	-	-	Eidgah
		Hussain Abad	-	1	-	-	-	-	-	-
		Jhoung Bilawal	4	5	-	1	-	-	-	-
		Juma Muhana	1	5	-	3	-	-	-	-
		Kandani	2	11	-	-	-	-	-	-
		Kotla Daulat	6	25	1	1	-	-	-	Eidgah & Madrsa
		Kotla Mubarik	1	9	-	1	-	-	-	-

Phase	Tehsil	Village Name	Schools	Mosques	Hospital / Clinic / BHU	Graveyard	Minority Graveyard	Minority Religious Places	Shrines	Other
		Kotla Nawab	6	13	-	5	-	-	-	-
		Kotla Niazi	2	12	-	2	-	-	-	-
		Lakhani	3	10	-	1	-	-	-	-
		Lal Shah	1	5	-	-	-	-	-	-
		Laoon Wala	3	7	-	-	-	-	-	Madrasa
		Malhani	3	9	-	2	-	-	-	Madrasa
		Malikpur	-	1	-	-	-	-	-	-
		Malkani	1	16	-	4	-	-	-	-
		Metla	2	4	2	1	-	-	-	Eidgah
		Mir Muhammad Lar	2	4	-	-	-	-	-	-
		Muhammad Daha	1	11	-	-	-	-	-	-
		Mujawraan	4	13	-	-	-	-	-	-
		Nala Musani	4	5	-	2	-	-	-	-
		Pakhi War	4	7	-	5	-	-	-	Madrasa
		Pararan Sharif	4	12	-	2	-	-	-	Madrasa
		Qadu Wali	4	16	-	3	-	-	-	-
		Rais Pathan	2	12	-	5	-	-	-	Madrasa
		Rashid Abad	1	2	-	-	-	-	-	-
		Rindan	8	7	-	2	-	-	-	-
		Sadiqpur	-	1	-	-	-	-	-	-
		Saidpur	2	4	-	-	-	-	-	Madrasa
		Shahbazpur Gharbi	1	2	-	1	-	-	-	-
		Shamsabad	2	5	-	1	-	-	1	-
		Shidani Sharif	3	24	-	6	-	-	-	-
		Talbani	7	25	-	5	-	-	-	-
		Tanwari	5	11	-	-	-	-	-	Eidgah
		Trinda Mir Khan	5	23	1	2	-	-	-	-
		Ther Posti	1	5	-	1	-	-	-	-

Phase	Tehsil	Village Name	Schools	Mosques	Hospital / Clinic / BHU	Graveyard	Minority Graveyard	Minority Religious Places	Shrines	Other
		Tibbi Sayyadan	2	15	-	2	-	-	-	-
		Wahid Bux Sial	5	8	-	-	-	-	-	-
		Yakhtar Maha	-	3	-	-	-	-	-	-
		Zaffar Abad	2	9	-	-	-	-	-	-
		Unran	1	6	-	-	-	-	-	-
	Rojhan	Badli	-	1	-	-	-	-	-	-
		Badli Chak Ladh	1	5	-	3	-	-	-	-
		Basti Nikka	-	1	-	-	-	-	-	-
		Chak Dim	-	2	-	-	-	-	-	-
		Chak Kariya	3	6	-	2	-	-	-	-
		Chak Mut-1	-	6	2	-	-	-	-	-
		Chak Mut-2	1	6	2	1	-	-	-	-
		Dera Dildar	5	3	-	3	-	-	-	Madrsa
		Dera Jewan Khas	1	2	-	-	-	-	-	-
		Garhi Soori	3	8	-	-	-	-	-	-
		Kaheeri	3	-	-	-	-	-	-	-
		Kin Khas	5	18	1	1	-	-	-	Madrsa
		Kotla Gulsher	2	9	-	-	-	-	-	-
		Kotla Hasan Jamra	-	3	-	-	-	-	-	-
		Rakh Kotla Hasan Jamra	-	-	-	-	-	-	-	-
		Lutairi	1	-	-	-	-	-	-	-
		Miranpur	3	4	-	1	-	-	-	-
		Patti Shah Wali	-	-	-	-	-	-	-	-
		Shah Wali	2	21	2	3	-	-	-	Imam-Bargah
		Solangi	-	2	-	-	-	-	-	-
		Wah Machka	8	14	-	2	-	-	-	-
	Shujabad	Agar Khani	3	2	-	1	-	-	1	-
		Amanullah Pur	1	2	-	-	-	-	-	-
		Bagrain	2	5	1	1	-	-	-	-
		Basti Chhaju Shah	-	2	-	-	-	-	-	-
		Bhana	-	3	-	1	-	-	-	1 (Dispensery)
		Chak Jakhar	2	8	-	1	-	-	1	-

Phase	Tehsil	Village Name	Schools	Mosques	Hospital / Clinic / BHU	Graveyard	Minority Graveyard	Minority Religious Places	Shrines	Other
		Chak No 13/F	1	3	-	-	-	-	-	-
		Chak Rs	6	7	-	1	-	-	1	-
		Choti	3	3	-	1	-	-	-	-
		Dairapur	1	1	-	-	-	-	-	-
		Dera Arvi	3	2	-	-	-	-	-	-
		Dhondo	2	4	-	1	-	-	1	-
		Gunwen	5	7	-	-	-	-	-	-
		Jai	-	3	-	-	-	-	-	-
		Jhangi	1	3	-	-	-	-	-	1 Eid Gah
		Kaser Pur	2	3	-	-	-	-	2	-
		Khalar	-	3	-	-	-	-	-	-
		Khanpur	2	4	-	-	-	-	-	2 Mudarasa
		Khas Punjani	-	2	-	-	-	-	-	1Mudarasa
		Kotli Najabat	6	6	-	-	-	-	-	3 Mudarasa
		Lasoorhi	1	1	-	-	-	-	-	-
		Lutf Pur	-	2	-	-	-	-	-	1 Mudarasa
		Mahara	-	1	-	-	-	-	-	1 Mudarasa
		Mochi Pura	2	3	1	-	-	-	-	-
		Mohan Pur Gharbi	-	1	-	-	-	-	-	-
		Pounta	1	4	-	1	-	-	-	-
		Punjani	4	6	1	1	-	-	1	3 Mudarasa
		Raja Raam	5	5	-	-	-	-	-	-
		Rasool Pur Janubi	-	2	-	-	-	-	-	1 Mudarasa
		Rasool Pur Shumali	1	4	-	-	-	-	-	-
		Rukan Hatti	1	3	-	-	-	-	-	1 Emam-Bargah
		Sat Burji	-	2	-	-	-	-	-	1 Mudarasa
		Seri	1	1	-	-	-	-	-	-
		Shah Musa	-	3	-	-	-	-	-	-
		Sheikhpur Shajra	1	2	-	-	-	-	-	1 Mudarasa
		Soman	2	2	-	1	-	-	-	-
		Tahir Pur	1	1	-	-	-	-	-	-
		Thath Galawan Junabi	1	2	-	-	-	-	-	1 Mudarasa
		Thatha Makhdoom Pur	1	3	-	-	-	-	-	1 Mudarasa
		Tudar Pur	1	1	-	-	-	-	-	1 Mudarasa
		Vainus	2	3	-	-	-	-	-	-

Phase	Tehsil	Village Name	Schools	Mosques	Hospital / Clinic / BHU	Graveyard	Minority Graveyard	Minority Religious Places	Shrines	Other
		Wahi Bhakar	1	1	-	1	-	-	-	1 Mudarasa
		Wai Sawaya	2	2	-	1	-	-	-	-
		Taror Jalalpur	-	3	-	-	-	-	-	-
	Alipur	Amir Pur Daha	-	1	-	-	-	-	-	-
		Baqar Shah Janubi	-	1	-	-	-	-	-	-
		Basti Haji	-	1	-	-	-	-	-	-
		Baz Wala	1	5	-	1	-	-	-	1 Mudarasa
		Bet Channa	1	4	-	-	-	-	-	-
		Bet Dewan Shah	-	1	-	-	-	-	1	-
		Bet Muiziddin	2	4	-	-	-	-	-	-
		Chak Dada	-	2	-	-	-	-	-	-
		Chak Daud Wala	-	1	-	-	-	-	-	1 Mudarasa
		Dahaka	1	2	-	-	-	-	-	-
		Damar Wala Janubi 1	1	3	-	-	-	-	1	-
		Damar Wala Janubi 2	2	4	-	-	-	-	-	1 Imam Bargah
		Daulut Pur	-	3	-	-	-	-	-	1 Mudarasa
		Fateh Pur Janubi 1	-	5	-	-	-	-	-	1 Imam Bargah
		Fateh Pur Janubi 2	2	2	-	-	-	-	-	1 Mudarasa
		Ghalwan 1	3	3	-	-	-	-	-	1 Mudarasa
		Ghalwan 2	1	3	-	1	-	-	1	-
		Ghari	2	4	-	1	-	-	-	-
		Kachi Lal	2	8	-	-	-	-	-	3 Mudarasa
		Khair Pur Para	1	3	-	1	-	-	-	-
		Khair Pur Sadat	8	7	-	-	-	-	-	3 Mudarasa
		Khan Pur Nahrka	1	1	-	-	-	-	-	-
		Khanani	1	3	-	-	-	-	-	1 Imam Bargah
		Khangarh Donma	1	4	-	1	-	-	-	-
		Kundai	1	3	-	-	-	-	-	1 Imam Bargah
		Kundrala	1	2	-	-	-	-	-	-
		Latti	1	2	1	-	-	-	-	1 Mudarasa
		Madd Sohanyara Shah	1	4	-	-	-	-	-	-
		Malik Arain	1	3	-	-	-	-	-	1 Mudarasa
		Misan Kot Behwa	2	1	-	-	-	-	-	-
		Mohib Shah	-	1	-	-	-	-	-	1 Mudarasa

Phase	Tehsil	Village Name	Schools	Mosques	Hospital / Clinic / BHU	Graveyard	Minority Graveyard	Minority Religious Places	Shrines	Other
		Mud Wala	3	2	-	-	-	-	-	-
		Mutfarqa	-	-	-	-	-	-	-	-
		Nussrat Pur	-	1	-	-	-	-	-	-
		Pakka Naich	1	6	-	1	-	-	-	-
		Phullan	2	4	-	-	-	-	-	2 Mudarasa
		Rakh Khanani	1	2	-	-	-	-	-	1 Imam Bargah
		Shah Wasava	2	3	-	-	-	-	-	1 Mudarasa
		Sheikhani	3	4	-	1	-	-	1	1 Imam Bargah
		Sultan Pur	2	3	-	1	-	-	1	-
		Tibi Arian	-	5	-	-	-	-	-	1 Imam Bargah
		Walwat	-	1	-	1	-	-	-	1 Mudarasa
	Kahror Pacca	Basti Lal	-	1	-	-	-	-	-	-
		Chak Qadirpur	1	6	-	1	-	-	-	-
		Dera Dilawar	-	11	1	2	-	-	1	-
		Kotkora Jhanda	-	7	-	1	-	-	1	-
		Arah	1	3	-	-	-	-	-	-
		Chak Allah Rakha Khan	-	1	-	1	-	-	-	-
		Dhorah Mahar	1	1	-	-	-	-	-	-
		Gopal Pur	1	4	-	1	-	-	1	-
		Gul Pur	-	-	-	-	-	-	-	-
		Bhinda Gerdan	-	1	-	-	-	-	1	-
		Chak Muhammad Murad	4	5	-	-	-	-	-	-
		19/M	1	3	-	1	-	-	1	-
		21/M	-	1	-	-	-	-	-	-
		30/M	2	4	-	-	-	-	-	-
		Kand Ahmed Asar	2	3	-	-	-	-	-	-
		Murshad Pur	1	3	-	-	-	-	-	-
		22M	1	3	-	1	-	-	1	-
		Chak Choki Kohna	2	4	-	-	-	-	-	-
		Hassa Joya	1	2	-	-	-	-	-	-
	Khairpur Tamewali	Fazlu Kukara	1	5	-	-	-	-	-	-
		Khairi Bhabhi	-	2	-	1	-	-	1	-
		Kotla Mahi	1	3	-	-	-	-	-	-

Phase	Tehsil	Village Name	Schools	Mosques	Hospital / Clinic / BHU	Graveyard	Minority Graveyard	Minority Religious Places	Shrines	Other
		Ladar	-	2	-	-	-	-	1	-
		Mamdu Mangero	1	2	-	-	-	-	-	-
		Bunga Yarani	1	1	-	-	-	-	-	-
		Darud Garan	1	3	-	-	-	-	-	-
		Goth Ali	1	4	-	1	-	-	-	-
		Gith Kamal	-	1	-	-	-	-	-	-
		Kamalia	2	2	-	1	-	1	-	-
		Ahmed Milkhi	1	4	-	-	-	-	-	-
		Amin Fatani	-	3	-	-	-	-	-	-
		Baghban	-	4	-	-	-	-	-	-
		Binda Chadhran	1	1	-	-	-	-	1	-
		Kharal Nau Baramad	-	1	-	-	-	-	-	-
		Chak No. 26	-	1	-	-	-	-	-	-
		Dharala Randu	-	3	-	-	-	-	-	-
		Haleem	-	3	-	-	-	-	1	-
		Khanan Arain	1	3	-	-	-	-	1	-
		Chak No. 24 Sharaf Shah	2	7	-	3	-	-	2	-
		Khuda Bux Seyal	2	2	-	-	-	-	1	-
		Kotla Qaim Khan	2	5	1	2	-	-	1	-
		Lal Sohanra	-	4	-	-	-	-	-	-
		Luthran	1	3	-	1	-	-	-	-
		Mehti	-	2	-	1	-	-	-	-
		Mohammad Sharif	1	1	-	1	-	-	-	-
		Muhammad Khan	-	4	-	-	-	-	-	-
		Mungrani	-	2	-	-	-	-	1	-
		Muradpur	1	2	-	2	-	-	-	-
		Muradpur Dhrala	1	4	-	1	-	-	-	-
		Nurrey	1	5	-	-	-	-	-	-
		Qazi Kalra	3	1	-	-	-	-	-	-
		Raja	-	4	-	-	-	-	-	-
		Rameli	1	5	-	1	-	-	1	-
		Rukrani	1	4	-	1	-	-	1	-
		Sardar Pur	2	4	-	1	-	-	-	-
		Azimpura	3	1	-	-	-	-	1	-
		Noor Mohd Khan	-	1	-	-	-	-	1	-

Phase	Tehsil	Village Name	Schools	Mosques	Hospital / Clinic / BHU	Graveyard	Minority Graveyard	Minority Religious Places	Shrines	Other
		Gaman Wagi	-	4	-	-	-	-	-	-
		Gawains	-	3	-	-	-	-	-	-
		Goth Jhumar	1	3	-	1	-	-	-	-
		Khairpur	1	5	-	-	-	-	-	-
	Bahawalnagar	Bonga Ihsan Bibi	1	3	-	-	-	-	-	-
		Hasan Raika	1	1	-	-	-	-	-	-
		Abrerah Uttar	1	1	-	-	-	-	-	-
		Amin Abad	1	3	-	-	-	-	-	-
		Boole Shah Hitthar	-	1	-	1	-	-	-	-
		Ramnagar	1	1	-	1	-	-	-	-
		Paran Wala	1	2	-	1	-	-	-	-
		Hussian Abad Hithar	1	1	-	-	-	-	-	-
		Hussian Abad Uttar	1	1	-	-	-	-	-	-
		Chak Abdul Haq	1	1	-	1	-	-	-	-
		Dhanraj Pura	1	2	-	1	-	-	-	-
		Ali Goher No. 326	1	1	-	-	-	-	-	-
		Jagga Sanatteka	1	4	-	1	-	-	-	-
		Mina Sanatteka	1	1	-	-	-	-	-	-
		Sharaf Din	-	1	-	-	-	-	-	-
		Mosla	-	1	-	-	-	-	-	-
		Pir Sikandar Otar	-	1	-	1	-	-	-	-
		Jhulan Chishtian	1	1	-	-	-	-	1	-
		Gauspur	1	1	-	-	-	-	-	-
		Gaman Dongi	-	1	-	-	-	-	-	-
		Akkanwali Khurd	-	1	-	-	-	-	-	-
		Kartar Singh	1	3	-	-	-	-	-	-
		Khawaja Bux Bodla	2	3	-	1	-	-	-	-
		Faqir Shah	1	1	-	1	-	-	-	-
		Khober	1	1	-	1	-	-	1	-
		Ramzan Shah	1	1	-	-	-	-	-	-
		Allahabad	-	2	-	-	-	-	-	-
		Muhammad Asad Khan	1	-	-	-	-	-	-	-
		Janoowala	1	1	-	1	-	-	1	-
		Tobi Qamar-Ud-Din	-	1	-	-	-	-	-	-
		Malak Pura	1	2	-	-	-	-	-	-
		Jalwala	1	1	-	-	-	-	-	-

Phase	Tehsil	Village Name	Schools	Mosques	Hospital / Clinic / BHU	Graveyard	Minority Graveyard	Minority Religious Places	Shrines	Other
		Dara Sanatteka	1	1	-	1	-	-	-	-
		Hira Bashnoai	1	1	-	1	-	-	1	-
		Sandar Bashnoi	1	1	-	-	-	-	-	-
		Sher Singh Wala	1	1	-	1	-	-	-	-
		Barasajwar Khan	1	1	-	1	-	-	-	-
		Noor Jahanian	2	1	-	-	-	-	-	-
		Dadoo Mammunka	1	1	-	-	-	-	-	-
		Bhole Shah Utar	1	1	-	1	-	-	1	-
		Abrerah Hitthar	-	1	-	-	-	-	-	-
		Bilara Nabi Bux	-	1	-	-	-	-	-	-
		Bilara Qasim Khan	1	-	-	1	-	-	-	-
		Madarsa	1	1	-	-	-	-	1	-
		Pir Shah	-	2	-	-	-	-	-	-
		Kakku Bodla	1	3	-	1	-	-	1	-
		Bhangran	-	1	-	-	-	-	-	-
		Khilowala	1	1	-	-	-	-	-	-
		Mamunka Hatar	2	2	-	-	-	-	-	-
		Muhsan Pura	1	2	-	-	-	-	-	-
		Beg Kanoor Pur	-	1	-	-	-	-	-	-
		Wara Piran	2	2	-	1	-	-	-	-
		Chaweka Hitthar	1	1	-	-	-	-	-	-
		Mamunka Uttar	1	1	-	1	-	-	-	-
		Dinpur Sharif	2	1	-	-	-	-	-	-
		Mari Mian Sahab Hithar	1	1	-	-	-	-	-	-
		Ramzan Langah	-	3	-	-	-	-	-	-
		Tughera Sharif	1	3	-	-	-	-	-	-
		Wilayat Pur	1	2	-	1	-	-	-	-
		Nanak Sar	2	2	-	-	-	-	-	-

Note: The socially sensitive receptors listed in the table above are within a radius of 100 meters of the execution of work. This distance of 100 meters has been taken as per screening checklist provided in ESMF and also validated through experiences of various EDCS Consultants.

4.5 Biological Environment

Project area is rich in biodiversity because of its diverse landscape and geographical location. The variety of ecosystem is evident and is home to various species. The following section describes the biological environment of the project area.

4.5.1 Flora

The major floral species found in the project area include the following:

Zone	Tehsils	Floral Species
North	Kot Momin	Kikar (*Acacia nilotica*), Tali (*Erythrophleum suaveolens*), Jaman (*Syzygium cumini*), Sufaida (*Eucalyptus camaldulensis*), Darek (*Melia Azedarach*), Poplar (*Populus alba*), Toot (*Morus alba*), Sharin (*Albizia lebbeck*), Bari (*Ziziphus mauritiana*), Simal (*Bombax cieba*), Orange Tree (*Citrus x sinensis*)
South-I	Liaqatpur	Kikar (*Acacia nilotica*). Neem (*Azadirachta indica*),Sheesham (*Dalbergia*),Khagi/ Ajwa Date Palm (*Phoenix dactylifera L.),* Sufaida (*Eucalyptus spp.*), Bari (*Ziziphus mauritiana*), Poplar (*Populus spp.*), Jaman (*Syzygium cumini*), Simal (*Bombax cieba*),
South-III	Bahawalnagar	*The Van (Salvadora oleoides), Karil (Capparis aphylla), Jand (Prosopis spicigera), Beri (Zizyphys jajaba),* mallha *(Zizyphus numularia)* and Shisham *(Dalbergia Sissoo)*
	Kahror Pakka	*The main crops are cotton and wheat, others include rice, sunflower and sugarcane. The main frits that are cultivated are citrus, mango and guava while the main vegetables are onion, tomato, potato and cauliflower. The lands in the sub- project area are fertile and farmers grow rice, fodder and vegetables during the Kharif season (April to November) and wheat, fodder and vegetables during Rabi season (April to October). Roadside plantations include kikar/farash (Tamarix aphylla), eucalyptus and the occasional, ornamental, bohr (Ficus bengalensis), as well as neem (Azadiracta indica), siris, ber, and bakain, which are commonly planted at farm houses*
	Khairpur Tamewali	Kikar (Acacia Nilotica), Frash (*Tamasix Aphylla*), Pillu (*Salvadora Oleoides*), Jand (*Prosopis Spicigera*), Karir (*Capparisaphylla*), Phog, Khar.
Central	Ahmadpur Sial	Jand trees (*Prosopis spicigera*), Karir (*Capparisaphylla*), Beri (*Zizyphus jajaba*), Van (*Salvadora abeoides*), Kikar (*Acacia arbica*), Shisham (*Dalbergia*), Aak (*Calotropois hamiltonit*), Kikar (*Acacia nilotica*), Eucalyptus (*Eucalyptus camaldulensis*), Jaman (*Syzygium cumini),* Sirris (*Albizzia lebbek*), Neem (*Azadiraccta indica*), Popular (*Salicaceae)*, Toot/Mulbery/Pilken (*Morus alba*), Beeri Patta (*Heterophragma adenophyllum*), Willow (*Salix babylonica*), Frash (*Tamarlx aphylia*), Simal (*Bombax cieba*) and Palm/Khajoor (*Phoenix dactiliferia*)
	Pakpattan	Sumbal (*Bombax ceiba*), Shesham (*Dalbergia sissoo*), Eucalyptus (*Eucalyptus globulus*), Kikar (*Acacia karoo*), Peepal (*Ficus religiosa*), Neem (*Azadirachta indica*), Poplar (*Populus*), Mulberries (*Morus rubra*), Beri (*Ziziphus mauritiana*), Peaches (*Prunus persica*) Guava (*Psidium guajava*), Sweet Lime (*Citrus Limetta*), Lime (*Citrus limon*), Date Palm (*Phoenix dactylifera*), Jaman (*Syzygium cumini*), Puth Kanda (*Achyranthes aspera*), Kharasan' thorn (*Fagonia cretica*), Stenotaphrum, Cyperus rotundus, Phalaris Minor, Sodom apple (*Calotropis procera*), Bathua (*Chenopodium album*)

Zone	Tehsils	Floral Species
	Darya Khan	Jand trees (*Prosopis spicigera*), Karir (*Capparisaphylla*), Beri (*Zizyphus jajaba*), Van (*Salvadora abeoides*), Kikar (*Acacia arbica*), Shisham (*Dalbergia*), Aak (*Calotropois hamiltonit*) Kikar (*Acacia* nilotica), Eucalyptus (*Eucalyptus camaldulensis*) Jaman (*Syzygium cumini*), Sirris (*Albizzia lebbek*), Neem (*Azadiraccta indica*), Popular (*Salicaceae*), Toot/Mulbery/Pilken (*Morus alba*), Beeri Patta (*Heterophragma adenophyllum*), Willow (*Salix babylonica*), Frash (*Tamarlx aphylia*), Simal (*Bombax cieba*) and Palm/Khajoor (*Phoenix dactiliferia*
	Bhawana	The vegetation in Tehsil Bhawana comprises a variety of native and commonly planted tree species. The dominant flora includes Jand (*Prosopis spicigera*), Karir (*Capparis aphyllA*), Beri (*Zizyphus jujaba*), Van (*Salvadora abeoides*), Kikar (*Acacia* arbica), *Shisham* (*Dalbergia*), Aak (*Calotropois hamiltonii*), Kikar (*Acacia nilotica*), Eucalyptus (*Eucalyptus camaldulensis*), Jaman (*Syzygium cumini*), Sirris (*Albizzia lebbek*), Neem (*Azadiraccta indica*), Popular (*Salicaceae*), Toot/Mulbery/Pilken (Morus *alba*), Beeri Patta (*Heterophragma adenophyllum*), Willow (*Salix babylonica*), Frash (*Tamarlx aphylia*), Simal (*Bombax cieba*) and Palm/Khajoor (*Phoenix dactiliferia*). These species are commonly found across agricultural fields, village landscapes, roadside plantation belts, and areas influenced by the Chenab River, contributing to the ecological diversity of the region.
South-II	Alipur	Kikar (*Acacia arabica*), Shisham (*Dalbergia sissoo*), Beri (*Ziziphus jujaba*), Toot/Mulberry (*Morus spp.*), Peeple (*Ficus religiosa*), Neem (*Melia indica*), Jand (*Prosopis spicigera*), Karir (*Capparis aphylla*) and Phulai (*Acacia modesta*)
	Shujabad	Jand (*Prosopis spicigera*), Karir (*Capparis aphylla*), Farash (*Tamarix articulata*), Kikar (*Acacia arabica*), Shisham (*Dalbergia sissoo*), Beri (*Ziziphus jujaba*), Toot/Mulberry (*Morus spp.*), Sirin (*Albizia lebbeck*), Neem (*Melia indica*), Peepal (*Ficus religiosa*), Date Palm (*Phoenix dactylifera*) and Poplar (*Populus euphratica*)

4.5.2 Fauna

The faunal species observed in the project areas were verified with the secondary data resources of the Punjab Forest, Wildlife and Fisheries Department and World Wildlife Fund (WWF). The species in vicinity include the following:

A. Mammals

Common animals found in the project area include wild cat, dogs, cats, jackals, Weasel, house rats, wild boar, bats, porcupine, bandicoot, soft furred rat and Indian gerbil. Domestic livestock observed during field visits include buffaloes, cattle, goats, sheep, and donkeys that are used by the local residents for their livelihood.

B. Amphibians

Bullfrog (*Hoplobatrachus tigernius*), Pahari tidda maindak (*Fejervarya limnocharis*), frog (rana tigrine) and Toad (Bufo bufo) are also present in the nearby ponds and canals during rainy season.

C. Birds

House sparrow (*Passer domesticus*), House crow (*Corvus splendens*) and Mynah (*Acredotheres tristis*) are the most common sight in the area. In addition, following birds are also seen in the project area**.**

Common Name	Scientific Name
Nightingale	*Pycnontus cafer*
Parrot	*Psittacula krameri*
Pigeon	*Columba livia*
Hoopoe	*Upupa epops*
Duck	*Anatidae*
Koel	*Eudynamys scolopacea*
Quail	*Coturnix coturnix*
Plover	*Charadriinae*
Black kite	*Mivus migrains*
Dove	*Columbidae*
Herons	*Ardeidae*
Mallard	*Anas platyrhynchos*
Gray Partridge	*Perdix perdix*
Black Partridge	*Melanoperdix niger*
Sandgrouse	*Pteroclidae*
Red wattled lapwing	*Vanellus indicus*
red-vented bulbul	*Pycnonotus cafer*
pewit	*Vanellus vanellus*
cuckoo	*Cuculidae*
jungle babbler	*Turdoides striata*

D. Reptiles

Common tree lizard (*Calotes versicolor*), Monitor lizard (*Varnus bengalensis*), fat tailed lizard (*Uromastix hardwickii*), fringed toed lizard (*Acanthodactylus cantoris*), Tortoise (Testudinidae), snakes (Serpentes), cobra (Naja) and Scorpions (Scorpiones) are observed in and around the proposed site. Saw-scale viper (Echis carinatus), Indian soft-shell turtle (*Aspideretes gangeticus*), striped keelback (Amphiesma stolatum) and Indian falpshell (*Lisseyms punctate andersoni*) are also reported by the local residents.

4.5.3 Endangered Species

There are no endangered species of flora and fauna observed in the Study Area.

4.5.4 Legally Protected Areas

The Government of Punjab through Punjab Legally Protected Areas act 2020 may declare an area to be called a protected area, with a specific name such as wetlands, national park, wildlife or game reserves. In order to provide for the protection, preservation, conservation and management of ecologically important areas.

A table indicating legally protected areas and other important ecological hotspots in different district of Punjab is attached below and the wetlands present in the district of the project areas are highlighted red and their distances from the project site is listed below.

Sr. No.	Name of Legally Protected Area	Status	District	Distance from nearest project village
1	Bajwat	Game Reserve	Sialkot	348 km
2	Ghamaghar Lake	Not Protected	Kasur	130 km
3	Head Islam	Game Reserve	Multan	80 km
4	Jahlar Lake	Not Protected	Khushab	103 km
5	Khabbaki Lake	Wildlife Sanctuary	Khushab	130 km
6	Kharrar (Kharal) Lake	Wildlife Sanctuary	Okara	80 km
7	Lal Suhanra (Patisar) Lake	National Park	Bahawalpur	105 km
8	Mangla Dam	Not Protected	Jhelum	145 km
9	Marala Headworks	Not Protected	Sailkot	230 km
10	Nammal Lake	Wildlife Sanctuary	Khushab	75 km
11	Qadirabad Barrage	Not Protected	Gujrawala	155 km
12	Qadirabad Link Canal	Game Reserve	Gujrat	145 km
13	Rasool (Rasul) Barrage	Wildlife Sanctuary	Gujrat	120 km
14	Soan River	Not Known	Chakwal	40 km
15	Taunsa Barrage	Wildlife Sanctuary	Muzaffargarh/DGK	45 km
16	Ucchali Lake	Ramsar Site	Khushab	90 km

As indicated from the above table, there are no legally protected areas in the area or in the influence of the project area. The nearest legally protected area is about 40 km away from the nearest project village. A map indicating wildlife sanctuaries and game reserve in different district of Punjab is attached below.

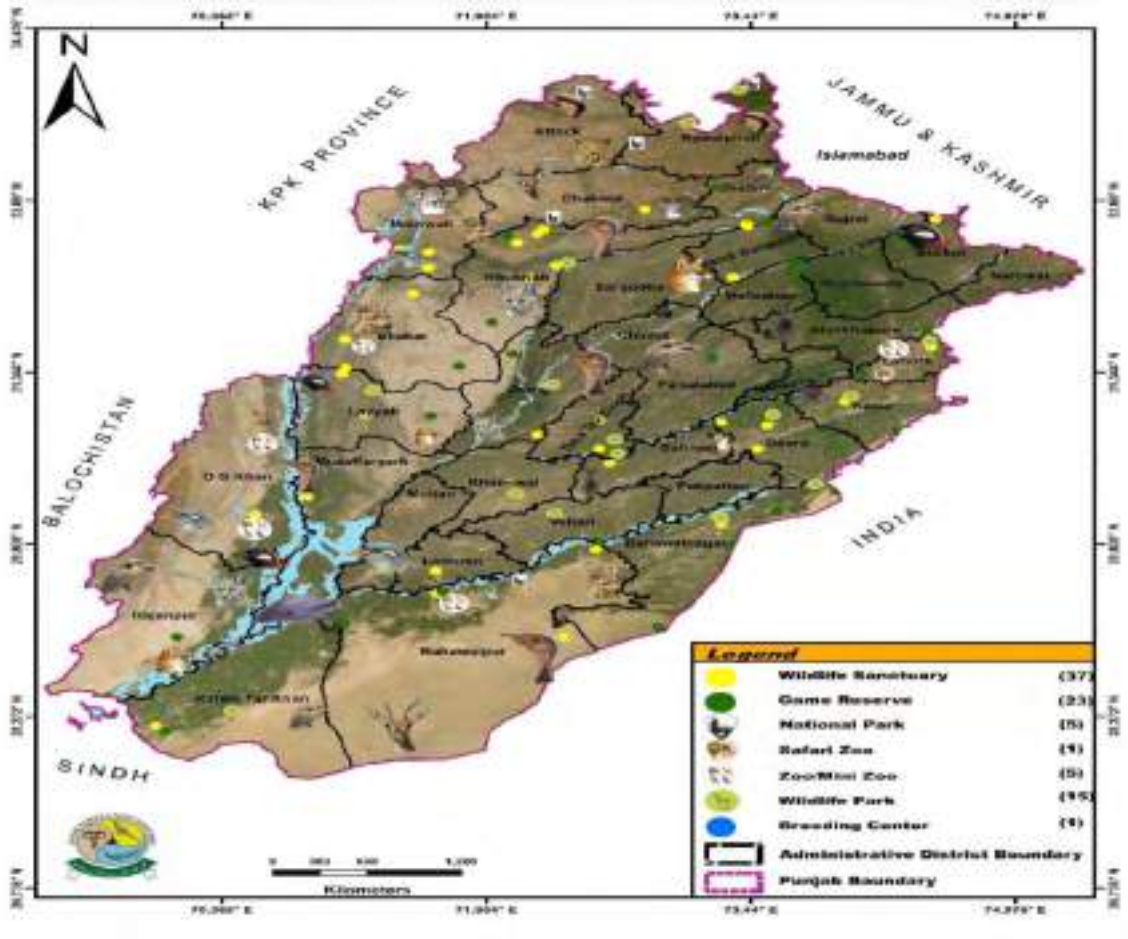

Figure 7: Wildlife Sanctuaries and Game Reserves

4.6 Socioeconomic Profile

4.6.1 Population Size

The project is expected to benefit about 1,478,678 households in the 425 villages. The average population size is 59,147 persons per village.

Table 21: Primary data results of Project Area

Sr. No	Zone	Tehsil	Villages		HH	M	F	Total
1	North	Kot Momin	Chak 08 /SB Kot raja		70	318	387	705
2			Baraham wala		60	208	240	448
3			Bahar wala		67	218	238	456
4			Dhudyan		67	315	299	614
5			Tridianwala		70	330	368	698
6			Bhakhi khurd		60	189	208	397
7			Bakh Daim	Settelment - 1	65	311	367	678
				Settelment - 2	60	270	328	598

Sr. No	Zone	Tehsil	Villages		HH	M	F	Total
8			Murad wala	Settelment - 1	35	182	184	366
				Settelment - 2	35	145	185	330
				Settelment - 3	35	206	160	366
				Settelment - 4	35	160	170	330
9			Dhingrala		30	150	156	306
10			Dhingrawali		50	209	217	426
11	Central	Ahmadpur Sial	Chak No.1/2-L		300	1170	830	2000
12			Chak No.3/2-L		300	4569	3431	8000
13			Jhok Dargahi Shah		300	156	144	500
14			Chak No.4/3-L		400	1260	1140	2400
15			Jhainder Niazi		400	1865	1635	3500
16			Basti Lal		150	1524	1476	3000
17			Chak 13/3-L		50	152	148	300
18			Chak No.2/4-R		150	1563	1437	3000
19			Chak No.3/3-L		200	1625	1375	3000
20			Basti Wali Muhammad Jandir		400	1367	1133	2500
21			Bela Badh		300	2563	2437	5000
22			Bhid Wal		85	452	398	850
23			Chak No.1/3-R		350	1635	865	2500
24			Laghari		200	1033	967	2000
25			Wahgah		150	1032	968	2000
26			Detisial		200	650	610	1260
27		Bhawana	Chak 248 Jb		120	756	744	1500
28			Kamoke		50	176	174	350
29			Kotla Shahzada		100	365	285	650
30			Maral Wala		400	1865	1635	3500
31			Saghar Wala		360	1155	685	1850
32			Thatta Kundal		55	194	156	350
33			Thatta Rasalu		227	1236	964	2200
34			Fateh Kot Taja		70	291	259	550
35			Abhulke		80	400	300	700
36			Malake Rajoke		100	190	180	370
37			Shah Fateh Ali		45	196	184	380
38			Nahre Hrseh		100	300	200	500
39			Kot Sahib		30	158	72	230
40			Mehroke		30	80	70	150
41			Thatta Viroka		36	200	100	300
42		Darya Khan	Chak No.177/T.D.A		70	300	200	500
43			Chak No.53-M.L		190	672	528	1200

Sr. No	Zone	Tehsil	Villages	HH	M	F	Total
44			Chak No.1 Rakh Dala	80	400	300	700
45			Karar Noon	88	316	212	528
46			Bilochan Wali	128	580	386	966
47			Chak No.51/M.L	80	300	200	500
48			Chak No.176/T.D.A	296	516	344	860
49			Chak No.50-M.L	26	87	69	156
50			Chak No.54-M.L	28	150	100	250
51			Surani Nasheb	184	564	686	1250
52			Daggar Qureshi Janub Gharbi	122	416	319	735
53			Chak No.5 Rakh Dallo Wala	65	280	110	390
54			Dulle Wala No.1	79	269	205	474
55			Chak No.2 Rakh Dala	140	446	394	840
56			Chak No.3 Rakh Dala	185	569	541	1110
57			Chak No.4 Rakh Dala	240	756	684	1440
58			Gadai No.2	1050	3460	2840	6300
59			Chak No.12-A/TDA	1050	3890	2410	6300
60		Pakpattan	Chak No.87/D.	149	457	437	894
61			Bahwan Shah	153	498	420	918
62			Chak Ilahi Bux	100	350	250	600
63			Chak Murad Khan	170	569	451	1020
64			Chak Nazam Din	120	372	348	720
65			Gobind Pur Bahmni	100	350	250	600
66			Jand Wala	163	598	498	1000
67			Nahla Abad	40	126	114	240
68			Dhamiana	115	365	325	690
69			Chak No.4 S.P.	180	578	502	1080
70			Chak Quder Tullah	83	251	247	498
71			Chilli Mamdana	135	420	390	810
72			Dada Ahluka	200	650	550	1200
73			Ghar Taj	260	785	775	1560
74			Ghazi Mardan	160	580	380	960
75			Arazi Tek Chand	170	523	497	1020
76			Ghuri	150	463	437	900
77			Rakh Ferozpur	130	458	322	780
78			Wara Piran Kalan	80	256	224	480
79			Kala Chishti	200	630	570	1200
80			Chak No.12. K.B.	160	496	464	960
81			Musteqim Mamunka	110	335	325	660
82			Malik Rahmun	180	565	515	1080
83			Amira Ahluka	60	185	175	360
84			Alam Mehteka	130	421	359	780

Sr. No	Zone	Tehsil	Villages		HH	M	F	Total
85			Chhinah		125	385	365	750
86			Maneke		130	423	362	785
87			Jalil Mehteka		100	320	280	600
88			Khatwan		242	865	857	1452
89			Faiz Pur		300	969	831	1800
90			Talibali		100	369	231	600
91			Jamal Pur Tahli		100	370	232	602
92			Chak Wasao		140	456	384	840
93			Chak No.105.D		85	253	257	510
94			Chak No.104/D		175	536	514	1050
95			Chak No.100/D		100	301	301	602
96			Chak No.88/D.		215	652	638	1290
97			Chak No.102/D		125	385	365	750
98			Bablana		145	465	405	870
99			Bahdar Khara		105	315	315	630
100			Bahmani		200	638	652	1200
101			Bonga Amam Din		105	325	305	630
102			Bounga Shamis		110	365	330	660
103			Chak No.91/D.		110	330	322	652
104			Chak Waso Kamboh		150	540	360	900
105			Kirparam		100	329	279	608
106			Lakh Wira		180	596	484	1080
107			Magan Pur		150	545	363	908
108			Nabi Bakish		60	200	160	360
109			Saleem Shah Bodla		190	584	556	1140
110			Chak No.106.D		110	256	404	660
111			Wara Peran Khurd		110	334	332	666
112			Chak No. 101./D		140	424	416	840
113	South -I	Liaqatpur	Ahmad Ali Lar	Mudlal	43	165	153	318
				Basti Nazir Shah	77	296	274	570
				Basti Ghulam Akbar Mohana	31	119	110	229
				Basti Akram Khan Daher	37	142	131	274
114			Allah Dita Bhela	Allah Dita Bhela	108	410	378	788
				Mohammad Baksh Bhela	59	224	207	431
				Jam Abdul Rasheed Lar	47	178	165	343
115			Allah Jiwaya Lar	Sardar Jam Iqbal Lar	51	183	169	352

Sr. No	Zone	Tehsil	Villages		HH	M	F	Total
				Allah Jiwaya Lar 1	171	614	566	1180
				Basti Malik Shahbaz(Haj i Yamin)	96	344	318	662
				Allah Jiwaya Lar 2	256	919	848	1766
116			Ashraf Shah	Basti Gopang Gorgage/Basti Manzoor Khan Koosh	46	163	150	313
				Basti Bado Lar	38	134	124	258
				Basti Abdul Majeed Khan Lashari	23	81	75	156
117			Bahan Wala	Bahan Wala	44	181	167	348
				Basti Wahid Bux	109	448	413	861
				Basti Jam Abdullah Vihaa	32	131	121	253
				Basti Abdul Aziz	38	156	144	300
				Basti Thathaan	52	214	197	411
				Basti Ghsoora	88	362	334	695
				Basti Dhoop Sari	45	185	171	356
				Basti Ahmad Din	22	90	83	174
118			Bahar Khaki	Bahar Khaki	566	1943	1793	3736
				Basti Waali	125	429	396	825
				Basti Malik Moj Ali Gabar	46	158	146	304
				Basti Malik Anahal	33	113	105	218
				Basti Ameer Shah	30	103	95	198
				Basti Noor Da Kowaan	39	134	124	257
				Basti Malik Shameer Kulyar	93	319	295	614
				Basti Jam Bahadar	78	268	247	515
				Basti Allah Bux	48	165	152	317
				Basti Azam Bux	54	185	171	356

Sr. No	Zone	Tehsil	Villages		HH	M	F	Total
119			Chak No.116-A-NP	Chak 116 NP Alif	49	191	177	368
120			Chak No 116 NP	Chak 116 NP	49	161	148	309
121			Chak No 117 NP	Basti Seth M. Bux Chak 117 NP	25	92	85	178
				Basti Abdur Rehman Chak 117 NP	32	118	109	227
				Basti Haji Abdul Ghani Chak 117 NP	46	170	157	327
122			Chak No 118 NP	Basti Allah Bux Chak 118 NP	26	104	96	200
123			Chak No 120 NP	Chak No 120 NP	11	53	49	101
124			Chak No 121 NP	Chak No 121 NP	66	202	187	389
				Basti Salwani	35	107	99	207
125			Chak No 122 NP	Chak No 122 NP	332	1295	1195	2490
126			Chak No 123 NP	Basti Haji Lal	52	187	172	359
127			Chak No 124 NP	Chak No 124 NP	111	392	362	755
128			Chak No 125 NP	Chak No 125 NP	100	296	274	570
				Chak No 125 NP Colony	40	119	109	228
129			Chak No 126 NP	Chak No 126 NP	53	212	196	408
130			Chak No 127 NP	Chak No 127 NP	29	112	103	215
				Jam Banna	242	931	860	1791
131			Chak No. 128 NP	Basti Haji Kalo	37	137	126	263
132			Chak No 129 NP	Chak No 129 NP	74	312	288	599
				Basti Shah Muhammad Chak 129-NP	56	236	218	454
133			Chak No 130 NP	Chak No 130 NP	38	126	117	243
134			Chak No 131 NP	Chak No 131 NP	119	402	371	774
135			Chak No 132 NP	Chak No 132 NP	177	690	637	1328

Sr. No	Zone	Tehsil	Villages		HH	M	F	Total
136			Chak No 133 NP	Chak No 133 NP	25	122	113	235
137			Chak No 138 NP	Chak No 138 NP	61	260	240	500
138			Chak No 34 Abbasia	Chak No 34 Abbasia	57	196	181	376
				Chak 34/A Colony	79	271	250	521
				Basti Channaan Chak 34/A	35	120	111	231
139			Chak No 35 Abbasia	Chak No 35 Abbasia	207	893	825	1718
				Dera Kalluwan	32	138	127	266
				Chak 35/A Colony/ Daiyaan Wali Colony	329	1420	1311	2731
				Chak 35/A Jadid	34	147	135	282
				Basti Shah Muhammad Chak 35/A	74	319	295	614
140			Chanjni	Basti Muhammad Naich	84	332	306	638
				Basti Aziz Arain	49	194	179	372
				Chanjni	131	518	478	996
				Basti Abdul Rasheed Ganjri	59	233	215	448
141			Chohan	Chohan	183	885	817	1702
142			Choudari	Basti Malik Aslam Mesan	21	78	72	149
				Chaudhri	56	207	191	398
				Basti Allah Ditta Khan Abbasi	63	233	215	447
				Basti Jato Sial	144	532	491	1022
				Basti Jato Sial	48	177	164	341
				Basti Rais Allah Ditta	95	351	324	675
				Basti Rais Muhammad Bux	55	203	187	391
				Basti beti	62	229	211	440
				Basti Sandheela	117	432	399	831

Sr. No	Zone	Tehsil	Villages		HH	M	F	Total
				Basti Meher Abdullah Sial	73	270	249	518
				Basti Manzoor Sial	36	133	123	256
				Basti Haider Nagar	49	181	167	348
143			Chur Wala	Basti Abdul Aziz	74	242	224	466
144			Duda Naich	Goind Wala	82	273	252	525
				Basti Machiyaan Solangi	212	706	651	1357
				Basti Ghulam Haider	117	389	359	749
145			Gabrani	Basti Gabraani	607	2494	2302	4795
				Basti Sultan Mehmood/Basti Nandaan	115	472	436	909
				Basti Bakhet Ali	69	283	262	545
				Basti Allah Bachya	70	288	265	553
				Basti Khan Abbasi/Basti Dufli	33	136	125	261
146			Gharib Shah	Basti Jam Abdullah Malik	50	195	180	375
				Basti Moosa Kaju	65	254	234	488
				Basti Jam Mushtaq Lar	38	148	137	285
				Basti Kulyar	71	277	256	533
				Basti Smaney Khan	50	195	180	375
				Basti Jam Pooly	34	133	122	255
147			Ghemi	Ghemi	84	293	270	563
				Shafique Abad	100	348	322	670
				Basti Kchala	127	442	408	851
				Basti Qalandar Shah	65	226	209	436
				Basti Haji Ahmad Jetaal Urf Khoo Wali	71	247	228	476
				Basti Jam Gaman	77	268	248	516

Sr. No	Zone	Tehsil	Villages		HH	M	F	Total
148			Ghuka	Ghuka	45	145	134	279
				Basti Theem	86	277	256	533
149			Goth Amin	Goth Amin 2	133	491	453	944
				Goth Amin 1	73	270	249	518
				Basti Ghulam Muhammad	84	310	286	596
				Basti Arain	80	295	273	568
150			Goth Hayat	Haji Ghulam Sarwar	88	334	308	642
				Goth Hayat	116	440	406	847
				Basti Faiz Ahmad Bohar	43	163	151	314
				Adda Chouk Fareed Amin Abad	155	588	543	1132
				Basti Jam Faiz	61	232	214	445
				Basti Meyani	92	349	322	672
				Basti Ghulam Haider Khokhar	48	182	168	350
151			Goth Mahi	Basti Ghulam Naich	41	147	136	283
				Goth Mahi	104	373	344	718
				Basti Panwaan	160	574	530	1104
				Basti Makool	60	215	199	414
				Basti M. Nawaz Shah	50	179	166	345
				Basti Nonari	145	520	480	1001
				Basti Ghunya	70	251	232	483
				Basti Malkan	70	251	232	483
				Basti Gul Hasan Arain	137	492	454	945
				Basti Hafiz Nazar Old	216	775	715	1490
				Basti Khokhraan	35	126	116	242
				Basti Hafiz Nazar	87	312	288	600
				Basti Qulaalan	56	201	185	386
				Basti New Hafiz Nazar Waseer	45	161	149	311

Sr. No	Zone	Tehsil	Villages		HH	M	F	Total
				Basti Malik Shabeer Ahmad	30	108	99	207
152			Gous Abad	Basti Doda Pally Khan	186	764	705	1469
				Basti Araain Da Baag	281	1154	1066	2220
				Basi Ahmad Ali	56	230	212	442
				Basti Amiabaa	57	234	216	450
				Basti Jam Bapar	41	168	155	324
				Basti Malik Noor Ahmad	27	111	102	213
				Basti Rehmat Nagar	68	279	258	537
153			Gul Muhammad Lar	Basti Noorpur Batwani	428	1825	1685	3510
				Basti Kalo Khan	55	235	216	451
				Basti Salar Lar	140	597	551	1148
				Gul Muhammad Lar	23	98	91	189
				Basti Makha Lar Paley Shah Darbar Haroonabad	66	281	260	541
154			Gulani	Gulani	35	127	118	245
				Malkani	83	302	279	581
				Shabbir Abad	96	349	323	672
				Basti Jajaan	172	626	578	1204
				Basti Gulani	72	262	242	504
				Basti Malik Hussain Bakhsh	69	251	232	483
				Basti Baloch(Haji Sarwar Khan)	43	157	144	301
				Basti Jam Samijah	40	146	134	280
				Basti Ray Parhar	30	109	101	210
				Basti Molviyaan	36	131	121	252
				Basti Palley Khan	51	186	171	357

Sr. No	Zone	Tehsil	Villages		HH	M	F	Total
				Basti Mugrani	51	186	171	357
				Basti Gulshan e Iqbal	48	175	161	336
				Basti Haq Nawaz	36	131	121	252
				Basti Khair Muhammad Khan	28	102	94	196
				Basti Haji Hussain Bakhsh	72	262	242	504
155			Haroon Abad	Haroon Abad	12	41	38	79
				Kotla Raiwalhin	117	402	371	772
				Basti Shaikh Peer Bux	170	583	539	1122
				Basti Kithraan+Basti Mochiaan	60	206	190	396
				Basti Kamoo	95	326	301	627
156			Hussain Abad	Hussain Abad	24	90	83	173
157			Jhoung Bilawal	Jhoung Bilawal	120	449	415	864
				Basti Noor Ahmad Shah	38	142	131	274
				Baseti M. Nawab Mehar	74	277	256	533
				Basti Abdul Rasheed Sial	104	389	359	749
158			Jumma Muhana	Jam Gulan	67	254	235	489
				Basti Allah Jiwaya	31	118	109	226
				Jumma Muhana	61	232	214	445
				Ayaz Lar	49	186	172	358
				Basti Abbasi	139	528	487	1015
				Basti Khokhran	88	334	308	642
				Basti Abdullah Treeli	65	247	228	475
				Basti Jam Javed	147	558	515	1073
159			Kandani	Kandani	660	2094	1932	4026
				Basti Moman	91	289	266	555
				Basti Sunnat Abad	192	609	562	1171

Sr. No	Zone	Tehsil	Villages		HH	M	F	Total
				Basti Jam Abdullah Darkhan	55	174	161	336
				Basti Elahi Bux Muhani	115	365	337	702
				Basti Mehmoodabad	51	162	149	311
160			Kotla Daaulat	Basti Kotla Dulat	140	597	551	1148
				Basti Elahi Bux Gopang	83	354	327	681
				Basti Mughrani/Ahmad Bux Gopang	122	520	480	1000
				Basti Mughrani/M. Bux Gopang	89	379	350	730
				Basti Jahani/Basti Janjh	55	235	216	451
				Basti Jahani/Basti Janjh	72	307	283	590
				Basti Kotla Gohraam	144	614	567	1181
				Basti Kotla Gohraam	161	687	634	1320
				Basti Muneer Khan	23	98	91	189
				Basti Jahaniya	64	273	252	525
161			Kotla Mubarik	Kotla Mubarik	105	437	403	840
				Basti Darkhan	30	125	115	240
				Basti Ghulam Haider	29	121	111	232
				Basti Hafizaan	46	191	177	368
162			Kotla Nawab	Kotla Nawab	175	719	664	1383
				Basti Ghani Machi	137	563	520	1082
				Basti Nazam Wala	194	797	736	1533
				Basti Qurashiaan	37	152	140	292
				Basti Langah	47	193	178	371
				Basti Abdul Aziz Samejah	31	127	118	245

Sr. No	Zone	Tehsil	Villages		HH	M	F	Total
				Basti Gaazer	78	320	296	616
				Basti Haji Imam Bux	43	177	163	340
				Basti Jam Jango Wiha	20	82	76	158
				Basti Shaikh Machian	40	164	152	316
163			Kotla Niazi	Kotla Niazi	85	323	298	621
				Basti Jatoi Balouch	61	232	214	445
				Basti Mujawraan Mori	241	915	844	1759
				Basti Hitam Khan	43	163	151	314
				Basti Abdul Kareem Saweetra	105	399	368	767
164			Lakhani	Lakhani	82	260	240	500
				Jailabad	122	387	357	744
				Basti Khuda Bux	311	986	911	1897
				Basti Hafiz Ghulam Mandi	253	803	741	1543
				Basti Rais Haji Atta Ullah/Hafeez	66	209	193	403
				Basti Adil Arain	70	222	205	427
				Basti Rais Tahir/Basti Noor Ahmad	33	105	97	201
165			Lal Shah	Lal shah	15	65	60	125
				Chakaran	156	673	622	1295
				Basti zaman shah	95	410	379	789
				Azeempura	128	552	510	1062
				Basti dad potra	68	293	271	564
166			Laoon Wala	Basti Jam Mehrab Wiha	28	98	90	188
				Basti Jamal Arain	93	324	299	623
				Basti Sheerani	77	268	248	516
				Basti Jhamat	61	213	196	409
				Basti Wazeer Khan	56	195	180	375

Sr. No	Zone	Tehsil	Villages		HH	M	F	Total
				Basti Haji Abdul Hameed Pahoor	69	240	222	462
				Basti Haji Ghulam Hussain	54	188	174	362
				Basti Ghulam Nabi Wiha	40	139	129	268
167			Malhani	Mulhani	31	118	109	226
				Basti Afzal Ghasoora	195	740	683	1424
				Basti Abdul Lateef Sial	88	334	308	642
				Basti Dandey Naich	184	698	645	1343
				Basti Haji Ghoos Bux	38	144	133	277
168			Malik Pur	Basti Khan Muhammad	42	140	129	269
				Basti Durani/Basti Maachi	33	110	101	211
169			Malkani	Mayani Moza Malkani	66	268	247	515
				Basti Roja Machi	88	357	329	686
				Basti Meero Khan	95	385	356	741
				Basti Haji Bakhat Ali	40	162	150	312
				Basti Meyani	81	329	303	632
				Basti Maande Machi	45	183	168	351
				Basti Muhammad Pur	33	134	124	257
				Basti Hakeem Abad	58	235	217	452
170			Metla	Metla	44	146	135	282
				Kurai	61	203	187	390
				Basti Jalmi	81	270	249	518
				Basti Saeed Metla	75	250	230	480
				Basti Mehar	135	449	415	864
171				Basti Salwani	101	294	271	566

Sr. No	Zone	Tehsil	Villages		HH	M	F	Total
			Mir Muhammad Lar	Basti Bagga Lar	35	102	94	196
				Basti Said Pur	30	87	81	168
172			Muhammad Daha	Fareed Shah Mor	14	55	51	106
				Mohammad Daha	127	502	463	965
				Basti Kumharan	80	316	292	608
				Basti Luqman Arain	125	494	456	950
				Basti Nizam Din	49	194	179	372
				Basti Shah Muhammad	69	273	252	524
				Basti Rais Muhammad Yar	41	162	150	312
173			Mujawraan	Basti Manoor Mujawraan	54	258	238	497
				Basti Haji Ramzan	50	239	221	460
				Basti Fazal Balli	63	301	278	580
				Basti Ali Khan	23	110	102	212
				Basti Rana M. Usman	179	856	790	1647
				Basti Gul M. Balli	76	364	336	699
				Basti Peer Bux Balliaan	68	325	300	626
				Basti Peer Bux Balliaan	100	478	442	920
174			Nala Musani	Nala Musani	308	1169	1079	2248
				Basti Kamley Wala	142	539	498	1037
175			Pakhi War	Pakhi War	118	491	453	944
				Basti Niaz Khan	121	503	465	968
				Basti Hayat M.	202	840	776	1616
				Basti Punnar+Basti Niaz Ahmad	61	254	234	488
				Basti Ahmad Nagar	160	666	614	1280
176			Pararan Sharif	Pararan Sharif	67	286	264	549
				Basti Kehri	36	154	142	295

Sr. No	Zone	Tehsil	Villages		HH	M	F	Total
				Basti Haslaan	60	256	236	492
				Basti Galgani	45	192	177	369
				Basti Jooya	33	141	130	271
				Basti Wazir Ahmad Derkhan	70	298	276	574
				Basti Molvi Hanif	52	222	205	426
				Basti Huraan	21	90	83	172
				Basti Rinda	30	128	118	246
177			Qadu Wali	Qadu Wali	38	119	109	228
				Habib Abad	102	318	294	612
				Basti Ahoora	37	115	107	222
				Basti Noor Jahaniya	29	90	84	174
				Basti Qadu Wali	64	200	184	384
				Basti Kandani	51	159	147	306
				Basti Malik Musa Naich	21	66	60	126
				Basti Malik Sadique	13	41	37	78
				Basti Gareebabad	86	268	248	516
				Basti Saymee Wali	62	193	179	372
				Basti Shaqlani	52	162	150	312
				Basti Allah Bux	47	147	135	282
				Basti Allah Bux	25	78	72	150
				Basti Ghulam Nabi Naich	17	53	49	102
178			Rais Pathan	Rais Pathan	56	207	191	398
				Basti Jhanjh	42	155	143	298
				Basti Mual	192	709	654	1363
				Basti Marrai Balouch	69	255	235	490
				Basti Khushal Khan	221	816	753	1569
				Basti Kalorran	106	391	361	753
179			Rashid Abad	Rashid Abad Jadid	75	281	259	540
				Rashid Abad	164	614	567	1181

Sr. No	Zone	Tehsil	Villages		HH	M	F	Total
				Basti Karmaniyan	71	266	245	511
180			Rindan	Rindan	147	527	487	1014
				Basti Daim Khan	38	136	126	262
				Basti Haji Hazoor Bux Naich	55	197	182	380
				Basti Gul Muhammad Naich	43	154	142	297
				Basti Mehar M. Ismail/Basti M Bux Sial	81	291	268	559
				Basti Haji M Khan Rind	82	294	272	566
				Basti Malik Azeem Naich	101	362	335	697
				Basti Ramzan Sial	43	154	142	297
				Basti Chanar/Basti Ghulam Nabi Khokhar	36	129	119	248
				Basti Molvi Ghulam Rasool	50	179	166	345
181			Sadiqpur	Sadiqpur	55	177	164	341
182			Said Pur	Said Pur	29	103	95	197
				Basti Kacha Pacca Arain	83	293	271	564
				Basti Jam Shah Muhammad/ Basti Mari Wala	55	194	180	374
				Tibba Kareem Abad	104	368	339	707
				Basti Pathan	95	336	310	646
				Basti Jam Sumaar	29	103	95	197
				Basti Kanal Lar	42	149	137	286
				Basti Jam M. Bux/Basti Ali Shah	25	88	82	170
				Basti Bhattiyaan	33	117	108	224
				Basti Balliyaan	39	138	127	265

Sr. No	Zone	Tehsil	Villages		HH	M	F	Total
183			Shahbaz Pur Gharbi	Basti Peer Iftekhar Shah	105	410	378	788
				Basti Veeha Lar	26	101	94	195
184			Shamsabad	Babay Da Khara	89	324	299	623
				Shamsabad	114	415	383	798
				Shamsabad	114	415	383	798
185			Shidani Sharif	Pul Wataran	32	126	117	243
				Shidani Sharif	606	2395	2211	4606
				Basti Ghulam	97	383	354	737
				Pul Watran Machi	172	680	627	1307
				Basti Qade Machi	89	352	325	676
				Basti Nabi Bux	100	395	365	760
				Basti Sadat	160	632	584	1216
186			Talbani	Utera	29	97	89	186
				Talbani	618	2057	1898	3955
				Adda Pul Basti Korai/Basti Korai	240	799	737	1536
				Basti Bhanad Blouch	60	200	184	384
				Chouk Maharvi and Bhatti	55	183	169	352
				Basti Sial	70	233	215	448
				Basti Haji Ghulam Sarwar Sameja	27	90	83	173
				Basti Allah Diwya/Allah Wasya Sial	22	73	68	141
				Basti Allah Diwya/Allah Wasya Sial	23	77	71	147
				Basti Shahbaz Khan Abbasi	111	369	341	710
				Basti Pathan	63	210	194	403
				Basti Utera	32	106	98	205
				Basti Khalifa	120	399	369	768
				Basti Sameja	26	87	80	166

Sr. No	Zone	Tehsil	Villages		HH	M	F	Total
187			Tanwari	Moosa Chouk	57	210	194	405
				Tanwari	259	956	883	1839
				Basti Bapraan	22	81	75	156
				Basti Jan Muhammad	103	380	351	731
				Basti Pehlwan	44	162	150	312
				Basti Chaki wali	29	107	99	206
				Kotla Punjabiyan	37	137	126	263
188			Tarinda Mir Khan	Basti Peer Bux Jath Malik	138	452	417	869
				Tarinda Mir Khan	379	1242	1146	2388
				Basti Malik Soobah	92	301	278	580
				Basti Ali Gabbar	88	288	266	554
				Basti Theekri	61	200	184	384
				Basti Usman Arain	54	177	163	340
				Basti Haleem Arain	37	121	112	233
				Basti Noor Ahmad Jhanj	27	88	82	170
				Basti Paari Malik	59	193	178	372
				Basti Khan Muhammad Lar	37	121	112	233
				Basti Aarib Shaikhaan	56	183	169	353
				Basti Umar Wada Janjh	42	138	127	265
				Basti Daiyat	22	72	67	139
				Basti Shahbaz pur Adda Chanji Chouk	165	541	499	1040
				Basti Hamdaabad	104	341	314	655
189			Ther Posti	Adda Ther Posti	152	537	496	1034
				Basti Ahmad Khan Kehwani	32	113	104	218
				Basti Gul Muhammad	48	170	157	326

Sr. No	Zone	Tehsil	Villages		HH	M	F	Total
190			Tibbi Sayyadan	Basti Milan Machi	74	296	274	570
				Basti Malik Hussain Bakhsh	74	296	274	570
				Rais Usman Moza Tibbi Sayyadan	64	256	237	493
				Basti Shahoo	78	312	288	601
				Basti Lamucha	56	224	207	431
				Basti Malik Mubarak	33	132	122	254
				Basti Dr. Abbasi	51	204	188	393
191			Wahid Bux Sial	Wahid Bux Sial 2	72	243	225	468
				Wahid Bux Sial 1	65	220	203	423
				Basti Langah	100	338	312	650
				Basti Chaty Khan	100	338	312	650
192			Yakhtar Maha	Yakhtar Maha 2	41	139	128	267
				Yakhtar Maha 1	27	91	84	176
				Basti Baba Ali	31	105	97	202
193			Zaffar Abad	Basti Gaman Khan	79	246	228	474
				Basti Mushtafabad / Dera Lahoriaan	49	153	141	294
				Zaffar Abad	636	1984	1832	3816
				Basti Mian Muhammad Akbar	83	259	239	498
				Basti Varmat Lar	56	175	161	336
				Basti Bahawal Shah	52	162	150	312
				Basti Gous Bux Shah	125	390	360	750
				Basti Haji Jummah	59	184	170	354
194			Chak No 119 NP	Chak No 119 NP	96	354	327	682
195			Chak No 119-A- NP	Chak No 119-A- NP	47	276	255	531
196			Chak No 137 NP	Chak No 137 NP	16	53	49	102

Sr. No	Zone	Tehsil	Villages		HH	M	F	Total
197			Unran	Raufabad	22	72	67	139
				Basti Haji Bakhat Ali	93	305	281	586
				Basti Gul Muhammad	30	98	91	189
				Basti Rook Allah Jawayia	22	72	67	139
				Basti Ahmad Bux	37	121	112	233
				Basti Elahi Bux Bhutta	24	79	73	151
198		Rojhan	Badli		136	403	372	775
199			Badli Chak Ladh		566	1795	1658	3453
200			Basti Nikka		44	204	188	392
201			Chak Dim		242	881	813	1694
202			Chak Karia		380	1087	1003	2090
203			Chak Mut-1		292	941	869	1810
204			Chak Mut-2		1078	3195	2950	6145
205			Dera Dildar		1062	3203	2957	6160
206			Dera Jiwan Khas		69	208	192	400
207			Garhi Soori		140	349	323	672
208			Kaheeri		107	295	272	567
209			Kin Khas		808	2563	2366	4929
210			Kotla Gulsher		738	2456	2267	4723
211			Kotla Hasan Jamra		126	380	351	731
212			Rakh Kotla Hasan Jamra		80	245	227	472
213			Lutairi		18	66	60	126
214			Miranpur		1031	4075	3761	7836
215			Patti Shah Wali		146	243	224	467
216			Shah Wali		864	3145	2903	6048
217			Solangi		56	239	220	459
218			Wah Machka		1507	4545	4196	8741
219	South -II	Shujabad	Agar Khani		875	2990	2760	5750
220			Amanullah Pur		400	980	1020	2000
221			Bagrain		825	2640	2860	5500
222			Basti Chhaju Shah		925	2818	2933	5750
223			Bhana		800	2352	2448	4800
224			Chak Jakhar		175	539	561	1100
225			Chak No 13/F		750	2250	2250	4500
226			Chak Rs		2250	6664	6936	13600
227			Choti		400	1274	1326	2600
228			Dairapur		1600	5500	5500	11000
229			Dera Arvi		525	1911	1989	3900

Sr. No	Zone	Tehsil	Villages	HH	M	F	Total
230			Dhondo	650	1992	2158	4150
231			Gunwen	2500	7840	8160	16000
232			Jai	1150	3640	3360	7000
233			Jhangi	1500	4560	4940	9500
234			Kaser Pur	2500	7656	8294	15950
235			Khalar	250	858	893	1750
236			Khanpur	1500	5500	5500	11000
237			Khas Punjani	500	1550	1550	3100
238			Kotli Najabat	5500	15925	16575	32500
239			Lasoorhi	350	1175	1175	2350
240			Lutf Pur	1300	3920	4080	8000
241			Mahara	400	1152	1199	2350
242			Mochi Pura	1175	3408	3692	7100
243			Mohan Pur Gharbi	600	1900	1900	3800
244			Pounta	1400	4260	4615	8875
245			Punjani	4000	12500	12500	25000
246			Raja Raam	2600	7920	8580	16500
247			Rasool Pur Janubi	600	1846	1704	3550
248			Rasool Pur Shumali	2300	6958	7242	14200
249			Rukan Hatti	2700	8400	9100	17500
250			Sat Burji	350	1050	1050	2100
251			Seri	200	588	637	1225
252			Shah Musa	1950	6048	6552	12600
253			Sheikhpur Shajra	1900	6250	6250	12500
254			Soman	1700	5520	5980	11500
255			Tahir Pur	275	925	925	1850
256			Thath Galawan Junabi	700	2250	2250	4500
257			Thatha Makhdoom Pur	525	1560	1440	3000
258			Tudar Pur	1550	4655	4845	9500
259			Vainus	1800	5880	6120	12000
260			Wahi Bhakar	2000	6983	7268	14250
261			Wai Sawaya	900	3000	3250	6250
262			Taror Jalalpur	275	792	858	1650
263		Alipur	Amir Pur Daha	200	662	689	1350
264			Baqar Shah Janubi	450	1325	1325	2650
265			Basti Haji	250	750	750	1500
266			Baz Wala	1925	7250	7250	14500
267			Bet Channa	650	1760	1691	3450
268			Bet Dewan Shah	550	2295	2205	4500
269			Bet Muiziddin	1000	3185	3315	6500

Sr. No	Zone	Tehsil	Villages	HH	M	F	Total
270			Chak Dada	375	1100	1100	2200
271			Chak Daud Wala	260	931	969	1900
272			Dahaka	450	16346	15705	32050
273			Damar Wala Janubi 1	2100	6885	6615	13500
274			Damar Wala Janubi 2	1875	6250	6250	12500
275			Daulut Pur	240	711	740	1450
276			Fateh Pur Janubi 1	1975	7750	7750	15500
277			Fateh Pur Janubi 2	3325	13000	13000	26000
278			Ghalwan 1	3559	14535	13965	28500
279			Ghalwan 2	3150	11800	11800	23600
280			Ghari	1900	6000	6000	12000
281			Kachi Lal	850	2640	2860	5500
282			Khair Pur Para	650	2352	2548	4900
283			Khair Pur Sadat	4200	15435	16065	31500
284			Khan Pur Nahrka	250	750	750	1500
285			Khanani	4200	13005	12495	25500
286			Khangarh Donma	950	3250	3250	6500
287			Kundai	1250	3800	3800	7600
288			Kundrala	1375	4214	4386	8600
289			Latti	2500	7020	6480	13500
290			Madd Sohanyara Shah	550	1920	2080	4000
291			Malik Arain	1150	4845	4655	9500
292			Misan Kot Behwa	2100	7800	7800	15600
293			Mohib Shah	425	1250	1250	2500
294			Mud Wala	2150	7548	7252	14800
295			Mutfarqa	14500	47334	49266	96600
296			Nussrat Pur	410	1368	1482	2850
297			Pakka Naich	1400	4998	4802	9800
298			Phullan	2100	7350	7650	15000
299			Rakh Khanani	400	1750	1750	3500
300			Shah Wasava	1350	4750	4750	9500
301			Sheikhani	1750	5464	5687	11150
302			Sultan Pur	3100	11025	11475	22500
303			Tibi Arian	1300	5250	5250	10500
304			Walwat	525	1862	1938	3800
305	South -III	Kahror Pacca	Basti Lal	110	320	340	660
306			Chak Qadirpur	500	1560	1440	3000

Sr. No	Zone	Tehsil	Villages	HH	M	F	Total
307			Dera Dilawar	1000	4000	2000	6000
308			Kotkora Jhanda	800	1500	900	2400
309			Arah	210	660	600	1260
310			Chak Allah Rakha Khan	160	600	400	1000
311			Dhorah Mahar	70	240	180	420
312			Gopal Pur	140	420	420	840
313			Gul Pur	70	320	280	600
314			Bhinda Gerdan	62	190	182	372
315			Chak Muhammad Murad	300	1000	800	1800
316			19/M	170	520	500	1020
317			21/M	180	580	500	1080
318			30/M	125	400	350	750
319			Kand Ahmed Asar	200	700	500	1200
320			Murshad Pur	80	400	480	480
321			22M	250	800	700	1500
322			Chak Choki Kohna	230	769	611	1380
323			Hassa Joya	153	468	450	918
324		Khairpur Tamewali	Fazlu Kukara	171	526	500	1026
325			Khairi Bhabhi	180	560	520	1080
326			Kotla Mahi	120	420	300	720
327			Ladar	250	750	750	1500
328			Mamdu Mangero	100	400	200	600
329			Bunga Yarani	90	250	290	540
330			Darud Garan	98	340	248	588
331			Goth Ali	155	560	370	930
332			Gith Kamal	78	264	264	468
333			Kamalia	60	200	160	360
334			Ahmed Milkhi	250	750	750	1500
335			Amin Fatani	180	550	530	1080
336			Baghban	75	230	220	450
337			Binda Chadhran	80	500	340	840
338			Kharal Nau Baramad	100	400	200	600
339			Chak No. 26	70	210	210	420
340			Dharala Randu	200	750	450	1200
341			Haleem	70	260	190	450
342			Khanan Arain	180	1160	840	2000
343			Chak No. 24 Sharaf Shah	600	650	550	1200
344			Khuda Bux Seyal	95	305	265	570
345			Kotla Qaim Khan	240	795	765	1560
346			Lal Sohanra	185	630	600	1230
347			Luthran	180	530	550	1080

Sr. No	Zone	Tehsil	Villages	HH	M	F	Total
348			Mehti	80	280	200	480
349			Mohammad Sharif	143	458	400	858
350			Muhammad Khan	80	300	280	480
351			Mungrani	120	462	258	720
352			Muradpur	150	454	446	900
353			Muradpur Dhrala	200	600	600	1200
354			Nurrey	210	610	650	1260
355			Qazi Kalra	100	400	200	600
356			Raja	200	620	580	1200
357			Rameli	240	740	700	1440
358			Rukrani	100	400	200	600
359			Sardar Pur	75	300	150	450
360			Azimpura	60	200	160	360
361			Noor Mohd Khan	25	77	73	150
362			Gaman Wagi	70	269	227	496
363			Gawains	22	65	67	132
364			Goth Jhumar	80	260	160	420
365			Khairpur	340	1040	1000	2040
366		Bahawalnagar	Bonga Ihsan Bibi	200	500	300	800
367			Hasan Raika	250	500	300	800
368			Abrerah Uttar	80	250	150	400
369			Amin Abad	149	547	347	894
370			Boole Shah Hitthar	55	400	200	600
371			Ramnagar	490	1500	800	2300
372			Paran Wala	110	450	250	700
373			Hussian Abad Hithar	65	225	100	325
374			Hussian Abad Uttar	188	400	150	550
375			Chak Abdul Haq	300	2100	1200	3300
376			Dhanraj Pura	270	2200	1100	3300
377			Ali Goher No. 326	70	225	95	350
378			Jagga Sanatteka	250	1050	500	1550
379			Mina Sanatteka	205	900	500	1400
380			Sharaf Din	50	150	80	230
381			Mosla	130	330	170	500
382			Pir Sikandar Otar	130	550	250	800
383			Jhulan Chishtian	130	390	140	530
384			Gauspur	100	500	300	800
385			Gaman Dongi	54	220	110	340
386			Akkanwali Khurd	90	400	200	600
387			Kartar Singh	280	856	824	1680
388			Khawaja Bux Bodla	10	350	250	600

Sr. No	Zone	Tehsil	Villages	HH	M	F	Total
389			Faqir Shah	200	800	400	1200
390			Khober	160	490	190	680
391			Ramzan Shah	80	300	180	480
392			Allahabad	140	470	240	710
393			Muhammad Asad Khan	40	160	95	255
394			Janoowala	230	800	400	1200
395			Tobi Qamar-Ud-Din	50	200	100	300
396			Malak Pura	125	1250	750	2000
397			Jalwala	105	950	750	1900
398			Dara Sanatteka	120	400	250	650
399			Hira Bashnoai	150	600	300	900
400			Sandar Bashnoi	190	900	520	1420
401			Sher Singh Wala	183	730	370	1170
402			Barasajwar Khan	80	300	100	400
403			Noor Jahanian	20	70	30	100
404			Dadoo Mammunka	100	300	150	450
405			Bhole Shah Utar	55	400	200	600
406			Abrerah Hitthar	80	250	150	400
407			Bilara Nabi Bux	50	150	50	200
408			Bilara Qasim Khan	57	230	126	356
409			Madarsa	114	470	200	670
410			Pir Shah	90	400	200	600
411			Kakku Bodla	60	250	100	350
412			Bhangran	377	950	530	1480
413			Khilowala	135	400	380	780
414			Mamunka Hatar	170	550	300	850
415			Muhsan Pura	100	400	200	600
416			Beg Kanoor Pur	120	400	300	700
417			Wara Piran	75	250	150	400
418			Chaweka Hitthar	5600	9530	4700	14500
419			Mamunka Uttar	170	550	300	850
420			Dinpur Sharif	250	900	600	1500
421			Mari Mian Sahab Hithar	350	1200	650	1750
422			Ramzan Langah	80	285	120	205
423			Tughera Sharif	280	1000	800	1800
424			Wilayat Pur	318	1700	990	2050
425			Nanak Sar	30	90	90	180
Total				**219,023**	**760,980**	**718,899**	**1,478,678**

4.6.2 Findings of Socioeconomic Survey

A. Occupational Status

Due to the availability of fertile land in most of the tehsils, agriculture is the primary occupation in the project area, followed by labour as the second largest profession because of weak socio-economic conditions of the population. However, in Kot Momin, Rojhan, Alipur and Shujabad most of the people are engaged in labour. The occupational trend in different tehsils can be observed in Figure below which presents percentages of the various occupations in the project area, based on interactions with project communities during field visits, consultations and limited surveys.

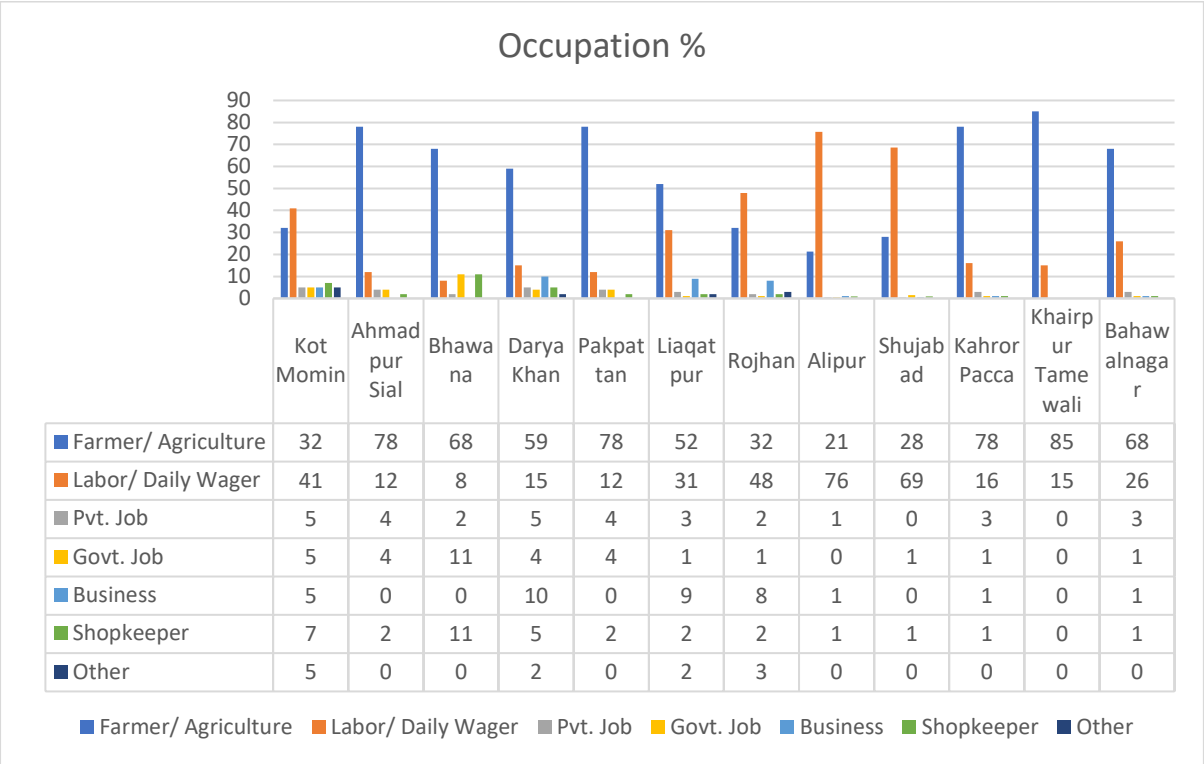

	Kot Momin	Ahmadpur Sial	Bhawana	Darya Khan	Pakpattan	Liaqatpur	Rojhan	Alipur	Shujabad	Kahror Pacca	Khairpur Tamewali	Bahawalnagar
Farmer/ Agriculture	32	78	68	59	78	52	32	21	28	78	85	68
Labor/ Daily Wager	41	12	8	15	12	31	48	76	69	16	15	26
Pvt. Job	5	4	2	5	4	3	2	1	0	3	0	3
Govt. Job	5	4	11	4	4	1	1	0	1	1	0	1
Business	5	0	0	10	0	9	8	1	0	1	0	1
Shopkeeper	7	2	11	5	2	2	2	1	1	1	0	1
Other	5	0	0	2	0	2	3	0	0	0	0	0

Figure 8: Occupational Status of the Respondents

B. Religion

Islam is the dominant religion in Punjab where, according to the 2023 census, Muslims constitute 97.75% of the population. The minorities include Christians (1.93%), followed by Hindus (0.20%), and other minority groups (0.12%). Based on the primary data collected all the respondents of all the tehsils of Phase-II were Muslims.

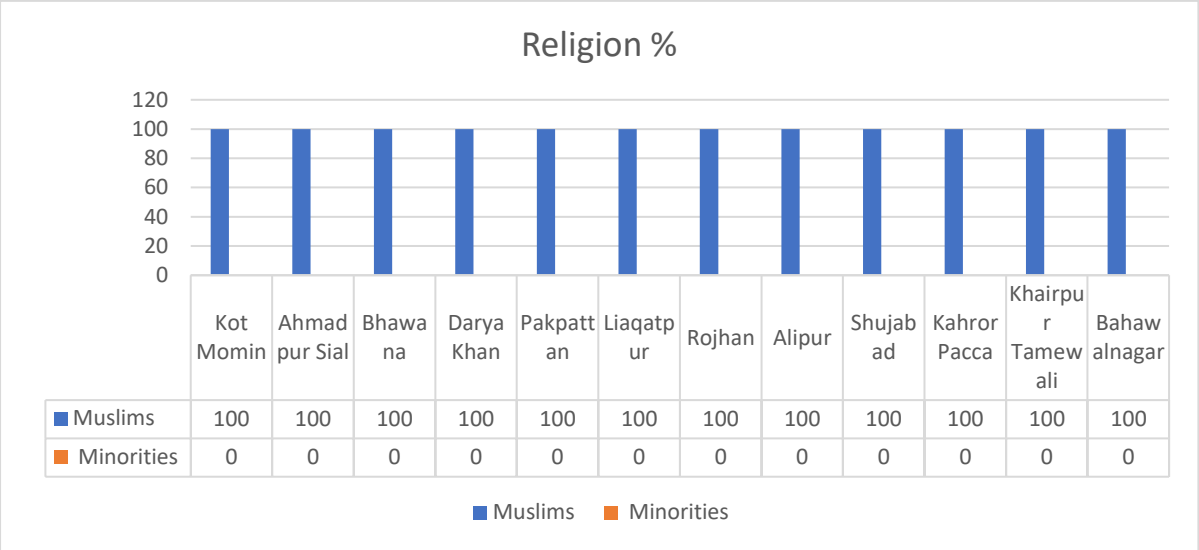

Figure 9: Occupational Status of the Respondents

C. Caste System

Several castes/clans have been reported in the project area. In Tehsil Kot Momin Ranjha, Gondal, Nissoana and Heral are mostly present. In tehsil Bahawalnagar, Pakpattan and Khairpur Tamewali, Chishti, Bodla, Arain, Bhatti, Bhindara, Hotiana Wattoo, Gardezi Syed, and Joiya are prominent castes. In Ahmdpur Sial, Sial Jutt, Syed, and Awan are major castes of the population, however, Rajput, Arain, and Bhatti are also present. Despite the concentration of one or two castes in some tehsils, no significant disputes exist among the different castes.

D. Income Levels

The monthly income earned by individuals from various sources varies widely ranging from less than Rs. 20,000 to above Rs. 50,000. Majority of the population reported that their income barely covers the basis of household expenses. In Tehsils Kot Momin, Ahmadpur Sial, Bhawana, Darya Khan, and Pakpattan, a majority of households earn moderate incomes, with only a small share in higher income brackets. Liaqatpur and Khairpur Tamewali show relatively better economic conditions, with a noticeable proportion of households earning higher incomes compared to other tehsils. Rojhan, Alipur, and Shujabad exhibit comparatively lower income levels, reflecting higher poverty and limited livelihood opportunities. In Kahror Pacca, household incomes are more evenly distributed, including some comparatively well-off households. In Bahawalnagar, most households earn moderate incomes, with very few in higher income categories. Overall, the data indicates that a large portion of the population across the project area belongs to low- to middle-income groups, highlighting economic constraints and reliance on agriculture and labor-based livelihoods.

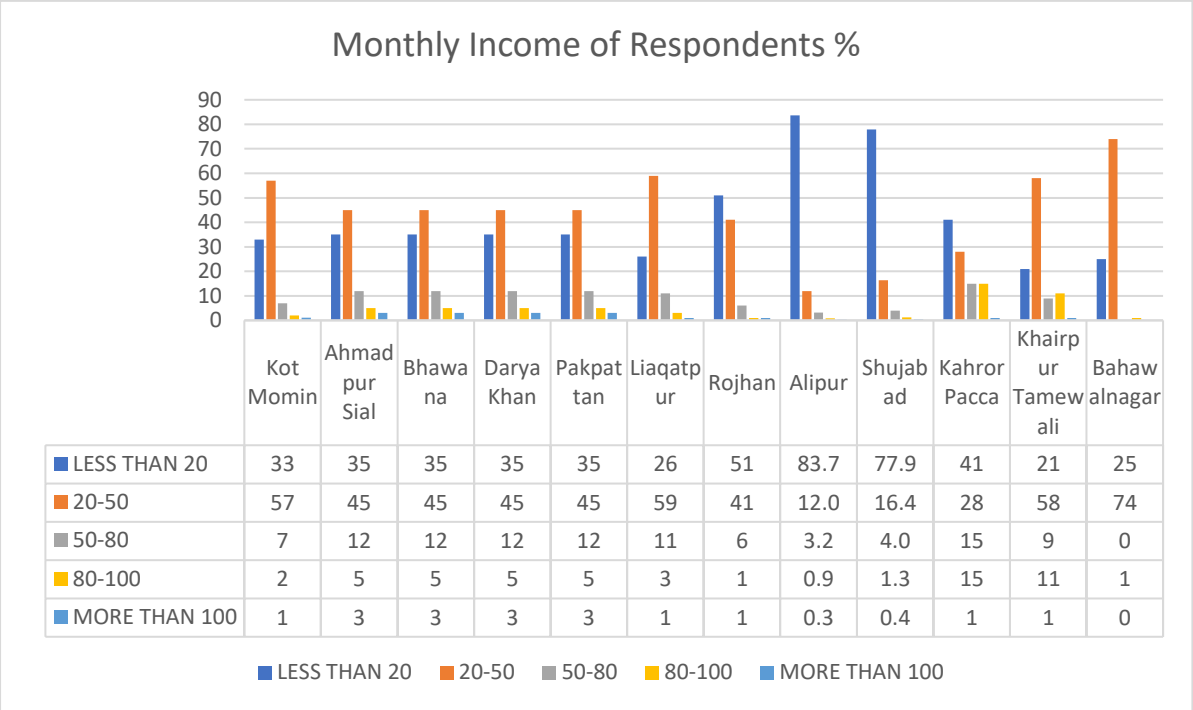

Figure 10: Monthly Income of the Respondents

D. Source of Drinking Water

The analysis indicates that handpumps are the primary source of drinking water in most villages, except in Tehsil Bhawana and Darya Khan, where borehole motors dominate. Borehole motors serve as a secondary source in other areas. Piped water supply is limited, occurring only in Shujabad, Kahror Pacca, Khairpur Tamewali, and Bahawalnagar, reflecting inadequate network coverage. RO filter plants are rare, observed only in Tehsil Alipur and Shujabad, indicating minimal reliance on treated water systems.

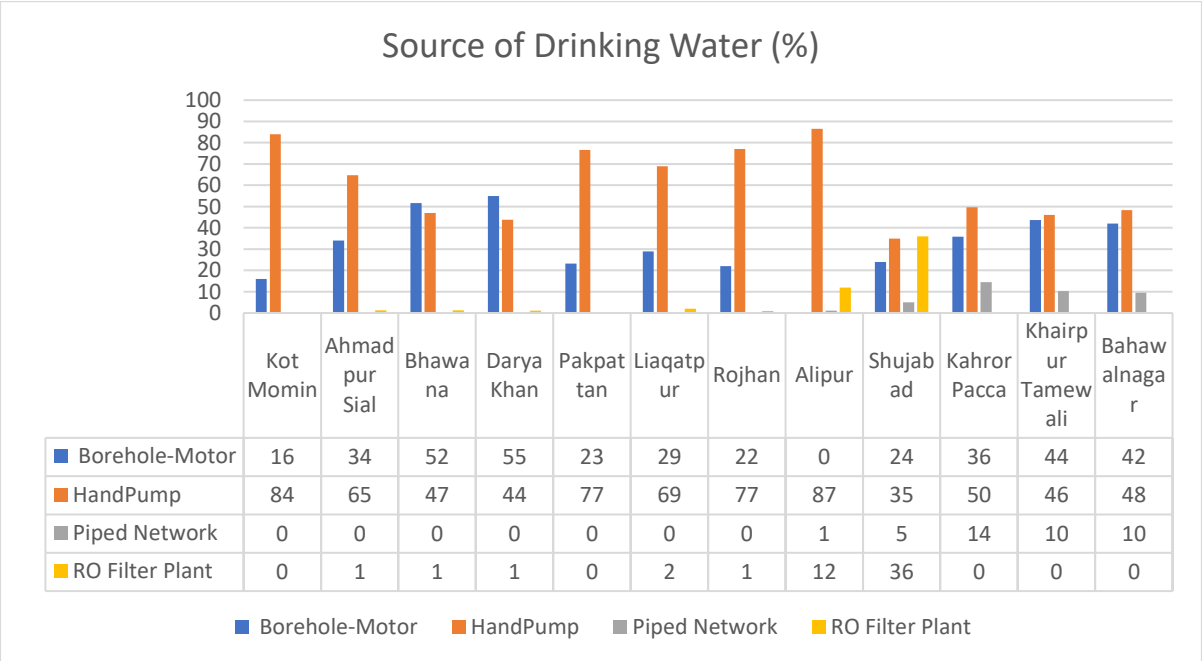

Figure 11: Monthly Income of the Respondents

E. Satisfaction with household water quality

The analysis indicates generally low satisfaction with household water quality across the surveyed Tehsils, with most households reporting dissatisfaction. Liaqatpur and Rojhan show complete dissatisfaction. Other tehsils, including Bhawana, Pakpattan, and Shujabad, have relatively higher satisfaction levels, but even in these areas, concerns over drinking water quality remain widespread.

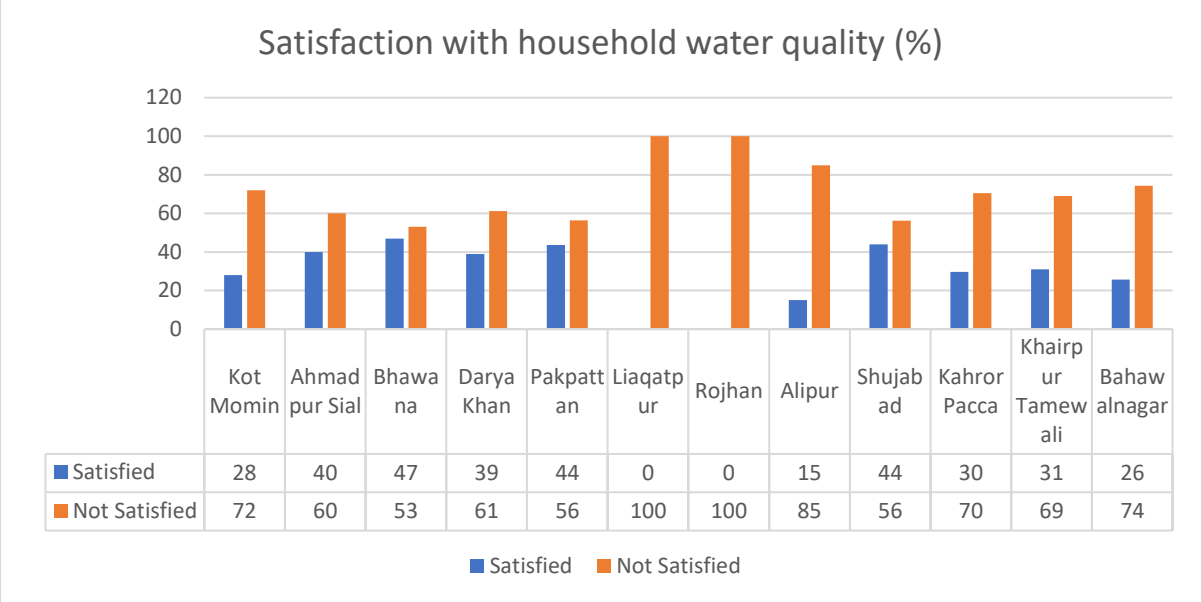

	Kot Momin	Ahmadpur Sial	Bhawana	Darya Khan	Pakpattan	Liaqatpur	Rojhan	Alipur	Shujabad	Kahror Pacca	Khairpur Tamewali	Bahawalnagar
Satisfied	28	40	47	39	44	0	0	15	44	30	31	26
Not Satisfied	72	60	53	61	56	100	100	85	56	70	69	74

Figure 12: Satisfaction with household water quality

F. Type of Sewerage System

The analysis shows that open drains are the predominant sewerage system in most tehsils, reflecting inadequate sanitation infrastructure. This trend is particularly evident in Kot Momin, Liaqatpur, and Rojhan, where open drainage is almost universal. Septic tanks are also widely used in several Tehsils, including Ahmadpur Sial, Bhawana, Darya Khan, Pakpattan, Alipur, Shujabad, Khairpur Tamewali, and Bahawalnagar, indicating partial reliance on on-site sanitation systems. Sewer lines are extremely limited and are observed only in a few Tehsils, including Ahmadpur Sial, Bhawana, Darya Khan, and Pakpattan, with negligible presence elsewhere. In most areas, wastewater from drains is ultimately discharged into open fields or nearby nullahs. Overall, although drainage facilities exist in many Tehsils, poor maintenance, solid waste accumulation, and inadequate design result in clogged drains, sewage overflow, and stagnant wastewater, adversely affecting sanitation conditions.

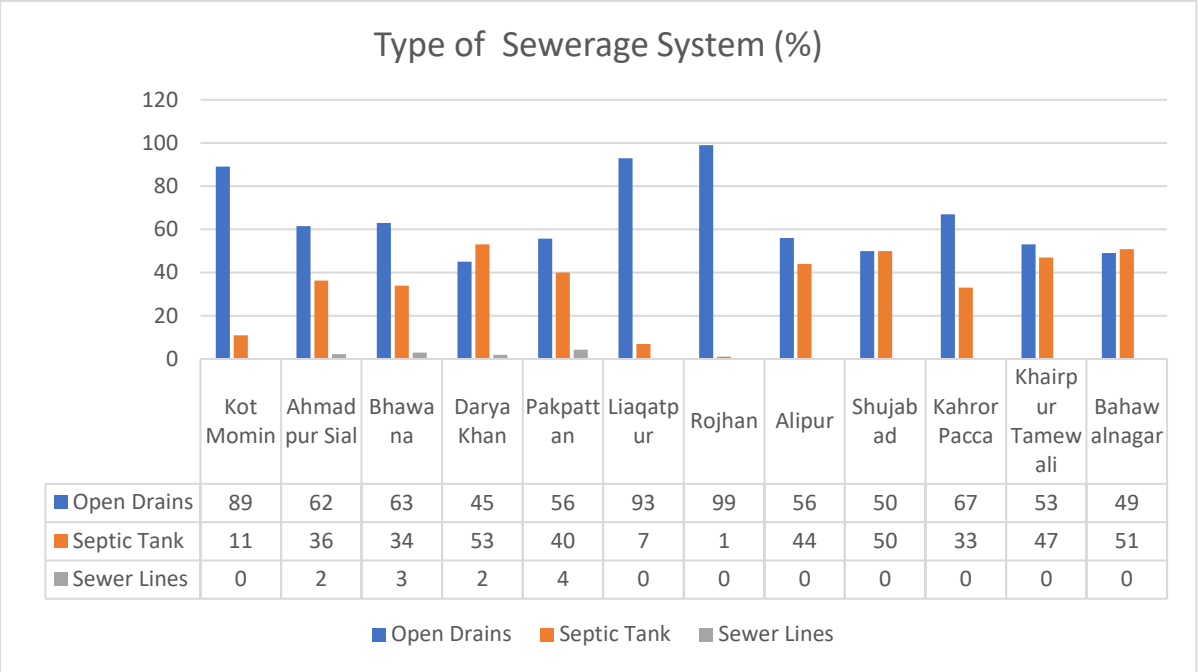

	Kot Momin	Ahmadpur Sial	Bhawana	Darya Khan	Pakpattan	Liaqatpur	Rojhan	Alipur	Shujabad	Kahror Pacca	Khairpur Tamewali	Bahawalnagar
Open Drains	89	62	63	45	56	93	99	56	50	67	53	49
Septic Tank	11	36	34	53	40	7	1	44	50	33	47	51
Sewer Lines	0	2	3	2	4	0	0	0	0	0	0	0

Figure 13: Type of Sewerage System

G. Type of sanitation Facility

The analysis indicates that toilet facilities are available to most households in the surveyed tehsils. Full coverage is observed in Ahmadpur Sial, Bhawana, Darya Khan, Pakpattan, Kahror Pacca, Khairpur Tamewali, and Bahawalnagar, whereas partial coverage and open defecation are reported in Kot Momin, Liaqatpur, Shujabad, Alipur, and Rojhan. These observations highlight gaps in sanitation access and the need for improved facilities and awareness campaigns to achieve full coverage.

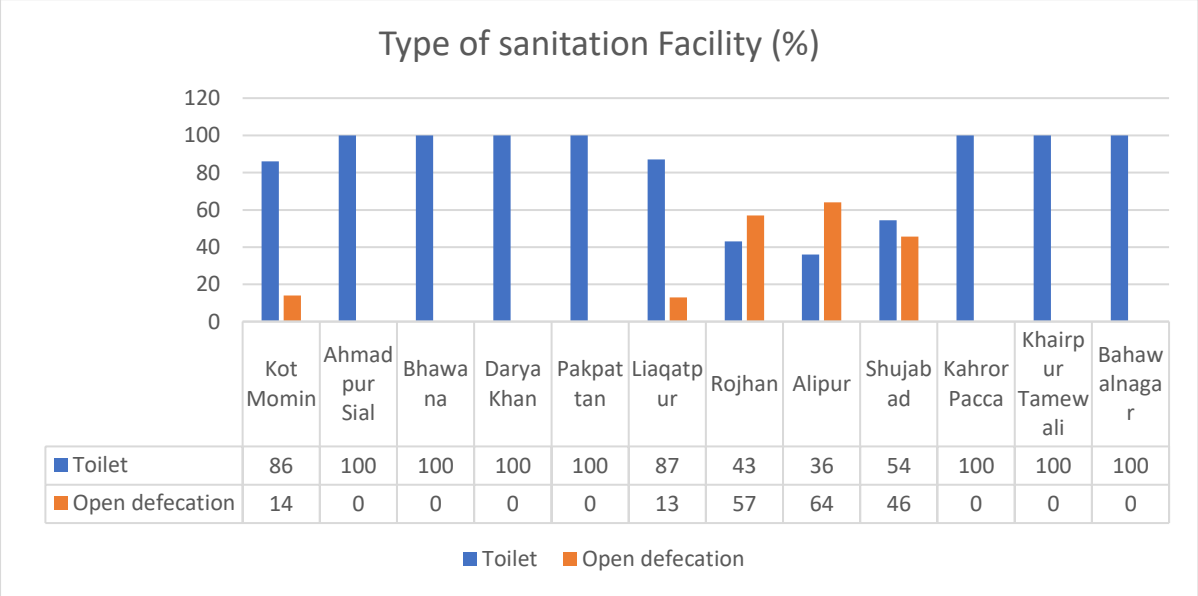

	Kot Momin	Ahmadpur Sial	Bhawana	Darya Khan	Pakpattan	Liaqatpur	Rojhan	Alipur	Shujabad	Kahror Pacca	Khairpur Tamewali	Bahawalnagar
Toilet	86	100	100	100	100	87	43	36	54	100	100	100
Open defecation	14	0	0	0	0	13	57	64	46	0	0	0

Figure 14: Type of Sanitation Facility

H. Solid Waste Facility

The analysis shows that solid waste management facilities are relatively better in Taunsa, Alipur, Kot Momin, and Shujabad. Other Tehsils, such as Ahmadpur Sial, Bhawana, Darya Khan, Pakpattan, Kahror Pacca, Khairpur Tamewali, Bahawalnagar, Liaqatpur, and Rojhan, face severe deficiencies, with most households lacking access to municipal solid waste services. Overall, the data indicate a need to improve solid waste management infrastructure across the study area.

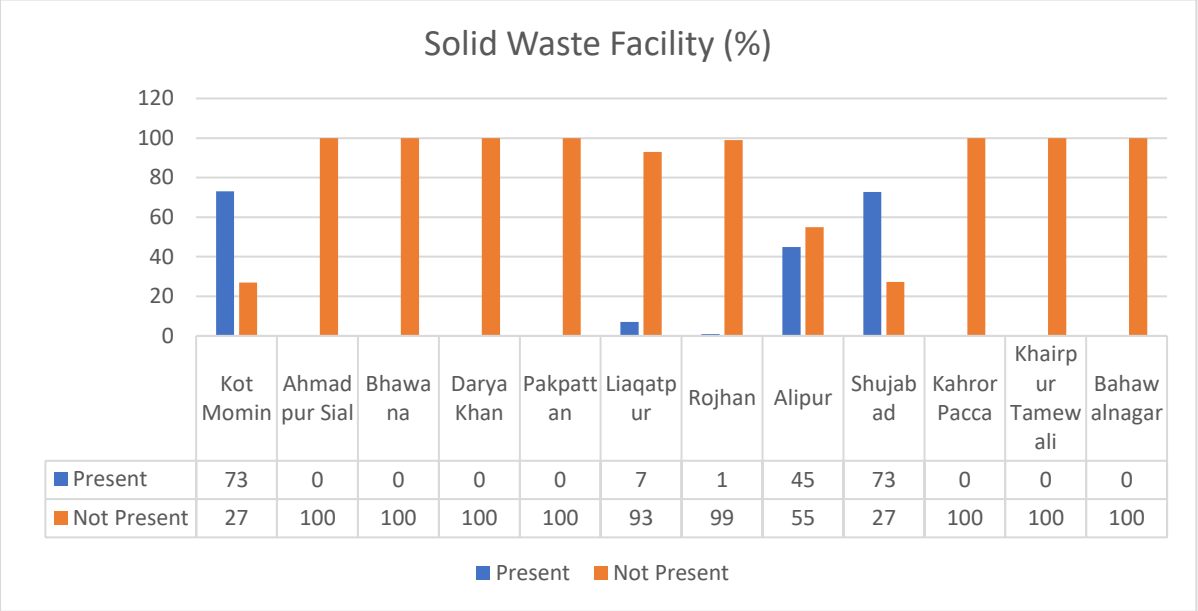

	Kot Momin	Ahmadpur Sial	Bhawana	Darya Khan	Pakpattan	Liaqatpur	Rojhan	Alipur	Shujabad	Kahror Pacca	Khairpur Tamewali	Bahawalnagar
Present	73	0	0	0	0	7	1	45	73	0	0	0
Not Present	27	100	100	100	100	93	99	55	27	100	100	100

Figure 15: Type of Solid Waste Facility

I. Housing Construction Pattern

During field visits, it was observed that the proposed project areas lack basic amenities. However, the trend of kacha houses has diminished and most people have built pacca houses with RCC roofs, stone walls with cement mortar, cement plastering & flooring. Kot Momin and Shujabad show a clear dominance of pacca houses, while semi-pacca structures are present in small numbers. In contrast, Tehsils such as Ahmadpur Sial, Darya Khan, Pakpattan, and Kahror Pacca continue to have a high share of kacha houses, reflecting limited access to permanent housing. Liaqatpur and Rojhan display a mixed pattern of pacca, semi-pacca, and kacha houses. Alipur and Bahawalnagar exhibit moderate coverage of pacca houses alongside semi-pacca and kacha structures. Overall, while pacca houses dominate in some Tehsils, kacha and semi-pacca houses remain common in areas with tenant populations and limited land ownership. Type of construction, as shown in **Figure 14**, also corresponds roughly with the income levels described above.

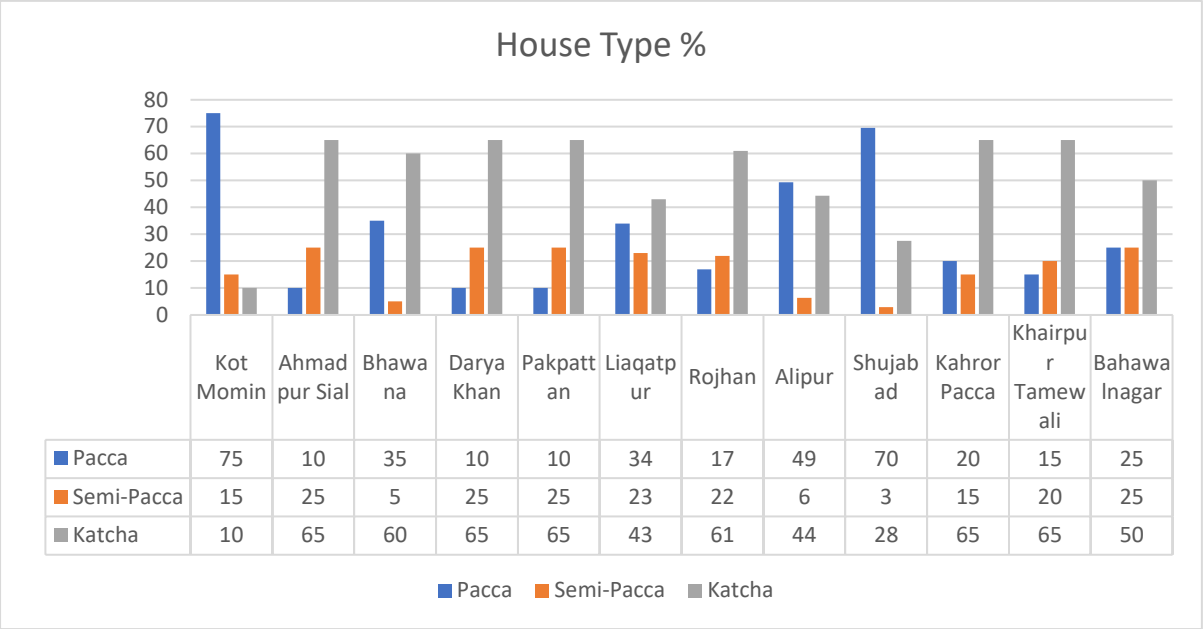

	Kot Momin	Ahmad pur Sial	Bhawana	Darya Khan	Pakpattan	Liaqatpur	Rojhan	Alipur	Shujabad	Kahror Pacca	Khairpur Tamewali	Bahawalnagar
Pacca	75	10	35	10	10	34	17	49	70	20	15	25
Semi-Pacca	15	25	5	25	25	23	22	6	3	15	20	25
Katcha	10	65	60	65	65	43	61	44	28	65	65	50

Note: Kacha = A structure constructed of mud.

Semi-Pacca = A structure constructed of a mixture of mud and bricks.

Pacca = A structure constructed of concrete and cement blocks/bricks.

Figure 16: Type of Construction of House

J. Mode of Transport

Public transport facilities are not sufficiently present in the south and North area and people use their personal motorbikes, cycles, and cars, etc. for traveling. However, in Center, people also use Rickshaws. In case of emergencies, they call Rescue 1122 and get aid in 5-10 minutes of time. The project activities are unlikely to impact the transportation modes. However, it will be ensured that access of Rescue 1122 vehicles is not hindered due to project activities.

K. Communications

The project area has telephone connections for internet services and mobile phone coverage is also available, allowing people to access to the internet through their mobile phones. The access roads to all the project sites are in good condition, although the situation of internal streets and roads is poor. The village roads and streets are either metaled, soling, or unpaved. Motorways pass through the project Tehsil Kot Momin, Alipur and Shujabad (the project villages are within 5-25 km distance from the motorway). In Tehsil Kehror Pakka, Shujabad, Darya Khan, Ahmadpur Sial, and Pakpattan Railway network is also available. Moreover, National and Provincial Highways are present in all tehsils of the project area.

L. Health Conditions and Facilities

The poor health conditions in the project area are one of the reasons for initiating the proposed project. The quality of potable water available throughout the project area is highly compromised, as indicated in Section 4.5.4. This has led to the prevalence of several waterborne disease and stunted growth in the project area. The most common diseases in these areas include typhoid, cholera, hepatitis, diarrhea, intestinal worms and skin allergies.

The project area has varying levels of access to health facilities. Since DHQs are present - in addition to THQs - in Pakpattan, Taunsa, and Bahawalnagar therefore they have good health facilities. In tehsils Darya Khan, and Shujabad, health facilities are above average due to their proximity to the DHQs. Whereas, in tehsils like Ahmadpur Sial, Kahror Pacca, Khairpur Tamewali, and Alipur THQs are present but are not fully functional. However, Basic Health Units (BHU) are also present in most of villages of project area, providing basic medical services to the population. In case of non-availability of BHU in a village, people of the village approach the nearest BHUs in other villages.

M. Educational Facilities

Primary, Middle and High schools are present in some of the proposed villages. The list of educational facilities located close to the proposed construction and excavation sites is provided as social sensitive receptors in Table-18.

N. Basic Civic Amenities in the Project Area

The proposed project area lacks basic civic amenities including water supply, sewerage system, stormwater drainage, solid waste management, gas supply. Telephone connections are available in the project area, but are limited in some areas. The only facility available in the proposed project area is electricity, which is also inadequate as people suffer long hours of load-shedding and low voltage issues.

O. Mechanism of Conflict Resolution

During the field survey, the project team conducted discussions with local communities to identify the types of disputes commonly prevailing in the project area. The survey revealed that disputes over land, water resources, and property inheritance are the most common causes of conflict. These disputes tend to escalate quickly and often result in violence, thereby causing loss of life, property damage, and displacement of communities. In some cases, the police and judicial system have been ineffective in resolving these conflicts, leading to a lack of trust in state institutions, especially in southern region of project area. In addition, inter-caste tensions, religious differences, and political affiliations may also contribute to the conflict, though no major fault-lines were observed along these.

At the community level in project area, conflict resolution is often handled through informal methods of mediation and negotiation. Local elders, community leaders, and religious figures play a significant role in resolving conflicts in proposed project villages. The traditional methods of dispute resolution include Jirgas (councils of elders) and Panchayats also called Kaths (village councils). These methods often involve face-to-face meetings, with both parties presenting their case and a neutral third party facilitating the resolution. In addition to these informal methods, legal systems such as the Punjab Local Government Act 2019 and the Alternative Dispute Resolution Act 2017 also provide a formal mechanism for resolving disputes. However, the use of formal systems is limited in project areas due to lack of accessibility, awareness and enforcement of aforementioned acts. Overall, conflict resolution at the community level in project area is a combination of traditional and modern approaches, with a focus on finding mutually agreeable solutions that maintain social harmony. The proposed GRM system of the project will also strengthen present conflict resolution systems (Village Councils, Jirgas, Panchayats etc.) of the project area. The proposed GRM system will not only improve but also make the Village Councils, Jirgas and Panchayats inclusive and will also sensitize the community about GRM.

P. Presence of NGOs/ CBOs

There are several INGOs, NGOs and CBOs present in the project area. According to stakeholder consultations and institutional stakeholder consultations, Punjab Rural Support Programme (PRSP) and National Rural Support Programme (NRSP) are working in Tehsil Kahror Pakka and Khairpur Tamewali. The scope of both NGOs is WASH, which is also within the mandate of PRMSC. Moreover, UNICEF, WaterAid Pakistan, JICA, Save the Children, WHO, International Rescue Committee (IRC), UNOPS, Muslimaid, Qatar Charity, Plan International have also been reported to be working in WASH related sector. Furthermore, Community-Based Organizations (CBOs) were also reported in Tehsil and Bahawalnagar to support marriages, funeral prayers, and other financial needs of the community. CBOs can play an important role in social mobilization, behavior change in target villages, and tariff collection and O&M of the schemes.

4.6.3 Results of Gender Situation Survey

- In Kot Momin the high rate of female illiteracy in the project area becomes evident when examining the current educational status of the respondents. Limited access to educational facilities and widespread unawareness further contributes to the persistence of illiteracy among women.
- The women's financial empowerment was checked by their authorization to spend their money. Many of them revealed that they don't have the power to spend their money the way they like.
- In addition to the lack of awareness in Kot Momin, the majority of adolescent girls reported using cloth instead of sanitary pads, indicating not only informational gaps but also possible constraints related to affordability, accessibility, or cultural acceptance of modern menstrual products.
- A gender situation analysis was conducted in all 425 villages/sub-villages across 12 tehsils through focus group discussions. The purpose of this qualitative survey was to identify women-related concerns, gender roles and responsibilities, education levels, occupational status, involvement in agriculture and livestock, access to health facilities, willingness to pay, access to power and resources, prevalence of gender-based violence, and needs assessment.
- Traditional gender roles and responsibilities in rural Punjab Center, North, and South are almost identical, with women primarily responsible for domestic and caregiving tasks and men serving as the primary breadwinners. Although females are engaged in agricultural and subsistence farming operations and livestock-related activities, they encounter obstacles in controlling resources, accessing land, credit, and other resources, limiting their productivity and economic opportunities in rural settings.
- Waterborne diseases are a significant public health concern for females and children in the surveyed areas, according to focus group discussions.
- Women-headed households are not uncommon in the surveyed areas, especially in South and North where men migrate for work to other cities or abroad.
- The majority of female respondents in South, North, and Center areas are not involved in decision-making processes, with their decisions limited to day-to-day household affairs. Males make major and decisive decisions, while in the center, some

respondents reported that decisions were made through mutual consultation and understanding.

- Although there were few reported violent incidents in South, respondents in other areas considered gender-based violence an act of boldness rather than a crime. The consultation found a lack of knowledge about sexual harassment (SH) and sexual exploitation and abuse (SEA) as crimes and how to report this while having social pressure to keep these incidents secret and treated as a matter of honor.

5 PUBLIC CONSULTATION

5.1 General

This section describes the outcomes of the public consultation sessions held with different stakeholders that may be directly or indirectly affected by the proposed project. The consultation with community and institutional stakeholders during project planning, designing and implementation stages is a key to sustainable development. Likewise, participation of stakeholders is essential to meet the objectives of meaningful consultation for preparation of ESMP.

5.2 Objectives and Principles of Consultation

The consultation process provided a forum where information relevant to the project was disseminated to the stakeholder. This participation enabled the integration of local and indigenous knowledge into the project design. This not only fosters goodwill and success in the project but also leads to a conflict- free project implementation.

The stakeholders including local community of 425 villages, government representatives, other regulators and the NGOs were met to appraise and discuss the environmental and social perspective of project activities. Their valuable concerns and suggestions were noted and thereafter incorporated in the Environmental and Social Management Plan.

The objectives of the consultation process were to:

- Identify, Inform and involve all stakeholders and local residents including females, minorities and disables, in the consultative and participation process;
- Share information with stakeholders on the construction of the proposed project and expected impacts on the physical, biological and socio-economic environment;
- Understand stakeholders' concerns and perceptions regarding various aspects of the project, including the existing available facilities and the likely impacts of construction and operation related activities of proposed Project; and
- Provide an opportunity to the public to provide valuable suggestions in the project design in a positive manner.

5.3 Consultation and Participation Process

To ascertain the perceptions of different stakeholders about the project scope, its implementation, operation and evaluation, consultation meetings were conducted. The consultation process was carried out in accordance with the World Bank Guidelines on public consultation. A series of consultation sessions were carried out with stakeholders (Govt. departments, farmers, teachers, businessman, women etc.), in November 2025 & February, 2026. Total 425 stakeholder consultation sessions were conducted details of sessions are presented in Annex-7.

The project team chose sites that are easily accessible and barrier-free to accommodate all persons. The consultative sessions/meetings are held mostly at Monasteries (Dera) with both men and women separately. The minutes of the meeting from the focus group discussions and community meetings have been noted down (listed in table 21, table 22 and table 23) and can be shared with the participants (that chose to share their contact information) and the

community. These consultative sessions were designed to exchange information, to discuss the strengths, weaknesses, opportunities, and threats of an idea or project. The consultation meetings proved very useful in information sharing and consensus building.

5.4 Identification of Stakeholders

Project stakeholders were engaged in the review and discussions on various project aspects, social and environmental issues at the early stage of impact assessments for feedback. There are two categories of stakeholders in the project:

Individual/Community Stakeholders

Project beneficiaries for instance, Residents of the project area, Shopkeepers, Employees, Customers, Road Users, Vulnerable and Gender.

Institutional Stakeholders

- Board of Revenue and Tehsil and District Administration, Environmental Protection Agency Punjab (EPA), Agriculture Department, Livestock Department Punjab, Tehsil Headquarter Hospital THQ.

5.5 Information Dissemination

Following information was discussed and disclosed to the stakeholders during the consultation meetings:

- Introduction of the project;
- Description of various project components, their activities and impacts;
- Discuss social and environmental impacts;
- Needs, priorities and reactions of the affected people regarding the proposed projects' impacts; and
- Need of Grievance Redress Mechanism (GRM) in all villages to address the issues & concerns of stakeholders.

For information dissemination to community, culturally appropriate techniques and local language was used.

5.6 Methods of Public Consultation

Public Consultations were carried out in order to establish stakeholder's opinions regarding project implementation. The following methods were used for public consultation and stakeholder's participation:

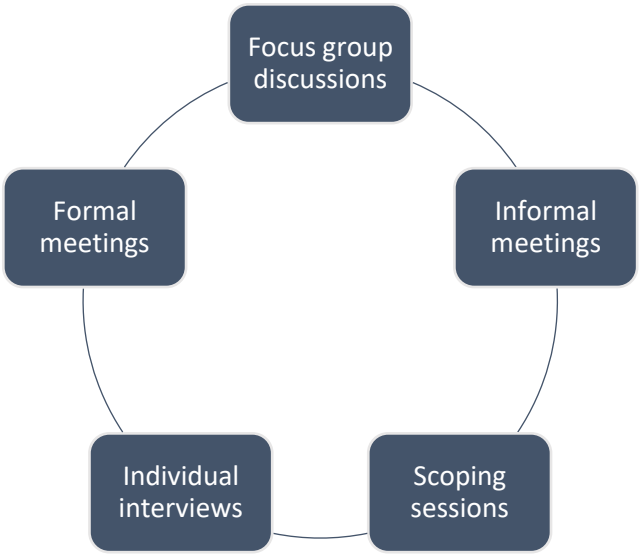

5.7 Approach Adopted for the Consultation

To hold the meetings, people were informed one day before the meeting to assemble in the villages. In addition, the Tehsil Office team contacted the council members and community representatives of each village and informed about the purpose of these consultation meetings. The representatives played a positive role in information dissemination to locals of villages. The meetings held in an encouraging environment where people expressed their concerns and views freely. Formal meetings and interviews were also conducted with female, vulnerable and disabled of the affected community, to explore their needs, problems and priorities related to project execution. In addition to the formal meetings, individual meetings/interviews were also held with the affected females to efficiently involve them in planning process.

5.8 Stakeholders Concerns towards the Project

Concerns raised by the participants, particularly with regard to environmental and social impacts of the project have been listed in following Tables which shows concern and responses as derived from scheme wise consultation meetings.

5.8.1 Concerns and Issues

Following **Table 21** shows concerns and responses of public consultation meetings.

Table 22: Findings of the Consultation Meetings

Sr. No	Concerns Raised	Locations	Response
16.	In Bagri, the water is not drinkable and there are several waterborne diseases including intestinal issues	Kot Momin	Provision of clean water is already part of our project, so waterborne diseases shall be reduced and there will be an improvement in public health.
17.	Will employment opportunities be generated for locals during the construction phase?	All project villages	It will be made sure that 75% of the workforce will be employed from the sub-project area.
18.	Arrangements should be made to suppress dust, curtail high-noise activities, and control the vibrations caused	Kot Momin	Regular sprinkling of water will be carried out over the loose soil to suppress the dust, the noisy activities will not be planned at night and the community will be informed before the

Sr. No	Concerns Raised	Locations	Response
	due to machinery, to protect the community's health		execution of any activity that would generate vibrations
19.	Privacy of people should be upheld during construction phase of the sub-project.	All project villages	Contractor will provide trainings to workers regarding gender and privacy issues.
20.	Construction activities should be minimized during schools' opening and closing times.	All project villages	Contractor will be bound to minimize construction activities during schools' opening and closing times.
21.	Will there be any closure of roads during construction phase?	All project villages	In case of road closures, the nearby community will be informed beforehand and alternative routes will be provided.
22.	Solid waste production during construction time is a major concern and that should not be piled up in the project area.	All project villages	The construction and other waste generated at the site shall be collected, stored and transported to the final disposal site by the contractor on daily basis.
23.	Will there be any tree cutting?	All project villages	No, no trees will be cut during the execution of the project.
24.	The construction activities will cause inconvenience to local residents due to hindrance in routine activities	Alipur, Shujabad,	The contractor will ensure that construction work do not create disturbance for local people's access to the local route and their routine life activities.
25.	Will this project cover all households in the village?	Alipur, Shujabad, Taunsa	Yes, all households located in the deh boundary in the selected villages will be covered.
26.	Who will bear the cost of operation and maintenance (O&M)?	Alipur, Shujabad	The community pay O&M in the form of water charges per month. Government or project may provide initial support.
27.	What about wastewater and drainage system?	Alipur, Shujabad	Proper drainage and wastewater disposal points will be included where technically and socially feasible.
28.	Will there be water meters or fixed charges?	Alipur, Shujabad	There will be fixed water charges. The Client may re-consider it whether meter or fixed charges.
29.	What if the water supply stops or gets damaged?	Alipur, Shujabad	The complaint can be registered in the office.
30.	Local people claim that the construction of the project will lead to noise pollutions and social disturbances during construction of the water supply.	Liaqatpur	Regular maintenance of construction machinery to prevent excessive noise. Provide early and continuous information disclosure.

5.9 Consultations with Female Community Members

Following **Table 22** shows concerns and responses of gender consultation meetings.

Table 23: Findings of the Female Consultation Meetings

Sr. No	Community Consultation with Women	Locations	Response
1.	Most of the women have to go out to the watercourses for washing clothes.	All project villages	This issue will be resolved by executing this project after the provision of water at the doorsteps.
2.	Many females raised their concerns about the health issues due to poor water supply system. Usage of hand pumps and	Kot Momin	Waterborne disease will be reduced and there will be an improvement in public health with the provision of clean and healthy drinking water.

Sr. No	Community Consultation with Women	Locations	Response
	boreholes water, may cause many diseases like kidney, hepatitis, liver problems and diarrhea.		
3.	the women claims that they could not give birth to the female baby. Their men want the baby boys.	Kot Momin	The concern has been noted and will be reported to the higher authority.
4.	Women wanted common washroom for their usage, as they have to go in fields, which raise privacy concerns	Kot Momin	The concern has been noted and will be reported to the higher authority.
5.	Inadequate sanitation facilities and the need to travel long distances to collect water exposes women and girls to different kind of harassment.	All project villages	To a significant extent, the issues of different kind of harassment will be mitigated through the implementation of the project, which seeks to facilitate doorstep access to clean water sources.
6.	Constrained accessibility to clean water and sanitation facilities imposes impediments in the effective management of hygiene during pregnancy and childbirth. Additionally, it affects the ability to care for newborns, thereby contributing to child stunting.	All project villages	The project will ensure the provision of improved WASH conditions to address these concerns for improved women's and their children's health as reduction in child stunting is the core objective of the project.
7.	The burden of fetching water negatively impacts on women's health, as well as limit their ability to pursue education, employment, and other opportunities.	All project villages	The implementation of the PRSWSSP project will reduce the burden of women, improve the quality of life and free up time for other pursuits, including education and income-generating activities.
8.	Increase in water borne disease due to poor sanitation or unsafe water sources.	Liaqatpur	The project aims to mitigate this by providing safe and treated drinking water to the community.

5.10 Consultation with Institutional Stakeholders

Table 23 shows the concerns of institutional stakeholders.

Table 24:Concerns of Relevant Government Departments

Sr. No.	Department	Coverage	Points of Discussion / Apprehensions	Response
1.	**Environmental Protection Department**	Punjab.	The project team described the project location and proposed activities to District Environmental Officer and inquired about their apprehensions/ suggestions regarding the project; • In conducting ESMP, Scoping sessions, and Individual interviews should be conducted with all stakeholders.	All the suggestions shall be incorporated. Institutional consultations are already underway and efforts shall be made to take all the stakeholders on board.

Sr. No.	Department	Coverage	Points of Discussion / Apprehensions	Response
			• Social issues regarding private land acquisition, were discussed in detail. • Baseline should be developed separately according to the baseline conditions. • Public Hearings must be done so that stakeholders who have different types of stakes along with their apprehensions can be listed down easily.	
2.	**Board of Revenue**	Punjab	The Project team described the project location and proposed activities and also briefed them about the requirement of state land for the construction of infrastructure in the project villages. Moreover, consultation meetings were also conducted with Tehsil and District Administrations of almost all the areas of the project.	The Board of Revenue and the respective Tehsil and District officials promised their full cooperation.
3.	**Municipal Committee**	Project Tehsils	The Project team described the project location and proposed activities Tehsil Manager and Assistant Manager and inquired about their apprehensions/ suggestions regarding the project; • Discussion on field planning and effective approach to adequately cover all the field aspects and collect requisite data. The possible constraints in data acquisition were discussed and an effective way out was decided.	Discussed the scope and main features of the project.
4.	**Tehsil Headquarter**	Project Tehsils	The project team described the project location and proposed activities to MS Hospital and inquired about their apprehensions/ suggestions regarding the project; • Show some serious concern regarding waterborne diseases. • Every third person in Tehsil Bhawana suffers from Hepatitis. Due to the lack of infrastructure and transportation facilities in villages, it becomes difficult for the patient to reach the THQ.	The objective of the proposed project is to provide clean drinking water to all the residents of the selected villages at their doorsteps through a piped network. Waterborne diseases will be resolved after the implementation of this project.
5.	**Agriculture Department**	Punjab	The Project team described the project location and proposed activities Field officer inquired about their apprehensions/ suggestions regarding the project;	PRMSC will ensure that wastewater will be used for irrigation (if needed) after adequate treatment.

Sr. No.	Department	Coverage	Points of Discussion / Apprehensions	Response
			• Field officer talked about the major crops Wheat and cotton cultivated in the project area. • The wastewater should not be used for agriculture purposes without treatment • Treated water is used for irrigation purposes Only individual-level solar tube well is present	
6.	**Irrigation Department**	Punjab.	The sub-project details were shared with the representatives of the Irrigation department to obtain land for project activities. The Project team described the project location and proposed activities to Executive Engineer and inquired about their apprehensions/ suggestions regarding the project; • The wastewater should not be used for agriculture purposes without treatment • Treated water is used for irrigation purposes Treated waste should not be disposed of in canals.	PRMSC will ensure that wastewater will be used for irrigation (if needed) after adequate treatment. No wastewater is going to be disposed of in any canal/ nearby water body.
7.	**Public Health Engineering Department**	Punjab	The Client team described the project location and objectives, as PHED is also working in the same domain it was requested to share their work plan for the relevant tehsils with PRMSC to avoid duplication of services or infrastructure. Moreover, PHED shares the lesson learned to improve service delivery.	Lessons learned will be considered in t project planning and designing phase to improve service delivery.
8.	**Livestock Department**	Punjab	The project team described the project location and proposed activities Deputy Director Livestock inquired about their apprehensions/ suggestions regarding the project; Waterborne disease and viral disease in animals were discussed	The proposed project will provide clean drinking water to all the residents of the selected villages and the provision of water for portable use include water for the animal's activities. Waterborne diseases in animals will be resolved after the implementation of this project.

Sr. No.	Department	Coverage	Points of Discussion / Apprehensions	Response
9.	**Fisheries Department**	Punjab	The project team described the project location and proposed activities Field officer inquired about their apprehensions/ suggestions regarding the project: Deputy Director District Office tells about the breed of fish in that area.	No wastewater is going to be disposed of in any nearby water body. So, no aquatic life is going to be affected by this project.
10.	**Department of Forest**	Punjab	The project team described the project location and proposed activities DFO and inquired about their apprehensions/ suggestions regarding the project.	There is no forest in the project boundary or near the project boundary that is going to be affect.

5.11 Consultation with NGO

There are several INGOs, NGOs and CBOs present in the project area. According to stakeholder consultations and institutional stakeholder consultations, Punjab Rural Support Programme (PRSP) and National Rural Support Programme (NRSP) are working in Tehsil Kehror Pakka and Khairpur Tamewali. The scope of both NGOs is WASH, which is also within the mandate of PRMSC. Moreover, UNICEF, WaterAid Pakistan, JICA, Save the Children, WHO, International Rescue Committee (IRC), UNOPS, Muslimaid, Qatar Charity, Plan International have also been reported to be working in WASH related sector. Furthermore, Community-Based Organizations (CBOs) were also reported in Tehsil Bahawalnagar to support marriages, funeral prayers, and other financial needs of the community. CBOs can play an important role in social mobilization, behavior change in target villages, and tariff collection and O&M of the schemes.

5.12 Pressing Needs of the Consulted Villages Suggested by Local People

Local people were consulted to determine the most pressing needs in the project area as perceived by them. The most important needs identified were the provision of water supply and sewerage systems, as well as schools, hospitals/dispensaries, and vocational training institutes for construction work. Due to restricted mobility, locals suggested that a friendly grievance mechanism be developed in all villages to address their concerns during the construction period. Additionally, they recommended that guidance and support be provided to local people for registration of complaints in proposed grievance mechanism.

5.13 Disclosure of ESMP

Public disclosure enables affected groups and interested parties to understand likely implications of the project and to provide input into project design. It promotes dialogue among stakeholders i.e., government, community, NGOs and implementing agencies. As per O.P 4.01, the environmental and social aspects must be discussed with the stakeholders.

The objectives of public disclosure are to aid meaningful public consultation and to ensure transparency of World Bank operations to its stakeholders and constituents.

The safeguard documents will be disclosed on the website of PRMSC and on the World Bank external website.

Presentations containing project information and relevant aspects of public interest will be delivered to the public. Furthermore, project brochures, handouts of presentations, and executive summaries of ESMP in Urdu and English languages will also be distributed to the public.

After the approval, Copies of the ESMP shall be made available to communities and interested parties in accessible locations through local government authorities, (e.g., Village councils, district offices etc.)

6 ANTICIPATED ENVIRONMENTAL IMPACTS & MITIGATION MEASURES

6.1 General

This chapter identifies the beneficial as well as the potentially significant adverse environmental and social impacts of the proposed project activities during design/ pre-construction, construction and operational phases of the proposed project on the physical, ecological and socio-economic domains of the environment. The appropriate mitigation and remedial measures are proposed in this chapter. A brief description of each aspect and the affected environment in the project area are presented below.

6.2 Scoping of Impacts

Potential environmental and social impacts from the proposed Project on key environmental and socio-economic features were identified through the following actions:

- Demarcation of the Area of Influence (AoI);
- Desk study of engineering investigations, studies and designs;
- Environmental monitoring of air, noise, surface water, wastewater and groundwater;
- Detailed review and analysis of primary and secondary data available for all environmental parameters in Project area such as physical, ecological and social resources;
- Socio-Economic survey to assess the extent of land acquisition, occupation, income and poverty levels of the affected households;
- Consultations with executing and implementing agencies, local government, affected community, and traditional and religious leaders of the community;
- Stakeholder consultations with relevant departments, government agencies, NGOs and locals; and
- Knowledge assimilation of international best practices on environmental assessment of infrastructure projects.

6.3 Methodology

Selection of an appropriate and customized methodology for the impact assessment is critical for the ESMP study. The impacts have been assessed based on the proposed project life cycle i.e., in Pre-Construction, Construction and Operational and Maintenance (O&M) stages. For the identification of the potentially significant and non-significant environmental and social impacts, different tools were utilized as detailed below:

6.3.1 Screening Checklist

Based on the findings of desk studies and processed satellite imageries, screening checklists were prepared to screen out the potentially significant adverse environmental and social impacts during pre-construction, construction and operational phase of the proposed project. The objective of the impact screening is to assess the significance of the issues related to the atmosphere, climate, water resources, land resources, ecological environment, socio-economic environment, transport, infrastructure and communication, natural risks, hazards and external constraints of the Project for the proposed development. After the compilation of baseline information and processing of acquired satellite imagery, the screening checklist was

filled to screen out the adverse impact of the proposed Project during the pre-construction, construction and operational phases.

6.3.2 Notion of Significance

Taking into account these criteria, potential significance was classified as either:

Low: an impact for which no mitigation is necessary;

Medium/moderate: an impact that requires effective mitigation; and

High: an impact, which, if not mitigated, could stop the Project from proceeding.

Reversible/Irreversible: Changes considered irreversible, for example, the loss of biodiversity due to a change in water quality;

The potentially significant impacts were then further investigated in more detail to make a comprehensive assessment of the actual impacts.

6.3.3 Study Area/ Area of Influence

Refer Chapter 4: Description of the Environment, **Section 4.3**.

6.4 Environmental & Social Considerations (E&S) in Project Design

Environmental and social (E&S) aspects have been given due considerations in the project design to make the project sustainable, environmentally friendly and socially acceptable. E&S considerations in project design are summarized below:

- The depth of sewer lines has been kept low in waterlogged villages of Pakpattan and Shujabad; to avoid groundwater contamination of shallow aquifer. Same practices will be applicable for similar conditions.
- Sewers shall be laid at least 1m away from water supply lines (except for few streets in each village, where the street width is less than 2 meters.
- In all cases, the sewer lines shall be laid below water pipeline (the difference between top of the sewer and bottom of water pipeline shall be at least 300 mm);
- Designed manhole covers to withstand anticipated loads & ensure that the covers can be readily replaced if broken to minimize silt/ garbage entry;
- Ensured sufficient hydraulic capacity to accommodate peak flows & adequate slope in gravity mains to ensure self-cleansing velocity in order to prevent built up of solids and hydrogen sulfide generation;
- All structural, layout and engineering designing are in strict accordance with the applicable codes and engineering standard;
- The location of overhead water tanks, pumping station and STP have been finalized in close consultation with local community and representatives of local authorities;
- Tree cutting has been avoided;
- Efficient seepage control measures have been considered in selection of pipe materials during the planning stage;
- Effluent generated during construction phase will be treated through septic tanks.

- Alignments of sewerage and water supply lines have been carefully selected to minimize disturbance to public utilities;
- Relocation of the public utilities, if any, shall be planned and approved in consultation with relevant departments/authorities/stakeholders before project commencement to avoid inconvenience to the public;

6.5 Anticipated Impacts during Pre-Construction/Design Phase

Impacts envisaged during Pre-construction/ Design Phase and the recommended mitigation measures are given below:

6.5.1 Layout Planning & Design

Potential Impact

Incompatible layout plans and engineering designs of the proposed project can undermine the overall aesthetics and ambience of the project area. Misutilization of the available spaces may result in a design with low social acceptability and functionality. This impact will be permanent and moderately adverse.

Mitigation Measures

- All structural, layout and engineering designs of the project are in strict accordance with the applicable national and international guidelines/ codes/ standards and engineering practices;
- The layouts of water supply and sewerage networks have been adjusted to cover the whole project area. The water supply system is a loop-based system and the sewerage system is based on gravity where the slopes have been provided to ensure gravity flow with adequate velocity.

6.5.2 Soil Instability

The sandy soil conditions in the project area may create challenges for laying water supply and sewer lines/drains. Trenches in sandy ground are prone to collapse, increasing excavation risks and construction difficulties. Higher infiltration rates in sandy areas may also lead to leakage and contamination concerns if pipes are not properly sealed. Stability of manholes and other structures could be compromised due to weak soil bearing capacity. These conditions may result in increased construction costs, time delays, and the need for additional stabilization measures.

Mitigation Measures

- Use proper shoring and trench support systems to prevent collapse in sandy soils.
- Seal pipes and joints with high-quality materials to control leakage and infiltration.
- Provide adequate bedding and foundation treatment for manholes and structures.
- Ensure regular site supervision for safe practices and timely corrective measures.

6.5.3 Impacts of Drains construction

Inadequate sizing or gradients may lead to poor flow, blockages, or flooding during peak conditions. Improper alignment can cause conflict with existing utilities and affect land use. Selection of unsuitable materials or inadequate lining may result in erosion,

siltation, or structural failure. Therefore, proper hydraulic design, durable materials, and integration with the overall sewerage system are critical for long-term performance.

Drain slab structures are vulnerable to damage when subjected to vehicular movement, especially from loads exceeding their design capacity. Continuous stress from unsuitable vehicles leads to cracks, structural deterioration, and eventual failure of the slabs. This not only disrupts drainage flow but also creates safety hazards in the project area.

Mitigation Measures

• Plan proper alignment and depth to avoid conflicts with existing utilities and infrastructure.

• Ensure accurate hydraulic design with proper gradients to maintain self-cleansing velocity and avoid blockages.

• Provide adequate cross-sections and freeboard to handle peak stormwater flows safely.

• Incorporate silt traps and access points for ease of maintenance and prevention of clogging and

• Use reinforced, traffic-rated slabs designed for expected vehicle loads, and restrict heavy vehicle movement over drains. Regular inspection and timely maintenance should also be ensured to prevent structural failure.

6.5.4 Environmentally Responsive Design Considerations

Potential Impact

Designing the project components without considering the prospective and futuristic needs can result in structures with low social acceptability and functionality. Improper-designed sewers may not carry the waste load, leading to system-failure and financial losses. The alignment of sewer lines and locations of sewerage pumping station and STP must be properly planned, or else it may lead to both technical and social problems along with environmental issues of backflow creating foul smell and unhygienic conditions.

There are chances of infiltration from sewers which may contaminate the soil and underground water resources. The seepage may also affect the water supply lines and contaminate the potable water.

The construction of high-rise overhead water tanks may cause visual obstruction. The surrounding community may face privacy issues and it may also cause blockage of direct sunlight.

Mitigation Measures

- All sewer lines including trunk, lateral and branch sewer lines have been designed considering the future population and waste generation rate;
- Limit the sewer depth where possible;
- Sewers will be laid 1m away from water supply lines if the width of the street will be sufficient to do so.

- In all cases, the sewer lines shall be laid below water pipeline (the difference between top of the sewer and bottom of water pipeline shall be at least 300 mm);
- Designed manhole covers to withstand anticipated loads & ensure that the covers can be readily replaced if broken to minimize silt/ garbage entry;
- Ensured sufficient hydraulic capacity to accommodate peak flows & adequate slope in gravity mains to ensure self-cleansing velocity in order prevent to built-up of solids.
- The location of overhead water tanks, pumping stations and STP have been finalized in close consultation with local community and representatives of local authorities.

6.5.5 Groundwater

Potential Impact

Groundwater contamination may occur during construction by the improper handling of construction material (fuel, lubricant, bitumen, asphalt etc.) or sanitary water from construction camps and domestic sewage. During operation probability of seepage through the sewers may also contaminate groundwater. This impact is permanent and moderate negative in nature.

Mitigation Measures

- Construction materials that may lead to groundwater contamination will be properly handled and stored.
- Procedure for efficient jointing of selected sewer pipes will be applied to avoid leakage from pipes;
- Alternate sewage disposal arrangements have been suggested in design to cater the sewage flow, generated from the project area, during construction phase.

6.5.6 Surface Water

Potential Impact

There is no existing piped sewerage network or pumping station in the village. There is one large sewage pond in the villages where sewage is disposed by unplanned drains. Thus, endangering the environment of the vicinity. The openly flooded sewage causes nuisance in terms of foul smell and serves as breeding ground for disease causing vectors. Some sewage is also used to irrigate nearby crops.

There will be net environmental improvement in terms of sewage collection thus reducing sewage ponding in the project area and enabling adequate treatment of wastewater.

Mitigation Measures

- The sewage will be collected through a piped network;
- An STP based on ABR technology will be established to treat the sewage;
- The treated effluent as per PEQS will be discharged into the existing watercourses i.e nullahs, for agricultural purposes.

6.5.7 Seismic & Other Hazard

Potential Impact

According to the seismic zoning map of Pakistan, the project area of Kot Momin located in Seismic Zone 2A. A low to moderate-intensity earthquake impacting the project site can adversely impact the development. Some area of Kot Momin faced flood recently as they are located on the belt of Chanab River.

Although Liaqatpur Tehsil lies within a low to moderate seismic zone, flooding represents the more significant natural hazard in recent years. Flooding is mainly driven by monsoon rainfall, canal overtopping or breaches, inadequate surface drainage, and backflow from irrigation systems rather than riverine sources. Approximately 20-25% of the tehsil is classified as high flood hazard, 35-40% as moderate risk, and the remaining 35-45% as low flood hazard. Vulnerability is highest in low-lying chaks near canals and drains, where prolonged waterlogging causes damage to housing, agriculture, and access infrastructure.

Several villages within the South-III Cluster (Tehsils Khairpur Tamewali and Bahawalnagar) and the Central Cluster (Tehsils Ahmadpur Sial, Bhawana, and Darya Khan) are located in flood-prone areas. In view of the associated flood risk, all proposed structural facilities have been designed with appropriate flood-resilience measures. These measures include elevating the structures approximately 3–4 feet above the existing ground level to reduce the risk of floodwater ingress and associated damage. The raised design is intended to enhance the safety, functionality, and long-term resilience of the infrastructure during seasonal flooding events.

This factor requires special consideration of the designers as project structures (especially overhead water tanks and STP) may be affected negatively in case of earthquake tremors and the significance of damage depends upon the severity of earthquake.

Mitigation Measures

- The components of the proposed project include laying of underground water supply network, sewer lines, construction of overhead water tanks, pumping station and STP have been designed to withstand moderate earthquakes; and
- To mitigate the seismic hazard, Seismic Building Code of Pakistan 2007 (SBC-07) has been adopted. This code specifies minimum requirements for seismic safety of buildings/ structures and has to be applied and used by engineers in conjunction with the necessary understanding of the concepts of structural, geotechnical and earthquake engineering.
- Avoid siting critical infrastructure in flood-prone villages where feasible;
- Raise plinth levels of buildings above known flood levels;
- Strengthen canal embankments and improve desilting of drains;
- Introduce flood-resilient sanitation designs (sealed latrines, raised platforms);
- Establish community-based flood early warning and evacuation plans.
- Improve surface drainage networks and regular maintenance of existing drains;
- Ensure proper solid waste management to prevent blockage of drainage paths;

- Promote flood-resilient housing improvements and water source protection measures.

6.5.8 Damage to Existing Infrastructure

Potential Impact

The proposed project interventions are mostly subsurface activities and are likely to affect the existing infrastructure. Public utilities such as electric poles might get affected during construction activities and movement of machinery and the community will face temporary electricity cuts. Furthermore, the roads will be cut for laying of water and sewerage pipes and will create accessibility issues.

Mitigation Measures

- Alignment of water supply and sewerage network carefully selected to minimize disturbance to public utilities;
- Relocation of the public utilities shall be planned and approved in consultation with relevant departments/authorities/stakeholders before project commencement if any, to avoid inconvenience to the public;
- The local community will be informed before the relocation of services (if any) and schedule of relocation services will be prepared after consultation with the community to minimize inconvenience to the public;

6.5.9 Physical Cultural Resources

Potential Impact

No historical/ archeological site is present in the project area. However, some cultural resources including mosques, graveyard and shrines are present. People visit the mosques five times a day. Shrines and graveyard are visited occasionally by the surrounding community and devotees. These will not be directly affected but the people may face access issues in visiting these facilities.

Mitigation Measures

- The alternative access routes will be provided in case the access has to be restricted during execution period; and
- There must not be any physical impact on the physical and cultural resources in the project area.
- The possible discovery of archaeological sites or random findings during the excavation and earthworks may occur. In such case, World Bank's OP 4.11 will be triggered. Furthermore, Annexure 4 for Chance Find Procedures will also be implemented.

6.5.10 Fire Fighting System

Potential Impact

Absence of a firefighting system may cause severe damage to the camp site and surrounding crops and houses during construction phase.

Mitigation Measures

- Contractor will provide an efficient firefighting system (i.e fire alarm and fire extinguishers) for campsite, workshop and construction site; and
- Campsite will be established in an area with easy access to the water source, helpful in firefighting in case of any incident.

6.5.11 Land Acquisition

The main focus of the project is to install sewers and water supply lines, which requires the use of existing streets and roads for right-of-way (ROW). If private streets or roads are encountered, the project team consults landowners prior to commencing any construction activities to gain permission for the use of their land. Moreover, land is also required for the construction of water supply infrastructure: stand-post, tube well, and OHR; wastewater treatment plant; and solid waste collection points. State land has been the priority for the project activities. Similarly, 2611.18 marla state land is being used for project infrastructure in 06 villages of Ahmadpur Sial and Pakpattan. Whereas, due to the unavailability of state land in the remaining villages, a total of 4921.37 marla private land through voluntary land donation (VLD) is being used. The process of VLD is given in Annex-8.

Priority has been given to the state land that is free of encumbrances i.e., free from any legal/ illegal claims of any squatters, illegal occupants, etc. Therefore, the implementation of RAP/ ARAP is not required in the Phase-II villages.

Mitigation Measures

- Primarily, state land was used for the project infrastructure activities, however, private land through Voluntary Land Donation (VLD) is also being used in case of unavailability of state land.
- Additionally, in order to minimize the potential negative socio-economic impacts of land acquisition, minimum parcel of land has been proposed to meet the needs of the proposed project in case of private land; unlike in the cases of state land where – considering the future needs of the project expansion – sufficient parcel of state land has been acquired/ proposed.
- In case there is no state land or private land through VLD is available, PRMSC will consider the option of land acquisition, after developing and implementing a Resettlement Action Plan (RAP) approved by the World Bank. Compensation will be paid in accordance with the resettlement framework outlined in the Environmental and Social Management Framework (ESMF).
- Furthermore, the approval / NoL for each VLD case will be sought exclusively from the World Bank.
- A VLD checklist form has also been developed to assess the potential negative socio-economic and livelihood impacts of private land acquisition (Annexure-8A).
- Besides the VLD checklist, VLD tracking sheet has also been developed (attached as Annexure-8B) which will be continuously updated, the same will be available for monitoring of VLD status.

- Without any transparent consent land will not be used through VLD (Procedure as per Annex 8 will be followed plus use of a screening form that assesses the impact of the VLD on the prospective donor is provided at Annex-8A);
- In case of private donors, only less than 10% of their land could be obtained;
- 100% compliance will be ensured of VLD procedure given in ESMP;
- VLD process will be executed by the PRMSC itself, and will not be devolved to any private parties (consultants or contractors).
- Before start of construction activities, it will be ensured that the land (private or public) is free from any form of encumbrances or where there are informal users, they are appropriately provided relocation assistance - in accordance with OP 4.12 – Involuntary Resettlement - before taking possession of land.

6.6 Anticipated Impacts during Construction Phase

Anticipated Impacts during Construction Phase and the recommended mitigation measures are given below:

6.6.1 Topography

Potential Impact

The construction activities are not expected to impact the topography of the area significantly except for those areas where physical activities i.e., earthwork is involved as well as stocking of material. The excavated material is to be mostly backfilled and the excessive material will be transported to strengthen the roadsides or will be dumped at the designated locations. This impact is site-specific, temporary, reversible, possible, and low significant.

Mitigation Measures

- Material stockpiles will be removed as soon as work is completed and the area will be reinstated;
- Temporary storage sites will be allocated for the storage of excavated material;
- Temporary storage sites will be lined and must not allow infiltration;
- The stockpiles must be covered with tarpaulin sheets or other adequate material;
- Pilling of material at large extent will not be allowed and the contractor will timely remove excavated material from the site.

6.6.2 Soil Erosion

Potential Impact

The soil would be exposed to erosion due to excavations for laying of sewers and water supply pipes. Construction activities such as clearing, excavation, filling, grading and setting up construction camps will affect the existing soil condition in the study area/ AoI. The clearing of vegetation can also loosen the soil and make it more susceptible to erosion due to wind and rain. There is also a possibility of silt runoff during rainy season causing soil erosion. This impact can be categorized as low adverse, site-specific, long-term, highly probable and reversible.

Mitigation Measures

- Good engineering practices such as proper compaction of backfill material and special slope protection measures will be adopted during the construction stage.
- Use of heavy machinery will be restricted as far as possible to avoid the destruction of soil structure;
- Confining excavations to the specified spots as per the approved engineering drawings and unnecessary excavations should be avoided;
- Stored excavated material shall be covered and preferably reused, e.g., in construction as backfill etc.
- Cutting of trees will be avoided to the best possibility to avoid soil erosion.

6.6.3 Soil Contamination

Potential Impact

Contamination of soil may be caused by oil and chemical spills from construction machinery or uncontrolled runoff from equipment washing yards. This impact is permanent and minor negative in nature.

Mitigation Measures

- Chemicals/ hazardous products and wastes will be stored on impermeable surfaces in secure, covered areas with clear labelling of containers and with a tray or bund to contain leaks;
- All construction wastes from the site will be regularly collected and transported to approved waste disposal sites;
- Awareness of emergency spill response procedures will be provided to the workers on-site;

6.6.4 Trench Failure

Potential Impact

The major construction activities involve excavation operations for laying water supply and sewerage lines. The major hazard associated with the excavation operations is trench failure. The unstable slopes may fail and settle in the trenches which may cause injuries and fatalities to the workers. This impact is probable, site specific and high adverse in nature.

Mitigation Measures

- Careful selection of the site for excavation in light of soil investigation is inevitable
- Provision of adequate shuttering in the trenches;
- Leftover shuttering may also be used in case of loose soil strata.

6.6.5 Construction Camps/Camp Sites

Potential Impact

Improper construction camp location and mismanagement of construction camp activities can lead to various social and environmental impacts which may include noise, health and safety, traffic problems, soil degradation, loss of vegetation and assets on the selected land, solid

waste and water pollution. Furthermore, cultural differences, the behavior of construction workers, potential disregard for local cultural norms can lead to increased tension between local communities and workers residing in the construction camps. This impact is temporary and moderately negative in nature.

Mitigation Measures

- Working hours of noisy activities will be limited to normal daytime working hours when near identified sensitive receptors;
- Waste Management Plan will be implemented to include procedures for the classification, storage and disposal of all construction wastes and the training of employees who handle hazardous materials; and
- Construction camps will be established away from populated areas and NOC/lease agreement will be obtained from private land owners.
- Regular training of workers will be carried out regarding local cultural norms, human behaviour, gender issues and GRM by the contractor during construction activities at site.
- Implementation of code of conduct

6.6.6 Water Quality

Potential Impact

Runoff from the construction works site may contain an increased load of sediments, suspended solids and other contaminants. Potential sources of pollution from the site include:

- Runoff and erosion from exposed soil surfaces, earthwork areas and stockpiles e.g., grouting and cement material with the rain;
- Wash water from dust suppression sprays;
- Fuel and lubricants from maintenance of construction vehicles and mechanical equipment;
- Spillage of liquids stored on-site such as oil, diesel, and solvents etc. are likely to result in water pollution; and
- Uncontrolled discharge of debris and garbage such as packaging, construction material and refuse.

Construction waste, if left unattended will result in forming leachate that will percolate through the soil strata and will reach underground water table and hence, will end up contaminating groundwater. There is a probability that various materials like fuel, lubricant oil and other oily products, which are used during the construction phase may contaminate groundwater and channels carrying water.

There is no major surface water body near the project sites, however, canal distributaries and watercourses are present for irrigation purposes which may get contaminated.

Mitigation Measures

- Protection of groundwater reserves from any source of contamination such as the construction and oil waste by making the ground impermeable through sheets or compaction;

- Stockpiles of cement and other construction materials will be kept covered when not being used;
- Maintenance of vehicles will be carried out only in impermeable areas where any oil spillages can be contained;
- Careful planning of the works to avoid soil excavation works during rainy seasons;
- Controlled activities will be undertaken during monsoon and careful attention must be paid to weather forecast before excavation operations.
- All kinds of waste will be stored in covered containers and disposed of safely as soon as possible; and
- By proper C&D waste management system in place, the contractor will ensure that construction debris does not find its way into the drainage or irrigation channels.

6.6.7 Air Quality

Potential Impact

Air quality will be affected by various construction activities like emissions from generator stack vehicular exhaust, VOCs from uncovered gasoline i.e petrol/diesel, and manoeuvring of construction and public vehicles on construction site. Emissions may be spread over longer distances depending upon the wind speed, direction, temperature of surrounding air and atmospheric stability. In certain climatic condition such as hot summer, airborne dust can become a major nuisance if control techniques are not properly employed.

The air emissions may cause health impacts such as dryness and roughness of the throat, eyes, nose, etc. to the workers, staff of the contractor and the residents of area. These emissions may also affect the bio-physical environment. The impact is negative and temporary in nature.

Mitigation Measures

- All vehicles, machinery, equipment and generators used during construction activities will be kept in good working condition, properly tuned and maintained to minimize the exhaust emissions;
- Open burning of solid waste from the contractor's camps will be strictly banned;
- Personal Protective Equipment (PPEs) like masks, goggles and gloves etc. will be provided to workers;
- PEQS applicable to gaseous emissions generated by construction vehicles, equipment and machinery will be enforced during construction works.
- Regular water sprinkling on the site and access roads will be carried out to suppress excessive dust emission(s);
- Blowing of dust and particulate matter from stockpiled loose materials (e.g., sand, soil) will be avoided either by sheeting them with tarpaulin or plastic sheets or by sprinkling them with light shower of water;
- The vehicles carrying construction materials and the construction material storage areas will be covered with tarpaulin.
- Sensitive receptors of the area will be informed accordingly

6.6.8 Noise

Potential Impact

Noise level is expected to increase during construction activities. Main sources of noise and vibration will be heavy machinery such as excavators and other equipment. Noise generated by construction machinery is likely to affect sensitive receptors located within AoI. Health risks associated with exposure to continuous noise levels include high blood pressure, hypertension, annoyance and sleep disturbance, temporary threshold shift etc. The impacts of noise will be temporary and highly adverse in nature.

Mitigation Measures

- Construction workers will be provided suitable hearing protection like ear cap, or earmuffs and training them in their use;
- Selection of up-to-date and well-maintained equipment with reduced noise levels will be ensured by suitable in-built damping techniques or appropriate muffling devices; and
- Residents will be notified earlier before the commencement of excavation operations.
- Construction activities will be restricted to the day-time.
- Sensitive receptors will be informed accordingly.

6.6.9 Municipal and Construction Waste/ Wastewater

Potential Impact

Due to construction activities municipal and construction waste will be generated from construction activities. The waste will include wastewater, domestic waste and construction waste etc.

Improper dumping of waste may generate odor and attract mosquitoes and other disease vectors. Waste bins containing toxic, flammable and corrosive materials may pose a hazard to the workers when handled without PPEs. Unsuited waste disposal site selection may pose a serious health concern to the locals and workers onsite. The impact is temporary and minor negative in nature.

Mitigation Measures

- Solid waste generated during construction and campsites will be safely stored, collected, transported and disposed of at the selected disposal site and the contractor will provide and implement a comprehensive solid waste management plan;
- Burning of waste will be prohibited;
- Proper labeling of containers, including the identification and quantity of the contents, hazard contact information etc;
- Closed waste storage bins will be provided on-site to store waste.

6.6.10 Chance of Finding Artifacts

Potential Impact

During excavation, there is a chance of finding artifacts. In case of finding any artifact, the contractor will immediately stop the activities and report through Supervision Consultant to

Directorate General (DG) of Archeology, Government of Punjab to take further appropriate action to preserve those antiques or sensitive remains. Chance find procedures are attached as Annexure 4.

6.6.11 Resource Conservation

Potential Impact

The materials used in the construction of proposed project would include coarse aggregates (crush), fine aggregates (sand), brick ballast, water and cement etc. Almost all the materials to be used in the construction of proposed project are non-renewable and therefore their sustainable use is necessary for future use.

Large quantities of water will be used in the construction of concrete pipes, drains, pumping stations, STP, cradles and in watering the unfinished surfaces.

Diesel and residual fuel oils will be used to operate construction machinery and equipment. Sustainable use of energy resources is very important and it will also help to reduce air emissions. For conservation of energy, efficiency of the engines and burning processes is very important.

Mitigation Measures

- Wastage of water will be reduced by training the workers involved in water use;
- Water jets and sprays will be used for watering surfaces rather than using overflow system.
- Reuse of construction waste materials will be considered.
- The efficient and well-maintained equipment and machinery will be used.
- The equipment and machinery will be turned off when not in use.

6.6.12 Biodiversity Conservation

Flora

Potential Impact

On account of construction of the proposed water supply and sewerage system, no trees are envisaged to be cut/disturbed but some herbs or shrubs may be required to be removed for excavation. The dust emissions due to excavation operations will stick to the leaves of existing trees and may close their stomata thus hindering the photosynthesis process. Reduced photosynthesis may also reduce the productivity of existing trees. This impact is however temporary but minor negative in nature.

Further, during construction activities the Contractor's workers may damage the vegetation and trees (for use as fire-wood to fulfill the camp's requirements).

Mitigation Measures

- The Contractor's staff and labour will be strictly directed not to damage any vegetation such as trees or bushes. They will use the paths and tracks for movement and will not be allowed to trespass through farmlands;
- Contractor will provide gas cylinders at the camps for cooking purposes and cutting of trees/ bushes for fuel will not be allowed.

Fauna

Potential Impact

There will be no damage to health and life of local animals mostly cats, dogs and jackals and especially the livestock i.e., goats and cows due to construction activities. Some reptiles and insects may get killed/ injured during excavation operations.

Mitigation Measures

- Excavations will be limited to the approved engineering drawings;
- Physical barricades will be provided at critical location near construction sites for restricted movement
- Harassing of animals will be prohibited.

6.6.13 Health and Safety

A. Occupational Health and Safety

Potential Impact

OHS-related risks include working at height (at excavation site & OHT construction site) Health risks and workers safety problems may result at the workplace if the working conditions provide an unsafe and/or unfavorable working environment. The health and safety issues are also associated with the operation of construction machinery and equipment, which may cause minor and severe injuries to workers. It will be a long-term and severe negative impact.

Mitigation Measures

- Obligatory insurance against accidents for labourers/workers;
- Providing basic medical training to specified work staff and basic medical service and supplies to workers;
- The Contractor's Health and Safety Officer will identify, record, and subsequently send the deployment and activity plan to the supervision consultant's Health & Safety Expert (HSE) who will analyze the hazards of the job and issue the No Objection Certificate (NOC), accordingly.
- Layout plan for camp site, indicating safety measures taken by the contractor, e.g., firefighting equipment, safe storage of hazardous material, first aid, security, fencing, and contingency measures in case of accidents;
- Use of Personal Protective Equipment (PPE) i.e., ear muffs, masks, safety shoes, gloves etc.;
- Use of safety signs at the construction site, as shown below.

- Contractor will immediately inform the consultant about the project related incident. The consultant will then submit a preliminary report to the PRMSC within 24 hours.

Resultantly, PRMSC will promptly notify the World Bank for project-related incident within a maximum timeframe of 48 hours.

B. Community Health and Safety

Potential Impact

The construction activities and vehicular movement at construction sites may result in roadside accidents particularly inflicting local communities who are not familiar with presence of heavy equipment. This is a temporary and moderate negative impact. Open trenches and deep manhole may cause trip & fall accidents for the local residents.

Mitigation Measures

- Medical screening of the laborers for communicable diseases will be conducted before hiring. Medical screenings are a basic requirement before the hiring of labour to prevent the spread of communicable diseases. However, on the basis of these screenings, diseased potential workers will not be barred from work; instead, necessary measures will be taken to prevent the spread of these diseases.
- The site will be restricted for the entry of irrelevant people particularly children.
- Provision of proper safety and diversion signage, particularly at sensitive/accident-prone spots;
- Setting up speed limits within the village.
- Open trenches and deep excavated manholes will be protected by fence/barricade to avoid any accident.
- Night time lighting will also be provided.
- Awareness campaign regarding HSE will also be provided to local community including at schools.
- Awareness/ training session of labourers will be conducted to promote clean behaviour practices and to curtail medical issues.
- Special consultation session will be held with the nearby medical facility to ensure that it is well informed and well equipped to handle any dust allergy cases if required.
- Contractor will immediately inform the consultant about the project related incident. The consultant will then submit a preliminary report to the PRMSC within 24 hours. Resultantly, PRMSC will promptly notify the World Bank for project-related incident within a maximum timeframe of 48 hours.

C. Emergency Response (Natural and Man-Made Disasters)

Potential Impact

Natural calamities such as flood and man-made disasters such as fire, falls, slips and trips may result in injuries, financial losses and may even lead to deaths. Flooding can result in inundation of the village area and excavation / trenches which may leads to accidents or can damage the infrastructure of the project activities. Similarly, during operation it can affect the water supply, and sewerage system. The workers will be trained and facilitated to cope with such emergencies.

Mitigation Measures

- Training of the staff/employees regarding the emergency procedures/plans will be regularly conducted;
- Emergency numbers will be clearly posted; and
- First aid boxes will be provided.
- Minor incidents and near misses will be reported and preventive measures will be formulated accordingly.

6.6.14 Traffic Management

Potential Impact

The traffic influx within the villages is very low. Most of the traffic within the villages include motorbikes and few cars. The project interventions will not create traffic congestion issues in the project area. However, their movement will be disturbed due to the excavation and construction works and people may face accessibility issues. This impact is temporary and major negative in nature.

Mitigation Measures

- The construction activities will be carried out in pockets/reaches, once a patch has been completed (i.e., pipes are laid and covered) then excavation on new patch shall be started;
- Local community will be taken on board to plan alternate access routes in connecting streets to ensure mobility of local traffic; and
- Plan work in a minimum possible time.

6.6.15 Nuisance/ Disturbance to Sensitive Receptors (Educational, Health and Religious Places)

Potential Impact

Since the proposed interventions will be carried out within the village boundaries, therefore, the socially sensitive sites/places including schools, hospitals and religious centers will be temporarily affected due to dust, noise and the community will face accessibility issues due to open trenches. Dust due to earthworks will create health hazard to children and people with ailments. This impact is temporary and major negative in nature.

Mitigation Measures

- Work will be conducted near the religious places with due social diligence and after informing all stakeholders
- Material transport to the site will be scheduled considering school timings;
- Notify concerned schools, hospitals/dispensary etc. 2 weeks prior to the work; conduct a 30 minutes awareness program on nature of work, likely disturbances and risks and construction work, mitigation measures in place, entry restrictions and dos and don’ts; and
- Implement all measures suggested in this report viz. dust and noise control, public safety, traffic management, strictly at the sites.

6.6.16 Accessibility

Potential Impact

Excavation of trenches and pipe/sewer laying work in the project area will obstruct access to residences, commercial buildings and businesses adjacent to the proposed project alignment. Disruption of access to commercial establishments may affect livelihood. The potential impacts are negative and moderate but short-term and temporary.

Mitigation Measures

- Leave space for access between mounds of excavated soil;
- Consult affected people to inform them in advance about the work schedule;
- If there are any holidays (i.e., Eid or Muharram etc.), the Contractor will complete the backfilling work of the trenches and will not leave any trench open before holidays;
- Provide sign boards for pedestrians to inform nature and duration of construction works and contact numbers for concerns/complaints.

6.6.17 Gender-Based Violence (GBV)

Potential Impacts

During the construction phase, gender-based violence might arise due to influx of outside labor. Sexual harassment against women might occur as a consequence of mixing of men and women at the construction site, and moving on the roads and markets.

Mitigation Measures

With the effective measures and monitoring, the risk of gender-based violence will be minimized by adopting the following mitigation measures:

- Awareness will be created among the females at community levels about the construction.
- Workers will not be allowed to crowd in the residential area/villages.
- Alternative routes and traffic management plans for the safety of the community particularly for women and children will be ensured.
- Raise awareness among the communities regarding the potential risks of GBV, and establish response services in the nearby communities that can respond to instances of GBV (particularly those related to issues of labor influx);
- Contractor will take proper measures and will ensure Gender Sensitive Grievance Redressal Mechanism to address and resolve issues relating to harassment, intimidation, and exploitation.
- GBV-related issues will be recorded through GRM, two separate focal persons for males and females are part of Village Organization VO – which will also work as members of the Grievance Redressal Committee (GRC) Tier-I. The female focal person – trained on the social protection referral directory – will be responsible for further referral of GBV-related complaints to the forums concerned. A multi-sectoral referral system is proposed, which will include referral to The Punjab Women's Toll-Free Helpline 1043 available 24/7. It is managed and supervised by Punjab Commission on the Status of Women (PCSW). Their helpline team comprises all-

women call agents, three legal advisors, a psychosocial counsellor, supervisors, and management staff. The Punjab Commission on the Status of Women (PCSW) has been identified as a key stakeholder. PCSW will be informed of the project activities and an institutional link will be established.

- At the PRMSC Tehsil Office, the Behavior Change and Communication (BCC) Officer – in addition to being member of GRC Tier-I&II – will initially deal with gender related issues/ complaints and further refer the same to the Gender Specialist at Head Office, PRMSC.
- The Contractor will prepare the Codes of Conduct to prevent occurrence of GBV and get it signed by all workers, and effectively communicate to all workers and project beneficiaries.

6.6.18 Influx of Labor

Potential Impacts

For the implementation of project activities, skilled and unskilled labor is required by the contractor. Mostly, skilled and unskilled workers have been associated with the contractor since a long which they utilize, where they are required for the projects, and while other workers are hired from different areas that belong to different cultural backgrounds. Social problems and conflicts that are associated with labor influx are as follows:

- **Risk of social conflict**: Conflicts may arise between the local community and the construction workers, which may be related to religious, cultural or ethnic differences, or based on competition for local resources;
- **Increased risk of illegitimate behavior and crime:** The influx of workers and service providers into communities may increase the rate of crimes and perception of insecurity by the local community. Such illegitimate behavior and crimes can include theft, physical assaults, substance abuse, sexual assault and human trafficking;
- **Increased risk of communicable diseases and burden on Tehsil & District health services:** The influx of people may bring communicable diseases to the project area, including sexually transmitted diseases (STDs), or the incoming workers may be exposed to diseases to which they have low resistance. Workers with health concerns relating to substance abuse, mental issues or STDs may not wish to visit the project's medical facility and instead go anonymously to the nearby medical center, this can result in an additional burden on tehsil & district health centres; and
- **Local inflation of prices, accommodations and rents:** A significant increase in demand for goods and services due to labor influx may lead to local price hikes and crowding out of community consumers. Depending on project worker income and form of accommodation provided, there may be increased demand for accommodations, which again may lead to price hikes and crowding out of local residents.

Mitigation Measures

- Labour camp(s) will be established away from residential areas;

- Preference will be given to the local people to work with contractor, and contractor should hire maximum labour force from the project area because this will reduce the labour influx;
- Awareness will be created among the workforce to ensure respect for local customs;
- An effective GRM has been established for the project to resolve all issues related to the community. Thus, progress regarding resolving the issues should be monitored closely.
- Create awareness among workers on proper sanitation and hygiene practices to endorse proper health and maintain good housekeeping practices at all project sites;
- Make arrangements to treat the affected workers on time to control the movement of vectors disease;
- Provide proper and free medical screening and counselling for site workers and community members;
- Develop and enforce a strict code of conduct for workers to regulate behaviour in the local communities;
- Labour will be required to sign a code of conduct translated into their local languages at the time of hiring.
- Prohibiting drugs, alcohol, weapons, and ammunition on the worksite among personnel;
- Appropriate fencing, security checkpoints, gates and security guards should be provided at the construction sites to ensure the security of all plant, equipment, machinery and materials, as well as to secure the safety of site staff; and
- The Contractor must guarantee that good relations are maintained with local communities and their leaders to help reduce the risk of vandalism and theft.

6.6.19 Social/ Cultural Conflicts

Potential Impact

During the construction phase of the project, conflicts may arise between labor force and local community. Furthermore, differences in cultural values may also cause discomfort to local residents. This impact is temporary and minor negative in nature.

Mitigation Measures

- Plan for social grievance redress mechanisms including the local leaders and community representatives;
- Local labor will preferably be employed for construction works;
- Careful planning and training of the workforce to minimize disturbance to the local people;
- Robust and transparent GRM will be implemented

6.6.20 Child Labor

Potential Impact

Due to poverty and the feeble financial situation of the area, the underage children might get involved with the contractor various construction works. This will be the violation of the Child Labor Act. Furthermore, SEA/SH issues might arise which will create social conflicts. This impact is adverse and temporary in nature.

Mitigation Measures

- Standard clause in the contracts related to child labor explicit prohibitions, etc. and contractor will ensure compliance to the contractual provisions as per law of land. Similarly equal wages for similar work will be followed.

6.6.21 Economic Activity

Potential Impact

Due to the construction of the proposed Project, economic activity will be generated in the project area as the laborers and semi-skilled staff will have an opportunity to work in the project area. This will provide them an opportunity to develop their skills and capacities. It will also benefit the local vendors of the project area. This is a positive impact.

6.7 Anticipated Impacts during Operational Phase

Anticipated impacts during Operational Phase and the recommended mitigation measures have been described under biophysical and socio-economic categories as follows:

6.7.1 Soil

Potential Impact of STP

The soil quality may be affected due to leakage/ infiltration from sewer lines and STP bed. The sludge generated from cleaning/ maintenance of pumping stations, manholes, sewers and STP may contaminate the soil. The liner of the STP, while desludging may get dried and cracks may lead to the seepage of wastewater and thus contaminate the soil. Improper disposal of scum and sludge is another concern. This is a moderate negative impact.

Potential Impact of Leachate from Dumping Site

The collected solid waste will be dumped into the existing dumping sites of Tehsils. There is no arrangement of leachate collection and no liner material is present there which will result in contamination of soil due to leachate. The situation will exacerbate in the rainy seasons. This is moderate negative impact.

Mitigation Measures

- Sludge shall be treated before ultimate use/disposal. Various options for sludge treatment include Digestion, Drying/ Dewatering, Composting, Lime Stabilization, Heat Treatment must be considered etc;
- The liner of STP must be regularly maintained and checked for any cracks and leakages;
- Treated sludge should be properly disposed of in an environmentally friendly manner.

6.7.2 Air Quality

Potential Impact of Sewerage System

The operation of sewerage scheme will result in generation of gases including H_2S and CH_4. H_2S is a foul-smelling poisonous gas that might be harmful to the sewer men and could be fatal sometimes. CH_4 is natural gas also referred to as a greenhouse gas. Pakistan is signatory to the United Nations Framework Convention on Climate Change (UNFCCC) and adopted Kyoto Protocol in 1997. Under the Kyoto Protocol, Pakistan is committed to reduce GHG emissions into the environment to prevent interference with climate change. The GHG emissions for the proposed project are a concern due to the anaerobic conditions in the sewer lines and wet wells of the disposal station.

Mitigation Measures

- Provision of exhaust gas vents at appropriate locations in the design;
- Sewer-men will cover their faces with gas mask while entering the sewer for cleaning or maintenance purposes;
- It's better to use sucking machinery for cleaning of sewers;
- Use gas detector before inspection;
- Adequate tree plantation must be done around the STP to control the spread of odour;

6.7.3 Odour

Potential Impact of STP

STP are designed on adequate waste loading and function well if they are not overloaded. The overloading will result in malfunctioning of STP and it will result in significant odour generation in the vicinity. This impact is temporary and high adverse in nature.

Mitigation Measures

- The STP should not be overloaded and personnel dealing in operation should be trained to avoid operational issues;
- Adequate tree plantation must be undertaken to avoid spread of odour in the vicinity.

6.7.4 Elite Capture

During the VLD process it was ensured that land will not be donated by landowners having more than 25 acres land size to avoid elite capture. This has resulted in a situation where the elites have disproportionate control over resources, policies, and decision-making processes in all over the province. Elite capture is often facilitated by corruption, nepotism, and patronage networks, which enable the elites to manipulate the system in their favor. The consequences of elite capture are far-reaching, with the general public often left without access to basic amenities such as health, education, water and sanitation. This has resulted in widespread inequality, marginalization, and poverty in Punjab. Landowners play role as elite capture while donating the land to get the rights to use of water, sewage treated water for agriculture.

Mitigation Measures

- To avoid elite, capture the VLD will not be accepted from the person having more than 25 acres land.

- To increase transparency and accountability in decision-making processes.
- Involving multiple stakeholders, including community members, in decision-making processes related to project activities.
- To promote the participation of marginalized groups, such as women and minorities, in decision-making processes. By ensuring that these groups have a voice in decision-making, the risk of elite capture can be reduced.
- Strengthening institutions such as VO's/VC's and regulatory agencies can help ensure that decisions are made in a fair and equitable manner, without undue influence from elites.
- To ensure an effective grievance mechanism for monitoring and reporting any cases of elite capture.
- Robust and transparent GRM will be implemented
- VO's will be strengthened to play a role during distribution of treated water to prioritize the needs of the entire community rather than just a select few elites.
- Due diligence will be held during VLD process to absolve the doner from all the associated land rights.

6.7.5 Social Inclusion

Social inclusion is the process in which individuals and groups take part in the society. Social inclusion in proposed project area is an important aspect for the overall development of the interventions. It is crucial to ensure that every stakeholder of the community have equal access on the provision of clean drinking water and sanitation facilities, improved healthcare facilities, educational facilities and on economic excess and job opportunities. In this proposed project efforts will be made to promote the participation of marginalized groups, such as women and minorities, elderly person in decision-making processes and community activities. These efforts include the participation of the public including marginalized groups in the community meetings for project disclosure, corner meetings for the nomination of their representatives for the Village Organizations/ Village Councils (VOs/VCs), and monthly community meetings. Moreover, due representation for these marginalized groups has also been ensured in the VO membership. In addition to the open electoral process, a minimum of 50% share of the total membership has been allocated for the women members, one seat reserved for the minority, and in case of other socio-lingual differences further quota has also been ensured. These efforts will help to improve the overall quality of life for residents in proposed project area to promote opportunities in inclusive manner.

Mitigation Measures

- Providing awareness campaigns to increase knowledge and understanding of the project and challenges faced by marginalized groups.
- Ensuring the implementing policies that promote diversity and inclusion, such as affirmative action policies and anti-discrimination laws.
- Providing awareness on the importance of clean drinking water & sanitation, education, job training, and community services to underserved and marginalized populations.

- Encouraging and supporting the active participation of marginalized groups in decision-making processes through VO's to providing opportunities for leadership.
- Fostering partnerships between PRMSC-TO and VOs/VCs to promote social inclusion to address the root causes of social exclusion.
- Regular monitoring and evaluation of project policies and programs to ensure they are effective and inclusive.

6.7.6 End Water User of Treated Wastewater

End wastewater users are the individuals and communities who will use the treated water for various irrigation perpose. These end-users play a crucial role in ensuring the sustainable use of treated wastewater. It is important to understand the value of treated water and the impact of their actions on wastewater availability. The treated wastewater will be available to all the peasants having lands in the proximity of ABR. However, in case of disputes, VO of the village will decide the distribution rights of treated wastewater in consultation with the community demands.

Mitigation Measures

- End water users will adopt water conservation measures such as reducing water wastage, using efficient irrigation methods
- Awareness campaigns will be conducted on the understanding and importance of water conservation and its impacts.
- VO will ensure monitoring and evaluation on regular basis regarding the usage and conservation of treated water.
- Distribution of treated wastewater will be decided by VO's/VCs in village
- Equal rights of the community on the usage of treated water will be ensured by the VOs.

6.7.7 Solid Waste

Domestic and hazardous wastes would be generated during cleaning and maintenance activities. The solid waste during operational phase will consist of plastics, metal and organic wastes present in sewer lines which can cause blockage in sewerage system. This impact is major negative and permanent in nature.

Potential Impact of Solid Waste Management

The waste containers, if not emptied timely, will create nuisance and attract mosquitoes and disease vectors. The situation will exacerbate in the rainy seasons. Furthermore, there would be littering during transportation of waste from the villages to the dumping site.

Mitigation Measures

- Waste shall be collected, stored and disposed of according to relevant standards in approved facilities;
- An organized collection system and its implementation through a licensed contractor;
- The containers will be timely removed and a fine will be imposed on contractor in case of violations;

- Closed containers will be used for transportation of waste to the dumping site;
- Schedule inspection of the sewer lines and STP to keep it clean and to identify any hazardous material; and
- Solid waste bins shall be placed at appropriate locations to avoid mixing in wastewater.

6.7.8 Sludge

Potential Impact

Sludge is semi-solid material which will be settled at the bottom of the STP due to anaerobic decomposition of biomass. Significant amount of sludge will not be produced in ABR, however, periodic desludging will be done to achieve good removal efficiency. The removed sludge in wet form, if left unattended will create nuisance i.e., odor, soil contamination, groundwater contamination (through percolation/ seepage) and will serve as a breeding ground for vector diseases. Sludge will be removed from the ABR once the 50% of the ABR is filled will the sludge.

Mitigation Measures

- Appropriate sludge treatment must be undertaken before disposal of sludge; sludge dewater and drying through sludge drying beds in case of ABR.
- Sludge testing / horticulture purpose/ campaigns. Priority will be given to the use of dried sludge as a land conditioner in the fields.
- If required remaining sludge will be transferred to a nearby dumping site designated by Tehsil Municipal Authority, these sites are already being used for dumping of solid waste.
- Sludge management plan will be followed for proper handling and disposal (Annexure-9).

6.7.9 Impact of Brine Disposal

In case of operation of Reverse Osmosis (RO) filtration Plants, around 75% of water is rejected and 25% is consumed as treated product water. It means that for every 2000 lph capacity RO plant; we require 6000 lph of raw water to be treated from which 4000 lph will be the RO reject or brine. So, per day 32000 litres of wastewater will be generated from a single RO. The rejected water is free from bacteria, viruses and other pathogens but has only dissolved particles in it. RO concentrate disposal issues present significant design and operational challenges that must be addressed. Conventional disposal techniques mostly suffer from direct or indirect contamination of water/soil.

Mitigation Measures

- Reuse of brine for dust suppression on unpaved roads can be considered where environmentally acceptable.
- Planting halophytic grasses and shrubs in designated areas can help utilize saline water while stabilizing soil.
- Small-scale ponds with brine-tolerant fish or shrimp species can be developed in suitable areas.

- Brine can be discharged into a borehole to safely isolate it from surface water and allow controlled infiltration or dilution.
- RO brine can be discharged into water ponds (if present nearby) for reuse in irrigation only if the pond has adequate dilution and circulation to reduce salinity to safe levels.
- Brine can be managed through controlled dilution with treated effluent to reduce salinity before reuse for irrigation of non-food vegetation e.g, in Barley

6.8 Positive Impacts

6.8.1 Improved Water Supply System

Clean tap water is a dire need of all project tehsils. The provision of adequate water supply system with a reasonable supply of water will provide relief to the community and will resolve the major issue of "water" in the project area. Further, there will be a net improvement in community's health.

6.8.2 Improved Sewerage System

The proposed project will improve the overall sewerage and drainage system of the project area. Currently, the open wastewater drains in the streets result in foul odor, serves as breeding ground for disease vector and results in inconvenience to the road users and local community. The project will improve this situation by controlling overflows and proper disposal of wastewater/ storm water.

6.8.3 Improvement in Public Health, Hygiene and Sanitation

With the improvement in sewerage and drainage system, improvement in health, hygiene and sanitation will also be observed. Foul odor will be eliminated and there would be no breeding grounds for diseases vectors. Thus, the project will improve public health, hygiene and sanitation conditions in the project area.

6.8.4 Landscape

Potential Impact

During the operation stage, new saplings of different plants would be planted to enhance the aesthetics to create a buffer zone and to compensate the environmental losses. This will have a positive impact of permanent nature. The presence of adequate flora at available spaces will help in absorbing flue gases and other air quality related impacts of proposed project operation. The plants will be beneficial in dust and noise suppression for the nearby community.

Mitigation Measures

- The saplings planted in the project area against the trees affected and for enhancement of environment should be properly maintained throughout their growth.

6.8.5 Commulative Impacts of Water Extraction & Sewerage Treatment

Potential Impact

Cumulative impact may occur as a result of development of several treatment plants or several water extraction points. Under considering in 425 villages, currently there is only one water extraction point for each selected village and the people in project area are fulfilling their water demands majorly from ground water resource (agriculture and domestic purpose

respectively). The current intervention will provide treated water in the replacement of raw water to the locals which will improve the health and reduce exposure to water borne diseases. Supply of treated water at door set will also discourage the installation of pumps in houses. Furthermore, this project will basically replace the one practice to another practice and will not majorly impact on the consumption rate as people reliance on existing water extraction system will become minimum after the completion of the project. However, there will be no cumulative impact in terms of depleting ground water resources.

On the other hand, for each project village, one Sewerage Treatment Plant (STP) will be installed, and the treated water will be discharged into an existing sewerage pond. This practice will also have no impact on quality of water resources because sewerage water is already dumped directly into existing sewerage ponds and after this project sewerage water will be discharged into the ponds after treatment which will help to improve the quality of sewerage pond. However, there will be more or less zero cumulative impact after the installation of ABR

Mitigation Measures

- Water quality monitoring should be done by the third party on quarterly basis to ensure the supply of safe drinking water.
- ground water table will be monitored periodically.
- Water metering system should be installed to know the total consumption of water.
- Ensure the treated effluent follows the National Environmental Quality Standards
- Maintenance of ABR should be done annually for its smooth operations.

6.8.6 Other Positive Impacts

Some other positive impacts include the following:

- Economic development
- Employment generation
- Development of deprived areas
- Formation of model villages of tehsil Bhawana

6.9 Operational Sustainability

The sewer pipes water supply lines and other components of the project will not function with improper operation and maintenance of sewerage system and water supply system which is the responsibility of the client.

Mitigation Measures

- Routine/ preventative maintenance shall be carried out as with the passage of time
- Major causes of deposition of silt and floating matters in the sewers are the mixing of solid waste and smaller diameter sewer pipes. Placement of sufficient number of solid waste litter bins/containers shall be ensured along the roads and in streets to avoid entrance of solid waste into sewers;
- Immediate response to all sewer/drainage related complaints followed by prompt correction of defective condition;

- Regular cleaning of sewer lines to remove grease, grit, and other debris that may lead to sewer backups. Cleaning shall be conducted more frequently for problem areas;
- Inspection of the condition of sanitary sewer structures and identifying areas that need repair or maintenance. Items to note may include cracked/deteriorating pipes; leaking joints or seals at manhole; frequent line blockages; lines that generally flow at or near capacity; and suspected infiltration or ex-filtration;
- Any repairs will be conducted by sealing off the affected sewer and pumping the contents into tankers, after which the faulty section will be exposed and repaired following the same basic procedure as when the sewer was built. Trenches will be dug around the faulty section and the leaking joint will be re-sealed, or the pipe will be removed and replaced.
- Water supply lines will be inspected on regular basis to avoid any leakages and loss of resources.

6.10 Induced Impacts

Beside some direct environmental social and economic impacts, the proposed project may have some induced impacts to the physical features of environment. The project is envisaged to improve the infrastructure of the project area.

7 ENVIRONMENTAL & SOCIAL MANAGEMENT & MONITORING PLAN

7.1 General

This section aims to address the measures which need to be adopted during each phase of the project to avoid, contain, mitigate or compensate for the potential impacts identified in **Section 6**. The Environmental & Social Management Plan (ESMP) is the major part of this section and forms the gist of this study. ESMP not only includes Best Management Practices (BMPs) but also includes monitoring indicators, frequency, responsibility, and estimated environmental budget. This ensures that mitigation, monitoring, and management consideration form a part of the documentation used for decision making and the basic benefit of defining the responsibilities is to make sure that the suggested mitigation measure will be implemented at the construction and operation stages of the project. A summary of the mitigation measures for potential impacts have also been given in this section to support ESMP. Moreover, a framework for the implementation of ESMP has been discussed in this section.

7.2 Implementation of Environmental & Social Management Plan (ESMP)

The institutional arrangement for the implementation of ESMP for PRSWSSP is presented below. The proponent PRMSC and supervisory consultants will be responsible for compliance of with environmental and social safeguard requirements of the proposed project.

The proposed project activities will be monitored and managed by the PIMU-PRMSC. The Environmental and Social Cell (ESC) staffed by qualified environmental and social specialists has already been established under PRSWSSP. The ESC will be the custodian of the ESMP. ESC will support ensuring the compliance of ESMP. ESC will submit progress reports for the implementation of the ESMP to WB and PEPA as per environmental approval/ NOC conditions for the PRSWSSP.

Figure 17: Organizational Setup for implementation of ESMP

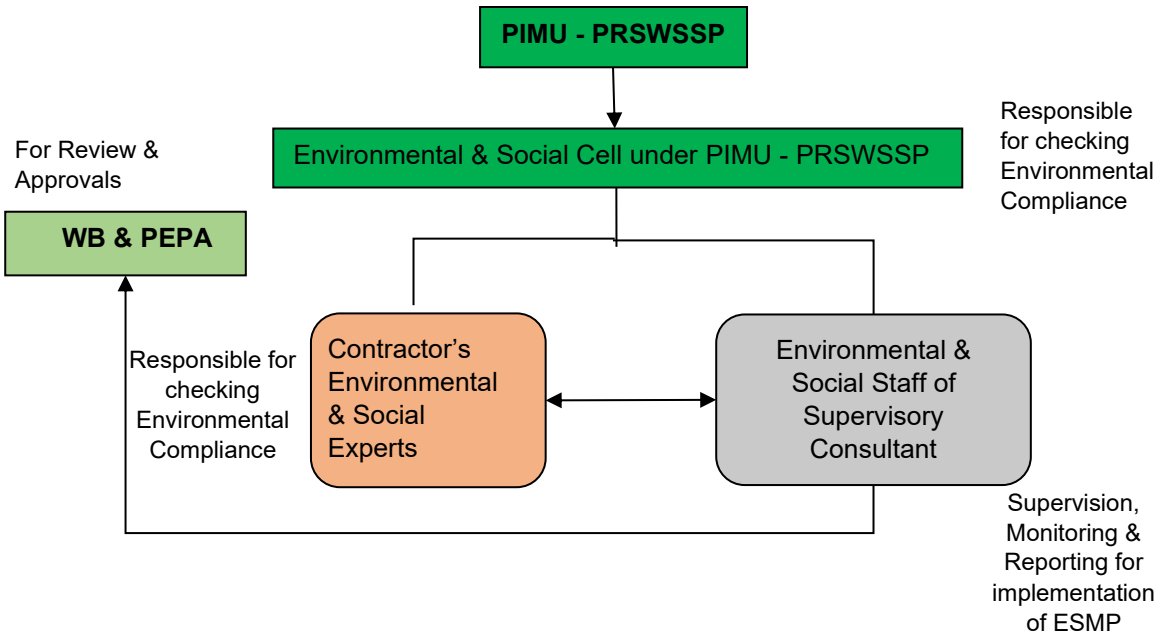

7.2.1 Roles and Responsibilities of the Functionaries involved in ESMP Implementation

A. World Bank

The current proposed project falls under category E2 as per ESMF guidelines; in view of limited environmental and social impacts and thus require an ESMP. World Bank shall review and approve the safeguard documents including ESMP. The Bank shall also review and approve the quarterly and biannually prepared progress reports.

B. Punjab Environmental Protection Department

As per Punjab Environmental Protection (Amendment) Act, 2012, Punjab EPD is responsible for environmental protection and pollution control. The Punjab EPD is responsible for the approval of the EIA/ IEE of all the developmental projects under their jurisdictions. As per Punjab Environmental Protection (Review of Initial IEE/EIA) Regulations 2022, Schedule-II, EIA is required for 'Water Supply, Sewerage System and Treatment (Category F) Based on the EIA and ESMP, Punjab EPD will monitor (as and when required) the project activities.

C. PRMSC

The Project Director of PRMSC is the in-charge for the financial and technical matters related to PRSWSSP. His responsibilities for monitoring the ESMP will consist of:

- Ensuring that the required environmental training is provided to the concerned PIU staff;
- To carry out random site visits to the construction sites to review the environmental performance of the Contractor;
- Review monitoring reports for the progress of environment-related activities;
- Make sure that the Contractor is implementing the additional measures suggested by the Supervision Consultant (SC) in environmental monitoring reports;
- To assist the Contractor in obtaining necessary approvals from the concerned departments;
- Maintaining interface with the other line departments/ stakeholders; and
- Reporting to the Punjab EPD on the status of ESMP implementation.

D. Environmental and Social Cell (ESC)

ESC has already been established in the PRMSC which is responsible to:

- Make sure that all the contractual obligations related to environmental and social compliance are met;
- Monitor the progress regarding the implementation of environmental and social safeguards as provided in the ESMP;
- Oversee the compliance of all the monitoring programs as given in ESMP;
- Check randomly whether monitoring of the environmental aspects of the proposed project during construction and operational phases is being properly carried out;

- Document and disclose monitoring results and identify necessary corrective and preventive actions in the periodic monitoring reports, and make follow-up on these actions to ensure progress toward the desired outcomes;
- Make sure that the contractor implements the additional measures suggested by the SC and PIMU; and
- Report the status of ESMP compliance to the Project Director, PRMSC.

E. Supervisory Consultant (SC)

The roles and responsibilities of SC will be:

- To oversee the performance of the Contractor to make sure that the Contractor is complying with ESMP;
- Ensuring that the day-to-day construction activities are carried out in an environmentally and socially sound and sustainable manner;
- Strong coordination with the Contractor and PRMSC;
- Preparing training materials and implementing programs;
- Ensure the implementation of the mitigation measures suggested in ESMP;
- To supervise and monitor environmental activities being performed at the site;
- Periodic reporting as mentioned in ESMP; and
- Suggest any additional mitigation measures (if required).

F. Construction Contractor (CC)

Contractors will be bound to appoint site-based Environmental and Social managers with relevant educational backgrounds and experience for PRSWSSP. The contractors' Environmental and Social manager will carry out the following activities:

- Implementation of the mitigation measures at the construction site;
- Contractor will be bound through the contract to take actions against all the special and general provisions of the contract document;
- Contractor will make sure the compliance of ESMP recommendations related to construction and will also be responsible for effective liaison with local heads of the community;
- Provision of proper Personal Protective Equipment (PPE) to the workers and train them for their proper use;
- To conduct the environmental and health & safety trainings to the workers/labour; and
- Coordinate with the Environmental Specialist and Social Development Specialist (SDS) of SC and PIMU.

7.2.2 Institutional Arrangement for Implementation of ESMP by PRMSC during O&M Phase

The proposed project will be administrated by PRMSC during the O&M phase. The Project Director, PRMSC with his ESC will be responsible for the following:

- Compliance with ESMP requirements for the O&M phase;

- Coordinating with the operational staff working under the ESC to monitor environmental compliance during project operation;
- Advising on, and monitoring tree plantations along the stagnant pool of water in the project area;
- Reporting on the progress of environmental compliance to the Punjab EPD;
- Assessing the long-term environmental impacts of project operation;
- Sustaining a working partnership among the PRMSC, Punjab Local Government Department, Punjab EPD, Agriculture, Irrigation, Forest and Wildlife departments of Punjab, NGOs, and other related public-private sector organizations.

7.3 Reporting

The contractor will prepare and submit monthly monitoring reports for compliance of implementation to the supervision consultant (SC) environmental team.

The distribution of periodic reports is given in **Table 24.**

Table 25: Distribution of Periodic Reports

Report	Prepared by	Reviewed by	Distribution
Monthly	Contractor	Reviewed by PRMSC-Environmental Unit; PRSWSSP	The Engineer and PRMSC
Quarterly	Contractor	Reviewed by PRMSC-Environmental Unit; PRSWSSP	The Engineer, PRMSC and The World Bank
Annual	Contractor	Reviewed by PRMSC-Environmental Unit; PRSWSSP	The Engineer, PRMSC and The World Bank
Final	Contractor	Reviewed by PRMSC-Environmental Unit; PRSWSSP	The Engineer, PRMSC and The World Bank

7.4 Non-Compliance with the ESMP

The implementation of the proposed ESMP involves inputs from various functionaries as discussed earlier. The contractor will be primarily responsible for ensuring the implementation of the mitigation measures proposed in the ESMP, which will be part of the contract documents. The provision of the environmental mitigation cost will be made in the total cost of the project. However, if the contractor fails to comply with the implementation of ESMP and submission of the monthly compliance reports, deductions will be made from the payments to the Contractor claimed under the heads of environmental components.

7.5 Contractors ESMP

The contractor will prepare a site-specific Contractor's ESMP (C-ESMP) based on the current ESMP and will get it approved by PRMSC before the start of work. This will ensure the implementation of the ESMP based on the site conditions at the time of execution, by the contractor.

The C-ESMP will include the following sub-plans:

- Traffic management plan,
- OHS plan,

- Pollution prevention plan,
- Camp management plan

7.6 Inclusion of ESMP in Bidding/ Contract Documents

The present ESMP will be included in the bidding/ contract documents and their implementation will be contractual binding for the contractors.

7.7 Environmental and Social Monitoring Plan

Monitoring will be carried out to ensure that the mitigation plans are regularly and effectively implemented. It will be performed at three levels. At the PRMSC level, the ESC will do ESMP monitoring to ensure that the mitigation plans are being effectively implemented. The environmental engineer of the Supervision Consultant will regularly monitor the ESMP implementation by the contractor. At the contractor's level, the environmental monitoring checklist will be filled on daily basis by their environmental manager and countersigned by the environmental engineer (EE) of the Supervision Consultant.

Table 25 outlines the parameters that will be monitored, the expected frequencies of monitoring, and the responsible agency for monitoring.

Table 26: Environmental and Social Management Plan (ESMP)

Activity	Impacts	Mitigation Measures	Implementation Responsibility	Monitoring Indicators	Monitoring Frequency	Monitoring Responsibility	Cost
Pre-Construction / Design Phase							
Layout Planning & Design	Incompatible layout plans and engineering designs of the proposed project can undermine the overall aesthetics and ambiance of the project area	• All structural, layout and engineering designs of the project are in strict accordance with the applicable national and international guidelines/ codes/ standards and engineering practices;	DC, PRMSC	Design provisions	Once (after completion of Detailed Design)	PIMU	N/A
Impacts of Drains construction	Inadequate sizing or gradients may lead to poor flow, blockages, or flooding during peak conditions. Improper alignment can cause conflict with existing utilities and affect land use. Selection of unsuitable materials or inadequate lining may result in erosion, siltation, or structural failure.	• Plan proper alignment and depth to avoid conflicts with existing utilities and infrastructure. • Ensure accurate hydraulic design with proper gradients to maintain self-cleansing velocity and avoid blockages. • Provide adequate cross-sections and freeboard to handle peak stormwater flows safely. • Incorporate silt traps and access points for ease of maintenance and prevention of	DC, PRMSC	Design provisions	Once (after completion of Detailed Design)	PIMU	N/A
Risk to Structures	In certain areas, katcha houses are present. This impact is considered sensitive due to its potential effect on local communities. Weak soil-bearing capacity of these structures makes them particularly vulnerable to vibration, settlement, or lateral soil movement	• Conduct pre-construction structural surveys of nearby katcha houses to assess vulnerability and design protective measures accordingly. • Implement controlled dewatering and soil compaction techniques to maintain ground stability and prevent settlement around excavated areas.	DC, PRMSC	Design provisions	Once (after completion of Detailed Design)	PIMU	N/A

Activity	Impacts	Mitigation Measures	Implementation Responsibility	Monitoring Indicators	Monitoring Frequency	Monitoring Responsibility	Cost
	during construction.						
Improperly Designed Sewers	Improper designed sewers may not carry the waste load, leading to system-failure and financial loss.	• All sewer lines including trunk, lateral and branch sewer lines have been designed considering the future population and waste generation rate;	DC, PRMSC	Design provisions	Once (after completion of Detailed Design)	PIMU	N/A
	The construction of high-rise overhead water tanks may cause visual obstruction.	• The location of groundwater storage tanks, overhead water tanks, pumping stations and STP have been finalized in close consultation with local community and representatives of local authorities.	DC, PRMSC	Design provisions	Once (after completion of Detailed Design)	PIMU	N/A
Groundwater	During operation probability of seepage through the sewers may also contaminate groundwater.	• Efficient seepage control measures have been considered in selection of pipe materials during the planning stage	DC, PRMSC	Design provisions	Once (after completion of Detailed Design)	PIMU	N/A
		• Procedure for efficient jointing of selected sewer pipes will be applied to avoid leakage from pipes	DC, PRMSC	Design provisions	Once (after completion of Detailed Design)	PIMU	N/A
Damage to Existing Infrastructure	There are no public utilities except the electric poles which might get affected during construction activities and movement of machinery and the community will face temporary electricity cuts.	• Alignment has been selected carefully to minimize disturbance to public utilities;	DC, PRMSC	Design provisions	Once (after completion of Detailed Design)	PIMU	N/A
		• Relocation of the public utilities shall be planned and approved in consultation with relevant departments/authorities/stakeholders before project commencement if any, to avoid inconvenience to the public.	DC, PRMSC	Design provisions	Once (after completion of Detailed Design)	PIMU	N/A
Physical Cultural	No historical/ archeological site is present in the project	• The alternative access routes will be provided in case the access has	DC, PRMSC	Design provisions	Once (after completion	PIMU	N/A

Activity	Impacts	Mitigation Measures	Implementation Responsibility	Monitoring Indicators	Monitoring Frequency	Monitoring Responsibility	Cost
Resources	area. However, some cultural resources including mosques, graveyards and shrines are present. These will not be directly affected but the people may face access issues in visiting these facilities.	to be restricted during the execution period			of Detailed Design)		
Fire Fighting System	In case of fire hazards, inefficient firefighting system at campsite may cause severe damage to the camp site and surrounding crops and houses. This will be a moderate adverse impact.	• Contractor will provide firefighting system for construction camp, workshop and construction site;	DC, PRMSC	Design provisions	Once (after completion of Detailed Design)	PIMU	N/A
		• A separate fire alarm system will also be installed at construction camp and near the construction site.	DC, PRMSC	Design provisions	Once (after completion of Detailed Design)	PIMU	N/A
Land Acquisition	Private land will be taken through VLD, State land will be used through NOC procedure. There will be no purchase of land, involuntary resettlement and no relocation of people or businesses.	• No one will be forced or pressurized to donate land • VLD should not be more than 10 % of the total land holding of the owner	DC, PRMSC	VLD procedure of ESMF	Once at the time of land acquisition	PIMU	N/A
Anticipated Impacts during the Construction Phase							
Topography	The construction activities are not expected to impact the topography of the area significantly except for those areas where physical activities i.e., earthwork is involved as well as stocking of	• Material stockpiles will be removed as soon as work is completed and the area will be reinstated;	CC, SC, PRMSC	Stockpiles and heaps of waste visible at the site.	Weekly	SC and PIMU	N/A
		• Temporary storage sites will be allocated for the storage of excavated material;	CC, SC, PRMSC	Site allocation and preparation	Once before the excavation activity	SC and PIMU	N/A

Activity	Impacts	Mitigation Measures	Implementation Responsibility	Monitoring Indicators	Monitoring Frequency	Monitoring Responsibility	Cost
	material. The excavated material is to be mostly backfilled and the excessive material will be transported to strengthen the roadsides or will be dumped at the designated locations. This impact is site-specific, temporary, reversible, possible, and low significant	• Temporary storage sites will be lined and must not allow infiltration	CC, SC, PRMSC	Site allocation and preparation	Before utilization of storage site	SC and PIMU	N/A
		• The stockpiles must be covered with tarpaulin sheets or other adequate material;	CC, SC, PRMSC	Provision of tarpaulin	Before start of construction activity	SC and PIMU	The cost of tarpaulin is provided in the ESMP Budget
		• Pilling of material at large extent will not be allowed and the contractor will timely remove excavated material from the site.	CC, SC, PRMSC	Stockpiles and heaps of waste visible at the site.	Weekly	SC and PIMU	N/A
Soil Erosion	The soil would be exposed to erosion due to excavations for laying of sewers and water supply pipes. Construction activities such as clearing, excavation, filling, grading and setting up construction camps will affect the existing soil condition in the study area/ AoI. The clearing of vegetation can also loosen the soil and make it more susceptible to erosion due to wind and	• Good engineering practices will help to control or minimize soil erosion both at the construction sites and in peripheral areas including provision of shuttering;	CC, SC, PRMSC	Provision of shuttering	Once	SC and PIMU	N/A
		• Use of heavy machinery will be restricted as far as possible to avoid the destruction of soil structure;	CC, SC, PRMSC	Movement of machinery	~~Hauling of machinery~~ During Construction Work	SC and PIMU	N/A
		• Confining excavations to the specified spots as per the approved engineering drawings and unnecessary excavations should be avoided;	CC, SC, PRMSC	Excavations beyond the specified spots	During excavation works	SC and PIMU	N/A

Activity	Impacts	Mitigation Measures	Implementation Responsibility	Monitoring Indicators	Monitoring Frequency	Monitoring Responsibility	Cost
	rain. There is also a possibility of silt runoff during rainy season causing soil erosion. During the rain, the eroded soil will mix with stagnant water to transform into slush, which can affect movement of vehicles and machinery and construction workers as well as limit the movements of local people. This impact can be categorized as low adverse, site-specific, long term, permanent, highly probable and reversible.	• Stored excavated material shall be covered and preferably reused, e.g., in construction as backfill etc.	CC, SC, PRMSC	Wastage of excavated material; Backfilling	During backfilling	SC and PIMU	
Soil Contamination	Contamination of soil may be caused by oil and chemical spills from construction machinery or uncontrolled runoff from equipment washing yards. This impact is permanent and minor negative in nature.	• Chemicals/ hazardous products and wastes will be stored on impermeable surfaces in secure, covered areas with clear labelling of containers and with a tray or bund to contain leaks;	CC, SC, PRMSC	Monitoring compliance to Regular disposal of Chemical/ Hazardous waste; Photographic record;	Monthly	SC and PIMU	N/A
		• All construction wastes from the site will be regularly removed and transported to approved waste disposal sites	CC, SC, PRMSC	No fall of transported material; Damaged road repaired. Record of harmful	Weekly	SC and PIMU	N/A

Activity	Impacts	Mitigation Measures	Implementation Responsibility	Monitoring Indicators	Monitoring Frequency	Monitoring Responsibility	Cost
				incidents that occurred.			
		• Washing yards will be paved to avoid seepage of runoff from the yard;	CC, SC, PRMSC	Visual Inspection	Weekly	SC and PIMU	N/A
		• Awareness in emergency spill response procedures will be conducted through trainings;	CC, SC, PRMSC	Training Sessions	Once	SC and PIMU	N/A
		• Oil leakages, chemicals and other liquids spills will be avoided/ minimized by providing appropriate storage places depending on the type of material for storage	CC, SC, PRMSC	Visual Inspection	Weekly	SC and PIMU	N/A
Trench Failure	The major construction activities involve excavation operations for laying water supply and sewerage lines. The major hazard associated with the excavation operations is trench failure. The unstable slopes may fail and settle in the trenches which may cause injuries and fatalities to the workers. This impact is probable, site specific and high adverse in nature.	• Provision of adequate shuttering in the trenches;	CC, SC, PRMSC	Visual Inspection	Weekly	SC and PIMU	N/A
		• Leftover shuttering may also be used in case of loose soil strata.	CC, SC, PRMSC	Visual Inspection	Weekly	SC and PIMU	N/A
Construction Camps/Camp Sites	Improper construction camp location and mismanagement of construction camp activities can lead to various social and	• Working hours of noisy activities will be limited to normal daytime working hours when near identified sensitive receptors;	CC, SC, PRMSC	Field Observations	Weekly	SC and PIMU	N/A
		• Waste Management Plan will be implemented to include	CC, SC, PRMSC	Compliance to waste	Monthly	SC and PIMU	N/A

Activity	Impacts	Mitigation Measures	Implementation Responsibility	Monitoring Indicators	Monitoring Frequency	Monitoring Responsibility	Cost
	environmental impacts which may include noise, health and safety, traffic problems, soil degradation, loss of vegetation and assets on the selected land, solid waste and water pollution. Furthermore, cultural differences, behavior of construction workers, potential disregard for local cultural norms can lead to increased tension between local communities and workers residing in the construction camps. This impact is temporary and moderate negative in nature.	procedures for the classification, storage and disposal of all construction wastes and the training of employees who handle hazardous materials;		management plan;			
		• Construction camps will be established away from populated areas	CC, SC, PRMSC	Camp established at least 500m away from the nearest community; Local hired workforce;	Once	SC and PIMU	N/A
		• NOC/ lease agreement will be signed between landowners and contractors.	CC, SC, PRMSC	Lease agreement signed / NOC obtained	Once before start of construction	SC and PIMU	N/A
		• Regular training of workers will be carried out regarding local cultural norms, human behaviour, gender issues by the contractor during construction activities at site.	CC, SC, PRMSC	Any complaint from the local community.	Weekly check complaint register	SC and PIMU	Cost is provide in the ESMP Budget
Water Quality	Runoff and erosion from exposed soil surfaces, earthwork areas and stockpiles e.g., grouting and cement material with the rain. Construction waste, if left unattended will result in forming leachate that will percolate through the soil strata and will reach underground water table and hence, will	• Protection of groundwater reserves from any source of contamination such as the construction and oily waste by making the ground impermeable through sheets or compaction;	CC, SC, PRMSC	Monitoring compliance; Water quality testing.	Quadrimesterly	SC and PIMU	N/A
		• Stockpiles of cement and other construction materials will be kept covered when not being used;	CC, SC, PRMSC	Use of tarpaulin for protection; Visual Inspection	Weekly	SC and PIMU	N/A

Activity	Impacts	Mitigation Measures	Implementation Responsibility	Monitoring Indicators	Monitoring Frequency	Monitoring Responsibility	Cost
	end up contaminating groundwater. There is a probability that various materials like fuel, lubricant oil and other oily products, which are used during the construction phase may contaminate groundwater and channels carrying water.	• Maintenance of vehicles will be carried out only in impermeable areas where any oil spillages can be contained;	CC, SC, PRMSC	Any spill observed; Availability of sealed containers for used oils and lubricants; Disposal options (e.g., local vendor) explored.	Weekly	SC and PIMU	N/A
		• Careful planning of the works to avoid soil excavation works during rainy seasons;	CC, SC, PRMSC	Visual Inspection	During rainy season	SC and PIMU	N/A
		• No activity will be undertaken in monsoon and careful attention must be paid to the weather forecast before excavation operations.	CC, SC, PRMSC	Visual Inspection	During rainy season	SC and PIMU	N/A
		• All kinds of waste will be stored in covered containers and disposed of safely as soon as possible;	CC, SC, PRMSC	Visual Inspection	Weekly	SC and PIMU	N/A
		• The contractor will ensure that construction debris do not find their way into the drainage or irrigation canals which may get clogged.	CC, SC, PRMSC	Visual Inspection	Weekly	SC and PIMU	N/A
Air Quality	Air quality will be affected by various construction activities. Emissions may be spread over longer distances depending upon	• All vehicles, machinery, equipment and generators used during construction activities will be kept in good working condition, properly tuned and maintained in order to	CC, SC, PRMSC	Dust emission controlled;	Weekly	SC and PIMU	N/A

Activity	Impacts	Mitigation Measures	Implementation Responsibility	Monitoring Indicators	Monitoring Frequency	Monitoring Responsibility	Cost
	the wind speed, direction, temperature of surrounding air and atmospheric stability. In certain climatic condition such as hot summer, airborne dust can become a major nuisance if control techniques are not properly employed	minimize the exhaust emissions;					
		• Open burning of solid waste from the contractor's camps will be strictly banned;	CC, SC, PRMSC	Monitoring compliance to disposal of waste;	Weekly	SC and PIMU	N/A
		• Fuel with substantially lower sulphur content will be preferred;	CC, SC, PRMSC			SC and PIMU	N/A
		• Personal Protective Equipment (PPEs) like masks, goggles and gloves etc. will be provided to workers;	CC, SC, PRMSC	Implementation of HSE; Visual Inspection	Daily	SC and PIMU	Cost given in ESMP Budget
		• PEQS applicable to gaseous emissions generated by construction vehicles, equipment and machinery will be enforced during construction works.	CC, SC, PRMSC	Monitoring of machinery and equipment;	Daily	SC and PIMU	N/A
		• Regular water sprinkling on the site and access roads will be carried out to suppress excessive dust emission(s)	CC, SC, PRMSC	Visual Monitoring	Daily	SC and PIMU	N/A
		• Excavated trenches will be restored immediately to original level and paved after laying of sewer pipes;	CC, SC, PRMSC	Visual Inspection	Daily	SC and PIMU	N/A
		• Vehicle speed in the project area will be prescribed not more than 20 km/hr and controlled accordingly;	CC, SC, PRMSC	Visual Inspection	Daily	SC and PIMU	N/A
		• Diversion will be provided for local traffic movement;	CC, SC, PRMSC	Visual Inspection	Daily	SC and PIMU	N/A
		• The vehicles carrying construction materials and the construction material storage areas will be covered with tarpaulin.	CC, SC, PRMSC	Use of tarpaulin for protection	Daily	SC and PIMU	N/A

Activity	Impacts	Mitigation Measures	Implementation Responsibility	Monitoring Indicators	Monitoring Frequency	Monitoring Responsibility	Cost
		• Air quality monitoring should be done by the 3rd party.	CC, SC, PRMSC	Air Quality	Monthly	SC and PIMU	Cost is provided in ESMP Budget
Dust	During construction stage, the dust level may increase considerably. Earthworks, site clearing, stockpiling and hauling of materials will generate dust and affect the local air shed. Local people and the workers may be exposed to high dust levels during landscaping, access road and site preparation. This impact is site-specific, temporary, reversible, likely and medium significant.	• Blowing of dust from potential sources at the worksite will be avoided by shielding them from the exterior, for example using polythene curtains or raising a fence of corrugated sheets around areas of active constructions	CC, SC, PRMSC	Visual Inspection Air levels measured.	Daily	SC and PIMU	N/A
		• All excavation work will be sprinkled with water to control dust;	CC, SC, PRMSC	Visual Inspection	Daily	SC and PIMU	N/A
		• Tires of all the vehicles leaving the site will be washed. No earth, mud, dust and the like will be deposited on the public road;	CC, SC, PRMSC	Visual Inspection	Daily	SC and PIMU	N/A
Noise	Noise level is expected to increase during construction activities. Main sources of noise and vibration will be heavy machinery such as excavators and other equipment. Noise generated by construction machinery is likely to affect sensitive receptors located within AoI. Health risks associated with exposure to continuous noise levels	• Construction workers will be provided suitable hearing protection like ear cap, or earmuffs and training them in their use;	CC, SC, PRMSC	Visual inspections; Noise levels measured.	Daily	SC and PIMU	Cost is provided in the ESMP Budget
		• Selection of up-to-date and well-maintained equipment with reduced noise levels will be ensured by suitable in-built damping techniques or appropriate muffling devices	CC, SC, PRMSC	Visual inspections; Noise levels measured.	Daily	SC and PIMU	N/A
		• Residents will be notified earlier before commencement of excavation operations.	CC, SC, PRMSC	Visual inspections;	Daily	SC and PIMU	N/A

Activity	Impacts	Mitigation Measures	Implementation Responsibility	Monitoring Indicators	Monitoring Frequency	Monitoring Responsibility	Cost
	include high blood pressure, hypertension, annoyance and sleep disturbance, temporary threshold shift etc. The impacts of noise will be temporary and highly adverse in nature.	• Noise quality monitoring should be done by the 3rd party.	CC, SC, PRMSC	Noise levels measured	Quarterly	SC and PIMU	Cost is provided in the ESMP Budget
Municipal and Construction Waste/ Wastewater	Due to construction activities municipal and construction waste will be generated from construction activities. The construction waste will include wastewater, oil spillage from machinery, domestic waste and construction waste etc.	• Solid waste generated during construction and camp sites will be safely disposed of in demarcated waste disposal sites and the contractor will provide and implement a comprehensive waste management plan;	CC, SC, PRMSC	Monitoring compliance;	Weekly	SC and PIMU	N/A
		• Burning of waste will be prohibited;	CC, SC, PRMSC	Visual Inspection	Daily	SC and PIMU	N/A
		• Proper labelling of containers, including the identification and quantity of the contents, hazard contact information etc;	CC, SC, PRMSC	Visual Inspection	Weekly	SC and PIMU	N/A
		• Emergency Response plan will be prepared to address the accidental spillage of fuels and hazardous goods;	CC, SC, PRMSC	Visual Inspection	Weekly	SC and PIMU	N/A
		• Containers with covers will be provided on site to store waste	CC, SC, PRMSC	Visual Inspection	Daily	SC and PIMU	N/A
Resource Conservation	The materials used in construction of proposed project would include coarse aggregates (crush), fine aggregates (sand), brick ballast, water and cement etc. Almost all the	• Wastage of water will be reduced by training the workers involved in water use;	CC, SC, PRMSC	Visual Inspection	Daily	SC and PIMU	N/A
		• Wastage of water will be controlled through providing proper valves and through controlling pressure of the water;	CC, SC, PRMSC	Visual Inspection	Daily	SC and PIMU	N/A

Activity	Impacts	Mitigation Measures	Implementation Responsibility	Monitoring Indicators	Monitoring Frequency	Monitoring Responsibility	Cost
	materials to be used in the construction of proposed project are non-renewable and therefore their sustainable use is necessary for the future use. Excessive water consumption for drinking and washing purposes by the construction staff may undermine water resources in the project area and in certain cases may disturb the existing water supplies in the project area.	• Water jets and sprays will be used for watering surfaces rather than using overflow system;	CC, SC, PRMSC	Visual Inspection	Daily	SC and PIMU	N/A
		• Source of water will be carefully selected. Water use will not disturb the existing community water supplies	CC, SC, PRMSC	Any conflict on the water availability.	Fortnightly	SC and PIMU	N/A
		• Reuse of construction waste materials will be considered;	CC, SC, PRMSC	Visual Inspection	Daily	SC and PIMU	N/A
		• Unnecessary equipment washings will be avoided;	CC, SC, PRMSC	Visual Inspection	Daily	SC and PIMU	N/A
		• The efficient and well-maintained equipment and machinery will be used;	CC, SC, PRMSC	Noise levels within permissible limits Gas emissions minimized; Dust emission controlled	Daily	SC and PIMU	N/A
		• The equipment and machinery will be turned off when not in use;	CC, SC, PRMSC	Visual Inspection	Daily	SC and PIMU	N/A
		• Regular maintenance of machinery to avoid fuel leakages;	CC, SC, PRMSC	Log of vehicle and equipment repairs;	Daily	SC and PIMU	N/A
Biodiversity Conservation	**FLORA** On account of construction of the proposed water supply and sewerage system, no trees are envisaged to be cut/disturbed. Hence there will be no direct impact on the flora of project area.	• Campsites will be established on vacant land as far as possible, at least 500 m away from the residential areas;	CC, SC, PRMSC	Visual Inspection	Daily	SC and PIMU	N/A
		• Construction vehicles, machinery and equipment will remain confined within their designated areas of movement;	CC, SC, PRMSC	Log Book of vehicle inventory	Daily	SC and PIMU	N/A
		• The Contractor's staff and labour	CC, SC, PRMSC	Any conflict	Daily	SC and PIMU	N/A

Activity	Impacts	Mitigation Measures	Implementation Responsibility	Monitoring Indicators	Monitoring Frequency	Monitoring Responsibility	Cost
	However, the dust emissions due to excavation operations will stick on the leaves of existing trees and may close their stomata thus hindering the photosynthesis process.	will be strictly directed not to damage any vegetation such as trees or bushes. They will use the paths and tracks for movement and will not be allowed to trespass through farmlands;		with locals.			
		• Contractor will provide gas cylinders at the camps for cooking purposes and cutting of trees/ bushes for fuel will not be allowed.	CC, SC, PRMSC	Visual Inspection	Daily	SC and PIMU	N/A
	FAUNA The local animals mostly cats, dogs and jackals and specially the livestock i.e., goats and cows will get disturbed due to construction activities, especially the noisy activities. However, there will be no damage to their health and life. Some reptiles and insects may get killed/ injured during excavation operations.	• Excavations will be limited to the approved engineering drawings;	CC, SC, PRMSC	Visual inspections; Photographic records.	Daily	SC and PIMU	N/A
		• Harassing of animals will be prohibited	CC, SC, PRMSC	Visual Inspection	Daily	SC and PIMU	N/A
Occupational Health and Safety	Health risks and worker's safety problems may result at the workplace if the working conditions provide unsafe and/or unfavorable working environment. The health and safety issues are also associated with the operation of construction machinery	• Obligatory insurance against accidents for labourers/workers;	CC, SC, PRMSC	Accident/ Incident reported.	If happened	SC and PIMU	N/A
		• Providing basic medical training to specified work staff and basic medical service and supplies to workers;	CC, SC, PRMSC	Maintained Training Record; Pictorial evidence	Weekly	SC and PIMU	N/A
		• Layout plan for camp site, indicating safety measures taken	CC, SC, PRMSC	Visual inspection	Daily	SC and PIMU	N/A

Activity	Impacts	Mitigation Measures	Implementation Responsibility	Monitoring Indicators	Monitoring Frequency	Monitoring Responsibility	Cost
	and equipment, which may cause minor and severe injuries to workers. It will be a long term and severe negative impact.	by the contractor, e.g., firefighting equipment, safe storage of hazardous material, first aid, security, fencing, and contingency measures in case of accidents;					
		• Work safety measures and good workmanship practices will be followed by the contractor to ensure no health risks for labourers, including use of Personal Protective Equipment (PPE) i.e., oxygen masks/ kits etc.;	CC, SC, PRMSC	Visual inspection	Daily	SC and PIMU	Cost is provided in ESMP Budget
		• Protection devices (ear muffs) will be provided to the workers doing job in the vicinity of high noise generating machines i.e., excavators;	CC, SC, PRMSC	Visual inspection	Daily	SC and PIMU	Cost is provided in ESMP Budget
		• Use of safety signs at the construction site will be ensured.	CC, SC, PRMSC	Visual inspection	Daily	SC and PIMU	N/A
		• Contractor will immediately inform the consultant about the project related incident. The consultant will then submit a preliminary report to the PRMSC within 24 hours. Resultantly, PRMSC will promptly notify the World Bank for project-related incident within a maximum timeframe of 48 hours.	CC, SC, PRMSC	Accident/ Incident reported.	If happened	SC and PIMU	N/A
Community Health and Safety	The construction activities and vehicular movement at construction sites may result in roadside accidents particularly inflicting local communities	• Medical screening of the laborers for communicable diseases will be conducted before hiring. Medical screenings are a basic requirement before the hiring of labour to prevent the spread of	CC, SC, PRMSC	Medical Reports Record;	Quarterly	Bi-Annual	

Activity	Impacts	Mitigation Measures	Implementation Responsibility	Monitoring Indicators	Monitoring Frequency	Monitoring Responsibility	Cost
	who are not familiar with presence of heavy equipment. Open trenches and deep manhole may cause trip & fall accidents for the local residents.	communicable diseases. However, on the basis of these screenings, diseased potential workers will not be barred from work; instead, necessary measures will be taken to prevent the spread of these diseases.					
		• Provision of proper safety and diversion signage, particularly at sensitive/accident-prone spots;	CC, SC, PRMSC	Visual inspection	Daily	SC and PIMU	N/A
		• The site will be restricted for the entry of irrelevant people particularly children.	CC, SC, PRMSC	Visual inspection	Daily	SC and PIMU	N/A
		• Open trenches and deep excavated manholes will be protected by fence/barricade to avoid any accident.	CC, SC, PRMSC	Visual inspection	Daily	SC and PIMU	N/A
		• Night time lighting will also be provided.	CC, SC, PRMSC	Visual inspection	Daily	SC and PIMU	N/A
		• Awareness campaign regarding HSE will also be provided to local	CC, SC, PRMSC	Visual inspection	Daily	SC and PIMU	N/A
		• Setting up speed limits within the village.	CC, SC, PRMSC	Visual inspection	Daily	SC and PIMU	N/A
		• Special consultation session will be held with the nearby medical facility to ensure that it is well informed and well equipped to handle any dust allergy cases if required.	CC, SC, PRMSC	Consultation Meeting Record	Bi-annually	SC and PIMU	N/A
		• Contractor will immediately inform the consultant about the project related incident. The consultant will then submit a preliminary report to the PRMSC within 24 hours.	CC, SC, PRMSC	Accident/ Incident reported.	If happened	SC and PIMU	N/A

Activity	Impacts	Mitigation Measures	Implementation Responsibility	Monitoring Indicators	Monitoring Frequency	Monitoring Responsibility	Cost
		Resultantly, PRMSC will promptly notify the World Bank for project-related incident within a maximum timeframe of 48 hours.					
Traffic Management	The traffic influx within the villages is very low. Most of the traffic within the villages include motorbikes and few cars. The project interventions will not create traffic congestion issues in the project area. However, their movement will be disturbed due to the excavation and construction works and people may face accessibility issues. This impact is temporary and major negative in nature.	• The construction activities will be carried out in pockets/reaches, once a patch has been completed (i.e., pipes are laid and covered) then excavation on new patch shall be started;	CC, SC, PRMSC	Visual inspection	Daily	SC and PIMU	N/A
		• Local community will be taken on board to plan alternate access routes in connecting streets to ensure mobility of local traffic;	CC, SC, PRMSC	Alternate route maps	Daily	SC and PIMU	N/A
		• Plan work in a minimum possible time.	CC, SC, PRMSC	Check targeted timeline	Daily	SC and PIMU	N/A
Nuisance/ Disturbance to Social Sensitive Areas	Since the proposed interventions will be carried out within the villages boundaries, therefore, the socially sensitive sites/places including schools, hospitals and religious centers will be temporarily affected due to dust, noise and the community will face accessibility issues due to open trenches. Dust due to earthworks will create	• No work will be conducted near the religious places during religious congregations;	CC, SC, PRMSC	Visual Inspection	Daily	SC and PIMU	N/A
		• Material transport to the site will be scheduled considering school timings;	CC, SC, PRMSC	Visual inspection	Daily	SC and PIMU	N/A
		• Notify concerned schools, hospitals/dispensary etc. 2 weeks prior to the work; conduct a 30 minutes awareness program on nature of work, likely disturbances and risks and construction work, mitigation measures in place, entry restrictions and dos and don'ts	CC, SC, PRMSC	Visual inspection	Daily	SC and PIMU	N/A

Activity	Impacts	Mitigation Measures	Implementation Responsibility	Monitoring Indicators	Monitoring Frequency	Monitoring Responsibility	Cost
	health hazard to children and people with ailments. This impact is temporary and major negative in nature.	• Implement all measures suggested elsewhere in this report – dust and noise control, public safety, traffic management, strictly at the sites.	CC, SC, PRMSC	Visual inspection	Daily	SC and PIMU	N/A
Accessibility	Excavation of trenches and pipe/sewer laying work in the project area will obstruct access to residences, commercial buildings and businesses adjacent to the proposed project alignment. Disruption of access to commercial establishments may affect livelihood. The potential impacts are negative and moderate but short-term and temporary.	• Leave space for access between mounds of excavated soil;	CC, SC, PRMSC	Visual inspection	Daily	SC and PIMU	N/A
		• Consult affected business people to inform them in advance about the work schedule;	CC, SC, PRMSC	Consultation meeting; Pictorial evidence	Weekly	SC and PIMU	N/A
		• If there are any holidays (i.e., Eid or Muharram etc.), the Contractor will complete the backfilling work of the trenches and will not leave any trench open before holidays;	CC, SC, PRMSC	Visual inspection Designated borrow and quarry areas used for access material;	Daily	SC and PIMU	N/A
		• Provide sign boards for pedestrians to inform nature and duration of construction works and contact numbers for concerns/complaints;	CC, SC, PRMSC	Visual inspection	Weekly	SC and PIMU	N/A
Resilience to Climate Change	There are chances that the open trenches may get flooded during rainy season. Flooding can hamper the construction of overhead storage tanks, pumping station and STP. This impact can be categorized as direct, local, medium term,	• Project components have been designed to withstand flooding;	CC, SC, PRMSC	Design provisions	Once (after completion of Detailed Design)	SC and PIMU	N/A
		• The capacity of the sewerage/ drainage system have been designed and constructed based on extreme weather conditions predicted under international climate change models for	CC, SC, PRMSC	Check Meteorological department prediction of rain	Before construction	SC and PIMU	N/A

Activity	Impacts	Mitigation Measures	Implementation Responsibility	Monitoring Indicators	Monitoring Frequency	Monitoring Responsibility	Cost
	temporary and reversible.	Bhawana region to cater for extreme storm water runoff.					
Liquid and Solid Waste from Construction Camps	Development of construction camps will generate significant quantities of liquid and solid waste. A total of five (05) nos. construction camps will be established in all five villages accommodating approximately 30 skilled and unskilled staff each (i.e., total 150 workers for all villages).	• The waste generated from the camp site will be disposed of at existing dumping site of the Tehsil Bhawana by the Contractor;	CC, SC, PRMSC	Visual inspection	Daily	SC and PIMU	N/A
		• Construction workers and supervisory staff will be encouraged and educated to practice waste minimization, reuse and recycling to reduce quantity of the waste;	CC, SC, PRMSC	Through Trainings Photographic record;	Monthly	SC and PIMU	N/A
		• Domestic and chemical effluents from the construction camp will be disposed of by the development of on-site sanitation systems i.e., septic tank prior to discharge to nearby drain. Septic tank will be located adjacent to the construction camp. Proper monitoring to check the compliance of PEQS will be carried out;	CC, SC, PRMSC	Visual inspection	Daily	SC and PIMU	N/A
		• All the solid waste from the camps will be properly collected at source by placing containers and disposed of through proper SWM system. Toxic waste will be handled, stored, transported and disposed separately;	CC, SC, PRMSC	Monitoring compliance to Regular disposal of waste; Photographic record;	Weekly	SC and PIMU	N/A
		• The waste will be properly sealed in containers with proper labels indicating the nature of the waste;	CC, SC, PRMSC	Covered disposal containers	Weekly	SC and PIMU	N/A

Activity	Impacts	Mitigation Measures	Implementation Responsibility	Monitoring Indicators	Monitoring Frequency	Monitoring Responsibility	Cost
				placed at camp;			
		• Solid waste will be segregated at source so that it can be re-used or recycled	CC, SC, PRMSC	Covered disposal containers placed at camp;	Weekly	SC and PIMU	N/A
Flammable and Hazardous Materials	Flammable materials to be used during the construction activities include diesel, furnace oil, petrol, Liquefied Petroleum Gas (LPG), kerosene oil and machinery fuels. These materials present little risk to the environment, if properly transported stored and used; otherwise, they are potentially very dangerous. Improper storage and handling practices for these flammable and explosive materials can pose dangers of fire and blasts in the area.	• Safety procedures will be followed by the contractor and labors strictly while using, handling and storage of these materials;	CC, SC, PRMSC	Visual inspection	Daily	SC and PIMU	N/A
		• Trainings will be provided to the contractor's staff for handling and using of flammable materials and explosives;	CC, SC, PRMSC	Monitoring compliance to handling of flammable material through inventory register; Photographic record;	Daily	SC and PIMU	N/A
		• For safety of construction labors and immediate communities, it is suggested that contractor's staff will be trained about the procedures of safe use, handling and storage of materials;	CC, SC, PRMSC	Visual observation	Twice a week	SC and PIMU	N/A
		• Emphasis will be to decrease the volume of mucking material by reusing and then the disposal at the marked area in environment friendly way. In order to reduce the volume of disposal material,	CC, SC, PRMSC	Visual inspection	Weekly	SC and PIMU	N/A

Activity	Impacts	Mitigation Measures	Implementation Responsibility	Monitoring Indicators	Monitoring Frequency	Monitoring Responsibility	Cost
		maximum part of the excavated material can be used in other activities filling of borrow areas and natural depressions in the project area. In order to increase the aesthetics of the area, native grass can be planted by dumping the surplus material in the proposed area with suitable soil cover.					
Gender Based Violence (GBV)	During construction phase, gender-based violence might arise due to discrimination made against women by unequal work distribution and unequal pay structure among others. Sexual harassment against women might occur as a consequence of mixing of men and women at the construction site, and moving on the roads and markets. This impact is negative in nature during construction stage.	• Awareness will be created among the females at individual and community levels about the construction sites;	CC, SC, PRMSC			SC and PIMU	N/A
		• Workers will not be allowed to crowd in the residential communities within the site;	CC, SC, PRMSC	Visual observation	Twice a week	SC and PIMU	N/A
		• Alternative routes for pedestrian will be provided to avoid mixing of women with workers;	CC, SC, PRMSC	Visual Inspection	Daily	SC and PIMU	N/A
		• Raise awareness among the communities of the potential risks of GBV, and establish response services in the nearby communities that can respond to instances of GBV (particularly those related to issues of labor influx);	CC, SC, PRMSC	Reported issues; Awareness compaigns	Daily	SC and PIMU	N/A
		• The Contractor will make sure that no discrimination is made on the basis of gender while hiring of workers;	CC, SC, PRMSC	Hiring Criteria	Before Hiring	SC and PIMU	N/A
		• Provisions of gender disaggregate bathing, changing, and sanitation facilities;	CC, SC, PRMSC	Design provisions	Once (before construction of construction	SC and PIMU	N/A

Activity	Impacts	Mitigation Measures	Implementation Responsibility	Monitoring Indicators	Monitoring Frequency	Monitoring Responsibility	Cost
					camps)		
		• Contractor will take proper measures to address and resolve issues relating to harassment, intimidation, and exploitation, especially in relation to women.	CC, SC, PRMSC	Visual inspection; Complaints reported	Daily	SC and PIMU	N/A
		• The Contractor will prepare the Codes of Conduct and get it signed by all workers, and effectively communicate to all workers and project beneficiaries.	CC, SC, PRMSC	Hiring Criteria	Before Hiring	SC and PIMU	N/A
Influx of Labor	Risk of social conflict: Conflicts may arise between the local community and the construction workers, which may be related to religious, cultural or ethnic differences, or based on competition for local resources; Increased risk of illegitimate behaviour and crime: The influx of workers and service providers into communities may increase the rate of crimes and a perception of insecurity by the local community. Such illegitimate behaviour and crimes can include theft, physical assaults, substance abuse, sexual	• Labour camp(s) will be established away from residential population;	CC, SC, PRMSC	As per approved site	Once	SC and PIMU	N/A
		• Preference will be given to the local people to work with contractor, and contractor should hire maximum labour force from the project area because this will reduce the labour influx	CC, SC, PRMSC	Hiring Criteria	Once before hiring	SC and PIMU	N/A
		• Awareness will be created among the work force to ensure respect for local customs;	CC, SC, PRMSC	Monitor training record	Monthly	SC and PIMU	N/A
		• Construction work will be completed within the stipulated time to move workers to next location;	CC, SC, PRMSC	Visual inspection	Daily	SC and PIMU	N/A
		• Labor force will be shuffled with the time;	CC, SC, PRMSC	Visual inspection	Weekly	SC and PIMU	N/A
		• Create awareness among workers on proper sanitation and hygiene practices to endorse proper health and maintain good housekeeping practices at all project sites;	CC, SC, PRMSC	Visual inspection	Daily	SC and PIMU	N/A
		• Provide adequate personal	CC, SC, PRMSC	Visual	Daily	SC and PIMU	N/A

Activity	Impacts	Mitigation Measures	Implementation Responsibility	Monitoring Indicators	Monitoring Frequency	Monitoring Responsibility	Cost
	assault and human trafficking;	hygiene facilities in good condition with adequate supply of clean water;		inspection			
		• Make arrangements to treat the affected workers on time to control the movement of vectors disease	CC, SC, PRMSC	Visual inspection; Complaint reported	Daily	SC and PIMU	N/A
		• Sensitize workers and surrounding communities on awareness and prevention of HIV/AIDS and sexually transmitted infections (STI) through training, awareness campaigns and workshops during community meetings;	CC, SC, PRMSC	Complaint reported	Weekly	SC and PIMU	N/A
		• Provide proper and free HIV/AIDS and STI health screening and counselling for site workers and community members;	CC, SC, PRMSC	Hiring protocols	Before hiring	SC and PIMU	N/A
		• Develop and enforce a strict code of conduct for workers to regulate behaviour in the local communities;	CC, SC, PRMSC	Visual inspection; Complaint reported	Weekly	SC and PIMU	N/A
		• Prohibiting drugs, alcohol, weapons, and ammunition on the worksite among personnel;	CC, SC, PRMSC	Visual inspection; Complaints reported	Daily	SC and PIMU	N/A
		• The Contractor must guarantee that good relations are maintained with local communities and their leaders to help reduce the risk of vandalism and theft.	CC, SC, PRMSC	Visual inspection	Daily	SC and PIMU	N/A
Social/ Cultural Conflicts	During the construction phase of the project, conflicts may arise	• Public notification through announcements in local mosques during the entire construction	CC, SC, PRMSC	Visual inspection	Daily	SC and PIMU	N/A

Activity	Impacts	Mitigation Measures	Implementation Responsibility	Monitoring Indicators	Monitoring Frequency	Monitoring Responsibility	Cost
	between labor force and local community. Use of local resources and products by the construction workers can generate stress on the local biophysical resources. Furthermore, difference in cultural values may also cause discomfort to local residents. This impact is temporary and minor negative in nature.	phase to avoid any inconvenience in accessibility to the locals;					
		• Establishment of formal links with affected communities;	CC, SC, PRMSC	Visual inspection	Weekly	SC and PIMU	N/A
		• Plan for social grievance redress mechanisms including the local leaders and community representatives;	CC, SC, PRMSC	During construction of the work	Weekly	SC and PIMU	N/A
		• Local labor will preferably be employed for construction works;	CC, SC, PRMSC	Hiring Policies	Once (Before Hiring)	SC and PIMU	N/A
		• Careful planning and training of workforce to minimize disturbance to the local people;	CC, SC, PRMSC	Visual inspection	Daily	SC and PIMU	N/A
		• Contractor will preferably arrange their own sources of water.	CC, SC, PRMSC	Visual observations	Daily	SC and PIMU	N/A
Child Labor	Due to poverty and feeble financial situation of the area, the underaged children might get involved with the contractor various construction works. This will be the violation of the Child Labor Act. Furthermore, SEA/SH issues might arise which will create social conflicts. This impact is adverse and temporary in nature.	• Standard clause in the contracts related to child labor explicit prohibitions, etc.) and contractor will ensure compliance to the contractual provisions on bonded and child labor, equal wages for similar work explicit prohibitions, etc.).	CC, SC, PRMSC	Visual Observation	Daily	SC and PIMU	N/A
Anticipated Impacts during Operational Phase							
Soil	The soil quality may be affected due to leakage/ infiltration from sewer lines and STP bed. The sludge generated from	• Sludge shall be treated prior to ultimate use/disposal. Various options for sludge treatment include Digestion, Drying/ Dewatering, Composting, Lime	PRMSC	Visual inspection	Weekly	PIMU-PRMSC	N/A

Activity	Impacts	Mitigation Measures	Implementation Responsibility	Monitoring Indicators	Monitoring Frequency	Monitoring Responsibility	Cost
	cleaning/ maintenance of pumping stations, manholes, sewers and STP may contaminate the soil. The liner of the STP, while desludging may get dried and cracks may lead to the seepage of wastewater and thus contaminate the soil. Improper disposal of scum and sludge is another concern. This is a moderate negative impact.	Stabilization, Heat Treatment must be considered;					
Air Quality	The operation of sewerage scheme will result in generation of gases including H_2S and CH_4. H_2S is a foul-smelling poisonous gas which might be harmful for the sewer-men and could be fatal sometimes. CH_4 is natural gas also referred to as a greenhouse gas	• Provision of exhaust gas vents at appropriate locations in the design	PRMSC	Visual inspection	Monthly	PIMU-PRMSC	N/A
		• Sewer-men will cover their faces with gas mask while entering the sewer for cleaning or maintenance purposes;	PRMSC	Visual inspection; Use of PPEs	Weekly	PIMU-PRMSC	Cost given in ESMP Budget
		• It's better to use sucking machinery for cleaning of sewers;	PRMSC	Availability	Once	PIMU-PRMSC	N/A
		• Use gas detector before inspection;	PRMSC	Visual inspection	Daily	PIMU-PRMSC	N/A
		• Adequate tree plantation must be done around the STP to control the spread of odour;	PRMSC	Visual inspection	Weekly (maintenance)	PIMU-PRMSC	N/A

Activity	Impacts	Mitigation Measures	Implementation Responsibility	Monitoring Indicators	Monitoring Frequency	Monitoring Responsibility	Cost
Odour	STP are designed on adequate waste loading and function well if they are not overloaded. The overloading will result in malfunctioning of STP and it will result in significant odour generation in the vicinity. This impact is temporary and high adverse in nature.	• The STP should not be overloaded and personnel dealing in operation should be trained to avoid operational issues;	PRMSC	Visual inspection	Daily	PIMU-PRMSC	N/A
Solid Waste	Domestic and hazardous wastes would be generated during cleaning and maintenance activities. The solid waste during operational phase will consist of plastics, metal and organic wastes present in sewer lines which can cause blockage in sewerage system.	• Waste shall be collected, stored and disposed of according to relevant standards in approved facilities;	PRMSC	Visual inspection	Weekly	PIMU-PRMSC	N/A
		• An organized collection system and its implementation through a licensed contractor;	PRMSC	Hiring of licensed contractor	Once	PIMU-PRMSC	N/A
		• The containers will be timely removed and the fine will be imposed on contractor in case of violations;	PRMSC	Visual inspection	Daily	PIMU-PRMSC	N/A
		• Closed containers will be used for transportation of waste to the dumping site;	PRMSC	Visual inspection	Weekly	PIMU-PRMSC	N/A
		• Schedule inspection of the sewer lines and STP to keep it clean and to identify any hazardous material;	PRMSC	Visual inspection	Daily	PIMU-PRMSC	N/A
		• Solid waste bins shall be placed at appropriate locations to avoid its mixing in wastewater.	PRMSC	Visual inspection	Weekly	PIMU-PRMSC	N/A
Sludge	Sludge is semi solid material which will be	• Appropriate sludge treatment must be undertaken before disposal of sludge;	PRMSC	Visual inspection	Monthly	PIMU-PRMSC	N/A

Activity	Impacts	Mitigation Measures	Implementation Responsibility	Monitoring Indicators	Monitoring Frequency	Monitoring Responsibility	Cost
	settled at the bottom of the STP due to anaerobic decomposition of biomass. Significant amount of sludge will not be produced in ABR; however, periodic desludging will be done to achieve good removal efficiency. The removed sludge in wet form, if left unattended will create nuisance i.e., odor, soil contamination, groundwater contamination (through percolation/ seepage) and will serve as breeding ground for disease vector.	• The sludge must never be left unattended and should be transferred to designated dumping site after adequate treatment;	PRMSC	Visual inspection	Monthly	PIMU-PRMSC	N/A
		• Dried sludge can be used as a land conditioner in the fields.	PRMSC	Visual inspection	Monthly	PIMU-PRMSC	N/A
		• In case of maintenance/sludge removal, alternative ponds shall remain functional;	PRMSC	Visual inspection	Monthly	PIMU-PRMSC	N/A
		• Inlet and outlet pipework access/maintenance pits should be inspected regularly for blockages. These pits should be covered at other times.	PRMSC	Visual inspection	Daily	PIMU-PRMSC	N/A
		• The water must be bypassed during rain and flooding.	PRMSC	Visual inspection	During rain	PIMU-PRMSC	N/A
Brine Disposal	In case of operation of RO filtration Plants, around 75% of water is rejected and 25% is consumed as treated product water. It means that for every 2000 lph capacity RO plant; we require 6000 lph of raw water to be treated from which 4000 lph will be the RO reject or brine. So, per day 32000 litres of wastewater will be generated from a single	• This water should not be thrown into municipal sewer, rather it should be reused. The reject water will be discharge into irrigation channels where flow will be controlled to ensure proper dilution and water will be used for irrigation. • Brine can be managed through controlled dilution with freshwater or treated effluent to reduce salinity before reuse for irrigation of non-food vegetation e.g, in Barley, sugar beet,	PRMSC	Visual inspection	Monthly	PIMU-PRMSC	

Activity	Impacts	Mitigation Measures	Implementation Responsibility	Monitoring Indicators	Monitoring Frequency	Monitoring Responsibility	Cost
	RO. The rejected water is free from bacteria, viruses and other pathogens but has only dissolved particles in it. RO concentrate disposal issues present significant design and operational challenges that must be addressed. Conventional disposal techniques mostly suffer from direct or indirect contamination of water/soil.	and date palms (southern Punjab). • Reuse of brine for dust suppression on unpaved roads can be considered where environmentally acceptable. • Planting halophytic grasses and shrubs in designated areas can help utilize saline water while stabilizing soil. • Small-scale ponds with brine-tolerant fish or shrimp species can be developed in suitable areas.					
Community Health Hazards	During desludging and cleaning operations the sludge will be piled up temporarily along the manholes and will be a hazard for passers-by and local community. This impact is temporary and moderate negative in nature. The treated wastewater from STP will be used in agricultures in nearby areas. The community using the part will be exposed to the effects of treated wastewater. This impact is permanent and moderate negative in nature.	• The treated wastewater shall be routed to the agricultural area in a way that there must not be physical contact of the community;	PRMSC	Visual inspection	Daily	PIMU-PRMSC	N/A
		• The community must be educated on the effects of treated wastewater to avoid health issues;	PRMSC	Through Seminars	Yearly	PIMU-PRMSC	N/A
		• The sludge must be timely removed from the site and the area must be barricaded during desludging and cleaning periods.	PRMSC	Visual inspection	Monthly	PIMU-PRMSC	N/A

Activity	Impacts	Mitigation Measures	Implementation Responsibility	Monitoring Indicators	Monitoring Frequency	Monitoring Responsibility	Cost
Cumulative Impact of Several Water extraction Points and Sewerage Treatment Systems	Cumulative impact may occur as a result of development of several treatment plants or several water extraction points.	• Water quality monitoring should be done by the third party on quarterly basis to ensure the supply of safe drinking water.	PRMSC	WHO Guideline /PEQS	Quarterly	PIMU-PRMSC	PCRWR through Separate contract
		• Groundwater table will be monitored periodically.	PRMSC	Depth in meter/feet	Quarterly	PIMU-PRMSC	N/A
		• Maintenance of ABR should be done annually for its smooth operations.	PRMSC	Visual inspection	Annually	PIMU-PRMSC	N/A
		• Ensure the treated effluent follows the National Environmental Quality Standards	PRMSC	PEQS	Monthly	PIMU-PRMSC	PCRWR through Separate contract
		• Water metering system should be installed to know the total consumption of water.	PRMSC	Water Meters	Once at the time of connection	PIMU-PRMSC	N/A
Social Inclusion	It is crucial to ensure that every stakeholder of the community have equal access on the provision of clean drinking water and sanitation facilities, improved healthcare facilities, educational facilities and on economic excess and job opportunities. In this proposed project efforts will be made to promote the participation of marginalized groups, such as women and minorities, elderly person in decision-	• Providing awareness campaigns to increase knowledge and understanding of the project and challenges faced by marginalized groups.	PRMSC	Visual inspection	Weekly	PIMU-PRMSC	N/A
		• Providing awareness on the importance of clean drinking water & sanitation, education, job training, and community services to underserved and marginalized populations.	PRMSC	Visual inspection	Weekly	PIMU-PRMSC	N/A
		• Fostering partnerships between PRMSC-TO and VOs/VCs to promote social inclusion to address the root causes of social exclusion.	PRMSC	Visual inspection	Monthly	PIMU-PRMSC	N/A
		• Regular monitoring and evaluation	PRMSC	Visual	Weekly	PIMU-PRMSC	N/A

Activity	Impacts	Mitigation Measures	Implementation Responsibility	Monitoring Indicators	Monitoring Frequency	Monitoring Responsibility	Cost
	making processes and community activities	of project policies and programs to ensure they are effective and inclusive		inspection			
Elite Capture	Elite capture is often facilitated by corruption, nepotism, and patronage networks, which enable the elites to manipulate the system in their favor. The consequences of elite capture are far-reaching, with the general public often left without access to basic amenities such as health, education, water and sanitation.	• To avoid elite capture the VLD will not be accepted from the person having more than 25 acres land	PRMSC	Visual inspection	Monthly in meeting of VO	PIMU-PRMSC	N/A
		• Involving multiple stakeholders, including community members, in decision-making processes related to project activities.	PRMSC	Visual inspection	Monthly in meeting of VO	PIMU-PRMSC	N/A
		• Robust and transparent GRM will be implemented	PRMSC	Visual inspection	Daily	PIMU-PRMSC	N/A
		• To promote the participation of marginalized groups, such as women and minorities, in decision-making processes	PRMSC				
		• Strengthening institutions such as VO's/VC's and regulatory agencies without undue influence from elites	PRMSC	Visual inspection	Once at the time of VO's formation or Change in VO's	PIMU-PRMSC	N/A
		• Due diligence will be held during VLD process to absolve the doner from all the associated land rights.	PRMSC	Visual inspection	Once at the time of VLD	PIMU-PRMSC	N/A
End users of Treated wastewater	The VO of the village will decide the distribution rights of treated wastewater according to the needs of community.	• End water users will adopt water conservation measures such as reducing water wastage, using efficient irrigation methods	PRMSC	Awareness campaigns	Weekly	PIMU-PRMSC	N/A
		• Equal rights of the community on the usage of treated water will be ensure by the VO's.	PRMSC	Visual inspection	Need Basis	PIMU-PRMSC	N/A
		• Distribution of treated wastewater will be decided by VO's/VCs in village	PRMSC	VO's Meeting	Need Basis	PIMU-PRMSC	N/A

Activity	Impacts	Mitigation Measures	Implementation Responsibility	Monitoring Indicators	Monitoring Frequency	Monitoring Responsibility	Cost
		• VO will ensure monitoring and evaluation on regular basis regarding the usage and conservation of treated water	PRMSC	Visual inspection	Need Basis	PIMU-PRMSC	N/A
		• Awareness campaigns will be conducted on the understanding and importance of water conservation and its impacts.	PRMSC	Awareness campaigns	Once at the time of VLD	PIMU-PRMSC	N/A
Occupational Health and Safety Hazards	Infections resulting from direct contact with treated wastewater, and from infected wounds; and Intestinal infections that are transmitted by flies feeding on the STP.	• The Contractor should prepare OHS and ERPs during operation phase;	PRMSC	Implementation of OHS & ERPs	Daily	PIMU-PRMSC	N/A
		• Instructing the workforce on handling of treated wastewater;	PRMSC	Visual inspection	Daily	PIMU-PRMSC	N/A
		• Provide basic medical training to the specified work staff and basic medical service and supplies to workers;	PRMSC	Visual inspection;	Daily	PIMU-PRMSC	N/A
		• Obligatory insurance of work laborers against accidents;	PRMSC	Visual inspection	Fortnightly	PIMU-PRMSC	N/A
		• Provision of safety measures such as emergency sirens, firefighting equipment, first aid, and contingency measures in case of accidents;	PRMSC	Visual inspection	Monthly	PIMU-PRMSC	Cost is provided in ESMP budget
		• PRMSC-Tehsil Office, within 24 hours, will promptly notify the World Bank for project-related incident within a maximum timeframe of 24 hours.	PRMSC- Tehsil Office	Accident/ Incident reported.	If happened	PRMSC	N/A

KEY

CC	Construction Contractor
DC	Design Consultant
EPA	Environment Protection Agency
SC	Supervision Consultant

7.8 Grievance Redressal Mechanism (GRM)

The Grievance Redress Mechanism (GRM), outlines the policy and procedure for documenting, addressing, responding, and employing methods to resolve project grievances and complaints that may emerge during and after PRSWSSP sub-projects implementation. It will also cater to managing any disconnects that emerge from the field level and that have significant implications for the effective implementation of the sub-project interventions.

In an effort to deter fraud and corruption, the use of a dedicated mobile application has been proposed for reporting grievances from the field level to district and provincial headquarters. This will not only provide a coherent system of checks and balances but will also enable swift redressal and effective monitoring of complaints.

The PIMU at the Local Government & Community Development Department (LG&CDD) level will serve as the Secretariat for the Grievance Redressal Committee (GRC Directorate) that will be responsible for providing oversight on the entire GRM process at a strategic level and monitoring complaints management.

Water supply & sanitation are imperative daily basis facilities. Due to, continuous use and all-time requirement, there is a tendency for routine O&M requirements of the facilities. O&M will be needed as soon as project interventions are completed in the village. Due to the huge number of beneficiaries spread, a comprehensive complaint redressal model is indispensable for Service Delivery Unit (SDU). The Grievance Redress Mechanism (GRM) will be consistent with the Component 4 Project Management and Monitoring sub-component 4.2 Grievance Redressal Model is part of the Project of PRSWSSP. Project activities may cause social friction if Projects do not have an effective GRM.

7.8.1 Objectives

The Grievance Redressal Mechanism (GRM) will be consistent with the requirements of the World Bank safeguard policies to ensure the mitigation of community concerns, risk management, and maximization of environmental and social benefits. The overall objective of the GRM is therefore to provide a robust system of procedures and processes that provides for transparent and rapid resolution of concerns and complaints identified at the village level.

The GRM will be accessible to diverse members of the community, including women, senior citizens, and other vulnerable groups. Culturally, appropriate communication mechanisms will be used at all sub-project sites both to spread awareness regarding the GRM process as well as complaints management. This GRM will be integrated with the PRSWSSP overall project GRM hotline

7.8.2 Disclosure of GRM

The final processes and procedures for the GRM will be translated into local languages and disseminated at all sub-project locations. These shall be made available (in both leaflet and poster format) to all subproject locations through the offices of each SDU. Dedicated male and female Grievance Focal Persons for each sub-project location will play an instrumental role in spreading awareness regarding the GRM, including the use of information technology for reporting and monitoring complaints. It will be ensured that the GRM will be easily accessible for all beneficiaries and workers to raise workplace concerns.

7.8.3 Records and Monitoring

The Project Director's Office will maintain an electronic database at the PIMU that will provide a summary of complaints received and mitigations. The PD office will also provide an analysis of the grievances at each sub-project location using a pre-designed Monitoring and Evaluation (M&E) template that will give insight into the type of complaints received and a qualitative and quantitative review of grievance redressal. The PD's office will also be responsible for uploading the actions and results for each grievance for each sub-project location on a periodic basis to the Project website. The dedicated mobile application that will be used to communicate grievances will provide the basis for recording complaints both at the provincial and district levels.

Apart from the electronic database that will be maintained at the PIMU level, a manual register of all complaints and actions taken will be maintained by the Environmental and Social Focal Persons at the Office of the SDU-TOs and a manual register of all day-to-day complaints and their grievance redressal details will be maintained by VOs their office.

GBV-related issues will be recorded through GRM, two separate focal persons for males and females are part of Village Organization VO – which will also work as tier-1 of the Grievance Redressal Committee (GRC). The female focal person – trained on the referral directory – will be responsible for further referral of GBV-related complaints to the forums concerned. A multi-sectoral referral system is proposed, which will include referral to The Punjab Women's Toll-Free Helpline 1043 available 24/7. It is managed and supervised by Punjab Commission on the Status of Women (PCSW). Their helpline team comprises all-women call agents, three legal advisors, a psychosocial counselor, supervisors, and management staff. Moreover, awareness and advocacy training at schools and community level would be conducted on social protection mechanisms/ referral mechanisms vis-à-vis Gender-Based Violence (physical, sexual, verbal, psychological, etc.), Sexual Exploitation and Abuse (SEA), and Sexual Harassment (SH). The Punjab Commission on the Status of Women (PCSW) has been identified as a key stakeholder. PCSW will be informed of the project activities and an institutional link will be established. Furthermore, at the PRMSC Tehsil Office, the Behavior Change and Communication (BCC) Officer – in addition to being member of GRC Tier-I&II – will initially deal with gender related issues/ complaints and further refer the same to the Gender Specialist at Head Office, PRMSC.

7.8.4 Proposed Institutional Mechanisms

It is proposed to establish the following prior to commencing project implementation activities including pre-construction activities:

Tehsil Level-Public Complaints Center (PCC) in SDU-TO will be responsible to receive, log, and resolve complaints at the site and in Village-level. The complainant would be able to launch a complaint on a toll-free number, mobile application, message, or telephone.

Tier 1: Village level –Panchayat/Village Councils (VC) made under Punjab Local Government (Amendment) Ordinance 2021 will act as the 1st Tier of GRM at the village/community level. Since VCs are not functional, the Project Appraisal Document (PAD) recommends establishment of informal Village Organizations (VOs) in lieu of VCs until formal VCs are elected. This informal VO will comprise of nine (09) members including a chairperson. All the members of the VO will be elected by the village community except a line department's representative and a BCC Officer of the PRMSC. These non-elected members are part of the VOs to give credence/ recognition to the VO. Moreover, the BCC Officer will forward the unaddressed complaints to the Tier-II of the GRC.

Tier 2: Grievance Redress Committee (GRC-Tehsil Level) in SDU-TO will be established for each tehsil that will manage GRM aspects for all sub-project locations in each tehsil including decisions to be taken, actions and monitoring of complaints resolution at the sub-project level. GRC-II, Tier-II comprises of nine (09) members. Respective Tehsil Manager will spearhead the Tier-II. Moreover, to ensure community participation in the Tier-II, the chairperson of the concerned village from where the complaint is lodged will also be a member.

The composition of GRCs of all tiers has been attached as Annexure-10.

7.8.5 GRM Process Implementation

The grievance redress process is described hereunder:

- Through the envisaged system, the complainant would be able to launch a complaint on a toll-free number, mobile application, message, or telephone (GRM can accept anonymous grievances).
- Details of the complaints and the complainants will be entered into the system and a complaint number will be provided to the complainant through SMS.
- In SDU a specific person will be designated to monitor the system and issue necessary instruction to relevant quarter for necessary action.
- The GRM will provide an interface to complainants to check the status of their complaint and a dashboard for SDU & PIMU to monitor the progress on the complaints.
- The system will bridge the gap between the masses and the service provider.
- Monitoring officers will precisely know the details of pending complaints in every SDU. The performance of the SDU could also be easily monitored through it.
- The GRM will have a built-in escalation system for moving unresolved complaints to higher levels.

7.8.6 Mode of Complaint

The complainant can lodge their complaints by opting the following modes:

Written Application	**Telephonically**	**Verbally**	**Android Application**	**Website**

7.8.7 GRM Procedures and Timelines

The tracking and documenting of grievance resolutions will include the following elements:

- Tracking complainant(s) from subprojects sites (field and community level) to PIMU;
- Dedicated staff to update the database routinely;
- Promote transparency, publicize how complaints are being handled, and periodically evaluate the overall functioning of the mechanism;
- Processes for informing stakeholders about the status of a case; and
- Procedures to retrieve data for reporting purposes, including the periodic reports, from Village and Tehsil and document them into the monthly progress reports at PIMU.

GR (Village level) will be responsible to receive, log, and resolve complaints at the village level. The Grievance Redress Committee at the village Panchayats will review and identify actions to be taken to address the complaints at its weekly meeting. If not resolved timely then complaint would be referred to GRC-Tehsil Level (SDU-TO) within 3 days after receiving.

GRC-SDU-TO will try to resolve the complaints in a satisfactory manner anyhow, if not satisfactorily resolved by the village panchayats/councils and Tehsil level, then the grievance will be referred for consideration by GRC at the PIMU/LG&CDD level within one week.

Every effort will be made to address or resolve grievances within the following fixed timelines, which will be an indicator of the performance of the handling system. Acknowledgment of a written submission will be issued to the complainant within three working days.

If the complainant is not satisfied, the complaint will have the option to seek redress through the court of law.

GRM Procedures for Contractor:

The contractor will add a detailed description of GRM, uptake channels, handling process, and confidential reporting system in C-ESMP.

8 ESMP Budget

8.1 ESMP Cost

As per letter Ref. No. PRMSC/PRSWSSP/EDCS/ESS/19 dated 10-01-2025, the Environmental and Social Management Plan (ESMP) cost has been finalized at PKR 1,520,575 per village, as agreed by PRMSC in consultation with the World Bank representative. Accordingly, for the total four hundred twenty-five (425) villages, the consolidated ESMP cost amounts to PKR 646,244,375. The implementation and expenditure of ESMP measures during the construction phase shall be the responsibility of the Contractor. Breakup cost is given below: Detail ESMP cost is attached as **Annex-XVI.**

Sr No.	Description	Amount PKR
1	ESMP cost for one Village	1,520,575
2	ESMP cost for 425 Villages	646,244,375
	Grand Total in Million (RS.)	**646.24**

The ESMP budget consists of six main components:

i. Personal Protective Equipment (PPE)
ii. Health Safety Environment and Trainings,
iii. Environmental testing and monitoring,
iv. CESMP formulation Cost,
v. HSE Supervision Cost (staffing),
vi. Waste Management and Housekeeping

Table 27: Village-wise ESMP Cost

Village-wise ESMP Cost		
Sr.	**ESMP Component**	**Cost (PKR)**
1	PPE	581950
2	HSE &Training	416500
3	Env. Monitoring	286125
4.	CESMP formulation Cost	50000
5	HSE Supervision Cost	120000
6.	Waste Management and Housekeeping	66000
	Total (one village)	**1520575**

Breakup of each component of the ESMP cost is provided below:

8.2 Budget Estimate for PPE During the Construction Phases

Personal Protective Equipment cost is including in the ESMP Cost significantly for Health, Safety and Environment and divided into two categories according to the size of villages small & Large. Breakup of the estimate of the HSE cost for villages is provided in table 27. Which includes safety items ear plugs, helmets, safety shoes, protective goggles, Gloves, Masks and first aid kits.

Table 28: Budget Estimate for HSE During the Construction Phase

Sr. No.	Item Description	ISO / Standard Code / Description	Unit	Unit Rate (Rs)	Quantity (Per Village)	Amount (Rs)
Personal Protective Equipments						
1	Safety Jackets	EN ISO 20471: 360-degree visibility Fluorescent yellow/orange; retro-reflective strips; breathable mesh fabric; secure Velcro or zipper closure, provided in appropriate sizes are required by Staff, PRMSC name and logo printed	Each	654	30	19620
2	Safety Helmets	EN-397 High-density polyethylene (HDPE) or ABS plastic; adjustable screw harness; Adjustable headbands, chin straps, and non-allergic sweatbands. color-coded (white for engineers, yellow for workers) PRMSC Branding and LOGO PRINTED with sr number mentioned on each helmet for ease of record keeping	Each	5668	30	170040
3	Safety Gloves	EN 388 : Nitrile-coated or leather palm; abrasion and cut-resistant; breathable back; conforms to EN388 safety ratings	Each	650	50	32500
4	Dust Mask (Dust proof mask)	ISO 16975: Disposable N95 or FFP2 class mask; elastic bands; nose clip for sealing; replace after use	Each	500	100	50000

Sr. No.	Item Description	ISO / Standard Code / Description	Unit	Unit Rate (Rs)	Quantity (Per Village)	Amount (Rs)
5	Safety Shoes & Toes	EN ISO 20345, requiring a toe cap to withstand a minimum 200-joule impact and 15 kilonewtons (kN) of compression Steel toe cap; anti-slip, oil-resistant sole; leather upper; ankle support for shoes only	Each	8175	35	286125
6	Safety Harness Belt	ISO 10333: High-tenacity polyester webbing, minimum width 45mm; adjustable shoulder and thigh straps with metal buckles; dorsal D-ring for fall arrest, side D-rings for positioning; and chest strap with quick-connect buckle; Renowned Brand	Each	4905	3	14715
7	Protective Goggles	ISO 16321: Anti-fog, scratch-resistant; side shielding for wrap-around protection; adjustable strap	Each	545	10	5450
8	Ear Plugs	ISO 4869-1: Soft polyurethane foam; noise reduction rating (NRR) of 30 dB or more	Each	175	20	3500

8.3 Break Up of Health Safety & Environment

Budget estimate for HSE composed of cost of medical screening of communicable diseases of the labors, cost of tarpaulins to cover the construction material while transporting or storage, cost of handling and disposal of hazardous materials and solid waste, provision of fire alarms and fire extinguishers for fire fighting in case of fire emergency. A special provision for the COVID-19 measure is also part of HSE budget estimate, which will not be utilized if corona situation aggravates and government announce special measures are required to be taken to contain spread of virus. Breakup of the estimate of the HSE cost for village is provided in table 27.

Table 29:Break Up of Personal Protective Equipment

Sr. No.	Item Description	ISO / Standard Code / Description	Unit	Unit Rate (Rs)	Quantity (Per Village)	Amount (Rs)
Health Safety Environment Materials / Testing						
9	First Aid Kit	ISO 7010-E003: Painkiller, eyewash solution, antibiotic ointment, thermometer, plasters, sterile gauze, dressings, sterile eye dressings, triangular bandages, crepe rolled bandages, safety pins, disposable sterile gloves and tweezers), pain killers, burn creams, pyodine solution (big bottle), other medication as required by tehsil team is adequate size and quantity	Each	27250	1	27250
10	Warning / Safety Signs	ISO 7010: Weatherproof PVC or Plastic or aluminum signs; reflective print; standardized colors and pictograms (danger, caution, mandatory)	Each	500	25	12500
11	Green Mesh	Green safety netting for site periphery; 50% shading; UV-stabilized HDPE material.	S.ft	40	200	8000
12	DCP Fire Extinguisher (Dry Chemical Powder)	ISO 7165: 6-kg; ABC type; The extinguishing agent is mono ammonium phosphate and ammonium sulphate powder and the discharge time of the agent is 13 second	No.	11990	1	11990
13	CO_2 Fire Extinguisher	ISO 7165: 5 kg; frost-free horn; suitable for electrical and liquid fires; discharge time of the agent in 13 second)	No.	14170	1	14170
14	Fire Alarm	ICS 13.030.10: Proper segregation, PPE for handlers, timely removal, recordkeeping per solid waste rules	No.	10900	2	21800
15	Trapuline	Waterproof tarpaulin sheet made from polyethylene or canva	Sq.ft	600	30	18000
16	Safety Cones	UV-resistant PVC or rubber material; at least 28 to 36 inches in height; high-visibility orange color with reflective collars (minimum 4-inch reflective band) for day and night visibility		3270	12	39240
17	Tree Plantation	5-6 feet height; Native species plantation; soil preparation and watering included	No.	545	100	54500

Sr. No.	Item Description	ISO / Standard Code / Description	Unit	Unit Rate (Rs)	Quantity (Per Village)	Amount (Rs)
18	Barricading / Fencing (Reflective tape, poles, safety mesh/netting)	ISO 13857: Includes poles, reflective tape, plastic mesh netting; minimum 3 feet height; durable and visible	Rft	20	300	6000
19	Trainings	HSE Training, Rescue Training, Labour Code of Conduct, Environmental Code of Conduct, Defensive Driver Trainings, Labour Laws and Labour Rights, GAP Training, C-ESMP Training and anyother as required by E&S wing	Quarterly	27250	4	109000
20	Water Sprinkling	Water sprinkling through tank mounted on tractor	Per Trip	1500	30	45000
21	Medical Screening for Workers	CBC, Anti HCV, HBsAG, HIV, RPR, LFTs, RFTs etc.	Persons	1635	30	49050

8.4 Environmental Monitoring Cost

Provision for the environmental monitoring is part of the cost of ESMP. Environmental Monitoring will help the client to assess the negative impacts on air and water quality of the concerned villages. Table 29 provide the cost of Environmental Monitoring in village.

Table 30: Environmental Monitoring Cost

Sr. No.	Item Description	ISO / Standard Code / Description	Unit	Unit Rate (Rs)	Quantity (Per Village)	Amount (Rs)
Environmental Testing and Monitoring						
22	Ambient Air Quality Monitoring	As per the parameters and methodology defined by EPA (Quarterly in every village	Each	27250	3	81750
23	Groundwater Quality Test	As per the parameters and methodology defined by EPA (Quarterly in every village	Each	21800	3	65400

Sr. No.	Item Description	ISO / Standard Code / Description	Unit	Unit Rate (Rs)	Quantity (Per Village)	Amount (Rs)
24	Surface Water Quality Test	(As per the parameters and methodology defined by EPA (Quarterly in every village	Each	21800	3	65400
25	waste Water Quality Test	(As per the parameters and methodology defined by EPA (Quarterly in every village	Each	21800	3	65400
26	Noise Level Monitoring	(As per the parameters and methodology defined by EPA (Quarterly in every village)	Each	2725	3	8175

8.5 Training Program

The environmental and social training will help to ensure that the requirements of the ESMP are clearly understood and followed by all project personnel. The primary responsibility of providing this training to all project personnel will be that of the contractor and ESC. The training will be provided to different professional groups separately such as managers, skilled personnel, unskilled labors, and camp staff. **Table 30** provides detail of the training required for the implementation of ESMP during the construction phase.

Table 31: Training for Contractors by PRMSC and EDCS consultants

Training Activity	Participants	Type of Training	Content	Scheduling
Construction Phase (10 months)				
Environment code of practices	Contractor Staff	Presentation	Awareness & applicability of environmental code of practices	Once
Revision of Environment code of practice	Contractor Staff	Presentation	Revision on Awareness & applicability of environmental code of practices	Once

Training Activity	Participants	Type of Training	Content	Scheduling
Waste Management	Contractor Staff	Lecture	Awareness associated with waste Storage, collection and safe disposal	Once
Workers Code of Conduct	Contractor Staff	Presentation & FGD	Do's and don't's of community interaction	twice
Grievance Redress Mechanism	All relevant project staff including contractor	Presentation & FGD	roles and procedures of GRM	
Awareness workshop regarding Covid 19 and other vector borne diseases	Contractor Staff	Presentation	Risk, Prevention and available treatment	Once
2Community/ occupational health and safety	Contractor Staff	Lecture	Awareness on EHS Guidelines	Once
Emergency Response	Contractor Staff	Workshop	Potential natural and other hazard/emergencies and dealing with emergency to minimize damage	Once
WB OPs & PEPA Regulations	Managerial Staff of Contractor	Lecture	Awareness on World Bank OPs, PEPA rules, guidelines, regulation and standards for satisfactory compliance	Once

Training Activity	Participants	Type of Training	Content	Scheduling
Resettlement Related Issues	Contractor and ESC Staff of PIMU	Lecture	Awareness on OP 4.12 (Involuntary Resettlement)	Once
Labour Code of Practise	Contractor Staff	Lecture	Awareness & applicability of Laboral code of practices	Once
Gender Aspects	Contractor Staff	Lecture	Awareness on gender inequalities/GBV OP 4.20	Once

8.6 Institutional Capacity & Strengthening

In order to ensure that the ESMP provisions are implemented efficiently and effectively, capacity building/ strengthening of the implementing parties are required. Therefore, based on the assessment of the institutional capacities of the parties involved in the implementation of the ESMP, the following broad areas of capacity building/strengthening have been identified and recommended for effective implementation of the ESMP.

Table 31 shows the positions proposed for institutional strengthening for effective implementation of environmental and social mitigation measures and a cost of PKR 120,000 is dedicated to each village and it is anticipated that each procurement package will consist of 8 to 12, villages providing sufficient financial compensation for the HSE supervision staff to be hired on contractor payroll.

Table 32: HSE Supervision

Institutional Strengthening	Position	Scheduling (Months)	Responsibility
Contractor	Environmental/ HSE Expert	10	▪ Responsible for the overall implementation of ESMF processes and procedures in the light of WB policies and Guidelines and local policies and procedures; ▪ Closely follow up the integration of safeguard assessment information and inclusion of safeguards self-screening process at the project development and design stage; ▪ Provide technical support during proposal development, project design, appraisal process, and resource mobilization plan for the sub-projects in all locations; ▪ Undertake follow-up monitoring to ensure that proposed mitigation measures are implemented according to an agreed-upon environmental and social mitigation implementation plan; ▪ Closely provide assistance and design capacity building/training program for the overall implementation of ESMF from PIMU to village level and deliver capacity building training to the field teams to close knowledge/skill gaps and minimize the likelihood of risks happening to sub-projects; ▪ Ensure that appropriate environmental and social mitigation measures are proposed and met; ▪ Undertake to follow-up monitoring to ensure that proposed mitigation measures are implemented according to an agreed-upon environmental and social mitigation and implementation plan; ▪ At the PIMU level, maintain the record of all information, documents evidence, and reports including progress reports, TPV Reports, training reports, ESMPs, Screening Checklists, etc.; ▪ Closely work with SSS and Gender Specialists at the PIMU level and provide technical assistance and advice to the Environment/ Water Quality Officers based at SDU-TO

8.7 ESMP Cost of Village

Table No. 32 provides the calculated cost of the Environmental and Social Management Plan (ESMP) The total estimated cost of ESMP is **PKR 646.244 million or 2.3 million US$** for 425 villages in 12 tehsils.

Table 33: ESMP IMPLEMENTATION COST - Village Wise

Sr. No.	Item Description	ISO / Standard Code / Description	PROPOSED FOR 1800 villages			
			Unit	Unit Rate (Rs)	Quantity (Per Village)	Amount (Rs)
Personal Protective Equipments						
1	Safety Jackets	EN ISO 20471: 360-degree visibility Fluorescent yellow/orange; retro-reflective strips; breathable mesh fabric; secure Velcro or zipper closure, provided in approriate sizes are required by Staff, PRMSC name and logo printed	Each	654	30	19620
2	Safety Helmets	EN-397 High-density polyethylene (HDPE) or ABS plastic; adjustable screw harness; Adjustable headbands, chin straps, and non-allergic sweatbands. color-coded (white for engineers, yellow for workers) PRMSC Brading and LOGO PRINTED with sr number mentioned on each helmet for ease of record keeping	Each	5668	30	170040
3	Safety Gloves	EN 388 Nitrile-coated or leather palm; abrasion and cut-resistant; breathable back; conforms to EN388 safety ratings	Each	650	50	32500
4	Dust Mask (Dust proof mask)	ISO 16975: Disposable N95 or FFP2 class mask; elastic bands; nose clip for sealing; replace after use	Each	500	100	50000
5	Safety Shoes & Toes	EN ISO 20345, requiring a toe cap to withstand a minimum 200-joule impact and 15 kilonewtons (kN) of compression Steel toe cap; anti-slip, oil-resistant sole; leather upper; ankle support for shoes only	Each	8175	35	286125

Sr. No.	Item Description	ISO / Standard Code / Description	PROPOSED FOR 1800 villages			
			Unit	Unit Rate (Rs)	Quantity (Per Village)	Amount (Rs)
6	Safety Harness Belt	ISO 10333: High-tenacity polyester webbing, minimum width 45mm; adjustable shoulder and thigh straps with metal buckles; dorsal D-ring for fall arrest, side D-rings for positioning; and chest strap with quick-connect buckle; Renowned Brand	Each	4905	3	14715
7	Protective Goggles	ISO 16321: Anti-fog, scratch-resistant; side shielding for wrap-around protection; adjustable strap	Each	545	10	5450
8	Ear Plugs	ISO 4869-1: Soft polyurethane foam; noise reduction rating (NRR) of 30 dB or more	Each	175	20	3500
Health Safety Environment Materials / Testing						
9	First Aid Kit	ISO 7010-E003: Painkiller, eyewash solution, antibiotic ointment, thermometer, plasters, sterile gauze, dressings, sterile eye dressings, triangular bandages, crepe rolled bandages, safety pins, disposable sterile gloves and tweezers), pain killers, burn creams, pyodine solution (big bottle), other medication as required by tehsil team is adequate size and quantity	Each	27250	1	27250
10	Warning / Safety Signs	ISO 7010: Weatherproof PVC or Plastic or aluminum signs; reflective print; standardized colors and pictograms (danger, caution, mandatory)	Each	500	25	12500
11	Green Mesh	Green safety netting for site periphery; 50% shading; UV-stabilized HDPE material.	S.ft	40	200	8000
12	DCP Fire Extinguisher (Dry Chemical Powder)	ISO 7165: 6-kg; ABC type; The extinguishing agent is mono ammonium phosphate and ammonium sulphate powder and the discharge time of the agent is 13 second	No.	11990	1	11990

Sr. No.	Item Description	ISO / Standard Code / Description	PROPOSED FOR 1800 villages			
			Unit	Unit Rate (Rs)	Quantity (Per Village)	Amount (Rs)
13	CO_2 Fire Extinguisher	ISO 7165: 5 kg; frost-free horn; suitable for electrical and liquid fires; discharge time of the agent in 13 second)	No.	14170	1	14170
14	Fire Alarm	ICS 13.030.10: Proper segregation, PPE for handlers, timely removal, recordkeeping per solid waste rules	No.	10900	2	21800
15	Trapuline	Waterproof tarpaulin sheet made from polyethylene or canva	Sq.ft	600	30	18000
16	Safety Cones	UV-resistant PVC or rubber material; at least 28 to 36 inches in height; high-visibility orange color with reflective collars (minimum 4-inch reflective band) for day and night visibility		3270	12	39240
17	Tree Plantation	5-6 feet height; Native species plantation; soil preparation and watering included	No.	545	100	54500
18	Barricading / Fencing (Reflective tape, poles, safety mesh/netting)	ISO 13857: Includes poles, reflective tape, plastic mesh netting; minimum 3 feet height; durable and visible	Rft	20	300	6000
19	Trainings	HSE Training, Rescue Training, Labour Code of Conduct, Environmental Code of Conduct, Defensive Driver Trainings, Labour Laws and Labour Rights, GAP Training, C-ESMP Training and anyother as required by E&S wing	Quaterly	27250	4	109000
20	Water Sprinkling	Water sprinkling through tank mounted on tractor	Per Trip	1500	30	45000
21	Medical Screening for Workers	CBC, Anti HCV, HBsAG, HIV, RPR, LFTs, RFTs etc.	Persons	1635	30	49050
Environmental Testing and Monitoring						

Sr. No.	Item Description	ISO / Standard Code / Description	PROPOSED FOR 1800 villages			
			Unit	Unit Rate (Rs)	Quantity (Per Village)	Amount (Rs)
22	Ambient Air Quality Monitoring	As per the parameters and methodology defined by EPA (Quarterly in every village	Each	27250	3	81750
23	Groundwater Quality Test	As per the parameters and methodology defined by EPA (Quarterly in every village	Each	21800	3	65400
24	Surface Water Quality Test	(As per the parameters and methodology defined by EPA (Quarterly in every village	Each	21800	3	65400
25	waste Water Quality Test	(As per the parameters and methodology defined by EPA (Quarterly in every village	Each	21800	3	65400
26	Noise Level Monitoring	(As per the parameters and methodology defined by EPA (Quarterly in every village)	Each	2725	3	8175
Site Specific / Contractors Environmental and Social Management Plan						
27	CESMP Formulation	By an individual or firm as approved by PRMSC Environment Wing	per village	50000	1	50000
HSE Staff						
28	HSE Supervisor	Bachelor's degree in Environmental Sciences / Engineering , NEBOSH or IOSH certification will be preffered, with over one year of experience in Occupational Health and Safety, one HSE person for 10-15 village, hiring of HSE staff will be approved by E&S prior to contract signing	Per month per village	10000	12	120000
Waste Management and House Keeping						
29	Handling and disposal of Hazardous Material	ICS 13.030.30: Safe storage, labeling, and transportation; spill kits and secondary containment as per MSDS	3 times per village for duration of contract	11000	3	33000

Sr. No.	Item Description	ISO / Standard Code / Description	PROPOSED FOR 1800 villages			
			Unit	Unit Rate (Rs)	Quantity (Per Village)	Amount (Rs)
30	Handling and disposal of Solid Waste Material	ICS 13.030.10: Proper segregation, PPE for handlers, timely removal, recordkeeping per solid waste rules	3 times per village for duration of contract	11000	3	33000
Note : Cost of ESMP implementation is village wise, PKR 1520575 will be multiplied with the number of villages in the civil work contract package to obtain total ESMP cost						
Total ESMP Implementation Cost per year (PKR)						**1520575**

Annexure-1
List of 2000 Villages

https://docs.google.com/spreadsheets/d/1J5kpPYwaqyjQ0sKS3lG6tNne33gA6Fvl/edit?usp=drive_link&ouid=117039326792292994503&rtpof=true&sd=true

Annexure- 2
Glimpse of Villages

Kot Momin

Chak 08/SB

Baraham Wala

Bahar Wala

Dhudyan

Tridiyan Wala

Bukhi Khurd

Bahk Daim

Murad Wala

Dhingrala

Dhingra wali

Tehsil Ahmedpur Sial

Basti Lal	**Basti Lal**
Basti Muhammad Jhandir	**Basti Muhammad Jhandir**
Bela Badh	**Bela Badh**
Bhid Wal	**Bhid Wal**
Chak No. 1/3-R	**Chak No. 1/3-R**

Chak ½-L

Chak ½-L

Chak No 2/3-R

Chak No 2/3-R

Chak No 2/4-R

Chak No 2/4-R

Chak 3/3-L

Chak 3/3-L

Chak 3/2-L

Chak 3/2-L

Chak 4/3-L	**Chak 4/3-L**
Chak 13/3-L	**Chak 13/3-L**
Jhainder Niazi	**Jhainder Niazi**
Jhok Dargahi Shah	**Jhok Dargahi Shah**

Laghari

Laghari

Wahgah

Wahgah

Detisial

Destisial

Bhinda Gonawala

Bhina Gonawala

Pirow	**Pirow**
Tehsil-Bhawana	
Abhulke	**Abhulke**
Chak 248	**Chak 248**
Fateh Kot Taja	**Fateh Kot Taja**

Kamoke	**Kamoke**
Kotla Shahzada	**Kotla Shahzada**
Malake Rajoke	**Malake Rajoke**
Maral Wala	**Maral Wala**

Samundar	**Samundar**
Nahre Hrseh	**Nahre Hrseh**
Sagarh Wala	**Sagarh Wala**
Saike Saloke	**Saike Saloke**

Shah Fateh Ali

Shah Fateh Ali

Thatta Kundal

Thatta Kundal

Thatta Rasalu

Thatta Rasalu

Thatta Viroka

Thatta Veroka

Kot Sahib

Kot Sahib

Mehroke

Mehroke

Tehsil-Darya Khan

Bilochan Wali

Bilochan Wali

Chak 01 Rakh Dala

Chak 01 Rakh Dala

Chak No 50 ML

Chak No 50 ML

Chak No 51 ML

Chak No 51 ML

Chak No 53.ML

Chak No 53.ML

Chak No 54.ML

Chak No 54.ML

Chak 176 TDA	**Chak 176 TDA**
Chak 177 TDA	**Chak 177 TDA**
Daggar Qureshi Janub Gharbi	**Daggar Qureshi Janub Gharbi**
Daggar Awan Sharqi	**Daggar Awan Sharqi**

Karar Non

Kara Non

Dhanraj Pura

Dhanraj Pura

Surani Nasheb

Surani Nasheb

Chak No 5 Rakh Dallo Wala

Chak No 5 Rakh Dallo Wala

Dulle Wala No 1

Dulle Wala No 1

Tehsil-Pakpattan

Alam Mehtheka

Alam Mehtheka

Amir Ahluka

Amir Ahluka

Arazi Tek Chand

Arazi Tek Chand

Bablana Khara

Bablana Khara

Bhawan Shah

Bhawan Shah

Bahdar Khara

Bahdar Khara

Bahmani

Bahmani

Bonga Aman Din

Bonga Aman Din

Bounga Shamas

Bounga Shams

Chak 12/KB

Chak 12/KB

Chak 87/D

Chak 87/D

Chak 88/D

Chak 88/D

Chak 91/D

Chak 91/D

Chak 100/D

Chak 100/D

Chak 101/D

Chak 101/D

Chak 102/D

Chak 102/D

Chak 104/D

Chak 104/D

Chak 105/D

Chak 105/D

Chak 106/D

Chak 106/D

Ghar Taj

Ghar Taj

Chak Ilahi Bux

Chak Ilahi BUx

Khatwan

Khatwan

Chak Murad Khan

Chak Murad Khan

Chak Nazam Din	**Chak Nazam Din**
Chak No. 4sp	**Chak No 4sp**
Chak Qudrat Ullah	**Chak Qudrat Ullah**
Chak Shah Khagga	**Chak Shah Khagga**

Chak Wasao

Chak Wasao

Chak Wasao Kamboh

Chak Wasao Kamboh

Chhinah

Chhinah

Chilli Mamdana

Chilli Mamdana

Dada Ahluka	**Dada Ahluka**
Dhamiana	**Dhamiana**
Faiz Pur	**Faiz Pur**
Ghazi Mardan	**Ghazi Mardan**

Ghuri

Ghuri

Gobind Pur Bahmni

Gobind Pur Bahmni

Jagga Baluch

Jagga Baluch

Jalil Metheka

Jalil Metheka

Jamal Pur Tahli

Jamal Pur Tahli

Jand Wala

Jand Wala

Kala Chisti

Kala Chisti

Khalita

Khalita

Kirparam	**Kirparam**
Lakh Wiran	**Lakh Wiran**
Magan Pur	**Magan Pur**
Malik Rehmun	**Malik Rehmun**

Maneka

Maneka

Musteqim Mamunka

Musteqim Mamunka

Nabi Bux

Nabi Bux

Nahla Abad

Nahla Abad

Rakh Ferozpur

Rakh Ferozpur

Saleem Shah Bodla

Saleem Shah Bodla

Talibali

Talibali

Waran Peran Khurd

Waran Peran Khurd

Waran Peran Kalan

Waran Peran Kalan

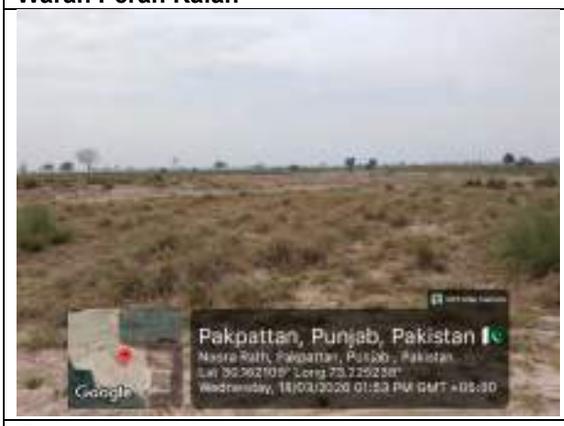

Bahadar Ali

Bahadar Ali

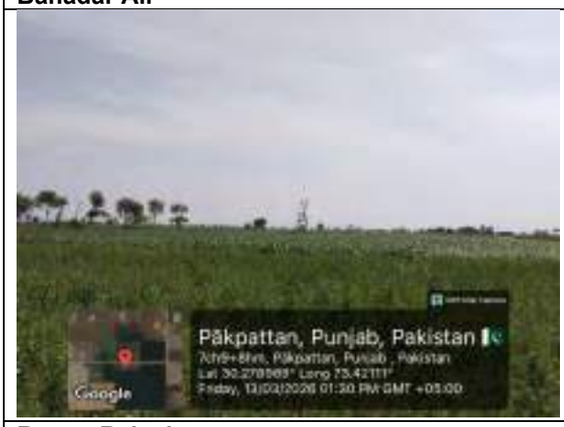

Bunga Baluch

Bunga Baluch

Qudus

Qudus

Sahan Wali

Sahan Wali

Shakhe ke

Shakhe ke

Tarsangai

Tarsangai

Tehsil Liaqatpur.

Village Chak 125 NP, Tehsil Liaqatpur.

Village Chak 131 NP, Tehsil Liaqatpur.

Basti Jatoi Sial, Tehsil Liaqatpur.	**Basti Abdullah Sial, Tehsil Liaqatpur.**
Moza Pararan Sharif,Tehsil Liaqatpur.	**Moza Chimi,Tehsil Liaqatpur.**
Village Nala Musani,Tehsil Liaqatpur.	**Village Goath AmeenTehsil Liaqatpur.**
Tehsil Rojhan	
Chak Dim,Tehsil Rojhan.	**Dera Jewan Khas ,Tehsil Rojhan.**

Chak Mut NO.2 ,Tehsil Rojhan.	**Chak Ladh,Tehsil Rojhan**
Alipur	
Beth Dewan Shib	**Bet Muizidin**
Bet Nabi Shah	**Dhaka**
Damar wala Janubi 1	**Damar wala Janubi 2**

Moza Ghari

Fateh Pur Janubi 1

Fateh Pur Janubi 2

Galwan 1

Galwan 2

Khair pur paran

Khair pur sadat

Khan Ghar Domna

Khundai	Latti
Madd Sohanyara Shah	**Mud wala**
Pakka Naich	**Sheikhani**
Shujabad	
Chak 13 faiz	**Chak Jhakhar**
Chak RS	**Gunwain**

Jalal Pur Khakhi

Khanpur

Moza Amanullah

Moza Taunta

Moza Rajaram

Tudarpur

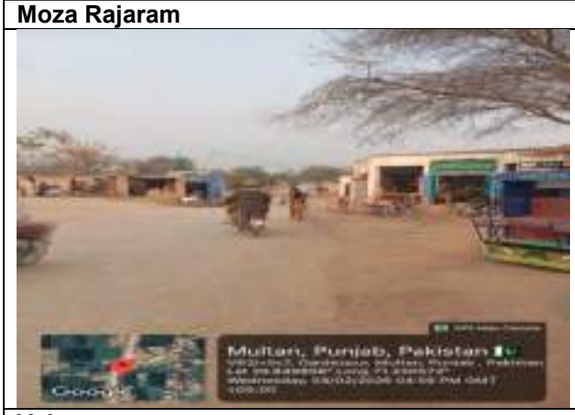

Vainus

Wai Sawaya

Annexure-3
Area of Influence

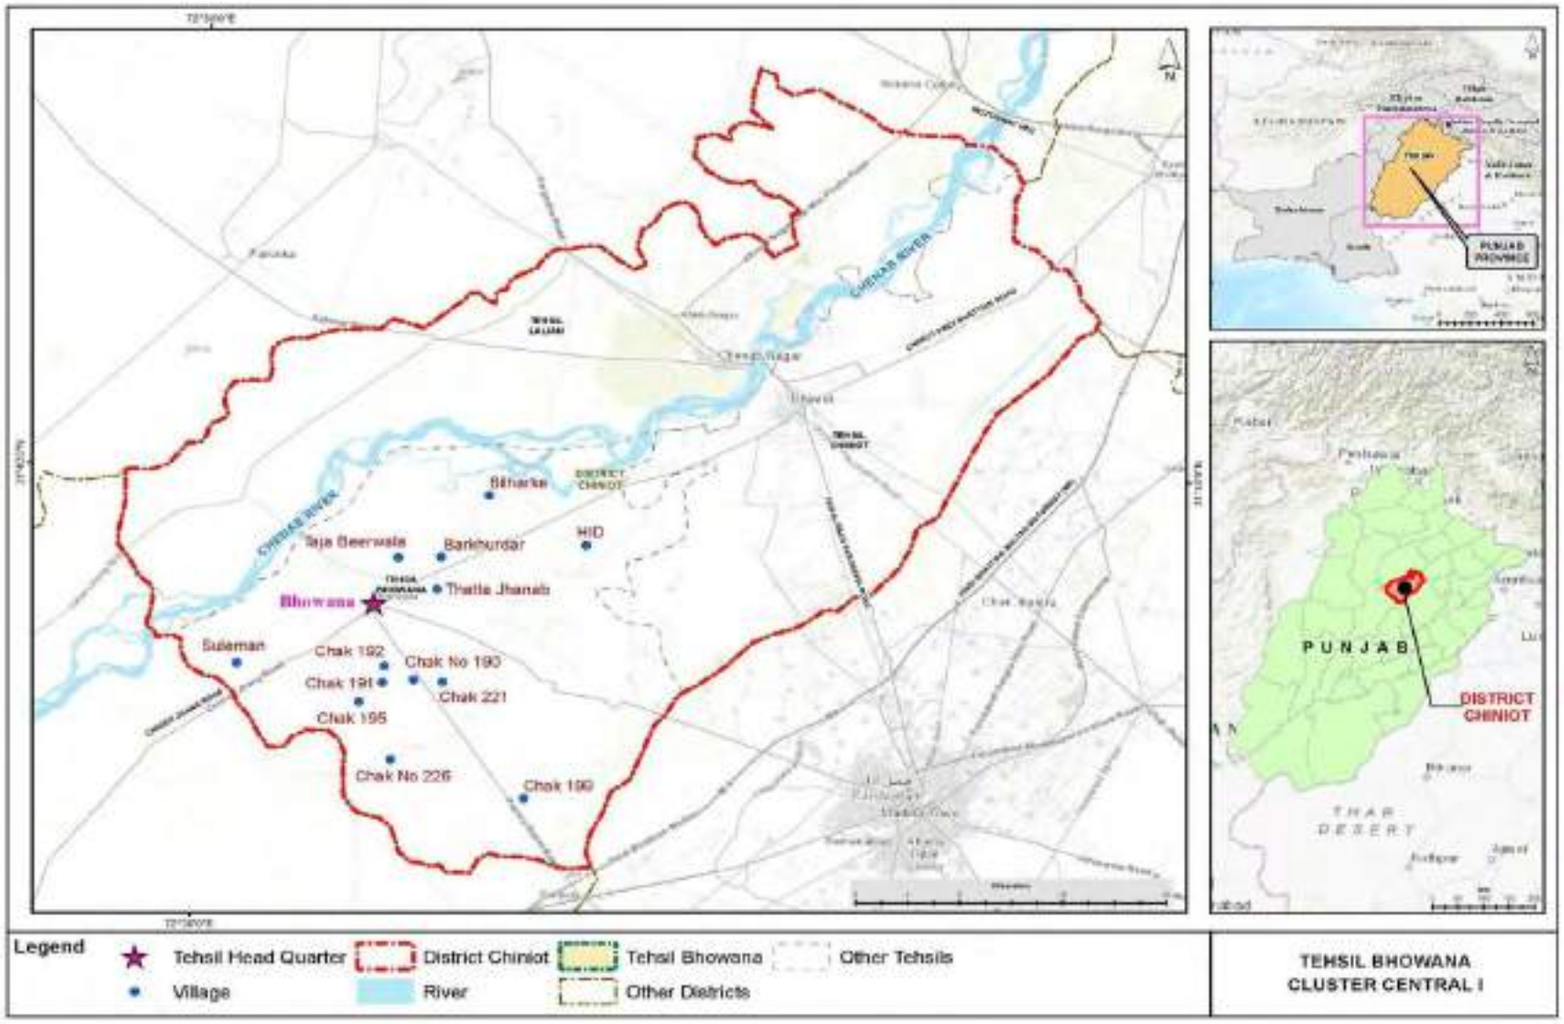

Map indicating the Tehsil Bhawana and relevant villages included in this ESMP

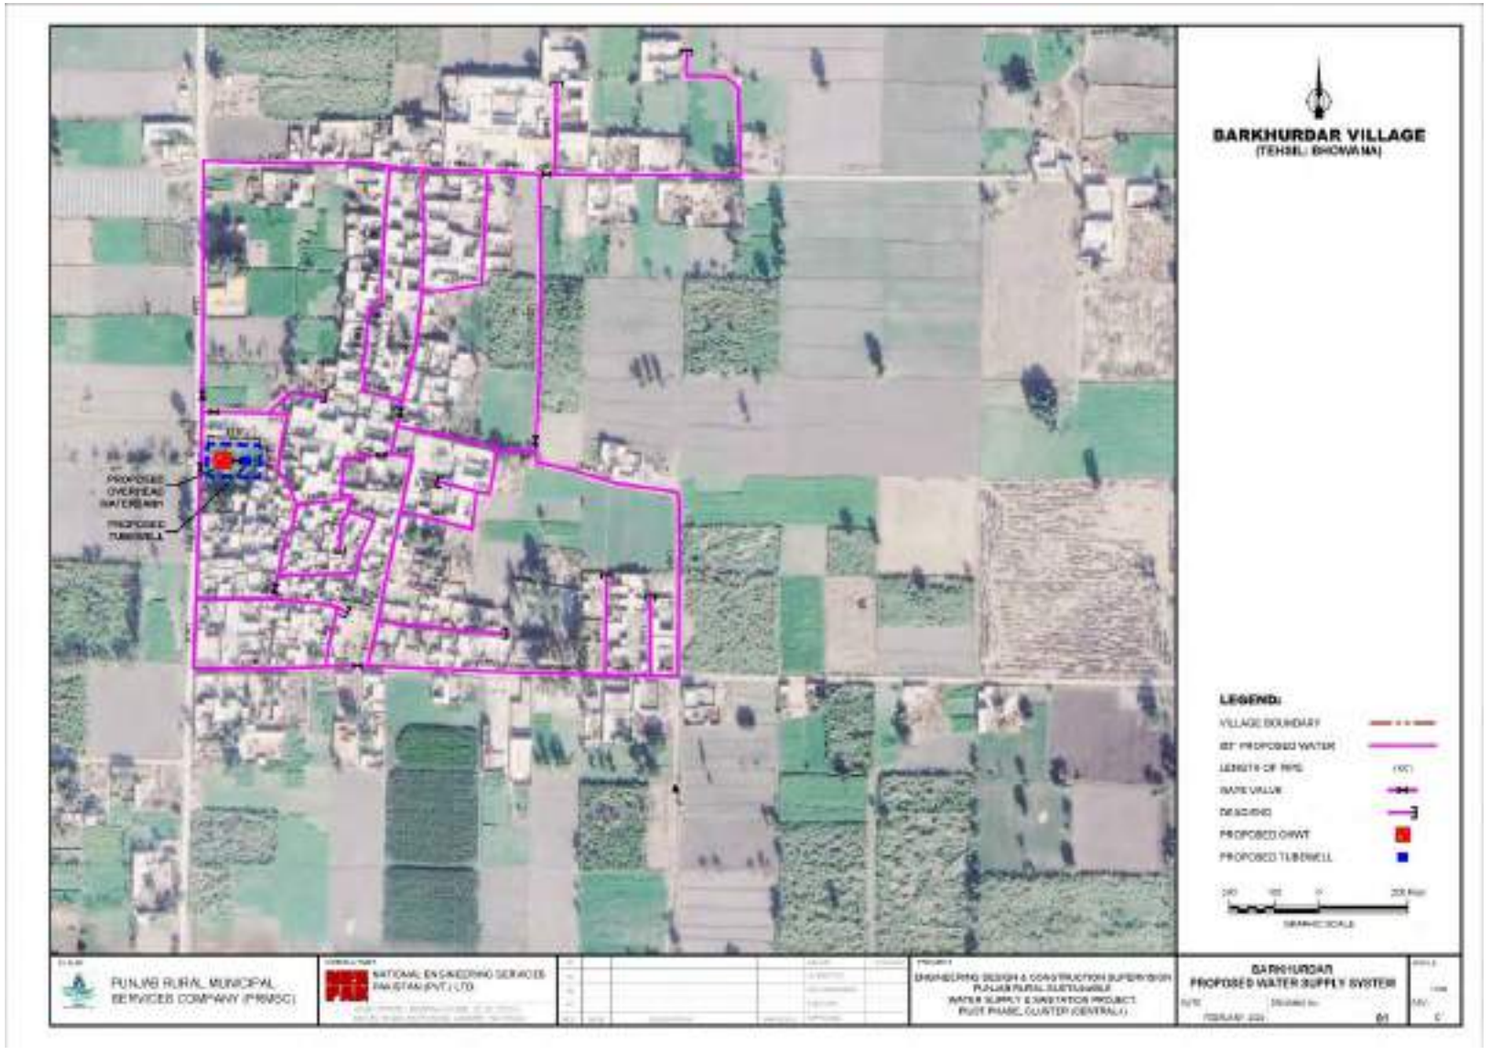

Layout Plan of Proposed Water Supply System in Barkhurdar

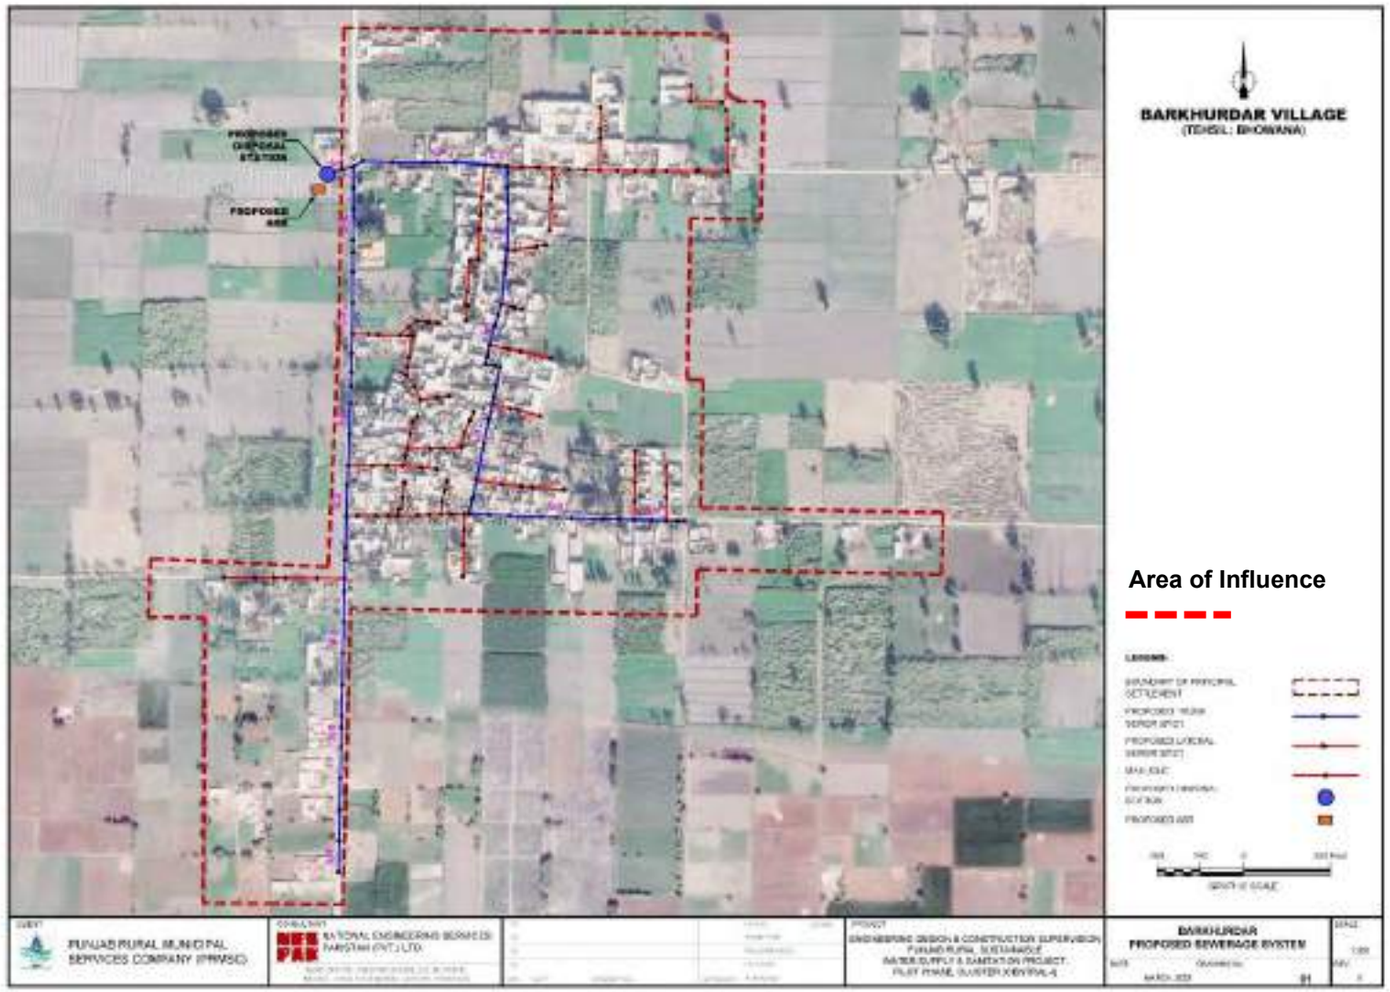

Map showing overview of Barkhurdar and surrounding area, dotted red line represents Area of Influence

Annexure-4
Chance Find Procedures

CHANCE FIND PROCEDURES

Project may involve deep excavation. Therefore, the possibility of chance find is not ignorable. In case of any chance find, the contractor will immediately report through Supervision Consultant to Directorate General (DG) of Antiquities & Archaeology, Government of Punjab to take further suitable action to preserve those antique or sensitive remains. Representative of the "Director Archaeology and Museum (DAM)" will visit the site and observed the significance of the antique, artifact and Cultural (religious) properties and significance of the project. The documentation will be completed and if required suitable action will be taken to preserve those antiques and sensitive remains.

In case any artifact, antiques and sensitive remains are discovered, chance find procedures should be adopted by contractor workers as follows:

- Stop the construction activities in the areas of chance find;
- Delineate the discovered site or area;
- Consult with the local community and provincial Archeological Department
- The suggestion of the local communities and the concerned authorities will be suitably incorporated during taking the preventive measures to conserve the antique, artifact and cultural (religious) properties
- Secure the site to prevent any damage or loss of removable objects. In case of removable antiquities or sensitive remain, a night guard shall be arranged until the responsible local authorities take over;
- After stopping work, the contractor must immediately report the discovery to the Supervision Engineer.

The contact Address of Directorate General of Antiquities & Archaeology is given below:

1st Floor Aiwan-e-Auqaf Building Near

Lahore High Court, Lahore, Pakistan

Tel: 042-99210870

Annexure-5
PEQS and other relevant standards

EXTRA ORDINARY ISSUE

REGISTERED No. L-7532

The Punjab Gazette

PUBLISHED BY AUTHORITY

LAHORE MONDAY AUGUST 15, 2016

GOVERNMENT OF THE PUNJAB
LAW AND PARLIAMENTARY AFFAIRS DEPARTMENT

NOTIFICATION
(121 of 2016)

12th August 2016

The following Notification No. SO(G)/EPD/7-26/2013, dated 05.08.2016 regarding the Punjab Environmental Quality Standards for Noise is published for general information:

DR SYED ABUL HASSAN NAJMEE
Secretary
Government of the Punjab
Law and Parliamentary Affairs
Department

Government of the Punjab
Environment Protection Department

NOTIFICATION: No. SO(G)/EPD/ 2-26 /2013. In exercise of the powers conferred under clause (c) of sub-section (1) of section 4 of the Punjab Environmental Protection Act, 1997 (XXXIV of 1997), the Environmental Protection Council has approved the following as the Punjab Environmental Quality Standards for Noise:

Punjab Environment Quality Standards for Noise

No.	Category of Area/Zone	Effective from 1st July, 2010		Effective from 1st July, 2013	
		Limits in dB(A) Leq*			
		Day Time	Night Time	Day Time	Night Time
1	Residential Area (A)	65	50	55	45
2	Commercial Area (B)	70	60	65	55
3	Industrial Area (C)	80	75	75	65
4	Silence Zone (D)	55	45	50	45

Note:

1. Day time hours; 6:00am to 10:00pm.
2. Night Time hours; 10:00 pm to 6:00 am.
3. Silence Zone: Zones which are declared as such by the competent authority. An area comprising not less than 100 meters around hospital, educational institutions and courts
4. Mixed categories of areas may be declared as one of the four above mentioned categories by the competent authority

* dB(A) Leq: Time weighted average of the level of sound in decibel on scale A which is relatable to human hearing

(IQBAL MOHAMMED CHAUHAN)
Secretary, Government of the Punjab
Environment Protection Department

EXTRA ORDINARY ISSUE

REGISTERED No. L-7532

The Punjab Gazette

PUBLISHED BY AUTHORITY

LAHORE MONDAY AUGUST 15, 2016

GOVERNMENT OF THE PUNJAB
LAW AND PARLIAMENTARY AFFAIRS DEPARTMENT

NOTIFICATION
(122 of 2016)

12th August 2016.

The following Notification No. SO(G)/EPD/7-26/2013, dated 05.08.2016 regarding the Punjab Environmental Quality Standards for Ambient Air is published for general information:

DR SYED ABUL HASSAN NAJMEE
Secretary
Government of the Punjab
Law and Parliamentary Affairs
Department

Price Rs. 10.00 Per Page (1097)

Government of the Punjab
Environment Protection Department

NOTIFICATION: No. SO(G)/EPD/2-26/2013. – In exercise of the powers conferred under clause (c) of sub-section (1) of section 4 of the Punjab Environmental Protection Act, 1997 (XXXIV of 1997), Environmental Protection Council has approved the following as the Punjab Environmental Quality Standards for Ambient Air:

Punjab Environmental Quality Standards for Ambient Air

Pollutant	Time-weighted average	Concentration in Ambient Air	Method of measurement
Sulfur Dioxide (SO_2)	Annual Average*	80 µg/m^3	Ultraviolet Fluorescence method
	24 hours**	120 µg/m^3	
Oxides of Nitrogen as (NO)	Annual Average*	40 µg/m^3	Gas Phase Chemiluminescence
	24 hours**	40 µg/m^3	
Oxides of Nitrogen as (NO_2)	Annual Average*	40 µg/m^3	Gas Phase Chemiluminescence
	24 hours**	80 µg/m^3	
Ozone (O_3)	1 hour	130µg/m^3	Non dispersive UV absorption method
Suspended Particulate Matter (SPM)	Annual Average*	360µg/m^3	High Volume Sampling, (Average flow rate not less than 1.1 m^3/min).
	24 hours**	500µg/m^3	
Respirable Particulate Matter PM_{10}	Annual Average*	120µg/m^3	Preferably β-Ray absorption method
	24 hours**	150µg/m^3	
Respirable Particulate Matter $PM_{2.5}$	Annual Average*	15µg/m^3	Preferably β-Ray absorption method
	24 hours**	35µg/m^3	

Pollutant	Time-weighted average	Concentration in Ambient Air	Method of measurement
	1 hour	15µg/m^3	
Lead (Pb)	Annual Average*	1 µg/m^3	ASS Method after sampling using EPM 2000 or equivalent Filter paper
	24 hours**	1.5µg/m^3	
Carbon Monoxide (CO)	8 hours**	5 mg/m^3	Non Dispersive Infra Red (NDIR) method
	1 hour	10 mg/m^3	

* Annual arithmetic mean of minimum 104 measurements in a year taken twice a week 24 hourly at uniform interval.

** 24 hourly /8 hourly values should be met 98% of the in a year. 2% of the time, it may exceed but not on two consecutive days.

(IQBAL MOHAMMED CHAUHAN)
Secretary, Government of the Punjab
Environment Protection Department

EXTRA ORDINARY ISSUE REGISTERED No. L-7532

The Punjab Gazette

PUBLISHED BY AUTHORITY

LAHORE MONDAY AUGUST 15, 2016

GOVERNMENT OF THE PUNJAB
LAW AND PARLIAMENTARY AFFAIRS DEPARTMENT

NOTIFICATION
(123 of 2016)

12th August 2016

The following Notification No. SO(G)/EPD/7-26/2013, dated 05.08.2016 regarding the Punjab Environmental Quality Standards for motor vehicle exhaust and noise is published for general information:

DR SYED ABUL HASSAN NAJMEE
Secretary
Government of the Punjab
Law and Parliamentary Affairs
Department

Price Rs. 10.00 Per Page (1201)

Government of the Punjab
Environment Protection Department

NOTIFICATION: No. SO(G)/EPD/7-26/2013. – In exercise of the powers conferred under clause (c) of sub-section (1) of section 4 of the Punjab Environmental Protection Act, 1997 (XXXIV of 1997), the Environmental Protection Council has approved the following as the Punjab Environmental Quality Standards for motor vehicle exhaust and noise:

Punjab Environmental Quality Standards for Motor Vehicle Exhaust and Noise

(i) For In-use Vehicles

No	Parameter	Standards (maximum permissible limit)	Measuring methods	Applicability
1	2	3	4	5
1	Smoke	40% or 2 on the Ringlemann Scale during engine acceleration mode	To be compared with Ringlemann Chart at a distance of 6 meters or more	Immediate effect
2	Carbon Monoxide	6%	Under idling conditions: Non dispersive infrared detection through gas analyzer	
3	Noise	85 dB(A)	Sound meter at 7.5 meter from the source	

(ii) For New Vehicles

EMISSION STANDARDS FOR DIESEL VEHICLES

(a) For Passenger Cars and Light Commercial Vehicles (g/km)

Type of Vehicle	Category/Class	Tiers	CO	HC+ NOx	PM	Measuring method	Applicability
1	2	3	4	5	6	7	8

Passenger Cars	M1* with reference mass (RW) upto 2500 kg	Pak-II, IDI	1.0	0.7	0.08		All imported and locally manufactured diesel vehicles with effect from 01-07-2012
	Cars with RW over 2500 kg to meet N1 category standards	Pak-II, DI	1.0	0.9	0.10	NEDC (ECE 15+EUDC L)	
Light Commercial Vehicles	N1-I(RW ≤ 1250kg)	Pak-II, IDI	1.0	0.70	0.08		
		Pak-II, DI	1.0	0.90	0.10		
	N1-II(1250kg< RW≤1700kg)	Pak-II IDI	1.25	1.0	0.12		
		Pak-II, DI	1.25	1.3	0.14		
	N1-III(RW >1700kg)	Pak-II, IDI	1.50	1.2	0.17		
		Pak-II, DI	1.50	1.6	0.20		

Parameters	Standards (maximum permissible limit)	Measuring method
	85 dB(A)	Sound-meter at 7.5 meters from the source

(b) For Heavy Duty Diesel Engine and Large Goods Vehicles (g/KWh)

Type of Vehicle	Category / Class	Tiers	CO	HC	NOx	PM	Measuring method	Applicability
1	2	3	4	5	6	7	8	9
Heavy Duty Diesel Engine	Trucks & Buses	Pak-II	4.0	1.3	7.0	0.15	ECE-R-49	All imported and locally manufactured diesel vehicles with effect from 01-07-2012
Large Goods Vehicle	N2 (3000) and up	Pak-II	4.0	1.3	7.0	0.15	EDC	

es		
Parameters	**Standards (maximum permissible limit)**	**Measuring methods**
Noise	85 dB(A)	Sound-meter at 7.5 meters from the source

EMISSION STANDARDS FOR PETROL VEHICLES (g/km)

Type of Vehicle	Category/Class	Tiers	CO	HC+ NOx	Measuring method	Applicability
1	2	3	4	5	6	7
Passenger Cars	M1: with reference mass (RW) upto 2500kg. Cars with RW over 2500kg to meet N1 category standards	Pak-II	2.20	0.5	NEDC(EC E15+EUDC L)	All imported and new models * locally manufactured petrol vehicles with effect from 01-07-2009**
Light Commercial Vehicles	N1-I(RW<1250kg)	Pak-II	2.20	0.5		
	N1-II(1250kg> RW<1700kg)	Pak-II	4.0	0.65		
	N1-III(RW>1700kg)	Pak-II	5.0	0.08		
Motor Rickshaws & Motor Cycles	2,4 strokes<150cc	Pak-II	5.5	1.5	ECER 40	
	2,4 strokes>150cc	Pak-II	5.5	1.3		

Parameters	Standards (maximum permissible limit)	Measuring method
Noise	85 dB(A)	Sound-meter at 7.5 meters from the source

Explanations:

DI: Direct Injection
IDI: Indirect Injection
EUDC: Extra Urban Driving Cycle
NEDC: New European Driving Cycle
ECE: Urban Driving Cycle
M: Vehicles designed and constructed for the carriage of passengers and comprising no more than eight seats in addition to the driver's seat
N Motor vehicles with at least four wheels designed and constructed for the carriage of goods
* New Model means both model and design type change
** The existing Model of petrol driven vehicles locally manufactured with immediately switched over to Pak-II emission standards but not later than 30th June 2012

(IQBAL MOHAMMED CHAUHAN)
Secretary, Government of the Punjab
Environment Protection Department

EXTRA ORDINARY ISSUE

REGISTERED No. L-7532

The Punjab Gazette

PUBLISHED BY AUTHORITY

LAHORE MONDAY AUGUST 15, 2016

GOVERNMENT OF THE PUNJAB
LAW AND PARLIAMENTARY AFFAIRS DEPARTMENT

NOTIFICATION
(124 of 2016)

12th August 2016.

The following Notification No. SO(G)/EPD/7-26/2013, dated 05.08.2016 regarding the Punjab Environmental Quality Standards for Drinking Water is published for general information:

DR SYED ABUL HASSAN NAJMEE
Secretary
Government of the Punjab
Law and Parliamentary Affairs
Department

Price Rs. 18.00 Per Page

Government of the Punjab
Environment Protection Department

NOTIFICATION: No. SO(G)/EPD/7-26/2013. – In exercise of the powers conferred under clause (c) of sub-section (1) of section 4 of the Punjab Environmental Protection Act, 1997 (XXXIV of 1997), the Environmental Protection Council has approved the following as the Punjab Environmental Quality Standards for Drinking Water:

Punjab Environmental Quality Standards for Drinking Water

Properties/Parameters	Standard Values	WHO Standards	Remarks
[redacted]			
All water intended for drinking (E. Coli or Thermo-tolerant Coliform bacteria)	Must not be detectable in any 100 ml sample	Must not be detectable in any 100 ml sample	Most Asian countries also follow WHO standards
Treated water entering the distribution system (E. Coli or thermo tolerant coliform and total coliform bacteria)	Must not be detectable in any 100 ml sample	Must not be detectable in any 100 ml sample	Most Asian countries also follow WHO standards
Treated water in the distribution system (E. Coli or thermo tolerant coliform and total coliform bacteria)	Must not be detectable in any 100 ml sample In case of large supplies, where sufficient samples are examined, must not be present in 95% of the samples taken throughout any 12- month period.	Must not be detectable in any 100 ml sample In case of large supplies, where sufficient samples are examined, must not be present in 95% of the samples taken throughout any 12- month period.	Most Asian countries also follow WHO standards
[redacted]			
Colour	≤15 TCU	≤15 TCU	
Taste	Non objectionable/ Acceptable	Non objectionable/ Acceptable	
Odour	Non objectionable/ Acceptable	Non objectionable/ Acceptable	
Turbidity	<5 NTU	<5 NTU	

Properties/Parameters	Standard Values	WHO Standards	Remarks
Total hardness as $CaCO_3$	< 500 mg/l	—	
TDS	<1000	< 1000	
pH	6.5 – 8.5	6.5 – 8.5	
[redacted]			
Essential Inorganic	mg/Litre	mg/Litre	
Aluminum (Al) mg/l	≤0.2	0.2	
Antimony (Sb)	≤0.005 (P)	0.02	
Arsenic (As)	≤0.05 (P)	0.01	Standard for Pakistan similar to most Asian developing countries
Barium (Ba)	0.7	0.7	
Boron (B)	0.3	0.3	
Cadmium (Cd)	0.01	0.003	Standard for Pakistan similar to most Asian developing countries
Chloride (Cl^-)	<250	250	
Chromium (Cr)	≤0.05	0.05	
Copper (Cu)	2	2	
Toxic Inorganic	mg/l	mg/l	
Cyanide (CN)	≤0.05	0.07	Standard for Pakistan similar to Asian developing countries
Fluoride (F)*	≤1.5	1.5	
Lead (Pb)	≤0.05	0.01	Standard for Pakistan similar to most Asian developing countries
Manganese (Mn)	≤ 0.5	0.5	
Mercury (Hg)	≤0.001	0.001	
Nickel (Ni)	≤0.02	0.02	
Nitrate (NO_3)*	≤50	50	
Nitrite (NO_2)*	≤3 (P)	3	
Selenium (Se)	0.01(P)	0.01	

Properties/Parameters	Standard Values	WHO Standards	Remarks
Residual chlorine	0.2-0.5 at consumer end 0.5-1.5 at source		
Zinc (Zn)	5.0	3	Standard for Pakistan similar to most Asian developing countries
Organic			
Pesticides mg/l			PSQCA No. 4639- 2004, Page No. 4 Table No. 3 Serial No. 20-58 may be consulted.**
Phenolic compounds (as Phenols) mg/l		[redacted]	
Poly-nuclear aromatic hydrocarbons (as PAHs) g/l		0.01 (By GC/MS method)	
[redacted]			
Alpha Emitters bq/L or pCi	0.1	0.1	
Beta emitters	1	1	

* Indicates priority health related inorganic constituents, which need regular monitoring.

** PSQCA: Pakistan Standards Quality Control Authority.

(IQBAL MOHAMMED CHAUHAN)
Secretary, Government of the Punjab
Environment Protection Department

Annexure-6
E & S Checklist

E & S Screening Checklist

Environmental and Social screening checklist of 42 proposed villages can be accessed through the following link

https://drive.google.com/drive/folders/1py1nOcQytPu9GyDXyWgvpn8DFgNUqBoo?usp=sharing

Annexure-7
Consultation Meetings

Consultation Meetings Tehsil-wise

Sr. No	Tehsil	Community Consultation Meeting	Number of Participants
1	Kot Momin	24	262
2	Ahmadpur Sial	16	128
3	Bhawana	15	120
4	Darya Khan	18	144
5	Pakpattan	53	424
6	Liaqatpur	65	536
7	Rojhan	11	165
8	Alipur	42	751
9	Shujabad	44	789
10	Kahror Pacca	19	152
11	Khairpur Tamewali	42	336
12	Bahawalnagar	60	480

Annexure-8
VLD Procedure

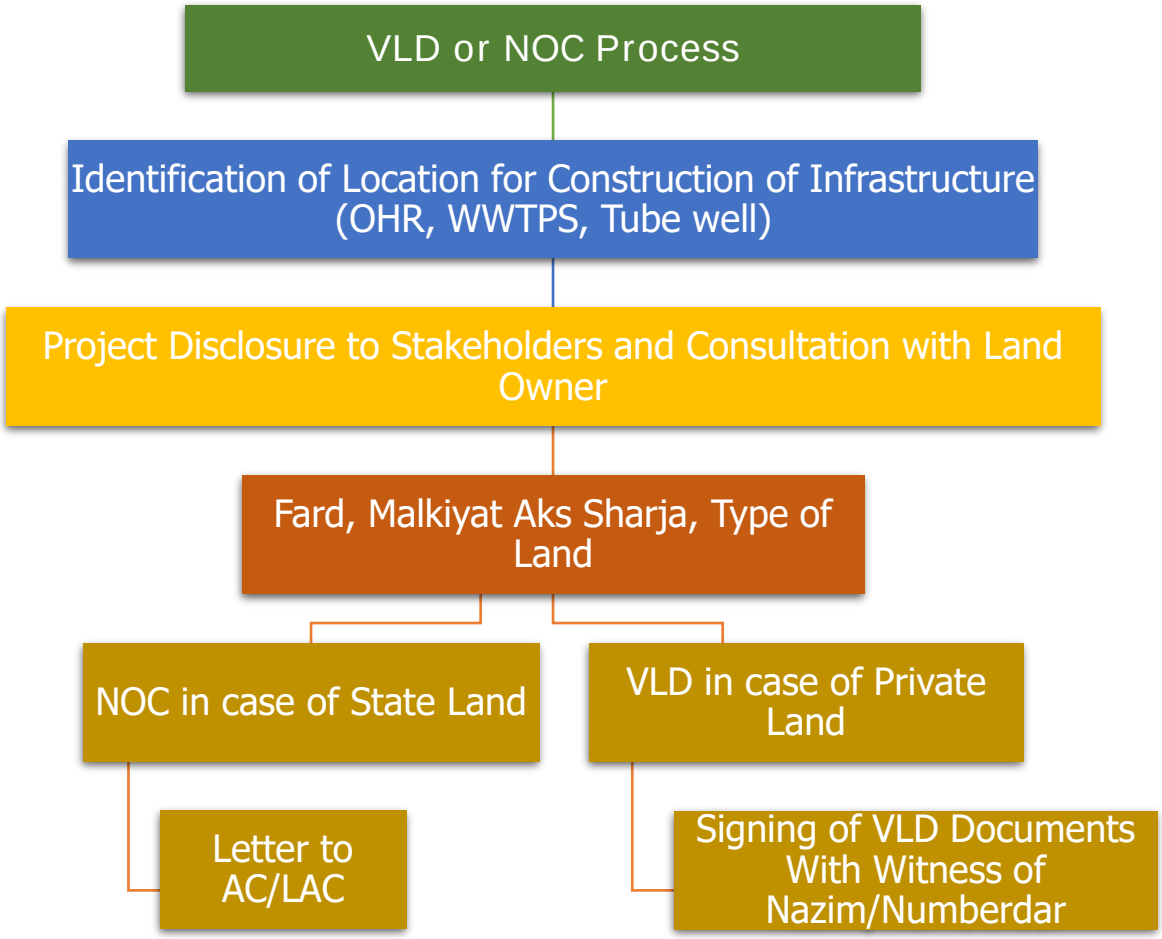

Specific conditions for the VLD procedure are provided in ESMF.

Annexure-8A
VLD Screening Checklist

Checklist of Voluntary Land Donation (VLD) Process			
Sr. No.	**Description**	**Checklist Yes=Y; No=N**	**Remarks**
A	**Requirement for Voluntary Land Donation**		
1.	The Purpose for Land Use of the Project		Land use plan (Purpose for which land is being taken)
2.	Area of land to be donated		Land donation plan
3.	Terms of land donation		Land donation agreement
4.	Parties intending to donate land		List of donor parties in the village
5.	Any details that are relevant to why donation may be appropriate		Record of reasons for land donation appropriateness
B	**Determine the appropriateness of VLD**		
6.	Has the viability of all other alternative locations/ sites been considered?		Must be Yes
7.	Is Govt. land available?		No, In case Yes, the following must be checked
8.	Verify land is free of squatters, encroachers, or other claims or encumbrances		Must be Yes
9.	Reasons for obtaining land through VLD in spite of the availability of govt. land?		Justifications/ Reasons for VLD
10.	Has the cost-benefit analysis been conducted for choosing VLD instead of Govt. land?		Cost
11.	Does the cost meet the minimum threshold required for opting for VLD instead of Govt. land?		Must be yes
12.	Ensure the landowner is not vulnerable*		Must be Yes
13.	VLD must not negatively impact households below the provincial poverty line.		Must be negligible
14.	Is the land obtained through VLD owned by a woman who is the family's sole earner?		VLD is not to be taken from the women-headed family.
15.	Does the VLD involve impacts on minority/ handicapped persons?		Must be negligible.
16.	If yes, what are the impacts on livelihood due to VLD in terms of percentage?		The percentage of impact on the livelihood must not exceed 5%.
C	**VLD Process Requirements**		

17.	The Titleholder should be holding more than the minimum prescribed land;		Minimum 2 kanals.
18.	Verify voluntary donation is not more than 10% of the area of the titleholder's holding		Must be Yes
19.	Verify impacts are minor and not requiring physical relocation of the titleholder		Must be Yes
20.	Verify land must be jointly identified by the Revenue Department/ VO or project authorities.		Must be Yes
21.	Do the project technical authorities have authorization that the land is appropriate for sub-project purposes?		Must be Yes
22.	Ensure land is appropriate for sub-project purposes and will not invite adverse social, health, environment, or safety impacts**		Must be Yes
23.	Verification of the voluntary nature of land donations must be obtained from each of the persons donating land.		Must be Yes
24.	Do the land donors/ tenants have access to and benefit from this sub-project?		If no, then describe the reasons.
D	**Verify requirements of donation and formalization of donation in the village assembly**		
25.	Verify donation is voluntary and obtain notarized, witness statements in a village assembly		Must be Yes
26.	Ensure the land donor must not possess more than 25 acres of land		The requirement must be met
27.	Ensure the land donor must not be a member of a Provincial Assembly, National Assembly, and member of the Senate		The requirement must be met
28.	Ensure titleholder understands they will have equal access to infrastructure built on donated land and cannot claim priority treatment		Must be Yes
E	**Due diligence on land ownership and use**		
29.	Type of land rights in the project area		Land rights assessment
30.	Users of land or any occupying parties (Tenants or leaseholders etc.)		Users identification
31.	Competing claims of ownership or use		Claims identification
32.	Structures and assets on the land		Assets on the proposed land (loss of agriculture, livelihood, assets, loss of economic trees etc.)

33.	Encumbrances on the land		Encumbrances assessment (Legal/ financial, Loans etc.)
F	**Consultation and Disclosure in a Village Assembly**		
34.	Consult with land donors and ensure they understand the terms and conditions of the donation		Must be Yes
35.	Disclose information about the donation process		Must be Yes
36.	Disclose any potential negative impacts on the owner		Must be Yes
37.	Informed consent of person donating land		Consent Agreement
38.	Indicate the concerns raised, if any.		Document the concerns
G	**Grievance Redress Mechanism (GRM)**		
39.	Establish and communicate the grievance redress mechanism		Must be Yes and Documented
40.	Disclosure of GRM process and GRC		Must be Yes
41.	Sharing of helpline for complaints and grievances		Must be Yes
H	**Monitoring and documentation**		
42.	Verify any land conflicts or conflicting land titling		Must be mentioned and avoided
43.	Establish informed consent of person donating land		Must be Yes and Documented
44.	Inform them they will be deprived of the title as well as any other right to use the land		Must be Yes and Documented
45.	They have the right to refuse to donate the land		Must be Yes and Documented
46.	Information about any other costs involved in the process which the owner has to pay.		Must be Yes and Documented
47.	They will be informed that neither they nor their family members will be able to get the land back after the mutation.		Must be Yes and Documented
48.	What they will need to do to donate the land;		The complete mutation process must be disclosed
49.	The intergenerational effect of the donation on their family, what they can do if they (or their family or heirs) want the land back.		Must be Yes and Documented
50.	The terms and conditions of the land donation must be mutually agreed upon and detailed in a written agreement.		Must be Yes and Documented
51.	Verify donors provide their informed consent		Must be Yes and Documented
52.	Monitor and document the donation process in monitoring reports		Must be Yes and Documented

Footnote:

* Vulnerable persons:
Households (with valid proof), as per provincial poverty line for rural areas;
Households without proof of the same and belonging to the following social categories:
Women headed households with women as sole earners;
Minority/ handicapped persons.
** adverse social, health, environmental, and safety impacts including but not limited to the potential social conflicts, community health, dust or air quality, occupational and community health, and safety respectively.

Annexure-8B
VLD Tracking Matrix

VLD Tracking Sheet of Tehsil Bhowana Phase-II

S.No	District	Tehsil	Village Name	Proposed Scheme Detail	Consultant Name	Total Land Required (Marlas)	Pvt Land requirement (Marlas)						Total number of private land donors (detail of actual land size and % of landholding to be provided for each donor)						Confirmation of Ownership & encumbrances - date	Documentation for Revenue Deptt (CNIC Khajra etc.) - date	Date of VLD documentation (Affidavits etc.)	Date of VLD cases submission to WB	Date of WB NOL	Mutation date	Remarks
							Tubewell	OHR	AHR	SW	Stand Post	Total	Donor 1 (SP)			Donor 2 (TW,OHR,AHR)								
													total landholding	donated land	%	total landholding	donated land	%							
1	District	Tehsil	Mouza Tajo Bazwala (Rehmano ka Thatha)	Stand Post	NESPAK	1					1	1	1250	1	0.08%				11-Apr-23	11-Apr-23	22-May-23	30-Jun-23			
2	District	Tehsil	Mouza Tajo Bazwala (Dispensary)	Stand Post	NESPAK	1					1	1	5000	1	0.05%				19-Apr-23	18-Apr-23	23-Apr-23	30-Jun-23			
3	District	Tehsil	Mouza Thatha Nanak	Stand Post	NESPAK	1					1	1	1440	1	0.07%				4-Apr-23	4-Apr-23	22-May-23	30-Jun-23			
4	District	Tehsil	Mouza Barkhandar	Pipe Solution	NESPAK	65	50	50	40		0	65				1500	50	7%	01-Feb-23	01-Feb-23	02-Feb-23	30-Jun-23			
			Mouza Barkhandar (Chak Nathaly)	Stand Post		1					1	1	480	1	0.21%				14-Apr-23	12-Apr-23	19-May-23	30-Jun-23			

Annexure-9
Sludge Management Plan

SLUDGE MANAGEMENT PLAN

Introduction:

An integrated sludge management plan would cover aspects across the value chain of on-site sanitation including safe collection, conveyance, treatment and disposal/reuse of the treated sludge.

Objectives of Sludge Management & Treatment

Following are the basic objectives of sludge management or treatment

- Reducing its Volume
- Stabilizing its Organic Materials
- Killing off the odor
- Ensure it can be reused
- Properly digested (Non activated)

Anaerobic Baffled Reactor (ABR)

An Anaerobic Baffled Reactor (ABR) technology will be used to treat sewerage water. ABR is an improved septic tank with a series of baffles under which the wastewater is forced to flow. This technology is easily adaptable and can be applied at the household level, in small neighborhoods or even in bigger catchment areas.

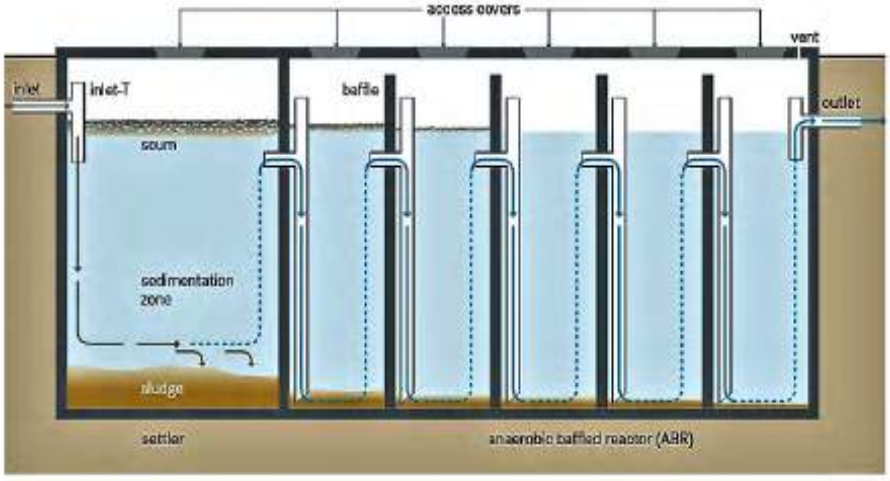

- **Sludge Production**

Sludge production is an inherent part of the operation of an anaerobic baffle reactor (ABR), as it involves the biological breakdown of organic matter by microorganisms.

During the treatment process, organic matter is converted to a residual sludge, which consists of biomass, undigested organic matter, and inorganic solids. The amount of sludge produced by an ABR will depend on several factors, including the influent characteristics, hydraulic retention time, and the operating conditions of the reactor. Generally, the longer the hydraulic retention time, the higher the sludge production will be. However, longer retention times may also lead to improved treatment efficiency. It is important to manage the sludge produced by the ABR to prevent excessive accumulation and ensure efficient operation of the system. This may include regular removal of sludge, sludge thickening, digestion, dewatering disposal and monitoring.

- **Sludge Removal from ABR**

Sludge removal from an Anaerobic Baffle Reactor (ABR) is typically required to maintain efficient operation of the system and prevent excessive accumulation of solids. The frequency of sludge removal will depend on factors such as the influent characteristics, hydraulic retention time, and the design of the ABR. In general, it is recommended that sludge should be removed from the ABR when it reaches a certain accumulation level, which can be determined by monitoring the sludge volume and concentration. A common practice is to remove the sludge volume when it reaches around 50% of the reactor volume.

- **Sludge Dewatering**

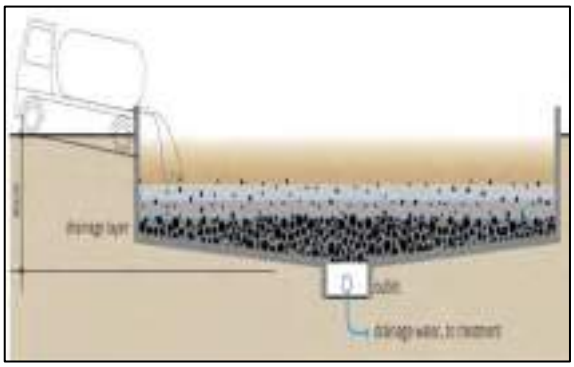

The digested sludge contains water content ranges from 70% to 95%, with an average of about 85%. This means that the sewerage sludge is relatively wet and contains a significant amount of water. But, even with that moisture content, sludge no longer behaves as a liquid and can be handled as a solid material. Sludge-drying beds provide the simplest method of dewatering. A digested sludge slurry is spread on an open bed of sand and allowed to remain until dry. Drying takes place by a combination of evaporation and gravity drainage through the sand. A piping network built under the sand collects the water, which is pumped back to the head of the plant.

After about six weeks of drying, the sludge cake, as it is called, may have a solids content of about 40 percent. It can then be removed from the sand with a pitchfork or a front-end loader. In order to reduce drying time in wet or cold weather, a glass enclosure may be built over the sand beds.

- **Sludge Disposal / Reuse**

The final destination of treated sewage sludge usually is the land. Dewatered sludge can be buried underground in a sanitary landfill. It also may be spread on agricultural land in order to make use of its value as a soil conditioner and fertilizer after the consent of Village Organization (VO).

- **Monitoring and Maintenance**

It is important to regularly monitor the sludge management process to ensure that it is operating effectively and efficiently. This includes monitoring the quality of the sludge and the effectiveness of the treatment processes.

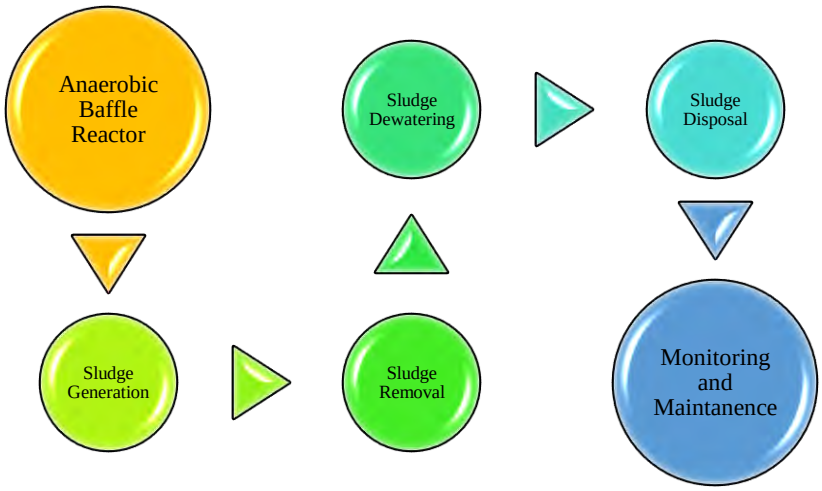

Sludge Management Plan Flowchart

Annexure-11
Grievance Redressal Committees
All three Tiers

Grievance Redressal Committee – (Tier- 1)

PUNJAB RURAL MUNICIPAL SERVICES COMPANY
(COMPANY REGISTERED WITH SECP UNDER SECTION 42 OF THE COMPANIES ACT, 2017)

PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT (PRSWSSP)

ESTABLISHMENT OF FIRST-TIER GRIEVANCES REDRESSAL COMMITTEE (GRC-I)

NOTIFICATION

NO.PRMSC/ORDERS/2022: 05

In pursuance of the Implementation of the Environment & Social Management Framework (ESMF), First Tier Grievance Redressal Committee (GRC-I) for the PRSWSSP is hereby constituted as under to address the resolution of outstanding/unsettled issues resulting from the Grievance Redressal Cell deliberation/proceedings.

1	Chairperson Village Organization	Convener
2	Vice Chairperson Village Organization	Member
3	Farmer/Worker	Member
4	Minority Member	Member
5	Youth Member	Member
6	Female Member (Focal Person Females)	Member
7	Lady Health Worker (LHW)	Member
8	BCC Officer, PRMSC	Member
9	Line Department concerned (Education, Health, Revenue etc.)	Member

This committee will be responsible to oversee the overall function of the GRM at a strategic level including monthly reviews at the village community level.

PRMSC

ASADULLAH (PAS)
CEO/PROJECT DIRECTOR
(PRMSC)

Dated Lahore, the 30th October, 2022

No. & Date Even

A copy is forwarded for information to:-

1. All DC's concerned
2. All AC's concerned
3. PA to CEO, PRMSC.
4. All Tehsil Managers, PRMSC.
5. All the remaining concerned
6. Master file

ADDRESS: 5TH FLOOR, KD PLAZA MM ALAM ROAD, LAHORE
EMAIL: info.prmsc@punjab.gov.pk | WEBSITE: www.prmsc.punjab.gov.pk | PHONE : (042) 99333608 - (042) 99333616

Grievance Redressal Committee – (Tier- 2)

PUNJAB RURAL MUNICIPAL SERVICES COMPANY
(COMPANY REGISTERED WITH SECP UNDER SECTION 42 OF THE COMPANIES ACT, 2017)

PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT (PRSWSSP)

ESTABLISHMENT OF SECOND-TIER GRIEVANCES REDRESSAL COMMITTEE (GRC-II)

NOTIFICATION

NO.PRMSC/ORDERS/2022: 04

In pursuance of the implementation of the Environment & Social Management Framework (ESMF), a Second Tier Grievance Redressal Committee (GRC-II) for the PRWSSP is hereby constituted as under to address resolution on outstanding/unsettled issues resulting from the Grievance Redressal Cell deliberation/proceedings.

1. Tehsil Manager PRMSC	Convener
2. Deputy Manager Operation PRMSC	Member
3. Deputy Manager Infrastructure PRMSC	Member
4. Research Analyst E&S Safeguards PRMSC	Member
5. BCC Officer PRMSC	Member (Focal Person)
6. Assistant Manager Water & Sewerage PRMSC	Member
7. Assistant Manager SWM PRMSC	Member
8. Chairperson VO/GRC-I of Village concerned	Member
9. Line Department concerned (Education, Health, Revenue etc.)	Member

This committee established in SDU-TO for each Tehsil, will manage GRM aspects for all sub-project locations in each tehsil including decisions to be taken, actions and monitoring of complaints resolution at the sub-project level.

PRMSC

ASADULLAH (PAS)
CEO/PROJECT DIRECTOR
(PRMSC)

Dated Lahore, the 30th October, 2022

No. & Date Even

A copy is forwarded for information to:-
1. All DC's concerned
2. All AC's concerned
3. PA to CEO, PRMSC.
4. All Tehsil Managers, PRMSC.
5. All the remaining concerned
3. Master file

ADDRESS: 5TH FLOOR, KD PLAZA MM ALAM ROAD, LAHORE
EMAIL: info.prmsc@punjab.gov.pk | WEBSITE: www.prmsc.punjab.gov.pk | PHONE: (042) 99333608 (042) 99333616

Grievance Redressal Committee – (Tier- 3)

PUNJAB RURAL MUNICIPAL SERVICES COMPANY
(COMPANY REGISTERED WITH SECP UNDER SECTION 42 OF THE COMPANIES ACT, 2017)

PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT (PRSWSSP)

ESTABLISHMENT OF A THIRD-TIER GRIEVANCES REDRESSAL COMMITTEE (GRC-III)

NOTIFICATION

NO.PRMSC/ORDERS/2022: 03

In pursuance of the implementation of the Environment & Social Management Framework (ESMF), a third Tier Grievance Redressal Committee (GRC-III) for the PRSWSSP is hereby constituted as under to address the resolution of outstanding/unsettled issues resulting from the Grievance Redressal Cell deliberation/proceedings.

1. Project Director / CEO PRMSC	Convener
2. Chief Operating Officer PRMSC	Member
3. Chief Infrastructure PRMSC	Member
4. Social & BCC Specialist PRMSC	Member (Focal Person)
5. Gender Specialist PRMSC	Member
6. Environmental Specialist	Member
7. Section Officer (Projects) LG&CD	Member
8. Chairperson VO/GRC-I of Village concerned	Member
9. Line Department concerned (Education, Health, Revenue etc.)	Member

This committee will be responsible to oversee the overall function of the GRM at a strategic level including monthly review.

PRMSC

ASADULLAH (PAS)
CEO/PROJECT DIRECTOR
(PRMSC)

Dated Lahore, the 30th October, 2022

No. & Date Even

A copy is forwarded for information to:-

1. All DC's concerned
2. All AC's concerned
3. PA to CEO, PRMSC.
4. All Tehsil Managers, PRMSC.
5. All the remaining concerned
6. Master file

ADDRESS: 5TH FLOOR, KD PLAZA MM ALAM ROAD, LAHORE
EMAIL: info.prmsc@punjab.gov.pk | WEBSITE: www.prmsc.punjab.gov.pk | PHONE: (042) 99332608 - (042) 99332616

Annexure-10
Environmental Testing Results

Environmental Monitoring

Environmental quality testing results including groundwater, surface water and air quality monitoring results of 42 proposed villages can be accessed through the following link

https://drive.google.com/file/d/1BIDeepcFfqIZbfXoWW0EAkGSzJ9A9HdQ/view?usp=sharing

Annexure-11

E&S Compliance Checklist

ENVIRONMENTAL & SOCIAL MONITORING

Project: Punjab Rural Sustainable Water Supply and Sanitation Project	Tehsil:	Phase:	Date of Visit:
Project Proposed Activities:			
E&S Category of Project: E-2 & S-3			
Instruments Developed for E&S Compliance: Environmental & Social Management Plan (ESMP) and Environmental & Social Impact Assessment (ESIA)			
Estimated Cost of E&S Instruments Implementation / Execution:			

A. Site-Specific Observations as per the approved E&S Instruments:

Sr. No.	Physical Observation at Site	Yes	No	Monitorable Indicators	Yes	No
1.	Contractors' **agreement has E**&S specific clauses and instruments are attached with agreement?			• Document Verification		
2.	E&S Items are filled by contractor in Bid?			• Document Verification		
3.	Contractor has approved C-ESMP / site specific ESMP?			• Document Verification		
4.	Relevant E&S Instruments copy is present at site?			• Document Verification		
5.	EHS SOPs for Labor / Construction Workers (Including Women Workers)-copy is present at site?			• Document Verification		
6.	First Aid Box?			• First Aid Box items / medicine is not expired?		
7.	Safety Signage?			• Visual Observation and Pictures		
8.	Construction area is cordoned off with reflective tapes?			• Visual Observation and pictures		

9.	Fire Safety Equipment?			• Fire Extinguisher is Filled? • Is there any trained worker / labor present at site who knows to handle the fire extinguisher in case of emergency?		
10.	Presence of Environmental Specialist / EHS Manager at site as per the approved E&S Instrument?			• Attendance registers to verify his presence?		
11.	**Social Specialist / Resettlement Specialist hired?**			• Attendance registers to verify his presence?		

Sr. No.	Environmental & Social Issues	Mitigation Measure	Means of Monitoring	Result Indicator	Status of Mitigation Measure be adopted		Remarks
					Yes	No	
A. Site Inspections							
1.	Noise	Use of machinery & equipment having less noise.	Visual Inspection Any complaint from the local residents				
		Well-tuned vehicles / machinery is being used					
2.	Fugitive Dust	Provision for personal protective equipment (PPEs) i.e., Mask by the labor/workers	Visual Inspection				
		Sprinkling of water	Visual Inspection to ensure water sprinkling is being implemented				
3.	Waste[8] Management	Immediately transport the accumulated construction	Visual inspection that solid waste is disposed-off at designated site				

[8] Debris and excavated material or parcel / unpacking materials related to

Sr. No.	Environmental & Social Issues	Mitigation Measure	Means of Monitoring	Result Indicator	Status of Mitigation Measure be adopted		Remarks
					Yes	No	
		waste to a site identified by the concerned MC	Any complaint from the local residents				
B. EHS Management of Labor and Worker							
4.	Health, Safety and Environmental	Labor Camp Management					
		Located away from any community.	Inspection of location of labor camp				
5.	SOPs for Labor / Workers (Including Women Workers)	Labor facilitated with potable water, Hygienic sanitary facilities and comfortable livings with heating & cooling facilities.	Visual Inspection				
		Provided with sewage treatment facility i.e., Septic Tanks & Soakage Pits[9]	Visual Inspection				
		Proper management of solid waste and garbage					
		Provided with firefighting station i.e., Fire extinguishers (DCP), Fire buckets, Spade, Fire Buzzer etc.	Visual Inspection				
		Provided with hygiene mess facility for labor.	Visual Inspection				

[9] In case of absence of sewerage / drainage system and flush toilets

Sr. No.	Environmental & Social Issues	Mitigation Measure	Means of Monitoring	Result Indicator	Status of Mitigation Measure be adopted		Remarks
					Yes	No	
		Provided with health care facilities					
		Separate rooms, toilets and health and hygiene facilities in case of women labor residents at labor camp					
		Construction Site Management					
		Adequate safety precautions (PPEs) such as helmets, safety shoes, gloves, etc. should be provided to the labor	Inspection of usage of Personal Protective Equipment during execution				
		Contractor shall provide health care facility at site i.e. First Aid Box, Ambulance etc. onsite as well as at labor campsite.	Visual Inspection				
		Children of less than 14 years of age and pregnant women are not hired.	Visual Inspection				
		Construction site safety ensured by Contractor. i.e., Safety Barricades, Safety Cones, Safety Boards etc.	Visual Inspection				
6.	Applicability of all other						

Sr. No.	Environmental & Social Issues	Mitigation Measure	Means of Monitoring	Result Indicator	Status of Mitigation Measure be adopted		Remarks
					Yes	No	
	instructions as per EHS SOPs						
C. Social Issues Management of Community							
7.	Public Consultation	Local residents will be consulted before and during execution phase regarding their views i.e., either they are satisfied with the Contractor's activities or not and grievance (if any)	Consultation with local residents / community				
8.	Vehicles Movement and Physical Obstructions	Provision of alternative routes	Visual inspection to see whether proper traffic signs, safety barriers / safety strips for traffic management are placed				
		Indicators / signboards regarding alternate routes and other instructions be provided at proper distance.					
		Display of emergency contact numbers					
9.	Infrastructure Losses i.e., loss of land, damage to structures, damage to plants etc.	Complaint from the local residents	Record of any grievance and mode of compensation provided				
		In case of any losses Contractor should					

Sr. No.	Environmental & Social Issues	Mitigation Measure	Means of Monitoring	Result Indicator	Status of Mitigation Measure be adopted		Remarks
					Yes	No	
		compensate the owner immediately					
10.	Obstruction in public access	Provision of alternate routes	Visual inspection Record of public grievance				
		Wooden blocks / ramps will be provided for safe passage of pedestrians / locals etc.	Visual inspection Record of public grievance				
11.	Privacy Issues	Workers should be trained to address privacy issues and ethically behaved.	Visual Inspection and record of grievance				
12.	Economic Losses	In case of obstruction of passage, shopkeepers / local businesses may affect, alternate routes will be provided. In case of any loss, compensation will be provided by the Contractor	Record of Public Grievance Visual Inspection				
13.	Nuisance / Disturbance to Social Sensitive Areas	No work will be conducted near the religious places during religious congregations.	Visual Inspection Issues Reported				
		Material transport to the site will be scheduled considering school timings.					

Sr. No.	Environmental & Social Issues	Mitigation Measure	Means of Monitoring	Result Indicator	Status of Mitigation Measure be adopted		Remarks
					Yes	No	
		Implement all measures suggested elsewhere in this report – dust and noise control, public safety, traffic management, strictly at the sites.					
14.	Influx of Labor	Labor camp(s) will be established away from residential population.	Visual Inspection Hiring Protocols Issues Reported				
		Preference will be given to the local people to work with contractor, and contractor should hire maximum labor force from the project area because this will reduce the labor influx.					
		Construction work will be completed within the stipulated time to move workers to next location.					
		Labor force will be shuffled with the time.					
		Contractor shall provide health care facility at site i.e. PPEs, First Aid Box, Ambulance etc. onsite as well as at labor campsite.					

Sr. No.	Environmental & Social Issues	Mitigation Measure	Means of Monitoring	Result Indicator	Status of Mitigation Measure be adopted		Remarks
					Yes	No	
		Prohibiting drugs, alcohol, weapons, and ammunition on the worksite among personnel.					
		Develop and enforce a strict code of conduct for workers to regulate behavior in the local communities.					
		Labor facilitated with potable water, Hygienic sanitary facilities and comfortable livings with heating & cooling facilities.					
15.	Gender Based Violence (GBV)	Workers will not be allowed to crowd in the residential communities within the site.	Visual Inspection Any Complaint from women. Reported Issues				
		Alternative routes for pedestrian will be provided to avoid mixing of women with workers.					
		The Contractor will make sure that no discrimination is made on the basis of gender in case of hiring of workers.					

Sr. No.	Environmental & Social Issues	Mitigation Measure	Means of Monitoring	Result Indicator	Status of Mitigation Measure be adopted		Remarks
					Yes	No	
		Contractor will take proper measures to address and resolve issues relating to harassment, intimidation, and exploitation, especially in relation to women.					
16.	Social / Cultural Conflicts	Local labor will preferably be employed for construction works.	Visual Inspection Record of public grievance				
		Careful planning and training of workforce to minimize disturbance to the local people.					
D. COVID-19 Related SOPs of Government of Punjab at Construction Sites[10]							
17.	Covid-19 SOPs Implementation	Usage of surgical face mask by workers	Visual Inspection				
		Keep social distancing / avoid gatherings of workers	Visual Inspection				
		Provision of hand washing facility onsite for workers	Visual Inspection				
18.	Any other Issue?						

[10] Will be applicable during the pandemic

Monitored by:	Monitored by:
Name:	Name:
Designation:	Designation:
Date:	Date:
Signature:	Signature:

ENVIRONMENTAL AND SOCIAL MANAGEMENT PLAN

Phase 1– 232 Villages

Punjab Rural Sustainable Water Supply and Sanitation Project (PRSWSSP)

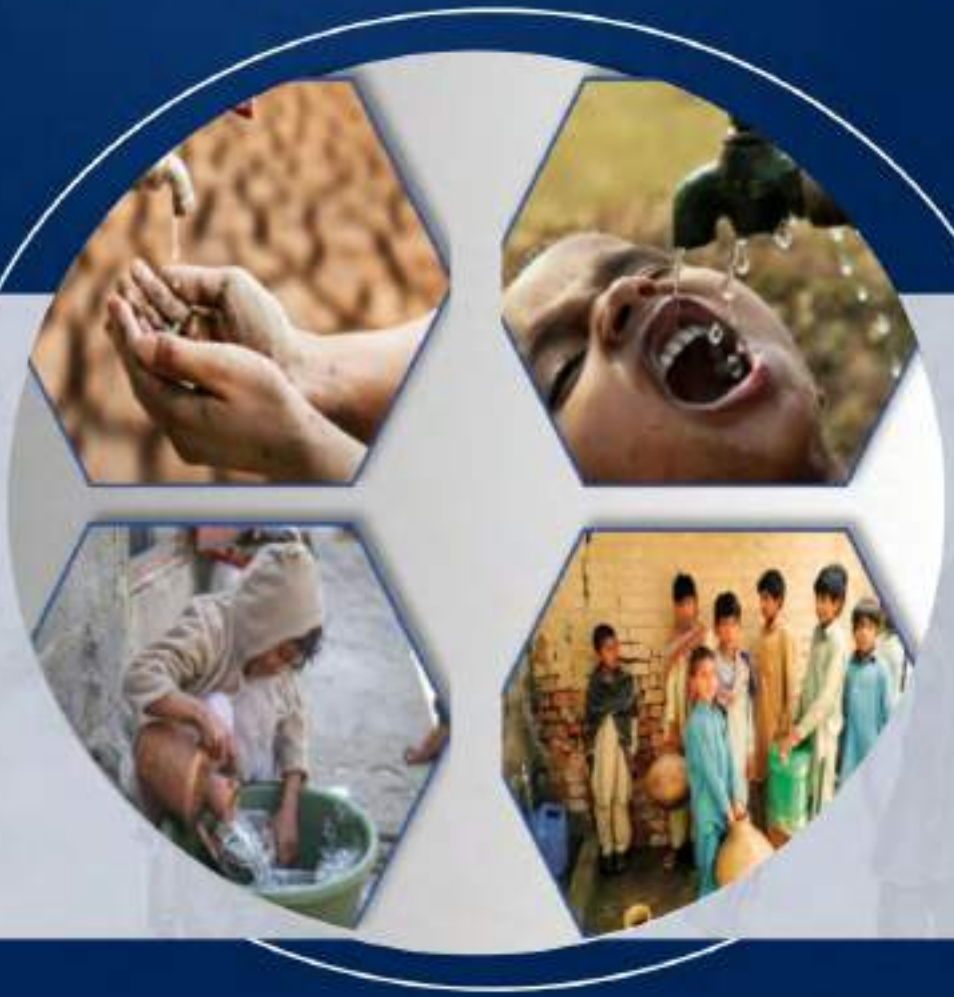

Punjab Rural Municipal Services Company
Local Government and Community Development Department ,
Government of Punjab

THE WORLD BANK

TABLE OF CONTENTS

Page No.

Contents

TABLE OF CONTENTS i

LIST OF FIGURES v

LIST OF TABLES vi

LIST OF ABBREVIATION vii

EXECUTIVE SUMMARY xii

1 INTRODUCTION 1-1

1.1 General 1-1
1.2 Project Background 1-2
1.3 Objective of ESMP 1-9
1.4 Scope of ESMP 1-10
1.5 Contractual Requirements/ Obligations of ESMP 1-10
1.6 Approach & Methodology to Work 1-11
1.6.1 Approach 1-11
1.6.2 Methodology 1-11
1.7 Structure of ESMP 1-14

2 LEGAL AND ADMINISTRATION FRAMEWORK 2-1

2.1 General 2-1
2.2 Summary of Key National Strategies, Policies, Acts and Legislation 2-1
2.3 Key Provincial Strategies / Policies, Legislation / Acts, Laws and Regulations 2-5
2.4 Applicable World Bank Policies 2-12
2.1.1 World Bank Operational Policies 2-12
2.5 Managing the Risks of Adverse Impacts on Communities from Temporary Project Induced Labor Influx 2-12
2.6 Environmental, Health & Safety Guidelines 2-13
2.7 International Labour Organization (ILO) Fundamental Conventions – Ratified by Pakistan 2-13
2.8 International Protocol/Conventions 2-13
2.9 Institution Responsible for Planning, Policies and Regulations 2-14
2.9.1 Environmental Protection Agency, Punjab 2-14

3 PROJECT DESCRIPTION 3-1

3.1 Need and Purpose of Project 3-3
3.2 Project Location 3-4
3.3 Objectives of Project 3-4
3.4 Project Description 3-5

3.4.1 Existing System 3-5
3.4.2 Proposed System 3-5
3.5 Land Acquisition 3-14
3.6 Project Administrative Jurisdiction 3-21
3.7 Project Implementation Schedule 3-21
3.8 Construction Activities and Required Machinery 3-21
3.9 Construction Camps 3-22
3.10 Construction Materials 3-22
3.11 Workforce Requirement 3-23
3.12 Solid Waste Generation 3-23
3.13 Water requirement 3-23
3.14 Wastewater Generation during Construction Phase 3-23

4 BASELINE PROFILE 4-1

4.1 General 4-1
4.2 Delineation of Study Area / Area of Influence (AoI) 4-1
4.3 Physical Environment 4-1
4.3.1 Topography 4-1
4.3.2 Geology 4-2
4.3.3 Climate and Meteorology 4-2
4.3.4 Water Resources 4-3
4.3.5 Environmental Monitoring, Sampling and Testing 4-4
4.1.1 Seismology 4-8
4.4 Sensitive Receptors 4-8
4.5 Biological Environment 4-16
4.5.1 Flora 4-16
4.5.2 Fauna 4-17
4.5.3 Endangered Species 4-18
4.1.2 Legally Protected Areas 4-18
4.6 Socioeconomic Profile 4-19
4.6.1 Population Size 4-19
4.6.2 Findings of Socioeconomic Survey 4-29
4.6.3 Results of Gender Situation Survey 4-36

5 PUBLIC CONSULTATION 5-0

5.1 General 5-0
5.2 Objectives and Principles of Consultation 5-0
5.3 Consultation and Participation Process 5-0
5.4 Identification of Stakeholders 5-1
5.5 Information Dissemination 5-1
5.6 Methods of Public Consultation 5-1
5.7 Approach Adopted for the Consultation 5-2
5.8 Stakeholders Concerns towards the Project 5-2
5.8.1 Concerns and Issues 5-2
5.9 Consultations with Female Community Members 5-3

5.10 Consultation with Institutional Stakeholders 5-4
5.11 Consultation with NGO 5-7
5.12 Pressing Needs of the Consulted Villages Suggested by Local People 5-7
5.13 Disclosure of ESMP 5-7

6 ANTICIPATED ENVIRONMENTAL IMPACTS & MITIGATION MEASURES 6-1

6.1 General 6-1
6.2 Scoping of Impacts 6-1
6.3 Methodology 6-1
6.3.1 Screening Checklist 6-1
6.3.2 Notion of Significance 6-2
6.3.3 Study Area/ Area of Influence 6-2
6.4 Environmental & Social Considerations (E&S) in Project Design 6-2
6.5 Anticipated Impacts during Pre-Construction/Design Phase 6-3
6.5.1 Layout Planning & Design 6-3
6.5.2 Soil Instability 6-3
6.5.3 Impacts of Drains construction 6-4
6.5.4 Environmentally Responsive Design Considerations 6-4
6.5.5 Groundwater 6-5
6.5.6 Surface Water 6-5
6.5.7 Seismic & Other Hazard 6-6
6.5.8 Damage to Existing Infrastructure 6-7
6.5.9 Physical Cultural Resources 6-7
6.5.10 Fire Fighting System 6-7
6.5.11 Land Acquisition 6-8
6.6 Anticipated Impacts during Construction Phase 6-9
6.6.1 Topography 6-9
6.6.2 Soil Erosion 6-9
6.6.3 Soil Contamination 6-10
6.6.4 Trench Failure 6-10
6.6.5 Construction Camps/Camp Sites 6-10
6.6.6 Water Quality 6-11
6.6.7 Air Quality 6-12
6.6.8 Noise 6-13
6.6.9 Municipal and Construction Waste/ Wastewater 6-13
6.6.10 Chance of Finding Artifacts 6-14
6.6.11 Resource Conservation 6-14
6.6.12 Biodiversity Conservation 6-14
6.6.13 Health and Safety 6-15
6.6.14 Traffic Management 6-17
6.6.15 Nuisance/ Disturbance to Sensitive Receptors (Educational, Health and Religious Places) 6-17
6.6.16 Accessibility 6-18
6.6.17 Gender-Based Violence (GBV) 6-18
6.6.18 Influx of Labor 6-19
6.6.19 Social/ Cultural Conflicts 6-20

6.6.20 Child Labor *6-21*
6.6.21 Economic Activity *6-21*
6.7 Anticipated Impacts during Operational Phase 6-21
6.7.1 Soil *6-21*
6.7.2 Air Quality *6-22*
6.7.3 Odour *6-22*
6.7.4 Elite Capture *6-22*
6.7.5 Social Inclusion *6-23*
6.7.6 End Water User of Treated Wastewater *6-24*
6.7.7 Solid Waste *6-24*
6.7.8 Sludge *6-25*
6.7.9 Impact of Brine Disposal *6-25*
6.8 Positive Impacts 6-26
6.8.1 Improved Water Supply System *6-26*
6.8.2 Improved Sewerage System *6-26*
6.8.3 Improvement in Public Health, Hygiene and Sanitation *6-26*
6.8.4 Landscape *6-26*
6.8.5 Commulative Impacts of Water Extraction & Sewerage Treatment *6-27*
6.8.6 Other Positive Impacts *6-27*
6.9 Operational Sustainability 6-28
6.10 Induced Impacts 6-28

7 ENVIRONMENTAL & SOCIAL MANAGEMENT & MONITORING PLAN 7-0

7.1 General 7-0
7.2 Implementation of Environmental & Social Management Plan (ESMP) 7-0
7.2.1 Roles and Responsibilities of the Functionaries involved in ESMP Implementation *7-1*
7.2.2 Institutional Arrangement for Implementation of ESMP by PRMSC during O&M Phase *7-2*
7.3 Reporting 7-3
7.4 Non-Compliance with the ESMP 7-3
7.5 Contractors ESMP 7-3
7.6 Inclusion of ESMP in Bidding/ Contract Documents 7-4
7.7 Environmental and Social Monitoring Plan 7-4
7.8 Grievance Redressal Mechanism (GRM) 7-36
7.8.1 Objectives *7-36*
7.8.2 Disclosure of GRM *7-36*
7.8.3 Records and Monitoring *7-37*
7.8.4 Proposed Institutional Mechanisms *7-37*
7.8.5 GRM Process Implementation *7-38*
7.8.6 Mode of Complaint *7-38*
7.8.7 GRM Procedures and Timelines *7-39*

8 ESMP Budget 8-1

8.1 ESMP Cost 8-1
8.2 Budget Estimate for PPE During the Construction Phases 8-1
8.3 Break Up of Health Safety & Environment 8-3

8.4 Environmental Monitoring Cost 8-5
8.5 Training Program 8-6
8.6 Institutional Capacity & Strengthening 8-7
8.7 ESMP Cost of Village 8-8

LIST OF FIGURES

	Page No.
Figure 1: Illustrating Project Intervention in Component 1 Sub Component 1.2	3-1
Figure 2: Illustrating Project Inventions in Component 1 Sub Component 1.1	3-1
Figure 3: Location Map of Project Area	3-4
Figure 4: Process Flow Diagram of STP / WWTP / ABR	3-14
Figure 5: Hydrology Map of Punjab Province	4-1
Figure 6: Seismic Zone Map of Project Area	4-8
Figure 7: Wildlife Sanctuaries and Game Reserves	4-19
Figure 8: Occupational Status of the Respondents	4-29
Figure 9: Occupational Status of the Respondents	4-30
Figure 10: Monthly Income of the Respondents	4-31
Figure 11: Source of Drinking Water	4-31
Figure 12: Satisfaction with household water quality	4-32
Figure 13: Type of Sewerage System	4-32
Figure 14: Type of Sanitation Facility	4-33
Figure 15: Type of Solid Waste Facility	4-33
Figure 16: Type of Construction of House	4-34
Figure 17: Organizational Setup for implementation of ESMP	7-0

LIST OF TABLES

Page No.

Table 1 : Project Area with Number of Villages 1-2
Table 2: Location and Name of Phase-1 Villages in Different Tehsils 1-3
Table 3: Key National Strategies / Policies, Legislation / Acts, Laws and Regulations and Their Relevance to the Project 2-2
Table 4: Key Provincial Strategies / Policies, Legislation / Acts, Laws and Regulations and Their Relevance to the Project 2-6
Table 5:International Agreements/Conventions Relevant to the Project 2-14
Table 6: Summary of Proposed Water Supply and Sewerage Components 3-5
Table 7: Manhole Spacing 3-12
Table 8: Manhole Diameter 3-12
Table 9: Land Requirement Details 3-14
Table 10: List of expected Machinery/Equipment 3-22
Table 11: Topographic Variations 4-2
Table 12: Temperature Variation in Summer and Winter Season 4-2
Table 13: Average Wind Speed and Windiest Month in Tehsils 4-3
Table 14: Surface Water Bodies in Targeted Villages of Relevant Tehsils 4-2
Table 15: Groundwater Analysis 4-3
Table 16: Ambient Air Quality Results 4-4
Table 17: Noise Monitoring Results 4-5
Table 18: Results of Wastewater 4-6
Table 19: Sensitive Receptors 4-8
Table 20: Primary Data Results of Project Area 4-19
Table 21: Findings of the Consultation Meetings 5-2
Table 22: Findings of the Female Consultation Meetings 5-3
Table 23:Concerns of Relevant Government Departments 5-4
Table 24: Distribution of Periodic Reports 7-3
Table 25: Environmental and Social Management Plan (ESMP) 7-5
Table 26: Village-wise ESMP Cost 8-1
Table 27: Budget Estimate for HSE During the Construction Phase 8-2
Table 28:Break Up of Personal Protective Equipment 8-3
Table 29: Environmental Monitoring Cost 8-5
Table 30: Training For Contractors by PRMSC and EDCS consultants 8-6
Table 31: HSE Supervision 8-8
Table 32: ESMP Implementation Cost - Village Wise 8-9

LIST OF ABBREVIATION

ABR	Anaerobic Baffled Reactor
AoI	Area of influence
BDL	Below detection limit
BHU	Basic Health Unit
BMPs	Best Management Practices
BOD	Biochemical Oxygen Demand
BOQs	Bills of Quantities
BPs	Bank Procedures
CBD	Convention on the Biological Diversity
CBO	Community Based Organization
CC	Construction Contractor
CFT	Cubic foot
CO	Carbon Mono Oxide
COD	Chemical Oxygen Demand
DC	Design Consultant
DC	Design Consultant
DG	Directorate General
EA	Environmental Assessment
ECO	Economic Cooperation Organization
ECO	Economic Cooperation Organization
EDCS	Engineering, Design & Supervision Consultancy Services
EE	Environmental Engineer
EHS	Environmental, Health & Safety
EIA	Environmental Impact Assessment

ENE	East-Northeast
EPA	Environmental Protection Agency
EPD	Environmental Protection Department
ERPs	Emergency Response Procedures
ESC	Environmental and Social Cell
ESMF	Environmental Social & Management Framework
ESMP	Environment and Social Management Plan
ESS	Environmental & Social Safeguard
GAP	Gender Action Plan
GBV	Gender Based Violence
GHG	Greenhouse Gas
GIIP	Good International Industry Practice
GPD	Gallons per Day
GRC	Grievance Redressal Committee
GRM	Grievance Redress Mechanisms
HDPE	High Density Polyethylene
HHs	Households
HSE	Health, Safety & Environment
IEE	Initial Environmental Examination
LG	Local Government
LPG	Liquefied Petroleum Gas
MGD	Million Gallon per Day
MS	Medical Superintend
MSDS	Material Safety Data Sheets
NCS	National Conservation Strategy
NE	North East

NESPAK	National Engineering Services Pakistan
NGOs	Non-Governmental Organizations
NNE	North-Northeast
NNW	North-Northwest
NO	Nitrogen Oxide
NO2	Nitrogen Di Oxide
NOC	No Objection Certificate
NTU	Nephelometeric Turbidity Unit
NW	North west
O&M	Operational and Maintenance
O3	Ozone
OHS	Occupational Health & Safety
OHWT	Overhead water Tank
OIC	Organization of the Islamic Conference
OP	Operational Policy
PATs	Pakistan Approaches to Total Sanitation
PCC	Public Complaints Center
PD	Project Director
PDWP	Provincial Development working party
PEPA	Punjab Environmental Protection Agency
PEQS	Punjab Environmental Quality Standards
PGA	Peak Ground Acceleration
PGA	Peak Ground Acceleration
PICs	Public Information Centers
PIMU	Project Implementation and monitoring unit
PIU	Programme implementation unit

PKR	Pakistan Rupees
PLGA	Punjab Local Government (Amendment)
PM	Particulate Matter
PPE	Personal Protective Equipment
PRMSC	Punjab Rural Municipal Services Company
PRSWSSP	Punjab Rural Sustainable Water Supply and Sanitation Project
PWA	Punjab Water Act
RCC	Reinforced Cement Concrete
ROW	Right of Way
SAARC	South Asian Association for Regional Cooperation
SBC	Seismic Building Code
SC	Supervision Consultant
SDS	Social Development Specialist
SDU	Service Delivery Unit
SEA	Sexual Exploitation and abuse
SH	Sexual Harassment
SO2	Sulfur Di Oxide
SOP	Standard Operating Procedures
SPM	Suspended particulate Matter
STDs	Sexually Transmitted Diseases
STI	Sexually Transmitted Infections
STP	Sewage Treatment Plant
SWM	Solid Waste Management
TC	Total Coliforms
TCU	True Color Unit
TDS	Total Dissolve Solids

THQ	Tehsil Head quarter
TOR	Terms of Reference
TPV	Third Party Verification
TSS	Total Suspended Solid
UNCCD	United Nation Convention to Combat Desertification
UNESCO	United Nation Educational Scientific and Cultural Organization
UNFCCC	United Nations Framework Convention on Climate Change
UNO	United Nations Organization
WASH	Water, Sanitation and Hygiene
WB	World Bank
WBG	World Bank Guideline
WHO	World Health Organization
WNW	West-Northwest
WWTP	Wastewater Treatment Plant

EXECUTIVE SUMMARY

1. Introduction

The Local Government & Community Development Department (LG&CDD), Government of Punjab, through its Punjab Rural Municipal Services Company (PRMSC), a company registered under section 42 of "The Companies Act 2017", is implementing Punjab Rural Sustainable Water Supply and Sanitation Project (PRSWSSP)" in target area of 2000 villages in 16 tehsils of Punjab province; with the financial assistance of the World Bank. The current document is the consolidated "Environmental and Social Management Plan (ESMP)" prepared in line with World Bank Safeguard Policies; and as per guidance provided in the project's Environmental Social & Management Framework (ESMF)".

Pilot Phase:

To implement this project, the Executive Committee of the National Economic Council (ECNEC) considered the summary dated 27th January, 2022 submitted by the Ministry of Planning, Development and Special Initiatives titled "Punjab Rural Sustainable Water Supply and Sanitation Project (PRSWSSP) and approved the proposal with the following directions:

i. A "Pilot Project" should be conducted, based on 10% of the approved project scope.

ii. After one year, lessons learned from the pilot phase should be shared with the Central Development Working Party (CDWP), with a specific focus on the operation and maintenance aspects of the project.

iii. The project timeline should be reduced to five years after gaining insights from the pilot phase.

To initiate the Project, an initial pilot phase was undertaken in 200 villages (Annex-1) to assess its feasibility and long-term sustainability. For this purpose, the 16 tehsils were organized into six geographical clusters, and the feasibility studies, engineering designs, PC-I documents, BOQs, and safeguard instruments for all 200 villages were completed across five implementation packages.

Summary of ESMP Prepared

Sr.No.	ESMP Phases	No. of Villages	Date of Approval
1.	Phase-1	26	18th May, 2023
2.	Phase-2	42	27th July, 2023
3.	Phase-3, 4 and 5	132	29th Nov, 2023

Lessons learnt during Pilot Phase and Recommendations for Next Phase

It was observed that the Environmental, Social and Biological baselines, were not properly established in the EIAs and ESMPs. EIAs and ESMPs where not comprehensive enough and documents were lagging in Traffic Management plan (Mobility Plan), Social Impact Assessment and Mitigation Plan, Stakeholder Engagement plan (SEP), Labor Management Plan, Labor Code of Conduct, GBV Plan and Gender action plans and its linkage with project

PDOs, man hours for E&S Safeguards related staff in EDCS consultants TORs were found to be not sufficient, which resulted in delayed approvals of E&S instruments.

The EDCS consultants were advised during the negotiations and bid meetings to establish the baselines through physical visits, rather than through online data and surveys available. E&S instrument must be comprehensive enough. 5% of E&S payment will be released after the approval of ESMPs from bank and EIAs from EPD. Consultants are responsible for FGDs, Stakeholder engagements and conducting public hearing sessions for the ESMP and EIAs.

It was decided that payment of HSE Expert, Social Expert, Gender Expert and inspector should be linked with HSE/PPE compliance in the field. Consultant should also promote PPE/HSE culture for their staff and enforce the same for contractor staff. The man-hours allocated to Environmental and Social (E&S) safeguards should be increased to ensure effective implementation, monitoring, and compliance with World Bank requirements.

During the implementation phase, it was observed that contractors were reluctant to prepare Contractor's ESMPs (C-ESMPs) and to deploy dedicated Health, Safety, and Environment (HSE) staff at construction sites, primarily due to the associated costs and negligence by EDCS consultants in timely compliance of E&S Safeguards as "the engineers/project managers". These costs were not explicitly included in the ESMP budget of pilot phase. To address these issues, the PRMSC Environmental and Social (E&S) Wing incorporated the cost of preparation of C-ESMPs and the hiring of HSE staff as mandatory and clearly defined line items within the ESMP budget approved for remaining 1800 villages.

Furthermore, the ESMP budget was initially a biddable item, which led contractors to quote the lower amounts to remain competitive to win the bid. As a result, contractors were reluctant to implement ESMP requirements or had to absorb these costs independently. To mitigate this risk, PRMSC, with the approval of the World Bank, revised the approach and made the ESMP budget a fixed, non-competitive item to be made part of the bid as provisional sum.

In addition, certain essential environmental and social mitigation measures—such as tree plantation, barricading tapes, and reflective safety jackets—were not included in the original budget. These items have now been incorporated into the revised ESMP budget to ensure comprehensive and effective implementation.

Moreover, the E&S wing of PRMSC recommends linking the contractor's Interim Payment Certificate (IPC) to compliance performance reflected in the E&S dashboard. Under this approach, the Tehsil Office should forward the IPC only when the contractor achieves an E&S compliance score exceeding 80%.

Remaining Scope of 1800 Villages:

Building on the lessons learned from the pilot phase of 200 villages, the CDWP granted approval on 12 December 2024 for PRMSC to proceed with the remaining scope of 1,800 villages. To initiate the preparation of feasibility studies, detailed engineering designs, PC-I documents, and safeguard instruments, PRMSC has reorganized the 16 tehsils into five geographical clusters and engaged five Engineering Design and Supervision Consultants (EDSCs) under the assignment titled "Consultancy Services for Engineering Design and Construction Supervision of Punjab Rural Sustainable Water Supply & Sanitation Project (PRSWSSP)."

Phase-0 (77 villages)

An ESMP of Phase-0 containing 77 villages was submitted on 1st December, 2025 and the E&S team of the World Bank granted no objection via email on 13th January, 2026. Email enclosed as **Annexure-1**.

Phase-1 (232 Villages)

Under Phase-1, covering an initial batch of 232 villages. To expedite implementation, the EDSCs have been instructed to submit feasibility studies, detailed engineering designs, PC-I documents, and environmental and social safeguard instruments on a phased basis.

Background

The Project Development Objective (PDO) of PRSWSSP is to provide equitable and sustainable access to safely managed water and sanitation services and to contribute to the reduction of child stunting. This objective will be achieved through improved sanitation systems, provision of clean drinking water, enhanced solid waste management, behavior change interventions, and capacity-building initiatives across rural settlements of Punjab.

For project implementation, the Punjab Rural Municipal Services Company (PRMSC) has divided the 16 tehsils into five clusters based on geographical proximity and has engaged five Engineering Design and Supervision Consultants (EDSCs), one for each cluster. The consultancy assignment, titled “Consultancy Services for Engineering Design and Construction Supervision of Punjab Rural Sustainable Water Supply & Sanitation Project (PRSWSSP),” requires the consultants to:

(i) prepare design documentation—including Sub-scheme/Project Documents (PC-I) and Bills of Quantities—for water supply and sanitation schemes to ensure economies of scale and effective outcomes; and

(ii) provide resident supervision during infrastructure development.

This Environmental and Social Management Plan (ESMP) addresses the potential impacts associated with the design, construction, and operation of water supply and sewerage facilities. A consolidated ESMP for Phase-1, covering 232 villages, has been prepared and is currently under review for approval by the Provincial Development Working Party (PDWP).

The anticipated environmental and social impacts for these 232 villages are largely localized, site-specific, and temporary in nature. Few, if any, impacts are irreversible, and all can be effectively mitigated through appropriate measures. Based on the Environmental and Social Screening and in accordance with the Environmental and Social Management Framework (ESMF) and Operational Policies (OPs), the project is classified as Category E2, necessitating the preparation and implementation of an ESMP. scope covered in this ESMP is provided below:

Cluster	Name of Consultant	Tehsil	Phase-1
North	NESPAK	Noorpur Thal	26
South-I	Alter	Liaqatpur	90
		Rojhan	12
South-III	Asian Consultants	Bahawalnagar	19
Central		Pakpattan	20

Cluster	Name of Consultant	Tehsil	Phase-1
South-II	Rehman Habib Consultants	Alipur	21
		Shujabad	10
		Taunsa	34
Total			**232**

2. Policy, Legal and Administrative Framework

The national and provincial Government has promulgated laws/acts, regulations, and standards for the protection, conservation, rehabilitation, and improvement of the environment. The Punjab Environmental Protection Agency (PEPA) is the regulatory authority, which has provided guidelines for conducting Environmental Impact Assessment (EIA) studies and has the authority to issue regulatory clearance/ No Objection Certificates (NOCs) for various projects.

In addition to the laws of the land (Punjab Environmental Protection Act 1997, Review of IEE/EIA Act 2000), World Bank Operational Policies (OPs) are also applicable to the project including Environmental Assessment (OP 4.01), Natural Habitat (OP 4.04), Physical Cultural Resources (OP 4.11), Resettlement and Projects on International Waterways OP/BP 7.50.

3. Project Description

The villages selected for this subproject will be provided with Water Sanitation and Hygiene (WASH) facilities. The subproject involves provision of water supply, sewerage, overhead tanks & Pumping stations with sewage treatment.

The water supply system is planned based on groundwater quality and village size. In areas with adequate underground sweet water and a relatively large number of houses, a complete water supply scheme will be provided, including a tube well, OHR, and transmission network as per demand. In smaller villages where sweet water pockets are limited, water supply will be provided through standposts. In areas where groundwater is brackish, RO plants will be installed to ensure safe drinking water.

The sewerage system is planned with multiple service options based on housing density, groundwater table depth, and local topography. In areas with a higher number of houses and where the groundwater table is not shallow, a conventional sewerage system will be provided, along with an ABR for treatment of wastewater prior to discharge. In areas with fewer houses, narrow streets, and shallow groundwater conditions, open drains will be provided to improve sanitation.

A hybrid system is introduced in which sewers are laid along main roads, while secondary drains from narrow streets discharge into these sewers. This approach is based on lessons learned from the pilot phase, where excavation in narrow streets caused damage to adjacent house walls. In low-density areas, communal septic tanks are proposed for wastewater treatment, with final discharge to nearby drains, watercourses, or ponds; where groundwater is deep, communal soakage pits will also be provided.

The estimated total cost of the project for the proposed 232 villages of Phase-1 is **15,062 million PKR or 53.79 million US$**[1]. Total man power required on site for proposed Project will be approximately 08-30 workers per day per village in construction phase.

[1] 01 USD = 281.55 PKR

Excavators and road cutters are used for trench excavation and cutting of existing pavements during water supply and sewerage works. Dumpers and concrete mixer machines support material handling and preparation of concrete for manholes and thrust blocks. Plate compactors ensure proper backfilling, while generators provide continuous power for site operations. Details of equipment are provided in Section 03 of consolidated ESMP.

PRMSC has divided the 16 tehsils into 5 zones based on geographical location and accordingly hired the services of 5 Engineering Design and Supervisory Consultants (EDCS) for the proposed project. Under Phase-1, interventions are planned across 08 tehsils, within which 232 villages have been identified for implementation. In order to fast track the project implementation and execution of the civil works, PRMSC with the help of consultants has divided 1800 pilot villages from sixteen different tehsils into 5 packages for designing and provision of Water Sanitation and Hygiene (WASH) facilities. This document pertains to 232 villages selected in phase-1 from 08 different tehsils. The subproject involves provision of water supply, sewerage, overhead tanks and Pumping stations with sewage treatment plants in all 232 villages.

Water Supply Issues:

- No water supply network in the villages;
- Most of the household use shallow groundwater;
- Shallow ground water is not fit for drinking;
- Polluted drinking water is causing water borne diseases.

Sewerage Issues:

- Properly designed sewerage system does not exist in most of the villages;
- Existing open drains are damaged and do not cover the entire settlements;
- No proper disposal Point in all the villages;
- Sewage collected in soakage pits and open plots seeps into ground and contaminates groundwater;
- Raw sewage ponds are a breeding ground for disease vectors.

Solid waste Issues:

- There is no proper solid waste management system and designated dumping sites in the project area, locals usually throw their waste into open plots or streets.
- There are heaps of waste which attract rodents, flies and disease vectors.
- Organic waste is usually burnt by the villagers, which causes health issues.
- Open drains are used as a garbage/solid waste disposal point thus resulting in decrease of water carrying capacity of these drains.
- During rain, storm water and sewage overflow from the drains and spread solid waste through the area thus causing nuisance, environmental issues and spread of diseases.
- The laying of piping network for water supply and sewerage system will not require land acquisition, as the pipeline will be buried underground. The network will be

designed in a manner that the pipeline is laid along the public roads / streets. However, if pipeline route is required to pass through any private lands, special permission for laying and periodic maintenance shall be sought from the landowners. The land required for the construction of overhead tank, pumping station and STP will consist of state land, acquired through process of No Objection Certificate (NOC). In cases where private land is needed, it shall be obtained through Voluntarily Land Donation (VLD).

- However, land through VLD is only obtained after satisfying the set criteria: first, that the state land is not available in the proposed village; second, when state land in the village is not technically viable – based on requirements of engineering design – for the construction of infrastructure; third, only after meeting the VLD Screening Checklist criteria attached as **Annexure-9.**

4. Baseline Profile

As per the environmental screening study conducted earlier, the project falls in “Category E2” which means that the impacts of the project activities are limited and within the boundary of project area. Therefore, the whole village has been considered Area of Influence (AoI).

A. Physical Environment

The proposed project sites are rural settlements comprising residential and agriculture areas. The topography of the project area is predominantly flat. The ground elevations vary from 285 ft to 659 ft in proposed villages.

Punjab’s area mostly consists of an alluvial plain formed by the southward-flowing Indus River and its four major tributaries. The general slope of the land is from northeast to southwest, but it rises in the areas between rivers Approximately 70 percent land area of the province comprises flood plans of Indus basin. Geologically, lands in the flood plains are lightly mantled with alluvial deposits transported from the Himalaya foothills. The underlying bedrock is composed of Precambrian metamorphic and tertiary consolidated rocks. The overlying alluvium consists of Pleistocene to recent unconsolidated deposits of sand, clay and silt. The formation age of the alluvium also dates from Pleistocene to recent, the latter being predominant earth river banks and the former around the central part of the plains, no major fault zone traverses the project area.

The project area has hot summer and cold winters. The summer starts from May and lasts till September. June is the hottest month. The mean maximum temperature varies between 39- 45 ºC and minimum temperature varies between 23-29 ºC respectively for month of June. The winter seasons lasts from November to February. January is the coldest month. The mean maximum ranges between 18 - 30 ºC and mean minimum temperature ranges between 05 - 14 ºC in January

In project areas, most of the times of the year sunny days dominate. A few days per month are partly cloudy and with seldom overcast days. The maximum precipitation is observed during June to August. In project areas are classified as arid region having average annual rainfall less than 250 mm in a year. Highest intensity of rain is recorded in month of July and August owing to monsoon season.

Groundwater

As per (Electrical Resistivity Survey) ERS studies, shallow groundwater is slightly brackish, whereas deep groundwater is relatively sweet at depths of around 200 ft. Handpumps

installed at depths of 50-200 ft yield sweet water and are commonly used by the local community for drinking purposes. In contrast, groundwater near the ground surface remains brackish.

As per ERS studies, groundwater at shallow depths of about 20–30 ft occurs in localized sweet water pockets. These pockets are limited to approximately 20 ft in thickness, below which the groundwater becomes brackish and unfit for drinking purposes.

In Liaqatpur groundwater is the primary source of domestic water supply. The quality of groundwater is generally brackish to moderately saline, with elevated Total Dissolved Solids (TDS) reported in several locations. In some areas, the presence of dissolved salts and occasional microbial contamination limits its direct suitability for drinking without basic treatment; however, it remains commonly used for household purposes and limited irrigation.

Groundwater depth in the tehsils of Alipur, Shujabad, and Taunsa in the ranges from 20 to 60 ft and serves as the primary source of water. The groundwater quality is non-objectionable in terms of taste and color, indicating generally acceptable groundwater conditions. In Pakpattan, TDS and total hardness are beyond PEQs and WHO standards.,

Surface Water

Punjab is land of Indus River and its four major tributaries in Pakistan, the Jhelum, Chenab, Ravi, and Sutlej rivers. Punjab Irrigation system is one of the world's largest irrigation systems with a command area of over 21 million acres. The system consists of 24 main canals and 12 barrages and vast network of canals, distributaries and minors spanning over 40,000 kilometers. Targeted villages in north, south and center of the Punjab are in command area of this irrigation system.

The tehsils of Alipur, Shujabad, and Taunsa in the South-II Cluster are served by major surface water resources, including the Indus and Chenab Rivers, as well as an extensive irrigation network comprising canals, distributaries, and minors. These water bodies are primarily used for irrigation and local water needs.

In Liaqatpur, canals associated with the Abbasia Canal system provide water primarily for agricultural activities, Surface water is not a major source of potable water but is widely used for irrigation, livestock, and groundwater recharge.

In Rojhan Tehsil, Indus River is the primary perennial surface water source for Rojhan. Durring the monsoon season, torrential rains in the Koh-e-Sulaiman hills generate hill torrents, which bring large volumes of surface water down into the plains of Rojhan and surrounding areas.

Surface water in Noorpur Thal is linked to the river Jhelum irrigation system, with supply conveyed through the Dulla distributary and its off-taking channels, including Adhi Kot, 2-L, and Tail Right. These channels support irrigation demands and contributes to localized surface drainage during operational periods.

In Bahwalnagar the overall water quality is assessed as moderate to poor. Most physico-chemical parameters comply with acceptable limits; however, elevated TSS and turbidity remain concerns.

Tehsil Pakpattan is served by one main canal and three distributaries, which primarily support irrigation and local water requirements, with generally moderate water quality.

B. Biological Environment

Project areas are rich in biodiversity because of its diverse landscape and geographical location. The variety of ecosystem is evident and is home to various species. The following section describes the biological environment of the project area.

Common animals found in the project area include wild cat, dogs, cats, jackals, Weasel, house rats, wild boar, bats, porcupine, bandicoot, soft furred rat and Indian gerbil. Domestic livestock observed during field visits include buffaloes, cattle, goats, sheep, and donkeys that are used by the local residents for their livelihood.

Bullfrog (*Hoplobatrachus tigernius*), Pahari tidda maindak (*Fejervarya limnocharis*), frog (rana tigrine) and Toad (Bufo bufo) are also present in the nearby ponds and canals during rainy season.

House sparrow (*Passer domesticus*), House crow (*Corvus splendens*) and Mynah (*Acredotheres tristis*) are the most common sight in the area. In addition, following birds are also seen in the project area**.**

Common tree lizard (*Calotes versicolor*), Monitor lizard (*Varnus bengalensis*), fat tailed lizard (*Uromastix hardwickii*), fringed toed lizard (*Acanthodactylus cantoris*), Tortoise (Testudinidae), snakes (Serpentes), cobra (Naja) and Scorpions (Scorpiones) are observed in and around the proposed site. Saw-scale viper (Echis carinatus), Indian soft-shell turtle (*Aspideretes gangeticus*), striped keelback (Amphiesma stolatum) and Indian falpshell (*Lisseyms punctate andersoni*) are also reported by the local residents.

The major floral species found in the project area include Jand trees, Karir, Beri, Van, Kikar, Sheeham, Neem, Peepal, Aak, Bair and Kikar.

There are no endangered species of either flora or fauna in the project tehsils. Neither any legally protected areas (wetlands, game reserve, biodiversity parks and forests) in the area or in the influence of the project area.

C. Social Environment

Socioeconomic baseline was established using primary and secondary data. Detailed site visits were conducted by Social Experts of consultants to appraise the prevailing socioeconomic conditions and to assess the socioeconomic impacts of the proposed project. During the field surveys, interviews and consultation meetings were held with the local representatives i.e., Numberdars, residents (Males & Females), shopkeepers, land owners, agriculturists, and their laborers, etc., in all 232 villages of Phase -1.

Primary data was collected through a socio-economic survey with the help of a structured and un-structured questionnaire. Random sample was conducted in all 232 villages of Phase-1, 08 tehsils of Center, North and South. Secondary data was collected from the Pakistan Bureau of Statistics (Census 2023), established literature, and research.

The analysis of water and sanitation conditions across the study area highlights several key issues. Handpumps and household level electric pumps are the primary source of drinking water, with deep pumps for satisfaction of household and better water quality. Open drains dominate the sewerage system, often clogged and poorly designed, causing sewage overflow, while septic tanks and soakage pits are limited to a few villages. Toilet facilities are available to most households, but open defecation persists in several areas, and solid waste management services are fully functional only in Taunsa, Alipur, and Shujabad, with other tehsils facing partial or severe deficiencies.

During survey it was revealed that the villages lacked adequate sanitation facilities, exposing the local poor WASHconditions. As a result, locals reported a prevalence of waterborne and water-related diseases, including diarrhea, dysentery, typhoid, cholera, intestinal infections, skin allergies. The absence of safe drinking water and proper sanitation systemalso adversely affected overall public health and nutritional status. With the provision of reliable water supply, improved sanitation, and appropriate wastewater management under the project, a significant reduction in waterborne diseases and overall improvement in community health and well-being is expected.

Relevance of Project-Supported WASH Interventions

The existing baseline conditions indicate a strong linkage between WASH deficiencies and adverse health and child stunting in villages. Project-supported WASH interventions such as improved access to safe drinking water, sanitation facilities, hygiene awareness, and safe wastewater management are expected to:

- Reduce the incidence of diarrheal and waterborne diseases, particularly among children under five;
- Improve nutrient absorption and overall health, thereby contributing to better nutrition outcomes;
- Reduce household expenditure on medical treatment and improve productivity; and
- Enhance community awareness regarding safe hygiene and sanitation practices.

Overall, the project interventions are likely to directly and positively impact the baseline situation of public health and child stunting, contributing to improved quality of life in villages.

Agriculture remains the dominant livelihood across most tehsils, supported by fertile land, while labour forms the second major occupation due to widespread socio-economic challenges. Monthly income levels vary significantly, with many households earning between 20,000–50,000 PKR, though a considerable share survives on even lower earnings in areas with infertile land such as Rojhan. Landlords in fertile regions generally maintain higher incomes, whereas tenant communities in multiple tehsils receive minimal returns for their work, leaving them economically vulnerable. Housing conditions differ across the project area, with most settlements shifting toward pacca construction, although tenant-based tehsils still show prevalence of semi-pacca and kacha structures. Basic amenities remain inadequate, with limited public transport, poor water quality, and widespread waterborne diseases impacting community health. Access to medical facilities varies, as some tehsils benefit from DHQs while others rely on under-resourced THQs and BHUs. Education facilities exist at primary to high school levels but are not uniformly distributed. Overall, the project area reflects a mix of agricultural dependency, financial vulnerability, limited infrastructure, and insufficient health and civic services.

5. Public Consultation and Information Disclosure

Engagement with stakeholders and disclosure is an integral part of the project's environmental and social assessment. The methods used for public consultation with project stakeholders in order to ascertain their stakes regarding project implementation were general/public meetings, rapid participatory appraisal, and on-site meetings.

Different categories of interested parties including project staff, government officials, and local communities were consulted to predict the nature and scale of risks, challenges, and

impacts of the project perceived by them. Concerns raised by the locals are as followed. In **Table ES1**.

Table ES1: Concerns raised by locals and their response

Sr. No	Concerns Raised	Locations	Response
1.	Will employment opportunities be generated for locals during the construction phase?	All project villages	It will be made sure that 75% of the workforce will be employed from the sub-project area.
2.	Arrangements should be made to suppress dust, curtail high-noise activities, and control the vibrations caused due to machinery, to protect the community's health	All project villages	Regular sprinkling of water will be carried out over the loose soil to suppress the dust, the noisy activities will not be planned at night and the community will be informed before the execution of any activity that would generate vibrations
3.	Privacy of people should be upheld during construction phase of the sub-project.	All project villages	Contractor will provide trainings to workers regarding gender and privacy issues.
4.	Construction activities should be minimized during schools' opening and closing times.	All project villages	Contractor will be bound to minimize construction activities during schools' opening and closing times.
5.	Will there be any closure of roads during construction phase?	All project villages	In case of road closures, the nearby community will be informed beforehand and alternative routes will be provided.
6.	Solid waste production during construction time is a major concern and that should not be piled up in the project area.	All project villages	The construction and other waste generated at the site shall be collected, stored and transported to the final disposal site by the contractor on daily basis.
7.	Will there be any tree cutting?	All project villages	No, no trees will be cut during the execution of the project.

6. Anticipated Environmental Impacts and Mitigation Measures

The construction activities would cause changes in topography, soil contamination, surface & groundwater pollution, air pollution, noise & vibration, solid waste generation, wastewater generation, hazardous waste, disturbance to flora and fauna, overburdening of resources, construction camps issues, health & safety issues, emergency situations, traffic disruption and social issues.

Anticipated impacts during operational stage will include water pollution, air pollution, soil contamination, ecological disturbance, solid waste generation, occupational health & safety issues and emergency situations.

The positive impacts of the project include, improved water supply system, improved sewerage system, improvement in public health, hygiene and sanitation, landscape, economic development, employment generation, development of deprived villages, formation of model villages, synergetic development with cooperation of NGOs, CBOs and other organizations.

7. Environmental and Social Management and Monitoring Plan

Recommended mitigation measures to control potential adverse impacts are described in this Environmental and Social and Management Plan (ESMP). ESMP shall become the part of construction contract agreement and shall be strictly enforced during the implementation of the proposed project.

The proponent PRMSC will be responsible for compliance of with environmental and social safeguard requirements of the proposed project.

The proposed project activities will be monitored and managed by the PRMSC. The Environmental and Social Wing (ESW) staffed by qualified environmental and social specialists has already been established under PRSWSSP. The ESW will be the custodian of the ESMP. ESW will support ensuring the compliance of ESMP. ESW will submit progress reports for the implementation of the ESMP to WB and PEPA as per environmental approval/ NOC conditions for the PRSWSSP.

8. Grievance Redress Mechanism (GRM)

The Grievance Redressal Mechanism (GRM) will be consistent with the requirements of the World Bank safeguard policies to ensure the mitigation of community concerns, risk management, and maximization of environmental and social benefits. The overall objective of the GRM is therefore to provide a robust system of procedures and processes that provides for transparent and rapid resolution of concerns and complaints identified at the village level.

The PRMSC (Head Office) will be responsible for providing oversight on the entire GRM process at a strategic level and monitoring complaints management.

The complaints may be lodged through:

- Tracking complainant(s) from subprojects sites (field and community level) to PRMSC;
- Dedicated staff to update the database routinely;
- Promote transparency, publicize how complaints are being handled, and periodically evaluate the overall functioning of the mechanism;
- Processes for informing stakeholders about the status of a case; and
- Procedures to retrieve data for reporting purposes, including the periodic reports, from Village and Tehsil and document them into the monthly progress reports at PRMSC.

GRC Tier-I

GRC (Village level) will be responsible to receive, log, and resolve complaints at the village level. The Grievance Redress Committee at the village Panchayats/Villages Organization (VO) will review and identify actions to be taken to address the complaints at its weekly meeting. If not resolved timely then complaint would be referred to GRC-Tehsil Level (PRMSC-TO) within 3 days after receiving.

GRC Tier-II

GRC-PRMSC-TO will try to resolve the complaints in a satisfactory manner.

GRC Tier-III

If the complaint is not satisfactorily resolved by the village panchayats/councils and Tehsil level, then the grievance will be referred for consideration by GRC at the PRMSC/LG&CDD level within one week.

Every effort will be made to address or resolve grievances within the following fixed timelines, which will be an indicator of the performance of the handling system. Acknowledgment of a written submission will be issued to the complainant within three working days.

If the complainant is not satisfied, the complainant will have the option to seek redress through the relevant court of law.

9. Environmental Budget

The total estimated cost for the implementation of ESMP is worked out to be about **PKR 352.773 million rupees or 1.26 million US$[2].**

[2] 1 US$ = 281.55 PKR

1 INTRODUCTION

1.1 General

The Local Government & Community Development Department (LG&CDD), Government of Punjab, through its Punjab Rural Municipal Services Company (PRMSC), a company registered under section 42 of “The Companies Act 2017”, is implementing Punjab Rural Sustainable Water Supply and Sanitation Project (PRSWSSP)” in 2000 villages in 16 tehsils of Punjab with the proposed assistance of the World Bank. To implement this project, Executive Committee of National Economic Council (ECNEC) has authorized Punjab Rural Municipal Services Company (PRMSC) to initially implement this project in 200 villages as pilot phase (**Annexure-2**) to understand feasibility and sustainability of the Project.

Pilot Phase:

To implement this project, the Executive Committee of the National Economic Council (ECNEC) considered the summary dated 27th January, 2022 submitted by the Ministry of Planning, Development and Special Initiatives titled “Punjab Rural Sustainable Water Supply and Sanitation Project (PRSWSSP) and approved the proposal with the following directions:

i. A "Pilot Project" should be conducted, based on 10% of the approved project scope.

ii. After one year, lessons learned from the pilot phase should be shared with the Central Development Working Party (CDWP), with a specific focus on the operation and maintenance aspects of the project.

iii. The project timeline should be reduced to five years after gaining insights from the pilot phase.

To initiate the Project, an initial pilot phase was undertaken in 200 villages (**Annexure-2**) to assess its feasibility and long-term sustainability. For this purpose, the 16 tehsils were organized into six geographical clusters, and the feasibility studies, engineering designs, PC-I documents, BOQs, and safeguard instruments for all 200 villages were completed across five implementation packages.

Remaining Scope of 1800 villages:

Building on the lessons learnt from the pilot phase of 200 villages, the CDWP granted approval on 12 December 2024 for PRMSC to proceed with the remaining scope of 1,800 villages. To initiate the preparation of feasibility studies, detailed engineering designs, PC-I documents, and safeguard instruments, PRMSC has reorganized the 16 tehsils into five geographical clusters and engaged five Engineering Design and Supervision Consultants (EDSCs) under the assignment titled “Consultancy Services for Engineering Design and Construction Supervision of Punjab Rural Sustainable Water Supply & Sanitation Project (PRSWSSP).”

Under this arrangement, Phase-1 has commenced, covering an initial batch of 232 villages. To expedite implementation, the EDSCs have been instructed to submit feasibility studies, detailed engineering designs, PC-I documents, and environmental and social safeguard instruments on a phased basis.

Table 1 indicates number of villages, covered in different selected tehsils:

Table 1 : Project Area with Number of Villages

Cluster	Name of Consultant	Tehsil	Phase-1
North	NESPAK	Noorpur Thal	26
South-I	Alter	Liaqatpur	90
		Rojhan	12
South-III	Asian Consultants	Bahawalnagar	19
Central		Pakpattan	20
South-II	Rehman Habib Consultants	Alipur	21
		Shujabad	10
		Taunsa	34
Total			**232**

The goal of PRSWSSP is to improve sanitation conditions, provide clean drinking water, improve living conditions through behavior change, and capacity building for the sustainability of the project in rural settlements of Punjab.

This Environmental and Social Management Plan (ESMP) has been prepared for the 232 villages in Phase-1 of the proposed project in line with World Bank Operational Policies (OPs) and Environmental Social & Management Framework (ESMF) for PRSWSSP. The current study covers various impacts of the design, construction, and operation of water supply, sewerage.

1.2 Project Background

Punjab is the most populous province of Pakistan with 110 million inhabitants out of which 70 million reside in rural areas[3]. The people living in rural areas of Punjab lack access to improved water and sanitation facilities which contribute to child stunting, malnutrition and water borne diseases. Poor condition of Water, Sanitation and Hygiene (WASH) not only affects the health of masses, but it also adversely affects the economic growth of the region.

Poverty and Shared Prosperity Report, 2020[4] reveals that 4 out of 5 people live below the international poverty line in rural areas. Studies conducted in different periods of time have linked improved water and sanitation facilities with the alleviation of poverty.

Despite making significant efforts by successive governments to improve the prevailing situation, 44% population of Punjab still does not have access to improved water and sanitation facilities as per globally established standards. Rural settlements of Punjab, which hold 73% of the province's population living in 23,000 revenue villages, are in dire need of investments to improve WASH. Reports show that 3 in 5 households in Punjab use E-Coli contaminated water and every 25th household in Punjab lacks access to the improved sources of drinking water. Similarly, the situation of sanitation is also immensely deplorable.

Outcomes of various studies and sector assessments have identified requirements for improving climate resilience and planned economic growth of 2,000 villages that will be the part of the project. Poverty, water contamination, child stunting, and sanitation condition of the areas have been taken as basic parameters for the selection of project sites/tehsils.

[3] https://pwd.punjab.gov.pk/population_profile
[4] https://www.worldbank.org/en/publication/poverty-and-shared-prosperity-2020

The Government of Punjab, with the assistance of the World Bank, will finance complete detailed engineering designs through Engineering, Design & Supervision Consultancy Services (EDCS) under the pilot phase project in the revenue villages of six (06) Geographical based Clusters of selected districts. The services will assist in; (i) design documentation, including Sub-scheme/Project Document (PC-I), Bill of Quantities, for water supply and sanitation services to achieve economies of scale and desired results, and (ii) resident supervision of infrastructure development.

The PRMSC has adopted a Phase wise approach for designing of villages, to fast track the implementation of the project in each cluster. Names of the 232 villages included in Phase-1 is listed in **Table 2.** It is to be noted that the current lot of 232 villages is located in 08 Tehsils (out of the original 16 tehsils covered under the geographical scope of the project).

Table 2: Location and Name of Phase-1 Villages in Different Tehsils

Cluster	District	Tehsils	Phase-1 Villages
North	Khushab	NoorpurThal	Rakh Dhammak
			Rakh Bambool
			Shergarh
			Daravi
			Chak No 020/M.B
			Burhan
			Rakh Baland
			Chak No 018/M.B
			Kaka
			Sidha
			Palohan
			Chak No 019/M.B
			Laghari
			Mahmood Shaheed
			Khai Kalan
			Jaura Kalan
			Khai Khurd
			Shah Hussain
			Rakh Shah Hussain
			Rakh Tahla Khatwan
			Adhikot
			Chan
			Chak No 035/M.B
			Chak No 036/M.B
			Nakro Shaheed
			Chak 13

Cluster	District	Tehsils	Phase-1 Villages
			Ahmed Yar
			Arif Baloch
			Chak 315 / 6R
			Chak 316 / 6 R
			Chak 317/6R
			Chak 08 Abbasia
			Chak 09 Abbasia
			Chak 11 Abbasia
			Chak 12 Abbasia
			Chak 313/6R
			Chak 134 NP
			Chak 135 NP
			Chak136 NP
			Chak 139 NP
			Chak 140 NP
			Chak 143 Abbasia
			Chak 144 Abbasia
			Chak 145 Abbasia
South-1	Rahimyar Khan	Liaqatpur	Chak 147 / 5R
			Chak 148 / 5R
			Chak 150 Abbasia
			Chak 152 / 7R
			Chak 153 / 7R
			Chak 154 / 7R
			Chak 155 / 7R
			Chak 156 / 7R
			Chak 157 / 7R
			Chak 159 / 7R
			Chak 174 / 7R
			Chak 175 / 7R
			Chak 177 / 7R
			Chak 178 / 7R
			Chak 179 / 7R
			Chak 180 / 7R
			Chak 182 / 1L
			Chak 183 / 7 R
			Chak 186 / 7 R

Cluster	District	Tehsils	Phase-1 Villages
			Chak 19 Abbasia
			Chak 191 / 1L
			Chak 194 / 1L
			Chak 195 / 1L
			Chak 20 Abbasia
			Chak 22 Abbasia
			Chak 23 Abbasia
			Chak 28 Abbasia
			Chak 31 Abbasia
			Chak 32 Abbasia
			Chak 33 Abbasia
			Chak 36 Abbasia
			Chak 37 Abbasia
			Chak 38 Abbasia
			Chak 39 Abbasia
			Chak 3 A
			Chak 40 Abbasia
			Chak 41 Abbasia
			Chak 42 Abbasia
			Chak 43 Abbasia
			Chak 46 Abbasia
			Chak 47 Abbasia
			Chak 48 Abbasia
			Chak 4 A
			Chak 63 Abbasia
			Chak 64 Abbasia
			Chak 65 Abbasia
			Chak 68 Abbasia
			Chak 69 Abbasia
			Chak 75 Abbasia
			Chak 77 Abbasia
			Chak 78 Abbasia
			Chak 79 Abbasia
			Chak 80 Abbasia
			Chak 81 Abbasia
			Chak 82 Abbasia
			Chak 83 Abbasia

Cluster	District	Tehsils	Phase-1 Villages
			Chak 84 Abbasia
			Chak 85 Abbasia
			Chak 86 Abbasia
			Chak 87 Abbasia
			Chak 88 Abbasia
			Chak 89 Abbasia
			Chapri Chatan Shah
			Gulshan Farid
			Hayat Lar
			Kanjki Wala
			Kotla Daraigh
			Kotla Khairay Khan
			Muradpur Sail
			Taranda Gurgujj
			Turkary
			Firoza
	Rajanpur	Rojhan	Bhagsar
			Dilber
			Dhora
			Gianmal
			Qadra Kass
			Rakh Kotla Hasan Jamra
			Mutafriq Mazari
			Rakh Qadra
			Rakh Sabzani
			Safdar Abad
			Salim Abad
			Tariq Abad
South-III	Bahawalnagar	Bahawalnagar	Bonga Ihsan Bibi
			Hasan Raika
			Bhole Shah Hitar
			Paran Wala
			Chak Abdul Haq
			Dhanraj Pura
			Jagga Sanatteka & Mini Sanatteka
			Mosla
			Pir Sikandar Otar

Cluster	District	Tehsils	Phase-1 Villages
			Jhulan Chistian
			Gauspur
			Amin Abad
			Abrarah Uttar
			Ali Gohar No. 326
			Ramnagar
			Hussain Abad Uttar
			Huusain Abad HIttar
			Gaman Dongi
			Sharaf Din
Central	Pakpattan	Pakpattan	Chak No.102/D
			Chak No.87/D.
			Bahwan Shah
			Chak Ilahi Bux
			Chak Murad Khan
			Chak Nazam Din
			Gobind Pur Bahmni
			Jand Wala
			Nahla Abad
			Dhamiana
			Chak No.4 S.P.
			Chak Quder Tullah
			Chilli Mamdana
			Dada Ahluka
			Ghar Taj
			Ghazi Mardan
			Nura Ahluka
			Ghuri
			Arazi Tek Chand
			Chak 103/D
South-II	Muzaffargarh	Alipur	Baqar Shah Shumali
			Bande Shah
			Maqwal Hadeir
			Nehal Wala
			Nauhabad
			Khayara
			Mithan Wali
			Ali Wali

Cluster	District	Tehsils	Phase-1 Villages
			Kotla Agal
			Makhan Bela
			Bet Barrah
			Marian
			Bet Mir Ahmad Jamal
			Kotla Ghulam Shah
			Sirki
			Tibba Barrah
			Bet Bagh Shah
			Yare Wali
			Kohar Faqiran
			Kotla Afghan
			Gagare Wali
	Multan	Shujabad	Wahi Riki
			Basti Dad
			Chah Miran Khan
			Nawan Chak
			Mohan Pur Sharqi
			Sangrai
			Shahpur Ubha
			Sarai
			Shah Pur Shumali
			Nasir Pur
	Taunsa	Taunsa	Aqupur
			Arakhar Dao
			Rind Wala
			Baghon Wala
			Bakhri
			Basti Habib
			Basti Nasir
			Basti Usman Shah
			Berand
			Bet Obai
			Bodo Mian
			Chak Sohanra Bacha
			Domra Janubi
			Domra Shumali
			Ghadi Sandila
			Ghali
			Jalal Khan
			Jhok Chhapri
			Jhok Mangla
			Jhok Rohal

Cluster	District	Tehsils	Phase-1 Villages
			Jhok Yaran
			Jinpur
			Khitran Wala
			Kotla Marrani
			Rakh Sanjar
			Rakh Zor
			Wani
			Mahnda
			Mirkhar
			Mundrani
			Pukan
			Rakh Mari Pachaudi
			Langah
			Rakhana

The anticipated environmental and social impacts of the project in the selected 232 villages are mostly localized, site-specific and temporary; which could be easily mitigated through appropriate mitigation measures. According to the findings of the Environmental and Social Screening study, this project falls in Category E2 and requires an ESMP.

Environmental clearance from the Environmental Protection and Climate Change Department (EP&CCD), Punjab is mandatory according to the Punjab Environmental Protection Act, 2012. Section 12 (1) of the Act states that:

As per Punjab Environmental Protection Agency (PEPA) Review of Initial Environmental Examination (IEE) and Environmental Impact Assessment (EIA) Regulations 2022, Schedule-II, EIA is required for 'Water Supply, Sewerage System and Treatment' (Category F).

A combined EIA isbeing prepared Tehsil wise and will be submitted in March, 2026 to EP&CCD for conductance of site inspection survey, public hearing. Issuance of Environmental Clearance (NOC) in anticipated by June 2026.

1.3 Objective of ESMP

The objective of this ESMP is the identification of possible environmental and social impacts of the proposed project on both short and long-term bases. Based on the level and nature of these observations, the ESMP delineates proper mitigation measures. As a planning tool, the ESMP aims to ensure that environmental, socio-economic, and cultural issues throughout the entire project lifecycle are anticipated and considered by the project proponent. It also serves as a framework for establishing project controls to reduce or prevent adverse environmental or socio-economic impacts.

The specific objectives of this ESMP are:

- To assess the existing environmental and socioeconomic conditions of the project area;
- To identify potential impacts of the proposed interventions on the environmental, ecological, and social aspects of the project area, to predict and evaluate these impacts and determine their significance;
- To propose appropriate mitigation measures that should be incorporated in the design of the project to avoid or minimize (if cannot eliminate) the potentially adverse impacts;
- To assess the compliance status of the proposed activities with respect to the national and provincial environmental legislation and WB's OPs;
- To provide institutional, monitoring, reporting, and documentation measures for environmental safeguards compliance; and estimated costs for implementing these measures; and
- To help decision-makers in taking informed decisions.

1.4 Scope of ESMP

The ESMP identifies the potentially significant impacts of the proposed project and suggests the applicable mitigation measures to avoid, minimize or reduce the magnitude of the impacts. It will also indicate the institutional and training requirements to implement mitigation measures during the construction and operation of the proposed project.

The current ESMP presents a preliminary roadmap for the environment and social management for the construction and operation of the water supply scheme, sewerage network and sewage treatment plant (STP) in all 232 villages of Phase-1 of eight (08) tehsils.

1.5 Contractual Requirements/ Obligations of ESMP

The impacts and their mitigation measures, summarized in ESMP, will be part of the Bidding Documents to ensure that Contractors implement ESMP recommendations at all project stages. The ESMP requirements will be part of the Contract and the details prescribed in the ESMP will be mandatory. The ESMP will be equally applicable to Subcontractors, including nominated Subcontractors (if any).

At the stage of the bidding process, the Contractor will be instructed to carefully consider the requirements for environmental and social management contained in this ESMP when preparing the bid and pricing the items of Work. The Contractor will need to accept that the prescriptions and clauses detailed in the ESMP are an integral part of the Contract for relevant items of Work; unless separate items are included in the Bill of Quantities (BoQs). The Contractor will need to accept that separate payment will not be made in respect to compliance with the ESMP. The Contractor should, therefore, be aware that in case the Contractor or Subcontractors fail to implement the ESMP recommendations, the Environment and Social team shall take necessary action(s) to ensure that the ESMP is properly implemented and/or to rectify the damages caused by such negligence.

1.6 Approach & Methodology to Work

1.6.1 Approach

The study has been conducted in accordance World Bank Safeguards policies (OP 4.01, OP 4.04, OP 4.11, OP 4.12, OP 4.20 & BP 17.50) applicable to this project. Further, Punjab Environmental Protection Agency (PEPA) guidelines were also considered in preparation of this document. The study is based on both primary and secondary data and information. The primary data includes data collected from field i.e., information about existing conditions; environmental sampling and analyses for air, water and noise; environmental sensitive receptors, ecological survey; social survey including demographic characteristics, income dependency & quality of life, occupation, and social amenities etc. The secondary data includes a review of relevant information from literature and previous reports. Discussions were held with stakeholders including government officials, community representatives and a wide range of local communities. The main purpose of this approach was to obtain an impartial impression of the people's perceptions of the project and its environmental and social impacts.

The assessment remains subject to change with respect to the finalization of technical specifications and alignment of the proposed sewer, water supply lines & location of overhead tanks, pumping station, and STP.

1.6.2 Methodology

An Environmental and Social Checklist for ESMP data collection was designed on Kobo Toolbox. This checklist ensures that the data provided by the EDCS consultants is consistent in format and covers the required extent, with the objectives of digital data collection and analysis to gain real-time insights on local dynamics of villages that can support in anticipating environmental and social impacts and suggesting proper mitigation measures. The following methodology was adopted to develop the ESMP of the proposed Project:

A. Orientation

Meetings and discussions were held among the members of the ESMP Consulting Team. This activity is aimed at achieving a common understanding of the various issues of the study.

B. Data Collection Planning

Subsequent to the concept clarification and understanding obtained in the preceding step, a detailed data acquisition plan was developed for the internal use of the ESMP Consulting Team. The plan included; identification of specific data requirements and their sources; determination of time schedules and responsibilities for their collection and the indication of the logistics and other supporting needs for the execution of the data acquisition plan. Field surveys were then conducted based on the data collection plan.

C. Detailed Field Survey

Detailed site visits and technical visits for environmental monitoring and social assessment for the collection of data were conducted in June to October, 2025. The data collected was transferred to Kobo-Tool box following WB-GEMS training in July- 2025, and an orientation session conducted for EDCS consultants. The data collected from the field include:

- Identification of environmentally sensitive receptors including air-sensitive receivers, noise-sensitive receivers, and water bodies expected to receive pollutant load;
- Sampling and analysis for air, noise wastewater, and groundwater;
- Ecological survey;
- Socioeconomic survey including public consultation;
- Stakeholders' consultations;

D. Sampling & Analysis of Physical Environmental Parameters

EPA Certified Laboratories (i.e., Pak Green, SEAL, Green Environmental Monitoring and ASIAN Laboratories) were hired for environmental monitoring. The Laboratories were mobilized from August 2025 to October 2025 for collection of water and wastewater samples as well as air and noise monitoring.

E. Review of Secondary Data

Previous environmental and social soundness assessment for 16 tehsils was collected in order to gain a complete understanding of existing environmental conditions of the area including:

- **Physical environment:** topography, geology, soils, surface and groundwater resources, and climate;
- **Biological environment:** flora and fauna (particularly rare or endangered species), critical habitats/zones, and vegetation communities within the project area;
- **Socio-economic environment:** settlements, socio-economic conditions, infrastructure, and land use.
- **Heritage aspects**: sites of cultural, archaeological, or historical significance.

F. Review of Environmental and Social Laws and Institutional Requirements

The project needs to comply with all the applicable national and provincial environmental and social policies, laws, guidelines, acts, and legislations and World Bank's Operational Policies (OPs) requirements. All these requirements and policies were reviewed.

G. Area of Influence (AoI)

Considering the project interventions simultaneously in primary settlement as well as number of secondary settlements of revenue villages, the whole revenue village is considered as area of influence of the sub project.

H. Environmental and Social Baseline Survey of the Project

Environmental and social surveys were carried out within the AoI to establish the baseline of the project area from June 2025 to December 2025 and all the data collected from the field was transferred to form generated on Kobo-Tool. Prior to the start of field activities, comprehensive checklists, proformas, and maps were developed to gather the following information:

(i) Physical Environment

The following information was acquired for the establishment of the physical environment baseline:

- Topography;
- Water resources (including available surface and groundwater resources and natural streams, hydrology, water supply, water contamination etc.);
- Climate data (including temperature, precipitation, humidity, wind speed, direction etc.);
- Water, surface water, ambient air quality and noise level monitoring data;
- Existing water supply and sewerage systems;
- Seismology;
- Geology
- Environmental Sensitive Receptors.

(ii) Ecological Environment

- Flora (trees, herbs, shrubs, grasses, and overall vegetation including valuable or rare trees and their loss due to implementation of the Project, etc.);
- Fauna/ Wildlife (Mammals, reptiles, amphibians, and avifauna.);
- Reserved forests, Guzara forests, Community forests/ Private forests, and wildlife sensitive or notified areas in AoI;
- Migratory birds' corridors; and
- Endangered species (both flora and fauna).

(iii) Socio-Economic Environment

Analysis is carried out on the basis of secondary data within the AoI in order to develop the socio-economic baseline information of the general settled population. Data and analyses of pertinent socio-economic parameters were revalidated in the socio-economic baseline survey of the sample population settled within the AoI. These aspects include the following:

- Demographic characteristics;
- Nature of business/occupation;
- Livelihood/income;
- Living standard of the population;
- Community Institution available;
- Gender issues;
- Housing construction patterns;
- Mode of transport;
- Basic amenities of the project area;
- Health facilities/ Educational facilities.

I. Stakeholder Consultations

There are two categories of stakeholders in the project:

- Community stakeholder

- Institutional stakeholder

For the current study, community stakeholder consultations were carried out through following techniques:

- Formal/ informal meetings (through village numberdars, politically influentials community resource persons)
- Individual interviews
- Group Discussions

The institutional stakeholder consultation session was carried out by holding meetings at the offices of relevant government functionaries. The study teams met with the institutional stakeholders, affected persons and local communities in and around the project area. The objective of the consultation was to disseminate information on the project and its expected impact, long-term as well as short-term, among primary and secondary stakeholders and to gather information on relevant issues so that the feedback received could be used to address these issues at an early stage. Stakeholder consultation is discussed in detail in chapter 5.

J. Impact Assessment and Mitigation Measures

A logical and systematic approach was adopted for impact identification and assessment. The process began during the screening and continued through scoping which identified the key issues and classified them into different categories. The tools were used for impact assessment, through environmental and social screening checklists for impact assessment of construction and operational phase.

Identification of potential environmental and social impacts in terms of their nature, magnitude, extent, location, timing, and duration was carried out. The impacts were correlated to the Project location, design stage, construction as well as operation stage. Based on the impacts prediction methods and as a result of public/stakeholder consultations, ESMP team screened the adverse environmental and social impacts for inclusion in the mitigation measures and environmental and social management plan.

ESMP team proposed practicable, economically feasible and socially acceptable mitigation measures for the significant adverse environmental and social impacts. Details of mitigation measures are provided in chapter 6.

1.7 Structure of ESMP

The structure of this ESMP is listed below:

Section 1: Introduction briefly presents the project background, objectives, methodology and need of the study.

Section 2: Legal and Administrative Framework Lists national as well as provincial laws, regulations and procedures and applicable World Bank Operational Policies (OPs).

Section 3: Project Description provides an overall description of the project including proposed networks, design considerations and concepts, manpower requirement, waste generation, machinery and material requirements.

Section 4: Baseline Profile gives a description of baseline physical, biological and socio-economic conditions of the project area.

Section 5: Public Consultation and Information Disclosure identify the main stakeholders and their concerns raised during scoping sessions and deal with the measures to mitigate the social impacts.

Section 6: Anticipated Environmental and Social Impacts and their Mitigations Measures identify, predict, and evaluate the impacts of the project activities during the construction and operation stages and deal with the measures proposed to mitigate potential environmental impacts of the proposed project.

Section 7: Environmental and Social Management & Monitoring Plan This section outlines the organizational framework, mitigation, and monitoring plans, and training requirements, defines roles and responsibilities and estimates budget requirements for satisfactory implementation.

2 LEGAL AND ADMINISTRATION FRAMEWORK

2.1 General

This section deals with the current environmental policy as well as legal and administrative framework required to develop Environmental & Social Management Plan (ESMP) for the proposed interventions in selected Phase-1 villages of 08 tehsils. All relevant provisions of environmental policies laid down by the Government of Pakistan, Government of Punjab along with applicable World Bank Policies have been duly discussed and the project proponent will be required to adhere to these regulations throughout the course of the project. The institutional arrangement for compliance with these laws has been described in ESMP (Section 7).

2.2 Summary of Key National Strategies, Policies, Acts and Legislation

The summary of key national strategies, policies, acts and legislation from environmental perspective are briefly described in **Table 3** below:

Table 3: Key National Strategies / Policies, Legislation / Acts, Laws and Regulations and Their Relevance to the Project

Sr. No.	Policy/Strategy	Brief Coverage	Relevance to project
1	Fatal Accidents Act 1855	An act to provide compensation to family's loss occasioned by the death of a person caused by actionable wrong. It is enacted as follows: ● Suit for compensation to the family of a person for loss occasioned to it by his death by actionable wrong ● Not more than one suit to be brought ● Plaintiff shall deliver particulars etc. ● Interpretation clause	The provisions of this act would be applicable if any fatal accident occurs during the execution of construction works for the proposed Project.
2	Pakistan Penal Code 1860	It authorizes fines, imprisonment or both for voluntary corruption or fouling of public springs or reservoirs so as to make them less fit for ordinary use.	The provisions of the Penal Code are applicable to the project in terms of penalties for effecting human lives and public property. It also addresses the control of noise, air emissions, and effluent disposal.
3	Land Acquisition Act, 1894 (Including Later Amendments)	The primary law for acquisition of land for public purposes in Pakistan is the "Land Acquisition Act, 1894". The Land Acquisition Act, 1894, is a "law for the acquisition of land needed for public purposes and for companies and for determining the amount of compensation to be paid on account of such acquisition". The exercise of the power of acquisition has been limited to public purposes.	No land acquisition will be carried out through the provisions of this Act under the project. State owned land will be preferred and used for the construction of overhead tanks, pumping stations & STP. Private land will be obtained through VLD, if required.
4	Protection of Trees and Brushwood Act, 1949	This Act prohibits cutting or lopping of trees and brushwood without permission of the Forest Department.	This act will be applicable to the proposed project in term of Tree Cutting which lies in jurisdiction of Forest Department.
5	Pakistan Antiquities Act 1975	The protection of cultural resources in Pakistan is ensured by the Antiquities Act of 1975, which provides a comprehensive definition of Antiquities. The law prohibits new construction in the proximity of a	The provisions of this act would be applicable if any accidental archaeological discoveries occur during the excavation

Sr. No.	Policy/Strategy	Brief Coverage	Relevance to project
		protected antiquity and empowers the Government to prohibit excavation in any area which may contain articles of archaeological significance.	works for the construction of proposed Project.
6	National Conservation Strategy 1992	Pakistan National Conservation Strategy (NCS) is the principal policy document on environmental issues in the Country. The NCS outlines the Country's primary approach towards encouraging sustainable development, conserving natural resources and improving efficiency in the use and management of resources. The NCS has 68 specific programs in 14 core areas in which policy intervention is considered crucial for the preservation of Pakistan's natural and physical environment.	The core areas that are relevant in the context of the proposed project are pollution prevention during construction, conserving, biodiversity and supporting forestry and plantation.
7	Guidelines for Public Consultation, 1997	The Pakistan Environmental Protection Ordinance 1997 requires public participation during the review of an EIA (Section 12(3)). The "Policy and procedures for the filing, review and approval of environmental assessments" requires proponents to consult with the affected community and relevant NGO's during the preparation of an environmental report.	These guidelines are applicable for the preparation of the EIA / ESMP. During the preparation of the ESMP, public consultations were carried out for: ● informing the stakeholders about what is proposed; ● providing an opportunity for those otherwise unrepresented to present their views and values, therefore allowing more sensitive consideration of mitigation measures and tradeoffs
8	Guidelines for Review and Preparation of Environmental Reports, 1997	These guidelines describe the format and content of IEE/EIA reports to be submitted to Provincial EPA/EPD for obtaining NOC. The guidelines present: ● The environmental assessment report format; ● Assessing impacts; ● Mitigation and impact management and preparing an environmental management plan;	These guidelines are applicable for the preparation of the EIA.

Sr. No.	Policy/Strategy	Brief Coverage	Relevance to project
		• Reporting; • Review and decision making; • Monitoring and auditing; and Project Management.	
9	National Sanitation Policy, 2006	The National Sanitation Policy of Pakistan, 2006, stresses on the safe disposal of excreta away from the dwellings, creation of an open defecation-free environment and, promotion of health and hygienic practices in the country.	This policy is applicable to the project for the efficient management of solid waste or wastewater during construction or operation phase of the project. This project primarily focused on provision of improve sanitation services in target areas.
10	Protection Against Harassment of Women at the Workplace Act, 2010	The Protection Against Harassment of Women at the Workplace Act refers to sexual harassment at the workplace.	This Act will be applicable to the project if women are employed for the construction of the proposed Project or women living in near vicinity of the project area.
11	Canal and Drainage Act 1873 and Amendment Act, 2016	This Act prohibits corruption or fouling of water in canals (defined to include channels, tube wells, reservoirs and watercourses), or obstruction of drainage.	This act is applicable to the project for the efficient management of wastewater disposal during the construction or operation phase of the project.
12	Punjab Local Government (Amendment) Ordinance 2021	The Ordinance establishes a new tier of local government at the village level called Village Councils, which incorporated the main functions of village panchayats prescribed in the Panchayats and Neighborhoods Councils Act, 2019 (PVPNCA 2019) with regards to water, sanitation, and waste management.	This act is applicable to the proposed project, village councils is informed about the project and will remain in contact during the construction or operation phase of the project.

2.3 Key Provincial Strategies / Policies, Legislation / Acts, Laws and Regulations

The provincial policies, strategies, acts and laws relevant for the environmental safeguard of the project activities are given below in **Table 4.**

After the 18th amendment to the constitution of Pakistan, many subjects, including environmental protection and pollution prevention, have been devolved to the provincial jurisdiction. Therefore, the apex environmental statute governing the proposed project will be the Punjab Environmental Protection Act 1997. However, detailed rules, regulations and guidelines required for the implementation of the policies and enforcement of legislation are still in various stages of formulation and discussion. The following description presents a brief overview of the relevance of various existing provincial policies, legislation and guidelines.

Table 4: Key Provincial Strategies / Policies, Legislation / Acts, Laws and Regulations and Their Relevance to the Project

Sr. No.	Strategies / Policies / Legislations / Acts / Laws & Regulations	Brief Coverage	Relevance to Project
1	Punjab Land Revenue Act, 1967	WHEREAS it is expedient to consolidate and amend the law relating to the making and maintenance of records-of-rights, the assessment and collection of land-revenue, the appointment and functions of Revenue Officers and other matters connected with the Land Revenue Administration in the Province of the Punjab, or incidental thereto	All the land required for the project, be it public or private, will be transferred in the name of PRMSC under the provisions of this Act
2	Punjab Plantation and Maintenance of Trees Act, 1974	The Punjab Plantation and Maintenance of Trees Act, (1974) regulates tree plantations and enforces measures for their protection. The requirements of this act are applicable in terms of planting new trees and their maintenance by the owner of the proposed Project land who would have the physical possession.	This act would be implemented if any tree cutting activity involved during construction.
3	The Punjab Wildlife (Protection, reservation, Conservation & Management) Act, 1974	This act provides for the protection, preservation, conservation and management of wildlife in the Province of Punjab. This act defines the wildlife sanctuary, game reserves, protected areas, and national parks. It also defines the rules and responsibilities of the relevant authorities and the relevant personnel to protect ecological resources. It also describes the penalties and punishments on offenses against the sections given in the act.	This policy is to avoid any disturbance to ecological system near project area due to construction activities.
4	Punjab Land Acquisition Rules, 1983	This Law provides for the acquisition of land needed for public purposes and for Companies, and determines the amount of compensation to be made on account of such acquisition. It also establishes the due process for land acquisition.	State land will be preferred and used for the construction of overhead tanks, pumping stations & STP. However, Private land if required will be acquired through VLD in this project.

Sr. No.	Strategies / Policies / Legislations / Acts / Laws & Regulations	Brief Coverage	Relevance to Project
5	The Motor Vehicles Rules, 2000	Subject to the provisions of this Act, and the rules and regulations, no person shall operate a motor vehicle from which air pollutants or noise are being emitted in an amount, concentration or level which is in excess of the National Environmental Quality Standards, or where applicable the standards customary under clause (g) of sub-section (I) of section 6.	During Construction all these rules will be followed to avoid emission of air pollutant from vehicles.
6	Guidelines and Checklists adopted by Government of Punjab after 18th Amendment	Post the adoption of the 18th Constitutional Amendment in 2011, the subject of environment was devolved and the provinces have been empowered for environmental protection and conservation. The Punjab Environmental Protection Act, 1997 (as Amended upto 2022) is comprehensive legislation and provides the legislative framework for protection, conservation, rehabilitation and improvement of the environment. The “environment" has been defined in the Act as: (a) air, water and land; (b) all layers of the atmosphere; (c) all organic and inorganic matter and living organisms; (d) the ecosystem and ecological relationships; (e) buildings, structures, roads, facilities and works; (f) all social and economic conditions affecting community life; and (g) the interrelationships between any of the factors specified in sub-clauses “a" to “f”.	All projects to be implemented in Punjab must comply with PEQS during all the phases i.e., construction and operation. No Objection Certificate (NOC) shall be required from Punjab Environmental Protection Agency (PEPA) before commencement of construction.
7	Punjab Drinking Water Policy 2011	The overall objective of Punjab's Water Policy is to provide clear policy directions to the Government of Punjab on the sustainable management and development of water from all sources of water (surface water, groundwater and rainwater), for all sub-sectors of water use (domestic, stock water, agriculture, industry).	This policy is applicable and drinking water supply will be designed according to this policy guidelines.
8	Punjab Environmental Tribunal Rules, 2012	According to Section-31 of the Punjab Environmental Protection Act, 1997 (XXXIV of 1997), the Tribunal shall make every effort to dispose of a complaint or an appeal or other proceedings regarding environmental problems associated with the construction and development of any	This is applicable to dispose of a complaint or an appeal or other proceedings regarding environmental problems associated with the construction

Sr. No.	Strategies / Policies / Legislations / Acts / Laws & Regulations	Brief Coverage	Relevance to Project
		project within sixty days from the date of filing of the complaint, appeal or other proceedings but any decision of the Tribunal shall not be rendered invalid by reason of any delay in the disposal of complaint, appeal or other proceedings.	and development of any project within sixty days from the date of filing of the complaint, appeal or other proceedings.
11	Punjab Antiquities Amendment Act, 2012	The Punjab Antiquities Amendment Act, 2012 is adopted from the Pakistan Antiquities Act of 1975 with a few minor changes.	The law will be applicable to the proposed project mainly due to its provision that „any construction activity within 61 meter or 200 ft. of protected antiquities, are prohibited". The provisions of this act would also be applicable, if any accidental archaeological discoveries may occur during the excavation works for the construction of proposed Project.
12	Punjab Local Government Musalihat Anjuman (Constitution and Functions) Rules, 2016	The dispute may be brought to the Musalihat Anjuman. The Musaliheen shall make every reasonable effort in encouraging and assisting the parties in arriving at an amicable settlement but for this purpose shall not impose, coerce or try to dictate terms for any specific resolution of the dispute.	The provisions of this rule would be applicable, if any dispute occur during the execution of proposed Project. The GRM under the project will also be aligned accordingly.
13	Punjab Environmental Quality Standards (PEQS), 2016	In exercise of the powers conferred under clause (c) of sub-section (1) of section 4 of the Punjab Environmental Protection Act, 1997 (XXXIV of 1997), the Environmental Protection Council has approved the Punjab Environmental Quality Standards (PEQS), 2016. They endow information on the permissible limits for discharges of municipal and industrial effluent parameters and industrial gaseous emissions in order to regulate environmental pollution. Results of environmental monitoring (ambient air, water and noise) conceded out at different locations in	These standards are applicable in compliance with all the Punjab Environmental Quality standards of different Environmental Parameters during Construction and operational phase.

Sr. No.	Strategies / Policies / Legislations / Acts / Laws & Regulations	Brief Coverage	Relevance to Project
		study area are compared with PEQS values and are conversed in later chapter of the report.	
14	The Punjab Flood Plain Regulation Act, 2016	This act regulates construction in the flood plains in the Punjab. According to this act, no construction can be carried out in flood plains without prior approval in writing from canal officer.	Construction work will be carried out in underground for installing of water supply lines and sewerage lines.
15	Punjab Restriction on Employment of Children Act, 2016	According to the sub-section 11(a) of this act, an occupier who employs or permits a child (person under the age of 15 years) to work in an establishment shall be liable to punishment with imprisonment for a term which may extend to six months, but which shall not be less than seven days, and a mandatory fine between 10,000 and 50,000 rupees.	This act will trigger if any contractor hires skilled and unskilled labor under the age of 15. This would be prohibited in the project
16	The Punjab Bonded Labour System (Abolition) Act 1992 & The Punjab Bonded Labour System (Abolition) (Amendment) Act 2018	The Act abolishes bonded and forced labour system with a view to preventing the economic and physical exploitation of the labour class.	This act will trigger on the payment of advance/ *peshgi,* whether in cash or kind. It will prevent bonded/ forced labour of any kind.
17	The Punjab Minimum Wages Act 2019	The Act regulates minimum rates of wages for unskilled and different categories of skilled workers employed in an industry, industrial and commercial establishments.	This Act will be applicable to ensure payment of minimum wages to the employees, labour, and all the skilled, semi-skilled, and skilled staff of the contractors and consultants during their engagement with this project.
18	The Workmen's Compensation Act 1923	This Act ensures the payment by certain classes of employers to their workmen of compensation for injury by accident.	This act will be applicable to ensure that the employees/ labour receive due compensation for injury by accident during

Sr. No.	Strategies / Policies / Legislations / Acts / Laws & Regulations	Brief Coverage	Relevance to Project
			the course of performance of project activities.
19	Punjab Protection of Women against Violence Act, 2016	This act counters gender-based discrimination, violence against women, and economic and social empowerment of women. This act will entail if gender-based violence observed in the project area during construction phase.	This Act will be applicable to the project if women are employed for the construction of the proposed Project or women living in near vicinity of the project area.
20	Punjab Tehsil / Town municipal Administration (Works) rules, 2003 (amendments, 2016)	According to Chapter VIII-A Occupational Safety & Hazard Clause 50 A Workplace Safety and clause 50 B pertains to responsibilities of the Local Government Engineer related to health and safety.	All the mentioned clauses will be applicable on construction labor/workers/ and sewer men/sanitary workers during execution of subprojects.
21	Punjab Environmental Protection Act 1997 (Amended 2022)	Post the adoption of the 18th Constitutional Amendment in 2011, the subject of environment was devolved and the provinces have been empowered for environmental protection and conservation. The Punjab Environmental Protection Act, 1997 (as Amended up to 2022) is comprehensive legislation and provides the legislative framework for protection, conservation, rehabilitation and improvement of the environment. The „environment" has been defined in the Act as: (a) air, water and land; (b) all layers of the atmosphere; (c) all organic and inorganic matter and living organisms; (d) the ecosystem and ecological relationships; (e) buildings, structures, roads, facilities and works; (f) all social and economic conditions affecting community life; and (g) the interrelationships between any of the factors specified in sub-clauses „a" to „f".	All projects to be implemented in Punjab must comply with PEQS during all the phases i.e., construction and operation. No Objection Certificate (NOC) shall be required from Punjab Environmental Protection Agency (PEPA) before commencement of construction.
22	Punjab Policy on Controlling Smog, 2025	The Punjab Environmental Protection Department issued this policy on controlling smog in 2025 It imposed a complete ban on open burning of rice stubble, solid waste and other hazardous materials. It focuses the	During construction and operational phases all PEQS will be followed in

Sr. No.	Strategies / Policies / Legislations / Acts / Laws & Regulations	Brief Coverage	Relevance to Project
	Smog Prevention and Control Rules 2023	reasons behind the formation of dense smog in the Punjab, especially in Lahore and its environs, on the onset of winters each year and provide a short and medium to long term plan, including measure for protection of school going children; minimizing road accidents and creating mass awareness on precautionary measures for citizens at large.	accordance with to compliance and to minimize pollution load to control smog.
23	Punjab Labor Policy, 2018	The Punjab Labor Policy, 2018 intends to guide and support the Government and the stakeholders in developing strategies, plans and programs for the protection and promotion of the rights and benefits of working community without jeopardizing the genuine concerns of the employers.	The labor policy will be relevant as it will deal with the protection of labor. Mitigation and enhancement measures have been proposed in this ESMP to ensure proper working conditions for project labor.
24	Punjab Growth Strategy 2018	The document endorses Punjab's health sector vision and strategy, which emphasizes improvement of water, sanitation and hygiene services to prevent communicable diseases.	This strategy will be adopted in design of proposed project.
25	Punjab Occupational Safety and Health Act, 2019	This law was enacted to ensure occupational safety and health of the persons at workplace. It aims at protection of workers against risks arising out of the occupational hazards and to promote safe and healthy working environment catering to the physiological and psychological needs of the employees at workplace.	This act will be applicable to the proposed project in term of the health and safety during the construction and operational phases of the project.
26	Punjab Water Act 2019	An Act to comprehensively manage and regulate water resources in the Punjab in the interest of conservation and sustainability. It is expedient to provide for comprehensive management of all water resources in the Punjab and to regulate their use in the interest of conservation and sustainability and matters connected with and ancillary thereto.	This act will be applicable to the proposed project. The drinking water supply will be designed in light of PWA, 2019.

2.4 Applicable World Bank Policies

2.1.1 World Bank Operational Policies

The World Bank operational policies applicable to the project and its compliance mechanism, are summarized in the description below;

Safeguard Policies	Triggered	Explanation
Environmental Assessment (OP 4.01)	Yes	Under this OP, the World Bank requires environmental assessment (EA) of projects proposed for Bank's financing to help ensure that they are environmentally sound and sustainable and thus to improve decision making through appropriate analysis of actions and of their likely environmental impacts
Natural Habitats (OP/BP 4.04)	No	This OP is not triggered.
Physical Cultural Resource OP/4.11	No	The sub-project does not lie near any cultural and heritage resource therefore OP 4.11 will not be triggered. The possible discovery of archaeological sites or random findings during the excavation and earthworks may occur. In such case, this OP will be triggered. Furthermore, Annexure 4 for Chance Find Procedures will also be implemented.
Involuntary Resettlement OP/4.12	Yes (Not relevant for Phase -0 villages)	OP 4.12 is not triggered as the sub-project does not require any land acquisition, therefore there will be no involuntary resettlement, livelihood impacts, or restrictions to access. Consequently, there is no need of a Resettlement Action Plan.
Forests (OP/BP 4.36)	No	The sub-project area does not fall under forest area and will not affect any forest. So, this OP is not triggered.
Access to information (BP 17.50)	Yes	The World Bank's Policy on Disclosure of Information is to be open about its activities and to welcome and seek out opportunities to explain its work to the widest possible audience. This policy is triggered for sub-projects categorized as A and B. The developer consults project affected groups and local NGOs: a) during scoping and before TORs are prepared; b) when the draft EA is available; and c) throughout project implementation as necessary. The developer provides relevant information in a timely manner prior to consultation and in a form and language accessible to the groups being consulted.
Projects on International Waterways (OP 7.50)	Yes	This policy will be triggered. The Project has got the PAD cleared from Legal department. An exemption for notification has been approved by the SAR VP.

2.5 Managing the Risks of Adverse Impacts on Communities from Temporary Project Induced Labor Influx

World Bank Management has developed a Guidance Note titled "MANAGING THE RISKS OF ADVERSE IMPACTS ON COMMUNITIES FROM TEMPORARY PROJECT INDUCED LABOR INFLUX" to assist Bank staff in establishing an approach to identifying risks to and impacts on local communities associated with the temporary influx of labor that typically results from construction works, and to advising Borrowers accordingly on how to best manage such risks. This guidance note provides guidance on identifying, assessing and managing the risks of adverse social and environmental impacts that are associated with the

temporary influx of labor resulting from Bank supported projects. The guidance note contains guiding principles and recommendations to be considered as part of the design and implementation of projects with civil works that require labor from outside the project's area of influence. This Note does not introduce new requirements, but rather seeks to provide concrete guidance on how to approach temporary labor influx within the environmental and social assessment process.

2.6 Environmental, Health & Safety Guidelines

In addition to operational policies (OP), the WBG has also established its EHS guidelines for all the interventions that are financed by the group. These EHS Guidelines are technical reference documents with general and sector-specific examples of Good International Industry Practice (GIIP). Following EHS guidelines are relevant to the proposed project during the construction and operation phase:

EHS Guidelines for Water & Sanitation (2007): Issues associated water and sanitation are presented in the EHS Guidelines for Water and Sanitation (2007).

EHS General Guidelines: Generic issues related to Environment, Health and Safety and good practices are discussed in EHS General Guideline

EHS Guidelines for Construction Materials Extraction: Issues associated with sourcing of construction materials are presented in the EHS Guidelines for Construction Materials Extraction.

2.7 International Labour Organization (ILO) Fundamental Conventions – Ratified by Pakistan

The following fundamental conventions of ILO shall be applicable to the project:

- Forced Labour Convention, 1930 (Convention No. 29)
- Freedom of Association and Protection of the Right to Organize Convention, 1948 (Convention No. 87)
- Right to Organize and Collective Bargaining Convention, 1949 (Convention No. 98)
- Equal Remuneration Convention, 1951 (Convention No. 100)
- Abolition of Forced Labour Convention, 1957 (Convention No. 105)
- Discrimination (Employment and Occupation) Convention, 1958 (Convention No. 111)
- Minimum Age Convention, 1973 (Convention No. 138) Minimum age specified: 14 years
- Worst Forms of Child Labour Convention, 1999 (Convention No. 182)

2.8 International Protocol/Conventions

As Pakistan is a member of a number of international organizations such as United Nations Organization (UNO), Organization of the Islamic Conference (OIC), South Asian Association for Regional Cooperation (SAARC), Economic Cooperation Organization (ECO) etc., so it has to follow the international protocols and obligations related to the environment. The major protocols, ratification dates by Pakistan and obligations related to the proposed project are provided in the following table.

Table 5:International Agreements/Conventions Relevant to the Project

Sr. No.	Agreement/ Convention	Ratification	Description/Relevance
1.	UNESCO Convention on the Protection of the World's Cultural and Natural Heritage, 1972 Web Link: http://whc.unesco.org/en/%20convention%20text/	Pakistan ratified this convention on 23 July 1976.	This Convention requires parties to adopt a general policy on the protection of the natural and cultural heritage, to set up services for such protection, to develop scientific and technical studies, to take appropriate legal, technical, scientific and administrative measures and to foster training and education for such protection. The proposed project design and ESS team paid due attention to archaeological sites and local norms. Both of these factors will also be considered during project implementation.
2.	Convention on Conservation of Migratory Species of Wild Animals, 1979 https://www.cms.int/	Pakistan signed this convention in 1981 and ratified it in December 1987.	Convention on the Conservation of Migratory Species deals with the conservation and protection of the migratory species. Species covered in the Convention should be given special attention during EA and monitoring and any impacts identified should be mitigated to acceptable levels.
3.	The Rio Declaration, 1992 Web Link: http://www.unesco.org/education/pdf/RIO_E.PDF	Pakistan signed the treaty on 13Jun 1992 and ratified on 1 June 1994	The Rio Declaration comprises 27 principles which address important issues such as; sustainable development to integrate environmental protection into the development process; common but differentiated responsibilities to conserve, protect and restore the earth's ecosystems; public participation and information access at the national level, reduce and eliminate unsustainable patterns of production and consumption.
4.	Convention on Biological Diversity, 1994 Web Link: https://www.cbd.int/	Pakistan signed this treaty in 1992 and it was ratified by cabinet in 1994.	The Convention on the Biological Diversity (CBD) has three main goals: Conservation of biological diversity (or biodiversity); sustainable use of its components; and fair and equitable sharing of benefits arising from genetic resources.

2.9 Institution Responsible for Planning, Policies and Regulations

2.9.1 Environmental Protection Agency, Punjab

Implementation of Punjab Environmental Protection Act 1997 (Amended 2012, 2017 & 2022) is the mandate of the Punjab-EPA. Punjab-EPA is headed by a Director General, and sections are headed by Directors, i.e., Director EIA, Technical, Director Administration and Finance, and Director Laboratory. Punjab-EPA has established District Environment Offices at district level.

As the proposed Project falls in 16 different Tehsil of Punjab, therefore, Punjab-EPA will be responsible for reviewing the reports, issuing environmental approval and overall monitoring of the proposed project activities.

3 PROJECT DESCRIPTION

The Punjab Rural Sustainable Water Supply and Sanitation Project (PRSWSSP) is being implemented across 2,000 villages in 16 tehsils of Punjab with support from the World Bank. ECNEC authorized PRMSC to initially execute the Project in 200 villages as a pilot phase (Annex-1) to assess its feasibility and long-term sustainability. With the pilot phase successfully completed, the Project is now progressing toward the remaining 1,800 villages. This ESMP specifically covers 232 villages located in 08 tehsils under Phase-1.

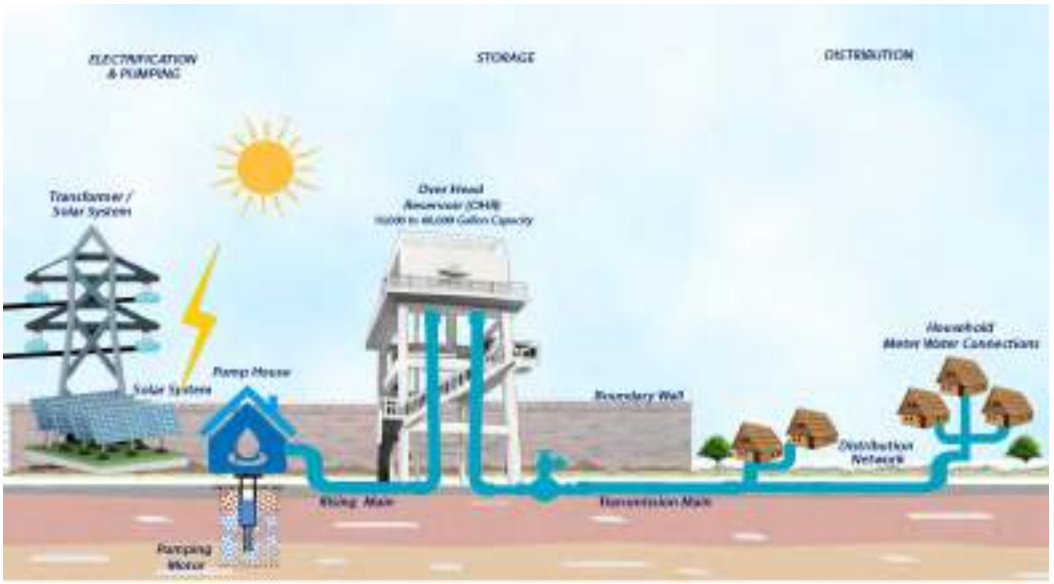

Figure 1: Illustrating Project Intervention in Component 1 Sub Component 1.2

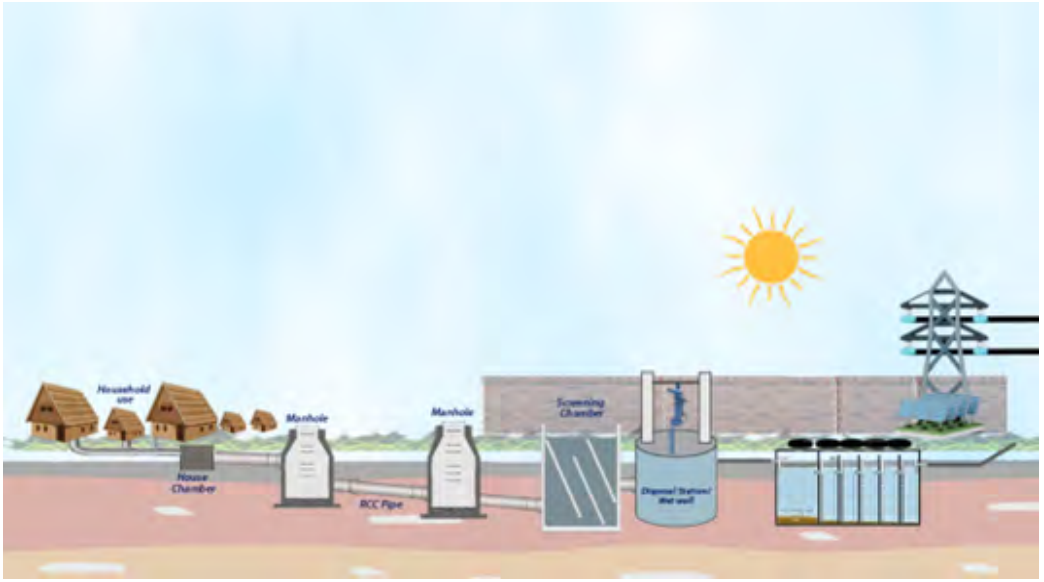

Figure 2: Illustrating Project Inventions in Component 1 Sub Component 1.1

Project components are briefly described below:

COMPONENT 1: Water Supply and Sanitation Infrastructure Development

Component 1 will fill the infrastructure gap in the existing traditional rural Water Supply and Sanitation (WSS) systems that underlies the low access to safely managed water and sanitation in rural Punjab.

. **Subcomponent 1.1: Sanitation Infrastructure Development.**

This subcomponent will focus on fecal sludge collection, transference, treatment and disposal.

 Sub-component 1.2: Water Supply Infrastructure Development

The study on technology options and their feasibility informed the choice of technology for water abstraction, treatment, and conveyance.

COMPONENT 2: Behavior Change and Capacity Development

This component will finance activities that facilitate and induce health protective behavior change and build community capacity to support WSS service delivery.

 Subcomponent 2.1 Awareness raising and behavior change related to safe WASH practices

The project will support basic hygiene, small-scale infrastructure to directly promote good hygiene practice and

 Subcomponent 2.2: Training and Capacity Building of Village-level Institutions

Trainings will target village-level institutions that have a defined role in water and sanitation service provision. These will be complemented by household behavior change but are distinct, in that they will build the capacity of informal village level organizations to perform tasks that both complement and the O&M responsibilities assigned to Service Delivery Units (SDU).

COMPONENT 3: Service delivery Improvement

 Subcomponent 3.1: Establishing institutions and building capacity for service delivery

The service delivery model of the project consists of three tiers: (i) a provincial SDU head office that has functions of both, the Project Implementation and Management Unit (PIMU) as the implementing body of the project and a public-owned section 42 company. (ii) Tehsil level units that are on frontlines of service delivery; and (iii) Community Caretakers and Operators (CCO) that may be part of Village Councils, Village Organizations, or just village residents.

 Subcomponent 3.2: Solid Waste and Animal Waste Management

Promoting the safe handling of solid waste is an integral aspect of the design of this project

- **Subcomponent 3.3: Water Quality Monitoring**

  The project will support a transition in Punjab towards regular and frequent water quality monitoring in rural areas for both drinking water supply and wastewater.

COMPONENT 4: Project Management and Monitoring

- **Subcomponent 4.1: Project Monitoring through a customized Management Information System**

  The project will develop and use a comprehensive IT based Management Information System (MIS) to track project implementation progress, WSS service delivery performance, the flow of public and donor funds earmarked for WASH and related financial management information, and outcome indicators.

- **Subcomponent 4.2: Strengthening of Project Implementation and Management Unit (PIMU)**

  The key implementation tier will be the Project implementation and management unit (PIMU), which will be associated with the Department of Local Government and Community Development (LG&CD) – the implementing agency - and led by a full-time Project Director.

PRMSC has divided the 16 tehsils into 5 zones based on geographical location and accordingly hired the services of 5 Engineering Design and Supervisory Consultants (EDCS) for the proposed project. Under Phase-1, interventions are planned across 8 tehsils, within which 232 villages have been identified for implementation. In order to fast track the project implementation and execution of the civil works, PRMSC with the help of consultants has divided 1800 pilot villages from sixteen different tehsils into 5 packages for designing and provision of Water Sanitation and Hygiene (WASH) facilities. This document pertains to 232 villages selected in Phase-1 from 8 different tehsils. The subproject involves provision of water supply, sewerage, overhead tanks and Pumping stations with sewage treatment plants in all 232 villages.

3.1 Need and Purpose of Project

The underlying issues related to water supply and sewerage in the target villages are summarized below:

Water Supply Issues:

- No water supply Network in the villages;
- Most of the household use shallow groundwater;
- Shallow ground water is not fit for drinking;
- Polluted drinking water is causing water borne diseases.

Sewerage Issues:

- Properly designed sewerage system does not exist in most of the villages;
- Existing open drains are damaged and do not cover the entire settlements;

- No proper disposal Point in all the villages;
- Sewage collected in soakage pits and open plots seeps into ground and contaminates groundwater;
- Raw sewage ponds are a breeding ground for disease vectors.

Solid Waste Issues:

- There is no proper solid waste management system and designated dumping sites in the project area, locals usually throw their waste into open plots or streets.
- There are heaps of waste which attract rodents, flies and disease vectors.
- Organic waste is usually burnt by the villagers, which causes health issues.
- Open drains are used as a garbage/solid waste disposal point thus resulting in decrease of water carrying capacity of these drains.
- During rain, storm water and sewage overflow from the drains and spread solid waste through the area thus causing nuisance, environmental issues and spread of diseases.

3.2 Project Location

Table 2 in section 01, indicates the cluster, district and tehsils of Phase -1 villages to understand the geographical location of the project. A map of project locations in relevant

tehsils is shown in Figure 1.

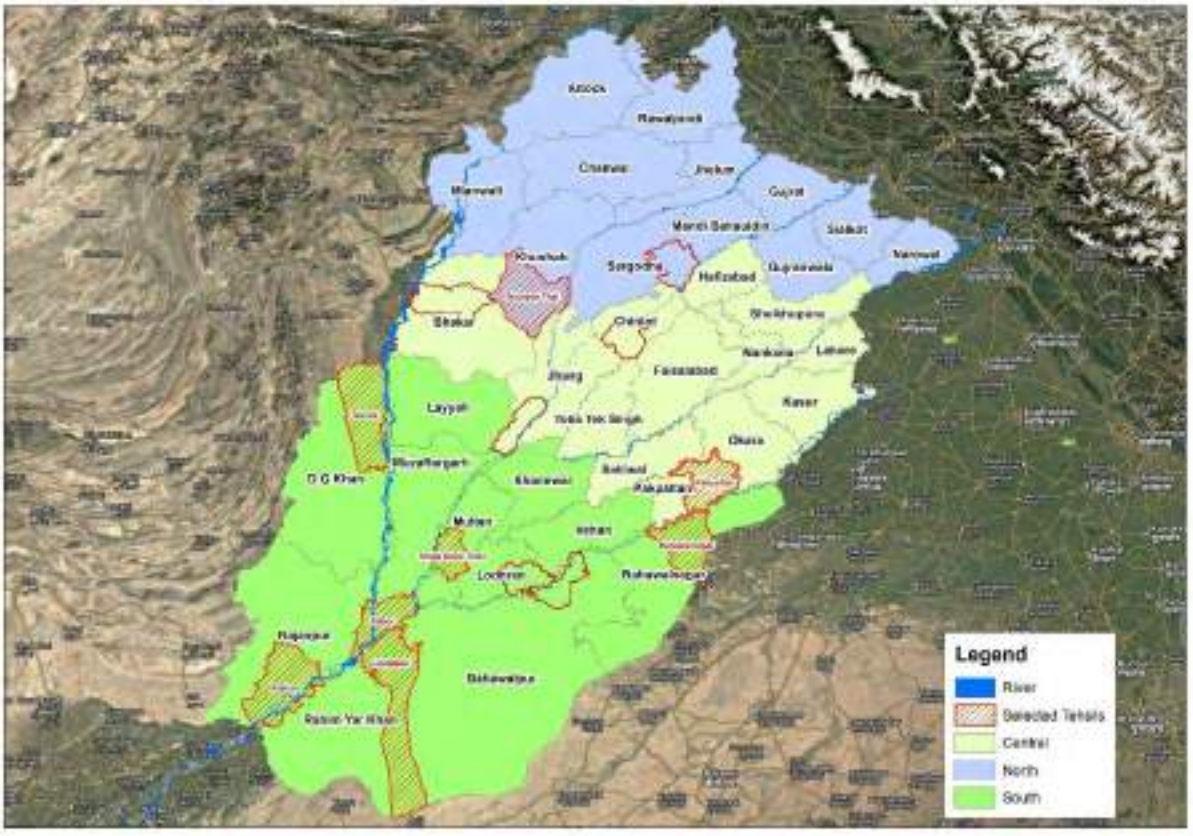

Figure 3: Location Map of Project Area

3.3 Objectives of Project

The project development objective is to provide equitable and sustainable access to safely managed water and sanitation and reduce child stunting.

3.4 Project Description

3.4.1 Existing System

The existing water and sewerage situation of the village is given below.

A. Existing Water Supply System

There is no existing functional water supply system in any of the Phase-1 villages hence no water supply network exists here. At present, domestic boreholes are the main water source for the village which is available at a depth of around 50-75 ft. Deeper tube wells at depth of around 150 ft are also bored which are used for irrigation purposes. People bring drinking water from deep boreholes (outside of the village or even from nearby villages) if their village have brackish groundwater (i.e., Shujabad, Bahawalnagar, Noorpur Thal). Where the sweet water is available people collect water from deep borehole within their villages. Many villagers perceive that this water is unhygienic which results in major waterborne diseases like hepatitis, cholera and diarrhea.

B. Existing Sewerage System

There is no existing sewerage pipe network or disposal station in the villages. The sewerage system is totally based on open drains of varying sizes and capacities. The sewage is first collected in house collection chamber (soakage pits), which is then carried through existing open channels, drains and ultimately dispose of into nearest sewage pond and fields. Some of this sewage is also used to irrigate nearby crops/farmlands through water courses.

A sewage pond exists in each village which is used as a main sewage recipient. Most of the drain's direct sewerage into this pond and rest of the drains after collecting sewage from the adjacent areas disposed of into nearest fields haphazardly.

C. Existing Solid Waste

Solid waste management system and designated dumping sites are not available in the project area. The waste is usually dumped in the streets, agricultural fields or open plots. The heaps of waste cause nuisance and the situation gets worse during rainy season. The organic waste is burnt to meet the fuel demands in the kitchens. Glimpses of existing conditions are shown in **Annexure-3.**

3.4.2 Proposed System

Summary of Proposed Water Supply and Sewerage Components are presented tehsil-wise in the table 6.

Table 6: Summary of Proposed Water Supply and Sewerage Components

Description	Unit	Total
Tehsil Noorpur Thal		
Length of Distribution Network (Ø6")	ft	44477
Length of Distribution Network (Ø4")	ft	23905
Length of Distribution Network (Ø3")	ft	72499
Proposed Drainage Network (10" x 12")	ft	96395
Proposed Drainage Network (12" x 12")	ft	78285
Proposed Drainage Network (15" x 12")	ft	97474
Proposed Sewer Network (Ø12")	ft	234087
Tehsil Rojhan		
Proposed No. of Tubewells (0.30 Cusecs)	No.	1
Proposed No. of Tubewells (0.50 Cusecs)	No.	3
Length of Distribution Network (Ø 6")	ft	7358
Length of Distribution Network (Ø 5")	ft	8406
Length of Distribution Network (Ø 4")	ft	2464

Description	Unit	Total
Length of Distribution Network (Ø 3.5”)	ft	40159
Proposed No. of OHWT (10,000 gallons)	No.	1
Proposed Drainage Network (6” x 6”)	ft	89795.6
Proposed Drainage Network (8” x 8”)	ft	6227
Tehsil Liaqatpur		
Proposed No. of Tubewells (0.25 Cusecs)	No.	4
Proposed No. of Tubewells (0.30 Cusecs)	No.	2
Proposed No. of Tubewells (0.50 Cusecs)	No.	24
Length of Distribution Network (Ø 8”)	ft	132
Length of Distribution Network (Ø 6”)	ft	23964
Length of Distribution Network (Ø 5”)	ft	16546
Length of Distribution Network (Ø 4”)	ft	84838
Length of Distribution Network (Ø 3.5”)	ft	353611
Proposed No. of OHWT (10,000 gallons)	No.	5
Proposed Drainage Network (6” x 6”)	ft	986957.3
Proposed Drainage Network (8” x 8”)	ft	45067.5
Tehsil Alipur		
Tube Wells (Nos.)	No.	10
OHR (Nos.)	No	6
OHR Capacity (Gallons)	No.	10000
Stand Posts (Nos.)	No.	41
Septic Tanks (Nos.)	No	157
Tehsil Shujabad		
Tube Wells (Nos.)	No.	2
OHR (Nos.)	No	1
OHR Capacity (Gallons)	No.	10000
Stand Posts (Nos.)	No.	22
Septic Tanks (Nos.)	No	98
Tehsil Taunsa		
Tube Wells (Nos.)	No.	3

Description	Unit	Total
OHR (Nos.)	No	3
OHR Capacity (Gallons)	No.	10000
Stand Posts (Nos.)	No.	42
Septic Tanks (Nos.)	No.	110
Tehsil Pakpattan		
Tubewell – 0.05 cusec	No.	10
Tubewell – 0.10 cusec	No.	12
Stand Post – Type I	No.	01
Stand Post – Type II	No.	17
Drain Type-1 (0.83' x 1')	Rft	88,733
Sullage Carrier (1.5' x 1.5')	Rft	33,341
Sullage Carrier (2' x 2')	Rft	100
Brick Soling	Sft	414,958
Tuff Pavers	No.	163,709
Sewage Pump	No.	19
Septic Tank – Type I	No.	05
Septic Tank – Type II	No.	07
Septic Tank – Type III	No.	07
Septic Tank – Type IV	No.	07
Septic Tank – Type V	No.	01
Septic Tank – Type VI	No.	01
RO Eject Pump	No.	03
Tehsil Bahawalnagar		
Tubewell – 0.05 cusec	No.	18
Tubewell – 0.15 cusec	No.	01
Tubewell – 0.1 cusec	No.	01
Stand Post – Type-I	No.	09
Stand Post – Type-II	No.	10
Stand Post – Type-III	No.	01
Stand Post – Type-VII	No.	01

Description	Unit	Total
Proposed Rising Main (90mm) from Tube-well to Stand-Post Type-I	Rft	41,875
Proposed Rising Main (110mm) from Tube-well to Stand-Post Type-I	Rft	5,286
Drain Type-1(0.83' x 1')	Rft	64,874
Sullage Carrier (1.5' x 1.5')	Rft	22,468
Brick Soling	100 Cft	302,852
Tuff Pavers	Sft	120,105
Septic Tank – Type I	No.	05
Septic Tank – Type II	No.	08
Septic Tank – Type III	No.	03
Septic Tank – Type IV	No.	01
Septic Tank – Type V	No.	01
Septic Tank – Type VI	No.	01
Sewage Pump	No.	02
RO Eject Pump	No.	19

A. Water Supply System

The project aims to improve the existing drinking water problems through provision of properly treated water as per World Health Organization (WHO) guidelines through metered pipe supply network. The project will help to reduce the water consumption as company plans to charge tariff on the basis of volumetric consumption. This project will also help to discourage the installation of wells in individual households. A comprehensive Behaviour Change Capacity is one of the components of the project in which residents of the villages will be sensitized on the importance of water conservation. Moreover, it is expected the provision of safe drinking water at door step will help to improve the socio-economic conditions of the society by curbing the medical expenses and saving of time required to fetch water. Moreover, the man-hours lost due to illness caused by the water borne diseases can be reduced. PRMSC has hired services of Independent third party PCRWR (Pakistan Council of Research for Water Resources) to ensure the water quality through frequent testing of the treated water at end of treatment train as well as point of use.

Water supply system can be characterized by following main components:

- Water Source
- Distribution System

Water Source

Number of tube wells for water supply system are proposed after assessment of total water demand of the project areas and where sustainable ground resources are available. The design criteria for tube wells are discussed in the following sections;

Design Criteria for Tube wells

An appropriate well design is a blend of hydraulic and economic efficiencies of the tube well over its life span. It includes the selection of the depth, diameter, construction materials (well casings, screens, filter pack etc.), pump and prime mover in consonance with the local hydro-geological conditions and the design capacity. All these major factors depend upon the "design capacity" which in turn is governed by the aquifer's geometry and parameters.

Capacity of the tube well is based upon the maximum day water requirements, for the served area, with design operational duration (working hours) of 12 hours per day.

In order to design the well, the following major factors are considered:

- Design, construction details, water quality of the existing tube wells;
- Depth to water table under existing and future conditions;
- Groundwater quality;
- Aquifer parameters.

Pumping Facilities

Pumps are devices used to transfer water (or other liquids) from point A to point B with pressure to overcome the resistance along its path. It is important to understand the different types of pumps, their applications, design differences and the procedures used to operate and maintain them.

Water Transmission System

The transmission system's function is to transport water from source to the reservoir, if any, and to the distribution point. Water conduits for the transmission system may be canals, aqueducts or tunnels, free-flow pipelines, or pressure pipelines. The transmission of water is either under gravity or pumping. Pressure pipeline is generally the type of water conduit used for water supply transmission systems.

Water Reservoirs

In distribution systems, whether water is obtained by gravity or by pumping, distribution reservoirs are usually necessary for the following reasons:

- To balance the supply and demand in the system. In small distribution systems, variations in demand may be three or more times the average hourly consumption.
- To maintain adequate and fairly uniform pressure throughout the distribution system.
- To avoid the total interruption of water service when repairing pipes between the source of supply and the reservoir.

- To allow pumps to be operated uniformly throughout the day. Such pumps may be much smaller than would otherwise be required.

Overhead Water Reservoir (OHR)

Overhead Reservoirs (OHRs) are also key component of water distribution system. In water supply system OHRs serve the following functions:

- Store water for use during electric load-shedding and during maintenance works of tube-wells/ pumps.
- Provide balancing of flow and pressure during peak hours.

As per “Technical and Service Delivery Standards for Water Supply and Sanitation Sectors” Storage Capacity of Overhead reservoirs should be based on around 1/6th of average day demand.

Water Distribution System

The purpose of a distribution network is to distribute the potable water from the storage reservoir over the area to be provided, and deliver it to the individual consumer in such a way that at any tap point and at any time sufficient water of good quality can be withdrawn.

Looped System

A distribution network is looped when there are only few or no pipe dead-ends, such that water can move through the system freely. The advantages of a looped system are;

- The lower water velocities in the main reduce head losses, resulting in greater capacity.
- Ma in breaks can be isolated, minimizing serv ice interruptions to consumers.
- Usually, better chlorine residual content is achieved.

Stand Post

The function of the standpost system is to deliver potable water from the distribution network to the public through fixed tapping points. Standposts serve as communal outlets where consumers can conveniently collect water for domestic use. They are typically located at accessible points within residential clusters to minimize walking distance. Each standpost is designed to provide an adequate and controlled flow rate to meet community demand. The system ensures equitable water distribution, promotes hygiene, and supports communities without individual household connections.

B. Sewerage System

The sewerage system of these villages has been designed so that the final disposal of collected sewage should be in the proposed pumping station. This pumping station will pump sewage into Anaerobic Baffled Reactor (ABR). After treatment, treated effluent complying with PEQS, would be discharged into existing nearby sewerage pond or community owned water courses. The sewerage systems have been designed for design year of 2050. Design criteria and consideration are briefly discussed below:

Design Criteria

The design criteria are based on Standards set forth under the Water and Sanitation Agency (WASA), Lahore criteria and past design experiences of similar projects.

The main objectives of the design criteria are as follows:

- To develop a sewerage system, that can be operated with minimum operation and maintenance cost;
- To collect sewage efficiently and safely to prevent diseases and nuisance; and
- To proposed efficient treatment system which will deliver an effluent that will meet the Punjab Environmental Quality Standards (PEQS)

Sewage Flow Estimation

The most fundamental factor for planning and designing sewerage systems is the estimation of the sewage flow. Otherwise, sewers may prove inadequate resulting in overflow or may prove too large in diameter, which may make the system uneconomical and hydraulically inefficient. For the project area, **80%** of the water demand has been taken as sewage generation.

Peak Factor & Flow

The capacities of the sanitary sewer are sufficient to carry peak flows, rather than the average flow because the rates of flows for any design point will vary substantially depending on the local water use customs, climate conditions, the day of the week, the hour of the day etc. So, waste water collection system has been designed to handle peak flows. The peak flow will be calculated by following formula:

Peak flow = Avg. daily flow * Peak factor

Peak Factor depends upon the population; it decreases with an increase in population. Peak Factor shown in the Table below will be taken for the computation of peak flows;

Population	Peak Factor
Up to 5,000	4.50
5,000 to 10 ,000	4.00
10,000 to 25,000	3.50
25,000 to 50,000	3.00
50,000 to 100,000	2.50
More than 100,000	2.00

Non-Domestic Sewage Flow

The non-domestic sewage flow has been taken as 80% of average non-domestic water consumption that will cover institutional, commercial and small industrial discharges.

Infiltration Rate

This is additional quantity due to groundwater seepage in to sewers through faulty joints or cracks formed in the pipes. The quantity of the water depends upon the height of the water table above the sewer invert level and permeability of the ground soil. If water table is well below the sewer invert level, the infiltration can occur only after rain when water is moving down through soil.

PHED Criteria has been followed for infiltration rate for the selected localities of the project area.

Storm Water Allowance

Keeping in view the project area, 33% of peak sewage flow has been taken as storm water allowance.

Total Sewage Flow

Total sewage flow is the sum of all the above flow and sewers / conduits has been designed on this total sewage flow.

Total flow = Peak sewerage flow + Infiltration + Storm water Allowance

Manholes

Manholes will be located according to conventional sewer network design i.e., starting point, junctions between sewers and change in direction and grades etc.

Following manhole spacing are adopted for the design of sewerage system;

Table 7: Manhole Spacing

Pipe Size	Interval
9 inches	50 Feet
12 inches	100 Feet
15 inches	150 Feet
18 inches	200 Feet
24 inches	250 Feet
30-42 inches	250 Feet
48-60 inches	250 Feet
Above 60 Inches	250 Feet

Following manholes dimensions are adopted for sewerage systems of project area;

Table 8: Manhole Diameter

Sewer Size	Manhole Internal Diameter
9-18 inches	04 Feet
24-30 inches	05 Feet
36-42 inches	6.5 Feet

Sewer Size	Manhole Internal Diameter
48-54 inches	7.5 Feet
60-66 inches	8 Feet
72 inches	9 Feet

Change in Sewer Diameter in Manhole

To minimize the risk of blockage in sewers, the diameter of the outgoing sewer is not less than the diameter of the largest incoming sewer. The top of smaller sewers entering a manhole will normally be at the same level as that of the outgoing sewer.

Slope of Channel Within Manhole

All manhole invert levels used in the sewer calculations has been the centre of the manhole and all distances and slopes has been calculated between canters of manholes.

Drop Manholes

The drop connections to manholes have been provided if the difference in pipe invert level is greater than 3.0 ft otherwise no drop manholes will be provided.

Manhole Steps

Ductile Iron and Malleable Cast iron steps etc. are usually used in the manholes. Keeping in view the project area and current practices malleable cast iron steps shall be used in the manhole.

Sewage Disposal Stations

Sewage lift / pump station is required to pump sewage collected from various sewage zones to the disposal point. The details of Sewage lift / pump station will be discussed in the following sections.

The pumping station consists of following structures:

i) One screen chamber (Two partitions)

ii) One Wet well (Two partitions)

iii) One Dry well

iv) One valve chamber

Pumps (working + standby) are proposed in dry well having capacity varying from 0.1 to 0.5 cusec depending on the volume of sewerage produce in the village. The sewage will be treated in ABR from where this treated effluent will be disposed into existing water course.

Anaerobic Baffled Reactor (ABR)

Proposed Sewage Treatment plant consists of Screening Chamber, Wet Well, Dry Well with Pumping Machinery and Sewage Force main up to Proposed STP. Anaerobic Baffled Reactor (ABR), which has chambers divided by baffles, provides a mechanism for both primary and secondary sedimentation. The majority of solids are removed by the ABR's first

chamber, which also has low sludge formation and high SRT. The bulk of shock loads may be handled by the technology with ease. The system's ease of construction makes it perfect for wastewater treatment. The anaerobic process reduces the formation of sludge biomass, the particles in the effluent are reduced due to significant sedimentation in the baffled chambers, and most importantly, the ABR has lower capital and operating costs than aerobic processes. Another significant benefit is that this technique works best in semi-arid and tropical environments.

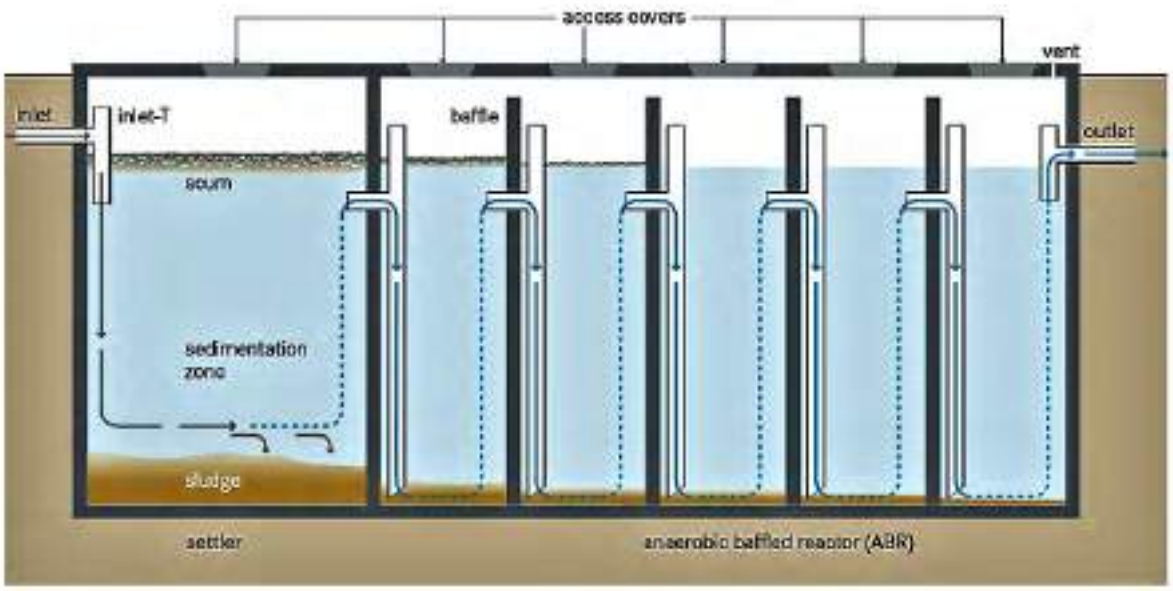

Figure 4: Process Flow Diagram of STP / WWTP / ABR

3.5 Land Acquisition

The laying of piping network for water supply and sewerage system will not require land acquisition, as the pipeline will be buried underground. The network will be designed in a manner that the pipeline is laid along the public roads / streets. However, if pipeline route is required to pass through any private lands, special permission for laying and periodic maintenance shall be sought from the landowners.

The land required for the construction of overhead tank, pumping station and STP will consist of state land, acquired through process of No Objection Certificate (NOC). In cases where private land is needed, it shall be obtained through Voluntarily Land Donation (VLD). Village wise breakup of land requirements given in **Table 9.** As is obvious from the table, state land is mostly available in villages called “Chak”. During British Raj, new canals were built to bring the barani areas under cultivation by introducing the irrigated areas around the core of new villages called *Chak*. As sufficient state land is available in these villages (Chaks), therefore NOC process was adopted. Whereas in other villages government land is not available hence private land, donated by community members through VLD procedure, shall be used.

However, land through VLD is only obtained after satisfying the set criteria: first, that the state land is not available in the proposed village; second, when state land in the village is not technically viable – based on requirements of engineering design – for the construction of infrastructure; third, only after meeting the VLD Screening Checklist criteria attached as Annexure-9A.

Table 9: Land Requirement Details

Sr. No.	Tehsil	Revenue Villages	Private Land required through VLD (in Marla)	State Land required through NOC (in Marla)
1	Noorpur Thal	Rakh Dhammak	3.50	---
2		Rakh Bambool	2	---
3		Shergarh	14.70	---
4		Daravi	20.04	---
5		Chak No 020/M.B	20.68	2.5
6		Burhan	19	---
7		Rakh Baland	20.54	---
8		Chak No 018/M.B	17.43	10
9		Kaka	24.96	---
10		Sidha	16.96	10
11		Palohan	19.93	---
12		Chak No 019/M.B	20.68	12
13		Laghari	29.15	8.5
14		Mahmood Shaheed	33.91	10
15		Khai Kalan	46.35	
16		Jaura Kalan	61.45	
17		Khai Khurd	34.70	
18		Shah Hussain	14.5	7
19		Rakh Shah Hussain	3.5	
20		Rakh Tahla Khatwan	5.07	
21		Adhikot	36.72	16.54
22		Chan	27.86	10.05
23		Chak No 035/M.B	7	
24		Chak No 036/M.B	5.15	
25		Nakro Shaheed	13.74	
26		Chak 13	3.5	
27	Liaqatpur	Ahmed Yar	3.7	1.92

Sr. No.	Tehsil	Revenue Villages	Private Land required through VLD (in Marla)	State Land required through NOC (in Marla)
28		Arif Baloch	20.19	
29		Chak 315 / 6R	6.83	0.4
30		Chak 316 / 6 R	6.97	0.4
31		Chak 317/6R	9.20	1.0
32		Chak 08 Abbasia	19.58	0.48
33		Chak 09 Abbasia	7.87	1.44
34		Chak 11 Abbasia	24.12	-
35		Chak 12 Abbasia	9.05	0.48
36		Chak 313/6R	6.83	0.5
37		Chak 134 NP	13.87	0.48
38		Chak 135 NP	3.70	0.48
39		Chak136 NP	5.65	0.48
40		Chak 139 NP	9.32	0.96
41		Chak 140 NP	5.66	0.48
42		Chak 143 Abbasia	17.36	0.48
43		Chak 144 Abbasia	7.26	0.48
44		Chak 145 Abbasia	5.30	0.48
45		Chak 147 / 5R	10.48	0.48
46		Chak 148 / 5R	6.83	0.48
47		Chak 150 Abbasia	6.75	0.48
48		Chak 152 / 7R	9.22	0.48
49		Chak 153 / 7R	9.05	0.48
50		Chak 154 / 7R	9.22	0.48
51		Chak 155 / 7R	9.49	0.48
52		Chak 156 / 7R	9.49	0.48
53		Chak 157 / 7R	14.38	0.48
54		Chak 159 / 7R	6.08	0.48
55		Chak 174 / 7R	7.66	0.48
56		Chak 175 / 7R	13,18	0.48
57		Chak 177 / 7R	5.49	0.48
58		Chak 178 / 7R	6.14	0.48
59		Chak 179 / 7R	5.73	0.48

Sr. No.	Tehsil	Revenue Villages	Private Land required through VLD (in Marla)	State Land required through NOC (in Marla)
60		Chak 180 / 7R	9.19	0.48
61		Chak 182 / 1L	3.56	0.48
62		Chak 183 / 7 R	7.39	0.48
63		Chak 186 / 7 R	4.76	0.48
64		Chak 19 Abbasia	25.53	-
65		Chak 191 / 1L	3.83	0.48
66		Chak 194 / 1L	11.48	0.48
67		Chak 195 / 1L	5.49	0.48
68		Chak 20 Abbasia	11.90	-
69		Chak 22 Abbasia	7.12	0.48
70		Chak 23 Abbasia	14.03	0.98
71		Chak 28 Abbasia	3.56	0.48
72		Chak 31 Abbasia	5.66	1.48
73		Chak 32 Abbasia	31.66	4
74		Chak 33 Abbasia	8.94	0.48
75		Chak 36 Abbasia	6.21	0.48
76		Chak 37 Abbasia	19.72	-
77		Chak 38 Abbasia	10.30	0.48
78		Chak 39 Abbasia	11.52	1.0
79		Chak 3 A	9.32	0.48
80		Chak 40 Abbasia	9.09	0.48
81		Chak 41 Abbasia	11.0	0.48
82		Chak 42 Abbasia	16.32	-
83		Chak 43 Abbasia	29.67	-
84		Chak 46 Abbasia	11.46	0.48
85		Chak 47 Abbasia	14.54	-
86		Chak 48 Abbasia	10.98	0.48
87		Chak 4 A	3.83	0.96
88		Chak 63 Abbasia	19.37	-
89		Chak 64 Abbasia	7.12	0.48
90		Chak 65 Abbasia	15.38	0.98
91		Chak 68 Abbasia	15.67	0.98

Sr. No.	Tehsil	Revenue Villages	Private Land required through VLD (in Marla)	State Land required through NOC (in Marla)
92		Chak 69 Abbasia	4.97	0.48
93		Chak 75 Abbasia	17.39	-
94		Chak 77 Abbasia	17.94	-
95		Chak 78 Abbasia	14.8	0.48
96		Chak 79 Abbasia	14.91	4.0
97		Chak 80 Abbasia	12.16	-
98		Chak 81 Abbasia	18.13	-
99		Chak 82 Abbasia	7.14	-
100		Chak 83 Abbasia	9.26	4.0
101		Chak 84 Abbasia	15.27	1.44
102		Chak 85 Abbasia	19.24	-
103		Chak 86 Abbasia	8.46	1.5
104		Chak 87 Abbasia	41.68	4.48
105		Chak 88 Abbasia	22.51	1.0
106		Chak 89 Abbasia	5.32	0.48
107		Chapri Chatan Shah	5.66	0.48
108		Gulshan Farid	17.27	0.98
109		Hayat Lar	20.41	0.4
110		Kanjki Wala	22.79	1.44
111		Kotla Daraigh	22.35	2.4
112		Kotla Khairay Khan	7.27	0.48
113		Muradpur Sail	29.63	2.8
114		Taranda Gurgujj	43.43	2.4
115		Turkary	65.05	5.9
116		Firoza	17.2	0.96
117	Rojhan	Bhagsar	28.91	4
118		Basti Dhora	9.49	0.4
119		Gianmal	39.7	2.4
120		Dilber	22.24	2.4
121		Qadra Kass	5.49	0.48
122		Kotla Hasan Shah	6.94	0.4
123		Rakh Qadra	39.72	2.4

Sr. No.	Tehsil	Revenue Villages	Private Land required through VLD (in Marla)	State Land required through NOC (in Marla)
124		Mutafriq Mazari	-	0.98
125		Rakh Sabzani	5.37	0.48
126		Safdar Abad	-	1.44
127		Salim Abad	17.36	2.44
128		Tariq Abad	-	1.44
129	Bahawalnagar	Bonga Ihsan Bibi	13	-
130		Hasan Raika	24	-
131		Bhole Shah Hitar	20	-
132		Paran Wala	16	-
133		Chak Abdul Haq	-	22
134		Dhanraj Pura	21	
135		Jagga Santteja & Mini Sanatteka	-	47
136		Mosla	17	-
137		Pir Sikandar Otar	20	-
138		Jhulan Chistian	-	12
139		Ghouspur	12	-
140		Amin Abad	34	-
141		Abrarah Uttar	16	-
142		Ali Gohar No. 326	06	-
143		Ramnagar	30	-
144		Hussain Abad Uttar	17	-
145		Hussain Abad Hithar	06	-
146		Gaman Dongi	15	-
147		Sharaf Din	-	12
148	Pakpattan	Chak No. 102/D	18.5	-
149		Chak No. 87/D	17	-
150		Bahwan Shah	16	-
151		Chak Ilahi Bux	28	-
152		Chak Murad Khan	27	-
153		Chak Nazam Din	19	-
154		Gobinc Pur Bahmni	16	-

Sr. No.	Tehsil	Revenue Villages	Private Land required through VLD (in Marla)	State Land required through NOC (in Marla)
155		Jand Wala	-	18
156		Nahla Abad	17	-
157		Dhamiana	20	-
158		Chak No. 4SP	19	-
159		Chak Qudar Tullah	-	-
160		Chilli Mamdana	29	-
161		Dada Ahluka	19	-
162		Ghar Taj	21	-
163		Ghazi Mardan	26.5	-
164		Nura Ahlukha	19	-
165		Arazi Tek Chand	28	-
166		Ghuri	27	-
167		Chak 103/D	19	-
168	Alipur	Baqar Shah Shumali	66	-
169		Bande Shah	38	-
170		Maqwal Hadeir	68	-
171		Nehal Wala	12	-
172		Nauhabad	6	-
173		Khayara	2	-
174		Mithan Wali	70	-
175		Ali Wali	70	-
176		Kotla Agar	18	-
177		Makhan Bela	30	-
178		Bet Barrah	18	-
179		Marian	10	-
180		Bet Mir Ahmad Jamal	2	-
181		Kotla Ghulam Shah	16	-
182		Sirki	14	-
183		Tibba Barrah	14	-
184		Bet Bagh Shah	14	-
185		Yare Wali	36	-
186		Kohar Faqiran	40	-
187		Kotla Afghan	8	-
188		Gagare Wali	48	-
189	Shujabad	Wahi Riki	16	-

Sr. No.	Tehsil	Revenue Villages	Private Land required through VLD (in Marla)	State Land required through NOC (in Marla)
190		Basti Dad	24	-
191		Chah Miran Khan	22	-
192		Nawan Chak	32	-
193		Mohan Pur Sharqi	24	-
194		Sangrai	18	-
195		Shahpur Ubha	70	-
196		Sarai	12	-
197		Shah Pur Shumali	32	-
198		Nasir Pur	30	-
199	Taunsa	Aqupur	8	-
200		Arakhar Dao	2	-
201		Rind Wala	20	-
202		Baghon Wala	2	-
203		Bakhri	2	-
204		Basti Habib	2	-
205		Basti Nasir	2	-
206		Basti Usman Shah	58	-
207		Berand	6	-
208		Bet Obai	2	-
209		Bodo Mian	10	-
210		Chak Sohanra Bacha	8	-
211		Domra Janubi	10	-
212		Domra Shumali	16	-
213		Ghadi Sandila	2	-
214		Ghali	12	-
215		Jalal Khan	12	-
216		Jhok Chhapri	16	-
217		Jhok Mangla	18	-
218		Jhok Rohal	6	-
219		Jhok Yaran	2	-
220		Jinpur	6	-
221		Khitran Wala	18	-
222		Kotla Marrani	2	-
223		Rakh Sanjar	8	-
224		Rakh Zor	8	-
225		Wani	10	-
226		Mahnda	40	-

Sr. No.	Tehsil	Revenue Villages	Private Land required through VLD (in Marla)	State Land required through NOC (in Marla)
227		Mirkhar	12	-
228		Mundrani	50	-
229		Pukan	8	-
230		Rakh Mari Pachaudi	12	-
231		Langah	2	-
232		Rakhana	2	-
Total			**3779.55**	**290.11**

Note: The total 3779.55 Marla land is required through VLD, whereas 290.11 Marla land is required through NOC. Similar to the trend observed in pilot phase, more area of land is being obtained through VLD because:

1. Suitable state land was not available in most of these villages;
2. In Phase-1 villages, the requirement of land for the installation of solar panels – for reduction of O&M cost for ensuring sustainability– has also been foreseen. However, due diligence has also been conducted to ensure that the socio-economic impacts of VLD are negligible.

Furthermore, the size of land required in different villages vary depending upon the population, water requirement, size of OHR, size of ABR, size of solar panel solutions and volume of sewerage generated.

3.6 Project Administrative Jurisdiction

The proposed project falls under the jurisdiction of Deputy Commissioners of relevant tehsils of province.

3.7 Project Implementation Schedule

The project will take 10 months in each village from start to finish. The commencement is scheduled simultaneously in March 2026.

3.8 Construction Activities and Required Machinery

Construction activities involve following:

- Earth work
- Structure/ Concrete works
- Pipe laying

Table 10 presents the list of expected machinery required for construction. The number of these machines will be finalized with the detailed design of the proposed road:

Table 10: List of expected Machinery/Equipment

1	Mobile Crane	15	Jack Hammer

2	Dumpers	16	Plate Compactor
3	Road/Power Roller	17	Wood Shuttering
4	Light Weight Compactor	18	Formwork
5	Ramming Machine	19	Steel Cage Shuttering Unit
6	Water Sprinkler and Water Tanker	20	Motor graders
7	Excavator	21	Generators
8	Tractor with Front Blade and Trolley	22	Welding Plant
9	Loader	23	Transit Mixer
10	Road Cutter	24	Vibrators
11	Pneumatic Tyred Roller (PTR	25	Scaffolding
12	Tandem Roller	26	Light Transport
13	Concrete Mixer Machine	27	Mini/ Hand Roller
14	Tower Crane	28	Barricades

3.9 **Construction Camps**

Camp sites will be selected based on following considerations:

- Number of workforces deployed;
- Type and quantity of machinery mobilized;
- Availability of adequate area for establishing camp sites including parking areas for machinery, stores and workshops;
- Access to communication and local markets;
- Appropriate distance from sensitive areas including settlements and religious and/or cultural facilities.

Final locations will be selected by the contractor with the assistance of Supervision Consultant. A centralized construction camp will be preferred in tehsils where villages are geographically in close proximity; this will result in resource efficiency and better monitoring of construction activities. Care will be taken to safeguard the existing environment of the area and location shall be selected away from settlements. If the campsite is to be established on privately owned land, the contractors will acquire it on rental basis from private landowners. The contractors will return the land on as received basis. All debris, construction materials, left over chemicals and machinery shall be removed before handing back the premises to landowners.

3.10 **Construction Materials**

The materials used in construction of water supply, sewerage, overhead tanks pumping station & sewage treatment plant (STP) in all villages, would include coarse aggregates (crush), bricks, fine aggregates (sand), soil, water, pipes (RCC & HDPE), cement, reinforcement, asphalt etc. Procurement, safe handling and transportation of these material

as per the EHS guidelines and other requisite standards will be responsibility of the Contractors. Local suppliers of construction materials should be preferred if they meet the financial and quality standards criteria.

3.11 Workforce Requirement

Workforce during Construction Phase

Total man power required on site for proposed Project will be approximately 08-30 workers per village per day, depending on the type of construction. Hiring of the local labor will be preferred.

Workforce during Operation Phase

Total man power required during operation phase for proposed Project will be approximately 5 workers per village comprising skilled and unskilled staff.

3.12 Solid Waste Generation

Due to construction activities waste will be generated at construction and contractors camp site. The construction waste will include wastewater, oil spillage from machinery, domestic waste and waste construction materials. Solid waste generated during construction and camp sites will be safely disposed of in demarcated waste disposal sites.

Construction and Operation Phase

The solid waste generation is estimated to be 0.28kg/capita/day during construction phase of the proposed Project.

3.13 Water requirement

Construction Phase

The water consumption is estimated to be 30 liter/day/worker[5] during construction phase of the proposed Project.

Operation Phase

The water consumption is estimated to be 30 liter/capita/day (during operation phase of the proposed project.

3.14 Wastewater Generation during Construction Phase

The wastewater generation is estimated to be 24 liter/capita/day[6] for during construction phase of the proposed Project. Temporary toilets with cesspit will be adequately installed and treated periodically, and after the completion of work, the ground will be restored.

[5] The most basic water requirement is stipulated by the World Health Organization (WHO) and varies between 20 and 50 litres per capita per day (LPCD).

[6] Design Criteria of Public Health Engineering for Water Supply, Sewerage and Storm Water Drain (Domestic sewage generation = 80% of water consumed/day)

4 BASELINE PROFILE

4.1 General

This chapter presents the current environment around the proposed development which has been considered with respect to physical, ecological and socio-economic resources. The ESMP of the proposed project covers a comprehensive description of the project area, including the resources which are expected to be affected by the project, as well as, those which are not expected to be directly affected by the construction and operation of the project.

ESMP teams conducted the reconnaissance and detailed field visits of the project area from June, 2025 to October, 2025. The prime objective of the field visits was to collect the baseline data on physical, eco-biological and environmental & social aspects along with identification, assessment and categorization of the significant environmental and social impacts of the proposed Project. The collected data was later transferred to IT based innovative tool (Kobo-Tool), for prompt retrieval. Further analysis and arriving at the meaningful results. The secondary data was collected from published sources/reports and relevant departments, which were also verified through visual observations during reconnaissance and detailed surveys.

4.2 Delineation of Study Area / Area of Influence (AoI)

As per the environmental screening study conducted earlier, the project falls in “Category E2”. The impacts of the project activities are limited and within the boundary of each targeted revenue village. The relevant revenue village is considered as project area and boundary of revenue village has been considered Area of Influence (AoI).

To further explain the area of influence on the basis of the project activities, maps explaining the geographical scale and setting of sewerage and water supply network, water and wastewater treatment and disposal of the treated effluent in the pond situated with in the principal settlement of the village are provided at **Annexure-4**. It is to be noted that the outfall of the treated effluent is into the existing wastewater collection pond located within the boundary of the village (within the confines of AoI). As the level of project intervention (water supply and treatment, wastewater collection and treatment system) and on ground conditions (such as sewerage ponds) are similar in all 232 villages therefore, maps of a typical village are shared to develop understanding of the area of influence.

As per the national and provincial regulations along with the requirements of World Bank’s OP’s, impacts and risks have been analyzed within the project AoI. Environmental and social impacts and risks will also be analyzed for all relevant stages of the project cycle, including pre-construction, construction and operation phases of the project.

4.3 Physical Environment

The physical environment includes topography, geology, soil, climate, hydrology, drainage, seismology, surface water, groundwater and ambient air.

4.3.1 Topography

The proposed project sites are rural settlements comprising residential and agriculture areas. The terrain of the project area in Central-I, Central-II, and South-I is mainly characterized by its flat nature. The ground elevations variation is given in **Table 11**:

Table 11: Topographic Variations

Sr. No.	Cluster	Tehsils	Elevation (ft)
1	North	Noorpur Thal	576.30 to 658.59
2	South-1	Liaqatpur	315
		Rojhan	289
3	South-III	Bahawalnagar	516 to 535
4	Central	Pakpattan	527 to 578
5	South-II	Alipur	285 to 410
		Shujabad	350 to 450
		Taunsa	450 to 620
Source: Field Survey conducted by EDCS Consultants			

4.3.2 Geology

Punjab's area mostly consists of an alluvial plain formed by the southward-flowing Indus River and its four major tributaries. The general slope of the land is from northeast to southwest, but it rises in the areas between rivers Approximately 70 percent land area of the province comprises flood plans of Indus basin. Geologically, lands in the flood plains are lightly mantled with alluvial deposits transported from the Himalaya foothills. The underlying bedrock is composed of Precambrian metamorphic and tertiary consolidated rocks. The overlying alluvium consists of Pleistocene to recent unconsolidated deposits of sand, clay and silt. The formation age of the alluvium also dates from Pleistocene to recent, the latter being predominant earth river banks and the former around the central part of the plains, no major fault zone traverses the project area.

4.3.3 Climate and Meteorology

A. Average Temperatures

The project area has hot summer and cold winters. The summer starts from May and lasts till September. June is the hottest month. The mean maximum temperature varies between 39- 45 ºC and minimum temperature varies between 24-29 ºC respectively for month of June. The winter seasons lasts from November to February. January is the

coldest month. The mean maximum ranges between 18 - 30 ºC and mean minimum temperature ranges between 06 - 14 ºC in January as shown in the following table:

Table 12: Temperature Variation in Summer and Winter Season

Sr. No.	Cluster	Tehsils	Average Annual Rainfall (mm)	Summer Season		Winter Season	
				Mean Max ^{0}C	Mean Min ^{0}C	Mean Max ^{0}C	Mean Min ^{0}C
1	North	Noorpur Thal	47	40	27	18	6
2	South-1	Liaqatpur	73	39	28	21	8
		Rojhan	123	43.2	29	25	11
3	South-III	Bahawalnagar	45	41	29	20	07
4	Central	Pakpattan	23	45	24	30	06
5	South-II	Alipur	253.7	39	28.6	26	12.8
		Shujabad	60	39.2	28.6	25.8	12.6
		Taunsa	181	39.8	29	25.8	13.4
Source: Meteoblue							

In project areas, most of the times of the year sunny days dominate. A few days per month are partly cloudy and with seldom overcast days. The maximum precipitation is observed during June to August. In project areas are classified as arid region having average annual rainfall less than 250 mm in a year. Highest intensity of rain is recorded in month of July and August owing to monsoon season.

B. Wind

In targeted tehsils windier part of the year is April to August. In North, Central-I and South-III zones of Punjab, April and July are notably the windiest months. Conversely, in the South-I and Central-II zones of Punjab, June experiences higher wind activity. Moreover, from April to July, dust storms are prevalent in the targeted tehsils.

Table 13: Average Wind Speed and Windiest Month in Tehsils

Sr. No.	Cluster	Tehsils	Windiest Month	Avg. Wind Speed
1	North	Noorpur Thal	June	5-10 km/h
2	South-1	Liaqatpur	June	13 km/h

		Rojhan	April	28 km/h
3	South-III	Bahawalnagar	June	14 km/h
4	Central	Pakpattan	June	12 km/h
5	South-II	Alipur	June	15.6 Km/h
		Shujabad	July	12.4 Km/h
		Taunsa	August	11 Km/h
Source: Meteoblue				

4.3.4 **Water Resources**

Description of surface water and groundwater of targeted villages in different tehsils is as under. Hydrology map of Punjab Province is shown in **Figure 5.**

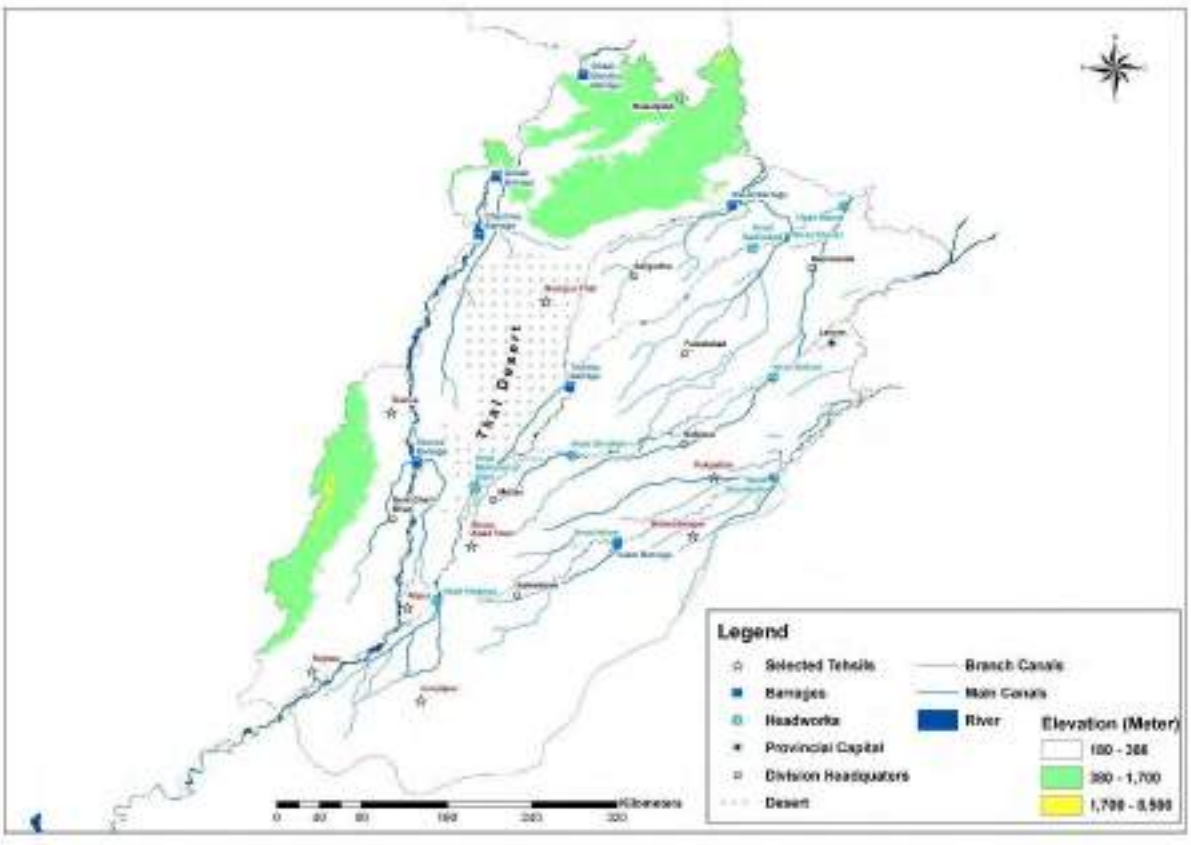

Figure 5: Hydrology Map of Punjab Province

Surface Water

Punjab is land of Indus River and its four major tributaries in Pakistan, the Jhelum, Chenab, Ravi, and Sutlej rivers. Punjab Irrigation system is one of the world's largest irrigation

systems with a command area of over 21 million acres. The system consists of 24 main canals and 12 barrages and vast network of canals, distributaries and minors spanning over 40,000 kilometers. Targeted villages in north, south and center of the Punjab are in command area of this irrigation system. The detail of canal and distributaries passing within or nearby the targeted villages is shared in **table 14:**

The tehsils of Alipur, Shujabad, and Taunsa are served by major surface water resources, including the Indus and Chenab Rivers, as well as an extensive irrigation network comprising canals, distributaries, and minors. These water bodies are primarily used for irrigation and local water needs.

In Liaqatpur, canals associated with the Abbasia Canal system provide water primarily for agricultural activities, Surface water is not a major source of potable water but is widely used for irrigation, livestock, and groundwater recharge.

In Rojhan Tehsil, Indus River is the primary perennial surface water source for Rojhan. Durring the monsoon season, torrential rains in the Koh-e-Sulaiman hills generate hill torrents, which bring large volumes of surface water down into the plains of Rojhan and surrounding areas.

Surface water in Noorpur Thal is linked to the river Jhelum irrigation system, with supply conveyed through the Dulla distributary and its off-taking channels, including Adhi Kot, 2-L, and Tail Right. These channels support irrigation demands and contributes to localized surface drainage during operational periods.

In Bahwalnagar the overall water quality is assessed as moderate to poor. Most physico-chemical parameters comply with acceptable limits; however, elevated TSS and turbidity remain concerns.

Tehsil Pakpattan is served by one main canal and three distributaries, which primarily support irrigation and local water requirements, with generally moderate water quality.

Table 14: Surface Water Bodies in Targeted Villages of Relevant Tehsils

Sr. No.	Cluster	Tehsils	Surface Water Bodies of targeted villages in Tehsils				
			River	Main Canal	Branch Canal	Distributary	Minor Canal
1	North	Noorpur Thal	Jhelum	-	Dulla	Adhi Kot (CJ link canal)	Shah Wala Minor, Amir kot Minor
2	South-1	Liaqatpur	Indus	Abbasia Canal, Abbasia Link Canal, Panjnad Main Line	-Minchin Branch	1-L/AC 1-R/AC 3-R/AC 4-R/AC 5-R/AC 6-R/AC 7-R/AC	1-L/1-R/AC Minor 1AL/3-R/AC Minor

Sr. No.	Cluster	Tehsils	Surface Water Bodies of targeted villages in Tehsils				
			River	Main Canal	Branch Canal	Distributary	Minor Canal
		Rojhan	Indus	-	,	Qadra,Bhagsari,Umarkot, Rojhan	Umarkot,Tariq,Ghous Bux
3	South-III	Bahawalnagar	-	Forwah Canal	Malik Canal	-	Gujiani Canal
4	Central	Pakpattan	-	100 Wali Canal	-	Malkans Rajwaya Distributary, Malka Hans Ranba	-
5	South-II	Alipur	Indus River	Rangpur Canal	Muzaffargarh Branch Canal	Distributaries of Muzaffargarh Branch Canal	-
6		Shujabad	Chenab River	Lower Chenab Canal	Shujabad Branch Canal	Faiz Distributary Rana Distributary Panjani Distributary Shujabad Distributary Wali Muhammad Distributary Mahmud Distributary	Sat Burji Minor
7		Taunsa	Indus River	Dera Ghazi Khan Canal	Muzaffargarh Branch Canal	-	-
Source: Irrigation Department of Punjab							

A. **Groundwater/Drinking Water Quality**

The findings of the groundwater investigation indicate that the project area has a plentiful supply of groundwater available at depths ranging from 21 ft to 50 ft, with the exception of the villages of Pakpattan, Noorpur Thal, and Shujabad. Pakpattan, Noorpur Thal, and Shujabad are characterized by water-logged conditions.

As per ERS (Electrical Resistivity Survey) studies, shallow groundwater is slightly brackish, whereas deep groundwater is relatively sweet at depths of around 200 ft. Handpumps installed at depths of 50-200 ft yield sweet water and are commonly used by the local community for drinking purposes. In contrast, groundwater near the ground surface remains brackish.

As per ERS studies, groundwater at shallow depths of about 20 ft–30 ft occurs in localized sweet water pockets. These pockets are limited to approximately 20 ft in thickness, below which the groundwater becomes brackish and unfit for drinking purposes.

In Liaqatpur and Rojhan groundwater is the primary source of domestic water supply. The quality of groundwater is generally brackish to moderately saline, with elevated Total Dissolved Solids (TDS) reported in several locations. In some areas, the presence of

dissolved salts and occasional microbial contamination limits its direct suitability for drinking without basic treatment; however, it remains commonly used for household purposes and limited irrigation.

Groundwater depth in the tehsils of Alipur, Shujabad, and Taunsa in the South-II Cluster ranges from 20 to 60 ft and serves as the primary source of water. The groundwater quality is non-objectionable in terms of taste and color, indicating generally acceptable groundwater conditions.

In Pakpattan, TDS and total hardness are beyond PEQs and WHO standards

The groundwater analysis of the targeted villages in different tehsils revealed the following facts in **table 15:**

Table 15: Groundwater Analysis

Sr. No.	Cluster	Tehsils	Groundwater Detail of targeted villages in Tehsils				
			Depth	Taste	Color	Source	Remarks
1	North	Noorpur Thal	8-35 feet	Slightly Brackish	Yellowish	Groundwater	TDS, Total Hardness, Chloride, & Fluoride are beyond the PEQ limits
2	South-1	Liaqatpur	15-30 feet	Non-Objectionable	0 (TCU)	Groundwater	Compliance with PEQS Limit
		Rojhan	15-40	Objectionable	04 (TCU	Groundwater	Optimal
3	South-III	Bahawalnagar	30 – 40 ft	Brackish	Clear	Seepage of Canal Water	High Fluoride.
4	Central	Pakpattan	> 56 ft	Non-Objectionable	Clear	Ground water	-
5	South-II	Alipur	20-60ft	Non-Objectionable	0 TCU	Groundwater	-
6		Shujabad	20-60tf	Non-Objectionable	0 TCU	Groundwater	-
7		Taunsa	20-50ft	Non-Objectionable	0 TCU	Groundwater	-
Source: Field surveys and test conducted by EDCS consultants							

Based on the data in the table 15, where the groundwater is brackish, seepage from the canal water will serve as the primary source of water for the water supply system. Whereas, in areas where the groundwater is deemed acceptable in terms of taste, it will be utilized as a source of water following appropriate treatment measures as indicated below:

- Chlorination for Microbial contamination
- Sand and carbon filters for turbidity

- Adsorption media filter for Arsenic / fluoride

4.3.5 Environmental Monitoring, Sampling and Testing

In order to determine the ambient air, noise levels, groundwater/ drinking water quality, environmental monitoring was carried out through EPA approved environmental labs tin the project area. The sampling locations for the environmental monitoring of ambient air, noise and groundwater/ drinking water and wastewater for the relevant tehsils lies within the boundary of the selected villages. To analyze the quality of groundwater and surface water, monitoring was performed for all the villages.

A. Ambient Air Quality

The ambient air quality monitoring period was 24 hours. The results of ambient air quality monitoring are given in **Table 16.**

Table 16: Ambient Air Quality Results

Sr. No.	Parameters		Carbon monoxide	Sulphur dioxide	Ozone	Nitric oxide	Nitrogen Dioxide	PM (2.5)	PM (10)	Suspended particulate Matter
	Unit		(24 hours) mg/m3	µg/m3	(1 hour) µg/m3	µg/m3	µg/m3	µg/m3	µg/m3	µg/m3
	PEQS		5	120	130	40	80	35	150	500
1	Noorpur Thal	Adhi Kot	1.70	46.49	74.2	10.82	29.41	47.1	164.9	472.5
		Sher Ghar	1.49	46.88	75.5	15.36	41.90	51.6	165.8	469.4
2	Liaqatpur	Chak 09 Abbasia	1.59	75.68	0.04	3.13	3.20	24	78	112
		Chak 88 Abbasia	1.40	79.23	0.03	3.80	2.16	20	81	111
3	Rojhan	Bhagsar	1.19	69.22	0.03	3.93	2.14	23	85	119
4	Bahawalnagar	Bahawalnagar	0.82	20.52	24	13.56	24.25	23	82	136
5	Pakpattan	Pakpattan	2.01	32.10	19.8	8.62	39.69	38	151	324
6	Alipur	Point-1	0.8	80	66	14	28	33	119	220
		Point-2	0.7	81	77	19	26	30	129	207
7	Shujabad	Point-1	2.9	69	69	12	24	42	121	281
		Point-2	0.9	88	70	15	25	41	122	227
8	Taunsa	Point-1	0.9	87	62	12	40	30	132	237
		Point-2	0.7	88	79	19	35	29	120	230

The ambient air quality monitoring is carried out via mobile air quality laboratories that are stationed at the sides of roads. As a result, areas with heavy traffic may exhibit higher concentrations of particulate matter and gases emanating from vehicular exhausts. The

central and northern regions of Punjab are comparatively more industrialized than the southern region, which leads to a greater prevalence of anthropogenic sources of air pollution. The above Table 15 indicates that at most testing location, air quality (majority of the parameters) is within PEQS limits with minor fluctuations. However, some of the parameters surpass the PEQS which are highlighted red in the above table.

B. Noise Level

Noise levels were monitored with the help of a potable digital sound meter at the project area for 24 (twenty-four) hours. The results of noise monitoring are given in **Table 17**.

Table 17: Noise Monitoring Results

Zone	Tehsils	Villages	Equivalent Noise Level (Leq) dB(A)		PEQS Limit dB(A)	
			Day Time	Night Time	Day Time	Night Time
North	Noorpur Thal	Adhi Kot	58.2	48.3	55	45
		Sher Garh	57.5	43.8		
		Mehmood Shaheed	56.6	44.9		
South -1	Liaqatpur	Chak 09 Abbasia	47	42		
		Chak 88 Abbasia	46	42		
	Rojhan	Bhagsar	46	45		
South-III	Bahawalnagar	Bahawalnaga	51.2	42.5		
Central	Pakpattan	Pakpattan	52.35	43.1		
South-II	Alipur	Point-1	53.6	46.6		
		Point-2	56.9	45.3		
	Shujabad	Point-1	54.5	45.4		
		Point-2	53.4	46.4		
	Taunsa	Point-1	53.4	47.6		
		Point-2	54.4	45.6		

The results of the noise monitoring conducted indicate that none of the readings obtained from any of the villages exceeded the prescribed noise limits as set forth by the Punjab Environmental Quality Standards

C. Wastewater Quality

Wastewater samples were collected and was analyzed. The analysis results of wastewater samples are compared with PEQS. The detailed monitored results for wastewater quality are given in **Table 18**. Detailed results of wastewater monitoring are provided at Annexure-12.

Table 18: Results of Wastewater

Sr. No.	Parameters		pH	COD	BOD	TSS	Oil & Grease
	Unit		-	mg/L	mg/L	mg/L	mg/L
	PEQS		6-9	150	80	200	10
1	Noorpur Thal	Adhi Kot	9.590at 23.0	400	248	160	BDL
		Shah Hussain	8.394 at 23.0	56	38	20	BDL
		Jauran Kallan	8.931 at 23.0	320	198	100	BDL
2	Liaqatpur	Chak 09 Abbasia	7.81	519	278	623	08
		Chak 88 Abbasia	6.57	2010	1075	934	9.5
3	Rojhan	Bhagsar	8.36	216	116	24	5.3
4	Bahawalnaga	Bahawalnaga	7.7	490	248	568	4.8
5	Pakpattan	Pakpattan	7.55	660	288	176	5.5
6	Alipur	Baqar Shah Shumali	7.27	480	231	280	3.6
		Bande Shah	6.84	278	130	167	4.8
		Maqwal Hadeir	7.08	422	187	221	9.6
		Nehal Wala	6.68	362	118	13400	7.2
		Khayara	6.68	362	118	13400	7.2
		Mithan Wali	7.63	910	398	3820	2.4
		Ali Wali	6.46	248	109	540	3.6
7	Shujabad	Wahi Riki	7.3	344	154	47	3.6
		Basti Dad	7.17	1122	488	13600	2.4
		Chah Miran Khan	7.03	75	40	89	2.4
		Nawan Chak	6.9	1030	460	12400	9.6
		Mohan Pur Sharqi	6.95	532	242	147	3.6
		Sangrai	7.44	143	68	79	8.4
		Shahpur Ubha	6.99	94	41	147	6
		Parhar	7.05	244	104	212	6
		Halal Waja	7.16	966	402	1080	4.8

Sr. No.	Parameters		pH	COD	BOD	TSS	Oil & Grease
	Unit		-	mg/L	mg/L	mg/L	mg/L
	PEQS		6-9	150	80	200	10
		Sarai	6.99	80	29	784	4.8
		Shah Pur Shumali	6.82	401	182	575	4.8
		Nasir Pur	7.04	1017	436	10200	7.2
8	Taunsa	Aqupur	6.88	3483	1508	11280	2.4
		Arakhar Dao	NA	NA	NA	NA	NA
		Baghon Wala	7.24	3640	1448	6080	3.6
		Basti Nasir	NA	NA	NA	NA	NA
		Basti Usman Shah	NA	NA	NA	NA	NA
		Berand	7.33	3890	1482	12660	4.8
		Bhauch	6.83	186	77	4600	1.2
		Bodo Mian	7.26	462	211	238	2.4
		Chak Sohanra Bacha	NA	NA	NA	NA	NA
		Domra Janubi	7.25	1030	491	8660	2.4
		Domra Shumali	7.25	1030	491	8660	2.4
		Ghadi Sandila	NA	NA	NA	NA	NA
		Ghali	7.44	116	47	2890	3.6
		Jalal Khan	7.15	210	101	147	BDL
		Jhok Chhapri	7.38	270	119	1367	BDL
		Jhok Mangla	7.26	516	207	232	2.4
		Jhok Rohal	NA	NA	NA	NA	NA
		Jhok Yaran	NA	NA	NA	NA	NA
		Jinpur	NA	NA	NA	NA	NA
		Khitran Wala	7.82	300	141	2390	1.2

Sr. No.	Parameters		pH	COD	BOD	TSS	Oil & Grease
	Unit		-	mg/L	mg/L	mg/L	mg/L
	PEQS		6-9	150	80	200	10
		Mahnda	6.96	309	140	178	1.2
		Malana	7.98	73	32	1680	BDL
		Mirkhar	7.56	896	382	2312	2.4
		Mundrani	7.67	3960	1578	294	6
		Langah	7.56	392	151	284	1.2

The collected samples of wastewater are not representative, as they are spot samples taken from open drains and channels. However, the analysis of the wastewater samples indicates that the levels of biological oxygen demand (BOD), chemical oxygen demand (COD), and total suspended solids (TSS) in most of the samples are higher than the limits established in the Punjab Environmental Quality Standards (PEQS). To meet the PEQS requirements, a potential solution is to utilize an Anaerobic Baffled Reactor (ABR) for wastewater treatment, which can readily ensure compliance with these standards.

Environmental Monitoring report can be accessed through the link provided below:

https://drive.google.com/drive/folders/1Xka-OzxfVziSpqu36cMHgvT1L8i0LvLr

4.1.1 Seismology

All tehsils of the project area fall within zone 2A and zone 2B according to the zoning developed by Government of Pakistan. Figure 4 shows the seismic zoning map of Pakistan.

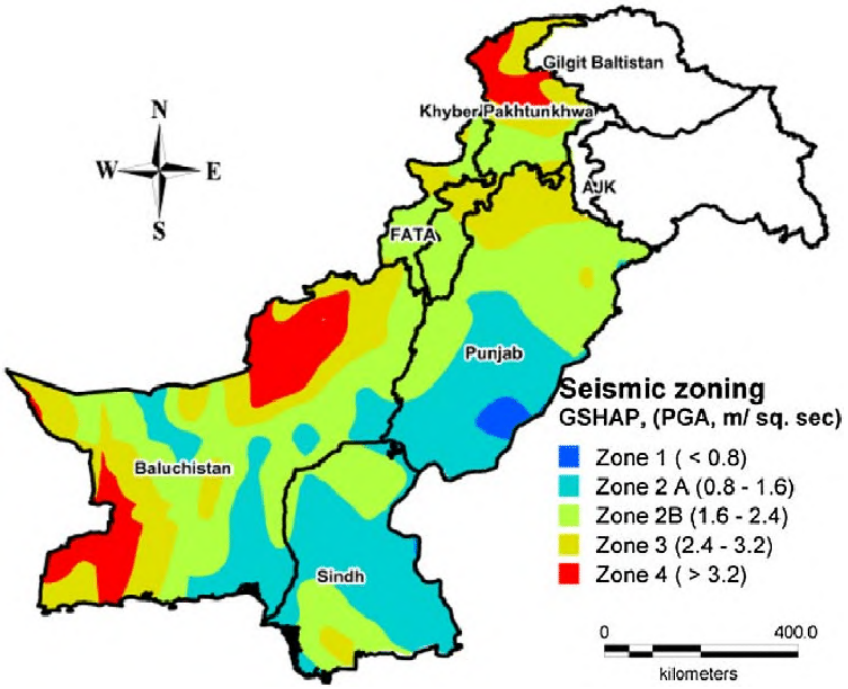

Figure 6: Seismic Zone Map of Project Area

4.4 Sensitive Receptors

Village wise sensitive receptors are identified in the table 19 below:

Table 19: Sensitive Receptors

Phase	Tehsil	Village Name	Schools	Mosques	Hospital / Clinic / BHU	Graveyard	Minority Graveyard	Minority Religious Places	Shrines	Other
Phase-1	Noor pur Thal	Rakh Dhammak	2	3	-	-	-	-	-	-
		Rakh Bambool	-	1	-	-	-	-	-	-
		Shergarh	3	4	2	-	-	-	-	1 Imam Bargah
		Daravi	2	2	-	1	-	-	1	1 Janazgah
		Chak No 020/M.B	4	3	1	2	-	-	-	-
		Burhan	2	5	-	1	-	-	-	-
		Rakh Baland	2	2	-	1	-	-	-	-
		Chak No 018/M.B	1	3	-	-	-	-	-	1 College
		Kaka	2	6	2	1	-	-	-	-
		Sidha	2	4	-	-	-	-	-	-
		Palohan	2	2	-	1	-		-	2 Imam Bargah-
		Chak No 019/M.B	1	5	1	1	-	-	-	-

Phase	Tehsil	Village Name	Schools	Mosques	Hospital / Clinic / BHU	Graveyard	Minority Graveyard	Minority Religious Places	Shrines	Other
		Laghari	3	6	1	2	-	-	2	-
		Mahmood Shaheed	3	5		2	-	-	1	-
		Khai Kalan	4	11	2	2	-	2 Mosque (Mirzai)	-	3 Imam Bargah
		Jaura Kalan	7	11	3	3	-	1 Temple	-	2 Imam Bargah 1 Janaz Gah
		Khai Khurd	6	10	-	2	-	-	2	2 Imam Bargah 1 Union Council Office
		Shah Hussain	4	5	-	1	-	-	-	-
		Rakh Shah Hussain	-	1	-	-	-	-	-	-
		Rakh Tahla Khatwan	1	1	-	1	-	-	-	-
		Adhikot	8	13	4	1	-	-	-	1 NRSP Office¸1Akhuwat Office, 1 Imam Bargarh, 1 Atomic Weather Station
		Chan	4	5	1	-	-	-	-	1 Hotel AL-Raza, 1 Imam Bargah
		Chak No 035/M.B	1	1	-	-	-	-	-	-
		Chak No 036/M.B	1	2	1	-	-	-	-	-
		Nakro Shaheed	2	2	-	-	-	-	1	-
		Chak 13	1	1	-	1	-	-	-	-
Phase-1	Liaqatpur & cluster-1	Ahmed Yar	2	5	-	1	-	-	-	-
		Arif Baloch	1	1	-	1	-	-	-	-
		Chak 315 / 6R	-	1	-	-	-	-	-	-
		Chak 316 / 6 R	-	1	-	-	-	-	-	-
		Chak 317/6R	1	2	-	-	-	-	-	-
		Chak 08 Abbasia	1	2	-	1	-	-	-	-
		Chak 09 Abbasia	-	3	-	-	-	-	-	-
		Chak 11 Abbasia	2	2	-	-	-	-	-	-
		Chak 12 Abbasia	2	2	-	1	-	-	-	-

Phase	Tehsil	Village Name	Schools	Mosques	Hospital / Clinic / BHU	Graveyard	Minority Graveyard	Minority Religious Places	Shrines	Other
		Chak 313/6R	-	1	-	-	-	-	-	-
		Chak 134 NP	1	2	-	-	-	-	-	-
		Chak 135 NP	-	1	-	-	-	-	-	-
		Chak136 NP	-	1	-	-	-	-	-	-
		Chak 139 NP	-	1	-	-	-	-	-	-
		Chak 140 NP	-	1	-	-	-	-	-	-
		Chak 143 Abbasia	1	2	-	1	-	-	-	-
		Chak 144 Abbasia	2	1	-	-	-	-	-	-
		Chak 145 Abbasia	-	1	-	-	-	-	-	-
		Chak 147 / 5R	1	2	1	-	-	-	-	-
		Chak 148 / 5R	2	4	-	-	-	-	-	-
		Chak 150 Abbasia	1	1	-	1	-	-	-	-
		Chak 152 / 7R	1	2	-	1	-	-	-	-
		Chak 153 / 7R	1	1	-	-	-	-	-	-
		Chak 154 / 7R	-	2	-	1	-	-	-	-
		Chak 155 / 7R	1	1	-	-	-	-	-	-
		Chak 156 / 7R	1	1	-	-	-	-	-	-
		Chak 157 / 7R	2	2	-	1	-	-	-	-
		Chak 159 / 7R	-	1	-	-	-	-	-	-
		Chak 174 / 7R	1	1	-	-	-	-	-	-
		Chak 175 / 7R	-	1	-	-	-	-	-	
		Chak 177 / 7R	-	1	-	-	-	-	-	-
		Chak 178 / 7R	1	1	1	-	-	-	-	-
		Chak 179 / 7R	1	1	-	-	-	-	-	-
		Chak 180 / 7R	2	1	-	-	-	-	-	-
		Chak 182 / 1L	-	1	-	-	-	-	-	-
		Chak 183 / 7 R	-	1	-	-	-	-	-	-
		Chak 186 / 7 R	1	1	1	1	-	-	-	-
		Chak 19 Abbasia	1	2	-	-	-	-	-	-
		Chak 191 / 1L	1	1	-	-	-	-	-	-
		Chak 194 / 1L	1	1	-	-	-	-	-	-

Phase	Tehsil	Village Name	Schools	Mosques	Hospital / Clinic / BHU	Graveyard	Minority Graveyard	Minority Religious Places	Shrines	Other
		Chak 195 / 1L	1	1	-	-	-	-	-	-
		Chak 20 Abbasia	7	9	-	-	-	-	-	-
		Chak 22 Abbasia	3	3	-	1	-	-	-	-
		Chak 23 Abbasia	5	5	-	-	-	-	-	-
		Chak 28 Abbasia	-	1	-	-	-	-	-	-
		Chak 31 Abbasia	1	4	-	-	-	-	-	-
		Chak 32 Abbasia	1	2	-	1	-	-	-	-
		Chak 33 Abbasia	2	1	-	-	-	-	-	-
		Chak 36 Abbasia	1	2	-	1	-	-	-	-
		Chak 37 Abbasia	2	3	1	1	-	-	-	-
		Chak 38 Abbasia	1	3	-	-	-	-	-	-
		Chak 39 Abbasia	1	2	-	-	-	-	-	-
		Chak 3 A	2	3	-	1	-	-	-	-
		Chak 40 Abbasia	1	1	-	-	-	-	-	-
		Chak 41 Abbasia	2	1	-	-	-	-	-	-
		Chak 42 Abbasia	1	1	-	-	-	-	-	-
		Chak 43 Abbasia	3	3	-	1	-	Janazgah - 1		
		Chak 46 Abbasia	2	1	-	-	-	-	-	-
		Chak 47 Abbasia	1	1	-	-	-	-	-	-
		Chak 48 Abbasia	2	1	-	-	-	-	-	-
		Chak 4 A	1	2	-	-	-	-	-	-
		Chak 63 Abbasia	2	1	-	-	-	-	-	-
		Chak 64 Abbasia	1	1	-	2	-	-	-	-
		Chak 65 Abbasia	2	2	-	-	-	-	-	-
		Chak 68 Abbasia	-	5	1	2	-	-		
		Chak 69 Abbasia	1	1	-	-	-	-	-	-
		Chak 75 Abbasia	3	4	1	1	-	Janazgah-1		
		Chak 77 Abbasia	2	3	1	1	-	-	-	-
		Chak 78 Abbasia	1	3	-	-	-	-	-	-
		Chak 79 Abbasia	2	2	-	1	-	-	-	-
		Chak 80 Abbasia	1	1	-	-	-	-	-	-

Phase	Tehsil	Village Name	Schools	Mosques	Hospital / Clinic / BHU	Graveyard	Minority Graveyard	Minority Religious Places	Shrines	Other
		Chak 81 Abbasia	2	3	-	1	-	-	-	-
		Chak 82 Abbasia	2	2	-	-	-	Janazgah-1		
		Chak 83 Abbasia	3	2	-	1	-	-	-	-
		Chak 84 Abbasia	1	2	-	-	-	-	-	-
		Chak 85 Abbasia	-	3	-	-	-	-	-	-
		Chak 86 Abbasia	1	1	-	-	-	-	-	-
		Chak 87 Abbasia	4	4	1	-	-	-	-	-
		Chak 88 Abbasia	4	3	-	-	-	-	-	-
		Chak 89 Abbasia	2	1	-	-	-	-	-	-
		Chapri Chatan Shah	1	1	-	-	-	-	-	-
		Gulshan Farid	1	3	-	1	-	-	-	-
		Hayat Lar	5	8	2	1	-	-	-	-
		Kanjki Wala	3	4	-	-	-	-	-	-
		Kotla Daraigh	3	7	-	1	-	-	-	-
		Kotla Khairay Khan	1	1	-	-	-	-	-	-
		Muradpur Sail	2	6	-	-	-	-	-	-
		Taranda Gurgujj	5	7	-	1	-	-	-	-
		Turkary	7	13	1	1	-	Imambargah-1		
		Firoza	2	4	1	1		-	-	-
	Rojhan	Bhagsar	1	1	1	2	-	Imambargah - 1		
		Dilber	1	-	-	-	-	-	-	-
		Basti Dhora	1	3	-	-	-	-	-	-
		Gianmal	4	11	-	1	-	-	-	-
		Qadra Kass	4	3	-	1	-	Janazgah - 1		
		Kotla Hasan Shah	-	3	-	-	-	-	-	-
		Rakh Qadra	3	10	-	-	-	-	-	-
		Rakh Sabzani	1	2	-	-	-	-	-	-
		Mutfriq Mazari	1	-	-	-	-	-	-	-
		Safdar Abad	1	-	-	-	-	-	-	-
		Salim Abad	2	2	-	-	-	-	-	-
		Tariq Abad	2	4	-	1	-	-	-	-

Phase	Tehsil	Village Name	Schools	Mosques	Hospital / Clinic / BHU	Graveyard	Minority Graveyard	Minority Religious Places	Shrines	Other
Phase-1	Bahawalnagar	Bonga Ihsab Bibi	2	2	-	-	-	-	-	-
		Hasan Raika	1	1	-	1	-	-	-	-
		Bhole Shah Hitar	-	1	-	-	-	-	-	-
		Paran Wala	1	2	-	1	-	-	-	-
		Chak Abdul Haq	1	1	-	1	-	-	-	-
		Dhanraj Pura	1	2	-	1	-	-	-	-
		Jagga Sanatteka	1	4	-	1	-	-	-	-
		Mosla	-	1	-	-	-	-	1	-
		Pir Sikandar Otar	1	-	-	1	-	-	-	-
		Julan Chistian	1	2	-	-	-	-	-	-
		Gauspur	1	1	-	-	-	-	-	-
		Aminabad	1	1	-	-	-	-	1	-
		Abrarah Utthar	1	1	-	-	-	-	-	-
		Ali Gohar No. 326	1	1	-	-	-	-	-	-
		Ramnagar	1	1	-	1	-	-	-	-
		Hussain Abad Uttar	1	1	-	-	-	-	-	-
		Hussain Abad Hithar	1	1	-	-	-	-	-	-
		Gaman Dongi	1	1	-	-	1	-	-	-
		Sharaf Din	-	1	-	-	-	-	-	-
Phase-1	Pakpattan	Chak 102D	3	1	-	1	-	-	-	-
		Chat 87D	2	2	-	1	-	-	-	-
		Bahawan Shah	1	2	-	-	-	-	-	-
		Chak Ilahi Bux	1	2	-	-	-	-	-	-
		Chak Murad Khan	1	-	-	-	-	-	-	-
		Chak Nazam Din	2	3	-	-	-	-	-	-
		Gobind Pur Bahmni	4	3	-	1	-	-	-	-
		Jand Wala	1	2	-	1	-	-	-	-
		Nahla Abad	1	3	-	2	-	-	-	-
		Dhamiana	1	2	-	1	-	-	1	-
		Chak No. 4SP	2	2	-	1	-	-	-	-
		Chak Qudar Tullah	1	1	-	-	-	-	-	-

Phase	Tehsil	Village Name	Schools	Mosques	Hospital / Clinic / BHU	Graveyard	Minority Graveyard	Minority Religious Places	Shrines	Other
		Chilli Mamdana	-	2	-	1	-	-	-	-
		Dada Ahluka	1	2	-	1	-	-	-	-
		Ghar Taj	1	-	-	1	-	-	-	-
		Ghazi Mardan	1	2	-	-	-	-	2	-
		Nura Ahluka	2	-	-	-	-	-	-	-
		Arazi The Chand	1	2	-	-	-	-	-	-
		Ghuri	2	1	-	1	-	-	1	-
		Chak 103D	1	1	-	-	-	-	-	-
Phase-1	Alipur	Baqar Shah Shumali	2	23	-	-	-	-	-	2 Madrassa
		Bande Shah	2	4	-	-	-	-	-	1 Imambargah
		Maqwal Hadeir	3	16	-	-	-	-	-	-
		Nehal Wala	-	5	-	-	-	-	-	-
		Nauhabad	-	1	-	-	-	-	-	-
		Khayara	-	3	-	-	-	-	-	-
		Mithan Wali	15	37	1	2	-	-	1	1 Eid gah
		Ali Wali	6	11	1	-	-	-	-	1 Madrassa, 1 Eid gah
		Kotla Agar	1	1	-	-	-	-	-	1
		Makhan Bela	1	1	-	-	-	-	-	-
		Bet Barrah	1	3	1	-	-	-	-	-
		Marian	2	2	1	-	-	-	-	1 Madrassa
		Bet Mir Ahmad Jamal	-	1	-	-	-	-	-	-
		Kotla Ghulam Shah	2	3	-	-	-	-	-	2 Imam-Bargaah
		Sirki	1	1	1	-	-	-	-	-
		Tibba Barrah	-	1	-	-	-	-	-	-
		Gabbar Arian	3	5	1	-	-	-	-	2 Madrassa
		Bet Bagh Shah	-	1	-	-	-	-	-	-
		Yare Wali	1	2	-	-	-	-	-	1 Madrassa
		Kohar Faqiran	4	2	1	-	1	-	-	-

Phase	Tehsil	Village Name	Schools	Mosques	Hospital / Clinic / BHU	Graveyard	Minority Graveyard	Minority Religious Places	Shrines	Other
		Kotla Afghan	2	1	-	1	-	-	-	1 Imam-Bargah, 1 Madrassa
		Gagare Wali	1	5	-	1	-	-	-	1 Madrassa
	Shujabad	Wahi Riki	2	4	-	-	-	-	-	-
		Basti Dad	2	7	-	-	-	-	-	1 Madrassa
		Chah Miran Khan	2	7	-	-	-	-	-	-
		Nawan Chak	-	2	-	-	-	-	-	-
		Mohan Pur Sharqi	2	3	-	-	-	-	-	-
		Sangrai	-	5	-	-	-	-	-	-
		Shahpur Ubha	3	4	1	1	-	-	-	1 Madrassa
		Sarai	3	3	-	-	-	-	-	-
		Shah Pur Shumali	2	6	-	-	-	-	-	-
		Nasir Pur	5	3	-	-	-	-	1	-
	Tausa	Aqupur	2	3	-	-	-	-	-	1 Madrassa
		Arakhar Dao	-	1	-	-	-	-	-	-
		Rind Wala	-	1	-	-	-	-	-	-
		Baghon Wala	1	2	-	-	-	-	-	-
		Bakhri	-	1	-	-	-	-	-	-
		Basti Habib	-	1	-	-	-	-	-	-
		Basti Nasir	1	1	-	-	-	-	-	-
		Basti Usman Shah	1	3	-	-	-	-	-	1 Madrassa
		Berand	-	1	-	-	-	-	-	-
		Bet Obai	-	1	-	-	-	-	-	-
		Bodo Mian	-	1	-	-	-	-	-	-
		Chak Sohanra Bacha	-	2	-	-	-	-	-	-
		Domra Janubi	-	1	-	-	-	-	-	-
		Domra Shumali	1	1	-	-	-	-	-	1 Madrassa
		Ghadi Sandila	-	2	-	-	-	-	-	-

Phase	Tehsil	Village Name	Schools	Mosques	Hospital / Clinic / BHU	Graveyard	Minority Graveyard	Minority Religious Places	Shrines	Other
		Ghali	2	5	-	-	-	-	-	1 Imambargah, 1 Madrassa
		Jalal Khan	2	2	-	-	-	-	-	1 Madrassa
		Jhok Chhapri	-		-	-	-	-	-	-
		Jhok Mangla	2	4	1	-	-	-	-	1 Madrassa
		Jhok Rohal	1	1	-	-	-	-	-	1 Madrassa
		Jhok Yaran	-	1	-	-	-	-	-	-
		Jinpur	-	1	-	-	-	-	-	-
		Khitran Wala	1	3	-	-	-	-	-	1 Madrassa
		Kotla Marrani	2	3	-	-	-	-	-	-
		Rakh Sanjar	-	1	-	-	-	-	-	-
		Rakh Zor	-	1	-	-	-	-	-	-
		Wani	-	1	-	-	-	-	-	-
		Mahnda	2	3	-	-	-	-	-	1 Madrassa
		Mirkhar	1	2	-	-	-	-	-	-
		Mundrani	2	3	-	1	-	-	1	1 Madrassa
		Pukan	-	1	-	-	-	-	-	-
		Rakh Mari Pachaudi	-	1	-	-	-	-	-	-
		Langah	2	7	-	1	-	-	1	-
		Rakhana	-	1	-	-	-	-	-	-

Note: The socially sensitive receptors listed in the table above are within a radius of 100 meters of the execution of work. This distance of 100 meters has been taken as per screening checklist provided in ESMF and also validated through experiences of various EDCS Consultants. Data is taken from Mouza Census and verified through physical survey.

4.5 Biological Environment

Project area is rich in biodiversity because of its diverse landscape and geographical location. The variety of ecosystem is evident and is home to various species. The following section describes the biological environment of the project area.

4.5.1 Flora

The major floral species found in the project area include the following:

Zone	Tehsils	Floral Species
North	Noorpur Thal	Kikar (Acacia nilotica), Cactus (Cactaceae), Sufaida (Eucalyptus camaldulensis), Poplar (Populus alba), Sufaida (Eucalyptus camaldulensis), Tali (Erythrophleum suaveolens), Neem (Azadirachta indica), Sharin (Albizia lebbeck), Bakain (Melia azedarach)
South-1	Liaqatpur	Kikar (Acacia nilotica). Neem (Azadirachta indica),Sheesham (Dalbergia),Khagi/ Ajwa Date Palm (Phoenix dactylifera L.), Sufaida (Eucalyptus spp.), Bari (Ziziphus mauritiana), Poplar (Populus spp.), Jaman (Syzygium cumini), Simal (Bombax cieba),
	Rojhan	Kikar (*Acacia arabica*), Shisham (*Dalbergia sissoo*), Beri (*Ziziphus jujaba*), Toot/Mulberry (*Morus spp.*), Peeple (*Ficus religiosa*), Neem (*Melia indica*), Jand (*Prosopis spicigera*), Karir (*Capparis aphylla*) and Phulai (*Acacia modesta*)
South-III	Bahawalnagar	The Van (Salvadora oleoides), Karil (Capparis aphylla), Jand (Prosopis spicigera), Beri (Zizyphys jajaba), mallha (Zizyphus numularia) and Shisham (Dalbergia Sissoo)
	Pakpattan	Sumbal (Bombax ceiba), Shesham (Dalbergia sissoo), Eucalyptus (Eucalyptus globulus), Kikar (Acacia karoo), Peepal (Ficus religiosa), Neem (Azadirachta indica), Poplar (Populus), Mulberries (Morus rubra), Beri (Ziziphus mauritiana), Peaches (Prunus persica) Guava (Psidium guajava), Sweet Lime (Citrus Limetta), Lime (Citrus limon), Date Palm (Phoenix dactylifera), Jaman (Syzygium cumini), Puth Kanda (Achyranthes aspera), Kharasan' thorn (Fagonia cretica), Stenotaphrum, Cyperus rotundus, Phalaris Minor, Sodom apple (Calotropis procera), Bathua (Chenopodium album)
South-II	Alipur	Kikar (*Acacia arabica*), Shisham (*Dalbergia sissoo*), Beri (*Ziziphus jujaba*), Toot/Mulberry (*Morus spp.*), Peeple (*Ficus religiosa*), Neem (*Melia indica*), Jand (*Prosopis spicigera*), Karir (*Capparis aphylla*) and Phulai (*Acacia modesta*)
	Shujabad	Jand (*Prosopis spicigera*), Karir (*Capparis aphylla*), Farash (*Tamarix articulata*), Kikar (*Acacia arabica*), Shisham (*Dalbergia sissoo*), Beri (*Ziziphus jujaba*), Toot/Mulberry (*Morus spp*.), Sirin (*Albizia lebbeck*), Neem (*Melia indica*), Peepal (*Ficus religiosa*), Date Palm (*Phoenix dactylifera*) and Poplar (*Populus euphratica*)
	Taunsa	Shisham (*Dalbergia sissoo*), Kikar (*Acacia arabica*), White Mulberry (*Morus alba*), Simal (*Bombax ceiba*), Kana (*Saccharum bengalense*) and Jand (*Prosopis cineraria*)

4.5.2 **Fauna**

The faunal species observed in the project areas were verified with the secondary data resources of the Punjab Forest, Wildlife and Fisheries Department and World Wildlife Fund (WWF). The species in vicinity include the following:

A. Mammals

Common animals found in the project area include wild cat, dogs, cats, jackals, Weasel, house rats, wild boar, bats, porcupine, bandicoot, soft furred rat and Indian gerbil. Domestic

livestock observed during field visits include buffaloes, cattle, goats, sheep, and donkeys that are used by the local residents for their livelihood.

B. Amphibians

Bullfrog (*Hoplobatrachus tigernius*), Pahari tidda maindak (*Fejervarya limnocharis*), frog (rana tigrine) and Toad (Bufo bufo) are also present in the nearby ponds and canals during rainy season.

C. Birds

House sparrow (*Passer domesticus*), House crow (*Corvus splendens*) and Mynah (*Acredotheres tristis*) are the most common sight in the area. In addition, following birds are also seen in the project area**.**

Common Name	Scientific Name
Nightingale	*Pycnontus cafer*
Parrot	*Psittacula krameri*
Pigeon	*Columba livia*
Hoopoe	*Upupa epops*
Duck	*Anatidae*
Koel	*Eudynamys scolopacea*
Quail	*Coturnix coturnix*
Plover	*Charadriinae*
Black kite	*Mivus migrains*
Dove	*Columbidae*
Herons	*Ardeidae*
Mallard	*Anas platyrhynchos*
Gray Partridge	*Perdix perdix*
Black Partridge	*Melanoperdix niger*
Sandgrouse	*Pteroclidae*
Red wattled lapwing	*Vanellus indicus*
red-vented bulbul	*Pycnonotus cafer*
pewit	*Vanellus vanellus*
cuckoo	*Cuculidae*
jungle babbler	*Turdoides striata*

D. Reptiles

Common tree lizard (*Calotes versicolor*), Monitor lizard (*Varnus bengalensis*), fat tailed lizard (*Uromastix hardwickii*), fringed toed lizard (*Acanthodactylus cantoris*), Tortoise (Testudinidae), snakes (Serpentes), cobra (Naja) and Scorpions (Scorpiones) are observed in and around the proposed site. Saw-scale viper (Echis carinatus), Indian soft-shell turtle

(*Aspideretes gangeticus*), striped keelback (Amphiesma stolatum) and Indian falpshell (*Lisseyms punctate andersoni*) are also reported by the local residents.

4.5.3 Endangered Species

There are no endangered species of flora and fauna observed in the Study Area.

4.1.2 Legally Protected Areas

The Government of Punjab through Punjab Legally Protected Areas act 2020 may declare an area to be called a protected area, with a specific name such as wetlands, national park, wildlife or game reserves. In order to provide for the protection, preservation, conservation and management of ecologically important areas.

A table indicating legally protected areas and other important ecological hotspots in different district of Punjab is attached below and the wetlands present in the district of the project areas are highlighted red and their distances from the project site is listed below.

Sr. No.	Name of Legally Protected Area	Status	District	Distance from Nearest Project Village
1	Bajwat	Game Reserve	Sialkot	348 km
2	Ghamaghar Lake	Not Protected	Kasur	130 km
3	Head Islam	Game Reserve	Multan	80 km
4	Jahlar Lake	Not Protected	Khushab	103 km
5	Khabbaki Lake	Wildlife Sanctuary	Khushab	130 km
6	Kharrar (Kharal) Lake	Wildlife Sanctuary	Okara	80 km
7	Lal Suhanra (Patisar) Lake	National Park	Bahawalpur	105 km
8	Mangla Dam	Not Protected	Jhelum	145 km
9	Marala Headworks	Not Protected	Sailkot	230 km
10	Nammal Lake	Wildlife Sanctuary	Khushab	75 km
11	Qadirabad Barrage	Not Protected	Gujrawala	155 km
12	Qadirabad Link Canal	Game Reserve	Gujrat	145 km
13	Rasool (Rasul) Barrage	Wildlife Sanctuary	Gujrat	120 km
14	Soan River	Not Known	Chakwal	40 km
15	Taunsa Barrage	Wildlife Sanctuary	Muzaffargarh/DGK	45 km
16	Ucchali Lake	Ramsar Site	Khushab	90 km
Source: Punjab Tourism and Wildlife Departments				

As indicated from the above table, there are no legally protected areas in the area or in the influence of the project area. The nearest legally protected area is about 40 km away from the nearest project village. A map indicating wildlife sanctuaries and game reserve in different district of Punjab is attached below.

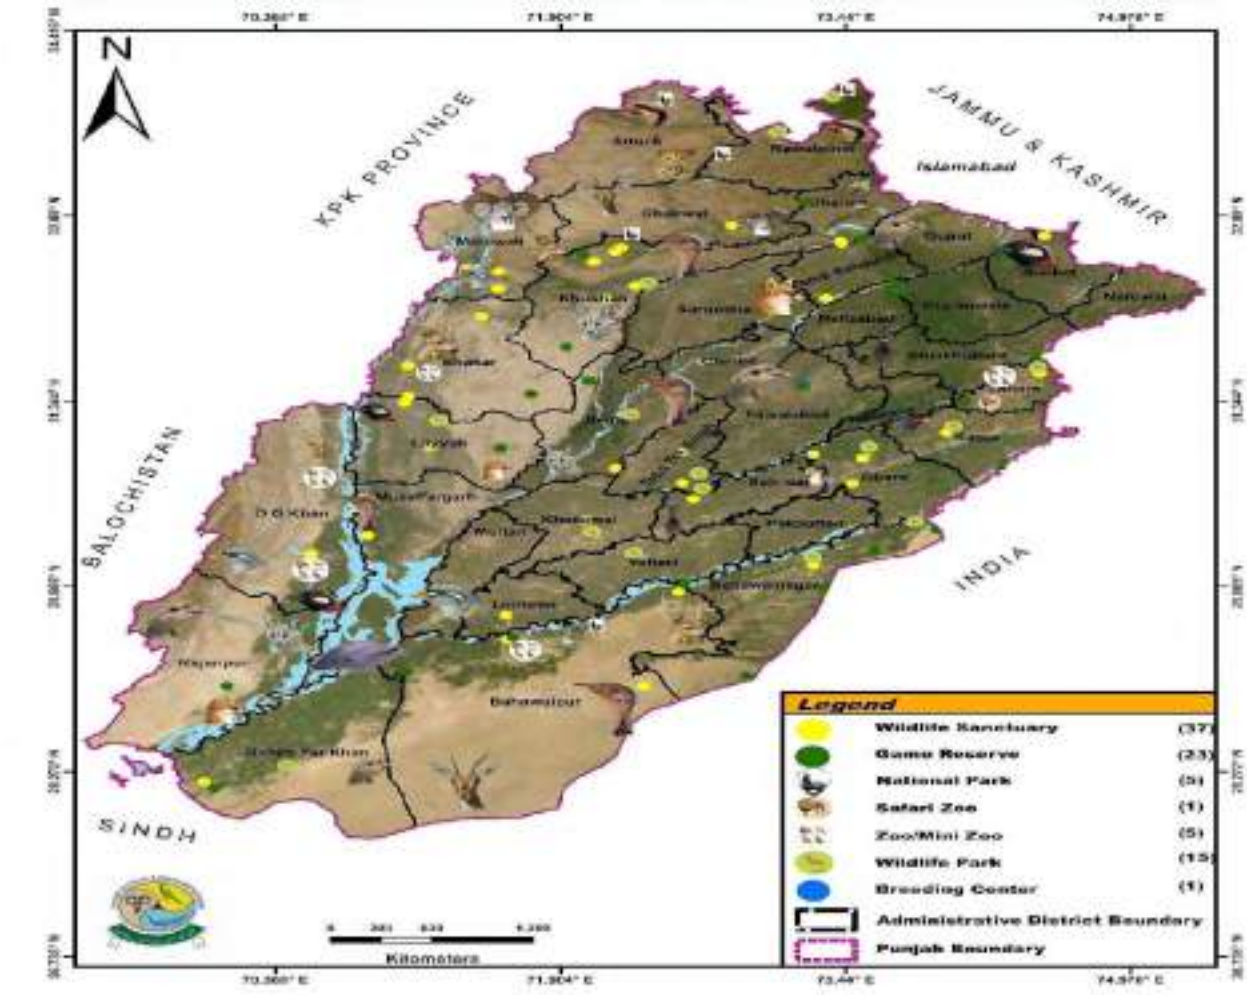

Figure 7: Wildlife Sanctuaries and Game Reserves

4.6 Socioeconomic **Profile**

4.6.1 **Population Size**

The project is expected to benefit about 66,350 households in the 232 villages. The average population size is 1,774 persons per village.

Table 20: Primary Data Results of Project Area

Sr. No	Zone	Tehsil	Villages	HH	M	F	Total
1	North	Noorpur Thal	Rakh Dhammak	50	133	137	270

Sr. No	Zone	Tehsil	Villages	HH	M	F	Total
2			Rakh Bambool	35	79	79	158
3			**Shergarh**				
			Sher Garh New	50	150	155	305
			Sher Garh Old	75	224	234	458
			Dhok Muzaffar Khan	80	240	248	488
4			Daravi	260	737	693	1,430
5			Chak No 020/M.B	450	1568	1537	3,105
6			Burhan	320	995	956	1,952
7			Rakh Baland	250	780	720	1,500
8			**Chak No 018/M.B**				
			Chak No 018/M.B Main	180	420	390	810
			Chak No 018/M.B Settlement	170	395	370	765
9			Kaka	400	1222	1378	2,600
10			Sidha	470	1515	1399	2,914
11			Palohan	450	1102	1103	2,205
12			Chak No 019/M.B	700	2041	1739	3,780
13			Laghari	850	2082	2168	4,250
14			Mahmood Shaheed	450	1170	1125	2,295
15			**Khai Kalan**				
			Obhal	780	1982	2074	4,056
			Sheikh Panjah	27	69	71	140
			Behlolpur	60	153	159	312
			Aura Syedan	100	250	270	520
16			**Jaura Kalan**				
			Jaura Kalan	900	2646	2754	5,400
			Thathi Kalak Bhan S-1	110	323	337	660
17			**Khai Khurd**				
			Khai Khurd Main Settlement	160	407	441	848
			Ahmadabad North (S-1)/Majoka	40	102	110	212
			Sath Sahani	225	573	620	1,193
			Allah Yar	90	226	251	477

Sr. No	Zone	Tehsil	Villages	HH	M	F	Total
			Naya Majoka	60	153	165	318
			Thathi Baksh Shah	105	267	290	557
18			**Shah Hussain**				
			Shah Hussain Main	300	749	691	1,440
			Jatoi Wala	285	608	562	1,170
19			Rakh Shah Hussain	45	105	89	194
20			Rakh Tahla Khatwan	70	229	212	441
21			Adhikot	1150	2874	2761	5,635
22			Chan	700	2030	2030	4,060
23			Chak No 035/M.B	30	96	96	192
24			Chak No 036/M.B	95	231	235	466
25			Nakro Shaheed	250	774	726	1500
26			Chak 13	110	306	332	638
27	South-1	Liaqatpur	**Ahmad Yar**				
			Ahmad Yar Tanwari	151	535	492	1,027
			Basti Noor Muhammad	74	262	241	503
			Basti Hussain Abad	93	329	303	632
			Basti Marri	55	195	179	374
28			Basti Khokhran	100	313	287	600
29			Chak 315/6R	65	271	249	520
30			Chak 316/6R	80	333	307	640
31			Chak 317/6R	135	570	524	1,094
32			**Chak No 08 Abbasia**				
			Chak No 08 Abbasia	332	1,280	1,177	2,457
			Chak No 08 Abbasia Jinnah Colony	70	270	248	518
33			**Chak No 09 Abbasia**				
			Chak No 09 Abbasia	120	419	385	804
			Chak No 09 Abbasia Colony	110	384	353	737
			Chak No 09 Abbasia Shiekhan	50	175	160	335
34			Chak No 11 Abbasia	346	1,208	1,110	2,318
35			Chak No 12 Abbasia	164	684	628	1,312

Sr. No	Zone	Tehsil	Villages	HH	M	F	Total
36			Chak No 313/6R	70	295	272	567
37			Chak No 134 NP	158	790	727	1,517
38			Chak No 135 NP	54	180	166	346
39			Chak No 136 NP	53	204	188	392
40			**Chak No 139 NP**				
			Chak No 139 NP	50	206	189	395
			Basti Elahi Bux Toor	63	259	239	498
41			Chak No 140 NP	73	270	248	518
42			Chak No 143 Abbasia	222	787	723	1,510
43			Chak No 144/ 5R	80	396	364	760
44			Chak No 145/ 5R	52	201	184	385
45			Chak No 147/ 5R	151	519	478	997
46			Chak No 148/ 5R	59	292	269	561
47			Chak No 150 Abbasia	63	210	193	403
48			Chak No 152 7R	111	538	494	1,032
49			Chak No 153 7R	101	500	460	960
50			Chak No 154 7R	133	603	554	1,157
51			Chak No 155 7R	120	488	448	936
52			Chak No 156 7R	106	514	472	986
53			Chak No 157 7R	193	975	897	1,872
54			Chak No 159 7R	92	369	339	708
55			Chak No 174 7R	91	422	388	810
56			Chak No 175 7R	180	994	914	1,908
57			Chak No 177 7R	51	231	213	444
58			Chak No 178 7R	119	440	405	845
59			Chak No 179 7R	53	227	208	435
60			Chak No 180 7R	87	440	404	844
61			Chak No 182 1L	88	376	346	722
62			Chak No 183 7R	117	451	415	866
63			Chak No 186 7R	127	252	231	483
64			Chak No 19 Abbasia	411	1,456	1,339	2,795
65			Chak No 191 1L	60	218	202	420
66			Chak No 194 1L	134	649	597	1,246

Sr. No	Zone	Tehsil	Villages	HH	M	F	Total
67			Chak No 195 1L	56	251	231	482
68			**Chak No 20 Abbasia**				
			Chak No 20 Abbasia Colony	400	1,271	1,169	2,440
			Chak No 20 Abbasia	305	970	891	1,861
69			**Chak No 22 Abbasia**				
			Chak No 22 Abbasia Jinnah Colony	393	1,413	1,299	2,712
			Chak No 22 Abbasia	180	647	595	1,242
70			**Chak No 23 Abbasia**				
			Chak No 23 Abbasia	226	824	758	1,582
			Chak No 23 Abbasia Colony_1	350	1,276	1,174	2,450
			Chak No 23 Abbasia Colony_2	70	255	235	490
71			Chak No 28 Abbasia	105	432	398	830
72			**Chak No 31 Abbasia**				
			Chak No 31 Abbasia Colony_2	80	300	276	576
			Chak No 31 Abbasia	158	593	545	1,138
			Chak No 31 Abbasia Colony_1	180	675	621	1,296
73			Chak No 32 Abbasia	564	2,263	2,080	4,343
74			Chak No 33 Abbasia	147	490	451	941
75			Chak No 36 Abbasia	115	407	375	782
76			Chak No 37 Abbasia	358	1,343	1,235	2,578
77			**Chak No 38 Abbasia**				
			Zia Colony Chak No 38 Abbasia	72	289	265	554
			Murad Colony Chak 38-A	60	241	221	462
78			Chak No 39 Abbasia	220	837	769	1,606
79			**Chak No 3A**				
			Chak No 3 Abbasia	130	433	399	832
			Chak No 3A Colony	155	517	475	992
80			Chak No 40 Abbasia	129	551	507	1,058

Sr. No	Zone	Tehsil	Villages	HH	M	F	Total
81			Chak No 41 Abbasia	184	623	573	1,196
82			Chak No 42 Abbasia	303	979	900	1,879
83			**Chak No 43 Abbasia**				
			Chak No 43 Abbasia	334	1,201	1,104	2,305
			Chak No 43 Abbasia Colony	120	431	397	828
84			Chak No 46 Abbasia	237	840	772	1,612
85			Chak No 47 Abbasia	271	1,045	960	2,005
86			Chak No 48 Abbasia	134	517	475	992
87			**Chak No 4A**				
			Chak No 4 Abbasia	52	181	167	348
			Basti Chak 04A	65	227	209	436
88			Chak No 63 Abbasia	384	1,320	1,214	2,534
89			Chak No 64 Abbasia	157	540	496	1,036
90			**Chak No 65 Abbasia**				
			Chak No 65 Abbasia	171	588	541	1,129
			Chak No 65 Abbasia Colony	135	464	427	891
91			**Chak No 68 Abbasia**				
			Chak No 68 Abbasia	137	457	420	877
			Chak No 68 Abbasia Colony_1	180	600	552	1,152
92			Chak No 69 Abbasia	159	530	488	1,018
93			Chak No 75 Abbasia	362	1,320	1,214	2,534
94			Chak No 77 Abbasia	305	1,144	1,052	2,196
95			**Chak No 78 Abbasia**				
			Chak No 78 Abbasia New	55	195	179	374
			Chak No 78 Abbasia Old	145	514	472	986
96			Chak No 79 Abbasia	423	1,455	1,337	2,792
97			Chak No 80 Abbasia	262	1,010	929	1,939
98			Chak No 81 Abbasia	384	1,281	1,177	2,458
99			Chak No 82 Abbasia	261	1,006	925	1,931
100			**Chak No 83 Abbasia**				

Sr. No	Zone	Tehsil	Villages	HH	M	F	Total
			Chak No 83 Abbasia	424	1,193	1,097	2,290
			Chak No 83 Abbasia Colony	90	253	233	486
101			**Chak No 84 Abbasia**				
			Chak No 84 Abbasia	113	377	346	723
			Chak No 84 Abbasia Colony	105	350	322	672
102			Chak No 85 Abbasia Colony	250	834	766	1,600
103			Chak No 86 Abbasia	168	735	676	1,411
104			**Chak No 87 Abbasia**				
			Chak No 87 Abbasia	432	1,710	1,573	3,283
			Adda Chak No 87 Abbasia	222	879	808	1,687
			Basti Abdul Ghafooor	65	257	237	494
105			**Chak No 88 Abbasia**				
			Chak No 88 Abbasia Bara	199	653	601	1,254
			Chak No 88 Abbasia Chota	253	830	764	1,594
106			Chak No 89 Abbasia	93	295	272	567
107			Basti Noor Din	85	315	289	604
108			Adda Gulshan Farid	224	934	858	1,792
109			**Hayat Lar**				
			Basti Tok	212	740	680	1,420
			Basti Saleh Muhammad	75	262	241	503
110			**Kanjki Wala**				
			Basti Ghalo	86	336	309	645
			Basti Kukara	100	391	359	750
			Basti Malik Pervaiz Akhter	76	297	273	570
111			**Kotla Darigh**				
			Basti Haji Mehar Ali Drig	82	329	302	631
			Basti Abdul Rasheed Lar	50	201	184	385

Sr. No	Zone	Tehsil	Villages	HH	M	F	Total
			Basti Manzoor Ahmed Lar	67	269	247	516
			Basti Malik Lal Machi	75	301	277	578
			Basti Marral	145	582	535	1,117
112			**Kotla Khairey Khan** Basti Malik Allah Ditta Solangi	92	340	313	653
113			**Muradpur Sail**				
			Basti Buraha	70	252	231	483
			Basti Haji Kamal	63	227	208	435
			Basti Bhattian	63	227	208	435
			Basti Jam M. Mazhar Mah	65	234	215	449
			Basti Ameer Bux	50	180	165	345
			Basti Haji Abdur Rehman Khosa	70	252	231	483
114			**Tranda Gurgajj**				
			Taranda Gurgaij	109	454	418	872
			Basti Goth Mehtab Shah	153	638	586	1,224
			Khangah	103	429	395	824
			Basti Sadiq Khan Gorgaje	77	321	295	616
			Basti Sanaullah Khan	56	233	215	448
115			**Turkary**				
			Basti Azmat Lar	60	213	195	408
			Jindu Pir Kamal	465	1,647	1,515	3,162
			Tarukri	89	315	290	605
			Basti Allah Bux/M. Murad	78	276	254	530
			Basti Waryam Solangi	86	305	280	585
			Basti Imam Bux	69	244	225	469
116			**Firoza**				
			Chak 70/A Firoza	320	1,117	1,027	2,144
			Ghudam Wala Chak 70/A	130	454	417	871

Sr. No	Zone	Tehsil	Villages	HH	M	F	Total
117	South-1	Rojhan	Bhagsar	390	1,565	1,438	3,003
118			Basti Dhora	183	819	755	1574
119			Gianmal	646	2385	2202	4587
120			Dilber	1383	4387	4049	8436
121			Qadra Kass	326	1,104	1,015	2,119
122			Kotla Hasan Shah	513	2401	2216	4617
123			Rakh Qadra	459	1814	1674	3488
124			Mutafriq Mazari	398	1801	1662	3463
125			Rakh Sabzani	50	143	132	275
126			Safdar Abad	697	2392	2208	4600
127			Salim Abad	933	3299	3045	6344
128			Tariq Abad	581	2205	2036	4241
129	South-III	Bahawalnagar	Bonga Ihsan Bibi	200	500	300	800
130			Hasan Raika	250	500	300	800
131			Bhole Shah Hitar	55	400	200	600
132			Paran Wala	110	450	250	700
133			Chak Abdul Haq	300	1200	600	1800
134			Dhanraj Pura	270	1200	1100	3300
135			Jagga Sanatteka & Mini Sanatteka	250	1050	300	1550
136			Mosla	130	330	170	330
137			Pir Sikandar Otar	130	550	250	800
138			Jhulan Chistian	130	390	140	530
139			Gauspur	100	500	300	800
140			Amin Abad	149	486	408	894
141			Abrarah Uttar	80	250	150	400
142			Ali Gohar No. 326	70	255	95	330
143			Ramnagar	490	1500	800	2300
144			Hussain Abad Uttar	188	400	150	550
145			Huusain Abad HIttar	65	225	100	325
146			Gaman Dongi	81	251	240	491
147			Sharaf Din	60	150	80	230
148	Central-I	Pakpattan	Chak No.102/d	125	385	355	750

Sr. No	Zone	Tehsil	Villages	HH	M	F	Total
149			Chak No.87/d.	149	486	408	894
150			Bahwan Shah	153	865	853	918
151			Chak Ilahi Bux	100	400	200	600
152			Chak Murad Khan	170	523	497	1020
153			Chak Nazam Din	120	369	351	720
154			Gobind Pur Bahmni	1000	3659	2341	6000
155			Jand Wala	163	509	469	978
156			Nahla Abad	150	472	428	900
157			Dhamiana	115	3965	295	690
158			Chak No.4 S.P.	180	564	516	1080
159			Chak Quder Tullah	83	298	200	498
160			Chilli Mamdana	135	426	384	810
161			Dada Ahluka	200	696	504	1200
162			Ghar Taj	260	795	765	1560
163			Ghazi Mardan	160	495	465	960
164			Nura Ahluka	190	695	445	1140
165			Ghuri	150	542	358	900
166			Arazi Tek Chand	170	516	504	1020
167			Chak 103/D	200	2500	1500	4000
168	South-II	Alipur	Baqar Shah Shumali	980	3028	2852	5880
169			Bande Shah	600	1854	1746	3600
170			Maqwal Hadeir	900	2781	2619	5400
171			Nehal Wala	157	485.0	457	942
172			Nauhabad	250	772.0	728	1500
173			Khayara	4	14	13	26
174			Mithan Wali	140	433	407	840
175			Ali Wali	1800	5562	5238	10800
176			Kotla Agar	210	649	611	1260
177			Makhan Bela	400	1236	1164	2400
178			Bet Barrah	230	711	669	1380
179			Marian	135	417	393	810
180			Bet Mir Ahmad Jamal	4	11	11	22
181			Kotla Ghulam Shah	155	479	451	930
182			Sirki	207	640	602	1242
183			Tibba Barrah	250	772	728	1500

Sr. No	Zone	Tehsil	Villages	HH	M	F	Total
184			Bet Bagh Shah	140	433	407	840
185			Yare Wali	450	1390	1310	2700
186			Kohar Faqiran	500	1545	1455	3000
187			Kotla Afghan	160	494	466	960
188			Gagare Wali	515	1591	1499	3090
189		Shujabad	Wahi Riki	290	884	856	1740
190			Basti Dad	450	1372	1328	2700
191			Chah Miran Khan	300	914	886	1800
192			Nawan Chak	275	838	812	1650
193			Mohan Pur Sharqi	310	945	915	1860
194			Sangrai	325	991	959	1950
195			Shahpur Ubha	1270	3871	3749	7620
196			Sarai	155	472	458	930
197			Shah Pur Shumali	181	552	534	1086
198			Nasir Pur	210	640	620	1260
199		Taunsa	Aqupur	275	850	800	1650
200			Arakhar Dao	3	11	10	21
201			Rind Wala	420	1298	1222	2520
202			Baghon Wala	5	16	15	31
203			Bakhri	6	19	18	37
204			Basti Habib	6	19	18	37
205			Basti Nasir	3	11	10	21
206			Basti Usman Shah	450	1390	1310	2700
207			Berand	280	865	815	1680
208			Bet Obai	3	8	8	16
209			Bodo Mian	140	433	407	840
210			Chak Sohanra Bacha	225	695	655	1350
211			Domra Janubi	250	772	728	1500
212			Domra Shumali	325	1004	946	1950
213			Ghadi Sandila	6	19	18	37
214			Ghali	100	309	291	600
215			Jalal Khan	120	371	349	720
216			Jhok Chhapri	450	1390	1310	2700
217			Jhok Mangla	390	1205	1135	2340
218			Jhok Rohal	70	216	204	420
219			Jhok Yaran	3	11	10	21
220			Jinpur	80	247	233	480
221			Khitran Wala	350	1081	1019	2100

Sr. No	Zone	Tehsil	Villages	HH	M	F	Total
222			Kotla Marrani	5	16	15	31
223			Rakh Sanjar	100	309	291	600
224			Rakh Zor	200	618	582	1200
225			Wani	120	370	350	720
226			Mahnda	755	2333	2197	4530
227			Mirkhar	2500	772	728	1500
228			Mundrani	680	2101	1979	4080
229			Pukan	160	494	466	960
230			Rakh Mari Pachaudi	240	742	698	1440
231			Langah	3	11	10	21
232			Rakhana	3	11	10	21
Total				**66,350**	**219,268**	**195,800**	**411,718**
Source: Census 2023, PBS							

4.6.2 Findings of Socioeconomic Survey

A. Occupational Status

Due to the availability of fertile land in most of the tehsils, agriculture is the primary occupation in the project area, followed by labour as the second largest profession because of weak socio-economic conditions of the population. However, in Taunsa most of the people are engaged in labour. Similarly, in Noorpur Thal as the mosty of the land is infertile therefore Labour is the second largest profession. The occupational trend in different tehsils can be observed in Figure below which presents percentages of the various occupations in the project area, based on interactions with project communities during field visits, consultations and limited surveys.

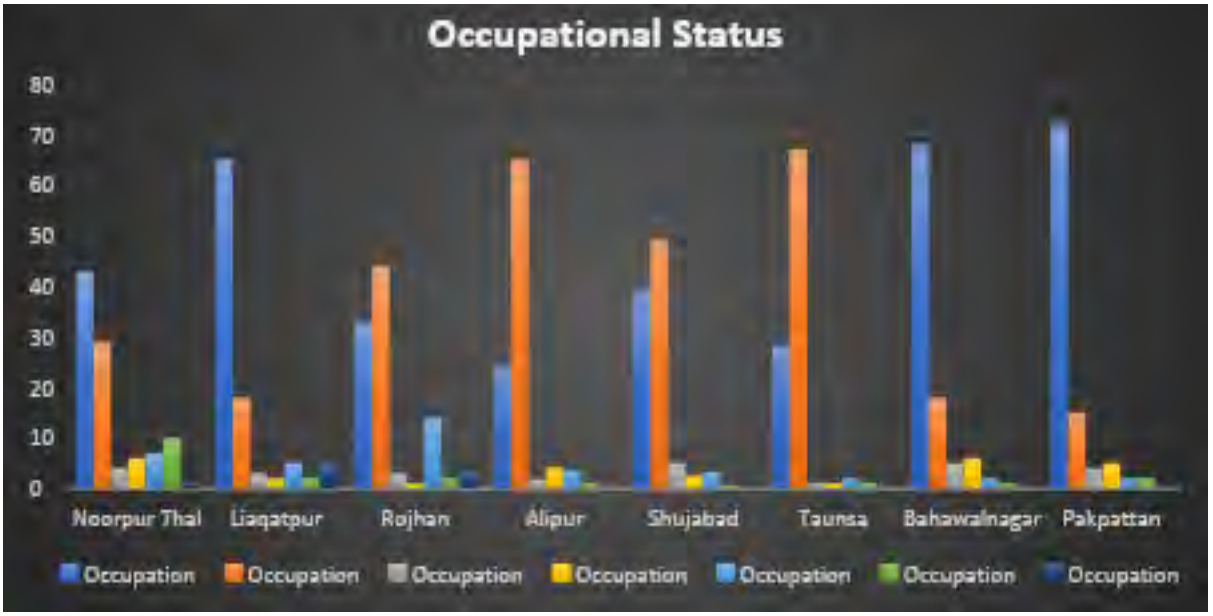

Figure 8: Occupational Status of the Respondents

B. Religion

Islam is the dominant religion in Punjab where, according to the 2023 census, Muslims constitute 97.75% of the population. The minorities include Christians (1.93%), followed by Hindus (0.20%), and other minority groups (0.12%). Based on the primary data collected mostly respondents were Muslims. Whereas few minorities were observed in Liaquatpur Tehsil.

Figure 9: Occupational Status of the Respondents

C. Caste System

Several castes/clans have been reported in the project area. In Tehsil Noorpur Thal, Rajput, Bhaghoor, Joiya, Gondal, Khattak and Awan are major tribes. In Tehsils Taunsa, Alipur, and Shujabad, Baloch are in majority, whereas, Rajput, Kanju, Jutt, Syed, and Awan are also found. In tehsil Bahawalnagar and Pakpattan, Chishti, Bodla, Arain, Bhatti, Bhindara, Hotiana Wattoo, Gardezi Syed, and Joiya are prominent castes. Despite the concentration of one or two castes in some tehsils, no significant disputes exist among the different castes.

D. Income Levels

The monthly income earned by individuals from various sources varies widely ranging from less than Rs. 20,000 to above Rs. 50,000. Majority of the population reported that their income barely covers the basis of household expenses.

In general, the agriculturists and landlords in the project area are well to do, with incomes exceeding Rs. 50,000 per month. Similarly, due to rich land fertility and high yields, the landlords in Tehsils, Alipur and Shujabad earn more than Rs. 50,000 per month. Whereas, majority of the population in tehsils, Bahawalnagar, and Alipur are tenants which are engaged in agriculture sector but only receive petty amount in lieu of their services, therefore

they earn Rs. 20,000-30,000 per month mostly. In Tehsil, Noorpur Thal, Liaqatpur and Rojhan most of the respondents reported an income range of 20,000–50,000 PKR, as the majority work as farmers or laborers. A significant proportion also earns below 20,000 PKR due to poverty and limited livelihood opportunities. Low soil fertility further restricts agricultural productivity, especially in Noorpur Thal, where households rely on cultivating seasonal crops for their income. Moreover, in remaining Tehsils laborers are financially vulnerable, with limited income and resources to support their families. Percentage of the average monthly income of the respondents is shown in **Figure 10**.

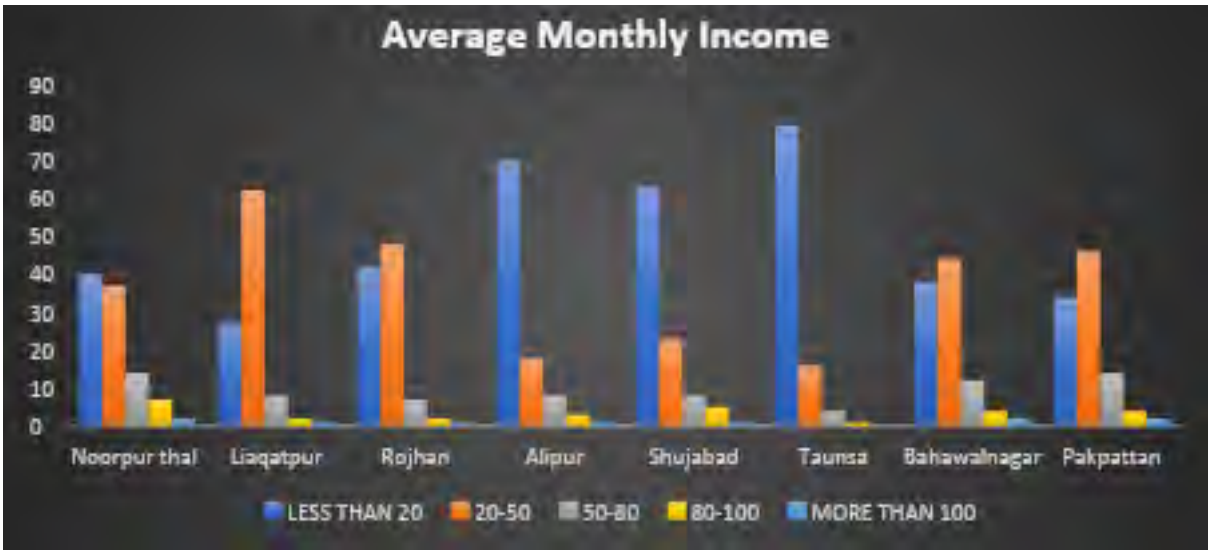

Figure 10: Monthly Income of the Respondents

E. Source of Drinking Water

The analysis shows that handpumps are the dominant source of drinking water across all villages. Most residents rely on deep handpumps installed at depths of around 200 ft for drinking water, as shallow groundwater near ground level is brackish. Handpumps installed within houses in Liaqatpur, typically at depths of 25-40 ft, yield brackish water and are not suitable for drinking purposes. Therefore, the local community depends on deep handpumps located outside their houses to meet drinking water needs. Borehole-motor usage is comparatively lower but remains a significant secondary source, particularly in Noor Pur Thal.Rojhan and Pakpattan. Piped water supply is limited and observed only in Alipur and Noorpur Thal, indicating inadequate network coverage. RO filter plants are negligible, and reflecting minimal reliance on treated water systems in the study area.

Figure 11: Source of Drinking Water

F. Satisfaction with household water quality

The analysis indicates low satisfaction with household water quality across all villages, with a clear majority of respondents reporting dissatisfaction. Liaqatpur and Rojhan shows that 100% of households are not satisfied with water quality. Even in relatively better-performing villages, satisfied households do not exceed 16%, highlighting widespread concerns over drinking water quality.

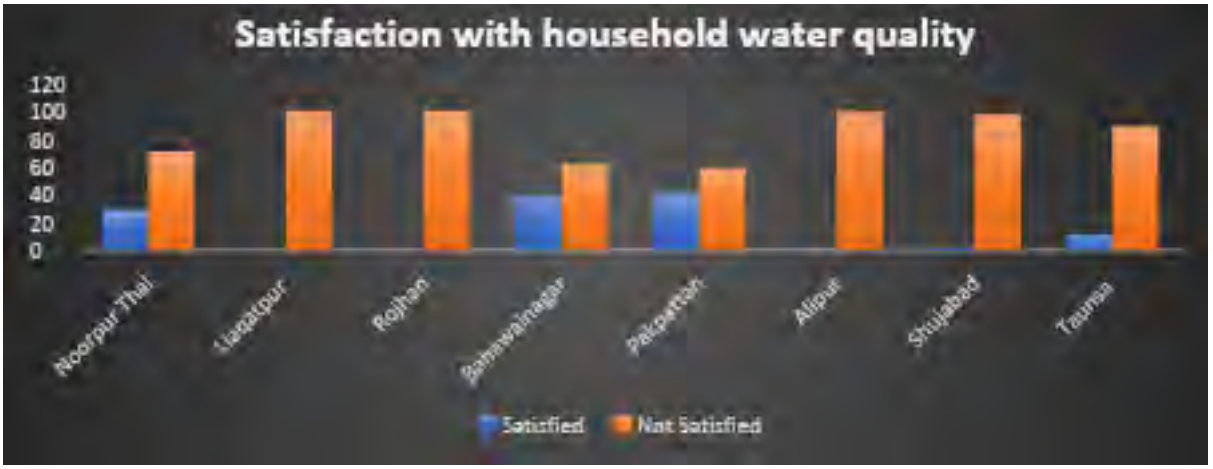

Figure 12: Satisfaction with household water quality

G. Type of Sewerage System

The analysis shows that open drains are the predominant sewerage system in most villages, indicating inadequate sanitation infrastructure. Septic tanks and kacha soakage pits are mainly present in Noorpur Thal, Bahawalnaga, Pakpattan, Alipur, Shujabad and Taunsa where sewage is seep down into ground however, few drains were also present which were

extended to some feet from houses and ultimately seep down to groundwater. Villages where drains were present their wastewater was ultimately discharge into open fields or nearby nullahs. Sewer lines are limited and observed in Taunsa, Shujabad and Alipur. Overall, drainage facilities are present in the majority of villages; however, many drains are clogged due to solid waste accumulation and sediment deposition. Poorly designed and uncovered drains have resulted in sewage overflow and stagnation on streets, adversely affecting sanitation conditions.

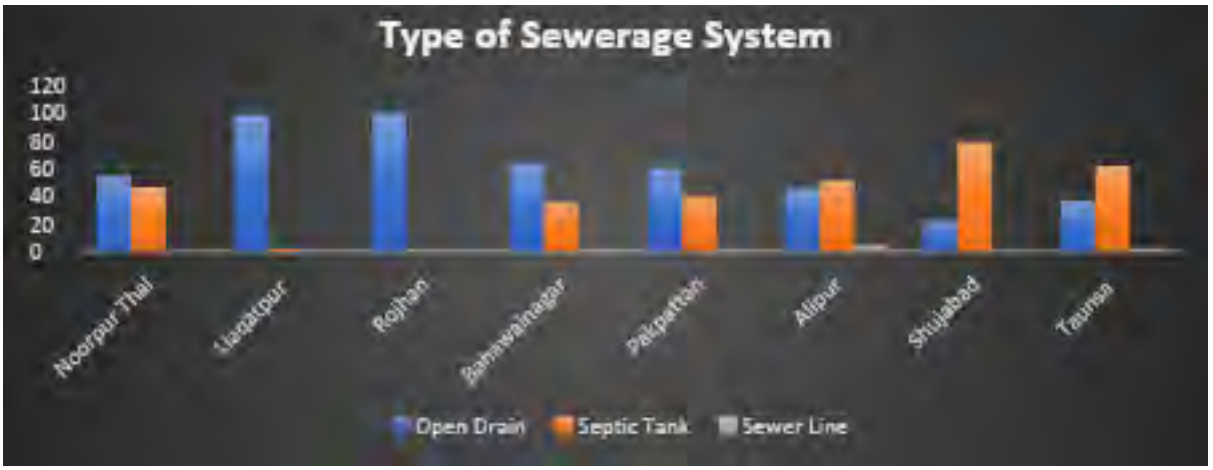

Figure 13: Type of Sewerage System

H. Type of Sanitation Facility

The analysis indicates that toilet facilities are available to the majority of households in all villages. However, open defecation was also observed in Rojhan, Alipur, Noorpur Thal, and Taunsa. Rojhan and Alipur, reflecting gaps in sanitation access and behavior. In remaining Tehsils washroom were present according to the locals during public consultation. Overall, the data highlight the need for improved sanitation facilities and awareness to achieve full coverage.

Figure 14: Type of Sanitation Facility

I. Solid Waste Facility

The analysis shows that solid waste management facilities are fully available in Taunsa, Alipur, and Shujabad, indicating relatively better municipal services. Liaqatpur and Noorpur Thal have partial coverage, with a notable proportion of households lacking access to waste facilities. In contrast, in remaining tehsils faces a severe deficiency, where mostly of households report the absence of solid waste management services.

Figure 15: Type of Solid Waste Facility

J. Housing Construction Pattern

During field visits, it was observed that the proposed project areas lack basic amenities. However, the trend *of kacha* houses has diminished and most people have built *pacca* houses with RCC roofs, stone walls with cement mortar, cement plastering & flooring. Similarly, In Noorpur Thal, many households have recently constructed new homes to minimize losses during the rainy season. A few semi-pacca houses and kacha houses were reported in all tehsils.

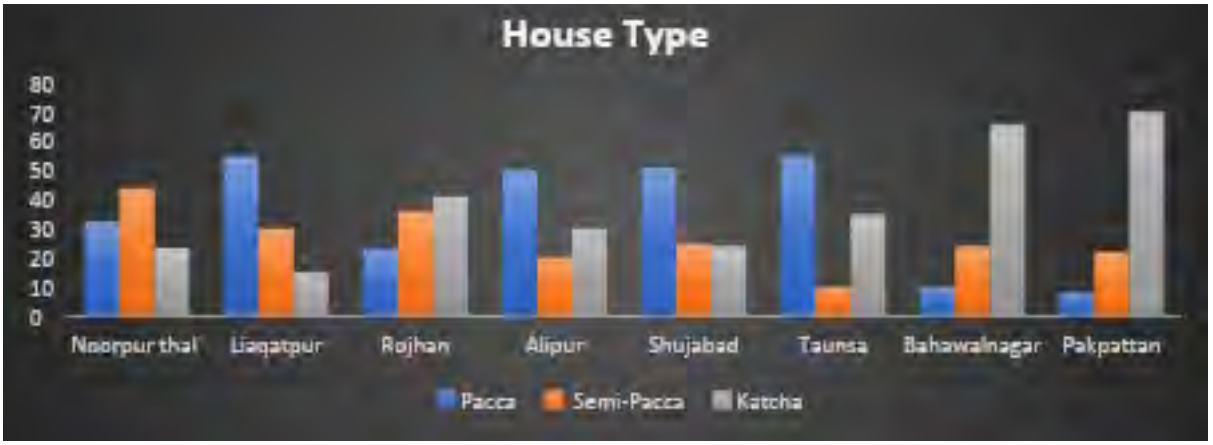

Note: Kacha = A structure constructed of mud.

Semi-Pacca = A structure constructed of a mixture of mud and bricks.

Pacca = A structure constructed of concrete and cement blocks/bricks.

Figure 16: Type of Construction of House

K. Mode of Transport

Public transport facilities are not sufficiently present in the South and North area and people use their personal motorbikes, cycles, and cars, etc. for traveling. However, in Center, people also use Rickshaws. In case of emergencies, they call Rescue 1122 and get aid in 5-10 minutes of time. The project activities are unlikely to impact the transportation modes. However, it will be ensured that access of Rescue 1122 vehicles is not hindered due to project activities.

L. Communications

The project area has telephone connections for internet services and mobile phone coverage is also available, allowing people to access to the internet through their mobile phones. The access roads to all the project sites are in good condition, although the situation of internal streets and roads is poor. The village roads and streets are either metaled, soling, or unpaved. Motorways pass through the project Tehsils Alipur and Shujabad (the project villages are within 5-25 km distance from the motorway). In Tehsil, Shujabad and Pakpattan Railway network is also available. Moreover, National and Provincial Highways are present in all tehsils of the project area.

M. Health Conditions and Facilities

The poor health conditions in the project area are one of the reasons for initiating the proposed project. The quality of potable water available throughout the project area is highly compromised, as indicated in Section 4.5.4. This has led to the prevalence of several waterborne disease and stunted growth in the project area. The most common diseases in these areas include typhoid, cholera, hepatitis, diarrhea, intestinal worms and skin allergies.

The project area has varying levels of access to health facilities. Since DHQs are present - in addition to THQs - in Pakpattan, Taunsa, and Bahawalnagar therefore they have good health facilities. In tehsil Shujabad, health facilities are above average due to their proximity to the DHQs. Whereas, in Tehsils Noorpur Thal and Alipur THQs are present but are not fully functional. However, Basic Health Units (BHU) are also present in most of villages of project area, providing basic medical services to the population. In case of non-availability of BHU in a village, people of the village approach the nearest BHUs in other villages.

N. Educational Facilities

Primary, Middle and High schools are present in some of the proposed villages. The list of educational facilities located close to the proposed construction and excavation sites is provided as social sensitive receptors in Table-18.

O. Basic Civic Amenities in the Project Area

The proposed project area lacks basic civic amenities including water supply, sewerage system, stormwater drainage, solid waste management, gas supply. Telephone connections are available in the project area, but are limited in some areas. The only facility available in the proposed project area is electricity, which is also inadequate as people suffer long hours of load-shedding and low voltage issues.

P. Mechanism of Conflict Resolution

During the field survey, the project team conducted discussions with local communities to identify the types of disputes commonly prevailing in the project area. The survey revealed that disputes over land, water resources, and property inheritance are the most common causes of conflict. These disputes tend to escalate quickly and often result in violence, thereby causing loss of life, property damage, and displacement of communities. In some cases, the police and judicial system have been ineffective in resolving these conflicts, leading to a lack of trust in state institutions, especially in southern region of project area. In addition, inter-caste tensions, religious differences, and political affiliations may also contribute to the conflict, though no major fault-lines were observed along these.

At the community level in project area, conflict resolution is often handled through informal methods of mediation and negotiation. Local elders, community leaders, and religious figures play a significant role in resolving conflicts in proposed project villages. The traditional methods of dispute resolution include Jirgas (councils of elders) and Panchayats also called Kaths (village councils). These methods often involve face-to-face meetings, with both parties presenting their case and a neutral third party facilitating the resolution. In addition to these informal methods, legal systems such as the Punjab Local Government Act 2019 and the Alternative Dispute Resolution Act 2017 also provide a formal mechanism for resolving disputes. However, the use of formal systems is limited in project areas due to lack of accessibility, awareness and enforcement of aforementioned acts. Overall, conflict resolution at the community level in project area is a combination of traditional and modern approaches, with a focus on finding mutually agreeable solutions that maintain social harmony. The proposed GRM system of the project will also strengthen present conflict resolution systems (Village Councils, Jirgas, Panchayats etc.) of the project area. The proposed GRM system will not only improve but also make the Village Councils, Jirgas and Panchayats inclusive and will also sensitize the community about GRM.

Q. Presence of NGOs/ CBOs

There are several INGOs, NGOs and CBOs present in the project area. According to stakeholder consultations and institutional stakeholder consultations, Punjab Rural Support Programme (PRSP) and National Rural Support Programme (NRSP) are working in Tehsils Liaqatpur and Rojhan. The scope of both NGOs is WASH, which is also within the mandate of PRMSC. Moreover, UNICEF, WaterAid Pakistan, JICA, Save the Children, WHO, International Rescue Committee (IRC), UNOPS, Muslimaid, Qatar Charity, Plan International have also been reported to be working in Tehsil Taunsa, Noorpur Thal, in WASH related sector. Furthermore, Community-Based Organizations (CBOs) were also reported in Tehsil

and Bahawalnagar to support marriages, funeral prayers, and other financial needs of the community. CBOs can play an important role in social mobilization, behavior change in target villages, and tariff collection and O&M of the schemes.

4.6.3 Results of Gender Situation Survey

- A gender situation analysis was conducted in all 232 villages/sub-villages across 08 tehsils through focus group discussions. The purpose of this qualitative survey was to identify women-related concerns, gender roles and responsibilities, education levels, occupational status, involvement in agriculture and livestock, access to health facilities, willingness to pay, access to power and resources, prevalence of gender-based violence, and needs assessment.
- Traditional gender roles and responsibilities in rural Punjab Center, North, and South are almost identical, with women primarily responsible for domestic and caregiving tasks and men serving as the primary breadwinners. Although females are engaged in agricultural and subsistence farming operations and livestock-related activities, they encounter obstacles in controlling resources, accessing land, credit, and other resources, limiting their productivity and economic opportunities in rural settings.
- Waterborne diseases are a significant public health concern for females and children in the surveyed areas, according to focus group discussions.
- Women-headed households are not uncommon in the surveyed areas, especially in South and North where men migrate for work to other cities or abroad.
- The majority of female respondents in South, North, and Center areas are not involved in decision-making processes, with their decisions limited to day-to-day household affairs. Males make major and decisive decisions, while in the center, some respondents reported that decisions were made through mutual consultation and understanding.
- Although there were few reported violent incidents in South, respondents in other areas considered gender-based violence an act of boldness rather than a crime. The consultation found a lack of knowledge about sexual harassment (SH) and sexual exploitation and abuse (SEA) as crimes and how to report this while having social pressure to keep these incidents secret and treated as a matter of honor.

5 PUBLIC CONSULTATION

5.1 General

This section describes the outcomes of the public consultation sessions held with different stakeholders that may be directly or indirectly affected by the proposed project. The consultation with community and institutional stakeholders during project planning, designing and implementation stages is a key to sustainable development. Likewise, participation of stakeholders is essential to meet the objectives of meaningful consultation for preparation of ESMP.

5.2 Objectives and Principles of Consultation

The consultation process provided a forum where information relevant to the project was disseminated to the stakeholder. This participation enabled the integration of local and indigenous knowledge into the project design. This not only fosters goodwill and success in the project but also leads to a conflict- free project implementation.

The stakeholders including local community of 232 villages, government representatives, other regulators and the NGOs were met to appraise and discuss the environmental and social perspective of project activities. Their valuable concerns and suggestions were noted and thereafter incorporated in the Environmental and Social Management Plan.

The objectives of the consultation process were to:

- Identify, Inform and involve all stakeholders and local residents including females, minorities and disables, in the consultative and participation process;
- Share information with stakeholders on the construction of the proposed project and expected impacts on the physical, biological and socio-economic environment;
- Understand stakeholders' concerns and perceptions regarding various aspects of the project, including the existing available facilities and the likely impacts of construction and operation related activities of proposed Project; and
- Provide an opportunity to the public to provide valuable suggestions in the project design in a positive manner.

5.3 Consultation and Participation Process

To ascertain the perceptions of different stakeholders about the project scope, its implementation, operation and evaluation, consultation meetings were conducted. The consultation process was carried out in accordance with the World Bank Guidelines on public consultation. A series of consultation sessions were carried out with stakeholders (Govt. departments, farmers, teachers, businessman, women etc.), in June 2025 & September 2025. Total 349 stakeholder consultation sessions were conducted details of sessions are presented in Annex-7.

The project team chose sites that are easily accessible and barrier-free to accommodate all persons. The consultative sessions/meetings are held mostly at Monasteries (Dera) with both men and women separately. The minutes of the meeting from the focus group

discussions and community meetings have been noted down (listed in table 21, table 22 and table 23) and can be shared with the participants (that chose to share their contact information) and the community. These consultative sessions were designed to exchange information, to discuss the strengths, weaknesses, opportunities, and threats of an idea or project. The consultation meetings proved very useful in information sharing and consensus building.

5.4 Identification of Stakeholders

Project stakeholders were engaged in the review and discussions on various project aspects, social and environmental issues at the early stage of impact assessments for feedback. There are two categories of stakeholders in the project:

Individual/Community Stakeholders

Project beneficiaries for instance, Residents of the project area, Shopkeepers, Employees, Customers, Road Users, Vulnerable and Gender.

Institutional Stakeholders

- Board of Revenue and Tehsil and District Administration, Environmental Protection Agency Punjab (EPA), Agriculture Department, Livestock Department Punjab, Tehsil Headquarter Hospital THQ.

5.5 Information Dissemination

Following information was discussed and disclosed to the stakeholders during the consultation meetings:

- Introduction of the project;
- Description of various project components, their activities and impacts;
- Discuss social and environmental impacts;
- Needs, priorities and reactions of the affected people regarding the proposed projects' impacts; and
- Need of Grievance Redress Mechanism (GRM) in all villages to address the issues & concerns of stakeholders.

For information dissemination to community, culturally appropriate techniques and local language was used.

5.6 Methods of Public Consultation

Public Consultations were carried out in order to establish stakeholder's opinions regarding project implementation. The following methods were used for public consultation and stakeholder's participation:

5.7 Approach Adopted for the Consultation

To hold the meetings, people were informed one day before the meeting to assemble in the villages. In addition, the Tehsil Office team contacted the council members and community representatives of each village and informed about the purpose of these consultation meetings. The representatives played a positive role in information dissemination to locals of villages. The meetings held in an encouraging environment where people expressed their concerns and views freely. Formal meetings and interviews were also conducted with female, vulnerable and disabled of the affected community, to explore their needs, problems and priorities related to project execution. In addition to the formal meetings, individual meetings/interviews were also held with the affected females to efficiently involve them in planning process.

5.8 Stakeholders Concerns towards the Project

Concerns raised by the participants, particularly with regard to environmental and social impacts of the project have been listed in following Tables which shows concern and responses as derived from scheme wise consultation meetings.

5.8.1 Concerns and Issues

Following **Table 21** shows concerns and responses of public consultation meetings.

Table 21: Findings of the Consultation Meetings

Sr. No	Concerns Raised	Locations	Response
1	The water is not drinkable and there are several waterborne diseases including intestinal issues	All project villages	Provision of clean water is already part of our project, so waterborne diseases shall be reduced and there will be an improvement in public health.
2	Will employment opportunities be generated for locals during the construction phase?	All project villages	It will be made sure that 75% of the workforce will be employed from the sub-project area.

Sr. No	Concerns Raised	Locations	Response
3	Arrangements should be made to suppress dust, curtail high-noise activities, and control the vibrations caused due to machinery, to protect the community's health	All project villages	Regular sprinkling of water will be carried out over the loose soil to suppress the dust, the noisy activities will not be planned at night and the community will be informed before the execution of any activity that would generate vibrations
4	Privacy of people should be upheld during construction phase of the sub-project.	All project villages	Contractor will provide trainings to workers regarding gender and privacy issues.
5	Construction activities should be minimized during schools' opening and closing times.	All project villages	Contractor will be bound to minimize construction activities during schools' opening and closing times.
6	Will there be any closure of roads during construction phase?	All project villages	In case of road closures, the nearby community will be informed beforehand and alternative routes will be provided.
7	Solid waste production during construction time is a major concern and that should not be piled up in the project area.	All project villages	The construction and other waste generated at the site shall be collected, stored and transported to the final disposal site by the contractor on daily basis.
8	Will there be any tree cutting?	All project villages	No, no trees will be cut during the execution of the project.
9	The construction activities will cause inconvenience to local residents due to hindrance in routine activities	Alipur, Shujabad, Taunsa	The contractor will ensure that construction work do not create disturbance for local people's access to the local route and their routine life activities.
10	Will this project cover all households in the village?	Alipur, Shujabad, Taunsa	Yes, all households located in the deh boundary in the selected villages will be covered.
11	Who will bear the cost of operation and maintenance (O&M)?	Alipur, Shujabad, Taunsa	The community pay O&M in the form of water charges per month. Government or project may provide initial support.
12	What about wastewater and drainage system?	Alipur, Shujabad, Taunsa	Proper drainage and wastewater disposal points will be included where technically and socially feasible.
13	Will there be water meters or fixed charges?	Alipur, Shujabad, Taunsa	There will be fixed water charges. The Client may re-consider it whether meter or fixed charges.
14	What if the water supply stops or gets damaged?	Alipur, Shujabad, Taunsa	The complaint can be registered in the office.
15	Local people claims that the construction of the project will lead to noise pollutions and social disturbances during construction of the water supply.	Liaqatpur Rojhan	Regular maintenance of construction machinery to prevent excessive noise. Provide early and continuous information disclosure.

5.9 Consultations with Female Community Members

Following **Table 22** shows concerns and responses of gender consultation meetings.

Table 22: Findings of the Female Consultation Meetings

Sr. No	Community Consultation with Women	Locations	Response
1	Most of the women have to go out to the watercourses for washing clothes.	All project villages	This issue will be resolved by executing this project after the provision of water at the doorsteps.
2	Many females raised their concerns about the health issues due to poor water supply system. Usage of hand pumps and boreholes water, may cause many diseases like kidney, hepatitis, liver problems and diarrhea.	All project villages	Waterborne disease will be reduced and there will be an improvement in public health with the provision of clean and healthy drinking water.
3	Inadequate sanitation facilities and the need to travel long distances to collect water exposes women and girls to different kind of harassment.	All project villages	To a significant extent, the issues of different kind of harassment will be mitigated through the implementation of the project, which seeks to facilitate doorstep access to clean water sources.
4	Constrained accessibility to clean water and sanitation facilities imposes impediments in the effective management of hygiene during pregnancy and childbirth. Additionally, it affects the ability to care for newborns, thereby contributing to child stunting.	All project villages	The project will ensure the provision of improved WASH conditions to address these concerns for improved women's and their children's health as reduction in child stunting is the core objective of the project.
5	Fetching water is the responsibility of women and they daily cover the passage of 3-4 kilometers to fulfill this duty.	Taunsa	The infrastructure of the said project will make clean water more accessible and reduce the time and effort required for water collection.
6	The burden of fetching water negatively impacts on women's health, as well as limit their ability to pursue education, employment, and other opportunities.	All project villages	The implementation of the PRSWSSP project will reduce the burden of women, improve the quality of life and free up time for other pursuits, including education and income-generating activities.
7	Increase in water borne disease due to poor sanitation or unsafe water sources.	Liaqatpur	The project aims to mitigate this by providing safe and treated drinking water to the community.

5.10 Consultation with Institutional Stakeholders

Table 23 shows the concerns of institutional stakeholders.

Table 23:Concerns of Relevant Government Departments

Sr. No.	Department	Coverage	Points of Discussion / Apprehensions	Response
1.	**Environmental Protection Department**	Punjab.	The project team described the project location and proposed activities to District Environmental Officer and inquired about their apprehensions/ suggestions regarding the project; ● In conducting ESMP, Scoping sessions, and Individual interviews should be conducted with all stakeholders. ● Social issues regarding private land acquisition, were discussed in detail. ● Baseline should be developed separately according to the baseline conditions. ● Public Hearings must be done so that stakeholders who have different types of stakes along with their apprehensions can be listed down easily.	All the suggestions shall be incorporated. Institutional consultations are already underway and efforts shall be made to take all the stakeholders on board.
2.	**Board of Revenue**	Punjab	The Project team described the project location and proposed activities and also briefed them about the requirement of state land for the construction of infrastructure in the project villages. Moreover, consultation meetings were also conducted with Tehsil and District Administrations of almost all the areas of the project.	The Board of Revenue and the respective Tehsil and District officials promised their full cooperation.
3.	**Municipal Committee**	Project Tehsils	The Project team described the project location and proposed activities Tehsil Manager and Assistant Manager and inquired about their apprehensions/ suggestions regarding the project; ● Discussion on field planning and effective approach to adequately cover all the field aspects and collect requisite data. The possible constraints in data acquisition were discussed and an effective way out was decided.	Discussed the scope and main features of the project.
4.	**Tehsil Headquarter**	Project Tehsils	The project team described the project location and proposed activities to MS Hospital and inquired about their apprehensions/ suggestions regarding the project;	The objective of the proposed project is to provide clean drinking water to all the residents of the selected villages at their doorsteps through a

Sr. No.	Department	Coverage	Points of Discussion / Apprehensions	Response
			● Show some serious concern regarding waterborne diseases. ● Every third person in Tehsil Bhawana suffers from Hepatitis. Due to the lack of infrastructure and transportation facilities in villages, it becomes difficult for the patient to reach the THQ.	piped network. Waterborne diseases will be resolved after the implementation of this project.
5.	**Agriculture Department**	Punjab	The Project team described the project location and proposed activities Field officer inquired about their apprehensions/ suggestions regarding the project; ● Field officer talked about the major crops Wheat and cotton cultivated in the project area. ● The wastewater should not be used for agriculture purposes without treatment ● Treated water is used for irrigation purposes Only individual-level solar tube well is present	PRMSC will ensure that wastewater will be used for irrigation (if needed) after adequate treatment.
6.	**Irrigation Department**	Punjab.	The sub-project details were shared with the representatives of the Irrigation department to obtain land for project activities. The Project team described the project location and proposed activities to Executive Engineer and inquired about their apprehensions/ suggestions regarding the project; ● The wastewater should not be used for agriculture purposes without treatment ● Treated water is used for irrigation purposes Treated waste should not be disposed of in canals.	PRMSC will ensure that wastewater will be used for irrigation (if needed) after adequate treatment. No wastewater is going to be disposed of in any canal/ nearby water body.
7.	**Public Health Engineering Department**	Punjab	The Client team described the project location and objectives, as PHED is also working in the same domain it was requested to share their work plan for the relevant tehsils with PRMSC to avoid duplication of services or infrastructure. Moreover, PHED shares	Lessons learned will be considered in t project planning and designing phase to improve service delivery.

Sr. No.	Department	Coverage	Points of Discussion / Apprehensions	Response
			the lesson learned to improve service delivery.	
8.	**Livestock Department**	Punjab	The project team described the project location and proposed activities Deputy Director Livestock inquired about their apprehensions/ suggestions regarding the project; Waterborne disease and viral disease in animals were discussed	The proposed project will provide clean drinking water to all the residents of the selected villages and the provision of water for portable use include water for the animal's activities. Waterborne diseases in animals will be resolved after the implementation of this project.
9.	**Fisheries Department**	Punjab	The project team described the project location and proposed activities Field officer inquired about their apprehensions/ suggestions regarding the project: Deputy Director District Office tells about the breed of fish in that area.	No wastewater is going to be disposed of in any nearby water body. So, no aquatic life is going to be affected by this project.
10.	**Department of Forest**	Punjab	The project team described the project location and proposed activities DFO and inquired about their apprehensions/ suggestions regarding the project.	There is no forest in the project boundary or near the project boundary that is going to be affect.

5.11 Consultation with NGO

There are several INGOs, NGOs and CBOs present in the project area. According to stakeholder consultations and institutional stakeholder consultations, Punjab Rural Support Programme (PRSP) and National Rural Support Programme (NRSP) are working in Tehsil Kehror Pakka and Khairpur Tamewali. The scope of both NGOs is WASH, which is also within the mandate of PRMSC. Moreover, UNICEF, WaterAid Pakistan, JICA, Save the Children, WHO, International Rescue Committee (IRC), UNOPS, Muslimaid, Qatar Charity, Plan International have also been reported to be working in Tehsil Taunsa and Noorpur Thal, in WASH related sector. Furthermore, Community-Based Organizations (CBOs) were also reported in Tehsil Bahawalnagar to support marriages, funeral prayers, and other financial needs of the community. CBOs can play an important role in social mobilization, behavior change in target villages, and tariff collection and O&M of the schemes.

5.12 Pressing Needs of the Consulted Villages Suggested by Local People

Local people were consulted to determine the most pressing needs in the project area as perceived by them. The most important needs identified were the provision of water supply and sewerage systems, as well as schools, hospitals/dispensaries, and vocational training

institutes for construction work. Due to restricted mobility, locals suggested that a friendly grievance mechanism be developed in all villages to address their concerns during the construction period. Additionally, they recommended that guidance and support be provided to local people for registration of complaints in proposed grievance mechanism.

5.13 **Disclosure of ESMP**

Public disclosure enables affected groups and interested parties to understand likely implications of the project and to provide input into project design. It promotes dialogue among stakeholders i.e., government, community, NGOs and implementing agencies. As per OP 4.01, the environmental and social aspects must be discussed with the stakeholders.

The objectives of public disclosure are to aid meaningful public consultation and to ensure transparency of World Bank operations to its stakeholders and constituents.

The safeguard documents will be disclosed on the website of PRMSC and on the World Bank external website.

Presentations containing project information and relevant aspects of public interest will be delivered to the public. Furthermore, project brochures, handouts of presentations, and executive summaries of ESMP in Urdu and English languages will also be distributed to the public.

After the approval, Copies of the ESMP shall be made available to communities and interested parties in accessible locations through local government authorities, (e.g., Village councils, District Offices etc.)

6 ANTICIPATED ENVIRONMENTAL IMPACTS & MITIGATION MEASURES

6.1 General

This chapter identifies the beneficial as well as the potentially significant adverse environmental and social impacts of the proposed project activities during design/ pre-construction, construction and operational phases of the proposed project on the physical, ecological and socio-economic domains of the environment. The appropriate mitigation and remedial measures are proposed in this chapter. A brief description of each aspect and the affected environment in the project area are presented below.

6.2 Scoping of Impacts

Potential environmental and social impacts from the proposed Project on key environmental and socio-economic features were identified through the following actions:

- Demarcation of the Area of Influence (AoI);
- Desk study of engineering investigations, studies and designs;
- Environmental monitoring of air, noise, surface water, wastewater and groundwater;
- Detailed review and analysis of primary and secondary data available for all environmental parameters in Project area such as physical, ecological and social resources;
- Socio-Economic survey to assess the extent of land acquisition, occupation, income and poverty levels of the affected households;
- Consultations with executing and implementing agencies, local government, affected community, and traditional and religious leaders of the community;
- Stakeholder consultations with relevant departments, government agencies, NGOs and locals; and
- Knowledge assimilation of international best practices on environmental assessment of infrastructure projects.

6.3 Methodology

Selection of an appropriate and customized methodology for the impact assessment is critical for the ESMP study. The impacts have been assessed based on the proposed project life cycle i.e., in Pre-Construction, Construction and Operational and Maintenance (O&M) stages. For the identification of the potentially significant and non-significant environmental and social impacts, different tools were utilized as detailed below:

6.3.1 Screening Checklist

Based on the findings of desk studies and processed satellite imageries, screening checklists were prepared to screen out the potentially significant adverse environmental

and social impacts during pre-construction, construction and operational phase of the proposed project. The objective of the impact screening is to assess the significance of the issues related to the atmosphere, climate, water resources, land resources, ecological environment, socio-economic environment, transport, infrastructure and communication, natural risks, hazards and external constraints of the Project for the proposed development. After the compilation of baseline information and processing of acquired satellite imagery, the screening checklist was filled to screen out the adverse impact of the proposed Project during the pre-construction, construction and operational phases.

6.3.2 Notion of Significance

Taking into account these criteria, potential significance was classified as either:

Low: an impact for which no mitigation is necessary;

Medium/moderate: an impact that requires effective mitigation; and

High: an impact, which, if not mitigated, could stop the Project from proceeding.

Reversible/Irreversible: Changes considered irreversible, for example, the loss of biodiversity due to a change in water quality;

The potentially significant impacts were then further investigated in more detail to make a comprehensive assessment of the actual impacts.

6.3.3 Study Area/ Area of Influence

Refer Chapter 4: Description of the Environment, **Section 4.3**.

6.4 Environmental & Social Considerations (E&S) in Project Design

Environmental and social (E&S) aspects have been given due considerations in the project design to make the project sustainable, environmentally friendly and socially acceptable. E&S considerations in project design are summarized below:

- The depth of sewer lines has been kept low in waterlogged villages of Pakpattan, Noorpur Thal and Shujabad; to avoid groundwater contamination of shallow aquifer. Same practices will be applicable for similar conditions.
- Sewers shall be laid at least 1m away from water supply lines (except for few streets in each village, where the street width is less than 2 meters.
- In all cases, the sewer lines shall be laid below water pipeline (the difference between top of the sewer and bottom of water pipeline shall be at least 300 mm);
- Designed manhole covers to withstand anticipated loads & ensure that the covers can be readily replaced if broken to minimize silt/ garbage entry;
- Ensured sufficient hydraulic capacity to accommodate peak flows & adequate slope in gravity mains to ensure self-cleansing velocity in order to prevent built up of solids and hydrogen sulfide generation;

- All structural, layout and engineering designing are in strict accordance with the applicable codes and engineering standard;
- The location of overhead water tanks, pumping station and STP have been finalized in close consultation with local community and representatives of local authorities;
- Tree cutting has been avoided;
- Efficient seepage control measures have been considered in selection of pipe materials during the planning stage;
- Effluent generated during construction phase will be treated through septic tanks.
- Alignments of sewerage and water supply lines have been carefully selected to minimize disturbance to public utilities;
- Relocation of the public utilities, if any, shall be planned and approved in consultation with relevant departments/authorities/stakeholders before project commencement to avoid inconvenience to the public;

6.5 Anticipated Impacts during Pre-Construction/Design Phase

Impacts envisaged during Pre-construction/ Design Phase and the recommended mitigation measures are given below:

6.5.1 Layout Planning & Design

Potential Impact

Incompatible layout plans and engineering designs of the proposed project can undermine the overall aesthetics and ambience of the project area. Mis-utilization of the available spaces may result in a design with low social acceptability and functionality. This impact will be permanent and moderately adverse.

Mitigation Measures

- All structural, layout and engineering designs of the project are in strict accordance with the applicable national and international guidelines/ codes/ standards and engineering practices;
- The layouts of water supply and sewerage networks have been adjusted to cover the whole project area. The water supply system is a loop-based system and the sewerage system is based on gravity where the slopes have been provided to ensure gravity flow with adequate velocity.

6.5.2 Soil Instability

The sandy soil conditions in the project area of Noorpur Thal may create challenges for laying water supply and sewer lines/drains. Trenches in sandy ground are prone to collapse, increasing excavation risks and construction difficulties. Higher infiltration rates in sandy areas may also lead to leakage and contamination concerns if pipes are not properly sealed. Stability of manholes and other structures could be compromised due to weak soil bearing

capacity. These conditions may result in increased construction costs, time delays, and the need for additional stabilization measures.

Mitigation Measures

- Use proper shoring and trench support systems to prevent collapse in sandy soils.
- Seal pipes and joints with high-quality materials to control leakage and infiltration.
- Provide adequate bedding and foundation treatment for manholes and structures.
- Ensure regular site supervision for safe practices and timely corrective measures.

6.5.3 Impacts of Drains construction

Inadequate sizing or gradients may lead to poor flow, blockages, or flooding during peak conditions. Improper alignment can cause conflict with existing utilities and affect land use. Selection of unsuitable materials or inadequate lining may result in erosion, siltation, or structural failure. Therefore, proper hydraulic design, durable materials, and integration with the overall sewerage system are critical for long-term performance.

Drain slab structures are vulnerable to damage when subjected to vehicular movement, especially from loads exceeding their design capacity. Continuous stress from unsuitable vehicles leads to cracks, structural deterioration, and eventual failure of the slabs. This not only disrupts drainage flow but also creates safety hazards in the project area.

Mitigation Measures

- Plan proper alignment and depth to avoid conflicts with existing utilities and infrastructure.
- Ensure accurate hydraulic design with proper gradients to maintain self-cleansing velocity and avoid blockages.
- Provide adequate cross-sections and freeboard to handle peak stormwater flows safely.
- Incorporate silt traps and access points for ease of maintenance and prevention of clogging and
- Use reinforced, traffic-rated slabs designed for expected vehicle loads, and restrict heavy vehicle movement over drains. Regular inspection and timely maintenance should also be ensured to prevent structural failure.

6.5.4 Environmentally Responsive Design Considerations

Potential Impact

Designing the project components without considering the prospective and futuristic needs can result in structures with low social acceptability and functionality. Improper-designed sewers may not carry the waste load, leading to system-failure and financial losses. The alignment of sewer lines and locations of sewerage pumping station and STP must be

properly planned, or else it may lead to both technical and social problems along with environmental issues of backflow creating foul smell and unhygienic conditions.

There are chances of infiltration from sewers which may contaminate the soil and underground water resources. The seepage may also affect the water supply lines and contaminate the potable water.

The construction of high-rise overhead water tanks may cause visual obstruction. The surrounding community may face privacy issues and it may also cause blockage of direct sunlight.

Mitigation Measures

- All sewer lines including trunk, lateral and branch sewer lines have been designed considering the future population and waste generation rate;
- Limit the sewer depth where possible;
- Sewers will be laid 1m away from water supply lines if the width of the street will be sufficient to do so.
- In all cases, the sewer lines shall be laid below water pipeline (the difference between top of the sewer and bottom of water pipeline shall be at least 300 mm);
- Designed manhole covers to withstand anticipated loads & ensure that the covers can be readily replaced if broken to minimize silt/ garbage entry;
- Ensured sufficient hydraulic capacity to accommodate peak flows & adequate slope in gravity mains to ensure self-cleansing velocity in order prevent to built-up of solids.
- The location of overhead water tanks, pumping stations and STP have been finalized in close consultation with local community and representatives of local authorities.

6.5.5 Groundwater

Potential Impact

Groundwater contamination may occur during construction by the improper handling of construction material (fuel, lubricant, bitumen, asphalt etc.) or sanitary water from construction camps and domestic sewage. During operation probability of seepage through the sewers may also contaminate groundwater. This impact is permanent and moderate negative in nature.

Mitigation Measures

- Construction materials that may lead to groundwater contamination will be properly handled and stored.
- Procedure for efficient jointing of selected sewer pipes will be applied to avoid leakage from pipes;
- Alternate sewage disposal arrangements have been suggested in design to cater the sewage flow, generated from the project area, during construction phase.

6.5.6 **Surface Water**

Potential Impact

There is no existing piped sewerage network or pumping station in the village. There is one large sewage pond in the villages where sewage is disposed by unplanned drains. Thus, endangering the environment of the vicinity. The openly flooded sewage causes nuisance in terms of foul smell and serves as breeding ground for disease causing vectors. Some sewage is also used to irrigate nearby crops.

There will be net environmental improvement in terms of sewage collection thus reducing sewage ponding in the project area and enabling adequate treatment of wastewater.

Mitigation Measures

- The sewage will be collected through a piped network;
- An STP based on ABR technology will be established to treat the sewage;
- The treated effluent as per PEQS will be discharged into the existing watercourses i.e nullahs, for agricultural purposes.

6.5.7 **Seismic & Other Hazard**

Potential Impact

According to the seismic zoning map of Pakistan, the project area of Noorpur Thal located in Seismic Zone 2A. A low to moderate-intensity earthquake impacting the project site can adversely impact the development.

Although Liaqatpur and Rojhan Tehsils lies within a low to moderate seismic zone, flooding represents the more significant natural hazard in recent years. Flooding is mainly driven by monsoon rainfall, canal overtopping or breaches, inadequate surface drainage, and backflow from irrigation systems rather than riverine sources. Approximately 20-25% of the tehsil is classified as high flood hazard, 35-40% as moderate risk, and the remaining 35-45% as low flood hazard. Vulnerability is highest in low-lying chaks near canals and drains, where prolonged waterlogging causes damage to housing, agriculture, and access infrastructure.

In view of the associated flood risk, all proposed structural facilities have been designed with appropriate flood-resilience measures. These measures include elevating the structures approximately 3–4 feet above the existing ground level to reduce the risk of floodwater ingress and associated damage. The raised design is intended to enhance the safety, functionality, and long-term resilience of the infrastructure during seasonal flooding events.

This factor requires special consideration of the designers as project structures (especially overhead water tanks and STP) may be affected negatively in case of earthquake tremors and the significance of damage depends upon the severity of earthquake.

Mitigation Measures

- The components of the proposed project include laying of underground water supply network, sewer lines, construction of overhead water tanks, pumping station and STP have been designed to withstand moderate earthquakes; and
- To mitigate the seismic hazard, Seismic Building Code of Pakistan 2007 (SBC-07) has been adopted. This code specifies minimum requirements for seismic safety of buildings/ structures and has to be applied and used by engineers in conjunction with the necessary understanding of the concepts of structural, geotechnical and earthquake engineering.
- Avoid siting critical infrastructure in flood-prone villages where feasible;
- Raise plinth levels of buildings above known flood levels;
- Strengthen canal embankments and improve desilting of drains;
- Introduce flood-resilient sanitation designs (sealed latrines, raised platforms);
- Establish community-based flood early warning and evacuation plans.
- Improve surface drainage networks and regular maintenance of existing drains;
- Ensure proper solid waste management to prevent blockage of drainage paths;
- Promote flood-resilient housing improvements and water source protection measures.

6.5.8 Damage to Existing Infrastructure

Potential Impact

The proposed project interventions are mostly subsurface activities and are likely to affect the existing infrastructure. Public utilities such as electric poles might get affected during construction activities and movement of machinery and the community will face temporary electricity cuts. Furthermore, the roads will be cut for laying of water and sewerage pipes and will create accessibility issues.

Mitigation Measures

- Alignment of water supply and sewerage network carefully selected to minimize disturbance to public utilities;
- Relocation of the public utilities shall be planned and approved in consultation with relevant departments/authorities/stakeholders before project commencement if any, to avoid inconvenience to the public;
- The local community will be informed before the relocation of services (if any) and schedule of relocation services will be prepared after consultation with the community to minimize inconvenience to the public;

6.5.9 Physical Cultural Resources

Potential Impact

No historical/ archeological site is present in the project area. However, some cultural resources including mosques, graveyard and shrines are present. People visit the mosques five times a day. Shrines and graveyard are visited occasionally by the surrounding community and devotees. These will not be directly affected but the people may face access issues in visiting these facilities.

Mitigation Measures

- The alternative access routes will be provided in case the access has to be restricted during execution period; and
- There must not be any physical impact on the physical and cultural resources in the project area.
- The possible discovery of archaeological sites or random findings during the excavation and earthworks may occur. In such case, World Bank's OP 4.11 will be triggered. Furthermore, **Annexure 5** for Chance Find Procedures will also be implemented.

6.5.10 Fire Fighting System

Potential Impact

Absence of a firefighting system may cause severe damage to the camp site and surrounding crops and houses during construction phase.

Mitigation Measures

- Contractor will provide an efficient firefighting system (i.e fire alarm and fire extinguishers) for campsite, workshop and construction site; and
- Campsite will be established in an area with easy access to the water source, helpful in firefighting in case of any incident.

6.5.11 Land Acquisition

The main focus of the project is to install sewers and water supply lines, which requires the use of existing streets and roads for right-of-way (ROW). If private streets or roads are encountered, the project team consults landowners prior to commencing any construction activities to gain permission for the use of their land. Moreover, land is also required for the construction of water supply infrastructure: stand-post, tube well, and OHR; wastewater treatment plant; and solid waste collection points. State land has been the priority for the project activities, a total of 3779.55 marla private land through voluntary land donation (VLD) is being used. The process of VLD is given in **Annexure-9.**

Priority has been given to the state land that is free of encumbrances i.e., free from any legal/ illegal claims of any squatters, illegal occupants, etc. Therefore, the implementation of RAP/ ARAP is not required in the Phase-1 villages.

Mitigation Measures

- Primarily, state land was used for the project infrastructure activities, however, private land through Voluntary Land Donation (VLD) is also being used in case of unavailability of state land.
- Additionally, in order to minimize the potential negative socio-economic impacts of land acquisition, minimum parcel of land has been proposed to meet the needs of the proposed project in case of private land; unlike in the cases of state land where – considering the future needs of the project expansion – sufficient parcel of state land has been acquired/ proposed.
- In case there is no state land or private land through VLD is available, PRMSC will consider the option of land acquisition, after developing and implementing a Resettlement Action Plan (RAP) approved by the World Bank. Compensation will be paid in accordance with the resettlement framework outlined in the Environmental and Social Management Framework (ESMF).
- Furthermore, the approval / NoL for each VLD case will be sought exclusively from the World Bank.
- A VLD checklist form has also been developed to assess the potential negative socio-economic and livelihood impacts of private land acquisition (Annexure-8A).
- Besides the VLD checklist, VLD tracking sheet has also been developed (attached as Annexure-8B) which will be continuously updated, the same will be available for monitoring of VLD status.
- Without any transparent consent land will not be used through VLD (Procedure as per Annex 8 will be followed plus use of a screening form that assesses the impact of the VLD on the prospective donor is provided at Annex-8A);
- In case of private donors, only less than 10% of their land could be obtained;
- 100% compliance will be ensured of VLD procedure given in ESMP;
- VLD process will be executed by the PRMSC itself, and will not be devolved to any private parties (consultants or contractors).
- Before start of construction activities, it will be ensured that the land (private or public) is free from any form of encumbrances or where there are informal users, they are appropriately provided relocation assistance - in accordance with OP 4.12 – Involuntary Resettlement - before taking possession of land.

6.6 Anticipated Impacts during Construction Phase

Anticipated Impacts during Construction Phase and the recommended mitigation measures are given below:

6.6.1 Topography

Potential Impact

The construction activities are not expected to impact the topography of the area significantly except for those areas where physical activities i.e., earthwork is involved as well as stocking of material. The excavated material is to be mostly backfilled and the excessive material will be transported to strengthen the roadsides or will be dumped at the designated locations. This impact is site-specific, temporary, reversible, possible, and low significant.

Mitigation Measures

- Material stockpiles will be removed as soon as work is completed and the area will be reinstated;
- Temporary storage sites will be allocated for the storage of excavated material;
- Temporary storage sites will be lined and must not allow infiltration;
- The stockpiles must be covered with tarpaulin sheets or other adequate material;
- Pilling of material at large extent will not be allowed and the contractor will timely remove excavated material from the site.

6.6.2 Soil Erosion

Potential Impact

The soil would be exposed to erosion due to excavations for laying of sewers and water supply pipes. Construction activities such as clearing, excavation, filling, grading and setting up construction camps will affect the existing soil condition in the study area/ AoI. The clearing of vegetation can also loosen the soil and make it more susceptible to erosion due to wind and rain. There is also a possibility of silt runoff during rainy season causing soil erosion. This impact can be categorized as low adverse, site-specific, long-term, highly probable and reversible.

Mitigation Measures

- Good engineering practices such as proper compaction of backfill material and special slope protection measures will be adopted during the construction stage.
- Use of heavy machinery will be restricted as far as possible to avoid the destruction of soil structure;
- Confining excavations to the specified spots as per the approved engineering drawings and unnecessary excavations should be avoided;
- Stored excavated material shall be covered and preferably reused, e.g., in construction as backfill etc.
- Cutting of trees will be avoided to the best possibility to avoid soil erosion.

6.6.3 Soil Contamination

Potential Impact

Contamination of soil may be caused by oil and chemical spills from construction machinery or uncontrolled runoff from equipment washing yards. This impact is permanent and minor negative in nature.

Mitigation Measures

- Chemicals/ hazardous products and wastes will be stored on impermeable surfaces in secure, covered areas with clear labelling of containers and with a tray or bund to contain leaks;
- All construction wastes from the site will be regularly collected and transported to approved waste disposal sites;
- Awareness of emergency spill response procedures will be provided to the workers on-site;

6.6.4 Trench Failure

Potential Impact

The major construction activities involve excavation operations for laying water supply and sewerage lines. The major hazard associated with the excavation operations is trench failure. The unstable slopes may fail and settle in the trenches which may cause injuries and fatalities to the workers. This impact is probable, site specific and high adverse in nature.

Mitigation Measures

- Careful selection of the site for excavation in light of soil investigation is inevitable
- Provision of adequate shuttering in the trenches;
- Leftover shuttering may also be used in case of loose soil strata.

6.6.5 Construction Camps/Camp Sites

Potential Impact

Improper construction camp location and mismanagement of construction camp activities can lead to various social and environmental impacts which may include noise, health and safety, traffic problems, soil degradation, loss of vegetation and assets on the selected land, solid waste and water pollution. Furthermore, cultural differences, the behavior of construction workers, potential disregard for local cultural norms can lead to increased tension between local communities and workers residing in the construction camps. This impact is temporary and moderately negative in nature.

Mitigation Measures

- Working hours of noisy activities will be limited to normal daytime working hours when near identified sensitive receptors;

- Waste Management Plan will be implemented to include procedures for the classification, storage and disposal of all construction wastes and the training of employees who handle hazardous materials; and
- Construction camps will be established away from populated areas and NOC/lease agreement will be obtained from private land owners.
- Regular training of workers will be carried out regarding local cultural norms, human behaviour, gender issues and GRM by the contractor during construction activities at site.
- Implementation of code of conduct

6.6.6 **Water Quality**

Potential Impact

Runoff from the construction works site may contain an increased load of sediments, suspended solids and other contaminants. Potential sources of pollution from the site include:

- Runoff and erosion from exposed soil surfaces, earthwork areas and stockpiles e.g., grouting and cement material with the rain;
- Wash water from dust suppression sprays;
- Fuel and lubricants from maintenance of construction vehicles and mechanical equipment;
- Spillage of liquids stored on-site such as oil, diesel, and solvents etc. are likely to result in water pollution; and
- Uncontrolled discharge of debris and garbage such as packaging, construction material and refuse.

Construction waste, if left unattended will result in forming leachate that will percolate through the soil strata and will reach underground water table and hence, will end up contaminating groundwater. There is a probability that various materials like fuel, lubricant oil and other oily products, which are used during the construction phase may contaminate groundwater and channels carrying water.

There is no major surface water body near the project sites, however, canal distributaries and watercourses are present for irrigation purposes which may get contaminated.

Mitigation Measures

- Protection of groundwater reserves from any source of contamination such as the construction and oil waste by making the ground impermeable through sheets or compaction;
- Stockpiles of cement and other construction materials will be kept covered when not being used;

- Maintenance of vehicles will be carried out only in impermeable areas where any oil spillages can be contained;
- Careful planning of the works to avoid soil excavation works during rainy seasons;
- Controlled activities will be undertaken during monsoon and careful attention must be paid to weather forecast before excavation operations.
- All kinds of waste will be stored in covered containers and disposed of safely as soon as possible; and
- By proper C&D waste management system in place, the contractor will ensure that construction debris does not find its way into the drainage or irrigation channels.

6.6.7 Air Quality

Potential Impact

Air quality will be affected by various construction activities like emissions from generator stack vehicular exhaust, VOCs from uncovered gasoline i.e petrol/diesel, and manoeuvring of construction and public vehicles on construction site. Emissions may be spread over longer distances depending upon the wind speed, direction, temperature of surrounding air and atmospheric stability. In certain climatic condition such as hot summer, airborne dust can become a major nuisance if control techniques are not properly employed.

The air emissions may cause health impacts such as dryness and roughness of the throat, eyes, nose, etc. to the workers, staff of the contractor and the residents of area. These emissions may also affect the bio-physical environment. The impact is negative and temporary in nature.

Mitigation Measures

- All vehicles, machinery, equipment and generators used during construction activities will be kept in good working condition, properly tuned and maintained to minimize the exhaust emissions;
- Open burning of solid waste from the contractor's camps will be strictly banned;
- Personal Protective Equipment (PPEs) like masks, goggles and gloves etc. will be provided to workers;
- PEQS applicable to gaseous emissions generated by construction vehicles, equipment and machinery will be enforced during construction works.
- Regular water sprinkling on the site and access roads will be carried out to suppress excessive dust emission(s);
- Blowing of dust and particulate matter from stockpiled loose materials (e.g., sand, soil) will be avoided either by sheeting them with tarpaulin or plastic sheets or by sprinkling them with light shower of water;

- The vehicles carrying construction materials and the construction material storage areas will be covered with tarpaulin.
- Sensitive receptors of the area will be informed accordingly

6.6.8 Noise

Potential Impact

Noise level is expected to increase during construction activities. Main sources of noise and vibration will be heavy machinery such as excavators and other equipment. Noise generated by construction machinery is likely to affect sensitive receptors located within AoI. Health risks associated with exposure to continuous noise levels include high blood pressure, hypertension, annoyance and sleep disturbance, temporary threshold shift etc. The impacts of noise will be temporary and highly adverse in nature.

Mitigation Measures

- Construction workers will be provided suitable hearing protection like ear cap, or earmuffs and training them in their use;
- Selection of up-to-date and well-maintained equipment with reduced noise levels will be ensured by suitable in-built damping techniques or appropriate muffling devices; and
- Residents will be notified earlier before the commencement of excavation operations.
- Construction activities will be restricted to the day-time.
- Sensitive receptors will be informed accordingly.

6.6.9 Municipal and Construction Waste/ Wastewater

Potential Impact

Due to construction activities municipal and construction waste will be generated from construction activities. The waste will include wastewater, domestic waste and construction waste etc.

Improper dumping of waste may generate odor and attract mosquitoes and other disease vectors. Waste bins containing toxic, flammable and corrosive materials may pose a hazard to the workers when handled without PPEs. Unsuited waste disposal site selection may pose a serious health concern to the locals and workers onsite. The impact is temporary and minor negative in nature.

Mitigation Measures

- Solid waste generated during construction and campsites will be safely stored, collected, transported and disposed of at the selected disposal site and the contractor will provide and implement a comprehensive solid waste management plan;
- Burning of waste will be prohibited;

- Proper labeling of containers, including the identification and quantity of the contents, hazard contact information etc;
- Closed waste storage bins will be provided on-site to store waste.

6.6.10 Chance of Finding Artifacts

Potential Impact

During excavation, there is a chance of finding artifacts. In case of finding any artifact, the contractor will immediately stop the activities and report through Supervision Consultant to Directorate General (DG) of Archeology, Government of Punjab to take further appropriate action to preserve those antiques or sensitive remains. Chance find procedures are attached as **Annexure 5.**

6.6.11 Resource Conservation

Potential Impact

The materials used in the construction of proposed project would include coarse aggregates (crush), fine aggregates (sand), brick ballast, water and cement etc. Almost all the materials to be used in the construction of proposed project are non-renewable and therefore their sustainable use is necessary for future use.

Large quantities of water will be used in the construction of concrete pipes, drains, pumping stations, STP, cradles and in watering the unfinished surfaces.

Diesel and residual fuel oils will be used to operate construction machinery and equipment. Sustainable use of energy resources is very important and it will also help to reduce air emissions. For conservation of energy, efficiency of the engines and burning processes is very important.

Mitigation Measures

- Wastage of water will be reduced by training the workers involved in water use;
- Water jets and sprays will be used for watering surfaces rather than using overflow system.
- Reuse of construction waste materials will be considered.
- The efficient and well-maintained equipment and machinery will be used.
- The equipment and machinery will be turned off when not in use.

6.6.12 Biodiversity Conservation

Flora

Potential Impact

On account of construction of the proposed water supply and sewerage system, no trees are envisaged to be cut/disturbed but some herbs or shrubs may be required to be removed for excavation. The dust emissions due to excavation operations will stick to the leaves of

existing trees and may close their stomata thus hindering the photosynthesis process. Reduced photosynthesis may also reduce the productivity of existing trees. This impact is however temporary but minor negative in nature.

Further, during construction activities the Contractor's workers may damage the vegetation and trees (for use as fire-wood to fulfill the camp's requirements).

Mitigation Measures

- The Contractor's staff and labour will be strictly directed not to damage any vegetation such as trees or bushes. They will use the paths and tracks for movement and will not be allowed to trespass through farmlands;
- Contractor will provide gas cylinders at the camps for cooking purposes and cutting of trees/ bushes for fuel will not be allowed.

Fauna

Potential Impact

There will be no damage to health and life of local animals mostly cats, dogs and jackals and especially the livestock i.e., goats and cows due to construction activities. Some reptiles and insects may get killed/ injured during excavation operations.

Mitigation Measures

- Excavations will be limited to the approved engineering drawings;
- Physical barricades will be provided at critical location near construction sites for restricted movement
- Harassing of animals will be prohibited.

6.6.13 Health and Safety

A. Occupational Health and Safety

Potential Impact

OHS-related risks include working at height (at excavation site & OHR construction site) Health risks and workers safety problems may result at the workplace if the working conditions provide an unsafe and/or unfavorable working environment. The health and safety issues are also associated with the operation of construction machinery and equipment, which may cause minor and severe injuries to workers. It will be a long-term and severe negative impact.

Mitigation Measures

- Obligatory insurance against accidents for labourers/workers;
- Providing basic medical training to specified work staff and basic medical service and supplies to workers;
- The Contractor's Health and Safety Officer will identify, record, and subsequently send the deployment and activity plan to the supervision consultant's Health & Safety

Expert (HSE) who will analyze the hazards of the job and issue the No Objection Certificate (NOC), accordingly.

- Layout plan for camp site, indicating safety measures taken by the contractor, e.g., firefighting equipment, safe storage of hazardous material, first aid, security, fencing, and contingency measures in case of accidents;
- Use of Personal Protective Equipment (PPE) i.e., ear muffs, masks, safety shoes, gloves etc.;
- Use of safety signs at the construction site, as shown below.

- Contractor will immediately inform the consultant about the project related incident. The consultant will then submit a preliminary report to the PRMSC within 24 hours. Resultantly, PRMSC will promptly notify the World Bank for project-related incident within a maximum timeframe of 48 hours.

B. Community Health and Safety

Potential Impact

The construction activities and vehicular movement at construction sites may result in roadside accidents particularly inflicting local communities who are not familiar with presence of heavy equipment. This is a temporary and moderate negative impact. Open trenches and deep manhole may cause trip & fall accidents for the local residents.

Mitigation Measures

- Medical screening of the laborers for communicable diseases will be conducted before hiring. Medical screenings are a basic requirement before the hiring of labour to prevent the spread of communicable diseases. However, on the basis of these screenings, diseased potential workers will not be barred from work; instead, necessary measures will be taken to prevent the spread of these diseases.
- The site will be restricted for the entry of irrelevant people particularly children.
- Provision of proper safety and diversion signage, particularly at sensitive/accident-prone spots;
- Setting up speed limits within the village.
- Open trenches and deep excavated manholes will be protected by fence/barricade to avoid any accident.
- Night time lighting will also be provided.

- Awareness campaign regarding HSE will also be provided to local community including at schools.
- Awareness/ training session of labourers will be conducted to promote clean behaviour practices and to curtail medical issues.
- Special consultation session will be held with the nearby medical facility to ensure that it is well informed and well equipped to handle any dust allergy cases if required.
- Contractor will immediately inform the consultant about the project related incident. The consultant will then submit a preliminary report to the PRMSC within 24 hours. Resultantly, PRMSC will promptly notify the World Bank for project-related incident within a maximum timeframe of 48 hours.

C. Emergency Response (Natural and Man-Made Disasters)

Potential Impact

Natural calamities such as flood and man-made disasters such as fire, falls, slips and trips may result in injuries, financial losses and may even lead to deaths. Flooding can result in inundation of the village area and excavation / trenches which may leads to accidents or can damage the infrastructure of the project activities. Similarly, during operation it can affect the water supply, and sewerage system. The workers will be trained and facilitated to cope with such emergencies.

Mitigation Measures

- Training of the staff/employees regarding the emergency procedures/plans will be regularly conducted;
- Emergency numbers will be clearly posted; and
- First aid boxes will be provided.
- Minor incidents and near misses will be reported and preventive measures will be formulated accordingly.

6.6.14 Traffic Management

Potential Impact

The traffic influx within the villages is very low. Most of the traffic within the villages include motorbikes and few cars. The project interventions will not create traffic congestion issues in the project area. However, their movement will be disturbed due to the excavation and construction works and people may face accessibility issues. This impact is temporary and major negative in nature.

Mitigation Measures

- The construction activities will be carried out in pockets/reaches, once a patch has been completed (i.e., pipes are laid and covered) then excavation on new patch shall be started;

- Local community will be taken on board to plan alternate access routes in connecting streets to ensure mobility of local traffic; and
- Plan work in a minimum possible time.

6.6.15 Nuisance/ Disturbance to Sensitive Receptors (Educational, Health and Religious Places)

Potential Impact

Since the proposed interventions will be carried out within the village boundaries, therefore, the socially sensitive sites/places including schools, hospitals and religious centers will be temporarily affected due to dust, noise and the community will face accessibility issues due to open trenches. Dust due to earthworks will create health hazard to children and people with ailments. This impact is temporary and major negative in nature.

Mitigation Measures

- Work will be conducted near the religious places with due social diligence and after informing all stakeholders
- Material transport to the site will be scheduled considering school timings;
- Notify concerned schools, hospitals/dispensary etc. 2 weeks prior to the work; conduct a 30 minutes' awareness program on nature of work, likely disturbances and risks and construction work, mitigation measures in place, entry restrictions and dos and don'ts; and
- Implement all measures suggested in this report viz. dust and noise control, public safety, traffic management, strictly at the sites.

6.6.16 Accessibility

Potential Impact

Excavation of trenches and pipe/sewer laying work in the project area will obstruct access to residences, commercial buildings and businesses adjacent to the proposed project alignment. Disruption of access to commercial establishments may affect livelihood. The potential impacts are negative and moderate but short-term and temporary.

Mitigation Measures

- Leave space for access between mounds of excavated soil;
- Consult affected people to inform them in advance about the work schedule;
- If there are any holidays (i.e., Eid or Muharram etc.), the Contractor will complete the backfilling work of the trenches and will not leave any trench open before holidays;
- Provide sign boards for pedestrians to inform nature and duration of construction works and contact numbers for concerns/complaints.

6.6.17 **Gender-Based Violence (GBV)**

Potential Impacts

During the construction phase, gender-based violence might arise due to influx of outside labor. Sexual harassment against women might occur as a consequence of mixing of men and women at the construction site, and moving on the roads and markets.

Mitigation Measures

With the effective measures and monitoring, the risk of gender-based violence will be minimized by adopting the following mitigation measures:

- Awareness will be created among the females at community levels about the construction.
- Workers will not be allowed to crowd in the residential area/villages.
- Alternative routes and traffic management plans for the safety of the community particularly for women and children will be ensured.
- Raise awareness among the communities regarding the potential risks of GBV, and establish response services in the nearby communities that can respond to instances of GBV (particularly those related to issues of labor influx);
- Contractor will take proper measures and will ensure Gender Sensitive Grievance Redressal Mechanism to address and resolve issues relating to harassment, intimidation, and exploitation.
- GBV-related issues will be recorded through GRM, two separate focal persons for males and females are part of Village Organization VO – which will also work as members of the Grievance Redressal Committee (GRC) Tier-I. The female focal person – trained on the social protection referral directory – will be responsible for further referral of GBV-related complaints to the forums concerned. A multi-sectoral referral system is proposed, which will include referral to The Punjab Women's Toll-Free Helpline 1043 available 24/7. It is managed and supervised by Punjab Commission on the Status of Women (PCSW). Their helpline team comprises all-women call agents, three legal advisors, a psychosocial counsellor, supervisors, and management staff. The Punjab Commission on the Status of Women (PCSW) has been identified as a key stakeholder. PCSW will be informed of the project activities and an institutional link will be established.
- At the PRMSC Tehsil Office, the Behavior Change and Communication (BCC) Officer – in addition to being member of GRC Tier-I&II – will initially deal with gender related issues/ complaints and further refer the same to the Gender Specialist at Head Office, PRMSC.
- The Contractor will prepare the Codes of Conduct to prevent occurrence of GBV and get it signed by all workers, and effectively communicate to all workers and project beneficiaries.

6.6.18 **Influx of Labor**

Potential Impacts

For the implementation of project activities, skilled and unskilled labor is required by the contractor. Mostly, skilled and unskilled workers have been associated with the contractor since a long which they utilize, where they are required for the projects, and while other workers are hired from different areas that belong to different cultural backgrounds. Social problems and conflicts that are associated with labor influx are as follows:

- **Risk of social conflict**: Conflicts may arise between the local community and the construction workers, which may be related to religious, cultural or ethnic differences, or based on competition for local resources;
- **Increased risk of illegitimate behavior and crime:** The influx of workers and service providers into communities may increase the rate of crimes and perception of insecurity by the local community. Such illegitimate behavior and crimes can include theft, physical assaults, substance abuse, sexual assault and human trafficking;
- **Increased risk of communicable diseases and burden on Tehsil & District health services:** The influx of people may bring communicable diseases to the project area, including sexually transmitted diseases (STDs), or the incoming workers may be exposed to diseases to which they have low resistance. Workers with health concerns relating to substance abuse, mental issues or STDs may not wish to visit the project's medical facility and instead go anonymously to the nearby medical center, this can result in an additional burden on tehsil & district health centres; and
- **Local inflation of prices, accommodations and rents:** A significant increase in demand for goods and services due to labor influx may lead to local price hikes and crowding out of community consumers. Depending on project worker income and form of accommodation provided, there may be increased demand for accommodations, which again may lead to price hikes and crowding out of local residents.

Mitigation Measures

- Labour camp(s) will be established away from residential areas;
- Preference will be given to the local people to work with contractor, and contractor should hire maximum labour force from the project area because this will reduce the labour influx;
- Awareness will be created among the workforce to ensure respect for local customs;
- An effective GRM has been established for the project to resolve all issues related to the community. Thus, progress regarding resolving the issues should be monitored closely.
- Create awareness among workers on proper sanitation and hygiene practices to endorse proper health and maintain good housekeeping practices at all project sites;

- Make arrangements to treat the affected workers on time to control the movement of vectors disease;
- Provide proper and free medical screening and counselling for site workers and community members;
- Develop and enforce a strict code of conduct for workers to regulate behaviour in the local communities;
- Labour will be required to sign a code of conduct translated into their local languages at the time of hiring.
- Prohibiting drugs, alcohol, weapons, and ammunition on the worksite among personnel;
- Appropriate fencing, security checkpoints, gates and security guards should be provided at the construction sites to ensure the security of all plant, equipment, machinery and materials, as well as to secure the safety of site staff; and
- The Contractor must guarantee that good relations are maintained with local communities and their leaders to help reduce the risk of vandalism and theft.

6.6.19 Social/ Cultural Conflicts

Potential Impact

During the construction phase of the project, conflicts may arise between labor force and local community. Furthermore, differences in cultural values may also cause discomfort to local residents. This impact is temporary and minor negative in nature.

Mitigation Measures

- Plan for social grievance redress mechanisms including the local leaders and community representatives;
- Local labor will preferably be employed for construction works;
- Careful planning and training of the workforce to minimize disturbance to the local people;
- Robust and transparent GRM will be implemented

6.6.20 Child Labor

Potential Impact

Due to poverty and the feeble financial situation of the area, the underage children might get involved with the contractor various construction works. This will be the violation of the Child Labor Act. Furthermore, SEA/SH issues might arise which will create social conflicts. This impact is adverse and temporary in nature.

Mitigation Measures

- Standard clause in the contracts related to child labor explicit prohibitions, etc. and contractor will ensure compliance to the contractual provisions as per law of land. Similarly, equal wages for similar work will be followed.

6.6.21 Economic Activity

Potential Impact

Due to the construction of the proposed Project, economic activity will be generated in the project area as the laborers and semi-skilled staff will have an opportunity to work in the project area. This will provide them an opportunity to develop their skills and capacities. It will also benefit the local vendors of the project area. This is a positive impact.

6.7 Anticipated Impacts during Operational Phase

Anticipated impacts during Operational Phase and the recommended mitigation measures have been described under biophysical and socio-economic categories as follows:

6.7.1 Soil

Potential Impact of STP

The soil quality may be affected due to leakage/ infiltration from sewer lines and STP bed. The sludge generated from cleaning/ maintenance of pumping stations, manholes, sewers and STP may contaminate the soil. The liner of the STP, while desludging may get dried and cracks may lead to the seepage of wastewater and thus contaminate the soil. Improper disposal of scum and sludge is another concern. This is a moderate negative impact.

Potential Impact of Leachate from Dumping Site

The collected solid waste will be dumped into the existing dumping sites of Tehsils. There is no arrangement of leachate collection and no liner material is present there which will result in contamination of soil due to leachate. The situation will exacerbate in the rainy seasons. This is moderate negative impact.

Mitigation Measures

- Sludge shall be treated before ultimate use/disposal. Various options for sludge treatment include Digestion, Drying/ Dewatering, Composting, Lime Stabilization, Heat Treatment must be considered etc;
- The liner of STP must be regularly maintained and checked for any cracks and leakages;
- Treated sludge should be properly disposed of in an environmentally friendly manner.

6.7.2 Air Quality

Potential Impact of Sewerage System

The operation of sewerage scheme will result in generation of gases including H_2S and CH_4. H_2S is a foul-smelling poisonous gas that might be harmful to the sewer men and could be

fatal sometimes. CH_4 is natural gas also referred to as a greenhouse gas. Pakistan is signatory to the United Nations Framework Convention on Climate Change (UNFCCC) and adopted Kyoto Protocol in 1997. Under the Kyoto Protocol, Pakistan is committed to reduce GHG emissions into the environment to prevent interference with climate change. The GHG emissions for the proposed project are a concern due to the anaerobic conditions in the sewer lines and wet wells of the disposal station.

Mitigation Measures

- Provision of exhaust gas vents at appropriate locations in the design;
- Sewer-men will cover their faces with gas mask while entering the sewer for cleaning or maintenance purposes;
- It's better to use sucking machinery for cleaning of sewers;
- Use gas detector before inspection;
- Adequate tree plantation must be done around the STP to control the spread of odour;

6.7.3 Odour

Potential Impact of STP

STP are designed on adequate waste loading and function well if they are not overloaded. The overloading will result in malfunctioning of STP and it will result in significant odour generation in the vicinity. This impact is temporary and high adverse in nature.

Mitigation Measures

- The STP should not be overloaded and personnel dealing in operation should be trained to avoid operational issues;
- Adequate tree plantation must be undertaken to avoid spread of odour in the vicinity.

6.7.4 Elite Capture

During the VLD process it was ensured that land will not be donated by landowners having more than 25 acres land size to avoid elite capture. This has resulted in a situation where the elites have disproportionate control over resources, policies, and decision-making processes in all over the province. Elite capture is often facilitated by corruption, nepotism, and patronage networks, which enable the elites to manipulate the system in their favor. The consequences of elite capture are far-reaching, with the general public often left without access to basic amenities such as health, education, water and sanitation. This has resulted in widespread inequality, marginalization, and poverty in Punjab. Landowners play role as elite capture while donating the land to get the rights to use of water, sewage treated water for agriculture.

Mitigation Measures

- To avoid elite, capture the VLD will not be accepted from the person having more than 25 acres' land.

- To increase transparency and accountability in decision-making processes.
- Involving multiple stakeholders, including community members, in decision-making processes related to project activities.
- To promote the participation of marginalized groups, such as women and minorities, in decision-making processes. By ensuring that these groups have a voice in decision-making, the risk of elite capture can be reduced.
- Strengthening institutions such as VO's/VC's and regulatory agencies can help ensure that decisions are made in a fair and equitable manner, without undue influence from elites.
- To ensure an effective grievance mechanism for monitoring and reporting any cases of elite capture.
- Robust and transparent GRM will be implemented
- VO's will be strengthened to play a role during distribution of treated water to prioritize the needs of the entire community rather than just a select few elites.
- Due diligence will be held during VLD process to absolve the doner from all the associated land rights.

6.7.5 Social Inclusion

Social inclusion is the process in which individuals and groups take part in the society. Social inclusion in proposed project area is an important aspect for the overall development of the interventions. It is crucial to ensure that every stakeholder of the community have equal access on the provision of clean drinking water and sanitation facilities, improved healthcare facilities, educational facilities and on economic excess and job opportunities. In this proposed project efforts will be made to promote the participation of marginalized groups, such as women and minorities, elderly person in decision-making processes and community activities. These efforts include the participation of the public including marginalized groups in the community meetings for project disclosure, corner meetings for the nomination of their representatives for the Village Organizations/ Village Councils (VOs/VCs), and monthly community meetings. Moreover, due representation for these marginalized groups has also been ensured in the VO membership. In addition to the open electoral process, a minimum of 50% share of the total membership has been allocated for the women members, one seat reserved for the minority, and in case of other socio-lingual differences further quota has also been ensured. These efforts will help to improve the overall quality of life for residents in proposed project area to promote opportunities in inclusive manner.

Mitigation Measures

- Providing awareness campaigns to increase knowledge and understanding of the project. and challenges faced by marginalized groups.
- Ensuring the implementing policies that promote diversity and inclusion, such as affirmative action policies and anti-discrimination laws.

- Providing awareness on the importance of clean drinking water & sanitation, education, job training, and community services to underserved and marginalized populations.
- Encouraging and supporting the active participation of marginalized groups in decision-making processes through VO's to providing opportunities for leadership.
- Fostering partnerships between PRMSC-TO and VOs/VCs to promote social inclusion to address the root causes of social exclusion.
- Regular monitoring and evaluation of project policies and programs to ensure they are effective and inclusive.

6.7.6 End Water User of Treated Wastewater

End wastewater users are the individuals and communities who will use the treated water for various irrigation perpose. These end-users play a crucial role in ensuring the sustainable use of treated wastewater. It is important to understand the value of treated water and the impact of their actions on wastewater availability. The treated wastewater will be available to all the peasants having lands in the proximity of ABR. However, in case of disputes, VO of the village will decide the distribution rights of treated wastewater in consultation with the community demands.

Mitigation Measures

- End water users will adopt water conservation measures such as reducing water wastage, using efficient irrigation methods
- Awareness campaigns will be conducted on the understanding and importance of water conservation and its impacts.
- VO will ensure monitoring and evaluation on regular basis regarding the usage and conservation of treated water.
- Distribution of treated wastewater will be decided by VO's/VCs in village
- Equal rights of the community on the usage of treated water will be ensured by the VOs.

6.7.7 Solid Waste

Domestic and hazardous wastes would be generated during cleaning and maintenance activities. The solid waste during operational phase will consist of plastics, metal and organic wastes present in sewer lines which can cause blockage in sewerage system. This impact is major negative and permanent in nature.

Potential Impact of Solid Waste Management

The waste containers, if not emptied timely, will create nuisance and attract mosquitoes and disease vectors. The situation will exacerbate in the rainy seasons. Furthermore, there would be littering during transportation of waste from the villages to the dumping site.

Mitigation Measures

- Waste shall be collected, stored and disposed of according to relevant standards in approved facilities;
- An organized collection system and its implementation through a licensed contractor;
- The containers will be timely removed and a fine will be imposed on contractor in case of violations;
- Closed containers will be used for transportation of waste to the dumping site;
- Schedule inspection of the sewer lines and STP to keep it clean and to identify any hazardous material; and
- Solid waste bins shall be placed at appropriate locations to avoid mixing in wastewater.

6.7.8 Sludge

Potential Impact

Sludge is semi-solid material which will be settled at the bottom of the STP due to anaerobic decomposition of biomass. Significant amount of sludge will not be produced in ABR; however, periodic desludging will be done to achieve good removal efficiency. The removed sludge in wet form, if left unattended will create nuisance i.e., odor, soil contamination, groundwater contamination (through percolation/ seepage) and will serve as a breeding ground for vector diseases. Sludge will be removed from the ABR once the 50% of the ABR is filled will the sludge.

Mitigation Measures

- Appropriate sludge treatment must be undertaken before disposal of sludge; sludge dewater and drying through sludge drying beds in case of ABR.
- Sludge testing / horticulture purpose/ campaigns. Priority will be given to the use of dried sludge as a land conditioner in the fields.
- If required remaining sludge will be transferred to a nearby dumping site designated by Tehsil Municipal Authority, these sites are already being used for dumping of solid waste.
- Sludge management plan will be followed for proper handling and disposal (Annexure-9).

6.7.9 Impact of Brine Disposal

In case of operation of Reverse Osmosis (RO) filtration Plants, around 75% of water is rejected and 25% is consumed as treated product water. It means that for every 2000 lph capacity RO plant; we require 6000 lph of raw water to be treated from which 4000 lph will be the RO reject or brine. So, per day 32,000 litres of wastewater will be generated from a single RO. The rejected water is free from bacteria, viruses and other pathogens but has only dissolved particles in it. RO concentrate disposal issues present significant design and

operational challenges that must be addressed. Conventional disposal techniques mostly suffer from direct or indirect contamination of water/soil.

Mitigation Measures

- Reuse of brine for dust suppression on unpaved roads can be considered where environmentally acceptable.
- Planting halophytic grasses and shrubs in designated areas can help utilize saline water while stabilizing soil.
- Small-scale ponds with brine-tolerant fish or shrimp species can be developed in suitable areas.
- Brine can be discharged into a borehole to safely isolate it from surface water and allow controlled infiltration or dilution.
- RO brine can be discharged into water ponds (if present nearby) for reuse in irrigation only if the pond has adequate dilution and circulation to reduce salinity to safe levels.
- Brine can be managed through controlled dilution with treated effluent to reduce salinity before reuse for irrigation of non-food vegetation e.g, in Barley

6.8 Positive Impacts

6.8.1 Improved Water Supply System

Clean tap water is a dire need of all project tehsils. The provision of adequate water supply system with a reasonable supply of water will provide relief to the community and will resolve the major issue of “water” in the project area. Further, there will be a net improvement in community’s health.

6.8.2 Improved Sewerage System

The proposed project will improve the overall sewerage and drainage system of the project area. Currently, the open wastewater drains in the streets result in foul odor, serves as breeding ground for disease vector and results in inconvenience to the road users and local community. The project will improve this situation by controlling overflows and proper disposal of wastewater/ storm water.

6.8.3 Improvement in Public Health, Hygiene and Sanitation

With the improvement in sewerage and drainage system, improvement in health, hygiene and sanitation will also be observed. Foul odor will be eliminated and there would be no breeding grounds for diseases vectors. Thus, the project will improve public health, hygiene and sanitation conditions in the project area.

6.8.4 Landscape

Potential Impact

During the operation stage, new saplings of different plants would be planted to enhance the aesthetics to create a buffer zone and to compensate the environmental losses. This will have a positive impact of permanent nature. The presence of adequate flora at available spaces will help in absorbing flue gases and other air quality related impacts of proposed project operation. The plants will be beneficial in dust and noise suppression for the nearby community.

Mitigation Measures

- The saplings planted in the project area against the trees affected and for enhancement of environment should be properly maintained throughout their growth.

6.8.5 Commulative Impacts of Water Extraction & Sewerage Treatment

Potential Impact

Cumulative impact may occur as a result of development of several treatment plants or several water extraction points, currently there is only one water extraction point for each selected village and the people in project area are fulfilling their water demands majorly from ground water resource (agriculture and domestic purpose respectively). The current intervention will provide treated water in the replacement of raw water to the locals which will improve the health and reduce exposure to water borne diseases. Supply of treated water at door set will also discourage the installation of pumps in houses. Furthermore, this project will basically replace the one practice to another practice and will not majorly impact on the consumption rate as people reliance on existing water extraction system will become minimum after the completion of the project. However, there will be no cumulative impact in terms of depleting ground water resources.

On the other hand, for each project village, one Sewerage Treatment Plant (STP) will be installed, and the treated water will be discharged into an existing sewerage pond. This practice will also have no impact on quality of water resources because sewerage water is already dumped directly into existing sewerage ponds and after this project sewerage water will be discharged into the ponds after treatment which will help to improve the quality of sewerage pond. However, there will be more or less zero cumulative impact after the installation of ABR

Mitigation Measures

- Water quality monitoring should be done by the third party on quarterly basis to ensure the supply of safe drinking water.
- ground water table will be monitored periodically.
- Water metering system should be installed to know the total consumption of water.
- Ensure the treated effluent follows the National Environmental Quality Standards
- Maintenance of ABR should be done annually for its smooth operations.

6.8.6 Other Positive Impacts

Some other positive impacts include the following:

- Economic development
- Employment generation
- Development of deprived areas
- Formation of model villages of tehsil Bhawana

6.9 Operational Sustainability

The sewer pipes water supply lines and other components of the project will not function with improper operation and maintenance of sewerage system and water supply system which is the responsibility of the client.

Mitigation Measures

- Routine/ preventative maintenance shall be carried out as with the passage of time
- Major causes of deposition of silt and floating matters in the sewers are the mixing of solid waste and smaller diameter sewer pipes. Placement of sufficient number of solid waste litter bins/containers shall be ensured along the roads and in streets to avoid entrance of solid waste into sewers;
- Immediate response to all sewer/drainage related complaints followed by prompt correction of defective condition;
- Regular cleaning of sewer lines to remove grease, grit, and other debris that may lead to sewer backups. Cleaning shall be conducted more frequently for problem areas;
- Inspection of the condition of sanitary sewer structures and identifying areas that need repair or maintenance. Items to note may include cracked/deteriorating pipes; leaking joints or seals at manhole; frequent line blockages; lines that generally flow at or near capacity; and suspected infiltration or ex-filtration;
- Any repairs will be conducted by sealing off the affected sewer and pumping the contents into tankers, after which the faulty section will be exposed and repaired following the same basic procedure as when the sewer was built. Trenches will be dug around the faulty section and the leaking joint will be re-sealed, or the pipe will be removed and replaced.
- Water supply lines will be inspected on regular basis to avoid any leakages and loss of resources.

6.10 Induced Impacts

Beside some direct environmental social and economic impacts, the proposed project may have some induced impacts to the physical features of environment. The project is envisaged to improve the infrastructure of the project area.

7 ENVIRONMENTAL & SOCIAL MANAGEMENT & MONITORING PLAN

7.1 General

This section aims to address the measures which need to be adopted during each phase of the project to avoid, contain, mitigate or compensate for the potential impacts identified in **Section 6**. The Environmental & Social Management Plan (ESMP) is the major part of this section and forms the gist of this study. ESMP not only includes Best Management Practices (BMPs) but also includes monitoring indicators, frequency, responsibility, and estimated environmental budget. This ensures that mitigation, monitoring, and management consideration form a part of the documentation used for decision making and the basic benefit of defining the responsibilities is to make sure that the suggested mitigation measure will be implemented at the construction and operation stages of the project. A summary of the mitigation measures for potential impacts have also been given in this section to support ESMP. Moreover, a framework for the implementation of ESMP has been discussed in this section.

7.2 Implementation of Environmental & Social Management Plan (ESMP)

The institutional arrangement for the implementation of ESMP for PRSWSSP is presented below. The proponent PRMSC and supervisory consultants will be responsible for compliance of with environmental and social safeguard requirements of the proposed project.

The proposed project activities will be monitored and managed by the PIMU-PRMSC. The Environmental and Social Cell (ESC) staffed by qualified environmental and social specialists has already been established under PRSWSSP. The ESC will be the custodian of the ESMP. ESC will support ensuring the compliance of ESMP. ESC will submit progress reports for the implementation of the ESMP to WB and PEPA as per environmental approval/ NOC conditions for the PRSWSSP.

Figure 17: Organizational Setup for implementation of ESMP

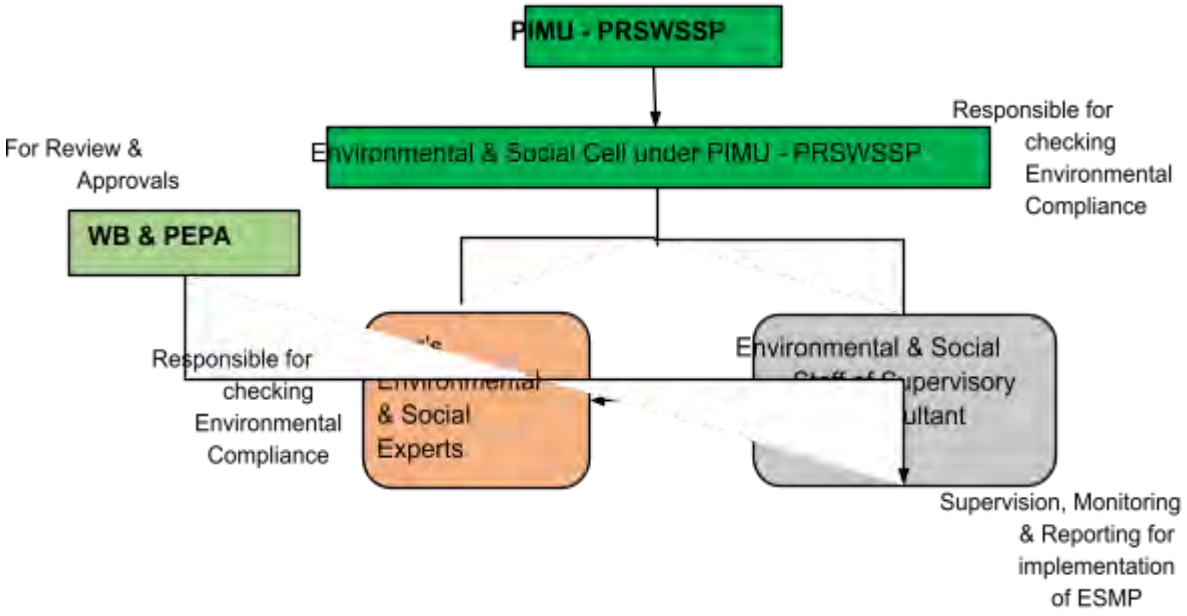

7.2.1 Roles and Responsibilities of the Functionaries involved in ESMP Implementation

A. World Bank

The current proposed project falls under category E2 as per ESMF guidelines; in view of limited environmental and social impacts and thus require an ESMP. World Bank shall review and approve the safeguard documents including ESMP. The Bank shall also review and approve the quarterly and biannually prepared progress reports.

B. Punjab Environmental Protection Department

As per Punjab Environmental Protection (Amendment) Act, 2012, Punjab EPD is responsible for environmental protection and pollution control. The Punjab EPD is responsible for the approval of the EIA/ IEE of all the developmental projects under their jurisdictions. As per Punjab Environmental Protection (Review of Initial IEE/EIA) Regulations 2022, Schedule-II, EIA is required for 'Water Supply, Sewerage System and Treatment (Category F) Based on the EIA and ESMP, Punjab EPD will monitor (as and when required) the project activities.

C. PRMSC

The Project Director of PRMSC is the in-charge for the financial and technical matters related to PRSWSSP. His responsibilities for monitoring the ESMP will consist of:

- Ensuring that the required environmental training is provided to the concerned PIU staff;
- To carry out random site visits to the construction sites to review the environmental performance of the Contractor;

- Review monitoring reports for the progress of environment-related activities;
- Make sure that the Contractor is implementing the additional measures suggested by the Supervision Consultant (SC) in environmental monitoring reports;
- To assist the Contractor in obtaining necessary approvals from the concerned departments;
- Maintaining interface with the other line departments/ stakeholders; and
- Reporting to the Punjab EPD on the status of ESMP implementation.

D. Environmental and Social Cell (ESC)

ESC has already been established in the PRMSC which is responsible to:

- Make sure that all the contractual obligations related to environmental and social compliance are met;
- Monitor the progress regarding the implementation of environmental and social safeguards as provided in the ESMP;
- Oversee the compliance of all the monitoring programs as given in ESMP;
- Check randomly whether monitoring of the environmental aspects of the proposed project during construction and operational phases is being properly carried out;
- Document and disclose monitoring results and identify necessary corrective and preventive actions in the periodic monitoring reports, and make follow-up on these actions to ensure progress toward the desired outcomes;
- Make sure that the contractor implements the additional measures suggested by the SC and PIMU; and
- Report the status of ESMP compliance to the Project Director, PRMSC.

E. Supervisory Consultant (SC)

The roles and responsibilities of SC will be:

- To oversee the performance of the Contractor to make sure that the Contractor is complying with ESMP;
- Ensuring that the day-to-day construction activities are carried out in an environmentally and socially sound and sustainable manner;
- Strong coordination with the Contractor and PRMSC;
- Preparing training materials and implementing programs;
- Ensure the implementation of the mitigation measures suggested in ESMP;
- To supervise and monitor environmental activities being performed at the site;
- Periodic reporting as mentioned in ESMP; and
- Suggest any additional mitigation measures (if required).

F. Construction Contractor (CC)

Contractors will be bound to appoint site-based Environmental and Social managers with relevant educational backgrounds and experience for PRSWSSP. The contractors' Environmental and Social manager will carry out the following activities:

- Implementation of the mitigation measures at the construction site;
- Contractor will be bound through the contract to take actions against all the special and general provisions of the contract document;
- Contractor will make sure the compliance of ESMP recommendations related to construction and will also be responsible for effective liaison with local heads of the community;
- Provision of proper Personal Protective Equipment (PPE) to the workers and train them for their proper use;
- To conduct the environmental and health & safety trainings to the workers/labour; and
- Coordinate with the Environmental Specialist and Social Development Specialist (SDS) of SC and PIMU.

7.2.2 Institutional Arrangement for Implementation of ESMP by PRMSC during O&M Phase

The proposed project will be administrated by PRMSC during the O&M phase. The Project Director, PRMSC with his ESC will be responsible for the following:

- Compliance with ESMP requirements for the O&M phase;
- Coordinating with the operational staff working under the ESC to monitor environmental compliance during project operation;
- Advising on, and monitoring tree plantations along the stagnant pool of water in the project area;
- Reporting on the progress of environmental compliance to the Punjab EPD;
- Assessing the long-term environmental impacts of project operation;
- Sustaining a working partnership among the PRMSC, Punjab Local Government Department, Punjab EPD, Agriculture, Irrigation, Forest and Wildlife departments of Punjab, NGOs, and other related public-private sector organizations.

7.3 Reporting

The contractor will prepare and submit monthly monitoring reports for compliance of implementation to the supervision consultant (SC) environmental team.

The distribution of periodic reports is given in **Table 24.**

Table 24: Distribution of Periodic Reports

Report	Prepared by	Reviewed by	Distribution
Monthly	Contractor	Reviewed by PRMSC-Environmental Unit; PRSWSSP	The Engineer and PRMSC
Quarterly	Contractor	Reviewed by PRMSC-Environmental Unit; PRSWSSP	The Engineer, PRMSC and The World Bank
Annual	Contractor	Reviewed by PRMSC-Environmental Unit; PRSWSSP	The Engineer, PRMSC and The World Bank
Final	Contractor	Reviewed by PRMSC-Environmental Unit; PRSWSSP	The Engineer, PRMSC and The World Bank

7.4 Non-Compliance with the ESMP

The implementation of the proposed ESMP involves inputs from various functionaries as discussed earlier. The contractor will be primarily responsible for ensuring the implementation of the mitigation measures proposed in the ESMP, which will be part of the contract documents. The provision of the environmental mitigation cost will be made in the total cost of the project. However, if the contractor fails to comply with the implementation of ESMP and submission of the monthly compliance reports, deductions will be made from the payments to the Contractor claimed under the heads of environmental components.

7.5 Contractors ESMP

The contractor will prepare a site-specific Contractor's ESMP (C-ESMP) based on the current ESMP and will get it approved by PRMSC before the start of work. This will ensure the implementation of the ESMP based on the site conditions at the time of execution, by the contractor.

The C-ESMP will include the following sub-plans:

- Traffic management plan,
- OHS plan,
- Pollution prevention plan,
- Camp management plan

7.6 Inclusion of ESMP in Bidding/ Contract Documents

The present ESMP will be included in the bidding/ contract documents and their implementation will be contractual binding for the contractors.

7.7 Environmental and Social Monitoring Plan

Monitoring will be carried out to ensure that the mitigation plans are regularly and effectively implemented. It will be performed at three levels. At the PRMSC level, the ESC will do ESMP monitoring to ensure that the mitigation plans are being effectively implemented. The environmental engineer of the Supervision Consultant will regularly monitor the ESMP

implementation by the contractor. At the contractor's level, the environmental monitoring checklist will be filled on daily basis by their environmental manager and countersigned by the environmental engineer (EE) of the Supervision Consultant.

Table 25 outlines the parameters that will be monitored, the expected frequencies of monitoring, and the responsible agency for monitoring.

Table 25: Environmental and Social Management Plan (ESMP)

Activity	Impacts	Mitigation Measures	Implementation Responsibility	Monitoring Indicators	Monitoring Frequency	Monitoring Responsibility	Cost
Pre-Construction / Design Phase							
Layout Planning & Design	Incompatible layout plans and engineering designs of the proposed project can undermine the overall aesthetics and ambiance of the project area	All structural, layout and engineering designs of the project are in strict accordance with the applicable national and international guidelines/ codes/ standards and engineering practices;	DC, PRMSC	Design provisions	Once (after completion of Detailed Design)	PIMU	N/A
Impacts of Drains construction	Inadequate sizing or gradients may lead to poor flow, blockages, or flooding during peak conditions. Improper alignment can cause conflict with existing utilities and affect land use. Selection of unsuitable materials or inadequate lining may result in erosion, siltation, or structural failure.	Plan proper alignment and depth to avoid conflicts with existing utilities and infrastructure. Ensure accurate hydraulic design with proper gradients to maintain self-cleansing velocity and avoid blockages. Provide adequate cross-sections and freeboard to handle peak stormwater flows safely. Incorporate silt traps and access points for ease of maintenance and prevention of	DC, PRMSC	Design provisions	Once (after completion of Detailed Design)	PIMU	N/A
Risk to Structures	In certain areas, katcha houses are present. This impact is considered sensitive due to its potential effect on local	Conduct pre-construction structural surveys of nearby katcha houses to assess vulnerability and design protective measures accordingly.	DC, PRMSC	Design provisions	Once (after completion of Detailed Design)	PIMU	N/A

Activity	Impacts	Mitigation Measures	Implementation Responsibility	Monitoring Indicators	Monitoring Frequency	Monitoring Responsibility	Cost
	communities. Weak soil-bearing capacity of these structures makes them particularly vulnerable to vibration, settlement, or lateral soil movement during construction.	Implement controlled dewatering and soil compaction techniques to maintain ground stability and prevent settlement around excavated areas.					
Improperly Designed Sewers	Improper designed sewers may not carry the waste load, leading to system-failure and financial loss.	All sewer lines including trunk, lateral and branch sewer lines have been designed considering the future population and waste generation rate;	DC, PRMSC	Design provisions	Once (after completion of Detailed Design)	PIMU	N/A
	The construction of high-rise overhead water tanks may cause visual obstruction.	The location of groundwater storage tanks, overhead reservoirs, pumping stations and STP have been finalized in close consultation with local community and representatives of local authorities.	DC, PRMSC	Design provisions	Once (after completion of Detailed Design)	PIMU	N/A
Groundwater	During operation probability of seepage through the sewers may also contaminate groundwater.	Efficient seepage control measures have been considered in selection of pipe materials during the planning stage	DC, PRMSC	Design provisions	Once (after completion of Detailed Design)	PIMU	N/A
		Procedure for efficient jointing of selected sewer pipes will be applied to avoid leakage from pipes	DC, PRMSC	Design provisions	Once (after completion of Detailed Design)	PIMU	N/A

Activity	Impacts	Mitigation Measures	Implementation Responsibility	Monitoring Indicators	Monitoring Frequency	Monitoring Responsibility	Cost
Damage to Existing Infrastructure	There are no public utilities except the electric poles which might get affected during construction activities and movement of machinery and the community will face temporary electricity cuts.	Alignment has been selected carefully to minimize disturbance to public utilities;	DC, PRMSC	Design provisions	Once (after completion of Detailed Design)	PIMU	N/A
		Relocation of the public utilities shall be planned and approved in consultation with relevant departments/authorities/stakeholders before project commencement if any, to avoid inconvenience to the public.	DC, PRMSC	Design provisions	Once (after completion of Detailed Design)	PIMU	N/A
Physical Cultural Resources	No historical/ archeological site is present in the project area. However, some cultural resources including mosques, graveyards and shrines are present. These will not be directly affected but the people may face access issues in visiting these facilities.	The alternative access routes will be provided in case the access has to be restricted during the execution period	DC, PRMSC	Design provisions	Once (after completion of Detailed Design)	PIMU	N/A
Fire Fighting System	In case of fire hazards, inefficient firefighting system at campsite may cause severe damage to the camp site and surrounding crops and houses. This will be a moderate adverse impact.	Contractor will provide firefighting system for construction camp, workshop and construction site;	DC, PRMSC	Design provisions	Once (after completion of Detailed Design)	PIMU	N/A
		A separate fire alarm system will also be installed at construction camp and near the construction site.	DC, PRMSC	Design provisions	Once (after completion of	PIMU	N/A

Activity	Impacts	Mitigation Measures	Implementation Responsibility	Monitoring Indicators	Monitoring Frequency	Monitoring Responsibility	Cost
					Detailed Design)		
Land Acquisition	Private land will be taken through VLD, State land will be used through NOC procedure. There will be no purchase of land, involuntary resettlement and no relocation of people or businesses.	No one will be forced or pressurized to donate land VLD should not be more than 10 % of the total land holding of the owner	DC, PRMSC	VLD procedure of ESMF	Once at the time of land acquisition	PIMU	N/A
Anticipated Impacts during the Construction Phase							
Topography	The construction activities are not expected to impact the topography of the area significantly except for those areas where physical activities i.e., earthwork is involved as well as stocking of material. The excavated material is to be mostly backfilled and the excessive material will be transported to strengthen the roadsides or will be dumped at the designated locations. This impact is site-specific, temporary,	Material stockpiles will be removed as soon as work is completed and the area will be reinstated;	CC, SC, PRMSC	Stockpiles and heaps of waste visible at the site.	Weekly	SC and PIMU	N/A
		Temporary storage sites will be allocated for the storage of excavated material;	CC, SC, PRMSC	Site allocation and preparation	Once before the excavation activity	SC and PIMU	N/A
		Temporary storage sites will be lined and must not allow infiltration	CC, SC, PRMSC	Site allocation and preparation	Before utilization of storage site	SC and PIMU	N/A
		The stockpiles must be covered with tarpaulin sheets or other adequate material;	CC, SC, PRMSC	Provision of tarpaulin	Before start of construction activity	SC and PIMU	The cost of tarpaulin is provided in the ESMP Budget

Activity	Impacts	Mitigation Measures	Implementation Responsibility	Monitoring Indicators	Monitoring Frequency	Monitoring Responsibility	Cost
	reversible, possible, and low significant	Pilling of material at large extent will not be allowed and the contractor will timely remove excavated material from the site.	CC, SC, PRMSC	Stockpiles and heaps of waste visible at the site.	Weekly	SC and PIMU	N/A
Soil Erosion	The soil would be exposed to erosion due to excavations for laying of sewers and water supply pipes. Construction activities such as clearing, excavation, filling, grading and setting up construction camps will affect the existing soil condition in the study area/ AoI. The clearing of vegetation can also loosen the soil and make it more susceptible to erosion due to wind and rain. There is also a possibility of silt runoff during rainy season causing soil erosion. During the rain, the eroded soil will mix with stagnant water to transform into slush, which can affect movement of vehicles and machinery and construction	Good engineering practices will help to control or minimize soil erosion both at the construction sites and in peripheral areas including provision of shuttering;	CC, SC, PRMSC	Provision of shuttering	Once	SC and PIMU	N/A
		Use of heavy machinery will be restricted as far as possible to avoid the destruction of soil structure;	CC, SC, PRMSC	Movement of machinery	During Construction Work	SC and PIMU	N/A
		Confining excavations to the specified spots as per the approved engineering drawings and unnecessary excavations should be avoided;	CC, SC, PRMSC	Excavations beyond the specified spots	During excavation works	SC and PIMU	N/A
		Stored excavated material shall be covered and preferably reused, e.g., in construction as backfill etc.	CC, SC, PRMSC	Wastage of excavated material; Backfilling	During backfilling	SC and PIMU	

Activity	Impacts	Mitigation Measures	Implementation Responsibility	Monitoring Indicators	Monitoring Frequency	Monitoring Responsibility	Cost
	workers as well as limit the movements of local people. This impact can be categorized as low adverse, site-specific, long term, permanent, highly probable and reversible.						
Soil Contamination	Contamination of soil may be caused by oil and chemical spills from construction machinery or uncontrolled runoff from equipment washing yards. This impact is permanent and minor negative in nature.	Chemicals/ hazardous products and wastes will be stored on impermeable surfaces in secure, covered areas with clear labelling of containers and with a tray or bund to contain leaks;	CC, SC, PRMSC	Monitoring compliance to Regular disposal of Chemical/ Hazardous waste; Photographic record;	Monthly	SC and PIMU	N/A
		All construction wastes from the site will be regularly removed and transported to approved waste disposal sites	CC, SC, PRMSC	No fall of transported material; Damaged road repaired. Record of harmful incidents that occurred.	Weekly	SC and PIMU	N/A
		Washing yards will be paved to avoid seepage of runoff from the yard;	CC, SC, PRMSC	Visual Inspection	Weekly	SC and PIMU	N/A

Activity	Impacts	Mitigation Measures	Implementation Responsibility	Monitoring Indicators	Monitoring Frequency	Monitoring Responsibility	Cost
		Awareness on emergency spill response procedures will be enhanced through training sessions;	CC, SC, PRMSC	Training Sessions	Once	SC and PIMU	N/A
		Oil leakages, chemicals and other liquids spills will be avoided/ minimized by providing appropriate storage places depending on the type of material for storage	CC, SC, PRMSC	Visual Inspection	Weekly	SC and PIMU	N/A
Trench Failure	The major construction activities involve excavation operations for laying water supply and sewerage lines. The major hazard associated with the excavation operations is trench failure. The unstable slopes may fail and settle in the trenches which may cause injuries and fatalities to the workers. This impact is probable, site specific and high adverse in nature.	Provision of adequate shuttering in the trenches;	CC, SC, PRMSC	Visual Inspection	Weekly	SC and PIMU	N/A
		Leftover shuttering may also be used in case of loose soil strata.	CC, SC, PRMSC	Visual Inspection	Weekly	SC and PIMU	N/A
Construction Camps/Camp Sites	Improper construction camp location and mismanagement of construction camp activities can lead to various social and environmental impacts	Working hours of noisy activities will be limited to normal daytime working hours when near identified sensitive receptors;	CC, SC, PRMSC	Field Observations	Weekly	SC and PIMU	N/A

Activity	Impacts	Mitigation Measures	Implementation Responsibility	Monitoring Indicators	Monitoring Frequency	Monitoring Responsibility	Cost
	which may include noise, health and safety, traffic problems, soil degradation, loss of vegetation and assets on the selected land, solid waste and water pollution. Furthermore, cultural differences, behavior of construction workers, potential disregard for local cultural norms can lead to increased tension between local communities and workers residing in the construction camps. This impact is temporary and moderate negative in nature.	Waste Management Plan will be implemented to include procedures for the classification, storage and disposal of all construction wastes and the training of employees who handle hazardous materials;	CC, SC, PRMSC	Compliance to waste management plan;	Monthly	SC and PIMU	N/A
		Construction camps will be established away from populated areas	CC, SC, PRMSC	Camp established at least 500m away from the nearest community; Local hired workforce;	Once	SC and PIMU	N/A
		NOC/ lease agreement will be signed between landowners and contractors.	CC, SC, PRMSC	Lease agreement signed / NOC obtained	Once before start of construction	SC and PIMU	N/A
		Regular training of workers will be carried out regarding local cultural norms, human behaviour, gender issues by the contractor during construction activities at site.	CC, SC, PRMSC	Any complaint from the local community.	Weekly check complaint register	SC and PIMU	Cost is provide in the ESMP Budget
Water Quality	Runoff and erosion from exposed soil surfaces, earthwork areas and stockpiles e.g., grouting	Protection of groundwater reserves from any source of contamination such as the construction and oily waste by making the ground	CC, SC, PRMSC	Monitoring compliance;	Quadrimesterly	SC and PIMU	N/A

Activity	Impacts	Mitigation Measures	Implementation Responsibility	Monitoring Indicators	Monitoring Frequency	Monitoring Responsibility	Cost
	and cement material with the rain. Construction waste, if left unattended will result in forming leachate that will percolate through the soil strata and will reach underground water table and hence, will end up contaminating groundwater. There is a probability that various materials like fuel, lubricant oil and other oily products, which are used during the construction phase may contaminate groundwater and channels carrying water.	impermeable through sheets or compaction;		Water quality testing.			
		Stockpiles of cement and other construction materials will be kept covered when not being used;	CC, SC, PRMSC	Use of tarpaulin for protection; Visual Inspection	Weekly	SC and PIMU	N/A
		Maintenance of vehicles will be carried out only in impermeable areas where any oil spillages can be contained;	CC, SC, PRMSC	Any spill observed; Availability of sealed containers for used oils and lubricants; Disposal options (e.g., local vendor) explored.	Weekly	SC and PIMU	N/A
		Careful planning of the works to avoid soil excavation works during rainy seasons;	CC, SC, PRMSC	Visual Inspection	During rainy season	SC and PIMU	N/A
		No activity will be undertaken in monsoon and careful attention must be paid to the weather forecast before excavation operations.	CC, SC, PRMSC	Visual Inspection	During rainy season	SC and PIMU	N/A

Activity	Impacts	Mitigation Measures	Implementation Responsibility	Monitoring Indicators	Monitoring Frequency	Monitoring Responsibility	Cost
		All kinds of waste will be stored in covered containers and disposed of safely as soon as possible;	CC, SC, PRMSC	Visual Inspection	Weekly	SC and PIMU	N/A
		The contractor will ensure that construction debris do not find their way into the drainage or irrigation canals which may get clogged.	CC, SC, PRMSC	Visual Inspection	Weekly	SC and PIMU	N/A
Air Quality	Air quality will be affected by various construction activities. Emissions may be spread over longer distances depending upon the wind speed, direction, temperature of surrounding air and atmospheric stability. In certain climatic condition such as hot summer, airborne dust can become a major nuisance if control techniques are not properly employed	All vehicles, machinery, equipment and generators used during construction activities will be kept in good working condition, properly tuned and maintained in order to minimize the exhaust emissions;	CC, SC, PRMSC	Dust emission controlled;	Weekly	SC and PIMU	N/A
		Open burning of solid waste from the contractor's camps will be strictly banned;	CC, SC, PRMSC	Monitoring compliance to disposal of waste;	Weekly	SC and PIMU	N/A
		Fuel with substantially lower sulphur content will be preferred;	CC, SC, PRMSC			SC and PIMU	N/A
		Personal Protective Equipment (PPEs) like masks, goggles and gloves etc. will be provided to workers;	CC, SC, PRMSC	Implementation of HSE; Visual Inspection	Daily	SC and PIMU	Cost given in ESMP Budget
		PEQS applicable to gaseous emissions generated by construction vehicles, equipment and machinery	CC, SC, PRMSC	Monitoring of machinery and equipment;	Daily	SC and PIMU	N/A

Activity	Impacts	Mitigation Measures	Implementation Responsibility	Monitoring Indicators	Monitoring Frequency	Monitoring Responsibility	Cost
		will be enforced during construction works.					
		Regular water sprinkling on the site and access roads will be carried out to suppress excessive dust emission(s)	CC, SC, PRMSC	Visual Monitoring	Daily	SC and PIMU	N/A
		Excavated trenches will be restored immediately to original level and paved after laying of sewer pipes;	CC, SC, PRMSC	Visual Inspection	Daily	SC and PIMU	N/A
		Vehicle speed in the project area will be prescribed not more than 20 km/hr and controlled accordingly;	CC, SC, PRMSC	Visual Inspection	Daily	SC and PIMU	N/A
		Diversion will be provided for local traffic movement;	CC, SC, PRMSC	Visual Inspection	Daily	SC and PIMU	N/A
		The vehicles carrying construction materials and the construction material storage areas will be covered with tarpaulin.	CC, SC, PRMSC	Use of tarpaulin for protection	Daily	SC and PIMU	N/A
		Air quality monitoring should be done by the 3rd party.	CC, SC, PRMSC	Air Quality	Monthly	SC and PIMU	Cost is provided in ESMP Budget
Dust	During construction stage, the dust level may increase considerably. Earthworks, site clearing, stockpiling and hauling of materials	Blowing of dust from potential sources at the worksite will be avoided by shielding them from the exterior, for example using polythene curtains or	CC, SC, PRMSC	Visual Inspection Air levels measured.	Daily	SC and PIMU	N/A

Activity	Impacts	Mitigation Measures	Implementation Responsibility	Monitoring Indicators	Monitoring Frequency	Monitoring Responsibility	Cost
	will generate dust and affect the local air shed. Local people and the workers may be exposed to high dust levels during landscaping, access road and site preparation. This impact is site-specific, temporary, reversible, likely and medium significant.	raising a fence of corrugated sheets around areas of active constructions					
		All excavation work will be sprinkled with water to control dust;	CC, SC, PRMSC	Visual Inspection	Daily	SC and PIMU	N/A
		Tires of all the vehicles leaving the site will be washed. No earth, mud, dust and the like will be deposited on the public road;	CC, SC, PRMSC	Visual Inspection	Daily	SC and PIMU	N/A
Noise	Noise level is expected to increase during construction activities. Main sources of noise and vibration will be heavy machinery such as excavators and other equipment. Noise generated by construction machinery is likely to affect sensitive receptors located within AoI. Health risks associated with exposure to continuous noise levels include high blood pressure, hypertension, annoyance and sleep disturbance, temporary	Construction workers will be provided suitable hearing protection like ear cap, or earmuffs and training them in their use;	CC, SC, PRMSC	Visual inspections; Noise levels measured.	Daily	SC and PIMU	Cost is provided in the ESMP Budget
		Selection of up-to-date and well-maintained equipment with reduced noise levels will be ensured by suitable in-built damping techniques or appropriate muffling devices	CC, SC, PRMSC	Visual inspections; Noise levels measured.	Daily	SC and PIMU	N/A
		Residents will be notified earlier before commencement of excavation operations.	CC, SC, PRMSC	Visual inspections;	Daily	SC and PIMU	N/A
		Noise quality monitoring should be done by the 3rd party.	CC, SC, PRMSC	Noise levels measured	Quarterly	SC and PIMU	Cost is provided in the ESMP Budget

Activity	Impacts	Mitigation Measures	Implementation Responsibility	Monitoring Indicators	Monitoring Frequency	Monitoring Responsibility	Cost
	threshold shift etc. The impacts of noise will be temporary and highly adverse in nature.						
Municipal and Construction Waste/ Wastewater	Due to construction activities municipal and construction waste will be generated from construction activities. The construction waste will include wastewater, oil spillage from machinery, domestic waste and construction waste etc.	Solid waste generated during construction and camp sites will be safely disposed of in demarcated waste disposal sites and the contractor will provide and implement a comprehensive waste management plan;	CC, SC, PRMSC	Monitoring compliance;	Weekly	SC and PIMU	N/A
		Burning of waste will be prohibited;	CC, SC, PRMSC	Visual Inspection	Daily	SC and PIMU	N/A
		Proper labelling of containers, including the identification and quantity of the contents, hazard contact information etc;	CC, SC, PRMSC	Visual Inspection	Weekly	SC and PIMU	N/A
		Emergency Response plan will be prepared to address the accidental spillage of fuels and hazardous goods;	CC, SC, PRMSC	Visual Inspection	Weekly	SC and PIMU	N/A
		Containers with covers will be provided on site to store waste	CC, SC, PRMSC	Visual Inspection	Daily	SC and PIMU	N/A
Resource Conservation	The materials used in construction of proposed project would include	Wastage of water will be reduced by training the workers involved in water use;	CC, SC, PRMSC	Visual Inspection	Daily	SC and PIMU	N/A

Activity	Impacts	Mitigation Measures	Implementation Responsibility	Monitoring Indicators	Monitoring Frequency	Monitoring Responsibility	Cost
	coarse aggregates (crush), fine aggregates (sand), brick ballast, water and cement etc. Almost all the materials to be used in the construction of proposed project are non-renewable and therefore their sustainable use is necessary for the future use. Excessive water consumption for drinking and washing purposes by the construction staff may undermine water resources in the project area and in certain cases may disturb the existing water supplies in the project area.	Wastage of water will be controlled through providing proper valves and through controlling pressure of the water;	CC, SC, PRMSC	Visual Inspection	Daily	SC and PIMU	N/A
		Water jets and sprays will be used for watering surfaces rather than using overflow system;	CC, SC, PRMSC	Visual Inspection	Daily	SC and PIMU	N/A
		Source of water will be carefully selected. Water use will not disturb the existing community water supplies	CC, SC, PRMSC	Any conflict on the water availability.	Fortnightly	SC and PIMU	N/A
		Reuse of construction waste materials will be considered;	CC, SC, PRMSC	Visual Inspection	Daily	SC and PIMU	N/A
		Unnecessary equipment washings will be avoided;	CC, SC, PRMSC	Visual Inspection	Daily	SC and PIMU	N/A
		The efficient and well-maintained equipment and machinery will be used;	CC, SC, PRMSC	Noise levels within permissible limits Gas emissions minimized; Dust emission controlled	Daily	SC and PIMU	N/A
		The equipment and machinery will be turned off when not in use;	CC, SC, PRMSC	Visual Inspection	Daily	SC and PIMU	N/A

Activity	Impacts	Mitigation Measures	Implementation Responsibility	Monitoring Indicators	Monitoring Frequency	Monitoring Responsibility	Cost
		Regular maintenance of machinery to avoid fuel leakages;	CC, SC, PRMSC	Log of vehicle and equipment repairs;	Daily	SC and PIMU	N/A
Biodiversity Conservation	<u>FLORA</u> On account of construction of the proposed water supply and sewerage system, no trees are envisaged to be cut/disturbed. Hence there will be no direct impact on the flora of project area. However, the dust emissions due to excavation operations will stick on the leaves of existing trees and may close their stomata thus hindering the photosynthesis process.	Campsites will be established on vacant land as far as possible, at least 500 m away from the residential areas;	CC, SC, PRMSC	Visual Inspection	Daily	SC and PIMU	N/A
		Construction vehicles, machinery and equipment will remain confined within their designated areas of movement;	CC, SC, PRMSC	Log Book of vehicle inventory	Daily	SC and PIMU	N/A
		The Contractor's staff and labour will be strictly directed not to damage any vegetation such as trees or bushes. They will use the paths and tracks for movement and will not be allowed to trespass through farmlands;	CC, SC, PRMSC	Any conflict with locals.	Daily	SC and PIMU	N/A
		Contractor will provide gas cylinders at the camps for cooking purposes and cutting of trees/ bushes for fuel will not be allowed.	CC, SC, PRMSC	Visual Inspection	Daily	SC and PIMU	N/A
	<u>FAUNA</u> The local animals mostly cats, dogs and jackals and specially the livestock i.e., goats and cows will get disturbed due to	Excavations will be limited to the approved engineering drawings;	CC, SC, PRMSC	Visual inspections; Photographic records.	Daily	SC and PIMU	N/A
		Harassing of animals will be prohibited	CC, SC, PRMSC	Visual Inspection	Daily	SC and PIMU	N/A

Activity	Impacts	Mitigation Measures	Implementation Responsibility	Monitoring Indicators	Monitoring Frequency	Monitoring Responsibility	Cost
	construction activities, especially the noisy activities. However, there will be no damage to their health and life. Some reptiles and insects may get killed/ injured during excavation operations.						
Occupational Health and Safety	Health risks and worker's safety problems may result at the workplace if the working conditions provide unsafe and/or unfavorable working environment. The health and safety issues are also associated with the operation of construction machinery and equipment, which may cause minor and severe injuries to workers. It will be a long term and severe negative impact.	Obligatory insurance against accidents for labourers/workers;	CC, SC, PRMSC	Accident/ Incident reported.	If happened	SC and PIMU	N/A
		Providing basic medical training to specified work staff and basic medical service and supplies to workers;	CC, SC, PRMSC	Maintained Training Record; Pictorial evidence	Weekly	SC and PIMU	N/A
		Layout plan for camp site, indicating safety measures taken by the contractor, e.g., firefighting equipment, safe storage of hazardous material, first aid, security, fencing, and contingency measures in case of accidents;	CC, SC, PRMSC	Visual inspection	Daily	SC and PIMU	N/A
		Work safety measures and good workmanship practices will be followed by the contractor to ensure no health risks for labourers, including	CC, SC, PRMSC	Visual inspection	Daily	SC and PIMU	Cost is provided in ESMP Budget

Activity	Impacts	Mitigation Measures	Implementation Responsibility	Monitoring Indicators	Monitoring Frequency	Monitoring Responsibility	Cost
		use of Personal Protective Equipment (PPE) i.e., oxygen masks/ kits etc.;					
		Protection devices (ear muffs) will be provided to the workers doing job in the vicinity of high noise generating machines i.e., excavators;	CC, SC, PRMSC	Visual inspection	Daily	SC and PIMU	Cost is provided in ESMP Budget
		Use of safety signs at the construction site will be ensured.	CC, SC, PRMSC	Visual inspection	Daily	SC and PIMU	N/A
		Contractor will immediately inform the consultant about the project related incident. The consultant will then submit a preliminary report to the PRMSC within 24 hours. Resultantly, PRMSC will promptly notify the World Bank for project-related incident within a maximum timeframe of 48 hours.	CC, SC, PRMSC	Accident/ Incident reported.	If happened	SC and PIMU	N/A
Community Health and Safety	The construction activities and vehicular movement at construction sites may result in roadside accidents particularly inflicting local communities who are not familiar with presence of heavy equipment. Open trenches and deep manhole may cause trip &	Medical screening of the laborers for communicable diseases will be conducted before hiring. Medical screenings are a basic requirement before the hiring of labour to prevent the spread of communicable diseases. However, on the basis of these screenings, diseased potential workers will not be barred from work; instead, necessary measures will be	CC, SC, PRMSC	Medical Reports Record;	Quarterly	Bi-Annual	

Activity	Impacts	Mitigation Measures	Implementation Responsibility	Monitoring Indicators	Monitoring Frequency	Monitoring Responsibility	Cost
	fall accidents for the local residents.	taken to prevent the spread of these diseases.					
		Provision of proper safety and diversion signage, particularly at sensitive/accident-prone spots;	CC, SC, PRMSC	Visual inspection	Daily	SC and PIMU	N/A
		The site will be restricted for the entry of irrelevant people particularly children.	CC, SC, PRMSC	Visual inspection	Daily	SC and PIMU	N/A
		Open trenches and deep excavated manholes will be protected by fence/barricade to avoid any accident.	CC, SC, PRMSC	Visual inspection	Daily	SC and PIMU	N/A
		Night time lighting will also be provided.	CC, SC, PRMSC	Visual inspection	Daily	SC and PIMU	N/A
		Awareness campaign regarding HSE will also be provided to locals.	CC, SC, PRMSC	Visual inspection	Daily	SC and PIMU	N/A
		Setting up speed limits within the village.	CC, SC, PRMSC	Visual inspection	Daily	SC and PIMU	N/A
		Special consultation session will be held with the nearby medical facility to ensure that it is well informed and well equipped to handle any dust allergy cases if required.	CC, SC, PRMSC	Consultation Meeting Record	Bi-annually	SC and PIMU	N/A
		Contractor will immediately inform the consultant about the project related incident. The consultant will then	CC, SC, PRMSC	Accident/ Incident reported.	If happened	SC and PIMU	N/A

Activity	Impacts	Mitigation Measures	Implementation Responsibility	Monitoring Indicators	Monitoring Frequency	Monitoring Responsibility	Cost
		submit a preliminary report to the PRMSC within 24 hours. Resultantly, PRMSC will promptly notify the World Bank for project-related incident within a maximum timeframe of 48 hours.					
Traffic Management	The traffic influx within the villages is very low. Most of the traffic within the villages include motorbikes and few cars. The project interventions will not create traffic congestion issues in the project area. However, their movement will be disturbed due to the excavation and construction works and people may face accessibility issues. This impact is temporary and major negative in nature.	The construction activities will be carried out in pockets/reaches, once a patch has been completed (i.e., pipes are laid and covered) then excavation on new patch shall be started;	CC, SC, PRMSC	Visual inspection	Daily	SC and PIMU	N/A
		Local community will be taken on board to plan alternate access routes in connecting streets to ensure mobility of local traffic;	CC, SC, PRMSC	Alternate route maps	Daily	SC and PIMU	N/A
		Plan the work within the minimum possible time..	CC, SC, PRMSC	Check targeted timeline	Daily	SC and PIMU	N/A
Nuisance/ Disturbance to Social Sensitive Areas	Since the proposed interventions will be carried out within the village's boundaries, therefore, the socially sensitive sites/places including schools, hospitals and religious centers will be	No work will be conducted near the religious places during religious congregations;	CC, SC, PRMSC	Visual Inspection	Daily	SC and PIMU	N/A
		Material transport to the site will be scheduled considering school timings;	CC, SC, PRMSC	Visual inspection	Daily	SC and PIMU	N/A
		Notify concerned schools, hospitals/dispensary etc. 2 weeks	CC, SC, PRMSC	Visual inspection	Daily	SC and PIMU	N/A

Activity	Impacts	Mitigation Measures	Implementation Responsibility	Monitoring Indicators	Monitoring Frequency	Monitoring Responsibility	Cost
	temporarily affected due to dust, noise and the community will face accessibility issues due to open trenches. Dust due to earthworks will create health hazard to children and people with ailments. This impact is temporary and major negative in nature.	prior to the work; conduct a 30 minutes awareness program on nature of work, likely disturbances and risks and construction work, mitigation measures in place, entry restrictions and dos and don'ts					
		Implement all measures suggested elsewhere in this report – dust and noise control, public safety, traffic management, strictly at the sites.	CC, SC, PRMSC	Visual inspection	Daily	SC and PIMU	N/A
Accessibility	Excavation of trenches and pipe/sewer laying work in the project area will obstruct access to residences, commercial buildings and businesses adjacent to the proposed project alignment. Disruption of access to commercial establishments may affect livelihood. The potential impacts are negative and moderate but short-term and temporary.	Leave space for access between mounds of excavated soil;	CC, SC, PRMSC	Visual inspection	Daily	SC and PIMU	N/A
		Consult affected business people to inform them in advance about the work schedule;	CC, SC, PRMSC	Consultation meeting; Pictorial evidence	Weekly	SC and PIMU	N/A
		If there are any holidays (i.e., Eid or Muharram etc.), the Contractor will complete the backfilling work of the trenches and will not leave any trench open before holidays;	CC, SC, PRMSC	Visual inspection Designated borrow and quarry areas used for access material;	Daily	SC and PIMU	N/A
		Provide sign boards for pedestrians to inform nature and duration of	CC, SC, PRMSC	Visual inspection	Weekly	SC and PIMU	N/A

Activity	Impacts	Mitigation Measures	Implementation Responsibility	Monitoring Indicators	Monitoring Frequency	Monitoring Responsibility	Cost
		construction works and contact numbers for concerns/complaints;					
Resilience to Climate Change	There are chances that the open trenches may get flooded during rainy season. Flooding can hamper the construction of overhead storage tanks, pumping station and STP. This impact can be categorized as direct, local, medium term, temporary and reversible.	Project components have been designed to withstand flooding;	CC, SC, PRMSC	Design provisions	Once (after completion of Detailed Design)	SC and PIMU	N/A
		The capacity of the sewerage/ drainage system has been designed and constructed based on extreme weather conditions predicted under international climate change models for Bhawana region to cater for extreme storm water runoff.	CC, SC, PRMSC	Check Meteorological department prediction of rain	Before construction	SC and PIMU	N/A
Liquid and Solid Waste from Construction Camps	Development of construction camps will generate significant quantities of liquid and solid waste. A total of five (05) nos. construction camps will be established in all five villages accommodating approximately 30 skilled and unskilled staff each (i.e., total 150 workers for all villages).	The waste generated from the camp site will be disposed of at existing dumping site of the Tehsil Bhawana by the Contractor;	CC, SC, PRMSC	Visual inspection	Daily	SC and PIMU	N/A
		Construction workers and supervisory staff will be encouraged and educated to practice waste minimization, reuse and recycling to reduce quantity of the waste;	CC, SC, PRMSC	Through Trainings Photographic record;	Monthly	SC and PIMU	N/A
		Domestic and chemical effluents from the construction camp will be disposed of by the development of on-site sanitation systems i.e., septic tank prior to discharge to nearby	CC, SC, PRMSC	Visual inspection	Daily	SC and PIMU	N/A

Activity	Impacts	Mitigation Measures	Implementation Responsibility	Monitoring Indicators	Monitoring Frequency	Monitoring Responsibility	Cost
		drain. Septic tank will be located adjacent to the construction camp. Proper monitoring to check the compliance of PEQS will be carried out;					
		All the solid waste from the camps will be properly collected at source by placing containers and disposed of through proper SWM system. Toxic waste will be handled, stored, transported and disposed separately;	CC, SC, PRMSC	Monitoring compliance to Regular disposal of waste; Photographic record;	Weekly	SC and PIMU	N/A
		The waste will be properly sealed in containers with proper labels indicating the nature of the waste;	CC, SC, PRMSC	Covered disposal containers placed at camp;	Weekly	SC and PIMU	N/A
		Solid waste will be segregated at source so that it can be re-used or recycled	CC, SC, PRMSC	Covered disposal containers placed at camp;	Weekly	SC and PIMU	N/A
Flammable and Hazardous Materials	Flammable materials to be used during the construction activities include diesel, furnace oil, petrol, Liquefied Petroleum	Safety procedures will be followed by the contractor and labors strictly while using, handling and storage of these materials;	CC, SC, PRMSC	Visual inspection	Daily	SC and PIMU	N/A

Activity	Impacts	Mitigation Measures	Implementation Responsibility	Monitoring Indicators	Monitoring Frequency	Monitoring Responsibility	Cost
	Gas (LPG), kerosene oil and machinery fuels. These materials present little risk to the environment, if properly transported stored and used; otherwise, they are potentially very dangerous. Improper storage and handling practices for these flammable and explosive materials can pose dangers of fire and blasts in the area.	Trainings will be provided to the contractor's staff for handling and using of flammable materials and explosives;	CC, SC, PRMSC	Monitoring compliance to handling of flammable material through inventory register; Photographic record;	Daily	SC and PIMU	N/A
		For safety of construction labors and immediate communities, it is suggested that contractor's staff will be trained about the procedures of safe use, handling and storage of materials;	CC, SC, PRMSC	Visual observation	Twice a week	SC and PIMU	N/A
		Emphasis will be to decrease the volume of mucking material by reusing and then the disposal at the marked area in environment friendly way. In order to reduce the volume of disposal material, maximum part of the excavated material can be used in other activities filling of borrow areas and natural depressions in the project area. In order to increase the aesthetics of the area, native grass can be planted by dumping the	CC, SC, PRMSC	Visual inspection	Weekly	SC and PIMU	N/A

Activity	Impacts	Mitigation Measures	Implementation Responsibility	Monitoring Indicators	Monitoring Frequency	Monitoring Responsibility	Cost
		surplus material in the proposed area with suitable soil cover.					
Gender Based Violence (GBV)	During construction phase, gender-based violence might arise due to discrimination made against women by unequal work distribution and unequal pay structure among others. Sexual harassment against women might occur as a consequence of mixing of men and women at the construction site, and moving on the roads and markets. This impact is negative in nature during construction stage.	Awareness will be created among the females at individual and community levels about the construction sites;	CC, SC, PRMSC			SC and PIMU	N/A
		Workers will not be allowed to crowd in the residential communities within the site;	CC, SC, PRMSC	Visual observation	Twice a week	SC and PIMU	N/A
		Alternative routes for pedestrian will be provided to avoid mixing of women with workers;	CC, SC, PRMSC	Visual Inspection	Daily	SC and PIMU	N/A
		Raise awareness among the communities of the potential risks of GBV, and establish response services in the nearby communities that can respond to instances of GBV (particularly those related to issues of labor influx);	CC, SC, PRMSC	Reported issues; Awareness compaigns	Daily	SC and PIMU	N/A
		The Contractor will make sure that no discrimination is made on the basis of gender while hiring of workers;	CC, SC, PRMSC	Hiring Criteria	Before Hiring	SC and PIMU	N/A
		Provisions of gender disaggregate bathing, changing, and sanitation facilities;	CC, SC, PRMSC	Design provisions	Once (before construction of construction camps)	SC and PIMU	N/A

Activity	Impacts	Mitigation Measures	Implementation Responsibility	Monitoring Indicators	Monitoring Frequency	Monitoring Responsibility	Cost
		Contractor will take proper measures to address and resolve issues relating to harassment, intimidation, and exploitation, especially in relation to women.	CC, SC, PRMSC	Visual inspection; Complaints reported	Daily	SC and PIMU	N/A
		The Contractor will prepare the Labor Code of Conduct and get it signed by all workers, and effectively communicate to all workers and project beneficiaries.	CC, SC, PRMSC	Hiring Criteria	Before Hiring	SC and PIMU	N/A
Influx of Labor	Risk of social conflict: Conflicts may arise between the local community and the construction workers, which may be related to religious, cultural or ethnic differences, or based on competition for local resources; Increased risk of illegitimate behaviour and crime: The influx of workers and service providers into communities may increase the rate of crimes and a perception of insecurity by the local community. Such	Labour camp(s) will be established away from residential population;	CC, SC, PRMSC	As per approved site	Once	SC and PIMU	N/A
		Preference will be given to the local people to work with contractor, and contractor should hire maximum labour force from the project area because this will reduce the labour influx	CC, SC, PRMSC	Hiring Criteria	Once before hiring	SC and PIMU	N/A
		Awareness will be created among the work force to ensure respect for local customs;	CC, SC, PRMSC	Monitor training record	Monthly	SC and PIMU	N/A
		Construction work will be completed within the stipulated time to move workers to next location;	CC, SC, PRMSC	Visual inspection	Daily	SC and PIMU	N/A
		Labor force will be shuffled with the time;	CC, SC, PRMSC	Visual inspection	Weekly	SC and PIMU	N/A

Activity	Impacts	Mitigation Measures	Implementation Responsibility	Monitoring Indicators	Monitoring Frequency	Monitoring Responsibility	Cost
	illegitimate behaviour and crimes can include theft, physical assaults, substance abuse, sexual assault and human trafficking;	Create awareness among workers on proper sanitation and hygiene practices to endorse proper health and maintain good housekeeping practices at all project sites;	CC, SC, PRMSC	Visual inspection	Daily	SC and PIMU	N/A
		Provide adequate personal hygiene facilities in good condition with adequate supply of clean water;	CC, SC, PRMSC	Visual inspection	Daily	SC and PIMU	N/A
		Make arrangements to treat the affected workers on time to control the movement of vectors disease	CC, SC, PRMSC	Visual inspection; Complaint reported	Daily	SC and PIMU	N/A
		Sensitize workers and surrounding communities on awareness and prevention of HIV/AIDS and sexually transmitted infections (STI) through training, awareness campaigns and workshops during community meetings;	CC, SC, PRMSC	Complaint reported	Weekly	SC and PIMU	N/A
		Provide proper and free HIV/AIDS and STI health screening and counselling for site workers and community members;	CC, SC, PRMSC	Hiring protocols	Before hiring	SC and PIMU	N/A
		Develop and enforce a strict code of conduct for workers to regulate behaviour in the local communities;	CC, SC, PRMSC	Visual inspection;	Weekly	SC and PIMU	N/A

Activity	Impacts	Mitigation Measures	Implementation Responsibility	Monitoring Indicators	Monitoring Frequency	Monitoring Responsibility	Cost
				Complaint reported			
		Prohibiting drugs, alcohol, weapons, and ammunition on the worksite among personnel;	CC, SC, PRMSC	Visual inspection; Complaints reported	Daily	SC and PIMU	N/A
		The Contractor must guarantee that good relations are maintained with local communities and their leaders to help reduce the risk of vandalism and theft.	CC, SC, PRMSC	Visual inspection	Daily	SC and PIMU	N/A
Social/ Cultural Conflicts	During the construction phase of the project, conflicts may arise between labor force and local community. Use of local resources and products by the construction workers can generate stress on the local biophysical resources. Furthermore, difference in cultural values may also cause discomfort to local residents. This impact is temporary and minor negative in nature.	Public notification through announcements in local mosques during the entire construction phase to avoid any inconvenience in accessibility to the locals;	CC, SC, PRMSC	Visual inspection	Daily	SC and PIMU	N/A
		Establishment of formal links with affected communities;	CC, SC, PRMSC	Visual inspection	Weekly	SC and PIMU	N/A
		Plan for social grievance redress mechanisms including the local leaders and community representatives;	CC, SC, PRMSC	During construction of the work	Weekly	SC and PIMU	N/A
		Local labor will preferably be employed for construction works;	CC, SC, PRMSC	Hiring Policies	Once (Before Hiring)	SC and PIMU	N/A

Activity	Impacts	Mitigation Measures	Implementation Responsibility	Monitoring Indicators	Monitoring Frequency	Monitoring Responsibility	Cost
		Careful planning and training of workforce to minimize disturbance to the local people;	CC, SC, PRMSC	Visual inspection	Daily	SC and PIMU	N/A
		Contractor will preferably arrange their own sources of water.	CC, SC, PRMSC	Visual observations	Daily	SC and PIMU	N/A
Child Labor	Due to poverty and feeble financial situation of the area, the underaged children might get involved with the contractor various construction works. This will be the violation of the Child Labor Act. Furthermore, SEA/SH issues might arise which will create social conflicts. This impact is adverse and temporary in nature.	Standard clause in the contracts related to child labor explicit prohibitions, etc.) and contractor will ensure compliance to the contractual provisions on bonded and child labor, equal wages for similar work explicit prohibitions, etc.).	CC, SC, PRMSC	Visual Observation	Daily	SC and PIMU	N/A
Anticipated Impacts during Operational Phase							
Soil	The soil quality may be affected due to leakage/ infiltration from sewer lines and STP bed. The sludge generated from cleaning/ maintenance of pumping stations, manholes, sewers and STP may contaminate	Sludge shall be treated prior to ultimate use/disposal. Various options for sludge treatment include Digestion, Drying/ Dewatering, Composting, Lime Stabilization, Heat Treatment must be considered;	PRMSC	Visual inspection	Weekly	PIMU-PRMSC	N/A

Activity	Impacts	Mitigation Measures	Implementation Responsibility	Monitoring Indicators	Monitoring Frequency	Monitoring Responsibility	Cost
	the soil. The liner of the STP, while desludging may get dried and cracks may lead to the seepage of wastewater and thus contaminate the soil. Improper disposal of scum and sludge is another concern. This is a moderate negative impact.						
Air Quality	The operation of sewerage scheme will result in generation of gases including H_2S and CH_4. H_2S is a foul-smelling poisonous gas which might be harmful for the sewer-men and could be fatal sometimes. CH_4 is natural gas also referred to as a greenhouse gas	Provision of exhaust gas vents at appropriate locations in the design	PRMSC	Visual inspection	Monthly	PIMU-PRMSC	N/A
		Sewer-men will cover their faces with gas mask while entering the sewer for cleaning or maintenance purposes;	PRMSC	Visual inspection; Use of PPEs	Weekly	PIMU-PRMSC	Cost given in ESMP Budget
		It's better to use sucking machinery for cleaning of sewers;	PRMSC	Availability	Once	PIMU-PRMSC	N/A
		Use gas detector before inspection;	PRMSC	Visual inspection	Daily	PIMU-PRMSC	N/A
		Adequate tree plantation must be done around the STP to control the spread of odour;	PRMSC	Visual inspection	Weekly (maintenance)	PIMU-PRMSC	N/A
Odour	STP are designed on adequate waste loading and function well if they are not overloaded. The	The STP should not be overloaded and personnel dealing in operation should be trained to avoid operational issues;	PRMSC	Visual inspection	Daily	PIMU-PRMSC	N/A

Activity	Impacts	Mitigation Measures	Implementation Responsibility	Monitoring Indicators	Monitoring Frequency	Monitoring Responsibility	Cost
	overloading will result in malfunctioning of STP and it will result in significant odour generation in the vicinity. This impact is temporary and high adverse in nature.						
Solid Waste	Domestic and hazardous wastes would be generated during cleaning and maintenance activities. The solid waste during operational phase will consist of plastics, metal and organic wastes present in sewer lines which can cause blockage in sewerage system.	Waste shall be collected, stored and disposed of according to relevant standards in approved facilities;	PRMSC	Visual inspection	Weekly	PIMU-PRMSC	N/A
		An organized collection system and its implementation through a licensed contractor;	PRMSC	Hiring of licensed contractor	Once	PIMU-PRMSC	N/A
		The containers will be timely removed and the fine will be imposed on contractor in case of violations;	PRMSC	Visual inspection	Daily	PIMU-PRMSC	N/A
		Closed containers will be used for transportation of waste to the dumping site;	PRMSC	Visual inspection	Weekly	PIMU-PRMSC	N/A
		Schedule inspection of the sewer lines and STP to keep it clean and to identify any hazardous material;	PRMSC	Visual inspection	Daily	PIMU-PRMSC	N/A
		Solid waste bins shall be placed at appropriate locations to avoid its mixing in wastewater.	PRMSC	Visual inspection	Weekly	PIMU-PRMSC	N/A

Activity	Impacts	Mitigation Measures	Implementation Responsibility	Monitoring Indicators	Monitoring Frequency	Monitoring Responsibility	Cost
Sludge	Sludge is semi solid material which will be settled at the bottom of the STP due to anaerobic decomposition of biomass. Significant amount of sludge will not be produced in ABR; however, periodic desludging will be done to achieve good removal efficiency. The removed sludge in wet form, if left unattended will create nuisance i.e., odor, soil contamination, groundwater contamination (through percolation/ seepage) and will serve as breeding ground for disease vector.	Appropriate sludge treatment must be undertaken before disposal of sludge;	PRMSC	Visual inspection	Monthly	PIMU-PRMSC	N/A
		The sludge must never be left unattended and should be transferred to designated dumping site after adequate treatment;	PRMSC	Visual inspection	Monthly	PIMU-PRMSC	N/A
		Dried sludge can be used as a land conditioner in the fields.	PRMSC	Visual inspection	Monthly	PIMU-PRMSC	N/A
		In case of maintenance/sludge removal, alternative ponds shall remain functional;	PRMSC	Visual inspection	Monthly	PIMU-PRMSC	N/A
		Inlet and outlet pipework access/maintenance pits should be inspected regularly for blockages. These pits should be covered at other times.	PRMSC	Visual inspection	Daily	PIMU-PRMSC	N/A
		The water must be bypassed during rain and flooding.	PRMSC	Visual inspection	During rain	PIMU-PRMSC	N/A
Brine Disposal	In case of operation of RO filtration Plants, around 75% of water is rejected and 25% is consumed as treated product water. It means that for every 2000 lph capacity RO plant; we require 6000 lph of raw water to be treated from	This water should not be thrown into municipal sewer, rather it should be reused. The reject water will be discharge into irrigation channels where flow will be controlled to ensure proper dilution and water will be used for irrigation. Brine can be managed through controlled dilution with freshwater or	PRMSC	Visual inspection	Monthly	PIMU-PRMSC	

Activity	Impacts	Mitigation Measures	Implementation Responsibility	Monitoring Indicators	Monitoring Frequency	Monitoring Responsibility	Cost
	which 4000 lph will be the RO reject or brine. So, per day 32000 litres of wastewater will be generated from a single RO. The rejected water is free from bacteria, viruses and other pathogens but has only dissolved particles in it. RO concentrate disposal issues present significant design and operational challenges that must be addressed. Conventional disposal techniques mostly suffer from direct or indirect contamination of water/soil.	treated effluent to reduce salinity before reuse for irrigation of non-food vegetation e.g, in Barley, sugar beet, and date palms (southern Punjab). Reuse of brine for dust suppression on unpaved roads can be considered where environmentally acceptable. Planting halophytic grasses and shrubs in designated areas can help utilize saline water while stabilizing soil. Small-scale ponds with brine-tolerant fish or shrimp species can be developed in suitable areas.					
Community Health Hazards	During desludging and cleaning operations the sludge will be piled up temporarily along the manholes and will be a hazard for passers-by and local community. This impact is temporary and moderate negative in nature.	The treated wastewater shall be routed to the agricultural area in a way that there must not be physical contact of the community;	PRMSC	Visual inspection	Daily	PIMU-PRMSC	N/A
		The community must be educated on the effects of treated wastewater to avoid health issues;	PRMSC	Through Seminars	Yearly	PIMU-PRMSC	N/A
		The sludge must be timely removed from the site and the area must be	PRMSC	Visual inspection	Monthly	PIMU-PRMSC	N/A

Activity	Impacts	Mitigation Measures	Implementation Responsibility	Monitoring Indicators	Monitoring Frequency	Monitoring Responsibility	Cost
	The treated wastewater from STP will be used in agricultures in nearby areas. The community using the part will be exposed to the effects of treated wastewater. This impact is permanent and moderate negative in nature.	barricaded during desludging and cleaning periods.					
Cumulative Impact of Several Water extraction Points and Sewerage Treatment Systems	Cumulative impact may occur as a result of development of several treatment plants or several water extraction points.	Water quality monitoring should be done by the third party on quarterly basis to ensure the supply of safe drinking water.	PRMSC	WHO Guideline /PEQS	Quarterly	PIMU-PRMSC	PCRWR through Separate contract
		Groundwater table will be monitored periodically.	PRMSC	Depth in meter/feet	Quarterly	PIMU-PRMSC	N/A
		Maintenance of ABR should be done annually for its smooth operations.	PRMSC	Visual inspection	Annually	PIMU-PRMSC	N/A
		Ensure the treated effluent follows the National Environmental Quality Standards	PRMSC	PEQS	Monthly	PIMU-PRMSC	PCRWR through Separate contract
		Water metering system should be installed to know the total consumption of water.	PRMSC	Water Meters	Once at the time of connection	PIMU-PRMSC	N/A

Activity	Impacts	Mitigation Measures	Implementation Responsibility	Monitoring Indicators	Monitoring Frequency	Monitoring Responsibility	Cost
Social Inclusion	It is crucial to ensure that every stakeholder of the community have equal access on the provision of clean drinking water and sanitation facilities, improved healthcare facilities, educational facilities and on economic excess and job opportunities. In this proposed project efforts will be made to promote the participation of marginalized groups, such as women and minorities, elderly person in decision-making processes and community activities	Providing awareness campaigns to increase knowledge and understanding of the project and challenges faced by marginalized groups.	PRMSC	Visual inspection	Weekly	PIMU-PRMSC	N/A
		Providing awareness on the importance of clean drinking water & sanitation, education, job training, and community services to underserved and marginalized populations.	PRMSC	Visual inspection	Weekly	PIMU-PRMSC	N/A
		Fostering partnerships between PRMSC-TO and VOs/VCs to promote social inclusion to address the root causes of social exclusion.	PRMSC	Visual inspection	Monthly	PIMU-PRMSC	N/A
		Regular monitoring and evaluation of project policies and programs to ensure they are effective and inclusive	PRMSC	Visual inspection	Weekly	PIMU-PRMSC	N/A
Elite Capture	Elite capture is often facilitated by corruption, nepotism, and patronage networks, which enable the elites to manipulate the system in their favor. The consequences of elite capture are far-reaching, with the general public	To avoid elite capture the VLD will not be accepted from the person having more than 25 acres land	PRMSC	Visual inspection	Monthly in meeting of VO	PIMU-PRMSC	N/A
		Involving multiple stakeholders, including community members, in decision-making processes related to project activities.	PRMSC	Visual inspection	Monthly in meeting of VO	PIMU-PRMSC	N/A

Activity	Impacts	Mitigation Measures	Implementation Responsibility	Monitoring Indicators	Monitoring Frequency	Monitoring Responsibility	Cost
	often left without access to basic amenities such as health, education, water and sanitation.	Robust and transparent GRM will be implemented	PRMSC	Visual inspection	Daily	PIMU-PRMSC	N/A
		To promote the participation of marginalized groups, such as women and minorities, in decision-making processes	PRMSC				
		Strengthening institutions such as VO's/VC's and regulatory agencies without undue influence from elites	PRMSC	Visual inspection	Once at the time of VO's formation or Change in VO's	PIMU-PRMSC	N/A
		Due diligence will be held during VLD process to absolve the doner from all the associated land rights.	PRMSC	Visual inspection	Once at the time of VLD	PIMU-PRMSC	N/A
End users of Treated wastewater	The VO of the village will decide the distribution rights of treated wastewater according to the needs of community.	End water users will adopt water conservation measures such as reducing water wastage, using efficient irrigation methods	PRMSC	Awareness campaigns	Weekly	PIMU-PRMSC	N/A
		Equal rights of the community on the usage of treated water will be ensure by the VO's.	PRMSC	Visual inspection	Need Basis	PIMU-PRMSC	N/A
		Distribution of treated wastewater will be decided by VO's/VCs in village	PRMSC	VO's Meeting	Need Basis	PIMU-PRMSC	N/A
		VO will ensure monitoring and evaluation on regular basis regarding	PRMSC	Visual inspection	Need Basis	PIMU-PRMSC	N/A

Activity	Impacts	Mitigation Measures	Implementation Responsibility	Monitoring Indicators	Monitoring Frequency	Monitoring Responsibility	Cost
		the usage and conservation of treated water					
		Awareness campaigns will be conducted on the understanding and importance of water conservation and its impacts.	PRMSC	Awareness campaigns	Once at the time of VLD	PIMU-PRMSC	N/A
Occupational Health and Safety Hazards	Infections resulting from direct contact with treated wastewater, and from infected wounds; and Intestinal infections that are transmitted by flies feeding on the STP.	The Contractor should prepare OHS and ERPs during operation phase;	PRMSC	Implementation of OHS & ERPs	Daily	PIMU-PRMSC	N/A
		Instructing the workforce on handling of treated wastewater;	PRMSC	Visual inspection	Daily	PIMU-PRMSC	N/A
		Provide basic medical training to the specified work staff and basic medical service and supplies to workers;	PRMSC	Visual inspection;	Daily	PIMU-PRMSC	N/A
		Obligatory insurance of work laborers against accidents;	PRMSC	Visual inspection	Fortnightly	PIMU-PRMSC	N/A
		Provision of safety measures such as emergency sirens, firefighting equipment, first aid, and contingency measures in case of accidents;	PRMSC	Visual inspection	Monthly	PIMU-PRMSC	Cost is provided in ESMP budget
		PRMSC-Tehsil Office, within 24 hours, will promptly notify the World Bank for project-related incident within a maximum timeframe of 24 hours.	PRMSC- Tehsil Office	Accident/ Incident reported.	If happened	PRMSC	N/A

KEY

CC	Construction Contractor
DC	Design Consultant
EPA	Environment Protection Agency
SC	Supervision Consultant
PIMU-PRMSC	project Implementation Unit – Punjab Rural Municipal Services Company

7.8 Grievance Redressal Mechanism (GRM)

The Grievance Redress Mechanism (GRM), outlines the policy and procedure for documenting, addressing, responding, and employing methods to resolve project grievances and complaints that may emerge during and after PRSWSSP sub-projects implementation. It will also cater to managing any disconnects that emerge from the field level and that have significant implications for the effective implementation of the sub-project interventions.

In an effort to deter fraud and corruption, the use of a dedicated mobile application has been proposed for reporting grievances from the field level to district and provincial headquarters. This will not only provide a coherent system of checks and balances but will also enable swift redressal and effective monitoring of complaints.

The PIMU at the Local Government & Community Development Department (LG&CDD) level will serve as the Secretariat for the Grievance Redressal Committee (GRC Directorate) that will be responsible for providing oversight on the entire GRM process at a strategic level and monitoring complaints management.

Water supply & sanitation are imperative daily basis facilities. Due to, continuous use and all-time requirement, there is a tendency for routine O&M requirements of the facilities. O&M will be needed as soon as project interventions are completed in the village. Due to the huge number of beneficiaries spread, a comprehensive complaint redressal model is indispensable for Service Delivery Unit (SDU). The Grievance Redress Mechanism (GRM) will be consistent with the Component 4 Project Management and Monitoring sub-component 4.2 Grievance Redressal Model is part of the Project of PRSWSSP. Project activities may cause social friction if Projects do not have an effective GRM.

7.8.1 Objectives

The Grievance Redressal Mechanism (GRM) will be consistent with the requirements of the World Bank safeguard policies to ensure the mitigation of community concerns, risk management, and maximization of environmental and social benefits. The overall objective of the GRM is therefore to provide a robust system of procedures and processes that provides for transparent and rapid resolution of concerns and complaints identified at the village level.

The GRM will be accessible to diverse members of the community, including women, senior citizens, and other vulnerable groups. Culturally, appropriate communication mechanisms will be used at all sub-project sites both to spread awareness regarding the GRM process as well as complaints management. This GRM will be integrated with the PRSWSSP overall project GRM hotline

7.8.2 Disclosure of GRM

The final processes and procedures for the GRM will be translated into local languages and disseminated at all sub-project locations. These shall be made available (in both leaflet and poster format) to all subproject locations through the offices of each SDU. Dedicated male

and female Grievance Focal Persons for each sub-project location will play an instrumental role in spreading awareness regarding the GRM, including the use of information technology for reporting and monitoring complaints. It will be ensured that the GRM will be easily accessible for all beneficiaries and workers to raise workplace concerns.

7.8.3 **Records and Monitoring**

The Project Director's Office will maintain an electronic database at the PIMU that will provide a summary of complaints received and mitigations. The PD office will also provide an analysis of the grievances at each sub-project location using a pre-designed Monitoring and Evaluation (M&E) template that will give insight into the type of complaints received and a qualitative and quantitative review of grievance redressal. The PD's office will also be responsible for uploading the actions and results for each grievance for each sub-project location on a periodic basis to the Project website. The dedicated mobile application that will be used to communicate grievances will provide the basis for recording complaints both at the provincial and district levels.

Apart from the electronic database that will be maintained at the PIMU level, a manual register of all complaints and actions taken will be maintained by the Environmental and Social Focal Persons at the Office of the SDU-TOs and a manual register of all day-to-day complaints and their grievance redressal details will be maintained by VOs their office.

GBV-related issues will be recorded through GRM, two separate focal persons for males and females are part of Village Organization VO – which will also work as tier-1 of the Grievance Redressal Committee (GRC). The female focal person – trained on the referral directory – will be responsible for further referral of GBV-related complaints to the forums concerned. A multi-sectoral referral system is proposed, which will include referral to The Punjab Women's Toll-Free Helpline 1043 available 24/7. It is managed and supervised by Punjab Commission on the Status of Women (PCSW). Their helpline team comprises all-women call agents, three legal advisors, a psychosocial counselor, supervisors, and management staff. Moreover, awareness and advocacy training at schools and community level would be conducted on social protection mechanisms/ referral mechanisms vis-à-vis Gender-Based Violence (physical, sexual, verbal, psychological, etc.), Sexual Exploitation and Abuse (SEA), and Sexual Harassment (SH). The Punjab Commission on the Status of Women (PCSW) has been identified as a key stakeholder. PCSW will be informed of the project activities and an institutional link will be established. Furthermore, at the PRMSC Tehsil Office, the Behavior Change and Communication (BCC) Officer – in addition to being member of GRC Tier-I&II – will initially deal with gender related issues/ complaints and further refer the same to the Gender Specialist at Head Office, PRMSC.

7.8.4 **Proposed Institutional Mechanisms**

It is proposed to establish the following prior to commencing project implementation activities including pre-construction activities:

Tehsil Level-Public Complaints Center (PCC) in SDU-TO will be responsible to receive, log, and resolve complaints at the site and in Village-level. The complainant would be able to launch a complaint on a toll-free number, mobile application, message, or telephone.

Tier 1: Village level –Panchayat/Village Councils (VC) made under Punjab Local Government (Amendment) Ordinance 2021 will act as the 1st Tier of GRM at the village/community level. Since VCs are not functional, the Project Appraisal Document (PAD) recommends establishment of informal Village Organizations (VOs) in lieu of VCs until formal VCs are elected. This informal VO will comprise of nine (09) members including a chairperson. All the members of the VO will be elected by the village community except a line department's representative and a BCC Officer of the PRMSC. These non-elected members are part of the VOs to give credence/ recognition to the VO. Moreover, the BCC Officer will forward the unaddressed complaints to the Tier-II of the GRC.

Tier 2: Grievance Redress Committee (GRC-Tehsil Level) in SDU-TO will be established for each tehsil that will manage GRM aspects for all sub-project locations in each tehsil including decisions to be taken, actions and monitoring of complaints resolution at the sub-project level. GRC-II, Tier-II comprises of nine (09) members. Respective Tehsil Manager will spearhead the Tier-II. Moreover, to ensure community participation in the Tier-II, the chairperson of the concerned village – from where the complaint is lodged – will also be a member.

Tier 3: PIMU Level-GRC at PMIU (LG&CDD) will be responsible to oversee the overall functions of the GRM at a strategic level including monthly review. GRC Tier-III will comprise of nine (09) members. The Project Director / Chief Executive Officer, PRMSC, will spearhead the Tier-III. Moreover, to ensure community participation in the Tier-III, the chairperson of the concerned village – from where the complaint is lodged – will also be a member.

The composition of GRCs of all tiers has been attached as Annexure-10.

7.8.5 GRM Process Implementation

The grievance redress process is described hereunder:

Through the envisaged system, the complainant would be able to launch a complaint on a toll-free number, mobile application, message, or telephone (GRM can accept anonymous grievances).

Details of the complaints and the complainants will be entered into the system and a complaint number will be provided to the complainant through SMS.

In SDU a specific person will be designated to monitor the system and issue necessary instruction to relevant quarter for necessary action.

The GRM will provide an interface to complainants to check the status of their complaint and a dashboard for SDU & PIMU to monitor the progress on the complaints.

The system will bridge the gap between the masses and the service provider.

Monitoring officers will precisely know the details of pending complaints in every SDU. The performance of the SDU could also be easily monitored through it.

The GRM will have a built-in escalation system for moving unresolved complaints to higher levels.

7.8.6 Mode of Complaint

The complainant can lodge their complaints by opting the following modes:

Written Application	**Telephonically**	**Verbally**	**Android Application**	**Website**

7.8.7 GRM Procedures and Timelines

The tracking and documenting of grievance resolutions will include the following elements:

- Tracking complainant(s) from subprojects sites (field and community level) to PIMU;
- Dedicated staff to update the database routinely;
- Promote transparency, publicize how complaints are being handled, and periodically evaluate the overall functioning of the mechanism;
- Processes for informing stakeholders about the status of a case; and
- Procedures to retrieve data for reporting purposes, including the periodic reports, from Village and Tehsil and document them into the monthly progress reports at PIMU.

GR (Village level) will be responsible to receive, log, and resolve complaints at the village level. The Grievance Redress Committee at the village Panchayats will review and identify

actions to be taken to address the complaints at its weekly meeting. If not resolved timely then complaint would be referred to GRC-Tehsil Level (SDU-TO) within 3 days after receiving.

GRC-SDU-TO will try to resolve the complaints in a satisfactory manner anyhow, if not satisfactorily resolved by the village panchayats/councils and Tehsil level, then the grievance will be referred for consideration by GRC at the PIMU/LG&CDD level within one week.

Every effort will be made to address or resolve grievances within the following fixed timelines, which will be an indicator of the performance of the handling system. Acknowledgment of a written submission will be issued to the complainant within three working days.

If the complainant is not satisfied, the complaint will have the option to seek redress through the court of law.

GRM Procedures for Contractor:

The contractor will add a detailed description of GRM, uptake channels, handling process, and confidential reporting system in C-ESMP.

8 ESMP Budget

8.1 ESMP Cost

As per letter Ref. No. PRMSC/PRSWSSP/EDCS/ESS/19 dated 10-01-2025, the Environmental and Social Management Plan (ESMP) cost has been finalized at PKR 1,520,575 per village, as agreed by PRMSC in consultation with the World Bank representative. Accordingly, for the total two hundred and thirty-two (232) villages, the consolidated ESMP cost amounts to PKR 352,773,400 The implementation and expenditure of ESMP measures during the construction phase shall be the responsibility of the Contractor. Breakup cost is given below: Detail ESMP cost is attached as **Annex-XVI.**

Sr No.	Description	Amount PKR
1	ESMP cost for one Village	1,520,575
2	ESMP cost for 232 Villages	352,773,400
Grand Total in Million (RS.)		**352.773**

The ESMP budget consists of six main components:

i. Personal Protective Equipment (PPE)
ii. Health Safety Environment and Trainings,
iii. Environmental testing and monitoring,
iv. CESMP formulation Cost,
v. HSE Supervision Cost (staffing),
vi. Waste Management and Housekeeping

Table 26: Village-wise ESMP Cost

Village-wise ESMP Cost		
Sr.	**ESMP Component**	**Cost (PKR)**
1	PPE	581,950
2	HSE &Training	416,500
3	Env. Monitoring	286,125
4.	CESMP formulation Cost	50,000
5	HSE Supervision Cost	120,000
6.	Waste Management and Housekeeping	66,000
Total (One Village)		**1,520,575**

Breakup of each component of the ESMP cost is provided below:

8.2 Budget Estimate for PPE During the Construction Phases

Personal Protective Equipment cost is including in the ESMP Cost significantly for Health, Safety and Environment and divided into two categories according to the size of villages

small & Large. Breakup of the estimate of the HSE cost for villages is provided in table 27. Which includes safety items ear plugs, helmets, safety shoes, protective goggles, Gloves, Masks and first aid kits.

Table 27: Budget Estimate for HSE During the Construction Phase

Sr. No.	Item Description	ISO / Standard Code / Description	Unit	Unit Rate (Rs)	Quantity (Per Village)	Amount (Rs)
Personal Protective Equipments						
1	Safety Jackets	EN ISO 20471: 360 degree visibility Fluorescent yellow/orange; retro-reflective strips; breathable mesh fabric; secure Velcro or zipper closure, provided in approriate sizes are required by Staff, PRMSC name and logo printed	Each	654	30	19620
2	Safety Helmets	EN-397 High-density polyethylene (HDPE) or ABS plastic; adjustable screw harness; Adjustable headbands, chin straps, and non-allergic sweatbands. color-coded (white for engineers, yellow for workers) PRMSC Brading and LOGO PRINTED with sr number mentioned on each helmet for ease of record keeping	Each	5668	30	170040
3	Safety Gloves	EN 388 : Nitrile-coated or leather palm; abrasion and cut-resistant; breathable back; conforms to EN388 safety ratings	Each	650	50	32500
4	Dust Mask (Dust proof mask)	ISO 16975: Disposable N95 or FFP2 class mask; elastic bands; nose clip for sealing; replace after use	Each	500	100	50000
5	Safety Shoes & Toes	EN ISO 20345, requiring a toe cap to withstand a minimum 200-joule impact and 15 kilonewtons (kN) of compression Steel toe cap; anti-slip, oil-resistant sole; leather upper; ankle support for shoes only	Each	8175	35	286125
6	Safety Harness Belt	ISO 10333: High-tenacity polyester webbing, minimum width 45mm; adjustable shoulder and thigh straps with metal buckles; dorsal D-ring for fall arrest, side D-rings for positioning; and chest strap with quick-connect buckle; Renowned Brand	Each	4905	3	14715

Sr. No.	Item Description	ISO / Standard Code / Description	Unit	Unit Rate (Rs)	Quantity (Per Village)	Amount (Rs)
7	Protective Goggles	ISO 16321: Anti-fog, scratch-resistant; side shielding for wrap-around protection; adjustable strap	Each	545	10	5450
8	Ear Plugs	ISO 4869-1: Soft polyurethane foam; noise reduction rating (NRR) of 30 dB or more	Each	175	20	3500

8.3 Break Up of Health Safety & Environment

Budget estimate for HSE composed of cost of medical screening of communicable diseases of the labors, cost of tarpaulins to cover the construction material while transporting or storage, cost of handling and disposal of hazardous materials and solid waste, provision of fire alarms and fire extinguishers for fire fighting in case of fire emergency. A special provision for the COVID-19 measure is also part of HSE budget estimate, which will not be utilized if corona situation aggravates and government announce special measures are required to be taken to contain spread of virus. Breakup of the estimate of the HSE cost for village is provided in table 27.

Table 28:Break Up of Personal Protective Equipment

Health Safety Environment Materials / Testing			Unit	Unit Rate (Rs)	Quantity (Per Village)	Amount (Rs)
9	First Aid Kit	ISO 7010-E003: Painkiller, eyewash solution, antibiotic ointment, thermometer, plasters, sterile gauze, dressings, sterile eye dressings, triangular bandages, crepe rolled bandages, safety pins, disposable sterile gloves and tweezers), pain killers, burn creams, pyodine solution (big bottle), other medication as required by tehsil team is adequate size and quantity	Each	27250	1	27250
10	Warning / Safety Signs	ISO 7010: Weatherproof PVC or Plastic or aluminum signs; reflective print; standardized colors and pictograms (danger, caution, mandatory)	Each	500	25	12500

Health Safety Environment Materials / Testing			Unit	Unit Rate (Rs)	Quantity (Per Village)	Amount (Rs)
11	Green Mesh	Green safety netting for site periphery; 50% shading; UV-stabilized HDPE material.	S.ft	40	200	8000
12	DCP Fire Extinguisher (Dry Chemical Powder)	ISO 7165: 6-kg; ABC type; The extinguishing agent is mono ammonium phosphate and ammonium sulphate powder and the discharge time of the agent is 13 second	No.	11990	1	11990
13	CO_2 Fire Extinguisher	ISO 7165: 5 kg; frost-free horn; suitable for electrical and liquid fires; discharge time of the agent in 13 second)	No.	14170	1	14170
14	Fire Alarm	ICS 13.030.10: Proper segregation, PPE for handlers, timely removal, recordkeeping per solid waste rules	No.	10900	2	21800
15	Trapuline	Waterproof tarpaulin sheet made from polyethylene or canva	Sq.ft	600	30	18000
16	Safety Cones	UV-resistant PVC or rubber material; at least 28 to 36 inches in height; high-visibility orange color with reflective collars (minimum 4-inch reflective band) for day and night visibility		3270	12	39240
17	Tree Plantation	5-6 feet height; Native species plantation; soil preparation and watering included	No.	545	100	54500
18	Barricading / Fencing (Reflective tape, poles, safety mesh/netting)	ISO 13857: Includes poles, reflective tape, plastic mesh netting; minimum 3 feet height; durable and visible	Rft	20	300	6000

Health Safety Environment Materials / Testing			Unit	Unit Rate (Rs)	Quantity (Per Village)	Amount (Rs)
19	Trainings	HSE Training, Rescue Training, Labour Code of Conduct, Environmental Code of Conduct, Defensive Driver Trainings, Labour Laws and Labour Rights, GAP Training, C-ESMP Training and anyother as required by E&S wing	Quaterly	27250	4	109000
20	Water Sprinkling	Water sprinkling through tank mounted on tractor	Per Trip	1500	30	45000
21	Medical Screening for Workers	CBC, Anti HCV, HBsAG, HIV, RPR, LFTs, RFTs etc.	Persons	1635	30	49050

8.4 Environmental Monitoring Cost

Provision for the environmental monitoring is part of the cost of ESMP. Environmental Monitoring will help the client to assess the negative impacts on air and water quality of the concerned villages. Table 29 provide the cost of Environmental Monitoring in village.

Table 29: Environmental Monitoring Cost

Environmental Testing and Monitoring			Unit	Unit Rate (Rs)	Quantity (Per Village)	Amount (Rs)
22	Ambient Air Quality Monitoring	As per the parameters and methodology defined by EPA (Quarterly in every village	Each	27250	3	81750
23	Groundwater Quality Test	As per the parameters and methodology defined by EPA (Quarterly in every village	Each	21800	3	65400
24	Surface Water Quality Test	(As per the parameters and methodology defined by EPA (Quarterly in every village	Each	21800	3	65400
25	waste Water Quality Test	(As per the parameters and methodology defined by EPA (Quarterly in every village	Each	21800	3	65400

Environmental Testing and Monitoring			Unit	Unit Rate (Rs)	Quantity (Per Village)	Amount (Rs)
26	Noise Level Monitoring	(As per the parameters and methodology defined by EPA (Quarterly in every village)	Each	2725	3	8175

8.5 Training Program

The environmental and social training will help to ensure that the requirements of the ESMP are clearly understood and followed by all project personnel. The primary responsibility of providing this training to all project personnel will be that of the contractor and ESC. The training will be provided to different professional groups separately such as managers, skilled personnel, unskilled labors, and camp staff. **Table 30** provides detail of the training required for the implementation of ESMP during the construction phase.

Table 30: Training For Contractors by PRMSC and EDCS consultants

Training Activity	Participants	Type of Training	Content	Scheduling
Construction Phase (10 months)				
Environment code of practices	Contractor Staff	Presentation	Awareness & applicability of environmental code of practices	Once
Revision of Environment code of practice	Contractor Staff	Presentation	Revision on Awareness & applicability of environmental code of practices	Once
Waste Management	Contractor Staff	Lecture	Awareness associated with waste Storage, collection and safe disposal	Once
Workers Code of Conduct	Contractor Staff	Presentation & FGD	Do's and don't's of community interaction	twice
Grievance Redress Mechanism	All relevant project staff including contractor	Presentation & FGD	roles and procedures of GRM	
Awareness workshop regarding Covid 19 and	Contractor Staff	Presentation	Risk, Prevention and available treatment	Once

Training Activity	Participants	Type of Training	Content	Scheduling
other vector borne diseases				
2Community/ occupational health and safety	Contractor Staff	Lecture	Awareness on EHS Guidelines	Once
Emergency Response	Contractor Staff	Workshop	Potential natural and other hazard/emergencies and dealing with emergency to minimize damage	Once
WB OPs & PEPA Regulations	Managerial Staff of Contractor	Lecture	Awareness on World Bank OPs, PEPA rules, guidelines, regulation and standards for satisfactory compliance	Once
Resettlement Related Issues	Contractor and ESC Staff of PIMU	Lecture	Awareness on OP 4.12 (Involuntary Resettlement)	Once
Labour Code of Practise	Contractor Staff	Lecture	Awareness & applicability of Laboral code of practices	Once
Gender Aspects	Contractor Staff	Lecture	Awareness on gender inequalities/GBV OP 4.20	Once

8.6 Institutional Capacity & Strengthening

In order to ensure that the ESMP provisions are implemented efficiently and effectively, capacity building/ strengthening of the implementing parties are required. Therefore, based on the assessment of the institutional capacities of the parties involved in the implementation of the ESMP, the following broad areas of capacity building/strengthening have been identified and recommended for effective implementation of the ESMP.

Table 31 shows the positions proposed for institutional strengthening for effective implementation of environmental and social mitigation measures and a cost of PKR 120,000 is dedicated to each village and it is anticipated that each procurement package will consist of 8 to 12, villages providing sufficient financial compensation for the HSE supervision staff to be hired on contractor payroll.

Table 31: HSE Supervision

Institutional Strengthening	Position	Scheduling (Months)	Responsibility

Contractor	Environmental/ HSE Expert	10	▪ Responsible for the overall implementation of ESMF processes and procedures in the light of WB policies and Guidelines and local policies and procedures; ▪ Closely follow up the integration of safeguard assessment information and inclusion of safeguards self-screening process at the project development and design stage; ▪ Provide technical support during proposal development, project design, appraisal process, and resource mobilization plan for the sub-projects in all locations; ▪ Undertake follow-up monitoring to ensure that proposed mitigation measures are implemented according to an agreed-upon environmental and social mitigation implementation plan; ▪ Closely provide assistance and design capacity building/training program for the overall implementation of ESMF from PIMU to village level and deliver capacity building training to the field teams to close knowledge/skill gaps and minimize the likelihood of risks happening to sub-projects; ▪ Ensure that appropriate environmental and social mitigation measures are proposed and met; ▪ Undertake to follow-up monitoring to ensure that proposed mitigation measures are implemented according to an agreed-upon environmental and social mitigation and implementation plan; ▪ At the PIMU level, maintain the record of all information, documents evidence, and reports including progress reports, TPV Reports, training reports, ESMPs, Screening Checklists, etc.; ▪ Closely work with SSS and Gender Specialists at the PIMU level and provide technical assistance and advice to the Environment/ Water Quality Officers based at SDU-TO

8.7 ESMP Cost of Village

Table No. 32 provides the calculated cost of the Environmental and Social Management Plan (ESMP) The total estimated cost of ESMP is **PKR 352.773 million or 1.26million US$** for 232 villages in 08 tehsils.

Table 32: ESMP Implementation Cost - Village Wise

ESMP IMPLEMENTATION COST - Village Wise						
Sr. No.	**Item Description**	**ISO / Standard Code / Description**	**PROPOSED FOR 1800 villages**			
			Unit	**Unit Rate (Rs)**	**Quantity (Per Village)**	**Amount (Rs)**
Personal Protective Equipments						
1	Safety Jackets	EN ISO 20471: 360 degree visibility Fluorescent yellow/orange; retro-reflective strips; breathable mesh fabric; secure Velcro or zipper closure, provided in approriate sizes are required by Staff, PRMSC name and logo printed	Each	654	30	19620
2	Safety Helmets	EN-397 High-density polyethylene (HDPE) or ABS plastic; adjustable screw harness; Adjustable headbands, chin straps, and non-allergic sweatbands. color-coded (white for engineers, yellow for workers) PRMSC Brading and LOGO PRINTED with sr number mentioned on each helmet for ease of record keeping	Each	5668	30	170040
3	Safety Gloves	EN 388 : Nitrile-coated or leather palm; abrasion and cut-resistant; breathable back; conforms to EN388 safety ratings	Each	650	50	32500
4	Dust Mask (Dust proof mask)	ISO 16975: Disposable N95 or FFP2 class mask; elastic bands; nose clip for sealing; replace after use	Each	500	100	50000

ESMP IMPLEMENTATION COST - Village Wise						
Sr. No.	Item Description	ISO / Standard Code / Description	PROPOSED FOR 1800 villages			
			Unit	Unit Rate (Rs)	Quantity (Per Village)	Amount (Rs)
5	Safety Shoes & Toes	EN ISO 20345, requiring a toe cap to withstand a minimum 200-joule impact and 15 kilonewtons (kN) of compression Steel toe cap; anti-slip, oil-resistant sole; leather upper; ankle support for shoes only	Each	8175	35	286125
6	Safety Harness Belt	ISO 10333: High-tenacity polyester webbing, minimum width 45mm; adjustable shoulder and thigh straps with metal buckles; dorsal D-ring for fall arrest, side D-rings for positioning; and chest strap with quick-connect buckle; Renowned Brand	Each	4905	3	14715
7	Protective Goggles	ISO 16321: Anti-fog, scratch-resistant; side shielding for wrap-around protection; adjustable strap	Each	545	10	5450
8	Ear Plugs	ISO 4869-1: Soft polyurethane foam; noise reduction rating (NRR) of 30 dB or more	Each	175	20	3500
Health Safety Environment Materials / Testing						
9	First Aid Kit	ISO 7010-E003: Painkiller, eyewash solution, antibiotic ointment, thermometer, plasters, sterile gauze, dressings, sterile eye dressings, triangular bandages, crepe rolled bandages, safety pins, disposable sterile gloves and tweezers), pain killers, burn creams, pyodine solution (big bottle), other medication as required by tehsil team is adequate size and quantity	Each	27250	1	27250

ESMP IMPLEMENTATION COST - Village Wise						
Sr. No.	Item Description	ISO / Standard Code / Description	PROPOSED FOR 1800 villages			
			Unit	Unit Rate (Rs)	Quantity (Per Village)	Amount (Rs)
10	Warning / Safety Signs	ISO 7010: Weatherproof PVC or Plastic or aluminum signs; reflective print; standardized colors and pictograms (danger, caution, mandatory)	Each	500	25	12500
11	Green Mesh	Green safety netting for site periphery; 50% shading; UV-stabilized HDPE material.	S.ft	40	200	8000
12	DCP Fire Extinguisher (Dry Chemical Powder)	ISO 7165: 6-kg; ABC type; The extinguishing agent is mono ammonium phosphate and ammonium sulphate powder and the discharge time of the agent is 13 second	No.	11990	1	11990
13	CO_2 Fire Extinguisher	ISO 7165: 5 kg; frost-free horn; suitable for electrical and liquid fires; discharge time of the agent in 13 second)	No.	14170	1	14170
14	Fire Alarm	ICS 13.030.10: Proper segregation, PPE for handlers, timely removal, recordkeeping per solid waste rules	No.	10900	2	21800
15	Trapuline	Waterproof tarpaulin sheet made from polyethylene or canva	Sq.ft	600	30	18000
16	Safety Cones	UV-resistant PVC or rubber material; at least 28 to 36 inches in height; high-visibility orange color with reflective collars (minimum 4-inch reflective band) for day and night visibility		3270	12	39240
17	Tree Plantation	5-6 feet height; Native species plantation; soil preparation and watering included	No.	545	100	54500

ESMP IMPLEMENTATION COST - Village Wise						
Sr. No.	Item Description	ISO / Standard Code / Description	PROPOSED FOR 1800 villages			
			Unit	Unit Rate (Rs)	Quantity (Per Village)	Amount (Rs)
18	Barricading / Fencing (Reflective tape, poles, safety mesh/netting)	ISO 13857: Includes poles, reflective tape, plastic mesh netting; minimum 3 feet height; durable and visible	Rft	20	300	6000
19	Trainings	HSE Training, Rescue Training, Labour Code of Conduct, Environmental Code of Conduct, Defensive Driver Trainings, Labour Laws and Labour Rights, GAP Training, C-ESMP Training and anyother as required by E&S wing	Quaterly	27250	4	109000
20	Water Sprinkling	Water sprinkling through tank mounted on tractor	Per Trip	1500	30	45000
21	Medical Screening for Workers	CBC, Anti HCV, HBsAG, HIV, RPR, LFTs, RFTs etc.	Persons	1635	30	49050
Environmental Testing and Monitoring						
22	Ambient Air Quality Monitoring	As per the parameters and methodology defined by EPA (Quarterly in every village	Each	27250	3	81750
23	Groundwater Quality Test	As per the parameters and methodology defined by EPA (Quarterly in every village	Each	21800	3	65400
24	Surface Water Quality Test	(As per the parameters and methodology defined by EPA (Quarterly in every village	Each	21800	3	65400
25	waste Water Quality Test	(As per the parameters and methodology defined by EPA (Quarterly in every village	Each	21800	3	65400

ESMP IMPLEMENTATION COST - Village Wise						
Sr. No.	Item Description	ISO / Standard Code / Description	PROPOSED FOR 1800 villages			
			Unit	Unit Rate (Rs)	Quantity (Per Village)	Amount (Rs)
26	Noise Level Monitoring	(As per the parameters and methodology defined by EPA (Quarterly in every village)	Each	2725	3	8175
Site Specific / Contractors Environmntal and Social Management Plan						
27	CESMP Formulation	By an individual or firm as approved by PRMSC Environment Wing	per village	50000	1	50000
HSE Staff						
28	HSE Supervisor	Bachelor's degree in Environmental Sciences / Engineering , NEBOSH or IOSH certification will be preffered, with over one year of experience in Occupational Health and Safety, one HSE person for 10-15 village, hiring of HSE staff will be approved by E&S prior to contract signing	Per month per village	10000	12	120000
Waste Management and House Keeping						
29	Handling and disposal of Hazardous Material	ICS 13.030.30: Safe storage, labeling, and transportation; spill kits and secondary containment as per MSDS	3 times per village for duration of contract	11000	3	33000
30	Handling and dispodal of Solid Waste Material	ICS 13.030.10: Proper segregation, PPE for handlers, timely removal, recordkeeping per solid waste rules	3 times per village for duration	11000	3	33000

ESMP IMPLEMENTATION COST - Village Wise						
Sr. No.	Item Description	ISO / Standard Code / Description	PROPOSED FOR 1800 villages			
			Unit	Unit Rate (Rs)	Quantity (Per Village)	Amount (Rs)
			of contract			
Note : Cost of ESMP implementation is village wise, PKR 1520575 will be multiplied with the number of villages in the civil work contract package to obtain total ESMP cost						
					Total ESMP Implementation Cost per year (PKR)	1,520,575

Annexure-1

World Bank Approval for ESMP-Phase 0 (77 villages)

Ibad Ur Rehman

Dear Hussain, Asma and Aman,

Thank you for sharing the revised consolidated ESMP. We feel that our comments have been adequately addressed, and there are no further comments from our side for the moment.

Nevertheless, as always, we all remain flexible and ready to incorporate any lessons learnt during implementation.

Best regards

Ibad - on behalf of WB E&S team

Official Use Only

Annexure-2
List of 2000 Villages

https://docs.google.com/spreadsheets/d/1J5kpPYwaqyjQ0sKS3lG6tNne33gA6Fvl/edit?usp=drive_link&ouid=117039326792292994503&rtpof=true&sd=true

Annexure- 3
Glimpse of Villages

Village Chak No.174-7R.Tehsil Liaqatpur	Village Chak No. 134-NP.Tehsil Liaqatpur
Village Chak No.84.Tehsil Liaqatpur	Village Chak No. 9.Tehsil Liaqatpur
Village Chak No. 15 Abbasia.Tehsil Liaqatpur	Village Chak No. 16 Abbasia.Tehsil Liaqatpur

Village Chak-No. 06 Channa.Tehsil Liaqatpur	Village Chak-138.Tehsil Liaqatpur
Village Rakh Kotla Hassan Shah.Tehsil Rojhan	**Village Rakh Qadra.Tehsil Rojhan**
Chak Dilbar, Tehsil Rojhan	**Kot Hassan Shan, Tehsil Rojhan**

Mutafraq Mazari, Tehsil Rojhan	**Safdarabad, Tehsil Rojhan**
Salimabad, Tehsil Rojhan	**Tariqabad, Tehsil Rojhan**
Chak No.102/D Tehsil Pakpattan	**Gobind Pur Bahmni Tehsil Pakpattan**

Dada Ahluka Tehsil Pakpattan	**Arazi Tek Chand Tehsil Pakpattan**
Paran Wala Tehsil Bahawal Nagar	Dhanraj Pura Tehsil Bahawal Nagar
Jagga Sanatteka Tehsil Bahawal Nagar	Pir Sikandar Otar Tehsil Bahawal Nagar

Gauspur Tehsil Bahawal Nagar	Hussain Abad Uttar Tehsil Bahawal Nagar
Tehsil Noorpur Thal	**Tehsil Noorpur Thal**
Tehsil Noorpur Thal	**Tehsil Noorpur Thal**

Tehsil Noorpur Thal	**Tehsil Noorpur Thal**
Marian, Tehsil Alipur	**Kotla Afghan, Tehsil Alipur**
Kohar Faqiran, Tehsil Alipur	**Kotla Ghulam Shah, Tehsil Alipur**

Kotla Marrani, Tehsil Alipur	**Gagare Wali, Tehsil Alipur**
Tibba Barrah, Tehsil Alipur	**Nasir Pur, Tehsil Shujabad**
Mohan Pur Sharqi, Tehsil Shujabad	**Shahpur Ubha, Tehsil Shujabad**

Wahi Riki, Tehsil Shujabad	**Basti Dad, Tehsil Shujabad**
Sangrai, Tehsil Shujabad	**Chah Miran Khan, Tehsil Shujabad**
Sarai, Tehsil Shujabad	**Shah Pur Shumali, Tehsil Shujabad**

Aqupur, Tehsil Taunsa	**Baghon Wala, Tehsil Taunsa**
Bodo Mian, Tehsil Taunsa	**Langah, Tehsil Taunsa**
Malana, Tehsil Taunsa	**Jhok Chhapri, Tehsil Taunsa**

Annexure-4
Area of Influence

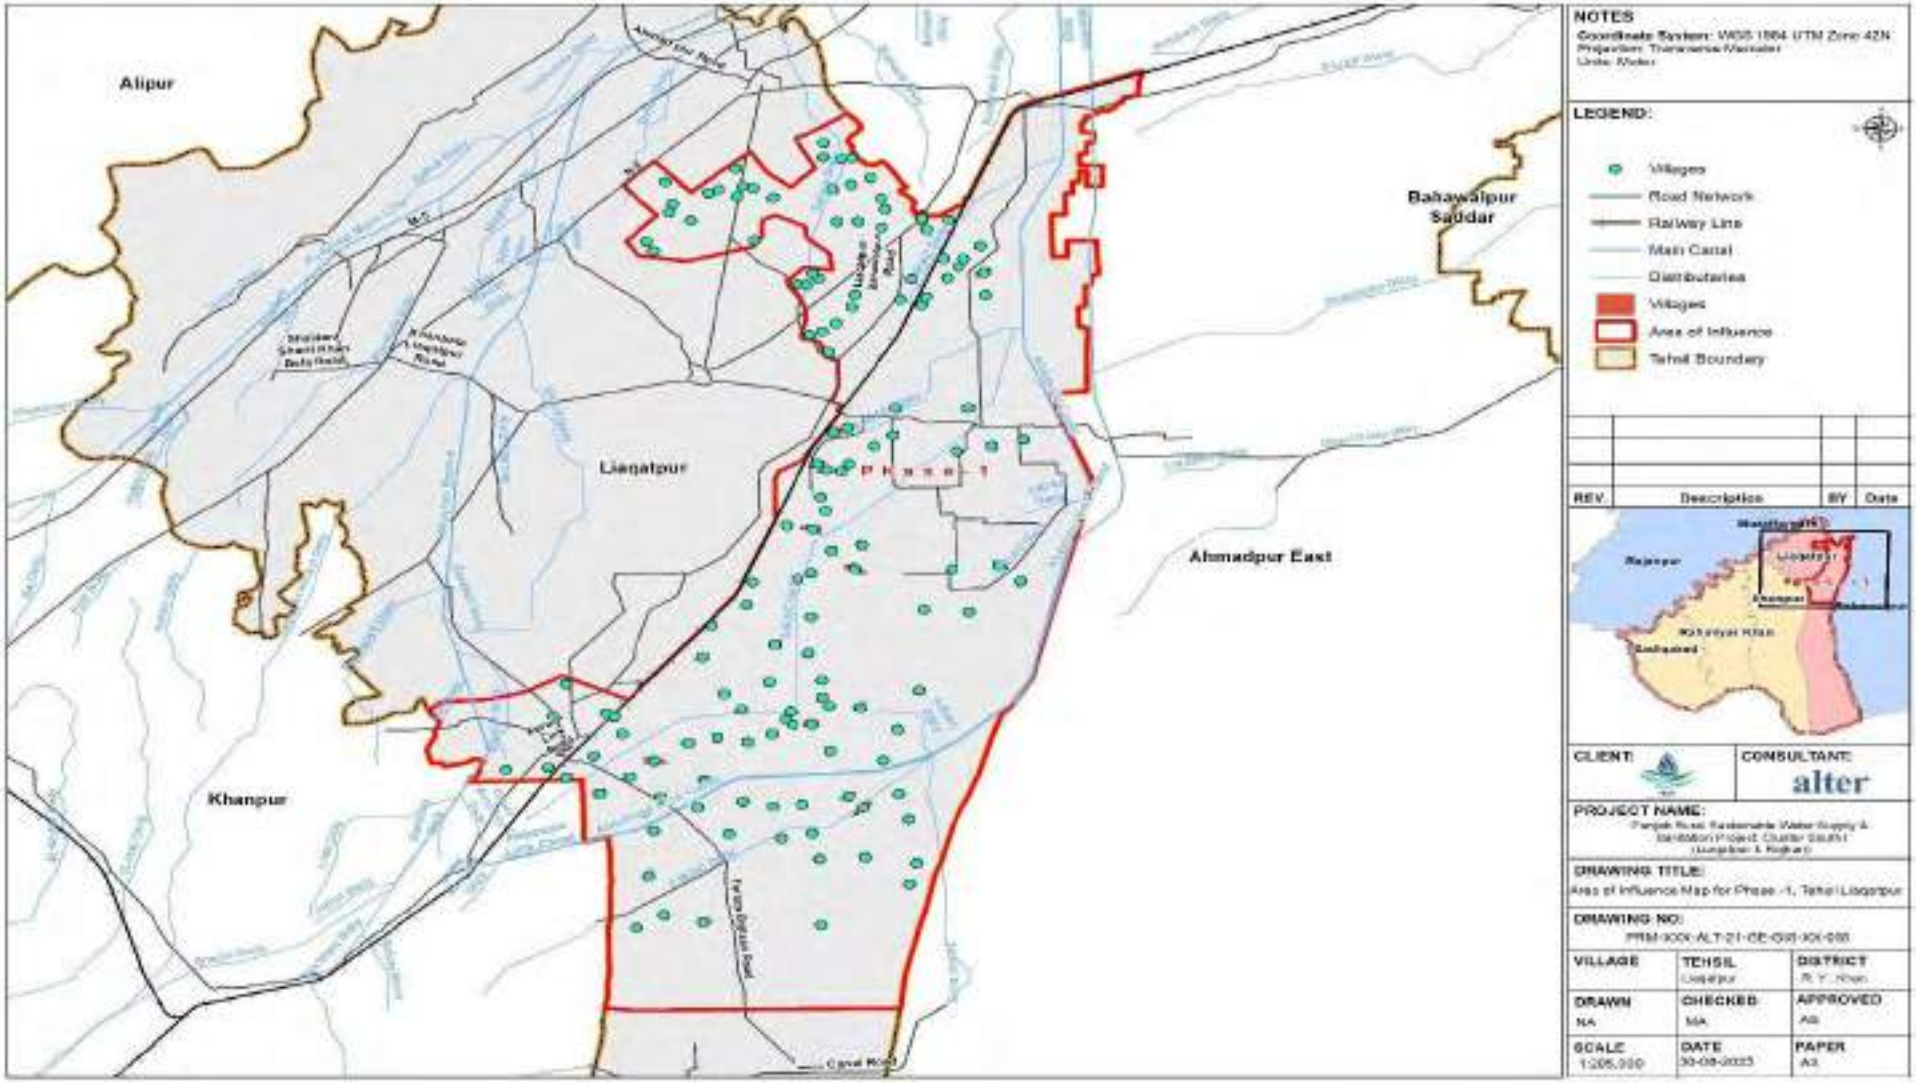
Alipur
Bahawalpur Saddar
Liaqatpur
Ahmadpur East
Khanpur
NOTES
LEGEND:
Villages
Road Network
Railway Line
Main Canal
Distributaries
Villages
Area of Influence
Tehsil Boundary
REV.
Description
BY
Date
CLIENT:
CONSULTANT:
alter
PROJECT NAME:
DRAWING TITLE:
Area of Influence Map for Phase -I, Tehsil Liaqatpur
DRAWING NO:
VILLAGE
TEHSIL
DISTRICT
DRAWN
CHECKED
APPROVED
SCALE
DATE
PAPER

Area of Influence Map for Tehsil Liaqatpur

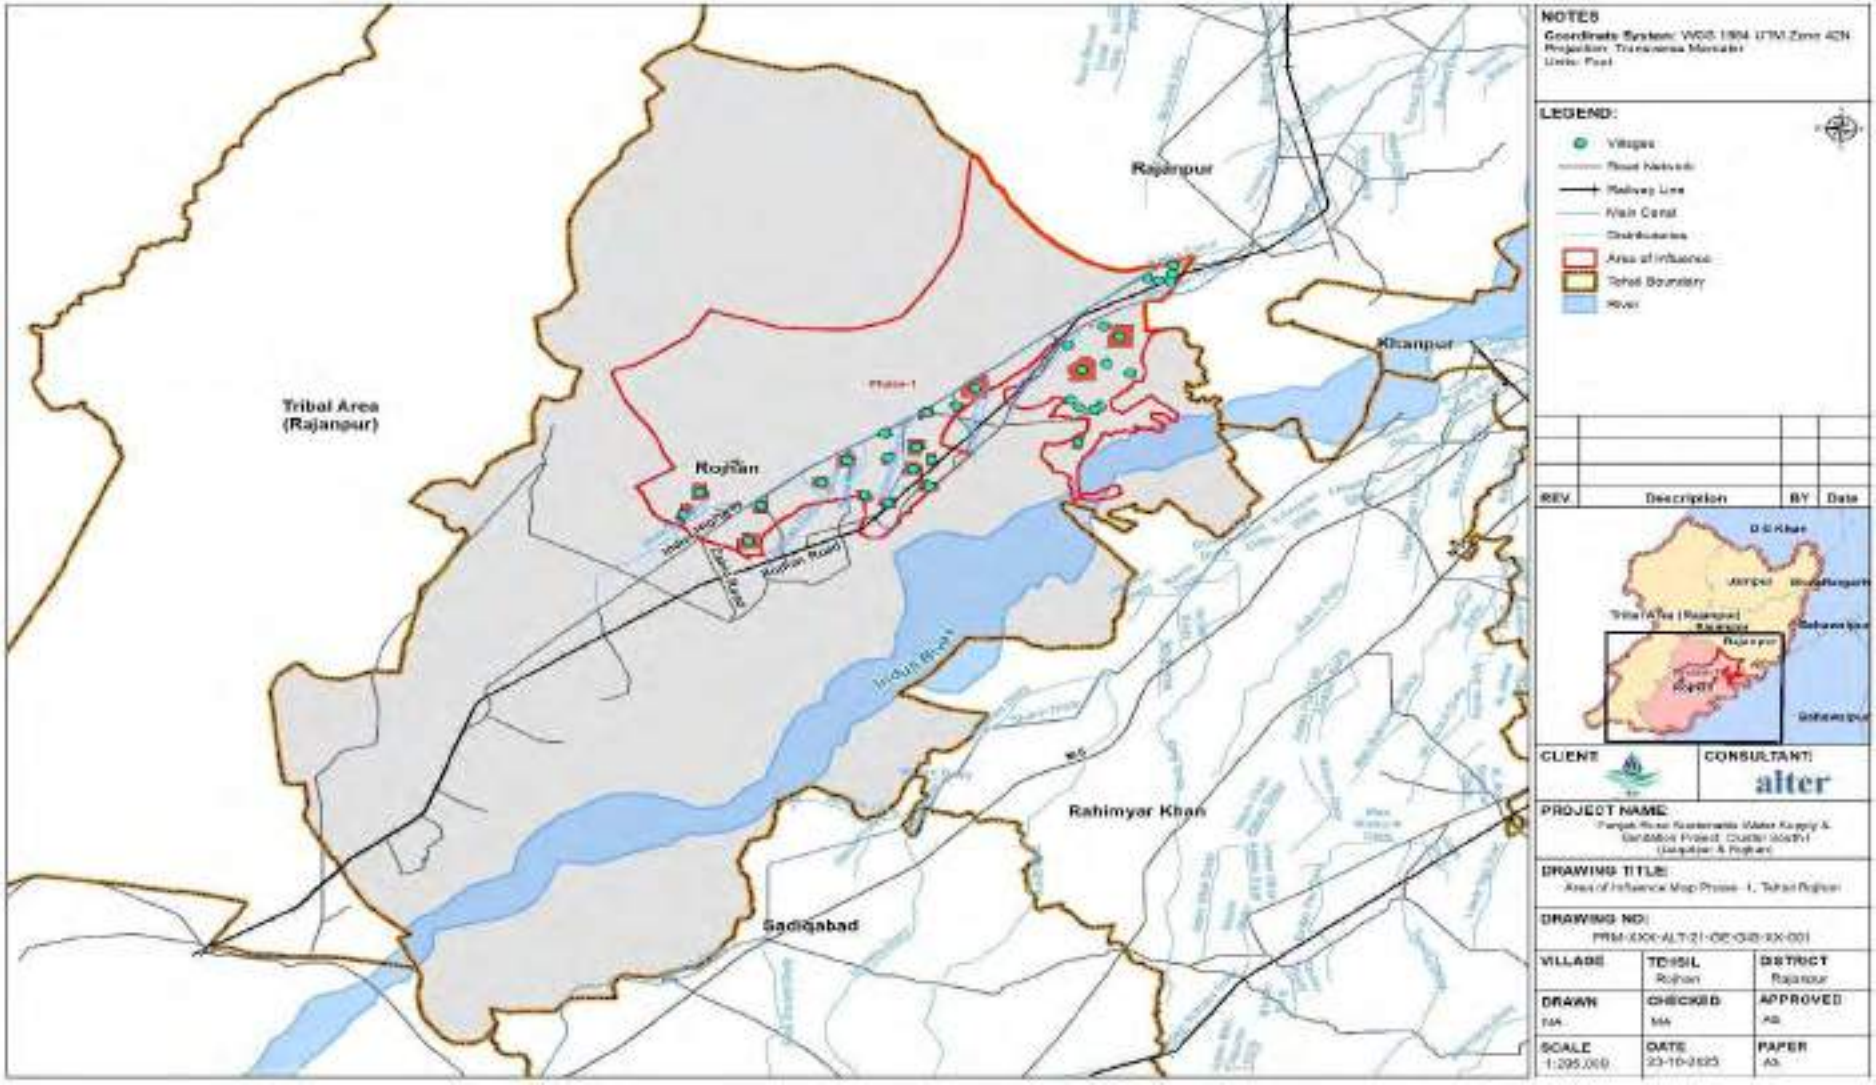
Rajanpur
Khanpur
Tribal Area
(Rajanpur)
Rojhan
Rahimyar Khan
Sadiqabad
NOTES
LEGEND:
Villages
Road Network
Railway Line
Main Canal
Distributaries
Area of Influence
Tehsil Boundary
River
REV
Description
BY
Date
CLIENT
CONSULTANT
alter
PROJECT NAME:
DRAWING TITLE:
DRAWING NO:
VILLAGE
TEHSIL
Rojhan
DISTRICT
Rajanpur
DRAWN
CHECKED
APPROVED
SCALE
DATE
PAPER

Area of Influence Map for Tehsil Rojhan

Annexure-5

Chance Find Procedures

CHANCE FIND PROCEDURES

Project may involve deep excavation. Therefore, the possibility of chance find is not ignorable. In case of any chance find, the contractor will immediately report through Supervision Consultant to Directorate General (DG) of Antiquities & Archaeology, Government of Punjab to take further suitable action to preserve those antique or sensitive remains. Representative of the “Director Archaeology and Museum (DAM)” will visit the site and observed the significance of the antique, artifact and Cultural (religious) properties and significance of the project. The documentation will be completed and if required suitable action will be taken to preserve those antiques and sensitive remains.

In case any artifact, antiques and sensitive remains are discovered, chance find procedures should be adopted by contractor workers as follows:

- Stop the construction activities in the areas of chance find;
- Delineate the discovered site or area;
- Consult with the local community and provincial Archeological Department
- The suggestion of the local communities and the concerned authorities will be suitably incorporated during taking the preventive measures to conserve the antique, artifact and cultural (religious) properties
- Secure the site to prevent any damage or loss of removable objects. In case of removable antiquities or sensitive remain, a night guard shall be arranged until the responsible local authorities take over;
- After stopping work, the contractor must immediately report the discovery to the Supervision Engineer.

The contact Address of Directorate General of Antiquities & Archaeology is given below:

1st Floor Aiwan-e-Auqaf Building Near

Lahore High Court, Lahore, Pakistan

Tel: 042-99210870

Annexure-6
PEQS and other relevant standards

EXTRA ORDINARY ISSUE

REGISTERED No. L-7532

The Punjab Gazette

PUBLISHED BY AUTHORITY

LAHORE MONDAY AUGUST 15, 2016

GOVERNMENT OF THE PUNJAB
LAW AND PARLIAMENTARY AFFAIRS DEPARTMENT

NOTIFICATION
(121 of 2016)

12th August 2016

The following Notification No. SO(G)/EPD/7-26/2013, dated 05.08.2016 regarding the Punjab Environmental Quality Standards for Noise is published for general information:

DR SYED ABUL HASSAN NAJMEE
Secretary
Government of the Punjab
Law and Parliamentary Affairs
Department

Government of the Punjab
Environment Protection Department

NOTIFICATION: No. SO(G)/EPD/7-26/2013. In exercise of the powers conferred under clause (c) of sub-section (1) of section 4 of the Punjab Environmental Protection Act, 1997 (XXXIV of 1997), the Environmental Protection Council has approved the following as the Punjab Environmental Quality Standards for Noise:

Punjab Environment Quality Standards for Noise

No.	Category of Area/Zone	Effective from 1st July, 2010		Effective from 1st July, 2013	
		Limits in dB(A) Leq*			
		Day Time	Night Time	Day Time	Night Time
1	Residential Area (A)	65	50	55	45
2	Commercial Area (B)	70	60	65	55
3	Industrial Area (C)	80	75	75	65
4	Silence Zone (D)	55	45	50	45

Note:

1. Day time hours; 6:00am to 10:00pm.
2. Night Time hours; 10:00 pm to 6:00 am.
3. Silence Zone: Zones which are declared as such by the competent authority. An area comprising not less than 100 meters around hospital, educational institutions and courts
4. Mixed categories of areas may be declared as one of the four above mentioned categories by the competent authority

* dB(A) Leq: Time weighted average of the level of sound in decibel on scale A which is relatable to human hearing.

(IQBAL MOHAMMED CHAUHAN)
Secretary, Government of the Punjab
Environment Protection Department

EXTRA ORDINARY ISSUE

REGISTERED No. L-7532

The Punjab Gazette

PUBLISHED BY AUTHORITY

LAHORE MONDAY AUGUST 15, 2016

GOVERNMENT OF THE PUNJAB
LAW AND PARLIAMENTARY AFFAIRS DEPARTMENT

NOTIFICATION
(122 of 2016)

12th August 2016.

The following Notification No. SO(G)/EPD/7-26/2013, dated 05.08.2016 regarding the Punjab Environmental Quality Standards for Ambient Air is published for general information:

DR SYED ABUL HASSAN NAJMEE
Secretary
Government of the Punjab
Law and Parliamentary Affairs
Department

Government of the Punjab
Environment Protection Department

NOTIFICATION: No. SO(G)/EPD/7-26/**2013.** – In exercise of the powers conferred under clause (c) of sub-section (1) of section 4 of the Punjab Environmental Protection Act, 1997 (XXXIV of 1997), Environmental Protection Council has approved the following as the Punjab Environmental Quality Standards for Ambient Air:

Punjab Environmental Quality Standards for Ambient Air

Pollutant	Time-weighted average	Concentration in Ambient Air	Method of measurement
Sulfur Dioxide (SO_2)	Annual Average*	80 µg/m^3	Ultraviolet Fluorescence method
	24 hours**	120 µg/m^3	
Oxides of Nitrogen as (NO)	Annual Average*	40 µg/m^3	Gas Phase Chemiluminescence
	24 hours**	40 µg/m^3	
Oxides of Nitrogen as (NO_2)	Annual Average*	40 µg/m^3	Gas Phase Chemiluminescence
	24 hours**	80 µg/m^3	
Ozone (O_3)	1 hour	130µg/m^3	Non dispersive UV absorption method
Suspended Particulate Matter (SPM)	Annual Average*	360µg/m^3	High Volume Sampling, (Average flow rate not less than 1.1 m^3/min).
	24 hours**	500µg/m^3	
Respirable Particulate Matter PM_{10}	Annual Average*	120µg/m^3	Preferably β-Ray absorption method
	24 hours**	150µg/m^3	
Respirable Particulate Matter $PM_{2.5}$	Annual Average*	15µg/m^3	Preferably β-Ray absorption method
	24 hours**	35µg/m^3	

Pollutant	Time-weighted average	Concentration in Ambient Air	Method of measurement
	1 hour	15µg/m^3	
Lead (Pb)	Annual Average*	1 µg/m^3	ASS Method after sampling using EPM 2000 or equivalent Filter paper
	24 hours**	1.5µg/m^3	
Carbon Monoxide (CO)	8 hours**	5 mg/m^3	Non Dispersive Infra Red (NDIR) method
	1 hour	10 mg/m^3	

* Annual arithmetic mean of minimum 104 measurements in a year taken twice a week 24 hourly at uniform interval.

** 24 hourly /8 hourly values should be met 98% of the in a year. 2% of the time, it may exceed but not on two consecutive days.

(IQBAL MOHAMMED CHAUHAN)
Secretary, Government of the Punjab
Environment Protection Department

EXTRA ORDINARY ISSUE

REGISTERED No. L-7532

The Punjab Gazette

PUBLISHED BY AUTHORITY

LAHORE MONDAY AUGUST 15, 2016

GOVERNMENT OF THE PUNJAB
LAW AND PARLIAMENTARY AFFAIRS DEPARTMENT

NOTIFICATION
(123 of 2016)

12th August 2016

The following Notification No. SO(G)/EPD/7-26/2013, dated 05.08.2016 regarding the Punjab Environmental Quality Standards for motor vehicle exhaust and noise is published for general information:

DR SYED ABUL HASSAN NAJMEE
Secretary
Government of the Punjab
Law and Parliamentary Affairs
Department

Government of the Punjab
Environment Protection Department

NOTIFICATION: No. SO(G)/EPD/7-26/2013. – In exercise of the powers conferred under clause (c) of sub-section (1) of section 4 of the Punjab Environmental Protection Act, 1997 (XXXIV of 1997), the Environmental Protection Council has approved the following as the Punjab Environmental Quality Standards for motor vehicle exhaust and noise:

Punjab Environmental Quality Standards for Motor Vehicle Exhaust and Noise

(i) For In-use Vehicles

No	Parameter	Standards (maximum permissible limit)	Measuring methods	Applicability
1	2	3	4	5
1	Smoke	40% or 2 on the Ringlemann Scale during engine acceleration mode	To be compared with Ringlemann Chart at a distance of 6 meters or more	Immediate effect
2	Carbon Monoxide	6%	Under idling conditions: Non dispersive infrared detection through gas analyzer	
3	Noise	85 dB(A)	Sound-meter at 7.5 meter from the source	

(ii) For New Vehicles

EMISSION STANDARDS FOR DIESEL VEHICLES

(a) For Passenger Cars and Light Commercial Vehicles (g/km)

Type of Vehicle	Category/Class	Tiers	CO	HC+ NOx	PM	Measuring method	Applicability
1	2	3	4	5	6	7	8

Passenger Cars	M1: with reference mass (RW) upto 2500 kg	Pak-II IDI	1.0	0.7	0.08		All imported and locally manufactured diesel vehicles with effect from 01-07-2012
	Cars with RW over 2500 kg to meet NI category standards	Pak-II, DI	1.0	0.9	0.10	NEDC (ECE 15+EUDCL)	
Light Commercial Vehicles	NI-I(RW<1250kg)	Pak-II, IDI	1.0	0.70	0.08		
		Pak-II, DI	1.0	0.90	0.10		
	NI-II(1250kg< RW<1700kg)	Pak-II, IDI	1.25	1.0	0.12		
		Pak-II, DI	1.25	1.3	0.14		
	NI-III(RW>1700kg)	Pak-II, IDI	1.50	1.2	0.17		
		Pak-II, DI	1.50	1.6	0.20		

Parameters Standards (maximum permissible limit)	Measuring method
85 dB(A)	Sound-meter at 7.5 meters from the source

(b) For Heavy Duty Diesel Engine and Large Goods Vehicles (g/KWh)

Type of Vehicle	Category/ Class	Tiers	CO	HC	NOx	PM	Measuring method	Applicability
1	2	3	4	5	6	7	8	9
Heavy Duty Diesel Engine	Trucks & Buses	Pak-II	4.0	1.1	7.0	0.15	ECE-R-49	All imported and locally manufactured diesel vehicles with effect from 01-07-2012
Large Goods Vehicl	N2(2000 and up)	Pak-II	4.0	7.0	1.1	0.15	EDC	

es								
Parameters	**Standards (maximum permissible limit)**							**Measuring methods**
Noise	85 dB(A)							Sound-meter at 7.5 meters from the source

EMISSION STANDARDS FOR PETROL VEHICLES (g/km)

Type of Vehicle	**Category/Class**	**Tiers**	**CO**	**HC+ NOx**	**Measuring method**	**Applicability**
1	**2**	**3**	**4**	**5**	**6**	**7**
Passenger Cars	M1: with reference mass (RW) upto 2500kg. Cars with RW over 2500kg to meet NI category standards	Pak-II	2.20	0.5	NEDC(ECE15+EUDCL)	All imported and new models * locally manufactured petrol vehicles with effect from 01-07-2009**
Light Commercial Vehicles	N1-I(RW<1250kg)	Pak-II	2.20	0.5		
	N1-II(1250kg> RW<1700kg)	Pak-II	4.0	0.65		
	N1-III(RW>1700kg)	Pak-II	5.0	0.08		
Motor Rickshaws & Motor Cycles	2.4 strokes<150cc	Pak-II	5.5	1.5	ECER 40	
	2.4 strokes>150cc	Pak-II	5.5	1.3		

Parameters	Standards (maximum permissible limit)	Measuring method
Noise	85 dB(A)	Sound-meter at 7.5 meters from the source

Explanations:

DI: Direct Injection
IDI: Indirect Injection
EUDCI :- Extra Urban Driving Cycle
NEDC: New European Driving Cycle
ECE: Urban Driving Cycle
M: Vehicles designed and constructed for the carriage of passengers and comprising no more than eight seats in addition to the driver's seat.
N: Motor vehicles with at least four wheels designed and constructed for the carriage of goods
* Now Model means both model and design type change
** The existing Model of petrol driven vehicles locally manufactured with immediately switched over to Pak-II emission standards but not later than 30th June 2012

(IQBAL MOHAMMED CHAUHAN)
Secretary, Government of the Punjab
Environment Protection Department

EXTRA ORDINARY ISSUE

REGISTERED No. L-7532

The Punjab Gazette

PUBLISHED BY AUTHORITY

LAHORE MONDAY AUGUST 15, 2016

GOVERNMENT OF THE PUNJAB
LAW AND PARLIAMENTARY AFFAIRS DEPARTMENT

NOTIFICATION
(124 of 2016)

12th August 2016

The following Notification No. SO(G)/EPD/7-26/2013, dated 05.08.2016 regarding the Punjab Environmental Quality Standards for Drinking Water is published for general information:

DR SYED ABUL HASSAN NAJMEE
Secretary
Government of the Punjab
Law and Parliamentary Affairs
Department

Government of the Punjab
Environment Protection Department

NOTIFICATION: No. SO(G)/EPD/7-26/2013. – In exercise of the powers conferred under clause (c) of sub-section (1) of section 4 of the Punjab Environmental Protection Act, 1997 (XXXIV of 1997), the Environmental Protection Council has approved the following as the Punjab Environmental Quality Standards for Drinking Water:

Punjab Environmental Quality Standards for Drinking Water

Properties/Parameters	Standard Values	WHO Standards	Remarks
[redacted]			
All water intended for drinking (E. Coli or Thermo-tolerant Coliform bacteria)	Must not be detectable in any 100 ml sample	Must not be detectable in any 100 ml sample	Most Asian countries also follow WHO standards
Treated water entering the distribution system (E. Coli or thermo tolerant coliform and total coliform bacteria)	Must not be detectable in any 100 ml sample	Must not be detectable in any 100 ml sample	Most Asian countries also follow WHO standards
Treated water in the distribution system (E. Coli or thermo tolerant coliform and total coliform bacteria)	Must not be detectable in any 100 ml sample In case of large supplies, where sufficient samples are examined, must not be present in 95% of the samples taken throughout any 12- month period.	Must not be detectable in any 100 ml sample In case of large supplies, where sufficient samples are examined, must not be present in 95% of the samples taken throughout any 12- month period.	Most Asian countries also follow WHO standards
[redacted]			
Colour	≤15 TCU	≤15 TCU	
Taste	Non objectionable/ Acceptable	Non objectionable/ Acceptable	
Odour	Non objectionable/ Acceptable	Non objectionable/ Acceptable	
Turbidity	<5 NTU	<5 NTU	

Properties/Parameters	Standard Values	WHO Standards	Remarks
Total hardness as $CaCO_3$	< 500 mg/l	---	
TDS	<1000	< 1000	
pH	6.5 – 8.5	6.5 – 8.5	
[redacted]			
Essential Inorganic	mg/Litre	mg/Litre	
Aluminum (Al) mg/l	≤0.2	0.2	
Antimony (Sb)	≤0.005 (P)	0.02	
Arsenic (As)	≤0.05 (P)	0.01	Standard for Pakistan similar to most Asian developing countries
Barium (Ba)	0.7	0.7	
Boron (B)	0.3	0.3	
Cadmium (Cd)	0.01	0.003	Standard for Pakistan similar to most Asian developing countries
Chloride (Cl^-)	<250	250	
Chromium (Cr)	≤0.05	0.05	
Copper (Cu)	2	2	
Toxic Inorganic	mg/l	mg/l	
Cyanide (CN)	≤0.05	0.07	Standard for Pakistan similar to Asian developing countries
Fluoride (F)*	≤1.5	1.5	
Lead (Pb)	≤0.05	0.01	Standard for Pakistan similar to most Asian developing countries
Manganese (Mn)	≤ 0.5	0.5	
Mercury (Hg)	≤0.001	0.001	
Nickel (Ni)	≤0.02	0.02	
Nitrate (NO_3)*	≤50	50	
Nitrite (NO_2)*	≤3 (P)	3	
Selenium (Se)	0.01(P)	0.01	

Properties/Parameters	Standard Values	WHO Standards	Remarks
Residual chlorine	0.2-0.5 at consumer end 0.5-1.5 at source		
Zinc (Zn)	5.0	3	Standard for Pakistan similar to most Asian developing countries
Organic			
Pesticides mg/l			PSQCA No. 4639- 2004, Page No. 4 Table No. 3 Serial No. 20-58 may be consulted.**
Phenolic compounds (as Phenols) mg/l		[redacted]	
Poly-nuclear aromatic hydrocarbons (as PAHs) g/l		0.01 (By GC/MS method)	
[redacted]			
Alpha Emitters bq/L or pCi	0.1	0.1	
Beta emitters	1	1	

* Indicates priority health related inorganic constituents, which need regular monitoring.

** PSQCA: Pakistan Standards Quality Control Authority.

(IQBAL MOHAMMED CHAUHAN)
Secretary, Government of the Punjab
Environment Protection Department

Annexure-7
E & S Checklist

E & S Screening Checklist

Environmental and Social screening checklist of 42 proposed villages can be accessed through the following link

https://drive.google.com/drive/folders/1py1nOcQytPu9GyDXyWgvpn8DFgNUqBoo?usp=sharing

Annexure-8
Consultation Meetings

Consultation Meetings Tehsil-Wise

Sr. No	Tehsil	Community Consultation Meeting	Number of Participants
1	Noorpur thal	58	593
2	Liaqatpur	140	2100
3	Rojhan	24	360
4	Shujabad	10	157
5	Taunsa	34	299
6	Alipur	21	263
7	Bhawalnagar	32	320
8	Pakpattan	30	300

Annexure-9
VLD Procedure

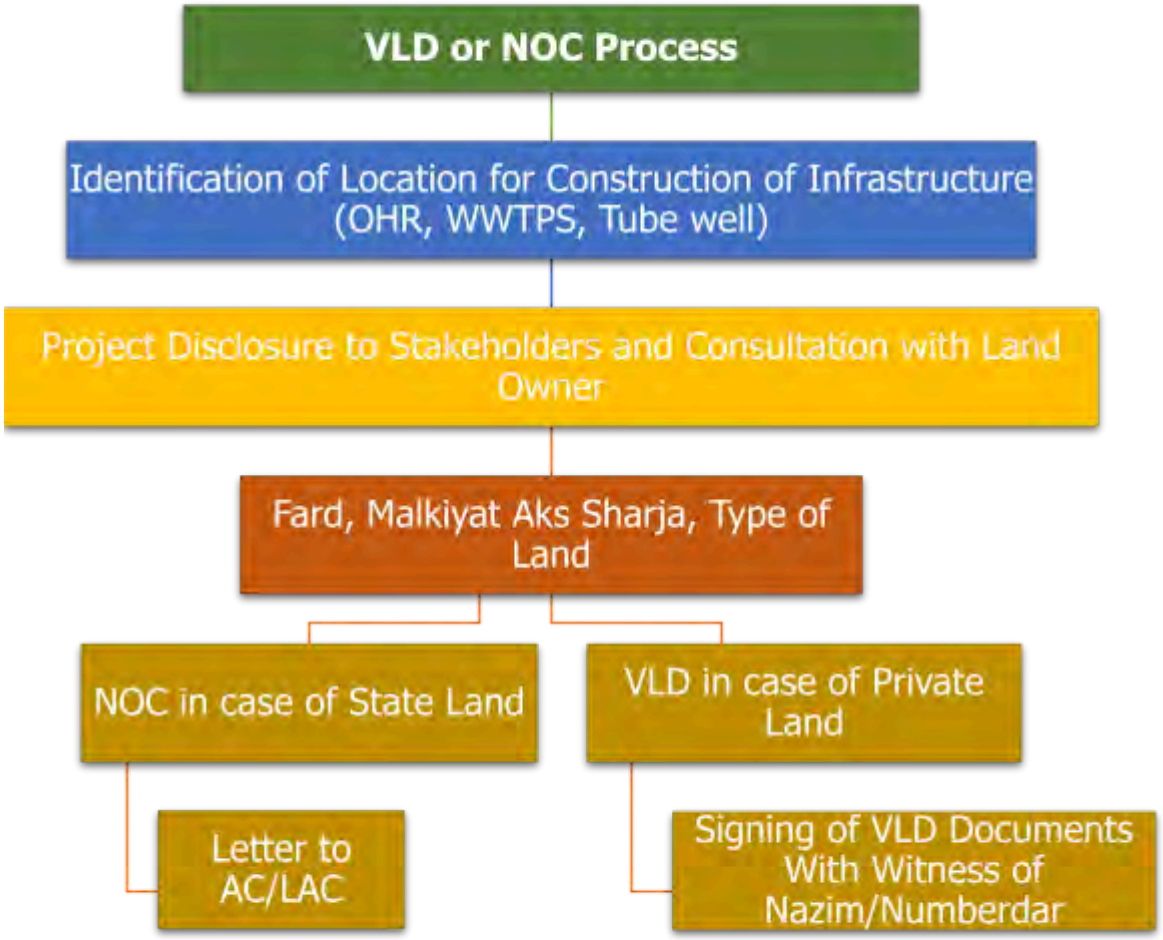

Specific conditions for the VLD procedure are provided in ESMF.

Annexure-9A
VLD Screening Checklist

Checklist of Voluntary Land Donation (VLD) Process			
Sr. No.	**Description**	**Checklist Yes=Y; No=N**	**Remarks**
A	**Requirement for Voluntary Land Donation**		
1.	The Purpose for Land Use of the Project		Land use plan (Purpose for which land is being taken)
2.	Area of land to be donated		Land donation plan
3.	Terms of land donation		Land donation agreement
4.	Parties intending to donate land		List of donor parties in the village
5.	Any details that are relevant to why donation may be appropriate		Record of reasons for land donation appropriateness
B	**Determine the appropriateness of VLD**		
6.	Has the viability of all other alternative locations/ sites been considered?		Must be Yes
7.	Is Govt. land available?		No, In case Yes, the following must be checked
8.	Verify land is free of squatters, encroachers, or other claims or encumbrances		Must be Yes
9.	Reasons for obtaining land through VLD in spite of the availability of govt. land?		Justifications/ Reasons for VLD
10.	Has the cost-benefit analysis been conducted for choosing VLD instead of Govt. land?		Cost
11.	Does the cost meet the minimum threshold required for opting for VLD instead of Govt. land?		Must be yes
12.	Ensure the landowner is not vulnerable*		Must be Yes
13.	VLD must not negatively impact households below the provincial poverty line.		Must be negligible

Checklist of Voluntary Land Donation (VLD) Process			
Sr. No.	**Description**	**Checklist Yes=Y; No=N**	**Remarks**
14.	Is the land obtained through VLD owned by a woman who is the family's sole earner?		VLD is not to be taken from the women-headed family.
15.	Does the VLD involve impacts on minority/ handicapped persons?		Must be negligible.
16.	If yes, what are the impacts on livelihood due to VLD in terms of percentage?		The percentage of impact on the livelihood must not exceed 5%.
C	**VLD Process Requirements**		
17.	The Titleholder should be holding more than the minimum prescribed land;		Minimum 2 kanals.
18.	Verify voluntary donation is not more than 10% of the area of the titleholder's holding		Must be Yes
19.	Verify impacts are minor and not requiring physical relocation of the titleholder		Must be Yes
20.	Verify land must be jointly identified by the Revenue Department/ VO or project authorities.		Must be Yes
21.	Do the project technical authorities have authorization that the land is appropriate for sub-project purposes?		Must be Yes
22.	Ensure land is appropriate for sub-project purposes and will not invite adverse social, health, environment, or safety impacts**		Must be Yes
23.	Verification of the voluntary nature of land donations must be obtained from each of the persons donating land.		Must be Yes
24.	Do the land donors/ tenants have access to and benefit from this sub-project?		If no, then describe the reasons.
D	**Verify requirements of donation and formalization of donation in the village assembly**		
25.	Verify donation is voluntary and obtain notarized, witness statements in a village assembly		Must be Yes
26.	Ensure the land donor must not possess more than 25 acres of land		The requirement must be met

Checklist of Voluntary Land Donation (VLD) Process			
Sr. No.	**Description**	**Checklist Yes=Y; No=N**	**Remarks**
27.	Ensure the land donor must not be a member of a Provincial Assembly, National Assembly, and member of the Senate		The requirement must be met
28.	Ensure titleholder understands they will have equal access to infrastructure built on donated land and cannot claim priority treatment		Must be Yes
E	**Due diligence on land ownership and use**		
29.	Type of land rights in the project area		Land rights assessment
30.	Users of land or any occupying parties (Tenants or leaseholders etc.)		Users identification
31.	Competing claims of ownership or use		Claims identification
32.	Structures and assets on the land		Assets on the proposed land (loss of agriculture, livelihood, assets, loss of economic trees etc.)
33.	Encumbrances on the land		Encumbrances assessment (Legal/ financial, Loans etc.)
F	**Consultation and Disclosure in a Village Assembly**		
34.	Consult with land donors and ensure they understand the terms and conditions of the donation		Must be Yes
35.	Disclose information about the donation process		Must be Yes
36.	Disclose any potential negative impacts on the owner		Must be Yes
37.	Informed consent of person donating land		Consent Agreement
38.	Indicate the concerns raised, if any.		Document the concerns
G	**Grievance Redress Mechanism (GRM)**		
39.	Establish and communicate the grievance redress mechanism		Must be Yes and Documented
40.	Disclosure of GRM process and GRC		Must be Yes
41.	Sharing of helpline for complaints and grievances		Must be Yes
H	**Monitoring and documentation**		

Checklist of Voluntary Land Donation (VLD) Process			
Sr. No.	**Description**	**Checklist Yes=Y; No=N**	**Remarks**
42.	Verify any land conflicts or conflicting land titling		Must be mentioned and avoided
43.	Establish informed consent of person donating land		Must be Yes and Documented
44.	Inform them they will be deprived of the title as well as any other right to use the land		Must be Yes and Documented
45.	They have the right to refuse to donate the land		Must be Yes and Documented
46.	Information about any other costs involved in the process which the owner has to pay.		Must be Yes and Documented
47.	They will be informed that neither they nor their family members will be able to get the land back after the mutation.		Must be Yes and Documented
48.	What they will need to do to donate the land;		The complete mutation process must be disclosed
49.	The intergenerational effect of the donation on their family, what they can do if they (or their family or heirs) want the land back.		Must be Yes and Documented
50.	The terms and conditions of the land donation must be mutually agreed upon and detailed in a written agreement.		Must be Yes and Documented
51.	Verify donors provide their informed consent		Must be Yes and Documented
52.	Monitor and document the donation process in monitoring reports		Must be Yes and Documented

Footnote:

* Vulnerable persons:
Households (with valid proof), as per provincial poverty line for rural areas;
Households without proof of the same and belonging to the following social categories:
Women headed households with women as sole earners;
Minority/ handicapped persons.
** adverse social, health, environmental, and safety impacts including but not limited to the potential social conflicts, community health, dust or air quality, occupational and community health, and safety respectively.

Annexure-9B
VLD Tracking Matrix

VLD Tracking Sheet of Tehsil Bhowana Phase-II																							
S.No	District	Tehsil	Village/ Mouza	Proposed Submitter Detail	Consultant Name	Total Land Required (Marlas)	Pvt Land requirement (Marlas)						Total number of private land donors (detail of actual land size and % of landholding to be provided for each donor)						Coordination of Ownership & encumbrances – date	Documentation for Harmony Deputy (Tehsildars etc.) – date	Date of VLD documentation (Affidavits etc.)	Date of VLD case submission to WB	Date of WB NOL	Mutation date	Remarks
							Tubewell	OHR	AHR	SW	Stand Post	Total	Donor 1 (SP)			Donor 2 (TW,OHR,AHR)							
													total landholding	donated land	%	total landholding	donated land	%					
1	District	Tehsil	Mouza Tiga Bozwala (Rehmaan ka Thatta)	Stand Post	NESPAK	1					1	1	1500	1	0.06%				11-Apr-03	11-Apr-03	25-May-03	30-Jun-03			
2	District	Tehsil	Mouza Tiga Bozwala (Dispensary)	Stand Post	NESPAK	1					1	1	2000	1	0.08%				15-Apr-03	15-Apr-03	25-Apr-03	30-Jun-03			
3	District	Tehsil	Mouza Thatha Sunda	Stand Post	NESPAK	1					1	1	1440	1	0.07%				4-Apr-03	4-Apr-03	20-May-03	30-Jun-03			
4	District	Tehsil	Mouza Barkhandar	Pipe Solution	NESPAK	50	20	20	40		0	80				1200	50	7%	01-Feb-03	01-Feb-03	20-Feb-03	30-Jun-03			
			Mouza Barkhandar (Shah Nawaba)	Stand Post		1					1	1	650	1	0.03%				14-Apr-03	15-Apr-03	15-May-03	30-Jun-03			

Annexure-10
Sludge Management Plan

SLUDGE MANAGEMENT PLAN

Introduction:

An integrated sludge management plan would cover aspects across the value chain of on-site sanitation including safe collection, conveyance, treatment and disposal/reuse of the treated sludge.

Objectives of Sludge Management & Treatment

Following are the basic objectives of sludge management or treatment

- Reducing its Volume
- Stabilizing its Organic Materials
- Killing off the odor
- Ensure it can be reused
- Properly digested (Non activated)

Anaerobic Baffled Reactor (ABR)

An Anaerobic Baffled Reactor (ABR) technology will be used to treat sewerage water. ABR is an improved septic tank with a series of baffles under which the wastewater is forced to flow. This technology is easily adaptable and can be applied at the household level, in small neighborhoods or even in bigger catchment areas.

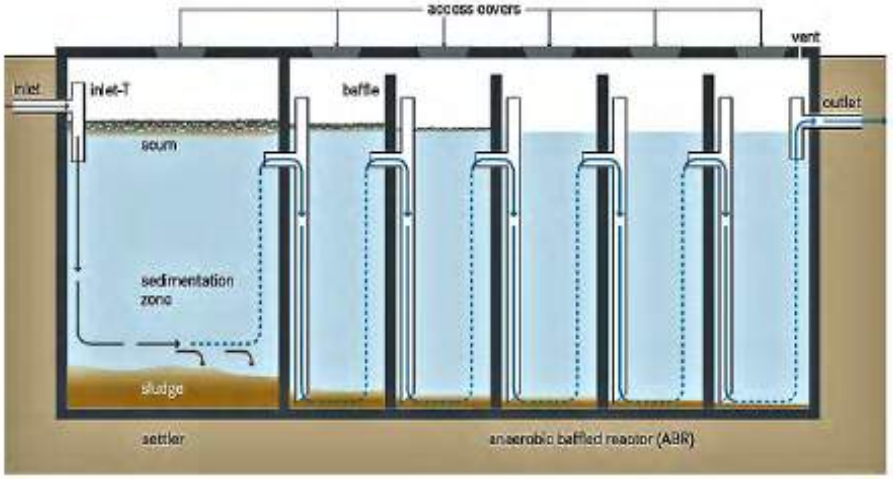

- **Sludge Production**

Sludge production is an inherent part of the operation of an anaerobic baffle reactor (ABR), as it involves the biological breakdown of organic matter by microorganisms. During the treatment process, organic matter is converted to a residual sludge, which consists of biomass, undigested organic matter, and inorganic solids. The amount of sludge produced by an ABR will depend on several factors, including the influent characteristics, hydraulic retention time, and the operating conditions of the reactor. Generally, the longer the hydraulic retention time, the higher the sludge production will be. However, longer retention times may also lead to improved treatment efficiency. It is important to manage the sludge produced by the ABR to prevent excessive accumulation and ensure efficient operation of the system. This may include regular removal of sludge, sludge thickening, digestion, dewatering disposal and monitoring.

- **Sludge Removal from ABR**

Sludge removal from an Anaerobic Baffle Reactor (ABR) is typically required to maintain efficient operation of the system and prevent excessive accumulation of solids. The frequency of sludge removal will depend on factors such as the influent characteristics, hydraulic retention time, and the design of the ABR. In general, it is recommended that sludge should be removed from the ABR when it reaches a certain accumulation level, which can be determined by monitoring the sludge volume and concentration. A common practice is to remove the sludge volume when it reaches around 50% of the reactor volume.

- **Sludge Dewatering**

The digested sludge contains water content ranges from 70% to 95%, with an average of about 85%. This means that the sewerage sludge is relatively wet and contains a significant amount of water. But, even with that moisture content, sludge no longer behaves as a liquid and can be handled as a solid material.

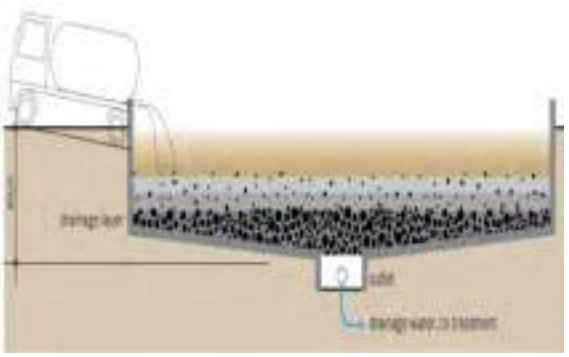

Sludge-drying beds provide the simplest method of dewatering. A digested sludge slurry is spread on an open bed of sand and allowed to remain until dry. Drying takes place by a combination of evaporation and gravity drainage through the sand. A piping network built under the sand collects the water, which is pumped back to the head of the plant. After about six weeks of drying, the sludge cake, as it is called, may have a solids content of about 40 percent. It can then be removed from the sand with a pitchfork or a front-end loader. In order to reduce drying time in wet or cold weather, a glass enclosure may be built over the sand beds.

- **Sludge Disposal / Reuse**

The final destination of treated sewage sludge usually is the land. Dewatered sludge can be buried underground in a sanitary landfill. It also may be spread on agricultural land in order to make use of its value as a soil conditioner and fertilizer after the consent of Village Organization (VO).

- **Monitoring and Maintenance**

It is important to regularly monitor the sludge management process to ensure that it is operating effectively and efficiently. This includes monitoring the quality of the sludge and the effectiveness of the treatment processes.

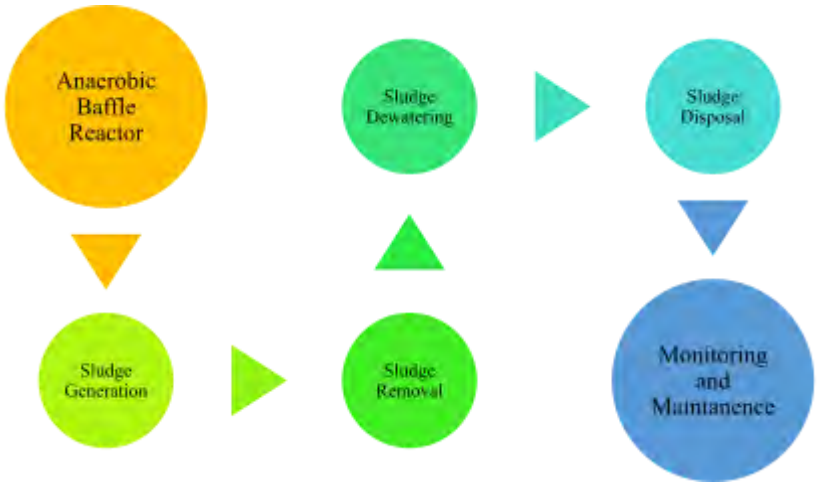

Sludge Management Plan Flowchart

Annexure-11
Grievance Redressal Committees
All three Tiers

Grievance Redressal Committee – (Tier- 1)

PUNJAB RURAL MUNICIPAL SERVICES COMPANY

(COMPANY REGISTERED WITH SECP UNDER SECTION 42 OF THE COMPANIES ACT, 2017)

PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT (PRSWSSP)

ESTABLISHMENT OF FIRST-TIER GRIEVANCES REDRESSAL COMMITTEE (GRC-I)

NOTIFICATION

NO.PRMSC/ORDERS/2022: 05

In pursuance of the implementation of the Environment & Social Management Framework (ESMF), First Tier Grievance Redressal Committee (GRC-I) for the PRSWSSP is hereby constituted as under to address the resolution of outstanding/unsettled issues resulting from the Grievance Redressal Cell deliberation/proceedings.

1	Chairperson Village Organization	Convener
2	Vice Chairperson Village Organization	Member
3	Farmer/Worker	Member
4	Minority Member	Member
5	Youth Member	Member
6	Female Member (Focal Person Females)	Member
7	Lady Health Worker (LHW)	Member
8	BCC Officer, PRMSC	Member
9	Line Department concerned (Education, Health, Revenue etc.)	Member

This committee will be responsible to oversee the overall function of the GRM at a strategic level including monthly reviews at the village community level.

PRMSC

ASADULLAH (PAS)
CEO/PROJECT DIRECTOR
(PRMSC)

Dated Lahore, the 30th October, 2022

No. & Date Even

A copy is forwarded for information to:-

1. All DC's concerned
2. All AC's concerned
3. PA to CEO, PRMSC
4. All Tehsil Managers, PRMSC
5. All the remaining concerned
6. Master file

ADDRESS: 5TH FLOOR, KD PLAZA MM ALAM ROAD, LAHORE
EMAIL: info.prmsc@punjab.gov.pk | WEBSITE: www.prmsc.punjab.gov.pk | PHONE: (042) 99333608 - (042) 99333616

Grievance Redressal Committee – (Tier- 2)

PUNJAB RURAL MUNICIPAL SERVICES COMPANY

(COMPANY REGISTERED WITH SECP UNDER SECTION 42 OF THE COMPANIES ACT, 2017)

PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT (PRSWSSP)

ESTABLISHMENT OF SECOND-TIER GRIEVANCES REDRESSAL COMMITTEE (GRC-II)

NOTIFICATION

NO.PRMSC/ORDERS/2022: 04

In pursuance of the implementation of the Environment & Social Management Framework (ESMF), a Second Tier Grievance Redressal Committee (GRC-II) for the PRWSSP is hereby constituted as under to address resolution on outstanding/unsettled issues resulting from the Grievance Redressal Cell deliberation/proceedings.

1. Tehsil Manager PRMSC	Convener
2. Deputy Manager Operation PRMSC	Member
3. Deputy Manager Infrastructure PRMSC	Member
4. Research Analyst E&S Safeguards PRMSC	Member
5. BCC Officer PRMSC	Member (Focal Person)
6. Assistant Manager Water & Sewerage PRMSC	Member
7. Assistant Manager SWM PRMSC	Member
8. Chairperson VO/GRC-I of Village concerned	Member
9. Line Department concerned (Education, Health, Revenue etc.)	Member

This committee established in SDU-TO for each Tehsil, will manage GRM aspects for all sub-project locations in each tehsil including decisions to be taken, actions and monitoring of complaints resolution at the sub-project level.

PRMSC

ASADULLAH (PAS)
CEO/PROJECT DIRECTOR
(PRMSC)

Dated Lahore, the 30th October, 2022

No. & Date Even

A copy is forwarded for information to:-

1. All DC's concerned
2. All AC's concerned
3. PA to CEO, PRMSC.
4. All Tehsil Managers, PRMSC.
5. All the remaining concerned
3. Master file

ADDRESS: 5TH FLOOR, BD PLAZA MM ALAM ROAD, LAHORE
EMAIL: ... WEBSITE: ... PHONE: ...

Grievance Redressal Committee – (Tier- 3)

PUNJAB RURAL MUNICIPAL SERVICES COMPANY

(COMPANY REGISTERED WITH SECP UNDER SECTION 42 OF THE COMPANIES ACT, 2017)

PUNJAB RURAL SUSTAINABLE WATER SUPPLY & SANITATION PROJECT (PRSWSSP)

ESTABLISHMENT OF A THIRD-TIER GRIEVANCES REDRESSAL COMMITTEE (GRC-III)

NOTIFICATION

NO.PRMSC/ORDERS/2022: 03

In pursuance of the implementation of the Environment & Social Management Framework (ESMF), a third Tier Grievance Redressal Committee (GRC-III) for the PRSWSSP is hereby constituted as under to address the resolution of outstanding/unsettled issues resulting from the Grievance Redressal Cell deliberation/proceedings.

1. Project Director / CEO PRMSC	Convener
2. Chief Operating Officer PRMSC	Member
3. Chief Infrastructure PRMSC	Member
4. Social & BCC Specialist PRMSC	Member (Focal Person)
5. Gender Specialist PRMSC	Member
6. Environmental Specialist	Member
7. Section Officer (Projects) LG&CD	Member
8. Chairperson VO/GRC-I of village concerned	Member
9. Line Department concerned (Education, Health, Revenue etc.)	Member

This committee will be responsible to oversee the overall function of the GRM at a strategic level including monthly review.

PRMSC

ASADULLAH (PAS)
CEO/PROJECT DIRECTOR
(PRMSC)

Dated Lahore, the 30th October, 2022

No. & Date Even

A copy is forwarded for information to:-

1. All DC's concerned
2. All AC's concerned
3. PA to CEO, PRMSC.
4. All Tehsil Managers, PRMSC.
5. All the remaining concerned
6. Master file

ADDRESS: 5TH FLOOR, KD PLAZA MM ALAM ROAD, LAHORE
EMAIL: info.prmsc@punjab.gov.pk | WEBSITE: www.prmsc.punjab.gov.pk | PHONE: (042) 99333808 – (042) 99333816

Annexure-12
Environmental Testing Results

Environmental Monitoring

Environmental quality testing results including groundwater, surface water and air quality monitoring results of 42 proposed villages can be accessed through the following link

https://drive.google.com/file/d/1BIDeepcFfqIZbfXoWW0EAkGSzJ9A9HdQ/view?usp=sharing

Annexure-13

E&S Compliance Checklist

ENVIRONMENTAL & SOCIAL MONITORING

Project: Punjab Rural Sustainable Water Supply and Sanitation Project	**Tehsil:**	**Phase:**	**Date of Visit:**
Project Proposed Activities:			
E&S Category of Project: E-2 & S-3			
Instruments Developed for E&S Compliance: Environmental & Social Management Plan (ESMP) and Environmental & Social Impact Assessment (ESIA)			
Estimated Cost of E&S Instruments Implementation / Execution:			

A. Site-Specific Observations as per the approved E&S Instruments:

Sr. No.	Physical Observation at Site	Yes	No	Monitorable Indicators	Yes	No
1.	**Contractors' agreement has E&S specific clauses and instruments are attached with agreement?**			• Document Verification		
2.	**E&S Items are filled by contractor in Bid?**			• Document Verification		
3.	**Contractor has approved C-ESMP / site specific ESMP?**			• Document Verification		
4.	**Relevant E&S Instruments copy is present at site?**			• Document Verification		
5.	**EHS SOPs for Labor / Construction Workers (Including Women Workers)-copy is present at site?**			• Document Verification		
6.	**First Aid Box?**			• First Aid Box items / medicine is not expired?		

7.	**Safety Signage?**			• Visual Observation and Pictures		
8.	**Construction area is cordoned off with reflective tapes?**			• Visual Observation and pictures		
9.	**Fire Safety Equipment?**			• Fire Extinguisher is Filled? • Is there any trained worker / labor present at site who knows to handle the fire extinguisher in case of emergency?		
10.	**Presence of Environmental Specialist / EHS Manager at site as per the approved E&S Instrument?**			• Attendance registers to verify his presence?		
11.	**Social Specialist / Resettlement Specialist hired?**			• Attendance registers to verify his presence?		

Sr. No.	**Environmental & Social Issues**	**Mitigation Measure**	**Means of Monitoring**	**Result Indicator**	**Status of Mitigation Measure be adopted**		**Remarks**
					Yes	**No**	
A. Site Inspections							
1.	**Noise**	Use of machinery & equipment having less noise.	Visual Inspection				

Sr. No.	Environmental & Social Issues	Mitigation Measure	Means of Monitoring	Result Indicator	Status of Mitigation Measure be adopted		Remarks
					Yes	No	
		Well-tuned vehicles / machinery is being used	Any complaint from the local residents				
2.	**Fugitive Dust**	Provision for personal protective equipment (PPEs) i.e., Mask by the labor/workers	Visual Inspection				
		Sprinkling of water	Visual Inspection to ensure water sprinkling is being implemented				
3.	**Waste[7] Management**	Immediately transport the accumulated construction waste to a site identified by the concerned MC	Visual inspection that solid waste is disposed-off at designated site				
			Any complaint from the local residents				
B. EHS Management of Labor and Worker							

[7] Debris and excavated material or parcel / unpacking materials related to

Sr. No.	Environmental & Social Issues	Mitigation Measure	Means of Monitoring	Result Indicator	Status of Mitigation Measure be adopted		Remarks
					Yes	No	
4.	**Health, Safety and Environmental**	**Labor Camp Management**					
		Located away from any community.	Inspection of location of labor camp				
5.	**SOPs for Labor / Workers (Including Women Workers)**	Labor facilitated with potable water, Hygienic sanitary facilities and comfortable livings with heating & cooling facilities.	Visual Inspection				
		Provided with sewage treatment facility i.e., Septic Tanks & Soakage Pits[8]	Visual Inspection				
		Proper management of solid waste and garbage					
		Provided with firefighting station i.e., Fire extinguishers (DCP), Fire	Visual Inspection				

[8] In case of absence of sewerage / drainage system and flush toilets

Sr. No.	Environmental & Social Issues	Mitigation Measure	Means of Monitoring	Result Indicator	Status of Mitigation Measure be adopted		Remarks
					Yes	No	
		buckets, Spade, Fire Buzzer etc.					
		Provided with hygiene mess facility for labor.	Visual Inspection				
		Provided with health care facilities					
		Separate rooms, toilets and health and hygiene facilities in case of women labor residents at labor camp					
		Construction Site Management					
		Adequate safety precautions (PPEs) such as helmets, safety shoes, gloves, etc. should be provided to the labor	Inspection of usage of Personal Protective Equipment during execution				
		Contractor shall provide health care facility at site i.e. First Aid Box,	Visual Inspection				

Sr. No.	Environmental & Social Issues	Mitigation Measure	Means of Monitoring	Result Indicator	Status of Mitigation Measure be adopted		Remarks
					Yes	No	
		Ambulance etc. onsite as well as at labor campsite.					
		Children of less than 14 years of age and pregnant women are not hired.	Visual Inspection				
		Construction site safety ensured by Contractor. i.e., Safety Barricades, Safety Cones, Safety Boards etc.	Visual Inspection				
6.	**Applicability of all other instructions as per EHS SOPs**						
C. Social Issues Management of Community							

Sr. No.	Environmental & Social Issues	Mitigation Measure	Means of Monitoring	Result Indicator	Status of Mitigation Measure be adopted		Remarks
					Yes	No	
7.	**Public Consultation**	Local residents will be consulted before and during execution phase regarding their views i.e., either they are satisfied with the Contractor's activities or not and grievance (if any)	Consultation with local residents / community				
8.	**Vehicles Movement and Physical Obstructions**	Provision of alternative routes	Visual inspection to see whether proper traffic signs, safety barriers / safety strips for traffic management are placed				
		Indicators / signboards regarding alternate routes and other instructions be provided at proper distance.					
		Display of emergency contact numbers					
9.	**Infrastructure Losses i.e., loss of land, damage to structures,**	Complaint from the local residents	Record of any grievance and mode of compensation provided				

Sr. No.	Environmental & Social Issues	Mitigation Measure	Means of Monitoring	Result Indicator	Status of Mitigation Measure be adopted		Remarks
					Yes	No	
	damage to plants etc.	In case of any losses Contractor should compensate the owner immediately					
10.	**Obstruction in public access**	Provision of alternate routes	Visual inspection Record of public grievance				
		Wooden blocks / ramps will be provided for safe passage of pedestrians / locals etc.	Visual inspection Record of public grievance				
11.	**Privacy Issues**	Workers should be trained to address privacy issues and ethically behaved.	Visual Inspection and record of grievance				
12.	**Economic Losses**	In case of obstruction of passage, shopkeepers / local businesses may affect, alternate routes will be provided. In case of any loss,	Record of Public Grievance Visual Inspection				

Sr. No.	Environmental & Social Issues	Mitigation Measure	Means of Monitoring	Result Indicator	Status of Mitigation Measure be adopted		Remarks
					Yes	No	
		compensation will be provided by the Contractor					
13.	**Nuisance / Disturbance to Social Sensitive Areas**	No work will be conducted near the religious places during religious congregations.	Visual Inspection Issues Reported				
		Material transport to the site will be scheduled considering school timings.					
		Implement all measures suggested elsewhere in this report – dust and noise control, public safety, traffic management, strictly at the sites.					
14.	**Influx of Labor**	Labor camp(s) will be established away from residential population.	Visual Inspection Hiring Protocols				

Sr. No.	Environmental & Social Issues	Mitigation Measure	Means of Monitoring	Result Indicator	Status of Mitigation Measure be adopted		Remarks
					Yes	No	
		Preference will be given to the local people to work with contractor, and contractor should hire maximum labor force from the project area because this will reduce the labor influx.	Issues Reported				
		Construction work will be completed within the stipulated time to move workers to next location.					
		Labor force will be shuffled with the time.					
		Contractor shall provide health care facility at site i.e. PPEs, First Aid Box, Ambulance etc. onsite as well as at labor campsite.					
		Prohibiting drugs, alcohol, weapons, and ammunition on the					

Sr. No.	Environmental & Social Issues	Mitigation Measure	Means of Monitoring	Result Indicator	Status of Mitigation Measure be adopted		Remarks
					Yes	No	
		worksite among personnel.					
		Develop and enforce a strict code of conduct for workers to regulate behavior in the local communities.					
		Labor facilitated with potable water, Hygienic sanitary facilities and comfortable livings with heating & cooling facilities.					
15.	**Gender Based Violence (GBV)**	Workers will not be allowed to crowd in the residential communities within the site.	Visual Inspection Any Complaint from women.				
		Alternative routes for pedestrian will be provided to avoid mixing of women with workers.					

Sr. No.	Environmental & Social Issues	Mitigation Measure	Means of Monitoring	Result Indicator	Status of Mitigation Measure be adopted		Remarks
					Yes	No	
		The Contractor will make sure that no discrimination is made on the basis of gender in case of hiring of workers.	Reported Issues				
		Contractor will take proper measures to address and resolve issues relating to harassment, intimidation, and exploitation, especially in relation to women.					
16.	**Social / Cultural Conflicts**	Local labor will preferably be employed for construction works.	Visual Inspection				
		Careful planning and training of workforce to minimize disturbance to the local people.	Record of public grievance				

Sr. No.	Environmental & Social Issues	Mitigation Measure	Means of Monitoring	Result Indicator	Status of Mitigation Measure be adopted		Remarks
					Yes	No	
D. COVID-19 Related SOPs of Government of Punjab at Construction Sites[9]							
17.	**Covid-19 SOPs Implementation**	Usage of surgical face mask by workers	Visual Inspection				
		Keep social distancing / avoid gatherings of workers	Visual Inspection				
		Provision of hand washing facility onsite for workers	Visual Inspection				
18.	**Any other Issue?**						

Monitored by:	**Monitored by:**
Name:	**Name:**
Designation:	**Designation:**

[9] Will be applicable during the pandemic

Date:	**Date:**
Signature:	**Signature:**
